

**342nd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
April 2014**



KATRA RAILWAY STATION



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-70
Sector wise Graph	71-81
ANNEXURE	82-82
Central Sector Projects	83-83
List of Projects Having Expenditure More than cost	84-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-106
List of On schedule Projects Original Schedule	107-113
List of Delayed Projects w.r.t Original Schedule	114-127
List of Projects Having Time and cost overrun w.r.t original	128-132
List of Projects Having cost overrun w.r.t original	133-144
List of Projects without Milestones	145-166
List of On schedule Projects w.r.t. Latest Schedule	167-174
List of Projects Ahead of Schedule w.r.t Latest Schedule	175-175
List of Delayed Projects w.r.t Latest Schedule	176-189

कार्यकारी सारांश

1. अप्रैल, 2014 की फ्लैश रिपोर्ट में ` 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 727 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अप्रैल, 2014 के दौरान किसी भी परियोजना के पूरा होने की सूचना नहीं दी गई है।

2. संदर्भाधीन माह के दौरान, 727 परियोजनाओं में से, 282 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 48 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 48 परियोजनाओं में से, 16 परियोजनाएं ` 1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	283	36	6	1
2.	सड़क परिवहन एवं राजमार्ग	136	82	22	6
3.	विद्युत	100	54	7	5
4.	पेट्रोलियम	84	53	5	1
5.	कोयला	56	28	0	0
6.	इस्पात	20	13	3	2
7.	पोत परिवहन एवं पत्तन	19	4	0	0
8.	दूरसंचार	10	4	3	0
9.	नागर विमानन	8	3	1	0
10.	शहरी विकास	5	1	0	0
11.	परमाणु ऊर्जा	4	4	1	1
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		727	282	48	16

3. 727 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ` 9,45,396.60 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ` 11,34,330.13 करोड़ रुपए होने की संभावना है जो 1,88,933.53 करोड़ (मूल लागत का 20.00%) की समय लागत वृद्धि को दर्शाता है। अप्रैल, 2014 तक इन परियोजनाओं पर किया गया व्यय ` 5,64,250.65 करोड़ है जो परियोजनाओं की अनुमानित लागत का 49.70% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (30.04.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (` करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	एन.आर.	2000.00	985.42

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (30.04.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	जिरीबाम से इंफाल (तुपु) (एनएल) (एनईएफआर)	रेलवे	04/2003	727.56	5996.00	5268.44
3	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.33	11609.00	5214.00
4	सुबानश्री लोअर एचईपी (एनएचपीसी)	विद्युत	09/2003	6285.33	10667.00	4381.67
5	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 727 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 123 समय पर तथा 282 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 259 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 22 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 295 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 282 विलंबित परियोजनाओं में से, 65 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 71 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 80 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 66 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (30.04.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
2	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2013	238
3	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	09/2013	143
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	12/2016	141
5	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	181

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, उपस्कर स्थापित करना, भूखनन की स्थिति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी

परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (30.04.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)		संचयी व्यय (रु. करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (30.04.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (30.04.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

□) नागर विमानन क्षेत्र में 8 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । 'पकियोंग (सिक्किम) में नए एयरपोर्ट का निर्माण, एएआई' नामक परियोजना के संबंध में खराब मौसम की स्थिति तथा श्रमिक की कमी के कारण 21 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

□□) परमाणु उर्जा क्षेत्र में, सभी 4 परियोजनाएं विलंबित हैं । परियोजना 'कुडनकुलम एटोमिक पावर प्लांट, (एनपीसीआईएल)' (मेगा परियोजना) में संविदात्मक मुद्दे के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

000) **इस्पात क्षेत्र** में 20 परियोजनाओं में से 13 परियोजनाएं विलंबित हैं । माह के दौरान, 3 परियोजनाओं के संबंध में 1-2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 बड़ी परियोजनाएं हैं । परियोजना 'कोक ओवन बैट्री सं. 4, चरण-00, आरआईएनएल' तथा 'इसको इस्पात संयंत्र का विस्तार, सेल' में क्रमशः कार्यों के आवंटन में हुए विलंब तथा कार्यों के क्षेत्र में परिवर्तन के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बोकारों इस्पात संयंत्र का विस्तार, सेल' में विद्युत के स्थिरीकरण तथा स्वचालन प्रणाली में विलंब के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

00) **दूरसंचार क्षेत्र** में, 10 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान 3 परियोजनाओं के संबंध में 1-9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'आपूर्ति स्थापना परीक्षण तथा ग्रामीण वाईमैक्स नेटवर्क की शुरुआत चरण-00, बीएसएनएल' में न्यायिक मामले के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं असम दूरसंचार क्षेत्र चरण-0.0, 2जी व 3जी बीएसएनएल' में कानून और व्यवस्था की समस्याओं के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; और परियोजना 'तैयार आधार पर बीएसएनएल में ईआरपी कार्यान्वयन, बीएसएनएल' में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

0) **रेलवे क्षेत्र** में 283 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं । माह के दौरान, 6 परियोजनाओं के संबंध में 3-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 बड़ी परियोजना है । परियोजनाएं 'रांची-लोहरदगा, (जीसी), एसईआर' तथा 'डैंगोआपोजी-राजखरस्वान तीसरी डबलिंग, एसईआर' के संबंध में क्रमशः कानून और व्यवस्था तथा तीव्र रेत और नींव की समस्या के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'गुना-इटावा वाया शिवपुरी- ग्वालियर-भिन्ड, एनएल, एनसीआर' में खंभों में दरार की घटना के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'आगरा-इटावा वाया फतेहाबाद और बाह, (एनएल), एनसीआर' में भूमि अधिग्रहण में विलंब के कारण 7 माह के अतिरिक्त

विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'खुर्जा-मेरठ-सहारनपुर तथा गाजियाबाद-मेरठ का विद्युतीकरण, आरई' तथा 'कानपुर-कासगंज-मथुरा, (जीसी), एनईआर' में क्रमशः 7 तथा 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

००) **पेट्रोलियम क्षेत्र** में, 84 परियोजनाओं में से 53 परियोजनाएं विलंबित हैं । माह के दौरान 5 परियोजनाओं के संबंध में 1-18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 परियोजना मेगा परियोजना है । परियोजना 'डी-1 क्षेत्र का अतिरिक्त विकास, ओएनजीसी' में वेल प्लेटफॉर्म की स्थापना में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बी-173 ए क्षेत्र का आईओआर, ओएनजीसी' में कार्यों के पुरस्कार में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'वैक्स परियोजना एनआरएल' में निर्माण गतिविधियों में धीमी प्रगति के कारण 18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पारादीप में मार्केटिंग टर्मिनल, आईओसीएल' तथा 'दाभोल बंगलौर पाइप लाइन परियोजना, चरण-००, गेल' में क्रमशः 3 तथा 17 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

०००) **विद्युत क्षेत्र** में, 100 परियोजनाओं में से 54 परियोजनाएं विलंबित हैं । माह के दौरान 7 परियोजनाओं के संबंध में 1-24 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 5 परियोजनाएं मेगा परियोजनाएं हैं । परियोजनाएं 'सुबनसिरी लोअर एच.ई.पी., एनएचपीसी' और 'नॉदर्न रिजन ट्रांसमिशन स्ट्रेंथनिंग स्कीम, पीजीसीआईएल' में क्रमशः कानून और व्यवस्था तथा आरओयू समस्याओं के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'तीस्ता लो डैम एचईपी, चरण-००, एनएचपीसी,' तथा 'डीवीसी तथा मैथूब आरबीसी सहित 765 केवी पूर्लिंग स्टेशन तथा नेटवर्क, पीजीसीआईएल' में क्रमशः सिविल ठेकेदार के वित्तीय संकट तथा पर्यावरण संबंधी अनुमति में विलंब के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'डीवीसी तथा मैथून आरबीसी से जुड़े पारेषण प्रणाली, पीजीसीआईएल' में माओवादी समस्या के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'छत्तीसगढ़ में आईपीपी जेनरेशन परियोजना हेतु चंपा तथा रायगढ़ में पूर्लिंग स्टेशनों की स्थापना, पीजीसीआईएल' में भूमि अधिग्रहण के कारण 4 माह के अतिरिक्त विलंब की

सूचना प्राप्त हुई है; 'दक्षिणी क्षेत्र-0000 पीजीसीआईएल में व्यवस्था के सुदृढीकरण' संबंधी परियोजना से 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

0000)सड़क क्षेत्र में 136 परियोजनाओं में से 82 परियोजनाएं विलंबित हैं । माह के दौरान 22 परियोजनाओं के संबंध में 3-23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 6 बड़ी परियोजनाएं हैं । परियोजनाएं 'धरमतुल से सोनापुर 205-183 कि.मी (एएस-20), एनएचएआई', 'दिल्ली/हरियाणा बॉर्डर से रोहतक, एनएचएआई' तथा 'पटना-बक्तजारपुर 181.3 कि.मी. से 231.95 कि.मी., एनएचएआई' प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'जोरबट्ट-बारापानी, एनएचएआई' और 'कृष्णागिरी-तिंदीबनम (अनुमोदित लंबाई 170 कि.मी.) का 2 लेनिंग, एनएचएआई' प्रत्येक में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'कुंदपुर-सुरथकल और मंगलौर, एनएचएआई' और 'होसुर-कृष्णागिरी का छः लेनिंग एनएच-7 33.130 कि.मी. से 93.00 कि.मी., एनएचएआई' प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'कृष्णागिरी का छः लेनिंग-बलझापेट सेक्शन 0.00 कि.मी. से 148.3 कि.मी. एनएच-46, एनएचएआई' तथा 'पनवेल-इन्दापुर, एनएचएआई' में भी प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'हरंगाजों से मैबंग, 164.08 कि.मी.-190.587 कि.मी. एनएच-54, एनएचएआई' तथा 'पूणे-सोलापुर, पीकेजी-00, एनएचएआई' प्रत्येक में 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पीएस मोतिहारी-रक्सौल के साथ 2 लेनिंग, एनएचएआई' तथा 'हरिद्वार-देहरादून (अनुमोदित लम्बाई 69), एनएचएआई' में क्रमशः 8 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'नागपुर-बेतुल का 4 लेनिंग, एनएचएआई' तथा 'क्वाजीगुंड-बनिहाल 220.00 कि.मी. से 188.00 कि.मी., एनएचएआई' प्रत्येक में 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'नाशरी छननी, एनएचएआई' तथा 'निरोली-राँवसी-राजमुंडा, एनएचएआई' प्रत्येक में 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'सिल्चर-उदारबंद (चरण-00) एनएच-54, 309 कि.मी. से 275 कि.मी., एनएचएआई' तथा 'वाराणसी-औरंगाबाद 786 कि.मी. से 978.40 कि.मी., एनएचएआई' प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पनिखोली-रिमोली, एनएचएआई' तथा 'वालायार-वडक्कनचेरी सेक्शन, एनएचएआई' में क्रमशः 13 तथा 20 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पीएस रायबरेली से इलाहाबाद के साथ 2 लेनिंग, एनएचएआई' में 23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

10. दिनांक 30.04.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ` 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for April 2014 contains information on the status of the 727 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During April 2014, no project has reported completion.

2. During the reference month, out of 727 projects, 282 projects are delayed with respect to original schedule and 48 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 48 projects, 16 are Mega Projects costing ₹ 1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	283	36	6	1
2.	ROAD TRANSPORT AND HIGHWAYS	136	82	22	6
3.	POWER	100	54	7	5
4.	PETROLEUM	84	53	5	1
5.	COAL	56	28	0	0
6.	STEEL	20	13	3	2
7.	SHIPPING AND PORTS	19	4	0	0
8.	TELECOMMUNICATIONS	10	4	3	0
9.	CIVIL AVIATION	8	3	1	0
10.	URBAN DEVELOPMENT	5	1	0	0
11.	ATOMIC ENERGY	4	4	1	1
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		727	282	48	16

3. Total original cost of implementation of the 727 projects was about ₹ 9,45,396.60 crore and their anticipated completion cost is likely to be ₹ 11,34,330.13 crore, which reflects an overall cost overruns of ₹ 1,88,933.53 crore (20.00 % of original cost). The expenditure incurred on these projects till April 2014 is ₹ 5,64,250.65 crore, which is 49.70 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as follows:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 30-04 -2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	AKOLA-KHANDWA GC AKOLA-AKOT	Railways	04/2008	184.26	N.R.	2000.00	985.42

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 30-04-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	5996.00	5268.44
3	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.33	11609.00	5214.00
4	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
5	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 727 projects, 5 projects are ahead of schedule, 123 are on schedule and 282 are delayed with respect to original schedule. However, the numbers of delayed projects further decrease to 259 if delay is calculated on the basis of latest schedule of completion. Further, 22 projects have been sanctioned without any commissioning schedule/date and for 295 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 282 delayed projects, 65 projects have overall delay in the range of 1 to 12 months, 71 projects have a delay in the range of 13 to 24 months, 80 projects have a delay in the range of 25 to 60

months and 66 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-04-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	238
3	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	143
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	181

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipments, fund constraints, geological surprises, equipment erection, geo-mining condition, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issue, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as follows:-

List of 5 Earliest Projects without Milestones (as on 30-04-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as follows:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30-04-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing or updating revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 30.04.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Civil Aviation Sector**, out of 8 projects, 3 projects are delayed. The project 'Construction of New Airport at Pakyong (Sikkim), AAI' has reported additional delay of 21 months due to bad weather condition and shortage of labour.

ii) In the **Atomic Energy Sector**, all the 4 projects are delayed. The project 'Kudankulam Atomic Power Plant, (NPCIL)' (Mega Project) has reported additional delay of 3 months due to contractual issue.

iii) In the **Steel Sector**, out of 20 projects, 13 projects are delayed. During the month, 3 projects have reported additional delays in the range of 1-2 months, out of which 2 are Mega projects. The project 'Coke Oven Battery No. 4 Phase-II, RINL' and 'Expansion of IISCO Steel Plant, SAIL' have reported additional delay of 1 month each due to delay in awarding of works and change in scope of works respectively; the project 'Expansion of Bokaro Steel Plant, SAIL' has reported additional delay of 2 months due to delay in stabilization of electrical and automation system.

iv) In the **Telecommunication Sector**, out of 10 projects, 4 projects are delayed. During the month, 3 projects have reported additional delay in the range of 1-9 months. The project 'Supply Installation Testing and Commissioning of Rural Wimax Network Phase-II, BSNL' has reported additional delay of 1 month due to court case; the project 'Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL' has reported additional delay of 3 months due to law & order problems; and the project 'ERP Implementation in BSNL on Turnkey Basis, BSNL' has reported additional delay of 9 months (however, no specific reasons have been reported by the project authority for the delay in this project).

v) In the **Railways Sector**, out of 283 projects, 36 projects are delayed. During the month 6 projects have reported additional delays in the range of 3-24 months, out of which 1 is Mega project. The projects 'Ranchi-Lohardaga, (GC), SER' and 'Dangoaposi-Rajkharswan 3rd Line Doubling, SER' have reported additional delays of 3 months each due to law & order problems and acute sand and foundation problem respectively; the project 'Guna-Etawah via Shivpuri-Gwalior –Bhind, NL, NCR' has reported additional delay of 5 months due to occurrence of cracks in piers; the project 'Agra-Etawah via Fatehabad and Bah, (NL), NCR' has reported additional delay of 7 months due to delay in

land acquisition; and the projects 'Electrification of Khurja-Meerut-Saharanpur and Ghaziabad-Meerut, RE' and 'Kanpur-Kasganj-Mathura, (GC), NER' have reported additional delays of 7 and 24 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

vi) In the **Petroleum Sector**, out of 84 projects, 53 projects are delayed. During the month 5 projects have reported additional delays in the range of 1-18 months, out of which 1 is Mega project. The project 'Additional Development of D-1 Field, ONGC' has reported additional delay of 1 month due to delay in installation of well platform; the project 'IOR of B-173A field, ONGC' has reported additional delay of 3 months due to delay in award of works; the project 'Wax Project, NRL' has reported additional delay of 18 months due to slow progress in construction activities; and the project 'Marketing Terminal at Paradeep, IOCL' and 'Dabhol Bangalore Pipeline Project Phase-II, GAIL' have reported additional delays of 3 and 17 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

vii) In the **Power Sector**, out of 100 projects, 54 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-24 months, out of which 5 are Mega projects. The projects 'Subansiri Lower H.E.P, NHPC' and 'Northern Region Transmission Strengthening Scheme, PGCIL' have reported additional delay of 1 month each due to law & order problems and ROW problems respectively; the projects 'Teesta Low Dam HEP, Stage-IV, NHPC' and '765 KV Pooling Station and Network with DVC and Maithob RBC, PGCIL' have reported additional delays of 2 months each due to financial crunch of civil contractor and environment clearance respectively; the project 'Supplimentary Transmission Associated with DVC and Maithon RBC, PGCIL' has reported additional delay of 3 months due to maoist problem; the project 'Establishment of Pooling Stations at Champa and Raigarh for IPP Generation Project in Chhattisgarh, PGCIL' has reported additional delay of 4 months due to delay in land acquisition; and the project 'System Strengthening in Southern Region – XXII, PGCIL' has reported additional delay of 24 months (however, no specific reason has been reported by the project authority for the delay in this project).

viii) In the **Road Sector**, out of 136 projects, 82 projects are delayed. During the month 22 projects have reported additional delays in the range of 3-23 months, out of which 6 are Mega projects. The projects 'Dharamtul to Sonapur, Km 205-183 (AS-20), NHAI', 'Delhi/ Haryana Border to Rohtak, NHAI' and 'Patna-Baktzarpur Km.181.3 to Km.231.95, NHAI' have reported additional delays of 3 months each; the projects 'Jorbat – Barapani, NHAI' and '2-Laning of Krishnagiri-Tindivanam (Approved Length 170 Km), NHAI' have reported additional delays of 5 months each; the projects 'Kundupur-Surathkal & Manglore, NHAI' and 'Six Lanning of Hosur- Krishnagri NH-7 Km.33.130 to Km.93.00, NHAI' have reported additional delays of 6 months each; the projects 'Six Lanning of Krishnagiri- Walajhapet Section Km.0.00 to Km.148.3 NH-46, NHAI' and 'Panvel-Indapur, NHAI' have also reported additional delays of 6 months each; the projects 'Harangajo to Maibang, Km 164.08-190.587 NH-54, NHAI' and 'Pune-Sholapur,PKG-II, NHAI' have reported additional delays of 7 months each; the projects '2-Lanning with PS Motihari-Raxaul, NHAI' and 'Haridwar-Dehradun (Approved Length 69), NHAI' have reported additional delays of 8 and 9 months respectively; the projects '4 Laning of Nagpur-Betul, NHAI' and 'Quazigund-Banihal Km.220.00 to Km.188.00, NHAI' have reported additional delays of 11months each; the projects 'Nashri Chanani, NHAI' and 'Niroli-Roxy-Rajamunda, NHAI' have also reported additional delays of 11months each; the projects 'Silchar-Udarband (Ph.II) NH-54, Km.309 to Km.275, NHAI' and 'Varanasi-Aurangabad Km.786 to Km.978.40, NHAI' have reported additional delays of 12 months each; the projects 'Panikholi-Rimoli, NHAI' and 'Four Lanning of Walayar-Vadakkancherry Section, NHAI' have reported additional delays of 13 and 20 months respectively; and the projects '2-Laning with PS Raibareili to Allahabad, NHAI' have reported additional delay of 23 months (however, no specific reasons have been reported by the project authority for the delay in these project).


10. The status as on 30.04.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	283	6
2	ROAD TRANSPORT AND HIGHWAYS	136	22
3	POWER	100	7
4	PETROLEUM	84	5
5	COAL	56	0
6	STEEL	20	3
7	SHIPPING AND PORTS	19	0
8	TELECOMMUNICATIONS	10	3
9	CIVIL AVIATION	8	1
10	URBAN DEVELOPMENT	5	0
11	ATOMIC ENERGY	4	1
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	727	48

Sectoral break up of on-going infrastructure projects.

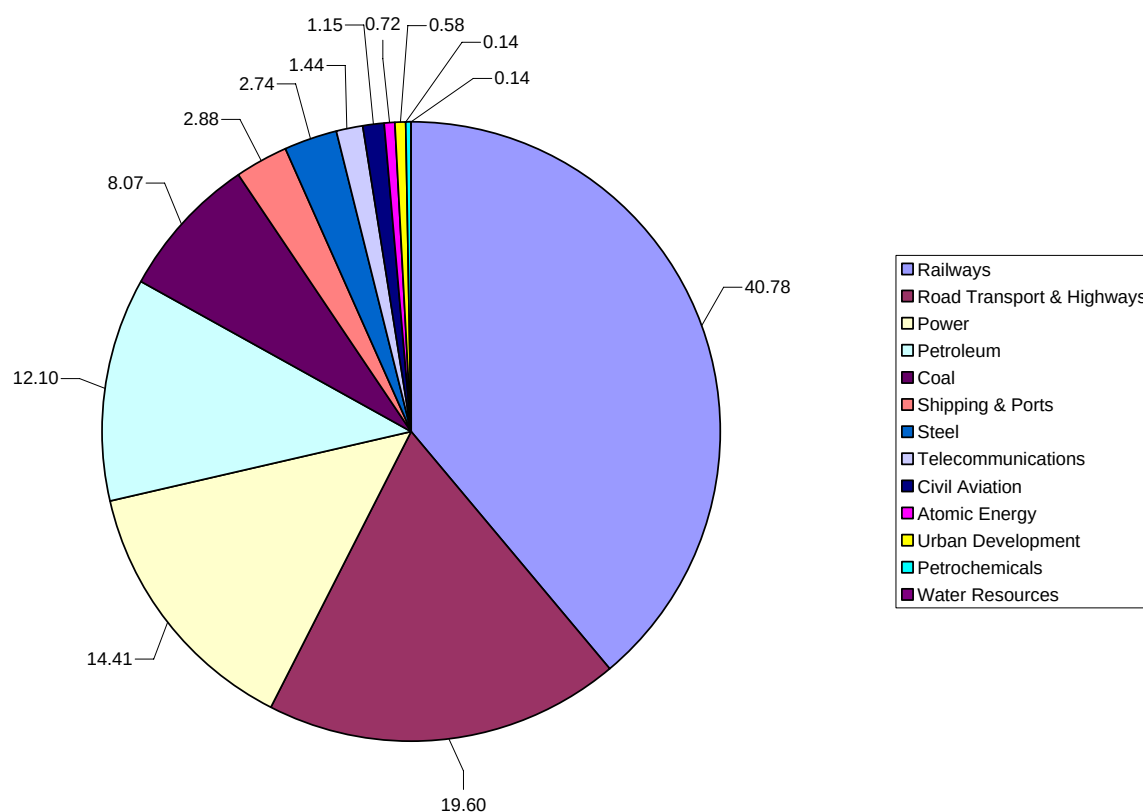

Summary of projects in the Flash Report for the month of April, 2014

Project Implementation - Current Status:


Number of Projects in Previous Month **710**

Number of Projects Added in Current Month **17**

Number of Projects in Current Month **727**


Brief Analysis

Project Status with respect to Original Schedule: Out of 727 projects, 5 projects are ahead of schedule, 123 projects are on schedule and 282 projects are delayed. Of the balance, 295 projects do not have fixed dates of commissioning while 22 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

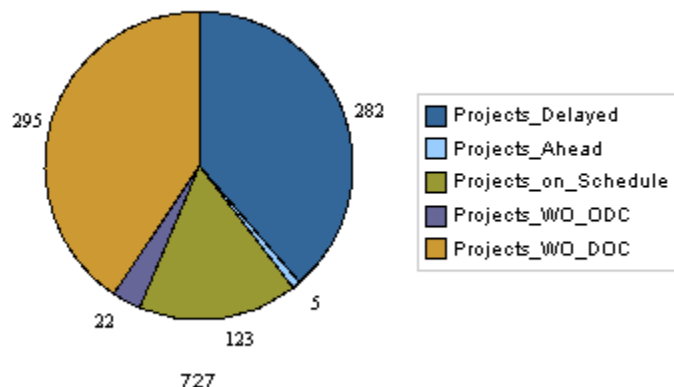

Investment Scenario

Total original cost of implementation of 727 projects when sanctioned, was of the order of Rs. 945396.6 crore but this was subsequently revised to Rs. 1134330.13 crore implying a cost overrun of 20%. The expenditure incurred on these projects till April, 2014 is Rs. 564250.65 crore, which is 49.7% of the revised cost of the projects.

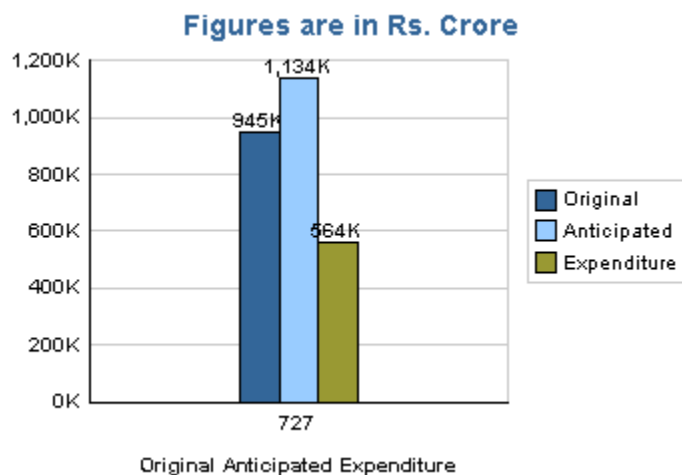

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	710
No of Projects Completed/Dropped/Frozen in Current Month	0
No of Projects added in Current Month	17
No of Projects in Current Month	727

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	282	5	123	22	295	727	38.79
Latest Approved (Date)	259	6	145	22	295	727	35.63

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	590	8,29,184.62	8,95,760.76	4,19,223.40	46.80	66,576.14	8.00
Project with Revision in Cost	137	1,80,994.94	2,38,569.37	1,45,027.25	60.80	57,574.43	31.80
Total	727	10,10,179.56	11,34,330.13	5,64,250.65	49.74	124150.57	12.29
Original Cost of All Projects							
Original Cost	727	9,45,396.60	11,34,330.13	5,64,250.65	49.70	1,88,933.53	20.00

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	282	495,981.30	605,591.00	398,067.36	65.70	109,609.70	22.10
Latest Approved (RCE)	259	512,764.91	579,699.52	386,841.07	66.70	66,934.61	13.10

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	48	81,592.66	95,657.05	77,667.43	81.20	14,064.39	17.20

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	4,086.1	4,996.7	22.3
3	COAL	56	38,737.4	48,559.5	25.4	8	9,767.8	20,187.6	106.7
4	STEEL	20	65,959.3	72,188.6	9.4	8	24,551.0	30,810.3	25.5
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	84	195,841.8	208,399.0	6.4	19	56,965.2	75,262.1	32.1
7	POWER	100	246,280.8	267,159.8	8.5	17	49,844.6	70,723.5	41.9
8	RAILWAYS	283	149,809.1	267,704.1	78.7	151	64,579.4	182,765.9	183.0
9	ROAD TRANSPORT AND HIGHWAYS	136	101,597.5	103,690.5	2.1	11	3,312.9	5,430.5	63.9
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	9	8,629.0	11,916.7	38.1
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		727	945,396.6	1,134,330.1	20.0	235	252,305.6	448,410.8	77.7

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	19	22,236.2	27,644.0	24.3	9	11,299.4	17,574.1	55.5
2	ARUNACHAL PRADESH	4	9,512.2	16,857.3	77.2	4	9,512.2	16,857.3	77.2
3	ASSAM	38	23,344.1	36,030.1	54.3	14	11,088.8	23,861.1	115.2
4	BIHAR	46	32,819.0	40,577.1	23.6	16	13,022.6	20,958.7	60.9
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	33	38,022.7	39,094.6	2.8	7	3,021.0	4,413.4	46.1
7	HARYANA	9	4,493.1	6,690.9	48.9	3	1,585.8	3,783.5	138.6
8	HIMACHAL PRADESH	6	15,762.0	22,232.8	41.1	4	11,798.2	18,269.0	54.8
9	JAMMU AND KASHMIR	7	11,965.4	32,751.3	173.7	3	4,904.9	25,690.8	423.8
10	KARNATAKA	35	79,606.4	94,510.7	18.7	18	14,297.2	29,539.7	106.6
11	KERALA	12	22,610.7	25,135.4	11.2	5	5,480.4	8,005.2	46.1
12	MADHYA PRADESH	19	30,777.4	32,003.8	4.0	5	3,317.9	4,963.7	49.6
13	MAHARASHTRA	51	93,259.9	108,351.1	16.2	18	32,687.3	49,813.8	52.4
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	724.1
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	187.8
18	ODISHA	29	59,053.9	65,530.7	11.0	11	32,790.4	39,267.2	19.8
19	PUNJAB	4	1,680.2	1,653.2	-1.6	0	0.0	0.0	0.0
20	RAJASTHAN	25	25,638.7	25,805.9	0.7	5	2,337.2	2,990.6	28.0
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	1,339.5	3,375.4	152.0
22	TAMIL NADU	38	51,343.6	67,575.3	31.6	20	30,997.2	47,228.9	52.4
23	TRIPURA	6	2,966.3	4,737.3	59.7	3	2,129.4	3,934.7	84.8
24	UTTAR PRADESH	28	21,445.4	26,034.4	21.4	10	3,821.3	8,458.5	121.4
25	WEST BENGAL	37	53,363.6	64,424.7	20.7	15	20,508.9	31,570.0	53.9
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,533.9	41,531.3	-0.0	0	0.0	0.0	0.0
28	CHHATISGARH	23	56,979.1	64,487.8	13.2	6	2,585.1	10,093.7	290.5
29	JHARKHAND	27	16,118.8	20,383.6	26.5	8	2,534.9	6,971.4	175.0
30	UTTARAKHAND	6	7,844.0	10,085.1	28.6	4	5,839.0	8,080.1	38.4
31	TELANGANA	20	8,274.1	10,274.9	24.2	4	1,306.9	3,307.7	153.1
32	MULTI STATE	189	200,079.6	224,532.9	12.2	38	21,567.5	48,177.6	123.4
Total		727	945,396.6	1,134,330.1	20.0	235	252,305.6	448,410.8	77.7

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 75
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	989.4	1,042.3	7 - 71
3	COAL	56	38,737.4	48,559.5	25.4	28	24,979.6	35,351.3	24 - 120
4	STEEL	20	65,959.3	72,188.6	9.4	13	64,208.3	70,162.3	10 - 69
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	84	195,841.8	208,399.0	6.4	53	141,092.2	155,263.5	3 - 122
7	POWER	100	246,280.8	267,159.8	8.5	54	135,932.9	155,469.8	1 - 113
8	RAILWAYS	283	149,809.1	267,704.1	78.7	36	26,090.2	77,208.6	3 - 243
9	ROAD TRANSPORT AND HIGHWAYS	136	101,597.5	103,690.5	2.1	82	54,878.3	55,764.5	3 - 114
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	4	2,856.3	4,264.9	2 - 99
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	37 - 68
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		727	945,396.6	1,134,330.1	20.0	282	495,981.3	605,591.0	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	19	22,236.2	27,644.0	24.3	7	15,797.3	19,004.0	11 - 69
2	ARUNACHAL PRADESH	4	9,512.2	16,857.3	77.2	3	9,356.2	16,449.3	25 - 96
3	ASSAM	38	23,344.1	36,030.1	54.3	30	15,347.2	23,699.3	12 - 116
4	BIHAR	46	32,819.0	40,577.1	23.6	11	20,719.4	25,083.5	3 - 98
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	23 - 23
6	GUJARAT	33	38,022.7	39,094.6	2.8	13	24,466.3	24,487.8	4 - 27
7	HARYANA	9	4,493.1	6,690.9	48.9	2	767.1	767.1	49 - 50
8	HIMACHAL PRADESH	6	15,762.0	22,232.8	41.1	4	12,798.3	17,349.0	32 - 106
9	JAMMU AND KASHMIR	7	11,965.4	32,751.3	173.7	5	10,698.4	31,457.5	10 - 181
10	KARNATAKA	35	79,606.4	94,510.7	18.7	6	16,777.3	17,020.6	10 - 44
11	KERALA	12	22,610.7	25,135.4	11.2	5	17,074.0	17,774.0	5 - 58
12	MADHYA PRADESH	19	30,777.4	32,003.8	4.0	8	3,545.9	3,658.7	3 - 72
13	MAHARASHTRA	51	93,259.9	108,351.1	16.2	22	43,279.5	52,051.2	2 - 129
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	72 - 72
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	1	536.0	536.0	5 - 5
16	MIZORAM	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	35 - 113
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	24 - 24
18	ODISHA	29	59,053.9	65,530.7	11.0	17	51,426.8	54,659.3	3 - 84
19	PUNJAB	4	1,680.2	1,653.2	-1.6	1	705.0	705.0	19 - 19
20	RAJASTHAN	25	25,638.7	25,805.9	0.7	6	15,364.0	14,917.7	3 - 68
21	SIKKIM	2	1,648.9	3,684.9	123.5	2	1,648.9	3,684.9	15 - 71
22	TAMIL NADU	38	51,343.6	67,575.3	31.6	15	36,540.7	45,969.7	3 - 99
23	TRIPURA	6	2,966.3	4,737.3	59.7	4	2,417.4	4,188.4	16 - 120
24	UTTAR PRADESH	28	21,445.4	26,034.4	21.4	12	7,265.5	10,068.4	10 - 84
25	WEST BENGAL	37	53,363.6	64,424.7	20.7	11	26,260.6	31,196.6	3 - 141
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,533.9	41,531.3	-0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	23	56,979.1	64,487.8	13.2	14	41,280.9	48,016.3	4 - 120
29	JHARKHAND	27	16,118.8	20,383.6	26.5	10	8,829.4	9,547.6	3 - 129
30	UTTARAKHAND	6	7,844.0	10,085.1	28.6	4	6,097.2	8,228.1	14 - 60
31	TELANGANA	20	8,274.1	10,274.9	24.2	5	1,898.8	3,098.7	24 - 47
32	MULTI STATE	189	200,079.6	224,532.9	12.2	58	99,143.0	107,340.2	1 - 243
Total		727	945,396.6	1,134,330.1	20.0	282	495,981.3	605,591.0	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 75
2	CIVIL AVIATION	8	6,035.5	6,946.0	15.1	3	989.4	1,042.3	7 - 71
3	COAL	56	38,737.4	48,559.5	25.4	27	23,791.2	27,739.0	24 - 84
4	STEEL	20	65,959.3	72,188.6	9.4	10	62,441.9	68,084.6	10 - 69
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	84	195,841.8	208,399.0	6.4	51	136,989.4	147,862.9	3 - 122
7	POWER	100	246,280.8	267,159.8	8.5	52	134,445.3	153,427.8	1 - 106
8	RAILWAYS	283	149,809.1	267,704.1	78.7	35	25,765.2	76,092.1	3 - 243
9	ROAD TRANSPORT AND HIGHWAYS	136	101,597.5	103,690.5	2.1	71	51,745.1	52,228.9	3 - 114
10	SHIPPING AND PORTS	19	15,617.1	18,600.6	19.1	1	1,228.0	2,158.2	58 - 58
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	4	2,018.2	1,843.9	37 - 68
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		727	945,396.6	1,134,330.1	20.0	259	482,349.6	579,699.5	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,625.0	6,946.0	4.8	2	2,660.6	2,981.7	12.1
3	COAL	56	48,533.9	48,559.5	0.1	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,209.4	72,188.6	2.8	3	14,993.1	17,002.3	13.4
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	84	208,537.0	208,399.0	-0.1	8	37,161.1	40,806.6	9.8
7	POWER	100	252,281.1	267,159.8	5.9	14	43,486.9	58,365.6	34.2
8	RAILWAYS	283	178,792.4	267,704.1	49.7	127	66,136.9	155,504.1	135.1
9	ROAD TRANSPORT AND HIGHWAYS	136	102,135.8	103,690.5	1.5	7	2,493.5	4,094.8	64.2
10	SHIPPING AND PORTS	19	17,488.0	18,600.6	6.4	6	4,617.6	5,941.7	28.7
11	TELECOMMUNICATIONS	10	5,079.3	4,982.9	-1.9	3	1,394.0	1,481.5	6.3
12	URBAN DEVELOPMENT	5	74,052.2	79,266.2	7.0	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		727	1,010,179.6	1,134,330.1	12.3	179	203,437.2	332,557.8	63.5

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	1,808.00	2,015.00	13- 13
3	COAL	56	38,737.38	48,559.52	25.36	1	1,188.31	7,612.33	120- 120
4	STEEL	20	65,959.26	72,188.55	9.44	5	9,557.89	13,808.07	37- 69
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	84	195,841.81	208,398.95	6.41	7	19,587.43	32,235.40	20- 122
7	POWER	100	246,280.79	267,159.75	8.48	1	1,657.00	2,978.86	79- 79
8	RAILWAYS	283	149,809.12	267,704.13	78.70	13	5,542.61	20,910.82	0- 141
9	ROAD TRANSPORT AND HIGHWAYS	136	101,597.54	103,690.49	2.06	3	580.65	797.69	67- 81
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	5	5,400.70	7,558.41	10- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		727	945396.6	1134330.13	19.98	36	45322.59	87916.58	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 75
2	CIVIL AVIATION	8	6,035.46	6,946.00	15.09	1	335.61	388.53	23- 23
3	COAL	56	38,737.38	48,559.52	25.36	6	9,127.17	19,498.95	24- 120
4	STEEL	20	65,959.26	72,188.55	9.44	4	23,538.89	29,522.85	31- 69
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	84	195,841.81	208,398.95	6.41	16	54,000.88	71,583.44	12- 122
7	POWER	100	246,280.79	267,159.75	8.48	14	42,009.56	61,546.42	10- 106
8	RAILWAYS	283	149,809.12	267,704.13	78.70	33	22,989.18	74,107.64	3- 243
9	ROAD TRANSPORT AND HIGHWAYS	136	101,597.54	103,690.49	2.06	9	2,038.62	2,949.35	57- 87
10	SHIPPING AND PORTS	19	15,617.12	18,600.58	19.10	3	2,344.46	3,752.98	2- 99
11	TELECOMMUNICATIONS	10	5,079.29	4,982.94	-1.90	1	149.15	158.72	60- 60
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		727	945396.6	1134330.13	19.98	89	173196.52	286455.88	

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	3/2014	3,076.00	9/2017	3,076.00	9/2017
2	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY	4/2013	480.00	2/2016	480.00	2/2016
3	NEW MARKETING TERMINAL AT ENNORE	11/2006	171.83	/	171.83	-
4	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	3,150.00	9/2017	3,150.00	9/2017
5	INSTALLATION OF DEMONSTRATION UNIT OF INDIA DEPT AT GUWAHATI REFINERY	2/2014	163.88	7/2016	163.88	7/2016
6	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS	3/2013	2,913.10	5/2016	2,910.30	5/2016
7	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	10/2013	429.06	10/2014	429.06	10/2014
8	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD	3/2014	2,476.82	12/2018	2,476.82	12/2018
	<u>POWER</u>					
9	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION	5/2014	829.98	9/2016	829.98	9/2016
10	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION	5/2014	303.07	7/2016	303.07	7/2016
11	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	522.29	11/2016	522.29	11/2016
12	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B	3/2014	155.57	3/2016	155.57	3/2016
13	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4	2/2014	378.71	10/2016	378.71	10/2016
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
14	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	1,693.75	8/2011	1,693.75	6/2014
15	4-LANING OF ROHATAK JIND(LENGTH 45 KM)	10/2013	283.25	10/2015	283.25	10/2015
16	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	1,916.79	11/2016	1,916.79	11/2016
17	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	1,266.60	9/2016	1,266.60	9/2016

Milestones (Cumulative due & achieved)		
Total	3447	
Achieved up to month	1429	

List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	12/2014	03/2015	3
	<u>CIVIL AVIATION</u>						
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT AAI	309.46	309.46	01/2011	03/2015	12/2016	21
	<u>STEEL</u>						
3	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	09/2008	05/2014	06/2014	1
4	EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	06/2014	07/2014	1
5	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	03/2014	05/2014	2
	<u>PETROLEUM</u>						
6	ADDITIONAL DEV. OF D-1 FIELD ONGC	2,163.64	2,331.62	06/2012	05/2014	06/2014	1
7	IOR OF B-173A FIELD ONGC	352.49	352.49	03/2014	12/2014	03/2015	3
8	MARKETING TERMINAL AT PARADEEP IOCL	199.75	199.75	06/2014	06/2014	09/2014	3
9	DABHOL BANGALORE PIPELINE PROJECT PHASE-II GAIL	486.00	486.00	09/2013	09/2013	02/2015	17
10	WAX PROJECT NRL	576.60	676.05	12/2013	03/2014	09/2015	18
	<u>POWER</u>						
11	SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	10,667.00	09/2010	08/2018	09/2018	1
12	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	04/2014	05/2014	1
13	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	07/2015	09/2015	2
14	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC PGCIL	7,075.33	7,075.33	08/2012	04/2014	06/2014	2
15	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC PGCIL	2,360.95	2,580.90	08/2012	06/2014	09/2014	3


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	1,961.87	1,961.87	05/2014	05/2014	09/2014	4
17	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII PGCIL	243.53	243.53	08/2014	08/2014	08/2016	24
	<u>RAILWAYS</u>						
18	RANCHI-LOHARDAGA(GC),SER SER	194.07	596.40	06/2004	12/2014	03/2015	3
19	DANGOAPOLI-RAJKHARWAN 3RD LINE DOUBLING SER	309.44	388.67	12/2015	12/2015	03/2016	3
20	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) NCR	158.77	608.02	03/1994	01/2014	06/2014	5
21	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT RE	171.10	246.44	03/2012	03/2014	10/2014	7
22	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	108.00	432.72	12/2009	03/2014	12/2014	9
23	KANPUR-KASGANJ-MATHURA(GC),NER NER	395.00	1,708.41	N.A.	03/2013	03/2015	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
24	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	07/2014	10/2014	3
25	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	03/2014	06/2014	3
26	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 NHAI	574.00	574.00	03/2014	03/2014	06/2014	3
27	JORBAT - BARAPANI NHAI	536.00	536.00	01/2014	01/2014	06/2014	5
28	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) NHAI	624.00	624.00	04/2014	04/2014	09/2014	5
29	KUNDUPUR-SURATHKAL & MANGLORE NHAI	671.00	671.00	N.A.	06/2014	12/2014	6
30	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 NHAI	535.00	535.00	12/2013	12/2013	06/2014	6
31	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 NHAI	1,250.00	1,250.00	12/2013	12/2013	06/2014	6
32	PANVEL-INDAPUR NHAI	942.69	942.69	06/2014	06/2014	12/2014	6
33	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 NHAI	212.00	333.83	09/2007	05/2014	12/2014	7


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
34	PUNE-SHOLAPUR,PKG-II NHAI	835.00	835.00	01/2014	01/2014	08/2014	7
35	2-LANNING WITH PS MOTIHARI-RAXAUL NHAI	375.09	375.09	04/2014	04/2014	12/2014	8
36	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) NHAI	478.00	478.00	10/2013	03/2014	12/2014	9
37	4 LANING OF NAGPUR-BETUL NHAI	2,498.76	2,498.76	08/2014	08/2014	07/2015	11
38	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 NHAI	1,987.00	1,987.00	07/2015	07/2015	06/2016	11
39	NASHRI CHANANI NHAI	2,159.00	2,159.00	06/2015	06/2015	05/2016	11
40	NIROLI-ROXY-RAJAMUNDA NHAI	586.00	586.00	01/2014	01/2014	12/2014	11
41	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHAI	157.47	157.47	09/2007	12/2013	12/2014	12
42	VARANASI-AURANGABAD KM.786 TO KM.978.40 NHAI	2,848.00	2,848.00	03/2014	03/2014	03/2015	12
43	PANIKHOLI-RIMOLI NHAI	1,410.00	1,410.00	09/2014	09/2014	10/2015	13
44	FOUR LANNING OF WALAYAR- VADAKKANCHERRY SECTION NHAI	682.00	682.00	10/2013	03/2014	11/2015	20
45	2-LANING WITH PS RAIBAREILI TO ALLAHABAD NHAI	291.36	291.36	01/2014	01/2014	12/2015	23
	<u>TELECOMMUNICATIONS</u>						
46	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II BSNL	1,148.19	964.37	05/2011	05/2014	06/2014	1
47	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	06/2014	09/2014	3
48	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS BSNL	384.00	384.00	10/2010	03/2014	12/2014	9

Graphical Presentation of All Projects w.r.t. Original Schedule

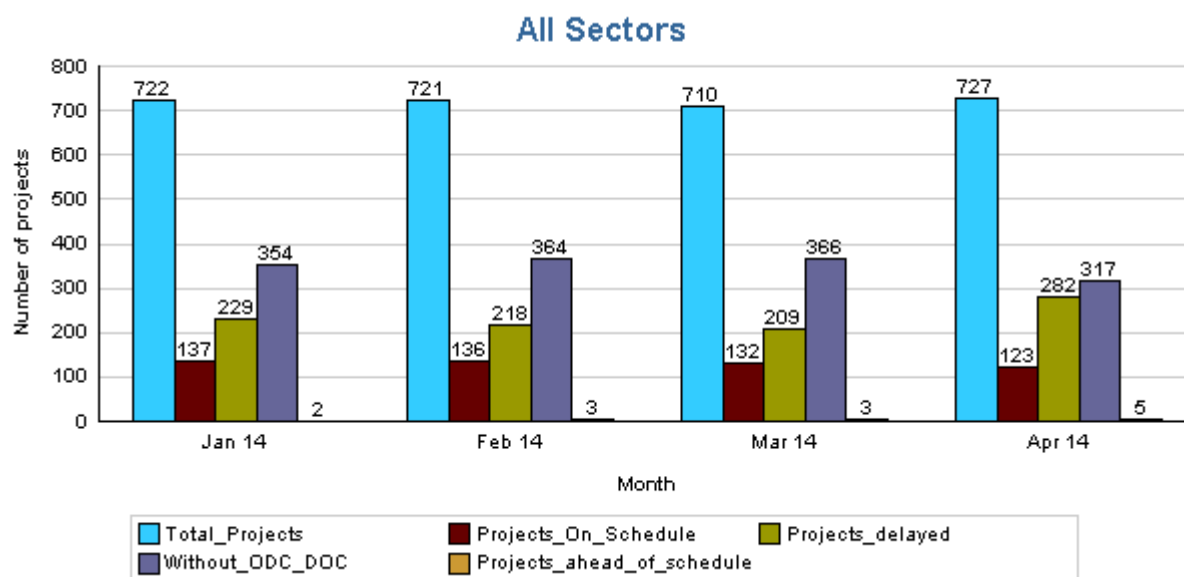


Break-up of 282 Delayed projects in April 2014

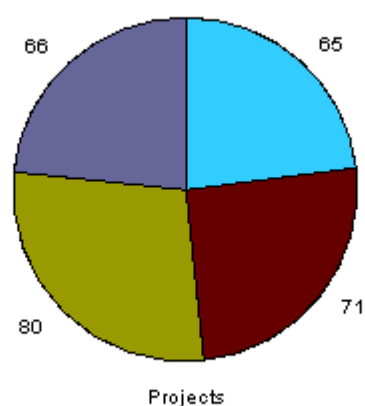


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
Projects	65	71	80	66

Graphical Presentation of All Projects w.r.t. Revised Schedule

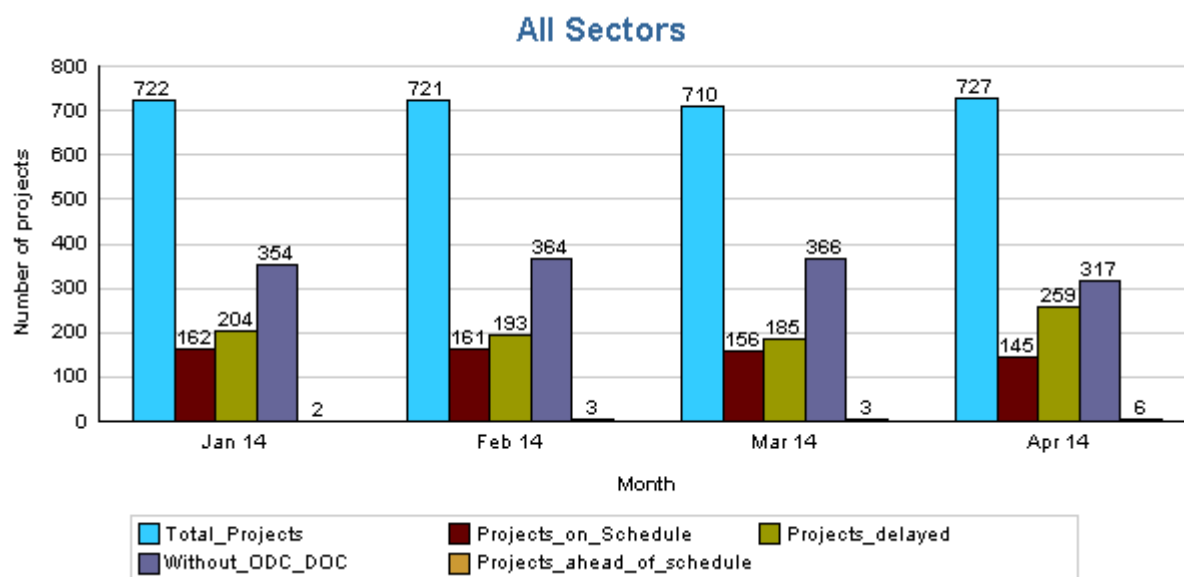


Break-up of 259 Delayed projects in April 2014

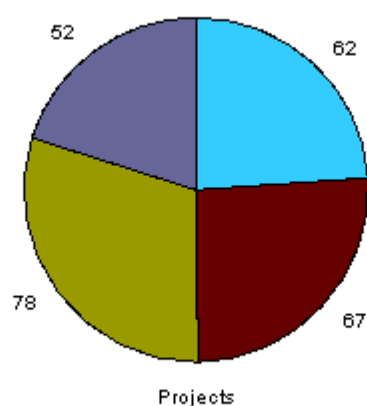


Delay in Months



Graphical Presentation of URBAN DEVELOPMENT Sector

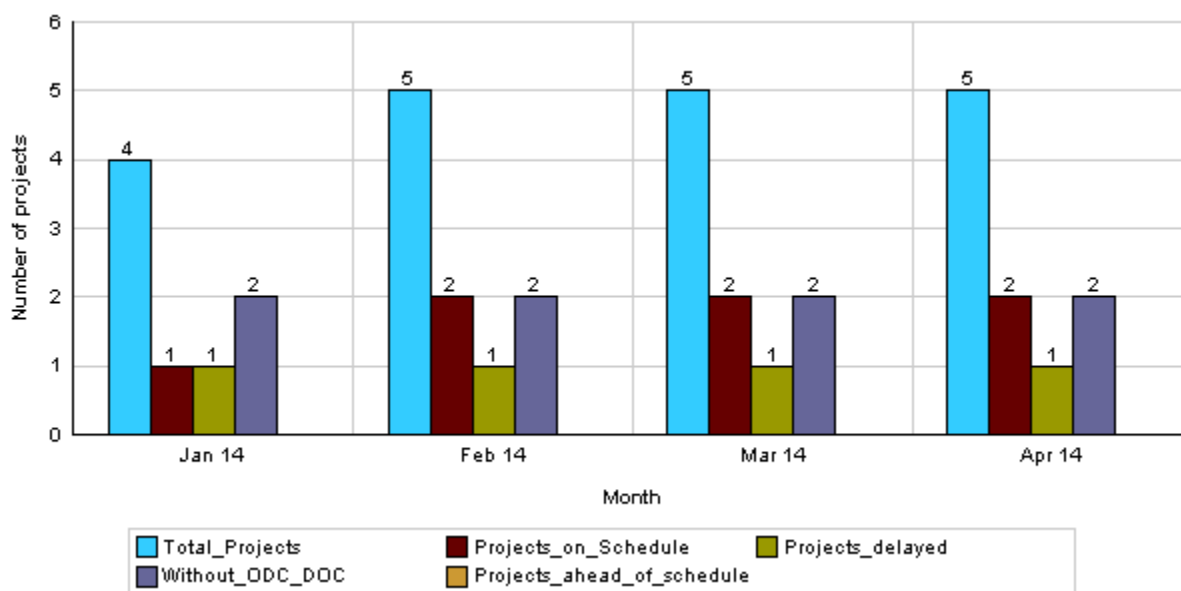


Break-up of 1 Delayed projects in April 2014




Delay in Months

Graphical Presentation of TELECOMMUNICATIONS Sector

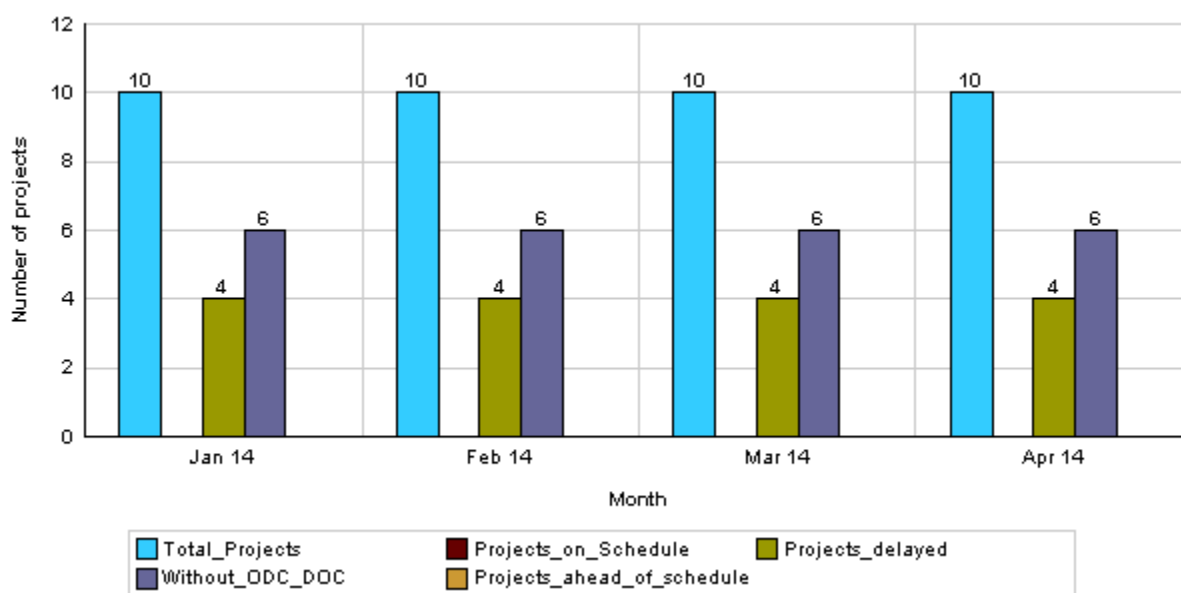


Break-up of 4 Delayed projects in April 2014

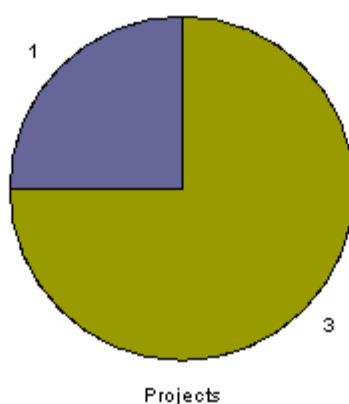


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	3	1

Graphical Presentation of SHIPPING AND PORTS Sector

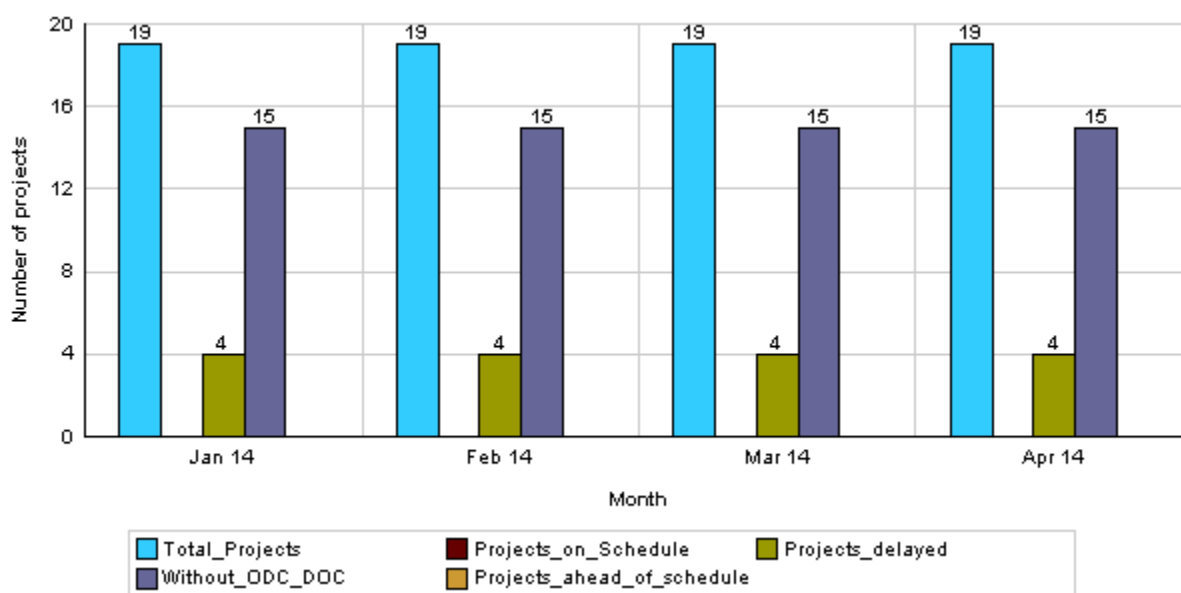


Break-up of 4 Delayed projects in April 2014

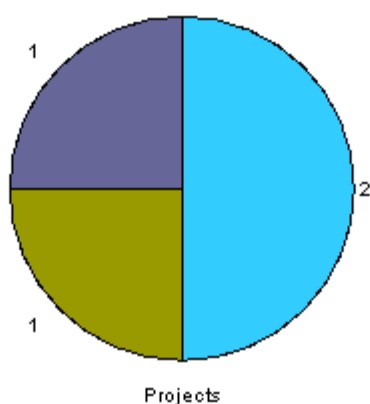


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	2	0	1	1

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

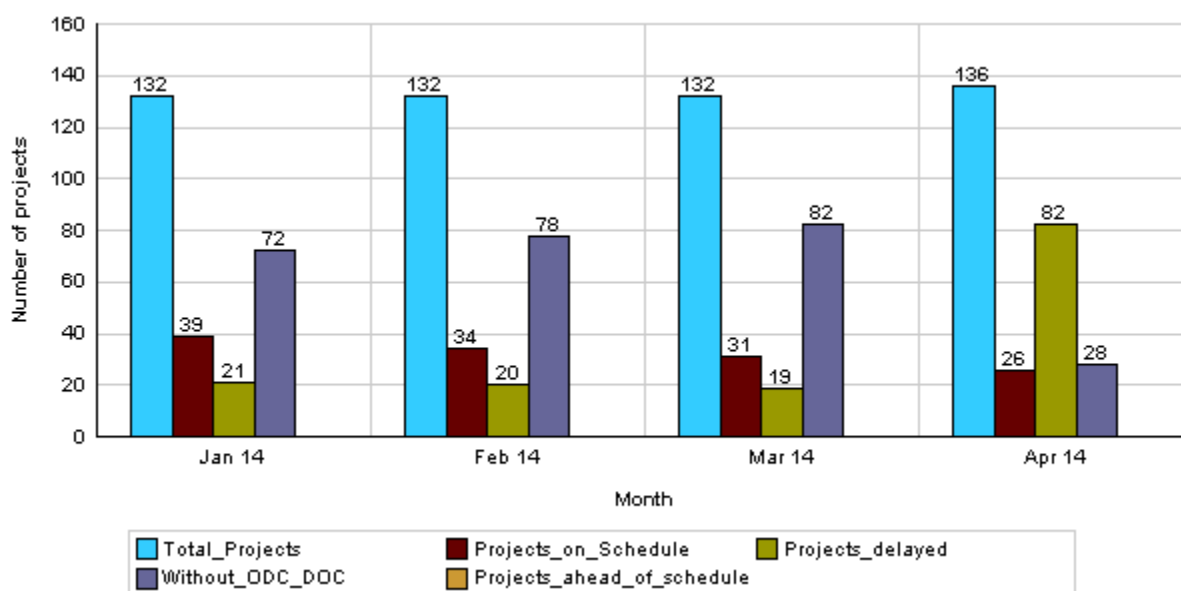


Break-up of 82 Delayed projects in April 2014

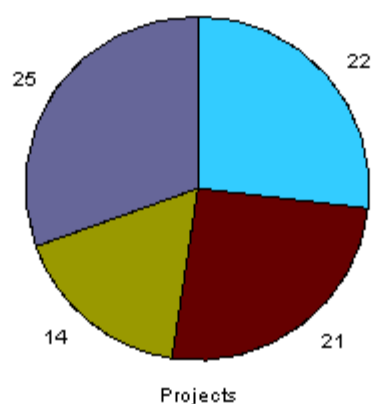


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
-----------------	------	-------	-------	--------------

Graphical Presentation of RAILWAYS Sector

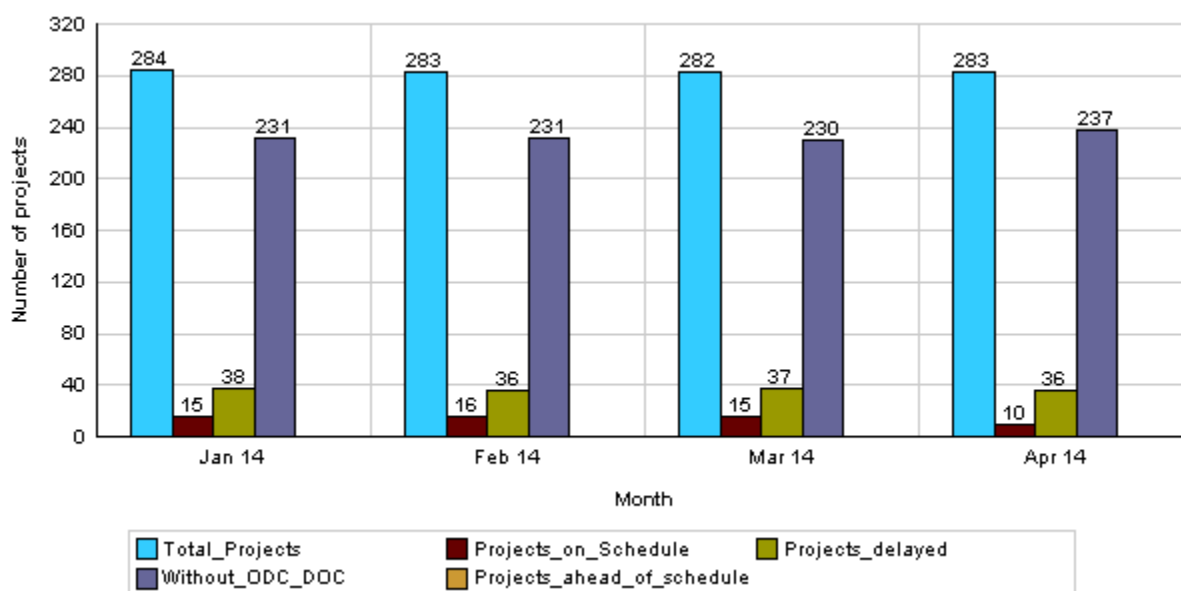


Break-up of 36 Delayed projects in April 2014

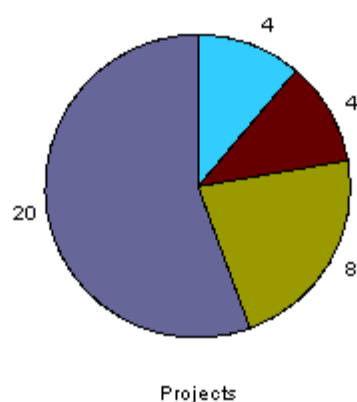


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

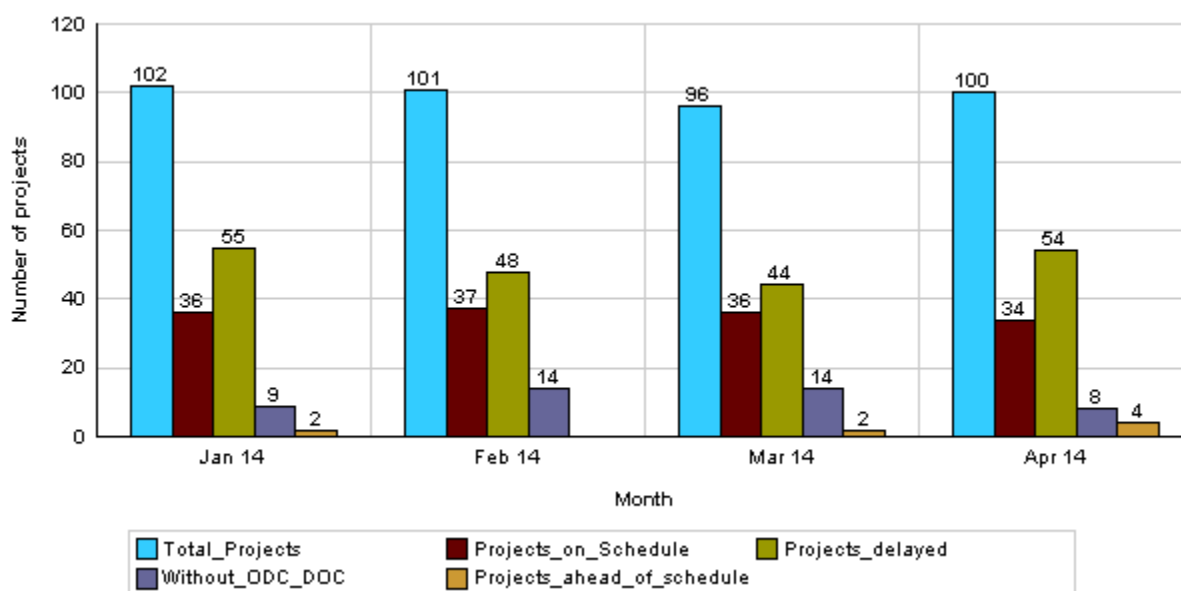


Break-up of 54 Delayed projects in April 2014

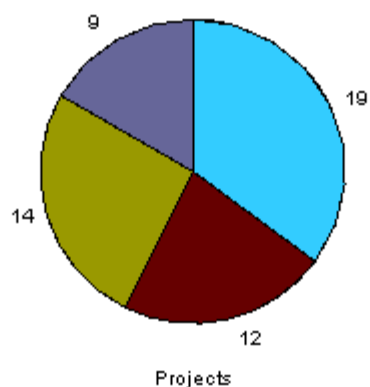


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	19	12	14	9

Graphical Presentation of PETROLEUM Sector

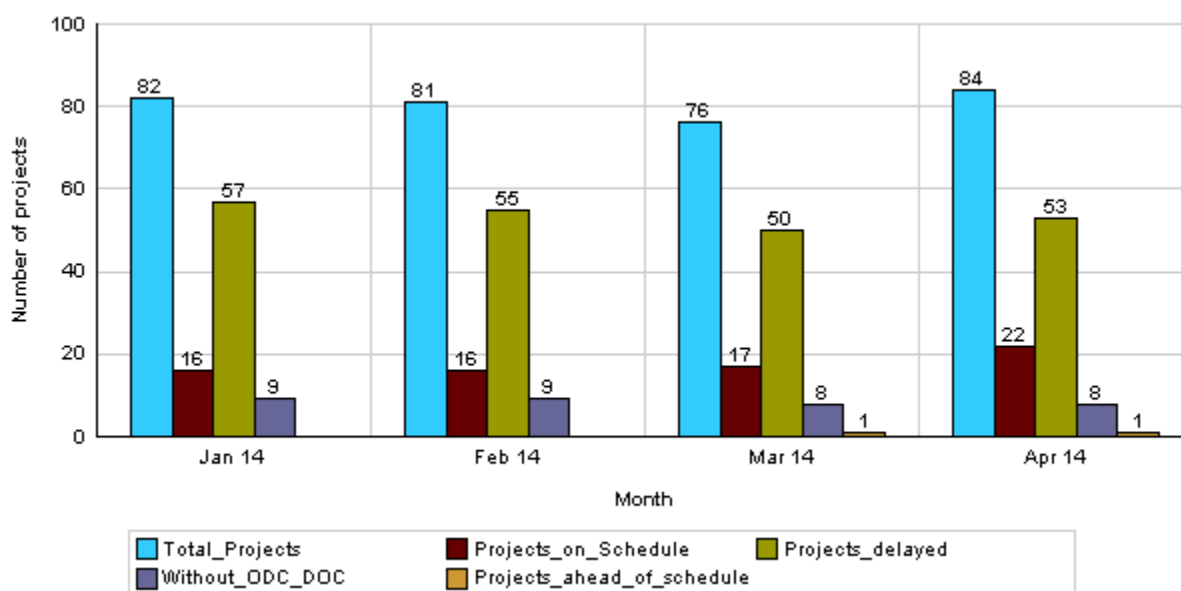


Break-up of 53 Delayed projects in April 2014

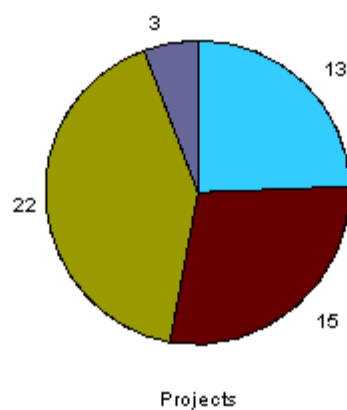


Delay in Months

Legend: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of STEEL Sector

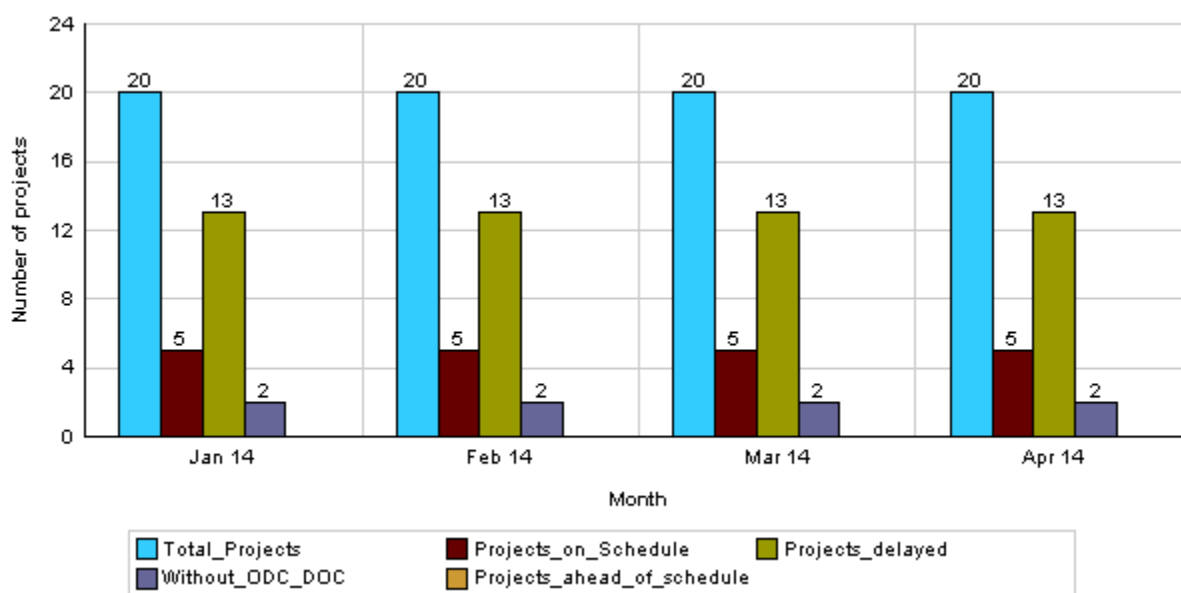


Break-up of 13 Delayed projects in April 2014

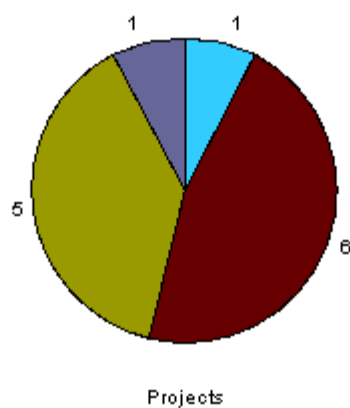


Delay in Months

Delay in Months	Count
1-12	1
13-24	6
25-60	5
MORE THAN 60	1

Graphical Presentation of COAL Sector

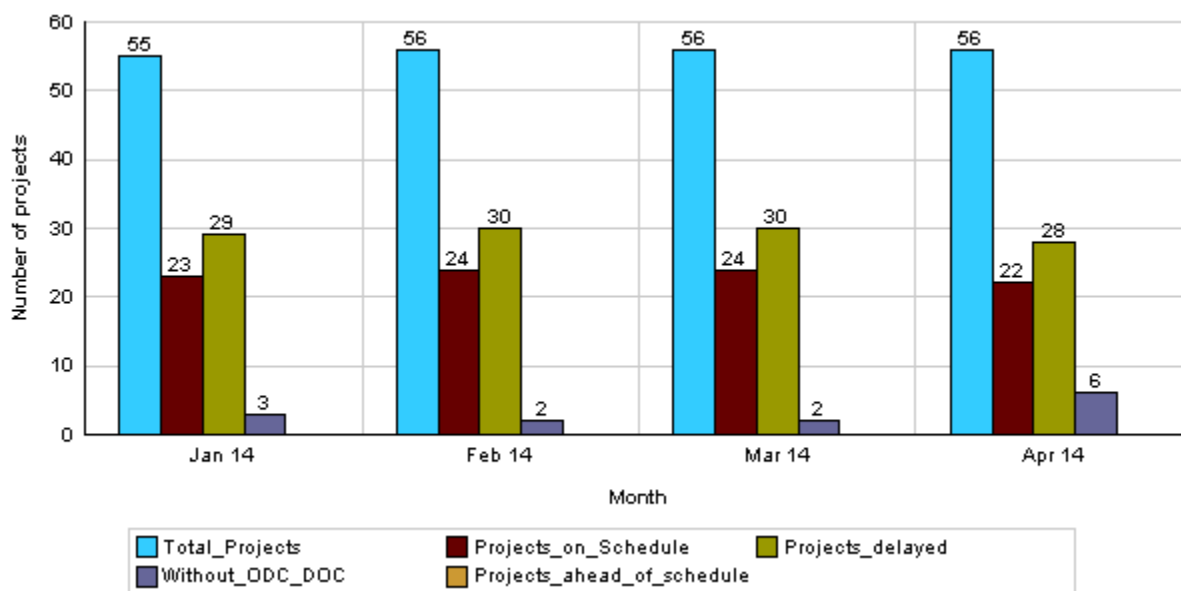


Break-up of 28 Delayed projects in April 2014

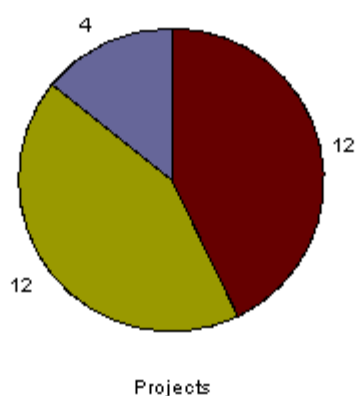


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	12	12	4	0

Graphical Presentation of CIVIL AVIATION Sector

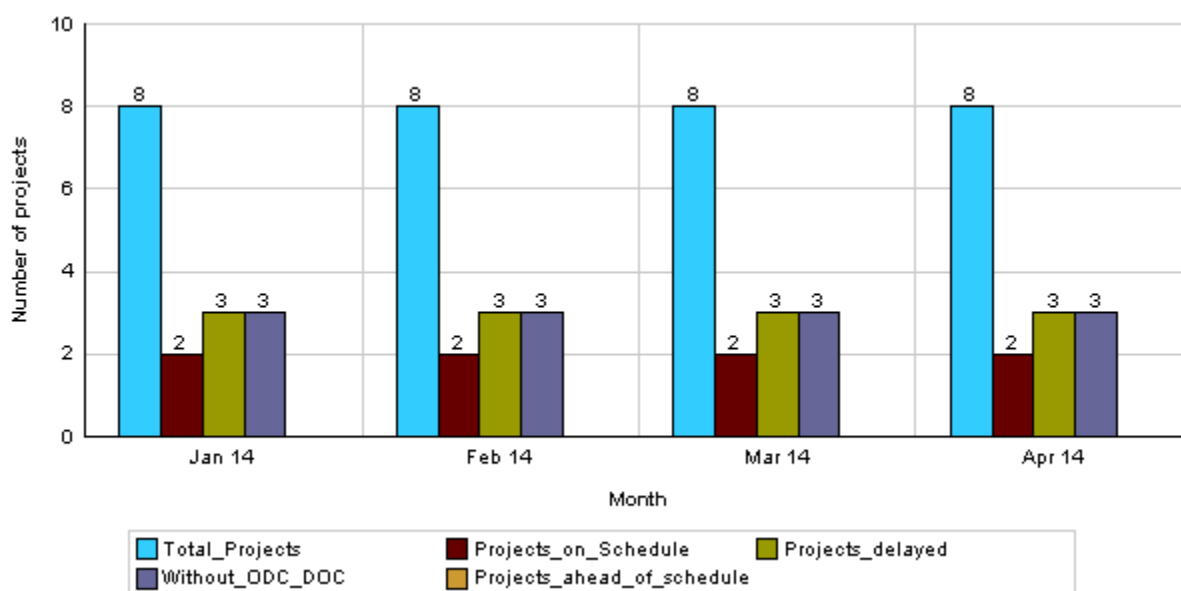


Break-up of 3 Delayed projects in April 2014




Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	0	0	0
13-24	0	1	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	1

Graphical Presentation of ATOMIC ENERGY Sector

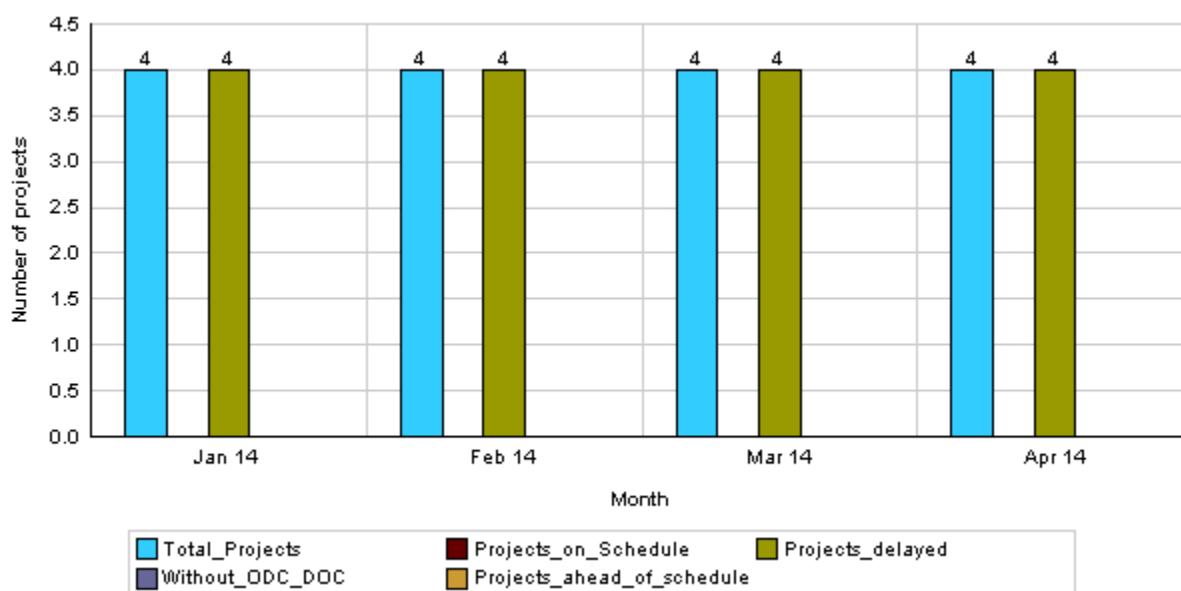

Break-up of 4 Delayed projects in April 2014

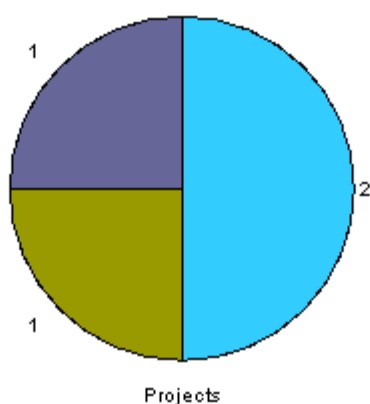

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	2	0	0	0
13-24	0	1	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	1

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	40,442.00	46,726.00	29,610.17
CIVIL AVIATION	8	6,035.46	6,624.95	6,946.00	5,775.55
COAL	56	38,737.38	48,533.93	48,559.52	17,920.92
STEEL	20	65,959.26	70,209.44	72,188.55	59,696.44
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	7,687.66
PETROLEUM	84	195,841.81	208,536.97	208,398.95	107,098.52
POWER	100	246,280.79	252,281.08	267,159.75	143,452.34
RAILWAYS	283	149,809.12	178,792.43	267,704.13	81,684.96
ROAD TRANSPORT AND HIGHWAYS	136	101,597.54	102,135.79	103,690.49	89,840.12
SHIPPING AND PORTS	19	15,617.12	17,487.95	18,600.58	8,395.88
TELECOMMUNICATIONS	10	5,079.29	5,079.29	4,982.94	1,769.33
URBAN DEVELOPMENT	5	73,993.32	74,052.22	79,266.22	11,283.27
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	727	945,396.60	1,010,179.56	1,134,330.13	564,250.65

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(April 2014)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	4,551.00	12/2015 -	11/2016	11(O) -	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,562.00	12/2008 -	03/2015	75(O) -	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,564.17	09/2010 -	03/2015	54(O) -	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	2,933.00	12/2016 -	03/2017	3(O) -	4/69
	Total		40,442.00 -	46,726.00	29,610.17				60/329
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	2,593.13	2,573.92	05/2011 -	03/2013	-	0/2
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	269.55	01/2011 04/2013	12/2016	71(O) 44(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	278.88	05/2012 -	04/2014	23(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,939.21	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	230.42	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	483.53	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,946.00	5,775.55				0/2
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,197.33	03/2013 09/2012	03/2015	24(O) 30(R)	19/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	90.56	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	619.15	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	95.88	03/2020 -	03/2020	0(O) -	0/3

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	126.88	03/2012 -	03/2016	48(O) -	5/6
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	99.00	03/2011 -	03/2014	-	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.41	03/2010 -	03/2016	72(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	55.25	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017	0(O) -	4/12
23	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]NCL,MULTI STATE	11/2006	168.97 -	168.97	43.09	03/2014 -	03/2014	-	0/2
24	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	227.23	03/2015 -	03/2015	0(O) -	0/3
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	610.33	-	03/2022 -	03/2022	0(O) -	0/0
26	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.86	03/2014 -	03/2016	24(O) -	2/8
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60(O) -	0/2
28	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,439.04	03/2014 -	03/2016	24(O) -	6/12
29	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,644.36	03/2014 -	03/2016	24(O) -	10/15
30	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	75.42	03/2015 -	03/2015	0(O) -	1/13
31	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	120.15	03/2013 -	03/2015	24(O) -	3/8
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
33	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2015	0(O) -	4/31
34	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
35	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.52	03/2011 -	03/2017	72(O) -	0/2
36	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	101.83	12/2012 -	03/2016	39(O) -	11/44
37	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	0.27	07/2016 -	07/2016	0(O) -	3/39
38	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	116.72	03/2013 -	03/2015	24(O) -	5/10
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	45.34	03/2014 -	03/2014	-	0/2
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
41	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	25.00	03/2018 -	03/2018	0(O) -	0/4

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
43	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	392.24	03/2013 -	03/2014	-	0/2
44	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	118.59	03/2010 -	03/2017	84(O) -	9/10
45	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	747.82	03/2013 03/2023	03/2023	120(O) 0(R)	0/9
46	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44(O) -	0/3
47	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	214.19	03/2014 -	03/2016	24(O) -	1/6
48	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36(O) -	4/6
49	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
50	MURAIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
51	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	340.71	12/2015 -	04/2018	28(O) -	5/33
52	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
53	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	59.08	03/2012 -	03/2017	60(O) -	0/2
54	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
55	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.43	03/2014 -	03/2016	24(O) -	0/1
56	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	120.97	03/2013 -	03/2015	24(O) -	0/3
57	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	33.46	03/2014 -	03/2016	24(O) -	0/2
58	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	219.03	03/2016 -	03/2016	0(O) -	0/2
59	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	221.35	03/2012 -	03/2015	36(O) -	24/27
60	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
61	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.14 -	430.14	65.51	03/2016 -	03/2016	0(O) -	5/48
62	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	5.43	06/2015 -	06/2015	0(O) -	2/51
63	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	94.45	03/2015 -	03/2015	0(O) -	8/31
64	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	62.01	03/2012 -	-	-	24/42
65	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	50.46	03/2016 -	03/2016	0(O) -	0/12
66	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	139.29	03/2012 -	03/2016	48(O) -	0/2

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,918.33	06/2009 -	06/2014	60(O) -	19/23
68	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,225.89	03/2012 -	08/2014	29(O) -	19/38
	Total		38,737.38 -	48,559.52	17,920.92				212/777
	STEEL								
69	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	379.86	04/2013 09/2014	09/2014	17(O) 0(R)	17/18
70	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	8.73	05/2016 -	05/2016	0(O) -	0/3
71	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	349.64	259.71	12/2009 08/2010	06/2013	-	1/1
72	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	343.58	292.89	01/2010 02/2011	11/2013	-	3/3
73	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	292.64	05/2013 01/2015	01/2015	20(O) 0(R)	13/20
74	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	309.45	09/2009 05/2012	07/2014	58(O) 26(R)	1/1
75	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	370.58	12/2011 01/2015	01/2015	37(O) 0(R)	15/20
76	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	06/2014	69(O) 6(R)	3/4
77	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	103.67	08/2014 -	08/2014	0(O) -	1/4
78	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	104.16	11/2013 -	06/2015	19(O) -	1/4
79	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,638.44	03/2013 -	03/2015	24(O) -	28/35
80	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,634.39	12/2011 -	05/2014	29(O) -	18/24
81	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,156.60	12/2012 -	12/2014	24(O) -	14/20
82	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,862.37	12/2011 -	07/2014	31(O) -	22/29
83	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,804.62	10/2009 10/2012	09/2014	59(O) 23(R)	66/67
84	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,055.89	03/2013 -	09/2014	18(O) -	16/20
85	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	124.72	10/2013 -	08/2014	10(O) -	0/5
86	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014	0(O) -	0/2
87	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	339.35	83.98	06/2015 -	06/2015	0(O) -	1/3

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	254.90	34.15	12/2014 -	12/2014	0(O) -	0/2
	Total		65,959.26 -	72,188.55	59,696.44				220/285
	<u>PETROCHEMICALS</u>								
89	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	8,920.00	7,687.66	04/2012 -	-	-	22/29
	Total		5,460.61 -	8,920.00	7,687.66				22/29
	<u>PETROLEUM</u>								
90	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	113.00	06/2012 -	07/2014	25(O) -	0/4
91	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	06/2014	24(O) -	0/0
92	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/0
93	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24(O) -	0/0
94	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24(O) -	0/0
95	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24(O) 12(R)	0/5
96	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	165.89	08/2015 -	08/2015	0(O) -	0/13
97	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	338.27	07/2012 07/2012	-	-	6/7
98	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	154.08	06/2012 -	06/2014	24(O) -	0/0
99	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	449.94	09/2011 -	12/2014	39(O) -	0/0
100	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	165.71	08/2013 -	09/2014	13(O) -	0/5
101	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	102.80	09/2012 -	12/2014	27(O) -	0/0
102	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12(O) -	0/5
103	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	11.56	07/2014 -	03/2015	8(O) -	0/5
104	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
105	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	102.78	09/2012 -	12/2014	27(O) -	0/5
106	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12(O) -	0/5
107	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	561.31	05/2013 06/2014	06/2014	13(O) 0(R)	0/5

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
108	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54(O) -	0/0
109	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	93.04	09/2013 -	02/2015	17(O) -	0/1
110	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	824.82	- -	08/2015	- -	0/12
111	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,728.25	04/2006 06/2012	06/2016	122(O) 48(R)	0/0
112	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,847.61	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
113	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
114	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,165.53	07/2010 05/2012	05/2014	46(O) 24(R)	0/0
115	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	247.67	05/2014 -	05/2015	12(O) -	0/9
116	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	3,068.29	12/2008 04/2013	09/2014	69(O) 17(R)	0/0
117	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
118	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
119	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	248.39	12/2014 -	12/2014	0(O) -	0/8
120	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	992.74	01/2014 -	12/2015	23(O) -	0/9
121	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2014	0(O) -	0/0
122	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,881.89	09/2011 05/2012	12/2014	39(O) 31(R)	6/76
123	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	34(O) 28(R)	56/59
124	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	42.23	09/2017 -	09/2017	0(O) -	0/0
125	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	2.61	- -	-	-	0/0
126	FIRE WATER NETWORK AT URAN - [N16000141]ONGC,MAHARASHTRA	05/2010	171.68 -	171.68	96.43	06/2013 -	05/2014	11(O) -	0/5
127	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	06/2014	32(O) -	0/9
128	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	2,435.26	05/2015 -	05/2015	0(O) -	0/17
129	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	0.05	07/2016 -	07/2016	0(O) -	0/0
130	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	593.64	03/2015 -	03/2015	0(O) -	0/12

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
131	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
132	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016	0(O) -	0/0
133	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	2,067.10	12/2015 -	05/2016	5(O) -	0/0
134	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	86.03	03/2014 -	03/2015	12(O) -	0/5
135	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0
136	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
137	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	312.00	286.76	01/2012 -	07/2013	-	0/1
138	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,391.24	12/2012 -	-	-	0/10
139	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.26	142.66	03/2015 -	03/2015	0(O) -	0/64
140	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015	-1(O) -	0/0
141	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	202.33	11/2015 -	11/2015	0(O) -	18/29
142	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	135.79	06/2014 -	09/2014	3(O) -	0/0
143	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23(O) -	0/0
144	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	69.71	12/2014 -	12/2014	0(O) -	0/0
145	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 -	12,160.26	11,362.40	01/2012 -	06/2014	29(O) -	0/108
146	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,719.76	09/2012 -	04/2014	19(O) -	0/0
147	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,920.81	05/2010 03/2013	04/2014	47(O) 13(R)	0/0
148	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
149	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	120.36	07/2015 -	12/2015	5(O) -	0/0
150	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	25,442.00	11/2012 -	12/2014	25(O) -	72/100
151	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	969.70	09/2012 -	08/2015	35(O) -	6/7
152	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,521.61	02/2014 -	06/2014	4(O) -	0/0
153	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	262.43	04/2012 -	06/2014	26(O) -	0/0
154	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	33.26	07/2016 -	07/2016	0(O) -	0/5

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
155	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,101.52	05/2014 -	05/2014	0(O) -	0/5
156	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
157	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	946.17	07/2012 -	06/2014	23(O) -	0/31
158	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	10/2015	10(O) -	0/0
159	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	686.58	63.96	04/2015 -	04/2015	0(O) -	0/0
160	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	468.42	12/2014 -	03/2015	3(O) -	0/0
161	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	-	02/2016 -	02/2016	0(O) -	0/0
162	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,910.30	-	05/2016 -	05/2016	0(O) -	0/0
163	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	523.84	11/2015 -	11/2015	0(O) -	12/25
164	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	957.10	648.92	04/2012 -	12/2013	-	0/0
165	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	829.83	10/2011 -	06/2015	44(O) -	0/0
166	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,178.42	01/2012 -	06/2015	41(O) -	0/0
167	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	951.32	10/2011 -	09/2014	35(O) -	0/0
168	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	-	04/2015	-	0/0
169	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22(O) -	0/5
170	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	871.35	12.13	03/2015 -	03/2015	0(O) -	0/5
171	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.83	10/2014 -	10/2015	12(O) -	0/0
172	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.42	03/2012 -	03/2015	36(O) -	13/20
173	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	519.57	12/2013 -	09/2015	21(O) -	0/0
	Total		195,841.81 -	208,398.95	107,098.52				189/716
	POWER								
174	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,322.56	08/2012 -	06/2014	22(O) -	0/11
175	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	173.77	-	-	-	0/17

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
176	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	03/2016	0(O) -	0/0
177	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	37.56	10/2014 -	10/2014	0(O) -	0/7
178	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,472.00	08/2013 -	03/2015	19(O) -	15/19
179	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,959.00	12/2009 -	03/2017	87(O) -	24/49
180	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 -	4,375.35	4,481.00	07/2011 -	08/2016	61(O) -	6/28
181	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	29.65	12/2015 -	12/2015	0(O) -	2/20
182	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,282.36	09/2014 -	12/2014	3(O) -	7/20
183	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	400.43	06/2015 -	06/2015	0(O) -	0/0
184	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,381.55	08/2014 -	08/2014	0(O) -	7/20
185	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.17	06/2014 -	06/2014	0(O) -	0/20
186	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
187	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	13.93	10/2014 -	10/2014	0(O) -	2/2
188	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	826.23	11/2012 -	06/2015	31(O) -	2/13
189	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	13.34	05/2016 -	04/2016	-1(O) -	0/0
190	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
191	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
192	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,412.45	05/2014 -	09/2014	4(O) -	2/8
193	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,118.00	09/2017 -	09/2017	0(O) -	7/38
194	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	609.80	08/2014 -	08/2014	0(O) -	1/16
195	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
196	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL, CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,359.35	12/2013 -	11/2014	11(O) -	2/7
197	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL, MAHARASHTRA	10/2013	1,315.90 -	1,315.90	40.47	11/2016 -	03/2016	-8(O) -	0/0
198	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, KARNATAKA	03/2005	596.45 -	1,007.16	941.31	12/2007 12/2009	-	-	2/11
199	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,816.40	12/2009 06/2016	03/2017	87(O) 9(R)	11/26
200	KISHANGANGA HEP - [N18000031]NHPC, JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	5,497.72	3,331.00	01/2016 -	11/2016	10(O) -	0/6
201	KOLDAM HEP (NTPC) - [180100211]NTPC, HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	5,886.00	04/2009 -	05/2015	73(O) -	2/9
202	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	12/2011	15,166.19 -	15,166.19	3,814.00	12/2016 -	12/2016	0(O) -	12/20
203	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,877.15	09/2008 -	03/2013	-	15/23
204	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,580.00	05/2017 -	05/2017	0(O) -	8/37
205	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00 -	1,527.00	71.00	08/2017 -	08/2017	0(O) -	0/8
206	MOUDA STPP - [N18000048]NTPC, MAHARASHTRA	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
207	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47 -	7,921.47	2,392.00	09/2016 -	09/2016	0(O) -	17/20
208	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, MULTI STATE	02/2009	11,130.19 -	11,130.19	8,056.80	08/2013 -	06/2015	22(O) -	0/17
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL, MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	0/0
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 -	752.64	379.82	07/2013 -	03/2015	20(O) -	2/11
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, MULTI STATE	02/2009	410.29 -	410.29	282.27	02/2012 -	12/2013	-	1/13
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, MULTI STATE	02/2009	509.66 -	509.66	399.76	11/2011 -	-	-	2/14
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL, MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	0/0
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL, MULTI STATE	08/2010	1,677.57 -	1,677.57	1,029.02	04/2013 -	12/2014	20(O) -	0/11
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL, MULTI STATE	11/2011	723.63 -	723.63	315.22	11/2014 -	11/2014	0(O) -	2/12
216	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL, MULTI STATE	09/2013	680.69 -	680.69	33.49	03/2016 -	03/2016	0(O) -	0/0
217	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL, MULTI STATE	09/2012	803.34 -	803.34	222.89	03/2015 -	03/2015	0(O) -	4/15
218	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL, MULTI STATE	09/2012	524.40 -	524.40	79.92	04/2015 -	05/2015	1(O) -	0/16

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
219	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, MULTI STATE	03/2010	965.58 -	965.58	657.74	11/2012 -	05/2014	18(O) -	0/11
220	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,349.46	10/2010 -	08/2014	46(O) -	1/2
221	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,439.96	09/2009 -	07/2018	106(O) -	1/12
222	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 -	1,128.38	811.78	08/2013 09/2015	09/2015	25(O) 0(R)	17/26
223	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	3,115.91	01/2012 -	09/2014	32(O) -	19/28
224	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	6,230.81	4,357.00	10/2012 -	10/2013	-	16/16
225	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	2,443.00	11/2016 -	11/2016	0(O) -	12/13
226	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	09/2016 -	09/2016	0(O) -	0/0
227	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	0/0
228	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,839.53	09/2010 -	09/2018	96(O) -	0/0
229	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL, MULTI STATE	08/2008	2,360.95 -	2,580.90	2,117.11	08/2012 -	09/2014	25(O) -	1/5
230	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	291.18	06/2016 -	12/2015	-6(O) -	0/20
231	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL, MULTI STATE	02/2010	232.34 -	232.34	176.79	06/2012 -	06/2014	24(O) -	0/3
232	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	632.68	12/2014 -	11/2014	-1(O) -	2/2
233	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	117.44	03/2014 -	06/2014	3(O) -	3/7
234	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	337.63	08/2014 -	05/2015	9(O) -	2/19
235	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	985.29	08/2012 -	12/2014	28(O) -	0/11
236	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL, MULTI STATE	02/2014	243.53 -	243.53	-	08/2014 -	08/2016	24(O) -	0/0
237	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	741.43	02/2015 -	02/2015	0(O) -	1/14
238	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	624.48	11/2014 -	11/2014	0(O) -	0/16
239	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	655.12	01/2015 -	01/2015	0(O) -	4/19
240	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	218.57	08/2014 -	08/2014	0(O) -	7/20

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
241	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	282.42	06/2014 -	09/2014	3(O) -	8/20
242	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,091.00	03/2013 -	03/2017	48(O) -	0/13
243	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,491.81	09/2009 -	09/2015	72(O) -	1/5
244	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	700.96	07/2010 02/2016	02/2017	79(O) 12(R)	1/10
245	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	148.12	01/2014 -	09/2014	8(O) -	3/15
246	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	963.76	08/2014 -	06/2015	10(O) -	2/19
247	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,470.41	10/2014 -	06/2015	8(O) -	3/18
248	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,868.48	10/2012 -	03/2015	29(O) -	0/11
249	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	31(O) -	0/4
250	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,696.00	12/2012 -	06/2015	30(O) -	0/11
251	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	470.75	01/2015 -	12/2015	11(O) -	2/20
252	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMP-PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	324.33	176.06	08/2014 -	08/2014	0(O) -	9/20
253	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,026.27	10/2014 -	10/2014	0(O) -	3/16
254	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	0/0
255	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	402.60	02/2014 -	06/2014	4(O) -	5/17
256	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	374.82	10/2013 -	06/2014	8(O) -	1/8
257	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	987.66	12/2013 -	06/2014	6(O) -	4/13
258	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	245.81	11/2013 -	03/2015	16(O) -	7/20
259	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,507.24	03/2013 -	09/2014	18(O) -	5/15
260	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,391.47	03/2014 -	12/2014	9(O) -	5/15

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
261	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL, ODISHA	12/2010	2,743.19 -	2,743.19	2,086.80	12/2013 -	12/2014	12(O) -	2/8
262	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL, MULTI STATE	05/2010	250.03 -	250.03	68.10	01/2013 -	06/2015	29(O) -	5/18
263	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL, MULTI STATE	03/2011	1,585.12 -	1,585.12	1,206.46	11/2013 -	06/2015	19(O) -	5/16
264	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL, MULTI STATE	03/2010	4,672.99 -	4,672.99	3,065.97	11/2012 -	03/2015	28(O) -	0/15
265	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL, CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,798.33	07/2014 -	12/2014	5(O) -	3/14
266	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, TRIPURA	07/2009	421.01 623.44	951.48	745.55	07/2013 -	11/2014	16(O) -	18/25
267	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	01/2011	913.63 -	913.63	573.22	07/2006 12/2015	12/2015	113(O) 0(R)	2/14
268	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL, MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
269	VINDHYACHAL STTP STAGE-V - [N18000134]NTPC, MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	980.00	08/2015 -	08/2015	0(O) -	16/16
270	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC, MADHYA PRADESH	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
271	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, UTTARAKHAND	08/2008	2,491.58 -	3,745.08	483.40	07/2014 -	07/2018	48(O) -	1/1
272	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, MAHARASHTRA	12/2007	477.69 -	477.69	483.79	09/2010 -	06/2014	45(O) -	0/5
273	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,649.59	06/2015 -	12/2015	6(O) -	3/28
	Total		246,280.79 -	267,159.75	143,452.34				386/1269
	RAILWAYS								
274	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	17.40	04/2012 -	03/2016	47(O) -	0/0
275	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	182.06 -	184.06	2.55	- -	-	-	0/0
276	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	1,741.00	562.77	03/2014 -	03/2017	36(O) -	0/0
277	AGARTALA-AKHAURA NL - [N22000195]NEFR, TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
278	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 427.21	432.72	400.84	12/2009 03/2011	12/2014	60(O) 45(R)	0/0
279	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	567.18	2.00	- -	-	-	0/0
280	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	385.60	56.73	03/2013 -	03/2013	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
281	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 -	2,820.00	309.40	- -	-	-	0/0
282	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	19.66	- -	-	-	0/0
283	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
284	AKKANAPET-MEDAK - [N22000285](SCR),TELANGANA	04/2012	153.00 -	153.00	-	- -	-	-	0/0
285	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
286	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	485.00	417.14	03/2011 03/2011	03/2011	-	0/0
287	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
288	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	106.15	- -	-	-	0/0
289	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	82.48	- -	03/2016	-	0/0
290	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	725.00	573.28	06/1999 03/2011	03/2011	-	0/0
291	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.74	- -	-	-	0/0
292	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
293	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
294	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
295	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
296	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.95	- -	-	-	0/0
297	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	199.75	47.41	- -	-	-	0/0
298	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	38.46	- -	-	-	0/0
299	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	7.47	- -	-	-	0/0
300	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	198.85	12/2012 -	12/2014	24(O) -	0/0
301	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	1,382.78	1.58	- -	-	-	0/0
302	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	1.76	- -	-	-	0/0
303	BANKURA - DAMODAR (GC) (SER) - [220100277]SR,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	479.18	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
304	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	245.15 1,106.62	1,106.62	234.88	12/2010 03/2011	03/2011	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
305	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	11.40	- -	-	-	0/0
306	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
307	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.48	369.66	03/2004 12/2010	12/2014	129(O) 48(R)	0/0
308	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),TELANGANA	04/2010	337.49 -	337.50	0.21	- -	-	-	0/0
309	BHADRACHALAM-KOVVUR - [N22000264](SCR),MULTI STATE	04/2012	923.23 -	923.23	-	- -	-	-	0/0
310	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
311	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	171.82	04/2014 -	03/2017	35(O) -	0/0
312	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.79	- -	-	-	0/0
313	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.14	03/2011 -	-	-	0/0
314	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	79.75	- -	-	-	0/0
315	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	795.45	03/2010 -	12/2015	69(O) -	0/0
316	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	484.61	2.07	03/2012 -	-	-	0/0
317	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
318	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.26	- -	-	-	0/0
319	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	267.37	34.01	- -	-	-	0/0
320	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	3,118.65	04/2008 03/2014	12/2017	116(O) 45(R)	0/0
321	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
322	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	57.10	03/2015 -	12/2015	9(O) -	0/0
323	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.17	- -	-	-	0/0
324	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	60.02	- -	-	-	0/0
325	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	556.85	- -	12/2014	- -	0/0
326	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
327	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	461.35	- -	-	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
328	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.03	- -	-	-	0/0
329	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	494.92	0.10	- -	-	-	0/0
330	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	106.98	- -	-	-	0/0
331	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
332	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
333	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.11	- -	-	-	0/0
334	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	0.10	- -	-	-	0/0
335	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	0.10	- -	-	-	0/0
336	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]JER,MULTI STATE	04/2005	595.91 -	595.91	88.26	- -	-	-	0/0
337	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	147.45	- -	-	-	0/0
338	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
339	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	407.98	413.00	- -	03/2014	-	0/0
340	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	959.41	03/2007 -	03/2017	120(O) -	0/0
341	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	267.12	- -	-	-	0/0
342	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
343	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	161.27	- -	-	-	0/0
344	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]JER, WEST BENGAL	04/2009	259.51 533.38	533.38	109.97	12/2011 02/2012	02/2012	-	0/0
345	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	138.39	12/2012 -	-	-	0/0
346	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	388.67	77.88	12/2015 -	03/2016	3(O) -	0/0
347	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	406.92	147.27	- -	-	-	0/0
348	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]JER,MULTI STATE	04/2010	296.44 -	296.44	3.90	- -	-	-	0/0
349	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	205.00	4.94	- -	-	-	0/0
350	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	244.77	- -	03/2014	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
351	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
352	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	143.34	- -	-	-	0/0
353	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	607.09	544.25	12/2012 12/2012	02/2013	-	0/0
354	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	2.00	- -	-	-	0/0
355	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	2.32	02/2019 -	02/2019	0(O) -	0/0
356	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	651.17	7.14	- -	-	-	0/0
357	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
358	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	914.98	757.65	- -	12/2012	-	0/0
359	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	100.00	03/2016 -	03/2016	0(O) -	0/0
360	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31(O) 10(R)	0/0
361	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
362	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
363	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	226.04	12/2008 -	09/2014	69(O) -	0/0
364	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	267.13	06/2013 06/2013	03/2015	21(O) 21(R)	0/0
365	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0
366	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240(O) -	0/0
367	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	0.10	- -	-	-	0/0
368	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	293.94	02/2011 02/2011	03/2013	-	0/0
369	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.88	- -	-	-	0/0
370	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
371	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	611.03	137.32	12/2011 11/2013	11/2013	-	0/0
372	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 -	261.70	79.25	02/2006 -	-	-	0/0
373	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	863.23	783.44	- -	03/2012	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
374	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
375	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	156.65	51.27	- -	-	-	0/0
376	GUDUR-DURGARAJAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0
377	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	442.83	- 05/2009	05/2009	-	0/0
378	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	585.09	03/1994 -	06/2014	243(O) -	0/0
379	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	9.14	- -	-	-	0/0
380	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
381	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
382	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	213.01	-	- -	-	-	0/0
383	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	324.66	196.47	- -	-	-	0/0
384	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.51	- -	-	-	0/0
385	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.77	- -	-	-	0/0
386	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	295.52	- 09/2009	-	-	0/0
387	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	0.33	- -	-	-	0/0
388	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
389	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	877.71	- -	01/2013	-	0/0
390	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	230.03	152.30	- -	03/2014	-	0/0
391	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	56.08	03/2015 -	03/2015	0(O) -	0/0
392	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
393	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	46.57	- -	-	-	0/0
394	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	41.67	- -	-	-	0/0
395	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	445.40	179.99	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
396	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
397	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	110.11	- -	-	-	0/0
398	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	185.24	01/1999 -	-	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
399	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.47	279.41	03/2014 -	03/2014	-	0/0
400	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	141.38	- -	-	-	0/0
401	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	838.15	06/2007 -	06/2007	-	0/0
402	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	1,043.56	732.94	03/2012 08/2012	-	-	0/0
403	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	14.00	- -	-	-	0/0
404	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	740.00	553.18	03/2012 03/2012	12/2012	-	0/0
405	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	2,152.99	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
406	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	2,050.00	87.88	- -	12/2014	- -	0/0
407	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	205.06	- -	-	-	0/0
408	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	53.51	- -	-	-	0/0
409	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	3.71	- -	-	-	0/0
410	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	1,708.41	1,561.91	- -	03/2015	- -	0/0
411	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
412	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	744.71	520.11	- -	03/2014	-	1/1
413	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	800.00	775.36	- -	10/2012	-	0/0
414	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	137.78	12/2012 -	03/2016	39(O) -	0/0
415	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	725.54	445.74	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
416	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	163.67	03/2017 -	03/2017	0(O) -	0/0
417	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	1,054.35	0.42	- -	-	-	0/0
418	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	162.87	126.82	- -	-	-	0/0
419	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	279.04	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
420	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	1,995.25	301.86	- -	12/2014	- -	0/0
421	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	359.86	2.22	- -	03/2015	- -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
422	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	768.87	540.50	- 03/2010	03/2010	-	0/0
423	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	2,957.21	1,786.63	07/2005 -	-	-	0/0
424	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	418.17	219.56	- -	-	-	0/0
425	KONDAPALLI-PENUBALLI - [N22000260](SCR),MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
426	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	341.41	295.38	03/2012 03/2013	03/2013	-	0/0
427	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	1,045.20	0.03	- -	-	-	0/0
428	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
429	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
430	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
431	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	140.49	- -	-	-	0/0
432	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	1,630.97	430.45	05/2008 03/2011	-	-	0/0
433	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	68.98	03/2014 -	03/2014	-	0/0
434	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	246.06	0.11	- -	-	-	0/0
435	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,114.91	4,142.69	03/2009 -	03/2017	96(O) -	0/0
436	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,MULTI STATE	07/1998	125.00 -	480.00	0.92	07/2008 -	07/2008	-	0/0
437	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	12.72	- -	-	-	0/0
438	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.52	- -	-	-	0/0
439	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	119.13	- -	-	-	0/0
440	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	472.00	191.82	- -	02/2013	-	0/0
441	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	900.05	815.65	12/2011 12/2011	03/2013	-	0/0
442	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,MULTI STATE	04/2006	378.56 671.82	791.59	0.99	- -	-	-	0/0
443	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.18	- -	03/2016	-	0/0
444	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	95.66	- -	-	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
445	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N2200002]ECR,BIHAR	04/1996	114.01 332.92	477.88	452.87	03/2012 03/2013	03/2013	-	0/0
446	MANUGURU-RAMAGUNDAM - [N22000259](SCR),TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
447	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	0.07	01/1999 -	-	-	0/0
448	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	965.16	557.96	- -	-	-	0/0
449	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	1,383.45	407.20	- -	-	-	0/0
450	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	0.50	- -	-	-	0/0
451	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
452	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
453	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
454	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	-	- -	-	-	0/0
455	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
456	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	390.60	2.11	- -	-	-	0/0
457	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,739.04	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
458	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	645.00	280.90	- -	03/2014	-	0/0
459	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	257.78	- -	-	-	0/0
460	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.46	- -	-	-	0/0
461	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
462	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	-	- -	-	-	0/0
463	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	169.82	24.33	- -	-	-	0/0
464	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	0.89	- -	-	-	0/0
465	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	883.00	679.78	02/2009 -	03/2012	-	0/0
466	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	1,036.78	384.20	07/2012 -	-	-	0/0
467	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	0.50	- -	-	-	0/0
468	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
469	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	532.87	44.11	- -	-	-	0/0
470	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	430.33	186.08	- -	03/2018	- -	0/0
471	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	39.68	- -	-	-	0/0
472	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	3.69	- -	-	-	0/0
473	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	227.81	- -	03/2014	-	0/0
474	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	03/2016	- -	0/0
475	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	22.39	- -	-	-	0/0
476	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.18	253.51	- -	03/2015	- -	0/0
477	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
478	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	40.39	- -	03/2017	- -	0/0
479	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	283.55	2.90	- -	03/2017	- -	0/0
480	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	1,327.78	949.35	- -	-	-	0/0
481	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24(O) -	0/0
482	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,575.90	12/2008 -	03/2017	99(O) -	0/0
483	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,298.42	64.64	03/2014 -	03/2014	-	0/0
484	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	2,913.51	441.08	03/2016 -	03/2016	0(O) -	0/0
485	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	84.44	03/2016 -	06/2016	3(O) -	0/0
486	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	3,951.98	417.81	03/2016 -	03/2016	0(O) -	0/0
487	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	1,117.11	425.14	03/2008 06/2008	-	-	0/0
488	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
489	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	293.74	139.12	12/2010 12/2010	12/2010	-	0/0
490	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	191.00 -	260.16	221.12	- -	05/2014	-	0/0
491	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 2,921.00	2,921.00	2,075.62	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
492	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 495.68	925.30	663.66	- -	02/2014	-	0/0
493	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	203.00 -	203.00	192.63	- -	03/2014	-	0/0
494	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	15.44	- -	-	-	0/0
495	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
496	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	14.68	03/2015 -	03/2015	0(O) -	0/0
497	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
498	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0
499	QADIAN-BEAS - [N22000295]NR, PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
500	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
501	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	838.28	- -	03/2013	-	0/6
502	RAICHUR-GUNTAKAL (DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	279.63	12/2007 03/2010	-	-	0/0
503	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 2,363.00	2,363.00	1,343.55	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
504	RAJATGARH-BARANG (LD), ECOR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	307.18	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
505	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	913.48	462.18	- -	-	-	0/0
506	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR, KARNATAKA	04/2007	482.00 -	874.57	565.36	03/2013 -	03/2014	-	0/0
507	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	727.13 727.13	1,225.90	238.69	- -	-	-	0/0
508	RANCHI-LOHARDAGA (GC), SER - [220100214]SER, JHARKHAND	04/1997	194.07 194.07	596.40	372.92	06/2004 -	03/2015	129(O) -	0/0
509	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR, MULTI STATE	01/2004	915.70 915.70	3,019.17	2,754.53	- -	03/2015	-	0/0
510	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR, RAJASTHAN	04/2012	288.97 -	288.97	0.12	- -	-	-	0/0
511	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR, RAJASTHAN	04/2010	739.65 -	872.22	788.17	- -	-	-	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
512	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	22.23	- -	-	-	0/0
513	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	327.41	03/2012 -	-	-	0/0
514	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	970.34	268.24	- -	-	-	0/0
515	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	2.56	- -	-	-	0/0
516	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	28.86	- 12/2017	12/2017	- 0(R)	0/0
517	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	16.46	- -	-	-	0/0
518	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	243.91	- -	-	-	0/0
519	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	338.97	- -	-	-	0/0
520	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	234.09	03/2010 -	-	-	0/0
521	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
522	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	84.67	12/2015 -	03/2017	15(O) -	0/0
523	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	1.06	- -	-	-	0/0
524	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	16.86	- -	-	-	0/0
525	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.81	- -	-	-	0/0
526	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	60.46	- -	-	-	0/0
527	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.10	- -	-	-	0/0
528	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	839.00	0.01	- -	-	-	0/0
529	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	114.41	02/2015 -	02/2015	0(O) -	0/0
530	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.41	- -	-	-	0/0
531	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	502.50	03/2014 -	03/2014	-	0/0
532	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	810.78	133.47	- -	-	-	0/0
533	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.52	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
534	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	06/2014	12(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
535	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.29	- -	-	-	0/0
536	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	1,188.91	674.09	- 12/2009	02/2012	-	0/0
537	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
538	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU	09/2006	456.00 456.00	820.00	188.32	- -	-	-	0/0
539	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 125.00	420.00	60.46	- -	-	-	0/0
540	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	167.73	89.01	03/2012 -	02/2013	-	0/0
541	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU	09/1995	100.00 100.00	900.00	568.29	- -	-	-	0/0
542	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	3,176.10	3,503.29	12/2006 08/2010	08/2010	-	0/0
543	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 -	167.50	1.07	- -	-	-	0/0
544	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	913.00 -	1,801.01	1.29	- -	-	-	0/0
545	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181(O) -	0/0
546	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	1,389.62	745.28	03/2014 -	03/2014	-	0/0
547	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH	04/2012	380.00 -	380.00	1.19	- -	-	-	0/0
548	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,116.53	283.53	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
549	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR, MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
550	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, MULTI STATE	04/1990	155.66 -	548.01	200.37	- 03/2010	-	-	0/0
551	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	685.17	110.81	- -	-	-	0/0
552	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	279.40	188.31	- -	04/2014	-	0/0
553	WARDHA-NANDED MAHARASHTRA - [N22000231]CR, MAHARASHTRA	04/2008	697.00 -	2,501.05	68.88	- -	-	-	0/0
554	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	297.85 -	297.85	5.17	- -	-	-	0/0
555	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	341.05 -	348.85	1.04	- -	-	-	0/0
556	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR, MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		149,809.12 -	267,704.13	81,684.96				1/7
	ROAD TRANSPORT AND HIGHWAYS								

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
557	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	338.30	08/2013 -	02/2015	18(O) -	0/0
558	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
559	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	347.90	10/2014 -	10/2014	0(O) -	0/0
560	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	263.80	07/2014 -	07/2014	0(O) -	0/0
561	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.20	05/2013 -	05/2013	-	0/0
562	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,177.00	11/2013 -	06/2014	7(O) -	0/0
563	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	431.70	04/2014 -	09/2014	5(O) -	0/0
564	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,293.00	10/2014 -	10/2014	0(O) -	0/0
565	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	45.35	07/2014 -	07/2014	0(O) -	0/0
566	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	133.50	01/2014 -	12/2015	23(O) -	0/0
567	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
568	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	699.80	02/2014 -	02/2014	-	0/0
569	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	314.60	04/2014 -	12/2014	8(O) -	0/0
570	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014	0(O) -	0/0
571	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	662.80	09/2014 -	09/2014	0(O) -	0/3
572	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,642.00	08/2014 -	07/2015	11(O) -	0/0
573	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,378.00	06/2013 -	06/2013	-	0/3
574	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	07/2014	10(O) -	0/0
575	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	919.40	08/2013 -	08/2013	-	0/3
576	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
577	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	457.60	02/2014 -	02/2014	-	0/0
578	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,523.00	08/2013 -	12/2014	16(O) -	0/0
579	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,607.00	08/2013 -	12/2014	16(O) -	0/0
580	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	325.10	08/2013 -	12/2015	28(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
581	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	183.90	10/2015 -	10/2015	0(O) -	0/0
582	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.40	07/2013 -	12/2014	17(O) -	0/0
583	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,602.00	09/2014 -	09/2014	0(O) -	0/0
584	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	278.40	09/2007 07/2011	06/2014	81(O) 35(R)	0/0
585	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	100.30	12/2015 -	12/2015	0(O) -	0/3
586	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,184.00	11/2012 -	06/2014	19(O) -	0/0
587	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
588	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	375.20	09/2013 -	12/2014	15(O) -	0/0
589	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2015	0(O) -	0/0
590	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,043.00	06/2014 -	06/2014	0(O) -	0/0
591	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	656.00	-	06/2014	-	2/2
592	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	10/2014	21(O) -	0/0
593	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19(O) -	0/0
594	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	304.60	06/2008 -	12/2014	78(O) -	0/0
595	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	266.60	06/2008 -	12/2014	78(O) -	0/0
596	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.00	06/2005 -	12/2014	114(O) -	0/0
597	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69(O) 0(R)	0/0
598	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65(O) -	0/0
599	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	879.90	03/2013 -	12/2014	21(O) -	0/0
600	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38(O) -	0/0
601	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2014	32(O) -	0/0
602	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,KARNATAKA	03/2011	839.00 -	839.00	691.90	-	05/2014	-	0/1
603	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	06/2014	13(O) -	0/0
604	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
605	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	470.90	04/2015 -	04/2015	0(O) -	0/0
606	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.80	05/2010 -	06/2014	49(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
607	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	720.60	07/2013 -	06/2014	11(O) -	0/0
608	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	05/2014	11(O) -	0/0
609	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	770.30	- -	05/2013	-	1/1
610	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	267.10	06/2008 -	06/2014	72(O) -	0/0
611	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.20	05/2008 07/2014	10/2014	77(O) 3(R)	0/0
612	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47(O) -	0/0
613	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	808.10	09/2015 -	09/2015	0(O) -	0/0
614	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	519.10	09/2008 -	06/2014	69(O) -	0/0
615	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	262.40	11/2016 -	11/2016	0(O) -	0/0
616	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	423.00	08/2015 -	08/2015	0(O) -	0/0
617	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	517.90	10/2013 -	11/2015	25(O) -	0/0
618	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	171.80	09/2008 -	06/2014	69(O) -	0/0
619	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,024.00	08/2013 06/2014	06/2014	10(O) 0(R)	0/0
620	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,398.00	09/2012 -	08/2014	23(O) -	2/3
621	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
622	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
623	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60(O) -	0/0
624	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	361.00	301.80	02/2009 -	05/2014	63(O) -	0/0
625	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	331.23	131.30	07/2009 -	04/2014	57(O) -	0/0
626	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	118.90	09/2007 -	12/2014	87(O) -	0/0
627	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	309.90	10/2013 -	12/2014	14(O) -	0/0
628	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	01/2013	-	0/0
629	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
630	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	598.40	05/2013 -	06/2014	13(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
631	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	08/2014	16(O) -	0/0
632	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	692.50	02/2013 -	02/2013	-	0/0
633	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,981.00	12/2012 -	12/2012	-	0/0
634	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,007.00	07/2013 -	06/2014	11(O) -	0/0
635	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	646.20	01/2014 -	06/2014	5(O) -	0/0
636	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	856.40	07/2013 -	10/2014	15(O) -	0/0
637	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	06/2014	25(O) -	0/0
638	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	283.30	10/2008 -	06/2014	68(O) -	0/0
639	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	678.20	07/2014 -	07/2014	0(O) -	0/0
640	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,077.00	-	12/2014	-	2/3
641	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	567.10	07/2012 -	07/2014	24(O) -	0/0
642	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	280.13	165.60	11/2008 12/2014	06/2014	67(O) -6(R)	0/0
643	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	122.40	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
644	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 167.64	167.64	109.80	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
645	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 200.00	200.00	193.50	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
646	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,230.00	06/2013 -	06/2014	12(O) -	0/0
647	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	586.90	03/2013 -	12/2015	33(O) -	0/0
648	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	311.60	06/2008 -	06/2014	72(O) -	0/0
649	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	284.60	10/2014 -	10/2014	0(O) -	0/0
650	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2015	01/2015	81(O) 0(R)	0/0
651	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 05/2014	05/2014	71(O) 0(R)	0/0
652	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
653	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	472.90	06/2015 -	05/2016	11(O) -	0/0
654	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	541.70	09/2013 -	09/2013	-	0/0
655	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,116.00	02/2010 -	12/2014	58(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
656	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11(O) -	0/0
657	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	645.00	09/2014 -	10/2015	13(O) -	0/0
658	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	11/2011	-	0/0
659	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	0(O) -	0/0
660	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	265.40	06/2014 -	12/2014	6(O) -	0/0
661	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	858.00	03/2014 -	06/2014	3(O) -	0/0
662	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	05/2014	15(O) -	0/0
663	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	940.00	1,341.00	07/2012 -	07/2012	-	0/0
664	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21(O) -	0/0
665	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	429.00	01/2014 -	08/2014	7(O) -	0/0
666	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
667	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,135.00	07/2015 -	06/2016	11(O) -	0/0
668	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	372.40	10/2008 -	10/2014	72(O) -	0/0
669	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	334.70	06/2015 -	06/2015	0(O) -	0/0
670	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51 -	333.51	264.60	09/2014 -	09/2014	0(O) -	0/0
671	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,161.00	11/2013 -	11/2013	-	0/0
672	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	812.80	03/2013 -	12/2014	21(O) -	0/0
673	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	962.50	05/2014 -	05/2014	0(O) -	0/0
674	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 - 157.47	157.47	260.60	09/2007 03/2014	12/2014	87(O) 9(R)	0/0
675	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
676	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	267.30	06/2014 -	06/2014	0(O) -	0/0
677	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	06/2014	6(O) -	0/0
678	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,258.00	12/2013 -	06/2014	6(O) -	0/0
679	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2014	0(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
680	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	154.60	08/2012 -	03/2015	31(O) -	0/0
681	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015	82(O) 0(R)	0/0
682	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	254.30	06/2014 -	06/2014	0(O) -	0/0
683	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	06/2014	34(O) -	2/2
684	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,376.00	11/2013 -	11/2013	-	0/0
685	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11(O) -	0/0
686	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	145.80	05/2013 -	05/2014	12(O) -	0/0
687	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	382.50	- -	05/2014	- -	2/2
688	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,038.00	03/2014 -	03/2015	12(O) -	0/0
689	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	193.10	200.40	03/2008 -	02/2008	-	0/0
690	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	62.32	11/2012 -	12/2014	25(O) -	0/0
691	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015	0(O) -	0/0
692	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	- -	-	-	0/0
	Total		101,597.54 -	103,690.49	89,840.12				14/29
	<u>SHIPPING AND PORTS</u>								
693	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	211.30	04/2011 11/2011	11/2011	-	0/0
694	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
695	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	47.32	01/2013 06/2013	06/2013	-	0/0
696	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
697	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	81.40	12/2011 10/2012	10/2012	-	0/0
698	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014	2(O) 0(R)	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
699	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
700	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58(O) 37(R)	0/0
701	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
702	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
703	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
704	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
705	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99(O) 0(R)	0/0
706	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
707	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
708	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
709	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
710	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
711	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	18,600.58	8,395.88				0/1
	TELECOMMUNICATIONS								
712	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	09/2014	68(O) -	0/0
713	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2014	50(O) 33(R)	0/0
714	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	930.60	828.48	11/2010 12/2012	09/2013	-	0/0
715	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	336.84	-	10/2009 -	-	-	0/0
716	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.81	06/2009 -	06/2014	60(O) -	0/0

Sector Wise Details

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
717	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
718	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
719	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEAPON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
720	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
721	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	37(O) -	0/0
	Total		5,079.29 -	4,982.94	1,769.33				0/0
	<u>URBAN DEVELOPMENT</u>								
722	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
723	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
724	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
725	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	8,365.81	03/2016 -	03/2016	0(O) -	0/0
726	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	649.89	09/2014 -	05/2015	8(O) -	0/0
	Total		73,993.32 -	79,266.22	11,283.27				3/3
	<u>WATER RESOURCES</u>								
727	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		945,396.60	1,134,330.13	564,250.65				1107/3447

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

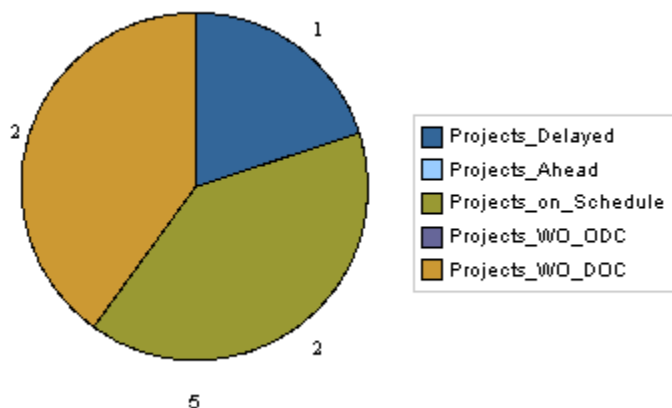

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 73993.32 crore but this was subsequently revised to Rs. 79266.22 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till April, 2014 is Rs. 11283.27 crore, which is 14.2% of the revised cost of the projects.

Figures are in Rs. Crore

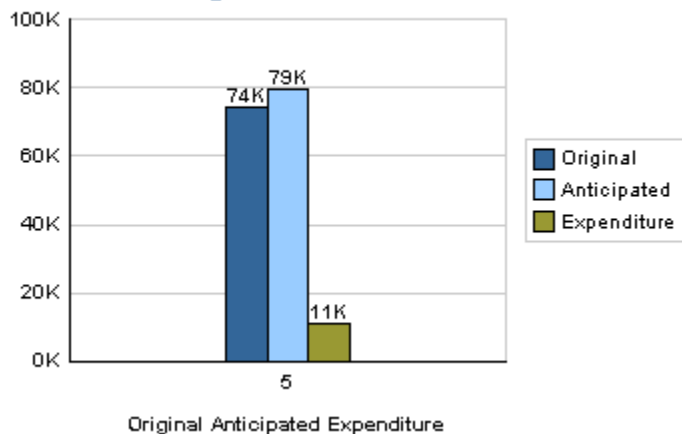

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	10
Number of Projects Delayed	4
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 10 projects, 4 projects are delayed .6 projects do not have fixed dates of commissioning.

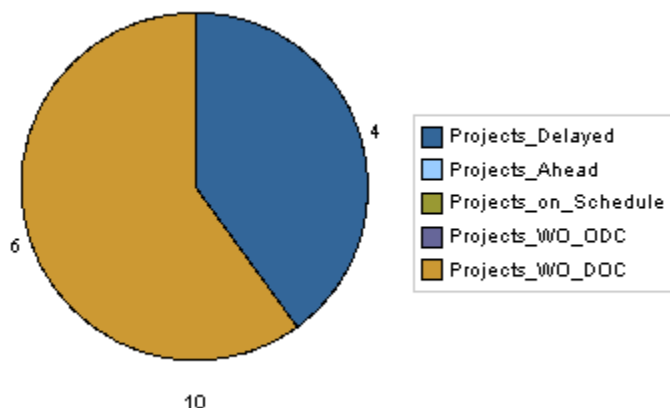

Investment Scenario

Total original cost of implementation of 10 projects when sanctioned, was of the order of Rs. 5079.29 crore but this was subsequently revised to Rs. 4982.94 crore implying a cost overrun of -1.9%. The expenditure incurred on these projects till April, 2014 is Rs. 1769.33 crore, which is 35.5% of the revised cost of the projects.

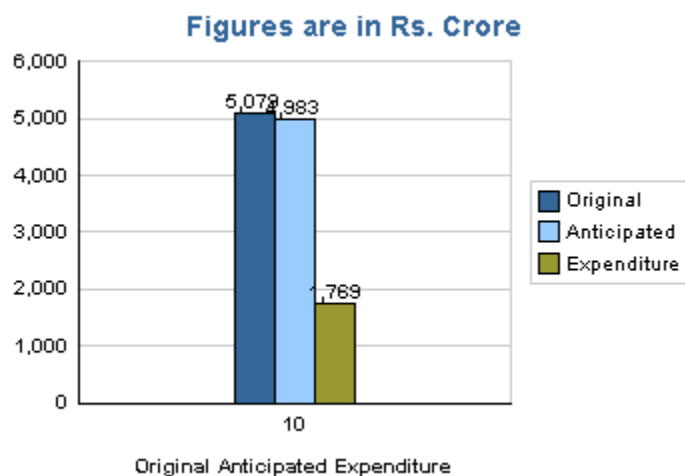

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects **19**

Number of Projects Delayed **4**

Number of Projects Without Date Of Commissioning **15**

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 4 projects are delayed .15 projects do not have fixed dates of commissioning.

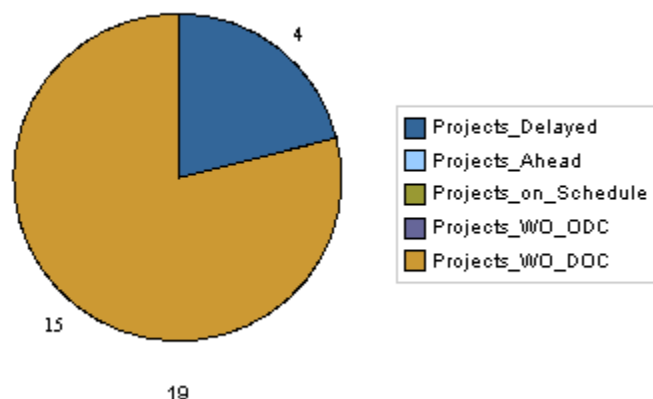

Investment Scenario

Total original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 18600.58 crore implying a cost overrun of 19.1%. The expenditure incurred on these projects till April, 2014 is Rs. 8395.88 crore, which is 45.1% of the revised cost of the projects.

Figures are in Rs. Crore

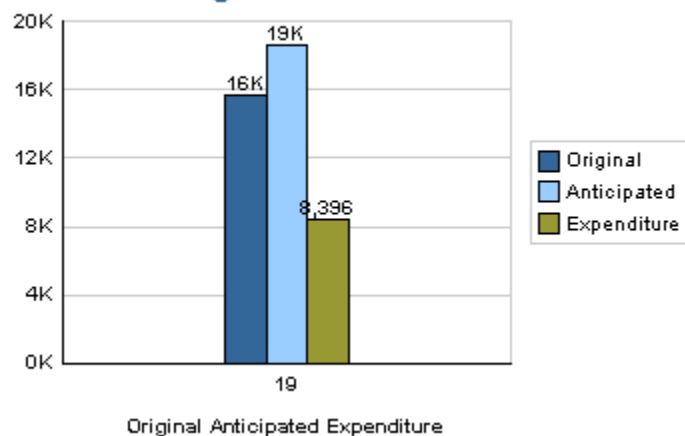

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHW


Current Status:

Number of Projects	136
Number of Projects On Schedule	26
Number of Projects Delayed	82

Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	24

Brief Analysis


Project Status with respect to Original Schedule: Out of 136 projects, 26 projects are on schedule and 82 projects are delayed .24 projects do not have fixed dates of commissioning.4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

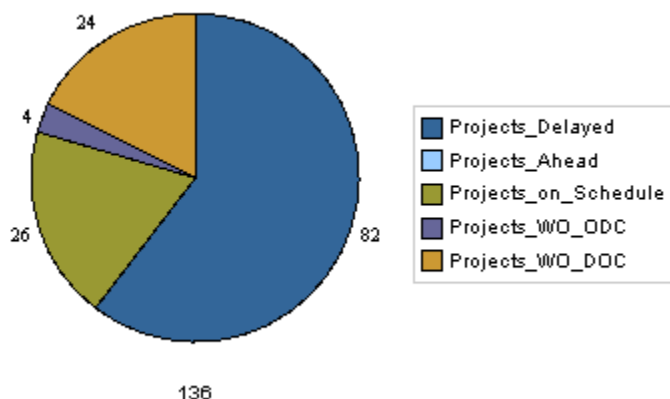

Investment Scenario

Total original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 101597.54 crore but this was subsequently revised to Rs. 103690.49 crore implying a cost overrun of 2.1%. The expenditure incurred on these projects till April, 2014 is Rs. 89840.12 crore, which is 86.6% of the revised cost of the projects.

Figures are in Rs. Crore

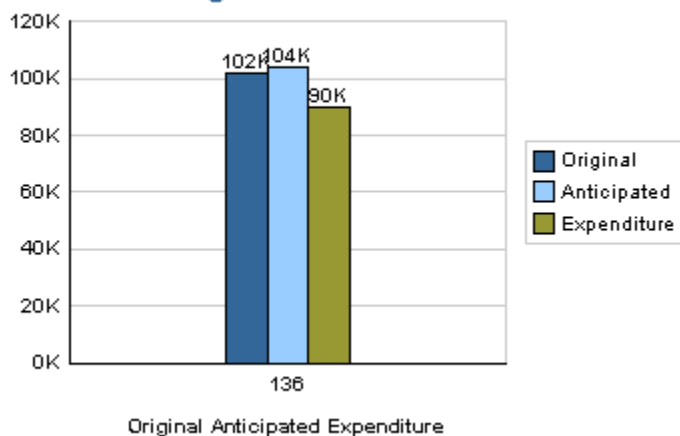

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	283
Number of Projects On Schedule	10
Number of Projects Delayed	36

Number of Projects Without Original Date of Commissioning	16
Number of Projects Without Date Of Commissioning	221

Brief Analysis


Project Status with respect to Original Schedule: Out of 283 projects, 10 projects are on schedule and 36 projects are delayed .221 projects do not have fixed dates of commissioning.16 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

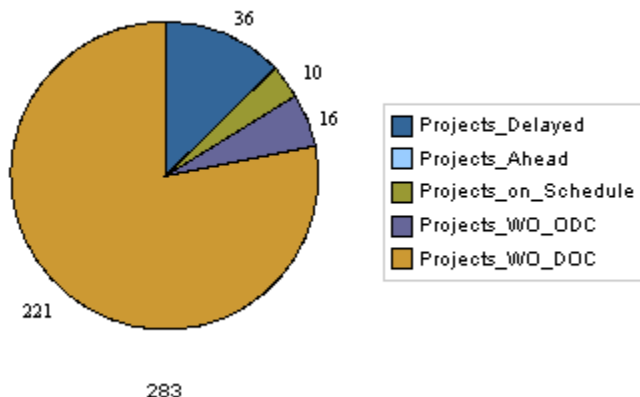

Investment Scenario

Total original cost of implementation of 283 projects when sanctioned, was of the order of Rs. 149809.12 crore but this was subsequently revised to Rs. 267704.13 crore implying a cost overrun of 78.7%. The expenditure incurred on these projects till April, 2014 is Rs. 81684.96 crore, which is 30.5% of the revised cost of the projects.

Figures are in Rs. Crore

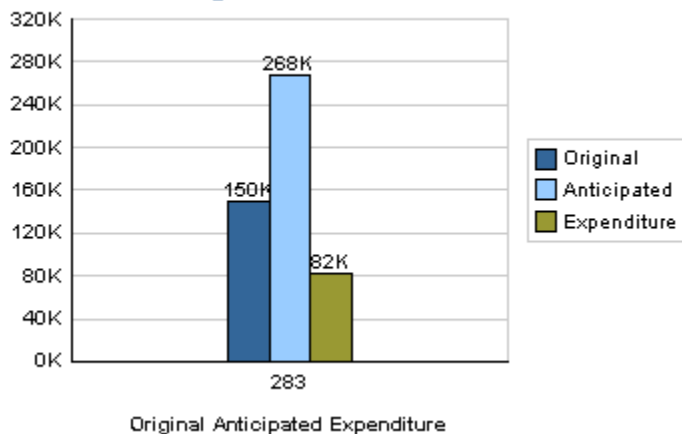

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	100
Number of Projects On Schedule	34
Number of Projects Delayed	54
Number of Projects Ahead	4
Number of Projects Without Date Of Commissioning	8

Brief Analysis


Project Status with respect to Original Schedule: Out of 100 projects, 4 projects are ahead of schedule, 34 projects are on schedule and 54 projects are delayed .8 projects do not have fixed dates of commissioning.

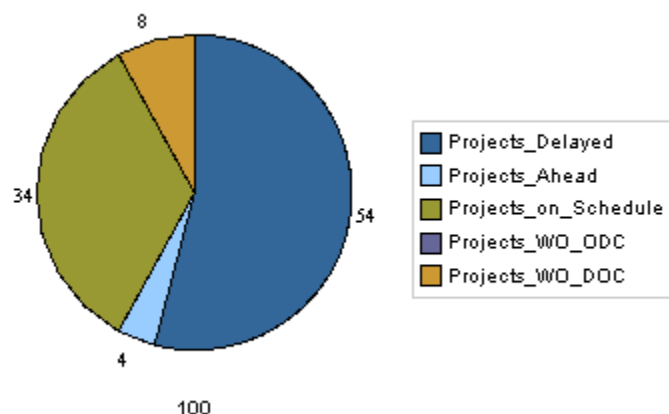

Investment Scenario

Total original cost of implementation of 100 projects when sanctioned, was of the order of Rs. 246280.79 crore but this was subsequently revised to Rs. 267159.75 crore implying a cost overrun of 8.5%. The expenditure incurred on these projects till April, 2014 is Rs. 143452.34 crore, which is 53.7% of the revised cost of the projects.

Figures are in Rs. Crore

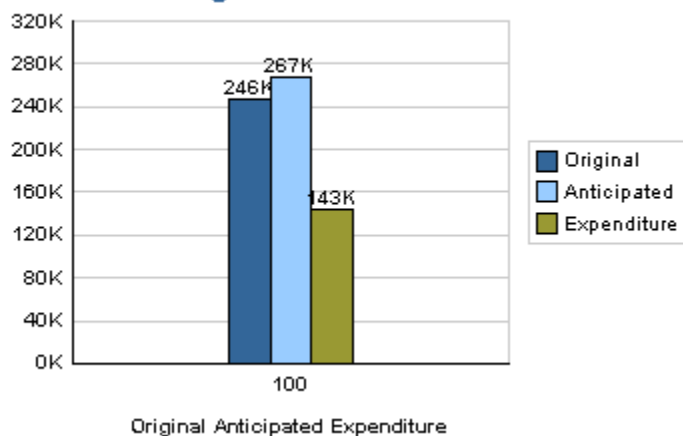

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	84
Number of Projects On Schedule	22
Number of Projects Delayed	53
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	6

Brief Analysis


Project Status with respect to Original Schedule: Out of 84 projects, 1 project are ahead of schedule, 22 projects are on schedule and 53 projects are delayed .6 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

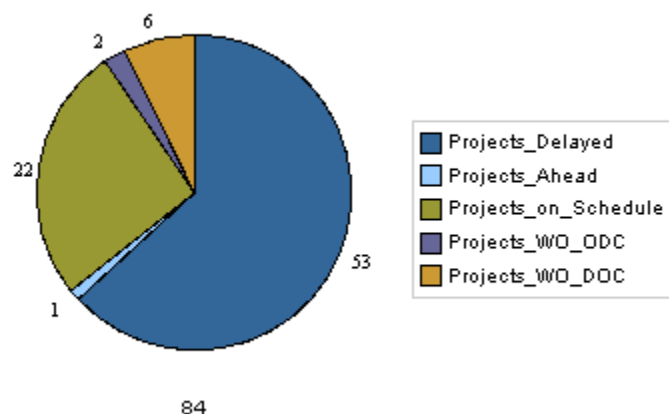

Investment Scenario

Total original cost of implementation of 84 projects when sanctioned, was of the order of Rs. 195841.81 crore but this was subsequently revised to Rs. 208398.95 crore implying a cost overrun of 6.4%. The expenditure incurred on these projects till April, 2014 is Rs. 107098.52 crore, which is 51.4% of the revised cost of the projects.

Figures are in Rs. Crore

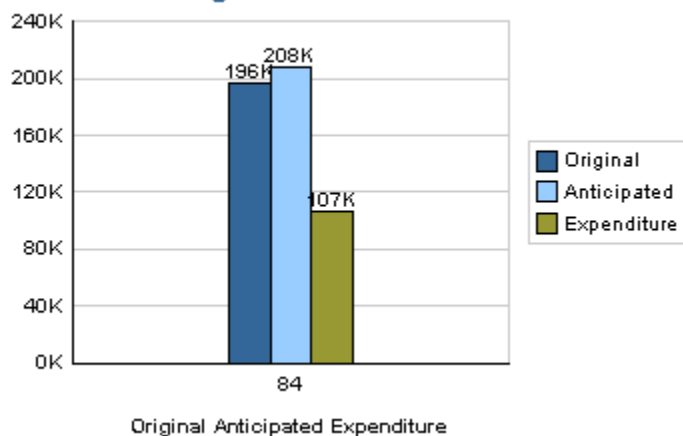

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	20
Number of Projects On Schedule	5
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 5 projects are on schedule and 13 projects are delayed .2 projects do not have fixed dates of commissioning.

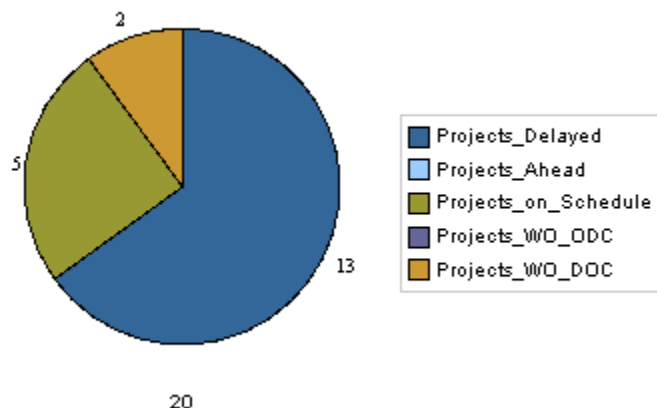

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 65959.26 crore but this was subsequently revised to Rs. 72188.55 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till April, 2014 is Rs. 59696.44 crore, which is 82.7% of the revised cost of the projects.

Figures are in Rs. Crore

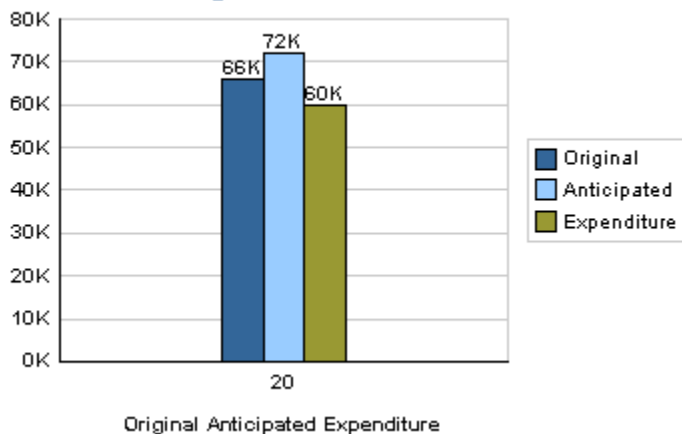

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	56
Number of Projects On Schedule	22
Number of Projects Delayed	28

Number of Projects Without Date Of Commissioning	6
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 56 projects, 22 projects are on schedule and 28 projects are delayed .6 projects do not have fixed dates of commissioning.

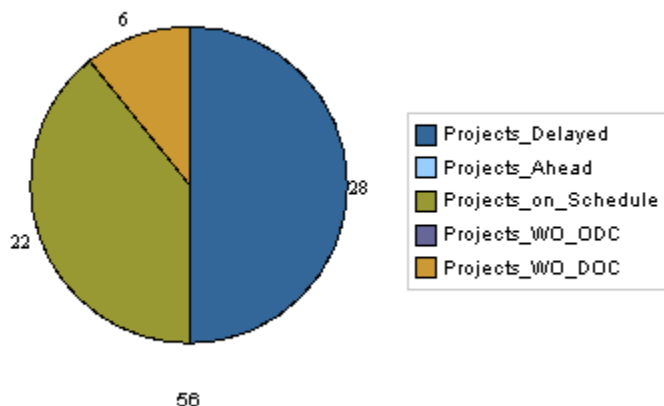

Investment Scenario

Total original cost of implementation of 56 projects when sanctioned, was of the order of Rs. 38737.38 crore but this was subsequently revised to Rs. 48559.52 crore implying a cost overrun of 25.4%. The expenditure incurred on these projects till April, 2014 is Rs. 17920.92 crore, which is 36.9% of the revised cost of the projects.

Figures are in Rs. Crore

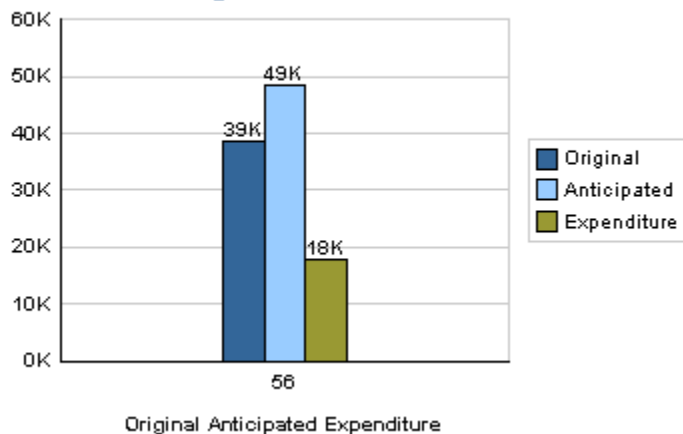

Sector wise current status of projects on the Flash Report

CIVIL AVIATION


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

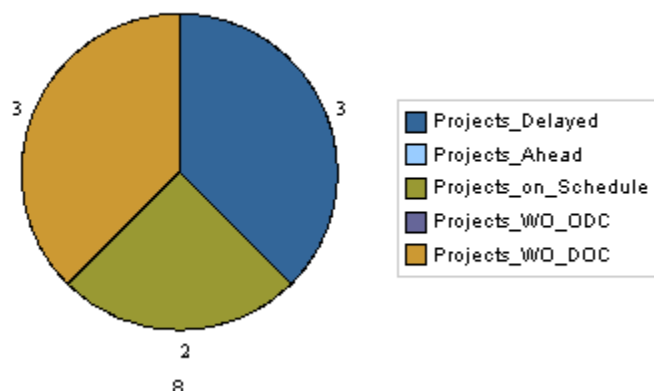

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6946 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till April, 2014 is Rs. 5775.55 crore, which is 83.1% of the revised cost of the projects.

Figures are in Rs. Crore

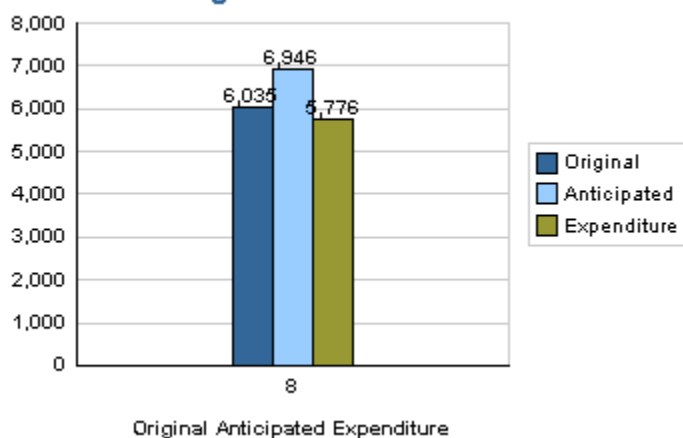

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

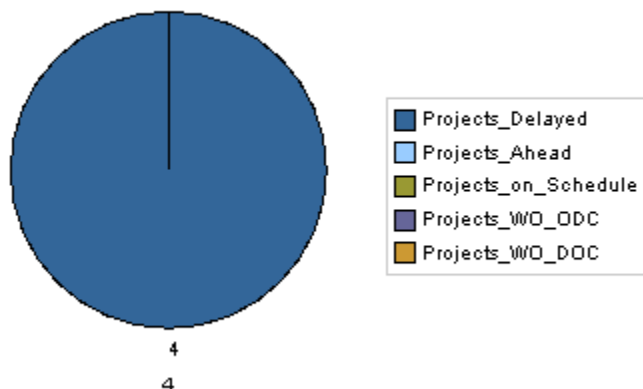

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till April, 2014 is Rs. 29610.17 crore, which is 63.4% of the revised cost of the projects.

Figures are in Rs. Crore

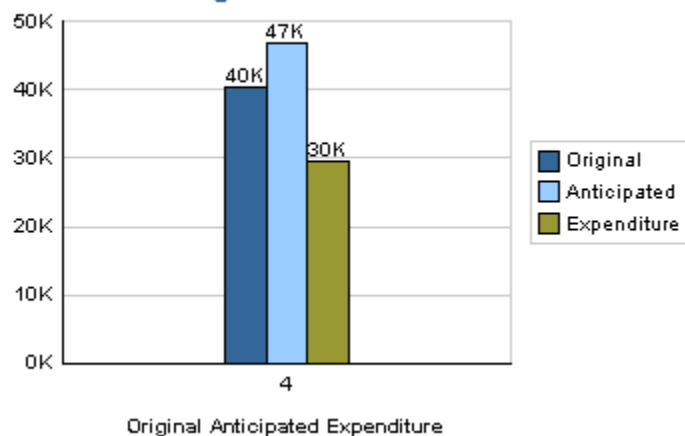

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	19	22,236.22	27,644	20,199.35
2	ARUNACHAL PRADESH	4	9,512.22	16,857.31	10,880.71
3	ASSAM	38	23,344.1	36,030.05	27,430.14
4	BIHAR	46	32,819.04	40,577.14	31,931.83
5	CHANDIGARH	1	452	452	230.42
6	CHHATISGARH	23	56,979.13	64,487.75	26,742.72
7	DELHI	4	41,533.88	41,531.33	9,067.71
8	GOA	1	335.61	388.53	278.88
9	GUJARAT	33	38,022.74	39,094.64	17,368.73
10	HARYANA	9	4,493.13	6,690.86	7,242.29
11	HIMACHAL PRADESH	6	15,762	22,232.81	16,094.52
12	JAMMU AND KASHMIR	7	11,965.4	32,751.28	15,205.6
13	JHARKHAND	27	16,118.82	20,383.59	11,381.81
14	KARNATAKA	35	79,606.44	94,510.66	28,384.95
15	KERALA	12	22,610.65	25,135.43	9,351.47
16	MADHYA PRADESH	19	30,777.43	32,003.81	11,670.84
17	MAHARASHTRA	51	93,259.91	1,08,351.14	55,780.66
18	MANIPUR	1	727.56	5,996	2,152.99
19	MEGHALAYA	3	4,845.02	4,845.02	932.19
20	MIZORAM	2	1,532.97	3,307.11	745.04
21	MULTI STATE	189	2,00,079.61	2,24,532.94	94,691.01
22	NAGALAND	2	5,124	6,720.57	9.23
23	ODISHA	29	59,053.87	65,530.66	45,554.43
24	PUNJAB	4	1,680.2	1,653.16	2,508.78
25	RAJASTHAN	25	25,638.72	25,805.94	12,941.33
26	SIKKIM	2	1,648.94	3,684.88	354.22
27	TAMIL NADU	38	51,343.56	67,575.26	46,413.18
28	TELANGANA	20	8,274.07	10,274.87	3,140.32
29	TRIPURA	6	2,966.26	4,737.26	2,651.57
30	UTTAR PRADESH	28	21,445.44	26,034.35	16,201.16
31	UTTARAKHAND	6	7,844.04	10,085.07	3,040.44
32	WEST BENGAL	37	53,363.62	64,424.71	33,672.13
TOTAL		727	9,45,396.6	11,34,330.13	5,64,250.65

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	17,562
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	ATOMIC ENERGY	09/2003	3,492	-	4,564.17
3	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,439.96
4	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,839.53
5	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	2,816.4
6	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	9,959
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,491.81
8	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	596.45	-	941.31
9	PARBATI H.E.P. STAGE -III (NHPC)	POWER	10/2005	2,304.56	-	2,349.46
10	VIRAMGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	200.37
11	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAYS	12/1994	124.43	495.68	663.66
12	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,805
13	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
14	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	877.71

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	155	775.36
16	NANDYAL-YERRAGUNTALA(NL), SCR	RAILWAYS	03/1996	155.74	429.49	679.78
17	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,000	1500	3,118.65
18	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	194.07	372.92
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	233	501.69	732.94
20	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	442.83
21	JALANDHAR-PATHANKOT-JAMMU-TAWI(LD), NR	RAILWAYS	03/2002	625.3	408.76	838.15
22	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	100	568.29
23	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	838.28
24	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,575.9
25	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3156.32	3,503.29
26	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	293.94
27	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	190.81	238.56	553.18
28	RAJATGARH-BARANG(LD), ECR	RAILWAYS	04/1999	166.16	-	307.18

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.53	2,152.99
30	DANIAWAN-BIHARSARIF (NL), ECR	RAILWAYS	04/2001	104.79	-	147.27
31	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	2,754.53
32	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	279.04
33	RAICHUR-GUNTAKAL(DL)(SCR)	RAILWAYS	04/2003	136.62	-	279.63
34	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	260.6
35	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	171.8
36	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	243
37	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	ROAD TRANSPORT AND HIGHWAYS	12/2003	166.27	-	200.4
38	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	266.6
39	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	304.6
40	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	519.1
41	KOTA BYPASS,RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	283.3
42	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	372.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	2325	2,573.92
44	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	15,862.37
45	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,847.61
46	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	PETROLEUM	07/2009	238.68	-	286.76
47	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	7,687.66
48	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	PETROLEUM	08/2009	246.81	-	262.43
49	RAMPUR HEP(412 MW)	POWER	01/2007	2,047.03	-	3,115.91
50	WESTERN REGION STRENGTHENING SCHEME-V	POWER	12/2007	477.69	-	483.79
51	BONGAIGAON THERMAL POWER PROJECT	POWER	01/2008	4,375.35	-	4,481
52	PARE HYDRO ELECTRIC PROJECT	POWER	12/2008	573.99	-	811.78
53	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	7,472
54	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	745.55
55	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	PETROLEUM	08/2008	144.02	-	154.08
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	114.01	332.92	452.87

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	795.45
58	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	404.19	407.2
59	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	343.17	757.65
60	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	170	417.14
61	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	RAILWAYS	09/1996	156	156	413
62	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	565.36
63	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.14
64	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	1676.31	4,142.69
65	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	462.18
66	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.96
67	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	788.17
68	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	243.91
69	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	267.12
70	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	461.35

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	227.81
72	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	959.41
73	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	556.85
74	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	949.35
75	PANVEL PEN DOUBLING	RAILWAYS	04/2006	191	-	221.12
76	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	257.78
77	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
78	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
79	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
80	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	311.6
81	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2
82	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
83	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	258.4
84	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	290.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.2
86	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	267.1
87	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,116
88	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	309.1
89	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	661.8
90	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,341
91	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,398
92	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
93	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,128
94	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
95	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762
96	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
97	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
98	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,981

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,376
100	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
101	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
102	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	879.9
103	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,077
104	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,184
105	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	720.6
106	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
107	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	770.3
108	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,230
109	4 LANING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,642
110	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	656
111	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	598.4
112	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,378
114	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	919.4
115	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,161
116	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	2,024
117	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,258
118	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	812.8
119	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	646.2
120	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
121	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	699.8
122	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	858
123	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	824.4
124	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,177
125	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	457.6
126	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	622.1

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	962.5
128	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	692.5
129	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,607
130	4-LANING OF BRAHAMPORE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,523
131	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,602
132	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	347.9
133	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

List of Projects Ahead of Schedule w.r.t. Original Schedule

						(April 2014)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>POWER</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	291.18	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	291.18		
	<u>PETROLEUM</u>						
2	LPG TERMINAL AT KOCHI - [N16000171	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015
	Total		607.06 -	607.06	20.38		
	<u>POWER</u>						
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	632.68	12/2014 -	11/2014
4	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	40.47	11/2016 -	03/2016
5	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155	10/2013	1,364.52 -	1,364.52	13.34	05/2016 -	04/2016
	Total		4,615.77 -	4,615.77	686.49		
	Grand Total		6,731.57	6,731.57	998.05		

List of Projects Without Original Date of Commissioning

(April 2014)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00	10,281.00	1.36	-	04/2015	-	0/0
2	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00	1,584.00	824.82	-	08/2015	-	0/12
	Total		11,865.00	11,865.00	826.18				0/12
	<u>RAILWAYS</u>								
3	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40	279.40	188.31	-	04/2014	-	0/0
4	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00	260.16	221.12	-	05/2014	-	0/0
5	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21	1,995.25	301.86	-	12/2014	-	0/0
6	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00	951.24	556.85	-	12/2014	-	0/0
7	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00	2,050.00	87.88	-	12/2014	-	0/0
8	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR, WEST BENGAL	04/1983	36.80	703.18	253.51	-	03/2015	-	0/0
9	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00	1,708.41	1,561.91	-	03/2015	-	0/0
10	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70	3,019.17	2,754.53	-	03/2015	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92	359.86	2.22	-	03/2015	-	0/0
12	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20	258.20	1.18	-	03/2016	-	0/0
13	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52	241.52	148.33	-	03/2016	-	0/0
14	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12	312.12	82.48	-	03/2016	-	0/0
15	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77	209.77	40.39	-	03/2017	-	0/0
16	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55	283.55	2.90	-	03/2017	-	0/0
17	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10	714.10	28.86	-	12/2017	0(R3)	0/0

(April 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR, ASSAM	09/2006	200.00 200.00	430.33	186.08	- -	03/2018	-	0/0
	Total		7,087.29 -	13,776.26	6,418.41				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
19	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, KARNATAKA	03/2011	839.00 -	839.00	691.90	- -	05/2014	-	0/1
20	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	680.00	382.50	- -	05/2014	-	2/2
21	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	656.00	- -	06/2014	-	2/2
22	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,077.00	- -	12/2014	-	2/3
	Total		2,670.00 -	2,670.00	2,807.40				6/8
	Grand Total		21,622.29	28,311.26	10,051.99				6/20

List of Projects Without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 2,325.00	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>COAL</u>				
4	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	03/2011 -	03/2014
5	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	03/2013 -	03/2014
6	BINA EXTN. PROJ(6.0 MTPA) - [N06000019]NCL,MULTI STATE	11/2006	168.97 -	03/2014 -	03/2014
7	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	03/2014 -	03/2014
8	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
9	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
	Total		2,309.78 -		
	<u>STEEL</u>				
10	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,ANDHRA PRADESH	08/2006	260.00 349.64	12/2009 08/2010	06/2013
11	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,ANDHRA PRADESH	07/2007	202.00 343.58	01/2010 02/2011	11/2013
	Total		462.00 -		
	<u>PETROCHEMICALS</u>				
12	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
13	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070]GAIL,MULTI STATE	07/2009	238.68 -	01/2012 -	07/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013
15	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-
16	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	12/2012 -	-
17	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
18	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
	Total		5,621.00 -		
	<u>POWER</u>				
19	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
20	MOUDA STPP - [N18000048]NTPC,MAHARASHTRA	11/2008	5,459.28 -	08/2012 -	03/2013
21	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,MADHYA PRADESH	01/2009	5,915.00 -	10/2012 -	03/2013
22	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,UTTAR PRADESH	01/2009	6,230.81 -	10/2012 -	10/2013
23	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	02/2012 -	12/2013
24	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	12/2007 12/2009	-
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	11/2011 -	-
26	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	- -	-
	Total		21,197.65 -		
	<u>RAILWAYS</u>				
27	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	06/2007
28	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,MULTI STATE	07/1998	125.00 -	07/2008 -	07/2008
29	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009
30	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010
31	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 08/2010	08/2010
32	PANDEBESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010
33	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011
34	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
35	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
36	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, MULTI STATE	02/1996	240.00 -	- -	02/2012
37	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012
38	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012
39	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012
40	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012
41	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU, BIHAR	04/2003	98.74 224.51	- -	03/2012
42	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, BIHAR	03/2005	470.09 1,417.97	- -	03/2012
43	KARUR-SALEM(NL), SR - [220100191]SR, TAMIL NADU	02/1997	155.55 155.00	- -	10/2012
44	JIND-SONEPAT (NL), NR - [220100280]NR, HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, TAMIL NADU	09/2006	343.17 343.17	- -	12/2012
46	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, KARNATAKA	02/1997	295.00 -	- -	01/2013
47	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013
48	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19 218.19	- -	02/2013
49	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013
50	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	- -	03/2013
51	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013
52	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013
53	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013
54	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	03/2013
55	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	12/2011 11/2013	11/2013
56	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 -	- -	12/2013
57	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 495.68	- -	02/2014
58	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	- -	03/2014
59	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	218.24 377.32	- -	03/2014

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
60	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	323.40 744.71	- -	03/2014
61	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014
62	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014
63	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	03/2014
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2014
65	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014
66	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	03/2014
67	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014
68	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014
69	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
70	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014
71	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
72	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
73	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
74	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
75	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
76	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
77	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
78	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
79	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
80	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
81	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
82	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
83	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 -	- -	-
84	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-
86	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
87	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-
88	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-
89	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-
90	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
91	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-
92	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-
93	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-
94	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-
95	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
96	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-
97	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-
98	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-
99	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-
100	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	- -	-
101	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,MULTI STATE	04/2006	378.56 671.82	- -	-
102	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 -	02/2006 -	-
103	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-
104	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-
105	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-
106	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-
107	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-
108	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	02/2013
109	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
110	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-
111	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
112	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-
113	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-
114	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-
115	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-
116	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-
117	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-
118	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-
119	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-
120	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
121	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
122	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-
123	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
124	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
125	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-
126	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
127	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
128	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
129	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
130	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
131	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
132	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
133	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
134	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
135	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-
136	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-
137	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
138	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-
139	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
140	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
141	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
142	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
143	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
144	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-
145	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
146	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
147	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
148	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
149	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
150	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
151	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
152	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
153	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
154	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
155	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
156	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
157	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
158	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
159	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
160	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
161	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
162	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
163	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
164	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
165	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
166	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
167	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
168	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-
169	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
170	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-
171	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
172	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
173	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP,WEST BENGAL	04/2009	573.78 -	- -	-
174	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
175	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
176	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
177	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
178	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
179	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
180	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
181	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
182	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
183	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
185	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRACHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
186	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
187	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
188	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-
189	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
190	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
191	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
192	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
193	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
194	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
195	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
196	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
197	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
198	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
199	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-
200	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
201	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
202	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
203	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
204	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
205	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
206	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
207	MANUGURU-RAMAGUNDAM - [N22000259](SCR),TELANGANA	04/2013	1,112.00 -	- -	-
208	KONDAPALLI-PENUBALLI - [N22000260](SCR),MULTI STATE	04/2013	723.00 -	- -	-
209	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-
210	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-
211	BHADRACHALAM-KOVVUR - [N22000264](SCR),MULTI STATE	04/2012	923.23 -	- -	-
212	GUDUR-DURGARAJAPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-
213	MEERUT-MUZAFFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
214	MANSABHATINDA PH-1 INCLUDING MM FOR RAMAMANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
215	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-
216	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
217	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
218	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
219	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
220	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
221	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
222	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
223	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
224	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
225	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
226	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-
227	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-
228	AKKANAPET-MEDAK - [N22000285](SCR),TELANGANA	04/2012	153.00 -	- -	-
229	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
230	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),TELANGANA	04/2010	337.49 -	- -	-
231	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
232	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
233	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
234	UNCHAHAAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
235	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
236	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
237	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
238	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
239	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
240	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
241	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
242	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
243	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
244	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
245	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
246	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-
247	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
	Total		101,108.80 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
248	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	02/2008
249	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	11/2011
250	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
251	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
252	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012
253	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013
254	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
255	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	- -	05/2013
256	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013
257	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
258	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
259	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
260	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
261	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
262	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013
263	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
264	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
265	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014
266	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	02/2014
267	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
268	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
269	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
270	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
271	WIDENING OF KHEDE-SINAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N240000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
	Total		15,689.05 -		
	SHIPPING AND PORTS				
272	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
273	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
274	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
275	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
276	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
277	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
278	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
279	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013
280	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
281	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
282	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
283	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
284	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
285	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
286	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		12,760.79 -		
	<u>TELECOMMUNICATIONS</u>				
287	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012
288	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013
289	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013
290	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-
291	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-
292	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-
	Total		3,061.14 -		
	<u>URBAN DEVELOPMENT</u>				
293	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
294	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>WATER RESOURCES</u>				
295	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		179,099.41		

List of On Schedule Projects w.r.t. Original Schedule

						(April 2014)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	230.42	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		669.60 -	669.60	230.46		
	<u>COAL</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	227.23	03/2015 -	03/2015
4	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017
5	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	50.46	03/2016 -	03/2016
6	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
7	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.56	03/2016 -	03/2016
8	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
9	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
10	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	95.88	03/2020 -	03/2020
12	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.14 -	430.14	65.51	03/2016 -	03/2016
13	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.27	07/2016 -	07/2016
14	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	5.43	06/2015 -	06/2015
15	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	55.25	03/2016 -	03/2016
16	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
17	MURAIH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
18	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
19	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	25.00	03/2018 -	03/2018
20	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	219.03	03/2016 -	03/2016

(April 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	94.45	03/2015 -	03/2015
22	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
23	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	75.42	03/2015 -	03/2015
24	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	619.15	03/2016 03/2016	03/2016
	Total		11,448.05 -	11,076.71	1,815.21		
	<u>PETROLEUM</u>						
25	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	593.64	03/2015 -	03/2015
26	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	248.39	12/2014 -	12/2014
27	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
28	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 -	10/2014
29	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,910.30	-	05/2016 -	05/2016
30	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	0.05	07/2016 -	07/2016
31	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
32	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	-	02/2016 -	02/2016
33	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.23	09/2017 -	09/2017
34	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
35	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
36	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.26	142.66	03/2015 -	03/2015
37	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	12.13	03/2015 -	03/2015
38	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	63.96	04/2015 -	04/2015
39	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
40	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	33.26	07/2016 -	07/2016
41	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	69.71	12/2014 -	12/2014
42	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	165.89	08/2015 -	08/2015
43	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	202.33	11/2015 -	11/2015

(April 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	523.84	11/2015 -	11/2015
45	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	1,101.52	05/2014 -	05/2014
46	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,435.26	05/2015 -	05/2015
	Total		36,656.56 -	35,670.51	5,727.36		
	<u>POWER</u>						
47	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,381.55	08/2014 -	08/2014
48	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	741.43	02/2015 -	02/2015
49	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	176.06	08/2014 -	08/2014
50	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	655.12	01/2015 -	01/2015
51	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	218.57	08/2014 -	08/2014
52	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	1,026.27	10/2014 -	10/2014
53	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	43.17	06/2014 -	06/2014
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	33.49	03/2016 -	03/2016
55	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	2/2013	11,638.55 -	11,638.55	1,118.00	09/2017 -	09/2017
56	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	400.43	06/2015 -	06/2015
57	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	29.65	12/2015 -	12/2015
58	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
59	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	71.00	08/2017 -	08/2017
60	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,580.00	05/2017 -	05/2017
61	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	13.93	10/2014 -	10/2014
62	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	37.56	10/2014 -	10/2014

(April 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
64	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
65	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
66	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
67	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
70	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
71	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	222.89	03/2015 -	03/2015
73	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	980.00	08/2015 -	08/2015
74	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	2,443.00	11/2016 -	11/2016
75	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	2,392.00	09/2016 -	09/2016
76	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	3,814.00	12/2016 -	12/2016
77	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	624.48	11/2014 -	11/2014
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	315.22	11/2014 -	11/2014
79	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	609.80	08/2014 -	08/2014
80	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
	Total		83,025.71 -	83,025.71	18,927.62		
	<u>RAILWAYS</u>						
81	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	114.41	02/2015 -	02/2015
82	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	56.08	03/2015 -	03/2015
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	441.08	03/2016 -	03/2016
84	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	417.81	03/2016 -	03/2016

(April 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	100.00	03/2016 -	03/2016
86	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.32	02/2019 -	02/2019
87	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
88	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.67	03/2017 -	03/2017
89	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	14.68	03/2015 -	03/2015
90	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
	Total		15,522.87 -	20,235.53	1,313.07		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
91	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
92	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2014
93	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	254.30	06/2014 -	06/2014
94	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	962.50	05/2014 -	05/2014
95	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	267.30	06/2014 -	06/2014
96	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
97	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	263.80	07/2014 -	07/2014
98	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	347.90	10/2014 -	10/2014
99	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	808.10	09/2015 -	09/2015
100	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	423.00	08/2015 -	08/2015
101	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	334.70	06/2015 -	06/2015
102	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	45.35	07/2014 -	07/2014
103	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	284.60	10/2014 -	10/2014
104	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	678.20	07/2014 -	07/2014
105	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,602.00	09/2014 -	09/2014
106	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	262.40	11/2016 -	11/2016
107	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	183.90	10/2015 -	10/2015

(April 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
108	BARSAT-KRISHNANAGAR - [N24000229]	8/2012	867.00 -	867.00	598.60	02/2015 -	02/2015
109	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
110	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	264.60	09/2014 -	09/2014
111	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,293.00	10/2014 -	10/2014
112	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]	3/2012	828.00 -	828.00	662.80	09/2014 -	09/2014
113	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	470.90	04/2015 -	04/2015
114	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	100.30	12/2015 -	12/2015
115	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	2,043.00	06/2014 -	06/2014
116	2LANING WITH PS GOPALGANJ-CHAPPRA - [N24000190]	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014
	Total		28,360.16 -	28,360.16	15,388.98		
	<u>STEEL</u>						
117	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	103.67	08/2014 -	08/2014
118	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	34.15	12/2014 -	12/2014
119	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	83.98	06/2015 -	06/2015
120	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014
121	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	8.73	05/2016 -	05/2016
	Total		1,288.94 -	1,333.05	249.39		
	<u>URBAN DEVELOPMENT</u>						
122	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,365.81	03/2016 -	03/2016
123	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	8,365.81		
	Grand Total		241,962.03	245,361.41	52,017.90		

List of Delayed Projects w.r.t. Original and Revised Schedule

(April 2014)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00	17,270.00	17,562.00	12/2008	03/2015	75	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00	5,677.00	4,564.17	09/2010	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00	11,459.00	4,551.00	12/2015	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00	12,320.00	2,933.00	12/2016	03/2017	3	-
	Total		40,442.00	46,726.00	29,610.17				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61	388.53	278.88	05/2012	04/2014	23	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28	344.28	-	03/2014	10/2014	7	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46	309.46	269.55	01/2011	12/2016	71	44
	Total		989.35	1,042.27	548.43				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78	3,027.59	2,918.33	06/2009	06/2014	60	-
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54	6,602.74	5,225.89	03/2012	08/2014	29	-
10	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34	1,228.39	1,197.33	03/2013	03/2015	24	30
11	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40	259.40	6.99	03/2012	03/2015	36	-
12	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77	457.77	116.72	03/2013	03/2015	24	-
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63	479.63	120.15	03/2013	03/2015	24	-
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97	418.97	221.35	03/2012	03/2015	36	-
15	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19	181.19	35.35	03/2012	03/2015	36	-
16	PURNADIIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98	210.98	120.97	03/2013	03/2015	24	-
17	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67	2,675.67	1,644.36	03/2014	03/2016	24	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
18	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66	1,943.66	1,439.04	03/2014	03/2016	24	-
19	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78	706.40	44.65	07/2012	03/2016	44	-
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	131.41	03/2010	03/2016	72	-
21	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35	462.35	273.86	03/2014	03/2016	24	-
22	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63	453.63	101.83	12/2012	03/2016	39	-
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82	153.82	33.46	03/2014	03/2016	24	-
24	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77	339.77	1.43	03/2014	03/2016	24	-
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	126.88	03/2012	03/2016	48	-
26	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44	178.44	-	03/2014	03/2016	24	-
27	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42	321.50	214.19	03/2014	03/2016	24	-
28	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	35.52	03/2011	03/2016	60	-
29	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68	264.68	139.29	03/2012	03/2016	48	-
30	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96	302.96	118.59	03/2010	03/2017	84	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18	287.17	36.52	03/2011	03/2017	72	-
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
33	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87	179.87	59.08	03/2012	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11	5,907.11	340.71	12/2015	04/2018	28	-
35	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	747.82	03/2013 03/2023	03/2023	120	0
	Total		24,979.55	35,351.32	15,451.72				
	STEEL								
36	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00	6,325.00	4,634.39	12/2011	05/2014	29	-
37	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	06/2014	69	6
38	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00	16,408.00	15,862.37	12/2011	07/2014	31	-
39	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00	450.00	309.45	09/2009 05/2012	07/2014	58	26
40	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33	187.33	124.72	10/2013	08/2014	10	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
41	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,804.62	10/2009 10/2012	09/2014	59	23
42	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,055.89	03/2013 -	09/2014	18	-
43	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	379.86	04/2013 09/2014	09/2014	17	0
44	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,156.60	12/2012 -	12/2014	24	-
45	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	295.89 607.17	607.17	370.58	12/2011 01/2015	01/2015	37	0
46	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	292.64	05/2013 01/2015	01/2015	20	0
47	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,638.44	03/2013 -	03/2015	24	-
48	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	104.16	11/2013 -	06/2015	19	-
	Total		64,208.32 -	70,162.28	58,894.45				
	PETROLEUM								
49	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,920.81	05/2010 03/2013	04/2014	47	13
50	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,719.76	09/2012 -	04/2014	19	-
51	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,847.61	08/2010 03/2012	05/2014	45	26
52	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,165.53	07/2010 05/2012	05/2014	46	24
53	FIRE WATER NETWORK AT URAN - [N16000141]ONGC, MAHARASHTRA	05/2010	171.68 -	171.68	96.43	06/2013 -	05/2014	11	-
54	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	06/2014	24	-
55	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22	-
56	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, MULTI STATE	08/2010	8,140.00 -	8,140.00	6,521.61	02/2014 -	06/2014	4	-
57	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN, KARNATAKA	05/2009	1,803.78 -	1,803.78	946.17	07/2012 -	06/2014	23	-
58	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN, KARNATAKA	08/2008	12,412.00 -	12,160.26	11,362.40	01/2012 -	06/2014	29	-
59	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 -	761.68	561.31	05/2013 06/2014	06/2014	13	0
60	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL, MAHARASHTRA	08/2009	246.81 -	276.83	262.43	04/2012 -	06/2014	26	-
61	GAS TURBINE GENERATION SET - [N18000146]OIL, ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	06/2014	32	-

(April 2014)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02	204.29	154.08	06/2012	06/2014	24	-
63	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, ANDHRA PRADESH	03/2009	3,597.00	2,730.00	3,128.58	09/2011	07/2014	34	28
64	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00	678.02	113.00	06/2012	07/2014	25	-
65	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, MAHARASHTRA	08/2006	3,195.16	3,690.37	3,068.29	12/2008	09/2014	69	17
66	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20	269.10	165.71	08/2013	09/2014	13	-
67	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, ANDHRA PRADESH	01/2006	672.00	1,038.00	951.32	10/2011	09/2014	35	-
68	MARKETING TERMINAL AT PARADEEP - [N16000168]OCL, ODISHA	07/2009	199.75	199.75	135.79	06/2014	09/2014	3	-
69	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC, MULTI STATE	03/2010	3,241.03	6,638.94	2,192.69	03/2013	11/2014	20	0
70	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, HARYANA	11/2007	281.07	281.07	4.42	10/2010	12/2014	50	-
71	PARADIP REFINERY PROJECT - [N16000058]OCL, ODISHA	02/2009	29,777.00	32,710.00	25,442.00	11/2012	12/2014	25	-
72	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, MAHARASHTRA	03/2009	3,284.00	2,174.00	1,881.89	09/2011	12/2014	39	31
73	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65	736.65	449.94	09/2011	12/2014	39	-
74	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESHWAR - [N16000099]ONGC, GUJARAT	03/2009	234.78	317.64	102.78	09/2012	12/2014	27	-
75	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26	240.95	102.80	09/2012	12/2014	27	-
76	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS (WIP) - [N16000127]ONGC, ASSAM	06/2010	202.94	202.94	2.00	01/2014	01/2015	12	-
77	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL, MULTI STATE	06/2009	486.00	486.00	93.04	09/2013	02/2015	17	-
78	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15	2,378.86	1,496.19	03/2013	03/2015	24	12
79	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32	330.47	270.42	03/2012	03/2015	36	-
80	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC, GUJARAT	10/2011	200.69	200.69	11.56	07/2014	03/2015	8	-
81	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49	352.49	86.03	03/2014	03/2015	12	-
82	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	01/1999	1,419.00	1,419.00	468.42	12/2014	03/2015	3	-
83	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17	2,592.17	247.67	05/2014	05/2015	12	-
84	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00	1,227.00	829.83	10/2011	06/2015	44	-
85	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA	01/2006	993.00	1,693.00	1,178.42	01/2012	06/2015	41	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00	1,793.00	969.70	09/2012	08/2015	35	-
87	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60	676.05	519.57	12/2013	09/2015	21	-
88	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81	309.82	67.83	10/2014	10/2015	12	-
89	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00	270.00	-	12/2014	10/2015	10	-
90	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74	260.74	0.52	11/2014	11/2015	12	-
91	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40	2,920.82	1,915.45	09/2010	12/2015	63	45
92	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18	7,596.18	13.50	01/2013	12/2015	35	-
93	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00	2,523.00	992.74	01/2014	12/2015	23	-
94	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00	913.00	120.36	07/2015	12/2015	5	-
95	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00	14,225.00	2,067.10	12/2015	05/2016	5	-
96	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82	2,735.65	2,728.25	04/2006	06/2016	122	48
97	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64	723.64	-	03/2013	06/2016	39	-
98	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10	1,916.10	784.46	12/2014	12/2016	24	-
99	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63	2,189.63	1,039.42	12/2014	12/2016	24	-
100	MEHSANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00	3,823.00	1,076.07	04/2015	03/2017	23	-
101	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56	374.56	10.60	09/2012	03/2017	54	-
	Total		141,092.19	155,263.53	97,856.80				
	POWER								
102	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58	965.58	657.74	11/2012	05/2014	18	-
103	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69	477.69	483.79	09/2010	06/2014	45	-
104	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19	184.19	161.72	11/2011	06/2014	31	-
105	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33	7,075.33	6,322.56	08/2012	06/2014	22	-
106	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34	232.34	176.79	06/2012	06/2014	24	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
107	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34	1,366.34	987.66	12/2013	06/2014	6	-
108	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51	425.51	374.82	10/2013	06/2014	8	-
109	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44	552.44	402.60	02/2014	06/2014	4	-
110	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78	213.78	117.44	03/2014	06/2014	3	-
111	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56	2,716.00	2,349.46	10/2010	08/2014	46	-
112	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95	2,580.90	2,117.11	08/2012	09/2014	25	-
113	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86	2,074.86	1,507.24	03/2013	09/2014	18	-
114	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87	1,961.87	1,412.45	05/2014	09/2014	4	-
115	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49	487.49	282.42	06/2014	09/2014	3	-
116	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28	259.28	148.12	01/2014	09/2014	8	-
117	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	745.55	07/2013	11/2014	16	-
118	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATTISGARH	08/2011	1,391.97	1,391.97	1,359.35	12/2013	11/2014	11	-
119	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83	1,216.83	985.29	08/2012	12/2014	28	-
120	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19	2,743.19	2,086.80	12/2013	12/2014	12	-
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57	1,677.57	1,029.02	04/2013	12/2014	20	-
122	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25	2,569.25	2,391.47	03/2014	12/2014	9	-
123	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13	1,940.13	1,282.36	09/2014	12/2014	3	-
124	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51	2,127.51	1,798.33	07/2014	12/2014	5	-
125	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04	7,341.04	7,472.00	08/2013	03/2015	19	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
126	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12	4,824.12	3,868.48	10/2012	03/2015	29	-
127	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99	4,672.99	3,065.97	11/2012	03/2015	28	-
128	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64	752.64	379.82	07/2013	03/2015	20	-
129	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26	558.26	245.81	11/2013	03/2015	16	-
130	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15	7,220.00	5,886.00	04/2009	05/2015	73	-
131	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65	1,746.65	337.63	08/2014	05/2015	9	-
132	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40	524.40	79.92	04/2015	05/2015	1	-
133	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19	11,130.19	8,056.80	08/2013	06/2015	22	-
134	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00	2,144.00	1,696.00	12/2012	06/2015	30	-
135	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03	250.03	68.10	01/2013	06/2015	29	-
136	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12	1,585.12	1,206.46	11/2013	06/2015	19	-
137	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80	1,272.80	826.23	11/2012	06/2015	31	-
138	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66	2,422.66	963.76	08/2014	06/2015	10	-
139	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44	3,201.44	1,470.41	10/2014	06/2015	8	-
140	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38	1,501.75	1,491.81	09/2009	09/2015	72	-
141	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99	1,128.38	811.78	08/2013	09/2015	25	0
142	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57	4,404.57	470.75	01/2015	12/2015	11	-
143	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	913.63	913.63	573.22	07/2006	12/2015	113	0
144	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76	9,569.76	1,649.59	06/2015	12/2015	6	-
145	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35	4,375.35	4,481.00	07/2011	08/2016	61	-
146	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53	243.53	-	08/2014	08/2016	24	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
147	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	5,497.72	3,331.00	01/2016 -	11/2016	10	-
148	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	700.96	07/2010 02/2016	02/2017	79	12
149	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,816.40	12/2009 06/2016	03/2017	87	9
150	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,959.00	12/2009 -	03/2017	87	-
151	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,091.00	03/2013 -	03/2017	48	-
152	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,439.96	09/2009 -	07/2018	106	-
153	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	483.40	07/2014 -	07/2018	48	-
154	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,839.53	09/2010 -	09/2018	96	-
155	RAMPUR HEP(412 MW) - [N18000024]SJVNL,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	3,115.91	01/2012 -	09/2014	32	-
	Total		135,932.92 -	155,469.78	108,058.79				
	<u>RAILWAYS</u>								
156	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	585.09	03/1994 -	06/2014	243	-
157	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	06/2014	12	-
158	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	307.18	02/2009 02/2009	08/2014	66	66
159	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	279.04	03/2009 03/2009	08/2014	65	65
160	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	226.04	12/2008 -	09/2014	69	-
161	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31	10
162	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.48	369.66	03/2004 12/2010	12/2014	129	48
163	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	400.84	12/2009 03/2011	12/2014	60	45
164	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,343.55	03/2009 12/2012	12/2014	69	24
165	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	198.85	12/2012 -	12/2014	24	-
166	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	-
167	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	445.40	179.99	03/2007 03/2007	03/2015	96	96
168	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.40	372.92	06/2004 -	03/2015	129	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
169	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	725.54	445.74	12/2010 12/2010	03/2015	51	51
170	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	267.13	06/2013 06/2013	03/2015	21	21
171	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	2,075.62	10/2007 12/2012	12/2015	98	36
172	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	795.45	03/2010 -	12/2015	69	-
173	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	57.10	03/2015 -	12/2015	9	-
174	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	331.40	137.78	12/2012 -	03/2016	39	-
175	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	388.67	77.88	12/2015 -	03/2016	3	-
176	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.40	04/2012 -	03/2016	47	-
177	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.52	06/2005 07/2011	06/2016	132	59
178	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL,WEST BENGAL	04/2010	2,397.72 -	2,397.72	84.44	03/2016 -	06/2016	3	-
179	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	479.18	03/2005 12/2008	12/2016	141	96
180	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,739.04	03/2014 03/2016	12/2016	33	9
181	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,575.90	12/2008 -	03/2017	99	-
182	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	5,996.00	2,152.99	03/2011 03/2014	03/2017	72	36
183	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	283.53	03/2010 03/2017	03/2017	84	0
184	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	1,741.00	562.77	03/2014 -	03/2017	36	-
185	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	171.82	04/2014 -	03/2017	35	-
186	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	84.67	12/2015 -	03/2017	15	-
187	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24	-
188	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	5,114.91	4,142.69	03/2009 -	03/2017	96	-
189	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	959.41	03/2007 -	03/2017	120	-
190	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181	-
191	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	4,996.19	3,118.65	04/2008 03/2014	12/2017	116	45

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		26,090.16	77,208.62	33,694.22				
	ROAD TRANSPORT AND HIGHWAYS								
192	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 331.23	331.23	131.30	07/2009 -	04/2014	57	-
193	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	361.00	301.80	02/2009 -	05/2014	63	-
194	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 05/2014	05/2014	71	0
195	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	05/2014	15	-
196	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	05/2014	11	-
197	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	145.80	05/2013 -	05/2014	12	-
198	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	171.80	09/2008 -	06/2014	69	-
199	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 241.28	280.13	165.60	11/2008 12/2014	06/2014	67	-6
200	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	519.10	09/2008 -	06/2014	69	-
201	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	283.30	10/2008 -	06/2014	68	-
202	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	311.60	06/2008 -	06/2014	72	-
203	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, ASSAM	12/2003	200.00 -	200.00	267.10	06/2008 -	06/2014	72	-
204	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	278.40	09/2007 07/2011	06/2014	81	35
205	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	486.00	661.80	05/2010 -	06/2014	49	-
206	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	06/2014	25	-
207	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	06/2014	34	-
208	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2014	32	-
209	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	06/2014	13	-
210	AMRITSAR-PATHANKOT - [N24000147]NHAI, PUNJAB	05/2010	705.00 -	705.00	2,184.00	11/2012 -	06/2014	19	-
211	DEOLI-KOTA - [N24000148]NHAI, RAJASTHAN	01/2011	593.00 -	593.00	720.60	07/2013 -	06/2014	11	-
212	MURADABAD-BAREILY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,230.00	06/2013 -	06/2014	12	-
213	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	598.40	05/2013 -	06/2014	13	-
214	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,007.00	07/2013 -	06/2014	11	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
215	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,024.00	08/2013 06/2014	06/2014	10	0
216	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	06/2014	6	-
217	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,258.00	12/2013 -	06/2014	6	-
218	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	646.20	01/2014 -	06/2014	5	-
219	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	858.00	03/2014 -	06/2014	3	-
220	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,177.00	11/2013 -	06/2014	7	-
221	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	07/2014	10	-
222	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	567.10	07/2012 -	07/2014	24	-
223	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47	-
224	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,398.00	09/2012 -	08/2014	23	-
225	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	08/2014	16	-
226	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	429.00	01/2014 -	08/2014	7	-
227	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11	-
228	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	431.70	04/2014 -	09/2014	5	-
229	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	372.40	10/2008 -	10/2014	72	-
230	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.20	05/2008 07/2014	10/2014	77	3
231	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	856.40	07/2013 -	10/2014	15	-
232	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	10/2014	21	-
233	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	260.60	09/2007 03/2014	12/2014	87	9
234	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.00	06/2005 -	12/2014	114	-
235	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	122.40	04/2009 12/2014	12/2014	68	0
236	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 167.64	167.64	109.80	11/2008 12/2014	12/2014	73	0
237	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 200.00	200.00	193.50	04/2009 12/2014	12/2014	68	0

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
238	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	266.60	06/2008 -	12/2014	78	-
239	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	304.60	06/2008 -	12/2014	78	-
240	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	118.90	09/2007 -	12/2014	87	-
241	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-
242	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,116.00	02/2010 -	12/2014	58	-
243	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	-
244	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	879.90	03/2013 -	12/2014	21	-
245	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	62.32	11/2012 -	12/2014	25	-
246	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21	-
247	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	812.80	03/2013 -	12/2014	21	-
248	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	314.60	04/2014 -	12/2014	8	-
249	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.40	07/2013 -	12/2014	17	-
250	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
251	BAREILLY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	375.20	09/2013 -	12/2014	15	-
252	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,607.00	08/2013 -	12/2014	16	-
253	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,523.00	08/2013 -	12/2014	16	-
254	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	309.90	10/2013 -	12/2014	14	-
255	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	265.40	06/2014 -	12/2014	6	-
256	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	01/2015	81	0
257	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015	82	0
258	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	01/2015	81	0
259	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2015	01/2015	81	0
260	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	338.30	08/2013 -	02/2015	18	-
261	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	154.60	08/2012 -	03/2015	31	-
262	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,038.00	03/2014 -	03/2015	12	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
263	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29	500.29	622.10	08/2013	03/2015	19	-
264	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00	281.31	180.10	02/2010	07/2015	65	-
265	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76	2,498.76	2,642.00	08/2014	07/2015	11	-
266	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	1,410.00	645.00	09/2014	10/2015	13	-
267	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00	682.00	517.90	10/2013	11/2015	25	-
268	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00	754.00	586.90	03/2013	12/2015	33	-
269	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43	580.43	325.10	08/2013	12/2015	28	-
270	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36	291.36	133.50	01/2014	12/2015	23	-
271	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	258.40	04/2010 01/2016	01/2016	69	0
272	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00	2,159.00	472.90	06/2015	05/2016	11	-
273	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00	1,987.00	1,135.00	07/2015	06/2016	11	-
	Total		54,878.33	55,764.45	51,074.26				
	<u>SHIPPING AND PORTS</u>								
274	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46	994.82	427.54	02/2014 04/2014	04/2014	2	0
275	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	99	0
276	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87	511.87	106.72	03/2014 08/2014	08/2014	5	0
277	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58	37
	Total		2,856.33	4,264.85	1,679.94				
	<u>TELECOMMUNICATIONS</u>								
278	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15	158.72	84.81	06/2009	06/2014	60	-
279	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19	964.37	251.27	05/2011	06/2014	37	-
280	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81	336.81	183.16	01/2009	09/2014	68	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
281	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2014	50	33
	Total		2,018.15 -	1,843.90	548.69				
	<u>URBAN DEVELOPMENT</u>								
282	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	649.89	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	649.89				
	Grand Total		495,981.30	605,591.00	398,067.36				

List of Projects Without Milestones w.r.t. Original Schedule

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013	0/0
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	05/2012 -	04/2014	0/0
4	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	03/2014 -	10/2014	0/0
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	03/2015 -	03/2015	0/0
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	03/2015 -	03/2015	0/0
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	01/2011 04/2013	12/2016	0/0
	Total		4,092.95 -			0/0
	<u>COAL</u>					
8	MURADIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
10	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	03/2022 -	03/2022	0/0
	Total		2,180.48 -			0/0
	<u>PETROLEUM</u>					
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]MANGALORE REFIN,KARNATAKA	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
12	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,MAHARASHTRA	10/2007	5,713.03 8,813.41	05/2010 03/2013	04/2014	0/0
13	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,MAHARASHTRA	01/2009	7,133.39 -	09/2012 -	04/2014	0/0
14	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,MAHARASHTRA	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2014	0/0
15	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,MULTI STATE	01/2010	2,163.64 2,331.62	06/2012 -	06/2014	0/0
16	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	02/2014 -	06/2014	0/0
17	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	04/2012 -	06/2014	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 -	06/2012 -	06/2014	0/0
19	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, MAHARASHTRA	08/2006	3,195.16 3,690.37	12/2008 04/2013	09/2014	0/0
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, ANDHRA PRADESH	01/2006	672.00 1,038.00	10/2011 -	09/2014	0/0
21	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL, ODISHA	07/2009	199.75 -	06/2014 -	09/2014	0/0
22	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC, MULTI STATE	10/2013	429.06 -	10/2014 -	10/2014	0/0
23	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, HARYANA	11/2007	281.07 -	10/2010 -	12/2014	0/0
24	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	09/2011 -	12/2014	0/0
25	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26 -	09/2012 -	12/2014	0/0
26	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL, TAMIL NADU	12/2012	279.00 -	12/2014 -	12/2014	0/0
27	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	01/1999	1,419.00 -	12/2014 -	03/2015	0/0
28	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC, MAHARASHTRA	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
29	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL, MULTI STATE	10/2012	10,281.00 -	- -	04/2015	0/0
30	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC, MULTI STATE	04/2013	284.82 -	04/2015 -	04/2015	0/0
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, KARNATAKA	01/2006	732.00 1,227.00	10/2011 -	06/2015	0/0
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL, KERALA	01/2006	993.00 1,693.00	01/2012 -	06/2015	0/0
33	WAX PROJECT - [N16000101]NRL, ASSAM	06/2010	576.60 -	12/2013 -	09/2015	0/0
34	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	11/2012	309.81 -	10/2014 -	10/2015	0/0
35	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	12/2014 -	10/2015	0/0
36	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, MAHARASHTRA	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
37	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
38	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	07/2015 -	12/2015	0/0
39	LPG TERMINAL AT KOCHI - [N16000171]IOCL, KERALA	12/2012	607.06 -	01/2016 -	12/2015	0/0
40	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC, MAHARASHTRA	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
41	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL, BIHAR	04/2013	480.00 -	02/2016 -	02/2016	0/0
42	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC, MULTI STATE	05/2013	4,124.35 -	04/2016 -	04/2016	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
43	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00	12/2015	05/2016	0/0
44	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10	05/2016	05/2016	0/0
45	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	04/2006 06/2012	06/2016	0/0
46	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64	03/2013	06/2016	0/0
47	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88	07/2016	07/2016	0/0
48	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10	12/2014	12/2016	0/0
49	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63	12/2014	12/2016	0/0
50	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00	04/2015	03/2017	0/0
51	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56	09/2012	03/2017	0/0
52	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00	09/2017	09/2017	0/0
53	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00	09/2017	09/2017	0/0
54	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82	12/2018	12/2018	0/0
55	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00	-	-	0/0
56	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83	-	-	0/0
	Total		104,021.79			0/0
	<u>POWER</u>					
57	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63	09/2014	09/2014	0/0
58	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20	06/2015	06/2015	0/0
59	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24	06/2015	06/2015	0/0
60	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40	12/2015	12/2015	0/0
61	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69	03/2016	03/2016	0/0
62	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90	11/2016	03/2016	0/0
63	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57	03/2016	03/2016	0/0
64	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52	05/2016	04/2016	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
65	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 -	04/2016	0/0
66	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
67	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	06/2016 -	06/2016	0/0
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	06/2016 -	06/2016	0/0
69	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	07/2016 -	07/2016	0/0
70	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	08/2014 -	08/2016	0/0
71	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	09/2016 -	09/2016	0/0
72	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	11/2016 -	11/2016	0/0
73	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	09/2018	0/0
	Total		17,888.18 -			0/0
	<u>RAILWAYS</u>					
74	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	06/2007	0/0
75	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,MULTI STATE	07/1998	125.00 -	07/2008 -	07/2008	0/0
76	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
77	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
78	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 08/2010	08/2010	0/0
79	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
80	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	120.90 663.01	06/1999 03/2011	03/2011	0/0
81	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
82	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
83	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012	0/0
84	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
85	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
86	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 429.49	02/2009 -	03/2012	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
87	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	381.17 863.23	- -	03/2012	0/0
88	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012	0/0
89	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012	0/0
90	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 155.00	- -	10/2012	0/0
91	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
92	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 343.17	- -	12/2012	0/0
93	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	01/2013	0/0
94	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
95	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 218.19	- -	02/2013	0/0
96	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
97	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	03/2013	0/0
98	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
99	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
100	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	03/2013 -	03/2013	0/0
101	GHUTIASARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL	04/2009	189.97 -	12/2011 11/2013	11/2013	0/0
102	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013	0/0
103	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 495.68	- -	02/2014	0/0
104	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	03/2014	0/0
105	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 377.32	- -	03/2014	0/0
106	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 230.03	- -	03/2014	0/0
107	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]NEFR,ARUNACHAL PRADESH	09/1996	156.00 156.00	- -	03/2014	0/0
108	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	03/2013 -	03/2014	0/0
109	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	03/2014 -	03/2014	0/0
110	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
111	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	03/2014	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
112	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
113	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	03/2014	0/0
114	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014	0/0
115	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	203.00 -	- -	03/2014	0/0
116	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	04/2014	0/0
117	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	191.00 -	- -	05/2014	0/0
118	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	06/2014	0/0
119	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	06/2013 -	06/2014	0/0
120	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
121	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
122	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	12/2008 -	09/2014	0/0
123	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	03/2012 12/2013	10/2014	0/0
124	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
125	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	12/2009 03/2011	12/2014	0/0
126	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 470.21	- -	12/2014	0/0
127	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
128	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	12/2012 -	12/2014	0/0
129	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	12/2014	0/0
130	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288](SCR),MULTI STATE	04/2008	2,050.00 -	- -	12/2014	0/0
131	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	02/2015	0/0
132	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
133	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	- -	03/2015	0/0
134	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	395.00 1,577.45	- -	03/2015	0/0
135	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
136	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	06/2004 -	03/2015	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
137	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
138	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,MULTI STATE	01/2004	915.70 915.70	- -	03/2015	0/0
139	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	03/2015	0/0
140	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 282.92	- -	03/2015	0/0
141	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015	0/0
142	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015	0/0
143	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
144	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	03/2010 -	12/2015	0/0
145	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	12/2015	0/0
146	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
147	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	03/2016 -	03/2016	0/0
148	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 227.90	12/2012 -	03/2016	0/0
149	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
150	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	12/2015 -	03/2016	0/0
151	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	- -	03/2016	0/0
152	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	03/2016	0/0
153	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	- -	03/2016	0/0
154	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	04/2012 -	03/2016	0/0
155	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	06/2005 07/2011	06/2016	0/0
156	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
157	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
158	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
159	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	12/2008 -	03/2017	0/0
160	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
161	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	03/2010 03/2017	03/2017	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
162	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 813.34	03/2014 -	03/2017	0/0
163	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	04/2014 -	03/2017	0/0
164	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
165	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
166	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 1,676.31	03/2009 -	03/2017	0/0
167	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	03/2007 -	03/2017	0/0
168	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	- -	03/2017	0/0
169	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR,WEST BENGAL	04/2012	283.55 -	- -	03/2017	0/0
170	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2017	0/0
171	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	03/2017 -	03/2017	0/0
172	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
173	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2017	0/0
174	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	- 12/2017	12/2017	0/0
175	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 200.00	- -	03/2018	0/0
176	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
177	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
178	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-	0/0
179	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-	0/0
180	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
181	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
182	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-	0/0
183	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
184	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-	0/0
185	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
186	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
187	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
188	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	03/2010	-	0/0
189	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-	0/0
190	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	353.08 -	- -	-	0/0
191	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-	0/0
192	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 450.00	07/2012 -	-	0/0
193	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-	0/0
194	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	491.19 2,957.21	07/2005 -	-	0/0
195	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,MULTI STATE	09/1998	925.00 -	05/2008 03/2011	-	0/0
196	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
197	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-	0/0
198	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	78.23 162.87	- -	-	0/0
199	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 100.00	- -	-	0/0
200	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 1,047.00	- -	-	0/0
201	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-	0/0
202	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	09/2009	-	0/0
203	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	324.66 528.65	- -	-	0/0
204	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 418.17	- -	-	0/0
205	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	104.79 -	- -	-	0/0
206	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	727.13 727.13	- -	-	0/0
207	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	726.96 -	- -	-	0/0
208	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,MULTI STATE	04/2006	378.56 671.82	- -	-	0/0
209	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	186.92 -	02/2006 -	-	0/0
210	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-	0/0
211	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 404.19	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
212	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 125.00	- -	-	0/0
213	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 456.00	- -	-	0/0
214	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 300.00	- -	-	0/0
215	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	02/2013	0/0
216	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-	0/0
217	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	-	0/0
218	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
219	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	- -	-	0/0
220	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	-	0/0
221	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	160.89 199.75	- -	-	0/0
222	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 295.00	- -	-	0/0
223	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	- -	-	0/0
224	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	- -	-	0/0
225	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	- -	-	0/0
226	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	- -	-	0/0
227	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-	0/0
228	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-	0/0
229	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	- -	-	0/0
230	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-	0/0
231	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-	0/0
232	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-	0/0
233	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-	0/0
234	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
235	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-	0/0
236	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
237	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-	0/0
238	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-	0/0
239	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-	0/0
240	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-	0/0
241	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	- -	-	0/0
242	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SWR,MULTI STATE	04/2010	553.63 -	- -	-	0/0
243	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
244	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-	0/0
245	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-	0/0
246	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-	0/0
247	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-	0/0
248	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-	0/0
249	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-	0/0
250	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-	0/0
251	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	366.73 -	- -	-	0/0
252	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
253	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
254	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-	0/0
255	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
256	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
257	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-	0/0
258	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-	0/0
259	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
260	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-	0/0
261	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
262	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
263	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
264	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-	0/0
265	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-	0/0
266	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
267	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
268	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR, WEST BENGAL	04/2010	221.42 -	- -	-	0/0
269	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-	0/0
270	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-	0/0
271	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
272	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-	0/0
273	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
274	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
275	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-	0/0
276	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-	0/0
277	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-	0/0
278	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-	0/0
279	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-	0/0
280	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
281	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-	0/0
282	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-	0/0
283	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
284	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
285	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
286	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
287	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
288	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-	0/0
289	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-	0/0
290	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-	0/0
291	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
292	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-	0/0
293	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-	0/0
294	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-	0/0
295	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	697.00 -	- -	-	0/0
296	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-	0/0
297	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
298	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
299	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-	0/0
300	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-	0/0
301	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
302	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-	0/0
303	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
304	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
305	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-	0/0
306	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-	0/0
307	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-	0/0
308	SANTOSHPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
309	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
310	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
311	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-	0/0
312	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-	0/0
313	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-	0/0
314	MANUGURU-RAMAGUNDAM - [N22000259](SCR),TELANGANA	04/2013	1,112.00 -	- -	-	0/0
315	KONDAPALLI-PENUBALLI - [N22000260](SCR),MULTI STATE	04/2013	723.00 -	- -	-	0/0
316	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261](SCR),MULTI STATE	04/2012	1,054.35 -	- -	-	0/0
317	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263](SCR),MULTI STATE	04/2008	184.26 -	- -	-	0/0
318	BHADRACHALAM-KOVVUR - [N22000264](SCR),MULTI STATE	04/2012	923.23 -	- -	-	0/0
319	GUDUR-DURGARAJPATNAM - [N22000265](SCR),ANDHRA PRADESH	04/2011	283.54 -	- -	-	0/0
320	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
321	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
322	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	159.20 -	- -	-	0/0
323	DELHI-SOHNANUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
324	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-	0/0
325	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-	0/0
326	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
327	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-	0/0
328	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-	0/0
329	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-	0/0
330	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-	0/0
331	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-	0/0
332	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
333	CUMBUM-PRODDATUR - [N22000282](SCR),ANDHRA PRADESH	04/2013	829.00 -	- -	-	0/0
334	MUDKHED-PARBHANI - [N22000283](SCR),MAHARASHTRA	04/2011	390.60 -	- -	-	0/0
335	AKKANAPET-MEDAK - [N22000285](SCR),TELANGANA	04/2012	153.00 -	- -	-	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
336	NADIKUDE-SRI KALAHASTI - [N22000286](SCR),ANDHRA PRADESH	04/2011	1,313.48 -	- -	-	0/0
337	BHADRACHALAM ROAD-SATTUPALLI - [N22000287](SCR),TELANGANA	04/2010	337.49 -	- -	-	0/0
338	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
339	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
340	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
341	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-	0/0
342	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
343	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0
344	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-	0/0
345	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-	0/0
346	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-	0/0
347	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-	0/0
348	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
349	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
350	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-	0/0
351	JAGGAYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-	0/0
352	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-	0/0
353	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-	0/0
354	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-	0/0
	Total		149,205.72 -			0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
355	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,JAMMU AND KASHMIR	12/2003	166.27 -	03/2008 -	02/2008	0/0
356	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	11/2011	0/0
357	PUNE-SHOLAPUR,PKG1 - [N24000127]NHAI,MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
358	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012	0/0
359	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012	0/0
360	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013	0/0
361	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013	0/0
362	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	05/2013 -	05/2013	0/0
363	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013	0/0
364	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
365	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013	0/0
366	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013	0/0
367	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013	0/0
368	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014	0/0
369	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014	0/0
370	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	02/2014 -	02/2014	0/0
371	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	07/2009 -	04/2014	0/0
372	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	02/2009 -	05/2014	0/0
373	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 05/2014	05/2014	0/0
374	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	05/2014	0/0
375	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	06/2013 -	05/2014	0/0
376	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	05/2014	0/0
377	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
378	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014	0/0
379	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	05/2014 -	05/2014	0/0
380	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	09/2008 -	06/2014	0/0
381	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	11/2008 12/2014	06/2014	0/0
382	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	09/2008 -	06/2014	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
383	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	10/2008 -	06/2014	0/0
384	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	06/2008 -	06/2014	0/0
385	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	06/2014	0/0
386	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	09/2007 07/2011	06/2014	0/0
387	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	06/2014	0/0
388	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	05/2012 -	06/2014	0/0
389	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	10/2011 -	06/2014	0/0
390	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	06/2014	0/0
391	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	11/2012 -	06/2014	0/0
392	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	07/2013 -	06/2014	0/0
393	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	06/2013 -	06/2014	0/0
394	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	06/2014	0/0
395	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
396	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	08/2013 06/2014	06/2014	0/0
397	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	12/2013 -	06/2014	0/0
398	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	06/2014	0/0
399	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	06/2014	0/0
400	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	06/2014	0/0
401	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	06/2014	0/0
402	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
403	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
404	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
405	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	09/2013 -	07/2014	0/0
406	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	07/2014	0/0
407	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	07/2014	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
408	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, BIHAR	07/2012	356.40 -	07/2014 -	07/2014	0/0
409	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	07/2014 -	07/2014	0/0
410	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI, MULTI STATE	12/2003	232.45 -	09/2010 -	08/2014	0/0
411	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	08/2014	0/0
412	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	01/2014 -	08/2014	0/0
413	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	09/2014	0/0
414	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
415	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	04/2014 -	09/2014	0/0
416	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	09/2014 -	09/2014	0/0
417	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	10/2008 -	10/2014	0/0
418	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	05/2008 07/2014	10/2014	0/0
419	PANIPAT-ROHTAK - [N24000151]NHAI, HARYANA	04/2011	807.00 -	10/2014 -	10/2014	0/0
420	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	10/2014	0/0
421	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	01/2013 -	10/2014	0/0
422	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, MAHARASHTRA	04/2012	484.19 -	10/2014 -	10/2014	0/0
423	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, UTTAR PRADESH	10/2012	250.50 -	10/2014 -	10/2014	0/0
424	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI, MADHYA PRADESH	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
425	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	09/2007 03/2014	12/2014	0/0
426	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, ASSAM	12/2003	230.00 -	06/2005 -	12/2014	0/0
427	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 12/2014	12/2014	0/0
428	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 167.64	11/2008 12/2014	12/2014	0/0
429	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 200.00	04/2009 12/2014	12/2014	0/0
430	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	06/2008 -	12/2014	0/0
431	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	06/2008 -	12/2014	0/0
432	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 333.83	09/2007 -	12/2014	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
433	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	12/2014	0/0
434	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	02/2010 -	12/2014	0/0
435	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	10/2011 -	12/2014	0/0
436	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	03/2013 -	12/2014	0/0
437	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	11/2012 -	12/2014	0/0
438	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	12/2014	0/0
439	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	03/2013 -	12/2014	0/0
440	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	12/2014	0/0
441	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	12/2014	0/0
442	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	01/2014 -	12/2014	0/0
443	BAREILY-SITAPUR - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	12/2014	0/0
444	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	08/2013 -	12/2014	0/0
445	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	08/2013 -	12/2014	0/0
446	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	10/2013 -	12/2014	0/0
447	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	06/2014 -	12/2014	0/0
448	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	04/2008 01/2015	01/2015	0/0
449	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 01/2015	01/2015	0/0
450	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	01/2015	0/0
451	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	04/2008 01/2015	01/2015	0/0
452	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	02/2015	0/0
453	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	02/2015 -	02/2015	0/0
454	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	03/2015	0/0
455	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	03/2015	0/0
456	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	08/2013 -	03/2015	0/0
457	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	04/2015	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
458	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
459	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	02/2010 -	07/2015	0/0
460	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
461	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
462	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
463	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
464	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	10/2015 -	10/2015	0/0
465	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	11/2015	0/0
466	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
467	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2015	0/0
468	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	08/2013 -	12/2015	0/0
469	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	12/2015	0/0
470	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	04/2010 01/2016	01/2016	0/0
471	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
472	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
473	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	09/2016	0/0
474	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	11/2016	0/0
475	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-	0/0
476	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-	0/0
477	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-	0/0
478	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-	0/0
	Total		89,578.45 -			0/0
	SHIPPING AND PORTS					
479	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
480	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
481	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012	0/0
482	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
483	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012	0/0
484	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012	0/0
485	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013	0/0
486	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013	0/0
487	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
488	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]PORT TRUST,KERALA	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
489	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
490	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
491	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	02/2014 04/2014	04/2014	0/0
492	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014	0/0
493	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
494	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2015	0/0
495	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
496	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	TELECOMMUNICATIONS					
497	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB - [N26000041]BSNL,PUNJAB	02/2008	373.94 -	12/2008 -	12/2012	0/0
498	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE - [N26000088]BSNL,JHARKHAND	03/2008	328.13 -	03/2009 -	01/2013	0/0
499	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]BSNL,MADHYA PRADESH	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
500	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	06/2009 -	06/2014	0/0
501	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	06/2014	0/0

			(April 2014)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
502	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	09/2014	0/0
503	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	10/2010 03/2012	12/2014	0/0
504	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT - [N26000072]BSNL,MULTI STATE	12/2007	952.88 -	03/2010 -	-	0/0
505	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT - [N26000073]BSNL,MULTI STATE	12/2007	152.65 -	03/2010 -	-	0/0
506	GSM EQUIPMENT OF 200000LINES (2G) UP(WEST)PHASE V.2 TELECOM CIRCLE - [N26000082]BSNL,UTTAR PRADESH	10/2008	336.84 -	10/2009 -	-	0/0
	Total		5,079.29 -			0/0
	<u>URBAN DEVELOPMENT</u>					
507	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
508	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	03/2016 -	03/2016	0/0
509	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	02/2019	0/0
510	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		67,598.32 -			0/0
	<u>WATER RESOURCES</u>					
511	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		455,650.36			0/0

List of Ongoing Projects having Time and Cost Overrun w.r.t Original Schedule

(April 2014)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12	75
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77	23
	Total		335.61 -	23,335.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50	24
5	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
7	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	06/2014	49.09	60
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63	29
	Total		9,127.17 -	42,834.48				
	<u>PETROLEUM</u>							
10	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85	24
11	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29	27
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16	26
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00	12
14	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	04/2006 -	06/2016	536.46	122

(April 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
15	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25	21
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	09/2014	54.46	35
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	06/2015	67.62	44
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	06/2015	70.49	41
19	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	06/2012 -	06/2014	7.76	24
20	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63
21	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	12/2008 -	09/2014	15.50	69
22	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
23	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2014	84.68	45
24	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	05/2010 -	04/2014	54.27	47
25	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85	25
	Total		54,000.88 -	114,417.92				
	<u>POWER</u>							
26	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00	16
27	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
28	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	09/2015	41.49	72
29	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79
30	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	5,497.72	01/2016 -	11/2016	145.58	10
31	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	08/2014	17.85	46
32	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32	25
33	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
35	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14	48

(April 2014)									
					Date of Commissioning				
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)	
1	2	3	4	5	6	7	8	9	
36	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106	
37	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48	73	
38	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	09/2018	69.71	96	
39	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87	
	Total		42,009.56 -	175,964.34					
	<u>RAILWAYS</u>								
40	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	445.40	03/2007 03/2007	03/2015	1,317.57	96	
41	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	725.54	12/2010 -	03/2015	625.54	51	
42	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67	60	
43	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141	
44	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49	69	
45	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65	
46	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38	12	
47	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2015	23.36	9	
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	06/2014	282.96	243	
49	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66	
50	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03	31	
51	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.40	06/2004 -	03/2015	207.31	129	
52	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39	
53	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50	132	
54	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60	3	
55	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84	
56	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58	129	
57	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240	

(April 2014)									
					Date of Commissioning				
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)	
1	2	3	4	5	6	7	8	9	
58	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46	35	
59	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98	
60	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47	
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69	
62	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12	72	
63	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75	99	
64	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06	36	
65	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83	24	
66	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80	120	
67	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69	
68	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62	116	
69	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99	15	
70	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,114.91	03/2009 -	03/2017	205.13	96	
71	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181	
72	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24	33	
	Total		22,989.18 -	250,071.98					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
73	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2014	30.10	69	
74	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68	67	
75	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99	57	
76	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75	68	
77	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	333.83	09/2007 -	12/2014	57.47	87	

(April 2014)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	T.O.R (in months)
1	2	3	4	5	6	7	8	9
78	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25	69
79	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29	65
80	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93	63
81	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2014	33.70	81
	Total		2,038.62 -	253,021.33				
	<u>SHIPPING AND PORTS</u>							
82	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00	99
83	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93	2
84	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75	58
	Total		2,344.46 -	256,774.31				
	<u>STEEL</u>							
85	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	06/2014	100.63	69
86	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20	37
87	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	09/2014	41.41	59
88	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	07/2014	13.61	31
	Total		23,538.89 -	286,297.16				
	<u>TELECOMMUNICATIONS</u>							
89	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42	60
	Total		149.15 -	286,455.88				
	Grand Total		173,196.52	1,712,119.93				

List of Ongoing Projects having Cost Overrun w.r.t. to Original Schedule

(April 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		4,086.12 -	27,943.66			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	06/2014	49.09
7	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
8	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
9	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50
10	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	08/2014	34.63
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,767.76 -	48,131.30			
	<u>PETROCHEMICALS</u>						
14	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,460.61	57,051.30			
			-				
	<u>PETROLEUM</u>						
15	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82	2,735.65	04/2006	06/2016	536.46
			-		-		
16	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16	3,690.37	12/2008	09/2014	15.50
			-		-		
17	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40	2,920.82	09/2010	12/2015	25.71
			-		03/2012		
18	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78	6,000.00	08/2010	05/2014	84.68
			-		03/2012		
19	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03	8,813.41	05/2010	04/2014	54.27
			-		-		
20	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00	32,710.00	11/2012	12/2014	9.85
			-		-		
21	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68	312.00	01/2012	07/2013	30.72
			-		-		
22	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64	2,331.62	06/2012	06/2014	7.76
			-		-		
23	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR [N16000099	03/2009	234.78	317.64	09/2012	12/2014	35.29
			234.78		-		
24	WAX PROJECT - [N16000101	06/2010	576.60	676.05	12/2013	09/2015	17.25
			-		-		
25	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03	6,638.94	03/2013	11/2014	104.84
			-		-		
26	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63	2,665.65	03/2015	03/2015	29.42
			-		-		
27	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81	276.83	04/2012	06/2014	12.16
			-		-		
28	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00	701.00	11/2015	11/2015	5.26
			-		-		
29	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81	309.82	10/2014	10/2015	0.00
			-		-		
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00	1,038.00	10/2011	09/2014	54.46
			-		-		
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00	1,227.00	10/2011	06/2015	67.62
			-		-		
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00	1,693.00	01/2012	06/2015	70.49
			-		-		
33	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02	204.29	06/2012	06/2014	41.85
			-		-		
	Total		56,965.19	132,313.39			
			-				
	<u>POWER</u>						

(April 2014)

								Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)		
1	2	3	4	5	6	7	8		
34	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90		
35	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48		
36	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	09/2018	69.71		
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39		
38	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00		
39	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	09/2015	41.49		
40	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86		
41	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	08/2014	17.85		
42	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34		
43	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77		
44	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14		
45	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	5,497.72	01/2016 -	11/2016	145.58		
46	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31		
47	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59		
48	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10		
49	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32		
50	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00		
	Total		49,844.58 -	203,036.93					
	<u>RAILWAYS</u>								
51	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	06/2014	282.96		
52	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58		
53	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06		
54	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63		

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overrun (%)
1	2	3	4	5	6	7	8
55	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
56	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
57	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.18	- -	03/2015	1,810.82
58	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
59	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
60	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58
61	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
62	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
63	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	01/2013	337.26
64	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
65	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
66	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
67	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
68	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
69	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2015	332.51
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62
71	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
72	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	445.40	03/2007 03/2007	03/2015	1,317.57
73	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.40	06/2004 -	03/2015	207.31
74	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
75	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
76	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
77	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88

(April 2014)

								Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)		
1	2	3	4	5	6	7	8		
78	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67		
79	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	725.54	12/2010 -	03/2015	625.54		
80	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73		
81	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	05/2009	248.16		
82	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47		
83	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28		
84	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19		
85	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	06/2007	35.57		
86	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00		
87	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71		
88	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73		
89	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75		
90	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,176.10	12/2006 -	08/2010	202.58		
91	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48		
92	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67		
93	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92		
94	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	1,382.78	- -	-	902.01		
95	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55		
96	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82		
97	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	12/2014	324.33		
98	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06		
99	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33		

(April 2014)

								Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)		
1	2	3	4	5	6	7	8		
100	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12		
101	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57		
102	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04		
103	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57		
104	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76		
105	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32		
106	RAMGANJMUNDI-BHOPAL (NL).WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59		
107	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71		
108	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33		
109	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	09/2014	104.49		
110	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67		
111	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59		
112	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88		
113	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53		
114	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22		
115	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16		
116	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11		
117	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	02/2006 -	-	40.01		
118	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35		
119	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052	04/2003	98.74 -	337.30	- -	03/2012	241.60		
120	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053	03/2005	470.09 -	1,417.97	- -	03/2012	201.64		
121	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66		
122	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41		

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
123	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
124	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	- -	12/2012	166.63
125	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
126	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	407.98	- -	03/2014	161.53
127	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	- -	-	236.00
128	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	- -	-	79.82
129	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	- -	03/2018	115.17
130	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	- -	-	77.62
131	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
132	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
133	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24
134	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03
135	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
136	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06
137	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
138	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
139	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
140	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2014	81.45
141	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
142	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
143	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
144	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
145	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
146	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
147	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
148	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
149	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
150	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,114.91	03/2009 -	03/2017	205.13
151	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
152	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
153	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
154	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
155	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
156	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
157	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
158	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
159	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
160	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
161	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2015	23.36
162	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38
163	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60
164	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
165	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80

(April 2014)

								Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)		
1	2	3	4	5	6	7	8		
166	ATTIPPATTU-PUTTUR - [N22000184	04/2008	446.87 -	528.00	- -	-	18.16		
167	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	1,200.00	- -	-	129.22		
168	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17		
169	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188	04/1999	271.24 -	520.00	- -	-	91.71		
170	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39 -	1,280.83	- -	-	55.74		
171	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	346.15	- -	-	28.14		
172	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192	04/1999	175.43 -	247.75	- -	03/2014	41.22		
173	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80		
174	ERODE-PALANI - [N22000199	04/2008	288.57 -	603.22	- -	-	109.04		
175	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	-	173.71		
176	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	247.00 -	951.24	- -	12/2014	285.12		
177	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	222.95	- -	-	16.29		
178	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	165.82 -	545.64	- -	-	229.06		
179	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,327.78	- -	-	153.80		
180	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06		
181	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02		
182	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	697.00 -	2,501.05	- -	-	258.83		
183	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72		
184	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	182.06 -	184.06	- -	-	1.10		
185	PANVEL PEN DOUBLING - [N22000255	04/2006	191.00 -	260.16	- -	05/2014	36.21		
186	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26		
187	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97		
188	BAGALKOT-KUDACHI NL - [N22000258	04/2010	377.93 -	986.30	- -	-	160.97		

(April 2014)

								Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)		
1	2	3	4	5	6	7	8		
189	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42		
190	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25		
191	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41		
192	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09		
193	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65		
194	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93		
195	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29		
196	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00		
197	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10		
198	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14		
199	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07		
200	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38		
201	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46		
	Total		64,579.43 -	385,802.82					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
202	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2014	30.10		
203	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	03/2008 -	02/2008	16.14		
204	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	05/2014	28.93		
205	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75		
206	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68		
207	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	333.83	09/2007 -	12/2014	57.47		
208	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	04/2014	68.99		
209	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	309.56	04/2010 -	01/2016	42.25		
210	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29		

(April 2014)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
211	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2014	33.70
212	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2011	106.50
	Total		3,312.89 -	391,233.27			
	<u>SHIPPING AND PORTS</u>						
213	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003]	10/2005	800.00 -	1,571.60	10/2008 -		96.45
214	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
215	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
216	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
217	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
218	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
219	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
220	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
221	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	403,149.93			
	<u>STEEL</u>						
222	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	09/2014	41.41
223	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	01/2015	105.20
224	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	06/2014	100.63
225	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	07/2014	13.61
226	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	202.00 -	343.58	01/2010 -	11/2013	70.09
227	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	08/2006	260.00 -	349.64	12/2009 -	06/2013	34.48

(April 2014)

								Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)		
1	2	3	4	5	6	7	8		
228	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51		
229	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	06/2015 -	06/2015	8.40		
	Total		24,551.03 -	433,960.25					
	<u>TELECOMMUNICATIONS</u>								
230	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42		
231	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50		
232	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52		
	Total		1,393.98 -	435,441.70					
	<u>URBAN DEVELOPMENT</u>								
233	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53		
234	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX, MUMBAI - [N28000048]	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59		
	Total		6,509.18 -	447,223.78					
	<u>WATER RESOURCES</u>								
235	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64		
	Total		542.90 -	448,410.78					
	Grand Total		252,305.64	3,436,646.11					

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(April 2014)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
1	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 241.28	280.13	165.60	11/2008 12/2014	06/2014
	Total		155.04 -	280.13	165.60		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	291.18	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	291.18		
	<u>PETROLEUM</u>						
3	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	20.38	01/2016 -	12/2015
	Total		607.06 -	607.06	20.38		
	<u>POWER</u>						
4	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35 -	1,935.35	632.68	12/2014 -	11/2014
5	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	40.47	11/2016 -	03/2016
6	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	13.34	05/2016 -	04/2016
	Total		4,615.77 -	4,615.77	686.49		
	Grand Total		6,886.61	7,011.70	1,163.65		

List of Projects on schedule w.r.t. Latest Schedule

(April 2014)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	230.42	03/2015 -	03/2015
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		669.60 -	669.60	230.46		
	<u>COAL</u>						
3	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]	6/2008	1,188.31 -	7,612.33	747.82	03/2013 03/2023	03/2023
4	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	619.15	03/2016 03/2016	03/2016
5	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	227.23	03/2015 -	03/2015
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	160.06	03/2017 -	03/2017
7	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	50.46	03/2016 -	03/2016
8	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	90.56	03/2016 -	03/2016
10	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	5.43	06/2015 -	06/2015
11	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	55.25	03/2016 -	03/2016
12	MOONIDIH XV SEAM UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
13	MURADIDH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
14	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	29.03	03/2015 -	03/2015
15	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
16	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	25.00	03/2018 -	03/2018
17	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	219.03	03/2016 -	03/2016
19	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
20	AMRAPALI OC(12MTY) - [N06000103	2/2012	858.11 -	858.11	95.88	03/2020 -	03/2020
21	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.14 -	430.14	65.51	03/2016 -	03/2016
22	KALYANIKHANI OPENCASE PROJECT - [N06000101	7/2012	417.33 -	417.33	0.27	07/2016 -	07/2016
23	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	94.45	03/2015 -	03/2015
24	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
25	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	75.42	03/2015 -	03/2015
	Total		12,636.36 -	18,689.04	2,563.03		
	<u>PETROLEUM</u>						
26	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	3/2010	3,241.03 -	6,638.94	2,192.69	03/2013 11/2014	11/2014
27	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY [N16000175	3/2014	3,076.00 -	3,076.00	42.23	09/2017 -	09/2017
28	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE [N16000173	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
29	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
30	KOTA JOBNER PIPELINE PROJECT - [N16000170	4/2011	276.26 -	276.26	142.66	03/2015 -	03/2015
31	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161	3/2013	1,138.50 -	686.58	63.96	04/2015 -	04/2015
32	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
33	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159	9/2011	202.25 -	160.16	33.26	07/2016 -	07/2016
34	MOUNDED BULLET PROJECT AT CPCL - [N16000154	12/2012	279.00 -	279.00	69.71	12/2014 -	12/2014
35	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149	8/2011	586.00 -	586.00	165.89	08/2015 -	08/2015
36	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
37	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) [N16000182	10/2013	429.06 -	429.06	-	10/2014 -	10/2014
38	REVAMP OF UNMANNED PLATFORMS PH-II IN MH & NH ASSETS - [N16000181	3/2013	2,913.10 -	2,910.30	-	05/2016 -	05/2016

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
39	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	0.05	07/2016 -	07/2016
40	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
41	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	-	02/2016 -	02/2016
42	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,435.26	05/2015 -	05/2015
43	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	248.39	12/2014 -	12/2014
44	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	12.13	03/2015 -	03/2015
45	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	1,101.52	05/2014 -	05/2014
46	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	202.33	11/2015 -	11/2015
47	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	523.84	11/2015 -	11/2015
48	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	593.64	03/2015 -	03/2015
49	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	761.68	561.31	05/2013 06/2014	06/2014
	Total		40,759.38 -	43,071.13	8,481.36		
	<u>POWER</u>						
50	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	811.78	08/2013 09/2015	09/2015
51	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	1,026.27	10/2014 -	10/2014
52	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	43.17	06/2014 -	06/2014
53	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
54	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
55	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
56	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
58	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
59	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
60	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
61	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138	12/2012	156.04 -	156.04	37.56	10/2014 -	10/2014
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	222.89	03/2015 -	03/2015
63	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	980.00	08/2015 -	08/2015
64	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	2,443.00	11/2016 -	11/2016
65	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	2,392.00	09/2016 -	09/2016
66	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	3,814.00	12/2016 -	12/2016
67	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	624.48	11/2014 -	11/2014
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	315.22	11/2014 -	11/2014
69	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	609.80	08/2014 -	08/2014
70	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
71	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152	9/2013	680.69 -	680.69	33.49	03/2016 -	03/2016
72	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151	2/2013	11,638.55 -	11,638.55	1,118.00	09/2017 -	09/2017
73	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145	6/2012	1,909.24 -	1,909.24	400.43	06/2015 -	06/2015
74	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144	3/2013	2,514.88 -	2,514.88	29.65	12/2015 -	12/2015
75	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
76	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	7/2012	1,527.00 -	1,527.00	71.00	08/2017 -	08/2017

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
77	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,580.00	05/2017 -	05/2017
78	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	13.93	10/2014 -	10/2014
79	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
80	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	176.06	08/2014 -	08/2014
81	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	218.57	08/2014 -	08/2014
82	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	655.12	01/2015 -	01/2015
83	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	741.43	02/2015 -	02/2015
84	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	1/2011	913.63 -	913.63	573.22	07/2006 12/2015	12/2015
85	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	1,381.55	08/2014 -	08/2014
	Total		84,513.33 -	85,067.72	20,312.62		
	<u>RAILWAYS</u>						
86	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	114.41	02/2015 -	02/2015
87	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.67	03/2017 -	03/2017
88	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
89	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	14.68	03/2015 -	03/2015
90	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.32	02/2019 -	02/2019
91	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
92	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	100.00	03/2016 -	03/2016
93	HIMMATNAGAR - UDAIPUR GAUGE CONVERSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	56.08	03/2015 -	03/2015
94	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	441.08	03/2016 -	03/2016

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	417.81	03/2016 -	03/2016
96	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	4/2006	325.00 -	1,116.53	283.53	03/2010 03/2017	03/2017
	Total		15,847.87 -	21,352.06	1,596.60		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
97	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	122.40	04/2009 12/2014	12/2014
98	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279	12/2003	167.64 -	167.64	109.80	11/2008 12/2014	12/2014
99	GUWHATI TO NALBARI (AS-4) - [N24000038	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	01/2015
100	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281	12/2003	200.00 -	200.00	193.50	04/2009 12/2014	12/2014
101	SONAPUR TO GUWAHTI (AS-3) - [N24000044	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	01/2015
102	NALBARI TO BIJNI (AS-6) - [N24000047	12/2003	225.00 -	225.00	258.40	06/2008 05/2014	05/2014
103	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	258.40	04/2010 01/2016	01/2016
104	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	2,024.00	08/2013 06/2014	06/2014
105	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
106	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	262.40	11/2016 -	11/2016
107	4-LANING OF ROHATAK JIND (LENGTH 45 KM) - [N24000231	10/2013	283.25 -	283.25	183.90	10/2015 -	10/2015
108	BARSAT-KRISHNANAGAR - [N24000229	8/2012	867.00 -	867.00	598.60	02/2015 -	02/2015
109	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
110	REENGUS SIKAR - [N24000227	3/2012	333.51 -	333.51	264.60	09/2014 -	09/2014
111	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226	10/2011	1,565.00 -	1,565.00	1,293.00	10/2014 -	10/2014
112	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225	3/2012	828.00 -	828.00	662.80	09/2014 -	09/2014
113	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	470.90	04/2015 -	04/2015
114	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	100.30	12/2015 -	12/2015

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
115	2 LANING WITH PS KANPUR KABRAI - [N24000221	1/2013	373.47 -	373.47	263.80	07/2014 -	07/2014
116	2 LANING WITH PS AGRA ALIGARH - [N24000220	10/2012	250.50 -	250.50	347.90	10/2014 -	10/2014
117	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	808.10	09/2015 -	09/2015
118	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	423.00	08/2015 -	08/2015
119	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	334.70	06/2015 -	06/2015
120	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI [N24000211	7/2012	356.40 -	356.40	45.35	07/2014 -	07/2014
121	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	284.60	10/2014 -	10/2014
122	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	678.20	07/2014 -	07/2014
123	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,602.00	09/2014 -	09/2014
124	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR [N24000205	12/2011	1,047.00 -	1,047.00	267.30	06/2014 -	06/2014
125	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	2,043.00	06/2014 -	06/2014
126	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	962.50	05/2014 -	05/2014
127	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014
128	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	254.30	06/2014 -	06/2014
129	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 [N24000183	11/2011	1,535.00 -	1,535.00	1,328.00	05/2014 -	05/2014
130	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
131	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	208.00	290.60	04/2008 01/2015	01/2015
132	GUWAHATI TO NALBARI (AS-5) - [N24000046	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	01/2015
	Total		31,338.34 -	31,615.61	19,562.18		
	<u>SHIPPING AND PORTS</u>						
133	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	139.80	03/2006 06/2014	06/2014
134	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	427.54	02/2014 04/2014	04/2014

(April 2014)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
135	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		1,628.33 -	2,106.69	674.06		
	<u>STEEL</u>						
136	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	1/2007	295.89 -	607.17	370.58	12/2011 01/2015	01/2015
137	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]	4/2011	572.00 -	572.00	379.86	04/2013 09/2014	09/2014
138	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]	2/2011	898.55 -	898.55	292.64	05/2013 01/2015	01/2015
139	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]	7/2012	332.65 -	332.65	103.67	08/2014 -	08/2014
140	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	6/2012	237.09 -	254.90	34.15	12/2014 -	12/2014
141	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	83.98	06/2015 -	06/2015
142	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]	10/2012	160.48 -	160.48	18.86	09/2014 -	09/2014
143	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	8.73	05/2016 -	05/2016
	Total		3,055.38 -	3,410.77	1,292.47		
	<u>URBAN DEVELOPMENT</u>						
144	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,365.81	03/2016 -	03/2016
145	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	8,365.81		
	Grand Total		255,438.73	270,972.76	63,078.59		

List of Delayed Projects w.r.t. Latest Schedule

(April 2014)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	17,562.00	12/2008 -	03/2015	75	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 -	5,677.00	4,564.17	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	4,551.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	2,933.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	29,610.17				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	278.88	05/2012 -	04/2014	23	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	-	03/2014 -	10/2014	7	-
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	269.55	01/2011 04/2013	12/2016	71	44
	Total		989.35 -	1,042.27	548.43				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	2,918.33	06/2009 -	06/2014	60	-
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,225.89	03/2012 -	08/2014	29	-
10	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,197.33	03/2013 09/2012	03/2015	24	30
11	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	-
12	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	116.72	03/2013 -	03/2015	24	-
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	120.15	03/2013 -	03/2015	24	-
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	221.35	03/2012 -	03/2015	36	-
15	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	35.35	03/2012 -	03/2015	36	-
16	PURNADIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND	07/2008	210.98 -	210.98	120.97	03/2013 -	03/2015	24	-
17	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,644.36	03/2014 -	03/2016	24	-
18	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,439.04	03/2014 -	03/2016	24	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44	-
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	131.41	03/2010 -	03/2016	72	-
21	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	273.86	03/2014 -	03/2016	24	-
22	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	101.83	12/2012 -	03/2016	39	-
23	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	33.46	03/2014 -	03/2016	24	-
24	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.43	03/2014 -	03/2016	24	-
25	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	126.88	03/2012 -	03/2016	48	-
26	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
27	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	214.19	03/2014 -	03/2016	24	-
28	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60	-
29	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	139.29	03/2012 -	03/2016	48	-
30	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	118.59	03/2010 -	03/2017	84	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	36.52	03/2011 -	03/2017	72	-
32	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
33	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	59.08	03/2012 -	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	340.71	12/2015 -	04/2018	28	-
	Total		23,791.24 -	27,738.99	14,703.90				
	<u>STEEL</u>								
35	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,634.39	12/2011 -	05/2014	29	-
36	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	160.73	09/2008 12/2013	06/2014	69	6
37	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,WEST BENGAL	06/2008	14,443.00 -	16,408.00	15,862.37	12/2011 -	07/2014	31	-
38	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	309.45	09/2009 05/2012	07/2014	58	26
39	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	124.72	10/2013 -	08/2014	10	-
40	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,804.62	10/2009 10/2012	09/2014	59	23
41	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,055.89	03/2013 -	09/2014	18	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,156.60	12/2012 -	12/2014	24	-
43	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	12,638.44	03/2013 -	03/2015	24	-
44	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	104.16	11/2013 -	06/2015	19	-
	Total		62,441.88 -	68,084.56	57,851.37				
	<u>PETROLEUM</u>								
45	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, MAHARASHTRA	10/2007	5,713.03 8,813.41	8,813.41	7,920.81	05/2010 03/2013	04/2014	47	13
46	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, MAHARASHTRA	01/2009	7,133.39 -	6,855.93	5,719.76	09/2012 -	04/2014	19	-
47	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,847.61	08/2010 03/2012	05/2014	45	26
48	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, MAHARASHTRA	06/2007	1,436.21 1,456.96	1,436.21	1,165.53	07/2010 05/2012	05/2014	46	24
49	FIRE WATER NETWORK AT URAN - [N16000141]ONGC, MAHARASHTRA	05/2010	171.68 -	171.68	96.43	06/2013 -	05/2014	11	-
50	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, MULTI STATE	01/2010	2,163.64 2,331.62	2,331.62	2,182.31	06/2012 -	06/2014	24	-
51	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 288.04	253.66	210.07	08/2012 -	06/2014	22	-
52	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, MULTI STATE	08/2010	8,140.00 -	8,140.00	6,521.61	02/2014 -	06/2014	4	-
53	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN, KARNATAKA	05/2009	1,803.78 -	1,803.78	946.17	07/2012 -	06/2014	23	-
54	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN, KARNATAKA	08/2008	12,412.00 -	12,160.26	11,362.40	01/2012 -	06/2014	29	-
55	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL, MAHARASHTRA	08/2009	246.81 -	276.83	262.43	04/2012 -	06/2014	26	-
56	GAS TURBINE GENERATION SET - [N18000146]OIL, ASSAM	07/2009	216.88 -	216.88	177.92	10/2011 -	06/2014	32	-
57	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 -	204.29	154.08	06/2012 -	06/2014	24	-
58	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	34	28
59	102 MW WIND POWER PROJECT - [N16000119]ONGC, RAJASTHAN	07/2010	1,106.00 -	678.02	113.00	06/2012 -	07/2014	25	-
60	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, MAHARASHTRA	08/2006	3,195.16 3,690.37	3,690.37	3,068.29	12/2008 04/2013	09/2014	69	17
61	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	165.71	08/2013 -	09/2014	13	-
62	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR, ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	951.32	10/2011 -	09/2014	35	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
63	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	135.79	06/2014 -	09/2014	3	-
64	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
65	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	32,710.00	25,442.00	11/2012 -	12/2014	25	-
66	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,MAHARASHTRA	03/2009	3,284.00 2,174.00	2,174.00	1,881.89	09/2011 05/2012	12/2014	39	31
67	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	449.94	09/2011 -	12/2014	39	-
68	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR - [N16000099]ONGC,GUJARAT	03/2009	234.78 234.78	317.64	102.78	09/2012 -	12/2014	27	-
69	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	102.80	09/2012 -	12/2014	27	-
70	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
71	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	93.04	09/2013 -	02/2015	17	-
72	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 03/2014	03/2015	24	12
73	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.42	03/2012 -	03/2015	36	-
74	CONSTRUCTION OF ONE ETP AT GGS-NADA, ANKLESHWAR - [N16000134]ONGC,GUJARAT	10/2011	200.69 -	200.69	11.56	07/2014 -	03/2015	8	-
75	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	86.03	03/2014 -	03/2015	12	-
76	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	468.42	12/2014 -	03/2015	3	-
77	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	247.67	05/2014 -	05/2015	12	-
78	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	829.83	10/2011 -	06/2015	44	-
79	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,178.42	01/2012 -	06/2015	41	-
80	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	969.70	09/2012 -	08/2015	35	-
81	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 -	676.05	519.57	12/2013 -	09/2015	21	-
82	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 -	309.82	67.83	10/2014 -	10/2015	12	-
83	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	10/2015	10	-
84	CONSTRUCTION OF THREE ETPS, MEHSANA - [N16000135]ONGC,GUJARAT	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2015	12	-
85	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,MAHARASHTRA	01/2007	2,323.40 2,920.82	2,920.82	1,915.45	09/2010 03/2012	12/2015	63	45
86	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	992.74	01/2014 -	12/2015	23	-
88	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	120.36	07/2015 -	12/2015	5	-
89	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 -	14,225.00	2,067.10	12/2015 -	05/2016	5	-
90	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 2,735.65	2,735.65	2,728.25	04/2006 06/2012	06/2016	122	48
91	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
92	AHMEDABAD REDEVELOPMENT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	784.46	12/2014 -	12/2016	24	-
93	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2016	24	-
94	MEHESANA REDEVELOPMENT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.07	04/2015 -	03/2017	23	-
95	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND ETP AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	374.56 -	374.56	10.60	09/2012 -	03/2017	54	-
	Total		136,989.37 -	147,862.91	95,102.80				
	<u>POWER</u>								
96	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	657.74	11/2012 -	05/2014	18	-
97	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	483.79	09/2010 -	06/2014	45	-
98	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	31	-
99	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,322.56	08/2012 -	06/2014	22	-
100	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	176.79	06/2012 -	06/2014	24	-
101	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	987.66	12/2013 -	06/2014	6	-
102	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,MADHYA PRADESH	08/2011	425.51 -	425.51	374.82	10/2013 -	06/2014	8	-
103	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	402.60	02/2014 -	06/2014	4	-
104	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	117.44	03/2014 -	06/2014	3	-
105	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,HIMACHAL PRADESH	10/2005	2,304.56 -	2,716.00	2,349.46	10/2010 -	08/2014	46	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
106	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 -	2,580.90	2,117.11	08/2012 -	09/2014	25	-
107	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,507.24	03/2013 -	09/2014	18	-
108	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,412.45	05/2014 -	09/2014	4	-
109	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	282.42	06/2014 -	09/2014	3	-
110	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	148.12	01/2014 -	09/2014	8	-
111	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	951.48	745.55	07/2013 -	11/2014	16	-
112	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,359.35	12/2013 -	11/2014	11	-
113	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	985.29	08/2012 -	12/2014	28	-
114	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,086.80	12/2013 -	12/2014	12	-
115	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,029.02	04/2013 -	12/2014	20	-
116	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,391.47	03/2014 -	12/2014	9	-
117	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,282.36	09/2014 -	12/2014	3	-
118	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,798.33	07/2014 -	12/2014	5	-
119	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,472.00	08/2013 -	03/2015	19	-
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,868.48	10/2012 -	03/2015	29	-
121	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,065.97	11/2012 -	03/2015	28	-
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	379.82	07/2013 -	03/2015	20	-
123	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	245.81	11/2013 -	03/2015	16	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
124	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	5,886.00	04/2009 -	05/2015	73	-
125	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	337.63	08/2014 -	05/2015	9	-
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	79.92	04/2015 -	05/2015	1	-
127	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	8,056.80	08/2013 -	06/2015	22	-
128	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP & BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,696.00	12/2012 -	06/2015	30	-
129	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	68.10	01/2013 -	06/2015	29	-
130	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,206.46	11/2013 -	06/2015	19	-
131	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	826.23	11/2012 -	06/2015	31	-
132	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	963.76	08/2014 -	06/2015	10	-
133	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,470.41	10/2014 -	06/2015	8	-
134	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,501.75	1,491.81	09/2009 -	09/2015	72	-
135	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	470.75	01/2015 -	12/2015	11	-
136	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	1,649.59	06/2015 -	12/2015	6	-
137	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC, ASSAM	01/2008	4,375.35 -	4,375.35	4,481.00	07/2011 -	08/2016	61	-
138	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	-	08/2014 -	08/2016	24	-
139	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	2,238.67 3,642.04	5,497.72	3,331.00	01/2016 -	11/2016	10	-
140	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTAR PRADESH	07/2006	1,657.00 2,978.86	2,978.86	700.96	07/2010 02/2016	02/2017	79	12
141	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	2,816.40	12/2009 06/2016	03/2017	87	9
142	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	9,959.00	12/2009 -	03/2017	87	-
143	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 -	3,846.30	2,091.00	03/2013 -	03/2017	48	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
144	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,439.96	09/2009 -	07/2018	106	-
145	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	483.40	07/2014 -	07/2018	48	-
146	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	10,667.00	6,839.53	09/2010 -	09/2018	96	-
147	RAMPUR HEP(412 MW) - [N18000024]SJVNL,HIMACHAL PRADESH	01/2007	2,047.03 -	2,047.03	3,115.91	01/2012 -	09/2014	32	-
	Total		134,445.30 -	153,427.77	106,673.79				
	<u>RAILWAYS</u>								
148	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	585.09	03/1994 -	06/2014	243	-
149	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	146.95 -	171.02	141.84	06/2013 -	06/2014	12	-
150	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	307.18	02/2009 02/2009	08/2014	66	66
151	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	279.04	03/2009 03/2009	08/2014	65	65
152	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	226.04	12/2008 -	09/2014	69	-
153	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	10/2014	31	10
154	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 495.44	1,814.48	369.66	03/2004 12/2010	12/2014	129	48
155	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	400.84	12/2009 03/2011	12/2014	60	45
156	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 2,363.00	2,363.00	1,343.55	03/2009 12/2012	12/2014	69	24
157	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER,WEST BENGAL	04/1999	207.52 207.52	207.52	198.85	12/2012 -	12/2014	24	-
158	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	-
159	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]RE,WEST BENGAL	04/1974	31.42 393.46	445.40	179.99	03/2007 03/2007	03/2015	96	96
160	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 194.07	596.40	372.92	06/2004 -	03/2015	129	-
161	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	100.00 492.98	725.54	445.74	12/2010 12/2010	03/2015	51	51
162	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	267.13	06/2013 06/2013	03/2015	21	21
163	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 2,921.00	2,921.00	2,075.62	10/2007 12/2012	12/2015	98	36
164	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	795.45	03/2010 -	12/2015	69	-
165	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	57.10	03/2015 -	12/2015	9	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
166	KATAKHAL TO BHAIRABI - [N22000126]NEFR, ASSAM	04/1998	227.90 227.90	331.40	137.78	12/2012 -	03/2016	39	-
167	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	388.67	77.88	12/2015 -	03/2016	3	-
168	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP, TELANGANA	04/2012	632.68 -	816.55	17.40	04/2012 -	03/2016	47	-
169	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,074.45	457.52	06/2005 07/2011	06/2016	132	59
170	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	84.44	03/2016 -	06/2016	3	-
171	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	479.18	03/2005 12/2008	12/2016	141	96
172	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 5,300.00	6,213.84	1,739.04	03/2014 03/2016	12/2016	33	9
173	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	2,483.04	1,575.90	12/2008 -	03/2017	99	-
174	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, MANIPUR	04/2003	727.56 727.53	5,996.00	2,152.99	03/2011 03/2014	03/2017	72	36
175	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, TRIPURA	04/2008	813.34 813.34	1,741.00	562.77	03/2014 -	03/2017	36	-
176	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, MIZORAM	04/2008	619.34 -	2,393.48	171.82	04/2014 -	03/2017	35	-
177	SEVOK RANGPO, NEFR - [N22000102]NEFR, SIKKIM	04/2008	1,339.48 -	3,375.42	84.67	12/2015 -	03/2017	15	-
178	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 850.00	2,446.57	9.23	03/2015 -	03/2017	24	-
179	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR, ASSAM	04/1996	1,676.31 1,676.31	5,114.91	4,142.69	03/2009 -	03/2017	96	-
180	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,242.25	959.41	03/2007 -	03/2017	120	-
181	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181	-
182	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201]NEFR, ASSAM	09/1997	1,000.00 1,500.00	4,996.19	3,118.65	04/2008 03/2014	12/2017	116	45
	Total		25,765.16 -	76,092.09	33,410.69				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
183	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 331.23	331.23	131.30	07/2009 -	04/2014	57	-
184	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	361.00	301.80	02/2009 -	05/2014	63	-
185	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	05/2014	15	-
186	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	05/2014	11	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
187	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	145.80	05/2013 -	05/2014	12	-
188	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	171.80	09/2008 -	06/2014	69	-
189	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	519.10	09/2008 -	06/2014	69	-
190	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	283.30	10/2008 -	06/2014	68	-
191	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	311.60	06/2008 -	06/2014	72	-
192	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	267.10	06/2008 -	06/2014	72	-
193	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	278.40	09/2007 07/2011	06/2014	81	35
194	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	661.80	05/2010 -	06/2014	49	-
195	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	06/2014	25	-
196	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	06/2014	34	-
197	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2014	32	-
198	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	06/2014	13	-
199	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,184.00	11/2012 -	06/2014	19	-
200	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	720.60	07/2013 -	06/2014	11	-
201	MURADABAD-BAREILLY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,230.00	06/2013 -	06/2014	12	-
202	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	598.40	05/2013 -	06/2014	13	-
203	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,007.00	07/2013 -	06/2014	11	-
204	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	06/2014	6	-
205	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,258.00	12/2013 -	06/2014	6	-
206	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	646.20	01/2014 -	06/2014	5	-
207	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	858.00	03/2014 -	06/2014	3	-
208	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,177.00	11/2013 -	06/2014	7	-
209	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	07/2014	10	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
210	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	567.10	07/2012 -	07/2014	24	-
211	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	309.10	09/2010 -	08/2014	47	-
212	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,398.00	09/2012 -	08/2014	23	-
213	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	08/2014	16	-
214	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	429.00	01/2014 -	08/2014	7	-
215	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11	-
216	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	431.70	04/2014 -	09/2014	5	-
217	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	372.40	10/2008 -	10/2014	72	-
218	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.20	05/2008 07/2014	10/2014	77	3
219	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	856.40	07/2013 -	10/2014	15	-
220	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	10/2014	21	-
221	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	157.47	260.60	09/2007 03/2014	12/2014	87	9
222	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.00	06/2005 -	12/2014	114	-
223	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	266.60	06/2008 -	12/2014	78	-
224	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	304.60	06/2008 -	12/2014	78	-
225	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	333.83	118.90	09/2007 -	12/2014	87	-
226	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-
227	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,116.00	02/2010 -	12/2014	58	-
228	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	-
229	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	879.90	03/2013 -	12/2014	21	-
230	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	62.32	11/2012 -	12/2014	25	-
231	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,207.00	03/2013 -	12/2014	21	-
232	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	812.80	03/2013 -	12/2014	21	-
233	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	314.60	04/2014 -	12/2014	8	-

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
234	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	824.40	07/2013 -	12/2014	17	-
235	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
236	BAREILY-SITAPUR - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	375.20	09/2013 -	12/2014	15	-
237	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	1,607.00	08/2013 -	12/2014	16	-
238	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	1,523.00	08/2013 -	12/2014	16	-
239	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	309.90	10/2013 -	12/2014	14	-
240	PANVEL-INDAPUR - [N24000216]NHAI, MULTI STATE	12/2011	942.69 -	942.69	265.40	06/2014 -	12/2014	6	-
241	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI, TAMIL NADU	09/2011	485.00 -	485.00	338.30	08/2013 -	02/2015	18	-
242	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	154.60	08/2012 -	03/2015	31	-
243	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	1,038.00	03/2014 -	03/2015	12	-
244	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19	-
245	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65	-
246	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,642.00	08/2014 -	07/2015	11	-
247	PANKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	1,410.00	645.00	09/2014 -	10/2015	13	-
248	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, KERALA	04/2011	682.00 -	682.00	517.90	10/2013 -	11/2015	25	-
249	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	754.00	586.90	03/2013 -	12/2015	33	-
250	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	325.10	08/2013 -	12/2015	28	-
251	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	291.36	133.50	01/2014 -	12/2015	23	-
252	NASHRI CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	472.90	06/2015 -	05/2016	11	-
253	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,135.00	07/2015 -	06/2016	11	-
	Total		51,745.11 -	52,228.87	46,735.46				
	<u>SHIPPING AND PORTS</u>								
254	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,005.88	12/2010 09/2012	10/2015	58	37
	Total		1,228.00 -	2,158.16	1,005.88				

(April 2014)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>TELECOMMUNICATIONS</u>								
255	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	84.81	06/2009 -	06/2014	60	-
256	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	37	-
257	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	183.16	01/2009 -	09/2014	68	-
258	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2014	50	33
	Total		2,018.15 -	1,843.90	548.69				
	<u>URBAN DEVELOPMENT</u>								
259	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	649.89	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	649.89				
	Grand Total		482,349.56	579,699.52	386,841.07				

List of ongoing projects having cost overrun w.r.t. to revised schedule

(April 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	03/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,593.13	05/2011 -	03/2013	33.49
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	04/2014	15.77
	Total		2,278.12 -	25,928.66			
	<u>COAL</u>						
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		1,431.79 -	27,645.25			
	<u>PETROCHEMICALS</u>						
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	36,565.25			
	<u>PETROLEUM</u>						
10	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2014	84.68
11	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	11/2012 -	12/2014	9.85

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
12	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070]	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
13	CONSTRUCTION OF SIX EFFLUENT TREATMENT PLANTS (ETP), AHMEDABAD AND ANKLESWAR [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	12/2014	35.29
14	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	09/2015	17.25
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	06/2014	12.16
16	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	10/2014 -	10/2015	0.00
17	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	06/2014	41.85
	Total		34,776.48 -	77,371.88			
	<u>POWER</u>						
18	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
19	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	09/2018	69.71
20	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39
21	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
22	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	09/2015	41.49
23	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
24	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	08/2014	17.85
25	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2017	29.14
26	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	5,497.72	01/2016 -	11/2016	145.58
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
28	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
29	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
30	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	09/2014	9.32
31	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	951.48	07/2013 -	11/2014	126.00

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		41,881.14 -	135,737.49			
	<u>RAILWAYS</u>						
32	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
33	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
34	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
35	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
36	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.18	- -	03/2015	1,810.82
37	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
38	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
39	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58
40	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
41	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	01/2013	337.26
42	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
43	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	10/2012	414.30
44	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
45	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
46	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2015	332.51
47	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2017	399.62
48	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2014	195.55
49	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	445.40	03/2007 03/2007	03/2015	1,317.57
50	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.40	06/2004 -	03/2015	207.31
51	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
52	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
54	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
55	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	725.54	12/2010 -	03/2015	625.54
56	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
57	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	05/2009	248.16
58	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	06/2007	35.57
59	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	900.00	- -	-	800.00
60	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,122.00	- -	03/2013	300.71
61	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75
62	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,176.10	12/2006 -	08/2010	202.58
63	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
64	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	1,382.78	- -	-	902.01
65	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
66	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	740.00	03/2012 -	12/2012	287.82
67	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	12/2014	324.33
68	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
69	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
70	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2017	724.12
71	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
72	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
73	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
74	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
75	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
76	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
77	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
78	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
79	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	- -	-	11.53
80	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
81	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
82	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
83	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	02/2006 -	-	40.01
84	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
85	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052	04/2003	98.74 -	337.30	- -	03/2012	241.60
86	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
87	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
88	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	404.19 -	1,383.45	- -	-	242.28
89	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	914.98	- -	12/2012	166.63
90	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082	12/2006	170.00 -	485.00	03/2011 -	03/2011	185.29
91	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083	09/1996	156.00 -	407.98	- -	03/2014	161.53
92	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	125.00 -	420.00	- -	-	236.00
93	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	456.00 -	820.00	- -	-	79.82
94	NEW B.G. LINE FROM TETELIA TO BYRNIAH (NATIONAL PROJECT), NEFR - [N22000086	09/2006	200.00 -	430.33	- -	03/2018	115.17
95	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	300.00 -	532.87	- -	-	77.62
96	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
97	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,213.84	03/2014 -	12/2016	17.24
98	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	03/2012 -	10/2014	44.03

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
99	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	06/2016	265.50
100	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06
101	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2017	286.46
102	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
103	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	03/2017	151.99
104	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2014	81.45
105	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
106	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
107	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
108	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	484.61	03/2012 -	-	52.28
109	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2017	187.83
110	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
111	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,114.91	03/2009 -	03/2017	205.13
112	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
113	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
114	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
115	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITSURGARH- UDAIPUR - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
116	RATANGARH-SARDARSAHAR (MM OF SADULPUR- BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
117	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
118	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
119	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2015	23.36
120	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	06/2014	16.38

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
121	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
122	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
123	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
124	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
125	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
126	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
127	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
128	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
129	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
130	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2017	38.80
131	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
132	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
133	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	12/2014	285.12
134	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
135	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	545.64	- -	-	229.06
136	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,327.78	- -	-	153.80
137	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
138	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
139	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	697.00 -	2,501.05	- -	-	258.83
140	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
141	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	182.06 -	184.06	- -	-	1.10
142	PANVEL PEN DOUBLING - [N22000255]	04/2006	191.00 -	260.16	- -	05/2014	36.21
143	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
144	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
145	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
146	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
147	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
148	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
149	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
150	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
151	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
152	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
153	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
154	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
155	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
156	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
157	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
158	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
	Total		55,806.96 -	291,241.61			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
159	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2014	30.10
160	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	03/2008 -	02/2008	16.14
161	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75
162	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68
163	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29
164	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2014	33.70
165	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	11/2011	106.50

(April 2014)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		2,407.28 -	295,336.44			
	<u>SHIPPING AND PORTS</u>						
166	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	10/2015	75.75
167	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
168	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
169	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
170	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	04/2014	2.93
171	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		4,174.13 -	301,278.14			
	<u>STEEL</u>						
172	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	07/2014	13.61
173	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]	06/2012	237.09 -	254.90	12/2014 -	12/2014	7.51
174	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	339.35	06/2015 -	06/2015	8.40
	Total		14,993.14 -	318,280.39			
	<u>TELECOMMUNICATIONS</u>						
175	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	06/2014	6.42
176	GSM EQUIPMENT OF 799000 LINES (2G) 101000 LINES 3(G) JHARKHAND PHASE V.1 TELECOM CIRCLE - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
177	GSM EQUIPMENT OF 1625000 LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	319,761.84			
	<u>URBAN DEVELOPMENT</u>						

(April 2014)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
178	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
	Total		6,395.00 -	331,370.84			
	<u>WATER RESOURCES</u>						
179	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	332,557.84			
	Grand Total		188,204.53	2,516,022.63			
