

दुनह; {k= dh ifj;ktukvk
CENTRAL SECTOR PROJECTS

₹150 djkm vkj vf/kd ykxr okyh

(₹ 150 Crore and above)

354oh ँYk'k fjikV@354 Flash Report

vij] 2015@April, 2015



d".kk xknkojh cf lu
Krishna Godavari basin



Hkkjr ljdkj / Government of India

lkf[; dh vkj dk; Øe dk; kUo; u e=ky;

Ministry of Statistics and Programme Implementation

vk/kkjh lijpu vkj ifj;ktuk i;ck/ku iHkkx
Infrastructure and Project Monitoring Division

ljnkj iV;y Hkou] liln ekx]

Sardar Patel Bhavan, Sansad Marg,

ub] fnYyh / New Delhi-110001

oc lkbV / Website- www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministrial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents	
	Pages
Executive Summary Hindi	2-20
Executive Summary English	21-35
Month wise List of Completed Projects Costing Rs. 150 crore and above during 2015-2016	36-36
Summary of projects	37-51
Graphical Presentation of All Projects	52-65
Sector wise Analysis of Projects	66-101
Sector wise Graph	102-115
Annexures	116-116
Status of central sector projects costing Rs.150 Crore and above	117-117
List of projects in which expenditure is more than approved cost	118-127
Details of Projects Without Date of Commissioning	128-140
List of projects without original Date of Commissioning	141-142
Details of On Schedule Projects w.r.t. Original Schedule	143-148
Details of Projects Ahead of Schedule w.r.t. Original Schedule	149-149
Details of Delayed Projects w.r.t. Original and Revised Schedule	150-181
Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule	182-193
Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule	193-198
Details Of Central Sector Projects Showing Time Overruns of 6 Months and More	199-213
Details of Central Sector Projects Showing Cost Overruns of More Than Rs. 100 Crore	214-223
Details Of Central Sector Projects Showing Time Overruns of 6 Months And More And Cost Overruns of Rs.100 Crore And Above	224-228
List of ongoing projects having cost overrun w.r.t. to revised schedule	229-238
List of Delayed Projects w.r.t. Latest Schedule	239-253
List of Projects Ahead of Schedule w.r.t. Latest Schedule	254-254
List of Projects on schedule w.r.t. Latest Schedule	255-262

कार्यकारी सारांश

1. अप्रैल, 2015 की फ्लैश रिपोर्ट में ₹ 150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 758 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अप्रैल, 2015 के दौरान 2 परियोजनाओं (पेट्रोलियम तथा सड़क परिवहन एवं राजमार्ग प्रत्येक क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 758 परियोजनाओं में से, 323 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 63 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 63 परियोजनाओं में से, 30 परियोजनाएं ₹1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं (सं.)	मूल समय-सारणी की तुलना में विलंबित परियोजनाएं (सं.)	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं (सं.)	अतिरिक्त विलंबित बड़ी परियोजनाएं (सं.)
1.	रेलवे	288	32	1	1
2.	सड़क परिवहन एवं राजमार्ग	133	99	14	8
3.	विद्युत	112	63	22	15
4.	पेट्रोलियम	71	46	12	3
5.	कोयला	73	41	11	3
6.	शहरी विकास	30	16	0	0
7.	इस्पात	26	16	1	0
8.	नागर विमानन	7	4	2	0
9.	पोत परिवहन एवं पत्तन	6	0	0	0
10.	परमाणु ऊर्जा	4	3	0	0
11.	दूरसंचार	4	1	0	0
12.	उर्वरक	1	0	0	0
13.	खदान	1	0	0	0
14.	पेट्रोसायन	1	1	0	0
15.	भारी उद्योग	1	1	0	0
कुल		758	323	63	30

3. 758 परियोजनाओं के कार्यान्वयन की कुल मूल लागत ₹10,69,127.84 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ₹12,78,256.35 करोड़ होने की संभावना है, जो ₹2,09,128.51 करोड़ (मूल लागत का 19.56%) की समग्र लागत वृद्धि को दर्शाता है। अप्रैल, 2015 तक इन परियोजनाओं पर किया गया व्यय ₹5,46,232.97 करोड़ है, जो परियोजनाओं की अनुमानित लागत का 42.73% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची
(30.04.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत(करोड़ रु.)	लागत वृद्धि(%)
परमाणु ऊर्जा					
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	62.57
2	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	31.12
नागर विमानन					
3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	15.77
4	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	12.18
5	चंडीगढ़ अंतराष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	8.19
कोयला					
6	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	478.50
7	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3477.21	71.23
8	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	50.37
9	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	34.63
10	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	31.87
भारी उद्योग					
11	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	122.78
पेट्रोरसायन					
12	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	80.08
पेट्रोलियम					
13	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	820.20

14	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	6100.00	87.76
15	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	75.35
16	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	70.49
17	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	67.62
विद्युत					
18	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	274.73
19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	159.38
20	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	159.15
21	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी)	09/2003	6285.33	15300.00	143.42
22	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.68	139.35
रेलवे					
23	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	3531.98
24	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2019.62
25	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	985.42
26	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	902.01
27	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
सड़क परिवहन एवं राजमार्ग					
28	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	92.75
29	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	363.74	85.58
30	हरंगाजो से मैबंग, 164.08 किमी. -190.587 किमी. एनएच-54	12/2003	212.00	386.10	82.12
31	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	80.68
32	ब्रह्मपुत्र ब्रिज एनएच सं.-31	12/2003	217.61	309.56	42.25
इस्पात					
33	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	42.39
34	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	41.41
शहरी विकास					
35	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	81.53

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीयसलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. पूर्ण रूप से लागतवृद्धि की अधिकतम प्रतिशतता वाली (अधिकतम संख्या में पांच) परियोजनाओं की क्षेत्र-वार सूची इस प्रकार है:-

**अधिकतम लागतवृद्धि (सीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30.04.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (रु. करोड़ में)	अनुमानित लागत (रु. करोड़ में)	लागतवृद्धि (रु. करोड़ में)
परमाणु ऊर्जा					
1	प्रोटोटाइप फास्ट ब्रीडर रिएक्टर (भाविनि, 500 एमडब्ल्यूई)	09/2003	3492.00	5677.00	2185.00
2	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	17270.00	4099.00
नागर विमानन					
3	नए अंतरराष्ट्रीय टर्मिनल भवन का निर्माण (गोवा)	05/2010	335.61	388.53	52.92
4	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	217.60	244.10	26.50
5	चंडीगढ़ अंतरराष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	452.00	489.00	37.00
कोयला					
6	अदरियाला शाफ्ट परियोजना	12/2009	212.34	1228.39	1016.05
7	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3477.21	1446.43
8	मगध ओसी 20 एमटीवाई (सीसीएल)	08/2008	469.78	706.40	236.62
9	तूतीकोरिन ताप विद्युत परियोजना 2X500 मेगावाट	05/2008	4904.54	6602.74	1698.20
10	अमलाई ओसी विस्तार, सेक्टर-बी (1.50 एमटीवाई)	11/2009	150.59	198.59	48.00
भारी उद्योग					
11	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	1718.00	3827.30	2109.30
पेट्रोरसायन					
12	असम गैस क्रैकर परियोजना	04/2006	5460.61	9833.52	4372.91

पेट्रोलियम					
13	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	429.82	3955.21	3525.39
14	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	6100.00	2851.22
15	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	506.35
16	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	700.00
17	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	495.00
विद्युत					
18	तुरीअल जल विद्युत परियोजना (60 मेगा.)	07/1998	368.72	1381.71	1012.99
19	कामेंग जल विद्युत परियोजना (नीपको)	12/2004	2496.90	6476.34	3979.44
20	पारे जल विद्युत परियोजना	12/2008	573.99	1487.49	913.50
21	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगा.) (एनएचपीसी)	09/2003	6285.33	15300.00	9014.67
22	त्रिपुरा गैस आधारित विद्युत परियोजना	07/2009	421.01	1007.68	586.67
रेलवे					
23	इकलाखी-बालुरघाट सहित गाजोल-इटाहार से नई बीजी रेलवे लाइन (एनएल), एनईएफआर	04/1983	36.80	1336.57	1299.77
24	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	111.90	2371.85	2259.95
25	अकोला-खांडवा जीसी अकोला-अकोट	04/2008	184.26	2000.00	1815.74
26	बंगलौर-सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	04/1996	138.00	1382.78	1244.78
27	तिरुचिरापल्लई-नागोरे-करायकल (एसआर) (जीसी)	09/1995	100.00	980.00	880.00
सड़क परिवहन एवं राजमार्ग					
28	मैबंग से लुमडिंग (एएस-25), 83.400 किमी. से 111.000 किमी.	12/2003	199.81	385.13	185.32
29	हरंगाजो से मैबंग, एनएच-54	12/2003	196.00	363.74	167.74
30	हरंगाजो से मैबंग, 164.08 किमी. - 190.587 किमी. एनएच-54	12/2003	212.00	386.10	174.10
31	मैबंग से लुमडिंग, (एएस-24) 111.000 किमी. से 126.450 किमी.	12/2003	155.04	280.13	125.09
32	ब्रह्मपुत्र ब्रिज एनएच सं.-31	12/2003	217.61	309.56	91.95
इस्पात					
33	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	145.40
34	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	8692.00	12291.00	3599.00

	शहरी विकास				
35	बंगलौर मेट्रो रेल परियोजना	05/2006	6395.00	11609.00	5214.00

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

5. 758 परियोजनाओं में से, 2 परियोजनाएं समय से पहले चल रही हैं, 120 समय पर तथा 323 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या में 293 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है। इसके अलावा, 29 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 284 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है। 323 विलंबित परियोजनाओं में से, 54 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 76 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 122 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 71 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम समयवृद्धि वाली परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

**अधिकतम समयवृद्धि (टीओआर) वाली (अधिकतम संख्या में 5) परियोजनाओं की क्षेत्र-वार सूची
(30.04.2015 की स्थिति के अनुसार)**

क्र.सं.	परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख	समय वृद्धि (महीना)
परमाणु ऊर्जा					
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	12/2008	06/2015	78
2	काकरापार परमाणु ऊर्जा परियोजना-3 और 4	10/2009	12/2015	10/2017	22
3	राजस्थान परमाणु ऊर्जा परियोजना-7 और 8 (2x700 मेवा)	10/2009	12/2016	04/2018	16
नागर विमानन					
4	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	01/2011	06/2017	77
5	नई अंतरराष्ट्रीय टर्मिनल भवन (गोवा) का निर्माण	05/2010	05/2012	03/2015	34
6	10 हवाई अड्डों में एयरपोर्ट संचालन नियंत्रण केन्द्रों की स्थापना	02/2010	03/2014	05/2015	14
7	विभिन्न हवाई अड्डों में 56 संख्या एयरफील्ड फायर निविदाओं की आपूर्ति	10/2012	03/2015	09/2015	6
8	चंडीगढ़ राष्ट्रीय हवाई अड्डे का विकास (मोहाली) फेज-II	02/2011	03/2015	04/2015	1

	कोयला				
9	कुल्दा ओसीपी (महानदी कोलफील्ड लिमिटेड)	01/2005	03/2010	03/2017	84
10	बलराम ओसीपी विस्तार, एमसीएल 8.00 एमटीवाई	12/2007	03/2010	03/2017	84
11	अशोक विस्तार ओसीपी सीसीएल (10 एमटीवाई)	12/2007	03/2011	03/2017	72
12	झंझरा आर-VI सीम पीएसएलडब्ल्यू	11/2006	03/2011	03/2017	72
13	गोपाल प्रसाद ओसीपी (15 एमटीवाई)	02/2008	03/2015	03/2021	72
	भारी उद्योग				
14	राष्ट्रीय औटोमोटिव टेस्टिंग तथा आरडी अवसंरचना परियोजना (एनएटीआरआईपी)	04/2011	09/2011	12/2017	75
	पेट्रोरसायन				
15	असम गैस क्रैकर परियोजना	04/2006	04/2012	06/2015	38
	पेट्रोलियम				
16	जी1 और जी एस-15 का विकास (ओएनजीसीएल)	04/2003	04/2006	06/2015	110
17	जगदीशपुर-हल्दिया पाइपलाइन परियोजना चरण-I	07/2009	01/2013	02/2019	73
18	वीकेपीएल उन्नयन तथा स्परलाइन बिछाना (भिलवाड़ा और चित्तौड़गढ़ के लिए)	12/2009	06/2011	03/2016	57
19	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	08/2010	05/2015	57
20	12 ऑफशोर आपूर्ति उपकरणों की निर्माण (ओएसवी)	06/2007	09/2011	12/2015	51
	विद्युत				
21	तुरीअल जल विद्युत परियोजना (60 मेगावाट)	07/1998	07/2006	10/2016	123
22	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	09/2009	12/2018	111
23	बाढ़ एसटीपीपी (3X660 मेगावाट) एनटीपीसी	02/2005	12/2009	03/2018	99
24	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2015	96
25	टेहरी पंढ भंडारण संयंत्र (1000 मेगावाट)	07/2006	07/2010	05/2018	94
	रेलवे				
26	गोंडिया-जबलपुर (जीसी), (एसईसीआर)	02/1997	03/1998	12/2019	261
27	गुना-इटावा वाया शिवपुरी-ग्वालियर भिंड एनएल, (एनसीआर)	04/1986	03/1994	03/2015	252
28	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	11/2002	12/2018	193

29	बांकुरा-दामोदर (जीसी) (एसईआर)	03/1998	03/2005	12/2019	177
30	तमलुक-दीघा लाइन दोहरीकरण, (एसईआर)	03/1984	06/2005	12/2019	174
	सड़क परिवहन एवं राजमार्ग				
31	असम/पश्चिम बंगाल सीमा से बिजनी चरण-II, 30.00 किमी. से 0.00 किमी., एनएच-31 सी	12/2003	06/2005	12/2015	126
32	हरंगाजो से मैबंग, 164.08 किमी. से 190.587 किमी. एनएच-54	12/2003	09/2007	04/2016	103
33	बिजनी से असम/पं. बंगाल सीमा (एनएच-31सी) (एनएचएआई)	12/2003	06/2008	05/2016	95
34	आगरा-बाड़पास (एनएस-1/यूपी-1), एनएच-2,3	12/2003	09/2007	06/2015	93
35	नलवाड़ी से बिजनी (एएस-7)	12/2003	04/2008	12/2015	92
	इस्पात				
36	आरएमएचपी में लौह अयस्क भंडारण की वृद्धि	07/2007	09/2009	06/2015	69
37	3 एमटी से 6.3 एमटी तक तरल इस्पात क्षमता का विस्तार (आरआईएनएल)	10/2005	10/2009	05/2015	67
38	बोकारो इस्पात संयंत्र का विस्तार	05/2010	12/2011	05/2015	41
39	बैलाडिला लौह अयस्क परियोजना डिपोजिट-11बी (एनएमडीसी)	01/2007	12/2011	03/2015	39
40	भिलाई इस्पात संयंत्र का विस्तार	08/2010	03/2013	09/2015	30
	दूरसंचार				
41	असम टेलीकॉम सर्कल, चरण-V.I, 2जीऔर 3जी	06/2007	01/2009	03/2015	74
42	टर्नकी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	10/2010	09/2015	59
	शहरी विकास				
43	सैन्य एमओडी स्टेशन मामुन पंजाब में वैवाहिक भवन का निर्माण	08/2005	08/2007	03/2015	91
44	आरएसवीवाई पटना के अधीन बिहार राज्य में राज्य राजमार्गों का विकास	11/2006	03/2010	10/2014	55
45	नागपुर महाराष्ट्र में राष्ट्रीय फायर सेवा कॉलेज का उन्नयन	06/2010	03/2012	04/2015	37
46	आईआईएसईआर कोलकाताके लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	06/2012	06/2015	36
47	प्रगति मैदान से सटे जमीन पर भारतीय उच्चतम न्यायालय के लिए अतिरिक्त परिसर का निर्माण	07/2012	08/2014	06/2017	34

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

6. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भूवैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारु बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

बिना उपलब्धियों वाली पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30.04.2015 की स्थिति के अनुसार)

क्र. सं.	परियोजनाएं	अनुमोदन की तारीख	मूल लागत (करोड़ रु.)	अनुमानित लागत (करोड़ रु.)	संचयी व्यय (करोड़ रु.)	शुरू करने की मूल तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन							
1	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	10 हवाई अड्डों पर एयरपोर्ट ऑपरेशन्स नियंत्रण केन्द्रों की स्थापना	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	चंडीगढ़ अंतरराष्ट्रीय हवाई अड्डा (मोहाली) का विकास चरण-II	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	नई अंतरराष्ट्रीय टर्मिनल भवन का निर्माण	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	गगन परियोजना	09/2008	626.00	626.00	514.70	06/2013	एन.ए.

	कोयला						
6	मुराईदीह यूजी	02/2011	339.88	339.88	0.00	04/2014	03/2016
7	उत्तरी तीसरा और दक्षिणी तीसरा विस्तार ओसीपी (6एमटीवाई)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	अमेरा ओसी आरसीई	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	अमृतधारा ओसी परियोजना	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	बिजारीओसीआरसीई (1.50 एमटीवाई)	05/2014	164.49	164.49	22.10	03/2020	03/2020
	उर्वरक						
11	नई सीवेज ट्रीटमेंट संयंत्र पैकेज, आरसीएफ ट्राम्बे	10/2014	197.79	197.79	13.09	11/2016	11/2016
	भारी उद्योग						
12	राष्ट्रीय ऑटोमोटिव टेस्टिंग आरडी अवसरचना परियोजना	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
	खान						
13	मलंजखंड खान का विस्तार- भूमिगत खान का विकास	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
	पेट्रोलियम						
14	मंगलौर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	पादुर में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	विजाग में सामरिक कच्चा तेल भंडारण परियोजना	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	एक बहुदेशीय सहायता वेसेल्स का निर्माण	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	बी-173ए क्षेत्र कीविकसित तेल वसूली	01/2012	352.49	352.49	115.81	03/2014	05/2016
	विद्युत						

19	बीआरबीसीएल- नवीनगर-जेवी	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	एनपीजीसीपीएल- नवीनगर-जेवी	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	यूआरटीडीएसएम चरण-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	दक्षिणी क्षेत्रकोसुदृढ बनानेकीयोजना-XXII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	किशनगंगा एचईपी के साथ जुड़ी पारिषण प्रणाली	01/2015	268.80	268.80	0.00	03/2018	03/2018
रेलवे							
24	जिंद-सोनीपत (एनएल), एनआर	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	लिंकड फिंगर के साथ-साथ रंगिया- मूरकॉगस्लेक	01/2004	915.70	3700.00	3198.30	एन.ए.	03/2015
26	कालीकट-मैंगलोर (डीएल) (एसआर)	02/1996	240.00	579.37	599.40	एन.ए.	02/2012
27	अहमदनगर-पर्ली वैजनाथ (एनएल),सीआर	02/1997	514.68	2820.00	329.67	एन.ए.	एन.ए.
28	दौसा-गंगापुर सीटी (एनएल), एनडब्ल्यूआर	02/1997	410.08	410.08	294.70	एन.ए.	एन.ए.
सड़क परिवहन एवं राजमार्ग							
29	छपरा-हाजीपुर की चार लेनिंग	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	देवली-कोटा	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	जोरबट-बारापानी	01/2011	536.00	536.00	0.00	01/2014	एन.ए.
32	कांडला-मुंदरा पोर्ट	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	पीएस कानपुर कबरई की दो लेनिंग	01/2013	373.47	373.47	0.00	07/2014	एन.ए.
पोत परिवहन एवं पत्तन							
34	सिंगल प्वाइंट मूरिंग (एसपीएम) तथा एली की स्थापना करना	02/2011	830.00	621.53	0.00	05/2013	एन.ए.
35	कोचीन पोर्ट ट्रस्ट के	03/2007	245.67	373.22	373.22	04/2009	एन.ए.

	वल्लारपदम में आईसीटी के लिए रेल संपर्क						
36	सेतुसमुद्रमशिपचैनल परियोजना	06/2005	2427.40	2427.40	831.23	10/2008	एन.ए.
37	मौजूदा बर्थ एन का संशोधन करना तथा सुदृढीकरण	06/2010	277.00	277.00	0.21	03/2012	एन.ए.
38	एन्नौर मनाली एक्सप्रेस वे, एफ/ओ स्पेशल पर्पस व्हीकल	10/2002	150.00	600.00	139.80	03/2006	एन.ए.
इस्पात							
39	गैस नेटवर्क बीएसएल	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	आरएसपी में नया एचएसएम	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	सिंटर मशीनों - 1 और 2 की सुधार	12/2009	343.00	488.40	24.02	10/2016	10/2016
दूरसंचार							
42	एनएफएस	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	रक्षा क्षेत्र के टेलीकॉम नेटवर्क आवश्यकता का निष्पादन	05/2006	1077.00	1077.00	0.00	03/2009	एन.ए.
44	असमटेलीकॉमसकिल, चरण-V.I, 2जीऔर3जी	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	टर्न की आधार पर बीएसएनएल में ईआरपी कार्यान्वयन	10/2009	384.00	384.00	55.22	10/2010	09/2015
शहरी विकास							
46	आईआईएसईआर कोलकाता के लिए हरिघंटा कल्याणी में शैक्षिक सहित आवासीय परिसर	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	एनआईटी कालीकट केरल के लिए मेगा होस्टल II कानिर्माण	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	आईआईटी हौज खास नई दिल्ली में लेक्चर थियेटर और लैब कॉम्प्लेक्स	01/2010	162.90	162.90	0.00	07/2012	06/2014

49	प्लॉट संख्या सी-41-4 पर आयकर विभाग के लिए कार्यालय भवन	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	बिहटा, पटना आईआईटी के कैम्पस के लिए आवासीय तथा अन्य परिसर	02/2012	171.10	171.10	0.00	09/2014	एन.ए.

एन.आर.: सूचित नहीं

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्य तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और उपलब्धियों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

8. यह भी पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागत वृद्धि संबंधी आंकड़े कम बताए गए हैं । बिना संशोधित लागत अनुमानों वाली शुरूआती (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची नीचे दी गई है:-

संशोधित लागत अनुमानों के बिना पहले की (सबसे पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30-04-2015 की स्थिति के अनुसार)

क्र.सं.	परियोजना	अनुमोदन की तारीख	मूल लागत (करोड़ रु. में)	संशोधित लागत (करोड़ रु. में)	संचयी व्यय (करोड़ रु. में)
	परमाणु ऊर्जा				
1	कुडनकुलम एपीपी (एनपीसीआईएल)	12/2001	13171.00	0.00	18271.00
	नागर विमानन				
2	सी/ओ पाकयांग (सिक्किम) हवाई अड्डा में नया हवाई अड्डा	01/2009	309.46	0.00	338.82
	कोयला				
3	टीपीएस-II विस्तार (1470 मेगावाट से 1970 मेगावाट) (एनएलसी)	10/2004	2030.78	3027.59	3207.92
	पेट्रोलियम				
4	बी-193 क्लस्टर क्षेत्रों का विकास	06/2007	3248.78	5633.44	5925.40
	विद्युत				
5	बाढ़ एसटीपीपी फेज-II	02/2008	7341.04	0.00	8631.00

6	सुबनसिरी लोअर एच.ई.पी. (8X250 मेगावाट) (एनएचपीसी)	09/2003	6285.33	0.00	7687.18
7	पार्वती एचईपी (4X200मेगावाट) (एनएचपीसी) II	09/2002	3919.59	0.00	5040.21
8	किशनगंगा एचईपी (3x110 मेवा)	01/2009	3642.04	0.00	3934.97
9	छत्तीसगढ़ में आईपीपीएस जेनरेशन परियोजनाओं के लिए डब्ल्यूआर के पश्चिमी भाग में पारेषण प्रणाली का सुदृढीकरण	11/2011	2127.51	0.00	2172.33
10	तीस्ता लो डैम एचईपी चरण-IV (4X40 मेवा) (एनएचपीसी)	09/2005	1061.38	0.00	1742.55
रेलवे					
11	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	03/1995	2500.00	3000.00	10658.34
12	लुमडिंग-सिलचर-जिरिबम बदरपुर-बराईग्राम-कुमारघाट राष्ट्रीय परियोजना	04/1996	1676.31	0.00	4734.45
13	दमदम-नावपारा और नावपारा-एनएससीपी एयरपोर्ट तक विस्तार के साथ टॉलीगंज-गरिया (एमटीपी)	03/2000	1049.69	3385.14	3541.20
14	बोगीबिल तथा लिंक लाइनों पर ब्रह्मपुत्र पुल, एनईएफआर	09/1997	1500.00	1000.00	3410.06
15	लिंकड फिंगर्स के साथ रंगिया-मुरकॉगसलेक एनईएफआर	01/2004	915.70	915.70	3198.30
सड़क परिवहन एवं राजमार्ग					
16	पानीपत-जालंधर छः लेनिंग (96 किमी. से 387.1 किमी.)	05/2009	1108.00	0.00	3466.00
17	नागपुर-बेतुल के चार लेनिंग	02/2011	2498.76	0.00	2786.00
18	सूरत-दहिसर (छः लेन) 263 किमी. से 502 किमी.	02/2009	1693.75	0.00	2762.00
19	गाजियाबाद-अलीगढ़एनएच-91	02/2011	1141.00	0.00	2445.00
20	मुरादाबाद-बरेली	04/2010	1267.00	0.00	2425.00
पोत परिवहन एवं पत्तन					
21	कोचीन पोर्ट्स के बल्लापाडम में आईसीटीटी के लिए रेल कनेक्टिविटी	03/2007	245.67	0.00	373.22

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और संशोधित लागत अनुमानों को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

शुरू करने की संशोधित तारीख के बिना पहले की परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची इस प्रकार है:-

शुरू करने की संशोधित अनुसूची के बिना पहले की (पुरानी) परियोजनाओं (अधिकतम संख्या में पांच) की क्षेत्र-वार सूची (30.04.2015 की स्थिति के अनुसार)

क्र. सं.	क्षेत्र/परियोजना	अनुमोदन की तारीख	शुरू करने की मूल तारीख	शुरू करने की संशोधित तारीख	शुरू करने की अनुमानित तारीख
नागर विमानन					
1	गगनपरियोजना	09/2008	06/2013	एन.आर.	06/2013
2	वीएसआई हवाई अड्डे, पोर्ट ब्लेयर में एकीकृत टर्मिनल भवन का निर्माण	10/2013	एन.आर.	एन.आर.	एन.आर.
कोयला					
1	शांतिखानी लॉगवॉल परियोजना-एससीसीएल	10/2006	03/2012	एन.आर.	एन.आर.
2	जल्लाराम शॉफ्ट परियोजना	09/2007	03/2013	एन.आर.	एन.आर.
3	रामागुंडम ओसी।। विस्तार	12/2009	03/2012	एन.आर.	एन.आर.
4	मुराडीहयूजी टर्न की परियोजना	02/2011	04/2014	एन.आर.	04/2014
5	कृष्णाशिला (एनसीएल) (4एमटीवाई)	06/2011	03/2013	एन.आर.	03/2014
पेट्रोरसायन					
1	असम गैस क्रैकर परियोजना	04/2006	04/2012	एन.आर.	एन.आर.
पेट्रोलियम					
1	एन्नोरमेंडविपणन टर्मिनल	11/2006	एन.आर.	एन.आर.	एन.आर.
2	बीपीसीआर/एचपीसीआरसे उरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण के लिए पाइप लाइन	08/2009	08/2012	एन.आर.	एन.आर.
3	एन्नोर-त्रिची-मदुरै एलपीजी पाइप लाइन	05/2013	एन.आर.	एन.आर.	एन.आर.
विद्युत					

1	कैगा 3 तथा 4 पारेषण प्रणाली (पीजीसीआईएल)	03/2005	12/2007	12/2009	एन.आर.
2	कुंदन कुलम एपीपी ट्रांस प्रणाली (पीजीसीआईएल)	05/2005	09/2008	एन.आर.	03/2013
3	एसआर -XII की व्यवस्था कासुदृढीकरण	02/2010	06/2012	एन.आर.	एन.आर.
4	आंध्रप्रदेश भाग-ए1 के वैमा गिरी क्षेत्र में आईएसजीएस परियोजनाओं से जुड़ी सामान्य प्रणाली	03/2012	06/2014	एन.आर.	एन.आर.
रेलवे					
1	नांगलडैम-तलवाड़ा (एनएल), एन.आर.	03/1981	07/2012	एन.आर.	एन.आर.
2	गजोली-ईटाहर(एनएल), एनईएफआरसहितएकलाखी-बालुरघाटसेनईबीजीरेलवेलाइन	04/1983	एन.आर.	एन.आर.	एन.आर.
3	तामलुकदीघा, लाइनदोहरीकरण (एसईआर)	03/1984	06/2005	07/2011	एन.आर.
4	नामखानाचंद्रनगर काकदीप-बुदाखाली तथा चंद्रनगर के लिए लक्ष्मीकांतपुर-नामखाना, इसके बाद एमएम	04/1987	एन.आर.	एन.आर.	एन.आर.
5	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	04/1990	एन.आर.	03/2010	एन.आर.
सड़क परिवहन एवं राजमार्ग					
1	लखनऊ-रायबरेली	07/1999	07/2012	एन.आर.	09/2014
2	दीवापुरसे यूपी/बिहारसीमा (एलएमएनएचपी-9) एनएच-28, किमी.402-360.915	12/2003	10/2008	एन.आर.	एन.आर.
3	सिलिगुडी से इस्लामपुर (पश्चिमबंगाल-7)	12/2003	07/2008	एन.आर.	एन.आर.
4	नलबाड़ी सेबिजनी (एएस-8)	12/2003	06/2008	एन.आर.	एन.आर.
5	पिंपलगांव-नासिक-गोंडी, एनएच-3 (एनएचडीपीचरणIII)	03/2005	07/2012	एन.आर.	07/2012
पोत परिवहन एवं पत्तन					
1	ट्यूना, कांडला पोर्ट ट्रस्ट के नजदीक टेकरा की बर्थिंग और संबंधित सुविधाओं का निर्माण	04/2005	02/2011	एन.आर.	12/2012
2	सेतुसमुद्रम शिप चैनल परियोजना	06/2005	10/2008	11/2010	एन.आर.
3	मुम्बई हार्बर चैनल और जेएनपीटी चैनल को चौड़ा करना और मजबूत करना	10/2005	10/2008	एन.आर.	एन.आर.
4	पारादीप बंदरगाह पर चैनल का सुदृढीकरण	12/2005	एन.आर.	01/2009	12/2010
5	कांडला में 13 और 14 कार्गो बर्थ का निर्माण	12/2005	03/2011	एन.आर.	03/2013
शहरी विकास					
1	सी/ओ सैन्य रक्षामंत्रालय स्टेशन मामुन पंजाब में वैवाहिक आवासीय	08/2005	08/2007	एन.आर.	एन.आर.

2	बंगलोर में ट्रोरेल परियोजना	05/2006	06/2011	एन.आर.	03/2013
3	सी/ओबांद्राकुर्ला कॉम्प्लेक्स, मुंबई में आईडीबीआई के लिए कार्यालय भवन	11/2006	04/2009	एन.आर.	एन.आर.
4	सी/ओएनआईटी कालीकट केरल के लिए मेगा हॉस्टल॥	01/2010	10/2012	एन.आर.	एन.आर.
5	आईआईटी हॉजखास नई दिल्ली में लेक्चर थिएटर और प्रयोगशाला परिसर	01/2010	07/2012	एन.आर.	07/2012

एन.आर.: सूचित नहीं.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यपालक तथा संबंधित प्रशासनिक मंत्रालय के सचिव और वित्तीय सलाहकार और शुरू करने की संशोधित तारीख को अंतिम रूप देने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- i) **इस्पात क्षेत्र में,** 26 परियोजनाओं में से 16 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'बीएसपी, भिलाई, छत्तीसगढ़ में कोक ओवन बैटरी-9 का कोल्ड रिपेयर, सेल' में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।
- ii) **रेलवे क्षेत्र में,** 208 परियोजनाओं में से 32 परियोजनाएं विलंबित हैं । माह के दौरान, 1 परियोजना 'बारानगर से बराकपुर तथा दक्षिणेश्वर (एमटीपी) तक मेट्रो रेलवे के निर्माण हेतु नया कार्य, आरवीएनएल' में निधि की कमियों के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- iii) **नागर विमानन क्षेत्र में,** 7 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में 1 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 10 एयरपोर्टों पर एयरपोर्ट ऑप्रेशन्स नियंत्रण केन्द्रों की स्थापना, एएआई' में उपस्करों की आपूर्ति में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा परियोजना 'पक्कोग (सिक्किम) एयरपोर्ट पर सी/ओ नया एयरपोर्ट, एएआई' में एएआई आवासीय कालोनी के लिए जमीन की उपलब्धता न होने के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।
- iv) **कोयला क्षेत्र में,** 73 परियोजनाओं में से 41 परियोजनाएं विलंबित हैं । माह के दौरान, 11 परियोजनाओं के संबंध में 1-48 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इन 11 परियोजनाओं में से 3 परियोजनाएं मेगा परियोजनाएं हैं । परियोजनाएं 'तूतीकोरिन थर्मल पावर परियोजना-2X500 मेवा., एनएलसी' में अपर्याप्त संसाधन जुटाने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'टीपीएस-II विस्तार (1470 मेवा से 1970 मेवा), एनएलसी' में सब 3 तथा 4 क्षेत्र में आग लगने जिससे यूनिट बंद हो गई के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'आरजी ओसी-III विस्तार (चरण-II) परियोजना, एससीसीएल' में भूमि अधिग्रहण के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त

हुई है, परियोजना 'पेनगाना ओसीपी (संशोधित), डब्ल्यूसीएल' में लंबित वन भूमि के परिवर्तन के कारण 48 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'इंद्रम ओसीपी की आरसीई (1.20 एमटीपीए), एससीसीएल', 'ब्लॉक-बी ओसीपी एनसीएल (3.5 एमटीवाई), एनसीएल' तथा 'आरकेपी ओसीपी चरण-I, एससीसीएल' में क्रमशः 1, 12 तथा 13 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'पूरनादीह ओसीपी (3.0 एमटीवाई), सीसीएल', 'जगन्नाथपुर ओसी, एसईसीएल' में क्रमशः 24 तथा 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'करताली (पूर्व) ओसीपी (2.50 एमटीवाई), एसईसीएल', 'मुनीदीह XV सेम यूजी, बीसीसीएल' प्रत्येकमें 48 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

V) पेट्रोलियम क्षेत्र में, 71 परियोजनाओं में से 46 परियोजनाएं विलंबित हैं। माह के दौरान, 12 परियोजनाओं के संबंध में 2-12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 12 परियोजनाओं में से 3 परियोजनाएं मेगा परियोजनाएं हैं। 4 परियोजनाओं के संबंध में संविदा संबंधी समस्या के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 1 परियोजना 'कोनबन जीजीएस तथा पाइपलाइन ग्रिड परियोजना, त्रिपुरा का उन्नयन, ओएनजीसी' में आरओयू समस्या के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, एक परियोजना "पारादीप हल्दिया दुर्गापुर एलपीजी पाइपलाइन, आईओसीएल' में भूमि अधिग्रहण के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'वीकेपीएल उन्नयन तथा स्परलाइन (भिलवाड़ा और छत्तीसगढ़ के लिए) बिछाना, गेल' तथा 'बीपीए और बीपीबी प्लेटफॉर्म का पुनर्निर्माण, ओएनजीसी' में संविदा संबंधी मुद्दे तथा ठेकेदार द्वारा धीमी गति से कार्य करने के कारण प्रत्येक में 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजना 'रेसिड उन्नयन परियोजना, सीपीसीएल' तथा 'एमएच दक्षिण क्षेत्र के पश्चिमी घेरे का विकास, ओएनजीसी' में क्रमशः नजदीकी परिचालन संयंत्रों की वजह से कार्य माहौल तथा संविदा संबंधी समस्या के कारण क्रमशः 8 तथा 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'बी-173 ए क्षेत्र की विकसित तेल वसूली, ओएनजीसी' तथा 'कोच्ची में एलपीजी टर्मिनल, आईओसीएल' में क्रमशः 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

VI) सड़क परिवहन एवं राजमार्ग क्षेत्र में 133 परियोजनाओं में से 99 परियोजनाएं विलंबित हैं। माह के दौरान, 14 परियोजनाओं के संबंध में 1-52 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। इन 14 परियोजनाओं में से 8 परियोजनाएं मेगा परियोजनाएं हैं। 1 परियोजना के संबंध में भूमि अधिग्रहण के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 3 परियोजनाओं के संबंध में भूमि अधिग्रहण के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, परियोजनाएं 'कृष्णागरी-टिंडीबलम (अनुमोदित लंबाई 170 किमी.) की दो लेनिंग, एनएचएआई' तथा परियोजना 'क्वाजीगुंद-बनिहाल 220.00 किमी. से 188.00 किमी., एनएचएआई' में निधि

की कमी तथा संविदात्मक मुद्दे के कारण क्रमशः 8 तथा 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बरेली-सीतापुर (एनएच-24), एनएचएआई' में भूमि अधिग्रहण के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'सूरत-दहिसर (छ: लेन) 263 किमी. से 502 किमी., एनएचएआई' में भूमि अधिग्रहण तथा कानून व व्यवस्था संबंधी मुद्दे के कारण 52 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'सोनापुर से गुवाहाटी (एएस-3), एनएचएआई और 'उड़ीसा-छत्तीसगढ़ बॉर्डर की चार लेनिंग, एनएचएआई' में क्रमशः 3 तथा 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'नागपुर-वैनगंगा पुल, एनएचएआई तथा 'दिल्ली-आगरा अनुमोदित लंबाई 180.0 किमी., एनएचएआई' प्रत्येक में 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'वालझापेट-पुनामेली किमी. 106.8 से किमी. 13.8, एनएचएआई तथा 'रांची-रर्गा-जमशेदपुर, एनएचएआई' में क्रमशः 16 तथा 18 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

vi) विद्युत क्षेत्र में, 112 परियोजनाओं में से 63 परियोजनाएं विलंबित हैं । माह के दौरान, 22 परियोजनाओं के संबंध में 1-11 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 22 परियोजनाओं में से 15 परियोजनाएं मेगा परियोजनाएं हैं । एक परियोजना के संबंध में भूमि अधिग्रहण के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 11 परियोजनाओं के संबंध में वन संबंधी अनुमति तथा विभिन्न आरओडब्ल्यू समस्या के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 5 परियोजनाओं के संबंध में विभिन्न आरओडब्ल्यू समस्या के कारण प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'पूर्वी क्षेत्र की प्रणाली को सुदृढ़ करने की योजना-III, पीजीसीआईएल', 'छत्तीसगढ़ में आईपीपी जेनरेशन परियोजना के लिए चंपा तथा रायगढ़ में पूलिंग स्टेशनों की स्थापना, पीजीसीआईएल' में क्रमशः वन संबंधी अनुमति तथा भूमि अधिग्रहण में विलंब के कारण 9 तथा 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'डब्ल्यूआर तथा एनआर (लाइनबे तथा रिएक्टर प्रावधान) के लिए सामान्य प्रणाली को सुदृढ़ करना, पीजीसीआईएल', 'टेहरी पंप स्टोरेज संयंत्र (पीएसपी) के साथ जुड़ी सामान्य पारेषण प्रणाली, पीजीसीआईएल' प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'श्रीकाकुलम क्षेत्र आंध्रप्रदेश भाग सी में इस्ट कोस्ट तथा एनसीसी विद्युत परियोजनाओं के साथ जुड़ी सामान्य पारेषण प्रणाली, पीजीसीआईएल' में 6 माह के विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

10. दिनांक 30.04.2015 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ₹150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for April 2015 contains information on the status of the 758 Central Sector Infrastructure Projects costing ₹150 crore and above. During April 2015, 2 projects (1 project each in Petroleum and Road Transport and Highways sector) have reported completion.

2. During the reference month, out of 758 projects, 323 projects are delayed with respect to original schedule and 63 projects have reported additional delay vis-à-vis the date of completion reported in the previous month. Of these 63 projects, 30 are Mega Projects costing ₹ 1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	RAILWAYS	288	32	1	1
2	ROAD TRANSPORT AND HIGHWAYS	133	99	14	8
3	POWER	112	63	22	15
4	PETROLEUM	71	46	12	3
5	COAL	73	41	11	3
6	URBAN DEVELOPMENT	30	16	0	0
7	STEEL	26	16	1	0
8	CIVIL AVIATION	7	4	2	0
9	SHIPPING AND PORTS	6	0	0	0
10	ATOMIC ENERGY	4	3	0	0
11	TELECOMMUNICATIONS	4	1	0	0
12	FERTILISERS	1	0	0	0
13	MINES	1	0	0	0
14	PETROCHEMICALS	1	1	0	0
15	HEAVY INDUSTRIES	1	1	0	0
Total		758	323	63	30

3. Total original cost of implementation of the 758 projects was ₹10,69,127.84 crore and their anticipated completion cost is likely to be ₹12,78,256.35 crore, which reflects overall cost overruns of ₹2,09,128.51 crore (19.56% of original cost). The expenditure incurred on these projects till April 2015 is ₹5,46,232.97 crore, which is 42.73% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost
Overruns (as on 30-04-2015)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	62.57
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	31.12
CIVIL AVIATION					
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	15.77
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	12.18
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	8.19
COAL					
6	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	478.50
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3477.21	71.23
8	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	50.37
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	34.63
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	31.87
HEAVY INDUSTRY					
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3827.30	122.78
PETROCHEMICALS					
12	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	80.08
PETROLEUM					
13	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	820.20
14	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	6100.00	87.76
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	75.35
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	67.62
POWER					
18	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	274.73
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	159.38
20	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	159.15
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	143.42
22	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.68	139.35
RAILWAYS					
23	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	3531.98
24	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2019.62
25	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	985.42
26	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	902.01
27	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	363.74	85.58
30	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	212.00	386.10	82.12
31	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
32	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	309.56	42.25
STEEL					
33	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
34	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT	10/2005	8692.00	12291.00	41.41

	TO 6.3MT (RINL)				
	URBAN DEVELOPMENT				
35	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	81.53

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 30-04-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs. crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	5677.00	2185.00
2	KUDANKULAM APP (NPCIL)	12/2001	13171.00	17270.00	4099.00
	CIVIL AVIATION				
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	335.61	388.53	52.92
4	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	244.10	26.50
5	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	452.00	489.00	37.00
	COAL				
6	ADRIYALA SHAFT PROJECT	12/2009	212.34	1228.39	1016.05
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	2030.78	3477.21	1446.43
8	MAGADH OC 20 MTY (CCL)	08/2008	469.78	706.40	236.62
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	05/2008	4904.54	6602.74	1698.20
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	150.59	198.59	48.00
	HEAVY INDUSTRY				
11	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
	PETROCHEMICALS				
12	ASSAM GAS CRACKER PROJECT	04/2006	5460.61	9833.52	4372.91
	PETROLEUM				
13	DEV OF G1 AND GS-15 (ONGCL)	04/2003	429.82	3955.21	3525.39
14	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	6100.00	2851.22
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	506.35
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	495.00
	POWER				
18	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	368.72	1381.71	1012.99
19	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	6476.34	3979.44
20	PARE HYDRO ELECTRIC PROJECT	12/2008	573.99	1487.49	913.50
21	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	15300.00	9014.67
22	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	1007.68	586.67
	RAILWAYS				
23	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	36.80	1336.57	1299.77
24	BANKURA - DAMODAR (GC) (SER)	03/1998	111.90	2371.85	2259.95
25	AKOLA-KHANDWA GC AKOLA-AKOT	04/2008	184.26	2000.00	1815.74

26	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	138.00	1382.78	1244.78
27	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	100.00	980.00	880.00
ROAD TRANSPORT AND HIGHWAYS					
28	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	185.32
29	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	363.74	167.74
30	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	12/2003	212.00	386.10	174.10
31	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	125.09
32	BRAHMPUTRA BRIDGE, NH NO-31	12/2003	217.61	309.56	91.95
STEEL					
33	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
34	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	8692.00	12291.00	3599.00
URBAN DEVELOPMENT					
35	BANGALORE METRO RAIL PROJECT	05/2006	6395.00	11609.00	5214.00

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 758 projects, 2 projects are ahead of schedule, 120 are on schedule and 323 are delayed with respect to original schedule. However, the number of delayed projects decreases to 293 if delay is calculated on the basis of latest schedule of completion. Further, 29 projects have been sanctioned without original commissioning schedule date and for 284 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 323 delayed projects, 54 projects have overall delay in the range of 1 to 12 months, 76 projects have delay in the range of 13 to 24 months, 122 projects have delay in the range of 25 to 60 months and 71 projects have delay of 61 months and above. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 30-04-2015)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR(IN MONTHS)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	12/2008	06/2015	78
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	10/2017	22
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	04/2018	16
CIVIL AVIATION					
4	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	01/2011	06/2017	77
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA)	05/2010	05/2012	03/2015	34
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	02/2010	03/2014	05/2015	14
7	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	03/2015	09/2015	6
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II	02/2011	03/2015	04/2015	1
COAL					
9	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2017	84
10	BALRAM OCP EXTENSION, MCL 8.00 MTY	12/2007	03/2010	03/2017	84

11	ASHOK EXPN OCP CCL (10 MTY)	12/2007	03/2011	03/2017	72
12	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2017	72
13	GOPAL PRASAD OCP (15MTY)	02/2008	03/2015	03/2021	72
HEAVY INDUSTRY					
14	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	09/2011	12/2017	75
PETROCHEMICALS					
15	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	06/2015	38
PETROLEUM					
16	DEV OF G1 AND GS-15 (ONGCL)	04/2003	04/2006	06/2015	110
17	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	07/2009	01/2013	02/2019	73
18	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	12/2009	06/2011	03/2016	57
19	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	08/2010	05/2015	57
20	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2015	51
POWER					
21	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	07/1998	07/2006	10/2016	123
22	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2018	111
23	BARH STPP(3X660MW) NTPC	02/2005	12/2009	03/2018	99
24	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2015	96
25	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	07/2010	05/2018	94
RAILWAYS					
26	GONDIA-JABALPUR(GC),(SECR)	02/1997	03/1998	12/2019	261
27	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	03/2015	252
28	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2018	193
29	BANKURA - DAMODAR (GC) (SER)	03/1998	03/2005	12/2019	177
30	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	12/2019	174
ROAD TRANSPORT AND HIGHWAYS					
31	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2015	126
32	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54	12/2003	09/2007	04/2016	103
33	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	12/2003	06/2008	05/2016	95
34	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	06/2015	93
35	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2015	92
STEEL					
36	AUGMENTATION OF IRON ORE STORAGE IN RMHP	07/2007	09/2009	06/2015	69
37	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2005	10/2009	05/2015	67
38	EXPANSION OF BOKARO STEEL PLANT	05/2010	12/2011	05/2015	41
39	BAILADILA IRON ORE PROJECT DEPOSIT-11B (NMDC)	01/2007	12/2011	03/2015	39
40	EXPANSION OF BHILAI STEEL PLANT	08/2010	03/2013	09/2015	30
TELECOMMUNICATIONS					
41	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	01/2009	03/2015	74
42	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	10/2010	09/2015	59
URBAN DEVELOPMENT					
43	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	03/2015	91
44	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA	11/2006	03/2010	10/2014	55
45	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	06/2010	03/2012	04/2015	37
46	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER	01/2009	06/2012	06/2015	36

	KOLKATA				
47	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	08/2014	06/2017	34

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones is as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 30-04-2015)**

S N	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	309.46	338.82	01/2011	06/2017
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI	02/2010	344.28	344.28	58.50	03/2014	05/2015
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO	02/2011	452.00	489.00	410.25	03/2015	04/2015
4	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	05/2010	335.61	388.53	297.58	05/2012	03/2015
5	GAGAN PROJECT	09/2008	626.00	626.00	514.70	06/2013	N.A.
COAL							
6	MURAI DIH UG	02/2011	339.88	339.88	0.00	04/2014	03/2016

7	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	02/2014	555.52	555.52	0.00	03/2021	03/2021
8	AMERA OC RCE	02/2015	335.97	335.97	30.30	03/2018	03/2018
9	AMRITDHARA OC PROJECT	02/2015	481.60	481.60	0.00	03/2023	03/2023
10	BIJARI OC RCE (1.50 MTY)	05/2014	164.49	164.49	22.10	03/2020	03/2020
FERTILISERS							
11	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	197.79	13.09	11/2016	11/2016
HEAVY INDUSTRY							
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (	04/2011	1718.00	3827.30	0.00	09/2011	12/2017
MINES							
13	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUN D MIN	09/2011	1856.00	1856.00	0.00	09/2017	09/2017
PETROLEUM							
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	01/2006	732.00	1227.00	944.84	10/2011	10/2015
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1398.50	01/2012	10/2015
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	01/2006	672.00	1178.35	1099.88	10/2011	10/2015
17	CONSTRUCTIO N OF ONE MULTIPURPOSE SUPPORT VESSEL	01/2010	723.64	723.64	0.00	03/2013	06/2016
18	IMPROVED OIL RECOVERY OF B-173A FIELD	01/2012	352.49	352.49	115.81	03/2014	05/2016
POWER							
19	BRBCL- NABINAGAR - JV	01/2007	5353.00	5353.00	0.00	05/2014	05/2014
20	NPGCPL- NABINAGAR - JV	01/2013	12964.60	12964.60	0.00	01/2018	01/2018
21	URTD SM PHASE-I	01/2014	374.63	374.63	0.00	04/2016	04/2016
22	SYSTEM STRENGTHENIN G IN SOUTHERN REGION - XXIII	01/2015	203.28	203.28	0.00	07/2017	07/2017
23	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAG	01/2015	268.80	268.80	0.00	03/2018	03/2018

	A HEP						
	RAILWAYS						
24	JIND-SONEPAT (NL),NR	01/2004	238.56	740.00	639.77	03/2012	12/2012
25	RANGIA-MURKONGSELE K, (GC) ALONG WITH LINKED FINGER	01/2004	915.70	3700.00	3198.30	N.A.	03/2015
26	CALICUT-MANGALORE (DL) (SR)	02/1996	240.00	579.37	599.40	N.A.	02/2012
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	02/1997	514.68	2820.00	329.67	N.A.	N.A.
28	DAUSA-GANGAPUR CITY(NL),NWR	02/1997	410.08	410.08	294.70	N.A.	N.A.
	ROAD TRANSPORT AND HIGHWAYS						
29	4-LANNING OF CHAPRA-HAJIPUR	01/2011	575.00	575.00	835.60	07/2013	12/2015
30	DEOLI-KOTA	01/2011	593.00	593.00	761.30	07/2013	04/2016
31	JORBAT - BARAPANI	01/2011	536.00	536.00	0.00	01/2014	N.A.
32	KANDLA - MUNDRA PORT	01/2011	953.88	953.88	953.88	07/2013	06/2015
33	2 LANING WITH PS KANPUR KABRAI	01/2013	373.47	373.47	0.00	07/2014	N.A.
	SHIPPING AND PORTS						
34	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIE	02/2011	830.00	621.53	0.00	05/2013	N.A.
35	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS	03/2007	245.67	373.22	373.22	04/2009	N.A.
36	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.23	10/2008	N.A.
37	MODIFICATION AND STRENGTHENING OF EXISTING BERTH N	06/2010	277.00	277.00	0.21	03/2012	N.A.
38	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI	10/2002	150.00	600.00	139.80	03/2006	N.A.
	STEEL						
39	GAS NETWORK BSL	03/2015	255.19	255.19	0.00	03/2018	03/2018
40	NEW HSM AT RSP	04/2015	3127.30	3127.30	0.00	04/2018	04/2018
41	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	24.02	10/2016	10/2016
	TELECOMMUNICATIONS						
42	NFS	03/2012	13334.00	13334.00	0.00	07/2015	07/2015
43	EXECUTION OF TELECOM NETWORK REQUIREMENT	05/2006	1077.00	1077.00	0.00	03/2009	N.A.

	OF DEFENCE						
44	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G	06/2007	336.81	336.81	199.37	01/2009	03/2015
45	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	10/2009	384.00	384.00	55.22	10/2010	09/2015
URBAN DEVELOPMENT							
46	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	01/2009	225.81	225.81	0.00	06/2012	06/2015
47	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	165.23	165.23	0.00	10/2012	09/2013
48	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	162.90	162.90	0.00	07/2012	06/2014
49	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C-41-4	02/2011	241.33	241.33	1.75	11/2014	12/2014
50	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA	02/2012	171.10	171.10	0.00	09/2014	N.A.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 30-04-2015)

SN	PROJECT	DOA	COST ORIGINAL (Rs. Crore)	COST REVISED (Rs. Crore)	CUMMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KUDANKULAM APP (NPCIL)	12/2001	13171.00	0.00	18271.00
CIVIL AVIATION					
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT	01/2009	309.46	0.00	338.82
COAL					
3	TPS-II EXPANSION (1470MW TO 1970MW)	10/2004	2030.78	3027.59	3207.92

	(NLC)				
	PETROLEUM				
4	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	3248.78	5633.44	5925.40
	POWER				
5	BARH STPP STAGE -II	02/2008	7341.04	0.00	8631.00
6	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	7687.18
7	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	5040.21
8	KISHANGANGA HEP (3X110 MW)	01/2009	3642.04	0.00	3934.97
9	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	11/2011	2127.51	0.00	2172.33
10	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	09/2005	1061.38	0.00	1742.55
	RAILWAYS				
11	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	3000.00	10658.34
12	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	04/1996	1676.31	0.00	4734.45
13	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	03/2000	1049.69	3385.14	3541.20
14	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	09/1997	1500.00	1000.00	3410.06
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	01/2004	915.70	915.70	3198.30
	ROAD TRANSPORT AND HIGHWAYS				
16	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	0.00	3466.00
17	4 LANING OF NAGPUR-BETUL	02/2011	2498.76	0.00	2786.00
18	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	02/2009	1693.75	0.00	2762.00
19	GHAZIABAD-ALIGARH NH-91	02/2011	1141.00	0.00	2445.00
20	MURADABAD-BAREILY	04/2010	1267.00	0.00	2425.00
	SHIPPING AND PORTS				
21	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	245.67	0.00	373.22

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 30-04-2015)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION				
1	GAGAN PROJECT	09/2008	06/2013	NR	06/2013
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	NR	N.R.	N.R.
	COAL				

1	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	N.R.	N.R.
2	JALLARAM SHAFT PROJECT	09/2007	03/2013	N.R.	N.R.
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	N.R.	N.R.
4	MURADIH UG TURN-KEY PROJECT	02/2011	04/2014	N.R.	04/2014
5	KRISHNASHILA (NCL) (4MTY)	06/2011	03/2013	N.R.	03/2014
PETROCHEMICALS					
1	ASSAM GAS CRACKER PROJECT	04/2006	04/2012	N.R.	N.R.
PETROLEUM					
1	NEW MARKETING TERMINAL AT ENNORE	11/2006	N.R.	N.R.	N.R.
2	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	08/2009	08/2012	N.R.	N.R.
3	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	N.R.	N.R.	N.R.
POWER					
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	03/2005	12/2007	12/2009	N.R.
2	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	09/2008	N.R.	03/2013
3	SYSTEM STRENGTHENING -XII OF SR	02/2010	06/2012	N.R.	N.R.
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	03/2012	06/2014	N.R.	N.R.
RAILWAYS					
1	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.R.	N.R.
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	N.R.	N.R.	N.R.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	07/2011	N.R.
4	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	N.R.	N.R.	N.R.
5	VIRAMGAM-BHILDI(WR),GC	04/1990	N.R.	03/2010	N.R.
ROAD TRANSPORT AND HIGHWAYS					
1	LUCKNOW-RAIBAREILI	07/1999	07/2012	N.R.	09/2014
2	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	N.R.	N.R.
3	SILIGURI TO ISLAMPUR (WB-7)	12/2003	07/2008	N.R.	N.R.
4	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	N.R.	N.R.
5	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	03/2005	07/2012	N.R.	07/2012
SHIPPING AND PORTS					
1	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST	04/2005	02/2011	N.R.	12/2012
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	11/2010	N.R.
3	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	10/2005	10/2008	N.R.	N.R.

4	DEEPENING OF CHANNEL AT PARADIP PORT	12/2005	N.R.	01/2009	12/2010
5	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	N.R.	03/2013
URBAN DEVELOPMENT					
1	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB	08/2005	08/2007	N.R.	N.R.
2	BANGALORE METRO RAIL PROJECT	05/2006	06/2011	N.R.	03/2013
3	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI	11/2006	04/2009	N.R.	N.R.
4	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.R.	N.R.
5	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI	01/2010	07/2012	N.R.	07/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

10. The Sector-wise details of additional delays are as under:-

- i) In the **Steel**, out of 26 projects, 16 projects are delayed. During the month 1 project Cold Repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh, SAIL has reported additional delay of 5 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
- ii) In the **Railways**, out of 288 projects, 32 projects are delayed. During the month 1 project 'New Work For Construction of Metro Railway From Baranagar to Barrackpore and Dakshineswar (MTP), RVNL' is delayed by 24 months due to fund constraints.
- iii) In the **Civil Aviation**, out of 7 projects, 4 projects are delayed. During the month 2 projects have reported additional delay of 1 and 12 months. Project 'Establishment of Airport Operations Control Centres at 10 Airports, AAI' is having additional delay of 1 month due to delay in supply of equipments and Project 'C/O New Airport at Pakyong (Sikkim) Airport, AAI' is delayed by 12 months due to non-availability of land for AAI residential colony.
- iv) In the **Coal Sector**, out of 73 projects, 41 projects are delayed. During the month, 11 projects have reported additional delay in the range of 1-48 months. Out of 11 projects 3 projects are mega projects. The Projects 'Tuticorin Thermal Power Project- 2X500 MW, NLC' has reported additional delay of 1 month due to inadequate resource mobilization,

the project 'TPS-II Expansion (1470 MW to 1970MW), NLC' has reported additional delay of 2 month due to fire in the area of Sub 3 and 4 causing unit shutdown, the project 'RG OC -III Extension (Phase -II) Project, SCCL' has reported additional delay of 12 months due to land acquisition, the project 'Penganga OCP (Revised), WCL' has reported additional delay of 48 months due to diversion of forest land pending, the projects 'RCE of Indaram OCP (1.20 MTPA), SCCL', 'Block-B OCP NCL (3.5 MTY) NCL' and 'RKP OCP Phase-I SCCL' have reported additional delay of 1, 12 and 13 months respectively, the projects 'Purnadih OCP (3.0 MTY), CCL', 'Jagannathpor OC SECL' have reported additional delay of 24 and 36 months respectively, the projects 'Kartali (East) OCP (2.50 MTY), SECL' and 'Moonidih XV Seam UG, BCCL' have reported additional delay of 48 months each (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).

- v) In the **Petroleum Sector**, out of 71 projects, 46 projects are delayed. During the month, 12 projects have reported additional delays in the range of 2-12 months. Out of 12 projects 3 projects are mega projects. 4 projects have reported additional delay of 2 months due to contractual problem, 1 project 'Up-Gradation of Konaban GGS and Pipeline Grid Project, Tripura, ONGC' reported additional delay of 3 months due to RoU issue, one project 'Paradip Haldia Durgapur LPG Pipeline IOCL' reported additional delay of 6 months due to land acquisition, the projects 'VKPL Upgradation and Laying of Spurline (to Bhilwara and Chittorgarh) GAIL' and 'Reconstruction of BPA and BPB Platforms ONGC' have reported additional delay of 8 months each due to contractual issue and slow work by contractor, the project 'Resid Upgradation Project CPCL' and 'Development of Western Periphery of MH South Field ONGC' have reported additional delay of 8 and 12 months respectively due to restricted working environment due to nearby operating plants and contractual problem respectively, the projects 'Improved Oil Recovery of B-173A Field ONGC' and 'LPG Terminal at Kochi IOCL' have reported additional delay of 2 and 3 months respectively (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).
- vi) In the **Road Transport and Highways Sector**, out of 133 projects, 99 projects are delayed. During the month, 14 projects have reported additional delays in the range of 1-52 months. Out of 14 projects 8 projects are mega projects. 1 project has reported additional delay of 1 month due to land acquisition, 3 projects have reported additional delay of 3 months each due to land acquisition, the projects '2-Laning of Krishnagiri-Tindivanam (Approved Length 170 KM), NHAI' and 'The project 'Quazigund-Banihal

KM.220.00 to KM.188.00, NHAI' have reported additional delay of 8 and 11 months respectively due to fund constraints and contractual issues; the project 'Bareilly-Sitapur (NH-24), NHAI' has reported additional delay of 12 months due to land acquisition, the project 'Surat- Dahisar (Six Lane) Km 263 to Km 502 NHAI' has reported additional delay of 52 months due to land acquisition and law & order issues, the projects 'Sonapur to Guwahti (AS-3), NHAI' and 'Four Laning of Orissa Chattishgarh Border NHAI' have reported additional delay of 3 and 6 months respectively, the projects 'Nagpur-Wainganga Bridge NHAI' and 'Delhi Agra Approved Length 180.0 km, NHAI' have reported additional delay of 12 months each, the projects 'Walajapet Poonamalee km 106.8 to km 13.8, NHAI' and 'Ranchi-Rarga-Jamsethpur, NHAI' have reported additional delay of 16 months and 18 months respectively (however, no specific reasons have been reported by the project implementing agency for the delay in these projects).


- vii) In the **Power Sector**, out of 112 projects, 63 projects are delayed. During the month, 22 projects have reported additional delay in the range of 1-11 months. Out of 22 projects 15 projects are mega projects. One project has reported additional delay of 1 month due to land acquisition, 11 projects have reported additional delay of 3 months each due to severe RoW problem and forest clearance, 5 projects have reported additional delay of 6 months each due to severe RoW problem, the projects 'Eastern Region Strengthening Scheme-III, PGCIL', 'Establishment of Pooling Stations at Champa and Raigarh for IPP Generation Project in Chhattisgarh, PGCIL' have reported additional delay of 9 and 11 months respectively due to forest clearance and land acquisition, the projects 'System Strengthening Common for WR and NR (Line Bays and Reactor Provision) PGCIL', 'Transmission System Associated with Tehri Pump Storage Plant (PSP) PGCIL' have reported additional delay of 1 month each, the project 'Common Tr. Sys. Associated with East Coast and NCC Power Projects in Srikakulam Area A.P. PART- C PGCIL' has reported additional delay of 6 months (however, no specific reasons have been reported by the project implementing agencies for the delay in this project).

11. The status as on 30.04.2015 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.
12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	288	1
2	ROAD TRANSPORT AND HIGHWAYS	133	14
3	POWER	112	22
4	COAL	73	11
5	PETROLEUM	71	12
6	URBAN DEVELOPMENT	30	0
7	STEEL	26	1
8	CIVIL AVIATION	7	2
9	SHIPPING AND PORTS	6	0
10	ATOMIC ENERGY	4	0
11	TELECOMMUNICATIONS	4	0
12	FERTILISERS	1	0
13	MINES	1	0
14	PETROCHEMICALS	1	0
15	HEAVY INDUSTRY	1	0
	Total	758	63

Sectoral break up of on-going infrastructure projects.

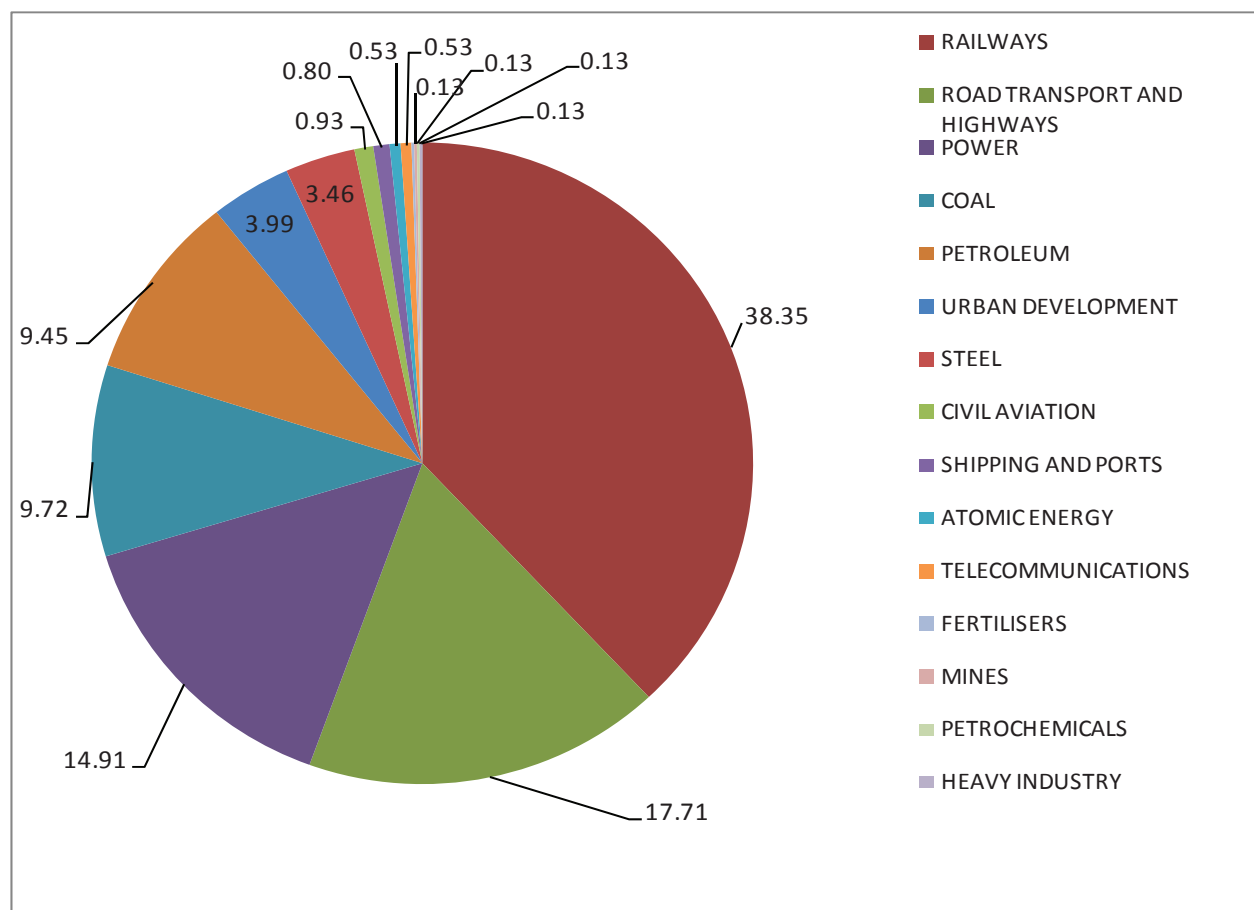

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2015-2016				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2015			
	<u>PETROLEUM</u>			
1	KOTA JOBNER PIPELINE PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000170]	276.26	12/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
2	PUNE-SHOLAPUR,PKG1 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000127]	1,110.00	05/2012	1,802.00


Summary of projects in the Flash Report for the month of April, 2015

Project Implementation - Current Status:

Number of Projects in Previous Month	751
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects elevated to the status of Major project during the current month	9
Number of Projects in Current Month	758


Brief Analysis

Project Status with respect to Original Schedule: Out of 758 projects, 2 projects are ahead of schedule, 120 projects are on schedule and 323 projects are delayed. Of the balance, 284 projects do not have fixed dates of commissioning while 29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

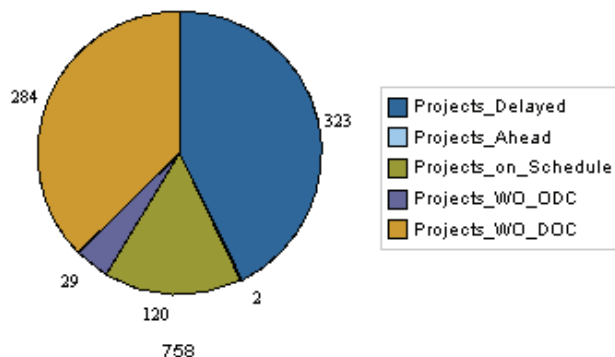

Investment Scenario

Total original cost of implementation of 758 projects when sanctioned, was of the order of Rs. 1069127.84 crore but this was subsequently revised to Rs. 1278256.35 crore implying a cost overrun of 19.6%. The expenditure incurred on these projects till April, 2015 is Rs. 546232.97 crore, which is 42.7% of the revised cost of the projects.

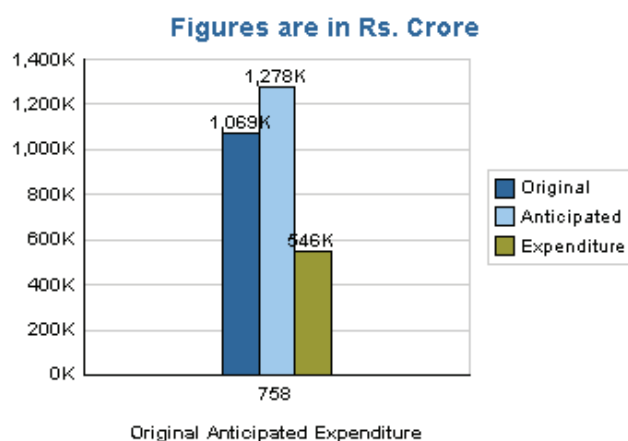

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	751
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	0
No of Projects in Current Month	758

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	323	2	120	29	284	758	42.61
Latest Approved (Date)	293	4	148	29	284	758	38.65

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	643	8,79,515.41	9,66,604.53	3,56,972.10	36.90	87,089.12	9.90
Project with Revision in Cost	115	2,52,970.86	3,11,651.82	1,89,260.87	60.70	58,680.96	23.20
Total	758	11,32,486.27	12,78,256.35	5,46,232.97	42.73	145770.08	12.87
Original Cost of All Projects							
Original Cost	758	10,69,127.84	12,78,256.35	5,46,232.97	42.73	2,09,128.51	19.56

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	323	561,446.59	678,495.08	402,406.87	59.30	117,048.49	20.80
Latest Approved (RCE)	295	545,029.09	606,866.48	374,172.27	61.70	61,837.39	11.30
Total	618	1,106,475.68	1,285,361.56	776,579.14	60.42	178885.88	16.17

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	63	85,175.26	90,741.52	53,083.96	58.50	5,566.26	6.50
Total	63	85,175.26	90,741.52	53,083.96	58.50	5566.26	6.54

Extent of cost overrun in projects with respect to original schedule(Sector Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	37.71
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	3	1,005.21	1,121.63	11.58
3	COAL	73	58,516.59	62,364.85	6.58	6	8,198.48	12,644.78	54.23
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	26	62,807.52	66,521.92	5.91	2	9,035.00	12,779.40	41.44
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	80.08
8	PETROLEUM	71	157,059.07	171,085.92	8.93	18	69,659.14	89,819.80	28.94
9	POWER	112	317,040.36	356,191.36	12.35	23	55,001.54	94,152.54	71.18
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS	288	163,518.20	291,060.49	78.00	161	86,817.46	215,415.19	148.12
12	ROAD TRANSPORT AND HIGHWAYS	133	98,941.44	101,089.44	2.17	10	3,146.62	5,322.13	69.14
13	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	3	1,623.67	2,433.22	49.86
14	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
Total		758	1,069,127.84	1,278,256.35	19.56	231	264,723.73	481,905.51	82.04

Extent of cost overrun in projects with respect to original schedule(State Wise)									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	27	24,854.07	31,076.50	25.04	7	11,072.36	17,294.79	56.20
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	3	9,356.22	23,263.83	148.65
3	ASSAM	36	23,508.04	42,053.86	78.89	16	17,045.87	35,709.35	109.49
4	BIHAR	49	58,759.98	72,729.61	23.77	16	14,639.50	29,268.75	99.93
5	GOA	1	335.61	388.53	15.77	1	335.61	388.53	15.77
6	GUJARAT	29	36,037.34	36,616.51	1.61	4	1,202.26	2,117.22	76.10
7	HARYANA	8	4,259.81	6,230.43	46.26	3	1,633.56	3,604.18	120.63
8	HIMACHAL PRADESH	5	11,681.24	19,906.33	70.41	3	9,493.62	17,718.71	86.64
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	2	6,142.04	25,062.72	308.05
10	KARNATAKA	32	64,122.20	79,084.94	23.33	17	13,700.79	28,669.56	109.25
11	KERALA	13	24,457.67	28,611.45	16.98	5	16,205.39	20,359.17	25.63
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	4	2,144.95	4,548.31	112.05
13	MAHARASHTRA	45	98,588.94	110,362.81	11.94	12	23,983.77	36,309.67	51.39
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	803.12
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	1	4,083.02	5,307.90	30.00
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	325.27
17	NAGALAND	2	5,124.00	7,461.12	45.61	2	5,124.00	7,461.12	45.61
18	ODISHA	42	72,202.55	81,290.49	12.59	14	35,439.50	44,548.78	25.70
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	0.00
20	RAJASTHAN	24	25,362.46	25,417.93	0.22	6	2,574.16	3,142.63	22.08
21	SIKKIM	2	1,648.94	4,499.46	172.87	1	1,339.48	4,190.00	212.81
22	TAMIL NADU	41	67,950.69	85,496.01	25.82	20	30,028.23	47,573.55	58.43
23	TRIPURA	6	2,966.26	6,629.97	123.51	5	2,678.22	6,376.31	138.08
24	UTTAR PRADESH	30	36,706.01	39,810.35	8.46	9	2,951.38	6,103.98	106.82
25	WEST BENGAL	39	42,838.90	52,831.79	23.33	13	8,447.62	18,669.36	121.00
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	8.19
27	DELHI	11	50,123.12	50,123.12	0.00	0	0.00	0.00	0.00
28	CHHATTISGARH	28	80,681.93	82,344.09	2.06	6	3,494.57	5,157.03	47.57
29	JHARKHAND	33	36,123.28	36,767.77	1.78	5	1,380.26	2,198.40	59.27
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,346.89	10,900.21	48.37
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	0.00
32	TELANGANA	21	9,410.62	12,180.44	29.43	6	1,903.46	4,673.28	145.52
33	MULTI STATE	187	218,287.38	244,588.58	12.05	42	28,809.38	60,026.46	108.36
Total		758	1,069,127.84	1,278,256.35	19.56	231	264,723.73	481,905.51	82.04

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	16 - 78
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	4	1,323.34	1,386.84	1 - 77
3	COAL	73	58,516.59	62,364.85	6.58	41	30,244.21	34,252.27	1 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	26	62,807.52	66,521.92	5.91	16	55,763.54	59,332.54	8 - 69
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38 - 38
8	PETROLEUM	71	157,059.07	171,085.92	8.93	46	96,164.54	107,538.43	4 - 110
9	POWER	112	317,040.36	356,191.36	12.35	63	147,954.14	178,090.47	2 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS	288	163,518.20	291,060.49	78.00	32	28,013.16	83,178.76	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	133	98,941.44	101,089.44	2.17	99	74,999.80	77,150.70	6 - 126
13	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	-
14	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	16	82,471.25	82,471.25	2 - 37
Total		758	1,069,127.84	1,278,256.35	19.56	323	561,446.59	678,495.08	

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>									
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	27	24,854.07	31,076.50	25.04	9	15,586.19	19,691.54	8 - 67
2	ARUNACHAL PRADESH	3	9,356.22	23,263.83	148.65	2	3,070.89	7,963.83	31 - 87
3	ASSAM	36	23,508.04	42,053.86	78.89	26	20,549.19	35,772.85	11 - 126
4	BIHAR	49	58,759.98	72,729.61	23.77	14	19,108.03	29,165.06	10 - 99
5	GOA	1	335.61	388.53	15.77	0	0.00	0.00	-
6	GUJARAT	29	36,037.34	36,616.51	1.61	10	23,853.58	23,776.89	14 - 48
7	HARYANA	8	4,259.81	6,230.43	46.26	3	2,244.00	3,424.00	28 - 62
8	HIMACHAL PRADESH	5	11,681.24	19,906.33	70.41	3	8,717.57	15,022.55	11 - 111
9	JAMMU AND KASHMIR	7	21,314.62	40,235.30	88.77	6	13,202.50	32,123.18	10 - 193
10	KARNATAKA	32	64,122.20	79,084.94	23.33	7	4,716.71	5,776.33	12 - 96
11	KERALA	13	24,457.67	28,611.45	16.98	4	2,774.06	3,474.06	18 - 65
12	MADHYA PRADESH	20	24,954.32	26,938.24	7.95	8	3,804.29	3,706.15	12 - 69
13	MAHARASHTRA	45	98,588.94	110,362.81	11.94	21	59,299.77	66,463.91	2 - 144
14	MANIPUR	1	727.56	6,570.75	803.12	1	727.56	6,570.75	96 - 96
15	MEGHALAYA	3	4,845.02	6,069.90	25.28	0	0.00	0.00	-
16	MIZORAM	2	988.06	4,201.96	325.27	2	988.06	4,201.96	47 - 123
17	NAGALAND	2	5,124.00	7,461.12	45.61	1	850.00	2,973.42	60 - 60
18	ODISHA	42	72,202.55	81,290.49	12.59	20	41,703.75	46,875.34	6 - 84
19	PUNJAB	3	792.50	765.46	-3.41	0	0.00	0.00	-
20	RAJASTHAN	24	25,362.46	25,417.93	0.22	10	19,145.38	18,699.10	9 - 84
21	SIKKIM	2	1,648.94	4,499.46	172.87	2	1,648.94	4,499.46	51 - 77
22	TAMIL NADU	41	67,950.69	85,496.01	25.82	19	54,157.00	61,780.41	3 - 90
23	TRIPURA	6	2,966.26	6,629.97	123.51	5	2,714.26	5,743.32	5 - 108
24	UTTAR PRADESH	30	36,706.01	39,810.35	8.46	12	15,417.45	17,324.13	9 - 93
25	WEST BENGAL	39	42,838.90	52,831.79	23.33	14	17,285.38	21,318.30	3 - 177
26	CHANDIGARH	1	452.00	489.00	8.19	1	452.00	489.00	1 - 1
27	DELHI	11	50,123.12	50,123.12	0.00	5	42,630.16	42,630.16	8 - 34
28	CHHATISGARH	28	80,681.93	82,344.09	2.06	14	55,685.34	56,167.39	9 - 72
29	JHARKHAND	33	36,123.28	36,767.77	1.78	19	12,682.27	13,201.47	2 - 138
30	UTTARAKHAND	6	9,351.89	12,905.21	38.00	4	7,605.06	11,048.24	26 - 94
31	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	0.00	0	0.00	0.00	-
32	TELANGANA	21	9,410.62	12,180.44	29.43	10	3,110.36	4,126.41	1 - 51
33	MULTI STATE	187	218,287.38	244,588.58	12.05	71	107,716.84	114,485.87	2 - 261
Total		758	1,069,127.84	1,278,256.35	19.56	323	561,446.59	678,495.08	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	3	36,950.00	41,049.00	16 - 78
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	4	1,323.34	1,386.84	1 - 77
3	COAL	73	58,516.59	62,364.85	6.58	38	22,766.95	26,775.01	1 - 84
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	-
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	-
6	STEEL	26	62,807.52	66,521.92	5.91	15	40,238.54	43,807.54	8 - 69
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38 - 38
8	PETROLEUM	71	157,059.07	171,085.92	8.93	28	69,021.98	76,179.57	4 - 73
9	POWER	112	317,040.36	356,191.36	12.35	60	142,063.89	166,843.77	2 - 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75 - 75
11	RAILWAYS	288	163,518.20	291,060.49	78.00	29	21,538.16	71,819.51	3 - 261
12	ROAD TRANSPORT AND HIGHWAYS	133	98,941.44	101,089.44	2.17	97	74,557.19	76,616.14	6 - 126
13	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	-
14	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	1	384.00	384.00	59 - 59
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	16	82,471.25	82,471.25	2 - 37
Total		758	1,069,127.84	1,278,256.35	19.56	293	498,493.91	600,993.45	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	42,627.00	46,726.00	9.62	1	13,171.00	17,270.00	31.12
2	CIVIL AVIATION	7	2,636.56	2,715.98	3.01	2	553.21	632.63	14.36
3	COAL	73	62,097.62	62,364.85	0.43	4	4,078.41	4,813.65	18.03
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0.00
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0.00
6	STEEL	26	66,406.52	66,521.92	0.17	1	343.00	488.40	42.39
7	PETROCHEMICALS	1	8,920.00	9,833.52	10.24	1	8,920.00	9,833.52	10.24
8	PETROLEUM	71	172,087.30	171,085.92	-0.58	6	20,981.61	23,955.34	14.17
9	POWER	112	339,587.61	356,191.36	4.89	5	17,399.92	34,003.67	95.42
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	122.78
11	RAILWAYS	288	176,325.78	291,060.49	65.07	155	91,569.27	207,575.25	126.69
12	ROAD TRANSPORT AND HIGHWAYS	133	99,055.39	101,089.44	2.05	9	2,929.01	5,012.57	71.14
13	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	3	1,623.67	2,433.22	49.86
14	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0.00
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	1	6,395.00	11,609.00	81.53
	Total	758	1,132,486.27	1,278,256.35	12.87	189	169,682.10	321,454.55	89.45

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	3,492.00	5,677.00	0- 0
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	0	0.00	0.00	0- 0
3	COAL	73	58,516.59	62,364.85	6.58	2	6,935.32	10,079.95	38- 72
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	26	62,807.52	66,521.92	5.91	1	8,692.00	12,291.00	67- 67
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38- 38
8	PETROLEUM	71	157,059.07	171,085.92	8.93	9	45,425.86	61,035.58	11- 110
9	POWER	112	317,040.36	356,191.36	12.35	12	24,428.77	39,474.49	10- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	0	0.00	0.00	0- 0
11	RAILWAYS	288	163,518.20	291,060.49	78.00	4	5,873.07	8,954.40	48- 174
12	ROAD TRANSPORT AND HIGHWAYS	133	98,941.44	101,089.44	2.17	2	425.61	517.56	68- 92
13	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		758	1069127.84	1278256.35	19.56	32	100733.24	147863.5	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	1	13,171.00	17,270.00	78- 78
2	CIVIL AVIATION	7	2,599.56	2,715.98	4.48	2	669.60	733.10	1- 6
3	COAL	73	58,516.59	62,364.85	6.58	4	7,617.44	12,014.74	30- 72
4	FERTILISERS	1	197.79	197.79	0.00	0	0.00	0.00	0- 0
5	MINES	1	1,856.00	1,856.00	0.00	0	0.00	0.00	0- 0
6	STEEL	26	62,807.52	66,521.92	5.91	1	8,692.00	12,291.00	67- 67
7	PETROCHEMICALS	1	5,460.61	9,833.52	80.08	1	5,460.61	9,833.52	38- 38
8	PETROLEUM	71	157,059.07	171,085.92	8.93	13	48,022.61	65,373.66	11- 110
9	POWER	112	317,040.36	356,191.36	12.35	22	48,716.21	78,852.54	5- 123
10	HEAVY INDUSTRY	1	1,718.00	3,827.30	122.78	1	1,718.00	3,827.30	75- 75
11	RAILWAYS	288	163,518.20	291,060.49	78.00	27	22,133.70	77,530.00	3- 261
12	ROAD TRANSPORT AND HIGHWAYS	133	98,941.44	101,089.44	2.17	10	3,146.62	5,322.13	43- 103
13	SHIPPING AND PORTS	6	5,158.07	5,759.15	11.65	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	4	15,131.81	15,131.81	0.00	0	0.00	0.00	0- 0
15	URBAN DEVELOPMENT	30	138,680.82	143,894.82	3.76	0	0.00	0.00	0- 0
Total		758	1069127.84	1278256.35	19.56	82	159347.79	283047.99	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	KOTA JOBNER PIPELINE PROJECT	04/2011	276.26	12/2015	276.27	03/2015	241.63
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
2	PUNE-SHOLAPUR,PKG1	11/2009	1,110.00	05/2012	1,110.00	05/2012	1,802.00

Milestones (Cumulative due & achieved)

Total	3753
Achieved up to month	1500

List of projects reporting additional delays							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>CIVIL AVIATION</u>						
1	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS AAI	344.28	344.28	03/2014	04/2015	05/2015	1
2	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT AAI	309.46	309.46	01/2011	06/2016	06/2017	12
	<u>COAL</u>						
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW NLC	4,904.54	6,602.74	03/2012	04/2015	05/2015	1
4	RCE OF INDARAM OCP(1.20 MTPA) SCCL	162.76	162.76	03/2015	03/2015	04/2015	1
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,477.21	06/2009	04/2015	06/2015	2
6	BLOCK-B OCP NCL (3.5 MTY) NCL	746.04	535.10	03/2015	03/2015	03/2016	12

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
7	RG OC -III EXTENSION (PHASE -II) PROJECT SCCL	365.01	365.01	06/2015	03/2016	03/2017	12
8	RKP OCP PHASE-I SCCL	209.78	209.78	03/2015	03/2015	04/2016	13
9	PURNADIH OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2015	03/2017	24
10	JAGANNATHPOR OC SECL	152.43	152.43	03/2015	03/2017	03/2020	36
11	PENGANGA OCP(REVISED) WCL	441.82	441.82	03/2020	03/2016	03/2020	48
12	KARTALI (EAST) OCP (2.50 MTY) SECL	178.44	178.44	03/2014	03/2016	03/2020	48
13	MOONIDIH XV SEAM UG BCCL	1,230.27	1,230.27	04/2015	04/2015	04/2019	48
	<u>STEEL</u>						
14	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH SAIL	332.65	332.65	08/2014	06/2015	11/2015	5
	<u>PETROLEUM</u>						
15	DEVELOPMENT OF CLUSTER-7 FIELDS ONGC	4,550.40	6,638.94	03/2013	03/2015	05/2015	2
16	CONSTRUCTION OF 6 ETPS ONGC	317.64	240.95	09/2012	10/2015	12/2015	2
17	DEVELOPMENT OF C-26 CLUSTER FIELDS ONGC	2,592.17	2,592.17	05/2014	03/2016	05/2016	2
18	IOR OF B-173A FIELD ONGC	352.49	352.49	03/2014	03/2016	05/2016	2
19	IMPROVED OIL RECOVERY OF B-173A FIELD ONGC	352.49	352.49	03/2014	03/2016	05/2016	2
20	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA ONGC	288.04	253.66	08/2012	03/2015	06/2015	3
21	LPG TERMINAL AT KOCHI IOCL	607.06	607.06	01/2016	04/2017	07/2017	3
22	PARADIP HALDIA DURGAPUR LPG PIPELINE IOCL	913.00	913.00	08/2015	12/2015	06/2016	6
23	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) GAIL	463.32	463.32	06/2011	07/2015	03/2016	8
24	RECONSTRUCTION OF BPA AND BPB PLATFORMS ONGC	1,138.50	686.58	04/2015	04/2015	12/2015	8
25	RESID UPGRADATION PROJECT CPCL	3,110.36	3,110.36	11/2015	11/2015	07/2016	8


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
26	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD ONGC	600.17	600.17	12/2014	05/2015	05/2016	12
	<u>POWER</u>						
27	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHHATTISGARH PGCIL	1,366.34	1,606.38	12/2013	05/2015	06/2015	1
28	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) PGCIL	213.78	213.78	03/2014	04/2015	05/2015	1
29	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) PGCIL	871.62	871.62	11/2017	10/2017	11/2017	1
30	WESTERN REGION STRENGTHENING SCHEME-V PGCIL	477.69	721.81	09/2010	12/2015	03/2016	3
31	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B PGCIL	4,404.57	4,404.57	01/2015	12/2015	03/2016	3
32	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME PGCIL	965.58	965.58	11/2012	12/2015	03/2016	3
33	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH PGCIL	2,127.51	2,127.51	07/2014	12/2015	03/2016	3
34	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,746.65	2,228.70	08/2014	12/2015	03/2016	3
35	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	12/2015	03/2016	3
36	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B PGCIL	1,927.16	1,927.16	10/2014	06/2015	09/2015	3
37	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	9,569.76	9,569.76	06/2015	12/2015	03/2016	3
38	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B PGCIL	3,201.44	3,201.44	10/2014	12/2015	03/2016	3
39	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID PGCIL	1,263.26	1,263.26	11/2014	06/2015	09/2015	3
40	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B PGCIL	2,514.88	2,514.88	12/2015	12/2015	03/2016	3


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
41	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A PGCIL	2,074.86	2,348.37	03/2013	06/2015	12/2015	6
42	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B PGCIL	1,585.12	1,585.12	11/2013	06/2015	12/2015	6
43	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L PGCIL	1,940.13	1,940.13	09/2014	12/2015	06/2016	6
44	SYTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	09/2015	03/2016	6
45	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV PGCIL	297.33	346.79	08/2014	06/2015	12/2015	6
46	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C PGCIL	514.20	514.20	06/2015	06/2015	12/2015	6
47	EASTERN REGION STRENGTHENING SCHEME- III PGCIL	1,272.80	1,272.80	11/2012	03/2016	12/2016	9
48	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	1,961.87	1,961.87	05/2014	04/2015	03/2016	11
	<u>RAILWAYS</u>						
49	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,069.60	03/2014	03/2014	03/2016	24
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
50	GUWAHATI TO NALBARI (AS-4) NHAI	175.96	175.96	04/2008	04/2015	05/2015	1
51	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	03/2015	06/2015	3
52	SONAPUR TO GUWAHATI (AS-3) NHAI	245.00	245.00	03/2008	03/2015	06/2015	3
53	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	06/2015	09/2015	3
54	MURADABAD-BAREILLY NHAI	1,267.00	1,267.00	06/2013	03/2015	06/2015	3
55	FOUR LANING OF ORISSA CHATTISHGARH BORDER NHAI	1,232.00	1,232.00	08/2015	08/2015	02/2016	6
56	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) NHAI	624.00	624.00	04/2014	07/2015	03/2016	8

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
57	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 NHAI	1,987.00	1,987.00	07/2015	07/2015	06/2016	11
58	BAREILLY-SITAPUR (NH-24) NHAI	1,046.00	1,046.00	09/2013	12/2015	12/2016	12
59	NAGPUR-WAINGANGA BRIDGE NHAI	484.19	484.19	10/2014	03/2015	03/2016	12
60	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI	1,928.22	1,928.22	04/2015	04/2015	04/2016	12
61	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 NHAI	1,287.95	1,287.95	11/2015	11/2015	03/2017	16
62	RANCHI-RARGA-JAMSETHPUR NHAI	1,479.00	1,479.00	06/2015	06/2015	12/2016	18
63	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 NHAI	1,693.75	1,693.75	08/2011	08/2011	12/2015	52

Graphical Presentation of All Projects w.r.t. Original Schedule

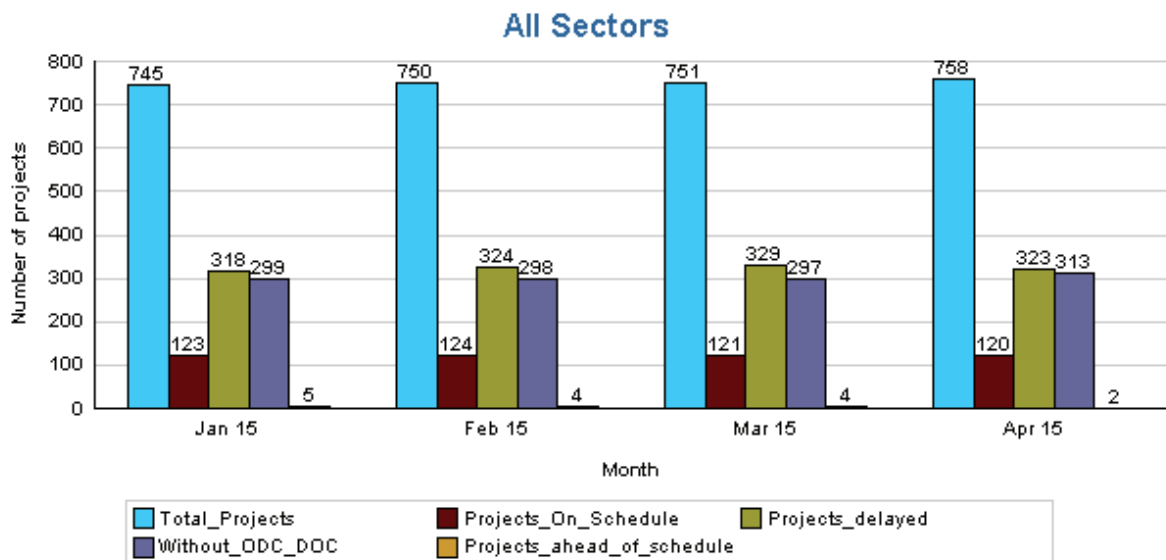


Break-up of 323 Delayed projects in April 2015

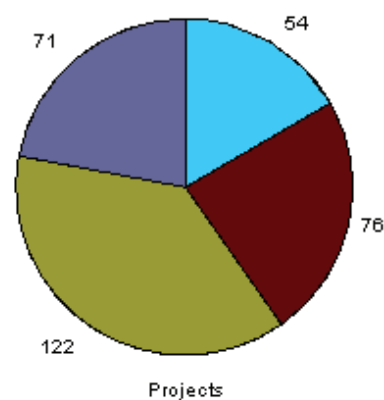


Delay in Months: 1-12 13-24 25-60 MORE THAN 60


Graphical Presentation of All Projects w.r.t. Revised Schedule

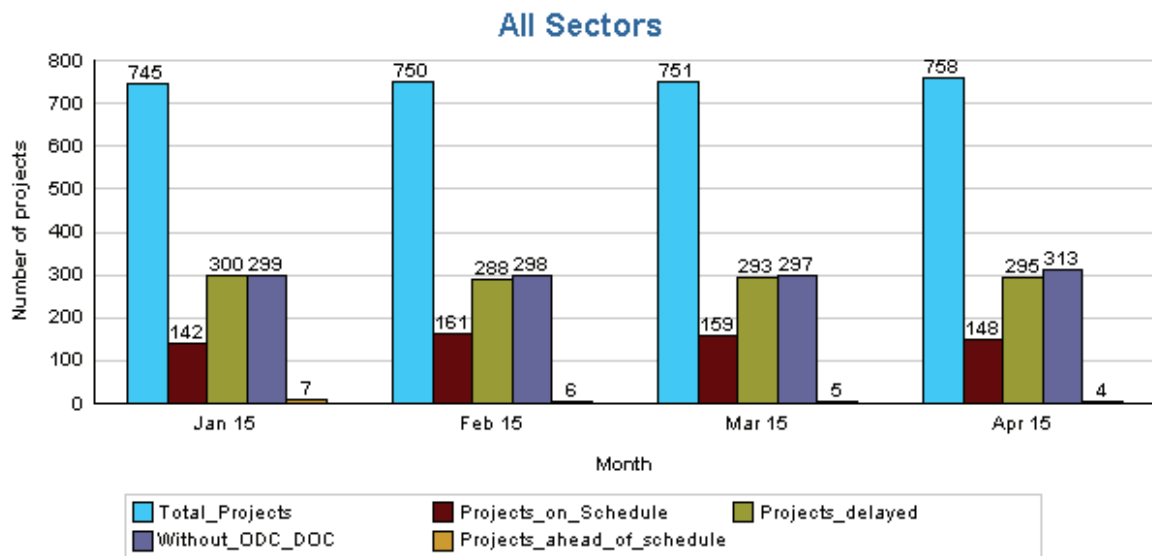


Break-up of 295 Delayed projects in April 2015

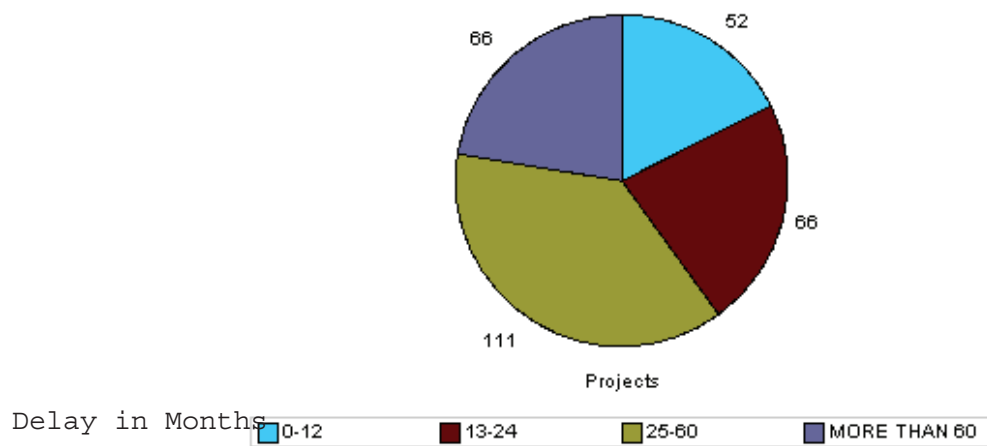


Graphical Presentation of ATOMIC ENERGY Sector

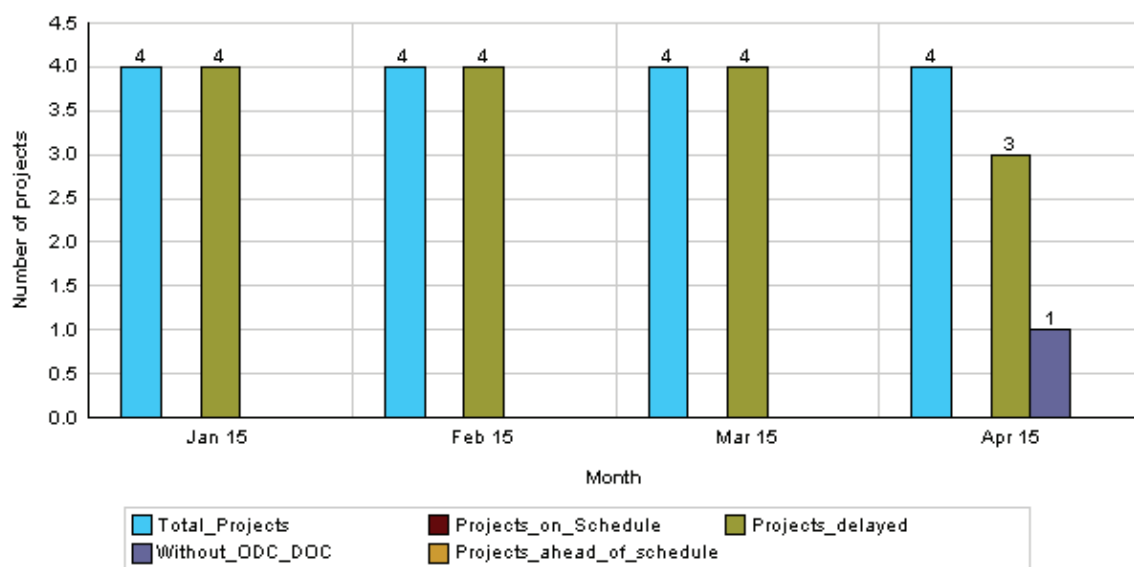


Break-up of 3 Delayed projects in April 2015

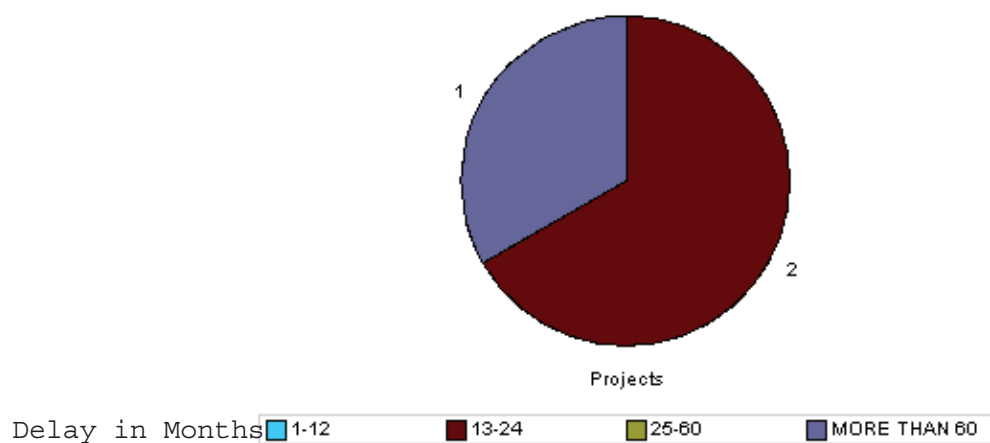


Graphical Presentation of CIVIL AVIATION Sector

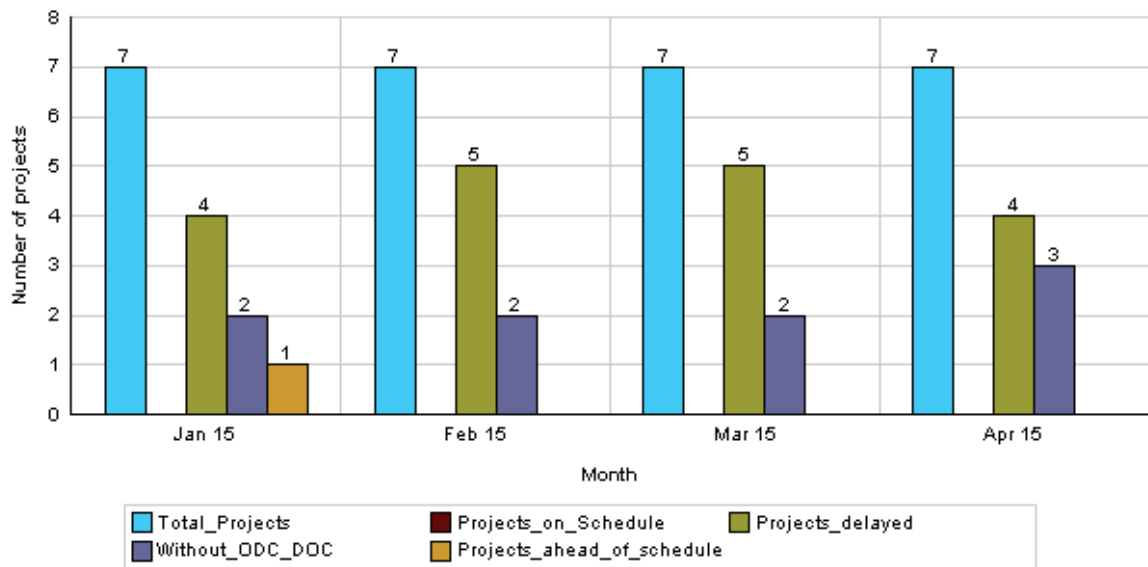


Break-up of 4 Delayed projects in April 2015

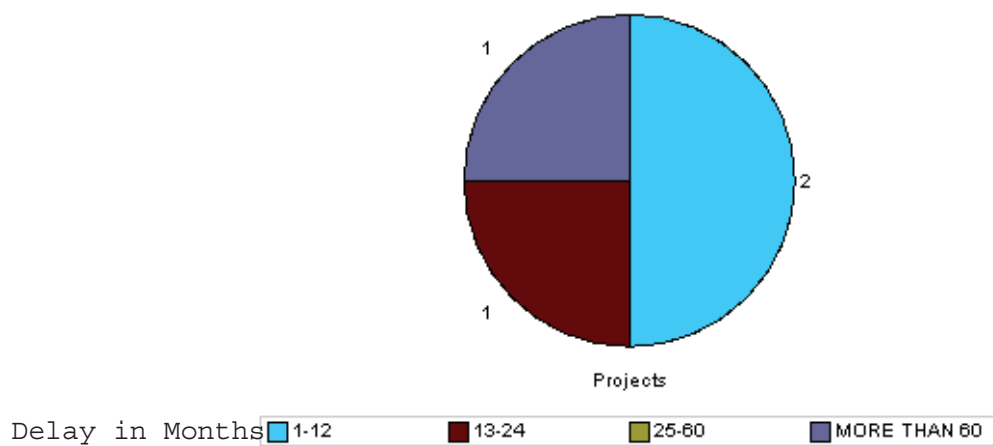


Graphical Presentation of COAL Sector

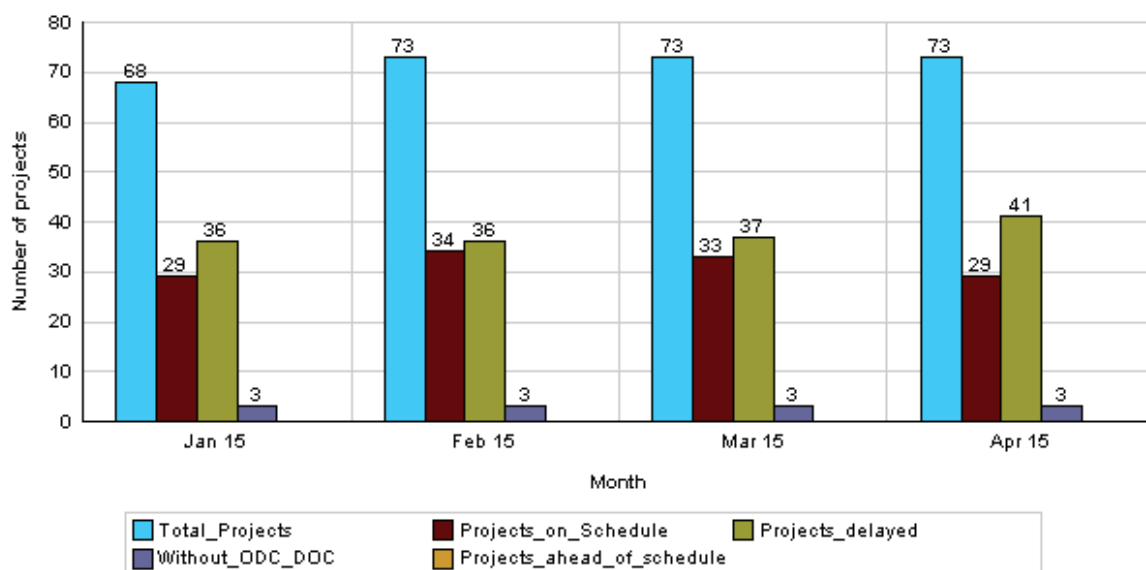


Break-up of 41 Delayed projects in April 2015

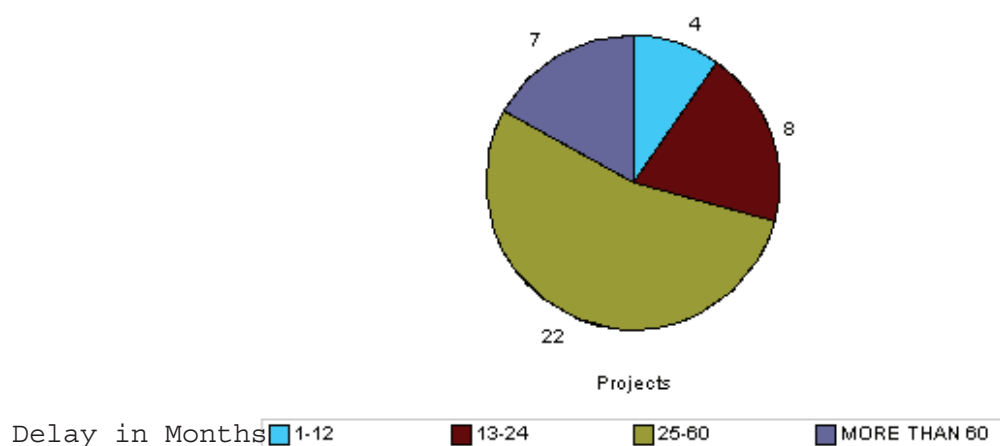


Graphical Presentation of STEEL Sector

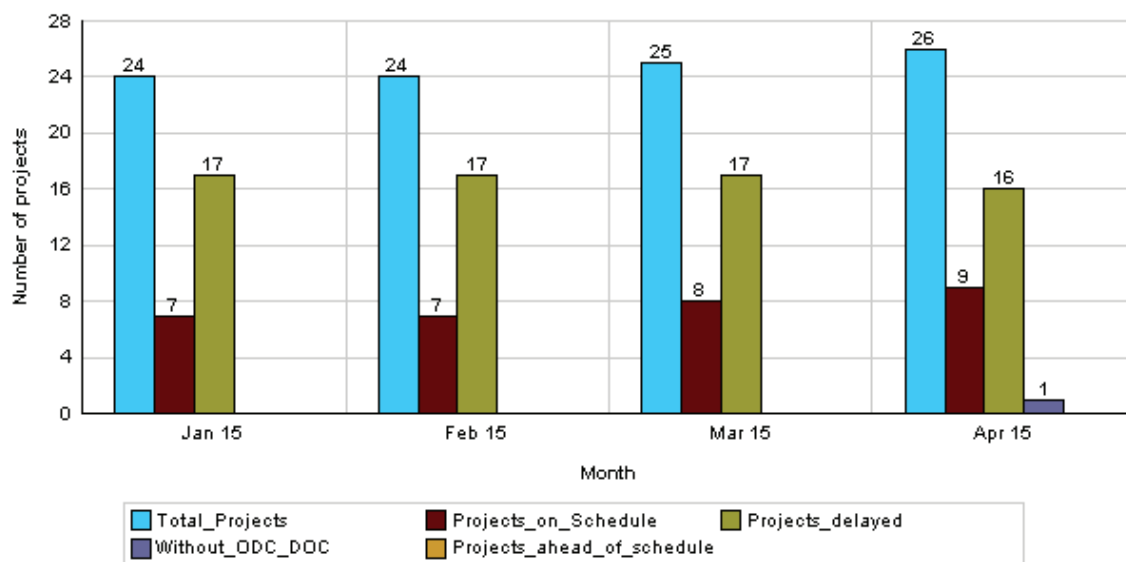


Break-up of 16 Delayed projects in April 2015

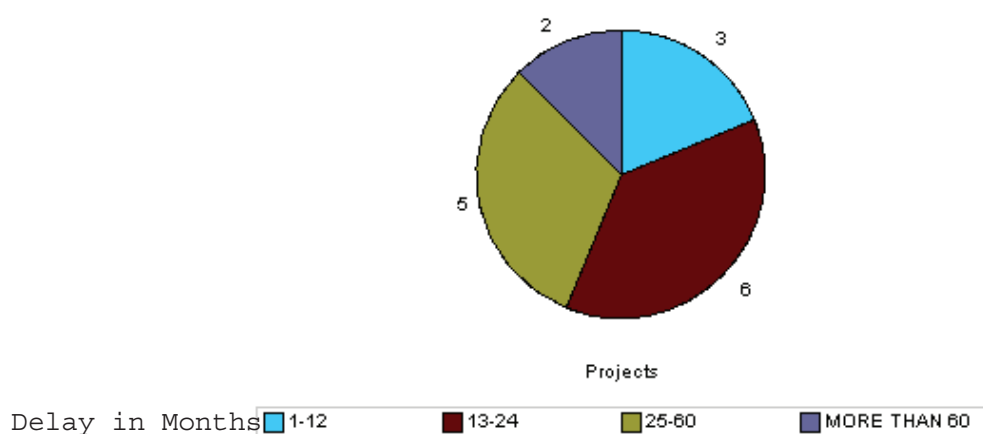


Graphical Presentation of PETROCHEMICALS Sector

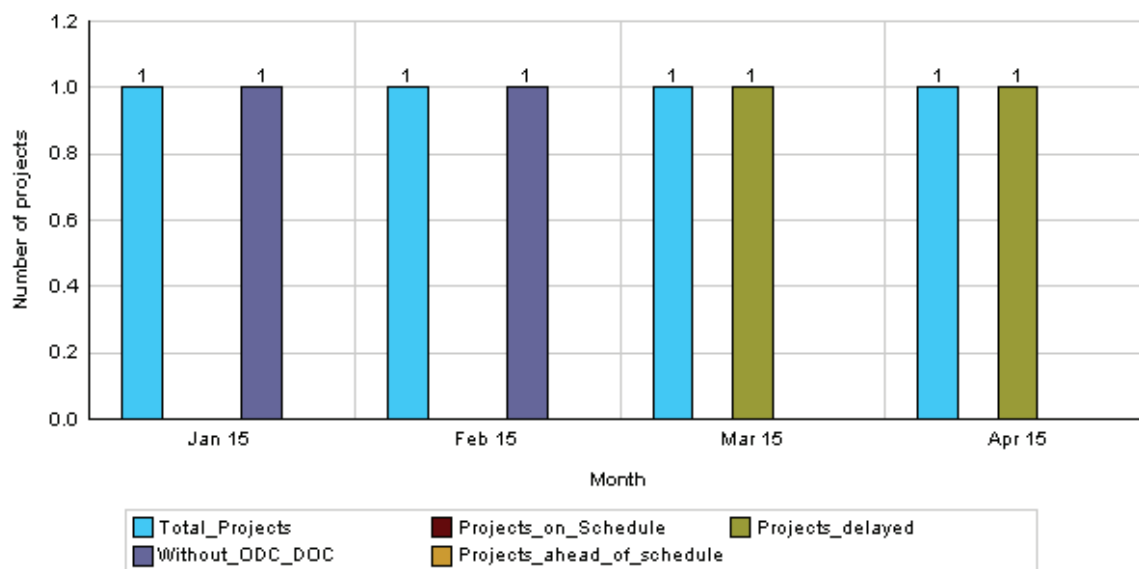


Break-up of 1 Delayed projects in April 2015

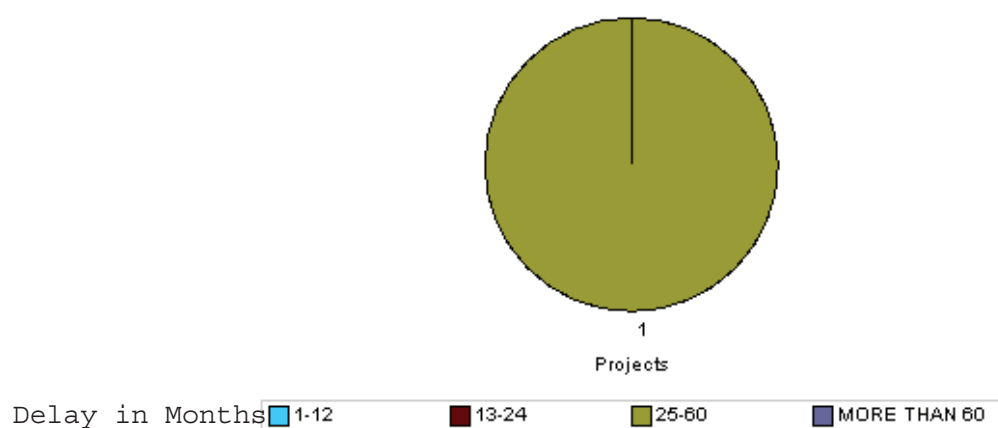


Graphical Presentation of PETROLEUM Sector

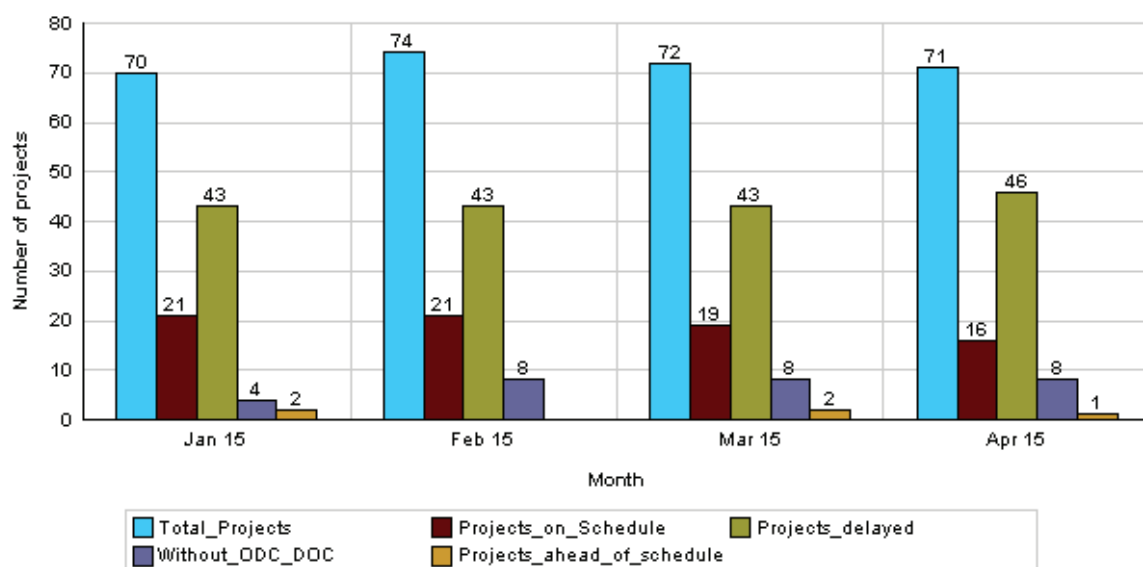


Break-up of 46 Delayed projects in April 2015

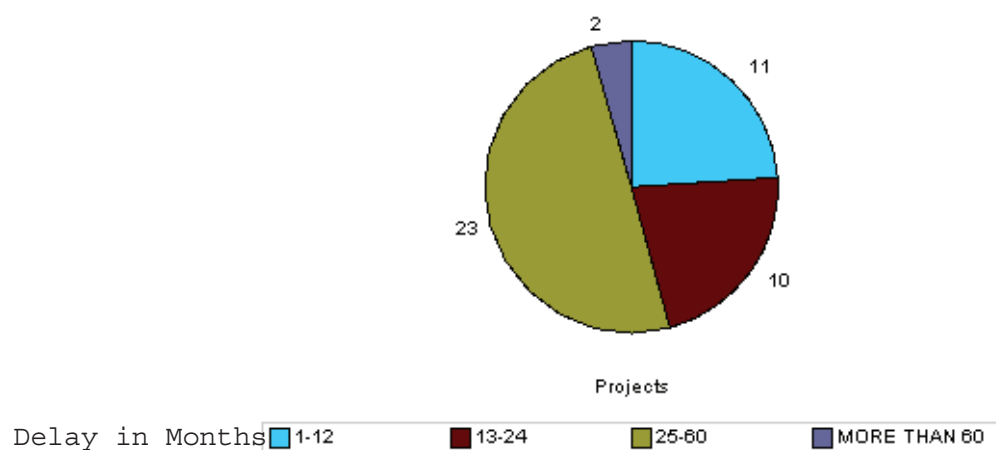

Graphical Presentation of POWER Sector

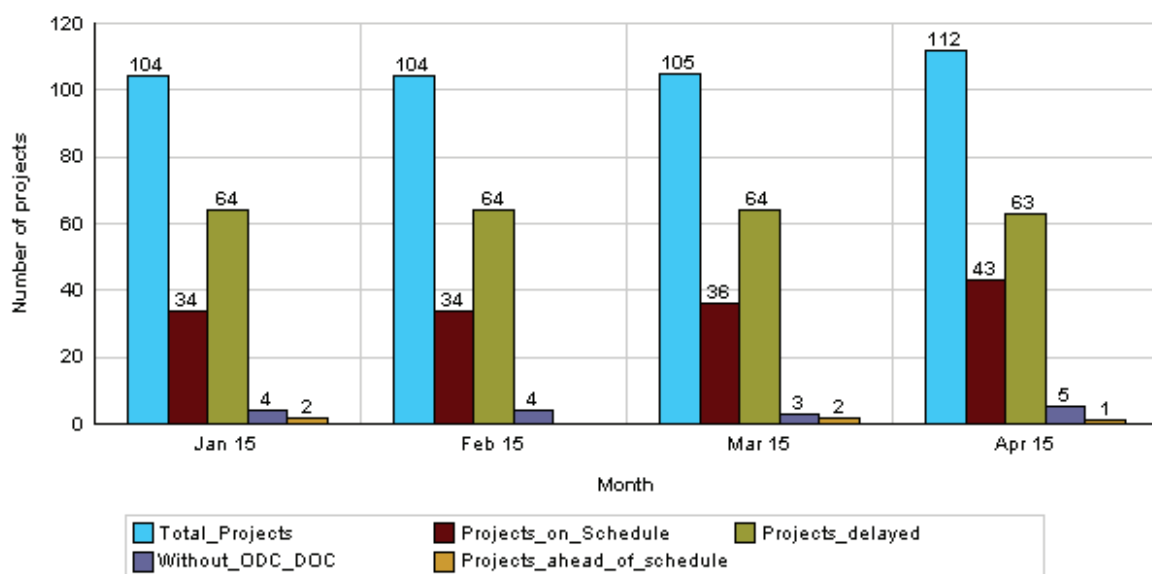


Break-up of 63 Delayed projects in April 2015

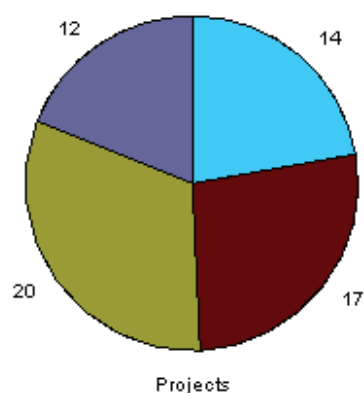


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

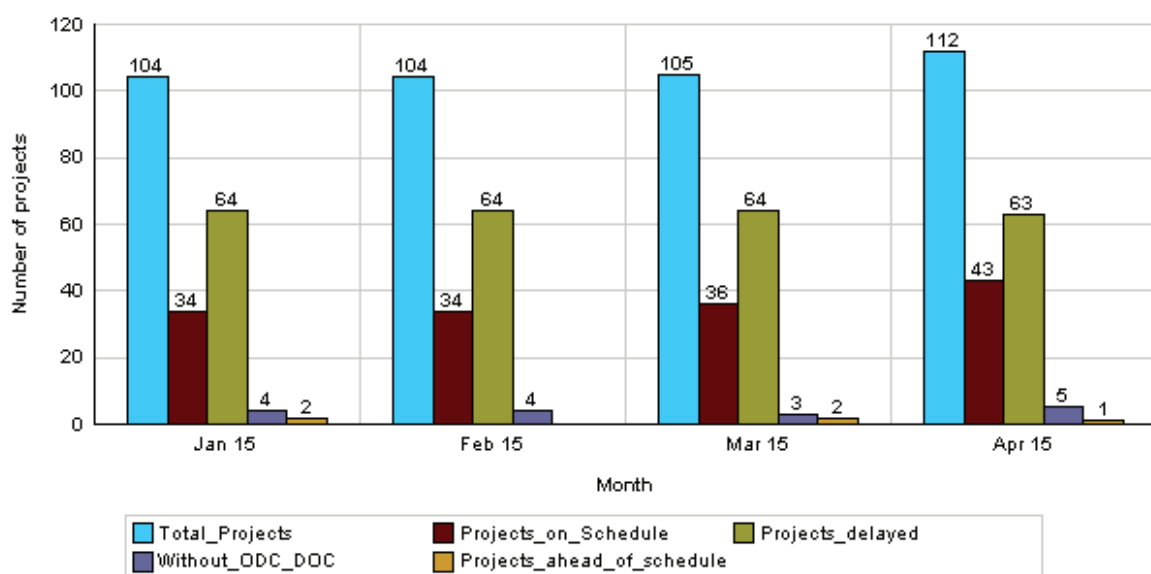


Break-up of 63 Delayed projects in April 2015

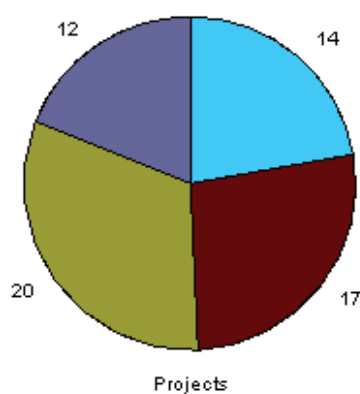


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60


Graphical Presentation of RAILWAYS Sector

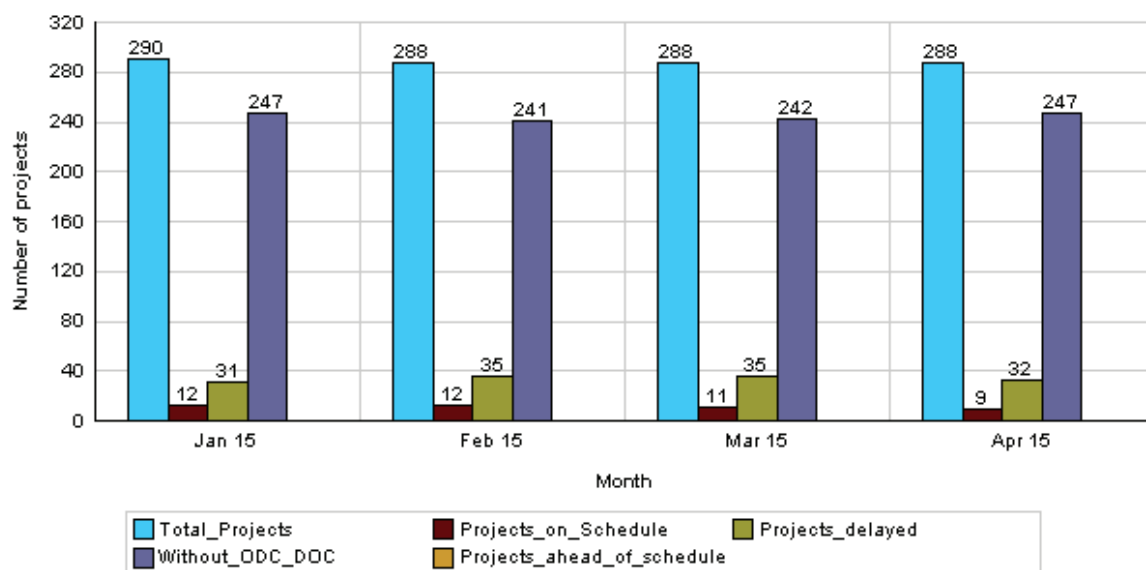


Break-up of 32 Delayed projects in April 2015

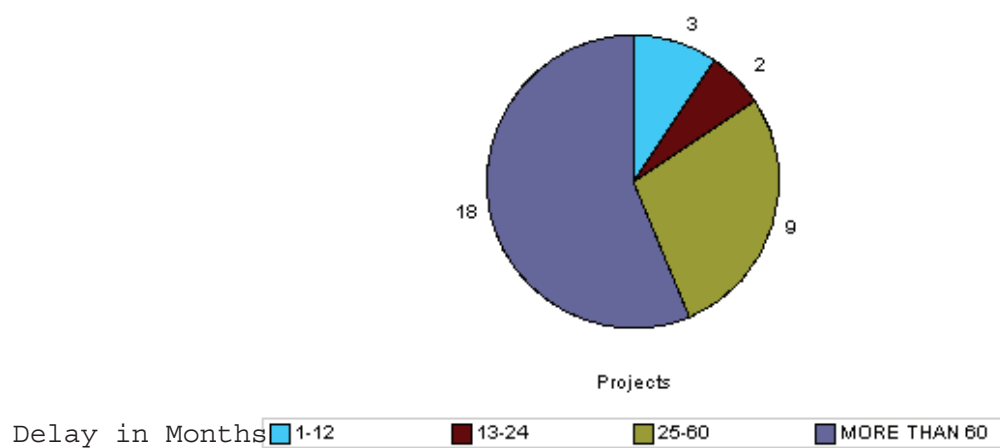


Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

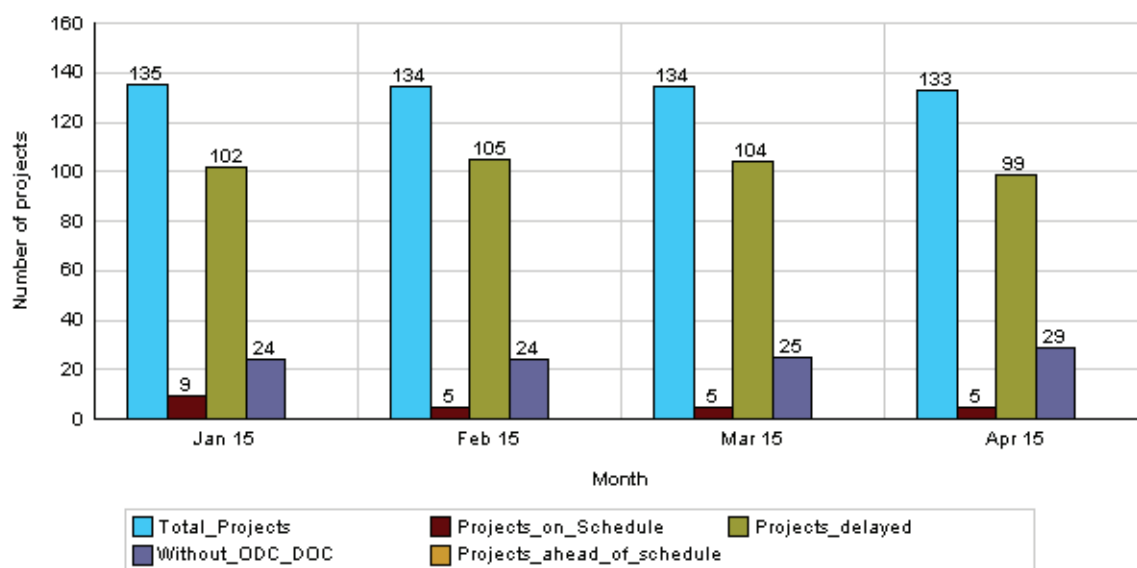


Break-up of 99 Delayed projects in April 2015

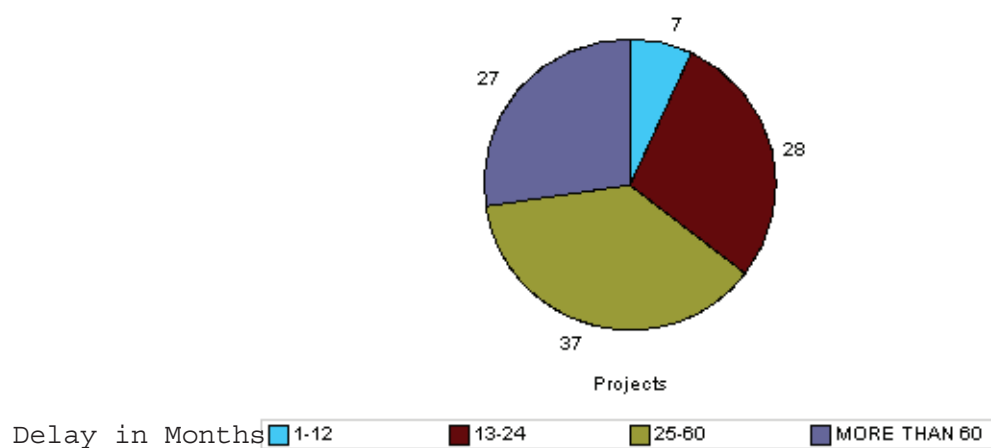


Graphical Presentation of TELECOMMUNICATIONS Sector

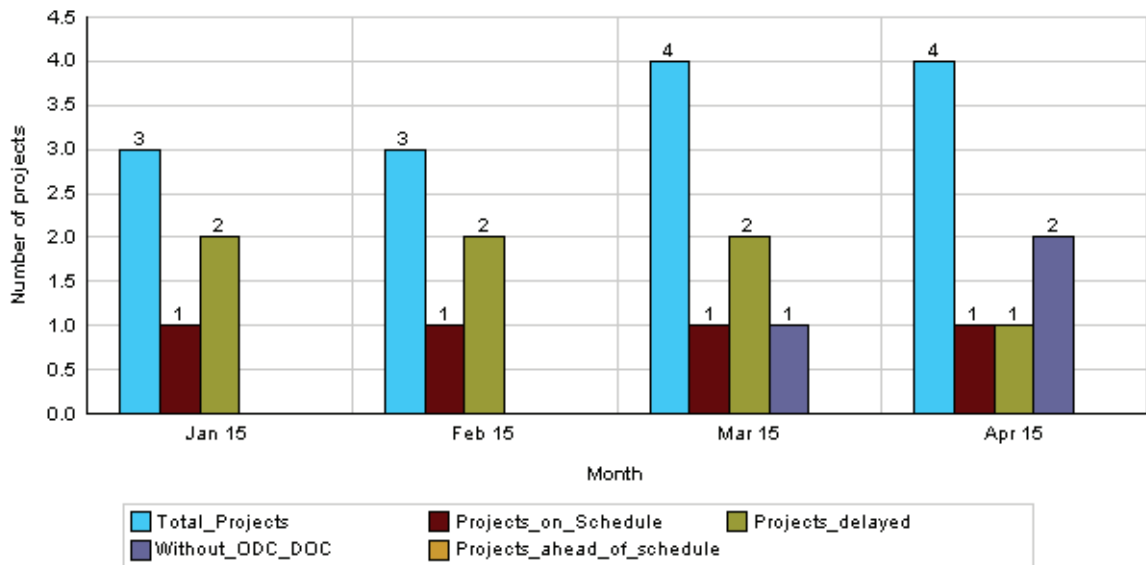


Break-up of 1 Delayed projects in April 2015

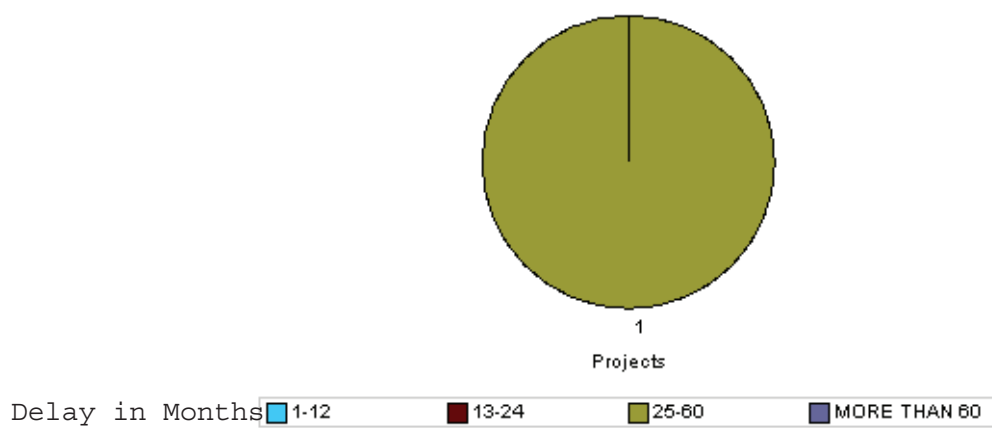

Graphical Presentation of URBAN DEVELOPMENT Sector

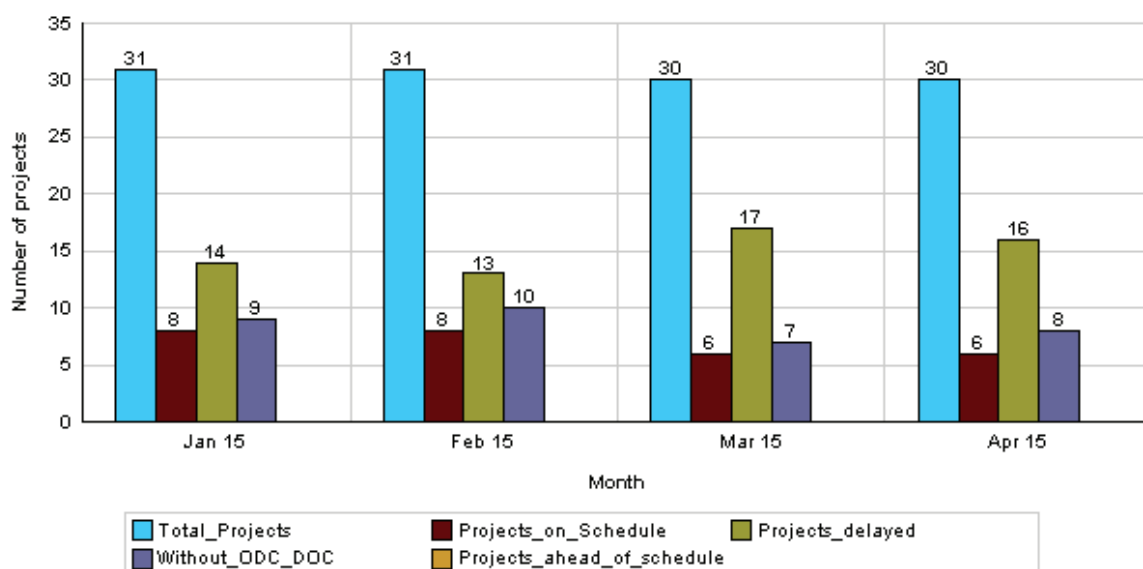

Break-up of 16 Delayed projects in April 2015

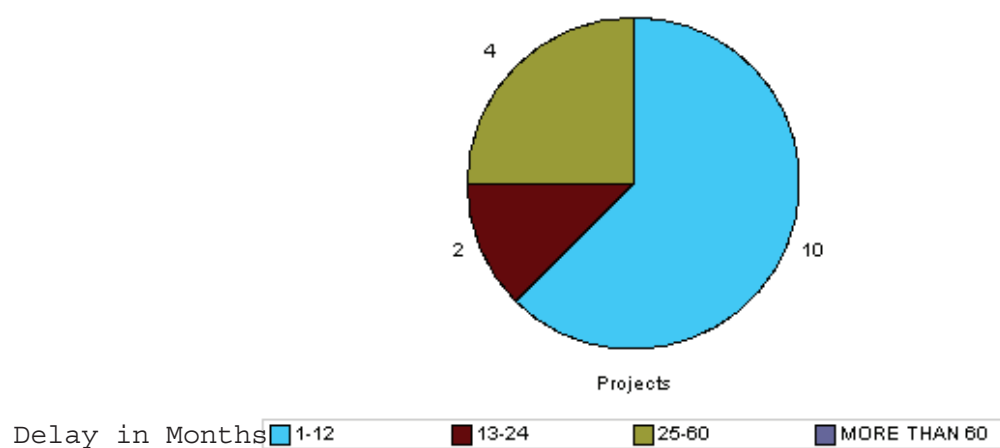

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	42,627.00	46,726.00	33,594.77
CIVIL AVIATION	7	2,599.56	2,636.56	2,715.98	1,637.71
COAL	73	58,516.59	62,097.62	62,364.85	21,734.85
FERTILISERS	1	197.79	197.79	197.79	13.09
MINES	1	1,856.00	1,856.00	1,856.00	0.00
STEEL	26	62,807.52	66,406.52	66,521.92	43,850.05
PETROCHEMICALS	1	5,460.61	8,920.00	9,833.52	8,595.08
PETROLEUM	71	157,059.07	172,087.30	171,085.92	75,485.57
POWER	112	317,040.36	339,587.61	356,191.36	157,703.34
HEAVY INDUSTRY	1	1,718.00	1,718.00	3,827.30	0.00
RAILWAYS	288	163,518.20	176,325.78	291,060.49	94,834.18
ROAD TRANSPORT AND HIGHWAYS	133	98,941.44	99,055.39	101,089.44	84,497.00
SHIPPING AND PORTS	6	5,158.07	5,158.07	5,759.15	2,393.83
TELECOMMUNICATIONS	4	15,131.81	15,131.81	15,131.81	254.59
URBAN DEVELOPMENT	30	138,680.82	138,680.82	143,894.82	21,638.91
Grand total	758	1,069,127.84	1,132,486.27	1,278,256.35	546,232.97

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00	11,459.00	6,297.00	12/2015	10/2017	22(O)	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00	17,270.00	18,271.00	12/2008	06/2015	78(O)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, TAMIL NADU	09/2003	3,492.00	5,677.00	4,967.77	09/2010	-	-	12/88
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00	12,320.00	4,059.00	12/2016	04/2018	16(O)	4/69
	Total		40,442.00	46,726.00	33,594.77				60/329
	CIVIL AVIATION								
5	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46	309.46	338.82	01/2011	06/2017	77(O)	0/0
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	17.82	-	09/2018	-	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61	388.53	297.58	05/2012	03/2015	-	0/0
8	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00	489.00	410.25	03/2015	04/2015	1(O)	0/0
9	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28	344.28	58.50	03/2014	05/2015	14(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI, MULTI STATE	09/2008	626.00	626.00	514.70	06/2013	-	-	0/0
11	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60	244.10	0.04	03/2015	09/2015	6(O)	0/0
	Total		2,599.56	2,715.98	1,637.71				0/0
	COAL								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34	1,228.39	879.85	03/2013	09/2015	30(O)	21/22
13	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97	335.97	30.30	03/2018	03/2018	0(O)	0/0
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	150.59	198.59	111.82	03/2016	03/2016	0(O)	3/7
15	AMLOHRI EPR (NCL) (6 MTY, INCR.) - [N06000010]NCL, MADHYA PRADESH	12/2009	1,352.04	1,143.54	778.30	03/2016	03/2016	0(O)	0/4
16	AMRAPALI OC(12MTY) - [N06000103]CCL, JHARKHAND	02/2012	858.11	858.11	101.90	03/2020	03/2020	0(O)	3/4

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60	481.60	-	03/2023	03/2023	0(O)	0/0
18	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28	207.28	172.80	03/2012	03/2017	60(O)	4/5
19	ASHOK EXPN OCP CCL (10 MTY) - [060100096]JCL,JHARKHAND	12/2007	471.66	341.63	117.84	03/2011	03/2017	72(O)	2/5
20	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08	172.08	148.02	03/2010	03/2017	84(O)	2/4
21	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56	258.56	74.44	03/2016	03/2016	0(O)	3/6
22	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	6.34	03/2019	03/2019	0(O)	1/9
23	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82	203.82	-	03/2015	03/2015	-	1/6
24	BHANEAGAON OC - [N06000121]WCL,MAHARASHTRA	02/2015	187.94	187.94	32.35	03/2023	03/2023	0(O)	0/21
25	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.10	490.10	186.68	03/2017	03/2017	0(O)	11/11
26	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH	05/2014	164.49	164.49	22.10	03/2020	03/2020	0(O)	0/0
27	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]MCL,MADHYA PRADESH	06/2011	746.04	535.10	367.12	03/2015	03/2016	12(O)	0/3
28	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.63	610.33	-	03/2022	03/2022	0(O)	1/7
29	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35	462.35	298.60	03/2014	03/2016	24(O)	5/9
30	CHURI BENTI UG (0.81 MTY) - [N06000083]JCL,JHARKHAND	08/2007	163.51	163.51	35.68	03/2011	03/2016	60(O)	0/4
31	DINESH OCP - [N06000118]WCL,MAHARASHTRA	11/2014	611.16	611.16	6.02	03/2020	03/2020	0(O)	0/15
32	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66	1,943.66	1,676.56	03/2014	03/2016	24(O)	10/13
33	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38	1,375.38	2.49	03/2021	03/2021	0(O)	1/9
34	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67	2,675.67	1,846.08	03/2014	03/2016	24(O)	11/16
35	GOKUL - [N06000120]WCL,MAHARASHTRA	11/2014	267.67	267.67	89.38	03/2018	03/2018	0(O)	0/18
36	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87	395.87	76.74	03/2015	03/2021	72(O)	2/13
37	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	479.53	118.94	03/2013	03/2017	48(O)	4/8
38	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA	05/2014	337.66	337.66	-	03/2019	03/2019	0(O)	2/6
39	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43	152.43	21.55	03/2015	03/2020	60(O)	1/7
40	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36(O)	4/13
41	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78	467.78	2.85	03/2013	-	-	6/83
42	JHANJRA R-VI SEAM PSLW - [N06000020]JCL,WEST BENGAL	11/2006	287.18	287.17	142.59	03/2011	03/2017	72(O)	5/15

Sector Wise Details

(April 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63	453.63	104.49	12/2012	03/2017	51(O)	11/44
44	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33	417.33	11.41	07/2016	03/2017	8(O)	6/28
45	KANCHAN OC EXPANSION - [N06000125]SECL, MADHYA PRADESH	12/2014	371.04	371.04	30.24	03/2021	03/2021	0(O)	0/0
46	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77	457.77	162.21	03/2013	03/2017	48(O)	8/9
47	KAPURIA UG(PSLW) - [N06000108]BCCL, JHARKHAND	08/2011	988.35	988.35	43.93	04/2017	04/2017	0(O)	0/0
48	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	69.64	03/2014	03/2017	36(O)	2/4
49	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44	178.44	-	03/2014	03/2020	72(O)	1/7
50	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA, 6MTPA INCREMENTAL) - [N06000091]NCL, UTTAR PRADESH	06/2011	1,131.28	1,131.28	77.88	03/2018	03/2018	0(O)	0/4
51	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29	242.29	0.06	03/2015	03/2018	36(O)	0/5
52	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88	741.62	466.94	03/2013	03/2016	36(O)	0/2
53	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03	289.03	-	03/2018	03/2018	0(O)	1/5
54	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL, ODISHA	01/2005	302.96	302.96	132.68	03/2010	03/2017	84(O)	8/10
55	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL, CHHATISGARH	08/2013	7,612.33	7,612.33	764.09	03/2023	03/2023	0(O)	1/16
56	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	469.78	706.40	55.30	07/2012	03/2016	44(O)	1/3
57	MAKARDHOKRA I OC - [N06000119]WCL, MAHARASHTRA	09/2014	266.23	266.23	70.90	03/2021	03/2021	0(O)	0/23
58	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50	321.50	211.71	03/2014	03/2016	24(O)	3/6
59	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48(O)	4/6
60	MOONIDH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27	1,230.27	84.78	04/2015	04/2019	48(O)	0/0
61	MURADH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88	339.88	-	04/2014	03/2016	23(O)	0/0
62	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11	5,907.11	845.30	12/2015	04/2018	28(O)	10/35
63	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40	259.40	12.53	03/2012	03/2016	48(O)	0/2
64	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL, JHARKHAND	02/2014	555.52	555.52	-	03/2021	03/2021	0(O)	0/0
65	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	83.27	03/2012	03/2017	60(O)	1/3
66	PELMA OCP(15.00MTY) - [N06000045]SECL, CHHATISGARH	11/2014	1,624.59	1,624.59	0.46	03/2023	03/2023	0(O)	1/1
67	PENGANGA OCP(REVISED) - [N06000066]WCL, MAHARASHTRA	09/2014	441.82	441.82	104.36	03/2020	03/2020	0(O)	0/27

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	PURNADIIH OCP (3.0 MTY) - [N06000085]JCL,JHARKHAND	07/2008	210.98 -	210.98	186.69	03/2013 -	03/2017	48(O) -	2/4
69	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	55.48	03/2014 -	03/2016	24(O) -	3/9
70	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	106.44	03/2021 -	03/2021	0(O) -	0/0
71	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCL,JHARKHAND	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016	0(O) -	2/4
72	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	326.51	03/2012 -	03/2016	48(O) -	0/2
73	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	04/2015	1(O) -	4/29
74	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45 -	431.45	69.94	03/2016 -	03/2016	0(O) -	6/39
75	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	03/2017	21(O) -	4/51
76	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	75.31	03/2015 -	04/2016	13(O) -	8/31
77	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	71.00	03/2012 -	-	-	27/42
78	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA	05/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026	0(O) -	3/15
79	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	148.67	03/2018 -	03/2018	0(O) -	1/10
80	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.36	03/2016 -	03/2020	48(O) -	2/11
81	TAPIN OCP (2.5 MTY) - [N06000086]JCL,JHARKHAND	08/2008	264.68 -	264.68	149.41	03/2012 -	03/2016	48(O) -	2/4
82	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,477.21	3,207.92	06/2009 03/2013	06/2015	72(O) 27(R)	22/23
83	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,175.16	03/2012 05/2014	05/2015	38(O) 12(R)	28/39
84	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]NLC,TAMIL NADU	04/2012	364.75 -	364.75	131.44	10/2014 -	06/2015	8(O) -	8/11
	Total		58,516.59 -	62,364.85	21,734.85				283/907
	<u>FERTILISERS</u>								
85	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 -	197.79	13.09	11/2016 -	11/2016	0(O) -	0/0
	Total		197.79 -	197.79	13.09				0/0
	<u>MINES</u>								
86	EXPANSION OF MALANJKHAND MINE- DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]JCL,MADHYA PRADESH	09/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017	0(O) -	0/0
	Total		1,856.00 -	1,856.00	.00				0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
87	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	457.14	04/2013 09/2014	06/2015	26(O) 9(R)	17/18
88	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL,JHARKHAND	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016	0(O) -	1/3
89	3RD CONVERTER AND 4TH CASTER - [N12000088]RINL,ANDHRA PRADESH	07/2011	974.76 -	974.76	79.15	07/2016 -	07/2016	0(O) -	1/2
90	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	379.89	05/2013 01/2015	08/2015	27(O) 7(R)	16/20
91	ALTERNATE GAS NETWORK AT BSL - [N12000093]SAIL,JHARKHAND	03/2015	255.19 -	255.19	-	03/2018 -	03/2018	0(O) -	0/0
92	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	377.33	09/2009 05/2012	06/2015	69(O) 37(R)	1/1
93	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	607.17 -	607.17	387.36	12/2011 01/2015	03/2015	-	20/20
94	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL,ANDHRA PRADESH	07/2011	877.73 -	877.73	175.54	07/2015 -	03/2016	8(O) -	0/2
95	CAPTIVE POWER PLANT - 2 - [N12000087]RINL,ANDHRA PRADESH	02/2011	677.00 -	677.00	512.18	09/2013 -	05/2015	20(O) -	0/1
96	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	174.36	08/2014 -	11/2015	15(O) -	3/4
97	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	188.93	16.95	04/2015 -	04/2015	0(O) -	1/3
98	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	125.27	11/2013 -	06/2015	19(O) -	2/4
99	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,389.17	03/2013 -	09/2015	30(O) -	31/35
100	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	5,111.95	12/2011 -	05/2015	41(O) -	20/24
101	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,585.10	12/2012 -	05/2015	29(O) -	18/20
102	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,301.23	10/2009 10/2012	05/2015	67(O) 31(R)	69/70
103	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	151.10	10/2013 -	08/2015	22(O) -	2/5
104	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	120.73	09/2014 -	06/2015	9(O) -	1/2
105	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018	0(O) -	0/0
106	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 -	15,525.00	6,807.44	05/2015 12/2016	12/2016	19(O) 0(R)	16/79
107	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL,WEST BENGAL	11/2012	313.05 -	313.05	217.48	06/2015 -	06/2015	0(O) -	2/3
108	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	164.00	12/2014 -	08/2015	8(O) -	1/2

Sector Wise Details

(April 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
109	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	24.02	10/2016 -	10/2016	0(O) -	0/0
110	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL,ANDHRA PRADESH	05/2012	404.16 -	404.16	149.34	07/2015 -	03/2017	20(O) -	0/1
111	TURBO BLOWER - 5 - [N12000092]RINL,ANDHRA PRADESH	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016	0(O) -	0/1
112	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	109.01	04/2016 -	04/2016	0(O) -	2/2
	Total		62,807.52 -	66,521.92	43,850.05				224/322
	<u>PETROCHEMICALS</u>								
113	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,595.08	04/2012 12/2013	06/2015	38(O) 18(R)	21/26
	Total		5,460.61 -	9,833.52	8,595.08				21/26
	<u>PETROLEUM</u>								
114	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39(O) 6(R)	0/1
115	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	44.52	12/2018 -	12/2018	0(O) -	0/9
116	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36(O) -	0/0
117	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48(O) -	0/0
118	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,768.09	03/2013 03/2016	03/2016	36(O) 0(R)	2/15
119	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	297.42	08/2015 -	12/2015	4(O) -	0/12
120	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 -	1,823.00	-	- -	-	-	0/0
121	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]GAIL,ANDHRA PRADESH	07/2014	419.04 -	419.04	34.08	01/2017 -	01/2017	0(O) -	0/0
122	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015	51(O) 0(R)	0/0
123	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 05/2015	05/2015	21(O) 0(R)	0/0
124	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	111.38	09/2012 04/2015	12/2015	39(O) 8(R)	0/5
125	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 11/2017	11/2017	46(O) 0(R)	0/2
126	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39(O) 0(R)	0/0
127	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 761.68	761.68	840.51	05/2013 06/2014	03/2015	-	1/5

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00	1,584.00	1,210.15	08/2015	12/2015	4(O)	0/12
129	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82	3,955.21	3,439.38	04/2006	06/2015	110(O)	0/5
130	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78	6,100.00	5,925.40	08/2010	05/2015	57(O)	3/13
131	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17	2,592.17	536.91	05/2014	05/2016	24(O)	0/21
132	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40	6,638.94	2,306.51	03/2013	05/2015	26(O)	0/10
133	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82	284.82	-	04/2015	05/2017	25(O)	0/5
134	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17	600.17	249.17	12/2014	05/2016	17(O)	0/8
135	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00	2,523.00	1,020.25	01/2014	12/2015	23(O)	0/13
136	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06	429.06	-	10/2014	10/2015	12(O)	0/0
137	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL, WEST BENGAL	03/2014	3,076.00	3,076.00	93.08	09/2017	09/2017	0(O)	0/0
138	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00	711.00	4.96	-	-	-	0/0
139	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40	5,608.40	3,576.16	05/2015	05/2015	0(O)	0/17
140	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49	352.49	115.81	03/2014	05/2016	26(O)	0/0
141	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88	163.88	17.38	07/2016	07/2016	0(O)	2/6
142	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63	2,665.65	854.50	03/2015	05/2016	14(O)	0/17
143	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07	4,619.94	0.47	02/2016	04/2017	14(O)	0/0
144	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35	4,124.35	75.24	04/2016	04/2016	0(O)	0/6
145	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	03/2012	14,225.00	16,504.00	6,072.90	05/2016	05/2016	0(O)	0/30
146	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49	352.49	115.81	03/2014	05/2016	26(O)	0/3
147	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18	3,957.00	4.01	01/2013	02/2019	73(O)	0/0
148	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00	890.00	-	-	-	-	0/0
149	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00	2,915.00	1,341.30	12/2012	06/2015	30(O)	0/14
150	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06	607.06	57.81	01/2016	07/2017	18(O)	11/48

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	02/2012	666.00 838.05	838.05	446.02	11/2015 11/2016	11/2016	12(O) 0(R)	24/29
152	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	183.48	07/2013 -	07/2015	24(O) -	0/1
153	MARKETING TOP AT KORBA - [N16000186]IOCL,CHHATISGARH	01/2011	141.86 -	232.00	132.71	09/2016 -	12/2015	-9(O) -	0/12
154	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32(O) 0(R)	0/0
155	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 5,813.25	5,813.25	379.10	05/2017 05/2017	05/2017	0(O) 0(R)	0/16
156	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	149.03	12/2014 -	07/2015	7(O) -	57/58
157	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
158	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	390.21	08/2015 -	06/2016	10(O) -	0/0
159	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 -	2,321.00	0.30	- -	-	-	0/0
160	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	-	- -	07/2018	-	0/31
161	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,946.07	11/2012 11/2013	10/2015	35(O) 23(R)	87/100
162	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,102.33	09/2012 -	03/2016	42(O) -	6/7
163	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	39.42	07/2016 -	07/2016	0(O) -	5/12
164	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 1,417.00	1,417.00	1,410.50	05/2014 05/2015	05/2015	12(O) 0(R)	0/0
165	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	96.36	09/2017 -	09/2017	0(O) -	0/0
166	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]IOIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41(O) 0(R)	0/0
167	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	393.72	04/2015 04/2015	12/2015	8(O) 8(R)	0/0
168	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	03/2012	1,419.00 -	1,419.00	1,124.50	12/2014 -	03/2015	-	0/20
169	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	29.03	02/2016 -	02/2016	0(O) -	2/6
170	RESID UPGRADE PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	561.70	11/2015 -	07/2016	8(O) -	37/52
171	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	82.71	05/2015 -	12/2015	7(O) -	0/12
172	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	13.86	05/2016 04/2018	04/2018	23(O) 0(R)	0/0
173	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]IOCL,GUJARAT	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016	0(O) 0(R)	0/0
174	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 1,446.34	1,446.34	1,024.42	11/2015 -	11/2015	0(O) -	17/25

Sector Wise Details						(April 2015)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
175	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	450.55	10.60	03/2017 -	03/2017	0(O) -	0/0
176	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	944.84	10/2011 -	10/2015	48(O) -	0/0
177	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45(O) -	0/0
178	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,099.88	10/2011 -	10/2015	48(O) -	0/0
179	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.44	04/2015 -	04/2015	0(O) -	0/0
180	TWENTY NOS. FEEDER GAS LINES - [N16000192]OIL,ASSAM	03/2009	228.64 -	214.19	123.67	12/2016 -	12/2016	0(O) -	0/0
181	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	220.84	08/2012 03/2015	06/2015	34(O) 3(R)	0/1
182	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	219.71	03/2015 11/2015	02/2016	11(O) 3(R)	0/5
183	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	12/2009	309.81 462.79	462.79	222.98	10/2014 10/2016	10/2016	24(O) 0(R)	23/40
184	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	278.85	06/2011 03/2012	03/2016	57(O) 48(R)	13/20
	Total		157,059.07 -	171,085.92	75,485.57				290/724
	POWER								
185	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	311.69	12/2014 -	05/2015	5(O) -	9/17
186	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	05/2016 -	05/2016	0(O) -	0/0
187	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	8,631.00	10/2013 -	03/2015	-	20/20
188	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,792.00	12/2009 10/2014	03/2018	99(O) 41(R)	26/46
189	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,186.00	09/2011 -	03/2017	66(O) -	12/35
190	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	5,353.00	-	05/2014 -	05/2014	-	0/0
191	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	559.65	12/2015 -	03/2016	3(O) -	9/19
192	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,757.36	09/2014 -	06/2016	21(O) -	12/19
193	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	678.43	06/2015 -	12/2015	6(O) -	0/7

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
194	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	5/20
195	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	105.00	06/2015 -	12/2015	6(O) -	5/7
196	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017	0(O) -	0/0
197	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA	02/2014	12,532.44 -	12,532.44	1,457.00	08/2018 -	08/2018	0(O) -	13/14
198	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	24.10	02/2014 -	09/2017	43(O) -	1/1
199	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	1.00	02/2016 -	02/2016	0(O) -	5/7
200	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	987.23	11/2012 -	12/2016	49(O) -	2/12
201	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	147.34	04/2016 -	04/2016	0(O) -	11/20
202	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	1.00	11/2016 -	11/2016	0(O) -	0/0
203	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	28.00	09/2014 -	06/2016	21(O) -	0/0
204	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	-	04/2018 -	04/2018	0(O) -	0/0
205	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,688.45	05/2014 -	03/2016	22(O) -	8/11
206	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH	07/2013	3,363.12 -	3,363.12	542.00	12/2016 -	12/2016	0(O) -	12/15
207	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	03/2013	11,638.55 -	11,638.55	3,011.00	09/2017 -	09/2017	0(O) -	16/40
208	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]PGCIL,MULTI STATE	04/2015	1,479.30 -	1,479.30	-	05/2017 -	05/2017	0(O) -	0/0
209	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]PGCIL,MULTI STATE	04/2015	3,705.61 -	3,705.61	-	05/2018 -	05/2018	0(O) -	0/0
210	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	926.80	08/2014 06/2015	06/2015	10(O) 0(R)	12/15
211	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	1.00	07/2016 -	07/2016	0(O) -	0/0
212	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]PGCIL,MULTI STATE	03/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017	0(O) -	0/0
213	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	380.47	10/2016 -	03/2016	-7(O) -	8/17

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
214	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]PGCIL,MULTI STATE	12/2014	6,517.36 -	6,517.36	22.00	04/2018 -	04/2018	0(O) -	0/0
215	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 1,007.16	1,007.16	989.31	12/2007 12/2009	12/2015	96(O) 72(R)	3/10
216	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,862.64	12/2009 03/2017	03/2017	87(O) 0(R)	13/29
217	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03 -	3,984.03	-	01/2013 -	03/2016	38(O) -	0/0
218	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPCL,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,934.97	01/2016 -	11/2016	10(O) -	4/6
219	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,584.00	04/2009 -	06/2015	74(O) -	8/9
220	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	01/2012	15,166.19 -	15,166.19	8,031.00	01/2017 -	01/2017	0(O) -	24/27
221	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,891.15	09/2008 08/2010	03/2016	90(O) 67(R)	17/23
222	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	12/2012	11,846.00 -	11,846.00	3,850.00	06/2017 -	06/2017	0(O) -	17/38
223	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017	0(O) -	0/9
224	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	3,959.00	09/2016 -	09/2016	0(O) -	21/26
225	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	-	12/2016 -	09/2017	9(O) -	0/0
226	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	14,366.58	2,071.00	02/2019 -	02/2019	0(O) -	1/1
227	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,373.80	08/2013 -	03/2016	31(O) -	4/17
228	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	25.00	06/2016 -	06/2016	0(O) -	10/20
229	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	479.82	07/2013 -	12/2015	29(O) -	3/10
230	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	318.27	02/2012 -	03/2016	49(O) -	4/13
231	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	461.76	11/2011 -	03/2016	52(O) -	4/13
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	16.00	06/2016 -	06/2016	0(O) -	9/20
233	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,244.02	04/2013 -	03/2016	35(O) -	3/11
234	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	501.22	11/2014 -	12/2015	13(O) -	11/16
235	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	185.49	03/2016 -	03/2016	0(O) -	8/17
236	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	589.89	03/2015 -	05/2015	2(O) -	13/17
237	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	178.92	04/2015 -	09/2015	5(O) -	11/18

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	725.74	11/2012 -	03/2016	40(O) -	2/11
239	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	12,964.60	-	01/2018 -	01/2018	0(O) -	0/0
240	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]NHPC,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020	0(O) -	0/0
241	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	7,531.72	5,040.21	09/2009 -	12/2018	111(O) -	7/12
242	PARE HYDRO ELECTRIC PROJECT - [N18000045]NNEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,007.25	08/2013 -	03/2016	31(O) -	28/37
243	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	109.00	09/2019 -	09/2019	0(O) -	2/2
244	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,728.00	11/2016 -	08/2017	9(O) -	19/22
245	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	08/2016 -	08/2016	0(O) -	0/0
246	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	48.00	12/2015 -	12/2015	0(O) -	6/7
247	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]PGCIL,MULTI STATE	11/2014	972.42 -	972.42	-	11/2017 -	11/2017	0(O) -	0/0
248	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	15,300.00	7,687.18	09/2010 -	-	-	0/0
249	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]PGCIL,ANDHRA PRADESH	03/2015	550.06 -	550.06	-	03/2018 -	03/2018	0(O) -	0/0
250	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	657.18	03/2015 -	09/2015	6(O) -	10/19
251	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	11.00	02/2017 -	02/2017	0(O) -	0/0
252	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	194.79	06/2012 -	-	-	1/3
253	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	195.44	03/2014 -	05/2015	14(O) -	7/7
254	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	950.63	08/2014 12/2015	03/2016	19(O) 3(R)	10/17
255	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,051.29	08/2012 -	03/2016	43(O) -	2/6
256	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	61.00	08/2016 -	08/2016	0(O) -	10/20
257	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	203.28	-	07/2017 -	07/2017	0(O) -	0/0
258	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,010.48	11/2014 -	09/2015	10(O) -	8/15
259	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	1,043.12	01/2015 -	03/2016	14(O) -	12/20

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
260	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	274.57	08/2014 06/2015	12/2015	16(O) 6(R)	13/19
261	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	355.42	06/2014 -	03/2016	21(O) -	15/19
262	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	682.00	03/2019 -	03/2019	0(O) -	5/5
263	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,434.00	03/2013 -	12/2018	69(O) -	1/14
264	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,742.55	09/2009 -	06/2016	81(O) -	2/5
265	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,198.84	07/2010 02/2016	05/2018	94(O) 27(R)	5/21
266	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,856.76	08/2014 -	09/2015	13(O) -	12/19
267	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	2,246.41	10/2014 -	03/2016	17(O) -	8/17
268	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,075.48	10/2012 -	03/2016	41(O) -	1/11
269	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	04/2017 -	04/2017	0(O) -	0/0
270	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,111.00	12/2012 -	03/2016	39(O) -	2/11
271	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	0/0
272	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	442.00	03/2018 -	03/2018	0(O) -	0/20
273	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,306.75	01/2015 -	03/2016	14(O) -	8/21
274	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	40.00	10/2016 -	10/2016	0(O) -	12/20
275	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 -	268.80	-	03/2018 -	03/2018	0(O) -	0/0
276	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,495.27	10/2014 -	09/2015	11(O) -	9/15
277	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	241.60	05/2016 -	05/2016	0(O) -	10/18
278	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	871.62	-	11/2017 -	11/2017	0(O) -	0/0
279	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	501.60	02/2014 -	09/2015	19(O) -	12/16

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
280	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,294.66	12/2013 04/2015	06/2015	18(O) 2(R)	9/12
281	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	429.81	11/2013 -	12/2015	25(O) -	12/20
282	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,823.24	03/2013 06/2015	12/2015	33(O) 6(R)	6/14
283	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,767.47	03/2014 06/2015	08/2015	17(O) 2(R)	8/14
284	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,701.80	12/2013 -	09/2015	21(O) -	7/12
285	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	117.10	01/2013 -	06/2015	29(O) -	9/21
286	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	12/2015	25(O) -	7/15
287	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,680.97	11/2012 -	07/2015	32(O) -	3/10
288	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,172.33	07/2014 -	03/2016	20(O) -	8/13
289	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	911.74	07/2013 -	08/2015	25(O) -	24/26
290	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72 1,381.71	1,381.71	805.32	07/2006 12/2015	10/2016	123(O) 10(R)	5/13
291	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
292	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	05/2012	3,180.40 -	3,180.40	1,782.00	08/2015 -	08/2015	0(O) -	21/22
293	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	619.75	07/2014 11/2018	11/2018	52(O) 0(R)	2/8
294	WARDHA-HYDERABAD 765 KV LINK - [N18000183]PGCIL,MULTI STATE	01/2015	3,662.02 -	3,662.02	5.00	05/2018 -	05/2018	0(O) -	0/0
295	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	519.79	09/2010 06/2013	03/2016	66(O) 33(R)	0/7
296	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	4,122.59	06/2015 -	03/2016	9(O) -	15/28
	Total		317,040.36 -	356,191.36	157,703.34				749/1376
	HEAVY INDUSTRY								
297	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00 -	3,827.30	-	09/2011 -	12/2017	75(O) -	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		1,718.00 -	3,827.30	.00				0/0
	<u>RAILWAYS</u>								
298	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	43.93	03/2016 -	03/2016	0(O) -	0/0
299	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	184.06	15.23	- -	-	-	0/0
300	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48(O) -	0/0
301	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	252.00 252.00	886.65	-	- -	03/2018	-	0/0
302	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66(O) 51(R)	0/0
303	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	31.99	- -	-	-	0/0
304	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	83.50	03/2013 -	-	-	0/0
305	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	329.67	- -	-	-	0/0
306	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	23.64	- -	-	-	0/0
307	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
308	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
309	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR,MULTI STATE	12/2006	170.00 -	485.00	417.70	03/2011 -	-	-	0/0
310	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
311	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	129.14	- -	-	-	0/0
312	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
313	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	586.75	06/1999 -	07/2012	-	0/0
314	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.86	- -	-	-	0/0
315	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
316	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	137.40	- -	-	-	0/0
317	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
318	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
319	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
320	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	76.08	- -	-	-	0/0

Sector Wise Details

(April 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
321	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93	986.30	88.13	-	-	-	0/0
322	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35	288.35	9.60	-	-	-	0/0
323	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33(O)	0/0
324	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00	1,382.78	2.76	-	-	-	0/0
325	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08	246.08	4.09	-	-	-	0/0
326	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177(O) 132(R)	0/0
327	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62	1,106.62	244.99	12/2010	-	-	0/0
328	BARIARPUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	450.55	13.53	-	-	-	0/0
329	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64	255.64	-	-	-	-	0/0
330	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	433.72	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
331	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49	337.49	0.21	-	-	-	0/0
332	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23	923.23	1.01	-	-	-	0/0
333	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67	837.33	1.15	-	-	-	0/0
334	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64	760.00	0.09	-	-	-	0/0
335	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47(O) 36(R)	0/0
336	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88	2,966.99	40.80	-	-	-	0/0
337	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.83	03/2011	-	-	0/0
338	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64	195.64	94.11	-	-	-	0/0
339	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20	800.00	793.71	03/2010	12/2015	69(O)	0/0
340	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24	321.62	2.91	03/2012	-	-	0/0
341	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20	326.20	1.68	-	-	-	0/0
342	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80	175.80	1.46	-	-	-	0/0
343	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37	434.00	35.90	-	-	-	0/0
344	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110(O) 39(R)	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
345	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
346	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21(O) -	0/0
347	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.30	- -	-	-	0/0
348	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	61.36	- -	-	-	0/0
349	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIC - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	619.87	- -	03/2015	-	0/0
350	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	112.40	- -	-	-	0/0
351	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	520.00	462.69	- -	-	-	0/0
352	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.07	- -	-	-	0/0
353	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	4.22	- -	-	-	0/0
354	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	111.71	- -	-	-	0/0
355	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 663.67	1,101.16	194.91	- -	03/2017	-	0/0
356	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	30.05	- -	-	-	0/0
357	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
358	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
359	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.60	- -	-	-	0/0
360	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	164.55	- -	-	-	0/0
361	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSHUPUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
362	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108(O) -	0/0
363	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.56	- -	-	-	0/0
364	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
365	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	225.00	193.37	- 10/2014	10/2014	-	0/0
366	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	187.84	- -	-	-	0/0
367	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	533.38	114.38	12/2011 -	-	-	0/0

Sector Wise Details

(April 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
368	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	139.48	12/2012 -	-	-	0/0
369	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3(O) -	0/0
370	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	406.92	155.87	-	-	-	0/0
371	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.55	-	-	-	0/0
372	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
373	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	294.70	-	-	-	0/0
374	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	234.71	137.01	03/2015 -	03/2015	-	0/0
375	DELHI-SOHNANUHI-FIROZPUR-JHIRKA-ALWAR - [N22000271]JNR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	-	-	-	0/0
376	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]JNR,MULTI STATE	04/2007	336.91 -	336.91	144.05	-	-	-	0/0
377	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	607.09	561.14	12/2012 12/2012	-	-	0/0
378	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	376.59	4.58	-	-	-	0/0
379	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	3.61	02/2019 -	02/2019	0(O) -	0/0
380	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	-	12/2019	-	0/0
381	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	4,487.70	-	-	-	-	0/0
382	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	846.18	-	03/2015	-	0/0
383	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,WEST BENGAL	03/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016	0(O) -	0/0
384	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2016	48(O) 27(R)	0/0
385	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	-	-	-	0/0
386	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.64	-	-	-	0/0
387	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008 -	10/2015	82(O) -	0/0
388	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	495.74	308.16	06/2013 06/2013	06/2013	-	0/0
389	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]JNR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	-	-	-	0/0
390	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	1.09	-	-	-	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
391	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	301.84	02/2011 02/2011	-	-	0/0
392	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.98	-	-	-	0/0
393	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	-	-	-	0/0
394	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	197.73	-	-	-	-	0/0
395	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	611.03	140.48	12/2011 11/2013	11/2013	-	0/0
396	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	259.82	177.01	02/2006 -	03/2016	121(O) -	0/0
397	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	04/1997	863.23 -	1,072.51	888.87	-	06/2015	-	0/0
398	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261(O) -	0/0
399	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.00	-	-	-	0/0
400	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.31	-	-	-	0/0
401	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	798.87	- 05/2009	03/2015	-	0/0
402	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	602.10	03/1994 -	03/2015	-	0/0
403	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	179.32	31.85	-	-	-	0/0
404	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	2.33	02/2020 -	02/2020	0(O) -	0/0
405	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	-	-	-	0/0
406	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	367.17	13.00	-	-	-	0/0
407	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	324.66	222.05	-	-	-	0/0
408	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	-	-	-	0/0
409	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	-	-	-	0/0
410	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	266.35	- 09/2009	-	-	0/0
411	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	2.38	-	-	-	0/0
412	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	1,060.40	-	-	-	0/0
413	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	172.58	-	-	-	0/0
414	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	93.12	03/2015 -	03/2015	-	0/0
415	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	-	-	-	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
416	HOSADURGA - CHICKAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	203.40	142.86	- -	-	-	0/0
417	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	282.11	- -	-	-	0/0
418	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	43.34	- -	-	-	0/0
419	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	1,026.00	181.48	03/2007 03/2007	03/2015	-	0/0
420	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
421	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	117.11	- -	-	-	0/0
422	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	230.62	01/1999 -	-	-	0/0
423	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 -	653.55	306.75	03/2014 -	-	-	0/0
424	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	143.62	- -	-	-	0/0
425	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	835.14	06/2007 -	-	-	0/0
426	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	1,043.56	808.47	03/2012 -	-	-	0/0
427	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	40.00	- -	-	-	0/0
428	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	230.00	218.67	- -	-	-	0/0
429	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	639.77	03/2012 03/2012	12/2012	-	0/0
430	JIRIBAM TO IMPHAL (TUPUI)(NL),(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96(O) 60(R)	0/0
431	KADAPA-BANGALORE (NL), KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	194.45	- -	-	-	0/0
432	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	208.10	- -	-	-	0/0
433	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	63.08	- -	-	-	0/0
434	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	4.73	- -	-	-	0/0
435	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,621.40	- -	03/2015	-	0/0
436	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
437	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	576.86	- -	03/2016	- -	1/1

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
438	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	800.66	- -	-	-	0/0
439	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39(O) -	0/0
440	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87(O) -	0/0
441	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	163.59	03/2017 -	03/2017	0(O) -	0/0
442	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	1,054.35	7.96	- -	-	-	0/0
443	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	541.00	148.58	- -	-	-	0/0
444	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	277.33	03/2009 03/2009	08/2014	-	0/0
445	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	355.02	- -	-	-	0/0
446	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
447	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	282.92 282.92	565.13	2.80	- 03/2014	03/2018	- 48(R)	0/0
448	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	567.94	- 03/2010	03/2010	-	0/0
449	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,857.31	07/2005 -	-	-	0/0
450	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	237.93	- -	-	-	0/0
451	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
452	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	320.98	03/2012 -	-	-	0/0
453	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,047.00	1.29	- -	-	-	0/0
454	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.48	- -	-	-	0/0
455	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
456	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.61	- -	-	-	0/0
457	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	406.99	141.55	- -	-	-	0/0
458	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	488.76	05/2008 -	-	-	0/0
459	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	67.97	03/2014 -	03/2014	-	0/0
460	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
461	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31	5,500.00	4,734.45	03/2009	03/2016	84(O)	0/0
462	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, TELANGANA	07/1998	125.00	480.00	3.51	07/2008	07/2008	-	0/0
463	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41	450.00	16.97	-	-	-	0/0
464	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR, MULTI STATE	04/2011	601.43	800.00	0.69	-	-	-	0/0
465	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	493.96	493.96	121.27	-	-	-	0/0
466	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, BIHAR	04/2003	218.19	343.00	216.17	-	-	-	0/0
467	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, JHARKHAND	04/1995	900.05	900.05	853.83	12/2011	-	-	0/0
468	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	378.56	791.59	5.41	-	-	-	0/0
469	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20	365.00	2.52	-	12/2017	-	0/0
470	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR, PUNJAB	04/2009	396.04	369.00	108.93	-	-	-	0/0
471	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	332.92	477.88	496.28	03/2012	-	-	0/0
472	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00	1,112.00	-	-	-	-	0/0
473	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	285.57	279.54	2.74	01/1999	-	-	0/0
474	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	456.00	855.16	557.72	-	-	-	0/0
475	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	404.19	1,383.45	457.88	-	-	-	0/0
476	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR, UTTAR PRADESH	04/2012	377.44	377.44	7.50	-	-	-	0/0
477	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88	439.88	0.78	-	-	-	0/0
478	MM FROM BURAMARA-CHAKULIA - [N22000305]SER, MULTI STATE	04/2008	466.48	800.00	0.83	01/1999	-	-	0/0
479	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69	426.00	-	01/1999	-	-	0/0
480	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93	250.93	0.14	-	-	-	0/0
481	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00	926.09	4.41	-	-	-	0/0
482	MUDKHED-PARBHANI - [N22000283]SCR, MAHARASHTRA	04/2011	390.60	390.60	4.69	-	-	-	0/0
483	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00	6,821.29	2,421.26	03/2014	03/2019	60(O) 0(R)	0/0

Sector Wise Details									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
484	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	309.19	- -	03/2015	-	0/0
485	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	339.53	- -	-	-	0/0
486	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
487	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]JECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
488	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]JECR,BIHAR	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
489	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	5.13	- -	-	-	0/0
490	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	755.50	02/2009 -	03/2015	-	0/0
491	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,100.00	391.95	07/2012 -	-	-	0/0
492	NAWADA-LAXMIPUR (NL) - [N22000167]JECR,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
493	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]JER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
494	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
495	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	200.00 200.00	496.24	213.72	- -	03/2017	-	0/0
496	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
497	NEW BG LINE FROM KALYANIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	- 48(R)	0/0
498	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 210.00	394.28	233.46	- -	03/2017	-	0/0
499	NEW BG LINE FROM KALYANAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.29	- -	03/2019	-	0/0
500	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
501	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
502	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77 190.39	441.45	85.78	- -	03/2018	-	0/0
503	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55 278.21	288.81	11.74	- -	03/2018	-	0/0
504	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
505	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60(O) 0(R)	0/0
506	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111(O) -	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
507	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.44	03/2014 -	03/2016	24(O) -	0/0
508	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.51	536.01	03/2016 -	03/2016	0(O) -	0/0
509	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	197.10	03/2016 -	06/2016	3(O) -	0/0
510	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	626.11	03/2016 -	03/2016	0(O) -	0/0
511	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	424.42	03/2008 06/2008	-	-	0/0
512	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	-	-	-	0/0
513	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	140.08	12/2010 -	-	-	0/0
514	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	240.21	-	01/2015	-	0/0
515	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
516	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	712.02	-	02/2014	-	0/0
517	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	227.84	-	03/2015	-	0/0
518	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	21.21	-	-	-	0/0
519	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	-	-	-	0/0
520	PLASSEY-JAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	29.10	03/2015 -	03/2015	-	0/0
521	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
522	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	-	-	-	0/0
523	QADIAN-BEAS - [N22000295]NJR, PUNJAB	04/2011	205.22 -	205.22	1.54	-	-	-	0/0
524	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	1,030.00	800.90	01/1999 -	-	-	0/0
525	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, MULTI STATE	03/1998	280.00 -	1,122.00	889.95	-	-	-	0/6
526	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, ANDHRA PRADESH	04/2003	136.62 -	289.93	277.09	12/2007 03/2010	-	-	0/0
527	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, BIHAR	04/2002	921.00 -	2,363.00	1,548.90	03/2009 12/2012	12/2014	-	0/0
528	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, ODISHA	04/1999	166.16 -	288.00	305.47	02/2009 02/2009	08/2014	-	0/0
529	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	209.00	2.64	12/2016 -	12/2016	0(O) -	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
530	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	913.48	457.67	- -	-	-	0/0
531	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	703.56	03/2013 -	09/2015	30(O) -	0/0
532	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	257.59	- -	03/2017	- -	0/0
533	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138(O) -	0/0
534	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	3,700.00	3,198.30	- -	03/2015	-	0/0
535	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.62	- -	-	-	0/0
536	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	794.78	- -	-	-	0/0
537	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	3,500.00	129.12	- -	-	-	0/0
538	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	420.33	03/2012 -	-	-	0/0
539	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	336.05	- -	-	-	0/0
540	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	576.18	3.40	- -	-	-	0/0
541	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	65.24	04/2016 -	03/2017	11(O) -	0/0
542	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	53.01	- -	-	-	0/0
543	SAKRI-HASANPUR ROAD (NL) - [N22000171]JECOR,BIHAR	04/1999	175.69 -	325.00	253.10	- -	-	-	0/0
544	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]JECR,BIHAR	04/2004	372.14 -	355.81	286.17	- -	-	-	0/0
545	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	230.21	03/2010 -	-	-	0/0
546	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]JECOR,ODISHA	03/2012	155.81 -	155.81	18.25	- -	-	-	0/0
547	SAMBALPUR-TALCHER DOUBLING - [N22000315]JECOR,ODISHA	03/2011	679.27 -	1,111.99	60.31	- -	-	-	0/0
548	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
549	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51(O) -	0/0
550	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.94	- -	-	-	0/0
551	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]JECR,BIHAR	04/2008	678.62 -	239.32	17.17	- -	-	-	0/0
552	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
553	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	67.82	- -	-	-	0/0
554	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	0.02	- -	-	-	0/0
555	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
556	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	183.23 -	818.29	113.50	02/2015 -	-	-	0/0
557	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.91	- -	-	-	0/0
558	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 732.06	516.23	596.43	03/2014 -	-	-	0/0
559	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, ODISHA	04/2005	810.78 -	810.80	160.80	- -	-	-	0/0
560	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174(O) 101(R)	0/0
561	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER, WEST BENGAL	04/2010	171.02 -	171.00	166.84	06/2013 -	01/2015	-	0/0
562	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.35	- -	-	-	0/0
563	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,188.91	687.63	- 12/2009	-	-	0/0
564	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	190.10	33.19	- -	-	-	0/0
565	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	262.00	-	- -	-	-	0/0
566	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	1,080.00	194.61	- -	-	-	0/0
567	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	490.00	67.57	- -	-	-	0/0
568	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	124.14	03/2012 -	-	-	0/0
569	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	980.00	596.66	- -	-	-	0/0
570	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	3,404.92	3,541.20	12/2006 -	-	-	0/0
571	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.32	- -	-	-	0/0
572	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	1.13	- -	-	-	0/0
573	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193(O) -	0/0
574	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	1,055.80	03/2014 -	-	-	0/0
575	UNHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.38	- -	-	-	0/0

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
576	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
577	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	341.60	- -	02/2017	- -	0/0
578	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	1,031.83	- -	-	-	0/0
579	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	201.26	- 03/2010	-	-	0/0
580	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	206.59	- -	-	-	0/0
581	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	249.02	- -	-	-	0/0
582	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	84.11	- -	-	-	0/0
583	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	7.17	- -	-	-	0/0
584	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
585	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		163,518.20 -	291,060.49	94,834.18				1/7
	ROAD TRANSPORT AND HIGHWAYS								
586	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28(O) -	0/0
587	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	-	11/2013 -	-	-	0/0
588	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	-	10/2014 -	-	-	0/0
589	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	-	07/2014 -	-	-	0/0
590	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	05/2015	24(O) -	0/0
591	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18(O) -	0/0
592	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	03/2016	23(O) -	0/0
593	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	07/2015	12(O) -	0/0
594	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	-	01/2014 -	-	-	0/0
595	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
596	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20(O) -	0/0
597	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2016	23(O) -	0/0

Sector Wise Details

(April 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
598	2 LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI, BIHAR	12/2011	325.00 -	325.00	160.20	05/2014 -	05/2014	-	0/0
599	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	11/2015	14(O)	0/3
600	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11(O)	0/0
601	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	06/2015	24(O)	0/3
602	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI, KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39(O)	0/0
603	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	785.50	941.00	08/2013 -	08/2013	-	0/3
604	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	1,266.60	178.20	09/2016 -	09/2016	0(O)	0/0
605	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI, JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19(O)	0/0
606	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI, MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47(O)	0/0
607	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36(O)	0/0
608	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI, MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45(O)	0/0
609	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI, HARYANA	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015	0(O)	0/0
610	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29(O)	0/0
611	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	12/2015	15(O)	0/0
612	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93(O)	0/0
613	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015	0(O)	0/3
614	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0
615	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39(O)	0/0
616	BARSAAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34(O)	0/0
617	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17(O)	0/0
618	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	665.80	-	05/2015	-	2/2
619	BHOPAL-SANCHI - [N24000192]NHAI, MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35(O)	0/0
620	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	06/2015	22(O)	0/0
621	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI, ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	05/2016	95(O)	0/0
622	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	09/2015	87(O)	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
623	BIJUI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126(O) -	0/0
624	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	457.70	04/2010 01/2016	12/2015	68(O) -1(R)	0/0
625	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84(O) -	0/0
626	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33(O) -	0/0
627	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56(O) -	0/0
628	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
629	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31(O) -	0/0
630	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
631	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12(O) -	0/0
632	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	07/2015	62(O) -	0/0
633	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33(O) -	0/0
634	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	75.85	06/2013 -	05/2015	23(O) -	0/0
635	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	808.70	-	05/2015	-	1/1
636	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	83(O) -	0/0
637	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	09/2015	88(O) 3(R)	0/0
638	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	04/2016	67(O) -	0/0
639	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015	0(O) -	0/0
640	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	06/2015	81(O) -	0/0
641	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016	0(O) -	0/0
642	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6(O) -	0/0
643	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	-	10/2013 -	-	-	0/0
644	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	06/2015	81(O) -	0/0
645	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	06/2015	22(O) -	0/0
646	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	-	09/2012 -	-	-	2/3

Sector Wise Details

(April 2015)

Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
647	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	03/2015	-	0/0
648	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI, ASSAM	12/2003	175.96 -	175.96	290.20	04/2008 04/2015	05/2015	85(O) 1(R)	0/0
649	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0
650	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	361.00	366.80	02/2009 -	12/2015	82(O) -	0/0
651	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	363.74	242.10	07/2009 -	08/2015	73(O) -	0/0
652	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]NHAI, ASSAM	12/2003	212.00 -	386.10	127.10	09/2007 -	04/2016	103(O) -	0/0
653	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26(O) -	0/0
654	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	28(O) -	0/0
655	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	946.00	737.50	-	-	-	3/3
656	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31(O) -	0/0
657	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32(O) -	0/0
658	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	06/2015	28(O) -	0/0
659	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	05/2015	29(O) -	0/0
660	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29(O) -	0/0
661	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	-	01/2014 -	-	-	0/0
662	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	953.88	07/2013 -	06/2015	23(O) -	0/0
663	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI, RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	08/2015	39(O) -	0/0
664	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	185.30	10/2008 -	07/2015	81(O) -	0/0
665	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31(O) -	0/0
666	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,273.00	-	06/2015	-	2/3
667	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	-	07/2012 -	-	-	0/0
668	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	10/2015	83(O) -	0/0
669	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	12/2015	80(O) -	0/0
670	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2015	85(O) -	0/0
671	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	12/2015	80(O) -	0/0

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
672	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00	1,267.00	2,425.00	06/2013	06/2015	24(O)	0/0
673	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00	754.00	593.50	03/2013	12/2015	33(O)	0/0
674	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72	264.72	315.90	06/2008	06/2015	84(O)	0/0
675	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19	484.19	285.50	10/2014	03/2016	17(O)	0/0
676	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00	208.00	334.10	04/2008	12/2015	92(O)	0/0
677	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00	225.00	276.70	06/2008	04/2015	82(O)	0/0
678	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00	200.00	281.60	06/2008	-	-	0/0
679	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00	2,159.00	622.70	06/2015	05/2016	11(O)	0/0
680	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00	1,655.00	655.20	09/2013	09/2013	-	0/0
681	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00	557.00	1,125.00	02/2010	07/2015	65(O)	0/0
682	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00	586.00	237.60	01/2014	12/2016	35(O)	0/0
683	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00	1,410.00	929.60	09/2014	06/2016	21(O)	0/0
684	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00	2,288.00	3,466.00	11/2011	06/2015	43(O)	0/0
685	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00	807.00	1,209.43	10/2014	10/2014	-	0/0
686	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69	942.69	286.80	06/2014	12/2015	18(O)	0/0
687	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00	574.00	991.70	03/2014	11/2015	20(O)	0/0
688	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30	671.30	632.70	02/2013	03/2016	37(O)	0/0
689	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00	940.00	1,601.00	07/2012	07/2012	-	0/0
690	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	1,724.55	1,292.00	03/2013	12/2015	33(O)	0/0
691	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00	835.00	476.40	01/2014	11/2015	22(O)	0/0
692	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00	1,987.00	1,170.00	07/2015	06/2016	11(O)	0/0
693	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03	251.03	326.30	10/2008	01/2015	-	0/0
694	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00	1,479.00	368.60	06/2015	12/2016	18(O)	0/0
695	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51	333.51	271.60	09/2014	06/2015	9(O)	0/0
696	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00	650.00	1,178.00	11/2013	03/2016	28(O)	0/0

Sector Wise Details

(April 2015)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
697	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33(O) -	0/0
698	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	06/2015	13(O) -	0/0
699	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	228.30	09/2007 03/2014	03/2015	-	0/0
700	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
701	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21(O) -	0/0
702	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2015	21(O) -	0/0
703	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2016	36(O) -	0/0
704	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	12/2015	19(O) -	0/0
705	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43(O) -	0/0
706	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	06/2015	87(O) 3(R)	0/0
707	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18(O) -	0/0
708	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2015	52(O) -	2/2
709	TALEGAON-AMRAVATI - [N24000140]NHAI, MAHARASHTRA	11/2009	567.00 -	567.00	1,388.00	11/2013 -	11/2013	-	0/0
710	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29(O) -	0/0
711	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI, TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24(O) -	0/0
712	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, KARNATAKA	11/2010	680.00 -	680.00	188.40	-	07/2014	-	2/2
713	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37(O) -	0/0
714	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI, ANDHRA PRADESH	09/2013	606.00 -	606.00	-	-	-	-	0/0
715	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49(O) -	0/0
716	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI, TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16(O) -	0/0
717	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30(O) -	0/0
718	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI, TELANGANA	04/2014	1,123.17 -	1,123.17	-	-	-	-	0/0
	Total		98,941.44 -	101,089.44	84,497.00				14/28

Sector Wise Details									
(April 2015)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>SHIPPING AND PORTS</u>								
719	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU, MAHARASHTRA	11/2007	1,228.00 -	1,460.00	1,049.37	12/2010 -	-	-	0/0
720	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST, TAMIL NADU	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
721	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST, GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	-	-	0/0
722	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL, KERALA	03/2007	245.67 -	373.22	373.22	04/2009 -	-	-	0/0
723	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 -	-	-	0/0
724	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST, GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	-	-	0/0
	Total		5,158.07 -	5,759.15	2,393.83				0/0
	<u>TELECOMMUNICATIONS</u>								
725	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL, ASSAM	06/2007	336.81 -	336.81	199.37	01/2009 -	03/2015	-	0/0
726	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL, MULTI STATE	10/2009	384.00 -	384.00	55.22	10/2010 08/2015	09/2015	59(O) 1(R)	0/0
727	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL, MULTI STATE	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
728	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE	03/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015	0(O) -	0/0
	Total		15,131.81 -	15,131.81	254.59				0/0
	<u>URBAN DEVELOPMENT</u>								
729	2000 BOYS HOSTEL (1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2(O) -	0/0
730	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36(O) -	0/0
731	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	-	-	3/3
732	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL, KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0
733	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD, PUNJAB	08/2005	191.24 -	191.24	-	08/2007 -	03/2015	-	0/0
734	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	-	10/2012 -	09/2013	-	0/0
735	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2(O) -	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
736	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,603.80	12/2015 -	08/2016	8(O) -	1/24
737	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34(O) -	0/0
738	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24(O) -	0/0
739	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30(O) -	0/0
740	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16(O) -	0/0
741	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD,ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6(O) -	0/0
742	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	07/2016	10(O) -	0/0
743	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	157.84	-	03/2017 -	03/2017	0(O) -	0/0
744	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9(O) -	0/0
745	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	2,727.89	-	03/2010 -	10/2014	-	0/0
746	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11(O) -	0/0
747	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017	0(O) -	0/0
748	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00 -	2,494.00	639.78	09/2014 -	05/2015	8(O) -	0/0
749	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017	0(O) -	0/0
750	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	162.90	-	07/2012 -	06/2014	-	0/0
751	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11(O) -	0/0
752	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018	0(O) -	0/0
753	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	241.33	1.75	11/2014 -	12/2014	-	0/0
754	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019	0(O) -	0/7
755	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	246.90	-	- -	-	-	0/0

Sector Wise Details									
(April 2015)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
756	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	171.10	-	09/2014 -	-	-	0/0
757	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	12/2016	3(O) -	0/0
758	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00 -	205.00	-	03/2012 -	04/2015	37(O) -	0/0
	Total		138,680.82 -	143,894.82	21,638.91				4/34
	Grand Total		1,069,127.84	1,278,256.35	546,232.97				1646/3753

Summary of projects in the Flash Report for the month of April, 2015


Project Implementation - Current Status:

Number of Projects in Previous Month	751
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects elevated to the status of Major project during the current month	9

Number of Projects in Current Month 758


Brief Analysis

Project Status with respect to Original Schedule: Out of 758 projects, 2 projects are ahead of schedule, 120 projects are on schedule and 323 projects are delayed. Of the balance, 284 projects do not have fixed dates of commissioning while 29 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

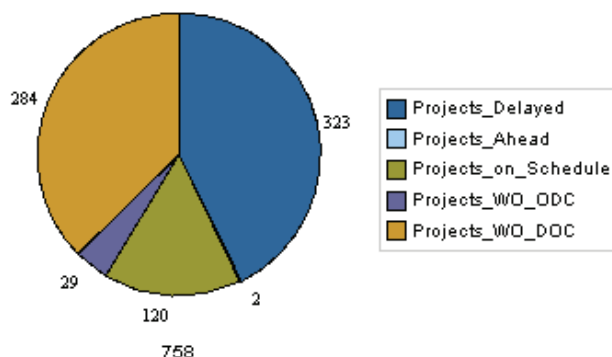

Investment Scenario

Total original cost of implementation of 758 projects when sanctioned, was of the order of Rs. 1069127.84 crore but this was subsequently revised to Rs. 1278256.35 crore implying a cost overrun of 19.6%. The expenditure incurred on these projects till April, 2015 is Rs. 546232.97 crore, which is 42.7% of the revised cost of the projects.

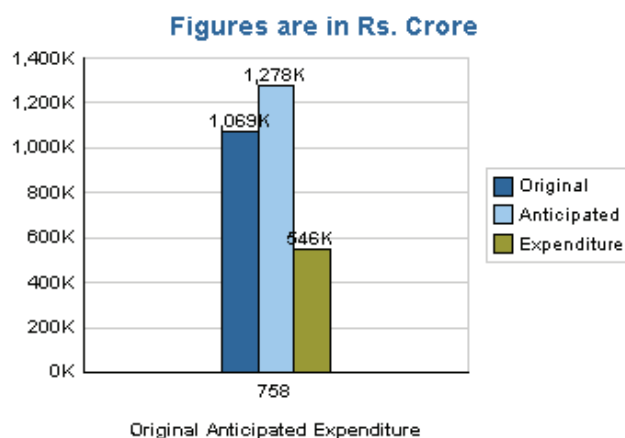

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project does not have fixed dates of commissioning.

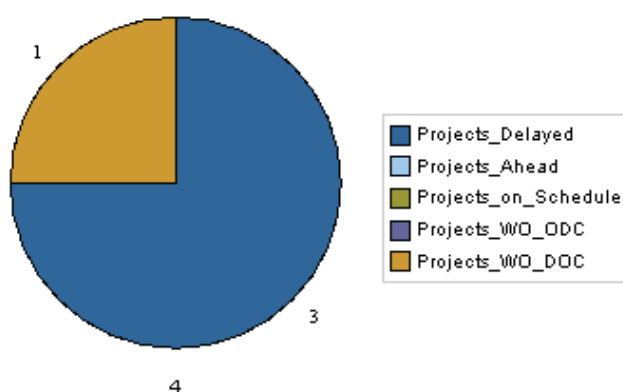

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently anticipated to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till April, 2015 is Rs. 33594.77 crore, which is 71.9% of the revised cost of the projects.

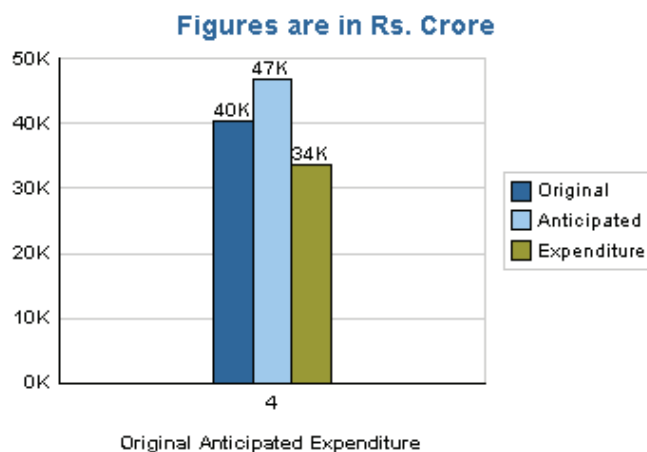

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	7
Number of Projects Delayed	4
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 4 projects are delayed .2 projects do not have fixed dates of commissioning.1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

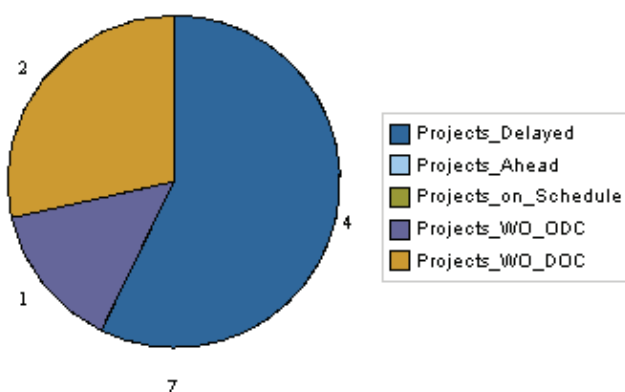

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2599.56 crore but this was subsequently anticipated to Rs. 2715.98 crore implying a cost overrun of 4.5%. The expenditure incurred on these projects till April, 2015 is Rs. 1637.71 crore, which is 60.3% of the revised cost of the projects.

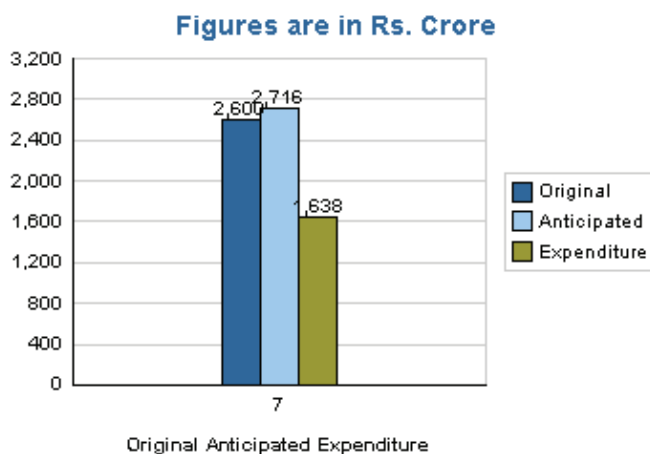

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	73
Number of Projects On Schedule	29
Number of Projects Delayed	41

Number of Projects Without Date Of Commissioning	3
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 73 projects, 29 projects are on schedule 41 projects are delayed .3 projects do not have fixed dates of commissioning.

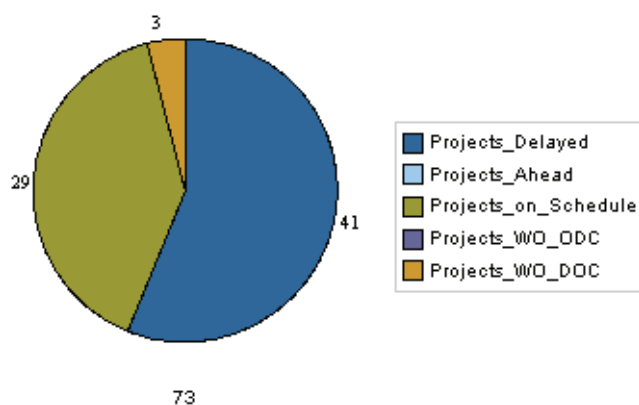

Investment Scenario

Total original cost of implementation of 73 projects when sanctioned, was of the order of Rs. 58516.59 crore but this was subsequently anticipated to Rs. 62364.85 crore implying a cost overrun of 6.6%. The expenditure incurred on these projects till April, 2015 is Rs. 21734.85 crore, which is 34.9% of the revised cost of the projects.

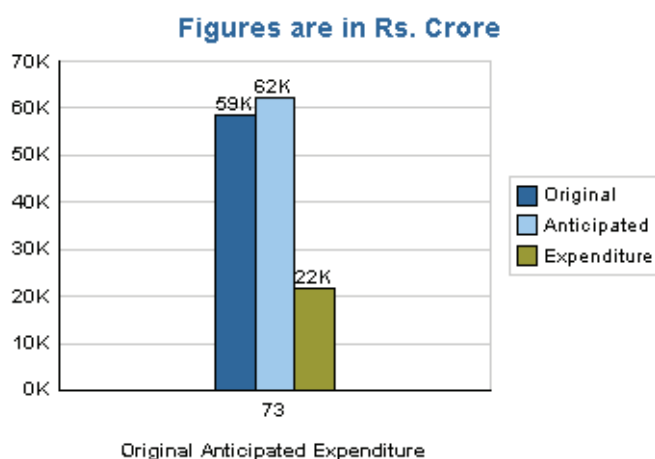

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	1
Number of Projects On Schedule	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

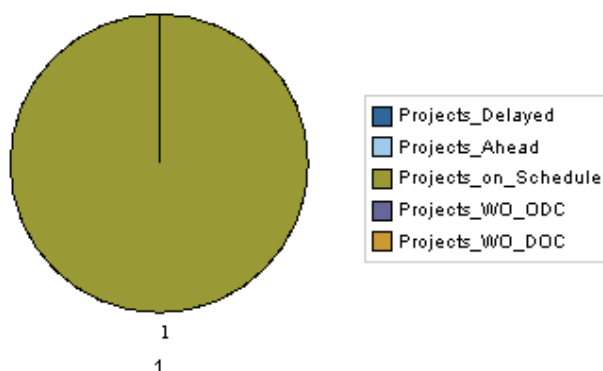

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 197.79 crore but this was subsequently anticipated to Rs. 197.79 crore. The expenditure incurred on these projects till April, 2015 is Rs. 13.09 crore, which is 6.6% of the revised cost of the projects.

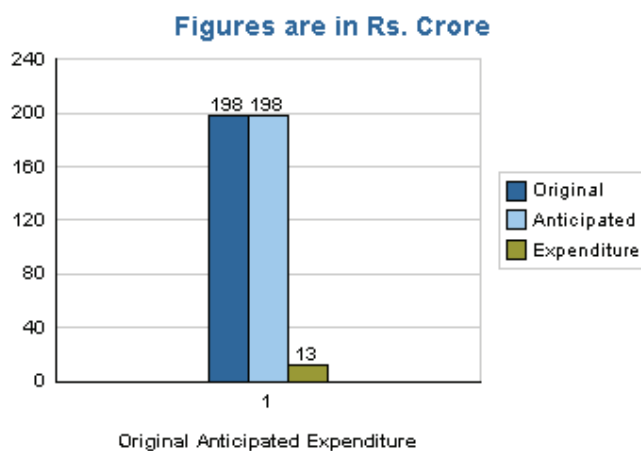

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	1
Number of Projects On Schedule	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is on schedule

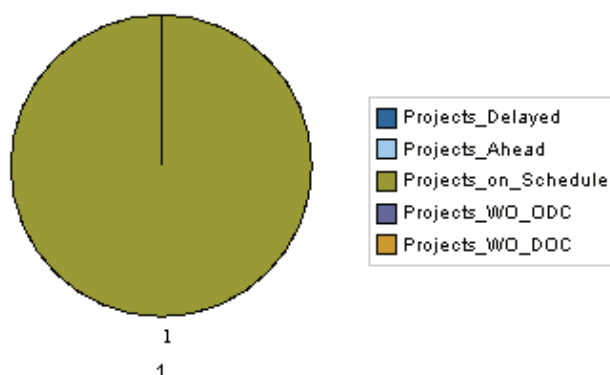

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 1856 crore but this was subsequently anticipated to Rs. 1856 crore.

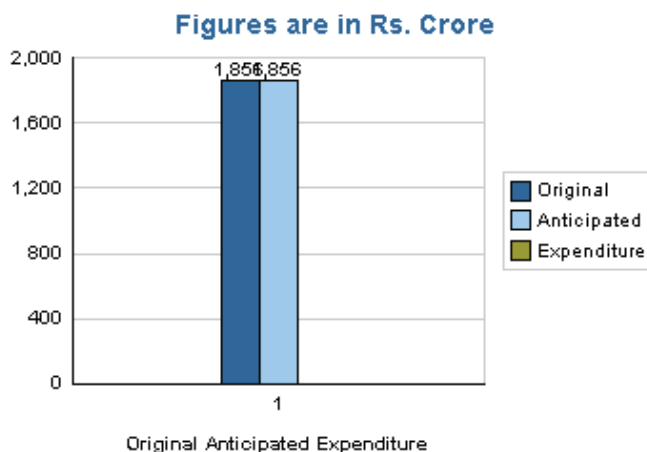

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	71
Number of Projects On Schedule	16
Number of Projects Delayed	46
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 71 projects, 1 project is ahead of schedule, 16 projects are on schedule 46 projects are delayed .7 projects do not have fixed dates of commissioning.1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

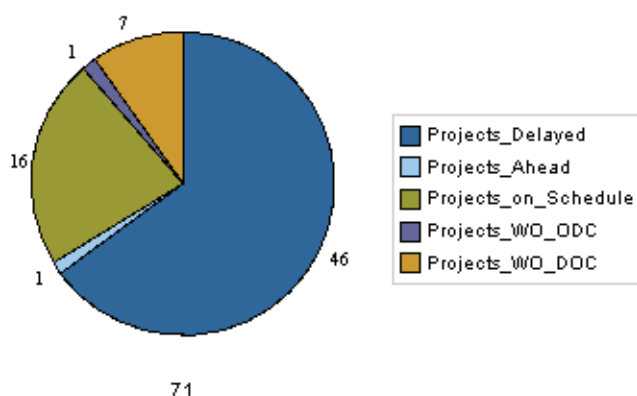

Investment Scenario

Total original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 157059.07 crore but this was subsequently anticipated to Rs. 171085.92 crore implying a cost overrun of 8.9%. The expenditure incurred on these projects till April, 2015 is Rs. 75485.57 crore, which is 44.1% of the revised cost of the projects.

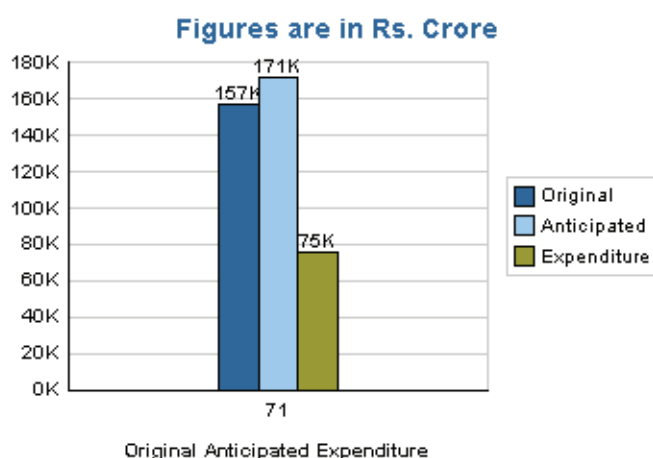

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	112
Number of Projects On Schedule	43
Number of Projects Delayed	63
Number of Projects Ahead	1

Number of Projects Without Date Of Commissioning	5
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 112 projects, 1 project is ahead of schedule, 43 projects are on schedule 63 projects are delayed .5 projects do not have fixed dates of commissioning.

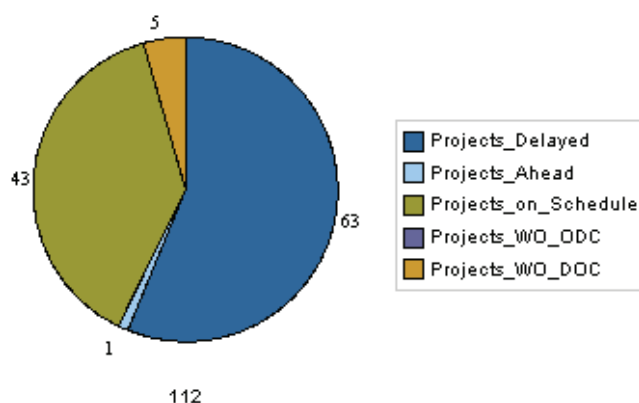

Investment Scenario

Total original cost of implementation of 112 projects when sanctioned, was of the order of Rs. 317040.36 crore but this was subsequently anticipated to Rs. 356191.36 crore implying a cost overrun of 12.3%. The expenditure incurred on these projects till April, 2015 is Rs. 157703.34 crore, which is 44.3% of the revised cost of the projects.

Figures are in Rs. Crore

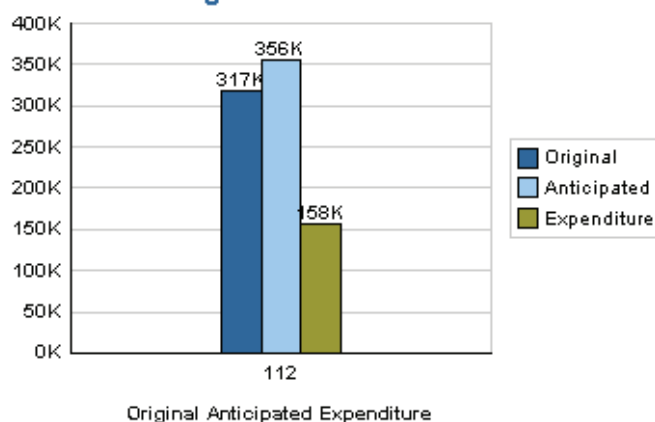

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	288
Number of Projects On Schedule	9
Number of Projects Delayed	32
Number of Projects Without Original Date of Commissioning	24
Number of Projects Without Date Of Commissioning	223


Brief Analysis

Project Status with respect to Original Schedule: Out of 288 projects, 9 projects are on schedule 32 projects are delayed .223 projects do not have fixed dates of commissioning.24 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

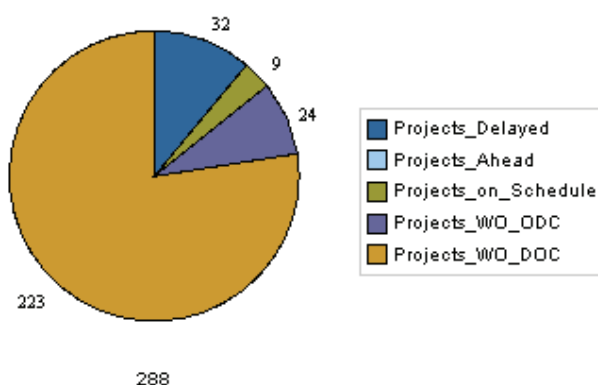

Investment Scenario

Total original cost of implementation of 288 projects when sanctioned, was of the order of Rs. 163518.2 crore but this was subsequently anticipated to Rs. 291060.49 crore implying a cost overrun of 78%. The expenditure incurred on these projects till April, 2015 is Rs. 94834.18 crore, which is 32.6% of the revised cost of the projects.

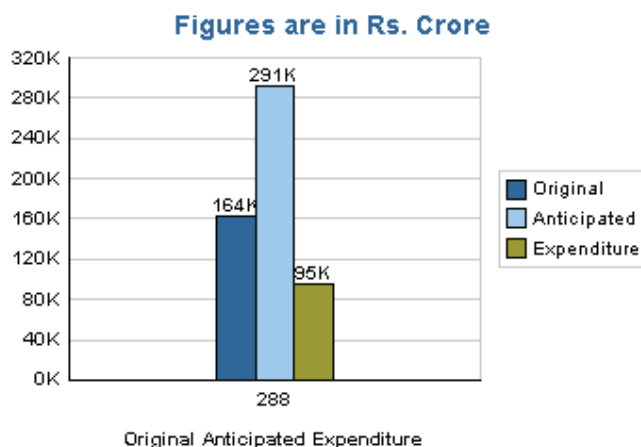

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHW

Current Status:

Number of Projects	133
Number of Projects On Schedule	5
Number of Projects Delayed	99
Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	26

Brief Analysis


Project Status with respect to Original Schedule: Out of 133 projects, 5 projects are on schedule 99 projects are delayed .26 projects do not have fixed dates of commissioning.3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

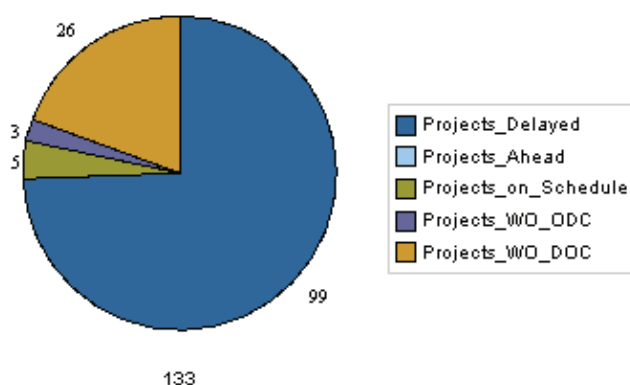

Investment Scenario

Total original cost of implementation of 133 projects when sanctioned, was of the order of Rs. 98941.44 crore but this was subsequently anticipated to Rs. 101089.44 crore implying a cost overrun of 2.2%. The expenditure incurred on these projects till April, 2015 is Rs. 84497 crore, which is 83.6% of the revised cost of the projects.

Figures are in Rs. Crore

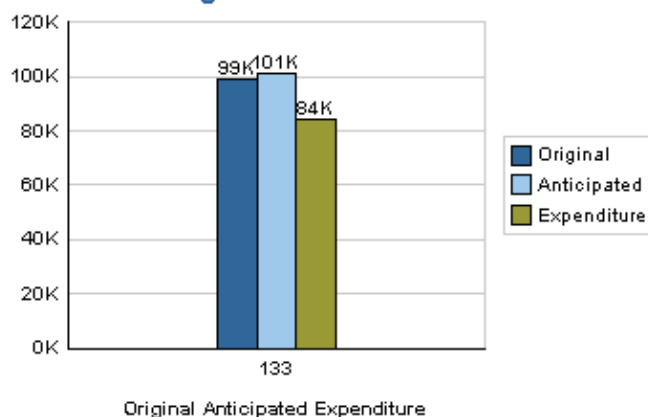

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects 6


Number of Projects Without Date Of Commissioning 6

Brief Analysis

Project Status with respect to Original Schedule: Out of 6 projects, 6 projects do not have fixed dates of commissioning.

**Investment Scenario**

Total original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5158.07 crore but this was subsequently anticipated to Rs. 5759.15 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till April, 2015 is Rs. 2393.83 crore, which is 41.6% of the revised cost of the projects.

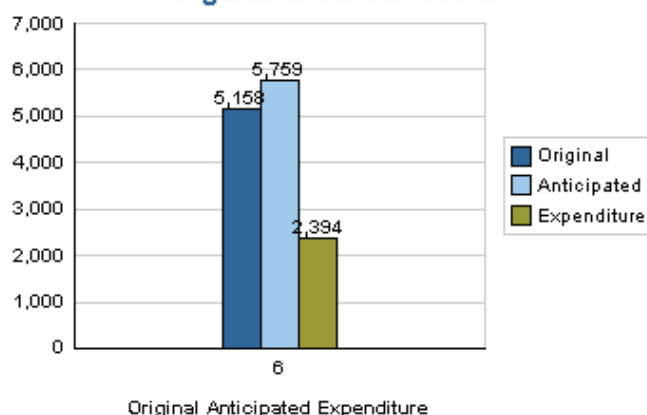Figures are in Rs. Crore

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	26
Number of Projects On Schedule	9
Number of Projects Delayed	16

Number of Projects Without Date Of Commissioning	1
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 9 projects are on schedule 16 projects are delayed .1 project does not have fixed dates of commissioning.

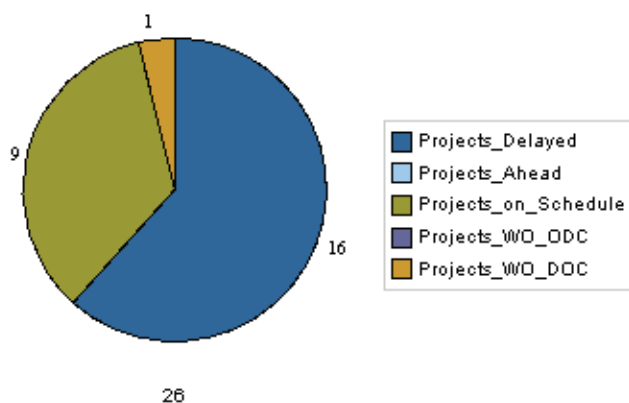

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 62807.52 crore but this was subsequently anticipated to Rs. 66521.92 crore implying a cost overrun of 5.9%. The expenditure incurred on these projects till April, 2015 is Rs. 43850.05 crore, which is 65.9% of the revised cost of the projects.

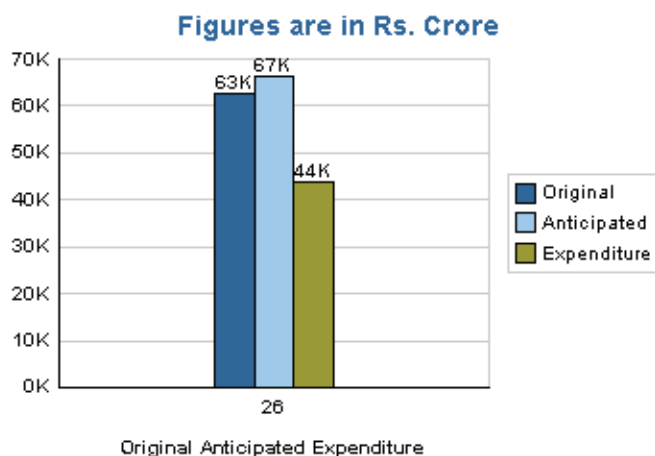

Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 1 project is on schedule 1 project is delayed .2 projects do not have fixed dates of commissioning.

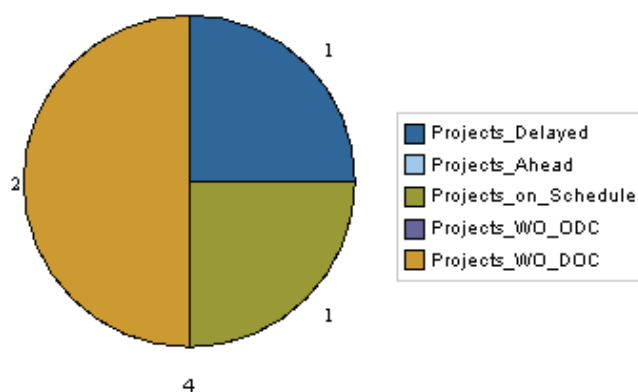

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 15131.81 crore but this was subsequently anticipated to Rs. 15131.81 crore The expenditure incurred on these projects till April, 2015 is Rs. 254.59 crore, which is 1.7% of the revised cost of the projects.

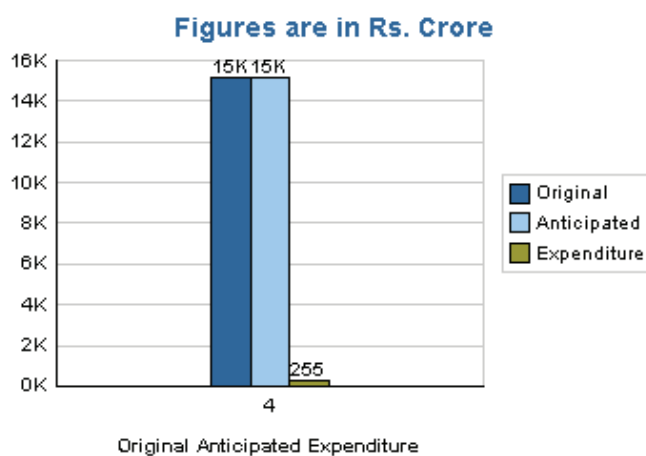

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	30
Number of Projects On Schedule	6
Number of Projects Delayed	16

Number of Projects Without Date Of Commissioning 8

Brief Analysis


Project Status with respect to Original Schedule: Out of 30 projects, 6 projects are on schedule 16 projects are delayed .8 projects do not have fixed dates of commissioning.

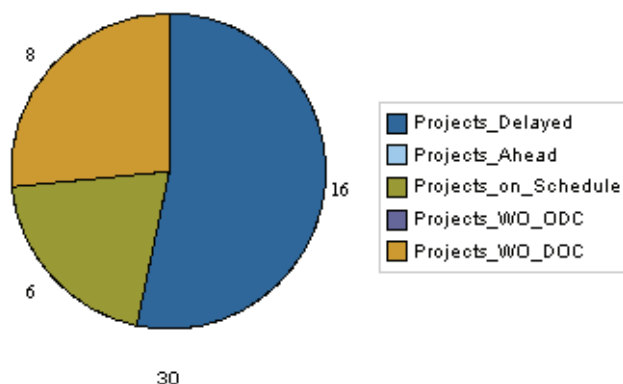

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 138680.82 crore but this was subsequently anticipated to Rs. 143894.82 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till April, 2015 is Rs. 21638.91 crore, which is 15% of the revised cost of the projects.

Figures are in Rs. Crore

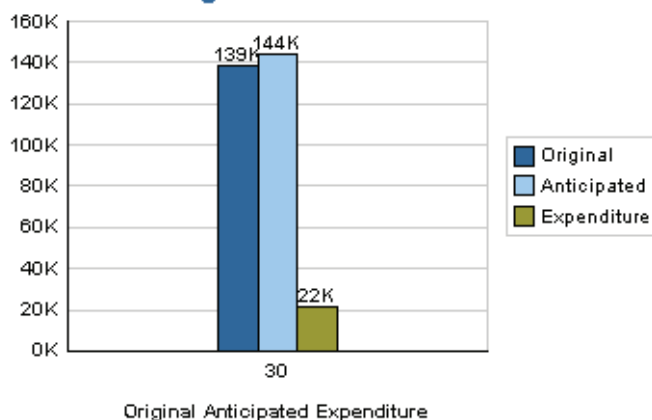

ANNEXURE

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs. 150 CRORE AND ABOVE

(All Cost/ Expenditure in Rs. Crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDAMAN & NICOBAR ISLANDS	1	314.61	314.61	17.82
2	ANDHRA PRADESH	27	24,854.07	31,076.50	19,298.43
3	ARUNACHAL PRADESH	3	9,356.22	23,263.83	12,557.07
4	ASSAM	36	23,508.04	42,053.86	33,680.34
5	BIHAR	49	58,759.98	72,729.61	34,556.14
6	CHANDIGARH	1	452	489	410.25
7	CHHATISGARH	28	80,681.93	82,344.09	41,351.63
8	DELHI	11	50,123.12	50,123.12	8,810.75
9	GOA	1	335.61	388.53	297.58
10	GUJARAT	29	36,037.34	36,616.51	17,630.32
11	HARYANA	8	4,259.81	6,230.43	7,382.50
12	HIMACHAL PRADESH	5	11,681.24	19,906.33	11,938.21
13	JAMMU AND KASHMIR	7	21,314.62	40,235.30	17,882.01
14	JHARKHAND	33	36,123.28	36,767.77	14,474.33
15	KARNATAKA	32	64,122.20	79,084.94	20,818.61
16	KERALA	13	24,457.67	28,611.45	9,437.13
17	MADHYA PRADESH	20	24,954.32	26,938.24	9,043.48
18	MAHARASHTRA	45	98,588.94	1,10,362.81	35,715.90
19	MANIPUR	1	727.56	6,570.75	2,787.99
20	MEGHALAYA	3	4,845.02	6,069.90	290.09
21	MIZORAM	2	988.06	4,201.96	1,004.63
22	MULTI STATE	187	2,18,287.38	2,44,588.58	87,423.98
23	NAGALAND	2	5,124	7,461.12	10.44
24	ODISHA	42	72,202.55	81,290.49	41,746.17
25	PUNJAB	3	792.5	765.46	110.47
26	RAJASTHAN	24	25,362.46	25,417.93	14,682.60
27	SIKKIM	2	1,648.94	4,499.46	427.38
28	TAMIL NADU	41	67,950.69	85,496.01	59,573.98
29	TELANGANA	21	9,410.62	12,180.44	3,190.86
30	TRIPURA	6	2,966.26	6,629.97	3,273.91
31	UTTAR PRADESH	30	36,706.01	39,810.35	12,446.90
32	UTTARAKHAND	6	9,351.89	12,905.21	4,726.67
33	WEST BENGAL	39	42,838.90	52,831.79	19,234.40
TOTAL		758	10,69,127.84	12,78,256.35	5,46,232.97

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	-	18,271
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	COAL	10/2004	2,030.78	3027.59	3,207.92
3	PARBATI HEP (4X200 MW) (NHPC) II	POWER	09/2002	3,919.59	-	5,040.21
4	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	POWER	09/2003	6,285.33	-	7,687.18
5	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	POWER	09/2005	1,061.38	-	1,742.55
6	VIRAMGAM-BHILDI (WR) ,GC	RAILWAYS	04/1990	155.66	-	201.26
7	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	RAILWAYS	12/1994	124.43	-	712.02
8	UDHAMPUR-SRINAGAR-BARAMULLA (NL) ,NR	RAILWAYS	03/1995	2,500	3000	10,658.34
9	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) ,NEFR	RAILWAYS	04/1983	36.8	36.38	255.55
10	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
11	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) ,SWR	RAILWAYS	02/1997	295	-	1,060.4
12	KARUR-SALEM (NL) ,SR	RAILWAYS	02/1997	155.55	-	800.66
13	NANDYAL-YERRAGUNTALA (NL) ,SCR	RAILWAYS	03/1996	155.74	164.36	755.5
14	KANPUR-KASGANJ-MATHURA (GC) ,NER	RAILWAYS	03/1997	677.97	1062.36	1,621.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	RAILWAYS	09/1997	1,500	1000	3,410.06
16	MUNEERABAD-MAHABOBNAGAR (NL) , SCR	RAILWAYS	04/1997	218.24	236.41	309.19
17	RANCHI-LOHARDAGA (GC) , SER	RAILWAYS	04/1997	194.07	-	230.67
18	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	488.76
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	RAILWAYS	04/1997	501.69	501.69	808.47
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	RAILWAYS	04/1999	108	427.21	436.85
21	KATI HAR - JOGBANI (GC) (NEFR)	RAILWAYS	09/2001	492.98	-	743.74
22	GULBARGA-BIDAR, SCR (NL)	RAILWAYS	02/1998	242.42	369.7	798.87
23	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	RAILWAYS	04/1997	863.23	-	888.87
24	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) , NR	RAILWAYS	03/2002	625.3	408.76	835.14
25	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	RAILWAYS	09/1995	100	-	596.66
26	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	RAILWAYS	03/1998	280	-	889.95
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) , NEFR	RAILWAYS	04/2000	733	733	1,732.43
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	RAILWAYS	03/2000	1,049.69	3385.14	3,541.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	GADWAL - RAICHUR (NL) , SCR	RAILWAYS	04/1998	92.63	-	301.84
30	JIND-SONEPAT (NL) ,NR	RAILWAYS	01/2004	238.56	-	639.77
31	RAJATGARH-BARANG (LD) , ECR	RAILWAYS	04/1999	166.16	-	305.47
32	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	RAILWAYS	04/2003	727.56	727.56	2,787.99
33	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	RAILWAYS	04/2002	921	-	1,548.9
34	PATNA GANGA BRIDGE (NL) , ECR	RAILWAYS	04/2001	624.47	-	2,339.6
35	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	915.7	3,198.3
36	ETAHAH-MAINPURI (NL) ,NCR	RAILWAYS	04/1997	120	245.39	249.33
37	CUTTACK - BARANG (LD)	RAILWAYS	04/1995	127.13	-	193.37
38	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RAILWAYS	04/2000	133.41	207	277.33
39	RAICHUR-GUNTAKAL (DL) (SCR)	RAILWAYS	04/2003	136.62	-	277.09
40	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	228.3
41	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	191.8
42	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	251.5

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	HARANGAJO TO MAIBANG (AS-23) , KM.126.450 TO KM.140.700	ROAD TRANSPORT AND HIGHWAYS	12/2003	280	-	366.8
44	MAIBANG TO LUMDING (AS-24) , KM.111.000 TO KM.126.450	ROAD TRANSPORT AND HIGHWAYS	12/2003	155.04	-	173.8
45	MAIBANG TO LUMDING (AS-27) , KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	207.6
46	BIJNI TO ASSAM WB BORDER (NH- 31.C) (1) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	280.3
47	BIJNI TO ASSAM /WB.BORDER (NH- 31.C) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	328.6
48	FORBESGANJ TO SIMRAHI (NH- 57) (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	550.3
49	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	326.3
50	C/O NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	CIVIL AVIATION	01/2009	309.46	-	338.82
51	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,925.4
52	KISHANGANGA HEP (3X110 MW)	POWER	01/2009	3,642.04	-	3,934.97
53	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	8,631
54	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	POWER	11/2011	2,127.51	-	2,172.33
55	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	496.28
56	BHOPAL BINA 3D LINE DOUBLING	RAILWAYS	09/2007	687.2	-	793.71

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	457.88
58	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	846.18
59	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.7
60	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	200	213.72
61	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	RAILWAYS	04/2006	325	-	420.71
62	AGARTALA SABROOM, NL, NEFR	RAILWAYS	04/2008	813.34	813.34	823.83
63	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	703.56
64	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	RAILWAYS	04/1999	207.52	-	223.44
65	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.83
66	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,734.45
67	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.72
68	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	794.78
69	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	253.1
70	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.56

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1998	271.24	-	462.69
72	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	RAILWAYS	04/2008	822.39	-	1,031.83
73	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	575	1,005.81
74	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	619.87
75	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	380.6	1,040.11
76	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	227.84
77	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	240.21
78	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	339.53
79	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	800.9
80	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	218.67
81	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
82	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	290.2
83	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	315.9
84	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
86	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	276.7
87	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	334.1
88	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	211.8
89	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	289.5
90	HARANGAJO TO MAIBANG, NH-54	ROAD TRANSPORT AND HIGHWAYS	12/2003	196	-	242.1
91	BRAHMPUTRA BRIDGE, NH NO-31	ROAD TRANSPORT AND HIGHWAYS	12/2003	217.61	309.56	457.7
92	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,125
93	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	317.5
94	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	667.1
95	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,601
96	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,133
97	CHENNAI-TADA (SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
98	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
100	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
101	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,983
102	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,388
103	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
104	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
105	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	901.6
106	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,273
107	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	761.3
108	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
109	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	808.7
110	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,425
111	4 LANING OF NAGPUR-BETUL	ROAD TRANSPORT AND HIGHWAYS	02/2011	2,498.76	-	2,786
112	BELGAUM-DHARWAD (NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	665.8

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	INDORE-DEWAS (NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	611.8
114	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.6
115	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,392
116	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	941
117	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,178
118	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	-	2,445
119	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,374
120	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	842.2
121	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
122	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,188
123	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	776.4
124	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	991.7
125	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	408.1
126	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	835.6

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
128	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	633.3
129	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	982.9
130	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	699.6
131	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,922
132	4-LANING OF BRAHAMPURE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,610
133	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	726.4
134	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	-	373.22

Details of Projects Without Date of Commissioning

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>ATOMIC ENERGY</u>				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 5,677.00	09/2010 09/2016	-
	Total		3,492.00 -		
	<u>CIVIL AVIATION</u>				
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI, GOA	05/2010	335.61 -	05/2012 -	03/2015
3	GAGAN PROJECT - [N04000065]AAI, MULTI STATE	09/2008	626.00 -	06/2013 -	-
	Total		961.61 -		
	<u>COAL</u>				
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, TELANGANA	10/2006	249.03 -	03/2012 -	-
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL, TELANGANA	09/2007	467.78 -	03/2013 -	-
6	BATURA OCP (2.0 MTY) - [N06000049]SECL, MADHYA PRADESH	09/2008	203.82 -	03/2015 -	03/2015
	Total		920.63 -		
	<u>STEEL</u>				
7	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	607.17 -	12/2011 01/2015	03/2015
	Total		607.17 -		
	<u>PETROLEUM</u>				
8	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 761.68	05/2013 06/2014	03/2015
9	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	03/2012	1,419.00 -	12/2014 -	03/2015
10	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL, TAMIL NADU	05/2013	711.00 -	- -	-
11	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL, TAMIL NADU	11/2006	171.83 -	- -	-
12	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL, MULTI STATE	01/2015	1,823.00 -	- -	-
13	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL, MULTI STATE	01/2015	2,321.00 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
14	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE	02/2015	890.00 -	- -	-
	Total		8,197.62 -		
	<u>POWER</u>				
15	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	05/2014 -	05/2014
16	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	10/2013 -	03/2015
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-
18	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
19	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
	Total		19,418.15 -		
	<u>RAILWAYS</u>				
20	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
21	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
22	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
23	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	07/2012
24	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
25	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	06/2013
26	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
27	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
28	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
29	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	02/2009 02/2009	08/2014
30	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	08/2014
31	CUTTACK - BARANG (LD) - [220100326]RVNL,ODISHA	04/1995	127.13 -	- 10/2014	10/2014
32	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	03/2009 12/2012	12/2014
33	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	06/2013 -	01/2015
34	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	01/2015

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
35	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	03/1994 -	03/2015
36	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2015
37	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	- -	03/2015
38	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	- -	03/2015
39	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 393.46	03/2007 03/2007	03/2015
40	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	- 05/2009	03/2015
41	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NFR,ASSAM	01/2004	915.70 915.70	- -	03/2015
42	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	03/2015
43	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	03/2015
44	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	- -	03/2015
45	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER,MULTI STATE	04/2011	248.07 -	03/2015 -	03/2015
46	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2015
47	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	03/2015 -	03/2015
48	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
49	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
50	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
51	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
52	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
53	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	-
54	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
55	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-
56	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
57	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
58	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
59	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 501.69	03/2012 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
60	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
61	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
62	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
63	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
64	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
65	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
66	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,385.14	12/2006 -	-
67	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
68	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-
69	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	12/2012 12/2012	-
70	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	138.00 -	- -	-
71	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
72	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
73	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
74	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
75	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
76	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
77	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
78	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
79	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	02/2015 -	-
80	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
81	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
82	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
83	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
84	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, CHHATISGARH	09/2006	324.90 -	03/2010 -	-
86	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	404.19 -	- -	-
87	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NFR, MULTI STATE	12/2006	170.00 -	03/2011 -	-
88	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	125.00 -	- -	-
89	TIDIVANAM-NAGARI (NL) - [N22000085]SR, TAMIL NADU	09/2006	456.00 -	- -	-
90	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
91	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR, RAJASTHAN	04/2008	653.19 -	03/2014 -	-
92	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR, RAJASTHAN	04/2008	516.23 732.06	03/2014 -	-
93	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER, JHARKHAND	04/2008	167.73 -	03/2012 -	-
94	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	533.38 -	12/2011 -	-
95	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
96	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
97	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	-
98	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	-
99	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	-
100	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-
101	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
102	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-
103	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-
104	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-
105	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-
106	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
107	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-
108	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-
109	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-
110	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
111	DHASA-JETALSAR (GC) - [N22000141]WR,GUJARAT	04/2012	376.59 -	- -	-
112	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	- -	-
113	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 913.48	- -	-
114	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR,GUJARAT	04/2013	1,266.89 -	- -	-
115	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	- -	-
116	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	- -	-
117	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
118	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
119	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
120	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
121	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
122	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
123	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
124	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
125	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
126	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
127	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
128	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
129	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
130	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-
131	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
132	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
133	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
134	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
135	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
136	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
137	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
138	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
139	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
140	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
141	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-
142	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
143	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
144	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
145	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
146	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
147	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
148	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
149	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
150	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
151	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
152	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
153	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
154	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	- -	-
155	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
156	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
157	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
158	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
159	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
160	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
161	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	- -	-
162	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
163	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
164	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
165	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
166	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
167	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
168	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
169	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
170	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
171	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
172	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
173	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
174	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
175	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
176	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
177	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
178	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
179	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-
180	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
181	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
182	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
183	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
185	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	- -	-
186	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
187	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
188	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
189	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
190	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
191	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
192	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
193	KONDAPALLI-PENUBALLI - [N22000260]SCR,MULTI STATE	04/2013	723.00 -	- -	-
194	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,054.35 -	- -	-
195	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCR,MULTI STATE	04/2008	184.26 -	- -	-
196	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
197	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
198	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
199	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
200	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
201	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
202	DELHI-SOHA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
203	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
204	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
205	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
206	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
207	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
208	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
209	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
210	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
211	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
212	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
213	MUDKHED-PARBHANI - [N22000283]SCR,MAHARASHTRA	04/2011	390.60 -	- -	-
214	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
215	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	337.49 -	- -	-
216	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	- -	-
217	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
218	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
219	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
220	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
221	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
222	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
223	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
224	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
225	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
226	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
227	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
228	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-
229	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
230	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-
231	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	01/1999 -	-
232	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	01/1999 -	-
233	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	01/1999 -	-
234	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	01/1999 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
235	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	01/1999 -	-
236	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	- -	-
237	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	- -	-
238	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	- -	-
239	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	- -	-
240	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
241	THANJAVUR - PONMALAI DOUBLING (46.96 KM) WITH BYE-PASS LINE BEFORE PONMALAI (1.13 KM) - [N22000322]SR,TAMIL NADU	04/2011	190.10 -	- -	-
242	HOSADURGA - CHICKJAJUR (28.89 KM) - [N22000324]SWR,KARNATAKA	04/2010	203.40 -	- -	-
	Total		105,458.60 -		
	ROAD TRANSPORT AND HIGHWAYS				
243	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
244	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
245	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
246	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013
247	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
248	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
249	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
250	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
251	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	10/2014 -	10/2014
252	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	10/2008 -	01/2015
253	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,ASSAM	12/2003	157.47 157.47	09/2007 03/2014	03/2015
254	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	04/2008 01/2015	03/2015
255	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
256	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
257	NALBARI TO BIJINI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
258	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
259	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
260	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-
261	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	-
262	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	07/2012 -	-
263	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
264	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	10/2013 -	-
265	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	10/2014 -	-
266	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	07/2014 -	-
267	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
268	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		15,172.76 -		
	<u>SHIPPING AND PORTS</u>				
269	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
270	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 -	12/2010 -	-
271	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
272	MODIFICATION AND STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	-
273	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 -	04/2009 -	-
274	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	-
	Total		5,158.07 -		
	<u>TELECOMMUNICATIONS</u>				
275	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	01/2009 -	03/2015
276	EXECUTION OF TELECOM NETWORK REQUIREMENT OF DEFENCE FORCES - [N26000065]BSNL,MULTI STATE	05/2006	1,077.00 -	03/2009 -	-
	Total		1,413.81 -		
	<u>URBAN DEVELOPMENT</u>				
277	C/O MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	09/2013

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
278	LECTURE THEATER AND LAB COMPLEX AT IIT HAUZKHAS NEW DELHI - [N28000064]CPWD,DELHI	01/2010	162.90 -	07/2012 -	06/2014
279	DEVELOPMENT OF STATE HIGHWAYS IN THE STATE OF BIHAR UNDER RSVY PATNA - [N28000078]CPWD,BIHAR	11/2006	2,727.89 -	03/2010 -	10/2014
280	OFFICE BUILDING FOR INCOME TAX DEPARTMENT ON PLOT NO C- 41-43 G BLOCK BANDRA - [N28000068]CPWD,MAHARASHTRA	02/2011	241.33 -	11/2014 -	12/2014
281	C/O MARRIED ACCOMODATION AT MILITARY MOD STATION MAMUN PUNJAB - [N28000070]CPWD,PUNJAB	08/2005	191.24 -	08/2007 -	03/2015
282	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	-
283	RESIDENTIAL AND OTHER COMPLEXES FOR THE CAMPUS OF IIT PATNA AT BIHTA - [N28000063]CPWD,BIHAR	02/2012	171.10 -	09/2014 -	-
284	REHABILITATION AND STRENGTHENING OF SEWETRAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI(IN ZONE 2 IN - [N28000082]JnNURM,ANDHRA PRADESH	08/2007	246.90 -	- -	-
	Total		10,301.59 -		
	Grand Total		171,102.01		

Details of Projects Without Original Date of Commissioning

(April 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>CIVIL AVIATION</u>								
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, ANDAMAN & NICOBAR ISLANDS	10/2013	314.61	314.61	17.82	-	09/2018	-	0/0
	Total		314.61	314.61	17.82				0/0
	<u>PETROLEUM</u>								
2	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL, MULTI STATE	01/2015	690.00	690.00	-	-	07/2018	-	0/31
	Total		690.00	690.00	.00				0/31
	<u>RAILWAYS</u>								
3	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, UTTAR PRADESH	04/1997	863.23	1,072.51	888.87	-	06/2015	-	0/0
4	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER, MULTI STATE	04/1999	744.71	744.71	576.86	-	03/2016	-	0/1
5	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71	1,503.71	341.60	-	02/2017	-	0/0
6	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314]WCR, MADHYA PRADESH	04/2001	470.92	1,225.90	257.59	-	03/2017	-	0/0
7	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79	1,101.16	194.91	-	03/2017	-	0/0
8	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	200.00	496.24	213.72	-	03/2017	-	0/0
9	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52	394.28	233.46	-	03/2017	-	0/0
10	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER, JHARKHAND	04/2012	258.20	365.00	2.52	-	12/2017	-	0/0
11	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	282.92	565.13	2.80	-	03/2018	48(R3)	0/0
12	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	252.00	886.65	-	-	03/2018	-	0/0
13	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NFR, WEST BENGAL	04/2011	209.77	441.45	85.78	-	03/2018	-	0/0
14	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NFR, WEST BENGAL	04/2012	283.55	288.81	11.74	-	03/2018	-	0/0

(April 2015)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 171.00	679.57	40.41	- -	03/2018	-	0/0
16	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	165.82 165.82	435.58	0.56	- -	03/2018	-	0/0
17	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NFR,MULTI STATE	04/1999	523.17 380.60	1,653.55	1,040.11	- -	03/2018	-	0/0
18	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	312.12 257.93	453.10	134.79	- -	03/2018	-	0/0
19	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	1,143.60	189.12	- -	03/2018	-	0/0
20	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	36.80 36.38	1,336.57	255.55	- -	03/2019	-	0/0
21	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	300.00 300.00	827.73	53.52	- -	03/2019	-	0/0
22	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 1,798.00	1,887.90	-	- -	03/2019	-	0/0
23	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 205.31	563.13	22.29	- -	03/2019	-	0/0
24	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 246.07	364.06	0.30	- -	03/2019	-	0/0
25	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 651.17	1,009.00	7.50	- -	12/2019	-	0/0
26	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	4,083.02 -	5,307.90	7.79	- 03/2016	03/2020	48(R3)	0/0
	Total		15,003.16 -	24,747.24	4,561.79				0/1
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
27	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	808.70	- -	05/2015	-	1/1
28	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	665.80	- -	05/2015	-	2/2
29	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,273.00	- -	06/2015	-	2/3
	Total		1,604.00 -	1,604.00	2,747.50				5/6
	Grand Total		17,611.77	27,355.85	7,327.11				5/38

Details of On Schedule Projects w.r.t. Original Schedule

							(April 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	764.09	03/2023 03/2023	03/2023
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	778.30	03/2016 -	03/2016
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.10 -	490.10	186.68	03/2017 -	03/2017
4	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	0.46	03/2023 03/2023	03/2023
5	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	104.36	03/2020 -	03/2020
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.82	03/2016 -	03/2016
7	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016
8	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	77.88	03/2018 -	03/2018
9	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	74.44	03/2016 -	03/2016
10	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	431.45	69.94	03/2016 -	03/2016
11	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	101.90	03/2020 -	03/2020
12	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.33	-	03/2022 -	03/2022
13	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	-	03/2021 -	03/2021
14	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017
15	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	148.67	03/2018 -	03/2018
16	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020
17	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]	5/2014	479.15 -	479.15	6.34	03/2019 -	03/2019
18	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026
19	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]	5/2014	337.66 -	337.66	-	03/2019 -	03/2019
20	KULDA EXPN OC. (5.00 MTY) - [N06000115]	6/2014	289.03 -	289.03	-	03/2018 -	03/2018
21	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021
22	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020

(April 2015)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
23	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	70.90	03/2021 -	03/2021
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	89.38	03/2018 -	03/2018
25	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	187.94	32.35	03/2023 -	03/2023
26	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
27	AMERA OC RCE - [N06000123]	2/2015	335.97 -	335.97	30.30	03/2018 -	03/2018
28	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	106.44	03/2021 -	03/2021
29	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	30.24	03/2021 -	03/2021
	Total		27,351.75 -	27,191.95	3,083.36		
	<u>FERTILISERS</u>						
30	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	13.09	11/2016 -	11/2016
	Total		197.79 -	197.79	13.09		
	<u>MINES</u>						
31	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
32	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	3,576.16	05/2015 -	05/2015
33	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	93.08	09/2017 -	09/2017
34	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	123.67	12/2016 -	12/2016
35	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
36	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	34.08	01/2017 -	01/2017
37	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	379.10	05/2017 05/2017	05/2017
38	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	44.52	12/2018 -	12/2018
39	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	17.38	07/2016 -	07/2016
40	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	96.36	09/2017 -	09/2017

							(April 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
41	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	29.03	02/2016 -	02/2016
42	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2016
43	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	6,072.90	05/2016 -	05/2016
44	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	39.42	07/2016 -	07/2016
45	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.44	04/2015 -	04/2015
46	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
47	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,024.42	11/2015 -	11/2015
	Total		51,865.05 -	54,527.98	11,619.87		
	<u>POWER</u>						
48	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,031.00	01/2017 -	01/2017
49	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	241.60	05/2016 -	05/2016
50	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME - PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	-	05/2018 -	05/2018
51	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	-	01/2018 -	01/2018
52	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
53	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	-	03/2018 -	03/2018
54	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
55	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
56	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	5.00	05/2018 -	05/2018
57	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	-	07/2017 -	07/2017
58	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	-	11/2017 -	11/2017
59	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	-	05/2017 -	05/2017
60	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	-	03/2018 -	03/2018
61	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	22.00	04/2018 -	04/2018
62	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	109.00	09/2019 -	09/2019

						(April 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,071.00	02/2019 -	02/2019
64	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,457.00	08/2018 -	08/2018
65	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	682.00	03/2019 -	03/2019
66	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	542.00	12/2016 -	12/2016
67	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	1.00	11/2016 -	11/2016
68	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	1.00	07/2016 -	07/2016
69	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
70	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	48.00	12/2015 -	12/2015
71	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	61.00	08/2016 -	08/2016
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	25.00	06/2016 -	06/2016
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	16.00	06/2016 -	06/2016
74	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
75	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	147.34	04/2016 -	04/2016
76	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
77	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
78	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	1.00	02/2016 -	02/2016
79	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
80	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	11.00	02/2017 -	02/2017
81	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	442.00	03/2018 -	03/2018
82	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
83	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	40.00	10/2016 -	10/2016
84	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	05/2016 -	05/2016
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	185.49	03/2016 -	03/2016
86	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	3,959.00	09/2016 -	09/2016

							(April 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
87	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	3,850.00	06/2017 -	06/2017
88	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017
89	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,011.00	09/2017 -	09/2017
90	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,782.00	08/2015 -	08/2015
	Total		148,352.17 -	148,352.17	26,884.43		
	<u>RAILWAYS</u>						
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	626.11	03/2016 -	03/2016
92	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
93	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
94	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
95	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	536.01	03/2016 -	03/2016
96	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
97	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
98	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	43.93	03/2016 -	03/2016
99	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016
	Total		15,043.28 -	19,672.48	3,750.32		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
100	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
101	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015
102	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
103	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	178.20	09/2016 -	09/2016
104	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
	Total		7,164.88 -	7,164.88	1,762.20		

							(April 2015)
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	STEEL						
105	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	217.48	06/2015 -	06/2015
106	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016
107	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	109.01	04/2016 -	04/2016
108	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]	4/2014	188.93 -	188.93	16.95	04/2015 -	04/2015
109	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	79.15	07/2016 -	07/2016
110	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	24.02	10/2016 -	10/2016
111	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016
112	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
113	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018
	Total		6,436.81 -	6,582.21	480.92		
	TELECOMMUNICATIONS						
114	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	URBAN DEVELOPMENT						
115	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
116	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
117	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
118	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019
119	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
120	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		45,907.98 -	45,907.98	.00		
	Grand Total		317,509.71	324,787.44	47,594.19		

Details of Projects Ahead of Schedule w.r.t. Original Schedule

						(April 2015)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 -	232.00	132.71	09/2016 -	12/2015
	Total		141.86 -	232.00	132.71		
	<u>POWER</u>						
2	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154	10/2013	1,315.90 -	1,315.90	380.47	10/2016 -	03/2016
	Total		1,315.90 -	1,315.90	380.47		
	Grand Total		1,457.76	1,547.90	513.18		

Details of Delayed Projects w.r.t. Original and Revised Schedule

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 -	17,270.00	18,271.00	12/2008 -	06/2015	78	31.12	
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	6,297.00	12/2015 -	10/2017	22	0	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,059.00	12/2016 -	04/2018	16	0	
	Total		36,950.00 -	41,049.00	28,627.00					
	<u>CIVIL AVIATION</u>									
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 489.00	489.00	410.25	03/2015 -	04/2015	1	8.19	
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	58.50	03/2014 -	05/2015	14	0	
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6	12.18	
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	338.82	01/2011 -	06/2017	77	0	
	Total		1,323.34 -	1,386.84	807.61					
	<u>COAL</u>									
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	04/2015	1	0	
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,175.16	03/2012 05/2014	05/2015	38	34.63	Inadequate mobilization of resources by the contractor M/s BHEL and slow progress of civil,structural fabrication and erection.

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,477.21	3,207.92	06/2009 03/2013	06/2015	72	71.23	i) Delay in acceptance testing and handover ii) Inadequate mobilization by the contractor
11	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	131.44	10/2014 -	06/2015	8	0	i) Delay in acquisition of private lands ii) Delay in civil works iii) Delay in equipment erection iv) Delay in acquisition of lands and completion of foundations by the contractor M/s LSML.
12	ADRIYALA SHAFT PROJECT - [N060000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.85	03/2013 09/2012	09/2015	30	478.5	i) Delay in supply of LW equipment ii) Delay in drive of gate roadways and installation of belt conveyors.
13	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,846.08	03/2014 -	03/2016	24	0	
14	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,676.56	03/2014 -	03/2016	24	0	
15	KRISHNASHILA (NCL) (4MTY) - [N060000007]NCL, UTTAR PRADESH	06/2011	789.88 -	741.62	466.94	03/2013 -	03/2016	36	-6.11	i) Delay in land acquisition ii) Delay in Environment clearance iii) Coal evacuation problem
16	BLOCK-B OCP NCL (3.5 MTY) - [N060000009]NCL, MADHYA PRADESH	06/2011	746.04 -	535.10	367.12	03/2015 -	03/2016	12	-28.27	
17	MAGADH OC 20 MTY (CCL) - [N060000015]JCL, JHARKHAND	08/2008	469.78 -	706.40	55.30	07/2012 -	03/2016	44	50.37	i) Law & Order ii) Environmental Clearance iii) Coal evacuation problem
18	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N060000033]NCL, MADHYA PRADESH	10/2007	259.40 -	259.40	12.53	03/2012 -	03/2016	48	0	
19	CHURCHA ROUG (1.35MTY) - [N060000046]SECL, CHHATISGARH	06/2008	462.35 -	462.35	298.60	03/2014 -	03/2016	24	0	
20	RAJMAHAL OC EXP. - [N060000056]JCL, JHARKHAND	09/2009	153.82 -	153.82	55.48	03/2014 -	03/2016	24	0	i) Law & Order ii) Contractual Issues iii) Land acquisitions iv) Rehabilitation & Resettlement Problems

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
21	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97 -	418.97	326.51	03/2012 -	03/2016	48	0	i) Delay in acquisition of private land ii) R & R problem iii) Law & order
22	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	181.19	36.60	03/2012 -	03/2016	48	0	i) Environmental Clearance ii) Land acquisition Problems iii) R & R problems
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	211.71	03/2014 -	03/2016	24	0	
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	35.68	03/2011 -	03/2016	60	0	i) Contractual Issues ii) Law & Order ii) Environmental Clearance
25	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	149.41	03/2012 -	03/2016	48	0	i) Rehabilitation & Resettlement Problems ii) Law & Order ii) coal evacuation Problems
26	MURADH UG TURN-KEY PROJECT - [N06000096]BCCL, JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 03/2016	03/2016	23	0	
27	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	209.78	75.31	03/2015 -	04/2016	13	0	
28	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	132.68	03/2010 -	03/2017	84	0	Coal Evacuation problem
29	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	471.66 341.63	341.63	117.84	03/2011 -	03/2017	72	-27.57	i) Law & Order ii) Coal evacuation problems
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18 -	287.17	142.59	03/2011 -	03/2017	72	0	i) Contractual Issues ii) environment clearance
31	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	162.21	03/2013 -	03/2017	48	0	i) Environmental Clearance ii) Coal evacuation Problems ii) Rehabilitations & Resettlement Problems
32	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	148.02	03/2010 -	03/2017	84	0	Rehabilitations & Resettlement Issues
33	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	453.63	104.49	12/2012 -	03/2017	51	0	i) Contractual Issues (TPO selection) ii) Adverse Geomining Conditions
34	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	172.80	03/2012 -	03/2017	60	0	i) Environmental Clearance ii) Delay in forest land Diversion

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53	479.53	118.94	03/2013	03/2017	48	0	Environmental Clearance
36	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	83.27	03/2012	03/2017	60	0	i) Rehabilitations & Resettlement Problems ii) Law & order iii) Coal evacuation problems
37	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98	210.98	186.69	03/2013	03/2017	48	0	i) Rehabilitations & Resettlement Problems ii) Law & Order iii) Environmental Clearance
38	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	69.64	03/2014	03/2017	36	0	i) Rehabilitations & Resettlement Problems ii) Law & Order iii) Authentication of land
39	RG OC -III EXTENSION (PHASE - II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Jallaram vague diversion
40	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33	417.33	11.41	07/2016	03/2017	8	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems
41	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29	242.29	0.06	03/2015	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land. iv) Environment clearance
42	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36	0	i) Land Acquisition ii) Rehabilitation & Resettlement Problems iii) Delay in diversion of forest land. iv) Environment clearance
43	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11	5,907.11	845.30	12/2015 04/2018	04/2018	28	0	Delay in opening and evaluation of bids
44	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27	1,230.27	84.78	04/2015 04/2019	04/2019	48	0	
45	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	0	Delay in Environment and forestry Clearance.
46	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	21.55	03/2015	03/2020	60	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
47	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44 -	-	03/2014 -	03/2020	72	0	
48	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87 -	76.74	03/2015 -	03/2021	72	0	i) Rehabilitation & resettlement problems. ii) Environmental clearance
	Total		30,244.21 -	34,252.27	18,577.64					
	<u>STEEL</u>									
49	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,301.23	10/2009 10/2012	05/2015	67	41.41	
50	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,111.95	12/2011 -	05/2015	41	0	
51	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,585.10	12/2012 -	05/2015	29	0	
52	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00 -	677.00	512.18	09/2013 -	05/2015	20	0	
53	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	377.33	09/2009 05/2012	06/2015	69	-6.25	
54	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	457.14	04/2013 09/2014	06/2015	26	0	
55	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	125.27	11/2013 -	06/2015	19	0	
56	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	120.73	09/2014 -	06/2015	9	0	
57	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	379.89	05/2013 01/2015	08/2015	27	0	
58	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	151.10	10/2013 -	08/2015	22	0	
59	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	164.00	12/2014 -	08/2015	8	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
60	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,389.17	03/2013 -	09/2015	30	0	
61	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	174.36	08/2014 -	11/2015	15	0	
62	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	175.54	07/2015 -	03/2016	8	0	
63	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	15,525.00	6,807.44	05/2015 12/2016	12/2016	19	0	
64	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	149.34	07/2015 -	03/2017	20	0	
	Total		55,763.54 -	59,332.54	42,981.77					
	<u>PETROCHEMICALS</u>									
65	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,595.08	04/2012 12/2013	06/2015	38	80.08	•
	Total		5,460.61 -	9,833.52	8,595.08					
	<u>PETROLEUM</u>									
66	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	6,100.00	5,925.40	08/2010 03/2012	05/2015	57	87.76	Contract terminated as contractor failed to submit PBG insurance. - Splitting of facility into three packages, scope optimisation in view of the price rise in oil field services/equipments and preparation of fresh bid packages. - Completion of well platforms and process platform got delayed. - Cost Overrun is due to increased facility and drilling cost.

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
67	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	05/2015	26	45.9	Due to delay in award of work for project facilities (well platforms & pipelines, hiring of FPSO) . -Delay in award of contract of Well platform and pipelines. -Cost hiring of FPSO is very high compared to the initial estimate during preparation of FR.
68	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 05/2015	05/2015	21	-18.75	Delay in award of work. - Slow progress by the contractors. -Custom bond issue with M/S SHM Shipcare and some vessels of M/s Abu Dhabi waiting for customs and DGFT clearances.
69	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 1,417.00	1,417.00	1,410.50	05/2014 05/2015	05/2015	12	-44.37	Technical issues encountered w.r.t. laying of balance 2 segment. -Delay by contractor.
70	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 04/2016	06/2015	110	820.2	Termination of Contract. - Non-cooperation by equipment's suppliers, sub-contractors and consultant. - Delay in availability of subsea manifold and prolonged repairing work. - Complications in well G-1-9 and well control activities. -Delay in proceedings in Mumbai High Court and prolonged legal battle. -Delay in finalisation of out of court settlement. ONGC took over the project in 2010 after settlement with M/S CEL.

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
71	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	220.84	08/2012 03/2015	06/2015	34	-11.94	
72	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,341.30	12/2012 -	06/2015	30	0	
73	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	149.03	12/2014 -	07/2015	7	0	Pre-commissioning activities are in progress. Hook up shutdown for Mounded bullet pipelines are to be done during existing refinery-III S/d which is planned in July 2015
74	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	183.48	07/2013 -	07/2015	24	20.02	
75	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	-38.7	Commissioning is pending as NOC is awaited from the MOD (air force) -ROW problem at site due to intervention of local villagers. Work commenced under police protection. -Scope revision and delay in award of work.
76	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,946.07	11/2012 11/2013	10/2015	35	16.05	
77	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPR,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,099.88	10/2011 -	10/2015	48	75.35	Completion delayed primarily because the rectification of rock wedge failure in cavern A1 took more time.Zones of poor geology encountered during excavation of balance bench.Slow construction progress of AG facility Works as it was dependent on completion of UG works.

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
78	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	944.84	10/2011 -	10/2015	48	67.62	Delay in finalization of crude filling and evacuation philosophy for Mangalore project. Delayed land acquisition for Mangalore. Delay in award. Slow construction progress of AG works
79	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45	70.49	Delay in getting Order for Mangalore-Padur pipeline. Delay in preparation/approval of DFR. Delay in land acquisition. Delay in site surveys. Delay in finalization of Basic Engg and Detailed Engg. Delay in finalization of crude filling and evacuation philosophy
80	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 429.00	429.06	-	10/2014 10/2015	10/2015	12	0	NIL
81	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015	41	-20.13	Delay in placement of order for 2 nos drilling rigs. One of the bidder went to court in anticipation of disqualification of their bid
82	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015	51	0	-Delay in preparation of drawing and additional model testing of Hull form in Austria . - Shortage of skilled manpower at contractor's end. - Inadequate ancillary/sub-contractors at the location -Lack of planning to match resources to work targets. - Change in delivery location. -Delay in procurement of steel by PSL.
83	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,210.15	08/2015 -	12/2015	4	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
84	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 2,523.00	2,523.00	1,020.25	01/2014 12/2015	12/2015	23	0	-Slow progress by contractor. - Slow progress by the contractor in laying of pipelines. - Delay in conversion work of Sagar Samrat to MOPU. - Delay in drilling of some wells due to non-availability of light rig.
85	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	111.38	09/2012 04/2015	12/2015	39	-24.14	Slow progress in civil work and fabrication work due to less resource mobilization. -Delay in finalization of Process package leading to delay in engg and procurement services. -Delay in delivery of Nut Shell filters and internal of IGF units.
86	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	297.42	08/2015 -	12/2015	4	0	
87	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	393.72	04/2015 04/2015	12/2015	8	-39.69	slow work by contractor
88	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	82.71	05/2015 -	12/2015	7	0	
89	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	219.71	03/2015 11/2015	02/2016	11	37.72	Heavy rain in Assam.Refloating of tender will have impact on timeline

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.89	1,768.09	03/2013 03/2016	03/2016	36	-3.5	Substantial time taken for mobilization by survey and other agency.ROU acquisition and issue related to payment. Delay in forest clearance.Inadequate manpower at working sites affected the construction progress.Local problem and court cases by tea gardener. Slow progress in engineering and procurement.
91	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,102.33	09/2012 -	03/2016	42	0	
92	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	278.85	06/2011 03/2012	03/2016	57	0	
93	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	854.50	03/2015 05/2016	05/2016	14	29.42	Non performance by the contractor -Punj Lloyd. Contractor served Notice of Arbitration to ONGC.
94	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 2,592.17	2,592.17	536.91	05/2014 05/2016	05/2016	24	0	-Delayed due to retendering. -Package-1 delayed due to representation by M/s Essar in IEM. -Slow progress by contractor.
95	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	249.17	12/2014 05/2015	05/2016	17	0	Non-performance on part of contractor-Punj Lloyd. Served Notice for Arbitration on 03.04.15.

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
96	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	115.81	03/2014 04/2015	05/2016	26	0	-Design platform integrity issue was raised by the contractor which required review of integrity analysis and this took time in resolution. - Clubbing of project facilities alongwith C-26 Cluster development project. - slow progress by the contractor.
97	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC, MAHARASHTRA	01/2012	352.49 -	352.49	115.81	03/2014 -	05/2016	26	0	
98	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC, MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016	39	0	Revision in scope of work. - High quoted price resulting in closure of the original tender. - Re-inviting tender after preparing revised BEC.
99	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, MULTI STATE	02/2011	913.00 -	913.00	390.21	08/2015 -	06/2016	10	0	
100	RESID UPGRADATION PROJECT - [N16000184]CPCL, TAMIL NADU	02/2011	3,110.36 -	3,110.36	561.70	11/2015 -	07/2016	8	0	Restricted working environment due to nearby operating plants, availability of limited space for storage & fabrication, Restricted timings for radiography activities etc.. were affecting the progress of the work.
101	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 462.79	462.79	222.98	10/2014 10/2016	10/2016	24	49.38	
102	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, KARNATAKA	02/2012	666.00 838.05	838.05	446.02	11/2015 11/2016	11/2016	12	25.83	
103	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC, MAHARASHTRA	12/2012	3,513.07 4,619.94	4,619.94	0.47	02/2016 04/2017	04/2017	14	31.51	nil
104	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC, MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 04/2015	05/2017	25	0	revised scope of work.

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
105	LPG TERMINAL AT KOCHI - [N16000171]OCL,KERALA	12/2012	607.06 607.06	607.06	57.81	01/2016 07/2017	07/2017	18	0	
106	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 188.89	188.89	2.00	01/2014 11/2017	11/2017	46	-6.92	Slow progress in engineering and procurement resulting in termination of contract. -Formulation of revised execution methodology for fresh tender and execution. lack of clear bid due to lack of understanding by the Bidders.
107	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,161.74	12/2014 -	12/2017	36	0	
108	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017	32	0	
109	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,913.10	13.86	05/2016 04/2018	04/2018	23	0	REVISED WORK SCOPE.
110	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,035.48	12/2014 -	12/2018	48	0	Preparation of TBP and cost estimation - Large no. of installations and non- availability of technical input such as as-built drawings, contour surveys and lay out of control rooms etc. - Preparation of pre-bid replies in view of the quantum and complexities. -Several round of discussions/clarification with the bidders. -Tender -Land Acquisition.
111	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	3,957.00	4.01	01/2013 -	02/2019	73	-47.91	
	Total		96,164.54 -	107,538.43	61,762.72					
	POWER									

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
112	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	195.44	03/2014 -	05/2015	14	0	
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	589.89	03/2015 -	05/2015	2	0	Severe ROW problem in western UP.
114	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 363.73	363.73	311.69	12/2014 -	05/2015	5	22.52	
115	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,584.00	04/2009 -	06/2015	74	59.48	
116	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	117.10	01/2013 -	06/2015	29	0	Delayed due to delay in land acquisition for Kishanganj S/stn. (land acquired in Aug 13).
117	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 1,606.38	1,606.38	1,294.66	12/2013 04/2015	06/2015	18	17.57	Delayed due to delay in land acquisition for Vadodra sub station (land acquired in June 13).
118	IMMEDIATE EVACUATION SYSTEM WITH BARR-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 1,025.28	1,025.28	926.80	08/2014 06/2015	06/2015	10	13.7	Implementation affected due to submergence in low area & pile foundation work. Issue re-solved. ROW problem faced due to court case.
119	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND - III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,680.97	11/2012 -	07/2015	32	0	Delay in forest clearance & sub station land acquisition.
120	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 1,007.68	1,007.68	911.74	07/2013 -	08/2015	25	139.35	
121	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 3,105.51	3,105.51	2,767.47	03/2014 06/2015	08/2015	17	20.87	Delayed due to delay in wildlife sanctuary clearance & forest clearance
122	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	657.18	03/2015 -	09/2015	6	0	Delayed due to delay in land acquisition for Kudgi Sub station.
123	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,701.80	12/2013 -	09/2015	21	0	Due to delay in forest clearance.

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
124	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,856.76	08/2014 -	09/2015	13	0	Gen. project anti. in 2016-17 & beyond. Delayed due to delay in land acquisition of Varansai S/stn. & forest clearance awaited.
125	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	501.60	02/2014 -	09/2015	19	0	Delayed due to severe ROW problem.
126	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UPPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,495.27	10/2014 -	09/2015	11	0	Implementation affected due to severe ROW problem in Pune area.
127	SYSTEM STRENGTHENING-VIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,010.48	11/2014 -	09/2015	10	0	Delayed due to severe ROW problem faced in Guttur & Krishna Distt of Andhra Pradesh.
128	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	178.92	04/2015 -	09/2015	5	0	Completion matching with Varansai S/stn. (delay due to delay in land acquisition).
129	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 1,007.16	1,007.16	989.31	12/2007 12/2009	12/2015	96	0	Severe ROW Problem
130	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,823.24	03/2013 06/2015	12/2015	33	13.18	Delay due to severe ROW problem.
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	479.82	07/2013 -	12/2015	29	0	Delayed due to forest clearance & limited working period due to snow-bound area.
132	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	12/2015	25	0	Delayed due to delay in land acquisition & severe ROW problem.
133	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	429.81	11/2013 -	12/2015	25	0	Delayed due to delay in forest clearance & delay in land acquisition for sub station (land acquired in Apr 13).
134	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	274.57	08/2014 06/2015	12/2015	16	16.63	Delayed due to severe ROW problem faced in Bengaluru area.
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	501.22	11/2014 -	12/2015	13	0	Delayed due to delay in forest clearance & severe ROW problem in Uttarakhand.

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
136	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	105.00	06/2015 -	12/2015	6	0	
137	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	678.43	06/2015 -	12/2015	6	0	Forest clearance awaited.
138	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,891.15	09/2008 08/2010	03/2016	90	21.34	Severe ROW problem faced in Kerala.
139	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	519.79	09/2010 06/2013	03/2016	66	51.1	Severe ROW problem & forest clearance awaited.
140	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,007.25	08/2013 -	03/2016	31	159.15	
141	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	461.76	11/2011 -	03/2016	52	0	Severe ROW problem in western UP (near Bagpat) due to farmers agitation & high compensation demand.
142	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	318.27	02/2012 -	03/2016	49	0	Severe ROW problem in western UP due to farmer agitation & high compensation.
143	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	4,075.48	10/2012 -	03/2016	41	0	Forest clearance awaited & contractual issues.
144	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	10,373.80	08/2013 -	03/2016	31	0	Generation Project delayed. Severe ROW problem & disturbance in NER.
145	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	1,306.75	01/2015 -	03/2016	14	0	Involves wildlife Sanctuary & delay in land acquisition for Alipurduar HVDC station. Generation project delayed.

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
146	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	2,111.00	12/2012 -	03/2016	39	0	Delayed due to stiff resistance/ local disturbances & geographical constraints in NER. Forest clearance also delayed.
147	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,051.29	08/2012 -	03/2016	43	0	Delay due to contractual/ legal issue arising out of ownership due to poor performance of the contractor.
148	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	725.74	11/2012 -	03/2016	40	0	Severe ROW problem in western UP (farmer agitation & high compensation demand).
149	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,244.02	04/2013 -	03/2016	35	0	Severe ROW problem in western UP due to farmer agitation demanding high compensation.
150	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATISGARH	05/2011	1,961.87 -	1,961.87	1,688.45	05/2014 -	03/2016	22	0	Delayed due to delay in Land acquisition for Champa Sub station & contractual issues in one line. packages re-awarded.
151	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	355.42	06/2014 -	03/2016	21	0	Delayed due to severe ROW problem in Karnataka & down stream portion executed by state not available.
152	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	2,172.33	07/2014 -	03/2016	20	0	Delayed due to delay in forest clearance (stage-I awaited) & severe ROW problems.
153	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 2,228.70	2,228.70	950.63	08/2014 12/2015	03/2016	19	27.6	Delayed due to delay in forest clearance (awaited) & non-readiness of Kudus extension (MSETCL).
154	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	1,043.12	01/2015 -	03/2016	14	0	Forest clearance awaited.

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
155	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL, CHHATTISGARH	03/2012	9,569.76 -	9,569.76	4,122.59	06/2015 -	03/2016	9	0	Delayed due to delay in land acquisition of Champa HVDC Terminal & Forest clearance awaited.
156	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL, MULTI STATE	02/2012	3,201.44 -	3,201.44	2,246.41	10/2014 -	03/2016	17	0	Generation project delayed & delay in land acquisition of Kanpur S/stn.
157	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL, MULTI STATE	03/2013	2,514.88 -	2,514.88	559.65	12/2015 -	03/2016	3	0	Completion likely to be delayed due to severe ROW problem & Huge forest clearance awaited.
158	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC, BIHAR	03/2010	3,984.03 -	3,984.03	-	01/2013 -	03/2016	38	0	
159	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38 -	1,929.15	1,742.55	09/2009 -	06/2016	81	81.76	1 Initial delay in handing over of forest land. 2 Bandh/ closure by locals, GJMM and its effect. 3 Contractual issues 4 Delay in award of E&M contract due to clarification regarding participation of Chinese firm.
160	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,757.36	09/2014 -	06/2016	21	0	Delayed due to severe ROW problem & contractual issue in one line.
161	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL, MULTI STATE	03/2012	198.63 -	198.63	28.00	09/2014 -	06/2016	21	0	ROW problems.
162	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, MIZORAM	07/1998	368.72 1,381.71	1,381.71	805.32	07/2006 12/2015	10/2016	123	274.73	

(April 2015)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
163	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04 -	5,497.72	3,934.97	01/2016 -	11/2016	10	50.95	1. Law & order problem in the project area and Kashmir Valley. 2. Delay in settlement of R&R plan of the project which is pending with J&K State Govt. for approval and strike by PFA's 3. Due to delay decision of International Court of Arbitration
164	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	987.23	11/2012 -	12/2016	49	0	Delayed due to delay in land acquisition & forest clearance awaited. Land yet to be acquired for Daltonganj S/stn.
165	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 6,476.34	6,476.34	3,862.64	12/2009 03/2017	03/2017	87	159.38	
166	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35 6,749.18	6,749.18	5,186.00	09/2011 -	03/2017	66	54.25	
167	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 -	9,395.18	4,728.00	11/2016 -	08/2017	9	0	
168	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 -	195.42	24.10	02/2014 -	09/2017	43	0	
169	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	-	12/2016 -	09/2017	9	0	
170	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97 15,095.67	15,095.67	10,792.00	12/2009 10/2014	03/2018	99	73.65	
171	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	1,198.84	07/2010 02/2016	05/2018	94	79.77	1.Non availability of Asena Quarry 2.Regular hindrances in Chopra dumping area 3.Fund crises with HCC civil contractor.
172	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	619.75	07/2014 11/2018	11/2018	52	50.31	Work affected by pending court case.

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
173	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59	7,531.72	5,040.21	09/2009	12/2018	111	92.16	Initial delay in start of Dam works due to delay in Revised Forest clearance 2.Burial of TBM during Nov, 06. Heavy ingress of water with silt from TBM face. Treatment of shear zone, 3.Back hill slope failure of Power House three times, 4.Ban on use of aggregates by Hon'ble High Court, Shimla
174	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,434.00	03/2013	12/2018	69	29.14	
	Total		147,954.14	178,090.47	113,881.50					
	HEAVY INDUSTRY									
175	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N200000001]HIPE,MULTI STATE	04/2011	1,718.00	3,827.30	-	09/2011	12/2017	75	122.78	
	Total		1,718.00	3,827.30	.00					
	RAILWAYS									
176	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	436.85	12/2009 03/2011	06/2015	66	300.67	Not Reported
177	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII-MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00	874.57	703.56	03/2013	09/2015	30	81.45	
178	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33	0	Not Reported
179	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 245.39	245.39	249.33	12/2008	10/2015	82	104.49	Not Reported

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
180	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	335.00	230.67	06/2004 -	12/2015	138	72.62	Law & Order issue affected the work progress. Material Modification for Electrification estimate are awaited from Jharkhand Govt.
181	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	367.76	Not Reported
182	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	16.41	Not Reported
183	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 495.44	1,781.98	433.72	03/2004 12/2010	03/2016	144	259.68	Fund constraint affecting the progress of projects.
184	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	259.82	177.01	02/2006 -	03/2016	121	-72	Progress is slow due to explosive stocking is not allowed by SP
185	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND GBAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2016	48	59.2	Initially the electrification of Khurja-Meerut-Saharanpur section was sanctioned in 1996-97 and subsequently the work was frozen. In 2007-08 electrification work of Khurja-Meerut-Saharanpur was defrozen and Ghaziabad-Meerut section also included as a material modification. Authorisation has been received on 13-08-2014 to run electric trains on Khurja-Meerut city. The electrification work on the balance portion is in progress and planned for completion by Nov 2015.
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.44	03/2014 -	03/2016	24	-9.96	
187	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	45.41	Not Reported

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
188	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR, ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	228.1	Land acquisition issue.
189	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER, JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	88.4	Work delayed due to foundation problem.
190	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	38.8	Section will be completed after Lumding-Silchar, Badarpur- Kumarghat GC Project.
191	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	197.10	03/2016 -	06/2016	3	0	Work hampered due to encroachment on Railway land along the proposed metro alignment.
192	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	53.44	Not Reported
193	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH	04/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017	84	381.4	Not Reported
194	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	65.24	04/2016 -	03/2017	11	0	Not Reported
195	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR, ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	233.08	Not Reported
196	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR, BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	250.37	Work affected due to fund constraint.
197	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	245.34	Work is affected due to land problems.
198	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	253.6	Supreme court approval is required for NBWL clearance.
199	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	355.36	Not Reported
200	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	682.6	Not Reported
201	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	803.12	Not Reported

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
202	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	6,821.29	2,421.26	03/2014 03/2019	03/2019	60	28.7	Fund constraint affecting the progress of projects.
203	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	299.79	Fund constraint & increase in scope of work.
204	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	2019.62	Local disturbance and fund constraint affected the work progress.
205	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	385.76	Land acquisition issue affected the work progress.
206	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	212.81	Delay in land acquisition affected the work progress.
207	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020	60	249.81	Land acquisition is pending.
	Total		28,013.16 -	83,178.76	37,002.57					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
208	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015	82	0	Land acquisition Utility Shifting Slow progress by contractor
209	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	290.20	04/2008 04/2015	05/2015	85	0	
210	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	83	0	
211	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	05/2015	29	0	
212	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	28	0	
213	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	05/2015	24	0	
214	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	75.85	06/2013 -	05/2015	23	0	
215	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
216	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	0	
217	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	06/2015	81	30.1	Land acquisition Removal of archaeological structures. Poor performance of the contractor.
218	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	06/2015	81	0	
219	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	06/2015	84	0	
220	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	06/2015	87	0	
221	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI, UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	33.7	Land acquisition Forest clearance Permission of Railways for 4 ROB.
222	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI, ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0	
223	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	06/2015	43	106.5	
224	MURADABAD-BAREILLY - [N24000154]NHAI, UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	06/2015	24	0	
225	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	06/2015	24	0	
226	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	06/2015	22	0	
227	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	953.88	07/2013 -	06/2015	23	0	
228	BHUBANESWAR TO PURI - [N24000195]NHAI, ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	06/2015	22	0	
229	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	06/2015	13	0	
230	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	267.81	699.60	02/2013 -	06/2015	28	0	
231	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	271.60	09/2014 -	06/2015	9	0	
232	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, RAJASTHAN	12/2003	275.00 -	250.39	185.30	10/2008 -	07/2015	81	-8.95	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
233	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,125.00	02/2010 -	07/2015	65	0	
234	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	667.10	05/2010 -	07/2015	62	0	
235	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	2,786.00	08/2014 -	07/2015	11	0	
236	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	276.30	07/2014 -	07/2015	12	0	
237	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	363.74	242.10	07/2009 -	08/2015	73	85.58	
238	KISHANGARH-AJMER-BEAWEAR - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,133.00	05/2012 -	08/2015	39	0	
239	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	280.30	06/2008 -	09/2015	87	0	
240	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	211.80	05/2008 06/2015	09/2015	88	0	
241	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00 -	535.00	52.80	12/2013 -	09/2015	21	0	
242	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	344.40	02/2014 -	09/2015	19	0	Project abandoned by contractor
243	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	280.13	173.80	11/2008 -	10/2015	83	80.68	
244	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	776.40	02/2014 -	10/2015	20	0	
245	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	991.70	03/2014 -	11/2015	20	0	
246	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	476.40	01/2014 -	11/2015	22	0	
247	BEAWEAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,301.00	06/2014 -	11/2015	17	0	
248	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	780.40	09/2014 -	11/2015	14	0	
249	BIJUNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	251.50	06/2005 -	12/2015	126	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
250	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	361.00	366.80	02/2009 -	12/2015	82	28.93	
251	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	159.20	04/2009 -	12/2015	80	92.75	
252	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	167.64	138.80	11/2008 -	12/2015	85	0	
253	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 -	200.00	207.60	04/2009 -	12/2015	80	0	
254	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.10	04/2008 04/2015	12/2015	92	0	Land acquisition Utility Shifting Poor planning by contractor
255	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	309.56	457.70	04/2010 01/2016	12/2015	68	42.25	
256	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0	
257	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2015	52	0	
258	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32	0	
259	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	0	
260	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31	0	
261	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	0	
262	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	0	
263	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29	0	
264	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28	0	
265	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
266	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	12/2015	19	0	
267	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	0	
268	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	0	
269	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	0	Land acquisition Forest clearance Poor progress by the contractor
270	MUZZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	0	
271	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	12/2015	15	0	
272	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	0	
273	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	0	
274	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6	0	
275	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	0	Funds constraint of contractor
276	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37	0	
277	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	03/2016	28	0	
278	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29	0	
279	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2016	23	0	
280	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21	0	
281	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
282	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	03/2016	23	0	
283	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	386.10	127.10	09/2007 -	04/2016	103	82.12	
284	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	04/2016	67	0	
285	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	0	
286	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12	0	
287	BIJINI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	05/2016	95	0	
288	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	0	
289	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	0	
290	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	0	
291	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	0	
292	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36	0	
293	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	0	
294	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	0	
295	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	0	
296	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2016	36	0	

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
297	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0	
298	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39	0	
299	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	12/2016	18	0	
300	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	2.29	
301	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31	0	
302	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16	0	
303	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	0	
304	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	450.70	08/2013 -	05/2017	45	0	
305	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,610.00	08/2013 -	07/2017	47	0	
306	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	12/2017	34	0	
	Total		74,999.80 -	77,150.70	70,746.17					
	<u>TELECOMMUNICATIONS</u>									
307	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	55.22	10/2010 08/2015	09/2015	59	0	
	Total		384.00 -	384.00	55.22					
	<u>URBAN DEVELOPMENT</u>									

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
308	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD, MAHARASHTRA	06/2010	205.00 -	205.00	-	03/2012 -	04/2015	37	0	1. Encroachment at both the sites. 2. Non availability of adequate funds during 2011-12 (only 9.8 Crore), 2012-13 (only 19.37 Crore), 2013-14 (only 33.99 Crore) and 2014-15 (only 12 Crore), Restriction of Expenditure and slow progress. 3. Heavy rains making expansive soil marshy and unapproachable for vehicular movement. 4. Raft foundation at 3 M because of poor bearing capacity. 5. Technical buildings works could not be started since MHA consultant did not provide complete details.
309	FARIDABAD EXTENSION - [N28000057]DMRCL, DELHI	09/2011	2,494.00 -	2,494.00	639.78	09/2014 -	05/2015	8	0	
310	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81 -	225.81	-	06/2012 -	06/2015	36	0	Progress of balance work was hampered due to heavy rains and consequent water logging of site and change in decision by the Client department. Scheme of Electrical Services particularly HVAC work was changed after detailed elaboration and award of work was delayed due to General Election in May 2014.
311	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43 -	238.43	-	02/2015 -	08/2015	6	0	Finalization of flooring work in 1st year lab building and approval of sample flat for Grade- A qtr from client awaited.
312	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD, MAHARASHTRA	12/2012	315.00 -	315.00	3.11	06/2015 -	08/2015	2	0	Initial Delay due to time taken in finalisation of Drawings by Architect/ Client

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
313	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	270.83	-	11/2014 -	10/2015	11	0	Pre-Construction: 1. Late approval of BOQ by IIT=3 Months. 2. Work awarded in 2nd call=2 Months. Post-Construction: 1. Late approvals: drawings from client (TCPO-21.10.13, Structural drws- 24.12.13, LOP: 06.02.14, EIA approval; 21.2.14)= 4 Months. 2. Client not agreed contractual action for 6 bldg--1.5 Month. 3. 9 Blocks still not cleared by IIT= 1.5 Months. 4. Retaining walls details not issued yet by IIT=3 Months. 5. Abnormal winter rains- 2014, 2015
314	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85 -	261.85	6.26	05/2013 -	11/2015	30	0	Initial delay of 1 year in availability of site, subsequent delay due to non-uniform flow of funds during 2012-13 & 2013-14, delay in finalization of interior scheme, non-availability of full site till date, non-performance of Interior Agency
315	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	12/2015	11	0	
316	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01 -	405.01	-	12/2014 -	04/2016	16	0	Extra time involved in finalization of tender for addressing certain issues of client department.
317	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	-	03/2016 -	05/2016	2	0	
318	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	-	09/2015 -	07/2016	10	0	NR

(April 2015)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
319	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 14,600.00	14,600.00	10,603.80	12/2015 -	08/2016	8	0	
320	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00 -	38,585.00	8,110.85	03/2016 -	12/2016	9	0	
321	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	0	The master layout plan was approved first time by the Client department in Feb. 2012 but it was modified thrice during 2013-14 and finally approved on 13-02-2014
322	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	12/2016	3	0	NR
323	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	0	The work was terminated on 24-07-2014 because of the non performance of the contractor for the first package. However, the tender for balance items of the package I along with package III has been awarded and work started at site.
	Total		82,471.25 -	82,471.25	19,369.59					
	Grand Total		561,446.59	678,495.08	402,406.87					

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2015	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	-	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	04/2015	8.19
5	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		1,005.21 -	1,121.63			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,477.21	06/2009 -	06/2015	71.23
7	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
8	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	05/2015	34.63
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
11	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	431.45	03/2016 -	03/2016	0.23
	Total		8,198.48 -	12,644.78			
	<u>HEAVY INDUSTRY</u>						
12	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>PETROCHEMICALS</u>						
13	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	06/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						
14	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,100.00	08/2010 03/2012	05/2015	87.76
16	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05
17	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	4,550.40 -	6,638.94	03/2013 -	05/2015	45.90
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42
19	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
20	REWARI KANPUR PIPELINE PROJECT - [N16000145]	02/2012	1,210.64 -	1,446.34	11/2015 -	11/2015	19.47
21	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.05	11/2015 -	11/2016	25.83
22	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38
23	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	10/2015	75.35
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
25	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51
26	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
27	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	07/2015	20.02
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
29	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
30	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	06/2014	5,706.47 -	5,813.25	05/2017 -	05/2017	1.87
31	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	02/2016	37.72
	Total		69,659.14 -	89,819.80			
	<u>POWER</u>						

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
32	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16
33	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	06/2015	59.48
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	12/2009 06/2016	03/2017	159.38
36	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67	12/2009 -	03/2018	73.65
37	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
38	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2016	21.34
39	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
40	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2018	29.14
41	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
42	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10
43	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18	09/2011 -	03/2017	54.25
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
45	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15
46	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35
47	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37	03/2013 -	12/2015	13.18
48	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]	03/2011	2,569.25 -	3,105.51	03/2014 -	08/2015	20.87
49	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH [N18000105]	09/2011	1,366.34 -	1,606.38	12/2013 -	06/2015	17.57
50	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63
51	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH [N18000116]	12/2011	1,746.65 -	2,228.70	08/2014 -	03/2016	27.60
52	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73
53	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	1,025.28	08/2014 -	06/2015	13.70
54	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		55,001.54	94,152.54			
	<u>RAILWAYS</u>						
55	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	03/2015	282.96
56	VIRAMGAM-BHILD(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
57	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
58	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
60	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
61	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
62	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
63	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
64	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
65	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
66	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
67	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
68	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
69	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
70	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
71	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
72	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
73	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
74	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
75	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
76	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
77	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
78	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
79	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
80	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
81	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
82	GULBARGA-BIDAR, SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
83	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255]	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
84	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	541.00	- -	-	232.17
85	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
86	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	980.00	- -	-	880.00
87	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
88	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,047.00	- -	-	217.27
89	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
90	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
91	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	02/2011 -	-	191.48
92	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	138.00 -	1,382.78	- -	-	902.01
93	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
94	JIND-SONEPAT (NL), NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
95	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	470.21 -	1,995.25	- -	-	324.33
96	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
97	RAJATGARH-BARANG(LD), ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
98	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
99	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	322.95 -	341.41	03/2012 -	-	5.72

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
100	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
101	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
102	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314]	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
103	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
104	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	343.00	- -	-	57.20
105	ETAWAH-MAINPURI (NL), NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	10/2015	104.49
106	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
107	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	02/2015 -	-	346.59
108	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	225.00	- -	10/2014	76.98
109	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
110	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	810.80	- -	-	0.00
111	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
112	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
113	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]	04/2006	378.56 -	791.59	- -	-	109.11
114	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
115	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
116	BHOPAL BINA 3D LINE DOUBLING - [N220000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
117	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N220000079]	09/2007	404.19 -	1,383.45	- -	-	242.28
118	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080]	09/2006	343.17 -	914.98	- -	03/2015	166.63
119	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
120	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084]	09/2006	125.00 -	490.00	- -	-	292.00
121	TIDIVANAM-NAGARI (NL) - [N220000085]	09/2006	456.00 -	1,080.00	- -	-	136.84
122	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086]	09/2006	200.00 -	496.24	- -	03/2017	148.12
123	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087]	09/2006	300.00 -	827.73	- -	03/2019	175.91

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
124	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
125	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70
126	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2016	59.20
127	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
128	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
129	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
130	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	565.13	- -	03/2018	99.75
131	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
132	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45
133	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
134	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
135	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
136	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
137	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
138	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
139	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
140	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
141	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
142	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
143	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
144	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
145	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
146	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
147	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
148	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
149	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
150	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
151	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
152	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
153	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
154	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
155	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
156	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
157	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
158	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
159	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
160	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
161	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
162	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
163	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
164	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
165	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
166	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
167	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
168	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
169	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42	563.13	-	03/2019	154.33
170	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00	1,242.25	03/2007	03/2016	38.80
171	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00	886.65	-	03/2018	251.85
172	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00	4,487.70	-	-	5.00
173	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77	441.45	-	03/2018	110.44
174	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55	288.81	-	03/2018	1.86
175	ERODE-PALANI - [N22000199]	04/2008	288.57	603.22	-	-	109.04
176	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41	450.00	-	-	173.71
177	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00	951.24	-	03/2015	285.12
178	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72	222.95	-	-	16.29
179	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02	5,307.90	-	03/2020	30.00
180	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22	679.57	-	03/2018	180.56
181	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52	394.28	-	03/2017	63.25
182	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82	435.58	-	03/2018	162.68
183	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17	1,653.55	-	03/2018	216.06
184	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12	453.10	-	03/2018	45.17
185	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07	364.06	-	03/2019	47.95
186	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68	816.55	03/2016	03/2016	29.06
187	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215]	04/2011	601.43	800.00	-	-	33.02
188	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30	2,501.05	-	-	400.91
189	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70	279.70	-	-	0.72
190	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74	203.00	-	03/2015	105.59
191	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16	260.16	-	01/2015	170.55
192	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00	1,801.01	-	-	97.26

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
193	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
194	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
195	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
196	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
197	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
198	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
199	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
200	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
201	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
202	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
203	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
204	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
205	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
206	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
207	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
208	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
209	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
210	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
211	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
212	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
213	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
214	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
215	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		86,817.46 -	215,415.19			

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	ROAD TRANSPORT AND HIGHWAYS						
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	06/2015	30.10
217	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	12/2015	28.93
218	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2015	92.75
219	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	10/2015	80.68
220	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2016	82.12
221	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	08/2015	85.58
222	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	12/2015	42.25
223	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
224	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
225	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2015	106.50
	Total		3,146.62 -	5,322.13			
	SHIPPING AND PORTS						
226	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
227	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
228	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	2,433.22			
	STEEL						
229	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	05/2015	41.41
230	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		9,035.00 -	12,779.40			
	URBAN DEVELOPMENT						
231	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			

(April 2015)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Grand Total		264,723.73	481,905.51			

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2015	31.12	78
	Total		13,171.00 -	17,270.00				
	<u>CIVIL AVIATION</u>							
2	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18	6
3	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	02/2011	452.00 -	489.00	03/2015 -	04/2015	8.19	1
	Total		669.60 -	733.10				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	09/2015	478.50	30
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,477.21	06/2009 -	06/2015	71.23	72
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	05/2015	34.63	38
	Total		7,617.44 -	12,014.74				
	<u>HEAVY INDUSTRY</u>							
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78	75
	Total		1,718.00 -	3,827.30				
	<u>PETROCHEMICALS</u>							
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	06/2015	80.08	38
	Total		5,460.61 -	9,833.52				
	<u>PETROLEUM</u>							

(April 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
10	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	07/2015	20.02	24
11	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	10/2014 -	10/2016	49.38	24
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110
13	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	02/2012	666.00 -	838.05	11/2015 -	11/2016	25.83	12
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,178.35	10/2011 -	10/2015	75.35	48
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	02/2016	37.72	11
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
18	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	05/2016	29.42	14
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,100.00	08/2010 03/2012	05/2015	87.76	57
20	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	02/2016 -	04/2017	31.51	14
21	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	4,550.40 -	6,638.94	03/2013 -	05/2015	45.90	26
22	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	10/2015	16.05	35
	Total		48,022.61 -	65,373.66				
	<u>POWER</u>							
23	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]	07/2012	296.87 -	363.73	12/2014 -	05/2015	22.52	5
24	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	346.79	08/2014 -	12/2015	16.63	16
25	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]	07/1998	368.72 -	1,381.71	07/2006 02/2015	10/2016	274.73	123
26	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	1,007.68	07/2013 -	08/2015	139.35	25
27	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	721.81	09/2010 -	03/2016	51.10	66
28	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,487.49	08/2013 -	03/2016	159.15	31
29	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	1,025.28	08/2014 -	06/2015	13.70	10

(April 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
30	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15 -	09/2009 -	06/2016	81.76	81
31	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	09/2011	1,366.34 -	1,606.38 -	12/2013 -	06/2015	17.57	18
32	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86 -	07/2010 -	05/2018	79.77	94
33	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	2,228.70 -	08/2014 -	03/2016	27.60	19
34	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07 -	09/2008 -	03/2016	21.34	90
35	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]	09/2010	2,074.86 -	2,348.37 -	03/2013 -	12/2015	13.18	33
36	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,745.08 -	07/2014 -	11/2018	50.31	52
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34 -	12/2009 06/2016	03/2017	159.38	87
38	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C [N18000096]	03/2011	2,569.25 -	3,105.51 -	03/2014 -	08/2015	20.87	17
39	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30 -	03/2013 -	12/2018	29.14	69
40	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72 -	01/2016 -	11/2016	50.95	10
41	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,531.72 -	09/2009 -	12/2018	92.16	111
42	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	6,749.18 -	09/2011 -	03/2017	54.25	66
43	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00 -	04/2009 -	06/2015	59.48	74
44	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	15,095.67 -	12/2009 -	03/2018	73.65	99
	Total		48,716.21 -	78,852.54 -				
	<u>RAILWAYS</u>							
45	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72 -	12/2009 -	06/2015	300.67	66
46	BANKURA - DAMODAR (GC) (SER) [220100277]	03/1998	111.90 -	2,371.85 -	03/2005 12/2008	12/2019	2,019.62	177
47	ETAWAH-MAINPURI (NL),NCR [220100318]	04/1997	120.00 -	245.39 -	12/2008 -	10/2015	104.49	82
48	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	230.00 -	03/2015 -	12/2016	53.44	21
49	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39 -	03/2012 -	03/2016	59.20	48

(April 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
50	RANCHI-LOHARDAGA(GC),SER - [N220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62	138
51	KATAKHAL TO BHAIRABI - [N22000126	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
52	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76	174
53	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40	3
54	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40	84
55	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79	261
56	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45	30
57	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37	87
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68	144
59	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36	47
60	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
61	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
62	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12	96
63	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34	111
64	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60	48
65	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81	60
66	CONSTRUCTION OF NL FROM KUMARGHAT- AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
67	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81	51
68	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08	110
69	LUMDING-SILCHAR JIRIBAM, BADARPUR- BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10	84
70	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60	193
71	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70	60
	Total		22,133.70 -	77,530.00				

(April 2015)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
72	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	06/2015	30.10	81
73	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	10/2015	80.68	83
74	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	08/2015	85.58	73
75	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2015	92.75	80
76	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2016	82.12	103
77	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063	12/2003	217.61 -	309.56	04/2010 -	12/2015	42.25	68
78	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29	84
79	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277	12/2003	280.00 -	361.00	02/2009 -	12/2015	28.93	82
80	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
81	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2015	106.50	43
	Total		3,146.62 -	5,322.13				
	<u>STEEL</u>							
82	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	05/2015	41.41	67
	Total		8,692.00 -	12,291.00				
	Grand Total		159,347.79	283,047.99				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	06/2015	13171	78
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	10/2017	11459	22
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	04/2018	12320	16

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
4	C/O NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT	AAI	01/2009	01/2011	06/2017	309.46	77
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS	AAI	02/2010	03/2014	05/2015	344.28	14
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	AAI	10/2012	03/2015	09/2015	217.6	6

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	06/2015	2030.78	72
8	KRISHNASHILA (NCL) (4MTY)	NCL	06/2011	03/2013	03/2016	789.88	36
9	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	44
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	05/2015	4904.54	38
11	CHURCHA ROUG (1.35MTY)	SECL	06/2008	03/2014	03/2016	462.35	24
12	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2017	172.08	84
13	TALABIRA OCP	MCL	03/2008	03/2016	03/2020	447.72	48
14	GOPAL PRASAD OCP (15MTY)	MCL	02/2008	03/2015	03/2021	395.87	72
15	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2017	457.77	48
16	NIGAHI OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	NCL	10/2007	03/2012	03/2016	259.4	48
17	JHANJRA R-VI SEAM PSLW	ECL	11/2006	03/2011	03/2017	287.18	72
18	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	30
19	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2018	447.06	36
20	KISTARAM OCP	SCCL	11/2010	03/2015	03/2018	242.29	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
21	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2017	162.46	36
22	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2016	264.68	48
23	PURNADIH OCP (3.0 MTY)	CCL	07/2008	03/2013	03/2017	210.98	48
24	NORTH URIMARI OCP (3.0 MTY)	CCL	12/2007	03/2012	03/2017	179.87	60
25	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2016	163.51	60
26	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2016	321.5	24
27	MANUGURU OC-II EXTENSION PHASE-II	SCCL	03/2010	03/2012	03/2016	181.19	48
28	RKP OCP PHASE-I	SCCL	03/2010	03/2015	04/2016	209.78	13
29	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2016	418.97	48
30	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
31	JAGANNATHPOR OC	SECL	09/2008	03/2015	03/2020	152.43	60
32	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2017	479.53	48
33	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2017	207.28	60
34	RAJMAHAL OC EXP.	ECL	09/2009	03/2014	03/2016	153.82	24
35	KAKATIYA LONGWALL	SCCL	12/2008	12/2012	03/2017	453.63	51
36	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU	NLC	04/2012	10/2014	06/2015	364.75	8
37	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2017	417.33	8
38	RG OC -III EXTENSION (PHASE -II) PROJECT	SCCL	06/2012	06/2015	03/2017	365.01	21
39	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
40	MURAI DIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	03/2016	339.88	23
41	NEYVELI NEW THERMAL POWER PROJECT (2X500 MW)	NLC	06/2011	12/2015	04/2018	5907.11	28
42	BLOCK-B OCP NCL (3.5 MTY)	NCL	06/2011	03/2015	03/2016	746.04	12
43	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2017	302.96	84

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
44	GEVRA EXPANSION OCP (SECL) (25-35) MTY	SECL	06/2010	03/2014	03/2016	2675.67	24
45	DIPKA EXPANSION OCP (SECL) (20-25) MTY	SECL	12/2009	03/2014	03/2016	1943.66	24
46	ASHOK EXPN OCP CCL (10 MTY)	CCL	12/2007	03/2011	03/2017	471.66	72

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
47	NATIONAL AUTOMOTIVE TESTING AND INFRASTRUCTURE PROJECT (NATRIIP)	RD HIPE	04/2011	09/2011	12/2017	1718	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
48	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	06/2015	5460.61	38

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
49	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	110
50	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	GAIL	07/2009	01/2013	02/2019	7596.18	73
51	PARADIP-RAIPUR- RANCHI PIPELINE	IOCL	08/2009	09/2012	03/2016	1793	42
52	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA	ONGC	07/2008	08/2012	06/2015	288.04	34
53	DEVELOPMENT OF CLUSTER-7 FIELDS	ONGC	03/2010	03/2013	05/2015	4550.4	26
54	MOUNDED BULLET PROJECT AT CPCL	CPCL	12/2012	12/2014	07/2015	279	7
55	PARADIP HALDIA DURGAPUR LPG PIPELINE	IOCL	02/2011	08/2015	06/2016	913	10
56	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666	12
57	IOR OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
58	PIPELINE REPLACEMENT PROJECT-3	ONGC	04/2012	05/2014	05/2015	2547.26	12
59	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD	ONGC	04/2012	12/2014	05/2016	600.17	17
60	DEVELOPMENT OF C-26 CLUSTER FIELDS	ONGC	03/2012	05/2014	05/2016	2592.17	24
61	INTEGRATED DEVELOPMENT OF B-127	ONGC	12/2011	03/2015	05/2016	2059.63	14

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	FIELDS						
62	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT	GAIL	06/2009	12/2012	06/2015	2915	30
63	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	IOCL	04/2011	05/2015	12/2015	191.96	7
64	IMPROVED OIL RECOVERY OF B-173A FIELD	ONGC	01/2012	03/2014	05/2016	352.49	26
65	RESID UPGRADATION PROJECT	CPCL	02/2011	11/2015	07/2016	3110.36	8
66	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1)	ONGC	10/2013	10/2014	10/2015	429.06	12
67	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS	ONGC	03/2013	05/2016	04/2018	2913.1	23
68	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE	ONGC	04/2013	04/2015	05/2017	284.82	25
69	LPG TERMINAL AT KOCHI	IOCL	12/2012	01/2016	07/2017	607.06	18
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	10/2015	993	45
71	MARKETING TERMINAL AT PARADEEP	IOCL	07/2009	07/2013	07/2015	199.75	24
72	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG	OIL	04/2010	06/2012	11/2015	270	41
73	RECONSTRUCTION OF BPA AND BPB PLATFORMS	ONGC	03/2013	04/2015	12/2015	1138.5	8
74	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	04/2017	3513.07	14
75	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	10/2015	732	48
76	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	10/2015	672	48
77	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	24
78	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	02/2016	871.35	11
79	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2017	202.94	46
80	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV)	ONGC	11/2010	08/2013	05/2015	331.2	21
81	ANKLESWAR REDEVELOPMENT	ONGC	11/2010	12/2014	12/2018	2189.63	48
82	MEHESANA REDEVELOPMENT PROJECT	ONGC	11/2010	04/2015	12/2017	3823	32
83	AHMEDABAD REDEVELOPMENT PROJECT	ONGC	11/2010	12/2014	12/2017	1916.1	36
84	102 MW WIND POWER PROJECT	ONGC	07/2010	06/2012	09/2015	1106	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
85	CONSTRUCTION OF 6 ETPS	ONGC	03/2009	09/2012	12/2015	317.64	39
86	DEVELOPMENT OF WO-16 CLUSTER FIELDS	ONGC	06/2010	01/2014	12/2015	2523	23
87	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV)	ONGC	01/2010	03/2013	06/2016	723.64	39
88	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	GAIL	12/2009	06/2011	03/2016	463.32	57
89	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV)	ONGC	06/2007	09/2011	12/2015	736.65	51
90	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	03/2016	2465.15	36
91	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	05/2015	3248.78	57
92	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	29777	35

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
93	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	111
94	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	90
95	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP)	PGCIL	12/2009	08/2012	03/2016	1216.83	43
96	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS.	PGCIL	02/2010	12/2012	03/2016	2144	39
97	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B	PGCIL	04/2010	01/2015	03/2016	4404.57	14
98	TRANSMISSION SYSTEM OF VINDHUACHAL - IV AND RIHAND -III GEN. PROJ.	PGCIL	03/2010	11/2012	07/2015	4672.99	32
99	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	25
100	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2016	11130.19	31
101	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	03/2016	4824.12	41
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	PGCIL	02/2009	02/2012	03/2016	410.29	49
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	PGCIL	02/2009	11/2011	03/2016	509.66	52
104	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	31
105	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	11/2018	2491.58	52

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
106	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	66
107	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	66
108	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	10
109	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	69
110	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657	94
111	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID	PGCIL	09/2012	03/2015	09/2015	1508.74	6
112	EASTERN REGION STRENGTHENING SCHEME-III	PGCIL	07/2010	11/2012	12/2016	1272.8	49
113	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B	PGCIL	03/2011	11/2013	12/2015	1585.12	25
114	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A	PGCIL	05/2010	01/2013	06/2015	250.03	29
115	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	17
116	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI	PGCIL	08/2010	04/2013	03/2016	1677.57	35
117	NORTHERN REGION SYSTEM STRENGHENING SCHEME XVI	PGCIL	07/2010	07/2013	12/2015	752.64	29
118	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B	PGCIL	12/2010	12/2013	09/2015	2743.19	21
119	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	12/2015	2074.86	33
120	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	PGCIL	03/2010	11/2012	03/2016	965.58	40
121	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	PGCIL	12/2011	08/2014	06/2015	901.77	10
122	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	03/2012	06/2015	03/2016	9569.76	9
123	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION)	PGCIL	03/2012	03/2014	05/2015	213.78	14
124	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	PGCIL	03/2012	09/2014	06/2016	198.63	21
125	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	PGCIL	02/2012	10/2014	09/2015	1927.16	11
126	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	123
127	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	PGCIL	01/2012	01/2015	03/2016	1422.85	14
128	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN	PGCIL	12/2011	08/2014	03/2016	1746.65	19

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	CHATTISGARH						
129	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV	PGCIL	12/2011	08/2014	12/2015	297.33	16
130	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	09/2017	9750.89	9
131	KBUNL-MUZAFFARPUR TPP STAGE-II-SUBSIDIARY (2X195 MW)	NTPC	03/2010	01/2013	03/2016	3984.03	38
132	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	09/2017	195.42	43
133	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI	PGCIL	06/2012	06/2015	12/2015	1909.24	6
134	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C	PGCIL	03/2013	06/2015	12/2015	514.2	6
135	SOLAPUR STPP	NTPC	03/2012	11/2016	08/2017	9395.18	9
136	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	PGCIL	06/2012	11/2014	09/2015	1263.26	10
137	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B	PGCIL	02/2012	10/2014	03/2016	3201.44	17
138	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV	PGCIL	11/2011	11/2014	12/2015	723.63	13
139	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	PGCIL	12/2011	02/2014	09/2015	552.44	19
140	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2	PGCIL	12/2011	08/2014	09/2015	2422.66	13
141	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH	PGCIL	11/2011	07/2014	03/2016	2127.51	20
142	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	03/2016	487.49	21
143	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	06/2015	1366.34	18
144	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1	PGCIL	10/2011	11/2013	12/2015	558.26	25
145	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L	PGCIL	09/2011	09/2014	06/2016	1940.13	21
146	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	PGCIL	05/2011	05/2014	03/2016	1961.87	22
147	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	06/2015	4527.15	74
148	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	03/2018	8692.97	99
149	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	81
150	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	PGCIL	03/2005	12/2007	12/2015	1007.16	96
151	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.9	87

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
152	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500	193
153	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	87
154	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.9	177
155	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
156	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	47
157	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	48
158	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	174
159	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	03/2016	171.1	48
160	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300	60
161	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325	84
162	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.2	69
163	GOELKERA-MANOHARPUR, (LD) (SER)	SER	03/1997	02/2006	03/2016	261.7	121
164	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	M RTP	04/2012	04/2016	03/2017	714.1	11
165	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895	108
166	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	SER	04/2010	03/2015	12/2016	149.9	21
167	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	84
168	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.9	39
169	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850	60
170	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER)	ER	04/1999	12/2012	09/2015	207.52	33
171	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	03/2016	2298.42	24
172	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
173	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	10/2015	120	82
174	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	98
175	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	96
176	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	03/2018	733	111
177	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108	66
178	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	144
179	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	12/2019	386.3	261
180	RANCHI -LOHARDAGA (GC) ,SER	SER	04/1997	06/2004	12/2015	194.07	138
181	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500	110

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
182	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	NHAI	12/2003	09/2008	06/2015	155	81
183	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	12/2015	280	82
184	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	12/2015	167.64	85
185	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500	NHAI	12/2003	04/2009	12/2015	200	80
186	BIJUNI TO ASSAM /WB.BORDER (NH- 31.C) (NHAI)	NHAI	12/2003	06/2008	05/2016	237.8	95
187	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	12/2003	10/2008	07/2015	275	81
188	FORBESGANJ TO SIMRAHI (NH-57) (NHAI)	NHAI	12/2003	09/2008	06/2015	332.94	81
189	INDORE-DEWAS (NH-3)	NHAI	11/2010	05/2013	12/2015	325	31
190	PUNE-SATARA (NH-4)	NHAI	10/2010	03/2013	12/2015	1724.55	33
191	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	08/2014	07/2015	2498.76	11
192	MURADABAD-BAREILLY	NHAI	04/2010	06/2013	06/2015	1267	24
193	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER	NHAI	03/2011	09/2013	12/2016	359	39
194	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM)	NHAI	02/2011	11/2012	12/2016	193.45	49

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
195	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION (KM 240-270KM)	NHAI	02/2010	08/2012	03/2016	617	43
196	DEOLI-KOTA	NHAI	01/2011	07/2013	04/2016	593	33
197	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM	NHAI	11/2010	05/2013	12/2015	1585	31
198	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	04/2017	2848	37
199	SAMAIKHIALI - GANDHIDHAM	NHAI	09/2010	03/2013	12/2015	805.39	33
200	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	10/2013	03/2016	571	29
201	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	NHAI	09/2011	08/2013	12/2015	485	28
202	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	05/2015	374	24
203	KANDLA - MUNDRA PORT	NHAI	01/2011	07/2013	06/2015	953.88	23
204	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	05/2015	600	23
205	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	12/2013	12/2016	1250	36
206	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	NHAI	06/2011	12/2013	09/2015	535	21
207	BAREILY-SITAPUR (NH-24)	NHAI	03/2011	09/2013	12/2016	1046	39
208	BEAWAR-PALI-PINDWARA	NHAI	12/2011	06/2014	11/2015	2388	17
209	JAIPUR-REENGUS	NHAI	08/2010	02/2013	06/2015	267.81	28
210	PANIKHOLI-RIMOLI	NHAI	03/2012	09/2014	06/2016	1410	21
211	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	NHAI	11/2011	05/2014	06/2015	909	13
212	BHUBANESWAR TO PURI	NHAI	03/2011	08/2013	06/2015	500.29	22
213	NIROLI-ROXY-RAJAMUNDA	NHAI	07/2011	01/2014	12/2016	586	35
214	PUNE-SHOLAPUR, PKG-II	NHAI	09/2011	01/2014	11/2015	835	22
215	BHOPAL-SANCHI	NHAI	10/2011	01/2013	12/2015	209	35
216	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	08/2016	1348.2	30
217	BARSAT-KRISHNANAGAR	NHAI	08/2012	02/2015	12/2017	867	34

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
218	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8	NHAI	06/2013	11/2015	03/2017	1287.95	16
219	REENGUS SIKAR	NHAI	03/2012	09/2014	06/2015	333.51	9
220	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6	NHAI	03/2012	09/2014	11/2015	828	14
221	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	04/2016	1928.22	12
222	FOUR LANING OF ORISSA CHATTISHGARH BORDER	NHAI	02/2013	08/2015	02/2016	1232	6
223	PANVEL-INDAPUR	NHAI	12/2011	06/2014	12/2015	942.69	18
224	RANCHI-RARGA-JAMSETHPUR	NHAI	12/2012	06/2015	12/2016	1479	18
225	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM)	NHAI	04/2012	04/2014	03/2016	624	23
226	HARIDWAR-DEHRADUN (APPROVED LENGTH 69)	NHAI	11/2011	10/2013	12/2015	478	26
227	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI	NHAI	07/2012	07/2014	07/2015	356.4	12
228	NAGPUR-WAINGANGA BRIDGE	NHAI	04/2012	10/2014	03/2016	484.19	17
229	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	02/2017	702.16	31
230	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	12/2015	1396.18	15
231	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	06/2014	03/2016	1047	21
232	4-LANING OF RAIGANJ-DALKOLA	NHAI	02/2011	08/2013	05/2017	580.43	45
233	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	07/2017	998.79	47
234	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2016	1078.84	36
235	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2015	754	33
236	4-LANING OF BARHI-HAZARIBAGH	NHAI	02/2012	02/2014	09/2015	398	19
237	SRINAGAR TO BANIHAL	NHAI	06/2011	06/2014	12/2015	1100.7	18
238	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	11/2013	05/2015	511.54	18
239	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	12/2015	575	29
240	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	04/2014	03/2016	375.09	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
241	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	03/2014	11/2015	574	20
242	2-LANNING WITH PS KHAGARIA-PURNEA	NHAI	05/2011	02/2014	10/2015	664	20
243	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	12/2015	1535	19
244	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	08/2013	06/2015	1141	22
245	ROHTAK-BAWAL	NHAI	05/2011	11/2013	03/2016	650	28
246	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	12/2010	06/2013	06/2015	1008.5	24
247	2 LANNING OF MOKAMA-MUNGER	NHAI	05/2011	05/2013	05/2015	351.54	24
248	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	03/2016	671.3	37
249	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	07/2013	12/2015	1813.76	29
250	NASHRI- CHANANI	NHAI	05/2011	06/2015	05/2016	2159	11
251	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	NHAI	07/2010	07/2015	06/2016	1987	11
252	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	NHAI	09/2010	03/2013	12/2015	852	33
253	HAZARIBAGH-RANCHI	NHAI	08/2010	01/2013	05/2015	625.07	28
254	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	04/2013	12/2015	1175	32
255	JAIPUR-TONK-DEOLI	NHAI	06/2010	12/2012	05/2015	792.06	29
256	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2015	1108	43
257	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	NHAI	05/2009	10/2011	06/2015	572.3	44
258	SURAT- DAHISAR (SIX LANE) KM 263 TO KM 502	NHAI	02/2009	08/2011	12/2015	1693.75	52
259	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	08/2015	196	73
260	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	04/2016	212	103
261	DHARAMTUL TO SONAPUR (AS-19)	NHAI	12/2003	06/2008	05/2015	200	83
262	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	09/2015	160	88
263	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2015	208	92

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
264	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2015	225	82
265	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	06/2015	245	87
266	NAGAON TO DHARAMTUL (AS-2)	NHAI	12/2003	06/2008	06/2015	264.72	84
267	GUWHATI TO NALBARI (AS-4)	NHAI	12/2003	04/2008	05/2015	175.96	85
268	CHENNAI-TADA(SIX LANE)	NHAI	04/2009	10/2011	06/2016	353.37	56
269	KISHANGARH-AJMER-BEAWER	NHAI	11/2009	05/2012	08/2015	795	39
270	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	04/2007	05/2010	07/2015	486	62
271	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	12/2003	09/2010	04/2016	232.45	67
272	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH	NHAI	03/2005	02/2010	07/2015	557	65
273	AGRA-BYPASS(NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	06/2015	348.16	93
274	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	12/2015	604	72
275	CHAMBAL BRIDGE, NH-76 (RJ-5)	NHAI	12/2003	02/2010	02/2017	275	84
276	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	12/2015	217.61	68
277	BIJNI TO ASSAM WB BORDER (NH-31.C) (1) (NHAI)	NHAI	12/2003	06/2008	09/2015	195	87
278	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	10/2015	155.04	83
279	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2015	199.81	80
280	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	NHAI	12/2003	06/2005	12/2015	230	126

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
281	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	05/2015	8692	67
282	AUGMENTATION OF IRON ORE STORAGE IN RMHP	RINL	07/2007	09/2009	06/2015	480	69
283	EXPANSION OF BOKARO STEEL PLANT	SAIL	05/2010	12/2011	05/2015	6325	41
284	EXPANSION OF BHILAI STEEL PLANT	SAIL	08/2010	03/2013	09/2015	17265	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
285	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC)	NMDC	04/2011	04/2013	06/2015	572	26
286	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC)	NMDC	02/2011	05/2013	08/2015	898.55	27
287	EXPANSION OF DURGAPUR STEEL PLANT	SAIL	08/2010	12/2012	05/2015	2875	29
288	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES	SAIL	11/2011	11/2013	06/2015	254.55	19
289	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES	SAIL	12/2011	10/2013	08/2015	187.33	22
290	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHATTISGARH	SAIL	07/2012	08/2014	11/2015	332.65	15
291	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA	SAIL	06/2012	12/2014	08/2015	237.09	8
292	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP	SAIL	10/2012	09/2014	06/2015	160.48	9
293	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	12/2016	15525	19
294	CAPTIVE POWER PLANT - 2	RINL	02/2011	09/2013	05/2015	677	20
295	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS	RINL	07/2011	07/2015	03/2016	877.73	8
296	SMS-1 CONVERTERS REVAMPING	RINL	05/2012	07/2015	03/2017	404.16	20

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
297	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS	BSNL	10/2009	10/2010	09/2015	384	59

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
298	DELHI MRTS PHASE-III	DMRCL	09/2011	03/2016	12/2016	38585	9
299	FARIDABAD EXTENSION	DMRCL	09/2011	09/2014	05/2015	2494	8
300	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL	CPWD	12/2012	12/2014	12/2016	188.87	24
301	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA	CPWD	01/2009	06/2012	06/2015	225.81	36
302	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	09/2015	07/2016	156.57	10
303	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	CPWD	11/2012	11/2014	10/2015	270.83	11
304	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS	CPWD	11/2012	02/2015	08/2015	238.43	6

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

Sn	Project	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)	
	LAB						
305	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI	CPWD	05/2009	05/2013	11/2015	261.85	30
306	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA	CPWD	06/2010	03/2012	04/2015	205	37
307	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI	CPWD	05/2012	12/2014	04/2016	405.01	16
308	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	CPWD	07/2012	08/2014	06/2017	884.3	34
309	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	08/2016	14600	8
310	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	12/2015	23136	11

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

ATOMIC ENERGY								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	5677	2185	
2	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	13171	17270	4099	
COAL								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
3	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	4904.54	6602.74	1698.2	
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	2030.78	3477.21	1446.43	
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	212.34	1228.39	1016.05	
6	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	469.78	706.4	236.62	
HEAVY INDUSTRY								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
7	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	HIPE	04/2011	09/2011	1718	3827.3	2109.3	
PETROCHEMICALS								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
8	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	5460.61	9833.52	4372.91	
PETROLEUM								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
9	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	672	1178.35	506.35	
10	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65	
11	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700	
12	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	666	838.05	172.05	
13	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	732	1227	495	
14	INTEGRATED REFINERY EXPANSION PROJECT	BPCL	03/2012	05/2016	14225	16504	2279	
15	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	3513.07	4619.94	1106.87	
16	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	3248.78	6100	2851.22	
17	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	429.82	3955.21	3525.39	

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	DEVELOPMENT OF CLUSTER-7 FIELDS	ONGC	03/2010	03/2013	4550.4	6638.94	2088.54
19	REWARI KANPUR PIPELINE PROJECT	HPCL	02/2012	11/2015	1210.64	1446.34	235.7
20	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	462.79	152.98
21	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	29777	34555	4778
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
23	MH NORTH REDEVELOPMENT PHASE III	ONGC	06/2014	05/2017	5706.47	5813.25	106.78

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
24	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	573.99	1487.49	913.5
25	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	6476.34	3979.44
26	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	15300	9014.67
27	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	PGCIL	12/2011	08/2014	901.77	1025.28	123.51
28	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	4527.15	7220	2692.85
29	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	3642.04	5497.72	1855.68
30	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	1746.65	2228.7	482.05
31	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	2569.25	3105.51	536.26
32	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	1366.34	1606.38	240.04
33	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	1061.38	1929.15	867.77
34	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	421.01	1007.68	586.67
35	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	1779.29	2159.07	379.78
36	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	2074.86	2348.37	273.51
37	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	368.72	1381.71	1012.99
38	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	721.81	244.12

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	TEHRI PUMPED STORAGE PLANT (1000MW)	THDCIL	07/2006	07/2010	1657	2978.86	1321.86
40	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
41	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	2491.58	3745.08	1253.5
42	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	7531.72	3612.13
43	BARH STPP (3X660MW) NTPC	NTPC	02/2005	12/2009	8692.97	15095.67	6402.7
44	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	4375.35	6749.18	2373.83

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
45	OBULAVARIPALLE-KRISHNAPATNAM (RVNL)	RVNL	07/2006	03/2008	743	1117.11	374.11
46	RAICHUR-GUNTAKAL (DL) (SCR)	RVNL	04/2003	12/2007	136.62	289.93	153.31
47	NANDYAL-YERRAGUNTALA (NL) , SCR	SCR	03/1996	02/2009	155.74	883	727.26
48	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	N.A.	312.12	453.1	140.98
49	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	227.9	331.4	103.5
50	KISHANGANJ JALALGARH, NL, NEFR	NFR	04/2008	N.A.	282.92	565.13	282.21
51	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	175.69	325	149.31
52	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
53	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
54	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	1500	4996.19	3496.19
55	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NFR	01/2004	N.A.	915.7	3700	2784.3
56	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) , NEFR	NFR	09/2006	N.A.	200	496.24	296.24
57	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	1676.31	5500	3823.69
58	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	N.A.	246.07	364.06	117.99
59	CHHINDWARA - NAGPUR (GC) (SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
60	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	687.2	800	112.8

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
61	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2012	603.04	1421.25	818.21
62	ANGAMALI-SABARIMALA (N.L.) (SR)	SR	10/1998	N.A.	550	1566	1016
63	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA (NL) , SWR	SWR	02/1997	N.A.	295	1289.92	994.92
64	HUBLI-ANKOLA (NL) , SWR	SWR	04/1997	N.A.	227	2135	1908
65	GULBARGA-BIDAR, SCR (NL)	SCR	02/1998	N.A.	242.42	844	601.58
66	BANGLORE - SATYAMANGALAM (NL) (SWR)	SWR	04/1996	N.A.	138	1382.78	1244.78
67	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
68	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
69	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
70	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.22	314.65
71	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
72	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	247	951.24	704.24
73	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	SR	04/1999	01/1999	460.94	1030	569.06
74	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4190	2850.52
75	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	NWR	04/2013	N.A.	456	855.16	399.16
76	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	NWR	04/2010	N.A.	739.65	872.22	132.57
77	MM FROM PANSKURA-GHATAL NL	SER	04/2011	01/1999	276.69	426	149.31
78	KANPUR-KASGANJ-MATHURA (GC) ,NER	NER	03/1997	N.A.	677.97	1651.54	973.57
79	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
80	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	04/1997	N.A.	863.23	1072.51	209.28
81	ETAWAH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	120	245.39	125.39
82	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	325	1564.54	1239.54
83	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	272.39	101.29

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
84	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	813.34	2876	2062.66
85	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1242.25	347.25
86	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	N.A.	601.43	800	198.57
87	PEN ROHA DOUBLING	CR	04/2007	N.A.	98.74	203	104.26
88	PANVEL PEN DOUBLING	CR	04/2006	N.A.	96.16	260.16	164
89	AKOLA-KHANDWA GC AKOLA-AKOT	SCR	04/2008	N.A.	184.26	2000	1815.74
90	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
91	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	970.34	1743	772.66
92	MM FROM BURAMARA-CHAKULIA	SER	04/2008	01/1999	466.48	800	333.52
93	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL) , NEFR	NFR	04/1983	N.A.	36.8	1336.57	1299.77
94	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
95	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL (SCR)	SCR	12/1994	N.A.	124.43	925.3	800.87
96	MACHERLA-NALGONDA (NL) (SCR)	SCR	07/1998	07/2008	125	480	355
97	MANOHARABAD-KOTHPALL NEW LINE (SCR)	SCR	04/2006	N.A.	378.56	791.59	413.03
98	MULTI MODAL TRANSPORT SYSTEM (MMTS) PHASE-II HYDERABAD	MRTP	04/2012	03/2016	632.68	816.55	183.87
99	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	329.97	110.14
100	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	194.07	335	140.93
101	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	583	273.56
102	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
103	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGDALPUR) , NL, RVNL	RVNL	04/1995	12/2012	304	968.6	664.6
104	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	N.A.	826.57	1143.6	317.03
105	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	608.02	449.25
106	VIRAMGAM-BHILDI (WR) , GC	WR	04/1990	N.A.	155.66	548.01	392.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
107	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
108	GONDIA-JABALPUR (GC) , (SECR)	SECR	02/1997	03/1998	386.3	1544.4	1158.1
109	NANGALDAM-TALWARA (NL) ,NR	NR	03/1981	07/2012	450	2100	1650
110	MUNEERABAD-MAHABOONAGAR (NL) , SCR	SCR	04/1997	N.A.	218.24	645	426.76
111	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	1630.97	1383.31
112	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) ,NR	NR	03/2002	06/2007	625.3	847.75	222.45
113	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC)	SR	03/1998	N.A.	280	1122	842
114	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) ,NEFR	NFR	04/2000	12/2008	733	2531.34	1798.34
115	GADWAL - RAICHUR (NL) , SCR	SCR	04/1998	02/2011	92.63	270	177.37
116	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NFR	12/2006	03/2011	170	485	315
117	CHHAPRA-BALLIA UP	NER	03/2013	N.A.	295	494.92	199.92
118	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	3500	1417.25
119	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	02/2020	1176.09	3845.6	2669.51
120	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR	NCR	04/2010	02/2019	622.41	2030.5	1408.09
121	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	N.A.	553.63	1009	455.37
122	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1200	676.48
123	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION	SR	04/2008	N.A.	822.39	1280.83	458.44
124	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	N.A.	242.22	679.57	437.35
125	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
126	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	N.A.	165.82	435.58	269.76
127	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	NFR	04/1999	N.A.	523.17	1653.55	1130.38
128	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
129	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	111.9	2371.85	2259.95

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
130	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	1428	1134.03
131	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
132	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	434	166.63
133	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
134	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	563.13	341.71
135	NEW COCHBEHAR TO SAMUKTALA	NFR	04/2011	N.A.	209.77	441.45	231.68
136	AGARTALA-AKHAURA NL	NFR	04/2012	N.A.	252	886.65	634.65
137	KARUR-SALEM (NL) , SR	SR	02/1997	N.A.	155.55	800	644.45
138	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	N.A.	100	980	880
139	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	N.A.	404.19	1383.45	979.26
140	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	914.98	571.81
141	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	125	490	365
142	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	456	1080	624
143	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
144	KHURDA ROAD-BOLANGIR (NL) ECOR	ECOR	04/1994	N.A.	470.21	1995.25	1525.04
145	HARIDASPUR-PARADEEP (NL)	RVNL	04/1996	N.A.	301.64	1185.64	884
146	RAJATGARH-BARANG (LD) , ECOR	RVNL	04/1999	02/2009	166.16	288	121.84
147	SUKINDA ROAD - ANGUL (NL) (ECOR)	RVNL	04/1998	02/2015	183.23	818.29	635.06
148	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	276	142.59
149	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	N.A.	679.27	1111.99	432.72
150	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	850	2973.42	2123.42
151	DIMAPUR-TIZIT NL	NFR	04/2013	N.A.	4274	4487.7	213.7
152	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	619.34	2820.25	2200.91

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
153	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	N.A.	4083.02	5307.9	1224.88
154	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	727.56	6570.75	5843.19
155	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	495.44	1781.98	1286.54
156	AHMEDNAGAR-PARLI VAIJNATH (NL) CR	CR	02/1997	N.A.	514.68	2820	2305.32
157	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	6821.29	1521.29
158	WARDHA-NANDED MAHARASHTRA	CR	04/2008	N.A.	499.3	2501.05	2001.75
159	RAMGANJMUNDI-BHOPAL (NL) , WCR	WCR	04/2001	N.A.	470.92	1225.9	754.98
160	SHIMOGA-HARIHAR NL	SWR	04/2011	N.A.	562.74	832.47	269.73
161	GADAG-WADI NL	SWR	04/2013	N.A.	1117	1922	805
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL) , NR	NR	03/1995	11/2002	2500	19565	17065
163	BHANUPALI-BILASPUR BERI NL	NR	04/2008	N.A.	1046.88	2966.99	1920.11
164	JIND-SONEPAT (NL) , NR	NR	01/2004	03/2012	238.56	740	501.44
165	ROHTAK-MEHAM HANSI	NR	04/2012	N.A.	287	576.18	289.18
166	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	N.A.	320.66	913.48	592.82
167	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	N.A.	446	685.17	239.17
168	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	482	874.57	392.57
169	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	913	1801.01	888.01
170	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
171	BAGALKOT-KUDACHI NL	SWR	04/2010	N.A.	377.93	986.3	608.37
172	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC) , ECR	ECR	04/1997	03/2012	501.69	1043.56	541.87
173	KATI HAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	492.98	1727.27	1234.29
174	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	541	378.13
175	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL) , ECR	ECR	04/2002	03/2009	921	2363	1442

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
176	PATNA GANGA BRIDGE (NL), ECR	ECR	04/2001	10/2007	624.47	2921	2296.53
177	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	N.A.	218.19	343	124.81
178	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	332.92	477.88	144.96
179	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	N.A.	300	827.73	527.73
180	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	N.A.	330	1047	717
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
181	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	363.74	167.74
182	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
183	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	212	386.1	174.1
184	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
185	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
186	AGRA-BYPASS (NS-1/UP-1), NH-2,3	NHAI	12/2003	09/2007	348.16	465.5	117.34
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
187	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	03/2007	04/2009	245.67	373.22	127.55
188	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL	MUMBAI PORT	11/2007	12/2010	1228	1460	232
189	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
190	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
191	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	8692	12291	3599

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

URBAN DEVELOPMENT								
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)	
192	BANGALORE METRO RAIL PROJECT	MRTP	05/2006	06/2011	6395	11609	5214	

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KUDANKULAM APP (NPCIL)	NPCIL	12/2001	12/2008	06/2015	1,3171.00	1,7270.00	4099	78

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	NLC	10/2004	06/2009	06/2015	2030.78	3477.21	1446.43	72
3	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2016	469.78	706.40	236.62	44
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW	NLC	05/2008	03/2012	05/2015	4904.54	6602.74	1698.2	38
5	ADRIYALA SHAFT PROJECT	SCCL	12/2009	03/2013	09/2015	212.34	1228.39	1016.05	30

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	HIPE	04/2011	09/2011	12/2017	1718.00	3827.30	2109.3	75

PETROCHEMICALS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
7	ASSAM GAS CRACKER PROJECT	BCPL	04/2006	04/2012	06/2015	5460.61	9833.52	4372.91	38

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	DEV OF G1 AND GS-15 (ONGCL)	ONGC	04/2003	04/2006	06/2015	429.82	3955.21	3525.39	110
9	DEVELOPMENT OF B-193 CLUSTER FIELDS	ONGC	06/2007	08/2010	05/2015	3248.78	6100.00	2851.22	57
10	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	05/2016	2059.63	2665.65	606.02	14
11	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	02/2016	871.35	1200.00	328.65	11
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	10/2015	993.00	1693.00	700	45

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	INTEGRATED DEVELOPMENT OF BASSEIN FIELD	ONGC	12/2012	02/2016	04/2017	3513.07	4619.94	1106.87	14
14	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE	ISPRL	01/2006	10/2011	10/2015	732.00	1227.00	495	48
15	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG	ISPRL	01/2006	10/2011	10/2015	672.00	1178.35	506.35	48
16	URAN CHAKAN/SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	10/2016	309.81	462.79	152.98	24
17	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL)	HPCL	02/2012	11/2015	11/2016	666.00	838.05	172.05	12
18	DEVELOPMENT OF CLUSTER-7 FIELDS	ONGC	03/2010	03/2013	05/2015	4550.40	6638.94	2088.54	26
19	PARADIP REFINERY PROJECT	IOCL	02/2009	11/2012	10/2015	2,9777.00	3,4555.00	4778	35

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
20	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2018	3919.59	7531.72	3612.13	111
21	BARH STPP(3X660MW) NTPC	NTPC	02/2005	12/2009	03/2018	8692.97	1,5095.67	6402.7	99
22	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	09/2008	03/2016	1779.29	2159.07	379.78	90
23	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC)	NHPC	09/2005	09/2009	06/2016	1061.38	1929.15	867.77	81
24	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	03/2017	2496.90	6476.34	3979.44	87
25	KOLDAM HEP (NTPC)	NTPC	10/2002	04/2009	06/2015	4527.15	7220.00	2692.85	74
26	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A	PGCIL	09/2010	03/2013	12/2015	2074.86	2348.37	273.51	33
27	TRIPURA GAS BASED POWER PROJECT	NEEPCO	07/2009	07/2013	08/2015	421.01	1007.68	586.67	25
28	PARE HYDRO ELECTRIC PROJECT	NEEPCO	12/2008	08/2013	03/2016	573.99	1487.49	913.5	31

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
29	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	07/2014	11/2018	2491.58	3745.08	1253.5	52
30	BONGAIGAON THERMAL POWER PROJECT	NTPC	01/2008	09/2011	03/2017	4375.35	6749.18	2373.83	66
31	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	03/2016	477.69	721.81	244.12	66
32	KISHANGANGA HEP (3X110 MW)	NHPC	01/2009	01/2016	11/2016	3642.04	5497.72	1855.68	10
33	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2018	2978.48	3846.30	867.82	69
34	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	07/2010	05/2018	1657.00	2978.86	1321.86	94
35	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS	PGCIL	12/2011	08/2014	06/2015	901.77	1025.28	123.51	10
36	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	NEEPCO	07/1998	07/2006	10/2016	368.72	1381.71	1012.99	123
37	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH	PGCIL	12/2011	08/2014	03/2016	1746.65	2228.70	482.05	19
38	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	PGCIL	09/2011	12/2013	06/2015	1366.34	1606.38	240.04	18
39	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C	PGCIL	03/2011	03/2014	08/2015	2569.25	3105.51	536.26	17

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
40	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2018	2500.00	1,9565.00	17065	193
41	GONDIA-JABALPUR (GC), (SECR)	SECR	02/1997	03/1998	12/2019	386.30	1544.40	1158.1	261
42	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR	NFR	09/1997	04/2008	06/2017	1500.00	4996.19	3496.19	110
43	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	06/2015	108.00	432.72	324.72	66
44	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	03/2018	733.00	2531.34	1798.34	111

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	DOA	DOC Original	DOC Anticipa ted	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)	
45	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR)	NFR	04/2003	03/2011	03/2019	727.56	6570.75	5843.19	96
46	ETAHAWH-MAINPURI (NL) ,NCR	NCR	04/1997	12/2008	10/2015	120.00	245.39	125.39	82
47	PATNA GANGA BRIDGE (NL) , ECR	ECR	04/2001	10/2007	12/2015	624.47	2921.00	2296.53	98
48	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	SWR	04/2007	03/2013	09/2015	482.00	874.57	392.57	30
49	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4190.00	2850.52	51
50	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	04/2014	03/2018	619.34	2820.25	2200.91	47
51	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	03/2018	813.34	2876.00	2062.66	48
52	TAMLUK DIGHA,LINE DOUBLING (SER)	SER	03/1984	06/2005	12/2019	293.97	1428.00	1134.03	174
53	ELECTRIFICATION OF KHURJA- MEERUT-SAHARANPUR AND G'BAD- MEERUT	RE	02/2008	03/2012	03/2016	171.10	272.39	101.29	48
54	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	03/2019	5300.00	6821.29	1521.29	60
55	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	03/2017	325.00	1564.54	1239.54	84
56	BHOPAL BINA 3D LINE DOUBLING	RVNL	09/2007	03/2010	12/2015	687.20	800.00	112.8	69
57	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	03/2016	895.00	1242.25	347.25	108
58	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	NFR	04/1996	03/2009	03/2016	1676.31	5500.00	3823.69	84
59	KATAKHAL TO BHAIRABI	NFR	04/1998	12/2012	03/2016	227.90	331.40	103.5	39
60	NEW LINE FROM DIMAPUR TO ZUBZA (KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2020	850.00	2973.42	2123.42	60
61	BANKURA - DAMODAR (GC) (SER)	SER	03/1998	03/2005	12/2019	111.90	2371.85	2259.95	177
62	KATIHAR - JOGBANI (GC) (NEFR)	NFR	09/2001	12/2010	03/2018	492.98	1727.27	1234.29	87

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF Rs.100 CRORE AND ABOVE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
63	RANCHI-LOHARDAGA (GC) , SER	SER	04/1997	06/2004	12/2015	194.07	335.00	140.93	138
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE (MTP)	M RTP	03/1996	03/2004	03/2016	495.44	1781.98	1286.54	144

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
65	MAIBANG TO LUMDING (AS-25) , KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	12/2015	199.81	385.13	185.32	80
66	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54	NHAI	12/2003	09/2007	04/2016	212.00	386.10	174.1	103
67	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	08/2015	196.00	363.74	167.74	73
68	PANIPAT-JALANDHAR 6 LANE (KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2015	1108.00	2288.00	1180	43
69	AGRA-BYPASS (NS-1/UP-1) , NH-2,3	NHAI	12/2003	09/2007	06/2015	348.16	465.50	117.34	93
70	MAIBANG TO LUMDING (AS-24) , KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	10/2015	155.04	280.13	125.09	83

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
71	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	10/2005	10/2009	05/2015	8692.00	1,2291.00	3599	67

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

List of ongoing projects having cost overrun w.r.t. to revised schedule

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00 -	12/2008 -	06/2015	31.12
	Total		13,171.00 -	17,270.00			
	<u>CIVIL AVIATION</u>						
2	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	03/2015	15.77
3	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	244.10	03/2015 -	09/2015	12.18
	Total		553.21 -	632.63			
	<u>COAL</u>						
4	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,477.21	06/2009 -	06/2015	71.23
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
6	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
7	RFR OF MANUGURU OC PROJECT - [N06000102]	11/2012	430.45 -	431.45	03/2016 -	03/2016	0.23
	Total		3,081.60 -	4,813.65			
	<u>HEAVY INDUSTRY</u>						
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]	04/2011	1,718.00 -	3,827.30	09/2011 -	12/2017	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROCHEMICALS</u>						
9	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	9,833.52	04/2012 -	06/2015	80.08
	Total		5,460.61 -	9,833.52			
	<u>PETROLEUM</u>						

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
10	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,100.00	08/2010 03/2012	05/2015	87.76
11	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	03/2012	14,225.00 -	16,504.00	05/2016 -	05/2016	16.02
12	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	450.55	03/2017 -	03/2017	27.79
13	MARKETING TERMINAL AT PARADEEP - [N16000168]	07/2009	199.75 -	239.73	07/2013 -	07/2015	20.02
14	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	10/2014 -	10/2015	0.00
15	MARKETING TOP AT KORBA - [N16000186]	01/2011	141.86 -	232.00	09/2016 -	12/2015	63.54
	Total		18,597.01 -	23,955.34			
	<u>POWER</u>						
16	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	7,531.72	09/2009 -	12/2018	92.16
17	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	15,300.00	09/2010 -	-	143.42
18	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]	09/2005	1,061.38 -	1,929.15	09/2009 -	06/2016	81.76
19	KISHANGANGA HEP (3X110 MW) - [N18000031]	01/2009	3,642.04 -	5,497.72	01/2016 -	11/2016	50.95
20	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	11/2018	50.31
	Total		17,399.92 -	34,003.67			
	<u>RAILWAYS</u>						
21	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	548.01	- 03/2010	-	252.06
22	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	- -	02/2014	643.63
23	AMRAVATI-MARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	725.00	06/1999 -	07/2012	9.35
24	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	19,565.00	11/2002 -	12/2018	682.60
25	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	36.80 274.41	1,336.57	- -	03/2019	3,531.98
26	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	12/2012 -	-	218.62
27	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	02/2012	141.40

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
28	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	1,781.98	03/2004 -	03/2016	259.68
29	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91
30	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	1,289.92	- -	-	337.26
31	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,544.40	03/1998 -	12/2019	299.79
32	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
33	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	800.00	- -	-	414.30
34	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2015	466.97
35	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53
36	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
37	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	06/2017	233.08
38	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2015	195.55
39	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	03/2015	160.76
40	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	335.00	06/2004 -	12/2015	72.62
41	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
42	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
43	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
44	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	06/2015	300.67
45	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	492.98 -	1,727.27	12/2010 -	03/2018	250.37
46	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
47	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	844.00	- 05/2009	03/2015	248.16
48	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255	04/1997	863.23 -	1,072.51	- -	06/2015	24.24
49	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	541.00	- -	-	232.17
50	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
51	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	980.00	- -	-	880.00
52	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
53	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,047.00	- -	-	217.27
54	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,531.34	12/2008 -	03/2018	245.34
55	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
56	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
57	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	04/1996	138.00 -	1,382.78	- -	-	902.01
58	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	2,371.85	03/2005 12/2008	12/2019	2,019.62
59	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
60	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
61	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
62	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
63	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	6,570.75	03/2011 -	03/2019	803.12
64	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
65	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
66	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
67	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	03/2017	160.32
68	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,700.00	- -	03/2015	304.06
69	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	343.00	- -	-	57.20
70	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	- -	03/2017	186.92
71	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	-	346.59
72	CUTTACK - BARANG (LD) - [220100326	04/1995	127.13 -	225.00	- -	10/2014	76.98
73	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
74	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328	04/2005	810.78 -	810.80	- -	-	0.00
75	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
76	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
77	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
78	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
79	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
80	BHOPAL BINA 3D LINE DOUBLING - [N220000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
81	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N220000079	09/2007	404.19 -	1,383.45	- -	-	242.28
82	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080	09/2006	343.17 -	914.98	- -	03/2015	166.63
83	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082	12/2006	170.00 -	485.00	03/2011 -	-	185.29
84	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084	09/2006	125.00 -	490.00	- -	-	292.00
85	TIDIVANAM-NAGARI (NL) - [N220000085	09/2006	456.00 -	1,080.00	- -	-	136.84
86	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086	09/2006	200.00 -	496.24	- -	03/2017	148.12
87	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N220000087	09/2006	300.00 -	827.73	- -	03/2019	175.91
88	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088	04/2006	325.00 -	1,564.54	03/2010 -	03/2017	381.40
89	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092	04/2008	5,300.00 -	6,821.29	03/2014 -	03/2019	28.70
90	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094	02/2008	171.10 -	272.39	03/2012 -	03/2016	59.20
91	TAMLUK DIGHA,LINE DOUBLING (SER) - [N220000097	03/1984	293.97 -	1,428.00	06/2005 -	12/2019	385.76
92	AGARTALA SABROOM, NL, NEFR - [N220000099	04/2008	813.34 -	2,876.00	03/2014 -	03/2018	253.60
93	BHAIRABI SAIRONG, NL, NEFR - [N220000100	04/2008	619.34 -	2,820.25	04/2014 -	03/2018	355.36
94	KISHANGANJ JALALGARH, NL, NEFR - [N220000101	04/2008	282.92 -	565.13	- -	03/2018	99.75
95	SEVOK RANGPO, NEFR - [N220000102	04/2008	1,339.48 -	4,190.00	12/2015 -	03/2020	212.81
96	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N220000107	04/2007	482.00 -	874.57	03/2013 -	09/2015	81.45

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
98	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.55	03/2014 -	-	0.06
99	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
100	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
101	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,973.42	03/2015 -	03/2020	249.81
102	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
103	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,500.00	03/2009 -	03/2016	228.10
104	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
105	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
106	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	3,500.00	- -	-	68.05
107	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	262.00	- -	-	10.58
108	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
109	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
110	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
111	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	434.00	- -	-	62.32
112	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	1,009.00	- -	12/2019	82.25
113	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
114	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	12/2016	53.44
115	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	583.00	12/2015 -	03/2016	88.40
116	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	12/2017	41.36
117	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
118	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
119	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
120	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
121	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]	04/2013	1,798.00 -	1,887.90	- -	03/2019	5.00
122	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
123	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
124	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
125	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
126	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
127	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
128	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
129	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	563.13	- -	03/2019	154.33
130	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
131	AGARTALA-AKHAURA NL - [N22000195]	04/2012	252.00 -	886.65	- -	03/2018	251.85
132	DIMAPUR-TIZIT NL - [N22000196]	04/2013	4,274.00 -	4,487.70	- -	-	5.00
133	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]	04/2011	209.77 -	441.45	- -	03/2018	110.44
134	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]	04/2012	283.55 -	288.81	- -	03/2018	1.86
135	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
136	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	-	173.71
137	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	247.00 -	951.24	- -	03/2015	285.12
138	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
139	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	4,083.02 -	5,307.90	- -	03/2020	30.00
140	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	679.57	- -	03/2018	180.56
141	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	03/2017	63.25

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
142	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	165.82 -	435.58	- -	03/2018	162.68
143	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]	04/1999	523.17 -	1,653.55	- -	03/2018	216.06
144	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	312.12 -	453.10	- -	03/2018	45.17
145	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	364.06	- -	03/2019	47.95
146	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	03/2016	29.06
147	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
148	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	499.30 -	2,501.05	- -	-	400.91
149	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72
150	PEN ROHA DOUBLING - [N22000254]	04/2007	98.74 -	203.00	- -	03/2015	105.59
151	PANVEL PEN DOUBLING - [N22000255]	04/2006	96.16 -	260.16	- -	01/2015	170.55
152	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	913.00 -	1,801.01	- -	-	97.26
153	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	-	651.97
154	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
155	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
156	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	576.18	- -	-	100.76
157	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
158	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
159	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
160	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
161	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
162	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
163	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
164	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
165	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
166	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
167	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
168	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	800.00	01/1999 -	-	71.50
169	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	01/1999 -	-	53.96
170	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
171	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	230.00	- -	-	14.43
172	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	826.57 -	1,143.60	- -	03/2018	38.35
173	DELANG-PURI DOUBLING - [N22000320]	03/2011	165.16 -	234.71	03/2015 -	03/2015	42.11
174	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
175	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	209.00	12/2016 -	12/2016	40.49
	Total		84,302.17 -	207,575.25			
	ROAD TRANSPORT AND HIGHWAYS						
176	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	06/2015	30.10
177	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	361.00	02/2009 -	12/2015	28.93
178	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	12/2015	92.75
179	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	10/2015	80.68
180	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	04/2016	82.12
181	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	08/2015	85.58
182	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	02/2017	2.29
183	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
184	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2015	106.50
	Total		2,929.01 -	5,012.57			

(April 2015)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>SHIPPING AND PORTS</u>						
185	CONST. AND DEV. OF 2 OFFSHORE CONTAINER BERTHS AND TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	-	18.89
186	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	-	300.00
187	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	04/2009 -	-	51.92
	Total		1,623.67 -	2,433.22			
	<u>STEEL</u>						
188	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091	12/2009	343.00 -	488.40	10/2016 -	10/2016	42.39
	Total		343.00 -	488.40			
	<u>URBAN DEVELOPMENT</u>						
189	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	-	81.53
	Total		6,395.00 -	11,609.00			
	Grand Total		155,574.20	321,454.55			

List of Delayed Projects w.r.t. Latest Schedule

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, TAMIL NADU	12/2001	13,171.00 -	17,270.00	18,271.00	12/2008 -	06/2015	78	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	11,459.00	6,297.00	12/2015 -	10/2017	22	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	4,059.00	12/2016 -	04/2018	16	-
	Total		36,950.00 -	41,049.00	28,627.00				
	<u>CIVIL AVIATION</u>								
4	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT (MOHALI) PH - II - [N04000070]AAI, CHANDIGARH	02/2011	452.00 489.00	489.00	410.25	03/2015 -	04/2015	1	-
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI, MULTI STATE	02/2010	344.28 -	344.28	58.50	03/2014 -	05/2015	14	-
6	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI, MULTI STATE	10/2012	217.60 -	244.10	0.04	03/2015 -	09/2015	6	-
7	C/O NEW AIRPORT AT PAKYONG (SIKKIM) AIRPORT - [N04000050]AAI, SIKKIM	01/2009	309.46 -	309.46	338.82	01/2011 -	06/2017	77	-
	Total		1,323.34 -	1,386.84	807.61				
	<u>COAL</u>								
8	RCE OF INDARAM OCP (1.20 MTPA) - [N06000093]SCCL, TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	04/2015	1	-
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	6,175.16	03/2012 05/2014	05/2015	38	12
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,477.21	3,207.92	06/2009 03/2013	06/2015	72	27
11	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	131.44	10/2014 -	06/2015	8	-
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, TELANGANA	12/2009	212.34 1,228.39	1,228.39	879.85	03/2013 09/2012	09/2015	30	36
13	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,846.08	03/2014 -	03/2016	24	-
14	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,676.56	03/2014 -	03/2016	24	-
15	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, UTTAR PRADESH	06/2011	789.88 -	741.62	466.94	03/2013 -	03/2016	36	-
16	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL, MADHYA PRADESH	06/2011	746.04 -	535.10	367.12	03/2015 -	03/2016	12	-
17	MAGADH OC 20 MTY (CCL) - [N06000015]JCL, JHARKHAND	08/2008	469.78 -	706.40	55.30	07/2012 -	03/2016	44	-

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, MADHYA PRADESH	10/2007	259.40	259.40	12.53	03/2012	03/2016	48	-
19	CHURCHA ROUG(1.35MTY) - [N06000046]SECL, CHHATISGARH	06/2008	462.35	462.35	298.60	03/2014	03/2016	24	-
20	RAJMAHAL OC EXP. - [N06000056]ECL, JHARKHAND	09/2009	153.82	153.82	55.48	03/2014	03/2016	24	-
21	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, TELANGANA	12/2009	418.97	418.97	326.51	03/2012	03/2016	48	-
22	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19	181.19	36.60	03/2012	03/2016	48	-
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50	321.50	211.71	03/2014	03/2016	24	-
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51	163.51	35.68	03/2011	03/2016	60	-
25	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68	264.68	149.41	03/2012	03/2016	48	-
26	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78	209.78	75.31	03/2015	04/2016	13	-
27	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96	302.96	132.68	03/2010	03/2017	84	-
28	ASHOK EXPN OCP CCL (10 MTY) - [060100096]CCL, JHARKHAND	12/2007	471.66	341.63	117.84	03/2011	03/2017	72	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, WEST BENGAL	11/2006	287.18	287.17	142.59	03/2011	03/2017	72	-
30	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77	457.77	162.21	03/2013	03/2017	48	-
31	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08	172.08	148.02	03/2010	03/2017	84	-
32	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63	453.63	104.49	12/2012	03/2017	51	-
33	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28	207.28	172.80	03/2012	03/2017	60	-
34	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53	479.53	118.94	03/2013	03/2017	48	-
35	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL, JHARKHAND	12/2007	179.87	179.87	83.27	03/2012	03/2017	60	-
36	PURNADIH OCP (3.0 MTY) - [N06000085]CCL, JHARKHAND	07/2008	210.98	210.98	186.69	03/2013	03/2017	48	-
37	KARMA OCP (1.0MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46	162.46	69.64	03/2014	03/2017	36	-
38	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01	365.01	6.56	06/2015	03/2017	21	-
39	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33	417.33	11.41	07/2016	03/2017	8	-
40	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29	242.29	0.06	03/2015	03/2018	36	-
41	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL, TELANGANA	07/2011	447.06	447.06	29.03	03/2015	03/2018	36	-
42	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72	447.72	52.36	03/2016	03/2020	48	-
43	JAGANNATHPOR OC - [N06000075]SECL, CHHATISGARH	09/2008	152.43	152.43	21.55	03/2015	03/2020	60	-

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
44	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2020	72	-
45	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL, ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	-
	Total		22,766.95 -	26,775.01	17,647.56				
	<u>STEEL</u>								
46	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	11,301.23	10/2009 10/2012	05/2015	67	31
47	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	5,111.95	12/2011 -	05/2015	41	-
48	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,585.10	12/2012 -	05/2015	29	-
49	CAPTIVE POWER PLANT - 2 - [N12000087]RINL, ANDHRA PRADESH	02/2011	677.00 -	677.00	512.18	09/2013 -	05/2015	20	-
50	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	377.33	09/2009 05/2012	06/2015	69	37
51	1.2 MTPA PELLET PLANT PROJECT, DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	457.14	04/2013 09/2014	06/2015	26	9
52	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	125.27	11/2013 -	06/2015	19	-
53	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL, ODISHA	10/2012	160.48 -	160.48	120.73	09/2014 -	06/2015	9	-
54	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	379.89	05/2013 01/2015	08/2015	27	7
55	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL, MAHARASHTRA	12/2011	187.33 -	187.33	151.10	10/2013 -	08/2015	22	-
56	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODISHA - [N12000079]SAIL, ODISHA	06/2012	237.09 -	237.09	164.00	12/2014 -	08/2015	8	-
57	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	14,389.17	03/2013 -	09/2015	30	-
58	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	174.36	08/2014 -	11/2015	15	-
59	BLAST FURNACE-2 CATEGORY-1 CAPITAL REPAIRS - [N12000089]RINL, ANDHRA PRADESH	07/2011	877.73 -	877.73	175.54	07/2015 -	03/2016	8	-
60	SMS-1 CONVERTERS REVAMPING - [N12000090]RINL, ANDHRA PRADESH	05/2012	404.16 -	404.16	149.34	07/2015 -	03/2017	20	-
	Total		40,238.54 -	43,807.54	36,174.33				
	<u>PETROCHEMICALS</u>								
61	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, ASSAM	04/2006	5,460.61 8,920.00	9,833.52	8,595.08	04/2012 12/2013	06/2015	38	18
	Total		5,460.61 -	9,833.52	8,595.08				

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	PETROLEUM								
62	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,100.00	5,925.40	08/2010 03/2012	05/2015	57	38
63	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	4,550.40 6,638.94	6,638.94	2,306.51	03/2013 11/2014	05/2015	26	6
64	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 253.66	253.66	220.84	08/2012 03/2015	06/2015	34	3
65	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,915.00	1,341.30	12/2012 -	06/2015	30	-
66	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	149.03	12/2014 -	07/2015	7	-
67	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	239.73	183.48	07/2013 -	07/2015	24	-
68	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 678.02	678.02	405.00	06/2012 03/2015	09/2015	39	6
69	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 34,555.00	34,555.00	28,946.07	11/2012 11/2013	10/2015	35	23
70	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPL,ANDHRA PRADESH	01/2006	672.00 1,178.35	1,178.35	1,099.88	10/2011 -	10/2015	48	-
71	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	944.84	10/2011 -	10/2015	48	-
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,398.50	01/2012 -	10/2015	45	-
73	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	1,210.15	08/2015 -	12/2015	4	-
74	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	317.64 -	240.95	111.38	09/2012 04/2015	12/2015	39	8
75	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	297.42	08/2015 -	12/2015	4	-
76	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 686.58	686.58	393.72	04/2015 04/2015	12/2015	8	8
77	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	82.71	05/2015 -	12/2015	7	-
78	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 1,200.00	1,200.00	219.71	03/2015 11/2015	02/2016	11	3
79	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,102.33	09/2012 -	03/2016	42	-
80	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	463.32	278.85	06/2011 03/2012	03/2016	57	48
81	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 600.17	600.17	249.17	12/2014 05/2015	05/2016	17	12
82	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	115.81	03/2014 04/2015	05/2016	26	13

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
83	IMPROVED OIL RECOVERY OF B-173A FIELD - [N16000185]ONGC,MAHARASHTRA	01/2012	352.49	352.49	115.81	03/2014	05/2016	26	-
84	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00	913.00	390.21	08/2015	06/2016	10	-
85	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36	3,110.36	561.70	11/2015	07/2016	8	-
86	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82	284.82	-	04/2015	05/2017	25	25
87	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10	1,916.10	1,161.74	12/2014	12/2017	36	-
88	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63	2,189.63	1,035.48	12/2014	12/2018	48	-
89	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18	3,957.00	4.01	01/2013	02/2019	73	-
	Total		69,021.98	76,179.57	50,251.05				
	POWER								
90	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78	213.78	195.44	03/2014	05/2015	14	-
91	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34	803.34	589.89	03/2015	05/2015	2	-
92	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NTPCO,TRIPURA	07/2012	296.87	363.73	311.69	12/2014	05/2015	5	-
93	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15	7,220.00	6,584.00	04/2009	06/2015	74	-
94	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03	250.03	117.10	01/2013	06/2015	29	-
95	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34	1,606.38	1,294.66	12/2013	06/2015	18	2
96	TRANSMISSION SYSTEM OF VINDDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99	4,672.99	3,680.97	11/2012	07/2015	32	-
97	TRIPURA GAS BASED POWER PROJECT - [N18000071]NTPCO,TRIPURA	07/2009	421.01	1,007.68	911.74	07/2013	08/2015	25	-
98	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25	3,105.51	2,767.47	03/2014	08/2015	17	2
99	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74	1,508.74	657.18	03/2015	09/2015	6	-
100	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19	2,743.19	2,701.80	12/2013	09/2015	21	-

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
101	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,856.76	08/2014 -	09/2015	13	-
102	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	501.60	02/2014 -	09/2015	19	-
103	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,495.27	10/2014 -	09/2015	11	-
104	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	1,010.48	11/2014 -	09/2015	10	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	178.92	04/2015 -	09/2015	5	-
106	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	1,007.16 1,007.16	1,007.16	989.31	12/2007 12/2009	12/2015	96	72
107	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 2,348.37	2,348.37	1,823.24	03/2013 06/2015	12/2015	33	6
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	479.82	07/2013 -	12/2015	29	-
109	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,452.46	11/2013 -	12/2015	25	-
110	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	429.81	11/2013 -	12/2015	25	-
111	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 346.79	346.79	274.57	08/2014 06/2015	12/2015	16	6
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	501.22	11/2014 -	12/2015	13	-
113	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	105.00	06/2015 -	12/2015	6	-
114	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. AND NCC POWER PROJECTS LTD. LTOA GENERATI - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	678.43	06/2015 -	12/2015	6	-
115	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,891.15	09/2008 08/2010	03/2016	90	67
116	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 721.81	721.81	519.79	09/2010 06/2013	03/2016	66	33
117	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,487.49	1,487.49	1,007.25	08/2013 -	03/2016	31	-
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	461.76	11/2011 -	03/2016	52	-
119	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	318.27	02/2012 -	03/2016	49	-

(April 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
120	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12	4,824.12	4,075.48	10/2012	03/2016	41	-
121	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19	11,130.19	10,373.80	08/2013	03/2016	31	-
122	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL, WEST BENGAL	04/2010	4,404.57	4,404.57	1,306.75	01/2015	03/2016	14	-
123	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00	2,144.00	2,111.00	12/2012	03/2016	39	-
124	SYSTEM STRENGTHENING IN NR FOR SASAN AND MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83	1,216.83	1,051.29	08/2012	03/2016	43	-
125	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58	965.58	725.74	11/2012	03/2016	40	-
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57	1,677.57	1,244.02	04/2013	03/2016	35	-
127	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87	1,961.87	1,688.45	05/2014	03/2016	22	-
128	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49	487.49	355.42	06/2014	03/2016	21	-
129	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATTISGARH	11/2011	2,127.51	2,127.51	2,172.33	07/2014	03/2016	20	-
130	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATTISGARH	12/2011	1,746.65 2,228.70	2,228.70	950.63	08/2014 12/2015	03/2016	19	3
131	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85	1,422.85	1,043.12	01/2015	03/2016	14	-
132	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76	9,569.76	4,122.59	06/2015	03/2016	9	-
133	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44	3,201.44	2,246.41	10/2014	03/2016	17	-
134	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88	2,514.88	559.65	12/2015	03/2016	3	-
135	KBUNL-MUZAFFARPUR TPP STAGE-II- SUBSIDIARY (2X195 MW) - [N18000191]NTPC,BIHAR	03/2010	3,984.03	3,984.03	-	01/2013	03/2016	38	-
136	TEESTA LOW DAM HEP, STAGE-IV (4X40 MW) (NHPC) - [180100243]NHPC, WEST BENGAL	09/2005	1,061.38	1,929.15	1,742.55	09/2009	06/2016	81	-

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13	1,940.13	1,757.36	09/2014	06/2016	21	-
138	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63	198.63	28.00	09/2014	06/2016	21	-
139	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	07/1998	368.72	1,381.71	805.32	07/2006	10/2016	123	10
140	KISHANGANGA HEP (3X110 MW) - [N18000031]NHPC,JAMMU AND KASHMIR	01/2009	3,642.04	5,497.72	3,934.97	01/2016	11/2016	10	-
141	EASTERN REGION STRENGTHENING SCHEME- III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80	1,272.80	987.23	11/2012	12/2016	49	-
142	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	4,375.35	6,749.18	5,186.00	09/2011	03/2017	66	-
143	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18	9,395.18	4,728.00	11/2016	08/2017	9	-
144	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42	195.42	24.10	02/2014	09/2017	43	-
145	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89	9,750.89	-	12/2016	09/2017	9	-
146	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	02/2005	8,692.97	15,095.67	10,792.00	12/2009	03/2018	99	41
147	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00	2,978.86	1,198.84	07/2010	05/2018	94	27
148	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59	7,531.72	5,040.21	09/2009	12/2018	111	-
149	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48	3,846.30	2,434.00	03/2013	12/2018	69	-
	Total		142,063.89	166,843.77	108,472.31				
	<u>HEAVY INDUSTRY</u>								
150	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]HIPE,MULTI STATE	04/2011	1,718.00	3,827.30	-	09/2011	12/2017	75	-
	Total		1,718.00	3,827.30	.00				
	<u>RAILWAYS</u>								
151	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00	432.72	436.85	12/2009	06/2015	66	51
152	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00	874.57	703.56	03/2013	09/2015	30	-
153	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]JER,WEST BENGAL	04/1999	207.52	207.52	223.44	12/2012	09/2015	33	-
154	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00	245.39	249.33	12/2008	10/2015	82	-
155	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07	335.00	230.67	06/2004	12/2015	138	-

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,339.60	10/2007 12/2012	12/2015	98	36
157	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	793.71	03/2010 -	12/2015	69	-
158	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]JMRT,MHARASHTRA	03/1996	495.44 495.44	1,781.98	433.72	03/2004 12/2010	03/2016	144	63
159	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	259.82	177.01	02/2006 -	03/2016	121	-
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2016	48	27
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,069.60	35.44	03/2014 -	03/2016	24	-
162	KATAKHAL TO BHAIRABI - [N22000126]NFR,ASSAM	04/1998	227.90 200.00	331.40	182.22	12/2012 -	03/2016	39	-
163	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NFR,ASSAM	04/1996	1,676.31 -	5,500.00	4,734.45	03/2009 -	03/2016	84	-
164	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 388.67	583.00	144.66	12/2015 -	03/2016	3	-
165	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR,TRIPURA	04/1999	895.00 575.00	1,242.25	1,005.81	03/2007 -	03/2016	108	-
166	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	197.10	03/2016 -	06/2016	3	-
167	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	230.00	68.67	03/2015 -	12/2016	21	-
168	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]JMRT,MHARASHTRA	04/2012	714.10 -	714.10	65.24	04/2016 -	03/2017	11	-
169	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES NEFR - [220100201]NFR,ASSAM	09/1997	1,500.00 1,000.00	4,996.19	3,410.06	04/2008 03/2014	06/2017	110	39
170	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	492.98 -	1,727.27	743.74	12/2010 -	03/2018	87	-
171	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	733.00 733.00	2,531.34	1,732.43	12/2008 -	03/2018	111	-
172	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR,TRIPURA	04/2008	813.34 813.34	2,876.00	823.83	03/2014 -	03/2018	48	-
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	619.34 619.34	2,820.25	199.31	04/2014 03/2015	03/2018	47	36
174	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 3,000.00	19,565.00	10,658.34	11/2002 -	12/2018	193	-
175	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	727.56 727.56	6,570.75	2,787.99	03/2011 03/2014	03/2019	96	60
176	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,157.54	1,544.40	590.26	03/1998 -	12/2019	261	-
177	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	2,371.85	486.25	03/2005 12/2008	12/2019	177	132
178	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER, WEST BENGAL	03/1984	293.97 1,013.74	1,428.00	466.36	06/2005 07/2011	12/2019	174	101

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	SEVOK RANGPO, NEFR - [N24000102]NFR,SIKKIM	04/2008	1,339.48 1,339.48	4,190.00	88.56	12/2015 -	03/2020	51	-
	Total		21,538.16 -	71,819.51	34,150.16				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
180	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	290.20	04/2008 04/2015	05/2015	85	1
181	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	289.50	06/2008 -	05/2015	83	-
182	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,983.00	12/2012 -	05/2015	29	-
183	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	05/2015	28	-
184	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.60	05/2013 -	05/2015	24	-
185	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	75.85	06/2013 -	05/2015	23	-
186	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	148.80	05/2013 -	05/2015	24	-
187	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	05/2015	18	-
188	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	191.80	09/2008 -	06/2015	81	-
189	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	550.30	09/2008 -	06/2015	81	-
190	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	315.90	06/2008 -	06/2015	84	-
191	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 03/2015	06/2015	87	3
192	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	322.70	09/2007 -	06/2015	93	-
193	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	-
194	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	06/2015	43	-
195	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,425.00	06/2013 -	06/2015	24	-
196	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,392.00	06/2013 -	06/2015	24	-
197	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	1,141.00	2,445.00	08/2013 -	06/2015	22	-
198	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	953.88	07/2013 -	06/2015	23	-
199	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	633.30	08/2013 -	06/2015	22	-
200	SAMBALPUR-BARGARH- CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,ODISHA	11/2011	909.00 -	909.00	982.90	05/2014 -	06/2015	13	-

(April 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
201	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81	267.81	699.60	02/2013	06/2015	28	-
202	REENGUS SIKAR - [N24000227]NHAI,RAJASTHAN	03/2012	333.51	333.51	271.60	09/2014	06/2015	9	-
203	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00	250.39	185.30	10/2008	07/2015	81	-
204	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00	557.00	1,125.00	02/2010	07/2015	65	-
205	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00	486.00	667.10	05/2010	07/2015	62	-
206	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76	2,498.76	2,786.00	08/2014	07/2015	11	-
207	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40	356.40	276.30	07/2014	07/2015	12	-
208	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00	363.74	242.10	07/2009	08/2015	73	-
209	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00	795.00	1,133.00	05/2012	08/2015	39	-
210	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00	195.00	280.30	06/2008	09/2015	87	-
211	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00	160.00	211.80	05/2008 06/2015	09/2015	88	3
212	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI,TAMIL NADU	06/2011	535.00	535.00	52.80	12/2013	09/2015	21	-
213	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00	398.00	344.40	02/2014	09/2015	19	-
214	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04	280.13	173.80	11/2008	10/2015	83	-
215	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00	664.00	776.40	02/2014	10/2015	20	-
216	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00	574.00	991.70	03/2014	11/2015	20	-
217	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00	835.00	476.40	01/2014	11/2015	22	-
218	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00	2,388.00	2,301.00	06/2014	11/2015	17	-
219	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00	828.00	780.40	09/2014	11/2015	14	-
220	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00	230.00	251.50	06/2005	12/2015	126	-
221	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00	361.00	366.80	02/2009	12/2015	82	-
222	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81	385.13	159.20	04/2009	12/2015	80	-
223	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64	167.64	138.80	11/2008	12/2015	85	-
224	MAIBANG TO LUMDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00	200.00	207.60	04/2009	12/2015	80	-
225	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	334.10	04/2008 04/2015	12/2015	92	8

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
226	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	-
227	SURAT - DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2015	52	-
228	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2015	32	-
229	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	901.60	03/2013 -	12/2015	33	-
230	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2015	31	-
231	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,292.00	03/2013 -	12/2015	33	-
232	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	611.80	05/2013 -	12/2015	31	-
233	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,173.00	07/2013 -	12/2015	29	-
234	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	363.00	08/2013 -	12/2015	28	-
235	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,GUJARAT	09/2010	805.39 -	805.39	842.20	03/2013 -	12/2015	33	-
236	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,188.00	05/2014 -	12/2015	19	-
237	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	835.60	07/2013 -	12/2015	29	-
238	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	323.00	06/2014 -	12/2015	18	-
239	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	11.28	01/2013 -	12/2015	35	-
240	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	593.50	03/2013 -	12/2015	33	-
241	6-LANNING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	636.20	09/2014 -	12/2015	15	-
242	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	328.70	10/2013 -	12/2015	26	-
243	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.80	06/2014 -	12/2015	18	-
244	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	590.90	08/2015 -	02/2016	6	-
245	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.90	08/2012 -	03/2016	43	-
246	PATNA-MUZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	632.70	02/2013 -	03/2016	37	-
247	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	650.00	1,178.00	11/2013 -	03/2016	28	-
248	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	03/2016	29	-
249	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	408.10	04/2014 -	03/2016	23	-

(April 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
250	SIX LANE OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	295.70	06/2014 -	03/2016	21	-
251	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.50	10/2014 -	03/2016	17	-
252	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	441.80	04/2014 -	03/2016	23	-
253	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 -	386.10	127.10	09/2007 -	04/2016	103	-
254	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	317.50	09/2010 -	04/2016	67	-
255	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	761.30	07/2013 -	04/2016	33	-
256	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	647.40	04/2015 -	04/2016	12	-
257	BIJINI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	328.60	06/2008 -	05/2016	95	-
258	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	2,159.00	622.70	06/2015 -	05/2016	11	-
259	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	06/2016	56	-
260	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,170.00	07/2015 -	06/2016	11	-
261	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	929.60	09/2014 -	06/2016	21	-
262	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,922.00	08/2013 -	08/2016	36	-
263	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	588.40	02/2014 -	08/2016	30	-
264	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	66.11	11/2012 -	12/2016	49	-
265	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.55	09/2013 -	12/2016	39	-
266	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,374.00	12/2013 -	12/2016	36	-
267	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	-
268	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	403.00	09/2013 -	12/2016	39	-
269	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,MULTI STATE	12/2012	1,479.00 -	1,479.00	368.60	06/2015 -	12/2016	18	-
270	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	02/2017	84	-
271	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	726.40	07/2014 -	02/2017	31	-
272	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.40	11/2015 -	03/2017	16	-
273	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,138.00	03/2014 -	04/2017	37	-

(April 2015)									
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
274	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43	580.43	450.70	08/2013	05/2017	45	-
275	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79	998.79	1,610.00	08/2013	07/2017	47	-
276	BARSAT-KRISHNANAGAR - [N24000229]NHAI, WEST BENGAL	08/2012	867.00	867.00	598.60	02/2015	12/2017	34	-
	Total		74,557.19	76,616.14	70,011.77				
	<u>TELECOMMUNICATIONS</u>								
277	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00	384.00	55.22	10/2010	09/2015	59	1
	Total		384.00	384.00	55.22				
	<u>URBAN DEVELOPMENT</u>								
278	UPGRADATION OF NATIONAL FIRE SERVICES COLLEGE AT NAGPUR MAHARASTRA - [N28000073]CPWD,MAHARASHTRA	06/2010	205.00	205.00	-	03/2012	04/2015	37	-
279	FARIDABAD EXTENSION - [N28000057]DMRCL,DELHI	09/2011	2,494.00	2,494.00	639.78	09/2014	05/2015	8	-
280	ACADEMIC CUM RESIDENTIAL CAMPUS AT HARINGHANTA KALYANI WB FOR IISER KOLKATA - [N28000061]CPWD, WEST BENGAL	01/2009	225.81	225.81	-	06/2012	06/2015	36	-
281	CONSTRUCTION OF MAIN BUILDING SCHOOL OF INFRASTRUCTURE INCLUDING TWI NOS LAB - [N28000066]CPWD, ODISHA	11/2012	238.43	238.43	-	02/2015	08/2015	6	-
282	C/O NISM CAMPUS AT PATALGANGA RASAYANI DISTT RAIGADH MAHARASTRA - [N28000074]CPWD,MAHARASHTRA	12/2012	315.00	315.00	3.11	06/2015	08/2015	2	-
283	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83	270.83	-	11/2014	10/2015	11	-
284	CONSTRUCTION OF EXTENSION BUILDING TO PARLIAMENT HOUSE ANNEXE PARLIAMENT HOUSE COMPLEX NEW DELHI - [N28000069]CPWD,DELHI	05/2009	261.85	261.85	6.26	05/2013	11/2015	30	-
285	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00	23,136.00	-	01/2015	12/2015	11	-
286	CONSTRUCTION OF HEAD OFFICE BUILDING OF PNB ON PLAT NO-4 SECTOR 10 DWARKA NEW DELHI - [N28000077]CPWD,DELHI	05/2012	405.01	405.01	-	12/2014	04/2016	16	-
287	2000 BOYS HOSTEL(1000 DOUNLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86	171.86	-	03/2016	05/2016	2	-
288	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57	156.57	-	09/2015	07/2016	10	-
289	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00	14,600.00	10,603.80	12/2015	08/2016	8	-
290	DELHI MRTS PHASE-III - [N28000056]DMRCL,DELHI	09/2011	38,585.00	38,585.00	8,110.85	03/2016	12/2016	9	-

(April 2015)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
291	CONSTRUCTION OF CENTRAL ACADEMY FOR POLICE TRAINING (CAPT) BHOPAL - [N28000059]CPWD,MADHYA PRADESH	12/2012	188.87 -	188.87	5.79	12/2014 -	12/2016	24	-
292	STAGE I OF PHASE C/O PERMANENT CAMPUS FOR IIM - [N28000060]CPWD,TAMIL NADU	04/2014	332.72 -	332.72	-	09/2016 -	12/2016	3	-
293	CONSTRUCTION OD ADDITIONAL COMPLEX FOR THE SUPREM COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	884.30	-	08/2014 -	06/2017	34	-
	Total		82,471.25 -	82,471.25	19,369.59				
	Grand Total		498,493.91	600,993.45	374,161.68				

List of Projects Ahead of Schedule w.r.t. Latest Schedule

						(April 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
1	DEV OF G1 AND GS-15 (ONGCL) - [160100231	4/2003	429.82 3,955.21	3,955.21	3,439.38	04/2006 04/2016	06/2015
2	MARKETING TOP AT KORBA - [N16000186	1/2011	141.86 -	232.00	132.71	09/2016 -	12/2015
	Total		571.68 -	4,187.21	3,572.09		
	<u>POWER</u>						
3	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) [N18000154	10/2013	1,315.90 -	1,315.90	380.47	10/2016 -	03/2016
	Total		1,315.90 -	1,315.90	380.47		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
4	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063	12/2003	217.61 309.56	309.56	457.70	04/2010 01/2016	12/2015
	Total		217.61 -	309.56	457.70		
	Grand Total		2,105.19	5,812.67	4,410.26		

List of Projects on schedule w.r.t. Latest Schedule

(April 2015)								
						Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated	
1	2	3	4	5	6	7	8	
	<u>COAL</u>							
1	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008	8/2013	7,612.33 -	7,612.33	764.09	03/2023 03/2023	03/2023	
2	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	778.30	03/2016 -	03/2016	
3	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034	12/2007	490.10 -	490.10	186.68	03/2017 -	03/2017	
4	PENGANGA OCP(REVISED) - [N06000066	9/2014	441.82 -	441.82	104.36	03/2020 -	03/2020	
5	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	223.68	03/2016 -	03/2016	
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095	6/2011	5,907.11 -	5,907.11	845.30	12/2015 04/2018	04/2018	
7	MOONIDIH XV SEAM UG - [N06000098	8/2011	1,230.27 -	1,230.27	84.78	04/2015 04/2019	04/2019	
8	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.45 -	431.45	69.94	03/2016 -	03/2016	
9	CHHAL OC SEAM -III (6.00 MTY) - [N06000104	12/2013	610.63 -	610.33	-	03/2022 -	03/2022	
10	GARJANBAHAL OCP - [N06000117	11/2014	1,375.38 -	1,375.38	2.49	03/2021 -	03/2021	
11	KULDA EXPN OC. (5.00 MTY) - [N06000115	6/2014	289.03 -	289.03	-	03/2018 -	03/2018	
12	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114	5/2014	337.66 -	337.66	-	03/2019 -	03/2019	
13	SIARMAL OCP (40.00MTY) - [N06000113	5/2014	3,756.36 -	3,756.36	0.65	03/2026 -	03/2026	
14	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112	5/2014	479.15 -	479.15	6.34	03/2019 -	03/2019	
15	BIJARI OC RCE (1.50 MTY) - [N06000111	5/2014	164.49 -	164.49	22.10	03/2020 -	03/2020	
16	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109	8/2012	1,055.05 -	1,055.05	148.67	03/2018 -	03/2018	
17	KAPURIA UG(PSLW) - [N06000108	8/2011	988.35 -	988.35	43.93	04/2017 04/2017	04/2017	
18	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106	2/2014	555.52 -	555.52	-	03/2021 -	03/2021	
19	KANCHAN OC EXPANSION - [N06000125	12/2014	371.04 -	371.04	30.24	03/2021 -	03/2021	
20	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124	12/2014	357.80 -	357.80	106.44	03/2021 -	03/2021	
21	AMERA OC RCE - [N06000123	2/2015	335.97 -	335.97	30.30	03/2018 -	03/2018	

(April 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
22	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
23	BHANEGAON OC - [N06000121]	2/2015	187.94 -	187.94	32.35	03/2023 -	03/2023
24	GOKUL - [N06000120]	11/2014	267.67 -	267.67	89.38	03/2018 -	03/2018
25	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	70.90	03/2021 -	03/2021
26	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	6.02	03/2020 -	03/2020
27	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	101.90	03/2020 -	03/2020
28	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	74.44	03/2016 -	03/2016
29	MURADIDH UG TURN-KEY PROJECT - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 03/2016	03/2016
30	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	77.88	03/2018 -	03/2018
31	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	111.82	03/2016 -	03/2016
32	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	0.46	03/2023 03/2023	03/2023
	Total		34,829.01 -	34,669.21	4,013.44		
	<u>FERTILISERS</u>						
33	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79 -	197.79	13.09	11/2016 -	11/2016
	Total		197.79 -	197.79	13.09		
	<u>MINES</u>						
34	EXPANSION OF MALANJKHAND MINE-DEVELOPMENT OF UNDERGROUND MINE UNDER EXISTING OPEN CAST MINE OF CAPAC - [N10000007]	9/2011	1,856.00 -	1,856.00	-	09/2017 -	09/2017
	Total		1,856.00 -	1,856.00	.00		
	<u>PETROLEUM</u>						
35	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.89	1,768.09	03/2013 03/2016	03/2016
36	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	6/2007	736.65 -	736.65	472.29	09/2011 12/2015	12/2015
37	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]	6/2010	2,523.00 -	2,523.00	1,020.25	01/2014 12/2015	12/2015

(April 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
38	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	188.89	2.00	01/2014 11/2017	11/2017
39	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]	11/2010	331.20 -	269.10	190.04	08/2013 05/2015	05/2015
40	MEHESANA REDEVELOPMENT PROJECT - [N16000121]	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 12/2017	12/2017
41	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]	1/2010	723.64 -	723.64	-	03/2013 06/2016	06/2016
42	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	854.50	03/2015 05/2016	05/2016
43	TWENTY NOS. FEEDER GAS LINES - [N16000192]	3/2009	228.64 -	214.19	123.67	12/2016 -	12/2016
44	REVERSE OSMOSIS PLANT FOR ETP AT GUJARAT REFINERY - [N16000191]	12/2011	160.00 -	160.00	2.47	02/2016 02/2016	02/2016
45	CHINCHINNADA KAKINADA JUNCTION POINT PIPE LINE - [N16000190]	7/2014	419.04 -	419.04	34.08	01/2017 -	01/2017
46	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,813.25	379.10	05/2017 05/2017	05/2017
47	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	44.52	12/2018 -	12/2018
48	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 10/2015	10/2015
49	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,913.10	13.86	05/2016 04/2018	04/2018
50	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	4,619.94	0.47	02/2016 04/2017	04/2017
51	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	39.42	07/2016 -	07/2016
52	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	462.79	222.98	10/2014 10/2016	10/2016
53	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	2/2012	666.00 -	838.05	446.02	11/2015 11/2016	11/2016
54	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,446.34	1,024.42	11/2015 -	11/2015
55	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	3/2012	14,225.00 -	16,504.00	6,072.90	05/2016 -	05/2016
56	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	1,410.50	05/2014 05/2015	05/2015
57	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]	3/2012	2,592.17 -	2,592.17	536.91	05/2014 05/2016	05/2016
58	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	3,576.16	05/2015 -	05/2015
59	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	17.38	07/2016 -	07/2016
60	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	96.36	09/2017 -	09/2017

(April 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
61	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	29.03	02/2016 -	02/2016
62	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	93.08	09/2017 -	09/2017
63	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	75.24	04/2016 04/2016	04/2016
64	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	57.81	01/2016 07/2017	07/2017
65	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	7/2011	352.56 -	450.55	10.60	03/2017 -	03/2017
66	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]	4/2010	270.00 -	215.66	-	06/2012 11/2015	11/2015
67	SURAT PARADIP PIPELINE PROJECT - [N16000163]	10/2012	10,281.00 -	10,281.00	1.44	04/2015 -	04/2015
	Total		78,577.79 -	81,931.63	19,692.16		
	<u>POWER</u>						
68	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	6,476.34	3,862.64	12/2009 03/2017	03/2017
69	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	8/2008	2,491.58 -	3,745.08	619.75	07/2014 11/2018	11/2018
70	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	3,959.00	09/2016 -	09/2016
71	VINDHYACHAL STPP STAGE-V - [N18000134]	5/2012	3,180.40 -	3,180.40	1,782.00	08/2015 -	08/2015
72	KUDGI STPP STAGE 1 - [N18000131]	1/2012	15,166.19 -	15,166.19	8,031.00	01/2017 -	01/2017
73	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	1,025.28	926.80	08/2014 06/2015	06/2015
74	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	11,846.00	3,850.00	06/2017 -	06/2017
75	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	11,638.55	3,011.00	09/2017 -	09/2017
76	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	08/2016 -	08/2016
77	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	48.00	12/2015 -	12/2015
78	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]	2/2014	243.53 -	243.53	61.00	08/2016 -	08/2016
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	25.00	06/2016 -	06/2016
80	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	16.00	06/2016 -	06/2016

(April 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
82	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	147.34	04/2016 -	04/2016
83	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	241.60	05/2016 -	05/2016
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	185.49	03/2016 -	03/2016
85	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-B) - [N18000179]	12/2014	6,517.36 -	6,517.36	22.00	04/2018 -	04/2018
86	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	109.00	09/2019 -	09/2019
87	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	14,366.58	2,071.00	02/2019 -	02/2019
88	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	12,532.44	1,457.00	08/2018 -	08/2018
89	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	682.00	03/2019 -	03/2019
90	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]	7/2013	3,363.12 -	3,363.12	542.00	12/2016 -	12/2016
91	SUB-STATION WORKS ASSOCIATED WITH SYSTEM STRENGTHENING IN SOUTHERN REGION FOR IMPORT OF POWER FROM E - [N18000173]	11/2014	972.42 -	972.42	-	11/2017 -	11/2017
92	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]	10/2014	8,112.12 -	8,112.12	-	04/2020 -	04/2020
93	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	1.00	02/2016 -	02/2016
94	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	1/2013	12,964.60 -	12,964.60	-	01/2018 -	01/2018
95	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	-	05/2017 -	05/2017
96	SUBSTATION WORKS ASSOCIATED WITH HYDERABAD (MAHESHWARAM) POOLING STATION - [N18000186]	3/2015	550.06 -	550.06	-	03/2018 -	03/2018
97	INSTALLATION OF STATCOMS IN WESTERN REGION - [N18000185]	3/2015	1,071.24 -	1,071.24	-	10/2017 -	10/2017
98	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]	3/2015	197.40 -	197.40	-	04/2018 -	04/2018
99	WARDHA-HYDERABAD 765 KV LINK - [N18000183]	1/2015	3,662.02 -	3,662.02	5.00	05/2018 -	05/2018
100	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	203.28	-	07/2017 -	07/2017
101	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	-	11/2017 -	11/2017

(April 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
102	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]	1/2015	268.80 -	268.80	-	03/2018 -	03/2018
103	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME (ISTS) - PART A - [N18000197]	4/2015	1,479.30 -	1,479.30	-	05/2017 -	05/2017
104	GREEN ENERGY CORRIDORS INTER-STATE TRANSMISSION SCHEME -PART B - [N18000196]	4/2015	3,705.61 -	3,705.61	-	05/2018 -	05/2018
105	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
106	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	11.00	02/2017 -	02/2017
107	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	442.00	03/2018 -	03/2018
108	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]	6/2014	400.47 -	400.47	-	04/2017 -	04/2017
109	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N18000166]	2/2014	378.71 -	378.71	40.00	10/2016 -	10/2016
110	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	05/2016 -	05/2016
111	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	1.00	11/2016 -	11/2016
112	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	1.00	07/2016 -	07/2016
113	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	143.00	08/2017 -	08/2017
	Total		154,242.42 -	159,598.87	32,293.62		
	<u>RAILWAYS</u>						
114	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	4/2006	325.00 -	1,564.54	420.71	03/2010 03/2017	03/2017
115	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	536.01	03/2016 -	03/2016
116	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	4/2006	850.00 -	2,973.42	10.44	03/2015 03/2020	03/2020
117	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	626.11	03/2016 -	03/2016
118	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	4/2008	5,300.00 -	6,821.29	2,421.26	03/2014 03/2019	03/2019

						(April 2015)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
119	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	2,371.00	03/2016 -	03/2016
120	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	3.61	02/2019 -	02/2019
121	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	4/2012	148.77 -	209.00	2.64	12/2016 -	12/2016
122	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	163.59	03/2017 -	03/2017
123	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
124	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	816.55	43.93	03/2016 -	03/2016
125	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	2.33	02/2020 -	02/2020
	Total		21,518.28 -	31,031.73	6,602.73		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
126	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	276.70	06/2008 04/2015	04/2015
127	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	928.70	09/2015 -	09/2015
128	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	218.80	10/2015 -	10/2015
129	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	178.20	09/2016 -	09/2016
130	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	273.20	11/2016 -	11/2016
131	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	163.30	12/2015 -	12/2015
	Total		7,389.88 -	7,389.88	2,038.90		
	<u>STEEL</u>						
132	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	217.48	06/2015 -	06/2015
133	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	32.31	05/2016 -	05/2016
134	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	109.01	04/2016 -	04/2016
135	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]	4/2014	188.93 -	188.93	16.95	04/2015 -	04/2015

(April 2015)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
136	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	15,525.00	6,807.44	05/2015 12/2016	12/2016
137	3RD CONVERTER AND 4TH CASTER - [N12000088]	7/2011	974.76 -	974.76	79.15	07/2016 -	07/2016
138	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	24.02	10/2016 -	10/2016
139	TURBO BLOWER - 5 - [N12000092]	12/2009	280.00 -	280.00	2.00	09/2016 -	09/2016
140	ALTERNATE GAS NETWORK AT BSL - [N12000093]	3/2015	255.19 -	255.19	-	03/2018 -	03/2018
141	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]	4/2015	3,127.30 -	3,127.30	-	04/2018 -	04/2018
	Total		21,961.81 -	22,107.21	7,288.36		
	<u>TELECOMMUNICATIONS</u>						
142	NETWORK FOR SPECTRUM - [N26000101]	3/2012	13,334.00 -	13,334.00	-	07/2015 -	07/2015
	Total		13,334.00 -	13,334.00	.00		
	<u>URBAN DEVELOPMENT</u>						
143	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
144	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,219.21	-	07/2017 -	07/2017
145	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]	6/2014	157.84 -	157.84	-	03/2017 -	03/2017
146	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,264.00	-	11/2019 -	11/2019
147	KOCHI METRO RAIL PROJECT - [N28000081]	7/2012	5,181.79 -	5,181.79	-	07/2017 -	07/2017
148	NAGPUR METRO RAIL - [N28000085]	8/2014	8,680.00 -	8,680.00	-	03/2018 -	03/2018
	Total		45,907.98 -	45,907.98	.00		
	Grand Total		379,814.96	398,024.30	71,942.30		
