

402th
FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
April, 2019



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
R.K.Puarm, East Block 6, Level 7
New Delhi-110066
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY

1. The Flash Report for April 2019 contains information on the status of the 1453 Central Sector Infrastructure Projects costing ₹150 crore and above. During April 2019, 7 projects (2 projects each in Coal and Power sector, 1 project each in Petroleum, Road Transport & Highways and Railways sectors) have reported completion.

2. During the reference month, out of 1453 projects, 388 projects are delayed with respect to their original schedules and 59 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 59 projects, 12 are Mega Projects costing ₹1000 crore and above.

S.No.	Sector	Projects on monitor (No.)	Delayed Projects w.r.t original schedule (No.)	Additionally delayed during the month under report (No.)	Additionally delayed Mega Projects (No.)
1	ROAD TRANSPORT AND HIGHWAYS	652	126	17	1
2	RAILWAYS	364	92	6	0
3	PETROLEUM	140	39	8	5
4	COAL	98	33	8	0
5	POWER	77	53	13	6
6	URBAN DEVELOPMENT	57	21	5	0
7	HEALTH AND FAMILY WELFARE	20	4	0	0
8	STEEL	14	10	0	0
9	SHIPPING AND PORTS	7	1	0	0
10	FERTILISERS	5	1	1	0
11	MINES	5	0	0	0
12	TELECOMMUNICATIONS	5	3	1	0
13	ATOMIC ENERGY	4	4	0	0
14	HEAVY INDUSTRY	2	0	0	0
15	DEFENCE PRODUCTION	2	0	0	0
16	CIVIL AVIATION	1	1	0	0
Total		1453	388	59	12

3. Total original cost of implementation of the 1453 projects was ₹18,32,579.17 crore and their anticipated completion cost is likely to be ₹21,61,313.18 crore, which reflects overall cost overruns of ₹3,28,734.01 crore (17.94% of original cost). The expenditure incurred on these projects till April 2019 is ₹8,84,906.88 crore, which is 40.94% of the anticipated cost of the projects. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns is as follows:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns (as on 01-05-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	40.28
COAL					
1	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
2	BHANEGAON OC	02/2015	187.94	409.68	117.98
3	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	80.24
5	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	19.86
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	5.89
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	24.10
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	3.45
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.06
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	122.78
PETROLEUM					
1	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	309.81	723.40	133.50
2	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	83.01
3	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	70.49
4	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
5	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	202.94	330.35	62.78
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	210.19
2	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	5024.35	203.22
3	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	197.14
4	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	139.69
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	90.82
RAILWAYS					
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	2360.35
2	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	04/2011	120.70	1800.00	1391.30

3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
4	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
5	MUNIRABAD (GINGERA) -RAICHUR NL	04/2007	179.65	1350.91	651.97
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) _NEW	09/2015	771.18	7558.00	880.06
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	106.50
3	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	104.00	201.00	93.27
4	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	199.81	385.13	92.75
5	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	155.04	280.13	80.68
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	300.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	82.72
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	12.88
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	22542.00	45.20
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	42.39
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	3.58
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	219.60	2.00
URBAN DEVELOPMENT					
1	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
2	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	44.80
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	30.58
4	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	30.53
5	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	02/2014	388.00	488.28	25.85

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

4. The sector wise list of projects (maximum five in numbers) having maximum cost overruns (COR) in absolute term is as below:-

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)
(as on 01-05-2019)

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	126.72
COAL					
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7080.41	1173.30
2	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
3	BHANEGAON OC	02/2015	187.94	409.68	221.74
4	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	249.03	448.86	199.83
5	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	186.52
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	197.79	209.44	11.65
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	99.78
2	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	523.00	17.42
3	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	156.65	0.09
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	3827.30	2109.30
PETROLEUM					
1	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
2	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
3	PARADIP HYDERABAD PIPELINE	01/2015	2321.00	3338.00	1017.00
4	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	1577.15	715.36
5	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	700.00
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	13211.01
2	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	6402.70
3	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9394.80	5475.21
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	2496.90	7419.34	4922.44
5	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	4317.94
RAILWAYS					
1	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00

3	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
4	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	13809.00	9354.83
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	6093.31	5845.65
ROAD TRANSPORT AND HIGHWAYS					
1	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	09/2015	771.18	7558.00	6786.82
2	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
3	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1928.22	2945.00	1016.78
4	FOUR LANING OF GWALIOR-SHIVPURI	05/2013	1055.00	1601.77	546.77
5	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	03/2017	993.16	1434.00	440.84
SHIPPING AND PORTS					
1	ENORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	450.00
2	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	303.07
3	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	275.98	31.48
STEEL					
1	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	22542.00	7017.00
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	343.00	488.40	145.40
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
2	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	8.30
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	219.60	4.30
URBAN DEVELOPMENT					
1	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	19058.00	4458.00
2	KOCHI METRO RAIL PROJECT	07/2012	5181.79	5687.79	506.00
3	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	1592.00	372.79
4	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	344.46
5	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	4439.23	175.23

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

5. Out of the 1453 projects, 294 are on schedule, 388 are delayed, 345 projects reported cost overrun and 134 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 317 if delay is calculated on the basis of latest schedule of completion. Further, for 749 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 388 delayed projects, 121 (31.19%) projects have overall delay in the range of 1 to 12 months, 78 (20.10%) projects have delay in the range of 13 to 24 months, 98 (25.26%) projects have delay in the range of 25 to 60 months and 91 (23.45%) projects have delay of 61 months and above. **The average time overrun in these 388**

delayed projects is 40.28 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are as below:

Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-05-2019)

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2021	133
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	06/2020	54
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	12/2020	48
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2020	21
COAL					
1	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	03/2010	03/2022	144
2	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	03/2012	03/2024	144
3	RAMAGUNDAM OC-II EXTENSION	12/2009	03/2012	03/2023	132
4	KULDA OCP (MAHANADI COALFIELDS LTD)	01/2005	03/2010	03/2020	120
5	CHURI BENTI UG (0.81 MTY)	08/2007	03/2011	03/2021	120
FERTILISERS					
1	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016	05/2019	30
HEALTH AND FAMILY WELFARE					
1	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	10/2020	83
2	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	07/2019	26
3	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	02/2018	06/2019	16
4	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	09/2019	16
PETROLEUM					
1	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
2	ASSAM RENEWAL PROJECT FOR GROUP A	03/2009	03/2013	12/2019	81
3	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	12/2019	79
4	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	06/2010	01/2014	11/2019	70
5	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014	08/2019	58
POWER					
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	12/2021	147
2	BARH STPP(3X660MW) NTPC	02/2005	01/2011	08/2021	127
3	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	05/2005	11/2008	05/2019	126
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009	06/2019	114
5	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	12/2022	114

	RAILWAYS				
1	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
2	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	03/2021	220
4	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/1996	03/2004	03/2020	192
5	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	05/2008	03/2023	178
	ROAD TRANSPORT AND HIGHWAYS				
1	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2019	140
2	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	06/2019	135
3	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	05/2019	132
4	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	04/2019	130
5	GWALIOR-JHANSI, NH-75	12/2003	12/2009	08/2020	128
	SHIPPING AND PORTS				
1	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	12/2017	05/2020	29
	STEEL				
1	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	10/2019	53
2	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016	03/2020	41
3	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	06/2020	32
4	COKE OVEN BATTERY-5	12/2011	12/2017	09/2019	21
5	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	05/2015	12/2017	06/2019	18
	TELECOMMUNICATIONS				
1	NETWORK FOR SPECTRUM	03/2012	07/2015	05/2020	58
2	MADHYA PRADESH ACCESS (LOT1)	08/2017	05/2018	05/2019	12
3	MAHARAstra ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	10/2018	05/2019	7
	URBAN DEVELOPMENT				
1	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	03/2020	89
2	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	03/2021	72
3	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	10/2019	70
4	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	02/2014	03/2015	10/2020	67
5	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	01/2015	05/2020	64

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions, slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation etc.

7. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are as below:-

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-05-2019)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
	CIVIL AVIATION						
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	314.61	441.33	85.79	09/2018	06/2020
	COAL						
1	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	176.87	12/2019	12/2019
2	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.13	09/2019	09/2019
3	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	07/2016	409.87	409.87	18.23	03/2022	03/2022
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	07/2016	17237.00	17237.80	5982.50	11/2021	11/2021
5	KOLAR PIMPRI EXTENSION OC	03/2017	362.73	362.73	279.61	03/2020	03/2020
	HEALTH AND FAMILY WELFARE						
1	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	113.50	12/2014	N.A.
2	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	513.89	147.00	11/2013	10/2020
3	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	703.00	272.00	06/2020	06/2020
4	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	785.00	39.35	04/2020	04/2020
5	CNCI KOLKATA WEST BENGAL	08/2016	244.00	244.00	247.47	09/2018	N.A.
	HEAVY INDUSTRY						
1	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	1554.00	335.03	09/2019	09/2019
	PETROLEUM						
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	1693.00	1549.85	01/2012	N.A.
2	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	07/2011	350.00	350.00	2.06	01/2019	09/2019
3	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	678.00	5.53	02/2017	N.A.
4	MMPL PIPELINE REROUTING PROJECT	04/2013	449.58	449.58	142.34	12/2019	12/2019
5	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	06/2020
	POWER						
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19496.34	10723.47	09/2010	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3152.58	10/2017	N.A.
3	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	187.24	04/2016	06/2019
4	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	1086.32	04/2020	12/2023
5	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9072.36	1083.08	12/2018	12/2019
	RAILWAYS						

1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2100.00	484.14	07/2012	N.A.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	274.82	03/2019	03/2020
4	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	293.97	749.69	0.00	06/2005	N.A.
5	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	634.48	629.43	03/1994	N.A.
ROAD TRANSPORT AND HIGHWAYS							
1	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	01/1991	520.01	520.01	0.00	N.A.	N.A.
2	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	642.41	642.41	84.54	N.A.	10/2020
3	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	478.35	0.00	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	319.68	0.00	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	01/1991	219.40	219.40	0.00	01/2018	N.A.
SHIPPING AND PORTS							
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	150.00	600.00	139.80	03/2006	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	2427.40	2427.40	831.21	10/2008	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	669.46	411.12	12/2010	N.A.
4	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	03/2016	600.00	257.90	1.45	12/2017	05/2020
5	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	05/2016	970.00	970.00	272.73	05/2020	05/2020
STEEL							
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	4749.00	4749.00	109.06	09/2017	N.A.
TELECOMMUNICATIONS							
1	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	8397.00	07/2015	05/2020
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	418.26	418.26	367.03	06/2017	N.A.
3	MADHYA PRADESH ACCESS (LOT1)	08/2017	215.30	219.60	33.46	05/2018	05/2019
4	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	01/2018	231.80	240.10	117.63	10/2018	05/2019
URBAN DEVELOPMENT							
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1113.34	1085.64	02/2014	N.A.
2	IRRIGATION WORK OF BAGMATI	10/2005	956.00	956.00	651.21	03/2015	03/2021
3	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	175.94	178.65	12/2015	N.A.
4	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	246.90	246.90	0.00	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	227.00	199.95	12/2016	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like review these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-05-2019)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
	ATOMIC ENERGY				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	0.00	5771.17
	COAL				
1	KANIHA OCP, MCL, (10.0 MTY)	12/2007	457.77	0.00	619.13
2	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	172.08	0.00	345.12
3	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	207.28	0.00	249.61
4	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	0.00	203.55
5	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	0.00	254.72
	HEALTH AND FAMILY WELFARE				
1	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	508.29
2	CNCI KOLKATA WEST BENGAL	08/2016	244.00	0.00	247.47
	HEAVY INDUSTRY				
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	1718.00	0.00	2289.00
	PETROLEUM				
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	993.00	0.00	1549.85
2	GAIL GAS LTD BENGALURU CGD PROJECT	02/2015	749.00	0.00	860.14
	POWER				
1	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	0.00	7244.66
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	0.00	10723.47
3	BARH STPP(3X660MW) NTPC	02/2005	8692.97	15095.67	15932.41
4	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	2978.48	0.00	3938.20
5	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	0.00	7128.72
	RAILWAYS				
1	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	0.00	484.14
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	04/1986	158.77	274.56	629.43
3	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	538.21
4	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	759.20
5	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	04/1994	320.66	0.00	534.00
	ROAD TRANSPORT AND HIGHWAYS				
1	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	422.51
2	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	0.00	268.94
3	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	203.98
4	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	391.12
5	NALBARI TO BIJNI (AS-6)	12/2003	225.00	0.00	312.79
	SHIPPING AND PORTS				
1	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	366.39	0.00	411.12

2	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	244.50	258.00	275.98
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	768.88	1070.97	1085.64
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	173.00	178.65
3	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	0.00	16352.77
4	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	5188.50

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

10. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are as below:

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-05-2019)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	NORTH URIMARI OCP (3.0 MTY)	12/2007	03/2012	N.A.	N.A.
2	KAKATIYA LONGWALL	12/2008	12/2012	N.A.	N.A.
3	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	03/2016	N.A.	03/2019
4	MANUGURU OC-II EXTENSION PHASE-II	03/2010	03/2012	N.A.	N.A.
5	RKP OCP PHASE-I	03/2010	03/2015	03/2019	03/2019
DEFENCE PRODUCTION					
1	CONSTRUCTION WORKS PHASE 4	12/2016	05/2018	03/2019	N.A.
HEALTH AND FAMILY WELFARE					
1	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	N.A.
2	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	N.A.
3	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	N.A.
4	CNCI KOLKATA WEST BENGAL	08/2016	09/2018	N.A.	N.A.
5	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH	08/2017	03/2019	N.A.	N.A.
HEAVY INDUSTRY					
1	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	N.A.	N.A.
PETROLEUM					
1	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	01/2006	01/2012	N.A.	N.A.
2	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	N.A.	N.A.
3	PARADIP-RAIPUR- RANCHI PIPELINE	08/2009	12/2016	N.A.	N.A.
4	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	04/2011	05/2015	N.A.	N.A.
5	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	03/2013	N.A.	N.A.
POWER					
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	N.A.	N.A.
2	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
3	KUDGI STPP STAGE 1	01/2012	01/2017	N.A.	N.A.
4	MOUDA STPP STAGE 2	03/2012	09/2016	N.A.	N.A.
5	SOLAPUR STPP	03/2012	11/2016	03/2019	03/2019
RAILWAYS					
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.
2	NANGALDAM-TALWARA(NL),NR	03/1981	07/2012	N.A.	N.A.
3	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	06/2005	N.A.	N.A.
4	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR)	04/1986	03/1994	N.A.	N.A.

5	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA- CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	03/2006	N.A.	01/2006
ROAD TRANSPORT AND HIGHWAYS					
1	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	01/1991	04/2014	N.A.	N.A.
2	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI	01/1991	05/2016	N.A.	N.A.
3	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	08/2016	N.A.	N.A.
4	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	01/1991	10/2016	N.A.	N.A.
5	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	01/1991	10/2016	N.A.	N.A.
SHIPPING AND PORTS					
1	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	06/2005	10/2008	N.A.	N.A.
3	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	01/2007	12/2010	N.A.	N.A.
4	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	02/2015	12/2017	N.A.	N.A.
STEEL					
1	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	02/2014	09/2017	N.A.	N.A.
2	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	04/2014	04/2015	N.A.	N.A.
TELECOMMUNICATIONS					
1	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	09/2014	09/2014	N.A.	N.A.
2	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	06/2016	06/2017	N.A.	N.A.
URBAN DEVELOPMENT					
1	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	05/2005	02/2014	N.A.	N.A.
2	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	N.A.	N.A.
3	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	08/2007	N.A.	N.A.	N.A.
4	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY- JHARKHAND	12/2007	06/2016	N.A.	N.A.
5	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	N.A.	N.A.

N.A.: Not Available.

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised commissioning schedule.

11. The status as on 30.04.2019 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs.150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	652	17
2	RAILWAYS	364	6
3	PETROLEUM	140	8
4	COAL	98	8
5	POWER	77	13
6	URBAN DEVELOPMENT	57	5
7	HEALTH AND FAMILY WELFARE	20	0
8	STEEL	14	0
9	SHIPPING AND PORTS	7	0
10	FERTILISERS	5	1
11	MINES	5	0
12	TELECOMMUNICATIONS	5	1
13	ATOMIC ENERGY	4	0
14	HEAVY INDUSTRY	2	0
15	DEFENCE PRODUCTION	2	0
16	CIVIL AVIATION	1	0
	Total	1453	59

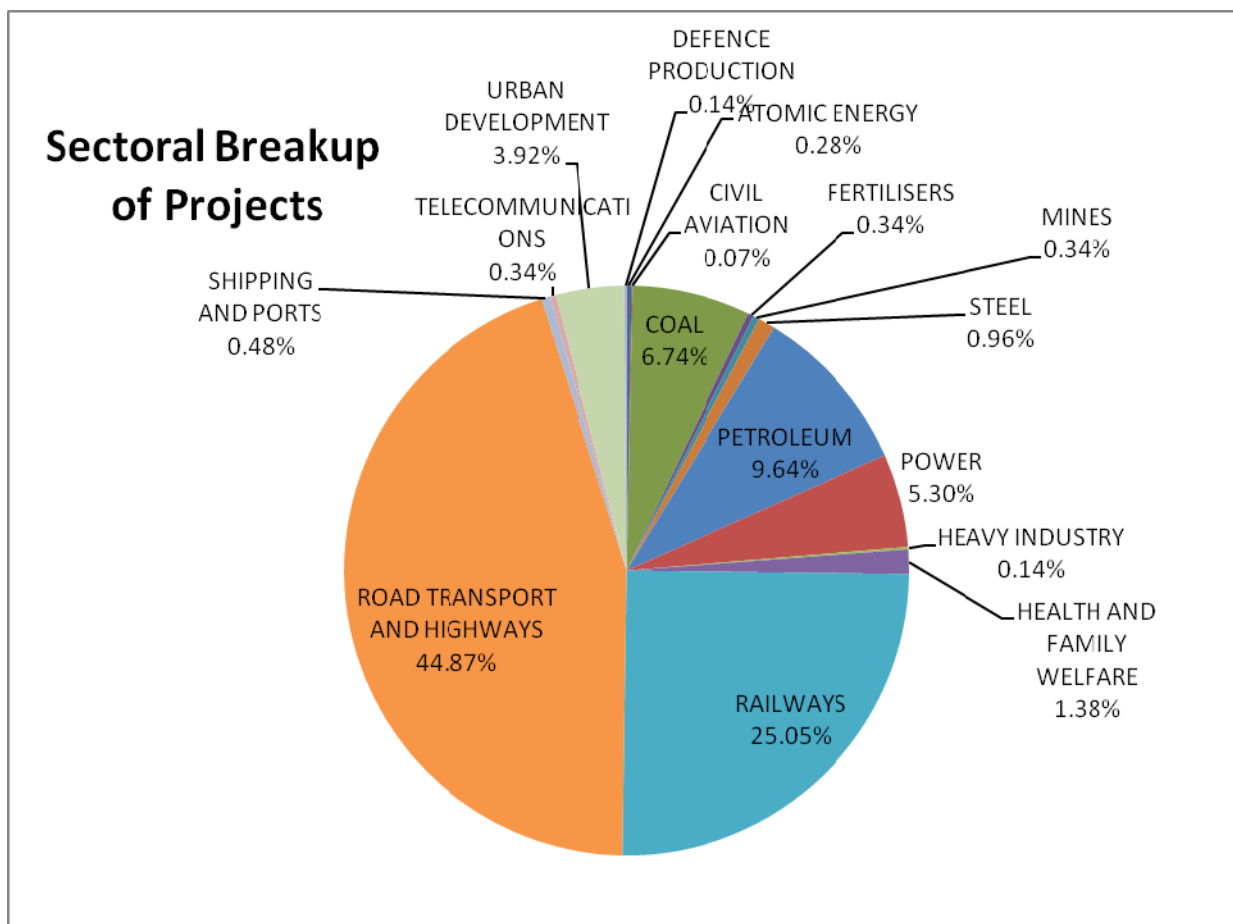


TABLE-2

Month wise List of Completed Projects Costing Rs.150 crore and above during				
2019-2020				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2019			
	<u>COAL</u>			
1	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI (NORTHERN COAL FIELDS LIMITED) - [N06000033]	259.40	03/2012	266.38
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) (NORTHERN COAL FIELDS LIMITED) - [N06000091]	1,131.28	03/2018	796.85
	<u>PETROLEUM</u>			
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY (INDIAN OIL CORPORATION LIMITED) - [N16000175]	3,076.00	09/2017	3,450.30
	<u>POWER</u>			
4	BONGAIGAON THERMAL POWER PROJECT (NATIONAL THERMAL POWER CORPORATION) - [N18000041]	4,375.35	09/2011	7,000.00
5	TRIPURA GAS BASED POWER PROJECT (NORTH EAST ELECTRIC POWER CORPORATION) - [N18000071]	421.01	07/2013	963.23
	<u>RAILWAYS</u>			
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) RAILWAY) - [N22000113]	653.19	03/2014	862.17
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000357]	567.51	03/2018	421.60

TABLE-3

Projects Added / Completed / Dropped / Frozen Rs.150 Crore and above

No of Projects in Previous Month	1405
No of Projects Completed/Dropped/Frozen in Current Month	7
No of Projects Elevated	1
No of Projects added in Current Month	56
No of Projects in Current Month	1453

Project status Rs.150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	388 (26.70%)	22 (1.51%)	294(20.23%)	103 (7.09%)	646(4.46%)	1453
Latest Approved (Date)	317 (21.82%)	26 (1.79%)	374(25.74%)	90 (6.19%)	646(4.46%)	1453

Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1244	15,26,017.47	17,38,131.91	6,76,664.73	38.90	2,12,114.44	13.90
Project with Revision in Cost	209	3,99,900.79	4,23,181.27	2,08,242.15	49.20	23,280.48	5.80
Total	1,453	19,25,918.26	21,61,313.18	8,84,906.88	40.94	2,35,394.92	12.22
Original Cost of All Projects							
Original Cost	1,453	18,32,579.17	21,61,313.18	8,84,906.88	40.94	3,28,734.01	17.94

Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	388	6,98,802.34	8,48,309.41	4,76,396.77	56.20	1,49,507.07	21.39
Latest Approved (RCE)	317	4,64,282.22	5,64,728.85	3,00,689.61	53.20	1,00,446.63	21.63

Additional Delayed Project cost Rs.150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	59	56,163.43	57,398.13	39,435.88	68.70	1,234.70	2.20
Total	59	56,163.43	57,398.13	39,435.88	68.71	1,234.70	2.20


Summary of projects in the Flash Report for the month of April, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1405
Number of Projects completed/dropped/frozen in Current Month	7
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	56
Number of Projects in Current Month	1453

Brief Analysis

Project Status with respect to Original Schedule: Out of 1453 projects, 22 projects are ahead of schedule, 294 projects are on schedule 388 projects are delayed. 646 projects do not have fixed dates of commissioning. 103 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

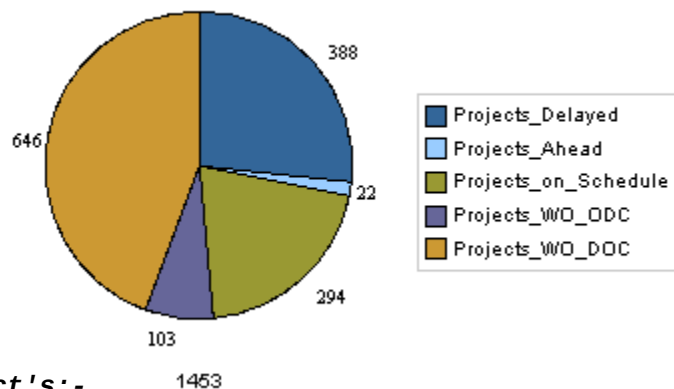

Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1453 projects when sanctioned, was of the order of Rs. 1832579.17 crore but this was subsequently revised to Rs. 2161313.18 crore implying a cost overrun of 17.9%. The expenditure incurred on these projects till April, 2019 is Rs. 884906.88 crore, which is 40.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

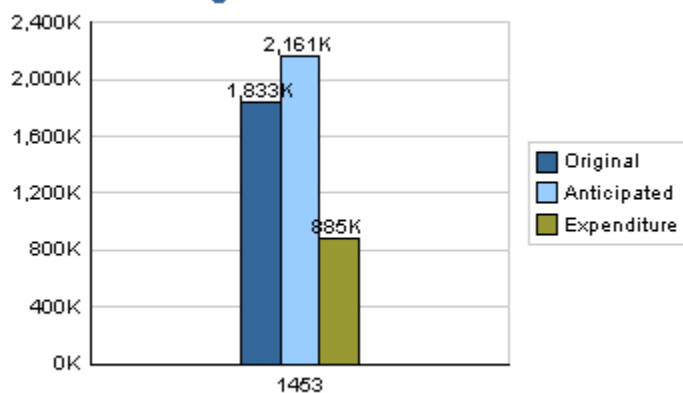


TABLE-4

<u>Extent of cost overrun in projects with respect to original schedule(Sector Wise)</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun [^]			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	75,589.00	12.62	2	14,951.00	23,420.00	56.65
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	98	99,419.73	99,873.07	0.46	11	25,725.94	28,037.55	8.99
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	5.89
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	14	32,793.01	39,597.41	20.75	2	15,868.00	23,030.40	45.14
7	PETROLEUM	140	2,29,497.78	2,34,857.89	2.34	19	27,989.65	36,251.99	29.52
8	POWER	77	2,87,073.06	3,45,343.53	20.30	33	1,61,106.73	2,19,894.25	36.49
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
11	RAILWAYS	364	4,84,549.30	7,01,059.04	44.68	205	1,72,046.28	3,98,507.24	131.63
12	ROAD TRANSPORT AND HIGHWAYS	652	4,28,477.95	4,41,091.58	2.94	49	28,447.55	41,837.22	47.07
13	SHIPPING AND PORTS	7	6,557.29	6,999.74	6.75	3	760.89	1,545.44	103.11
14	TELECOMMUNICATIONS	5	16,310.53	27,553.13	68.93	3	13,781.10	25,123.70	82.31
15	URBAN DEVELOPMENT	57	1,60,233.35	1,66,436.66	3.87	12	28,109.46	34,312.77	22.07
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0.00
Total		1453	18,32,579.17	21,61,313.18	17.94	345	4,92,093.25	8,37,632.17	70.22

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-5

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs. 150						Core and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	70	1,07,777.49	1,11,737.53	3.67	9	7,934.53	12,551.72	58.19
2	ARUNACHAL PRADESH	30	16,173.50	34,539.39	113.56	5	9,181.79	27,547.68	200.03
3	ASSAM	45	24,146.83	26,425.96	9.44	11	3,482.32	6,089.65	74.87
4	BIHAR	92	77,203.90	1,12,701.23	45.98	33	40,972.00	76,544.96	86.82
5	GOA	10	4,292.52	4,292.52	0.00	0	0.00	0.00	0.00
6	GUJARAT	47	48,487.41	53,770.51	10.90	5	13,190.88	19,045.90	44.39
7	HARYANA	33	22,750.09	24,653.74	8.37	4	2,139.14	4,176.00	95.22
8	HIMACHAL PRADESH	12	16,702.17	26,210.39	56.93	2	6,886.58	16,394.80	138.07
9	JAMMU AND KASHMIR	12	24,323.57	49,772.57	104.63	1	2,500.00	27,949.00	1017.96
10	KARNATAKA	47	82,362.96	88,262.78	7.16	13	23,620.24	29,732.82	25.88
11	KERALA	25	39,778.48	42,459.10	6.74	7	12,657.77	15,533.93	22.72
12	MADHYA PRADESH	76	72,266.49	76,649.63	6.07	8	25,097.05	33,454.26	33.30
13	MAHARASHTRA	127	1,85,046.27	1,99,526.36	7.83	27	32,092.78	47,476.97	47.94
14	MANIPUR	3	5,188.43	14,543.26	180.30	1	4,454.17	13,809.00	210.02
15	MEGHALAYA	8	4,791.25	9,884.79	106.31	1	906.46	6,000.00	561.92
16	MIZORAM	12	7,570.66	10,145.19	34.01	1	2,393.47	4,968.00	107.56
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	28.95
18	ODISHA	85	99,874.49	1,05,744.50	5.88	20	25,790.34	31,662.01	22.77
19	PUNJAB	37	18,777.92	18,883.93	0.56	3	1,716.50	1,849.55	7.75
20	RAJASTHAN	53	44,518.04	46,273.48	3.94	11	5,056.33	6,811.77	34.72
21	SIKKIM	9	3,476.73	6,281.03	80.66	2	1,727.48	4,532.06	162.35
22	TAMIL NADU	73	1,17,053.81	1,36,870.39	16.93	26	37,544.85	58,452.64	55.69
23	TRIPURA	8	4,001.35	7,266.74	81.61	6	3,134.46	6,399.85	104.18
24	UTTAR PRADESH	110	1,42,809.15	1,46,215.66	2.39	19	26,906.98	32,364.19	20.28
25	WEST BENGAL	65	59,118.49	67,700.99	14.52	21	15,855.16	24,773.35	56.25
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	2	552.41	679.33	22.98
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
28	DELHI	22	55,263.55	62,738.78	13.53	6	6,981.71	14,456.94	107.07
29	CHHATISGARH	44	78,300.50	88,747.57	13.34	7	32,475.21	44,295.14	36.40
30	JHARKHAND	48	47,744.98	52,512.74	9.99	9	22,304.03	27,075.57	21.39
31	UTTARAKHAND	29	35,073.18	41,560.88	18.50	9	9,874.84	16,363.05	65.70
32	TELANGANA	42	34,989.10	37,661.78	7.64	12	5,777.95	8,772.11	51.82
33	MULTI STATE	149	3,30,533.70	4,34,560.31	31.47	63	1,06,559.30	2,14,869.92	101.64
Total		1453	18,32,579.17	21,61,313.18	17.94	345	4,92,093.25	8,37,632.17	70.22

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-6

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	75,589.00	12.62	4	67,120.00	75,589.00	36 - 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	98	99,419.73	99,873.07	0.46	33	19,498.59	20,712.21	12 - 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	30 - 30
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	14	32,793.01	39,597.41	20.75	10	26,773.72	33,578.12	9 - 53
7	PETROLEUM	140	2,29,497.78	2,34,857.89	2.34	39	95,490.39	98,165.42	1 - 110
8	POWER	77	2,87,073.06	3,45,343.53	20.30	53	1,94,077.23	2,37,297.00	1 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	4	1,135.49	1,235.27	16 - 83
11	RAILWAYS	364	4,84,549.30	7,01,059.04	44.68	92	1,12,936.23	1,84,461.48	1 - 324
12	ROAD TRANSPORT AND HIGHWAYS	652	4,28,477.95	4,41,091.58	2.94	126	97,501.48	1,00,719.03	1 - 140
13	SHIPPING AND PORTS	7	6,557.29	6,999.74	6.75	1	600.00	257.90	29 - 29
14	TELECOMMUNICATIONS	5	16,310.53	27,553.13	68.93	3	13,781.10	25,123.70	7 - 58
15	URBAN DEVELOPMENT	57	1,60,233.35	1,66,436.66	3.87	21	69,375.71	70,519.51	2 - 89
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	-
Total		1453	18,32,579.17	21,61,313.18	17.94	388	6,98,802.34	8,48,309.41	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-7

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	70	1,07,777.49	1,11,737.53	3.67	20	54,828.69	57,097.22	2 - 168
2	ARUNACHAL PRADESH	30	16,173.50	34,539.39	113.56	2	2,635.83	7,574.34	36 - 114
3	ASSAM	45	24,146.83	26,425.96	9.44	11	5,081.71	6,414.27	1 - 140
4	BIHAR	92	77,203.90	1,12,701.23	45.98	22	39,585.28	56,126.55	6 - 127
5	GOA	10	4,292.52	4,292.52	0.00	0	0.00	0.00	-
6	GUJARAT	47	48,487.41	53,770.51	10.90	9	15,911.86	21,571.16	2 - 54
7	HARYANA	33	22,750.09	24,653.74	8.37	7	3,403.78	4,537.46	2 - 91
8	HIMACHAL PRADESH	12	16,702.17	26,210.39	56.93	4	8,595.51	14,070.72	4 - 147
9	JAMMU AND KASHMIR	12	24,323.57	49,772.57	104.63	4	14,917.75	40,366.75	10 - 220
10	KARNATAKA	47	82,362.96	88,262.78	7.16	21	46,211.83	47,262.52	2 - 264
11	KERALA	25	39,778.48	42,459.10	6.74	7	15,794.39	16,934.02	8 - 89
12	MADHYA PRADESH	76	72,266.49	76,649.63	6.07	22	30,721.83	34,013.47	2 - 96
13	MAHARASHTRA	127	1,85,046.27	1,99,526.36	7.83	36	69,133.25	72,746.67	2 - 192
14	MANIPUR	3	5,188.43	14,543.26	180.30	2	4,670.86	14,025.69	67 - 108
15	MEGHALAYA	8	4,791.25	9,884.79	106.31	3	1,379.19	1,379.19	13 - 64
16	MIZORAM	12	7,570.66	10,145.19	34.01	1	2,393.47	4,968.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	4	3,525.63	4,199.11	36 - 79
18	ODISHA	85	99,874.49	1,05,744.50	5.88	27	37,452.59	42,753.70	2 - 147
19	PUNJAB	37	18,777.92	18,883.93	0.56	5	2,036.78	2,138.79	1 - 25
20	RAJASTHAN	53	44,518.04	46,273.48	3.94	20	23,024.48	24,103.83	1 - 68
21	SIKKIM	9	3,476.73	6,281.03	80.66	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	73	1,17,053.81	1,36,870.39	16.93	19	66,748.21	72,158.74	5 - 133
23	TRIPURA	8	4,001.35	7,266.74	81.61	1	569.63	650.00	31 - 31
24	UTTAR PRADESH	110	1,42,809.15	1,46,215.66	2.39	20	37,924.85	37,954.89	2 - 68
25	WEST BENGAL	65	59,118.49	67,700.99	14.52	26	24,168.36	27,257.78	3 - 324
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
28	DELHI	22	55,263.55	62,738.78	13.53	5	3,429.61	3,902.18	5 - 83
29	CHHATISGARH	44	78,300.50	88,747.57	13.34	8	29,978.49	38,759.59	13 - 111
30	JHARKHAND	48	47,744.98	52,512.74	9.99	15	23,350.25	25,238.44	9 - 120
31	UTTARAKHAND	29	35,073.18	41,560.88	18.50	8	24,701.77	30,701.89	8 - 114
32	TELANGANA	42	34,989.10	37,661.78	7.64	15	18,688.31	19,551.72	7 - 144
33	MULTI STATE	149	3,30,533.70	4,34,560.31	31.47	41	80,197.98	1,09,482.39	1 - 178
Total		1453	18,32,579.17	21,61,313.18	17.94	388	6,98,802.34	8,48,309.41	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	75,589.00	4.63	4	72,241.00	75,589.00	36 - 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21 - 21
3	COAL	98	1,00,548.03	99,873.07	-0.67	27	17,847.32	18,154.38	0 - 144
4	FERTILISERS	5	1,310.72	1,310.72	0.00	1	209.44	209.44	30 - 30
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	-
6	STEEL	14	32,793.01	39,597.41	20.75	9	11,248.72	11,036.12	9 - 41
7	PETROLEUM	140	2,36,011.61	2,34,857.89	-0.49	21	21,463.78	21,405.23	1 - 110
8	POWER	77	3,04,800.98	3,45,343.53	13.30	22	68,315.92	87,017.91	1 - 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	-
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	4	1,135.49	1,235.27	16 - 83
11	RAILWAYS	364	5,46,383.13	7,01,059.04	28.31	81	99,404.09	1,62,211.37	0 - 220
12	ROAD TRANSPORT AND HIGHWAYS	652	4,29,421.30	4,41,091.58	2.72	126	97,700.00	1,00,719.03	1 - 140
13	SHIPPING AND PORTS	7	6,228.79	6,999.74	12.38	1	258.00	257.90	29 - 29
14	TELECOMMUNICATIONS	5	16,323.13	27,553.13	68.80	1	13,334.00	24,664.00	58 - 58
15	URBAN DEVELOPMENT	57	1,60,608.10	1,66,436.66	3.63	19	60,809.85	61,787.87	0 - 89
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	-
Total		1453	19,25,918.26	21,61,313.18	12.22	317	4,64,282.22	5,64,728.85	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of cost overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	72,241.00	75,589.00	4.63	1	3,492.00	6,840.00	95.88
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	40.28
3	COAL	98	1,00,548.03	99,873.07	-0.67	2	17,389.43	17,697.29	1.77
4	FERTILISERS	5	1,310.72	1,310.72	0.00	0	0.00	0.00	0.00
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0.00
6	STEEL	14	32,793.01	39,597.41	20.75	2	15,868.00	23,030.40	45.14
7	PETROLEUM	140	2,36,011.61	2,34,857.89	-0.49	9	10,247.51	11,730.65	14.47
8	POWER	77	3,04,800.98	3,45,343.53	13.30	19	1,28,935.81	1,69,478.36	31.44
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	3	1,076.25	1,193.54	10.90
11	RAILWAYS	364	5,46,383.13	7,01,059.04	28.31	196	1,43,706.17	3,10,082.41	115.78
12	ROAD TRANSPORT AND HIGHWAYS	652	4,29,421.30	4,41,091.58	2.72	35	24,113.91	36,748.19	52.39
13	SHIPPING AND PORTS	7	6,228.79	6,999.74	12.38	3	774.39	1,545.44	99.57
14	TELECOMMUNICATIONS	5	16,323.13	27,553.13	68.80	1	13,334.00	24,664.00	84.97
15	URBAN DEVELOPMENT	57	1,60,608.10	1,66,436.66	3.63	10	28,054.28	33,938.78	20.98
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0.00
Total		1453	19,25,918.26	21,61,313.18	12.22	283	3,89,024.36	6,41,217.69	64.83

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-10

Extent of time & cost overrun in projects with respect to latest schedule						Rs. 150	Crore and above		
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	75,589.00	4.63	1	3,492.00	6,840.00	133- 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	98	1,00,548.03	99,873.07	-0.67	1	152.43	459.49	60- 60
4	FERTILISERS	5	1,310.72	1,310.72	0.00	0	0.00	0.00	0- 0
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	14	32,793.01	39,597.41	20.75	1	343.00	488.40	41- 41
7	PETROLEUM	140	2,36,011.61	2,34,857.89	-0.49	2	3,382.56	3,488.31	33- 110
8	POWER	77	3,04,800.98	3,45,343.53	13.30	8	38,106.88	56,808.87	12- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
11	RAILWAYS	364	5,46,383.13	7,01,059.04	28.31	47	45,002.06	1,09,195.40	3- 220
12	ROAD TRANSPORT AND HIGHWAYS	652	4,29,421.30	4,41,091.58	2.72	15	13,212.66	16,239.91	1- 140
13	SHIPPING AND PORTS	7	6,228.79	6,999.74	12.38	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	5	16,323.13	27,553.13	68.80	1	13,334.00	24,664.00	58- 58
15	URBAN DEVELOPMENT	57	1,60,608.10	1,66,436.66	3.63	4	7,446.31	8,338.27	5- 40
16	DEFENCE PRODUCTION	2	454.00	453.64	-0.08	0	0.00	0.00	0- 0
Total		1453	19,25,918.26	21,61,313.18	12.22	82	1,25,200.62	2,27,477.87	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-11

<u>Extent of time & cost overrun in projects with respect to original schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	75,589.00	12.62	2	14,951.00	23,420.00	54- 133
2	CIVIL AVIATION	1	314.61	441.33	40.28	1	314.61	441.33	21- 21
3	COAL	98	99,419.73	99,873.07	0.46	9	8,301.00	10,390.07	12- 144
4	FERTILISERS	5	1,299.07	1,310.72	0.90	1	197.79	209.44	30- 30
5	MINES	5	7,078.62	7,078.62	0.00	0	0.00	0.00	0- 0
6	STEEL	14	32,793.01	39,597.41	20.75	2	15,868.00	23,030.40	41- 53
7	PETROLEUM	140	2,29,497.78	2,34,857.89	2.34	10	19,112.71	23,473.71	2- 110
8	POWER	77	2,87,073.06	3,45,343.53	20.30	28	1,33,100.12	1,76,319.89	4- 147
9	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
10	HEALTH AND FAMILY WELFARE	20	8,129.23	8,246.52	1.44	1	414.11	513.89	83- 83
11	RAILWAYS	364	4,84,549.30	7,01,059.04	44.68	52	50,678.32	1,22,621.45	3- 324
12	ROAD TRANSPORT AND HIGHWAYS	652	4,28,477.95	4,41,091.58	2.94	19	14,725.66	18,022.09	1- 140
13	SHIPPING AND PORTS	7	6,557.29	6,999.74	6.75	0	0.00	0.00	0- 0
14	TELECOMMUNICATIONS	5	16,310.53	27,553.13	68.93	3	13,781.10	25,123.70	7- 58
15	URBAN DEVELOPMENT	57	1,60,233.35	1,66,436.66	3.87	6	7,948.75	9,092.55	5- 70
16	DEFENCE PRODUCTION	2	453.64	453.64	0.00	0	0.00	0.00	0- 0
Total		1453	18,32,579.17	21,61,313.18	17.94	134	2,79,393.17	4,32,658.52	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-12

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	70	1,07,777.49	1,11,737.53	3.67	5	3,397.13	6,023.66	2 - 168
2	ARUNACHAL PRADESH	30	16,173.50	34,539.39	113.56	2	2,635.83	7,574.34	36 - 114
3	ASSAM	45	24,146.83	26,425.96	9.44	5	1,155.95	2,645.46	12 - 140
4	BIHAR	92	77,203.90	1,12,701.23	45.98	11	31,379.06	47,928.04	12 - 127
5	GOA	10	4,292.52	4,292.52	0.00	0	0.00	0.00	-
6	GUJARAT	47	48,487.41	53,770.51	10.90	2	11,779.66	17,438.96	36 - 54
7	HARYANA	33	22,750.09	24,653.74	8.37	1	1,108.00	2,288.00	91 - 91
8	HIMACHAL PRADESH	12	16,702.17	26,210.39	56.93	1	3,919.59	9,394.80	147 - 147
9	JAMMU AND KASHMIR	12	24,323.57	49,772.57	104.63	1	2,500.00	27,949.00	220 - 220
10	KARNATAKA	47	82,362.96	88,262.78	7.16	4	2,604.52	3,671.22	2 - 36
11	KERALA	25	39,778.48	42,459.10	6.74	2	9,770.08	10,933.75	15 - 29
12	MADHYA PRADESH	76	72,266.49	76,649.63	6.07	3	22,065.60	25,357.24	4 - 96
13	MAHARASHTRA	127	1,85,046.27	1,99,526.36	7.83	14	12,473.25	16,858.54	2 - 192
14	MANIPUR	3	5,188.43	14,543.26	180.30	1	4,454.17	13,809.00	108 - 108
15	MEGHALAYA	8	4,791.25	9,884.79	106.31	0	0.00	0.00	-
16	MIZORAM	12	7,570.66	10,145.19	34.01	1	2,393.47	4,968.00	81 - 81
17	NAGALAND	21	13,711.07	14,384.55	4.91	1	2,326.52	3,000.00	79 - 79
18	ODISHA	85	99,874.49	1,05,744.50	5.88	10	22,990.87	28,291.98	3 - 147
19	PUNJAB	37	18,777.92	18,883.93	0.56	2	1,142.54	1,244.55	1 - 25
20	RAJASTHAN	53	44,518.04	46,273.48	3.94	7	2,727.62	3,806.97	5 - 67
21	SIKKIM	9	3,476.73	6,281.03	80.66	1	1,339.48	4,084.69	51 - 51
22	TAMIL NADU	73	1,17,053.81	1,36,870.39	16.93	5	15,862.66	22,364.40	26 - 133
23	TRIPURA	8	4,001.35	7,266.74	81.61	1	569.63	650.00	31 - 31
24	UTTAR PRADESH	110	1,42,809.15	1,46,215.66	2.39	4	2,520.14	2,894.95	5 - 68
25	WEST BENGAL	65	59,118.49	67,700.99	14.52	8	10,138.10	13,227.53	12 - 324
26	A & N ISLANDS	8	2,385.01	2,492.59	4.51	1	314.61	441.33	21 - 21
27	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
28	DELHI	22	55,263.55	62,738.78	13.53	2	1,633.32	2,105.89	5 - 83
29	CHHATISGARH	44	78,300.50	88,747.57	13.34	4	28,155.21	36,936.31	33 - 111
30	JHARKHAND	48	47,744.98	52,512.74	9.99	3	15,641.24	17,529.43	31 - 48
31	UTTARAKHAND	29	35,073.18	41,560.88	18.50	4	7,241.32	13,241.95	70 - 114
32	TELANGANA	42	34,989.10	37,661.78	7.64	7	3,574.19	4,563.95	12 - 144
33	MULTI STATE	149	3,30,533.70	4,34,560.31	31.47	21	51,579.41	81,434.58	12 - 178
Total		1453	18,32,579.17	21,61,313.18	17.94	134	2,79,393.17	4,32,658.52	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

EXECUTIVE SUMMARY COSTING Rs.1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	166	0
2	ROAD TRANSPORT AND HIGHWAYS	138	5
3	PETROLEUM	48	5
4	POWER	43	5
5	COAL	15	1
6	URBAN DEVELOPMENT	13	0
7	STEEL	7	0
8	ATOMIC ENERGY	4	0
9	HEAVY INDUSTRY	2	0
10	SHIPPING AND PORTS	2	0
11	TELECOMMUNICATIONS	2	0
12	MINES	1	0
	Total	441	16

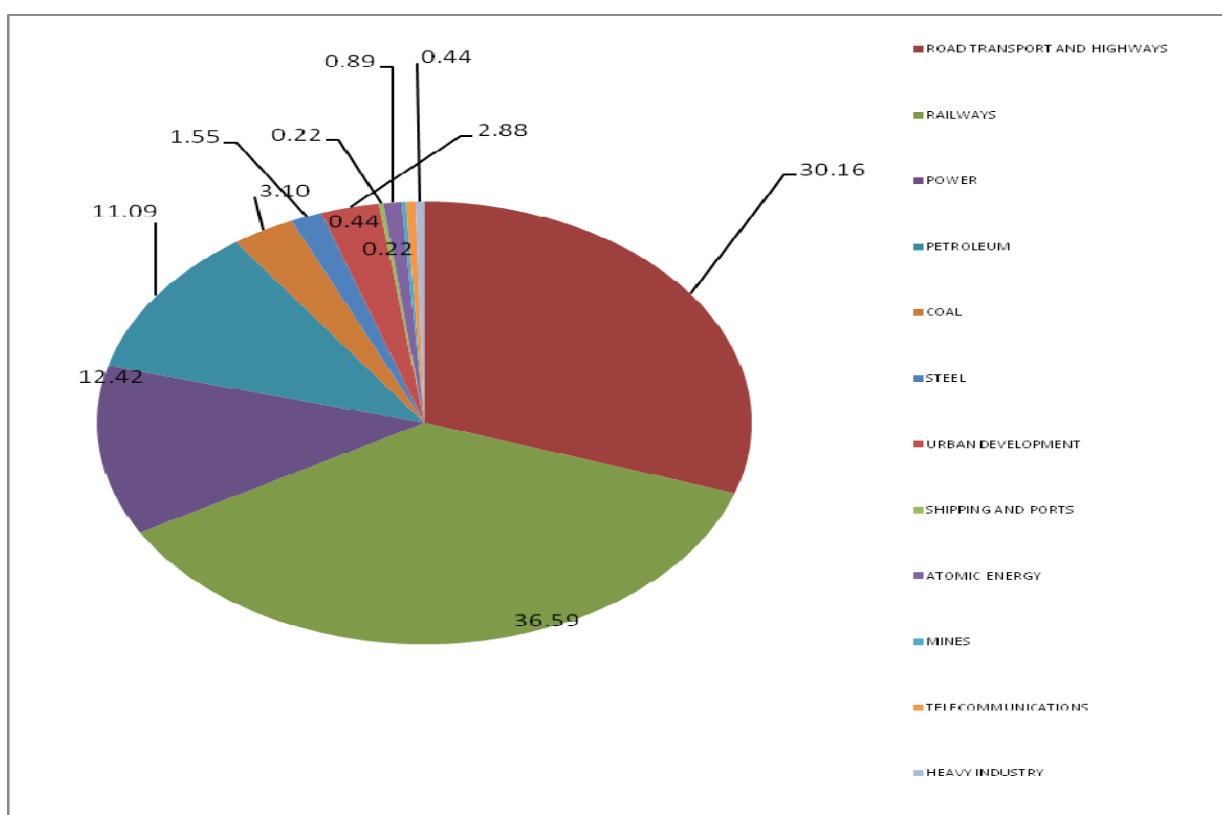


TABLE-14

Projects Added / Completed / Dropped / Frozen Rs.1000 Crore and above

No of Projects in Previous Month	443
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	4
No of Projects in Current Month	441

Project status Rs.1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	155 (35.15%)	6 (1.36%)	109(24.72%)	36 (8.16%)	135(0.61%)	441
Latest Approved (Date)	117 (26.53%)	8 (1.81%)	148(33.56%)	33 (7.48%)	135(0.61%)	441

Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	366	11,54,477.04	13,53,206.71	5,59,709.49	41.40	1,98,729.67	17.20
Project with Revision in Cost	75	3,44,876.96	3,65,628.84	1,80,004.53	49.20	20,751.88	6.00
Total	441	14,99,354.00	17,18,835.55	7,39,714.02	43.04	2,19,481.55	14.64
Original Cost of All Projects							
Original Cost	441	14,07,998.86	17,18,835.55	7,39,714.02	43.04	3,10,836.69	22.08

Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	155	5,98,083.56	7,42,135.87	4,25,679.09	57.40	1,44,052.31	24.09
Latest Approved (RCE)	117	3,78,641.85	4,75,128.58	2,58,114.83	54.30	96,486.73	25.48

Additional Delayed Project cost Rs.1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	16	39,209.97	39,829.79	27,570.52	69.20	619.82	1.60
Total	16	39,209.97	39,829.79	27,570.52	69.22	619.82	1.58

TABLE-15

<u>Extent of cost overrun in projects with respect to original schedule(Sector Wise)</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	75,589.00	12.62	2	14,951.00	23,420.00	56.65
2	COAL	15	64,463.42	65,637.52	1.82	2	23,144.11	24,318.21	5.07
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	36,789.34	22.10	1	15,525.00	22,542.00	45.20
5	PETROLEUM	48	1,90,922.65	1,95,287.85	2.29	10	24,120.75	31,069.32	28.81
6	POWER	43	2,73,282.51	3,30,657.66	20.99	23	1,56,988.55	2,14,880.75	36.88
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	166	4,03,158.50	6,05,214.36	50.12	102	1,40,215.20	3,46,416.36	147.06
9	ROAD TRANSPORT AND HIGHWAYS	138	2,02,785.85	2,14,328.45	5.69	15	17,709.70	29,252.30	65.18
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,508.50	3.97	5	26,033.88	31,890.36	22.50
Total		441	14,07,998.86	17,18,835.55	22.08	162	4,33,740.19	7,52,280.60	73.44

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-16

Extent of cost overrun in projects with respect to original schedule(State Wise) Rs.							1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	22	90,958.16	95,039.23	4.49	6	7,059.25	11,498.32	62.88
2	ARUNACHAL PRADESH	3	10,035.33	28,168.78	180.70	2	8,782.23	26,915.68	206.48
3	ASSAM	6	9,758.02	11,096.86	13.72	2	1,256.55	2,732.00	117.42
4	BIHAR	25	46,998.89	79,080.11	68.26	17	34,744.64	66,825.86	92.33
5	GUJARAT	14	32,725.85	37,953.55	15.97	2	12,434.62	17,662.32	42.04
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	2	6,886.58	16,394.80	138.07
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	1017.96
9	KARNATAKA	20	68,819.94	74,167.37	7.77	7	21,059.46	26,602.90	26.32
10	KERALA	10	32,670.86	35,060.11	7.31	3	11,336.08	13,749.37	21.29
11	MADHYA PRADESH	19	44,612.91	49,979.67	12.03	8	25,097.05	33,454.26	33.30
12	MAHARASHTRA	43	1,49,592.87	1,62,593.17	8.69	15	28,028.61	41,800.78	49.14
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	210.02
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	1	906.46	6,000.00	561.92
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	107.56
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	28.95
17	ODISHA	32	77,491.03	82,424.12	6.37	9	22,712.87	27,645.96	21.72
18	PUNJAB	3	3,627.54	3,627.54	0.00	0	0.00	0.00	0.00
19	RAJASTHAN	12	24,891.45	25,784.58	3.59	3	2,525.45	3,418.58	35.37
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	204.95
21	TAMIL NADU	26	97,537.75	1,15,127.79	18.03	12	33,965.50	51,555.54	51.79
22	TRIPURA	2	2,037.00	5,140.20	152.34	2	2,037.00	5,140.20	152.34
23	UTTAR PRADESH	43	1,11,994.14	1,15,394.84	3.04	8	24,042.65	28,215.30	17.36
24	WEST BENGAL	23	43,206.76	49,098.29	13.64	7	10,923.31	16,845.27	54.21
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	0.00
26	DELHI	7	50,481.91	57,816.75	14.53	3	6,254.39	13,589.23	117.28
27	CHHATISGARH	14	64,313.38	75,826.25	17.90	6	32,322.78	43,835.65	35.62
28	JHARKHAND	12	34,294.40	38,256.27	11.55	4	20,763.50	24,725.37	19.08
29	UTTARAKHAND	7	27,696.84	33,819.80	22.11	4	8,654.06	14,777.02	70.75
30	TELANGANA	6	19,991.02	22,068.25	10.39	2	2,378.60	4,455.84	87.33
31	MULTI STATE	62	2,91,205.31	3,91,919.48	34.59	31	95,446.91	1,98,341.66	107.80
Total		441	14,07,998.86	17,18,835.55	22.08	162	4,33,740.19	7,52,280.60	73.44

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-17

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	75,589.00	12.62	4	67,120.00	75,589.00	36 - 133
2	COAL	15	64,463.42	65,637.52	1.82	3	8,192.43	9,365.73	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	36,789.34	22.10	6	25,381.34	32,040.34	9 - 53
5	PETROLEUM	48	1,90,922.65	1,95,287.85	2.29	16	86,413.25	88,425.30	2 - 110
6	POWER	43	2,73,282.51	3,30,657.66	20.99	29	1,83,953.74	2,26,278.36	2 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	-
8	RAILWAYS	166	4,03,158.50	6,05,214.36	50.12	55	96,430.88	1,64,826.21	3 - 324
9	ROAD TRANSPORT AND HIGHWAYS	138	2,02,785.85	2,14,328.45	5.69	36	52,635.78	55,446.00	2 - 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,508.50	3.97	5	64,622.14	65,500.93	5 - 64
Total		441	14,07,998.86	17,18,835.55	22.08	155	5,98,083.56	7,42,135.87	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-18

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	95,039.23	4.49	11	51,368.01	53,490.64	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	28,168.78	180.70	1	2,496.90	7,419.34	114 - 114
3	ASSAM	6	9,758.02	11,096.86	13.72	2	2,850.35	3,910.86	12 - 81
4	BIHAR	25	46,998.89	79,080.11	68.26	10	32,659.99	48,769.28	12 - 127
5	GUJARAT	14	32,725.85	37,953.55	15.97	2	13,417.88	18,538.88	2 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	3	8,322.31	13,797.52	15 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	4	14,917.75	40,366.75	10 - 220
9	KARNATAKA	20	68,819.94	74,167.37	7.77	9	38,464.45	39,234.70	2 - 264
10	KERALA	10	32,670.86	35,060.11	7.31	4	14,207.19	15,346.82	8 - 33
11	MADHYA PRADESH	19	44,612.91	49,979.67	12.03	5	25,413.32	28,704.96	4 - 96
12	MAHARASHTRA	43	1,49,592.87	1,62,593.17	8.69	16	60,215.65	63,463.81	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	32	77,491.03	82,424.12	6.37	12	30,417.75	35,195.88	3 - 147
18	PUNJAB	3	3,627.54	3,627.54	0.00	0	0.00	0.00	-
19	RAJASTHAN	12	24,891.45	25,784.58	3.59	3	14,579.12	14,965.38	5 - 67
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	26	97,537.75	1,15,127.79	18.03	9	60,882.75	67,340.08	21 - 133
22	TRIPURA	2	2,037.00	5,140.20	152.34	0	0.00	0.00	-
23	UTTAR PRADESH	43	1,11,994.14	1,15,394.84	3.04	12	34,676.06	34,802.33	2 - 32
24	WEST BENGAL	23	43,206.76	49,098.29	13.64	10	17,375.13	19,894.76	18 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	1	6,086.08	5,842.31	5 - 5
26	DELHI	7	50,481.91	57,816.75	14.53	2	2,613.73	2,986.52	5 - 31
27	CHHATISGARH	14	64,313.38	75,826.25	17.90	3	28,002.78	36,476.82	33 - 111
28	JHARKHAND	12	34,294.40	38,256.27	11.55	6	20,635.13	22,295.09	9 - 48
29	UTTARAKHAND	7	27,696.84	33,819.80	22.11	4	23,343.06	29,191.95	15 - 114
30	TELANGANA	6	19,991.02	22,068.25	10.39	4	14,450.02	14,727.41	7 - 144
31	MULTI STATE	62	2,91,205.31	3,91,919.48	34.59	17	69,066.51	97,224.09	2 - 178
Total		441	14,07,998.86	17,18,835.55	22.08	155	5,98,083.56	7,42,135.87	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

Extent of time overrun in projects with respect to latest schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	75,589.00	4.63	4	72,241.00	75,589.00	36 - 133
2	COAL	15	65,636.72	65,637.52	0.00	3	9,365.73	9,365.73	24 - 48
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	-
4	STEEL	7	30,130.34	36,789.34	22.10	5	9,856.34	9,498.34	9 - 32
5	PETROLEUM	48	1,96,102.79	1,95,287.85	-0.42	5	16,003.15	15,858.62	2 - 110
6	POWER	43	2,90,184.15	3,30,657.66	13.95	12	64,004.50	82,637.55	2 - 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	-
8	RAILWAYS	166	4,65,835.47	6,05,214.36	29.92	47	85,259.21	1,45,248.41	3 - 220
9	ROAD TRANSPORT AND HIGHWAYS	138	2,02,785.85	2,14,328.45	5.69	36	52,635.78	55,446.00	2 - 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	-
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58 - 58
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,508.50	3.75	4	55,942.14	56,820.93	5 - 64
Total		441	14,99,354.00	17,18,835.55	14.64	117	3,78,641.85	4,75,128.58	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-20

<u>Extent of cost overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns [^]			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	72,241.00	75,589.00	4.63	1	3,492.00	6,840.00	95.88
2	COAL	15	65,636.72	65,637.52	0.00	1	17,237.00	17,237.80	0.00
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
4	STEEL	7	30,130.34	36,789.34	22.10	1	15,525.00	22,542.00	45.20
5	PETROLEUM	48	1,96,102.79	1,95,287.85	-0.42	4	8,085.04	9,189.66	13.66
6	POWER	43	2,90,184.15	3,30,657.66	13.95	17	1,28,022.46	1,68,495.97	31.61
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	1	1,718.00	3,827.30	122.78
8	RAILWAYS	166	4,65,835.47	6,05,214.36	29.92	97	1,13,295.88	2,59,627.47	129.16
9	ROAD TRANSPORT AND HIGHWAYS	138	2,02,785.85	2,14,328.45	5.69	15	17,709.70	29,252.30	65.18
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0.00
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	84.97
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,508.50	3.75	5	26,335.97	31,890.36	21.09
Total		441	14,99,354.00	17,18,835.55	14.64	143	3,44,755.05	5,73,566.86	66.37

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-21

Extent of time & cost overrun in projects with respect to latest schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	72,241.00	75,589.00	4.63	1	3,492.00	6,840.00	133- 133
2	COAL	15	65,636.72	65,637.52	0.00	0	0.00	0.00	0- 0
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	36,789.34	22.10	0	0.00	0.00	0- 0
5	PETROLEUM	48	1,96,102.79	1,95,287.85	-0.42	1	3,030.00	3,049.47	110- 110
6	POWER	43	2,90,184.15	3,30,657.66	13.95	7	37,573.38	56,206.43	12- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	166	4,65,835.47	6,05,214.36	29.92	29	38,600.17	1,00,024.89	3- 220
9	ROAD TRANSPORT AND HIGHWAYS	138	2,02,785.85	2,14,328.45	5.69	11	11,890.31	14,700.53	2- 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	13	1,47,954.11	1,53,508.50	3.75	2	6,401.00	7,279.79	5- 29
Total		441	14,99,354.00	17,18,835.55	14.64	52	1,14,320.86	2,12,765.11	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-22

Extent of time & cost overrun in projects with respect to original schedule						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	75,589.00	12.62	2	14,951.00	23,420.00	54- 133
2	COAL	15	64,463.42	65,637.52	1.82	1	5,907.11	7,080.41	45- 45
3	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
4	STEEL	7	30,130.34	36,789.34	22.10	1	15,525.00	22,542.00	53- 53
5	PETROLEUM	48	1,90,922.65	1,95,287.85	2.29	6	18,112.40	21,810.42	15- 110
6	POWER	43	2,73,282.51	3,30,657.66	20.99	19	1,29,772.07	1,72,096.69	4- 147
7	HEAVY INDUSTRY	2	3,272.00	5,381.30	64.47	0	0.00	0.00	0- 0
8	RAILWAYS	166	4,03,158.50	6,05,214.36	50.12	33	43,482.23	1,12,042.60	3- 324
9	ROAD TRANSPORT AND HIGHWAYS	138	2,02,785.85	2,14,328.45	5.69	11	11,890.31	14,700.53	2- 91
10	SHIPPING AND PORTS	2	4,226.40	4,226.40	0.00	0	0.00	0.00	0- 0
11	TELECOMMUNICATIONS	2	15,445.17	26,675.17	72.71	1	13,334.00	24,664.00	58- 58
12	URBAN DEVELOPMENT	13	1,47,652.02	1,53,508.50	3.97	2	6,401.00	7,279.79	5- 29
Total		441	14,07,998.86	17,18,835.55	22.08	76	2,59,375.12	4,05,636.44	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-23

State-Wise Position of Central Sector Projects costing Rs.1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	22	90,958.16	95,039.23	4.49	3	2,819.63	5,300.26	2 - 168
2	ARUNACHAL PRADESH	3	10,035.33	28,168.78	180.70	1	2,496.90	7,419.34	114 - 114
3	ASSAM	6	9,758.02	11,096.86	13.72	1	385.20	1,532.00	12 - 12
4	BIHAR	25	46,998.89	79,080.11	68.26	8	29,968.32	46,077.61	12 - 127
5	GUJARAT	14	32,725.85	37,953.55	15.97	1	11,459.00	16,580.00	54 - 54
6	HARYANA	6	10,890.69	12,070.69	10.83	1	1,108.00	2,288.00	91 - 91
7	HIMACHAL PRADESH	6	14,146.19	23,654.41	67.21	1	3,919.59	9,394.80	147 - 147
8	JAMMU AND KASHMIR	9	23,449.96	48,898.96	108.52	1	2,500.00	27,949.00	220 - 220
9	KARNATAKA	20	68,819.94	74,167.37	7.77	2	1,824.74	2,611.00	3 - 4
10	KERALA	10	32,670.86	35,060.11	7.31	2	9,770.08	10,933.75	15 - 29
11	MADHYA PRADESH	19	44,612.91	49,979.67	12.03	3	22,065.60	25,357.24	4 - 96
12	MAHARASHTRA	43	1,49,592.87	1,62,593.17	8.69	8	10,784.12	14,804.15	2 - 192
13	MANIPUR	1	4,454.17	13,809.00	210.02	1	4,454.17	13,809.00	108 - 108
14	MEGHALAYA	2	2,400.94	7,494.48	212.15	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	4,968.00	107.56	1	2,393.47	4,968.00	81 - 81
16	NAGALAND	3	7,896.52	8,570.00	8.53	1	2,326.52	3,000.00	79 - 79
17	ODISHA	32	77,491.03	82,424.12	6.37	8	21,764.83	26,542.96	3 - 147
18	PUNJAB	3	3,627.54	3,627.54	0.00	0	0.00	0.00	-
19	RAJASTHAN	12	24,891.45	25,784.58	3.59	1	829.74	1,216.00	67 - 67
20	SIKKIM	1	1,339.48	4,084.69	204.95	1	1,339.48	4,084.69	51 - 51
21	TAMIL NADU	26	97,537.75	1,15,127.79	18.03	4	15,675.40	22,132.73	26 - 133
22	TRIPURA	2	2,037.00	5,140.20	152.34	0	0.00	0.00	-
23	UTTAR PRADESH	43	1,11,994.14	1,15,394.84	3.04	2	2,111.72	2,387.00	5 - 12
24	WEST BENGAL	23	43,206.76	49,098.29	13.64	4	8,466.71	10,986.35	36 - 324
25	D & N HAVELI	1	6,086.08	5,842.31	-4.01	0	0.00	0.00	-
26	DELHI	7	50,481.91	57,816.75	14.53	1	1,219.21	1,592.00	5 - 5
27	CHHATISGARH	14	64,313.38	75,826.25	17.90	3	28,002.78	36,476.82	33 - 111
28	JHARKHAND	12	34,294.40	38,256.27	11.55	2	15,492.47	17,152.43	31 - 48
29	UTTARAKHAND	7	27,696.84	33,819.80	22.11	3	7,127.06	12,975.95	76 - 114
30	TELANGANA	6	19,991.02	22,068.25	10.39	1	1,266.60	1,544.00	33 - 33
31	MULTI STATE	62	2,91,205.31	3,91,919.48	34.59	11	47,803.78	76,521.36	12 - 178
Total		441	14,07,998.86	17,18,835.55	22.08	76	2,59,375.12	4,05,636.44	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-24

List of projects completed/dropped/Frozen during current month					Rs. 150		Crore and above	
(All Cost/ Expenditure in Rs. crore)								
			Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure	
	<u>COAL</u>							
1	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	10/2007	259.40	03/2012	486.57	04/2019	266.38	
2	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	06/2011	1,131.28	03/2018	793.32	04/2019	796.85	
	<u>PETROLEUM</u>							
3	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY	03/2014	3,076.00	09/2017	4,190.00	04/2019	3,450.30	
	<u>POWER</u>							
4	BONGAIGAON THERMAL POWER PROJECT	01/2008	4,375.35	09/2011	8,150.00	03/2019	7,000.00	
5	TRIPURA GAS BASED POWER PROJECT	07/2009	421.01	07/2013	1,078.31	04/2019	963.23	
	<u>RAILWAYS</u>							
6	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GAUGE CONVERSION (NWR)	04/2008	653.19	03/2014	1,116.00	04/2019	862.17	
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
7	PHALODI -JAISALMER SECTION OF NH-15 TO TWO/FOUR LANE WITH PS	09/2015	567.51	03/2018	567.51	04/2019	421.60	

TABLE-25

List of projects added Rs. 150 Crore and above					(April 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	NAKRAKONDA KUMARDIH B OCP	8/2018	502.68	3/2029	502.68	3/2029
2	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	2,838.87	3/2029	2,838.87	3/2029
	<u>PETROLEUM</u>					
3	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	204.00	9/2019	204.00	9/2019
4	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	286.42	8/2020	286.42	8/2020
	<u>POWER</u>					
5	KHURJA SUPER THERMAL POWER PROJECT	3/2019	11,089.42	9/2023	11,089.42	9/2023
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
6	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	1,383.78	7/2018	1,383.78	7/2018
7	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86	3/2014	170.00	2/2015	170.00	2/2015
8	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	519.09	9/2019	519.09	9/2019
9	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	640.07	9/2019	640.07	9/2019
10	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	642.96	9/2019	642.96	9/2019
11	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	473.18	9/2019	473.18	9/2019
12	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	537.82	9/2019	537.82	9/2019
13	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	518.53	9/2019	518.53	9/2019
14	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND	4/2017	404.29	9/2019	404.29	9/2019

List of projects added Rs. 150 Crore and above					(April 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	GEOMETRIC IMPROVEMENTS FRO					
15	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	428.11	9/2019	428.11	9/2019
16	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	404.17	8/2018	404.17	8/2018
17	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	216.00	11/2018	216.00	11/2018
18	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	253.44	7/2019	253.44	7/2019
19	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	517.57	10/2018	517.57	10/2018
20	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	162.56	3/2018	162.56	12/2019
21	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 & NH-10 O	8/2014	600.87	11/2017	720.97	11/2017
22	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	823.20	11/2017	937.76	7/2019
23	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	166.21	8/2018	166.21	6/2020
24	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	271.17	11/2018	291.20	11/2019
25	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	169.63	3/2018	169.63	7/2020
26	R & U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	326.99	/	326.99	-
27	REHABILITATION & UPGADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHANDE	1/2017	396.86	9/2019	396.86	12/2019
28	REHABILITATION AND UPGADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	235.91	2/2018	235.91	11/2019
29	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	202.69	11/2019	202.69	11/2019
30	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	426.18	9/2020	426.18	9/2020
31	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	184.62	2/2018	184.62	11/2020
32	UPGRADATION OF NH-512 WITH A MINIMUM 2-	2/2018	218.70	11/2020	218.70	11/2020

List of projects added Rs. 150 Crore and above					(April 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4					
33	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	254.30	10/2020	254.30	10/2020
34	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	191.21	11/2019	191.21	11/2019
35	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	160.27	8/2019	160.27	8/2021
36	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	236.78	8/2019	236.78	8/2021
37	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	205.05	3/2017	205.05	4/2019
38	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	279.70	8/2017	398.22	8/2019
39	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	214.69	3/2018	214.69	11/2020
40	UPGRADATION OF PORSABHIND ROAD TO 2L + PS	3/2018	217.22	8/2018	217.22	6/2020
41	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	233.04	3/2018	233.04	11/2019
42	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	249.05	7/2018	249.05	1/2020
43	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	254.17	2/2018	254.17	11/2019
44	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	279.44	3/2018	279.44	4/2020
45	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	287.34	1/2019	287.34	1/2019
46	WIDENING TO 2-LANE+PS WITH RECONSTRUCTION OF BRIDGES & CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	373.82	9/2019	373.82	9/2019
47	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	809.16	7/2018	809.16	6/2020
48	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	877.79	6/2019	877.79	11/2019
49	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	818.00	/	818.00	-
50	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	306.28	5/2019	306.28	5/2019
51	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375	1/2017	247.25	3/2019	247.25	9/2019

List of projects added Rs. 150 Crore and above					(April 2019)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS					
52	REHABILITATION & UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH-3	3/2018	322.48	7/2020	322.48	7/2020
53	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	173.24	6/2020	173.24	6/2020
54	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	276.01	3/2019	276.01	5/2019
55	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	1,069.59	10/2019	1,069.59	10/2019
56	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0+000	3/2018	170.57	11/2020	170.57	11/2020

TABLE-26

Milestones (Cumulative due & achieved)	Rs.	150	Crore and above
Total		4617	
Achieved up to month		2533	

TABLE-27

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above							(April 2019)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>COAL</u>						
1	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) NLC	5,907.11	7,080.41	12/2015	06/2019	09/2019	3
2	HINGULA OC-II EXP. PH-III (15 MTY) MCL	479.53	479.53	03/2013	03/2020	03/2021	12
3	RFR OF MANUGURU OC PROJECT SCCL	430.45	415.37	03/2016	03/2019	03/2020	12
4	KAKATIYAKHANI OPENCAS-2 PROJECT SCCL	397.09	442.42	03/2019	03/2019	03/2020	12
5	KOYAGUDEM OPENCAS PROJECT SCCL Central Sector Projects	426.79	426.79	03/2018	03/2019	03/2020	12
6	KULDA OCP (MAHANADI COALFIELDS LTD) MCL	302.96	302.96	03/2010	03/2018	03/2020	24
7	KANIHA OCP, MCL, (10.0 MTY) MCL	457.77	457.77	03/2013	03/2020	03/2022	24
8	BALRAM OCP EXTENSION,MCL 8.00 MTY MCL	172.08	172.08	03/2010	03/2020	03/2022	24
	<u>FERTILISERS</u>						
9	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY RCF	197.79	209.44	11/2016	04/2019	05/2019	1
	<u>PETROLEUM</u>						
10	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I GAIL	3,957.00	3,397.00	12/2018	04/2019	05/2019	1
11	POLYPROPYLENE PLANT AT PARADIP REFINERY IOCL	3,150.00	3,150.00	09/2017	04/2019	06/2019	2
12	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY IOCL	822.66	822.66	11/2018	04/2019	06/2019	2
13	BSVI UPGRADATION MANGALORE REFIN	1,810.00	1,810.00	12/2019	12/2019	02/2020	2
14	SITARGANJ LPG PROJECT IOCL Central Sector Projects	160.10	160.10	02/2020	02/2020	10/2020	8
15	KHARAGPUR LPG BOTTLING PLANT IOCL	163.02	163.02	04/2020	04/2020	03/2021	11
16	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT GAIL	2,881.40	2,000.00	12/2020	12/2019	12/2020	12

List of projects reporting additional delayed Rs. 150 Crore and above							(April 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
17	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II GAIL Central Sector Projects	2,915.00	3,049.47	12/2012	09/2019	02/2022	29
	<u>POWER</u>						
18	KUNADANKULAM APP TRANS SYSTEM (PGCIL) PGCIL	1,779.29	2,187.32	11/2008	04/2019	05/2019	1
19	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX PGCIL	539.82	575.67	06/2016	04/2019	05/2019	1
20	EASTERN REGION STRENGTHENING SCHEME -IX PGCIL	196.58	225.28	02/2016	04/2019	05/2019	1
21	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP PGCIL	268.80	340.88	03/2018	04/2019	05/2019	1
22	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN PGCIL	1,429.38	1,429.38	01/2019	05/2019	06/2019	1
23	SOUTHERN REGION STRENGTHENING SCHEME-XXI PGCIL	562.25	562.25	03/2019	04/2019	05/2019	1
24	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL	608.24	608.24	04/2019	04/2019	05/2019	1
25	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA PGCIL	844.64	844.64	04/2019	04/2019	06/2019	2
26	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI PGCIL Central Sector Projects	3,654.00	3,654.00	04/2019	04/2019	06/2019	2
27	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	639.46	06/2014	06/2019	09/2019	3
28	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) PGCIL Central Sector Projects	445.89	445.89	02/2019	06/2019	09/2019	3
29	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D PGCIL	3,519.59	3,519.59	05/2019	05/2019	09/2019	4
30	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	06/2019	12/2019	6
	<u>RAILWAYS</u>						
31	MULTI MODAL LOGISTICS PARK AT KATHUWAS CCOI	493.17	493.17	03/2018	12/2019	03/2020	3


List of projects reporting additional delayed Rs. 150 Crore and above							(April 2019)
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
32	AJMER-BANGURGRAM NWR	213.39	244.02	11/2019	11/2019	05/2020	6
33	MULTI MODAL LOGISTICS PARK AT TIHI CCOI	174.00	174.00	03/2019	08/2019	02/2020	6
34	BANGURGRAM-GURIYA PATCH DOUBLING NWR	246.08	348.55	12/2019	11/2019	06/2020	7
35	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN CCOI	305.00	305.00	03/2019	03/2019	12/2019	9
36	MULTI MODAL LOGISTICS PARK AT BARHI CCOI	346.32	300.00	03/2019	03/2019	03/2020	12
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
37	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	167.98	05/2008	04/2019	05/2019	1
38	JORBAT - BARAPANI NHAI PPP (ANNUITY)	536.00	536.00	01/2014	04/2019	05/2019	1
39	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 NHAI	273.06	273.06	N.A.	04/2019	05/2019	1
40	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA NHAI	831.58	1,177.00	03/2020	06/2020	07/2020	1
41	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 NHAI	199.81	385.13	04/2009	03/2019	05/2019	2
42	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 NHAI	1,387.11	1,387.11	11/2017	05/2019	08/2019	3
43	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION NHAI	479.00	479.00	N.A.	03/2019	06/2019	3
44	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV NHAI	810.22	810.22	N.A.	03/2019	06/2019	3
45	FOUR LANING OF HOSPET - CHITRADURGA NHAI PPP (BOT)	1,388.00	1,388.00	08/2018	04/2019	11/2019	7
46	FOUR LANING OF CHANDIGARH - KHARAR NHAI	447.29	447.29	12/2017	04/2019	12/2019	8
47	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA NHAI	229.37	229.37	11/2018	04/2019	12/2019	8
48	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN NHAI	649.50	649.50	03/2019	12/2019	12/2020	12
49	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY NHAI	701.40	701.40	03/2019	07/2019	11/2020	16

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (April 2019)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
50	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM NHAI	950.69	950.69	08/2019	08/2019	12/2020	16
51	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 NHAI	605.84	605.84	07/2018	07/2018	12/2019	17
52	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG NHAI	1,550.98	1,550.98	N.A.	12/2019	07/2021	19
53	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION NHAI PPP (BOT)	1,655.01	1,655.01	08/2016	03/2019	12/2020	21
	<u>TELECOMMUNICATIONS</u>						
54	MADHYA PRADESH ACCESS (LOT1) BSNL Central Sector Projects	215.30	219.60	05/2018	04/2019	05/2019	1
	<u>URBAN DEVELOPMENT</u>						
55	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA CPWD	156.57	156.57	08/2016	05/2019	07/2019	2
56	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA CPWD	165.23	165.23	10/2012	12/2019	03/2020	3
57	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI CPWD	209.00	209.00	10/2019	10/2019	03/2020	5
58	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP CPWD	206.58	206.58	03/2019	03/2019	08/2019	5
59	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR CPWD Central Sector Projects	216.69	216.69	03/2015	11/2019	10/2020	11


TABLE-28

<u>Sector wise analysis of projects</u> Rs.150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	722,41.00	75,589.00	43,899.17
CIVIL AVIATION	1	314.61	3,14.61	441.33	85.79
COAL	98	99,419.73	1,005,48.03	99,873.07	33,228.20
FERTILISERS	5	1,299.07	13,10.72	1,310.72	438.42
MINES	5	7,078.62	70,78.62	7,078.62	579.13
STEEL	14	32,793.01	327,93.01	39,597.41	22,967.39
PETROLEUM	140	2,29,497.78	2,360,11.61	2,34,857.89	80,994.92
POWER	77	2,87,073.06	3,048,00.98	3,45,343.53	2,26,754.76
HEAVY INDUSTRY	2	3,272.00	32,72.00	5,381.30	2,624.03
HEALTH AND FAMILY WELFARE	20	8,129.23	81,29.23	8,246.52	2,946.15
RAILWAYS	364	4,84,549.30	5,463,83.13	7,01,059.04	2,11,064.80
ROAD TRANSPORT AND HIGHWAYS	652	4,28,477.95	4,294,21.30	4,41,091.58	1,69,517.06
SHIPPING AND PORTS	7	6,557.29	62,28.79	6,999.74	2,229.89
TELECOMMUNICATIONS	5	16,310.53	163,23.13	27,553.13	9,169.02
URBAN DEVELOPMENT	57	1,60,233.35	1,606,08.10	1,66,436.66	78,206.60
DEFENCE PRODUCTION	2	453.64	4,54.00	453.64	201.55
Grand total	1453	18,32,579.17	19,25,918.26	21,61,313.18	8,84,906.88

Graphical Presentation of All Projects w.r.t. Original Schedule

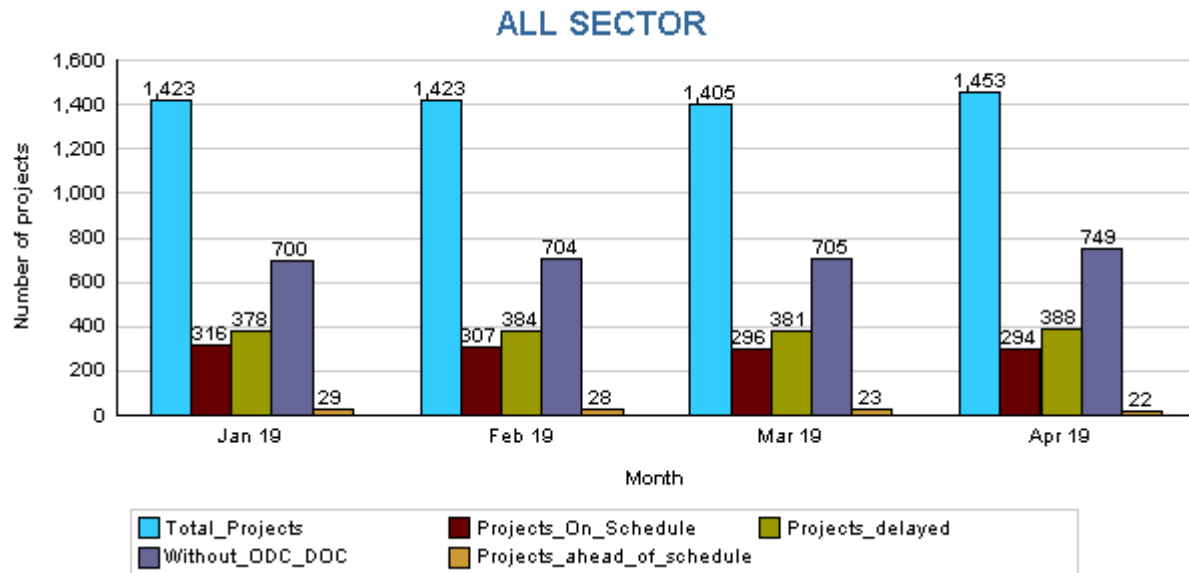


Break-up of 388 Delayed projects in April 2019

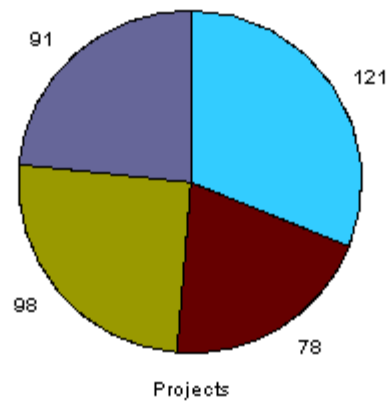


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

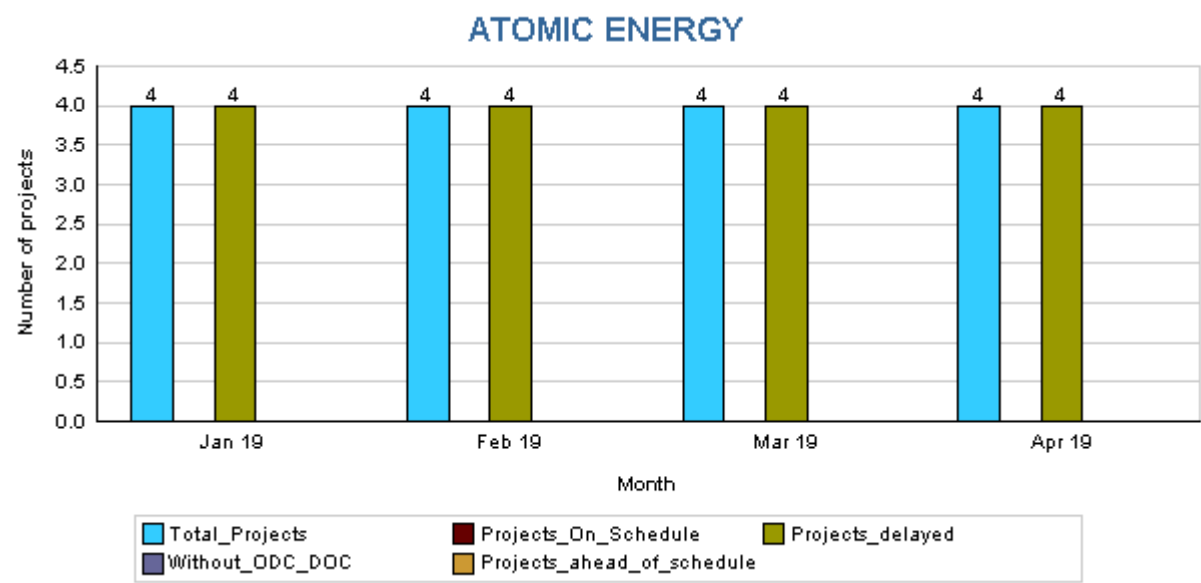


Break-up of 4 Delayed projects in April 2019

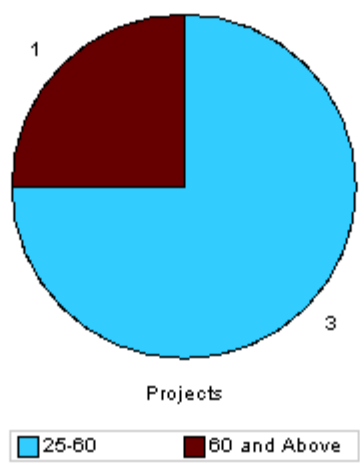


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

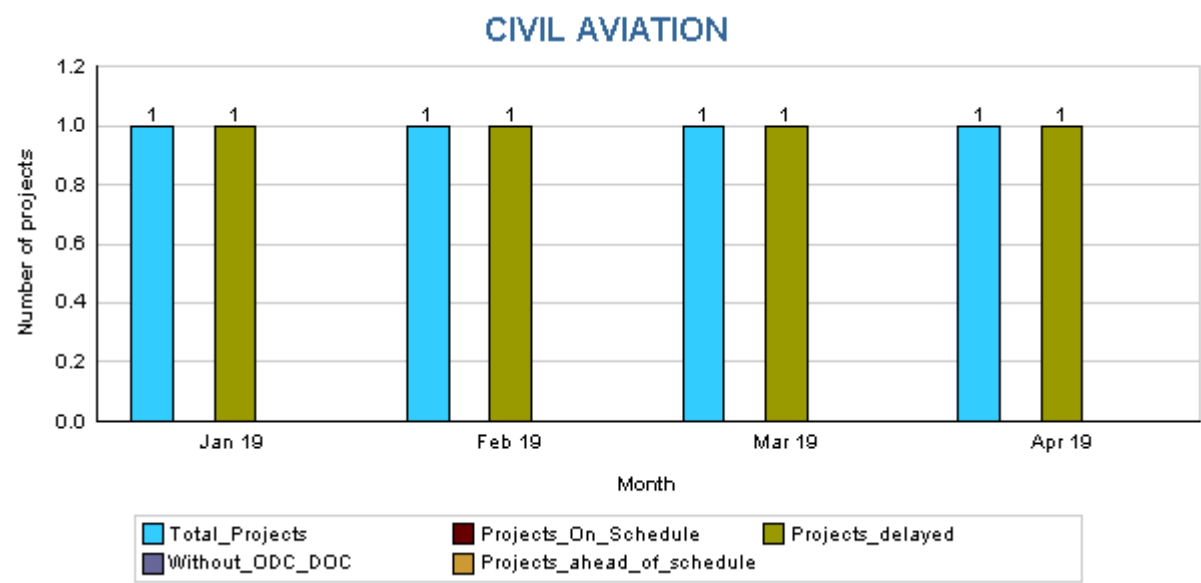


Break-up of 1 Delayed projects in April 2019




Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

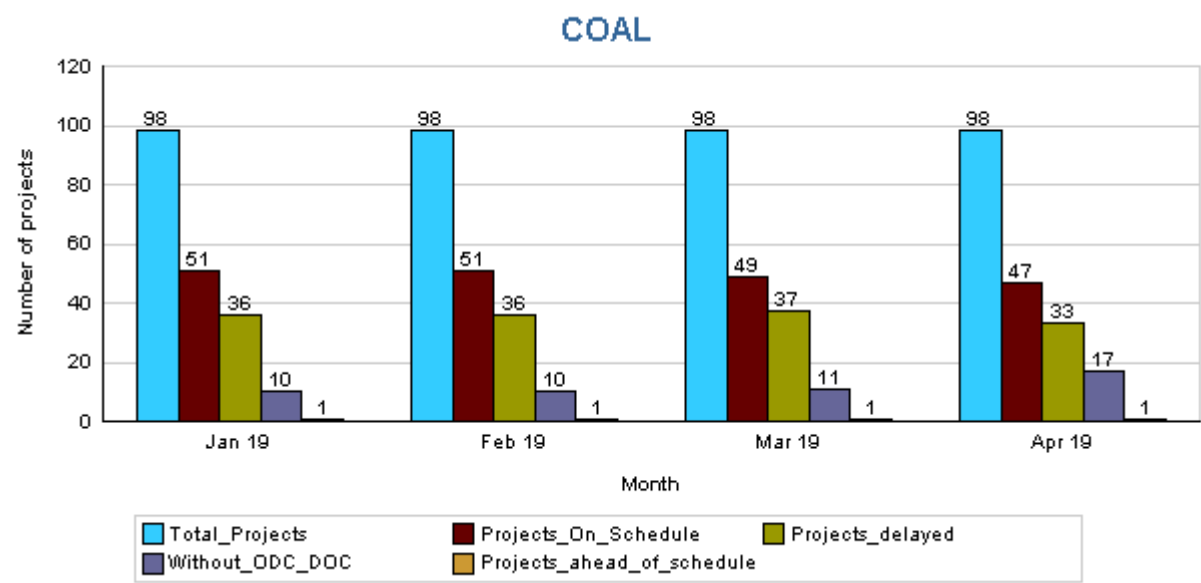


Break-up of 33 Delayed projects in April 2019

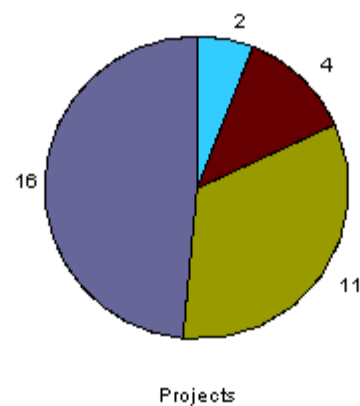


Delay in Months

1-12	13-24	25-60	60 and Above


Graphical Presentation of All Projects w.r.t. Original Schedule

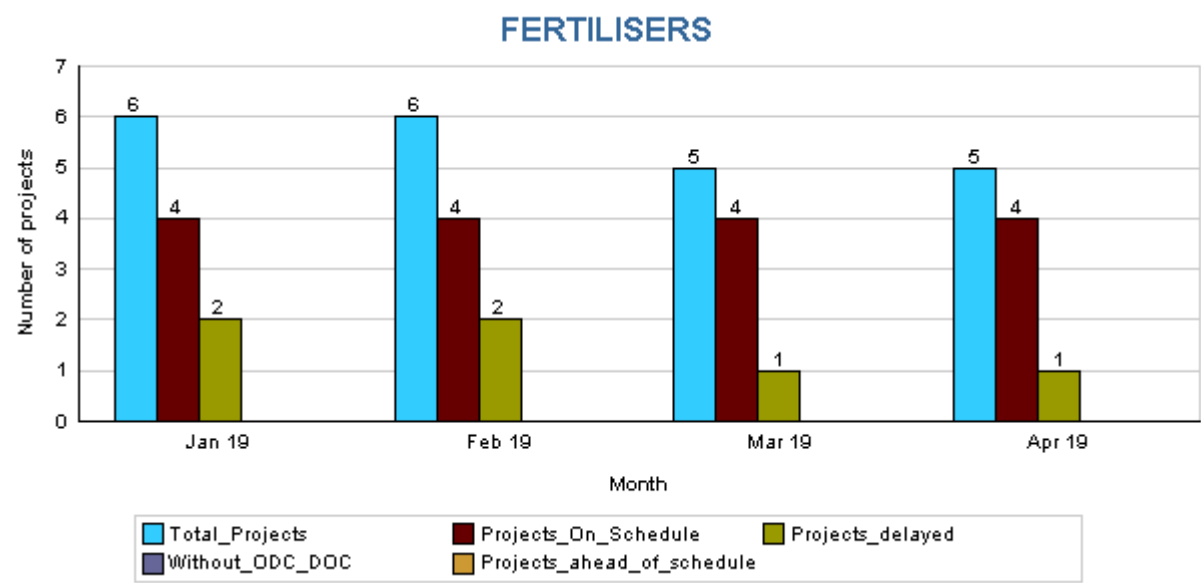


Break-up of 1 Delayed projects in April 2019



Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

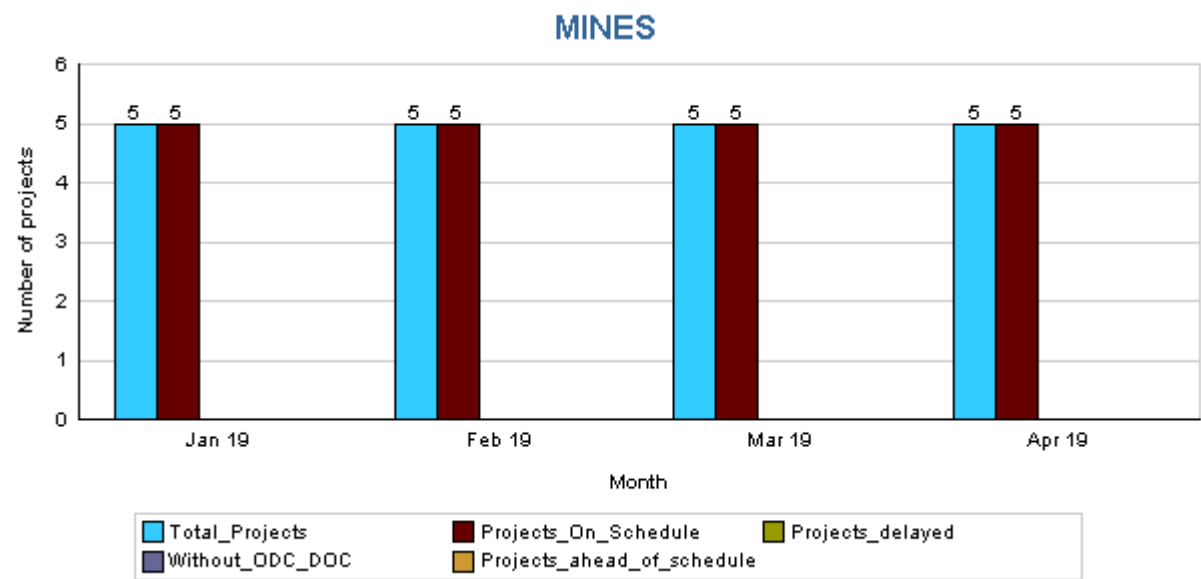


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

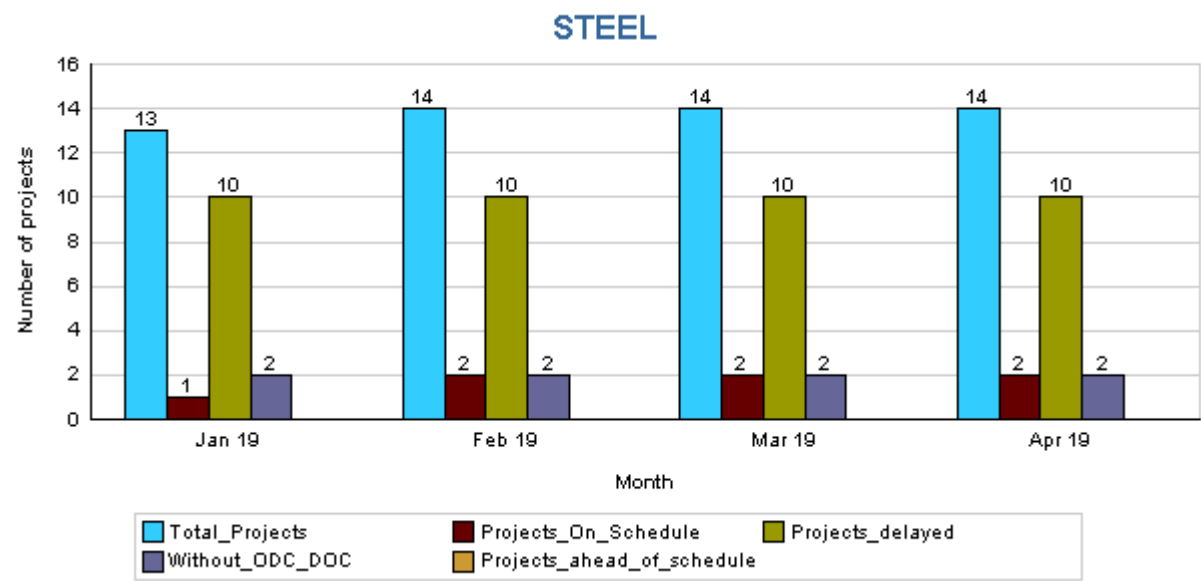


Break-up of 10 Delayed projects in April 2019

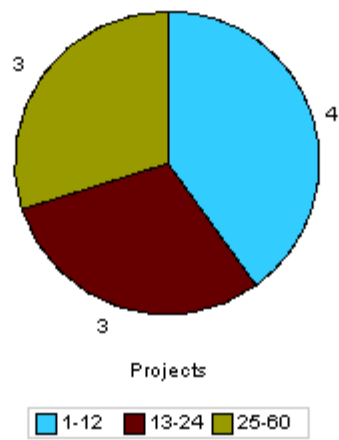


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

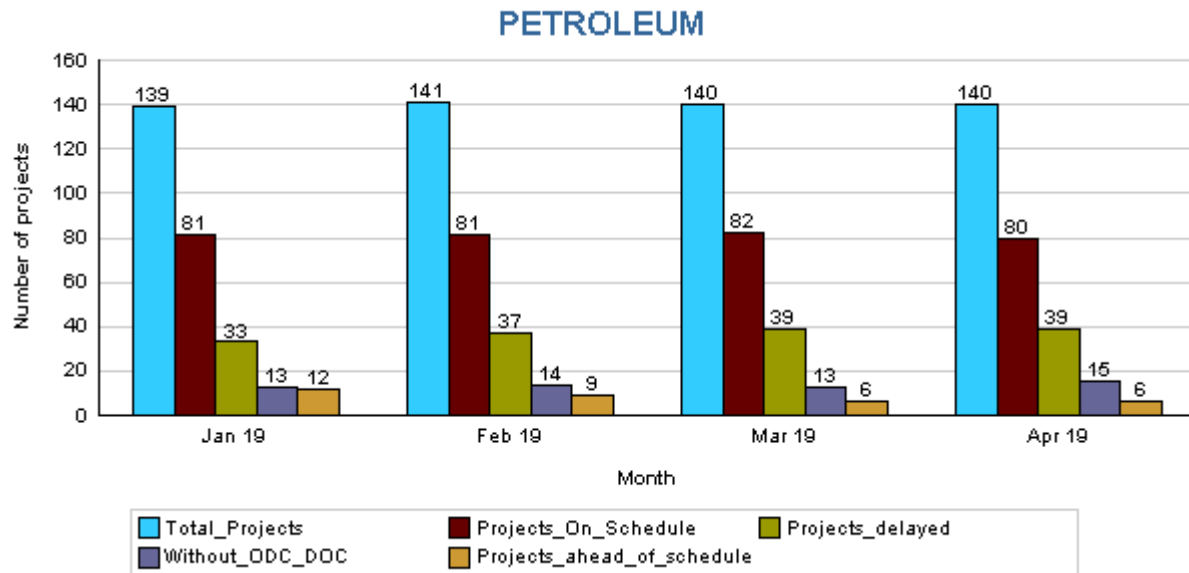


Break-up of 39 Delayed projects in April 2019

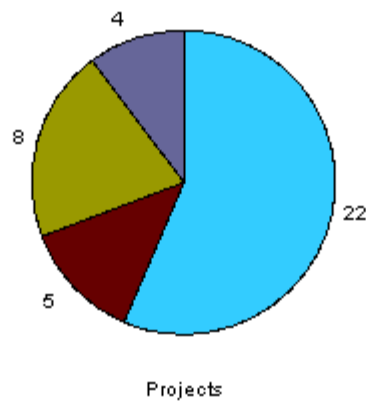

Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

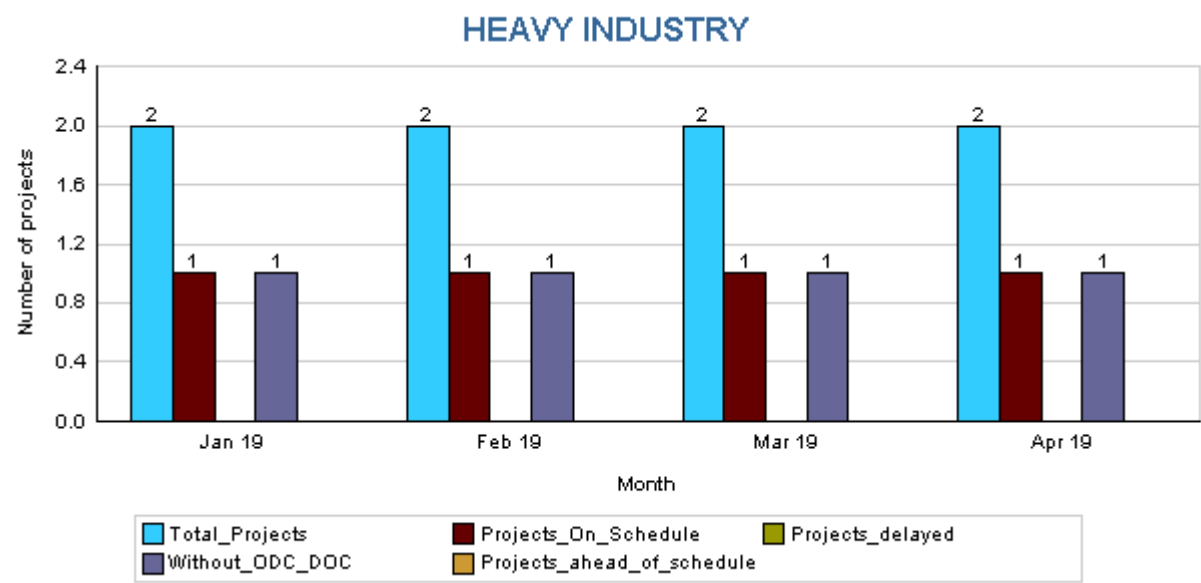


Delay in Months


Graphical Presentation of All Projects w.r.t. Original Schedule

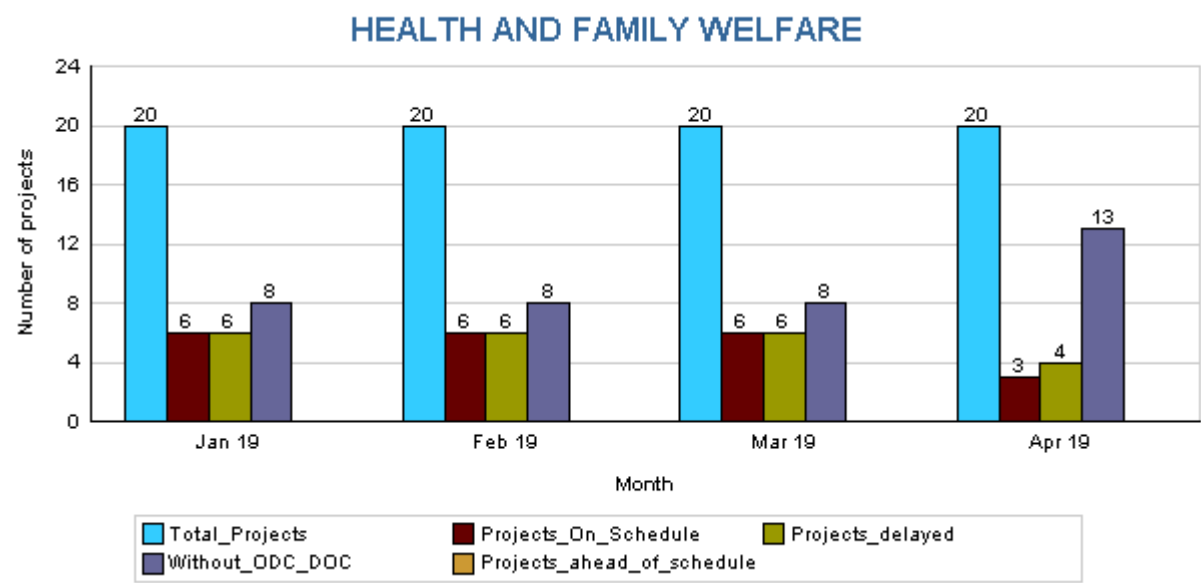


Break-up of 4 Delayed projects in April 2019

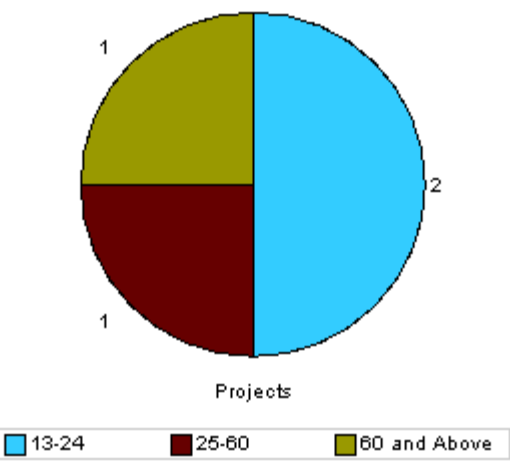

Graphical Presentation of All Projects w.r.t. Original Schedule

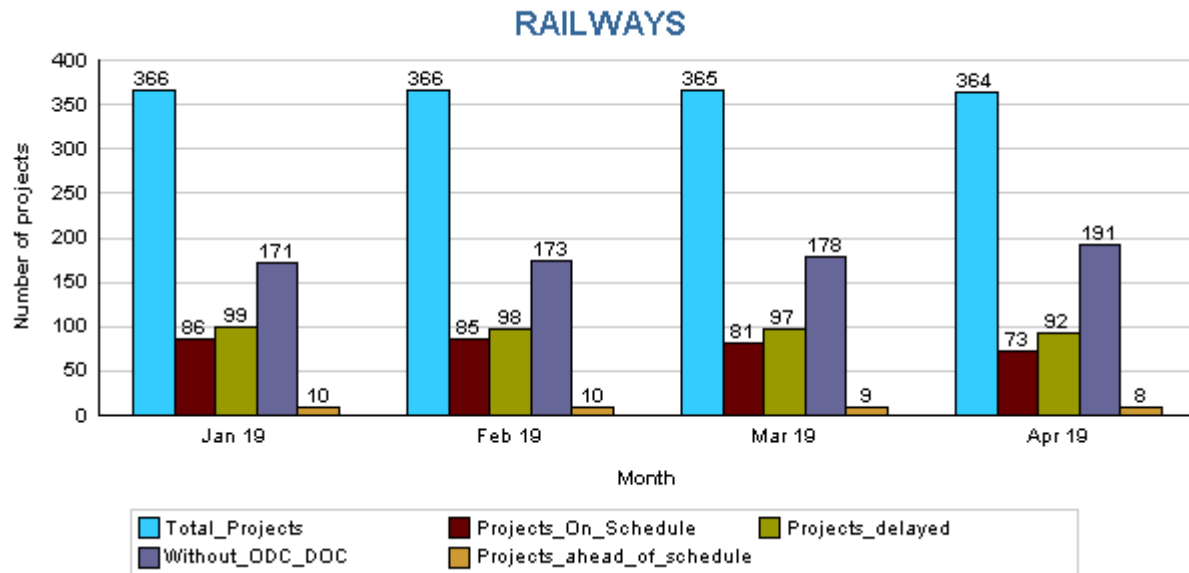


Break-up of 92 Delayed projects in April 2019

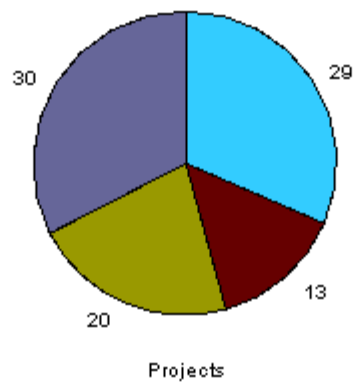


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

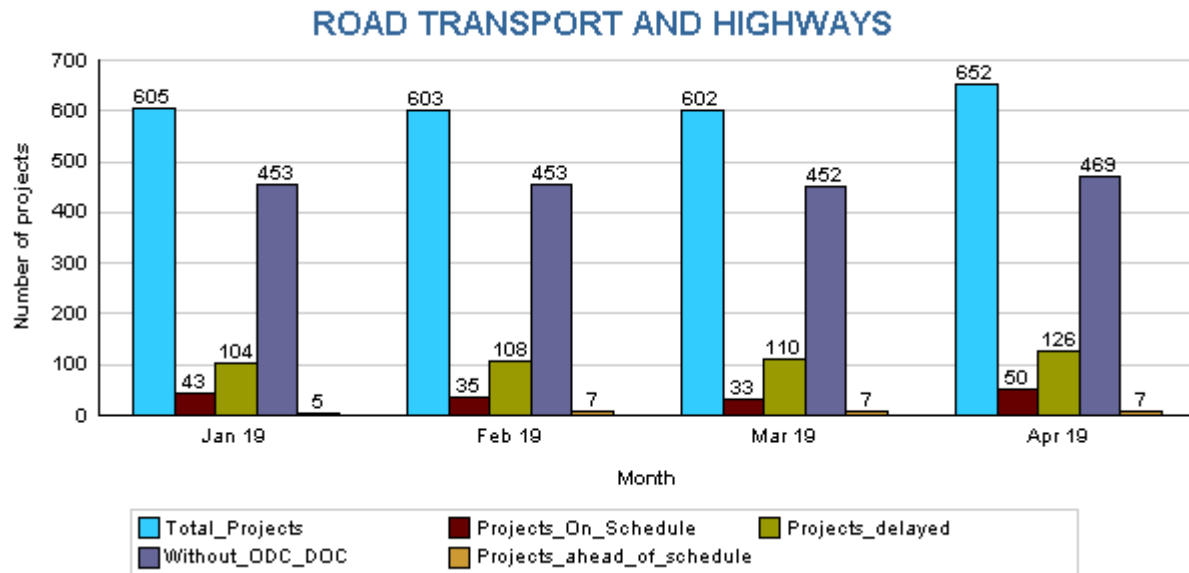


Break-up of 126 Delayed projects in April 2019

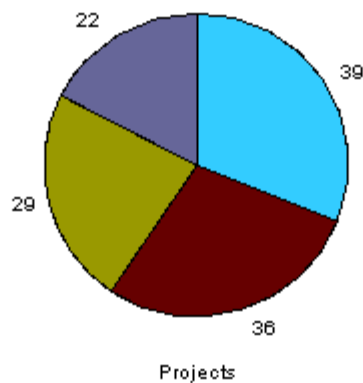


Delay in Months




Graphical Presentation of All Projects w.r.t. Original Schedule

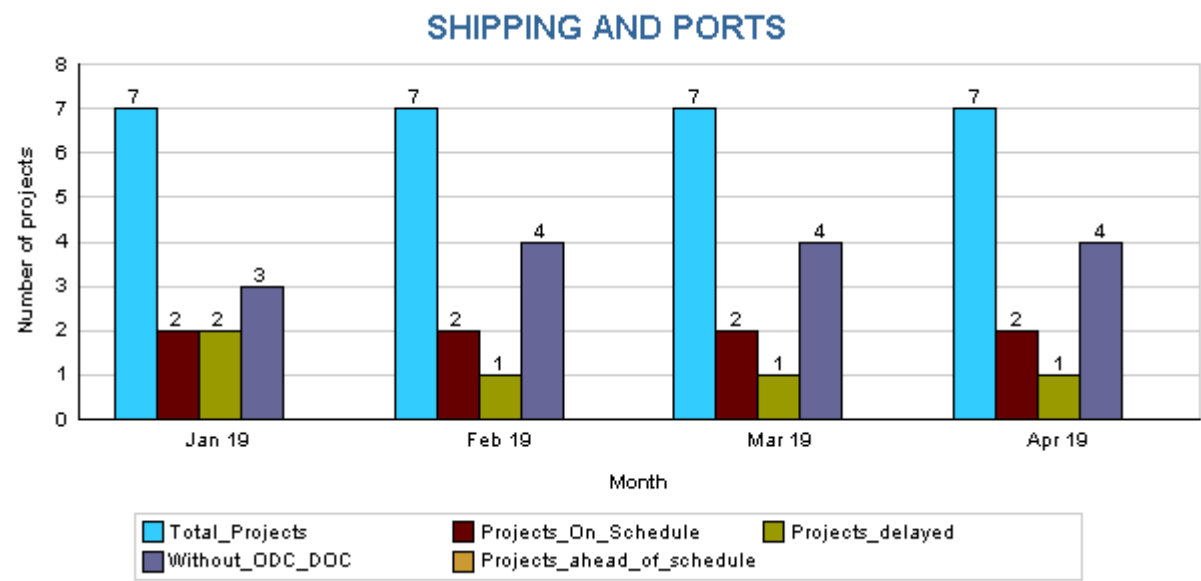


Break-up of 1 Delayed projects in April 2019

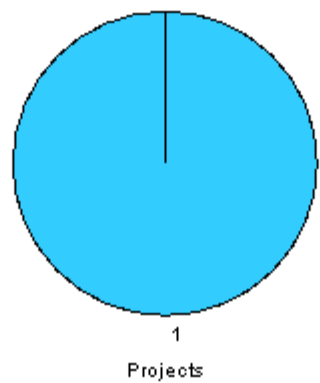


Delay in Months



Graphical Presentation of All Projects w.r.t. Original Schedule

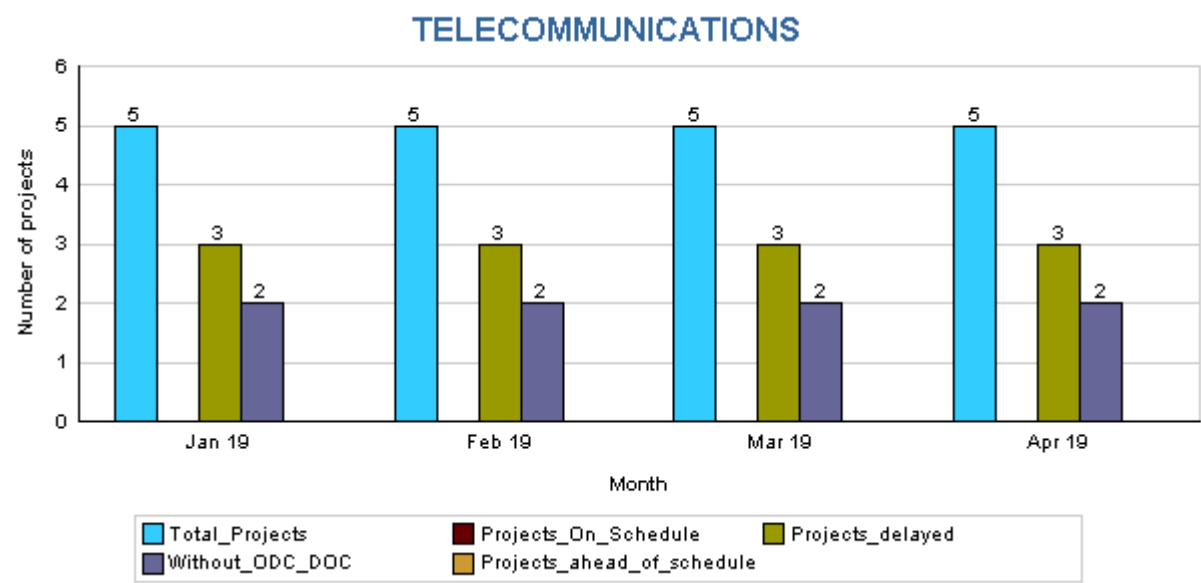


Break-up of 3 Delayed projects in April 2019

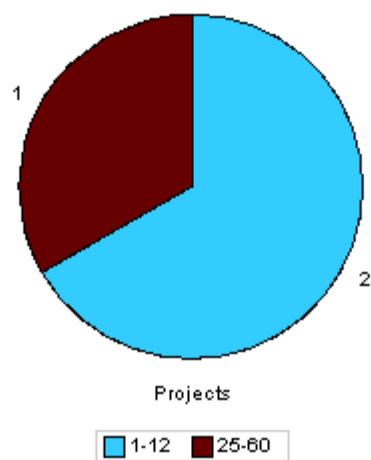


Delay in Months

Graphical Presentation of All Projects w.r.t. Original Schedule

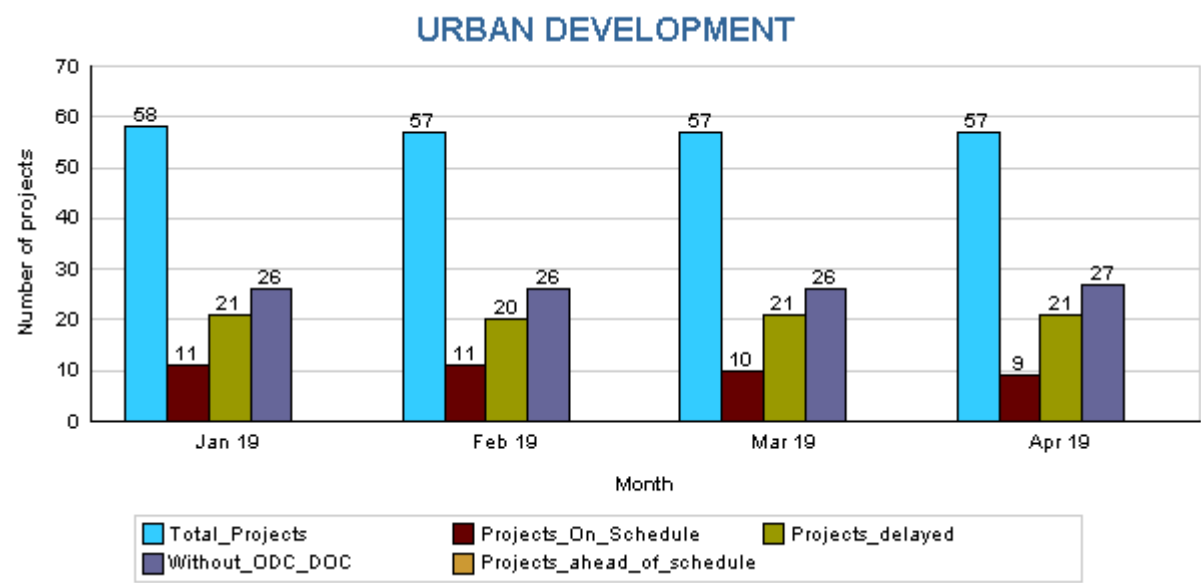


Break-up of 21 Delayed projects in April 2019

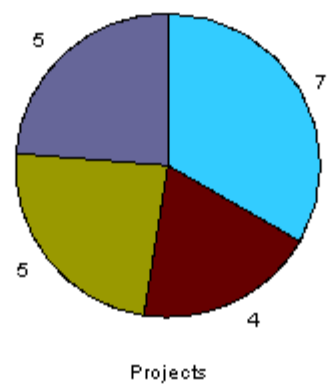

Delay in Months

1-12	13-24	25-60	60 and Above

Graphical Presentation of All Projects w.r.t. Original Schedule

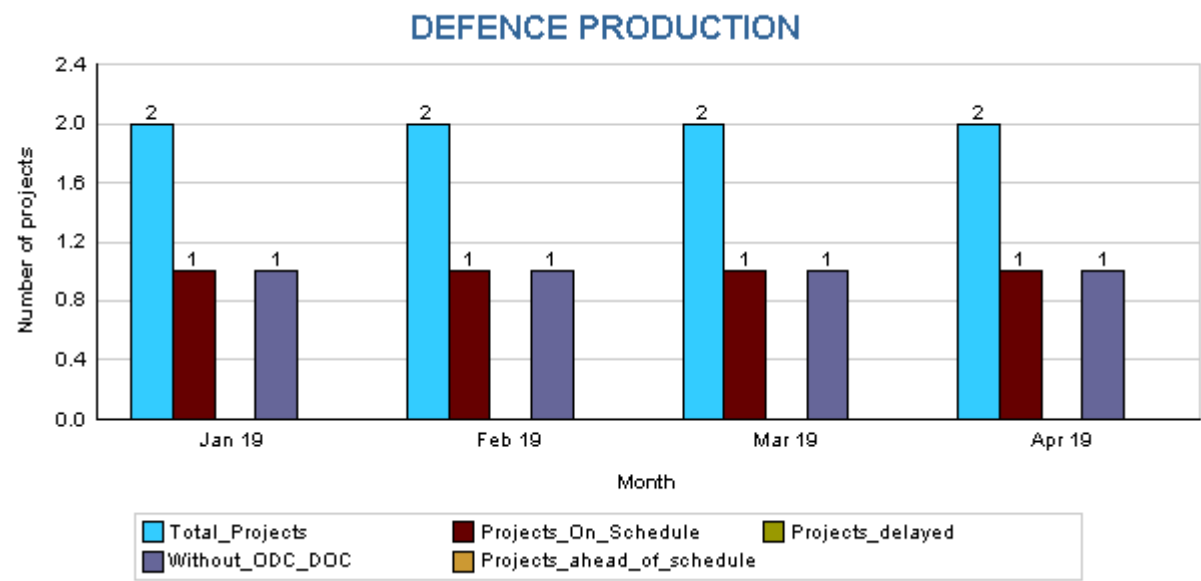

Delay in Months

TABLE-29

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00 16,580.00	16,580.00	13,469.00	12/2015 11/2016	06/2020	54(O) 0	52/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00 -	12,320.00	10,749.00	12/2016 03/2017	12/2020	48(O) 0	40/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00 -	6,840.00	5,771.17	09/2010 -	10/2021	133(O) -	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00 -	39,849.00	13,910.00	11/2020 -	11/2023	36(O) -	23/76
	Total		67,120.00 -	75,589.00	43,899.17				198/301
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21(O) -	0/0
	Total		314.61 -	441.33	85.79				0/0
	<u>COAL</u>								
6	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	2,900.98	03/2023 -	03/2023	0(O) -	14/19
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,057.66	03/2023 -	03/2023	0(O) -	7/21
8	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023	0(O) -	1/12
9	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 -	459.49	203.55	03/2015 -	03/2020	60(O) -	6/10
10	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72(O) -	2/8
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	207.31	03/2014 -	03/2021	84(O) -	0/5
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH ,	11/2009	198.59 -	198.59	169.59	03/2016 -	03/2019	-	7/9
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH ,	04/2012	258.56 -	258.56	172.88	03/2016 -	03/2019	-	4/7
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022	0(O) -	2/10
15	BIJARI OC RCE (1.50 MTY) - [N06000111]SECL,CHHATISGARH ,	05/2014	164.49 -	164.49	80.25	03/2020 -	03/2020	0(O) -	5/9
16	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	51.96	03/2018 -	-	-	1/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
17	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	65.52	03/2020 -	03/2020	0(O) -	1/6
18	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	3.94	03/2023 -	03/2023	0(O) -	1/11
19	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2024	0(O) -	1/5
20	VIJAY WEST OPENCAS PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	75.96	03/2026 -	03/2026	0(O) -	0/1
21	MAHAMAYA OPENCAS PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	9.53	03/2026 -	03/2026	0(O) -	0/1
22	JHIRIA WEST OPENCAS PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	0/1
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND ,	08/2008	706.40 -	706.40	185.62	07/2012 -	03/2022	116(O) -	5/6
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND ,	08/2007	163.51 -	163.51	104.04	03/2011 -	03/2021	120(O) -	4/6
25	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND ,	12/2007	179.87 -	179.87	175.21	03/2012 -	03/2019	-	5/6
26	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND ,	08/2008	264.68 -	264.68	179.16	03/2012 -	03/2021	108(O) -	5/6
27	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND ,	12/2009	510.85 -	510.85	366.52	03/2016 -	03/2021	60(O) -	5/6
28	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND ,	06/2009	162.46 -	162.46	89.30	03/2014 -	03/2021	84(O) -	6/6
29	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	12.08	04/2014 -	10/2018	-	4/7
30	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	344.32	04/2015 -	04/2019	48(O) -	2/6
31	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND ,	02/2012	858.11 -	858.11	185.90	03/2020 -	03/2020	0(O) -	6/7
32	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.24	03/2021 -	03/2021	0(O) -	0/2
33	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND ,	08/2011	988.35 -	988.35	45.26	04/2017 -	-	-	1/3
34	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	228.68	05/2014 -	04/2018	-	0/8
35	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	182.72	04/2014 -	04/2018	-	0/10
36	HURA - C OC (3 MTY) - [N06000143]ECL,JHARKHAND ,	10/2015	359.69 -	359.69	46.93	03/2022 -	03/2022	0(O) -	2/22
37	CHITRA EAST (RCE) OCP - [N06000169]ECL,JHARKHAND ,	08/2018	513.98 -	513.98	78.84	03/2024 -	03/2024	0(O) -	0/16
38	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH ,	08/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021	-24(O) -	3/10
39	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2023	0(O) -	2/9
40	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	115.40	03/2021 -	03/2021	0(O) -	3/10
41	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	47.54	03/2021 -	03/2021	0(O) -	3/8
42	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	.00	03/2022 -	03/2022	0(O) -	1/8

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
43	MALACHUA OPENCAST PROJECT - [N06000139]SECL,MADHYA PRADESH ,	10/2015	488.33 -	488.33	24.29	03/2023 -	03/2023	0(O) -	0/4
44	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	112.35	03/2021 -	03/2021	0(O) -	2/5
45	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	409.87 -	409.87	18.23	03/2022 -	03/2022	0(O) -	0/0
46	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	250.33	03/2021 -	03/2021	0(O) -	0/9
47	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022	0(O) -	0/9
48	PENGANGA OCP(REVISED) - [N06000066]WCL,MAHARASHTRA ,	09/2014	441.82 -	441.82	206.72	03/2020 -	03/2020	0(O) -	8/11
49	DINESH OCP - [N06000118]WCL,MAHARASHTRA ,	11/2014	611.16 -	611.16	409.85	03/2020 -	03/2020	0(O) -	3/8
50	MAKARDHOKRA I OC - [N06000119]WCL,MAHARASHTRA ,	09/2014	266.23 -	266.23	144.38	03/2021 -	03/2021	0(O) -	12/12
51	GOKUL - [N06000120]WCL,MAHARASHTRA ,	11/2014	267.67 -	267.67	208.29	03/2018 -	03/2018	-	7/7
52	BHANEAGAN OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	101.05	03/2023 02/2017	03/2023	0(O) 0	7/11
53	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 -	295.56	115.83	03/2019 -	03/2019	-	10/13
54	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	112.45	03/2020 -	03/2020	0(O) -	6/10
55	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 -	483.69	165.09	03/2021 -	03/2021	0(O) -	2/6
56	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 -	727.28	239.42	03/2025 -	03/2025	0(O) -	5/13
57	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 333.43	333.43	.07	03/2023 03/2024	03/2024	12(O) 0	3/10
58	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA ,	11/2015	277.65 313.34	313.34	37.51	03/2021 09/2018	03/2024	36(O) 0	3/6
59	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]WCL,MAHARASHTRA ,	11/2015	498.42 -	498.42	138.73	03/2020 -	03/2020	0(O) -	2/6
60	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 -	198.68	254.72	03/2019 -	-	-	2/9
61	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 -	304.52	130.28	03/2019 -	03/2019	-	2/8
62	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 -	362.73	279.61	03/2020 -	03/2020	0(O) -	0/0
63	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 -	319.76	58.04	03/2022 -	03/2022	0(O) -	0/3
64	DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	458.07 -	458.07	20.86	03/2022 -	03/2022	0(O) -	1/12
65	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	98.04	03/2021 -	03/2021	0(O) -	1/6
66	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA ,	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120(O) -	10/10
67	BHUBANESWARI OCP MCL (20.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	490.10 -	490.10	467.50	03/2017 -	03/2020	36(O) -	11/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	KANIHA OCP MCL (10.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	457.77 -	457.77	619.13	03/2013 -	03/2022	108(O) -	8/9
69	BALRAM OCP EXTENSION MCL 8.00 MTY - [N06000044]MCL,ODISHA ,	12/2007	172.08 -	172.08	345.12	03/2010 -	03/2022	144(O) -	3/4
70	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	249.61	03/2012 -	03/2021	108(O) -	5/7
71	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	479.53	404.31	03/2013 -	03/2021	96(O) -	6/9
72	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	194.57	03/2019 -	03/2024	60(O) -	2/9
73	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	1,174.58	03/2026 -	03/2026	0(O) -	7/15
74	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL,ODISHA ,	05/2014	337.66 -	337.66	70.05	03/2019 -	03/2021	24(O) -	5/6
75	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL,ODISHA ,	06/2014	289.03 -	289.03	29.93	03/2018 -	03/2020	24(O) -	4/6
76	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	433.20	03/2021 -	03/2021	0(O) -	6/9
77	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	79.92	03/2027 -	03/2027	0(O) -	2/12
78	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,109.33	03/2029 -	03/2029	0(O) -	0/9
79	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.13	09/2019 -	09/2019	0(O) -	0/0
80	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	176.87	12/2019 -	12/2019	0(O) -	0/0
81	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,080.41	7,080.41	6,300.55	12/2015 06/2019	09/2019	45(O) 3	30/35
82	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	430.69	06/2015 09/2019	09/2019	51(O) 0	5/7
83	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA ,	10/2006	249.03 448.86	448.86	203.77	03/2012 03/2024	03/2024	144(O) 0	35/42
84	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA ,	12/2008	453.63 -	453.63	121.91	12/2012 -	-	-	11/44
85	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 489.62	489.62	329.15	03/2012 03/2023	03/2023	132(O) 0	0/2
86	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA ,	03/2010	209.78 -	209.78	156.37	03/2015 03/2019	03/2019	-	30/31
87	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA ,	03/2010	181.19 -	181.19	159.87	03/2012 -	-	-	6/6
88	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 164.04	164.04	104.08	03/2015 03/2021	03/2021	72(O) 0	2/5
89	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 349.28	349.28	2.82	03/2015 03/2021	03/2021	72(O) 0	4/29
90	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 473.22	473.22	417.24	03/2015 03/2021	03/2021	72(O) 0	8/13
91	RG OC -III EXTENSION (PHASE-II) PROJECT - [N06000100]SCCL,TELANGANA ,	06/2012	365.01 -	365.01	192.63	06/2015 03/2019	03/2019	-	35/36
92	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 384.32	384.32	75.36	07/2016 -	03/2020	44(O) -	24/28
93	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 415.37	415.37	175.42	03/2016 03/2019	03/2020	48(O) 12	38/39

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
94	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 442.42	442.42	68.57	03/2019 03/2019	03/2020	12(O) 12	15/18
95	KOYAGUDEM OPENCAS PROJECT - [N06000146]SCCL,TELANGANA , Central Sector Projects	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24(O) -	0/9
96	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]SCCL,TELANGANA ,	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020	0(O) -	5/17
97	KAKATIYAKHANI OPENCAS III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	50.72	03/2019 -	03/2022	36(O) -	1/11
98	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	5,982.50	11/2021 -	11/2021	0(O) -	0/0
99	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	602.86 -	602.86	307.30	03/2022 -	03/2022	0(O) -	9/13
100	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	434.55	03/2018 -	03/2020	24(O) -	11/16
101	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	2,661.73	215.58	08/2019 -	-	-	0/19
102	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	.00	03/2026 -	03/2026	0(O) -	0/21
103	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	.00	03/2029 -	03/2029	0(O) -	0/22
	Total		99,419.73 -	99,873.07	33,228.20				523/1062
	<u>FERTILISERS</u>								
104	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	67.89	11/2019 -	11/2019	0(O) -	0/2
105	NEW SEWAGE TREATMENT PLANT PACKAGE RCF TROMBAY - [N08000009]RCF,MAHARASHTRA ,	10/2014	197.79 209.44	209.44	161.24	11/2016 04/2019	05/2019	30(O) 1	1/13
106	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	70.98	04/2020 -	04/2020	0(O) -	1/14
107	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	69.23	11/2019 -	11/2019	0(O) -	0/2
108	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	69.08	11/2019 -	11/2019	0(O) -	0/2
	Total		1,299.07 -	1,310.72	438.42				2/33
	<u>MINES</u>								
109	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 5,540.00	5,540.00	96.98	04/2021 04/2021	04/2021	0(O) 0	3/3
110	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 534.00	534.00	315.25	01/2020 01/2020	01/2020	0(O) 0	1/2
111	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020	0(O) -	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
112	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	.00	04/2021 04/2021	04/2021	0(O) 0	1/1
113	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 -	166.62	134.98	06/2019 -	06/2019	0(O) -	1/1
	Total		7,078.62 -	7,078.62	579.13				8/9
	<u>STEEL</u>								
114	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH ,	12/2009	343.00 -	488.40	249.30	10/2016 -	03/2020	41(O) -	1/2
115	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,500.00	1,207.76	12/2017 -	09/2019	21(O) -	5/6
116	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH ,	08/2015	320.66 -	320.66	190.91	08/2018 -	06/2019	10(O) -	2/4
117	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH ,	07/2015	465.85 -	465.85	382.25	07/2018 -	06/2019	11(O) -	4/4
118	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH ,	04/2014	188.93 -	188.93	132.20	04/2015 -	-	-	4/5
119	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 -	22,542.00	15,401.64	05/2015 10/2019	10/2019	53(O) 0	64/86
120	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]NMDC,CHHATISGARH ,	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020	0(O) -	5/12
121	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	423.33	10/2017 -	06/2020	32(O) -	0/2
122	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND ,	05/2015	1,154.18 -	1,154.18	910.60	12/2017 -	06/2019	18(O) -	1/2
123	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND ,	02/2014	4,749.00 -	4,749.00	109.06	09/2017 -	-	-	0/0
124	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	84.26	06/2019 -	06/2020	12(O) -	0/1
125	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA ,	04/2015	3,127.30 -	3,127.30	2,749.95	04/2018 -	05/2019	13(O) -	3/3
126	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	1,682.85	1,094.53	09/2018 -	06/2019	9(O) -	4/5
127	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	.00	09/2020 -	09/2020	0(O) -	0/4
	Total		32,793.01 -	39,597.41	22,967.39				93/136
	<u>PETROLEUM</u>								
128	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 -	20,928.00	4,501.16	07/2020 -	07/2020	0(O) -	81/111
129	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]HPCL,ANDHRA PRADESH ,	09/2016	407.00 -	407.00	328.48	09/2019 -	09/2019	0(O) -	24/27

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
130	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	34,012.00	2,465.32	06/2020 08/2021	08/2021	14(O) 0	15/20
131	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH ,	01/2015	342.00 -	342.00	.00	03/2021 -	03/2021	0(O) -	0/0
132	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH ,	07/2014	247.00 -	247.00	.00	03/2021 -	03/2021	0(O) -	0/0
133	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003 NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH ,	04/2017	420.76 -	420.76	105.21	09/2018 04/2019	04/2019	7(O) 0	3/5
134	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	66.38	04/2021 -	04/2021	0(O) -	0/0
135	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	5.39	04/2021 -	07/2021	3(O) -	0/0
136	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	8.03	04/2022 -	02/2023	10(O) -	0/0
137	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	12.16	10/2021 -	10/2021	0(O) -	0/0
138	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM ,	03/2009	2,465.15 -	2,378.86	2,132.88	03/2013 12/2019	12/2019	81(O) 0	6/15
139	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM ,	06/2010	202.94 341.70	330.35	129.67	01/2014 11/2019	11/2019	70(O) 0	6/7
140	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	423.00	256.37	08/2019 -	09/2019	1(O) -	5/13
141	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]IOCL,ASSAM ,	02/2016	2,582.00 -	2,582.00	1,451.96	11/2019 -	11/2019	0(O) -	13/17
142	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 249.85	244.70	145.01	05/2020 05/2020	05/2020	0(O) 0	4/5
143	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM ,	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8(O) -	0/0
144	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]IOCL,ASSAM ,	05/2018	1,222.00 -	1,222.00	403.95	09/2019 -	09/2019	0(O) -	6/7
145	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 -	682.90	2.40	02/2020 -	02/2020	0(O) -	1/14
146	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	86.47	02/2020 -	02/2020	0(O) -	1/5
147	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM ,	09/2012	871.35 -	1,200.00	565.63	03/2015 -	-	-	0/5
148	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR ,	07/2015	822.66 -	822.66	822.02	11/2018 -	06/2019	7(O) -	8/8
149	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]IOCL,BIHAR ,	05/2016	664.00 -	664.00	528.48	12/2020 -	02/2020	-10(O) -	4/5
150	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]IOCL,BIHAR ,	09/2015	324.00 -	324.00	143.56	06/2020 -	06/2020	0(O) -	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
151	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	.00	03/2021 -	03/2021	0(O) -	10/26
152	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	51.40	10/2020 -	10/2020	0(O) -	2/2
153	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	52.16	10/2022 -	10/2022	0(O) -	0/0
154	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	4.55	01/2021 -	01/2021	0(O) -	2/8
155	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	16.56	03/2021 -	03/2021	0(O) -	0/0
156	FUEL QUALITY UPGRADATION (NSU NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]IOCL,BIHAR ,	06/2017	951.64 -	951.64	246.28	10/2019 -	10/2019	0(O) -	9/11
157	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATISGARH ,	12/2016	300.00 -	300.00	.00	04/2021 -	04/2021	0(O) -	0/0
158	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI ,	08/2014	6,086.08 5,842.31	5,842.31	4,778.58	05/2019 10/2019	10/2019	5(O) 0	13/14
159	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	141.46	04/2018 -	03/2019	-	18/20
160	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 1,162.56	1,162.56	338.79	03/2026 03/2026	03/2026	0(O) 0	7/10
161	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]IOCL,GUJARAT , Central Sector Projects	09/2016	208.35 -	208.35	96.96	07/2020 -	07/2020	0(O) -	10/10
162	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT , Central Sector Projects	10/2014	279.00 -	279.00	200.05	08/2018 -	-	-	0/0
163	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]IOCL,GUJARAT ,	03/2018	3,380.00 -	3,380.00	1,683.93	09/2019 -	09/2019	0(O) -	7/9
164	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	27.50	02/2020 10/2020	10/2020	8(O) 0	4/8
165	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 -	588.20	.00	- -	-	-	6/17
166	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 -	225.54	.00	02/2021 -	02/2021	0(O) -	2/8
167	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]HPCL,HARYANA ,	11/2017	255.00 -	255.00	47.50	11/2020 -	11/2020	0(O) -	18/46
168	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 -	206.63	5.53	02/2020 -	02/2020	0(O) -	3/6
169	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]IOCL,HARYANA ,	12/2017	3,529.00 -	3,529.00	1,238.56	07/2019 -	07/2019	0(O) -	7/9
170	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	144.71	08/2020 -	08/2020	0(O) -	3/6
171	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	9.93	01/2021 -	01/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
172	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	13.67	02/2020 -	02/2020	0(O) -	3/4
173	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 -	286.42	.00	08/2020 -	08/2020	0(O) -	5/16
174	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH ,	02/2016	151.00 -	151.00	139.69	09/2019 -	02/2019	-	4/4
175	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND ,	04/2011	191.96 -	191.96	176.28	05/2015 -	-	-	8/12
176	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	658.62 910.23	910.23	237.35	03/2023 03/2022	03/2022	-12(O) 0	6/10
177	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	17.78	06/2020 -	06/2020	0(O) -	0/0
178	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	39.19	10/2022 -	10/2022	0(O) -	9/17
179	CITY GAS DISTRIBUTION (CGD) NETWORK JAMSHEDPUR - [N16000330]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	36.75	10/2022 -	10/2022	0(O) -	0/0
180	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPR,KARNATAKA ,	01/2006	993.00 -	1,693.00	1,549.85	01/2012 -	-	-	0/0
181	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA , Central Sector Projects	02/2015	749.00 -	842.00	860.14	02/2020 -	02/2020	0(O) -	0/0
182	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RU - [N16000255]MANGALORE REFIN,KARNATAKA ,	05/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019	0(O) -	8/8
183	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA ,	10/2015	135.00 171.00	170.70	132.43	03/2019 -	05/2019	2(O) -	11/11
184	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	176.25	12/2019 -	02/2020	2(O) -	8/9
185	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 -	581.00	.00	03/2020 -	03/2020	0(O) -	2/3
186	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	.00	03/2021 -	03/2021	0(O) -	0/0
187	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 714.25	714.25	354.58	10/2017 -	03/2019	-	39/52
188	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	2,868.71	08/2018 11/2019	11/2019	15(O) 0	0/20
189	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL,KERALA ,	02/2016	3,313.00 3,288.96	3,288.96	718.31	02/2020 10/2020	10/2020	8(O) 0	0/20
190	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019	0(O) -	0/0
191	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	12.63	03/2023 -	03/2023	0(O) -	0/0
192	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 -	236.00	16.55	06/2020 -	08/2020	2(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
193	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,577.15	1,577.15	1,240.37	05/2013 03/2019	12/2019	79(O) 0	4/8
194	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA ,	12/2011	2,059.63 2,665.65	2,665.65	1,906.55	03/2015 12/2019	12/2019	57(O) 0	14/18
195	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA ,	11/2014	6,068.80 6,068.80	5,296.93	4,731.48	04/2019 12/2019	12/2019	8(O) 0	8/9
196	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA ,	08/2015	2,818.88 -	2,818.88	2,073.56	03/2019 05/2020	05/2020	14(O) 0	4/5
197	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA , Central Sector Projects	01/2015	4,619.94 4,619.94	4,619.94	4,255.37	12/2017 03/2020	03/2020	27(O) 0	4/5
198	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 -	3,247.19	2,167.85	04/2018 05/2020	05/2020	25(O) 0	13/15
199	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	834.52	08/2021 -	08/2021	0(O) -	4/5
200	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]BPCL,MAHARASHTRA ,	02/2016	554.00 -	554.00	260.09	02/2020 -	02/2020	0(O) -	0/10
201	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA ,	04/2013	449.58 -	449.58	142.34	12/2019 -	12/2019	0(O) -	0/17
202	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	20.65	01/2021 -	04/2021	3(O) -	0/0
203	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 -	348.00	14.73	01/2021 -	10/2021	9(O) -	0/0
204	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	20.36	01/2021 -	01/2021	0(O) -	0/0
205	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA ,	09/2015	4,199.00 -	4,199.00	194.97	03/2020 -	07/2019	-8(O) -	104/135
206	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]ONGC,MAHARASHTRA , Central Sector Projects	01/2017	474.15 474.15	474.15	346.77	05/2019 05/2019	05/2019	0(O) 0	5/5
207	DEVELOPMENT OF B-147 FIELD - [N16000292]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	546.15 546.15	546.15	366.12	11/2019 11/2019	11/2019	0(O) 0	4/5
208	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	511.30 511.30	511.30	358.81	11/2019 11/2019	11/2019	0(O) 0	4/5
209	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]ONGC,MAHARASHTRA , Central Sector Projects	02/2017	968.61 968.61	968.61	815.29	11/2019 11/2019	11/2019	0(O) 0	4/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
210	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,006.83	4,006.83	2,354.21	05/2021 05/2021	05/2021	0(0) 0	11/15
211	PUNE POL STORAGE DEPOT - [N16000313]BPCL,MAHARASHTRA ,	08/2016	282.64 -	282.64	88.28	08/2020 -	08/2020	0(0) -	0/15
212	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	58.33	06/2020 -	06/2020	0(0) -	0/0
213	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]ONGC,MAHARASHTRA ,	04/2018	766.37 -	766.37	345.40	12/2019 -	12/2019	0(0) -	4/5
214	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE ,	03/2015	3,957.00 3,561.00	3,397.00	2,543.54	12/2018 -	05/2019	5(0) -	39/39
215	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE ,	06/2007	736.65 -	571.47	543.05	09/2011 -	-	-	3/3
216	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE ,	08/2009	1,793.00 -	1,793.00	1,788.86	12/2016 -	-	-	8/8
217	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE ,	12/2009	309.81 723.40	723.40	645.53	10/2014 08/2019	08/2019	58(0) 0	34/40
218	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE ,	07/2011	352.56 -	438.84	220.73	03/2017 -	12/2019	33(0) -	2/15
219	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	670.40	12/2020 -	12/2020	0(0) -	4/5
220	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	1,393.27	12/2020 -	08/2020	-4(0) -	4/5
221	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]IOCL,MULTI STATE ,	02/2015	890.00 -	887.00	591.29	10/2019 -	06/2019	-4(0) -	5/6
222	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	236.57	07/2018 10/2020	10/2020	27(0) 0	23/36
223	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]HPCL,MULTI STATE ,	09/2016	1,879.00 -	1,879.00	1,308.78	06/2020 -	06/2020	0(0) -	18/24
224	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	63.20	10/2020 -	10/2020	0(0) -	6/12
225	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	112.73	12/2019 -	12/2019	0(0) -	6/22
226	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,162.20	12/2020 12/2020	12/2020	0(0) 12	19/24
227	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	1,168.02	12/2020 -	12/2020	0(0) -	16/24
228	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 -	3,437.00	1,177.26	12/2020 -	12/2020	0(0) -	17/24
229	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 3,030.00	3,049.47	2,112.19	12/2012 02/2019	02/2022	110(0) 29	18/42

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
230	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	2,677.00	358.80	03/2021 -	03/2021	0(O) -	8/26
231	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE ,	11/2015	500.00 -	500.00	.00	06/2017 -	-	-	0/0
232	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 -	3,308.00	192.71	12/2021 -	12/2021	0(O) -	10/20
233	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA ,	03/2014	3,150.00 -	3,150.00	2,589.31	09/2017 06/2019	06/2019	21(O) 2	6/6
234	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	967.24	12/2020 -	12/2020	0(O) -	18/24
235	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL,ODISHA ,	05/2016	429.00 -	429.00	290.69	01/2019 12/2019	12/2019	11(O) 0	6/6
236	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	34.33	12/2019 -	12/2019	0(O) -	17/26
237	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 243.53	243.53	45.20	07/2022 -	07/2022	0(O) -	0/0
238	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	108.80	12/2021 -	12/2021	0(O) -	2/3
239	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	181.20	25.90	07/2022 -	07/2022	0(O) -	0/0
240	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	235.99	10/2021 -	10/2021	0(O) -	2/10
241	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]BPCL,ODISHA ,	08/2017	750.00 -	750.00	29.15	12/2020 -	12/2020	0(O) -	0/14
242	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	7.01	10/2021 -	10/2021	0(O) -	0/1
243	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN ,	11/2011	310.00 -	370.00	17.84	03/2013 -	-	-	0/24
244	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	69.19	- -	03/2021	-	5/26
245	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	06/2020	0(O) -	0/0
246	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU ,	03/2013	3,110.36 -	3,110.36	2,915.42	11/2015 -	-	-	52/52
247	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 -	678.00	5.53	02/2017 -	-	-	0/0
248	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	390.52 390.52	390.52	221.40	03/2019 -	05/2020	14(O) -	4/5
249	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	428.96	12/2018 -	02/2021	26(O) -	4/5
250	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	5.79	06/2020 -	06/2020	0(O) -	4/5
251	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	757.22	12/2019 -	12/2019	0(O) -	0/0
252	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	421.00	62.32	08/2020 -	08/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
253	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	4.04	10/2020 -	08/2021	10(O) -	0/0
254	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022	0(O) -	0/0
255	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 -	287.49	117.30	04/2022 -	04/2022	0(O) -	32/43
256	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	30.32	08/2021 -	11/2021	3(O) -	0/0
257	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]IOCL,UTTAR PRADESH ,	01/2018	666.64 -	666.64	323.69	09/2019 -	09/2019	0(O) -	5/6
258	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	.31	08/2020 -	08/2020	0(O) -	1/1
259	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	8.18	12/2021 -	12/2021	0(O) -	2/3
260	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH ,	03/2014	204.00 -	204.00	.00	09/2019 -	09/2019	0(O) -	0/6
261	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	32.67	02/2020 -	10/2020	8(O) -	18/26
262	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL,WEST BENGAL ,	03/2015	694.00 1,097.54	694.00	568.96	10/2018 06/2019	06/2019	8(O) 0	0/15
263	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL ,	04/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020	0(O) -	0/0
264	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	60.93	12/2020 -	12/2020	0(O) -	12/24
265	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL ,	04/2017	163.02 -	163.02	39.00	04/2020 -	03/2021	11(O) -	17/26
266	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]IOCL,WEST BENGAL ,	05/2018	2,934.40 -	2,934.40	1,252.80	09/2019 -	09/2019	0(O) -	10/11
267	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL,WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	31.02	09/2022 -	06/2021	-15(O) -	1/1
	Total		2,29,497.78 -	2,34,857.89	80,994.92				1049/1690
	POWER								
268	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH ,	09/2003	6,285.33 -	19,496.34	10,723.47	09/2010 -	-	-	0/0
269	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH ,	12/2004	2,496.90 7,419.34	7,419.34	7,131.10	12/2009 06/2019	06/2019	114(O) 0	30/30
270	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR ,	02/2005	8,692.97 15,095.67	15,095.67	15,932.41	10/2011 08/2021	08/2021	118(O) 0	26/47
271	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR ,	01/2007	5,353.00 -	7,998.00	7,128.72	07/2012 -	05/2019	82(O) -	12/25

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
272	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR , Joint Venture	01/2013	12,964.60 -	13,731.26	12,695.00	05/2018 -	05/2020	24(O) -	33/45
273	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN,BIHAR ,	05/2015	436.68 533.50	602.44	557.22	12/2016 -	05/2019	29(O) -	16/19
274	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR ,	04/2016	790.13 790.30	790.30	530.54	06/2019 06/2019	06/2019	0(O) 0	0/0
275	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH ,	12/2012	11,846.00 -	12,739.82	11,850.13	10/2017 03/2020	03/2020	29(O) 0	35/41
276	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,420.87	11/2019 -	11/2019	0(O) -	0/0
277	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI ,	03/2015	1,394.52 1,394.52	1,394.52	338.19	05/2017 06/2019	12/2019	31(O) 6	4/9
278	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT ,	11/2016	330.00 -	330.00	330.23	11/2017 -	04/2019	17(O) -	4/4
279	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT , Central Sector Projects	05/2017	175.64 175.64	175.64	83.54	09/2018 09/2019	09/2019	12(O) 0	0/0
280	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPAT AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT ,	12/2017	193.14 193.14	193.14	24.40	06/2019 09/2019	09/2019	3(O) 0	0/0
281	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 -	9,394.80	7,244.66	09/2009 -	12/2021	147(O) -	3/5
282	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	1,086.32	04/2020 -	12/2023	44(O) -	0/0
283	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND ,	02/2014	14,366.58 -	15,164.05	8,617.47	06/2019 09/2021	09/2021	27(O) 0	22/23
284	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,152.58	10/2017 -	-	-	0/0
285	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA ,	01/2012	15,166.19 -	16,934.65	15,364.00	01/2017 -	-	-	48/48
286	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 445.89	445.89	258.66	02/2019 12/2019	09/2019	7(O) 3	0/0
287	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH ,	03/2013	11,638.55 -	12,865.92	11,086.44	01/2018 03/2020	03/2020	26(O) 0	39/42
288	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC,MADHYA PRADESH ,	03/2015	9,870.51 -	11,148.86	7,697.03	01/2020 01/2020	01/2020	0(O) 0	32/39
289	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 1,587.16	1,587.16	296.17	09/2020 -	09/2020	0(O) -	9/16
290	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA ,	12/2007	477.69 738.48	738.48	689.46	09/2010 04/2019	04/2019	103(O) 0	5/8
291	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA ,	03/2012	7,921.47 -	7,921.47	5,302.00	09/2016 -	-	-	41/41
292	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA ,	03/2012	9,395.18 -	9,395.18	9,363.22	01/2017 03/2019	03/2019	-	39/39
293	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 5,071.94	5,071.94	4,554.87	10/2012 12/2019	12/2019	86(O) 0	8/11

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
294	NORTH- EAST NORTH WESTERN INTERCONNECTOR PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,733.20	08/2013 03/2022	03/2022	103(O) 0	23/26
295	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 639.46	639.46	518.50	06/2014 09/2019	09/2019	63(O) 3	10/12
296	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 1,891.41	1,891.41	1,230.98	04/2016 08/2019	08/2019	40(O) 0	8/12
297	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 374.63	374.63	187.24	04/2016 12/2017	06/2019	38(O) 0	0/0
298	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE ,	02/2014	539.82 575.67	575.67	426.83	06/2016 09/2019	05/2019	35(O) 1	9/11
299	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	447.83	11/2016 12/2019	12/2019	37(O) 0	8/12
300	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 5,151.37	5,151.37	3,063.80	03/2018 12/2019	12/2019	21(O) 0	9/12
301	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE ,	02/2014	196.58 225.28	225.28	152.32	02/2016 04/2019	05/2019	39(O) 1	16/17
302	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE ,	01/2015	268.80 340.88	340.88	248.10	03/2018 03/2019	05/2019	14(O) 1	1/3
303	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 871.62	871.62	496.12	10/2017 09/2019	09/2019	23(O) 0	0/5
304	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 260.03	260.03	188.36	07/2017 06/2019	06/2019	23(O) 0	3/5
305	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	74.71	03/2018 03/2018	05/2019	14(O) 0	0/0
306	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 808.63	808.63	458.26	01/2018 12/2019	12/2019	23(O) 0	0/0
307	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 3,519.59	3,519.59	2,215.60	05/2019 05/2019	09/2019	4(O) 4	0/0
308	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 14,733.37	14,733.37	6,580.05	11/2019 11/2019	11/2019	0(O) 0	0/0
309	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE ,	09/2016	562.25 562.25	562.25	195.50	03/2019 03/2019	05/2019	2(O) 1	0/0
310	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE ,	03/2017	251.60 251.60	251.60	167.81	06/2019 06/2019	06/2019	0(O) 0	0/0
311	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 283.72	283.72	164.25	11/2019 11/2019	11/2019	0(O) 0	0/0
312	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 408.46	408.46	221.54	01/2019 09/2019	09/2019	8(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
313	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 608.24	608.24	388.00	04/2019 04/2019	05/2019	1(O) 1	0/0
314	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL,MULTI STATE ,	02/2017	195.05 195.05	195.05	109.10	02/2020 02/2020	02/2020	0(O) 0	0/0
315	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 322.30	322.30	127.38	02/2019 06/2019	06/2019	4(O) 0	0/0
316	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 235.53	235.53	84.89	06/2019 06/2019	06/2019	0(O) 0	0/0
317	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 379.85	379.95	28.42	12/2019 12/2019	12/2019	0(O) 0	0/0
318	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 5,070.13	5,070.13	1,773.41	04/2020 04/2020	04/2020	0(O) 0	0/0
319	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE ,	03/2017	337.75 337.75	337.75	35.50	06/2019 06/2019	06/2019	0(O) 0	0/0
320	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 4,754.42	9,072.36	1,083.08	12/2018 12/2018	12/2019	12(O) 0	0/0
321	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 5,111.33	6,880.36	1,143.65	12/2018 12/2018	12/2020	24(O) 0	0/0
322	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,130.07	04/2019 -	06/2019	2(O) -	0/0
323	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,500.00	1,051.50	07/2020 -	07/2020	0(O) -	0/0
324	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 1,931.39	1,931.39	810.69	02/2020 02/2020	02/2020	0(O) 0	0/0
325	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 198.49	198.49	41.70	09/2019 02/2020	02/2020	5(O) 0	0/0
326	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 358.83	358.83	5.00	05/2020 05/2020	05/2020	0(O) 0	0/0
327	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC,ODISHA ,	02/2014	12,532.44 -	13,740.53	9,101.85	12/2018 02/2020	02/2020	14(O) 0	33/38
328	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA ,	04/2016	844.64 844.64	844.64	341.30	04/2019 04/2019	06/2019	2(O) 2	0/0
329	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN ,	07/2016	1,429.38 1,429.38	1,429.38	916.66	01/2019 07/2019	06/2019	5(O) 1	0/0
330	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU ,	05/2005	1,779.29 2,187.32	2,187.32	2,133.02	11/2008 06/2019	05/2019	126(O) 1	20/22

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
331	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 186.17	186.17	80.77	07/2019 07/2019	07/2019	0(0) 0	0/0
332	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 -	10,598.98	4,370.06	11/2020 02/2021	02/2021	3(0) 0	23/23
333	FGUTPP UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC,UTTAR PRADESH ,	07/2013	3,363.12 -	3,363.12	2,244.00	12/2016 -	-	-	28/28
334	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC,UTTAR PRADESH ,	09/2014	9,188.98 -	9,188.98	5,961.47	07/2019 03/2020	03/2020	8(0) 0	32/35
335	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH ,	05/2011	195.42 294.60	294.60	257.04	02/2014 02/2018	10/2019	68(0) 0	7/8
336	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH , Joint Venture	04/2012	9,750.89 -	9,750.89	8,893.00	02/2018 -	08/2019	18(0) -	33/40
337	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	.00	09/2023 -	09/2023	0(0) -	0/0
338	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 2,978.86	5,024.35	2,809.51	02/2016 05/2021	06/2022	76(0) 0	16/30
339	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 -	3,846.30	3,938.20	03/2013 12/2020	12/2020	93(0) 0	6/15
340	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 -	4,105.30	1,608.70	06/2013 -	12/2022	114(0) -	10/13
341	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.16	08/2017 -	-	-	0/15
342	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	648.33	207.87	12/2021 -	12/2021	0(0) -	3/32
343	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.84	429.14	09/2019 02/2022	02/2022	29(0) 0	5/9
344	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 454.11	454.11	270.92	04/2018 01/2020	01/2020	21(0) 0	0/0
	Total		2,87,073.06 -	3,45,343.53	2,26,754.76				709/915
	<u>HEAVY INDUSTRY</u>								
345	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019	0(0) -	0/0
346	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 -	3,827.30	2,289.00	09/2011 -	-	-	23/25
	Total		3,272.00 -	5,381.30	2,624.03				23/25
	<u>HEALTH AND FAMILY WELFARE</u>								
347	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS-MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.19	111.92	03/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
348	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	96.75	- -	02/2020	- -	0/0
349	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	113.50	12/2014 -	-	-	0/0
350	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	875.00	174.00	05/2021 -	05/2021	0(O) -	0/0
351	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83(O) -	0/0
352	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	204.44	176.22	05/2017 -	07/2019	26(O) -	2/2
353	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	293.65	282.43	05/2017 -	-	-	3/5
354	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	156.65	54.94	- -	02/2020	- -	0/0
355	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.01	46.28	- -	05/2020	- -	0/0
356	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	523.00	508.29	03/2018 -	-	-	1/2
357	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	125.36	03/2019 -	-	-	0/0
358	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	61.17	- -	02/2020	- -	0/0
359	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	145.51	05/2018 -	09/2019	16(O) -	0/0
360	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	152.95	95.16	02/2018 -	06/2019	16(O) -	1/1
361	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	703.00	272.00	06/2020 -	06/2020	0(O) -	0/0
362	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	68.33	- -	04/2020	- -	0/0
363	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	785.00	39.35	04/2020 -	04/2020	0(O) -	0/0
364	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	244.00	247.47	09/2018 -	-	-	0/0
365	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	122.43	03/2019 -	-	-	0/0
366	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL , Central Sector Projects	04/2018	651.99 -	651.99	58.04	- -	02/2020	- -	0/0
	Total		8,129.23 -	8,246.52	2,946.15				7/10
	<u>RAILWAYS</u>								
367	NANDYAL-YERRAGUNTALA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
368	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	289.91	03/2009 -	03/2023	168(O) -	0/0
369	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH ,	07/2006	732.81 -	1,993.00	2,121.12	03/2008 -	03/2020	144(O) -	0/0
370	GUDUR-DURGARAJPATNAM - [N22000265]SCR,ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	-	-	-	0/0
371	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH ,	04/2013	829.00 -	1,599.39	.94	-	-	-	1/1
372	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH ,	04/2011	2,288.70 -	2,288.70	506.48	03/2021 -	03/2022	12(O) -	0/1
373	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH ,	03/2012	1,503.71 -	1,503.71	36,195.04	03/2020 -	03/2022	24(O) -	0/0
374	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.07	-	-	-	0/0
375	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH ,	04/2016	3,631.00 -	3,631.00	305.25	03/2022 -	03/2023	12(O) -	0/0
376	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.67	633.52	12/2023 -	12/2023	0(O) -	0/0
377	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	209.89	03/2022 -	03/2022	0(O) -	0/0
378	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH ,	01/2013	387.70 -	387.70	323.91	03/2018 -	-	-	0/0
379	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH ,	08/2016	234.50 -	235.00	5.59	03/2019 -	12/2020	21(O) -	0/0
380	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR,ASSAM ,	09/2006	385.20 -	1,532.00	581.00	03/2019 -	03/2020	12(O) -	0/0
381	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM ,	04/2011	314.00 486.96	551.00	660.21	03/2019 -	03/2019	-	0/0
382	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM ,	04/2012	246.07 614.81	398.93	413.64	03/2019 -	03/2019	-	0/0
383	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM ,	04/2015	2,232.32 -	2,182.00	475.48	03/2022 -	03/2020	-24(O) -	0/0
384	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM ,	04/2015	870.96 -	821.00	399.61	03/2021 -	03/2021	0(O) -	0/0
385	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR,BIHAR ,	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96(O) -	0/0
386	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR ,	09/2001	792.46 724.31	1,320.00	944.77	12/2010 -	-	-	0/0
387	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR ,	04/1997	162.87 -	589.15	183.72	-	03/2022	-	0/0
388	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR,BIHAR ,	04/2003	528.65 -	2,066.77	330.82	-	03/2023	-	0/0
389	KOSI BRIDGE (NL) ECR - [220100304]ECR,BIHAR ,	04/2002	499.41 -	516.02	640.78	03/2020 -	03/2020	0(O) -	0/0
390	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR,BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
391	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR ,	04/2003	218.19 -	413.56	379.47	06/2018 -	10/2018	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
392	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR ,	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96(O) -	0/0
393	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR,BIHAR ,	09/2006	532.87 2,132.03	2,145.00	932.38	03/2019 -	03/2020	12(O) -	0/0
394	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR,BIHAR ,	04/2008	333.76 -	360.00	4.98	- -	03/2020	- -	0/0
395	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR ,	04/2008	633.87 -	2,396.88	.39	- -	-	-	0/0
396	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR ,	04/2008	620.57 -	2,626.98	.00	- -	-	-	0/0
397	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	2,860.55	.00	- -	-	-	0/0
398	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	1.68	- -	-	-	0/0
399	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 -	729.92	253.10	- -	03/2021	- -	0/0
400	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	2,614.36	111.71	- -	03/2022	- -	0/0
401	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	- -	-	-	0/0
402	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	926.09	4.41	- -	-	-	0/0
403	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	2,393.23	17.17	- -	-	-	0/0
404	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.52	- -	-	-	0/0
405	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	.19	- -	03/2023	- -	0/0
406	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.38	- -	-	-	0/0
407	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.58	- -	-	-	0/0
408	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 -	1,474.47	338.44	- -	03/2021	- -	0/0
409	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	785.87	40.00	03/2020 -	03/2020	0(O) -	0/0
410	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	367.17	13.00	- -	-	-	0/0
411	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	380.00	.00	- -	-	-	0/0
412	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 -	1,200.20	.00	03/2020 -	10/2021	19(O) -	0/1
413	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	.00	03/2020 -	10/2021	19(O) -	1/1
414	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	559.91	538.21	07/2014 -	-	-	0/0
415	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
416	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]JECR,BIHAR ,	04/2016	731.64 -	1,185.73	.00	03/2021 -	03/2022	12(O) -	0/0
417	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]JECR,BIHAR ,	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61(O) -	0/0
418	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]JECR,BIHAR ,	04/1998	180.82 -	528.26	462.75	- -	-	-	0/0
419	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]JECR,BIHAR ,	04/1991	329.39 -	566.41	759.20	- -	12/2021	-	0/0
420	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR) NL RVNL - [220100149]RVNL,CHHATISGARH ,	04/1995	631.78 632.00	1,195.00	731.65	12/2012 -	03/2022	111(O) -	0/0
421	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]JECR,CHHATISGARH ,	12/2012	1,160.00 -	1,160.83	582.11	03/2020 -	03/2020	0(O) -	1/1
422	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	958.09	970.78	03/2020 -	03/2020	0(O) -	0/0
423	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
424	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH ,	04/2011	1,471.93 -	543.00	.00	03/2022 -	03/2022	0(O) -	0/1
425	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 -	1,279.00	.00	12/2019 -	12/2019	0(O) -	0/0
426	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021	0(O) -	0/1
427	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022	0(O) -	0/0
428	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.00	600.00	09/2018 -	-	-	0/0
429	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	197.17	56.10	- -	-	-	0/0
430	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	295.68	1.20	- -	-	-	0/0
431	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 -	385.60	629.92	03/2020 -	03/2020	0(O) -	0/0
432	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 -	321.62	125.76	03/2012 -	03/2019	-	0/0
433	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	203.00	202.29	03/2011 -	-	-	0/0
434	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,082.32	830.71	12/2021 -	12/2021	0(O) -	0/0
435	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	644.38	210.07	03/2021 -	03/2021	0(O) -	0/0
436	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 -	844.10	79.08	- -	03/2023	-	0/0
437	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	36(O) -	0/0
438	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,548.66	1,061.88	12/2021 -	12/2021	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
439	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 -	1,002.39	324.69	03/2021 -	03/2020	-12(O) -	0/0
440	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	310.09	03/2019 -	12/2019	9(O) -	0/0
441	GANDHINAGAR REDEVELOPMENT OF STATION ALO WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
442	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0
443	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
444	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 -	551.51	257.05	03/2019 -	-	-	0/0
445	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 -	691.84	54.87	03/2020 -	03/2020	0(O) -	0/0
446	JIND-SONEPAT (NL) NR - [220100280]NR,HARYANA ,	01/2004	238.56 -	740.00	722.65	03/2012 -	-	-	0/0
447	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	625.00	4.38	12/2011 -	-	-	0/0
448	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA ,	04/2013	400.00 -	400.00	.00	- -	-	-	0/0
449	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	300.00	286.56	03/2019 -	03/2020	12(O) -	0/0
450	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	7,000.00	363.94	12/2026 -	12/2026	0(O) -	0/0
451	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 -	27,949.00	17,336.24	11/2002 -	03/2021	220(O) -	0/0
452	MANDARHILL-DUMKA-RAMPURHAT (NL) ER - [220100168]JER,JHARKHAND ,	04/1995	1,125.89 -	1,988.38	2,040.42	03/2016 -	03/2020	48(O) -	0/0
453	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]JECR,JHARKHAND ,	03/1999	1,033.07 -	3,020.94	.00	- -	03/2021	-	0/0
454	KODERMA-TILAIYA (NL) ECR - [220100305]JECR,JHARKHAND ,	04/2002	459.91 -	459.91	221.54	- -	-	-	0/0
455	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND ,	04/2010	309.44 -	525.81	525.93	12/2015 12/2018	02/2019	-	0/0
456	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	365.00	224.01	- 12/2018	01/2020	- 0	0/0
457	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	166.55	12/2016 08/2018	09/2019	33(O) 0	0/0
458	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 1,724.20	1,724.20	289.76	03/2021 03/2021	12/2021	9(O) 0	0/0
459	GARHWA ROAD-RAMNA - [N22000465]JECR,JHARKHAND ,	03/2015	348.23 -	348.23	136.13	03/2021 -	12/2020	-3(O) -	0/0
460	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 -	2,135.00	144.75	- -	12/2024	-	0/0
461	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
462	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 1,801.01	1,801.01	42.34	- 12/2023	12/2023	- 0	0/0
463	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA ,	04/2007	179.65 1,350.91	1,350.91	892.53	- -	12/2023	- -	0/1
464	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 986.30	986.30	295.49	03/2016 12/2023	12/2023	93(O) 0	0/1
465	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 692.43	692.43	.00	- 12/2023	12/2023	- 0	0/0
466	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96(O) 0	0/0
467	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 348.85	348.85	.36	- 12/2023	12/2023	- 0	0/0
468	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	2,900.00	1,390.53	03/2023 -	03/2023	0(O) -	0/1
469	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	- 0	0/0
470	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 2,841.84	2,841.84	92.75	12/2018 12/2024	12/2024	72(O) 0	0/0
471	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	- 0	0/0
472	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 279.54	279.54	26.28	03/2016 12/2023	12/2023	93(O) 0	0/0
473	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 1,140.93	1,140.93	754.97	03/2020 03/2020	03/2021	12(O) 0	0/5
474	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 578.00	578.00	498.04	03/2020 03/2020	03/2020	0(O) 0	0/2
475	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 889.52	889.52	438.16	03/2017 -	03/2020	36(O) -	0/0
476	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	254.53	- -	-	-	0/0
477	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	252.96	8.50	- -	-	-	0/0
478	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA ,	04/2006	191.72 -	369.83	432.50	- -	-	-	0/0
479	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	189.24	6.70	- -	-	-	0/0
480	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	23.84	- -	-	-	0/0
481	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	828.50	.08	- -	-	-	0/0
482	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
483	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA ,	02/2005	241.00 -	241.00	294.63	03/2014 -	-	-	0/0
484	RAMGANJMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021	0(O) -	0/14
485	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 -	1,101.16	194.91	- -	-	-	0/0
486	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 -	1,030.29	1,195.16	03/2022 -	03/2022	0(O) -	0/0
487	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	1,763.93	.00	03/2020 -	10/2021	19(O) -	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
488	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,485.85	960.26	12/2020 -	12/2020	0(O) -	0/0
489	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022	0(O) -	0/10
490	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 -	1,260.61	.00	03/2022 -	03/2022	0(O) -	0/1
491	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	148.20	03/2019 -	02/2020	11(O) -	0/0
492	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 -	1,420.39	104.10	02/2019 -	-	-	0/1
493	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH ,	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96(O) -	0/0
494	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021	0(O) -	0/0
495	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 -	700.00	47.80	06/2020 -	06/2020	0(O) -	0/0
496	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA ,	06/1994	663.01 668.34	858.96	718.23	06/1999 -	-	-	0/0
497	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 1,781.98	2,973.73	1,362.86	03/2004 -	03/2020	192(O) -	0/0
498	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 2,271.50	3,712.50	2,075.20	03/2021 -	03/2021	0(O) -	0/0
499	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	7,986.04	2,423.55	03/2014 -	-	-	0/0
500	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0
501	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 3,168.29	3,168.29	1,108.46	03/2023 -	03/2023	0(O) -	0/0
502	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 792.89	792.89	293.18	03/2021 -	03/2021	0(O) -	0/0
503	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 199.12	298.70	255.25	03/2019 -	03/2019	-	0/0
504	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 540.02	540.02	195.62	03/2022 -	03/2022	0(O) -	0/0
505	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
506	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
507	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	03/2024	0(O) -	0/0
508	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 1,272.19	1,272.19	231.61	03/2022 -	03/2022	0(O) -	0/0
509	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 2,449.91	2,449.91	125.72	03/2023 -	03/2023	0(O) -	0/0
510	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.47	3,627.47	510.70	03/2024 -	03/2024	0(O) -	0/0
511	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 2,081.27	2,081.27	59.41	03/2023 -	03/2023	0(O) -	0/0
512	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 1,035.16	1,035.16	51.24	03/2022 -	03/2023	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
513	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 637.95	637.95	36.16	03/2023 -	03/2023	0(O) -	0/0
514	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	1,750.00	1,773.46	03/2020 -	03/2020	0(O) -	0/0
515	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.22	12/2025 -	03/2025	-9(O) -	0/0
516	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 -	2,686.63	.00	03/2023 -	03/2023	0(O) -	0/1
517	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	259.28	03/2019 -	12/2019	9(O) -	0/0
518	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	- -	-	-	0/0
519	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	- -	-	-	0/0
520	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 -	403.00	36.28	12/2021 -	12/2021	0(O) -	0/1
521	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	13,809.00	9,672.60	03/2011 -	03/2020	108(O) -	0/0
522	NEW BG LINE FROM BYRNIAHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	6,000.00	260.68	03/2021 -	03/2021	0(O) -	0/0
523	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 2,393.48	4,968.00	2,671.70	03/2014 12/2020	12/2020	81(O) 0	0/0
524	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL (NCR) - [220100007]NCR,MULTI STATE ,	04/1986	158.77 274.56	634.48	629.43	03/1994 -	-	-	0/0
525	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE ,	02/1996	240.00 -	579.37	537.30	- -	-	-	0/0
526	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020	0(O) -	0/1
527	NANGALDAM-TALWARA(NL) NR - [220100188]NR,MULTI STATE ,	03/1981	450.00 -	2,100.00	484.14	07/2012 -	-	-	0/0
528	MUNEERABAD-MAHABOONNAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	645.00	838.33	03/2000 -	03/2019	-	0/0
529	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178(O) -	0/9
530	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE ,	04/1999	744.71 -	1,126.79	751.05	- -	-	-	1/1
531	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD) NR - [220100258]NR,MULTI STATE ,	03/2002	625.30 408.76	876.10	841.57	06/2007 -	-	-	0/0
532	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE ,	03/1998	280.00 -	1,122.00	834.87	- -	-	-	0/6
533	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	3,300.00	3,165.68	12/2008 -	03/2019	-	0/0
534	DEOGHAR - SULTANGANJ (NL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	635.03	635.24	02/2013 -	-	-	0/0
535	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	770.08	277.14	12/2022 -	05/2019	-43(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
536	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	104.79	12/2021 -	-	-	0/0
537	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	477.31	217.90	01/2019 -	01/2020	12(O) -	0/0
538	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 -	1,347.26	679.79	03/2022 -	03/2022	0(O) -	0/0
539	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 -	1,640.04	645.15	03/2022 -	03/2022	0(O) -	0/0
540	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,261.71	183.82	-	-	-	0/1
541	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022	0(O) -	0/3
542	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	10.34	-	12/2022	-	0/0
543	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108(O) 0	0/0
544	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	14.62	-	-	-	0/0
545	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 -	1,798.00	.00	03/2019 -	03/2019	-	0/0
546	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	2,350.00	2.27	-	-	-	0/0
547	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	317.14	-	-	-	0/0
548	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	67.41	03/2020 -	03/2020	0(O) -	0/0
549	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	394.28	148.33	-	-	-	0/0
550	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	661.00	121.59	03/2020 -	03/2020	0(O) -	0/0
551	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	-	-	-	0/0
552	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	1,800.00	114.45	03/2019 -	03/2019	-	0/0
553	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	544.72	147.86	03/2006 -	01/2006	-	0/0
554	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	288.85	9.31	-	-	-	0/0
555	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	10.84	-	-	-	0/0
556	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	915.96	322.47	03/2022 -	03/2022	0(O) -	0/0
557	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	238.36	273.54	-	-	-	0/0
558	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	332.14	360.58	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
559	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	792.27	506.12	03/2016 02/2010	02/2010	-	0/0
560	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	538.37	110.00	03/2017 -	05/2010	-	0/0
561	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	175.99	57.51	- -	-	-	0/0
562	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.52	137.85	03/2016 -	03/2020	48(O) -	0/0
563	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	296.43	118.48	03/2017 -	-	-	0/0
564	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	50.69	11/2018 -	-	-	0/0
565	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	19.82	- -	-	-	0/0
566	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.73	- -	-	-	0/0
567	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	542.18	374.20	03/2020 -	03/2020	0(O) -	0/0
568	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	173.91	139.80	- -	-	-	0/0
569	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	269.60	1.12	03/2017 -	-	-	0/0
570	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	492.68	32.00	03/2005 -	-	-	0/0
571	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	153.02	52.10	- -	-	-	0/0
572	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	355.44	72.84	- -	-	-	0/0
573	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	665.75	152.07	02/2012 12/2013	12/2013	-	0/0
574	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	258.73	113.51	03/2014 -	-	-	0/0
575	SANTOSHAPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE ,	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
576	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	246.00	- -	-	-	0/0
577	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	2,200.00	278.36	03/2023 -	03/2024	12(O) -	0/0
578	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE ,	04/2012	923.23 -	1,787.00	2.46	- -	-	-	1/1
579	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE ,	04/2013	1,239.00 -	1,239.00	.00	- -	-	-	0/0
580	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	336.91	143.18	- -	-	-	0/0
581	SRINIVASA-PURAMADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- 12/2023	12/2023	- 0	0/0
582	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE ,	04/2007	2,062.30 2,062.30	2,062.20	817.00	- -	03/2022	- -	0/2
583	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 704.31	704.31	139.69	03/2020 03/2020	03/2020	0(O) 0	1/1
584	KADAPA-BANGALORE (NL) KADAPA-PENDIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	2,132.77	214.54	03/2014 03/2023	03/2023	108(O) 0	1/1
585	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE ,	04/2010	338.54 -	338.54	212.64	- -	-	-	0/0
586	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE ,	04/2008	162.96 -	162.96	153.31	- -	-	-	0/0
587	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE ,	04/2013	876.00 -	876.00	.00	- -	-	-	0/0
588	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE ,	04/2007	328.14 -	1,540.00	45.20	- -	-	-	0/0
589	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	259.23	199.46	- -	-	-	0/0
590	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE ,	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	- 0	0/0
591	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	685.99	4.78	03/2020 -	04/2022	25(O) -	0/0
592	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE ,	03/2015	1,830.00 1,190.92	1,190.92	161.34	- 03/2021	03/2021	- 0	0/0
593	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 860.43	860.43	677.98	03/2020 03/2020	03/2020	0(O) 0	0/0
594	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,870.41	1,870.41	880.72	03/2019 03/2021	03/2021	24(O) 0	0/0
595	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 -	678.54	.00	03/2019 -	03/2020	12(O) -	0/38
596	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
597	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	632.48	03/2021 -	03/2021	0(O) -	0/0
598	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
599	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	2,568.77	12/2023 12/2023	12/2023	0(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
600	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020	0(O) -	0/0
601	CHANDIGARH-BADDI - [N22000467]JNR,MULTI STATE ,	04/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023	0(O) -	0/0
602	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]JNR,MULTI STATE ,	03/2002	625.00 -	845.58	.00	03/2016 -	-	-	0/0
603	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 2,446.57	3,000.00	734.88	03/2015 10/2021	10/2021	79(O) 0	0/0
604	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	03/2020	0(O) -	0/0
605	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147(O) -	0/0
606	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,603.22	12/2017 -	03/2020	27(O) -	0/0
607	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 245.00	1,202.70	801.40	02/2015 -	12/2021	82(O) -	0/0
608	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	385.00	384.55	03/2009 03/2009	03/2019	-	1/1
609	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 -	1,928.07	574.98	06/2021 -	03/2023	21(O) -	0/0
610	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.96	03/2015 -	-	-	0/0
611	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	765.60	02/2019 -	03/2021	25(O) -	0/0
612	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 -	843.04	81.26	10/2020 -	03/2021	5(O) -	0/0
613	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 -	238.03	180.78	03/2020 -	03/2020	0(O) -	0/0
614	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 -	1,547.38	205.59	03/2022 -	03/2022	0(O) -	0/0
615	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	87.60	03/2022 -	03/2022	0(O) -	0/0
616	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28(O) -	0/0
617	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27(O) -	0/0
618	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,151.81	450.25	03/2020 03/2020	06/2020	3(O) 0	0/0
619	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA ,	04/1995	524.43 -	939.00	184.33	12/2021 12/2024	12/2024	36(O) 0	0/0
620	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 2,335.67	2,335.67	441.95	12/2024 -	12/2024	0(O) -	0/0
621	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	1,103.00	1,132.87	03/2020 -	03/2020	0(O) -	0/0
622	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,120.00	941.20	03/2019 -	03/2021	24(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
623	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JRCON,ODISHA ,	04/2016	5,200.00 -	5,200.00	.00	03/2020 -	03/2020	0(O) -	0/0
624	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB ,	04/2009	396.04 -	369.00	186.27	- -	-	-	0/0
625	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	205.22	3.18	- -	-	-	0/0
626	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 780.98	795.01	493.64	02/2019 -	12/2021	34(O) -	0/0
627	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN ,	04/2008	829.74 -	1,216.00	805.25	03/2015 -	10/2020	67(O) -	0/0
628	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	348.55	179.50	12/2019 -	06/2020	6(O) -	0/0
629	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	294.90	169.51	10/2018 -	09/2019	11(O) -	0/0
630	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	1,099.54	.00	- -	-	-	0/1
631	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	432.22	.00	- -	-	-	0/0
632	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 295.02	420.18	118.27	03/2020 -	06/2020	3(O) -	0/0
633	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	244.02	240.62	11/2019 -	05/2020	6(O) -	0/0
634	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	349.00	329.33	02/2019 -	12/2019	10(O) -	0/0
635	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	1,103.04	2.69	- -	-	-	0/0
636	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	435.76	03/2018 -	03/2020	24(O) -	0/0
637	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	12.41	08/2022 -	09/2022	1(O) -	0/0
638	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51(O) -	0/0
639	KARUR-SALEM(NL) SR - [220100191]SR,TAMIL NADU ,	02/1997	155.55 -	920.00	856.94	- -	-	-	0/0
640	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	445.91	06/2013 -	-	-	1/4
641	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,072.50	1,188.90	02/2019 -	02/2019	-	0/0
642	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU ,	09/2006	343.17 -	1,065.00	1,049.68	- -	-	-	0/0
643	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	900.00	61.97	- -	-	-	0/0
644	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	2,300.00	237.73	- -	-	-	0/0
645	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	1,105.00	3.34	02/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
646	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	1,500.00	.61	- -	-	-	0/0
647	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	556.64	303.72	- -	-	-	0/0
648	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU ,	04/1998	271.24 -	520.00	468.18	- -	-	-	0/0
649	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	1,140.00	1.63	- -	-	-	0/0
650	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	450.00	83.15	- -	03/2020	-	0/0
651	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71(O) -	0/0
652	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU ,	02/1997	458.63 -	458.63	.92	03/2015 -	-	-	0/0
653	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU ,	02/2000	200.84 -	200.84	394.26	03/2014 -	-	-	0/0
654	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	302.02	304.07	03/2005 -	-	-	0/0
655	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 -	257.00	.00	03/2018 -	03/2018	-	0/0
656	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
657	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU ,	02/2005	600.00 600.00	645.54	671.00	03/2010 -	-	-	0/0
658	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,700.00	.00	03/2022 -	03/2022	0(O) -	0/0
659	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU ,	02/2003	199.55 -	330.32	2.12	03/2009 -	-	-	0/0
660	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,182.31	.00	03/2020 -	03/2020	0(O) -	0/0
661	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU ,	02/2006	208.00 -	208.00	3.58	03/2012 -	-	-	0/0
662	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA ,	07/1998	458.25 -	458.26	3.69	- -	-	-	0/0
663	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.47	222.40	03/2010 -	03/2022	144(O) -	1/1
664	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	816.55	666.41	03/2016 03/2017	12/2020	57(O) 0	0/0
665	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
666	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA ,	04/2013	723.00 -	616.08	.00	- -	-	-	0/1
667	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	169.16	03/2021 -	03/2021	0(O) -	3/3
668	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	773.94	284.16	12/2024 -	12/2024	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
669	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA ,	04/2017	119.73 185.00	184.97	.00	03/2022 -	03/2022	0(O) -	0/0
670	AGARTALA SABROOM NL NEFR - [N22000099]NFR, TRIPURA ,	04/2008	1,142.00 3,407.00	3,407.00	3,422.67	03/2014 12/2019	03/2019	-	0/0
671	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA ,	04/1999	895.00 984.97	1,733.20	1,563.33	03/2007 -	04/2016	-	0/0
672	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA ,	04/2012	569.63 -	650.00	.00	03/2020 -	10/2022	31(O) -	2/3
673	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH ,	04/1999	108.00 -	432.72	446.52	12/2009 -	-	-	0/0
674	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR, UTTAR PRADESH ,	04/1997	120.00 -	245.39	210.67	12/2008 -	-	-	0/0
675	UTRATIA-ZAFRABAD NR (LINE DOUBLING) - [N22000088]NR, UTTAR PRADESH ,	04/2006	369.90 -	1,581.53	618.19	03/2010 -	-	-	0/0
676	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
677	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
678	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH ,	03/2008	195.64 -	435.00	455.83	- -	03/2018	-	0/0
679	AUNRIHAR MANDUADIH - [N22000133]NER, UTTAR PRADESH ,	03/2012	199.75 -	378.26	283.53	08/2018 -	01/2019	-	0/0
680	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
681	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR, UTTAR PRADESH ,	04/2012	377.44 -	377.44	182.85	- -	-	-	0/0
682	FAIZABAD-LALGANJ VIA AKBARGANJ MAHARAJGANJ AND RAEBARELI - [N22000270]NR, UTTAR PRADESH ,	04/2013	654.00 -	654.00	.00	- -	-	-	0/0
683	UNCHAHAR-AMETHI - [N22000294]NR, UTTAR PRADESH ,	04/2012	1,229.00 -	380.00	4.12	- -	-	-	0/0
684	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
685	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER, UTTAR PRADESH ,	03/2015	1,295.42 -	1,295.42	183.61	03/2022 -	12/2019	-27(O) -	0/0
686	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR, UTTAR PRADESH ,	04/2015	668.70 668.00	668.00	.00	03/2020 -	03/2020	0(O) -	4/6
687	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH ,	04/2015	943.60 -	943.60	238.36	03/2022 -	12/2024	33(O) -	0/0
688	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL, UTTAR PRADESH ,	04/2011	927.01 -	1,077.00	1,052.21	03/2019 -	03/2020	12(O) -	0/0
689	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	405.85	03/2023 -	12/2024	21(O) -	0/0
690	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH ,	03/2012	1,183.25 -	1,183.25	952.52	12/2020 -	03/2021	3(O) -	0/0
691	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	397.88	03/2020 -	03/2021	12(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
692	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	47.38	03/2019 -	12/2019	9(O) -	0/0
693	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH ,	04/1997	233.00 -	318.42	348.82	04/1999 -	-	-	0/0
694	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	2.05	04/2016 -	02/2020	46(O) -	0/0
695	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	01/2022	0(O) -	0/0
696	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH ,	04/1997	609.04 1,063.00	1,807.88	1,805.98	04/1999 -	03/2019	-	0/0
697	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	150.00	.00	04/2017 -	10/2022	66(O) -	0/0
698	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,345.00	.00	01/2018 -	-	-	0/0
699	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	426.74	107.98	04/2017 -	01/2020	33(O) -	0/0
700	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
701	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	4.62	-	-	-	0/0
702	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	5.92	01/2022 -	01/2020	-24(O) -	0/0
703	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	1.79	12/2019 -	04/2021	16(O) -	0/0
704	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	.00	03/2023 -	03/2023	0(O) -	0/0
705	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	.00	03/2021 -	03/2021	0(O) -	0/6
706	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
707	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	38.33	-	-	-	0/0
708	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	16,216.00	1,317.68	12/2024 -	03/2026	15(O) -	0/0
709	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	274.82	03/2019 -	03/2020	12(O) -	0/0
710	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
711	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,544.30	12/2006 -	-	-	0/0
712	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,620.01	849.73	03/2019 12/2009	03/2022	36(O) 0	0/0
713	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,092.20	671.23	12/2010 -	12/2017	-	7/7
714	TAMLUK DIGHA LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL ,	03/1984	293.97 -	749.69	.00	06/2005 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
715	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0
716	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141(O) -	0/0
717	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,092.40	03/2016 -	03/2025	108(O) -	0/0
718	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 4,200.00	2,913.50	838.07	03/2016 -	03/2025	108(O) -	0/0
719	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL ,	04/2009	259.51 -	533.59	145.59	02/2012 -	09/2016	-	0/0
720	GHUTIASHARIF-CANNING (ER) - [N22000117]ER, WEST BENGAL ,	04/2009	193.08 -	612.45	156.24	12/2011 -	09/2012	-	0/0
721	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	4,874.58	1,881.65	03/2016 -	-	-	0/0
722	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	- 0	0/0
723	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL ,	04/2011	289.64 -	760.00	.13	- -	-	-	0/0
724	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	102.82	- -	03/2020	-	0/0
725	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.67	- -	-	-	0/0
726	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	88.25	- -	-	-	0/0
727	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL ,	04/2011	276.69 -	426.00	.00	- 03/2030	03/2030	- 0	0/0
728	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	612.00	93.63	12/2021 -	03/2020	-21(O) -	0/0
729	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER, WEST BENGAL ,	01/1991	1,013.45 1,013.45	1,428.00	484.58	12/2021 12/2021	12/2021	0(O) 0	0/0
730	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 1,966.70	2,373.00	484.92	03/2003 03/2030	03/2030	324(O) 0	0/0
	Total		4,84,549.30 -	7,01,059.04	2,11,064.80				28/144
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
731	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL, A & N ISLANDS ,	03/2015	262.97 -	262.97	.00	10/2018 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
732	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	.00	12/2017 -	-	-	0/4
733	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	.00	04/2017 -	-	-	2/4
734	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	.00	10/2018 -	-	-	0/4
735	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	.00	10/2018 -	-	-	0/4
736	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH,A & N ISLANDS ,	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019	0(O) -	0/0
737	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019	0(O) -	0/0
738	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2010	1,585.00 -	1,585.00	2,322.02	05/2013 -	04/2019	71(O) -	0/0
739	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.52	10/2013 -	-	-	0/0
740	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,008.77	05/2014 -	06/2019	61(O) -	0/0
741	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH,ANDHRA PRADESH , EPC	12/2014	201.12 201.00	201.12	.00	02/2015 -	-	-	4/4
742	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH ,	02/2015	241.61 -	241.61	7.71	02/2017 -	-	-	0/1
743	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH , EPC	11/2014	297.78 330.00	330.00	.00	02/2017 -	-	-	0/0
744	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH ,	01/2014	361.30 -	207.40	44.08	07/2014 -	-	-	1/1
745	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH , EPC	02/2014	258.99 -	258.99	16.54	07/2014 -	-	-	0/1
746	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH , EPC	07/2014	251.55 -	251.55	7.74	02/2015 -	-	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
747	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH , EPC	03/2015	175.03 -	175.00	.00	- -	-	-	0/1
748	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH , EPC	02/2015	266.00 -	266.00	.00	- -	-	-	4/4
749	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH,ANDHRA PRADESH , EPC	07/2015	314.43 -	314.43	.00	- -	-	-	0/0
750	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH ,	07/2015	333.21 333.21	333.21	.00	12/2015 -	-	-	0/2
751	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
752	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH , EPC	02/2014	170.21 -	170.21	5.65	11/2014 -	-	-	0/4
753	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH , EPC	10/2015	480.21 -	480.21	.00	- -	-	-	0/0
754	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	05/2015 -	-	-	4/4
755	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH , EPC	03/2015	309.01 -	309.01	.00	09/2015 -	-	-	0/4
756	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	.00	10/2015 -	-	-	0/0
757	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH ,	07/2015	333.21 -	333.21	.00	12/2015 -	-	-	0/2
758	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH , EPC	02/2014	417.61 -	417.61	.00	06/2014 -	-	-	2/2
759	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH , EPC	10/2015	333.21 -	333.21	.00	11/2015 -	-	-	0/0
760	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH , EPC	02/2015	224.83 -	224.83	.00	04/2015 -	-	-	0/0
761	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	73.29	11/2018 -	05/2019	6(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
762	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	54.13	02/2017 -	-	-	0/0
763	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH ,	03/2017	648.32 -	503.10	15.10	03/2020 -	11/2019	-4(O) -	0/0
764	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH ,	03/2017	1,041.62 -	1,187.10	143.09	03/2020 -	05/2020	2(O) -	0/0
765	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH , Central Sector Projects	06/2017	648.33 -	648.33	49.59	06/2017 -	11/2019	29(O) -	0/0
766	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	.00	- -	06/2019	- -	0/0
767	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	- -	-	-	0/0
768	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	- -	-	-	0/0
769	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	.00	- -	-	-	0/0
770	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	1,532.62	.00	03/2021 -	03/2021	0(O) -	0/0
771	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	.00	- -	07/2021	- -	0/0
772	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	.00	- -	-	-	0/0
773	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	.00	- -	12/2020	- -	0/0
774	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	.00	- -	-	-	0/0
775	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2011	156.63 276.00	276.00	132.21	02/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
776	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2011 -	-	-	0/0
777	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH , ITEM RATE	03/2012	207.03 -	207.03	.00	05/2012 -	-	-	0/0
778	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	194.11 -	194.11	30.54	05/2018 -	-	-	3/4
779	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH , EPC	10/2015	179.82 -	179.82	8.99	01/2019 -	-	-	3/4
780	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH , EPC	07/2015	197.16 -	197.16	38.50	10/2018 -	-	-	1/4
781	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 -	394.00	.00	06/2018 -	-	-	1/3
782	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH , ITEM RATE	01/2011	264.16 -	264.16	.00	- -	-	-	0/0
783	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	165.00 -	165.00	.00	09/2010 -	-	-	0/0
784	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH , ITEM RATE	12/2009	104.00 -	201.00	.00	09/2010 -	-	-	0/0
785	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	235.08 -	235.08	47.81	05/2018 -	-	-	4/4
786	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450 - [N24000614]NHIDCL,ARUNACHAL PRADESH ,	01/2016	183.65 -	183.65	.00	11/2016 -	-	-	0/4
787	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL,ARUNACHAL PRADESH ,	01/2016	334.22 -	334.22	.00	06/2016 -	-	-	4/4
788	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	.00	- -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
789	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL,ARUNACHAL PRADESH ,	04/2016	198.00 -	198.00	.00	10/2016 -	-	-	2/4
790	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL,ARUNACHAL PRADESH ,	11/2015	434.06 -	434.06	.00	- -	-	-	2/4
791	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH ,	12/2016	138.93 155.00	155.00	.00	01/2017 -	01/2020	36(O) -	2/4
792	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL,ARUNACHAL PRADESH ,	01/2017	1,253.10 -	1,253.10	.00	03/2017 -	-	-	1/4
793	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 -	284.09	.00	04/2017 -	-	-	1/4
794	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	195.23	.00	04/2017 -	-	-	1/4
795	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	203.36	.00	04/2017 -	-	-	1/4
796	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL,ARUNACHAL PRADESH ,	01/2017	194.66 -	194.66	.00	04/2017 -	-	-	1/4
797	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL,ARUNACHAL PRADESH ,	02/2017	168.32 -	168.32	.00	04/2017 -	-	-	1/4
798	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	.00	04/2017 -	-	-	0/4
799	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH ,	02/2017	216.71 -	216.71	.00	04/2017 -	-	-	0/4
800	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	.00	04/2017 -	-	-	0/1
801	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	198.22	.00	04/2017 -	-	-	1/4
802	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
803	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	280.00	422.51	02/2009 -	-	-	0/0
804	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	385.13	211.69	04/2009 -	05/2019	121(O) -	0/0
805	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	167.64	268.94	11/2008 -	-	-	0/0
806	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	280.13	195.35	11/2008 -	-	-	0/0
807	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 174.34	174.34	270.88	03/2008 -	06/2019	135(O) -	0/0
808	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130(O) -	0/0
809	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	308.94	04/2008 -	12/2019	140(O) -	0/0
810	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	203.98	05/2008 -	05/2019	132(O) -	0/0
811	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	331.23	340.12	07/2009 -	-	-	0/0
812	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	217.61	391.12	04/2010 -	04/2019	108(O) -	0/0
813	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	22.74	05/2018 -	-	-	2/4
814	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	21.86	06/2018 -	-	-	0/4
815	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	9.26	06/2018 -	-	-	0/4
816	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM , EPC	06/2016	829.00 -	829.00	59.85	01/2019 -	-	-	0/4
817	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	16.84	11/2018 -	-	-	2/4
818	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	80.00	11/2018 -	-	-	2/4
819	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM , EPC	11/2010	268.08 -	268.08	.00	05/2017 -	-	-	0/0
820	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM , ITEM RATE	11/2010	470.20 -	470.20	.00	02/2011 -	-	-	0/0
821	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM , ITEM RATE	05/2011	176.22 -	176.22	.00	02/2018 -	-	-	0/0
822	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM , EPC	11/2014	218.31 -	218.31	.00	02/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
823	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM , EPC	12/2015	225.02 -	159.20	.00	12/2018 -	-	-	0/4
824	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM , EPC	12/2015	223.30 -	223.30	.00	06/2018 -	-	-	0/2
825	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM , EPC	01/1991	520.01 -	520.01	.00	-	-	-	1/4
826	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM , EPC	12/2015	289.99 -	289.99	.00	12/2018 -	-	-	0/4
827	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM , EPC	01/2016	294.17 -	294.17	.00	01/2016 -	-	-	1/4
828	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM , EPC	01/2016	252.00 -	252.00	.00	01/2016 -	-	-	0/4
829	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM ,	03/2015	829.00 -	829.00	.00	01/2016 -	-	-	2/3
830	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL, ASSAM ,	10/2017	818.00 -	818.00	.00	-	-	-	0/4
831	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	884.84	02/2013 -	06/2019	76(O) -	0/0
832	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR , PPP (ANNUITY)	05/2011	351.54 -	351.54	329.40	05/2013 -	-	-	0/0
833	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.73	03/2014 -	-	-	0/0
834	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
835	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	842.31	07/2013 -	06/2019	71(O) -	0/0
836	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR , PPP (ANNUITY)	05/2011	511.54 -	511.54	565.81	11/2013 -	12/2018	-	0/0
837	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH, BIHAR , EPC	01/1991	675.00 -	675.00	.00	-	-	-	0/0
838	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH, BIHAR , ITEM RATE	01/1991	282.41 -	282.41	67.52	08/2016 -	-	-	0/0
839	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH, BIHAR , ITEM RATE	01/1991	358.22 -	358.22	188.71	10/2016 -	-	-	0/0
840	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR ,	08/2015	556.07 -	556.07	.00	-	-	-	0/0
841	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR ,	12/2015	1,041.10 -	1,041.10	191.74	04/2019 -	04/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
842	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	814.04	328.86	- -	01/2020	- -	0/0
843	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 -	322.09	71.28	04/2018 -	04/2020	24(O) -	0/0
844	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	642.41	84.54	- -	10/2020	- -	0/0
845	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,167.45	78.28	- -	12/2019	- -	0/0
846	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	399.54	178.16	04/2019 -	10/2019	6(O) -	0/0
847	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR ,	01/1991	478.35 -	478.35	.00	- -	-	-	0/0
848	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	854.80	575.71	- -	03/2019	-	0/0
849	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	516.13	410.36	04/2018 -	-	-	0/0
850	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR , EPC	01/1991	154.62 -	154.62	.00	- -	-	-	0/0
851	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR , EPC	01/1991	319.68 -	319.68	.00	- -	-	-	0/0
852	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR ,	10/2014	377.64 -	377.64	.00	03/2014 -	-	-	0/0
853	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR ,	10/2013	278.39 -	278.39	.00	08/2014 -	-	-	0/0
854	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR ,	01/2013	322.01 -	322.01	.00	08/2014 -	-	-	0/0
855	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR ,	11/2013	683.83 -	683.83	.00	07/2016 -	-	-	0/0
856	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR ,	02/2014	665.50 -	665.50	.00	07/2016 -	-	-	0/0
857	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR ,	02/2016	178.85 -	178.85	.00	05/2016 -	-	-	0/0
858	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR ,	02/2016	369.77 -	369.77	.00	06/2016 -	-	-	0/0
859	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR ,	02/2016	553.30 -	553.30	.00	05/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
860	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR ,	01/2014	1,408.85 -	1,408.85	.00	10/2016 -	-	-	0/0
861	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR - [N24000580]MORTH,BIHAR ,	03/2015	206.80 -	206.80	.00	07/2016 -	-	-	0/0
862	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR ,	08/2015	288.24 -	288.24	.00	11/2015 -	-	-	0/0
863	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25(O) -	0/0
864	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	.00	12/2016 -	-	-	0/0
865	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	.00	03/2020 -	03/2020	0(O) -	0/0
866	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	.00	03/2020 -	05/2021	14(O) -	0/0
867	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	.00	08/2017 -	02/2022	54(O) -	0/0
868	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 -	2,598.00	.00	- -	-	-	0/0
869	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	.00	- -	-	-	0/0
870	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	- -	-	-	0/0
871	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	496.20	.00	- -	-	-	0/0
872	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH , EPC	10/2014	213.47 -	213.47	.00	03/2015 -	-	-	0/0
873	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH , EPC	10/2014	298.34 -	298.34	.00	03/2015 -	-	-	0/0
874	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH , EPC	11/2014	262.54 -	262.54	.00	03/2015 -	-	-	0/0
875	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH , EPC	12/2015	291.05 -	291.05	.00	- -	-	-	0/0
876	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- [N24000283]PWD,CHHATISGARH , ITEM RATE	12/2010	169.26 -	169.26	.00	12/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
877	REHABILITATION AND UP GRADATION OF NH-12A FROM KM.246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH , EPC	12/2014	394.20 -	394.20	.00	- -	-	-	0/0
878	REHABILITATION AND UPGADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH , EPC	11/2015	485.44 -	485.44	.00	12/2015 -	-	-	0/0
879	REHABILITATION AND UPGADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH , EPC	03/2015	422.34 -	422.34	22.25	- -	-	-	0/0
880	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	333.94	05/2018 -	06/2019	13(O) -	0/0
881	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	7.21	04/2018 -	-	-	0/0
882	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH ,	12/2015	726.67 -	726.67	323.95	04/2018 -	06/2019	14(O) -	0/0
883	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,029.96	.00	- -	-	-	0/0
884	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I) NEW - [N24000609]NHAI,DELHI ,	09/2015	771.18 -	7,558.00	261.77	- -	-	-	0/0
885	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA , EPC	03/2015	297.00 -	297.00	38.33	04/2018 -	-	-	0/1
886	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH,GOA ,	03/2015	298.33 -	298.33	16.10	- -	-	-	0/4
887	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH,GOA , EPC	03/2015	184.05 -	184.05	10.72	- -	-	-	2/4
888	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH,GOA , EPC	03/2015	280.16 -	280.16	16.06	- -	-	-	3/4
889	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA , EPC	10/2015	936.40 -	936.40	.00	- -	-	-	0/0
890	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA , EPC	12/2015	773.98 -	773.98	.00	- -	-	-	0/0
891	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA , EPC	12/2015	819.95 -	819.95	.00	- -	-	-	0/0
892	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,187.21	09/2012 -	-	-	2/3
893	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	976.79	07/2013 -	12/2018	-	0/0
894	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,659.71	12/2015 -	-	-	0/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
895	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT ,	03/2014	503.16 -	503.16	346.60	08/2016 -	-	-	0/0
896	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT ,	05/2016	998.18 -	998.18	263.46	- -	08/2019	-	0/0
897	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT ,	05/2016	834.64 -	834.64	81.26	- -	10/2019	-	0/0
898	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT ,	05/2016	723.64 -	723.64	174.10	- -	09/2019	-	0/0
899	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	207.06	- -	08/2019	-	0/0
900	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	03/2019	-	0/0
901	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	364.56	56.16	- -	12/2019	-	0/0
902	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	74.67	- -	01/2020	-	0/0
903	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	173.51	- -	09/2019	-	0/0
904	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 -	1,251.11	842.34	- -	01/2021	-	0/0
905	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,958.88	933.00	06/2020 -	08/2020	2(O) -	0/0
906	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
907	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 -	1,052.21	.00	- -	01/2021	-	0/0
908	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,702.05	.00	- -	-	-	0/0
909	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 -	1,437.64	.00	- -	-	-	0/0
910	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
911	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.00	05/2010 -	10/2018	-	0/0
912	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 -	2,288.00	3,965.17	11/2011 -	06/2019	91(O) -	0/0
913	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA ,	08/2015	723.54 -	723.54	530.94	02/2018 -	-	-	0/0
914	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	602.95	417.86	06/2016 -	04/2019	34(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
915	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	574.28	436.21	07/2018 -	04/2019	9(O) -	0/0
916	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	970.58	04/2019 -	04/2019	0(O) -	0/0
917	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA ,	11/2015	867.66 -	867.66	502.66	05/2018 -	-	-	0/0
918	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA ,	08/2016	248.97 -	248.97	225.48	05/2019 -	08/2019	3(O) -	0/0
919	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA ,	09/2016	1,004.67 -	1,004.67	.00	05/2019 -	05/2019	0(O) -	0/0
920	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA ,	03/2017	639.79 -	552.90	476.34	03/2020 -	06/2019	-9(O) -	0/0
921	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	.00	-	-	-	0/0
922	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	.00	-	03/2020	-	0/0
923	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	.00	-	03/2020	-	0/0
924	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	634.70	.00	-	-	-	0/0
925	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 -	795.50	.00	-	-	-	0/0
926	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	.00	-	03/2020	-	0/0
927	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	.00	-	-	-	0/0
928	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	.00	-	-	-	0/0
929	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA ,	01/2017	247.25 -	247.25	139.32	03/2019 -	09/2019	6(O) -	0/0
930	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA ,	01/2017	276.01 -	276.01	155.40	03/2019 -	05/2019	2(O) -	0/0
931	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019	29(O) -	0/0
932	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	384.88	03/2018 -	03/2019	-	0/0
933	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	4(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
934	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	- -	0/0
935	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	.00	- -	07/2020	- -	0/0
936	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	162.78	- -	11/2019	- -	0/0
937	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	136.69	06/2020 -	09/2021	15(O) -	0/0
938	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	.00	- -	05/2021	- -	0/0
939	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	2,529.39	07/2015 -	03/2019	-	0/0
940	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,159.00	3,986.82	06/2015 -	-	-	0/0
941	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,393.99	07/2013 -	-	-	0/0
942	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,075.87	06/2014 -	-	-	0/0
943	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	239.74	06/2019 -	12/2020	18(O) -	0/0
944	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,124.97	12/2018 -	10/2019	10(O) -	0/0
945	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 -	1,471.75	274.09	- -	-	-	0/0
946	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	.00	08/2018 -	08/2018	-	1/4
947	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	.00	11/2018 -	11/2018	-	0/4
948	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	.00	07/2019 -	07/2019	0(O) -	0/0
949	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND , PPP (ANNUITY)	12/2012	1,479.00 -	1,479.00	740.26	06/2015 -	-	-	0/0
950	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND ,	02/2016	997.15 -	997.15	392.99	03/2019 -	03/2019	-	0/0
951	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	458.03	59.62	- -	12/2019	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
952	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	323.72	77.31	08/2018 -	08/2019	12(O) -	0/0
953	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND ,	03/2017	165.50 -	172.16	45.34	03/2020 -	06/2019	-9(O) -	0/0
954	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND ,	03/2017	239.68 -	235.90	84.03	03/2020 -	06/2019	-9(O) -	0/0
955	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	273.46	.00	- -	-	-	0/0
956	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	.00	- -	-	-	0/0
957	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 -	1,005.08	.00	- -	-	-	0/0
958	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	04/2019	10(O) -	3/3
959	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	.00	11/2015 -	-	-	0/0
960	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA , EPC	03/2015	159.12 -	159.12	.00	11/2015 -	-	-	0/0
961	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA ,	05/2015	709.00 -	709.00	419.34	09/2017 -	05/2019	20(O) -	0/0
962	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA , EPC	01/1991	219.40 -	219.40	.00	01/2018 -	-	-	0/0
963	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	12/2020	52(O) -	0/0
964	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,040.75	08/2018 -	11/2019	15(O) -	0/0
965	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20(O) -	0/0
966	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	12.95	03/2019 -	11/2020	20(O) -	0/0
967	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA ,	05/2014	720.69 -	720.69	99.03	- -	-	-	0/0
968	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	500.79	04/2020 -	04/2020	0(O) -	0/0
969	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	1,167.42	237.03	03/2019 -	03/2019	-	0/0
970	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 -	950.69	720.79	08/2019 -	12/2020	16(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
971	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	440.28	03/2020 -	07/2020	4(O) -	0/0
972	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	515.09	03/2020 -	06/2020	3(O) -	0/0
973	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	.00	- -	-	-	0/0
974	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	1,995.34	.00	- -	-	-	0/0
975	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,177.80	.00	- -	-	-	0/0
976	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88(O) -	0/0
977	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA , EPC	01/2014	255.75 348.00	348.43	231.56	09/2017 -	-	-	0/0
978	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA , EPC	01/2014	267.16 352.00	352.05	201.35	11/2017 -	-	-	0/0
979	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	845.24	758.13	- -	10/2019	-	0/0
980	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	341.74	06/2018 -	12/2019	18(O) -	0/0
981	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,124.11	157.94	09/2017 -	06/2020	33(O) -	0/0
982	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,424.77	.00	- -	-	-	0/0
983	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,342.77	04/2013 -	-	-	0/0
984	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	325.00	469.54	05/2013 -	-	-	0/0
985	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH , EPC	02/2015	377.83 -	377.83	57.42	07/2017 -	-	-	0/0
986	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH , BOT (TOLL)	01/2012	320.48 -	320.48	189.49	08/2015 -	-	-	0/0
987	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	43.25	- -	-	-	0/0
988	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	704.26 -	704.26	5.21	05/2015 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
989	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH , BOT (TOLL)	03/2013	257.80 -	257.80	59.30	02/2016 -	-	-	0/0
990	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH , EPC	11/2013	497.05 -	497.05	.00	05/2017 -	-	-	0/0
991	SHAHDL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH , EPC	06/2015	532.49 -	532.49	137.08	05/2017 -	-	-	0/0
992	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH , BOT (TOLL)	08/2015	257.80 -	257.00	12.38	- -	-	-	0/0
993	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH , BOT (TOLL)	11/2011	954.43 -	871.15	332.25	09/2015 -	-	-	0/0
994	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH , EPC	06/2015	641.02 -	641.02	89.88	12/2017 -	-	-	0/0
995	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	381.86	252.03	04/2015 -	-	-	0/0
996	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH , BOT (TOLL)	11/2011	670.82 -	670.82	590.00	02/2015 -	-	-	0/0
997	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	795.76	504.40	- -	03/2019	-	0/0
998	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	794.30	442.07	- -	05/2019	-	0/0
999	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH ,	02/2015	327.32 -	327.32	142.73	05/2017 -	-	-	0/0
1000	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	20.74	01/2020 -	-	-	0/0
1001	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH , EPC	12/2015	957.54 -	927.54	29.17	02/2020 -	-	-	0/0
1002	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	540.03	- -	03/2019	-	0/0
1003	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	12/2018	-	0/0
1004	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	439.07	03/2016 -	-	-	0/0
1005	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	516.64	- -	06/2019	-	0/0
1006	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH , PPP (BOT)	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	5(O) -	0/0
1007	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	40.87	08/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1008	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	104.96	01/2019 -	03/2019	-	0/0
1009	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	239.96	10/2017 -	01/2020	27(O) -	0/0
1010	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	374.40	.00	09/2017 -	-	-	0/0
1011	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	.00	09/2017 -	-	-	0/0
1012	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	.00	-	-	-	0/0
1013	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH ,	01/2018	960.24 -	960.24	.00	-	08/2020	-	0/0
1014	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	.00	-	-	-	0/0
1015	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 - [N24000856]PWD,MADHYA PRADESH ,	03/2014	170.00 -	170.00	.00	02/2015 -	02/2015	-	0/0
1016	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH ,	03/2018	162.56 -	162.56	.00	03/2018 -	12/2019	21(O) -	0/0
1017	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH ,	03/2018	166.21 -	166.21	.00	08/2018 -	06/2020	22(O) -	0/0
1018	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH ,	02/2018	169.63 -	169.63	.00	03/2018 -	07/2020	28(O) -	0/0
1019	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH ,	11/2017	235.91 -	235.91	.00	02/2018 -	11/2019	21(O) -	0/0
1020	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH ,	11/2017	184.62 -	184.62	.00	02/2018 -	11/2020	33(O) -	0/0
1021	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH ,	03/2018	191.21 -	191.21	.00	11/2019 -	11/2019	0(O) -	0/0
1022	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH ,	01/2017	205.05 -	205.05	.00	03/2017 -	04/2019	25(O) -	0/0
1023	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH ,	03/2018	214.69 -	214.69	.00	03/2018 -	11/2020	32(O) -	0/0
1024	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH ,	03/2018	217.22 -	217.22	.00	08/2018 -	06/2020	22(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1025	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH ,	03/2018	233.04 -	233.04	.00	03/2018 -	11/2019	20(O) -	0/0
1026	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH ,	11/2017	249.05 -	249.05	.00	07/2018 -	01/2020	18(O) -	0/0
1027	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH ,	11/2017	254.17 -	254.17	.00	02/2018 -	11/2019	21(O) -	0/0
1028	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH ,	02/2018	279.44 -	279.44	.00	03/2018 -	04/2020	25(O) -	0/0
1029	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH ,	09/2016	287.34 -	287.34	.00	01/2019 -	01/2019	-	0/0
1030	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH ,	01/2017	373.82 -	373.82	.00	09/2019 -	09/2019	0(O) -	0/0
1031	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH ,	01/2016	809.16 -	809.16	.00	07/2018 -	06/2020	23(O) -	0/0
1032	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH ,	03/2016	877.79 -	877.79	.00	06/2019 -	11/2019	5(O) -	0/0
1033	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,289.31	03/2013 -	06/2019	75(O) -	0/0
1034	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA ,	12/2011	942.69 -	942.69	704.56	06/2014 -	06/2019	60(O) -	0/0
1035	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64(O) -	2/2
1036	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA ,	06/2014	260.39 -	260.39	87.43	11/2016 -	-	-	0/2
1037	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	13.43	-	-	-	0/4
1038	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	57.60	07/2016 -	-	-	0/12
1039	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	87.62	-	-	-	3/4
1040	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA , EPC	12/2013	220.72 -	220.72	95.02	11/2016 -	-	-	0/4
1041	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	.00	-	-	-	0/0
1042	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH,MAHARASHTRA , ITEM RATE	12/2011	156.26 227.00	156.26	65.16	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1043	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH,MAHARASHTRA , ITEM RATE	03/2011	185.82 292.00	185.82	205.97	- -	-	-	0/0
1044	REHABILITATION AND UPGRADE OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	6.50	- -	-	-	0/0
1045	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	2,288.18 -	2,288.18	.00	05/2019 -	05/2019	0(O) -	0/0
1046	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	514.02	05/2018 -	03/2019	-	0/0
1047	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12(O) -	0/0
1048	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019	0(O) -	0/0
1049	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 -	593.26	60.83	05/2018 -	04/2019	11(O) -	0/0
1050	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	193.70	03/2019 -	12/2020	21(O) -	0/0
1051	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	505.00	454.85	05/2018 -	04/2019	11(O) -	0/0
1052	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,485.07	07/2017 -	12/2018	-	0/0
1053	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	695.52	11/2016 -	06/2019	31(O) -	0/0
1054	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA ,	09/2005	168.00 -	168.00	226.24	06/2006 -	-	-	0/0
1055	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	3,385.90	01/2018 -	02/2019	-	0/0
1056	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1057	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA ,	01/2014	292.98 -	292.98	95.60	11/2014 -	-	-	0/0
1058	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	22.27	07/2018 -	-	-	0/0
1059	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	463.21	07/2019 -	07/2019	0(O) -	0/0
1060	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	609.09	07/2019 -	07/2019	0(O) -	0/0
1061	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA ,	03/2016	244.00 -	244.00	.00	07/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1062	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	.00	- -	-	-	0/0
1063	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	.00	- -	-	-	0/0
1064	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,071.61	.00	- -	07/2021	-	0/0
1065	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,064.88	.00	- -	07/2021	-	0/0
1066	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6(O) -	0/0
1067	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8(O) -	0/0
1068	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	290.73	159.04	- -	05/2019	-	0/0
1069	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	189.17	05/2019 -	07/2019	2(O) -	0/0
1070	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 -	904.16	333.48	02/2020 -	05/2020	3(O) -	0/0
1071	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	.00	03/2020 -	02/2020	-1(O) -	0/0
1072	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	03/2020	0(O) -	0/0
1073	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	863.82	03/2020 -	05/2020	2(O) -	0/0
1074	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	925.93	03/2020 -	08/2020	5(O) -	0/0
1075	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	256.29	03/2017 -	11/2020	44(O) -	0/0
1076	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	233.60	03/2020 -	06/2019	-9(O) -	0/0
1077	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	648.57	03/2020 -	08/2020	5(O) -	0/0
1078	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 -	404.94	39.25	- -	10/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1079	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	.00	- -	-	-	0/0
1080	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	.00	- -	04/2021	-	0/0
1081	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	5.16	- -	11/2020	-	0/0
1082	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	5.76	- -	11/2020	-	0/0
1083	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	.00	- -	07/2021	-	0/0
1084	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	642.13	47.07	- -	12/2020	-	0/0
1085	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	517.57	.00	10/2018 -	10/2018	-	1/4
1086	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA , PPP (ANNUITY)	01/2011	536.00 -	536.00	844.31	01/2014 -	05/2019	64(O) -	0/0
1087	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA , ITEM RATE	12/2010	1,494.48 -	1,494.48	.00	02/2011 -	-	-	0/0
1088	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA ,	12/2015	479.20 -	479.20	475.02	05/2018 -	06/2019	13(O) -	0/0
1089	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA ,	04/2017	553.51 -	553.51	159.00	- -	-	-	0/4
1090	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA ,	03/2019	306.28 -	306.28	.00	05/2019 -	05/2019	0(O) -	0/0
1091	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM , ITEM RATE	11/2010	624.41 -	624.41	.00	03/2011 -	-	-	0/0
1092	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM , ITEM RATE	08/2010	193.69 -	193.69	.00	10/2010 -	-	-	0/0
1093	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM , ITEM RATE	08/2010	195.04 -	195.04	130.82	10/2010 -	-	-	0/0
1094	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	.00	09/2019 -	09/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1095	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	.00	09/2019 -	09/2019	0(O) -	0/0
1096	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	.00	09/2019 -	09/2019	0(O) -	0/0
1097	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	.00	09/2019 -	09/2019	0(O) -	0/0
1098	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	.00	09/2019 -	09/2019	0(O) -	0/0
1099	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	.00	09/2019 -	09/2019	0(O) -	0/0
1100	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	.00	09/2019 -	09/2019	0(O) -	0/0
1101	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	.00	09/2019 -	09/2019	0(O) -	0/0
1102	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128(O) -	0/0
1103	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,675.28	08/2011 -	-	-	2/2
1104	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1105	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	2,848.00	1,149.72	03/2014 -	12/2019	69(O) -	0/0
1106	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81(O) -	0/0
1107	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 -	2,945.00	3,070.11	04/2015 -	-	-	0/0
1108	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE , EPC	03/2015	789.83 -	789.83	109.77	-	-	-	0/0
1109	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE ,	09/2015	788.51 -	788.51	103.37	03/2018 -	-	-	0/0
1110	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	85.00	-	02/2020	-	0/0
1111	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,294.47	.00	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1112	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	998.70	.00	- -	-	-	0/0
1113	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD MON-TAMLU-MERANGKONG ROAD PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND , ITEM RATE	12/2010	1,296.00 -	1,296.00	.00	02/2011 -	-	-	0/0
1114	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	373.07	.00	08/2016 -	08/2019	36(O) -	0/4
1115	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	.00	08/2016 -	08/2019	36(O) -	0/4
1116	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	.00	08/2016 -	08/2019	36(O) -	0/4
1117	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND ,	02/2017	507.68 -	507.68	.00	04/2017 -	-	-	1/4
1118	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	.00	09/2018 -	-	-	0/4
1119	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	.00	09/2018 -	-	-	0/0
1120	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	.00	09/2018 -	-	-	0/0
1121	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	.00	09/2018 -	-	-	0/4
1122	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	.00	09/2018 -	-	-	0/0
1123	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	.00	09/2018 -	-	-	0/2
1124	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	.00	09/2018 -	-	-	0/2
1125	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	.00	09/2018 -	-	-	0/2
1126	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	.00	09/2018 -	-	-	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1127	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	.00	09/2018 -	-	-	0/2
1128	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	.00	09/2018 -	-	-	0/2
1129	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	.00	09/2018 -	-	-	0/2
1130	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	.00	09/2018 -	-	-	0/0
1131	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	.00	09/2018 -	-	-	0/0
1132	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	1,555.96	09/2014 -	03/2019	-	0/0
1133	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,633.88	06/2014 -	-	-	0/0
1134	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA , EPC	01/1991	218.63 -	218.63	29.27	10/2017 -	-	-	0/0
1135	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA , EPC	12/2013	319.80 -	319.80	.00	10/2016 -	-	-	0/0
1136	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA ,	01/1991	229.41 -	229.41	6.65	05/2018 -	-	-	0/0
1137	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA , EPC	07/2014	342.05 -	342.05	.00	01/2017 -	-	-	0/0
1138	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	.00	-	04/2020	-	0/0
1139	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	.00	-	11/2019	-	0/0
1140	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA , EPC	12/2011	159.39 -	159.39	.00	11/2017 -	-	-	0/0
1141	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA , EPC	12/2011	191.08 -	191.08	.00	08/2015 -	-	-	0/0
1142	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	.00	-	06/2019	-	0/0
1143	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	.00	08/2019 -	08/2019	0(O)	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1144	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	130.32	- -	07/2020	- -	0/0
1145	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA ,	03/2014	191.50 192.00	192.00	.00	05/2016 -	-	-	0/0
1146	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA ,	01/2015	326.63 327.00	327.00	.00	04/2018 -	-	-	0/0
1147	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA ,	02/2015	239.91 240.00	240.00	.00	10/2017 -	-	-	0/0
1148	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA ,	03/2015	226.31 226.00	226.00	.00	10/2017 -	-	-	0/0
1149	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA ,	12/2013	319.80 320.00	320.00	.00	05/2016 -	-	-	0/0
1150	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA ,	07/2014	342.05 342.00	342.00	.00	01/2017 -	-	-	0/0
1151	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA ,	08/2013	171.96 172.00	172.00	.00	06/2016 -	-	-	0/0
1152	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA ,	06/2016	157.30 157.00	157.00	.00	06/2018 -	-	-	0/0
1153	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA ,	03/2014	162.51 163.00	163.00	.00	05/2016 -	-	-	0/0
1154	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	115.12	03/2020 -	03/2021	12(O) -	0/0
1155	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	.00	07/2017 -	11/2020	40(O) -	0/0
1156	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	.00	- -	07/2020	- -	0/0
1157	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	.00	- -	-	-	0/0
1158	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	.00	- -	-	-	0/0
1159	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	.00	- -	05/2020	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1160	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	.00	- -	-	-	0/0
1161	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	.00	- -	-	-	0/0
1162	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	.00	- -	-	-	0/0
1163	REHABILITATION AND UPGADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	.00	- -	03/2020	-	0/0
1164	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	.00	- -	-	-	0/0
1165	REHABILITATION AND UPGADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	.00	- -	-	-	0/0
1166	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	.00	- -	06/2021	-	0/0
1167	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	.00	- -	-	-	0/0
1168	REHABILITATION AND UPGADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB , EPC	03/2015	435.90 -	435.90	31.02	- -	-	-	0/0
1169	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB , EPC	01/2015	279.68 -	279.68	25.28	- -	-	-	0/0
1170	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB , EPC	11/2014	463.65 546.00	463.65	280.16	- -	-	-	0/0
1171	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB , EPC	11/2014	573.96 605.00	605.00	209.74	- -	-	-	0/0
1172	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB , EPC	02/2015	483.38 -	483.38	65.76	- -	-	-	0/0
1173	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB , EPC	02/2015	616.36 -	616.36	68.58	- -	-	-	0/0
1174	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB , EPC	02/2015	486.74 -	486.74	189.39	- -	-	-	0/0
1175	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB , EPC	03/2015	312.79 -	312.79	17.57	- -	-	-	0/0
1176	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOUA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB , EPC	07/2014	319.80 -	319.80	102.55	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1177	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB , EPC	12/2015	766.36 -	766.36	99.86	- -	-	-	0/0
1178	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB , EPC	11/2015	847.02 -	847.02	299.81	- -	-	-	0/0
1179	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB , EPC	11/2015	889.24 -	889.24	389.64	- -	-	-	0/0
1180	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB , EPC	12/2015	578.38 -	578.38	128.53	- -	-	-	0/0
1181	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB ,	09/2015	273.06 -	273.06	199.72	- -	05/2019	- -	0/0
1182	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	453.09	- -	06/2019	- -	0/0
1183	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB ,	10/2015	447.29 -	447.29	189.15	12/2017 -	12/2019	24(O) -	0/0
1184	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB , EPC	06/2015	892.17 -	892.17	26.92	- -	-	-	0/0
1185	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB , EPC	06/2015	899.21 -	899.21	25.08	- -	-	-	0/0
1186	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,388.34	1,017.40	09/2019 -	09/2019	0(O) -	0/0
1187	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 -	1,169.61	361.32	- -	04/2020	- -	0/0
1188	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	72.04	03/2020 -	04/2020	1(O) -	0/0
1189	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	261.76	7.90	- -	01/2021	- -	0/0
1190	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	9.03	- -	-	-	0/0
1191	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	9.03	- -	01/2020	- -	0/0
1192	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH - [N24000905]PWD,PUNJAB ,	03/2018	322.48 -	322.48	48.73	07/2020 -	07/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1193	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB ,	03/2018	173.24 -	173.24	10.97	06/2020 -	06/2020	0(O) -	0/0
1194	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB ,	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019	0(O) -	0/0
1195	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]PWD,PUNJAB ,	03/2018	170.57 -	170.57	8.14	11/2020 -	11/2020	0(O) -	0/0
1196	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN , EPC	10/2014	269.22 -	269.22	33.24	01/2015 -	-	-	0/0
1197	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN , EPC	10/2014	257.09 -	257.09	14.80	01/2015 -	-	-	0/0
1198	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN , EPC	10/2013	278.87 -	278.87	.00	05/2014 -	-	-	0/0
1199	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN , ITEM RATE	01/1991	376.52 -	376.52	.00	04/2014 -	-	-	0/0
1200	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN , EPC	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51(O) -	0/0
1201	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN , EPC	12/2015	621.43 -	621.43	.00	06/2018 -	-	-	0/4
1202	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	297.72	09/2016 -	03/2019	-	0/0
1203	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN ,	01/1991	269.26 -	269.26	212.72	10/2016 -	-	-	0/0
1204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAUJI - [N24000406]MORTH,RAJASTHAN , ITEM RATE	01/1991	208.87 -	208.87	206.78	05/2016 -	-	-	0/0
1205	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	605.33	10/2017 -	04/2019	18(O) -	0/0
1206	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	675.73	08/2016 -	02/2019	-	0/0
1207	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	753.50	04/2018 -	03/2019	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1208	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183.000 TO KM 221.400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	33.73	10/2013 -	06/2019	68(O) -	0/0
1209	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN , BOT (TOLL)	09/2012	511.00 -	511.00	.00	10/2013 -	-	-	0/4
1210	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 09/2017	03/2019	-	0/0
1211	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI,RAJASTHAN ,	08/2015	275.90 -	275.90	256.10	- -	03/2019	-	0/0
1212	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3(O) -	0/0
1213	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	155.23	06/2019 -	11/2019	5(O) -	0/0
1214	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN ,	06/2016	649.00 -	649.00	.00	06/2019 -	09/2019	3(O) -	0/0
1215	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN ,	07/2016	688.70 -	688.70	552.52	- -	11/2019	- -	0/0
1216	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN ,	07/2016	331.46 -	331.46	261.25	10/2018 -	-	-	0/0
1217	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN ,	08/2016	320.30 -	320.30	228.17	01/2019 -	04/2019	3(O) -	0/0
1218	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN ,	09/2016	1,239.82 -	1,239.82	795.68	- -	05/2020	- -	0/0
1219	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN ,	09/2016	1,100.19 -	1,100.19	750.00	- -	12/2019	- -	0/0
1220	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	- -	0/0
1221	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN ,	04/2017	894.00 -	894.00	15.00	04/2020 -	11/2019	-5(O) -	0/0
1222	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	211.90	10/2017 -	11/2020	37(O) -	0/0
1223	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	.00	- -	12/2020	- -	0/0
1224	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	129.11	- -	09/2020	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1225	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN ,	02/2018	741.86 -	741.86	.00	- -	-	-	0/0
1226	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN ,	02/2018	716.76 -	716.76	.00	- -	-	-	0/0
1227	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN ,	03/2018	874.25 -	874.25	.00	- -	-	-	0/0
1228	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	.00	- -	-	-	0/0
1229	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM ,	04/2013	151.59 -	151.59	.00	08/2013 -	-	-	0/0
1230	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM , ITEM RATE	04/2013	166.27 -	166.27	.00	08/2013 -	-	-	0/0
1231	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM , ITEM RATE	01/2013	182.28 -	182.00	24.36	02/2013 -	-	-	0/0
1232	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	.00	10/2017 -	-	-	1/4
1233	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM ,	04/2017	318.42 -	318.42	7.50	11/2017 -	-	-	1/4
1234	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	.00	- -	-	-	0/0
1235	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	18.12	11/2017 -	-	-	1/4
1236	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	.00	06/2018 -	-	-	0/4
1237	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,330.22	12/2013 -	-	-	0/0
1238	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	325.55	06/2013 -	-	-	0/0
1239	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	374.00	237.00	05/2013 -	-	-	0/0
1240	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU , PPP (ANNUITY)	09/2011	485.00 -	485.00	406.68	08/2013 -	12/2018	-	0/0
1241	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	350.79	04/2014 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1242	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU , EPC	03/2015	258.97 -	268.92	.00	08/2015 -	-	-	0/0
1243	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU , EPC	03/2015	157.18 162.00	162.00	.00	07/2015 -	-	-	0/0
1244	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - - [N24000318]MORTH,TAMIL NADU , EPC	11/2015	154.14 -	154.14	.00	08/2015 -	-	-	0/0
1245	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	956.75	11/2017 -	08/2019	21(O) -	0/0
1246	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	97.07	12/2017 -	08/2019	20(O) -	0/0
1247	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1248	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	627.47	07/2008 -	-	-	0/0
1249	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	277.66	08/2018 -	03/2020	19(O) -	0/0
1250	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	355.39	07/2018 -	05/2020	22(O) -	0/0
1251	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	44.06	03/2020 -	03/2020	0(O) -	0/0
1252	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	352.71	07/2016 -	04/2019	33(O) -	0/0
1253	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	.00	08/2017 -	09/2020	37(O) -	0/0
1254	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	.00	09/2017 -	-	-	0/0
1255	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	.00	09/2017 -	08/2020	35(O) -	0/0
1256	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	62.24	-	03/2020	-	0/0
1257	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,166.26	.00	-	-	-	0/0
1258	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	32.77	-	11/2020	-	0/0
1259	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	31.45	-	11/2020	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1260	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	633.55	.00	- -	-	-	0/0
1261	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,016.92	.00	- -	-	-	0/0
1262	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,065.96	.00	- -	-	-	0/0
1263	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,429.59	09/2016 -	06/2019	33(O) -	0/0
1264	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA , EPC	12/2013	177.18 -	177.18	40.51	03/2016 -	-	-	4/4
1265	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPLLY SECTIO - [N24000242]PWD,TELANGANA , EPC	12/2013	158.65 -	158.65	103.50	03/2016 -	-	-	4/4
1266	YAN TO NIRMAL SEREHALITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA , EPC	12/2013	244.08 -	244.08	38.32	03/2016 -	-	-	4/4
1267	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA , EPC	01/2014	340.00 -	340.00	.00	03/2016 -	-	-	2/2
1268	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA , EPC	01/2014	270.00 -	270.00	19.84	03/2016 -	-	-	1/4
1269	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA , EPC	10/2014	244.30 -	156.09	.00	12/2016 -	-	-	4/4
1270	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA , EPC	10/2014	295.47 -	313.27	.00	02/2017 -	-	-	0/1
1271	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA , EPC	03/2015	153.21 -	153.21	.00	01/2017 -	-	-	0/0
1272	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA ,	03/2011	218.31 -	339.82	208.28	12/2015 -	-	-	0/3
1273	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,423.96	605.35	11/2018 -	07/2019	8(O) -	0/0
1274	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1275	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	.00	- -	-	-	0/0
1276	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	.00	- -	-	-	0/0
1277	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	.00	- -	-	-	0/0
1278	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1279	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	288.63	03/2018 -	-	-	3/4
1280	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA , EPC	05/2014	497.89 -	497.89	70.47	04/2017 -	-	-	4/4
1281	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.42	08/2013 -	-	-	0/0
1282	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH , PPP (BOT)	03/2011	1,046.00 -	1,046.00	805.19	09/2013 -	-	-	0/0
1283	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	291.36	451.29	01/2014 -	09/2018	-	0/0
1284	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	1,998.25	09/2015 -	-	-	0/0
1285	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH , EPC	03/2015	629.74 -	629.74	.00	- -	-	-	0/0
1286	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	.00	03/2016 -	-	-	0/0
1287	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH , EPC	10/2014	227.74 -	227.74	.00	10/2016 -	-	-	0/0
1288	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1289	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	351.34	425.99	01/2016 -	-	-	0/0
1290	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	232.93	09/2016 -	-	-	0/0
1291	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH ,	06/2014	301.04 -	301.04	207.94	01/2016 -	-	-	0/0
1292	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	495.78	617.93	01/2016 -	-	-	0/0
1293	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH , EPC	10/2013	445.89 -	445.89	.00	03/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1294	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH , ITEM RATE	11/2010	305.49 -	305.49	.00	03/2017 -	-	-	0/0
1295	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH , EPC	01/2014	397.04 -	397.04	.00	10/2016 -	-	-	0/0
1296	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH , EPC	06/2015	774.57 -	774.57	.00	03/2018 -	-	-	0/0
1297	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH , EPC	10/2013	317.76 -	317.76	15.47	03/2017 -	-	-	0/0
1298	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH , EPC	10/2013	283.45 -	283.45	.00	10/2016 -	-	-	0/0
1299	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH , EPC	10/2013	493.94 -	493.94	.00	03/2017 -	-	-	0/0
1300	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH ,	09/2015	785.78 -	785.78	839.63	03/2018 -	-	-	0/0
1301	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH , PPP (BOT)	07/2015	1,657.20 -	1,657.20	2,270.00	01/2019 -	01/2019	-	0/0
1302	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	718.15	06/2016 -	-	-	0/0
1303	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	478.12	06/2018 -	-	-	0/0
1304	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	557.65	06/2018 -	-	-	0/0
1305	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	441.72	07/2018 -	-	-	0/0
1306	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	512.93	06/2018 -	-	-	0/0
1307	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	.00	08/2015 -	-	-	0/0
1308	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1309	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH , EPC	12/2014	207.88 -	207.88	.00	- -	-	-	0/0
1310	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	683.24	565.33	- -	-	-	0/0
1311	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,081.57	892.00	06/2019 -	06/2019	0(O) -	0/0
1312	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	623.35	04/2019 -	04/2019	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1313	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	301.48	- -	-	-	0/0
1314	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	225.06	- -	-	-	0/0
1315	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	1,587.49	274.39	04/2019 -	04/2019	0(O) -	0/0
1316	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM 204.300 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	512.49	04/2019 -	04/2019	0(O) -	0/0
1317	4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	490.12	- -	02/2020	- -	0/0
1318	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	5.71	- -	07/2020	- -	0/0
1319	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	178.80	- -	04/2020	- -	0/0
1320	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,820.02	04/2019 -	11/2019	7(O) -	0/0
1321	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	534.55	361.36	- -	-	-	0/0
1322	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	350.99	- -	-	-	0/0
1323	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	336.65	03/2020 -	11/2020	8(O) -	0/0
1324	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	253.84	03/2020 -	08/2020	5(O) -	0/0
1325	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	896.05	03/2020 -	05/2020	2(O) -	0/0
1326	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	1,377.59	03/2020 -	03/2020	0(O) -	0/0
1327	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,232.21	637.48	- -	05/2020	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1328	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1329	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1330	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1331	FOR REHABILITATION AND UPGRADEATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	.00	- -	-	-	0/0
1332	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	.00	- -	-	-	0/0
1333	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	925.40	.00	- -	-	-	0/0
1334	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	-	-	0/0
1335	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	.00	- -	-	-	0/0
1336	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,120.57	.00	- -	-	-	0/0
1337	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	1,025.80	.00	- -	-	-	0/0
1338	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	1,115.28	.00	- -	-	-	0/0
1339	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	.00	- -	-	-	0/0
1340	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	.00	- -	-	-	0/0
1341	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69(O) -	0/0
1342	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	244.82	- -	10/2019	- -	0/0
1343	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	275.21	- -	02/2020	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1344	4 LANEING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019	17(O) -	0/0
1345	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	.00	05/2018 -	-	-	0/4
1346	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	.00	06/2018 -	-	-	1/4
1347	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	.00	05/2018 -	-	-	1/4
1348	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	.00	12/2019 -	12/2019	0(O) -	0/0
1349	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019	0(O) -	0/0
1350	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019	0(O) -	0/0
1351	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	45.92	06/2019 -	06/2019	0(O) -	0/0
1352	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019	0(O) -	0/0
1353	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH,UTTARAKHAND ,	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019	0(O) -	0/0
1354	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019	0(O) -	0/0
1355	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	74.52	02/2020 -	02/2020	0(O) -	0/0
1356	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	.14	-	-	-	0/0
1357	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	.00	05/2020 -	05/2020	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	.74	- -	-	-	0/0
1359	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	3.80	07/2018 -	07/2018	-	0/5
1360	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,317.74	08/2013 -	06/2019	70(O) -	0/0
1361	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,837.93	08/2013 -	06/2020	82(O) -	0/0
1362	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	05/2019	56(O) -	0/0
1363	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL , PPP (ANNUITY)	02/2012	702.16 -	702.16	465.22	07/2014 -	05/2019	58(O) -	0/0
1364	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH, WEST BENGAL ,	01/1991	322.00 -	322.00	56.41	03/2018 -	-	-	0/0
1365	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 -	361.15	77.11	- -	01/2020	-	0/0
1366	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 -	1,083.00	225.46	06/2018 -	12/2019	18(O) -	0/0
1367	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	1,665.00	1,901.17	- -	03/2019	-	0/0
1368	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	24.78	11/2018 -	12/2019	13(O) -	0/0
1369	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	228.73	08/2018 -	09/2019	13(O) -	0/0
1370	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL, WEST BENGAL ,	03/2017	158.65 -	158.65	.00	06/2018 -	-	-	0/0
1371	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 -	1,261.98	.00	- -	-	-	0/0
1372	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B NH-31C NH-31 NH-10 O - [N24000871]PWD, WEST BENGAL ,	08/2014	600.87 720.97	720.97	.00	11/2017 -	11/2017	-	0/0
1373	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717 NH-31 NH-31C NH-317A O - [N24000873]PWD, WEST BENGAL ,	08/2014	823.20 937.76	937.76	.00	11/2017 -	07/2019	20(O) -	0/0
1374	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL ,	03/2016	271.17 291.20	291.20	.00	11/2018 -	11/2019	12(O) -	0/0
1375	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]PWD, WEST BENGAL ,	01/2017	396.86 -	396.86	.00	09/2019 -	12/2019	3(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1376	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD,WEST BENGAL ,	03/2017	202.69 -	202.69	.00	11/2019 -	11/2019	0(O) -	0/0
1377	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD,WEST BENGAL ,	02/2018	426.18 -	426.18	.00	09/2020 -	09/2020	0(O) -	0/0
1378	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD,WEST BENGAL ,	02/2018	218.70 -	218.70	.00	11/2020 -	11/2020	0(O) -	0/0
1379	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]PWD,WEST BENGAL ,	03/2018	254.30 -	254.30	.00	10/2020 -	10/2020	0(O) -	0/0
1380	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL ,	03/2016	160.27 -	160.27	.00	08/2019 -	08/2021	24(O) -	0/0
1381	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL ,	06/2016	236.78 -	236.78	.00	08/2019 -	08/2021	24(O) -	0/0
1382	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL ,	04/2014	279.70 398.22	398.22	.00	08/2017 -	08/2019	24(O) -	0/0
	Total		4,28,620.09 -	4,41,091.58	1,69,517.06				107/369
	<u>SHIPPING AND PORTS</u>								
1383	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL,KERALA ,	07/2016	1,799.00 -	1,799.00	297.60	05/2021 -	05/2021	0(O) -	0/0
1384	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL,KERALA ,	05/2016	970.00 -	970.00	272.73	05/2020 -	05/2020	0(O) -	0/0
1385	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA , PPP (BOT)	01/2007	366.39 -	669.46	411.12	12/2010 -	-	-	0/0
1386	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU , Public Private (SPV)	06/2005	2,427.40 -	2,427.40	831.21	10/2008 -	-	-	0/0
1387	ENNORE MANALI EXPRESS WAY F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU , Public Private (SPV)	10/2002	150.00 -	600.00	139.80	03/2006 -	-	-	0/0
1388	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU , PPP (ANNUITY)	02/2015	244.50 258.00	275.98	275.98	12/2017 -	-	-	1/1
1389	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU ,	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		6,557.29 -	6,999.74	2,229.89				1/1
	<u>TELECOMMUNICATIONS</u>								
1390	GSM-RF EXPANSION PROJECT MTNL DELHI (3G) - [N26000105]MTNL,DELHI ,	06/2016	418.26 -	418.26	367.03	06/2017 -	-	-	0/0
1391	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA , Central Sector Projects	08/2017	215.30 219.60	219.60	33.46	05/2018 05/2019	05/2019	12(O) 1	0/0
1392	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA , Central Sector Projects	01/2018	231.80 240.10	240.10	117.63	10/2018 05/2019	05/2019	7(O) 0	0/0
1393	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE ,	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58(O) -	0/0
1394	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE , Central Sector Projects	09/2014	2,111.17 -	2,011.17	253.90	09/2014 -	-	-	0/70
	Total		16,310.53 -	27,553.13	9,169.02				0/70
	<u>URBAN DEVELOPMENT</u>								
1395	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH ,	07/2014	232.00 -	232.00	.00	- -	-	-	0/0
1396	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH ,	06/2014	157.84 -	157.84	155.25	03/2017 -	-	-	4/5
1397	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM,ANDHRA PRADESH ,	08/2007	246.90 -	246.90	.00	- -	-	-	0/0
1398	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH ,	01/2018	206.58 -	206.58	82.25	03/2019 -	08/2019	5(O) -	0/7
1399	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72(O) -	0/0
1400	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR ,	02/2016	496.18 496.00	498.99	61.43	06/2017 07/2017	10/2020	40(O) 0	0/0
1401	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI ,	09/2011	38,585.00 -	38,585.00	34,763.15	03/2016 -	-	-	0/0
1402	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	1,592.00	496.57	10/2019 -	03/2020	5(O) -	0/7
1403	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI ,	07/2012	884.30 -	884.30	689.94	12/2015 -	-	-	0/0
1404	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI ,	06/2012	4,264.00 -	4,439.23	3,936.53	11/2019 -	11/2019	0(O) -	3/7

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1405	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD,DELHI ,	06/2015	197.33 -	197.33	25.15	04/2019 06/2020	06/2020	14(O) 0	0/2
1406	REDEVELOPMENT OF GPRA COLONY AT NAUROI NAGAR - [N28000105]NBCC,DELHI ,	07/2016	2,694.00 -	2,694.00	.00	- -	-	-	0/0
1407	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI ,	11/2017	238.56 -	238.56	33.40	05/2020 -	05/2020	0(O) -	0/0
1408	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI ,	12/2017	188.00 -	188.00	131.55	06/2019 -	06/2019	0(O) -	0/0
1409	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI ,	10/2016	422.00 250.00	422.00	.00	- 12/2020	12/2020	- 0	0/0
1410	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 250.00	392.00	11.91	- 08/2020	03/2021	- 0	0/0
1411	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI ,	10/2016	248.20 -	248.20	28.59	04/2018 -	-	-	0/0
1412	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI ,	10/2017	271.90 -	271.90	17.39	11/2019 -	11/2019	0(O) -	0/0
1413	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR GUJARAT - [N12000106]HSCL,GUJARAT ,	01/2013	175.00 -	175.00	1.83	- -	-	-	0/0
1414	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	163.97	11/2014 -	-	-	2/8
1415	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND ,	12/2007	253.92 253.92	253.92	193.97	06/2016 -	-	-	0/0
1416	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI KODERMA HAZARIBAG RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND ,	12/2007	200.00 -	200.00	131.15	03/2018 -	-	-	0/0
1417	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND ,	02/2014	787.29 -	787.29	285.30	12/2016 -	-	-	0/0
1418	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND ,	04/2013	170.00 -	170.00	88.91	04/2018 -	-	-	0/0
1419	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	73.90	03/2016 -	09/2020	54(O) -	1/6
1420	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA ,	05/2005	768.88 1,070.97	1,113.34	1,085.64	02/2014 -	-	-	0/0
1421	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA ,	07/2011	324.87 324.87	324.87	262.93	12/2015 -	-	-	0/0
1422	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA ,	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13(O) -	0/0
1423	RESIDENTIAL QUATERS FOR HAL BANGLORE - [N28000103]CPWD,KARNATAKA ,	12/2016	246.31 -	246.31	51.14	02/2020 09/2020	09/2020	7(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1424	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	77.70	10/2012 -	03/2020	89(O) -	1/6
1425	KOCHI METRO RAIL PROJECT - [N28000081]KMRL,KERALA ,	07/2012	5,181.79 -	5,687.79	5,188.50	07/2017 -	12/2019	29(O) -	0/0
1426	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	2.58	03/2020 -	03/2020	0(O) -	2/7
1427	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA ,	08/2014	8,680.00 8,680.00	8,680.00	5,632.05	03/2018 12/2019	12/2019	21(O) 0	0/0
1428	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRL,MAHARASHTRA ,	07/2013	23,136.00 -	23,136.00	.00	01/2015 -	05/2020	64(O) -	0/0
1429	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	24.40	07/2020 -	09/2020	2(O) -	3/14
1430	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 -	11,420.00	2,377.05	11/2021 -	11/2021	0(O) -	0/0
1431	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR , Central Sector Projects	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67(O) -	0/10
1432	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCP - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	7.15	09/2017 -	-	-	0/0
1433	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR PUNJAB - [N28000088]CPWD,PUNJAB ,	02/2014	388.00 488.28	488.28	410.91	05/2017 02/2019	06/2019	25(O) 0	8/12
1434	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR PUNJAB - [N28000102]CPWD,PUNJAB ,	08/2016	294.00 349.94	294.00	167.44	04/2019 09/2019	12/2019	8(O) 0	4/8
1435	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	430.00	46.28	05/2020 -	05/2020	0(O) -	1/5
1436	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN ,	05/2015	189.00 -	189.00	.00	03/2017 -	-	-	0/0
1437	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	559.49	291.77	07/2019 -	12/2019	5(O) -	0/0
1438	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 -	19,058.00	16,352.77	12/2015 -	-	-	12/24
1439	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	209.00	105.72	10/2019 -	03/2020	5(O) -	1/6
1440	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	.00	03/2018 -	-	-	0/2
1441	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	12.00	- -	11/2021	- -	0/0
1442	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	27.18	03/2020 -	03/2020	0(O) -	0/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(April 2019)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1443	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	175.94	178.65	12/2015 -	-	-	0/0
1444	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	227.00	199.95	12/2016 -	-	-	0/0
1445	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	206.71	141.28	12/2016 -	-	-	0/0
1446	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	2,536.77	03/2019 -	03/2019	-	0/0
1447	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	3.50	03/2020 07/2020	03/2020	0(O) 0	0/0
1448	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	10/2019	70(O) -	0/0
1449	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL , Central Sector Projects	08/2012	185.37 -	185.37	178.30	03/2016 -	-	-	0/0
1450	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL ,	02/2014	156.57 -	156.57	154.15	08/2016 -	07/2019	35(O) -	10/16
1451	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL , Central Sector Projects	10/2014	162.88 -	162.88	115.59	04/2018 -	07/2019	15(O) -	5/6
	Total		1,60,233.35 -	1,66,436.66	78,206.60				57/163
	<u>DEFENCE PRODUCTION</u>								
1452	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL,GOA ,	12/2016	167.69 168.00	167.69	127.00	05/2018 03/2019	-	-	7/10
1453	CONSTRUCTION WORKS PHASE 3B - [N39000002]GSL,GOA ,	12/2016	285.95 286.00	285.95	74.55	08/2020 -	08/2020	0(O) -	7/16
	Total		453.64 -	453.64	201.55				14/26
	Grand Total		18,32,721.31	21,61,313.18	8,84,906.88				2819/4954


Summary of projects in the Flash Report for the month of April, 2019

Project Implementation - Current Status:

Number of Projects in Previous Month	1405
Number of Projects completed/dropped/frozen in Current Month	7
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	56
Number of Projects in Current Month	1453

Brief Analysis

Project Status with respect to Original Schedule: Out of 1453 projects, 22 projects are ahead of schedule, 294 projects are on schedule 388 projects are delayed. 646 projects do not have fixed dates of commissioning. 103 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

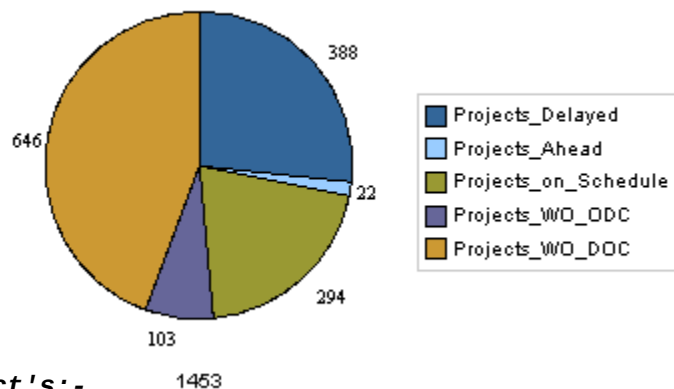


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1453 projects when sanctioned, was of the order of Rs. 1832579.17 crore but this was subsequently revised to Rs. 2161313.18 crore implying a cost overrun of 17.9%. The expenditure incurred on these projects till April, 2019 is Rs. 884906.88 crore, which is 40.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

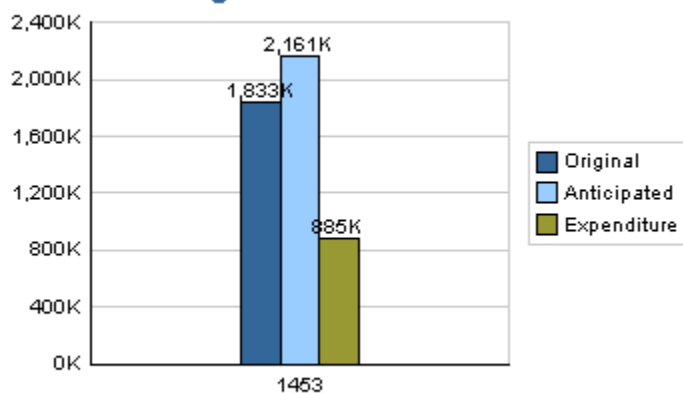

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

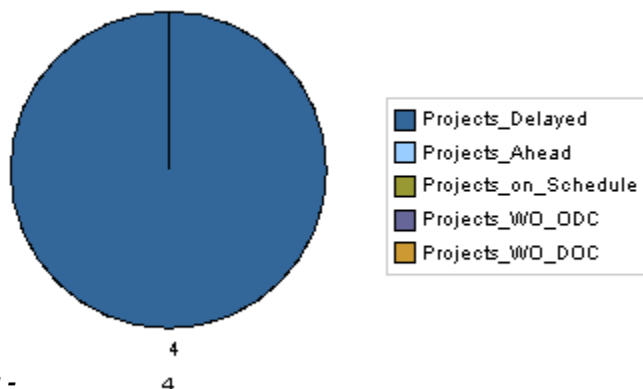


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 75589 crore implying a cost overrun of 12.6%. The expenditure incurred on these projects till April, 2019 is Rs. 43899.17 crore, which is 58.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

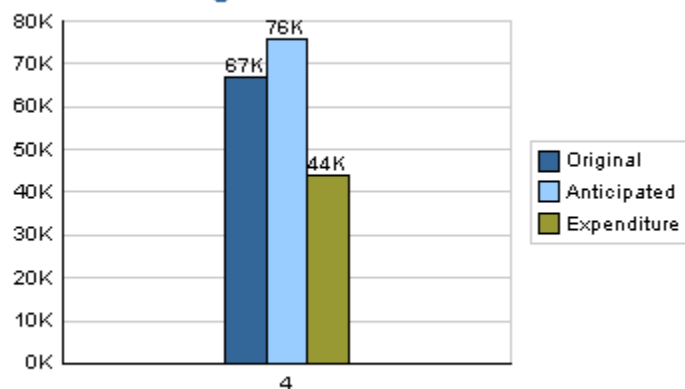

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	1
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 1 project, 1 project is delayed.

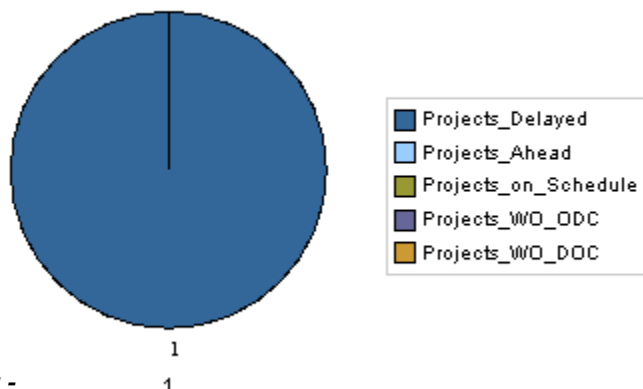


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1 project when sanctioned, was of the order of Rs. 314.61 crore but this was subsequently anticipated to Rs. 441.33 crore implying a cost overrun of 40.3%. The expenditure incurred on these projects till April, 2019 is Rs. 85.79 crore, which is 19.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

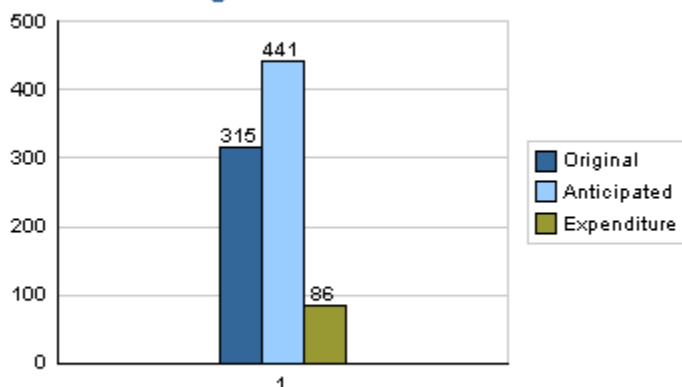

Sector wise current status of projects on the Flash Report


COAL

Current Status:

Number of Projects	98
Number of Projects On Schedule	47
Number of Projects Delayed	33
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	17

Brief Analysis

Project Status with respect to Original Schedule: Out of 98 projects, 1 project is ahead of schedule, 47 projects are on schedule 33 projects are delayed. 17 projects do not have fixed dates of commissioning.

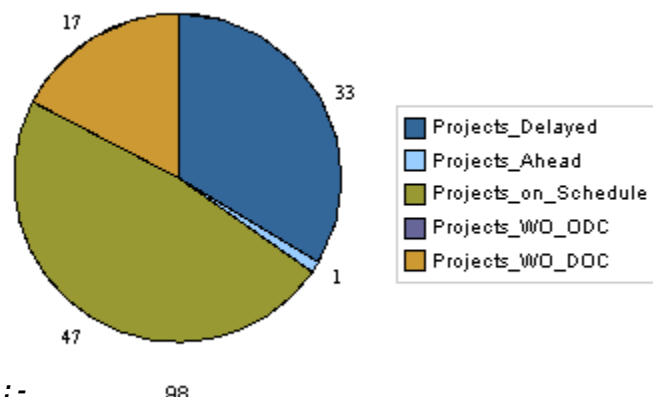


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 99419.73 crore but this was subsequently anticipated to Rs. 99873.07 crore implying a cost overrun of .5%. The expenditure incurred on these projects till April, 2019 is Rs. 33228.2 crore, which is 33.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

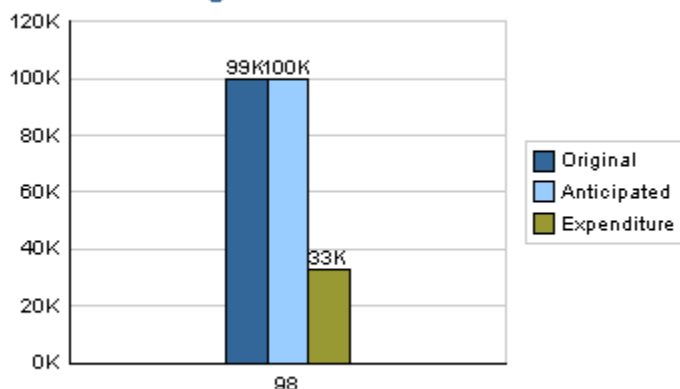

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	5
Number of Projects On Schedule	4
Number of Projects Delayed	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are on schedule 1 project is delayed.

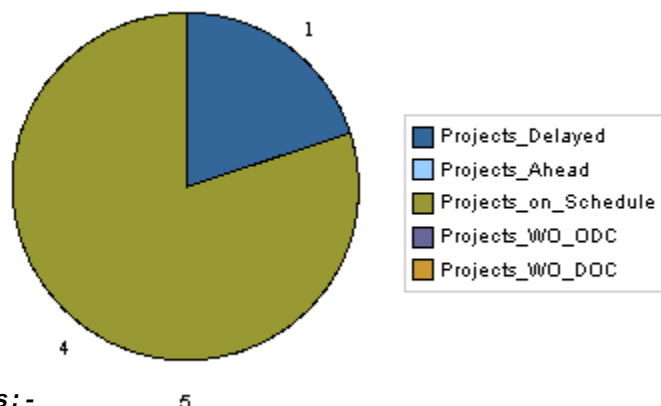


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 1299.07 crore but this was subsequently anticipated to Rs. 1310.72 crore implying a cost overrun of .9%. The expenditure incurred on these projects till April, 2019 is Rs. 438.42 crore, which is 33.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

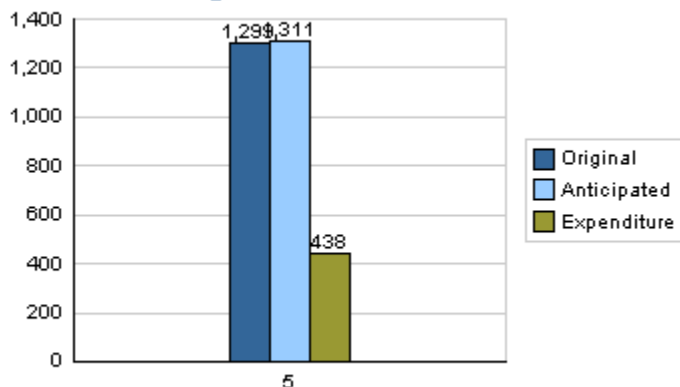

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects On Schedule	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 5 projects are on schedule

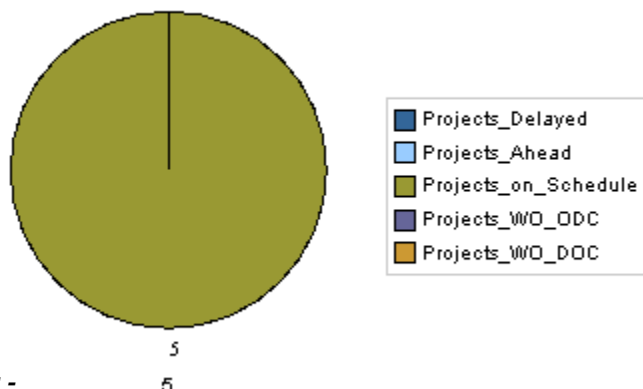


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7078.62 crore. The expenditure incurred on these projects till April, 2019 is Rs. 579.13 crore, which is 8.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

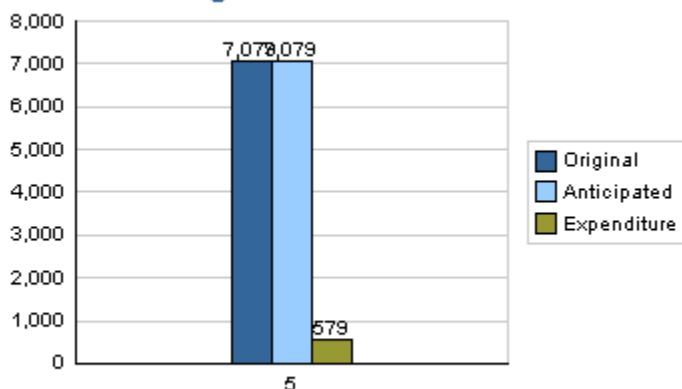

Sector wise current status of projects on the Flash Report

STEEL


Current Status:

Number of Projects	14
Number of Projects On Schedule	2
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 14 projects, 2 projects are on schedule 10 projects are delayed. 2 projects do not have fixed dates of commissioning.

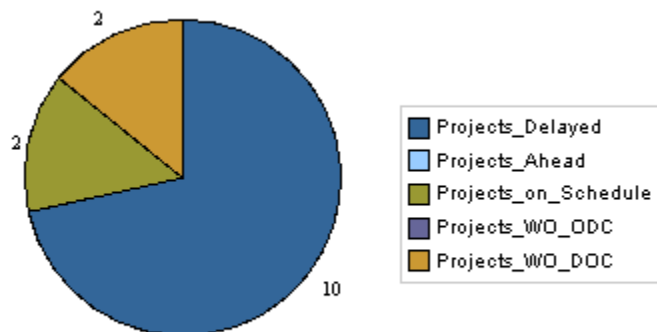


Total No Of Project's:-

14

Investment Scenario

Total original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 32793.01 crore but this was subsequently anticipated to Rs. 39597.41 crore implying a cost overrun of 20.7%. The expenditure incurred on these projects till April, 2019 is Rs. 22967.39 crore, which is 58% of the anticipated cost of the projects.

Figures are in Rs. Crore

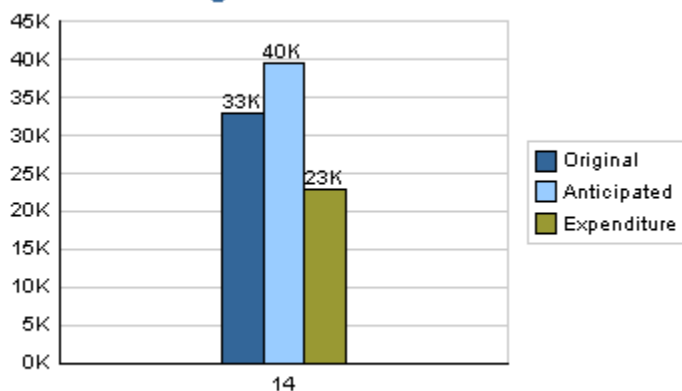

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	140
Number of Projects On Schedule	80
Number of Projects Delayed	39
Number of Projects Ahead	6
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	14

Brief Analysis

Project Status with respect to Original Schedule: Out of 140 projects, 6 projects are ahead of schedule, 80 projects are on schedule 39 projects are delayed. 14 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

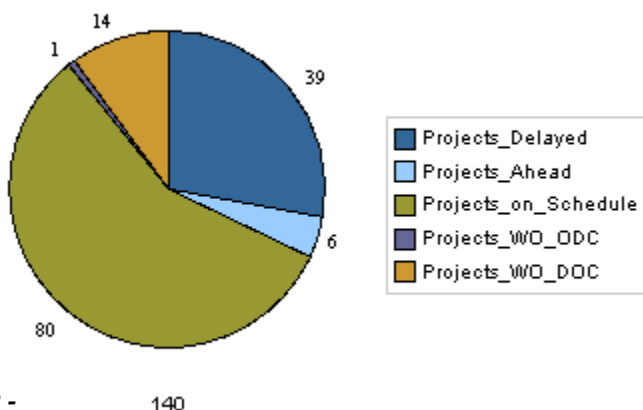


Total No Of Project's:-

140

Investment Scenario

Total original cost of implementation of 140 projects when sanctioned, was of the order of Rs. 229497.78 crore but this was subsequently anticipated to Rs. 234857.89 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till April, 2019 is Rs. 80994.92 crore, which is 34.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

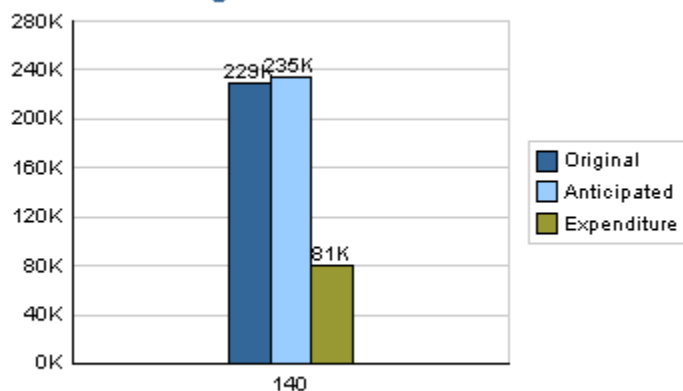

Sector wise current status of projects on the Flash Report

POWER


Current Status:

Number of Projects	77
Number of Projects On Schedule	17
Number of Projects Delayed	53

Number of Projects Without Date Of Commissioning 7

Brief Analysis

Project Status with respect to Original Schedule: Out of 77 projects, 17 projects are on schedule 53 projects are delayed. 7 projects do not have fixed dates of commissioning.

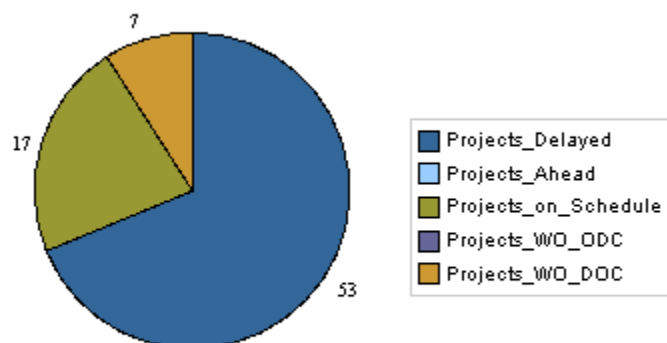


Total No Of Project's:- 77

Investment Scenario

Total original cost of implementation of 77 projects when sanctioned, was of the order of Rs. 287073.06 crore but this was subsequently anticipated to Rs. 345343.53 crore implying a cost overrun of 20.3%. The expenditure incurred on these projects till April, 2019 is Rs. 226754.76 crore, which is 65.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

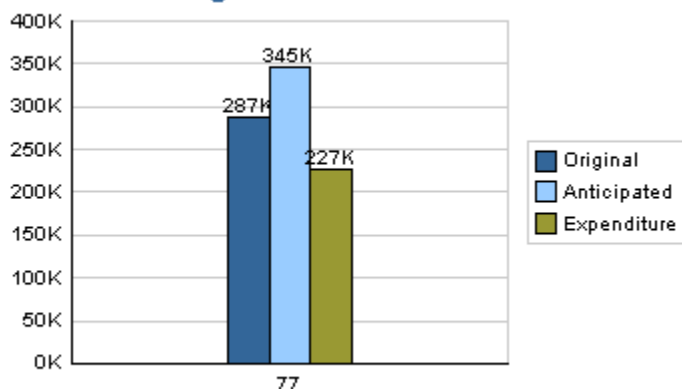

Sector wise current status of projects on the Flash Report

HEAVY INDUSTRY


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.




Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 3272 crore but this was subsequently anticipated to Rs. 5381.3 crore implying a cost overrun of 64.5%. The expenditure incurred on these projects till April, 2019 is Rs. 2624.03 crore, which is 48.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

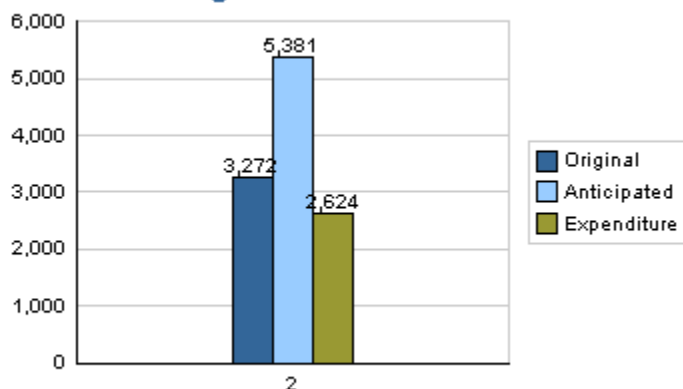

Sector wise current status of projects on the Flash Report

HEALTH AND FAMILY WELFARE


Current Status:

Number of Projects	20
Number of Projects On Schedule	3
Number of Projects Delayed	4

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	7

Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 3 projects are on schedule 4 projects are delayed. 7 projects do not have fixed dates of commissioning. 6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

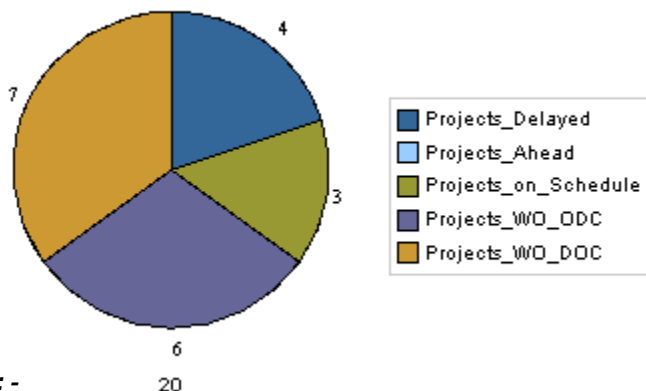


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 8129.23 crore but this was subsequently anticipated to Rs. 8246.52 crore implying a cost overrun of 1.4%. The expenditure incurred on these projects till April, 2019 is Rs. 2946.15 crore, which is 35.7% of the anticipated cost of the projects.

Figures are in Rs. Crore

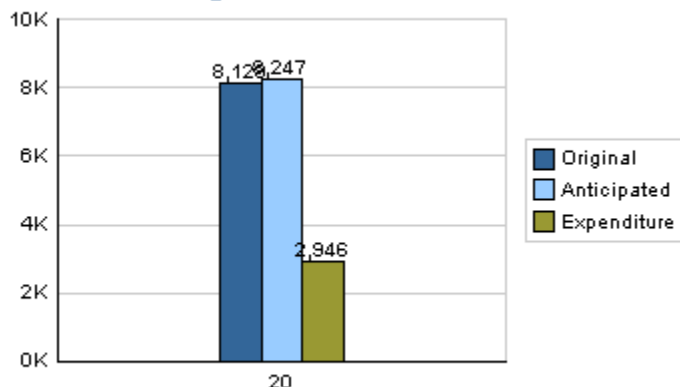

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	364
Number of Projects On Schedule	73
Number of Projects Delayed	92
Number of Projects Ahead	8
Number of Projects Without Original Date of Commissioning	27
Number of Projects Without Date Of Commissioning	164

Brief Analysis

Project Status with respect to Original Schedule: Out of 364 projects, 8 projects are ahead of schedule, 73 projects are on schedule 92 projects are delayed. 164 projects do not have fixed dates of commissioning. 27 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.


Total No Of Project's:-

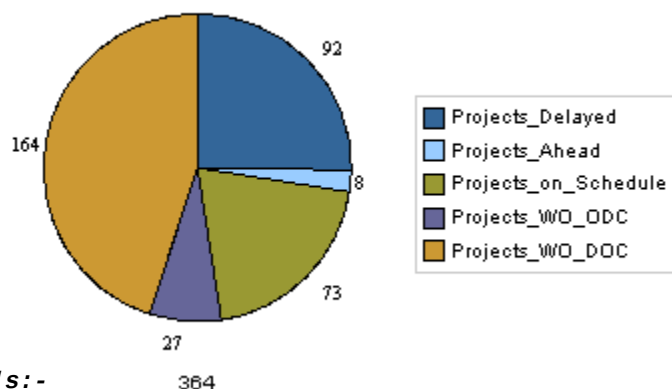

Investment Scenario

Total original cost of implementation of 364 projects when sanctioned, was of the order of Rs. 484549.3 crore but this was subsequently anticipated to Rs. 701059.04 crore implying a cost overrun of 44.7%. The expenditure incurred on these projects till April, 2019 is Rs. 211064.8 crore, which is 30.1% of the anticipated cost of the projects.

Figures are in Rs. Crore

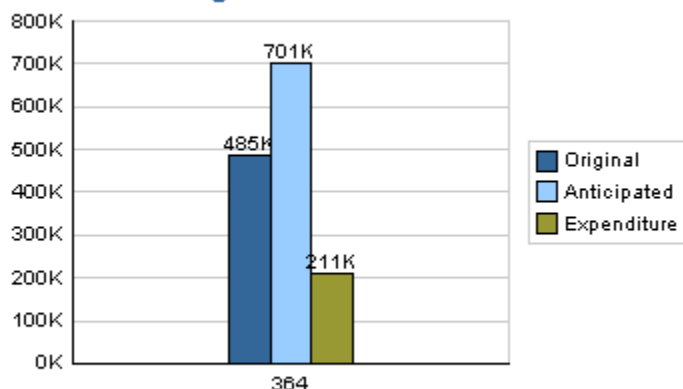

Sector wise current status of projects on the Flash Report


ROAD TRANSPORT AND HIGHWAYS

Current Status:

Number of Projects	652
Number of Projects On Schedule	50
Number of Projects Delayed	126
Number of Projects Ahead	7
Number of Projects Without Original Date of Commissioning	66
Number of Projects Without Date Of Commissioning	403

Brief Analysis

Project Status with respect to Original Schedule: Out of 652 projects, 7 projects are ahead of schedule, 50 projects are on schedule 126 projects are delayed. 403 projects do not have fixed dates of commissioning. 66 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

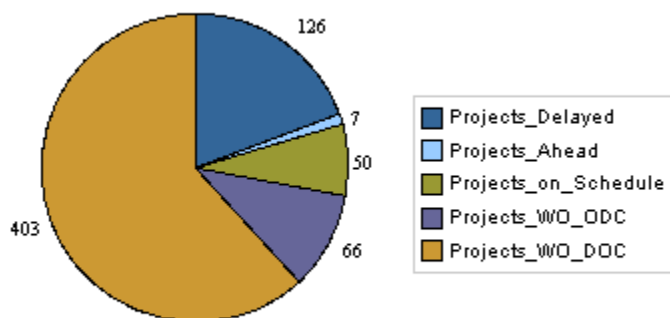


Total No Of Project's:-

652

Investment Scenario

Total original cost of implementation of 652 projects when sanctioned, was of the order of Rs. 428477.95 crore but this was subsequently anticipated to Rs. 441091.58 crore implying a cost overrun of 2.9%. The expenditure incurred on these projects till April, 2019 is Rs. 169517.06 crore, which is 38.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

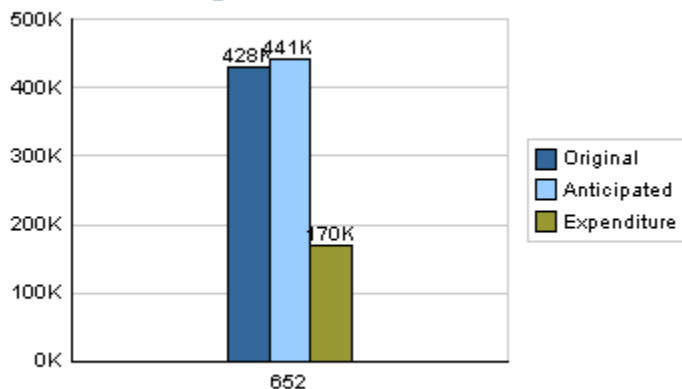

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS


Current Status:

Number of Projects	7
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	4
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 2 projects are on schedule 1 project is delayed. 4 projects do not have fixed dates of commissioning.

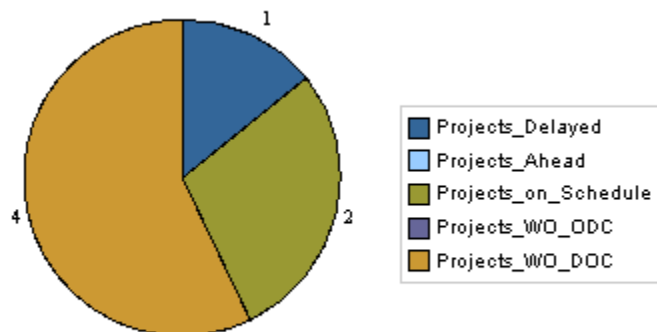


Total No Of Project's:-

7

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 6557.29 crore but this was subsequently anticipated to Rs. 6999.74 crore implying a cost overrun of 6.7%. The expenditure incurred on these projects till April, 2019 is Rs. 2229.89 crore, which is 31.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

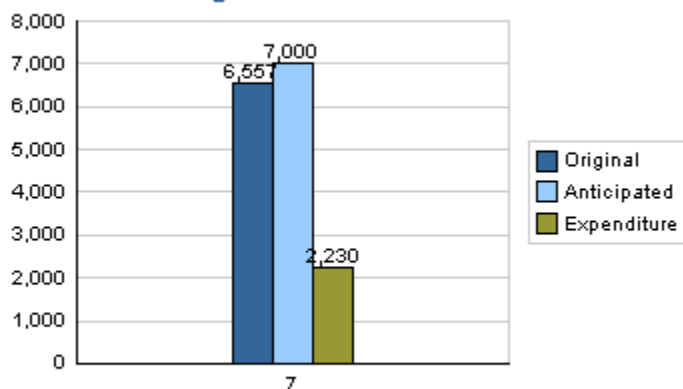

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	5
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed. 2 projects do not have fixed dates of commissioning.

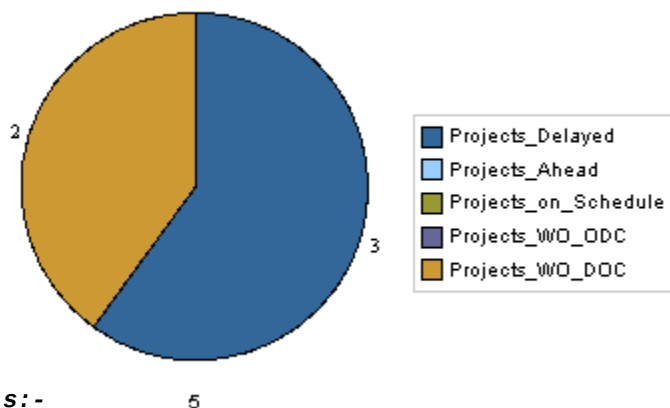


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 16310.53 crore but this was subsequently anticipated to Rs. 27553.13 crore implying a cost overrun of 68.9%. The expenditure incurred on these projects till April, 2019 is Rs. 9169.02 crore, which is 33.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

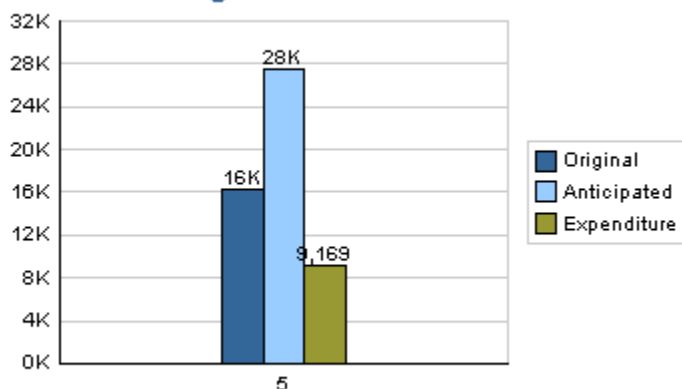

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	57
Number of Projects On Schedule	9
Number of Projects Delayed	21

Number of Projects Without Original Date of Commissioning	3
Number of Projects Without Date Of Commissioning	24

Brief Analysis

Project Status with respect to Original Schedule: Out of 57 projects, 9 projects are on schedule 21 projects are delayed. 24 projects do not have fixed dates of commissioning. 3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

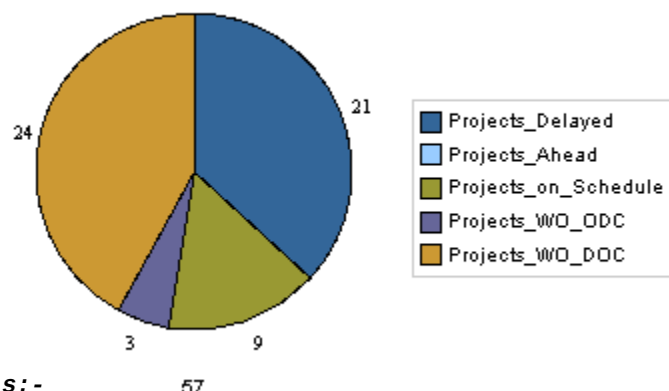


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 57 projects when sanctioned, was of the order of Rs. 160233.35 crore but this was subsequently anticipated to Rs. 166436.66 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till April, 2019 is Rs. 78206.6 crore, which is 47% of the anticipated cost of the projects.

Figures are in Rs. Crore

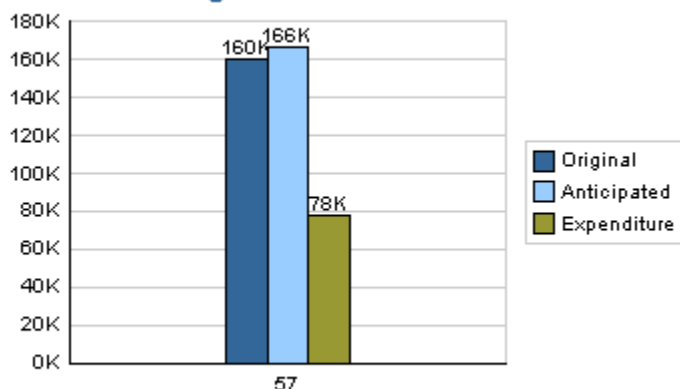

Sector wise current status of projects on the Flash Report

DEFENCE PRODUCTION


Current Status:

Number of Projects	2
Number of Projects On Schedule	1

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 2 projects, 1 project is on schedule 1 project does not have fixed dates of commissioning.

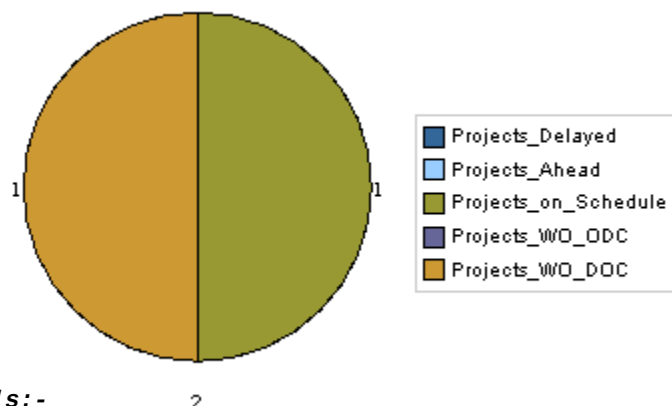


Total No Of Project's:-

2

Investment Scenario

Total original cost of implementation of 2 projects when sanctioned, was of the order of Rs. 453.64 crore but this was subsequently anticipated to Rs. 453.64 crore The expenditure incurred on these projects till April, 2019 is Rs. 201.55 crore, which is 44.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

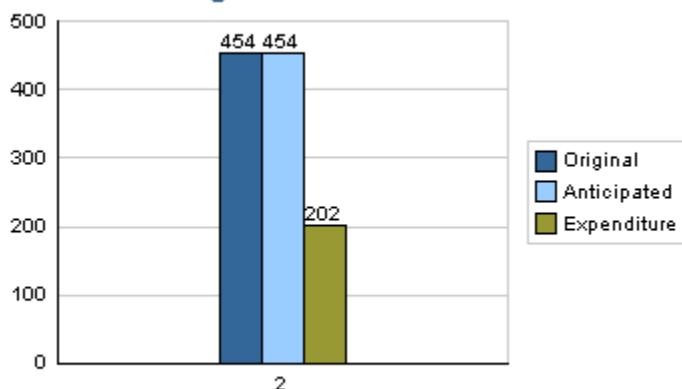

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (APRIL 2019)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	8	2,385.01	2,492.59	156.31
2	ANDHRA PRADESH	70	1,07,777.49	1,11,737.53	57,890.63
3	ARUNACHAL PRADESH	30	16,173.5	34,539.39	18,112.62
4	ASSAM	45	24,146.83	26,425.96	11,130.71
5	BIHAR	92	77,203.9	1,12,701.23	53,195.74
6	CHHATISGARH	44	78,300.5	88,747.57	38,805.95
7	D & N HAVELI	1	6,086.08	5,842.31	4,778.58
8	DELHI	22	55,263.55	62,738.78	42,154.09
9	GOA	10	4,292.52	4,292.52	329.04
10	GUJARAT	47	48,487.41	53,770.51	32,993.97
11	HARYANA	33	22,750.09	24,653.74	11,339.63
12	HIMACHAL PRADESH	12	16,702.17	26,210.39	11,036.45
13	JAMMU AND KASHMIR	12	24,323.57	49,772.57	31,047.43
14	JHARKHAND	48	47,744.98	52,512.74	21,811.59
15	KARNATAKA	47	82,362.96	88,262.78	31,275.24
16	KERALA	25	39,778.48	42,459.1	13,556.8
17	MADHYA PRADESH	76	72,266.49	76,649.63	33,597.8
18	MAHARASHTRA	127	1,85,046.27	1,99,526.36	82,364.08
19	MANIPUR	3	5,188.43	14,543.26	9,724.6
20	MEGHALAYA	8	4,791.25	9,884.79	1,891.67
21	MIZORAM	12	7,570.66	10,145.19	2,802.52
22	MULTI STATE	149	3,30,533.7	4,34,560.31	1,30,948.16
23	NAGALAND	21	13,711.07	14,384.55	734.88
24	ODISHA	85	99,874.49	1,05,744.5	35,269.75
25	PUNJAB	37	18,777.92	18,883.93	6,295.83
26	RAJASTHAN	53	44,518.04	46,273.48	25,695.62
27	SIKKIM	9	3,476.73	6,281.03	433.9
28	TAMIL NADU	73	1,17,053.81	1,36,870.39	62,738.94
29	TELANGANA	42	34,989.1	37,661.78	10,251.79
30	TRIPURA	8	4,001.35	7,266.74	5,864.98
31	UTTAR PRADESH	110	1,42,809.15	1,46,215.66	58,090.8
32	UTTARAKHAND	29	35,073.18	41,560.88	12,177.14
33	WEST BENGAL	65	59,118.49	67,700.99	26,409.64
TOTAL		1,453	18,32,579.17	21,61,313.18	8,84,906.88

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

ATOMIC ENERGY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	3492	-	5771.17
COAL						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
2	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	457.77	-	619.13
3	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	172.08	-	345.12
4	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	207.28	-	249.61
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	152.43	-	203.55
6	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	198.68	-	254.72
HEALTH AND FAMILY WELFARE						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
7	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	HSCC	09/2014	505.58	-	508.29
8	CNCI KOLKATA WEST BENGAL	HSCC	08/2016	244	-	247.47
HEAVY INDUSTRY						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	1718	-	2289
PETROLEUM						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	993	-	1549.85
11	GAIL GAS LTD BENGALURU CGD PROJECT	GAIL	02/2015	749	-	860.14
POWER						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
12	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	3919.59	-	7244.66
13	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	6285.33	-	10723.47
14	BARH STPP(3X660MW) NTPC	NTPC	02/2005	8692.97	15095.67	15932.41
15	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	2978.48	-	3938.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
16	KUDGI STPP STAGE 1	NTPC	01/2012	15166.19	-	15364
17	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	11846	-	11850.13
18	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	5353	-	7128.72
19	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	436.68	533.5	557.22
20	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	330	-	330.23
RAILWAYS						
Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
21	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	158.77	274.56	629.43
22	AMRAVATI-NARKHER NL(CR)	CR	06/1994	663.01	668.34	718.23
23	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	2500	-	17336.24
24	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	631.78	632	731.65
25	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	240	-	537.3
26	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	1125.89	-	2040.42
27	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	511.86	-	967.96
28	NANGALDAM-TALWARA(NL), NR	NR	03/1981	450	-	484.14
29	KARUR-SALEM(NL), SR	SR	02/1997	155.55	-	856.94
30	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	164.36	-	999.64
31	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	247.66	-	972.82
32	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	324.73	-	876.49
33	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	108	-	446.52
34	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	792.46	724.31	944.77
35	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	744.71	-	751.05
36	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	162.87	-	183.72
37	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	625.3	408.76	841.57

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
38	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	280	-	834.87
39	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	1180.19	2531.34	3165.68
40	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	1049.69	-	3544.3
41	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	607.09	-	635.24
42	JIND-SONEPAT (NL), NR	NR	01/2004	238.56	-	722.65
43	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	1185.64	-	1603.22
44	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	4454.17	-	9672.6
45	KOSI BRIDGE (NL), ECR	ECR	04/2002	499.41	-	640.78
46	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	424.6	-	898.83
47	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	218.19	-	379.47
48	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	120	-	210.67
49	HATHUA-BHATNI (N L) (NER)	NER	04/2005	230.03	-	277.14
50	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	133.41	207	384.55
51	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	477.88	283.95	495.4
52	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	732.81	-	2121.12
53	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' - AGASTIYAMPALLI	SR	09/2007	724.69	-	1188.9
54	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	343.17	-	1049.68
55	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	385.2	-	581
56	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	369.9	-	618.19
57	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	1142	3407	3422.67
58	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	2393.47	2393.48	2671.7
59	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	WR	04/2006	117.36	196.95	202.29

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
60	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	195.64	-	455.83
61	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	199.75	-	283.53
62	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	320.66	-	534
63	AJMER-BANGURGRAM	NWR	04/2011	213.39	-	240.62
64	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	242.09	-	329.33
65	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	309.44	-	525.93
66	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	198.68	-	303.72
67	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	271.24	-	468.18
68	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	270.14	-	317.14
69	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	895	984.97	1563.33
70	CHENGANNUR-CHINGAVANAM	SR	04/2006	191.72	-	432.5
71	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	819.23	-	1082.01
72	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	314	486.96	660.21
73	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	632.68	-	666.41
74	PIRPAINTI-BHAGALPUR	ER	04/2011	261.38	-	360.58
75	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	184.06	199.12	255.25
76	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	ER	04/2011	166.89	-	246
77	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	1503.71	-	36195.04
78	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	155.81	-	180.78
79	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	148.77	-	166.55
80	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	332.15	-	538.21
81	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	927.01	-	1052.21
82	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	713.48	-	1773.46

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
83	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	948.04	-	1132.87
84	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	SR	02/2000	200.84	-	394.26
85	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	268.87	-	304.07
86	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	SR	02/2005	600	600	671
87	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	SR	02/2005	241	-	294.63
88	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	NER	04/1997	233	-	348.82
89	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	609.04	1063	1805.98
90	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	180.82	-	462.75
91	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	329.39	-	759.2

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
92	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	280	-	422.51
93	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	199.81	-	211.69
94	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	167.64	-	268.94
95	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	155.04	-	195.35
96	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	245	174.34	270.88
97	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	225	-	312.79
98	NALBARI T BIJNI (AS-7)	NHAI	12/2003	208	-	308.94
99	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	160	-	203.98
100	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	196	-	340.12
101	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	217.61	-	391.12
102	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	NHAI	03/2010	1509.1	-	3187.21
103	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	NHAI	02/2009	1693.75	-	2675.28
104	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1	NHAI	05/2009	1108	-	3965.17

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
	KM)					
105	INDORE-JHABUA-GUJRAT/MP	NHAI	10/2010	1175	-	1342.77
106	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	1585	-	2322.02
107	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	617	-	943.17
108	4 LANING OF NAGPUR-BETUL	NHAI	02/2011	2498.76	-	2531.46
109	PUNE-SATARA(NH-4)	NHAI	10/2010	1724.55	-	2289.31
110	INDORE-DEWAS(NH-3)	NHAI	11/2010	325	-	469.54
111	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	NHAI	07/2010	1987	-	2529.39
112	NASHRI- CHANANI	NHAI	05/2011	2159	-	3986.82
113	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	NHAI	07/2010	1813.76	-	2393.99
114	PATNA-MUZZAFFARPUR	NHAI	08/2010	671.3	-	884.84
115	GHAZIABAD-ALIGARH NH-91	NHAI	02/2011	1141	-	1715.42
116	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	NHAI	09/2011	1250	-	1330.22
117	KANDLA - MUNDRA PORT	NHAI	01/2011	953.88	-	976.79
118	TIRUPATI - TIRUTHANI - CHENNAI	NHAI	04/2011	571	-	582.52
119	JORBAT - BARAPANI	NHAI	01/2011	536	-	844.31
120	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	1535	-	3008.77
121	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	NHAI	09/2011	574	-	768.73
122	2-LANNING WITH PS MOTIHARI-RAXAUL	NHAI	10/2011	375.09	-	494.33
123	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	575	-	842.31
124	2 LANNING OF MUZAFFARPUR - SONBARSA	NHAI	05/2011	511.54	-	565.81
125	SRINAGAR TO BANIHAI	NHAI	06/2011	1100.7	-	2075.87
126	PANIKHOLI-RIMOLI	NHAI	03/2012	1410	-	1555.96

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
127	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	754	-	1363.43
128	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	1078.84	-	2317.74
129	4-LANING OF BRAHAMPURE-FARAKA	NHAI	02/2011	998.79	-	1837.93
130	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	NHAI	12/2011	1047	-	1633.88
131	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	1396.18	-	2614.84
132	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	291.36	-	451.29
133	ETAWAH CHAKERI	NHAI	03/2013	1573	-	1998.25
134	AHMEDABAD TO VADODARA SECTION	NHAI	01/2013	2125.24	-	4659.71
135	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	1928.22	-	3070.11
136	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	1348.2	-	1792.9
137	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	NHAI	11/2013	1916.79	-	1948.92
138	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	1266.6	-	1429.59
139	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	NHAI	04/2014	351.34	-	425.99
140	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	NHAI	04/2014	495.78	-	617.93
141	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	597	-	605.33
142	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	NHAI	11/2012	530.07	-	675.73
143	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	NHAI	09/2015	414.51	-	514.02
144	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	NHAI	09/2015	785.78	-	839.63
145	6 LANING OF AGRA - ETAWAH BYPASS	NHAI	07/2015	1657.2	-	2270
146	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	NHAI	01/2015	972.5	-	1485.07
147	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	NHAI	12/2015	611.65	-	718.15
148	NAGPUR - KONDHALI	NHAI	09/2005	168	-	226.24
149	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	NHAI	02/2008	1673.7	-	3326.93

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(APRIL 2019)

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
150	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	1055	-	1393.4
151	FOUR LANING OF AURANGABAD - YEDISHI	NHAI	07/2015	1871.34	-	3385.9
152	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	NHAI	04/2010	1170.52	-	2051.36
153	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	1665	-	1901.17
154	TRICHY - KARUR	NHAI	03/2007	516	-	627.47
155	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	591.66	-	609.09
156	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	605.84	-	722.46

SHIPPING AND PORTS

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
157	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	MUMBAI PORT	01/2007	366.39	-	411.12
158	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	KPL	02/2015	244.5	258	275.98

URBAN DEVELOPMENT

Sn	Project	Agency	Date of Approval	Cost Original (Rs.crore)	Cost Revised (Rs.crore)	Cumm Expenditure (Rs.crore)
159	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	149.73	173	178.65
160	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	768.88	1070.97	1085.64
161	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	5181.79	-	5188.5
162	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	14600	-	16352.77

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,393.27	12/2020 -	08/2020
4	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	31.02	09/2022 -	06/2021
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	528.48	12/2020 -	02/2020
6	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	591.29	10/2019 -	06/2019
	Total		11,786.00 -	12,784.00	2,739.03		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 575.67	575.67	426.83	06/2016 09/2019	05/2019
8	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 2,187.32	2,187.32	2,133.02	11/2008 06/2019	05/2019
9	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 1,429.38	1,429.38	916.66	01/2019 07/2019	06/2019
10	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 445.89	445.89	258.66	02/2019 12/2019	09/2019
	Total		4,194.38 -	4,638.26	3,735.17		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						
11	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	136.13	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
12	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	475.48	03/2022 -	03/2020
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	612.00	93.63	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
14	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	05/2019
15	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	183.61	03/2022 -	12/2019
16	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	366.71	5.92	01/2022 -	01/2020
	<u>Rail Vikas Nigam Ltd.</u>						
17	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	.22	12/2025 -	03/2025
	<u>Western Railway</u>						
18	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	324.69	03/2021 -	03/2020
	Total		7,034.44 -	7,300.61	1,496.82		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
19	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	02/2020
20	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	233.60	03/2020 -	06/2019
21	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	476.34	03/2020 -	06/2019
22	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32	503.10	15.10	03/2020 -	11/2019
23	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	45.34	03/2020 -	06/2019
24	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]	3/2017	239.68 -	235.90	84.03	03/2020 -	06/2019
25	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	15.00	04/2020 -	11/2019
	Total		3,130.50 -	2,769.55	869.41		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
26	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	3.50	03/2020 07/2020	03/2020
	Total		171.72 -	171.72	3.50		
	Grand Total		27,503.68	27,867.96	8,961.48		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	185.90	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	307.30	03/2022 -	03/2022
4	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	46.93	03/2022 -	03/2022
5	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	78.84	03/2024 -	03/2024
6	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
7	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
	<u>Mahanadi Coal Fields Limited</u>						
8	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	433.20	03/2021 -	03/2021
9	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	79.92	03/2027 -	03/2027
10	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,109.33	03/2029 -	03/2029
11	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,174.58	03/2026 -	03/2026
	<u>Neyveli Lignite Corporation</u>						
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	5,982.50	11/2021 -	11/2021
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.13	09/2019 -	09/2019
14	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	176.87	12/2019 -	12/2019
	<u>Northern Coal Fields Limited</u>						
15	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
16	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	250.33	03/2021 -	03/2021
	<u>Singareni Colliers Company Limited</u>						
17	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
	<u>South-Eastern Coal Fields Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
18	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.35	03/2021 -	03/2021
19	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
20	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.94	03/2023 -	03/2023
21	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
22	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
23	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,900.98	03/2023 -	03/2023
24	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023
25	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	80.25	03/2020 -	03/2020
26	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022
27	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
28	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
29	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	65.52	03/2020 -	03/2020
30	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.54	03/2021 -	03/2021
31	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
32	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	24.29	03/2023 -	03/2023
33	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.40	03/2021 -	03/2021
34	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.66	03/2023 -	03/2023
	<u>Western Coal Fields Limited</u>						
35	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	239.42	03/2025 -	03/2025
36	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	98.04	03/2021 -	03/2021
37	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	409.85	03/2020 -	03/2020
38	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	279.61	03/2020 -	03/2020
39	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.23	03/2022 -	03/2022
40	BHANEAGAON OC - [N06000121]	2/2015	187.94 -	409.68	101.05	03/2023 02/2017	03/2023
41	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	165.09	03/2021 -	03/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
42	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	144.38	03/2021 -	03/2021
43	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
44	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	138.73	03/2020 -	03/2020
45	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	112.45	03/2020 -	03/2020
46	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	206.72	03/2020 -	03/2020
47	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
	Total		70,936.24 -	71,158.78	17,517.41		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
48	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	74.55	08/2020 -	08/2020
	Total		285.95 -	285.95	74.55		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
49	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	69.08	11/2019 -	11/2019
50	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	67.89	11/2019 -	11/2019
51	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	69.23	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
52	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	70.98	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	277.18		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
53	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
54	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
55	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		2,363.00 -	2,363.00	485.35		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
56	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
57	UTKAL D AND E COAL BLOCK - [N10000011	5/2016	534.00 -	534.00	315.25	01/2020 01/2020	01/2020
58	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014	9/2017	166.62 -	166.62	134.98	06/2019 -	06/2019
59	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
60	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
61	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
	Total		7,078.62 -	7,078.62	579.13		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
62	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347	10/2018	206.26 -	206.26	-	03/2021 -	03/2021
63	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260	2/2016	554.00 -	554.00	260.09	02/2020 -	02/2020
64	MMPL PIPELINE REROUTING PROJECT - [N16000261	4/2013	449.58 -	449.58	142.34	12/2019 -	12/2019
65	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
66	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346	9/2018	11,130.00 -	11,130.00	12.63	03/2023 -	03/2023
67	PUNE POL STORAGE DEPOT - [N16000313	8/2016	282.64 -	282.64	88.28	08/2020 -	08/2020
68	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341	8/2017	750.00 -	750.00	29.15	12/2020 -	12/2020
	<u>Chennai Petroleum Corporation Limited</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
69	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	757.22	12/2019 -	12/2019
70	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	62.32	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
71	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	39.19	10/2022 -	10/2022
72	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]	10/2017	221.45 -	221.45	36.75	10/2022 -	10/2022
73	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	967.24	12/2020 -	12/2020
74	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	52.16	10/2022 -	10/2022
75	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	60.93	12/2020 -	12/2020
76	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,177.26	12/2020 -	12/2020
77	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	181.20	25.90	07/2022 -	07/2022
78	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,168.02	12/2020 -	12/2020
79	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,162.20	12/2020 12/2020	12/2020
80	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	-	08/2020 -	08/2020
81	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	117.30	04/2022 -	04/2022
82	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	45.20	07/2022 -	07/2022
83	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	860.14	02/2020 -	02/2020
84	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	192.71	12/2021 -	12/2021
	<u>Hindustan Petroleum Corporation Limited</u>						
85	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	358.80	03/2021 -	03/2021
86	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
87	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,308.78	06/2020 -	06/2020
88	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA - [N16000312]	11/2017	255.00 -	255.00	47.50	11/2020 -	11/2020
89	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
90	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
91	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT - [N16000237]	9/2016	407.00 -	407.00	328.48	09/2019 -	09/2019
92	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	4,501.16	07/2020 -	07/2020
	<u>Indian Oil Corporation Limited</u>						
93	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
94	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	16.56	03/2021 -	03/2021
95	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,451.96	11/2019 -	11/2019
96	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	51.40	10/2020 -	10/2020
97	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
98	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	9.93	01/2021 -	01/2021
99	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	670.40	12/2020 -	12/2020
100	120 TMTPL LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	-	09/2019 -	09/2019
101	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
102	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020
103	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	12.16	10/2021 -	10/2021
104	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	144.71	08/2020 -	08/2020
105	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	4/2018	206.63 -	206.63	5.53	02/2020 -	02/2020
106	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	7.01	10/2021 -	10/2021
107	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	403.95	09/2019 -	09/2019
108	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	20.36	01/2021 -	01/2021
109	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	66.38	04/2021 -	04/2021
110	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	323.69	09/2019 -	09/2019
111	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	0.31	08/2020 -	08/2020
112	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	246.28	10/2019 -	10/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
113	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	13.67	02/2020 -	02/2020
114	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	235.99	10/2021 -	10/2021
115	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	34.33	12/2019 -	12/2019
116	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	96.96	07/2020 -	07/2020
117	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	5.79	06/2020 -	06/2020
118	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
119	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	143.56	06/2020 -	06/2020
120	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
121	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	4.55	01/2021 -	01/2021
122	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	834.52	08/2021 -	08/2021
123	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]	8/2017	315.00 -	315.00	108.80	12/2021 -	12/2021
124	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,683.93	09/2019 -	09/2019
125	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	86.47	02/2020 -	02/2020
126	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,252.80	09/2019 -	09/2019
127	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	8.18	12/2021 -	12/2021
128	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,238.56	07/2019 -	07/2019
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
129	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019
130	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
131	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	145.01	05/2020 05/2020	05/2020
132	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	2,354.21	05/2021 05/2021	05/2021
133	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	345.40	12/2019 -	12/2019
134	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	338.79	03/2026 03/2026	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
135	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	346.77	05/2019 05/2019	05/2019
136	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	358.81	11/2019 11/2019	11/2019
137	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	366.12	11/2019 11/2019	11/2019
138	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	815.29	11/2019 11/2019	11/2019
	<u>Oil India Limited</u>						
139	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	112.73	12/2019 -	12/2019
140	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	2.40	02/2020 -	02/2020
141	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	63.20	10/2020 -	10/2020
	Total		1,10,195.61 -	1,10,728.20	28,531.36		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
142	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,420.87	11/2019 -	11/2019
	<u>Power Grid Corporation Of India Limited</u>						
143	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	109.10	02/2020 02/2020	02/2020
144	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	810.69	02/2020 02/2020	02/2020
145	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	80.77	07/2019 07/2019	07/2019
146	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,051.50	07/2020 -	07/2020
147	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	167.81	06/2019 06/2019	06/2019
148	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	5.00	05/2020 05/2020	05/2020
149	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	530.54	06/2019 06/2019	06/2019
150	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	35.50	06/2019 06/2019	06/2019
151	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	164.25	11/2019 11/2019	11/2019
152	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	28.42	12/2019 12/2019	12/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
153	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244	2/2017	235.53 -	235.53	84.89	06/2019 06/2019	06/2019
154	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247	2/2017	5,070.13 -	5,070.13	1,773.41	04/2020 04/2020	04/2020
155	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219	5/2016	14,733.37 -	14,733.37	6,580.05	11/2019 11/2019	11/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
156	NAITWAR MORI HEP - [N18000265	10/2017	648.33 -	648.33	207.87	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
157	KHURJA SUPER THERMAL POWER PROJECT - [N18000272	3/2019	11,089.42 -	11,089.42	-	09/2023 -	09/2023
158	AMELIA COAL MINE - [N18000252	1/2017	2,104.21 -	1,587.16	296.17	09/2020 -	09/2020
	Total		45,099.58 -	44,582.70	13,346.84		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
159	KALYAN-KASARA 3RD LINE - [N22000233	4/2011	792.89 -	792.89	293.18	03/2021 -	03/2021
160	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358	2/2015	2,449.91 -	2,449.91	125.72	03/2023 -	03/2023
161	PUNE-MIRAJ-LONDA (467 KM) - [N22000359	2/2015	3,627.47 3,627.00	3,627.47	510.70	03/2024 -	03/2024
162	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	2/1997	2,271.50 -	3,712.50	2,075.20	03/2021 -	03/2021
163	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024
164	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29 -	3,168.29	1,108.46	03/2023 -	03/2023
165	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356	2/2015	1,272.19 -	1,272.19	231.61	03/2022 -	03/2022
166	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
167	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00 -	2,081.27	59.41	03/2023 -	03/2023
168	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
169	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362	2/2016	637.95 -	637.95	36.16	03/2023 -	03/2023
170	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250	4/2012	540.02 -	540.02	195.62	03/2022 -	03/2022
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
171	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>East Central Railways</u>						
172	KOSI BRIDGE (NL), ECR - [N220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
173	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
174	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
175	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	582.11	03/2020 -	03/2020
176	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	87.60	03/2022 -	03/2022
177	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	205.59	03/2022 -	03/2022
178	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	209.89	03/2022 -	03/2022
179	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
180	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	374.20	03/2020 -	03/2020
181	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	322.47	03/2022 -	03/2022
	<u>North Central Railway</u>						
182	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
183	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
184	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021
185	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
	<u>North East Frontier Railway</u>						
186	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	399.61	03/2021 -	03/2021
187	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.59	03/2020 -	03/2020
188	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	260.68	03/2021 -	03/2021
189	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	67.41	03/2020 -	03/2020
190	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
191	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
192	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
193	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,568.77	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
194	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
195	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,390.53	03/2023 -	03/2023
196	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	960.26	12/2020 -	12/2020
197	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	284.16	12/2024 -	12/2024
198	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE- GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	1,750.00	1,773.46	03/2020 -	03/2020
199	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	830.71	12/2021 -	12/2021
200	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	363.94	12/2026 -	12/2026
201	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	441.95	12/2024 -	12/2024
202	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	1,061.88	12/2021 -	12/2021
203	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	958.09	970.78	03/2020 -	03/2020
204	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,103.00	1,132.87	03/2020 -	03/2020
205	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	210.07	03/2021 -	03/2021
206	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	633.52	12/2023 -	12/2023
	<u>South Central Railway</u>						
207	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	632.48	03/2021 -	03/2021
208	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	139.69	03/2020 03/2020	03/2020
209	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL- DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
	<u>South East Central Railway</u>						
210	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
211	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
212	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
213	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
214	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
215	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
216	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
217	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
	<u>South Eastern Railway</u>						
218	TAMLUK DIGHA 88.9 KM WITH MM DESHPURAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.58	12/2021 12/2021	12/2021
	<u>South Western Railway</u>						
219	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	498.04	03/2020 03/2020	03/2020
220	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	677.98	03/2020 03/2020	03/2020
	<u>Southern Railway</u>						
221	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
222	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
	<u>West Central Railway</u>						
223	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
224	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
225	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021
	<u>Western Railway</u>						
226	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	700.00	47.80	06/2020 -	06/2020
227	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	385.60	629.92	03/2020 -	03/2020
228	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	691.84	54.87	03/2020 -	03/2020
229	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	1,030.29	1,195.16	03/2022 -	03/2022
230	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	679.79	03/2022 -	03/2022
231	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	645.15	03/2022 -	03/2022
	Total		2,41,075.31 -	2,99,432.19	51,584.30		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Ministry Of Road Transport And Highways</u>						
232	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019
233	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019
234	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019
235	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	-	05/2020 -	05/2020
236	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
237	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
238	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019
239	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	45.92	06/2019 -	06/2019
240	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
241	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	74.52	02/2020 -	02/2020
242	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
243	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
244	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903	3/2019	306.28 -	306.28	-	05/2019 -	05/2019
245	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
246	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
247	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868	3/2018	253.44 -	253.44	-	07/2019 -	07/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
248	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
249	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
250	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
251	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
252	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
253	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
254	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	8/2016	1,388.34 -	1,388.34	1,017.40	09/2019 -	09/2019
255	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	1,377.59	03/2020 -	03/2020
256	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544	3/2016	676.73 -	676.73	623.35	04/2019 -	04/2019
257	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
258	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	970.58	04/2019 -	04/2019
259	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556	3/2016	899.00 -	899.00	512.49	04/2019 -	04/2019
260	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
261	FOUR LANNING OF VIKRAVANDI-SETHIAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652	3/2017	848.45 -	848.45	44.06	03/2020 -	03/2020
262	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
263	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541	1/2016	1,081.57 -	1,081.57	892.00	06/2019 -	06/2019
264	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551	3/2016	1,587.49 -	1,587.49	274.39	04/2019 -	04/2019
265	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602	8/2016	1,664.20 -	1,664.20	500.79	04/2020 -	04/2020
266	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439	7/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
267	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	609.09	07/2019 -	07/2019
268	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	463.21	07/2019 -	07/2019
269	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
270	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
271	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	1,041.10	191.74	04/2019 -	04/2019
	<u>Public Works Dept Of State</u>						
272	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
273	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]	3/2017	202.69 -	202.69	-	11/2019 -	11/2019
274	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0+000 - [N24000910]	3/2018	170.57 -	170.57	8.14	11/2020 -	11/2020
275	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]	3/2018	254.30 -	254.30	-	10/2020 -	10/2020
276	WIDENING TO 2-LANE+PS WITH RECONSTRUCTION OF BRIDGES & CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]	1/2017	373.82 -	373.82	-	09/2019 -	09/2019
277	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
278	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]	2/2018	426.18 -	426.18	-	09/2020 -	09/2020
279	REHABILITATION & UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH-3 - [N24000905]	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
280	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]	2/2018	218.70 -	218.70	-	11/2020 -	11/2020
281	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]	3/2018	191.21 -	191.21	-	11/2019 -	11/2019
	Total		36,216.42 -	36,880.26	10,299.47		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
282	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	297.60	05/2021 -	05/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
283	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	272.73	05/2020 -	05/2020
	Total		2,769.00 -	2,769.00	570.33		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmdc)</u>						
284	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (Sail)</u>						
285	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	-	09/2020 -	09/2020
	Total		1,081.36 -	1,081.36	31.60		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
286	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]	11/2017	171.72 -	171.72	3.50	03/2020 07/2020	03/2020
287	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]	1/2018	430.00 -	430.00	46.28	05/2020 -	05/2020
288	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]	10/2016	209.84 -	209.84	27.18	03/2020 -	03/2020
289	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	33.40	05/2020 -	05/2020
290	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
291	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]	12/2017	188.00 -	188.00	131.55	06/2019 -	06/2019
292	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]	10/2017	271.90 -	271.90	17.39	11/2019 -	11/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
293	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	2,377.05	11/2021 -	11/2021
	<u>National Building Construction Corporation Ltd</u>						
294	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	6/2012	4,264.00 -	4,439.23	3,936.53	11/2019 -	11/2019
	Total		17,344.31 -	17,519.54	6,575.46		
	Grand Total		5,37,100.68	5,96,534.88	1,30,208.01		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	<u>Nuclear Power Corporation Of India Limited</u>						
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69
	Total		14,951.00 -	23,420.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	09/2019	19.86
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>Singareni Colliers Company Limited</u>						
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24
8	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42
9	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85
10	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60
	<u>South-Eastern Coal Fields Limited</u>						
11	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	<u>Western Coal Fields Limited</u>						
12	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
13	BHANEGAON OC - [N06000121	02/2015	187.94 -	409.68	03/2023 -	03/2023	117.98
14	ADASA UG TO OC - [N06000133	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41
	Total		25,725.94 -	28,037.55			
	<u>FERTILISERS</u>						
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
15	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009	10/2014	197.79 -	209.44	11/2016 -	05/2019	5.89
	Total		197.79 -	209.44			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
16	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
17	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
18	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						
19	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
20	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	08/2018 -	11/2019	14.33
	<u>Gas Authority Of India Limited</u>						
21	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
22	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
23	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	10/2014 -	08/2019	133.50
24	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Oil Corporation Limited</u>						
25	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	714.25	10/2017 -	-	17.66
26	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	12/2020 -	12/2020	66.09
27	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	12/2020 -	08/2020	43.82
28	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	12/2018 -	02/2021	33.98
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
29	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
30	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00 171.00	170.70	03/2019 -	05/2019	26.44
	<u>Oil & Natural Gas Corporation Limited</u>						
31	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) [N16000127]	06/2010	202.94 -	330.35	01/2014 -	11/2019	62.78
32	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	1,577.15	05/2013 -	12/2019	83.01
33	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	03/2015 -	12/2019	29.42
34	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
35	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	03/2023 -	03/2022	38.20
	<u>Oil India Limited</u>						
36	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
37	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
38	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	682.90	02/2020 -	02/2020	25.55
	Total		27,989.65 -	36,251.99			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
39	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69
40	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
41	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	03/2020	10.55
42	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
43	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	02/2020	9.64
44	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	09/2021	5.55
45	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
46	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
47	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	15,095.67	01/2011 -	08/2021	73.65
48	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
49	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	03/2020	7.55
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
51	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	01/2020	12.95
52	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>North East Electric Power Corporation</u>						
53	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]	12/2004	2,496.90 -	7,419.34	12/2009 06/2016	06/2019	197.14
	<u>Power Grid Corporation Of India Limited</u>						
54	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	09/2010 -	04/2019	54.59
55	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	10/2012 -	12/2019	5.14
56	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	08/2013 -	03/2022	32.24
57	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	04/2016 -	08/2019	38.61

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
58	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	02/2014	539.82 -	575.67	06/2016 -	05/2019	6.64
59	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	11/2016 -	12/2019	4.61
60	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58 -	225.28	02/2016 -	05/2019	14.60
61	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP - [N18000180]	01/2015	268.80 -	340.88	03/2018 -	05/2019	26.82
62	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	07/2017 -	06/2019	27.92
63	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	06/2014 -	09/2019	31.17
64	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,187.32	11/2008 -	05/2019	22.93
65	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	04/2016	790.13 -	790.30	06/2019 -	06/2019	.02
66	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
67	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Satluj Jal Vidyut Nigam Limited</u>						
68	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	05/2019	37.96
	<u>Thdc India Limited</u>						
69	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42 -	294.60	02/2014 -	10/2019	50.75
70	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2022	64.77
71	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,61,106.73 -	2,19,894.25			
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
72	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	298.70	03/2019 -	03/2019	62.28
73	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44
74	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	29.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
75	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
76	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
77	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
78	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
79	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	- -	-	143.17
80	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	03/2020 -	03/2020	207.99
	<u>East Central Railways</u>						
81	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	- -	03/2021	192.42
82	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	- -	03/2023	290.95
83	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	56.73
84	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
85	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
86	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
87	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	-	323.32
88	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
89	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
90	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	- -	03/2021	296.21
91	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
92	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
93	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
94	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37
95	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
96	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
97	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	04/1998	180.82 -	528.26	- -	-	192.15
98	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	566.41	- -	12/2021	71.96
	<u>East Coast Railway</u>						
99	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
100	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96
101	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43
102	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2020	.07
103	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
104	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168	04/2008	445.25 -	2,860.55	- -	-	542.46
105	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	- -	-	32.26
106	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	- -	-	818.15
107	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00 -	729.92	- -	03/2021	124.59
108	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	2,614.36	- -	03/2022	590.61
109	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
110	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26
111	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	635.03	02/2013 -	-	4.60
112	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116	04/2009	259.51 -	533.59	02/2012 -	09/2016	105.61
113	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	- -	-	44.46
114	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242	04/2003	337.96 -	355.44	- -	-	5.17
115	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	665.75	02/2012 -	12/2013	33.16

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
116	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]	04/2009	257.42 -	258.73	03/2014 -	-	.51
117	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	259.23	- -	-	3.31
118	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	-	6.48
119	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	1,125.89 -	1,988.38	03/2016 -	03/2020	76.61
120	GHUTIASHARIF-CANNING (ER) - [N22000117]	04/2009	193.08 -	612.45	12/2011 -	09/2012	217.20
121	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	544.72	03/2006 -	01/2006	33.84
122	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	-	51.19
123	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	332.14	- -	-	27.07
124	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]	04/2010	174.56 -	175.99	- -	-	.82
<u>Metropolitan Rapid Transport Projects</u>							
125	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
126	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,973.73	03/2004 -	03/2020	500.22
127	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	06/2013 -	-	48.06
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,986.04	03/2014 -	-	50.68
<u>North Central Railway</u>							
129	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	634.48	03/1994 -	-	299.62
130	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	245.39	12/2008 -	-	104.49
131	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	-	300.67
132	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
<u>North East Frontier Railway</u>							
133	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51
134	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
135	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56
136	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,300.00	12/2008 -	03/2019	179.62
137	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
138	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
139	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
140	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
141	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	1,142.00 -	3,407.00	03/2014 -	03/2019	198.34
142	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2020	7.86
143	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
144	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
145	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,733.20	03/2007 -	04/2016	93.65
146	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11
147	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
148	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
149	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
150	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
151	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
152	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00	03/2019 -	03/2019	75.48
153	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]	04/2012	246.07 -	398.93	03/2019 -	03/2019	62.12
154	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
	<u>North Eastern Railway</u>						
155	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56	06/2018 -	-	89.54

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
156	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
157	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	-	234.77
158	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
159	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
160	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
161	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	-	267.13
162	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	435.00	- -	-	122.35
163	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	378.26	08/2018 -	-	89.37
164	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
165	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
166	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
167	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16
168	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	03/2019	196.84
169	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
170	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
<u>North Western Railway</u>							
171	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	12/2021	93.87
172	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
173	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
174	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	10/2020	46.55
175	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
176	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,261.71	- -	-	104.62
177	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	09/2019	24.47

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
178	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	- -	-	33.76
179	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	- -	-	33.81
180	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35
181	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	12/2019	44.16
	<u>Northern Railway</u>						
182	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
183	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
184	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	12/2011 -	-	117.77
185	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
186	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
187	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
188	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96
189	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	40.11
190	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
191	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
192	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
193	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
194	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	03/2019	188.58
195	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97
196	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93
197	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
198	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
200	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
201	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
202	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
203	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
204	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18
205	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,750.00	03/2020 -	03/2020	145.28
206	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,103.00	03/2020 -	03/2020	16.35
207	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
208	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
209	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
210	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
211	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
212	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
213	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
214	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
215	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
216	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	184.97	03/2022 -	03/2022	54.49
	<u>South East Central Railway</u>						
217	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	1,101.16	- -	-	186.92
218	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	511.86 -	1,756.00	04/2020 -	04/2020	243.06
219	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
220	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]	04/2010	585.93 -	1,420.39	02/2019 -	-	142.42
221	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	403.00	12/2021 -	12/2021	75.98
222	CHHINDWARA-MANDLA FORT GC - [N22000481]	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22
223	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	04/2008	872.00 -	1,279.00	12/2019 -	12/2019	46.67
224	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,919.00	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
225	MM FROM BURAMARA-CHAKULIA - [N22000305]	04/2008	466.48 -	1,000.00	- -	12/2024	114.37
226	MM FROM PANSKURA-GHATAL NL - [N22000309]	04/2011	276.69 -	426.00	- -	03/2030	53.96
227	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76
228	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	749.69	06/2005 -	-	155.02
229	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]	04/2012	148.77 -	377.00	12/2016 -	09/2019	153.41
230	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89
231	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99
232	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]	04/2011	289.64 -	760.00	- -	-	162.39
233	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	230.00	03/2015 -	-	53.44
234	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	525.81	12/2015 -	02/2019	69.92
235	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	365.00	- -	01/2020	41.36
236	ARA-BHABHUA ROAD (NL) - [N22000166]	04/2008	633.87 -	2,396.88	- -	-	278.13
237	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76
238	TAMLUK DIGHA 88.9 KM WITH MM DESHPURAN NADIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90
239	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
240	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
241	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]	04/2007	179.65 -	1,350.91	- -	12/2023	651.97
242	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	12/2023	24.09
243	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65
244	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14
245	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	12/2023	12.38
246	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,870.41	03/2019 -	03/2021	15.84
247	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	889.52	03/2017 -	03/2020	37.96
	<u>Southern Railway</u>						
248	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	- -	-	141.40
249	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	920.00	- -	-	491.45
250	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
251	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 -	2,072.50	02/2019 -	-	185.98
252	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	1,065.00	- -	-	210.34
253	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	227.40 -	900.00	- -	-	295.78
254	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	2,300.00	- -	-	294.63
255	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	- -	-	79.80
256	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
257	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	2,350.00	- -	-	348.88
258	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	1,500.00	- -	-	78.78
259	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
260	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC [N22000188]	04/1998	271.24 -	520.00	- -	-	91.71
261	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	-	69.20

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
262	ERODE-PALANI - [N22000199]	04/2008	288.57 -	1,140.00	- -	-	295.05
263	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	450.00	- -	03/2020	173.71
264	CHENGANNUR-CHINGAVANAM - [N22000203]	04/2006	191.72 -	369.83	- -	-	92.90
265	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 -	1,800.00	03/2019 -	-	1,391.30
266	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 -	231.67	04/2014 -	03/2020	23.72
267	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 -	302.02	03/2005 -	-	12.33
268	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00 600.00	645.54	03/2010 -	-	7.59
269	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55 -	330.32	03/2009 -	-	65.53
270	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 -	1,182.31	03/2020 -	03/2020	55.57
	<u>West Central Railway</u>						
271	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 -	2,713.09	03/2021 -	03/2021	538.98
272	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	6,093.31	05/2008 -	03/2023	2,360.35
273	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13 -	1,260.61	03/2022 -	03/2022	116.55
	<u>Western Railway</u>						
274	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95	203.00	03/2011 -	-	72.97
275	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	03/2019	1.06
276	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	858.96	03/2019 -	03/2022	167.87
	Total		1,72,046.28 -	3,98,507.24			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
277	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	08/2015 -	-	3.84
278	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]	03/2015	157.18 162.00	162.00	07/2015 -	-	3.07

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
279	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	05/2016 -	-	.26
280	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]	01/2015	326.63 327.00	327.00	04/2018 -	-	.11
281	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]	02/2015	239.91 240.00	240.00	10/2017 -	-	.04
282	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]	12/2013	319.80 320.00	320.00	05/2016 -	-	.06
283	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	06/2016 -	-	.02
284	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]	03/2014	162.51 163.00	163.00	05/2016 -	-	.30
285	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	11/2019 -	11/2019	.17
286	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	- -	-	.06
287	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
288	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]	12/2016	138.93 155.00	155.00	01/2017 -	01/2020	11.57
289	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
290	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	05/2019	92.75
291	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	-	80.68
292	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	05/2008 -	05/2019	4.99
293	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	331.23	07/2009 -	-	68.99
294	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
295	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58
296	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
297	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
298	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83
299	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW [N24000609	09/2015	771.18 -	7,558.00	- -	-	880.06
300	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
301	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
302	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
303	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
304	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
305	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
306	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23
307	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
308	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
309	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
310	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
311	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
312	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
313	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
314	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292	11/2014	573.96 605.00	605.00	- -	-	5.41

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
315	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]	12/2011	156.63 276.00	276.00	02/2012 -	-	76.21
316	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]	10/2014	295.47 -	313.27	02/2017 -	-	6.02
317	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]	03/2011	218.31 -	339.82	12/2015 -	-	55.66
318	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24
319	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]	01/2014	267.16 352.00	352.05	11/2017 -	-	31.78
320	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]	11/2014	297.78 330.00	330.00	02/2017 -	-	10.82
321	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]	12/2009	104.00 -	201.00	09/2010 -	-	93.27
322	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 & NH-10 O - [N24000871]	08/2014	600.87 720.97	720.97	11/2017 -	11/2017	19.99
323	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]	08/2014	823.20 937.76	937.76	11/2017 -	07/2019	13.92
324	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39
325	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]	04/2014	279.70 398.22	398.22	08/2017 -	08/2019	42.37
	Total		28,447.55 -	41,837.22			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
326	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]	02/2015	244.50 258.00	275.98	12/2017 -	-	12.88
	<u>Mumbai Port Trust</u>						
327	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]	01/2007	366.39 -	669.46	12/2010 -	-	82.72
	<u>Port Trust</u>						
328	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Antici Pated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
329	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	22,542.00	05/2015 -	10/2019	45.20
	<u>Rastriya Ispat Nigam Limited</u>						
330	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2020	42.39
	Total		15,868.00 -	23,030.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
331	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	08/2017	215.30 -	219.60	05/2018 -	05/2019	2.00
332	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	01/2018	231.80 -	240.10	10/2018 -	05/2019	3.58
	<u>Department Of Telecommunication</u>						
333	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,781.10 -	25,123.70			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
334	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00 -	488.28	05/2017 -	06/2019	25.85
335	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
336	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.57
337	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013 -	10/2019	132.80
338	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.49	07/2019 -	12/2019	1.85
	<u>Chennai Metro Rail Ltd</u>						
339	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(April 2019)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>Hindustan Steelwork Construction Limited</u>						
340	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	227.00	12/2016 -	-	12.04
341	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]	10/2011	175.49 206.71	206.71	12/2016 -	-	17.79
342	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	44.80
343	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	17.50
	<u>Kochi Metro Rail Corporation Ltd</u>						
344	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
345	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		28,109.46 -	34,312.77			
	Grand Total		4,92,093.25	8,37,632.17			

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,771.17	09/2010 -	10/2021	133	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	13,469.00	12/2015 11/2016	06/2020	54	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	10,749.00	12/2016 03/2017	12/2020	48	0	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	13,910.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	75,589.00	43,899.17					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	40.28	
	Total		314.61 -	441.33	85.79					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
6	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	344.32	04/2015 -	04/2019	48	0	
	<u>Central Coal Fields Limited</u>									
7	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	104.04	03/2011 -	03/2021	120	0	
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	179.16	03/2012 -	03/2021	108	0	
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	366.52	03/2016 -	03/2021	60	0	
10	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	89.30	03/2014 -	03/2021	84	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
11	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND <u>Eastern Coal Fields Limited</u>	08/2008	706.40 -	706.40	185.62	07/2012 -	03/2022	116	0	
12	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL <u>Mahanadi Coal Fields Limited</u>	08/2012	1,055.05 -	1,055.05	434.55	03/2018 -	03/2020	24	0	
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [N060100092]MCL, ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	0	
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	467.50	03/2017 -	03/2020	36	0	
15	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	29.93	03/2018 -	03/2020	24	0	
16	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	249.61	03/2012 -	03/2021	108	0	
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	404.31	03/2013 -	03/2021	96	0	
18	JAGANNATH RE-ORGANISATION OC. (6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	70.05	03/2019 -	03/2021	24	0	
19	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	619.13	03/2013 -	03/2022	108	0	
20	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	345.12	03/2010 -	03/2022	144	0	
21	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA <u>Neyveli Lignite Corporation</u>	05/2014	479.15 -	479.15	194.57	03/2019 -	03/2024	60	0	
22	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,300.55	12/2015 06/2019	09/2019	45	19.86	
23	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU <u>Singareni Colliers Company Limited</u>	04/2013	1,458.17 709.06	709.06	430.69	06/2015 09/2019	09/2019	51	-51.37	
24	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 384.32	384.32	75.36	07/2016 -	03/2020	44	-7.91	
25	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 415.37	415.37	175.42	03/2016 03/2019	03/2020	48	-3.5	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
26	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 442.42	442.42	68.57	03/2019 03/2019	03/2020	12	11.42	
27	KOYAGUDEM OPENCAS-2 PROJECT - [N06000146]SCCL,TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	0	
28	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 164.04	164.04	104.08	03/2015 03/2021	03/2021	72	-32.3	
29	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 349.28	349.28	2.82	03/2015 03/2021	03/2021	72	114.6	
30	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 473.22	473.22	417.24	03/2015 03/2021	03/2021	72	5.85	
31	KAKATIYAKHANI OPENCAS-3 PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	50.72	03/2019 -	03/2022	36	0	
32	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 489.62	489.62	329.15	03/2012 03/2023	03/2023	132	16.86	
33	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 448.86	448.86	203.77	03/2012 03/2024	03/2024	144	80.24	
	<u>South-Eastern Coal Fields Limited</u>									
34	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	459.49	203.55	03/2015 -	03/2020	60	201.44	
35	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	0	
36	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	207.31	03/2014 -	03/2021	84	0	
	<u>Western Coal Fields Limited</u>									
37	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	.07	03/2023 03/2024	03/2024	12	15.41	
38	KAMPTEE DEEP OC MINE - [N06000141]WCL,MAHARASHTRA	11/2015	277.65 313.34	313.34	37.51	03/2021 09/2018	03/2024	36	12.85	
	Total		19,498.59 -	20,712.21	12,999.38					
	<u>FERTILISERS</u>									
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
39	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF,MAHARASHTRA	10/2014	197.79 209.44	209.44	161.24	11/2016 04/2019	05/2019	30	5.89	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Total		197.79 -	209.44	161.24					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
40	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC, CHHATISGARH	01/2010	15,525.00 -	22,542.00	15,401.64	05/2015 10/2019	10/2019	53	45.2	
	<u>Rastrya Ispat Nigam Limited</u>									
41	FORGED WHEEL PLANT - [N12000116]RINL, UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,094.53	09/2018 -	06/2019	9	0	
42	CENTRAL DISPATCH YARD - [N12000119]RINL, ANDHRA PRADESH	08/2015	320.66 -	320.66	190.91	08/2018 -	06/2019	10	0	No
43	ADDITIONAL WATER STORAGE RESERVOIR (KBR-II) - [N12000120]RINL, ANDHRA PRADESH	07/2015	465.85 -	465.85	382.25	07/2018 -	06/2019	11	0	No
44	COKE OVEN BATTERY-5 - [N12000117]RINL, ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,207.76	12/2017 -	09/2019	21	-12.53	No
45	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL, ANDHRA PRADESH	12/2009	343.00 -	488.40	249.30	10/2016 -	03/2020	41	42.39	No
	<u>Steel Authority Of India Limited (Sail)</u>									
46	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL, ODISHA	04/2015	3,127.30 -	3,127.30	2,749.95	04/2018 -	05/2019	13	0	
47	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL, JHARKHAND	05/2015	1,154.18 -	1,154.18	910.60	12/2017 -	06/2019	18	0	
48	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	423.33	10/2017 -	06/2020	32	0	
49	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	84.26	06/2019 -	06/2020	12	0	
	Total		26,773.72 -	33,578.12	22,694.53					
	<u>PETROLEUM</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Bharat Petroleum Corporation Limited</u>									
50	HALDIA LPG IMPORT FACILITY - [N16000223]BPCL, WEST BENGAL	03/2015	694.00 1,097.54	694.00	568.96	10/2018 06/2019	06/2019	8	0	
51	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 5,245.96	5,245.96	2,868.71	08/2018 11/2019	11/2019	15	14.33	
52	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]BPCL, KERALA	02/2016	3,313.00 3,288.96	3,288.96	718.31	02/2020 10/2020	10/2020	8	-73	
	<u>Gas Authority Of India Limited</u>									
53	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	03/2015	3,957.00 3,561.00	3,397.00	2,543.54	12/2018 -	05/2019	5	-14.15	
54	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL, GUJARAT	09/2018	225.54 -	225.54	-	01/2018 -	02/2021	37	0	
55	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL, MULTI STATE	06/2009	2,915.00 3,030.00	3,049.47	2,112.19	12/2012 02/2019	02/2022	110	4.61	
	<u>Hindustan Petroleum Corporation Limited</u>									
56	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	12/2009	309.81 723.40	723.40	645.53	10/2014 08/2019	08/2019	58	133.5	
	<u>Indian Oil Corporation Limited</u>									
57	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL, ODISHA	03/2014	3,150.00 -	3,150.00	2,589.31	09/2017 06/2019	06/2019	21	0	
58	FUEL QUALITY UPGRADATION (DHD/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL, BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	06/2019	7	0	
59	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL, ASSAM	06/2016	423.00 -	423.00	256.37	08/2019 -	09/2019	1	0	
60	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY - [N16000277]IOCL, ODISHA	05/2016	429.00 -	429.00	290.69	01/2019 12/2019	12/2019	11	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
61	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	16.55	06/2020 -	08/2020	2	0	
62	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	236.57	07/2018 10/2020	10/2020	27	0	
63	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	32.67	02/2020 -	10/2020	8	0	
64	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT	10/2017	906.00 -	906.00	27.50	02/2020 10/2020	10/2020	8	0	
65	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	428.96	12/2018 -	02/2021	26	33.98	
66	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL,WEST BENGAL	04/2017	163.02 -	163.02	39.00	04/2020 -	03/2021	11	0	
67	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	20.65	01/2021 -	04/2021	3	0	
68	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	5.39	04/2021 -	07/2021	3	0	
69	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	4.04	10/2020 -	08/2021	10	0	
70	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	14.73	01/2021 -	10/2021	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
71	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	30.32	08/2021 -	11/2021	3	0	
72	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	8.03	04/2022 -	02/2023	10	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
73	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 171.00	170.70	132.43	03/2019 -	05/2019	2	26.44	
74	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	176.25	12/2019 -	02/2020	2	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
75	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]ONGC,ANDHRA PRADESH	04/2017	420.76 -	420.76	105.21	09/2018 04/2019	04/2019	7	0	
76	DAMAN DEVELOPMENT PROJECT - [N16000198]ONGC,D & N HAVELI	08/2014	6,086.08 5,842.31	5,842.31	4,778.58	05/2019 10/2019	10/2019	5	-4.01	
77	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,ASSAM	06/2010	202.94 341.70	330.35	129.67	01/2014 11/2019	11/2019	70	62.78	
78	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	2,132.88	03/2013 12/2019	12/2019	81	-3.5	
79	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,577.15	1,577.15	1,240.37	05/2013 03/2019	12/2019	79	83.01	
80	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	1,906.55	03/2015 12/2019	12/2019	57	29.42	
81	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]ONGC,MAHARASHTRA	11/2014	6,068.80 6,068.80	5,296.93	4,731.48	04/2019 12/2019	12/2019	8	-12.72	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
82	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]ONGC,MAHARASHTRA	01/2015	4,619.94 4,619.94	4,619.94	4,255.37	12/2017 03/2020	03/2020	27	0	
83	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]ONGC,MAHARASHTRA	08/2015	2,818.88 -	2,818.88	2,073.56	03/2019 05/2020	05/2020	14	0	
84	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 -	3,247.19	2,167.85	04/2018 05/2020	05/2020	25	1.77	
85	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	221.40	03/2019 -	05/2020	14	0	
86	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	34,012.00	2,465.32	06/2020 08/2021	08/2021	14	0	
	<u>Oil India Limited</u>									
87	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	0	
88	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	220.73	03/2017 -	12/2019	33	24.47	
	Total		95,490.39 -	98,165.42	41,019.75					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
89	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,086.32	04/2020 -	12/2023	44	0	
	<u>National Hydro-Electric Power Corporation</u>									
90	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,394.80	7,244.66	09/2009 -	12/2021	147	139.69	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>National Thermal Power Corporation</u>									
91	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 -	05/2019	60	49.41	
92	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC, UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,893.00	12/2016 -	08/2019	32	0	
93	KHARGONE STPP STAGE I (1320 MW) - [N18000205]NTPC, MADHYA PRADESH	03/2015	9,870.51 -	11,148.86	7,697.03	09/2019 01/2020	01/2020	4	12.95	
94	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]NTPC, ODISHA	02/2014	12,532.44 -	13,740.53	9,101.85	08/2018 02/2020	02/2020	18	9.64	
95	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC, CHHATISGARH	12/2012	11,846.00 -	12,739.82	11,850.13	06/2017 03/2020	03/2020	33	7.55	
96	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC, MADHYA PRADESH	03/2013	11,638.55 -	12,865.92	11,086.44	09/2017 03/2020	03/2020	30	10.55	
97	TANDA TPP STAGE-II (2X660 MW) - [N18000175]NTPC, UTTAR PRADESH	09/2014	9,188.98 -	9,188.98	5,961.47	03/2019 03/2020	03/2020	12	0	
98	NGGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR	01/2013	12,964.60 -	13,731.26	12,695.00	01/2018 -	05/2020	28	5.91	
99	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC, UTTARAKHAND	11/2006	2,978.48 -	3,846.30	3,938.20	03/2013 12/2020	12/2020	93	29.14	
100	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC, TELANGANA	01/2016	10,598.98 -	10,598.98	4,370.06	07/2020 02/2021	02/2021	7	0	
101	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 15,095.67	15,095.67	15,932.41	01/2011 08/2021	08/2021	127	73.65	
102	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC, JHARKHAND	02/2014	14,366.58 -	15,164.05	8,617.47	02/2019 09/2021	09/2021	31	5.55	
103	RAMMAM-III HEP (3X40 MW) - [N18000178]NTPC, WEST BENGAL	09/2014	1,381.84 -	1,381.84	429.14	09/2019 02/2022	02/2022	29	0	
	<u>North East Electric Power Corporation</u>									
104	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, ARUNACHAL PRADESH	12/2004	2,496.90 7,419.34	7,419.34	7,131.10	12/2009 06/2019	06/2019	114	197.14	
	<u>Power Grid Corporation Of India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
105	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 738.48	738.48	689.46	09/2010 04/2019	04/2019	103	54.59	
106	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,187.32	2,187.32	2,133.02	11/2008 06/2019	05/2019	126	22.93	- Implementation of balance 01 line (Edamam-Muvattupuzha line) was affected due to severe ROW problem (long pending) in Kerala. 1 Tower Erection is held up due to court case filed by land owner, order pending.
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 575.67	575.67	426.83	06/2016 09/2019	05/2019	35	6.64	
108	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	152.32	02/2016 04/2019	05/2019	39	14.6	
109	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	248.10	03/2018 03/2019	05/2019	14	26.82	Progress affected due to ROW compensation issue. 1.6 Km stringing stretch was held up due to severe ROW which is now being resolved with the help of administration.
110	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	74.71	03/2018 03/2018	05/2019	14	0	
111	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 562.25	562.25	195.50	03/2019 03/2019	05/2019	2	0	
112	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 608.24	608.24	388.00	04/2019 04/2019	05/2019	1	0	
113	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	187.24	04/2016 12/2017	06/2019	38	0	
114	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 260.03	260.03	188.36	07/2017 06/2019	06/2019	23	27.92	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
115	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 844.64	844.64	341.30	04/2019 04/2019	06/2019	2	0	
116	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 1,429.38	1,429.38	916.66	01/2019 07/2019	06/2019	5	0	:- Bhadla (PG) - Bhadla (RVPN) line alongwith 1x500 MVA ICT at Bhadla S/S charged in Apr'19. Progress of 765 KV Bhadla-Bikaner line is getting affected due to delay in forest clearance, awaited. ROW also being faced.
117	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 322.30	322.30	127.38	02/2019 06/2019	06/2019	4	0	Work of downstream system yet to be taken up by UT Chandigarh. Underground cable laying done in 5 Kms. 05 locations under severe ROW. Land owners have taken stay from Hon'ble Court.
118	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,130.07	04/2019 -	06/2019	2	0	
119	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 1,891.41	1,891.41	1,230.98	04/2016 08/2019	08/2019	40	38.61	Severe ROW problem at Rajarhat area due to protest by political groups. Work in Rajarhat was on hold since Jan'17. Work of TL resumed in Jun'18 & substation resumed in Aug'18 after intervention from State and Distt. Admn. Presently, works of TL at 2 loc. in Distt. Pargana 24 South are held up.
120	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 639.46	639.46	518.50	06/2014 09/2019	09/2019	63	31.17	. Issues are being resolved with the help of State/ District admn. Slow progress in stgg. due to high compensation demand. Work almost stopped in Bangalore Urban area (6.5 km) due to ROW.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
121	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 871.62	871.62	496.12	10/2017 09/2019	09/2019	23	0	04 locs. under severe ROW problem. Line linked with Tehri Generation completion expected by December 2020.
122	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 3,519.59	3,519.59	2,215.60	05/2019 05/2019	09/2019	4	0	Defence aviation clearance received with condition of reduction in tower height at 29 locn. for different route. New application submitted for defence aviation clearance on 31.12.18. NOC for revised route received on 23.04.19.
123	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 408.46	408.46	221.54	01/2019 09/2019	09/2019	8	0	
124	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 175.64	175.64	83.54	09/2018 09/2019	09/2019	12	0	Gen. delayed. Completion matching with Banaskantha (Radhanesda) S/stn
125	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 445.89	445.89	258.66	02/2019 12/2019	09/2019	7	0	
126	SUPPLEMENTARY TRANS. SYSTEM FOR UMSP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 193.14	193.14	24.40	06/2019 09/2019	09/2019	3	0	Gen. delayed. Award placed in Dec'17. Work under progress.
127	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 5,071.94	5,071.94	4,554.87	10/2012 12/2019	12/2019	86	5.14	
128	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	447.83	11/2016 12/2019	12/2019	37	4.61	
129	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 5,151.37	5,151.37	3,063.80	03/2018 12/2019	12/2019	21	0	Implementation of CK-II terminals affected due to delay in land acquisition & delay in off-shore supplies.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
130	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 1,394.52	1,394.52	338.19	05/2017 06/2019	12/2019	31	0	Implementation affected due to delayed land acquisition (land handed over for Dwarka-I S/s in Aug'16 & Rajghat in Dec'16). Rajghat substation annulled. Additional bays at Maharanibagh in place of Rajghat S/stn. However, only 400KV line bays are being made at Maharanibagh. Award placed in Jan'18. Forest proposal under DPTA & FCA submitted. Approval & tree cutting permission awaited. During meeting convened by MOUD in Nov'18, it has been decided to re-route the line (LILo at Dwarka-I) through Golf course to reduce forest area. Working permission for routing of line through Golf course area issued by DDA on 18/02/19 using pole type structure which has been awarded in Mar'19.
131	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 808.63	808.63	458.26	01/2018 12/2019	12/2019	23	0	Implementation affected due to forest (Tiger reserve) clearance. Line passing through buffer zone of Tiger reserve area. Wildlife proposal cleared in NBWL. Stage-I issued on 18.10.18. Working permission received in Feb'19. Gen. Project ant. by May'19. Alternate arrangements made for evacuation (contingency through Punatsangchu ATS, ready)
132	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 4,754.42	9,072.36	1,083.08	12/2018 12/2018	12/2019	12	90.82	
133	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 454.11	454.11	270.92	04/2018 01/2020	01/2020	21	0	Schedule extended due to corridor constraint at Jeerat. Work to be executed by WBSETCL on deposit basis. Awarded to JV of M/s Techno & Xian in Nov'18.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
134	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 198.49	198.49	41.70	09/2019 02/2020	02/2020	5	0	
135	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 5,111.33	6,880.36	1,143.65	12/2018 12/2018	12/2020	24	34.61	
136	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,733.20	08/2013 03/2022	03/2022	103	32.24	Balance 02 lines (linked to Gen. Proj.) to be completed matching with Gen. Proj. Lower Subhansiri HEP (schedule uncertain). Works presently stand-still over uncertainty of generation on a/c of local disturbance/ agitation against big dams.
	<u>Satluj Jal Vidyut Nigam Limited</u>									
137	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	330.23	11/2017 -	04/2019	17	0	
138	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 533.50	602.44	557.22	12/2016 -	05/2019	29	37.96	
	<u>Thdc India Limited</u>									
139	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	257.04	02/2014 02/2018	10/2019	68	50.75	Need to expedite the cutting of trees by Forest Deptt.GoUP.
140	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	5,024.35	2,809.51	02/2016 05/2021	06/2022	76	203.22	Renewal of lease for 3.0 Ha land at Asena Quarry and Transfer of additional 05 Ha. Forest land and permission for mining are pending. It needs to be expedited.
141	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,105.30	1,608.70	06/2013 -	12/2022	114	64.77	Post Award: 1. There were frequent hindrances by local villagers since mobilization of works since Jan 2014. Local hindrances have minimized in VPHEP with the strong intervention of MoP and support of District Administration. Regular support of Distt. Administration is required.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		1,94,077.23 -	2,37,297.00	1,67,109.49					
	<u>HEALTH AND FAMILY WELFARE</u>									
	<u>Hospital Services Consultancy Corporation Ltd</u>									
142	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	95.16	02/2018 -	06/2019	16	0	
143	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	176.22	05/2017 -	07/2019	26	0	
144	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	145.51	05/2018 -	09/2019	16	0	
145	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	24.1	
	Total		1,135.49 -	1,235.27	563.89					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
146	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	1,035.16	51.24	03/2022 -	03/2023	12	0	
	<u>Container Corporation Of India</u>									
147	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	259.28	03/2019 -	12/2019	9	0	
148	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	310.09	03/2019 -	12/2019	9	0	
149	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	148.20	03/2019 -	02/2020	11	0	
150	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	435.76	03/2018 -	03/2020	24	0	
151	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	300.00	286.56	03/2019 -	03/2020	12	-13.37	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
152	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	5.59	03/2019 -	12/2020	21	.21	
	<u>East Central Railways</u>									
153	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57 -	528.57	47.38	03/2019 -	12/2019	9	0	
154	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96	256.11	
155	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	56.73	
156	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	0	
157	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	397.88	03/2020 -	03/2021	12	0	
158	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	468.48	
159	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	0	
160	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	0	
161	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	63.37	
162	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	62.06	
	<u>East Coast Railway</u>									
163	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	765.60	02/2019 -	03/2021	25	38.43	
164	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	81.26	10/2020 -	03/2021	5	0	
165	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28	15.45	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
166	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27	0	
167	KHURDA ROAD- BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147	29.96	
168	TALCHER- BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	574.98	06/2021 -	03/2023	21	137.8	
	<u>Eastern Railways</u>									
169	MANDARHILL-DUMKA- RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	1,988.38	2,040.42	03/2016 -	03/2020	48	76.61	Acquisition by State Govt. is awaited.
170	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.52	137.85	03/2016 -	03/2020	48	-3.88	
171	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,620.01	849.73	03/2019 12/2009	03/2022	36	36.26	Land Acquisition – 1. Acquisition of land in stretch of 15.19 KM between Kamarpukur and Mayanapur. 2. Villagers of Vill.Bhadadighi, Hooghly District,are not allowing to work over a pond namely .Bhabadighi between Goghat and Kamarpukur . 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line , Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non availability of land Land acquisition for the main project Tarkeshwar – Bishnupur including their all MM works are yet to be received from State Government.
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
172	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,973.73	1,362.86	03/2004 -	03/2020	192	500.22	
	<u>North East Frontier Railway</u>									
173	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	614.00	274.82	03/2019 -	03/2020	12	106.51	
174	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	13,809.00	9,672.60	03/2011 -	03/2020	108	210.02	
175	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	1,532.00	581.00	03/2019 -	03/2020	12	297.72	
176	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	2,145.00	932.38	03/2019 -	03/2020	12	302.54	
177	SEVOK RANGPO, NEFR - [N22000102]NFR, SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	204.95	
178	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 2,393.48	4,968.00	2,671.70	03/2014 12/2020	12/2020	81	107.56	
179	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 2,446.57	3,000.00	734.88	03/2015 10/2021	10/2021	79	28.95	
180	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	14.11	
	<u>North Eastern Railway</u>									
181	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	477.31	217.90	01/2019 -	01/2020	12	61.8	
182	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50 427.00	426.74	107.98	04/2017 -	01/2020	33	-31.45	
183	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	213.35	2.05	04/2016 -	02/2020	46	.16	
184	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	1.79	12/2019 -	04/2021	16	-12.65	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
185	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	0	
186	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	0	
	<u>North Western Railway</u>									
187	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	169.51	10/2018 -	09/2019	11	24.47	
188	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	349.00	329.33	02/2019 -	12/2019	10	44.16	
189	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	240.62	11/2019 -	05/2020	6	14.35	
190	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	179.50	12/2019 -	06/2020	6	41.64	
191	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 295.02	420.18	118.27	03/2020 -	06/2020	3	0	
192	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	805.25	03/2015 -	10/2020	67	46.55	
193	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	795.01	493.64	02/2019 -	12/2021	34	93.87	
194	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	4.78	03/2020 -	04/2022	25	14.33	
195	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	12.41	08/2022 -	09/2022	1	0	
	<u>Northern Railway</u>									
196	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	17,336.24	11/2002 -	03/2021	220	1017.96	
	<u>Rail Vikas Nigam Ltd.</u>									
197	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,603.22	12/2017 -	03/2020	27	55.57	
198	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	1,993.00	2,121.12	03/2008 -	03/2020	144	171.97	
199	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,077.00	1,052.21	03/2019 -	03/2020	12	16.18	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
200	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL, TELANGANA	04/2012	632.68 -	816.55	666.41	03/2016 03/2017	12/2020	57	29.06	
201	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL, ODISHA	03/2009	942.95 -	1,120.00	941.20	03/2019 -	03/2021	24	18.78	
202	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL, UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	952.52	12/2020 -	03/2021	3	0	
203	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, ODISHA	04/1998	1,202.70 245.00	1,202.70	801.40	02/2015 -	12/2021	82	0	
204	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL - [220100149]RVNL, CHHATISGARH	04/1995	631.78 632.00	1,195.00	731.65	12/2012 -	03/2022	111	89.15	
205	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	36,195.04	03/2020 -	03/2022	24	0	
206	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL, UTTAR PRADESH	04/2015	943.60 -	943.60	238.36	03/2022 -	12/2024	33	0	
207	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL, UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	405.85	03/2023 -	12/2024	21	0	
208	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,092.40	03/2016 -	03/2025	108	7.78	
209	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	838.07	03/2016 -	03/2025	108	0	
210	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	18.95	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
211	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,317.68	12/2024 -	03/2026	15	0	
	<u>South Central Railway</u>									
212	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.47	222.40	03/2010 -	03/2022	144	0	
213	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	506.48	03/2021 -	03/2022	12	0	
214	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	289.91	03/2009 -	03/2023	168	102.85	
215	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	2,132.77	214.54	03/2014 03/2023	03/2023	108	0	
216	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	305.25	03/2022 -	03/2023	12	0	
217	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	278.36	03/2023 -	03/2024	12	18.47	
	<u>South East Central Railway</u>									
218	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	141.22	
	<u>South Eastern Railway</u>									
219	RAJKHARSWAN-CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	166.55	12/2016 08/2018	09/2019	33	153.41	
220	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,151.81	450.25	03/2020 03/2020	06/2020	3	18.76	
221	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	289.76	03/2021 03/2021	12/2021	9	0	
222	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024	108	54.99	
223	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43 -	939.00	184.33	12/2021 12/2024	12/2024	36	79.05	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(April 2019)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
224	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	2,373.00	484.92	03/2003 03/2030	03/2030	324	130.97	
	<u>South Western Railway</u>									
225	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.52	889.52	438.16	03/2017 -	03/2020	36	37.96	
226	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.93	1,140.93	754.97	03/2020 03/2020	03/2021	12	-1.38	
227	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,870.41	1,870.41	880.72	03/2019 03/2021	03/2021	24	15.84	
228	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 986.30	986.30	295.49	03/2016 12/2023	12/2023	93	0	
229	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 279.54	279.54	26.28	03/2016 12/2023	12/2023	93	0	
230	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 1,382.78	1,382.78	7.35	03/2002 03/2024	03/2024	264	0	
231	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024	96	0	
232	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 2,841.84	2,841.84	92.75	12/2018 12/2024	12/2024	72	0	
	<u>Southern Railway</u>									
233	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71	23.72	
234	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
	<u>West Central Railway</u>									
235	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	0	
236	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	2360.35	
	<u>Western Railway</u>									
237	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	36	167.87	
	Total		1,12,936.23 -	1,84,461.48	1,03,758.58					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways</u>									
238	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
239	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	0	
240	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	0	
241	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	0	
242	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHIDCL,ARUNACHAL PRADESH	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	11.57	
	<u>National Highways Authority Of India</u>									
243	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130	0	
244	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	217.61	391.12	04/2010 -	04/2019	108	0	
245	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	04/2019	10	0	
246	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,322.02	05/2013 -	04/2019	71	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
247	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019	29	0	
248	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	597.00	605.33	10/2017 -	04/2019	18	0	
249	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI, MAHARASHTRA	10/2015	593.26 -	593.26	60.83	05/2018 -	04/2019	11	0	
250	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	602.95	417.86	06/2016 -	04/2019	34	0	
251	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	574.28	436.21	07/2018 -	04/2019	9	0	
252	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	505.00	454.85	05/2018 -	04/2019	11	0	
253	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI, RAJASTHAN	08/2016	320.30 -	320.30	228.17	01/2019 -	04/2019	3	0	
254	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	352.71	07/2016 -	04/2019	33	0	
255	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	385.13	211.69	04/2009 -	05/2019	121	92.75	
256	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	167.98	203.98	05/2008 -	05/2019	132	4.99	
257	JORBAT - BARAPANI - [N24000180]NHAI, MEGHALAYA	01/2011	536.00 -	536.00	844.31	01/2014 -	05/2019	64	0	
258	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	05/2019	56	0	
259	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, WEST BENGAL	02/2012	702.16 -	702.16	465.22	07/2014 -	05/2019	58	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
260	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	419.34	09/2017 -	05/2019	20	0	
261	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12	0	
262	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	73.29	11/2018 -	05/2019	6	0	
263	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	174.34	270.88	03/2008 -	06/2019	135	-28.84	
264	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,965.17	11/2011 -	06/2019	91	106.5	
265	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,289.31	03/2013 -	06/2019	75	0	
266	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	884.84	02/2013 -	06/2019	76	0	
267	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,008.77	05/2014 -	06/2019	61	0	
268	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	842.31	07/2013 -	06/2019	71	0	
269	4-LANNING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,317.74	08/2013 -	06/2019	70	0	
270	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	704.56	06/2014 -	06/2019	60	0	
271	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64	0	
272	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,429.59	09/2016 -	06/2019	33	21.9	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
273	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	695.52	11/2016 -	06/2019	31	0	
274	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	333.94	05/2018 -	06/2019	13	0	
275	FOUR LANING OF BIAORA - DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	5	0	
276	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	323.95	04/2018 -	06/2019	14	0	
277	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	475.02	05/2018 -	06/2019	13	0	
278	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	4	0	
279	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	0	
280	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-11	
281	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	605.35	11/2018 -	07/2019	8	0	
282	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	189.17	05/2019 -	07/2019	2	0	
283	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	956.75	11/2017 -	08/2019	21	0	
284	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	97.07	12/2017 -	08/2019	20	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
285	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	77.31	08/2018 -	08/2019	12	0	
286	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	225.48	05/2019 -	08/2019	3	0	
287	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	0	
288	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	0	
289	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	228.73	08/2018 -	09/2019	13	0	
290	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6	0	
291	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,124.97	12/2018 -	10/2019	10	0	
292	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	178.16	04/2019 -	10/2019	6	0	
293	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,040.75	08/2018 -	11/2019	15	0	
294	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	155.23	06/2019 -	11/2019	5	0	
295	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,820.02	04/2019 -	11/2019	7	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
296	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8	0	
297	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	49.59	06/2017 -	11/2019	29	0	
298	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	308.94	04/2008 -	12/2019	140	10.58	
299	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	0	
300	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,149.72	03/2014 -	12/2019	69	0	
301	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	0	
302	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	225.46	06/2018 -	12/2019	18	0	
303	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	189.15	12/2017 -	12/2019	24	0	
304	CONSTRUCTION OF ROB – FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	24.78	11/2018 -	12/2019	13	0	
305	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	341.74	06/2018 -	12/2019	18	0	
306	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019	17	0	
307	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	239.96	10/2017 -	01/2020	27	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
308	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	277.66	08/2018 -	03/2020	19	0	
309	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	71.28	04/2018 -	04/2020	24	0	
310	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	72.04	03/2020 -	04/2020	1	.23	
311	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	355.39	07/2018 -	05/2020	22	0	
312	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	333.48	02/2020 -	05/2020	3	0	
313	4-LANNING OF WARDHA-BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	863.82	03/2020 -	05/2020	2	3.4	
314	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FROM - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	896.05	03/2020 -	05/2020	2	0	
315	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	143.09	03/2020 -	05/2020	2	13.97	
316	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,837.93	08/2013 -	06/2020	82	0	
317	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	515.09	03/2020 -	06/2020	3	44.39	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
318	4-LANNING OF THALSERRY - MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	157.94	09/2017 -	06/2020	33	0	
319	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	440.28	03/2020 -	07/2020	4	41.54	
320	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	0	
321	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	253.84	03/2020 -	08/2020	5	10.58	
322	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	925.93	03/2020 -	08/2020	5	5.56	
323	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	648.57	03/2020 -	08/2020	5	5.7	
324	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	933.00	06/2020 -	08/2020	2	0	
325	4-LANNING OF STHIYATHOPUCHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	-	09/2017 -	08/2020	35	0	
326	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	-	08/2017 -	09/2020	37	0	
327	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	0	
328	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	12.95	03/2019 -	11/2020	20	0	
329	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	336.65	03/2020 -	11/2020	8	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
330	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	256.29	03/2017 -	11/2020	44	1.06	
331	REHABILITATION AND UPGRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	0	
332	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	211.90	10/2017 -	11/2020	37	0	
333	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	193.70	03/2019 -	12/2020	21	0	
334	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	12/2020	52	0	
335	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	239.74	06/2019 -	12/2020	18	0	
336	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	720.79	08/2019 -	12/2020	16	0	
337	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	115.12	03/2020 -	03/2021	12	10.24	
338	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-3.27	
339	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	136.69	06/2020 -	09/2021	15	0	
340	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	-	08/2017 -	02/2022	54	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>Public Works Dept Of State</u>									
341	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	-	03/2017 -	04/2019	25	0	
342	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	276.01	155.40	03/2019 -	05/2019	2	0	
343	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	511.00	33.73	10/2013 -	06/2019	68	0	
344	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	937.76	-	11/2017 -	07/2019	20	13.92	
345	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.22	398.22	-	08/2017 -	08/2019	24	42.37	
346	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	139.32	03/2019 -	09/2019	6	0	
347	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	291.20	-	11/2018 -	11/2019	12	7.39	
348	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	-	02/2018 -	11/2019	21	0	
349	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	-	03/2018 -	11/2019	20	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
350	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	-	02/2018 -	11/2019	21	0	
351	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	-	06/2019 -	11/2019	5	0	
352	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	-	03/2018 -	12/2019	21	0	
353	REHABILITATION & UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHANDE - [N24000876]PWD,WEST BENGAL	01/2017	396.86 -	396.86	-	09/2019 -	12/2019	3	0	
354	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	-	07/2018 -	01/2020	18	0	
355	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	-	03/2018 -	04/2020	25	0	
356	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	-	08/2018 -	06/2020	22	0	
357	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	-	08/2018 -	06/2020	22	0	
358	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	-	07/2018 -	06/2020	23	0	
359	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	-	03/2018 -	07/2020	28	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
360	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	-	02/2018 -	11/2020	33	0	
361	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	-	03/2018 -	11/2020	32	0	
362	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD,WEST BENGAL	03/2016	160.27 -	160.27	-	08/2019 -	08/2021	24	0	
363	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD,WEST BENGAL	06/2016	236.78 -	236.78	-	08/2019 -	08/2021	24	0	
	Total		97,501.48 -	1,00,719.03	61,393.68					
	<u>SHIPPING AND PORTS</u>									
	<u>Kamarajar Port Limited</u>									
364	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-57.02	
	Total		600.00 -	257.90	1.45					
	<u>TELECOMMUNICATIONS</u>									
	<u>Bharat Sanchar Nigam Limited</u>									
365	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 219.60	219.60	33.46	05/2018 05/2019	05/2019	12	2	
366	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	240.10	117.63	10/2018 05/2019	05/2019	7	3.58	
	<u>Department Of Telecommunication</u>									
367	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	84.97	
	Total		13,781.10 -	25,123.70	8,548.09					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>URBAN DEVELOPMENT</u>									
	<u>Bangalore Metro Rail Corporation Limited</u>									
368	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	0	
	<u>Central Public Works Department</u>									
369	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 488.28	488.28	410.91	05/2017 02/2019	06/2019	25	25.85	
370	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD,WEST BENGAL	02/2014	156.57 -	156.57	154.15	08/2016 -	07/2019	35	0	
371	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 -	162.88	115.59	04/2018 -	07/2019	15	0	
372	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD,ANDHRA PRADESH	01/2018	206.58 -	206.58	82.25	03/2019 -	08/2019	5	0	
373	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	132.8	
374	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD,PUNJAB	08/2016	294.00 349.94	294.00	167.44	04/2019 09/2019	12/2019	8	0	
375	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	559.49	291.77	07/2019 -	12/2019	5	1.85	
376	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	1,592.00	496.57	10/2019 -	03/2020	5	30.58	
377	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	165.23	77.70	10/2012 -	03/2020	89	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
378	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	209.00	105.72	10/2019 -	03/2020	5	0	
379	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 -	197.33	25.15	04/2019 06/2020	06/2020	14	0	
380	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	171.86	73.90	03/2016 -	09/2020	54	0	
381	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	246.31	51.14	02/2020 09/2020	09/2020	7	0	
382	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	223.37	24.40	07/2020 -	09/2020	2	0	
383	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD,MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	0	
384	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	61.43	06/2017 07/2017	10/2020	40	.57	
	<u>Hindustan Steelwork Construction Limited</u>									
385	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	0	
	<u>Kochi Metro Rail Corporation Ltd</u>									
386	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.50	07/2017 -	12/2019	29	9.76	
	<u>Mumbai Metro Rail Corporation Ltd</u>									
387	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	0	
	<u>Nagpur Metro Rail Corporation Ltd</u>									
388	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 8,680.00	8,680.00	5,632.05	03/2018 12/2019	12/2019	21	0	
	Total		69,375.71 -	70,519.51	14,161.73					

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (April 2019)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	Grand Total		6,98,802.34	8,48,309.41	4,76,396.77					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(April 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88	133
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	12/2015 -	06/2020	44.69	54
	Total		14,951.00 -	23,420.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28	21
	Total		314.61 -	441.33				
	<u>COAL</u>							
	<u>Neyveli Lignite Corporation</u>							
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,080.41	12/2015 -	09/2019	19.86	45
	<u>Singareni Colliers Company Limited</u>							
5	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	03/2015 -	03/2021	114.60	72
6	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	03/2019 -	03/2020	11.42	12
7	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	03/2012 -	03/2024	80.24	144
8	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	03/2015 -	03/2021	5.85	72
9	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	03/2012 -	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>							
10	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44	60
	<u>Western Coal Fields Limited</u>							
11	KAMPTEE DEEP OC MINE - [N06000141]	11/2015	277.65 -	313.34	03/2021 -	03/2024	12.85	36
12	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	03/2023 -	03/2024	15.41	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		8,301.00	10,390.07				
	<u>FERTILISERS</u>							
	<u>Rashtriya Chemical & Fertiliser Limited</u>							
13	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]	10/2014	197.79	209.44	11/2016	05/2019	5.89	30
	Total		197.79	209.44				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Hospital Services Consultancy Corporation Ltd</u>							
14	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11	513.89	11/2013	10/2020	24.10	83
	Total		414.11	513.89				
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
15	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29	5,245.96	08/2018	11/2019	14.33	15
	<u>Gas Authority Of India Limited</u>							
16	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00	3,049.47	12/2012	02/2022	4.61	110
	<u>Hindustan Petroleum Corporation Limited</u>							
17	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81	723.40	10/2014	08/2019	133.50	58
	<u>Indian Oil Corporation Limited</u>							
18	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00	6,025.00	12/2018	02/2021	33.98	26
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
19	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]	10/2015	135.00	170.70	03/2019	05/2019	26.44	2
	<u>Oil & Natural Gas Corporation Limited</u>							
20	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	06/2010	202.94	330.35	01/2014	11/2019	62.78	70
21	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79	1,577.15	05/2013	12/2019	83.01	79
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63	2,665.65	03/2015	12/2019	29.42	57

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
23	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69	3,247.19	04/2018	05/2020	1.77	25
	<u>Oil India Limited</u>							
24	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	07/2011	352.56	438.84	03/2017	12/2019	24.47	33
	Total		19,112.71	23,473.71				
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
25	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59	9,394.80	09/2009	12/2021	139.69	147
	<u>National Thermal Power Corporation</u>							
26	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48	3,846.30	03/2013	12/2020	29.14	93
27	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00	7,998.00	05/2014	05/2019	49.41	60
28	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51	11,148.86	09/2019	01/2020	12.95	4
29	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) [N18000140]	12/2012	11,846.00	12,739.82	06/2017	03/2020	7.55	33
30	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I [N18000151]	03/2013	11,638.55	12,865.92	09/2017	03/2020	10.55	30
31	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60	13,731.26	01/2018	05/2020	5.91	28
32	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44	13,740.53	08/2018	02/2020	9.64	18
33	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97	15,095.67	01/2011	08/2021	73.65	127
34	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58	15,164.05	02/2019	09/2021	5.55	31
	<u>North East Electric Power Corporation</u>							
35	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	7,419.34	12/2009 06/2016	06/2019	197.14	114
	<u>Power Grid Corporation Of India Limited</u>							
36	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	02/2014	196.58	225.28	02/2016	05/2019	14.60	39
37	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28	260.03	07/2017	06/2019	27.92	23
38	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP [N18000180]	01/2015	268.80	340.88	03/2018	05/2019	26.82	14
39	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29	546.36	11/2016	12/2019	4.61	37

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
40	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	02/2014	539.82	575.67	06/2016	05/2019	6.64	35
41	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49	639.46	06/2014	09/2019	31.17	63
42	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69	738.48	09/2010	04/2019	54.59	103
43	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52	1,891.41	04/2016	08/2019	38.61	40
44	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	2,187.32	11/2008	05/2019	22.93	126
45	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12	5,071.94	10/2012	12/2019	5.14	86
46	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33	6,880.36	12/2018	12/2020	34.61	24
47	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42	9,072.36	12/2018	12/2019	90.82	12
48	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	14,719.10	08/2013	03/2022	32.24	103
	<u>Satluj Jal Vidyut Nigam Limited</u>							
49	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68	602.44	12/2016	05/2019	37.96	29
	<u>Thdc India Limited</u>							
50	DHUKWAN SMALL HYDRO PROJECT - [N18000189]	05/2011	195.42	294.60	02/2014	10/2019	50.75	68
51	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58	4,105.30	06/2013	12/2022	64.77	114
52	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	5,024.35	02/2016	06/2022	203.22	76
	Total		1,33,100.12	1,76,319.89				
	<u>RAILWAYS</u>							
	<u>Container Corporation Of India</u>							
53	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50	235.00	03/2019	12/2020	.21	21
	<u>East Central Railways</u>							
54	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012	03/2020	56.73	96
55	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73	1,156.41	03/2012	03/2020	256.11	96

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
56	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06	12
57	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37	12
58	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48	61
	<u>East Coast Railway</u>							
59	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45	28
60	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43	25
61	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80	21
62	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96	147
	<u>Eastern Railways</u>							
63	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26	36
64	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	1,125.89 -	1,988.38	03/2016 -	03/2020	76.61	48
	<u>Metropolitan Rapid Transport Projects</u>							
65	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,973.73	03/2004 -	03/2020	500.22	192
	<u>North East Frontier Railway</u>							
66	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51	12
67	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11	31
68	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72	12
69	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54	12
70	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95	79
71	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95	51
72	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56	81
73	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02	108
	<u>North Eastern Railway</u>							

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
74	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16	46
75	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80	12
	<u>North Western Railway</u>							
76	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35	6
77	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	09/2019	24.47	11
78	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64	6
79	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	12/2019	44.16	10
80	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33	25
81	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	12/2021	93.87	34
82	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	10/2020	46.55	67
	<u>Northern Railway</u>							
83	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96	220
	<u>Rail Vikas Nigam Ltd.</u>							
84	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06	57
85	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18	12
86	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78	24
87	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15	111
88	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57	27
89	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97	144
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
91	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108
	<u>South Central Railway</u>							
92	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85	168

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
93	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95	2,200.00	03/2023	03/2024	18.47	12
	<u>South East Central Railway</u>							
94	CHHINDWARA-MANDLA FORT GC - [N22000481]	03/2011	556.54	1,342.46	03/2012	03/2020	141.22	96
	<u>South Eastern Railway</u>							
95	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND [N22000323]	04/2012	148.77	377.00	12/2016	09/2019	153.41	33
96	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	04/1995	524.43	939.00	12/2021	12/2024	79.05	36
97	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00	1,009.00	03/2015	03/2024	54.99	108
98	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83	1,151.81	03/2020	06/2020	18.76	3
99	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40	2,373.00	03/2003	03/2030	130.97	324
	<u>South Western Railway</u>							
100	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78	889.52	03/2017	03/2020	37.96	36
101	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59	1,870.41	03/2019	03/2021	15.84	24
	<u>Southern Railway</u>							
102	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26	231.67	04/2014	03/2020	23.72	71
	<u>West Central Railway</u>							
103	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66	6,093.31	05/2008	03/2023	2,360.35	178
	<u>Western Railway</u>							
104	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66	858.96	03/2019	03/2022	167.87	36
	Total		50,678.32	1,22,621.45				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
105	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 [N24000676]	12/2016	138.93	155.00	01/2017	01/2020	11.57	36
	<u>National Highways Authority Of India</u>							
106	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	167.98	05/2008	05/2019	4.99	132

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
107	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58	140
108	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	05/2019	92.75	121
109	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23	1
110	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56	5
111	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40	2
112	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06	44
113	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70	5
114	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54	4
115	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97	2
116	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58	5
117	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24	12
118	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39	3
119	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90	33
120	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50	91
	<u>Public Works Dept Of State</u>							
121	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	11/2018 -	11/2019	7.39	12
122	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889	04/2014	279.70 398.22	398.22	08/2017 -	08/2019	42.37	24
123	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873	08/2014	823.20 937.76	937.76	11/2017 -	07/2019	13.92	20
	Total		14,725.66 -	18,022.09				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
124	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00	22,542.00	05/2015	10/2019	45.20	53
	<u>Rastrya Ispat Nigam Limited</u>							
125	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00	488.40	10/2016	03/2020	42.39	41
	Total		15,868.00	23,030.40				
	<u>TELECOMMUNICATIONS</u>							
	<u>Bharat Sanchar Nigam Limited</u>							
126	MADHYA PRADESH ACCESS (LOT1) - [N26000110]	08/2017	215.30	219.60	05/2018	05/2019	2.00	12
127	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]	01/2018	231.80	240.10	10/2018	05/2019	3.58	7
	<u>Department Of Telecommunication</u>							
128	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00	24,664.00	07/2015	05/2020	84.97	58
	Total		13,781.10	25,123.70				
	<u>URBAN DEVELOPMENT</u>							
	<u>Central Public Works Department</u>							
129	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	12/2013	10/2019	132.80	70
130	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]	02/2014	388.00	488.28	05/2017	06/2019	25.85	25
131	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017	10/2020	.57	40
132	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31	559.49	07/2019	12/2019	1.85	5
133	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21	1,592.00	10/2019	03/2020	30.58	5
	<u>Kochi Metro Rail Corporation Ltd</u>							
134	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79	5,687.79	07/2017	12/2019	9.77	29
	Total		7,948.75	9,092.55				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(April 2019)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Grand Total		2,79,393.17	4,32,658.52				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	05/2014 -	04/2018
2	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2018
3	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	10/2018
4	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	04/2017 -	-
	<u>Central Coal Fields Limited</u>				
5	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	03/2012 -	03/2019
	<u>Eastern Coal Fields Limited</u>				
6	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73 -	08/2019 -	-
	<u>Singareni Colliers Company Limited</u>				
7	RKP OCP PHASE-I - [N06000079]SCCL, TELANGANA	03/2010	209.78 -	03/2015 03/2019	03/2019
8	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL, TELANGANA	06/2012	365.01 -	06/2015 03/2019	03/2019
9	KAKATIYA LONGWALL - [N06000048]SCCL, TELANGANA	12/2008	453.63 -	12/2012 -	-
10	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, TELANGANA	03/2010	181.19 -	03/2012 -	-
	<u>South-Eastern Coal Fields Limited</u>				
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL, CHHATISGARH	11/2009	198.59 -	03/2016 -	03/2019
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL, CHHATISGARH	04/2012	258.56 -	03/2016 -	03/2019
13	AMERA OC RCE - [N06000123]SECL, CHHATISGARH	02/2015	335.97 -	03/2018 -	-
	<u>Western Coal Fields Limited</u>				
14	GOKUL - [N06000120]WCL, MAHARASHTRA	11/2014	267.67 -	03/2018 -	03/2018
15	NEW MAJRI UG TO OC - [N06000128]WCL, MAHARASHTRA	05/2015	295.56 -	03/2019 -	03/2019
16	BHATADI EXPANSION OC MINE - [N06000150]WCL, MAHARASHTRA	02/2016	304.52 -	03/2019 -	03/2019
17	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL, MAHARASHTRA	02/2016	198.68 -	03/2019 -	-
	Total		7,798.26 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>STEEL</u>				
	<u>Steel Authority Of India Limited (Sail)</u>				
18	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL,CHHATISGARH	04/2014	188.93 -	04/2015 -	-
19	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-
	Total		4,937.93 -		
	<u>PETROLEUM</u>				
	<u>Bharat Petroleum Corporation Limited</u>				
20	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-
	<u>Chennai Petroleum Corporation Limited</u>				
21	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	03/2013	3,110.36 -	11/2015 -	-
	<u>Gas Authority Of India Limited</u>				
22	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	04/2018 -	03/2019
	<u>Hindustan Petroleum Corporation Limited</u>				
23	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209]HPCL,RAJASTHAN	11/2011	310.00 -	03/2013 -	-
	<u>Indian Oil Corporation Limited</u>				
24	BRANCH PIPELINE OF PAJPL TO UNA - [N16000250]IOCL,HIMACHAL PRADESH	02/2016	151.00 -	09/2019 -	02/2019
25	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	12/2016 -	-
26	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	05/2015 -	-
27	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-
28	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL,GUJARAT	03/2018	588.20 -	- -	-
29	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 714.25	10/2017 -	03/2019
	<u>Indian Strategic Petroleum Reserves Ltd</u>				
30	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
31	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	09/2011 -	-
	<u>Oil India Limited</u>				
32	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-
33	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	03/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		11,137.36		
	<u>POWER</u>				
	<u>National Hydro-Electric Power Corporation</u>				
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH	09/2003	6,285.33	09/2010	-
	<u>National Thermal Power Corporation</u>				
35	SOLAPUR STPP - [N18000133]NTPC, MAHARASHTRA	03/2012	9,395.18	11/2016 03/2019	03/2019
36	KUDGI STPP STAGE 1 - [N18000131]NTPC, KARNATAKA	01/2012	15,166.19	01/2017	-
37	MOUDA STPP STAGE 2 - [N18000132]NTPC, MAHARASHTRA	03/2012	7,921.47	09/2016	-
38	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC, UTTARAKHAND	07/2012	1,527.00	08/2017	-
39	FGUTPP, UNCHAHAR STAGE-IV (1X500 MW) - [N18000174]NTPC, UTTAR PRADESH	07/2013	3,363.12	12/2016	-
40	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC, JHARKHAND	10/2004	4,237.96 4,238.00	10/2017	-
	Total		47,896.25		
	<u>HEAVY INDUSTRY</u>				
	<u>Natrip Implementation Society</u>				
41	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001]NATIS, MULTI STATE	04/2011	1,718.00	09/2011	-
	Total		1,718.00		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Hospital Services Consultancy Corporation</u>				
42	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC, ANDHRA PRADESH	08/2017	272.19	03/2019	-
	<u>Hospital Services Consultancy Corporation Ltd</u>				
43	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC, ASSAM	07/2012	175.57	12/2014	-
44	AIIMS - OPD(NEW) - [N21000009]HSCC, DELHI	08/2014	293.65	05/2017	-
45	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC, HARYANA	09/2014	505.58	03/2018	-
46	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00	09/2018	-
47	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC, MAHARASHTRA	08/2017	274.19	03/2019	-
48	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15	03/2019	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		2,120.33		
			-		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
49	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR, MAHARASHTRA	04/2011	184.06 199.12	03/2019 -	03/2019
50	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-
	<u>Container Corporation Of India</u>				
51	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
52	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
53	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
	<u>East Central Railways</u>				
54	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, JHARKHAND	04/2002	459.91 -	- -	-
55	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
56	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
57	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
58	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
59	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
60	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	- -	-
61	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
62	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
63	HAJIPUR-RAMDALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- -	-
64	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR	05/2015	380.00 -	- -	-
65	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR, BIHAR	01/1991	332.15 -	07/2014 -	-
66	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR	04/1998	180.82 -	- -	-
	<u>East Coast Railway</u>				
67	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR, BIHAR	04/2008	445.25 -	- -	-
68	GAYA-CHATRA (NL) - [N22000169]ECOR, MULTI STATE	04/2008	415.67 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
69	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
	<u>Eastern Railways</u>				
70	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	01/2006
71	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 02/2010	02/2010
72	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	05/2010
73	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	193.08 -	12/2011 -	09/2012
74	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 12/2013	12/2013
75	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 -	02/2012 -	09/2016
76	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	12/2017
77	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	-
78	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
79	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
80	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
81	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
82	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
83	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-
84	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	-
85	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
86	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
87	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
88	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-
89	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	-
90	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
91	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
92	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	-
93	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
94	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
95	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
96	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
97	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
98	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
99	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	06/2013 -	-
100	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
101	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
102	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
103	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
104	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 274.56	03/1994 -	-
105	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-
106	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
	<u>North East Frontier Railway</u>				
107	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 984.97	03/2007 -	04/2016
108	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	03/2019
109	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	1,142.00 3,407.00	03/2014 12/2019	03/2019
110	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019
111	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	03/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
112	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR,ASSAM	04/2012	246.07 614.81	03/2019 -	03/2019
113	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	792.46 724.31	12/2010 -	-
114	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-
115	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-
	<u>North Eastern Railway</u>				
116	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	01/2019
117	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	04/1999 -	03/2019
118	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	- -	-
119	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
120	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
121	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
122	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
123	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-
124	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
125	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-
126	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	10/2018
127	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	-
128	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018
	<u>North Western Railway</u>				
129	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
130	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
131	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
132	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
	<u>Northern Railway</u>				
133	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-
134	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
135	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-
136	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-
137	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
138	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
139	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
140	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-
141	DELHI-SOHNANUHIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
142	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-
143	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
144	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
145	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
146	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
147	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
148	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
149	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
150	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-
151	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
152	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
153	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
154	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
	<u>Rail Vikas Nigam Ltd.</u>				
155	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	03/2019
	<u>Railway Electrification</u>				
156	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
157	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2019
158	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
159	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-
160	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
161	BHADRACHALAM-KOVVUR - [N22000264]SCR,MULTI STATE	04/2012	923.23 -	- -	-
162	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
163	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
164	KONDAPALLI-KOTHAGUDEM - [N22000364]SCR,TELANGANA	04/2013	723.00 -	- -	-
165	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
166	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	-
167	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 -	02/2019 -	-
168	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00 -	09/2018 -	-
	<u>South Eastern Railway</u>				
169	DANGO APOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	12/2015 12/2018	02/2019
170	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
171	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 -	-
172	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
173	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
174	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	633.87 -	- -	-
	<u>Southern Railway</u>				
175	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2019
176	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	03/2019
177	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 -	03/2018 -	03/2018
178	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-
179	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
180	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
181	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	-
182	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-
183	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
184	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-
185	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
186	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
187	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
188	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
189	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-
190	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
191	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
192	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
193	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
194	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
195	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
196	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
197	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-
198	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-
199	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-
200	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
201	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-
202	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-
203	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-
204	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Western Railway</u>				
205	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	03/2019
206	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-
207	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR, GUJARAT	03/2017	243.60 -	- -	-
208	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR, MAHARASHTRA	03/2010	265.88 -	- -	-
209	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR, MAHARASHTRA	03/2012	217.38 -	- -	-
210	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR, GUJARAT	03/2012	248.26 -	- -	-
211	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR, GUJARAT	03/2012	153.83 -	- -	-
212	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR, GUJARAT	02/1991	551.51 -	03/2019 -	-
	Total		1,04,040.73 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Dept Of Road Transport & Highways</u>				
213	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]DORTH, GOA	03/2015	298.33 -	- -	-
214	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]DORTH, GOA	03/2015	184.05 -	- -	-
215	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]DORTH, GOA	03/2015	280.16 -	- -	-
216	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A - [N24000262]DORTH, ANDHRA PRADESH	12/2014	201.12 201.00	02/2015 -	-
	<u>Ministry Of Road Transport And Highways</u>				
217	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMAPATNAM TO CHANDR - [N24000273]MORTH, ANDHRA PRADESH	07/2015	314.43 -	- -	-
218	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH, MAHARASHTRA	10/2015	289.60 -	- -	-
219	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH, MAHARASHTRA	12/2011	156.26 227.00	- -	-
220	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH, MAHARASHTRA	03/2011	185.82 292.00	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH,CHHATISGARH	03/2015	422.34 -	- -	-
222	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-
223	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-
224	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-
225	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-
226	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-
227	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-
228	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-
229	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-
230	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-
231	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
232	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-
233	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH - [N24000333]MORTH,RAJASTHAN	12/2015	621.43 -	06/2018 -	-
234	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
235	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-
236	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-
237	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-
238	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
239	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-
240	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-
241	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-
242	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-
243	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-
244	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-
245	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-
246	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-
247	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
248	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
249	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-
250	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-
251	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-
252	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-
253	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-
254	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-
255	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-
256	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-
258	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-
259	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-
260	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-
261	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-
262	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-
263	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-
264	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
265	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-
266	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-
267	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-
268	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-
269	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-
270	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-
271	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
272	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-
273	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-
274	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
275	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
276	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	07/2018 -	07/2018
277	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	08/2018
278	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	10/2018 -	10/2018
279	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	11/2018
280	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	05/2018 -	-
281	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	06/2018 -	-
282	FOUR LANING OF JHANJI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	06/2018 -	-
283	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 - [N24000321]NHIDCL,ASSAM	06/2016	829.00 -	01/2019 -	-
284	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	11/2018 -	-
285	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	11/2018 -	-
286	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59 - [N24000324]NHIDCL,ARUNACHAL PRADESH	03/2015	194.11 -	05/2018 -	-
287	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS - [N24000325]NHIDCL,ARUNACHAL PRADESH	10/2015	179.82 -	01/2019 -	-
288	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH - [N24000326]NHIDCL,ARUNACHAL PRADESH	07/2015	197.16 -	10/2018 -	-
289	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 -	06/2018 -	-
290	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
291	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO - [N24000329]NHIDCL,TRIPURA	05/2014	497.89 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
292	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28 - [N24000421]NHIDCL, ARUNACHAL PRADESH	03/2015	235.08 -	05/2018 -	-
293	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37 ON EPC BASIS - [N24000429]NHIDCL, ASSAM	12/2015	225.02 -	12/2018 -	-
294	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000430]NHIDCL, ASSAM	12/2015	223.30 -	06/2018 -	-
295	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL, ASSAM	01/1991	520.01 -	- -	-
296	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	12/2018 -	-
297	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	01/2016 -	-
298	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	01/2016 -	-
299	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM. 583.450 - [N24000614]NHIDCL, ARUNACHAL PRADESH	01/2016	183.65 -	11/2016 -	-
300	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE - [N24000615]NHIDCL, ARUNACHAL PRADESH	01/2016	334.22 -	06/2016 -	-
301	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	- -	-
302	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. - [N24000617]NHIDCL, ARUNACHAL PRADESH	04/2016	198.00 -	10/2016 -	-
303	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH - [N24000618]NHIDCL, ARUNACHAL PRADESH	11/2015	434.06 -	- -	-
304	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN - [N24000677]NHIDCL, ARUNACHAL PRADESH	01/2017	1,253.10 -	03/2017 -	-
305	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 -	04/2017 -	-
306	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	04/2017 -	-
307	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	04/2017 -	-
308	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000681]NHIDCL, ARUNACHAL PRADESH	01/2017	194.66 -	04/2017 -	-
309	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS - [N24000682]NHIDCL, ARUNACHAL PRADESH	02/2017	168.32 -	04/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
310	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	-
311	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS - [N24000684]NHIDCL,ARUNACHAL PRADESH	02/2017	216.71 -	04/2017 -	-
312	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	-
313	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-
314	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	04/2017 -	-
315	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
316	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	05/2018 -	-
317	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	06/2018 -	-
318	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	05/2018 -	-
319	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	10/2018 -	-
320	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	12/2017 -	-
321	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	04/2017 -	-
322	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	10/2018 -	-
323	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	10/2018 -	-
324	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	09/2018 -	-
325	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-
326	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-
327	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND	03/2018	239.30 -	09/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
328	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-
329	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	09/2018 -	-
330	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	09/2018 -	-
331	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	09/2018 -	-
332	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	09/2018 -	-
333	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	09/2018 -	-
334	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	09/2018 -	-
335	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	09/2018 -	-
336	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-
337	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-
338	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-
339	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
340	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	11/2017 -	-
341	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
342	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-
343	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	- -	-
344	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-
345	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>National Highways Authority Of India</u>				
346	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018
347	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	10/2018
348	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2018
349	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018
350	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2018
351	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	12/2018
352	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018
353	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019
354	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	02/2019
355	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	02/2019
356	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019
357	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	03/2019
358	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019
359	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 -	03/2019
360	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2019
361	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	03/2019
362	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 09/2017	03/2019
363	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	03/2019
364	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	03/2019
365	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	03/2019
366	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	03/2019
367	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	03/2019
368	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	03/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
369	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	03/2019
370	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI, KARNATAKA	08/2016	1,167.42 -	03/2019 -	03/2019
371	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI, MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019
372	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	-
373	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	-
374	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	-
375	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	-
376	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
377	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
378	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
379	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
380	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
381	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
382	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
383	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-
384	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
385	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
386	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-
387	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-
388	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-
389	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-
390	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI, UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-
391	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
392	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, TAMIL NADU	04/2012	624.00 -	04/2014 -	-
393	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, JHARKHAND	12/2012	1,479.00 -	06/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
394	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
395	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	12/2015 -	-
396	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-
397	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-
398	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
399	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-
400	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
401	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-
402	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
403	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-
404	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
405	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-
406	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-
407	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
408	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-
409	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
410	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
411	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-
412	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
413	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
414	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
415	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
416	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-
417	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)					
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
418	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-
419	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-
420	MEERUT-BULANDSHAHAR - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-
421	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
422	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-
423	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
424	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-
425	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
426	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-
427	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-
428	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
429	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
430	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
431	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
432	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
433	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
434	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
435	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-
436	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-
437	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
438	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-
439	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
440	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
441	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	-
442	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-
443	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
444	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
445	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
446	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
447	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
448	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-
449	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-
450	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
451	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-
452	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-
453	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
454	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
455	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
456	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
457	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
458	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
459	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-
460	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
461	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-
462	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
463	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 -	- -	-
464	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
465	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
466	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-
467	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-
468	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-
469	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
470	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-
471	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
472	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
473	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
474	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
475	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
476	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
477	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-
478	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
479	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
480	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-
481	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-
482	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
483	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-
484	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
485	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
486	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	-
487	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
488	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
489	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
490	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	-
491	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
492	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
493	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-
494	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-
495	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
496	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-
497	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
498	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
499	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
500	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
501	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-
502	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-
503	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
<u>National Highways Development Project</u>					
504	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337 - [N24000250]NHDP,MAHARASHTRA	06/2014	260.39 -	11/2016 -	-
505	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE - [N24000251]NHDP,GOA	03/2015	297.00 -	04/2018 -	-
506	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]NHDP,MAHARASHTRA	03/2015	168.30 -	- -	-
507	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]NHDP,MAHARASHTRA	01/2014	446.77 -	- -	-
508	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 161.570 TO 211.00 - [N24000255]NHDP,MAHARASHTRA	12/2013	220.72 -	11/2016 -	-
509	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-
510	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-
511	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-
512	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
513	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-
514	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-
515	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-
516	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-
517	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-
518	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-
519	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-
520	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-
521	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-
522	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-
523	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-
524	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-
525	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-
526	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-
527	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-
	<u>Public Works Dept Of State</u>				
528	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	01/2019
529	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 - [N24000856]PWD,MADHYA PRADESH	03/2014	170.00 -	02/2015 -	02/2015
530	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 & NH-10 O - [N24000871]PWD, WEST BENGAL	08/2014	600.87 720.97	11/2017 -	11/2017
531	REHABILITATION AND UPGRADEMENT OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S - [N24000241]PWD,TELANGANA	12/2013	177.18 -	03/2016 -	-
532	REHABILITATION AND UPGRADEMENT OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO - [N24000242]PWD,TELANGANA	12/2013	158.65 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
533	YAN TO NIRMAL SEREABILITATION AND UPGADATION OF NH - 222 FROM KM 615.00 TO 668.60 (KALCTION) TO TW - [N24000243]PWD,TELANGANA	12/2013	244.08 -	03/2016 -	-
534	REHABILITATION AND UPGADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T - [N24000244]PWD,TELANGANA	01/2014	340.00 -	03/2016 -	-
535	REHABILITATION AND UPGADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]PWD,TELANGANA	01/2014	270.00 -	03/2016 -	-
536	REHABILITATION AND UPGADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO - [N24000246]PWD,TELANGANA	10/2014	244.30 -	12/2016 -	-
537	REHABILITATION AND UPGADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247]PWD,TELANGANA	10/2014	295.47 -	02/2017 -	-
538	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD,TELANGANA	03/2015	153.21 -	01/2017 -	-
539	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S - [N24000249]PWD,TELANGANA	03/2011	218.31 -	12/2015 -	-
540	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO - [N24000253]PWD,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
541	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD,KERALA	01/2014	255.75 348.00	09/2017 -	-
542	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD,KERALA	01/2014	267.16 352.00	11/2017 -	-
543	REHABILITATION AND UPGADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION) - [N24000263]PWD,ANDHRA PRADESH	02/2015	241.61 -	02/2017 -	-
544	REHABILITATION AND UPGADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD,ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-
545	REHABILITATION AND UPGADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC - [N24000266]PWD,ANDHRA PRADESH	01/2014	361.30 -	07/2014 -	-
546	REHABILITATION AND UPGADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION) - [N24000267]PWD,ANDHRA PRADESH	02/2014	258.99 -	07/2014 -	-
547	REHABILITATION UPGADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC - [N24000268]PWD,ANDHRA PRADESH	07/2014	251.55 -	02/2015 -	-
548	REHABILITATION AND UPGADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T - [N24000269]PWD,ANDHRA PRADESH	03/2015	175.03 -	- -	-
549	REHABILITATION AND UPGADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP - [N24000272]PWD,ANDHRA PRADESH	02/2015	266.00 -	- -	-
550	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C - [N24000274]PWD,ANDHRA PRADESH	07/2015	333.21 333.21	12/2015 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
551	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD,CHHATISGARH	10/2014	213.47 -	03/2015 -	-
552	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD,CHHATISGARH	10/2014	298.34 -	03/2015 -	-
553	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD,CHHATISGARH	11/2014	262.54 -	03/2015 -	-
554	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD,CHHATISGARH	12/2015	291.05 -	- -	-
555	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]PWD,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
556	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD,CHHATISGARH	12/2010	169.26 -	12/2012 -	-
557	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO - [N24000284]PWD,ANDHRA PRADESH	02/2014	170.21 -	11/2014 -	-
558	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD,CHHATISGARH	12/2014	394.20 -	- -	-
559	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD,CHHATISGARH	11/2015	485.44 -	12/2015 -	-
560	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD,PUNJAB	03/2015	435.90 -	- -	-
561	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD,PUNJAB	01/2015	279.68 -	- -	-
562	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD,PUNJAB	11/2014	463.65 546.00	- -	-
563	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD,PUNJAB	11/2014	573.96 605.00	- -	-
564	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150 - [N24000299]PWD,ANDHRA PRADESH	02/2015	224.83 -	05/2015 -	-
565	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDU - [N24000300]PWD,ANDHRA PRADESH	03/2015	309.01 -	09/2015 -	-
566	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]PWD,ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-
567	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD,ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-
568	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION - [N24000303]PWD,ANDHRA PRADESH	02/2014	417.61 -	06/2014 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
569	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD,MIZORAM	11/2010	624.41 -	03/2011 -	-
570	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD,ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-
571	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-
572	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-
573	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-
574	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-
575	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-
576	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-
577	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-
578	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-
579	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-
580	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-
581	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-
582	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-
583	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-
584	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-
585	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-
586	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-
587	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
588	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-
589	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-
590	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-
591	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-
592	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-
593	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-
594	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-
595	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-
596	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-
597	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-
598	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-
599	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-
600	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-
601	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-
602	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-
603	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-
604	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING - [N24000470]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	-
605	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-
606	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(April 2019)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
607	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-
608	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-
609	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-
610	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-
611	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-
612	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-
613	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-
614	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-
615	R & U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-
	Total		2,38,465.63 -		
	<u>SHIPPING AND PORTS</u>				
	<u>Kamarajar Port Limited</u>				
616	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066]KPL,TAMIL NADU	02/2015	244.50 258.00	12/2017 -	-
	<u>Mumbai Port Trust</u>				
617	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	-
	<u>Port Trust</u>				
618	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-
619	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-
	Total		3,188.29 -		
	<u>TELECOMMUNICATIONS</u>				
	<u>Indian Telephone Industry</u>				
620	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY - [N26000102]ITI,MULTI STATE	09/2014	2,111.17 -	09/2014 -	-
	<u>Mahanagar Telephone Nigam Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
621	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-
	Total		2,529.43 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Central Public Works Department</u>				
622	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
623	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD - [N28000076]CPWD,ANDHRA PRADESH	06/2014	157.84 -	03/2017 -	-
624	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-
625	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-
	<u>Chennai Metro Rail Ltd</u>				
626	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 -	12/2015 -	-
627	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
628	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-
629	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-
630	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-
631	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-
632	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-
633	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-
634	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-
635	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-
636	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-
637	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-
638	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(April 2019)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
639	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-
640	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-
641	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>				
642	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
643	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL, UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019
	<u>Maharashtra Metro Rail Corporation Ltd.</u>				
644	DELHI MRTS PHASE-III - [N28000056]MMRC, DELHI	09/2011	38,585.00 -	03/2016 -	-
	<u>National Building Construcion Corporation Ltd</u>				
645	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI	07/2016	2,694.00 -	- -	-
	Total		72,350.56 -		
	<u>DEFENCE PRODUCTION</u>				
	<u>Goa Shipyard Limited</u>				
646	CONSTRUCTION WORKS PHASE 4 - [N39000001]GSL, GOA	12/2016	167.69 168.00	05/2018 03/2019	-
	Total		167.69 -		
	Grand Total		4,96,350.46		

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
1	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN	03/2018	229.80 -	229.80	69.19	- -	03/2021	-	5/26
	Total		229.80 -	229.80	69.19				5/26
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation</u>								
2	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	601.02	96.75	- -	02/2020	-	0/0
3	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	582.99	61.17	- -	02/2020	-	0/0
4	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99	58.04	- -	02/2020	-	0/0
5	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	268.84	68.33	- -	04/2020	-	0/0
6	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	249.01	46.28	- -	05/2020	-	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>								
7	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	156.65	54.94	- -	02/2020	-	0/0
	Total		2,510.41 -	2,510.50	385.51				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								
8	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 -	3,020.94	-	- -	03/2021	-	0/0
9	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	1,474.47	338.44	- -	03/2021	-	0/0
10	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39 -	566.41	759.20	- -	12/2021	-	0/0
11	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	589.15	183.72	- -	03/2022	-	0/0
12	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	2,066.77	330.82	- -	03/2023	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
13	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	1,605.17	.19	- -	03/2023	-	0/0
	<u>East Coast Railway</u>								
14	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	325.00 -	729.92	253.10	- -	03/2021	-	0/0
15	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	378.56 -	2,614.36	111.71	- -	03/2022	-	0/0
	<u>North Central Railway</u>								
16	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	2,030.50	10.34	- -	12/2022	-	0/0
	<u>North East Frontier Railway</u>								
17	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	360.00	4.98	- -	03/2020	-	0/0
18	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	380.00	102.82	- -	03/2020	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>								
19	RAYADURGA-TUMKUR NL - [N22000279]RVNL,MULTI STATE	04/2007	2,062.30 2,062.30	2,062.20	817.00	- -	03/2022	-	0/2
	<u>South Eastern Railway</u>								
20	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	365.00	224.01	- 12/2018	01/2020	13(R3)	0/0
21	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024	0(R3)	0/0
22	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	620.00	40.77	- 03/2025	03/2025	0(R3)	0/0
23	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	426.00	-	- 03/2030	03/2030	0(R3)	0/0
	<u>South Western Railway</u>								
24	MIRAJ-LONDA - [N22000327]SWR,MULTI STATE	03/2015	1,830.00 1,190.92	1,190.92	161.34	- 03/2021	03/2021	0(R3)	0/0
25	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 1,801.01	1,801.01	42.34	- 12/2023	12/2023	0(R3)	0/0
26	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 1,350.91	1,350.91	892.53	- -	12/2023	-	0/1
27	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 692.43	692.43	-	- 12/2023	12/2023	0(R3)	0/0
28	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- 12/2023	12/2023	0(R3)	0/0
29	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 348.85	348.85	.36	- 12/2023	12/2023	0(R3)	0/0
30	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 167.50	167.50	.34	- 12/2023	12/2023	0(R3)	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
31	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 367.77	367.77	.31	- 12/2023	12/2023	0(R3)	0/0
32	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 -	2,135.00	144.75	- -	12/2024	-	0/0
	<u>Southern Railway</u>								
33	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	83.15	- -	03/2020	-	0/0
	<u>Western Railway</u>								
34	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	844.10	79.08	- -	03/2023	-	0/0
	Total		19,462.59 -	29,726.03	4,582.13				0/3
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>National Highways Authority Of India</u>								
35	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	794.30	442.07	- -	05/2019	-	0/0
36	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	273.06	199.72	- -	05/2019	-	0/0
37	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	290.73	159.04	- -	05/2019	-	0/0
38	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	479.00	453.09	- -	06/2019	-	0/0
39	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	810.22	516.64	- -	06/2019	-	0/0
40	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	1,069.65	-	- -	06/2019	-	0/0
41	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	328.67	-	- -	06/2019	-	0/0
42	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	998.18	263.46	- -	08/2019	-	0/0
43	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	763.08	207.06	- -	08/2019	-	0/0
44	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	723.64	174.10	- -	09/2019	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
45	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI, GUJARAT	12/2016	417.19 -	417.19	173.51	- -	09/2019	-	0/0
46	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	845.24	758.13	- -	10/2019	-	0/0
47	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	720.00	244.82	- -	10/2019	-	0/0
48	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	834.64	81.26	- -	10/2019	-	0/0
49	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI, ODISHA	12/2015	752.28 -	752.28	-	- -	11/2019	-	0/0
50	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN	07/2016	688.70 -	688.70	552.52	- -	11/2019	-	0/0
51	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI, HIMACHAL PRADESH	10/2016	447.75 -	447.75	162.78	- -	11/2019	-	0/0
52	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	1,167.45	78.28	- -	12/2019	-	0/0
53	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI, GUJARAT	05/2016	364.56 -	364.56	56.16	- -	12/2019	-	0/0
54	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI, JHARKHAND	07/2016	458.03 -	458.03	59.62	- -	12/2019	-	0/0
55	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN	09/2016	1,100.19 -	1,100.19	750.00	- -	12/2019	-	0/0
56	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	361.15	77.11	- -	01/2020	-	0/0
57	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI, BIHAR	08/2015	814.04 -	814.04	328.86	- -	01/2020	-	0/0
58	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI, GUJARAT	07/2016	829.97 -	829.97	74.67	- -	01/2020	-	0/0
59	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	196.05	9.03	- -	01/2020	-	0/0
60	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	1,443.00	275.21	- -	02/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
61	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	1,668.00	490.12	- -	02/2020	-	0/0
62	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	1,244.10	85.00	- -	02/2020	-	0/0
63	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	379.90	62.24	- -	03/2020	-	0/0
64	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	686.65	-	- -	03/2020	-	0/0
65	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	275.12	-	- -	03/2020	-	0/0
66	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	307.79	-	- -	03/2020	-	0/0
67	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	198.05	-	- -	03/2020	-	0/0
68	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	1,282.94	-	- -	04/2020	-	0/0
69	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	1,737.00	178.80	- -	04/2020	-	0/0
70	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	1,169.61	361.32	- -	04/2020	-	0/0
71	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	1,239.82	795.68	- -	05/2020	-	0/0
72	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	1,232.21	637.48	- -	05/2020	-	0/0
73	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	668.86	-	- -	05/2020	-	0/0
74	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	1,408.00	5.71	- -	07/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
75	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	1,273.71	-	- -	07/2020	-	0/0
76	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	1,008.96	130.32	- -	07/2020	-	0/0
77	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	686.65	-	- -	07/2020	-	0/0
78	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	1,031.95	367.00	- -	08/2020	-	0/0
79	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	960.24	-	- -	08/2020	-	0/0
80	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	1,583.18	234.67	- -	09/2020	-	0/0
81	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	1,103.88	129.11	- -	09/2020	-	0/0
82	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	642.41	84.54	- -	10/2020	-	0/0
83	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	404.94	39.25	- -	10/2020	-	0/0
84	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	505.35	32.77	- -	11/2020	-	0/0
85	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	628.71	31.45	- -	11/2020	-	0/0
86	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	291.53	5.16	- -	11/2020	-	0/0
87	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	289.21	5.76	- -	11/2020	-	0/0
88	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	1,308.73	-	- -	12/2020	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
89	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI, ANDHRA PRADESH	03/2018	314.43 -	314.43	-	- -	12/2020	-	0/0
90	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	642.13	47.07	- -	12/2020	-	0/0
91	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI, GUJARAT	01/2017	1,251.11 -	1,251.11	842.34	- -	01/2021	-	0/0
92	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB	02/2018	261.76 -	261.76	7.90	- -	01/2021	-	0/0
93	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	1,052.21	-	- -	01/2021	-	0/0
94	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI, MAHARASHTRA	01/2018	621.00 -	621.00	-	- -	04/2021	-	0/0
95	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	478.74	-	- -	05/2021	-	0/0
96	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	503.88	-	- -	06/2021	-	0/0
97	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	1,071.61	-	- -	07/2021	-	0/0
98	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	1,064.88	-	- -	07/2021	-	0/0
99	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI, ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	-	- -	07/2021	-	0/0
100	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA	03/2018	1,162.92 -	1,162.92	-	- -	07/2021	-	0/0
	Total		53,163.92 -	53,163.92	10,670.83				0/0
	URBAN DEVELOPMENT								
	Central Public Works Department								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (April 2019)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
101	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 250.00	422.00	-	- 12/2020	12/2020	0(R3)	0/0
102	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 250.00	392.00	11.91	- 08/2020	03/2021	7(R3)	0/0
103	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	348.77	12.00	- -	11/2021	-	0/0
	Total		1,162.77 -	1,162.77	23.91				0/0
	Grand Total		76,529.49	86,793.02	15,731.57				5/29

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS	10/2013	314.61 -	09/2018 -	06/2020	0/0
	<u>COAL</u>					
	<u>Mahanadi Coal Fields Limited</u>					
2	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA	11/2018	2,838.87 -	03/2029 -	03/2029	0/0
	<u>Neyveli Lignite Corporation</u>					
3	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	09/2019	0/0
4	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	12/2019	0/0
5	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH	07/2016	17,237.00 -	11/2021 -	11/2021	0/0
	<u>Western Coal Fields Limited</u>					
6	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 -	03/2020 -	03/2020	0/0
7	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	409.87 -	03/2022 -	03/2022	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					
8	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT - [N12000097]SAIL,JHARKHAND	02/2014	4,749.00 -	09/2017 -	-	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
9	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 -	06/2019 -	06/2019	0/0
10	MMPL PIPELINE REROUTING PROJECT - [N16000261]BPCL,MAHARASHTRA	04/2013	449.58 -	12/2019 -	12/2019	0/0
11	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	03/2021 -	03/2021	0/0
12	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA	09/2018	11,130.00 -	03/2023 -	03/2023	0/0
13	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU	11/2012	678.00 -	02/2017 -	-	0/0
	<u>Chennai Petroleum Corporation Limited</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
14	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00	12/2019	12/2019	0/0
15	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00	08/2020	08/2020	0/0
	<u>Gas Authority Of India Limited</u>					
16	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]GAIL,KARNATAKA	02/2015	749.00	02/2020	02/2020	0/0
17	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42	08/2020	08/2020	0/0
18	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA	07/2017	243.53	07/2022	07/2022	0/0
19	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]GAIL,ODISHA	07/2017	182.20	07/2022	07/2022	0/0
20	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR	10/2017	359.25	10/2022	10/2022	0/0
21	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR - [N16000330]GAIL,JHARKHAND	10/2017	221.45	10/2022	10/2022	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
22	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]HPCL,MAHARASHTRA	09/2015	4,199.00	03/2020	07/2019	0/0
23	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26	06/2020	06/2020	0/0
24	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50	06/2020	06/2020	0/0
25	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR-CHAMPA IN STATE OF CHHATTISGARH - [N16000311]HPCL,CHHATTISGARH	12/2016	300.00	04/2021	04/2021	0/0
	<u>Indian Oil Corporation Limited</u>					
26	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]IOCL,UTTAR PRADESH	03/2014	204.00	09/2019	09/2019	0/0
27	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00	02/2020	02/2020	0/0
28	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00	06/2020	06/2020	0/0
29	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00	06/2020	08/2020	0/0
30	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]IOCL,WEST BENGAL	04/2016	1,021.00	12/2020	12/2020	0/0
31	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00	01/2021	01/2021	0/0
32	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00	01/2021	01/2021	0/0
33	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]IOCL,ANDHRA PRADESH	01/2015	342.00	03/2021	03/2021	0/0
34	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM - [N16000270]IOCL,ANDHRA PRADESH	07/2014	247.00	03/2021	03/2021	0/0
35	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00	03/2021	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
36	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	01/2021 -	04/2021	0/0
37	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 -	04/2021	0/0
38	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	04/2021 -	07/2021	0/0
39	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	10/2020 -	08/2021	0/0
40	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	01/2021 -	10/2021	0/0
41	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA	04/2018	5,654.00 -	10/2021 -	10/2021	0/0
42	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 -	10/2021	0/0
43	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2021	0/0
44	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	04/2022	0/0
45	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
46	REPLACEMENT OF KV SECTION OF KSPL - [N16000287]IOCL,GUJARAT	10/2014	279.00 -	08/2018 -	-	0/0
<u>Indian Strategic Petroleum Reserves Ltd</u>						
47	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRL,KARNATAKA	01/2006	993.00 -	01/2012 -	-	0/0
<u>Mangalore Refinery And Petrochemicals Limited</u>						
48	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 -	03/2020 -	03/2020	0/0
<u>Oil India Limited</u>						
49	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	01/2019 -	09/2019	0/0
50	50MW WIND ENERGY POWER PROJECT - [N16000298]OIL,MULTI STATE	11/2015	500.00 -	06/2017 -	-	0/0
<u>POWER</u>						
<u>Chenab Valley Power Projects [P] Limited</u>						
51	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	12/2023	0/0
<u>National Hydro-Electric Power Corporation</u>						
52	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	09/2010 -	-	0/0
<u>National Thermal Power Corporation</u>						
53	TALAI PALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	11/2019	0/0
54	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Power Grid Corporation Of India Limited</u>					
55	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 03/2018	05/2019	0/0
56	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 562.25	03/2019 03/2019	05/2019	0/0
57	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 608.24	04/2019 04/2019	05/2019	0/0
58	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	04/2016 12/2017	06/2019	0/0
59	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]PGCIL,BIHAR	04/2016	790.13 790.30	06/2019 06/2019	06/2019	0/0
60	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 844.64	04/2019 04/2019	06/2019	0/0
61	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]PGCIL,RAJASTHAN	07/2016	1,429.38 1,429.38	01/2019 07/2019	06/2019	0/0
62	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]PGCIL,MULTI STATE	03/2017	251.60 251.60	06/2019 06/2019	06/2019	0/0
63	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE	02/2017	322.30 322.30	02/2019 06/2019	06/2019	0/0
64	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 235.53	06/2019 06/2019	06/2019	0/0
65	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]PGCIL,MULTI STATE	03/2017	337.75 337.75	06/2019 06/2019	06/2019	0/0
66	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	06/2019	0/0
67	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 186.17	07/2019 07/2019	07/2019	0/0
68	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 3,519.59	05/2019 05/2019	09/2019	0/0
69	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 408.46	01/2019 09/2019	09/2019	0/0
70	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 175.64	09/2018 09/2019	09/2019	0/0
71	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 445.89	02/2019 12/2019	09/2019	0/0
72	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 193.14	06/2019 09/2019	09/2019	0/0
73	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 14,733.37	11/2019 11/2019	11/2019	0/0
74	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 283.72	11/2019 11/2019	11/2019	0/0
75	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 808.63	01/2018 12/2019	12/2019	0/0
76	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 379.85	12/2019 12/2019	12/2019	0/0
77	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 4,754.42	12/2018 12/2018	12/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
78	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL, WEST BENGAL	04/2016	454.11 454.11	04/2018 01/2020	01/2020	0/0
79	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]PGCIL, MULTI STATE	02/2017	195.05 195.05	02/2020 02/2020	02/2020	0/0
80	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALAR EN - [N18000264]PGCIL, MULTI STATE	08/2017	1,931.39 1,931.39	02/2020 02/2020	02/2020	0/0
81	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL, MULTI STATE	09/2017	198.49 198.49	09/2019 02/2020	02/2020	0/0
82	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL, MULTI STATE	02/2017	5,070.13 5,070.13	04/2020 04/2020	04/2020	0/0
83	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL, MULTI STATE	11/2017	358.83 358.83	05/2020 05/2020	05/2020	0/0
84	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL, MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 -	07/2020	0/0
85	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL, MULTI STATE	12/2014	5,111.33 5,111.33	12/2018 12/2018	12/2020	0/0
	<u>Thdc India Limited</u>					
86	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL, UTTAR PRADESH	03/2019	11,089.42 -	09/2023 -	09/2023	0/0
	<u>HEAVY INDUSTRY</u>					
	<u>Bharat Heavy Electricals Limited</u>					
87	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL, DELHI	08/2016	1,554.00 -	09/2019 -	09/2019	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>HII Infra Tech Services Limited</u>					
88	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES, UTTAR PRADESH	07/2016	785.00 -	04/2020 -	04/2020	0/0
89	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES, PUNJAB	07/2016	703.00 -	06/2020 -	06/2020	0/0
90	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES, ASSAM	05/2017	875.00 -	05/2021 -	05/2021	0/0
	<u>Hospital Services Consultancy Corporation</u>					
91	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	- -	02/2020	0/0
92	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	- -	02/2020	0/0
93	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	02/2020	0/0
94	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC, UTTAR PRADESH	03/2018	268.84 -	- -	04/2020	0/0
95	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC, GOA	01/2018	249.01 -	- -	05/2020	0/0
96	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC, ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Hospital Services Consultancy Corporation Ltd</u>					
97	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	09/2019	0/0
98	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	02/2020	0/0
99	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	10/2020	0/0
100	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	-	0/0
101	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	-	0/0
102	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	-	0/0
103	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15 -	03/2019 -	-	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
104	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 199.12	03/2019 -	03/2019	0/0
105	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 2,271.50	03/2021 -	03/2021	0/0
106	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 792.89	03/2021 -	03/2021	0/0
107	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 540.02	03/2022 -	03/2022	0/0
108	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 1,272.19	03/2022 -	03/2022	0/0
109	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 3,168.29	03/2023 -	03/2023	0/0
110	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 2,449.91	03/2023 -	03/2023	0/0
111	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 2,081.27	03/2023 -	03/2023	0/0
112	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 1,035.16	03/2022 -	03/2023	0/0
113	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 637.95	03/2023 -	03/2023	0/0
114	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
115	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
116	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	03/2024	0/0
117	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 3,627.47	03/2024 -	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
118	AMRAVATI-NARKHER NL(CR) - [220100118]CR, MAHARASHTRA	06/1994	663.01 668.34	06/1999 -	-	0/0
	<u>Container Corporation Of India</u>					
119	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	12/2019	0/0
120	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	12/2019	0/0
121	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	02/2020	0/0
122	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	03/2020	0/0
123	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	03/2020	0/0
124	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	12/2020	0/0
125	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
126	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
127	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	03/2020	0/0
128	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
	<u>East Central Railways</u>					
129	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	03/2019 -	12/2019	0/0
130	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, BIHAR	04/1997	324.73 -	03/2012 -	03/2020	0/0
131	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 -	03/2020 -	03/2020	0/0
132	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR	04/1996	477.88 283.95	03/2012 -	03/2020	0/0
133	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR, BIHAR	04/2009	548.00 -	03/2020 -	03/2020	0/0
134	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	03/2021 -	12/2020	0/0
135	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, JHARKHAND	03/1999	1,033.07 -	- -	03/2021	0/0
136	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 -	- -	03/2021	0/0
137	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	03/2020 -	03/2021	0/0
138	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR, BIHAR	11/2001	624.47 -	02/2016 -	03/2021	0/0
139	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FROM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR, BIHAR	04/1991	329.39 -	- -	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
140	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	03/2022	0/0
141	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 -	03/2022	0/0
142	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	03/2021 -	03/2022	0/0
143	HAJIPUR-SAGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	03/2023	0/0
144	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17 -	- -	03/2023	0/0
145	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-	0/0
146	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-	0/0
147	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	- -	-	0/0
148	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-	0/0
149	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-	0/0
150	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-	0/0
151	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-	0/0
152	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-	0/0
153	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-	0/0
154	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-	0/0
155	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	- -	-	0/0
156	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
157	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82 -	- -	-	0/0
	<u>East Coast Railway</u>					
158	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	03/2020 -	03/2020	0/0
159	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]ECOR,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2020	0/0
160	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	325.00 -	- -	03/2021	0/0
161	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	03/2021	0/0
162	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	10/2020 -	03/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
163	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 -	03/2021	0/0
164	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	12/2018 -	03/2021	0/0
165	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	03/2009 -	06/2021	0/0
166	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	378.56 -	-	03/2022	0/0
167	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 -	03/2022 -	03/2022	0/0
168	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 -	03/2022	0/0
169	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2022 -	03/2022	0/0
170	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	06/2021 -	03/2023	0/0
171	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	-	-	0/0
172	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	-	-	0/0
173	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	-	-	0/0
<u>Eastern Railways</u>						
174	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	01/2006	0/0
175	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 02/2010	02/2010	0/0
176	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	05/2010	0/0
177	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	193.08 -	12/2011 -	09/2012	0/0
178	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 12/2013	12/2013	0/0
179	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER,WEST BENGAL	04/2009	259.51 -	02/2012 -	09/2016	0/0
180	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	03/2016 -	03/2020	0/0
181	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2020	0/0
182	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2020	0/0
183	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2022	0/0
184	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2022	0/0
185	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
186	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-	0/0
187	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-	0/0
188	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-	0/0
189	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-	0/0
190	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-	0/0
191	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	-	0/0
192	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	-	0/0
193	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-	0/0
194	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-	0/0
195	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-	0/0
196	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	-	0/0
197	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	-	0/0
198	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-	0/0
199	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-	0/0
200	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	-	0/0
201	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-	0/0
202	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-	0/0
203	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-	0/0
204	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER,WEST BENGAL	04/2012	255.64 -	- -	-	0/0
Kochi Metro Rail Corporation Ltd						
205	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KMRCL,WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-	0/0
Metropolitan Rapid Transport Projects						
206	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	03/2004 -	03/2020	0/0
207	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
209	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
210	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-	0/0
211	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
212	JHANSI BINA DOUBLING - [N22000496]NCR, UTTAR PRADESH	09/2016	2,001.00 -	03/2021 -	03/2021	0/0
213	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR, MULTI STATE	04/2011	2,912.96 -	03/2022 -	03/2022	0/0
214	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	12/2022	0/0
215	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	03/2023	0/0
216	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR, MULTI STATE	04/1986	158.77 274.56	03/1994 -	-	0/0
217	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, UTTAR PRADESH	04/1999	108.00 -	12/2009 -	-	0/0
218	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
	<u>North East Frontier Railway</u>					
219	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NFR, TRIPURA	04/1999	895.00 984.97	03/2007 -	04/2016	0/0
220	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	03/2019	0/0
221	AGARTALA SABROOM, NL, NEFR - [N22000099]NFR, TRIPURA	04/2008	1,142.00 3,407.00	03/2014 12/2019	03/2019	0/0
222	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 -	03/2019 -	03/2019	0/0
223	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	03/2019	0/0
224	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NFR, ASSAM	04/2012	246.07 614.81	03/2019 -	03/2019	0/0
225	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	03/2020	0/0
226	JIRIBAM TO IMPHAL (TUPUI) (NL) (NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	03/2011 -	03/2020	0/0
227	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	03/2019 -	03/2020	0/0
228	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2020	0/0
229	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
230	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
231	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	03/2020	0/0
232	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	03/2020	0/0
233	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	03/2020	0/0
234	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	03/2020	0/0
235	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2020	0/0
236	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR,WEST BENGAL	04/2016	602.27 -	12/2021 -	03/2020	0/0
237	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 2,393.48	03/2014 12/2020	12/2020	0/0
238	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	03/2021	0/0
239	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2021	0/0
240	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 2,446.57	03/2015 10/2021	10/2021	0/0
241	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NFR,BIHAR	09/2001	792.46 724.31	12/2010 -	-	0/0
242	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- -	-	0/0
243	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
<u>North Eastern Railway</u>						
244	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	08/2018 -	01/2019	0/0
245	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]NER,UTTAR PRADESH	04/1997	609.04 1,063.00	04/1999 -	03/2019	0/0
246	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42 -	03/2022 -	12/2019	0/0
247	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	01/2020	0/0
248	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	01/2020	0/0
249	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00 -	01/2022 -	01/2020	0/0
250	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	02/2020	0/0
251	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
252	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00 -	01/2022 -	01/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
253	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	04/2017 -	04/2022	0/0
254	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	04/2017 -	10/2022	0/0
255	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-	0/0
256	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-	0/0
257	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-	0/0
258	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-	0/0
259	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]NER,UTTAR PRADESH	04/1997	233.00 -	04/1999 -	-	0/0
260	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-	0/0
261	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	- -	-	0/0
262	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	06/2018 -	10/2018	0/0
263	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	12/2022 -	05/2019	0/0
264	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	-	0/0
265	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	- -	03/2018	0/0
<u>North Western Railway</u>						
266	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	09/2019	0/0
267	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	12/2019	0/0
268	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	05/2020	0/0
269	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	06/2020	0/0
270	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 295.02	03/2020 -	06/2020	0/0
271	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	03/2015 -	10/2020	0/0
272	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	02/2019 -	12/2021	0/0
273	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	03/2020 -	04/2022	0/0
274	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	08/2022 -	09/2022	0/0
275	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
276	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-	0/0
	<u>Northern Railway</u>					
277	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	11/2002 -	03/2021	0/0
278	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14 -	03/2023 -	03/2023	0/0
279	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	07/2012 -	-	0/0
280	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-	0/0
281	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 -	-	0/0
282	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	369.90 -	03/2010 -	-	0/0
283	MEERUT-MUZAFFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-	0/0
284	MANSABHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-	0/0
285	GRADE SEPARATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-	0/0
286	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-	0/0
287	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-	0/0
288	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	-	0/0
289	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-	0/0
290	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-	0/0
291	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-	0/0
292	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-	0/0
293	JAKHAL-MANSAB DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-	0/0
294	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-	0/0
295	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-	0/0
296	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	- -	-	0/0
297	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-	0/0
298	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
299	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
300	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00 -	12/2023 12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
301	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
302	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	03/2020	0/0
303	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	03/2008 -	03/2020	0/0
304	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	03/2019 -	03/2020	0/0
305	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	03/2020 -	03/2020	0/0
306	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	03/2020 -	03/2020	0/0
307	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	03/2020 -	03/2020	0/0
308	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	03/2016 03/2017	12/2020	0/0
309	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	12/2020 -	12/2020	0/0
310	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	03/2021	0/0
311	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	03/2019 -	03/2021	0/0
312	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	12/2020 -	03/2021	0/0
313	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 245.00	02/2015 -	12/2021	0/0
314	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62 -	12/2021 -	12/2021	0/0
315	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	12/2021 -	12/2021	0/0
316	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	631.78 632.00	12/2012 -	03/2022	0/0
317	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	03/2020 -	03/2022	0/0
318	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26 -	12/2023 -	12/2023	0/0
319	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	03/2022 -	12/2024	0/0
320	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94 -	12/2024 -	12/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
321	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	03/2023 -	12/2024	0/0
322	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 2,335.67	12/2024 -	12/2024	0/0
323	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	03/2016 -	03/2025	0/0
324	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 4,200.00	03/2016 -	03/2025	0/0
325	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78 -	12/2025 -	03/2025	0/0
326	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	03/2014 -	12/2025	0/0
327	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	12/2024 -	03/2026	0/0
328	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99 -	12/2026 -	12/2026	0/0
<u>Railway Electrification</u>						
329	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-	0/0
<u>South Central Railway</u>						
330	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000 -	03/2019	0/0
331	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2021	0/0
332	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022 -	03/2022	0/0
333	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	03/2009 -	03/2023	0/0
334	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2023	0/0
335	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
336	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
337	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	458.25 -	- -	-	0/0
338	GUDUR-DURGARAJAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
339	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
340	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 -	12/2019 -	12/2019	0/0
341	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	03/2012 -	03/2020	0/0
342	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 -	04/2020 -	04/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
343	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00	03/2021	03/2021	0/0
344	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00	12/2021	12/2021	0/0
345	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00	12/2021	12/2021	0/0
346	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM - [N22000482]SECR,CHHATISGARH	04/2011	1,471.93	03/2022	03/2022	0/0
347	GEVRA ROAD PENDRA ROAD - [N22000488]SECR,CHHATISGARH	02/2014	2,288.00	03/2022	03/2022	0/0
348	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51	03/2023	03/2023	0/0
349	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79	-	-	0/0
350	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93	02/2019	-	0/0
351	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]SECR,CHHATISGARH	04/2013	3,055.00	09/2018	-	0/0
<u>South Eastern Railway</u>						
352	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44	12/2015 12/2018	02/2019	0/0
353	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77	12/2016 08/2018	09/2019	0/0
354	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20	- 12/2018	01/2020	0/0
355	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83	03/2020 03/2020	06/2020	0/0
356	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	03/2021 03/2021	12/2021	0/0
357	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]SER,WEST BENGAL	01/1991	1,013.45 1,013.45	12/2021 12/2021	12/2021	0/0
358	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00	03/2015 03/2024	03/2024	0/0
359	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48	- 12/2024	12/2024	0/0
360	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]SER,ODISHA	04/1995	524.43	12/2021 12/2024	12/2024	0/0
361	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37	- 03/2025	03/2025	0/0
362	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69	- 03/2030	03/2030	0/0
363	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 1,966.70	03/2003 03/2030	03/2030	0/0
364	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
365	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97	06/2005 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
366	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	- -	-	0/0
367	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
368	ARA-BHABHUA ROAD (NL) - [N22000166]SER, BIHAR	04/2008	633.87 -	- -	-	0/0
<u>South Western Railway</u>						
369	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 860.43	03/2020 03/2020	03/2020	0/0
370	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 889.52	03/2017 -	03/2020	0/0
371	MIRAJ-LONDA - [N22000327]SWR, MULTI STATE	03/2015	1,830.00 1,190.92	- 03/2021	03/2021	0/0
372	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE	03/2015	1,614.59 1,870.41	03/2019 03/2021	03/2021	0/0
373	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01 1,801.01	- 12/2023	12/2023	0/0
374	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR, KARNATAKA	04/2013	558.00 692.43	- 12/2023	12/2023	0/0
375	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR, MULTI STATE	04/2013	296.00 -	- 12/2023	12/2023	0/0
376	WHITE FIELD-KOLAR NL - [N22000280]SWR, KARNATAKA	04/2011	348.85 348.85	- 12/2023	12/2023	0/0
377	TORANAGALLU-RANJITPURA DL - [N22000298]SWR, KARNATAKA	04/2011	146.75 167.50	- 12/2023	12/2023	0/0
378	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR, KARNATAKA	04/2013	327.25 367.77	- 12/2023	12/2023	0/0
379	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	279.54 279.54	03/2016 12/2023	12/2023	0/0
380	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, KARNATAKA	04/1996	1,382.78 1,382.78	03/2002 03/2024	03/2024	0/0
381	SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA	04/2011	832.47 -	03/2016 03/2024	03/2024	0/0
382	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, KARNATAKA	04/1997	2,315.00 -	- -	12/2024	0/0
383	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	2,841.84 2,841.84	12/2018 12/2024	12/2024	0/0
<u>Southern Railway</u>						
384	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	724.69 -	02/2019 -	02/2019	0/0
385	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR, MULTI STATE	04/2011	120.70 -	03/2019 -	03/2019	0/0
386	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR, TAMIL NADU	02/1999	257.00 -	03/2018 -	03/2018	0/0
387	MADURAI-BODINAYAKKANUR - [N22000201]SR, TAMIL NADU	04/2008	164.41 -	- -	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
388	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	03/2020	0/0
389	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	03/2020	0/0
390	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	03/2022	0/0
391	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
392	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	-	0/0
393	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	-	0/0
394	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-	0/0
395	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	- -	-	0/0
396	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-	0/0
397	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	-	0/0
398	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-	0/0
399	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-	0/0
400	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-	0/0
401	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-	0/0
402	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1998	271.24 -	- -	-	0/0
403	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-	0/0
404	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-	0/0
405	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-	0/0
406	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-	0/0
407	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-	0/0
408	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-	0/0
409	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-	0/0
410	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION - [N22000439]SR,TAMIL NADU	02/1997	458.63 -	03/2015 -	-	0/0
411	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION - [N22000440]SR,TAMIL NADU	02/2000	200.84 -	03/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
412	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	-	0/0
413	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-	0/0
414	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]SR,TAMIL NADU	02/2005	600.00 600.00	03/2010 -	-	0/0
415	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANAL ROAD) (62.05 KM) DOUBLING - [N22000450]SR,TAMIL NADU	02/2003	199.55 -	03/2009 -	-	0/0
416	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION. - [N22000453]SR,TAMIL NADU	02/2006	208.00 -	03/2012 -	-	0/0
417	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING. - [N22000454]SR,KERALA	02/2005	241.00 -	03/2014 -	-	0/0
	<u>West Central Railway</u>					
418	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	03/2021 -	03/2021	0/0
	<u>Western Railway</u>					
419	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	03/2012 -	03/2019	0/0
420	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 -	03/2020 -	03/2020	0/0
421	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 -	03/2021 -	03/2020	0/0
422	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 -	03/2020 -	03/2020	0/0
423	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 -	06/2020 -	06/2020	0/0
424	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 -	03/2022 -	03/2022	0/0
425	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	03/2022 -	03/2022	0/0
426	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	03/2022 -	03/2022	0/0
427	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	03/2019 -	03/2022	0/0
428	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 -	- -	03/2023	0/0
429	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
430	GANDHINAGAR REDEVELOPMENT OF STATION ALONG WITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATION - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
431	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
432	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
433	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
434	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR, GUJARAT	03/2012	153.83 -	- -	-	0/0
435	BHILDI-VIRANGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR, GUJARAT	02/1991	551.51 -	03/2019 -	-	0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					
	<u>Ministry Of Road Transport And Highways</u>					
436	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH, RAJASTHAN	02/2015	383.40 -	03/2015 -	06/2019	0/0
437	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MORTH, UTTARAKHAND	06/2017	282.08 -	06/2019 -	06/2019	0/0
438	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MORTH, UTTARAKHAND	11/2017	232.81 -	11/2019 -	11/2019	0/0
439	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MORTH, UTTARAKHAND	11/2017	283.51 -	11/2019 -	11/2019	0/0
440	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MORTH, UTTARAKHAND	11/2017	266.52 -	11/2019 -	11/2019	0/0
441	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MORTH, A & N ISLANDS	11/2017	237.80 -	11/2019 -	11/2019	0/0
442	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MORTH, A & N ISLANDS	11/2017	257.34 -	11/2019 -	11/2019	0/0
443	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MORTH, UTTARAKHAND	12/2017	257.34 -	12/2019 -	12/2019	0/0
444	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MORTH, UTTARAKHAND	12/2017	200.34 -	12/2019 -	12/2019	0/0
445	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MORTH, UTTARAKHAND	12/2017	248.22 -	12/2019 -	12/2019	0/0
446	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MORTH, UTTARAKHAND	02/2018	418.88 -	02/2020 -	02/2020	0/0
447	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MORTH, UTTARAKHAND	05/2018	248.00 -	05/2020 -	05/2020	0/0
448	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735 (IBRAHIMPATNAM TO CHANDR - [N24000273]MORTH, ANDHRA PRADESH	07/2015	314.43 -	- -	-	0/0
449	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MORTH, MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
450	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION - [N24000276]MORTH, MAHARASHTRA	12/2011	156.26 227.00	- -	-	0/0
451	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA - [N24000277]MORTH, MAHARASHTRA	03/2011	185.82 292.00	- -	-	0/0
452	REHABILITATION AND UPGRADEATION OF NH-64 FROM KM.0.00 TO 28.110 (ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I - [N24000288]MORTH, CHHATISGARH	03/2015	422.34 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
453	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K - [N24000293]MORTH,ANDHRA PRADESH	10/2015	480.21 -	- -	-	0/0
454	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K - [N24000294]MORTH,RAJASTHAN	10/2014	269.22 -	01/2015 -	-	0/0
455	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING - [N24000295]MORTH,RAJASTHAN	10/2014	257.09 -	01/2015 -	-	0/0
456	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS - [N24000296]MORTH,RAJASTHAN	10/2013	278.87 -	05/2014 -	-	0/0
457	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O - [N24000297]MORTH,RAJASTHAN	01/1991	376.52 -	04/2014 -	-	0/0
458	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MORTH,TAMIL NADU	03/2015	258.97 -	08/2015 -	-	0/0
459	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO - [N24000317]MORTH,TAMIL NADU	03/2015	157.18 162.00	07/2015 -	-	0/0
460	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I - [N24000318]MORTH,TAMIL NADU	11/2015	154.14 -	08/2015 -	-	0/0
461	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE) - [N24000330]MORTH,UTTAR PRADESH	03/2015	629.74 -	- -	-	0/0
462	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
463	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MORTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
464	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MORTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
465	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU - [N24000335]MORTH,KARNATAKA	03/2015	159.12 -	11/2015 -	-	0/0
466	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE - [N24000336]MORTH,UTTAR PRADESH	10/2014	227.74 -	10/2016 -	-	0/0
467	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI - [N24000369]MORTH,RAJASTHAN	01/1991	269.26 -	10/2016 -	-	0/0
468	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB - [N24000376]MORTH,KARNATAKA	01/1991	219.40 -	01/2018 -	-	0/0
469	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB - [N24000379]MORTH,ODISHA	01/1991	218.63 -	10/2017 -	-	0/0
470	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MORTH,BIHAR	01/1991	675.00 -	- -	-	0/0
471	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL - [N24000397]MORTH,WEST BENGAL	01/1991	322.00 -	03/2018 -	-	0/0
472	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000398]MORTH,BIHAR	01/1991	282.41 -	08/2016 -	-	0/0
473	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000402]MORTH,BIHAR	01/1991	358.22 -	10/2016 -	-	0/0
474	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARAULI - [N24000406]MORTH,RAJASTHAN	01/1991	208.87 -	05/2016 -	-	0/0
475	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK - [N24000414]MORTH,ODISHA	01/1991	229.41 -	05/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
476	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MORTH,GOA	10/2015	936.40 -	- -	-	0/0
477	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
478	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000512]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
479	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MORTH,GOA	12/2015	773.98 -	- -	-	0/0
480	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MORTH,GOA	12/2015	819.95 -	- -	-	0/0
481	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF - [N24000519]MORTH,BIHAR	01/1991	478.35 -	- -	-	0/0
482	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE) - [N24000529]MORTH,UTTAR PRADESH	12/2014	207.88 -	- -	-	0/0
483	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000536]MORTH,BIHAR	10/2014	377.64 -	03/2014 -	-	0/0
484	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH - [N24000537]MORTH,BIHAR	10/2013	278.39 -	08/2014 -	-	0/0
485	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG - [N24000573]MORTH,BIHAR	01/2013	322.01 -	08/2014 -	-	0/0
486	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MORTH,BIHAR	11/2013	683.83 -	07/2016 -	-	0/0
487	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING - [N24000575]MORTH,BIHAR	02/2014	665.50 -	07/2016 -	-	0/0
488	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MORTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
489	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000577]MORTH,BIHAR	02/2016	369.77 -	06/2016 -	-	0/0
490	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MORTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
491	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MORTH,BIHAR	01/2014	1,408.85 -	10/2016 -	-	0/0
492	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV - [N24000580]MORTH,BIHAR	03/2015	206.80 -	07/2016 -	-	0/0
493	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE - [N24000581]MORTH,BIHAR	08/2015	288.24 -	11/2015 -	-	0/0
494	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MORTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
495	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MORTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
496	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGEWAY W - [N24000640]MORTH,ODISHA	01/2015	326.63 327.00	04/2018 -	-	0/0
497	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM - [N24000641]MORTH,ODISHA	02/2015	239.91 240.00	10/2017 -	-	0/0
498	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900 - [N24000642]MORTH,ODISHA	03/2015	226.31 226.00	10/2017 -	-	0/0
499	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED - [N24000643]MORTH,ODISHA	12/2013	319.80 320.00	05/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
500	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN - [N24000644]MORTH,ODISHA	07/2014	342.05 342.00	01/2017 -	-	0/0
501	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MORTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
502	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG - [N24000646]MORTH,ODISHA	06/2016	157.30 157.00	06/2018 -	-	0/0
503	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8 - [N24000647]MORTH,ODISHA	03/2014	162.51 163.00	05/2016 -	-	0/0
504	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MORTH,UTTARAKHAND	02/2018	293.68 -	- -	-	0/0
505	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MORTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
National Highways And Infrastructure Development Corporation Ltd.						
506	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL,MEGHALAYA	03/2019	306.28 -	05/2019 -	05/2019	0/0
507	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	07/2019	0/0
508	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	09/2019 -	09/2019	0/0
509	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	09/2019 -	09/2019	0/0
510	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	09/2019 -	09/2019	0/0
511	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	09/2019 -	09/2019	0/0
512	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	09/2019 -	09/2019	0/0
513	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	09/2019 -	09/2019	0/0
514	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	09/2019 -	09/2019	0/0
515	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	09/2019 -	09/2019	0/0
516	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	- -	-	0/0
517	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683 - [N24000689]NHIDCL,NAGALAND	02/2017	507.68 -	04/2017 -	-	0/0
518	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
519	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	09/2018 -	-	0/0
520	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	09/2018 -	-	0/0
521	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	09/2018 -	-	0/0
522	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	09/2018 -	-	0/0
523	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	09/2018 -	-	0/0
524	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWAY TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA - [N24000766]NHIDCL,SIKKIM	04/2017	318.42 -	11/2017 -	-	0/0
525	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-	0/0
526	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-	0/0
527	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I - [N24000770]NHIDCL,WEST BENGAL	03/2017	158.65 -	06/2018 -	-	0/0
528	FOUR LANEING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	01/2016 -	-	0/0
National Highways Authority Of India						
529	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	09/2018	0/0
530	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	10/2018	0/0
531	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	12/2018	0/0
532	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	08/2013 -	12/2018	0/0
533	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	12/2018	0/0
534	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	12/2018	0/0
535	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	12/2018	0/0
536	6 LANING OF AGRA - ETAWAH BYPASS - [N24000452]NHAI,UTTAR PRADESH	07/2015	1,657.20 -	01/2019 -	01/2019	0/0
537	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	02/2019	0/0
538	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	02/2019	0/0
539	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	03/2019	0/0
540	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	03/2019	0/0
541	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	03/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
542	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 -	03/2019	0/0
543	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	04/2018 -	03/2019	0/0
544	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	03/2019	0/0
545	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 09/2017	03/2019	0/0
546	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018	03/2019	0/0
547	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	03/2019	0/0
548	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI,WEST BENGAL	04/2014	1,665.00 -	- -	03/2019	0/0
549	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI,RAJASTHAN	08/2015	275.90 -	- -	03/2019	0/0
550	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR	08/2015	854.80 -	- -	03/2019	0/0
551	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION - [N24000548]NHAI,JHARKHAND	02/2016	997.15 -	03/2019 -	03/2019	0/0
552	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	03/2019	0/0
553	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 -	03/2019	0/0
554	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	03/2019	0/0
555	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	04/2019	0/0
556	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	04/2019	0/0
557	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	05/2013 -	04/2019	0/0
558	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	04/2019	0/0
559	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	10/2017 -	04/2019	0/0
560	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	05/2018 -	04/2019	0/0
561	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	04/2019	0/0
562	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	04/2019	0/0
563	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	04/2019 -	04/2019	0/0
564	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 -	04/2019	0/0
565	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	04/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
566	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH	03/2016	676.73 -	04/2019 -	04/2019	0/0
567	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	04/2019	0/0
568	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	04/2019	0/0
569	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	01/2019 -	04/2019	0/0
570	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	04/2019	0/0
571	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	05/2019	0/0
572	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	05/2019	0/0
573	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	01/2014 -	05/2019	0/0
574	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	05/2019	0/0
575	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	07/2014 -	05/2019	0/0
576	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	09/2017 -	05/2019	0/0
577	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425]NHAI,MAHARASHTRA	07/2015	2,288.18 -	05/2019 -	05/2019	0/0
578	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 -	05/2019	0/0
579	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	05/2019	0/0
580	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	-	05/2019	0/0
581	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1 - [N24000476]NHAI,PUNJAB	09/2015	273.06 -	-	05/2019	0/0
582	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	05/2019	0/0
583	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]NHAI,HARYANA	09/2016	1,004.67 -	05/2019 -	05/2019	0/0
584	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	-	05/2019	0/0
585	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	03/2008 -	06/2019	0/0
586	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	11/2011 -	06/2019	0/0
587	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	03/2013 -	06/2019	0/0
588	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	06/2019	0/0
589	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	06/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
590	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	07/2013 -	06/2019	0/0
591	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL	02/2011	1,078.84 -	08/2013 -	06/2019	0/0
592	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	06/2014 -	06/2019	0/0
593	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	06/2019	0/0
594	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	06/2019	0/0
595	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	06/2019	0/0
596	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	06/2019	0/0
597	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH	03/2015	810.22 -	- -	06/2019	0/0
598	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	01/2019 -	06/2019	0/0
599	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	04/2018 -	06/2019	0/0
600	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	05/2018 -	06/2019	0/0
601	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	06/2019	0/0
602	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	06/2019	0/0
603	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA	02/2016	1,069.65 -	- -	06/2019	0/0
604	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	06/2019	0/0
605	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	06/2019	0/0
606	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]NHAI,HARYANA	03/2017	639.79 -	03/2020 -	06/2019	0/0
607	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]NHAI,JHARKHAND	03/2017	165.50 -	03/2020 -	06/2019	0/0
608	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) - [N24000670]NHAI,JHARKHAND	03/2017	239.68 -	03/2020 -	06/2019	0/0
609	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	06/2019	0/0
610	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	07/2019	0/0
611	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	11/2018 -	07/2019	0/0
612	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	07/2019	0/0
613	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	07/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
614	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	07/2019	0/0
615	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	08/2019	0/0
616	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	08/2019	0/0
617	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	08/2019	0/0
618	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	08/2019	0/0
619	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	08/2019	0/0
620	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	05/2019 -	08/2019	0/0
621	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	08/2019	0/0
622	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	09/2019	0/0
623	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019	0/0
624	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	09/2019	0/0
625	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	09/2019	0/0
626	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	09/2019	0/0
627	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	09/2019	0/0
628	2-LANE WITH PAVED SHOULDER OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	09/2019	0/0
629	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- -	10/2019	0/0
630	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	10/2019	0/0
631	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	04/2019 -	10/2019	0/0
632	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	10/2019	0/0
633	FOUR LANING OF TALAJA - MAHUA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	10/2019	0/0
634	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28 -	- -	11/2019	0/0
635	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	11/2019	0/0
636	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	11/2019	0/0
637	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	11/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
638	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	11/2019	0/0
639	4-LANNING OF KODEBAD-DHANTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	11/2019	0/0
640	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	11/2019	0/0
641	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]NHAI,ANDHRA PRADESH	03/2017	648.32 -	03/2020 -	11/2019	0/0
642	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	11/2019	0/0
643	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	06/2017 -	11/2019	0/0
644	NALBARI T BIJINI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	12/2019	0/0
645	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	12/2019	0/0
646	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2019	0/0
647	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	12/2019	0/0
648	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 -	06/2018 -	12/2019	0/0
649	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	12/2017 -	12/2019	0/0
650	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR	12/2015	1,167.45 -	- -	12/2019	0/0
651	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	12/2019	0/0
652	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	12/2019	0/0
653	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	- -	12/2019	0/0
654	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH- [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	12/2019	0/0
655	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	12/2019	0/0
656	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	12/2019	0/0
657	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 -	- -	01/2020	0/0
658	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	- -	01/2020	0/0
659	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	01/2020	0/0
660	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	01/2020	0/0
661	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	01/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
662	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	02/2020	0/0
663	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	02/2020	0/0
664	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	02/2020	0/0
665	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	02/2020	0/0
666	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	03/2020	0/0
667	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	03/2020	0/0
668	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	03/2020	0/0
669	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	03/2020	0/0
670	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	03/2020	0/0
671	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2020	0/0
672	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	03/2020	0/0
673	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	03/2020	0/0
674	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	03/2020	0/0
675	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	03/2020	0/0
676	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	04/2020	0/0
677	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	04/2018 -	04/2020	0/0
678	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	04/2020	0/0
679	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 -	- -	04/2020	0/0
680	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	04/2020	0/0
681	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	04/2020	0/0
682	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	05/2020	0/0
683	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	05/2020	0/0
684	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	02/2020 -	05/2020	0/0
685	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	05/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
686	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	05/2020	0/0
687	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	05/2020	0/0
688	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	05/2020	0/0
689	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	05/2020	0/0
690	4-LANING OF BRAHAMPURE-FARAKA - [N24000203]NHAI, WEST BENGAL	02/2011	998.79 -	08/2013 -	06/2020	0/0
691	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	06/2020	0/0
692	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	06/2020	0/0
693	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	07/2020	0/0
694	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	07/2020	0/0
695	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	07/2020	0/0
696	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	07/2020	0/0
697	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	07/2020	0/0
698	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 -	08/2020	0/0
699	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	08/2020	0/0
700	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	08/2020	0/0
701	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	08/2020	0/0
702	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	08/2020	0/0
703	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	08/2020	0/0
704	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	08/2020	0/0
705	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO - [N24000727]NHAI,MADHYA PRADESH	01/2018	960.24 -	- -	08/2020	0/0
706	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	09/2020	0/0
707	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	09/2020	0/0
708	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	09/2020	0/0
709	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR	01/1991	642.41 -	- -	10/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
710	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 -	- -	10/2020	0/0
711	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	11/2020	0/0
712	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020	0/0
713	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	03/2020 -	11/2020	0/0
714	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	11/2020	0/0
715	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	11/2020	0/0
716	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	11/2020	0/0
717	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	11/2020	0/0
718	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	11/2020	0/0
719	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	11/2020	0/0
720	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	11/2020	0/0
721	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 -	12/2020	0/0
722	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020	0/0
723	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	12/2020	0/0
724	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	08/2019 -	12/2020	0/0
725	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	12/2020	0/0
726	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	12/2020	0/0
727	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	12/2020	0/0
728	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 -	- -	01/2021	0/0
729	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	01/2021	0/0
730	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021	0/0
731	REHABILITATION AND UPGRADATION BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	03/2021	0/0
732	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 -	03/2021	0/0
733	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	04/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
734	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	05/2021	0/0
735	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	- -	05/2021	0/0
736	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) - [N24000739]NHAI, ODISHA	01/2018	503.88 -	- -	06/2021	0/0
737	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- -	07/2021	0/0
738	4-LANNING OF TARSOD-FAGNE (FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- -	07/2021	0/0
739	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI, ANDHRA PRADESH	03/2018	1,550.98 -	- -	07/2021	0/0
740	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021	0/0
741	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI, HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
742	SIX LANNING OF AUNTA-SIMARIA (GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI, BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
743	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
744	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
745	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
746	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
747	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-	0/0
748	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
749	INDORE-DEWAS (NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-	0/0
750	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
751	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
752	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	-	0/0
753	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
754	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
755	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	06/2013 -	-	0/0
756	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
757	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
758	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	-	0/0
759	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	09/2013 -	-	0/0
760	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
761	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	-	0/0
762	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,JHARKHAND	12/2012	1,479.00 -	06/2015 -	-	0/0
763	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
764	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	04/2015 -	-	0/0
765	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE - I - [N24000347]NHAI,HARYANA	08/2015	723.54 -	02/2018 -	-	0/0
766	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
767	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
768	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
769	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
770	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
771	2-LANING WITH PS SITARGANJ BAREILY SECTION - [N24000364]NHAI,UTTAR PRADESH	06/2014	301.04 -	01/2016 -	-	0/0
772	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
773	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III) - [N24000446]NHAI,MULTI STATE	09/2015	788.51 -	03/2018 -	-	0/0
774	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II) - [N24000450]NHAI,UTTAR PRADESH	09/2015	785.78 -	03/2018 -	-	0/0
775	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
776	NAGPUR - KONDHALI - [N24000472]NHAI,MAHARASHTRA	09/2005	168.00 -	06/2006 -	-	0/0
777	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
778	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
779	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2 - [N24000492]NHAI,HARYANA	11/2015	867.66 -	05/2018 -	-	0/0
780	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
781	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
782	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
783	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
784	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
785	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
786	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR	08/2015	516.13 -	04/2018 -	-	0/0
787	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
788	MEERUT-BULANDSHAHAH - [N24000539]NHAI,UTTAR PRADESH	01/2016	683.24 -	- -	-	0/0
789	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
790	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
791	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
792	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR-HYDERABAD SECTION NS-60 - [N24000561]NHAI,MAHARASHTRA	03/2016	244.00 -	07/2018 -	-	0/0
793	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
794	4-LANING OF HOSKOTE-DOBBASPET - [N24000598]NHAI,KARNATAKA	05/2014	720.69 -	- -	-	0/0
795	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609]NHAI,DELHI	09/2015	771.18 -	- -	-	0/0
796	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0
797	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
798	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
799	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
800	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-	0/0
801	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-	0/0
802	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0
803	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	- -	-	0/0
804	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 -	- -	-	0/0
805	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
806	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 -	- -	-	0/0
807	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
808	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
809	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
810	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
811	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-	0/0
812	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-	0/0
813	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-	0/0
814	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
815	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12 UNDE - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
816	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	- -	-	0/0
817	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	-	0/0
818	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-	0/0
819	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	- -	-	0/0
820	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	- -	-	0/0
821	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-	0/0
822	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-	0/0
823	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
824	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
825	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-	0/0
826	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
827	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	-	0/0
828	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
829	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	-	0/0
830	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
831	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 -	- -	-	0/0
832	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
833	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
834	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
835	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	-	0/0
836	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH. - [N24000797]NHAI,RAJASTHAN	02/2018	716.76 -	- -	-	0/0
837	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
838	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	-	0/0
839	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
840	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
841	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
842	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
843	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
844	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
845	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	-	0/0
846	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
847	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
848	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	-	0/0
849	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	-	0/0
850	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
851	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
852	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTR - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
853	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
854	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	-	0/0
855	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
856	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
857	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0
858	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	-	0/0
859	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-	0/0
860	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- -	-	0/0
861	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 -	- -	-	0/0
862	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-	0/0
863	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
864	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 -	- -	-	0/0
865	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-	0/0
866	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-	0/0
867	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-	0/0
868	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-	0/0
869	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 -	- -	-	0/0
870	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	05/2013 -	-	0/0
871	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0
National Highways Development Project						
872	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4 - [N24000310]NHDP,MADHYA PRADESH	02/2015	377.83 -	07/2017 -	-	0/0
873	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 - [N24000371]NHDP,UTTAR PRADESH	10/2013	445.89 -	03/2017 -	-	0/0
874	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150 - [N24000377]NHDP,UTTAR PRADESH	01/2014	397.04 -	10/2016 -	-	0/0
875	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]NHDP,MADHYA PRADESH	06/2015	390.51 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
876	BHOPAL-BIORA (4L) OF NH-12 IN MP - [N24000380]NHDP,MADHYA PRADESH	11/2011	704.26 -	05/2015 -	-	0/0
877	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP - [N24000381]NHDP,MADHYA PRADESH	03/2013	257.80 -	02/2016 -	-	0/0
878	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 - [N24000388]NHDP,MADHYA PRADESH	11/2013	497.05 -	05/2017 -	-	0/0
879	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH - [N24000393]NHDP,UTTAR PRADESH	06/2015	774.57 -	03/2018 -	-	0/0
880	SHAHNOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADHYA PRADESH KM 142/200 TO 245/0 - [N24000394]NHDP,MADHYA PRADESH	06/2015	532.49 -	05/2017 -	-	0/0
881	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP - [N24000395]NHDP,MADHYA PRADESH	08/2015	257.80 -	- -	-	0/0
882	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43 - [N24000399]NHDP,UTTAR PRADESH	10/2013	317.76 -	03/2017 -	-	0/0
883	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93 - [N24000403]NHDP,UTTAR PRADESH	10/2013	283.45 -	10/2016 -	-	0/0
884	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A - [N24000410]NHDP,MADHYA PRADESH	06/2015	641.02 -	12/2017 -	-	0/0
885	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]NHDP,MADHYA PRADESH	01/2012	381.86 -	04/2015 -	-	0/0
886	SONOLI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0 - [N24000418]NHDP,UTTAR PRADESH	10/2013	493.94 -	03/2017 -	-	0/0
887	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP - [N24000447]NHDP,MADHYA PRADESH	11/2011	670.82 -	02/2015 -	-	0/0
888	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A - [N24000474]NHDP,MADHYA PRADESH	02/2015	327.32 -	05/2017 -	-	0/0
889	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]NHDP,MADHYA PRADESH	11/2015	628.45 -	03/2018 -	-	0/0
890	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]NHDP,MADHYA PRADESH	12/2015	927.54 -	06/2018 -	-	0/0
Public Works Dept Of State						
891	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 - [N24000895]PWD,MADHYA PRADESH	09/2016	287.34 -	01/2019 -	01/2019	0/0
892	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86 - [N24000856]PWD,MADHYA PRADESH	03/2014	170.00 -	02/2015 -	02/2015	0/0
893	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	03/2017 -	04/2019	0/0
894	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 & NH-10 O - [N24000871]PWD,WEST BENGAL	08/2014	600.87 720.97	11/2017 -	11/2017	0/0
895	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	03/2019 -	05/2019	0/0
896	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	10/2013 -	06/2019	0/0
897	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	11/2017 -	07/2019	0/0
898	REHABILITATION AND UPGADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.22	08/2017 -	08/2019	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
899	WIDENING TO 2-LANE+PS WITH RECONSTRUCTION OF BRIDGES & CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]PWD,MADHYA PRADESH	01/2017	373.82 -	09/2019 -	09/2019	0/0
900	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	03/2019 -	09/2019	0/0
901	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]PWD,PUNJAB	10/2017	1,069.59 -	10/2019 -	10/2019	0/0
902	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD, WEST BENGAL	03/2016	271.17 291.20	11/2018 -	11/2019	0/0
903	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	02/2018 -	11/2019	0/0
904	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]PWD, WEST BENGAL	03/2017	202.69 -	11/2019 -	11/2019	0/0
905	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]PWD,MADHYA PRADESH	03/2018	191.21 -	11/2019 -	11/2019	0/0
906	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	03/2018 -	11/2019	0/0
907	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	02/2018 -	11/2019	0/0
908	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	06/2019 -	11/2019	0/0
909	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	03/2018 -	12/2019	0/0
910	REHABILITATION & UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHANDE - [N24000876]PWD, WEST BENGAL	01/2017	396.86 -	09/2019 -	12/2019	0/0
911	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	07/2018 -	01/2020	0/0
912	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	03/2018 -	04/2020	0/0
913	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	08/2018 -	06/2020	0/0
914	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	08/2018 -	06/2020	0/0
915	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	07/2018 -	06/2020	0/0
916	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]PWD,PUNJAB	03/2018	173.24 -	06/2020 -	06/2020	0/0
917	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	03/2018 -	07/2020	0/0
918	REHABILITATION & UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH-3 - [N24000905]PWD,PUNJAB	03/2018	322.48 -	07/2020 -	07/2020	0/0
919	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]PWD, WEST BENGAL	02/2018	426.18 -	09/2020 -	09/2020	0/0
920	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO) - [N24000883]PWD, WEST BENGAL	03/2018	254.30 -	10/2020 -	10/2020	0/0
921	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	02/2018 -	11/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
922	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]PWD, WEST BENGAL	02/2018	218.70 -	11/2020 -	11/2020	0/0
923	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD, MADHYA PRADESH	03/2018	214.69 -	03/2018 -	11/2020	0/0
924	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0+000 - [N24000910]PWD, PUNJAB	03/2018	170.57 -	11/2020 -	11/2020	0/0
925	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 -	08/2019 -	08/2021	0/0
926	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 -	08/2019 -	08/2021	0/0
927	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]PWD, TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
928	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]PWD, KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
929	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261]PWD, KERALA	01/2014	267.16 352.00	11/2017 -	-	0/0
930	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR - NELLORE SECTION) IN - [N24000265]PWD, ANDHRA PRADESH	11/2014	297.78 330.00	02/2017 -	-	0/0
931	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION. - [N24000278]PWD, CHHATISGARH	10/2014	213.47 -	03/2015 -	-	0/0
932	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHIKONDA) UNDER NHDP-IV - [N24000279]PWD, CHHATISGARH	10/2014	298.34 -	03/2015 -	-	0/0
933	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHIKONDA TO JAGDALPUR) UNDER NHDP-I - [N24000280]PWD, CHHATISGARH	11/2014	262.54 -	03/2015 -	-	0/0
934	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]PWD, CHHATISGARH	12/2015	291.05 -	- -	-	0/0
935	CONSTRUCTION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH- - [N24000283]PWD, CHHATISGARH	12/2010	169.26 -	12/2012 -	-	0/0
936	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION. - [N24000286]PWD, CHHATISGARH	12/2014	394.20 -	- -	-	0/0
937	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION - [N24000287]PWD, CHHATISGARH	11/2015	485.44 -	12/2015 -	-	0/0
938	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE - [N24000289]PWD, PUNJAB	03/2015	435.90 -	- -	-	0/0
939	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6 - [N24000290]PWD, PUNJAB	01/2015	279.68 -	- -	-	0/0
940	4-LANING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO - [N24000291]PWD, PUNJAB	11/2014	463.65 546.00	- -	-	0/0
941	4 LANING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM - [N24000292]PWD, PUNJAB	11/2014	573.96 605.00	- -	-	0/0
942	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]PWD, ANDHRA PRADESH	03/2015	271.45 -	10/2015 -	-	0/0
943	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) - [N24000302]PWD, ANDHRA PRADESH	07/2015	333.21 -	12/2015 -	-	0/0
944	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]PWD, MIZORAM	11/2010	624.41 -	03/2011 -	-	0/0
945	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA - [N24000307]PWD, ARUNACHAL PRADESH	12/2011	156.63 276.00	02/2012 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
946	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]PWD,MIZORAM	08/2010	193.69 -	10/2010 -	-	0/0
947	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P - [N24000309]PWD,ARUNACHAL PRADESH	11/2010	305.49 -	03/2011 -	-	0/0
948	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR - [N24000311]PWD,ARUNACHAL PRADESH	03/2012	207.03 -	05/2012 -	-	0/0
949	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]PWD,SIKKIM	04/2013	151.59 -	08/2013 -	-	0/0
950	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]PWD,SIKKIM	04/2013	166.27 -	08/2013 -	-	0/0
951	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]PWD,SIKKIM	01/2013	182.28 -	02/2013 -	-	0/0
952	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA - [N24000315]PWD,NAGALAND	12/2010	1,296.00 -	02/2011 -	-	0/0
953	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI - [N24000370]PWD,PUNJAB	02/2015	483.38 -	- -	-	0/0
954	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0 - [N24000372]PWD,PUNJAB	02/2015	616.36 -	- -	-	0/0
955	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE - [N24000373]PWD,UTTAR PRADESH	11/2010	305.49 -	03/2017 -	-	0/0
956	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYPASS SEC.OF NH-64(- [N24000374]PWD,PUNJAB	02/2015	486.74 -	- -	-	0/0
957	SATANA-BELA SECTION OF NH-75(4L) IN MP - [N24000375]PWD,MADHYA PRADESH	01/2012	320.48 -	08/2015 -	-	0/0
958	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(- [N24000383]PWD,PUNJAB	03/2015	312.79 -	- -	-	0/0
959	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOLA BYPASS(EXISTING KM.138.030 TO K - [N24000384]PWD,PUNJAB	07/2014	319.80 -	- -	-	0/0
960	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS - [N24000385]PWD,PUNJAB	12/2015	766.36 -	- -	-	0/0
961	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A' - [N24000387]PWD,ARUNACHAL PRADESH	01/2011	264.16 -	- -	-	0/0
962	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 - [N24000389]PWD,PUNJAB	11/2015	847.02 -	- -	-	0/0
963	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA - [N24000390]PWD,MEGHALAYA	12/2010	1,494.48 -	02/2011 -	-	0/0
964	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]PWD,PUNJAB	11/2015	889.24 -	- -	-	0/0
965	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]PWD,ASSAM	11/2010	268.08 -	05/2017 -	-	0/0
966	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR - [N24000396]PWD,ASSAM	11/2010	470.20 -	02/2011 -	-	0/0
967	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP - [N24000401]PWD,MADHYA PRADESH	11/2011	871.15 -	09/2015 -	-	0/0
968	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM - [N24000404]PWD,PUNJAB	12/2015	578.38 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
969	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA - [N24000405]PWD,MULTI STATE	03/2015	789.83 -	- -	-	0/0
970	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C - [N24000407]PWD,ANDHRA PRADESH	10/2015	333.21 -	11/2015 -	-	0/0
971	STRENGTHENING AND CONSTRUCTION OF PAVED SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM - [N24000409]PWD,ASSAM	05/2011	176.22 -	02/2018 -	-	0/0
972	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ - [N24000411]PWD,ASSAM	11/2014	218.31 -	02/2018 -	-	0/0
973	IMPROVEMENT FROM KM 0/0 TO 68/0 - [N24000413]PWD,ODISHA	12/2013	319.80 -	10/2016 -	-	0/0
974	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]PWD,MIZORAM	08/2010	195.04 -	10/2010 -	-	0/0
975	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70 - [N24000416]PWD,ANDHRA PRADESH	02/2015	224.83 -	04/2015 -	-	0/0
976	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH - [N24000417]PWD,ODISHA	07/2014	342.05 -	01/2017 -	-	0/0
977	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA - [N24000419]PWD,ARUNACHAL PRADESH	12/2009	165.00 -	09/2010 -	-	0/0
978	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420]PWD,ARUNACHAL PRADESH	12/2009	104.00 -	09/2010 -	-	0/0
979	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]PWD,MADHYA PRADESH	03/2015	511.83 -	08/2017 -	-	0/0
980	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA - [N24000523]PWD,ODISHA	12/2011	159.39 -	11/2017 -	-	0/0
981	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA - [N24000524]PWD,PUNJAB	06/2015	892.17 -	- -	-	0/0
982	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO - [N24000526]PWD,PUNJAB	06/2015	899.21 -	- -	-	0/0
983	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]PWD,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
984	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 - [N24000530]PWD,BIHAR	01/1991	154.62 -	- -	-	0/0
985	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]PWD,BIHAR	01/1991	319.68 -	- -	-	0/0
986	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO - [N24000538]PWD,MAHARASHTRA	01/2014	292.98 -	11/2014 -	-	0/0
987	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]PWD,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
988	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]PWD,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
989	R & U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]PWD,UTTAR PRADESH	11/2016	326.99 327.00	- -	-	0/0
	<u>SHIPPING AND PORTS</u>					
	<u>Cochin Shipyard Ltd</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
990	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]CSL,KERALA	05/2016	970.00 -	05/2020 -	05/2020	0/0
991	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]CSL,KERALA	07/2016	1,799.00 -	05/2021 -	05/2021	0/0
	<u>Kamarajar Port Limited</u>					
992	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	12/2017 -	05/2020	0/0
	<u>Mumbai Port Trust</u>					
993	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063]MUMBAI PORT TRU,MAHARASHTRA	01/2007	366.39 -	12/2010 -	-	0/0
	<u>Port Trust</u>					
994	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 -	-	0/0
995	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 -	03/2006 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
996	MADHYA PRADESH ACCESS (LOT1) - [N26000110]BSNL,MAHARASHTRA	08/2017	215.30 219.60	05/2018 05/2019	05/2019	0/0
997	MAHARASHTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113]BSNL,MAHARASHTRA	01/2018	231.80 240.10	10/2018 05/2019	05/2019	0/0
	<u>Department Of Telecommunication</u>					
998	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	07/2015 -	05/2020	0/0
	<u>Mahanagar Telephone Nigam Limited</u>					
999	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G) - [N26000105]MTNL,DELHI	06/2016	418.26 -	06/2017 -	-	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Bangalore Metro Rail Corporation Limited</u>					
1000	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	02/2019 -	03/2020	0/0
	<u>Central Public Works Department</u>					
1001	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107]CPWD,DELHI	12/2017	188.00 -	06/2019 -	06/2019	0/0
1002	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	10/2019	0/0
1003	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	11/2019	0/0
1004	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	12/2019	0/0
1005	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 07/2020	03/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1006	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 -	05/2020 -	05/2020	0/0
1007	RESIDENTIAL QUATERS FOR HAL,BANGLORE - [N28000103]CPWD,KARNATAKA	12/2016	246.31 -	02/2020 09/2020	09/2020	0/0
1008	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	06/2017 07/2017	10/2020	0/0
1009	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 250.00	- 12/2020	12/2020	0/0
1010	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 250.00	- 08/2020	03/2021	0/0
1011	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU	11/2017	348.77 -	- -	11/2021	0/0
1012	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN - [N28000079]CPWD,DELHI	07/2012	884.30 -	12/2015 -	-	0/0
1013	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2016	248.20 -	04/2018 -	-	0/0
	<u>Chennai Metro Rail Ltd</u>					
1014	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-	0/0
	<u>Hindustan Steelwork Construction Limited</u>					
1015	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	03/2021	0/0
1016	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	12/2015 -	-	0/0
1017	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	12/2016 -	-	0/0
1018	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	12/2016 -	-	0/0
1019	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]HSCL,KARNATAKA	05/2005	768.88 1,070.97	02/2014 -	-	0/0
1020	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA - [N12000102]HSCL,KARNATAKA	07/2011	324.87 324.87	12/2015 -	-	0/0
1021	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	09/2017 -	-	0/0
1022	CONSTRUCTION OF 123 BLOCKS IN TELEGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA - [N12000104]HSCL,ANDHRA PRADESH	07/2014	232.00 -	- -	-	0/0
1023	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT - [N12000106]HSCL,GUJARAT	01/2013	175.00 -	- -	-	0/0
1024	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS - [N12000107]HSCL,RAJASTHAN	05/2015	189.00 -	03/2017 -	-	0/0
1025	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTENANCE UNDER PMGSY-JHARKHAND - [N12000109]HSCL,JHARKHAND	12/2007	253.92 253.92	06/2016 -	-	0/0
1026	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT - [N12000110]HSCL,JHARKHAND	12/2007	200.00 -	03/2018 -	-	0/0
1027	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII - [N12000111]HSCL,JHARKHAND	02/2014	787.29 -	12/2016 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (April 2019)						
			Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
1028	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY - [N12000112]HSCL,JHARKHAND	04/2013	170.00 -	04/2018 -	-	0/0
1029	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG - [N12000114]HSCL, WEST BENGAL	08/2012	185.37 -	03/2016 -	-	0/0
	<u>Jawahar Lal Nehru National Urban Renewal Mission</u>					
1030	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2 - [N28000082]JNNURM, ANDHRA PRADESH	08/2007	246.90 -	- -	-	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
1031	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 -	12/2019	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
1032	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	03/2019	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
1033	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 -	11/2021 -	11/2021	0/0
1034	DELHI MRTS PHASE-III - [N28000056]MMRC,DELHI	09/2011	38,585.00 -	03/2016 -	-	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
1035	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	01/2015 -	05/2020	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
1036	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 8,680.00	03/2018 12/2019	12/2019	0/0
	<u>National Building Construcion Corporation Ltd</u>					
1037	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00 -	- -	-	0/0
	Total		11,58,364.78 -			0/0
	Grand Total		11,58,364.78			0/0

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>South-Eastern Coal Fields Limited</u>						
1	BATURA OCP (2.0 MTY) - [N06000049]	8/2015	1,186.64 -	203.82	117.55	03/2023 -	03/2021
	Total		1,186.64 -	203.82	117.55		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
2	MUMBAI REFINERY EXPANSION PROJECT - [N16000281]	9/2015	4,199.00	4,199.00	194.97	03/2020 -	07/2019
	<u>Indian Oil Corporation Limited</u>						
3	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 3,338.00	3,338.00	1,393.27	12/2020 -	08/2020
4	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00 -	3,696.00	31.02	09/2022 -	06/2021
5	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL - [N16000252]	5/2016	664.00 -	664.00	528.48	12/2020 -	02/2020
6	JAIPUR-PANIPAT NAPHTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE - [N16000195]	2/2015	890.00 -	887.00	591.29	10/2019 -	06/2019
	Total		11,786.00 -	12,784.00	2,739.03		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
7	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX [N18000158]	2/2014	539.82 575.67	575.67	426.83	06/2016 09/2019	05/2019
8	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	5/2005	1,779.29 2,187.32	2,187.32	2,133.02	11/2008 06/2019	05/2019
9	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN - [N18000227]	7/2016	1,429.38 1,429.38	1,429.38	916.66	01/2019 07/2019	06/2019
10	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	5/2017	445.89 445.89	445.89	258.66	02/2019 12/2019	09/2019
	Total		4,194.38 -	4,638.26	3,735.17		
	<u>RAILWAYS</u>						
	<u>East Central Railways</u>						

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
11	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	348.23	136.13	03/2021 -	12/2020
	<u>North East Frontier Railway</u>						
12	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	4/2015	2,232.32 -	2,182.00	475.48	03/2022 -	03/2020
13	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	612.00	93.63	12/2021 -	03/2020
	<u>North Eastern Railway</u>						
14	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	770.08	277.14	12/2022 -	05/2019
15	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,295.42	183.61	03/2022 -	12/2019
16	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]	4/2016	600.00 -	366.71	5.92	01/2022 -	01/2020
	<u>Rail Vikas Nigam Ltd.</u>						
17	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78 -	723.78	0.22	12/2025 -	03/2025
	<u>Western Railway</u>						
18	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	324.69	03/2021 -	03/2020
	Total		7,034.44 -	7,300.61	1,496.82		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>National Highways Authority Of India</u>						
19	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]	3/2017	247.02 -	157.49	-	03/2020 -	02/2020
20	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]	3/2017	296.19 -	254.00	233.60	03/2020 -	06/2019
21	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL - [N24000664]	3/2017	639.79 -	552.90	476.34	03/2020 -	06/2019
22	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER - [N24000667]	3/2017	648.32	503.10	15.10	03/2020 -	11/2019
23	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669]	3/2017	165.50 -	172.16	45.34	03/2020 -	06/2019
24	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00) [N24000670]	3/2017	239.68 -	235.90	84.03	03/2020 -	06/2019
25	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]	4/2017	894.00	894.00	15.00	04/2020 -	11/2019
	Total		3,130.50 -	2,769.55	869.41		
	<u>URBAN DEVELOPMENT</u>						

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Central Public Works Department</u>						
26	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111	11/2017	171.72 -	171.72	3.50	03/2020 07/2020	03/2020
	Total		171.72 -	171.72	3.50		
	Grand Total		27,503.68	27,867.96	8,961.48		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	185.90	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	307.30	03/2022 -	03/2022
4	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	78.84	03/2024 -	03/2024
5	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
6	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	46.93	03/2022 -	03/2022
7	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
	<u>Mahanadi Coal Fields Limited</u>						
8	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,174.58	03/2026 -	03/2026
9	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	433.20	03/2021 -	03/2021
10	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	79.92	03/2027 -	03/2027
11	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,109.33	03/2029 -	03/2029
	<u>Neyveli Lignite Corporation</u>						
12	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	430.69	06/2015 09/2019	09/2019
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.13	09/2019 -	09/2019
14	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	176.87	12/2019 -	12/2019
15	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	5,982.50	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
16	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	250.33	03/2021 -	03/2021
17	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	329.15	03/2012 03/2023	03/2023
19	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	2.82	03/2015 03/2021	03/2021
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	203.77	03/2012 03/2024	03/2024
21	KISTARAM OCP - [N06000089]	11/2010	242.29 -	164.04	104.08	03/2015 03/2021	03/2021
22	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
23	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	473.22	417.24	03/2015 03/2021	03/2021
	<u>South-Eastern Coal Fields Limited</u>						
24	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022
26	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
27	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
28	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
29	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.35	03/2021 -	03/2021
31	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,900.98	03/2023 -	03/2023
32	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.66	03/2023 -	03/2023
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.94	03/2023 -	03/2023
34	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	65.52	03/2020 -	03/2020
35	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
36	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.54	03/2021 -	03/2021
37	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.40	03/2021 -	03/2021
38	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
39	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	80.25	03/2020 -	03/2020
40	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	24.29	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Western Coal Fields Limited</u>						
41	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	138.73	03/2020 -	03/2020
42	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	112.45	03/2020 -	03/2020
43	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	239.42	03/2025 -	03/2025
44	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	279.61	03/2020 -	03/2020
45	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	98.04	03/2021 -	03/2021
46	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
47	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
48	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.23	03/2022 -	03/2022
49	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	206.72	03/2020 -	03/2020
50	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	333.43	.07	03/2023 03/2024	03/2024
51	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	165.09	03/2021 -	03/2021
52	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	144.38	03/2021 -	03/2021
53	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	409.85	03/2020 -	03/2020
	Total		74,015.48 -	73,716.61	18,904.18		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
54	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	74.55	08/2020 -	08/2020
	Total		285.95 -	285.95	74.55		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	67.89	11/2019 -	11/2019
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	69.08	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	69.23	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
58	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	70.98	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	277.18		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
59	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
60	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
61	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
	Total		2,363.00 -	2,363.00	485.35		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
62	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
63	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
64	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	315.25	01/2020 01/2020	01/2020
65	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
66	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
67	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	166.62	134.98	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		7,078.62 -	7,078.62	579.13		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
68	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	568.96	10/2018 06/2019	06/2019
69	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	142.34	12/2019 -	12/2019
70	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	718.31	02/2020 10/2020	10/2020
71	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	2,868.71	08/2018 11/2019	11/2019
72	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
73	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	-	03/2021 -	03/2021
74	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	12.63	03/2023 -	03/2023
75	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	29.15	12/2020 -	12/2020
76	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	88.28	08/2020 -	08/2020
77	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	260.09	02/2020 -	02/2020
	<u>Chennai Petroleum Corporation Limited</u>						
78	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	757.22	12/2019 -	12/2019
79	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	62.32	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
80	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	860.14	02/2020 -	02/2020
81	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	-	08/2020 -	08/2020
82	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	192.71	12/2021 -	12/2021
83	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	36.75	10/2022 -	10/2022
84	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	39.19	10/2022 -	10/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
85	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	181.20	25.90	07/2022 -	07/2022
86	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	52.16	10/2022 -	10/2022
87	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	45.20	07/2022 -	07/2022
88	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	117.30	04/2022 -	04/2022
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	60.93	12/2020 -	12/2020
90	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,177.26	12/2020 -	12/2020
91	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,168.02	12/2020 -	12/2020
92	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	967.24	12/2020 -	12/2020
93	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,162.20	12/2020 12/2020	12/2020
<u>Hindustan Petroleum Corporation Limited</u>							
94	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	645.53	10/2014 08/2019	08/2019
95	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
96	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
97	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	47.50	11/2020 -	11/2020
98	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	328.48	09/2019 -	09/2019
100	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,308.78	06/2020 -	06/2020
101	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	4,501.16	07/2020 -	07/2020
102	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	358.80	03/2021 -	03/2021
<u>Indian Oil Corporation Limited</u>							
103	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
104	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
105	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	143.56	06/2020 -	06/2020
106	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
107	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	-	09/2019 -	09/2019
108	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	13.67	02/2020 -	02/2020
109	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	9.93	01/2021 -	01/2021
110	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
111	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	12.16	10/2021 -	10/2021
112	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	246.28	10/2019 -	10/2019
113	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	7.01	10/2021 -	10/2021
114	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	16.56	03/2021 -	03/2021
115	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	144.71	08/2020 -	08/2020
116	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	86.47	02/2020 -	02/2020
117	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	235.99	10/2021 -	10/2021
118	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	4.55	01/2021 -	01/2021
119	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	8.18	12/2021 -	12/2021
120	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	27.50	02/2020 10/2020	10/2020
121	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,238.56	07/2019 -	07/2019
122	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	51.40	10/2020 -	10/2020
123	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	.31	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
124	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,252.80	09/2019 -	09/2019
125	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	5.53	02/2020 -	02/2020
126	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	403.95	09/2019 -	09/2019
127	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
128	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,683.93	09/2019 -	09/2019
129	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY [N16000308]	8/2017	315.00 -	315.00	108.80	12/2021 -	12/2021
130	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	323.69	09/2019 -	09/2019
131	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	66.38	04/2021 -	04/2021
132	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	5.79	06/2020 -	06/2020
133	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	96.96	07/2020 -	07/2020
134	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	34.33	12/2019 -	12/2019
135	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY [N16000277]	5/2016	429.00 -	429.00	290.69	01/2019 12/2019	12/2019
136	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	20.36	01/2021 -	01/2021
137	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
138	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	834.52	08/2021 -	08/2021
139	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	236.57	07/2018 10/2020	10/2020
140	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	670.40	12/2020 -	12/2020
141	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,451.96	11/2019 -	11/2019
142	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	2,589.31	09/2017 06/2019	06/2019
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
143	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
144	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
145	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,132.88	03/2013 12/2019	12/2019
146	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	345.40	12/2019 -	12/2019
147	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	2,354.21	05/2021 05/2021	05/2021
148	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	815.29	11/2019 11/2019	11/2019
149	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	358.81	11/2019 11/2019	11/2019
150	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	366.12	11/2019 11/2019	11/2019
151	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	346.77	05/2019 05/2019	05/2019
152	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	105.21	09/2018 04/2019	04/2019
153	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	338.79	03/2026 03/2026	03/2026
154	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	145.01	05/2020 05/2020	05/2020
155	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	2,465.32	06/2020 08/2021	08/2021
156	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	237.35	03/2023 03/2022	03/2022
157	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,167.85	04/2018 05/2020	05/2020
158	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,255.37	12/2017 03/2020	03/2020
159	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,906.55	03/2015 12/2019	12/2019
160	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	129.67	01/2014 11/2019	11/2019
161	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,073.56	03/2019 05/2020	05/2020
162	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,778.58	05/2019 10/2019	10/2019
163	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,731.48	04/2019 12/2019	12/2019
	<u>Oil India Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
164	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	63.20	10/2020 -	10/2020
165	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	2.40	02/2020 -	02/2020
166	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	112.73	12/2019 -	12/2019
	Total		1,86,879.20 -	1,88,398.62	61,460.76		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
167	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	11,086.44	09/2017 03/2020	03/2020
168	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,938.20	03/2013 12/2020	12/2020
169	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	11,850.13	06/2017 03/2020	03/2020
170	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,420.87	11/2019 -	11/2019
171	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	4,370.06	07/2020 02/2021	02/2021
172	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	7,697.03	09/2019 01/2020	01/2020
173	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	15,932.41	01/2011 08/2021	08/2021
174	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	9,101.85	08/2018 02/2020	02/2020
175	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	8,617.47	02/2019 09/2021	09/2021
176	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	429.14	09/2019 02/2022	02/2022
177	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	5,961.47	03/2019 03/2020	03/2020
	<u>North East Electric Power Corporation</u>						
178	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,419.34	7,131.10	12/2009 06/2019	06/2019
	<u>Power Grid Corporation Of India Limited</u>						
179	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	689.46	09/2010 04/2019	04/2019
180	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,733.20	08/2013 03/2022	03/2022
181	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	24.40	06/2019 09/2019	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
182	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	5.00	05/2020 05/2020	05/2020
183	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]	9/2017	198.49 -	198.49	41.70	09/2019 02/2020	02/2020
184	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	810.69	02/2020 02/2020	02/2020
185	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	80.77	07/2019 07/2019	07/2019
186	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	83.54	09/2018 09/2019	09/2019
187	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,051.50	07/2020 -	07/2020
188	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	127.38	02/2019 06/2019	06/2019
189	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	109.10	02/2020 02/2020	02/2020
190	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	221.54	01/2019 09/2019	09/2019
191	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	164.25	11/2019 11/2019	11/2019
192	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	167.81	06/2019 06/2019	06/2019
193	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	530.54	06/2019 06/2019	06/2019
194	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	6,580.05	11/2019 11/2019	11/2019
195	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	270.92	04/2018 01/2020	01/2020
196	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	458.26	01/2018 12/2019	12/2019
197	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	35.50	06/2019 06/2019	06/2019
198	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	1,773.41	04/2020 04/2020	04/2020
199	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	28.42	12/2019 12/2019	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
200	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	84.89	06/2019 06/2019	06/2019
201	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	518.50	06/2014 09/2019	09/2019
202	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	188.36	07/2017 06/2019	06/2019
203	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	496.12	10/2017 09/2019	09/2019
204	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	3,063.80	03/2018 12/2019	12/2019
205	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	546.36	447.83	11/2016 12/2019	12/2019
206	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,230.98	04/2016 08/2019	08/2019
207	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,554.87	10/2012 12/2019	12/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
208	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	207.87	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
209	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	296.17	09/2020 -	09/2020
210	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	-	09/2023 -	09/2023
	Total		1,68,285.15 -	1,90,223.53	1,24,613.00		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
211	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,108.46	03/2023 -	03/2023
212	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	36.16	03/2023 -	03/2023
213	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	59.41	03/2023 -	03/2023
214	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	3,627.47	510.70	03/2024 -	03/2024
215	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	125.72	03/2023 -	03/2023
216	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	231.61	03/2022 -	03/2022
217	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
218	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
219	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
220	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	2,075.20	03/2021 -	03/2021
221	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	195.62	03/2022 -	03/2022
222	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	293.18	03/2021 -	03/2021
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
223	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
224	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
225	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
226	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	582.11	03/2020 -	03/2020
227	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	205.59	03/2022 -	03/2022
228	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	209.89	03/2022 -	03/2022
229	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
230	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	87.60	03/2022 -	03/2022
231	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
232	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	374.20	03/2020 -	03/2020
233	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	322.47	03/2022 -	03/2022
	<u>North Central Railway</u>						
234	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
235	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
236	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
237	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
238	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	4,968.00	2,671.70	03/2014 12/2020	12/2020
239	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
240	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	4/2006	2,326.52 -	3,000.00	734.88	03/2015 10/2021	10/2021
241	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	260.68	03/2021 -	03/2021
242	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	399.61	03/2021 -	03/2021
243	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.59	03/2020 -	03/2020
244	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	67.41	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
245	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						
246	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
247	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,568.77	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
248	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
249	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	363.94	12/2026 -	12/2026
250	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,390.53	03/2023 -	03/2023
251	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	830.71	12/2021 -	12/2021
252	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	210.07	03/2021 -	03/2021
253	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	1,061.88	12/2021 -	12/2021
254	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	960.26	12/2020 -	12/2020
255	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	958.09	970.78	03/2020 -	03/2020
256	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,103.00	1,132.87	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
257	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	441.95	12/2024 -	12/2024
258	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	3/2009	713.48 -	1,750.00	1,773.46	03/2020 -	03/2020
259	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	284.16	12/2024 -	12/2024
260	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	633.52	12/2023 -	12/2023
	<u>South Central Railway</u>						
261	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	139.69	03/2020 03/2020	03/2020
262	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
263	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	632.48	03/2021 -	03/2021
264	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	4/2008	2,132.77 -	2,132.77	214.54	03/2014 03/2023	03/2023
	<u>South East Central Railway</u>						
265	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
266	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
267	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
268	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
269	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
270	KENDRI-DHAMTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
271	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
272	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
	<u>South Eastern Railway</u>						
273	MM FROM BURAMARA-CHAKULIA - [N22000305]	4/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024
274	MM FROM PANSKURA-GHATAL NL - [N22000309]	4/2011	276.69 -	426.00	-	- 03/2030	03/2030
275	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024
276	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	184.33	12/2021 12/2024	12/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
277	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	4/1998	1,027.40 -	2,373.00	484.92	03/2003 03/2030	03/2030
278	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.58	12/2021 12/2021	12/2021
279	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.77	- 03/2025	03/2025
<u>South Western Railway</u>							
280	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	4/2011	1,801.01 -	1,801.01	42.34	- 12/2023	12/2023
281	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	4/1996	1,382.78 -	1,382.78	7.35	03/2002 03/2024	03/2024
282	MARIKUPPAM - KUPPAM - [N22000308]	4/2012	279.54 -	279.54	26.28	03/2016 12/2023	12/2023
283	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	4/2013	327.25 -	367.77	.31	- 12/2023	12/2023
284	GADAG-WADI NL - [N22000299]	4/2013	2,841.84 -	2,841.84	92.75	12/2018 12/2024	12/2024
285	TORANAGALLU-RANJITPURA DL - [N22000298]	4/2011	146.75 -	167.50	.34	- 12/2023	12/2023
286	BAGALKOT-KUDACHI NL - [N22000258]	4/2010	986.30 -	986.30	295.49	03/2016 12/2023	12/2023
287	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	4/2013	558.00 -	692.43	-	- 12/2023	12/2023
288	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	4/2013	296.00 -	466.65	-	- 12/2023	12/2023
289	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,870.41	880.72	03/2019 03/2021	03/2021
290	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	498.04	03/2020 03/2020	03/2020
291	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	677.98	03/2020 03/2020	03/2020
292	MIRAJ-LONDA - [N22000327]	3/2015	1,830.00 -	1,190.92	161.34	- 03/2021	03/2021
293	WHITE FIELD-KOLAR NL - [N22000280]	4/2011	348.85 -	348.85	.36	- 12/2023	12/2023
294	SHIMOGA-HARIHAR NL - [N22000278]	4/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024
<u>Southern Railway</u>							
295	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
296	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
<u>West Central Railway</u>							
297	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
298	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
299	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
	<u>Western Railway</u>						
300	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	1,030.29	1,195.16	03/2022 -	03/2022
301	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	691.84	54.87	03/2020 -	03/2020
302	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	700.00	47.80	06/2020 -	06/2020
303	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	679.79	03/2022 -	03/2022
304	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	645.15	03/2022 -	03/2022
305	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	385.60	629.92	03/2020 -	03/2020
	Total		2,64,386.82 -	3,29,128.43	57,432.45		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
306	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
307	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019
308	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]	6/2017	282.08 -	282.08	45.92	06/2019 -	06/2019
309	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019
310	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	74.52	02/2020 -	02/2020
311	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
312	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019
313	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
314	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019
315	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019
316	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
317	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
318	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
319	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903	3/2019	306.28 -	306.28	-	05/2019 -	05/2019
320	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868	3/2018	253.44 -	253.44	-	07/2019 -	07/2019
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
324	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
325	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
326	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
327	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
328	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	970.58	04/2019 -	04/2019
329	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541	1/2016	1,081.57 -	1,081.57	892.00	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
330	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	274.39	04/2019 -	04/2019
331	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	463.21	07/2019 -	07/2019
332	4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
333	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	44.06	03/2020 -	03/2020
334	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
335	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
336	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	500.79	04/2020 -	04/2020
337	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	1,017.40	09/2019 -	09/2019
338	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	609.09	07/2019 -	07/2019
339	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	512.49	04/2019 -	04/2019
340	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	623.35	04/2019 -	04/2019
341	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
342	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,377.59	03/2020 -	03/2020
343	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
344	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	1,041.10	191.74	04/2019 -	04/2019
345	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]	7/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019
	<u>Public Works Dept Of State</u>						
346	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]	3/2017	202.69 -	202.69	-	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
347	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]	2/2018	426.18 -	426.18	-	09/2020 -	09/2020
348	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]	2/2018	218.70 -	218.70	-	11/2020 -	11/2020
349	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0+000 - [N24000910]	3/2018	170.57 -	170.57	8.14	11/2020 -	11/2020
350	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
351	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
352	REHABILITATION & UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH-3 - [N24000905]	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
353	WIDENING TO 2-LANE+PS WITH RECONSTRUCTION OF BRIDGES & CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]	1/2017	373.82 -	373.82	-	09/2019 -	09/2019
354	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]	3/2018	191.21 -	191.21	-	11/2019 -	11/2019
355	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]	3/2018	254.30 -	254.30	-	10/2020 -	10/2020
	Total		36,216.42 -	36,880.26	10,299.47		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
356	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	297.60	05/2021 -	05/2021
357	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	272.73	05/2020 -	05/2020
	Total		2,769.00 -	2,769.00	570.33		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
358	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	22,542.00	15,401.64	05/2015 10/2019	10/2019
359	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (SAIL)</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
360	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121	12/2018	263.36 -	263.36	-	09/2020 -	09/2020
	Total		16,606.36 -	23,623.36	15,433.24		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
361	MADHYA PRADESH ACCESS (LOT1) - [N26000110	8/2017	215.30 -	219.60	33.46	05/2018 05/2019	05/2019
362	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	1/2018	231.80 -	240.10	117.63	10/2018 05/2019	05/2019
	Total		447.10 -	459.70	151.09		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
363	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	6/2015	197.33 -	197.33	25.15	04/2019 06/2020	06/2020
364	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120	1/2018	430.00 -	430.00	46.28	05/2020 -	05/2020
365	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 -	271.90	17.39	11/2019 -	11/2019
366	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098	10/2016	209.84 -	209.84	27.18	03/2020 -	03/2020
367	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	33.40	05/2020 -	05/2020
368	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107	12/2017	188.00 -	188.00	131.55	06/2019 -	06/2019
369	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
370	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110	10/2016	422.00 -	422.00	-	- 12/2020	12/2020
371	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103	12/2016	246.31 -	246.31	51.14	02/2020 09/2020	09/2020
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
372	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	2,377.05	11/2021 -	11/2021
	<u>Nagpur Metro Rail Corporation Ltd</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
373	NAGPUR METRO RAIL - [N28000085 <u>National Building Construcion Corporation Ltd</u>	8/2014	8,680.00 -	8,680.00	5,632.05	03/2018 12/2019	12/2019
374	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,936.53	11/2019 -	11/2019
	Total		26,718.23 -	26,893.46	12,280.30		
	Grand Total		7,88,706.61	8,84,475.82	3,02,896.06		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>COAL</u>						
	<u>Bharat Coking Coal Limited</u>						
1	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	5.24	03/2021 -	03/2021
	<u>Central Coal Fields Limited</u>						
2	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	185.90	03/2020 -	03/2020
	<u>Eastern Coal Fields Limited</u>						
3	JHANJRA COMBINED PR(3.50 MTY) - [N06000020]	11/2015	602.86 -	602.86	307.30	03/2022 -	03/2022
4	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	78.84	03/2024 -	03/2024
5	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	-	03/2026 -	03/2026
6	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	46.93	03/2022 -	03/2022
7	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	-	03/2029 -	03/2029
	<u>Mahanadi Coal Fields Limited</u>						
8	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	1,174.58	03/2026 -	03/2026
9	GARJANBAHAL OCP - [N06000117]	11/2014	1,375.38 -	1,375.38	433.20	03/2021 -	03/2021
10	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	79.92	03/2027 -	03/2027
11	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,109.33	03/2029 -	03/2029
	<u>Neyveli Lignite Corporation</u>						
12	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	430.69	06/2015 09/2019	09/2019
13	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]	3/2015	522.45 -	522.45	9.13	09/2019 -	09/2019
14	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]	3/2015	513.63 -	513.63	176.87	12/2019 -	12/2019
15	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	5,982.50	11/2021 -	11/2021
	<u>Northern Coal Fields Limited</u>						
16	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]	5/2017	1,783.09 -	1,783.09	250.33	03/2021 -	03/2021
17	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]	11/2017	1,255.17 -	1,255.17	94.84	03/2022 -	03/2022
	<u>Singareni Colliers Company Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	329.15	03/2012 03/2023	03/2023
19	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	2.82	03/2015 03/2021	03/2021
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	448.86	203.77	03/2012 03/2024	03/2024
21	KISTARAM OCP - [N06000089]	11/2010	242.29 -	164.04	104.08	03/2015 03/2021	03/2021
22	KALYANIKHANI 6 INCLINE PROJECT - [N06000147]	12/2015	477.65 -	477.65	2.11	03/2020 -	03/2020
23	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	473.22	417.24	03/2015 03/2021	03/2021
	<u>South-Eastern Coal Fields Limited</u>						
24	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	6.21	03/2023 -	03/2023
25	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	88.29	03/2022 -	03/2022
26	MADANNAGAR OPENCAST PROJECT - [N06000140]	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2024
27	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
28	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	9.53	03/2026 -	03/2026
29	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	75.96	03/2026 -	03/2026
30	AMADAND OPENCAST EXPANSION PROJECT - [N06000148]	3/2016	869.44 -	869.44	112.35	03/2021 -	03/2021
31	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	2,900.98	03/2023 -	03/2023
32	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,057.66	03/2023 -	03/2023
33	DURGAPUR OPENCAST PROJECT - [N06000136]	2/2015	916.24 -	916.24	3.94	03/2023 -	03/2023
34	AMGAON OPENCAST PROJECT RCE - [N06000135]	7/2015	316.10 -	316.10	65.52	03/2020 -	03/2020
35	BATURA HIGHWALL PROJECT - [N06000134]	7/2015	231.92 -	231.92	-	03/2022 -	03/2022
36	KANCHAN OC EXPANSION - [N06000125]	12/2014	371.04 -	371.04	47.54	03/2021 -	03/2021
37	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	115.40	03/2021 -	03/2021
38	AMRITDHARA OC PROJECT - [N06000122]	2/2015	481.60 -	481.60	-	03/2023 -	03/2023
39	BIJARI OC RCE (1.50 MTY) - [N06000111]	5/2014	164.49 -	164.49	80.25	03/2020 -	03/2020
40	MALACHUA OPENCAST PROJECT - [N06000139]	10/2015	488.33 -	488.33	24.29	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Western Coal Fields Limited</u>						
41	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE - [N06000142]	11/2015	498.42 -	498.42	138.73	03/2020 -	03/2020
42	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	112.45	03/2020 -	03/2020
43	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	727.28	239.42	03/2025 -	03/2025
44	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	362.73	279.61	03/2020 -	03/2020
45	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]	2/2017	328.00 -	328.00	98.04	03/2021 -	03/2021
46	DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	458.07 -	458.07	20.86	03/2022 -	03/2022
47	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	319.76	58.04	03/2022 -	03/2022
48	COAL PROJECT NAME JAMUNIA UG (0.84 MTY) - [N06000153]	7/2016	409.87 -	409.87	18.23	03/2022 -	03/2022
49	PENGANGA OCP(REVISED) - [N06000066]	9/2014	441.82 -	441.82	206.72	03/2020 -	03/2020
50	ADASA UG TO OC - [N06000133]	8/2015	288.90 -	333.43	.07	03/2023 03/2024	03/2024
51	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	6/2015	483.69 -	483.69	165.09	03/2021 -	03/2021
52	MAKARDHOKRA I OC - [N06000119]	9/2014	266.23 -	266.23	144.38	03/2021 -	03/2021
53	DINESH OCP - [N06000118]	11/2014	611.16 -	611.16	409.85	03/2020 -	03/2020
	Total		74,015.48 -	73,716.61	18,904.18		
	<u>DEFENCE PRODUCTION</u>						
	<u>Goa Shipyard Limited</u>						
54	CONSTRUCTION WORKS PHASE 3B - [N39000002]	12/2016	285.95 286.00	285.95	74.55	08/2020 -	08/2020
	Total		285.95 -	285.95	74.55		
	<u>FERTILISERS</u>						
	<u>National Fertiliser Limited</u>						
55	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]	1/2018	215.92 -	215.92	67.89	11/2019 -	11/2019
56	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]	1/2018	239.81 -	239.81	69.08	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]	1/2018	218.83 -	218.83	69.23	11/2019 -	11/2019
	<u>Rashtriya Chemical & Fertiliser Limited</u>						
58	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	70.98	04/2020 -	04/2020
	Total		1,101.28 -	1,101.28	277.18		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>HII Infra Tech Services Limited</u>						
59	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]	7/2016	785.00 -	785.00	39.35	04/2020 -	04/2020
60	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	875.00	174.00	05/2021 -	05/2021
61	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]	7/2016	703.00 -	703.00	272.00	06/2020 -	06/2020
	Total		2,363.00 -	2,363.00	485.35		
	<u>HEAVY INDUSTRY</u>						
	<u>Bharat Heavy Electricals Limited</u>						
62	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]	8/2016	1,554.00 -	1,554.00	335.03	09/2019 -	09/2019
	Total		1,554.00 -	1,554.00	335.03		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						
63	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	96.98	04/2021 04/2021	04/2021
64	UTKAL D AND E COAL BLOCK - [N10000011]	5/2016	534.00 -	534.00	315.25	01/2020 01/2020	01/2020
65	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	-	04/2021 04/2021	04/2021
66	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]	12/2015	355.00 -	355.00	31.92	11/2020 -	11/2020
67	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]	9/2017	166.62 -	166.62	134.98	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		7,078.62 -	7,078.62	579.13		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
68	HALDIA LPG IMPORT FACILITY - [N16000223]	3/2015	694.00 -	694.00	568.96	10/2018 06/2019	06/2019
69	MMPL PIPELINE REROUTING PROJECT - [N16000261]	4/2013	449.58 -	449.58	142.34	12/2019 -	12/2019
70	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY - [N16000263]	2/2016	3,313.00 -	3,288.96	718.31	02/2020 10/2020	10/2020
71	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	2,868.71	08/2018 11/2019	11/2019
72	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,112.00	108.79	06/2019 -	06/2019
73	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]	10/2018	206.26 -	206.26	-	03/2021 -	03/2021
74	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	12.63	03/2023 -	03/2023
75	2G ETHANOL BIO REFINERY AT BARGARH - [N16000341]	8/2017	750.00 -	750.00	29.15	12/2020 -	12/2020
76	PUNE POL STORAGE DEPOT - [N16000313]	8/2016	282.64 -	282.64	88.28	08/2020 -	08/2020
77	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY - [N16000260]	2/2016	554.00 -	554.00	260.09	02/2020 -	02/2020
	<u>Chennai Petroleum Corporation Limited</u>						
78	BS-VI PROJECTS - [N16000295]	9/2017	1,858.00 -	1,858.00	757.22	12/2019 -	12/2019
79	RE-LIQUIFIED NATURAL GAS - [N16000301]	8/2017	421.00 -	421.00	62.32	08/2020 -	08/2020
	<u>Gas Authority Of India Limited</u>						
80	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210]	2/2015	749.00 -	842.00	860.14	02/2020 -	02/2020
81	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	8/2018	286.42 -	286.42	-	08/2020 -	08/2020
82	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,308.00	192.71	12/2021 -	12/2021
83	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR [N16000330]	10/2017	221.45 -	221.45	36.75	10/2022 -	10/2022
84	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	39.19	10/2022 -	10/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
85	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	181.20	25.90	07/2022 -	07/2022
86	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	52.16	10/2022 -	10/2022
87	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	45.20	07/2022 -	07/2022
88	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	287.49	117.30	04/2022 -	04/2022
89	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	60.93	12/2020 -	12/2020
90	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,437.00	1,177.26	12/2020 -	12/2020
91	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	1,168.02	12/2020 -	12/2020
92	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	967.24	12/2020 -	12/2020
93	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]	7/2015	2,881.40 -	2,000.00	1,162.20	12/2020 12/2020	12/2020
<u>Hindustan Petroleum Corporation Limited</u>							
94	URAN CHAKAN SHIKRAPUR LPG PIPELINE - [N16000155]	12/2009	309.81 -	723.40	645.53	10/2014 08/2019	08/2019
95	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]	6/2017	161.50 -	161.50	17.78	06/2020 -	06/2020
96	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA [N16000315]	6/2017	249.26 -	249.26	58.33	06/2020 -	06/2020
97	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA [N16000312]	11/2017	255.00 -	255.00	47.50	11/2020 -	11/2020
98	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH - [N16000311]	12/2016	300.00 -	300.00	-	04/2021 -	04/2021
99	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT [N16000237]	9/2016	407.00 -	407.00	328.48	09/2019 -	09/2019
100	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION - [N16000238]	9/2016	1,879.00 -	1,879.00	1,308.78	06/2020 -	06/2020
101	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	7/2016	20,928.00 -	20,928.00	4,501.16	07/2020 -	07/2020
102	EXTENSION OF VISAKH-VIJAYAWADA- SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00 -	2,677.00	358.80	03/2021 -	03/2021
<u>Indian Oil Corporation Limited</u>							
103	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]	5/2013	711.00 -	711.00	11.12	06/2020 -	06/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
104	HALDIA BARAUNI PRODUCT PIPELINE - [N16000251]	4/2016	1,021.00 -	1,021.00	4.45	12/2020 -	12/2020
105	MOTIHARI AMLEKHGANJ PIPELINE - [N16000254]	9/2015	324.00 -	324.00	143.56	06/2020 -	06/2020
106	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM [N16000270]	7/2014	247.00 -	247.00	-	03/2021 -	03/2021
107	120 TMTPA LPG BOTTLING PLANT AT GORAKHPUR UP - [N16000354]	3/2014	204.00 -	204.00	-	09/2019 -	09/2019
108	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	13.67	02/2020 -	02/2020
109	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	9.93	01/2021 -	01/2021
110	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]	12/2018	611.00 -	611.00	1.68	04/2022 -	04/2022
111	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP [N16000350]	10/2018	316.20 -	316.20	12.16	10/2021 -	10/2021
112	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY - [N16000348]	6/2017	951.64 -	951.64	246.28	10/2019 -	10/2019
113	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]	10/2018	1,297.50 -	1,297.50	7.01	10/2021 -	10/2021
114	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	16.56	03/2021 -	03/2021
115	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	144.71	08/2020 -	08/2020
116	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]	8/2018	557.00 -	557.00	86.47	02/2020 -	02/2020
117	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	235.99	10/2021 -	10/2021
118	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]	7/2018	189.00 -	189.00	4.55	01/2021 -	01/2021
119	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	8.18	12/2021 -	12/2021
120	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	27.50	02/2020 10/2020	10/2020
121	BS-VI PROJECT AT PANIPAT REFINERY - [N16000325]	12/2017	3,529.00 -	3,529.00	1,238.56	07/2019 -	07/2019
122	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	51.40	10/2020 -	10/2020
123	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	.31	08/2020 -	08/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
124	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY - [N16000322]	5/2018	2,934.40 -	2,934.40	1,252.80	09/2019 -	09/2019
125	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY [N16000321]	4/2018	206.63 -	206.63	5.53	02/2020 -	02/2020
126	BS-VI PROJECT AT BONGAIGAON REFINERY - [N16000320]	5/2018	1,222.00 -	1,222.00	403.95	09/2019 -	09/2019
127	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	-	03/2021 -	03/2021
128	BS-VI PROJECT AT GUJARAT REFINERY - [N16000310]	3/2018	3,380.00 -	3,380.00	1,683.93	09/2019 -	09/2019
129	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY [N16000308]	8/2017	315.00 -	315.00	108.80	12/2021 -	12/2021
130	BS-VI PROJECT AT MATHURA REFINERY - [N16000306]	1/2018	666.64 -	666.64	323.69	09/2019 -	09/2019
131	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]	8/2017	384.58 -	384.58	66.38	04/2021 -	04/2021
132	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	5.79	06/2020 -	06/2020
133	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY - [N16000284]	9/2016	208.35 -	208.35	96.96	07/2020 -	07/2020
134	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	34.33	12/2019 -	12/2019
135	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY [N16000277]	5/2016	429.00 -	429.00	290.69	01/2019 12/2019	12/2019
136	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]	5/2016	261.00 -	261.00	20.36	01/2021 -	01/2021
137	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE - [N16000269]	1/2015	342.00 -	342.00	-	03/2021 -	03/2021
138	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	834.52	08/2021 -	08/2021
139	PARADIP LPG IMPORT FACILITY - [N16000196]	1/2015	690.00 -	690.00	236.57	07/2018 10/2020	10/2020
140	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	670.40	12/2020 -	12/2020
141	INDMAX PROJECT AT BONGAIGAON REFINERY - [N16000243]	2/2016	2,582.00 -	2,582.00	1,451.96	11/2019 -	11/2019
142	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	2,589.31	09/2017 06/2019	06/2019
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
143	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255]	5/2015	224.00 207.00	207.25	99.99	04/2019 -	04/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
144	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	581.00	-	03/2020 -	03/2020
	<u>Oil & Natural Gas Corporation Limited</u>						
145	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	3/2009	2,465.15 -	2,378.86	2,132.88	03/2013 12/2019	12/2019
146	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE) - [N16000335]	4/2018	766.37 -	766.37	345.40	12/2019 -	12/2019
147	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]	2/2017	4,006.83 -	4,006.83	2,354.21	05/2021 05/2021	05/2021
148	4TH PHASE DEVELOPMENT OF NBP FIELD - [N16000294]	2/2017	968.61 -	968.61	815.29	11/2019 11/2019	11/2019
149	DEVELOPMENT OF BSE-11 BLOCK - [N16000293]	2/2017	511.30 -	511.30	358.81	11/2019 11/2019	11/2019
150	DEVELOPMENT OF B-147 FIELD - [N16000292]	2/2017	546.15 -	546.15	366.12	11/2019 11/2019	11/2019
151	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY - [N16000290]	1/2017	474.15 -	474.15	346.77	05/2019 05/2019	05/2019
152	FIELD DEVELOPMENT OF NELP BLOCK KG-ONN-2003, NAGAYALANKA-KG - [N16000280]	4/2017	420.76 -	420.76	105.21	09/2018 04/2019	04/2019
153	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]	2/2017	1,162.56 -	1,162.56	338.79	03/2026 03/2026	03/2026
154	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	7/2016	249.85 250.00	244.70	145.01	05/2020 05/2020	05/2020
155	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]	3/2016	34,012.00 -	34,012.00	2,465.32	06/2020 08/2021	08/2021
156	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	658.62 -	910.23	237.35	03/2023 03/2022	03/2022
157	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]	12/2015	3,190.69 -	3,247.19	2,167.85	04/2018 05/2020	05/2020
158	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA - [N16000212]	1/2015	4,619.94 -	4,619.94	4,255.37	12/2017 03/2020	03/2020
159	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	1,906.55	03/2015 12/2019	12/2019
160	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	330.35	129.67	01/2014 11/2019	11/2019
161	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY - [N16000204]	8/2015	2,818.88 -	2,818.88	2,073.56	03/2019 05/2020	05/2020
162	DAMAN DEVELOPMENT PROJECT - [N16000198]	8/2014	6,086.08 -	5,842.31	4,778.58	05/2019 10/2019	10/2019
163	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III - [N16000197]	11/2014	6,068.80 -	5,296.93	4,731.48	04/2019 12/2019	12/2019
	<u>Oil India Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
164	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]	5/2016	406.00 -	406.00	63.20	10/2020 -	10/2020
165	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	1/2018	543.91 -	682.90	2.40	02/2020 -	02/2020
166	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]	9/2016	571.66 -	571.66	112.73	12/2019 -	12/2019
	Total		1,86,879.20 -	1,88,398.62	61,460.76		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
167	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	3/2013	11,638.55 -	12,865.92	11,086.44	09/2017 03/2020	03/2020
168	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	3,938.20	03/2013 12/2020	12/2020
169	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	11,850.13	06/2017 03/2020	03/2020
170	TALAIPALLI COAL MINING PROJECT - [N18000266]	9/2015	3,004.00 -	3,004.00	1,420.87	11/2019 -	11/2019
171	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	1/2016	10,598.98 -	10,598.98	4,370.06	07/2020 02/2021	02/2021
172	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	3/2015	9,870.51 -	11,148.86	7,697.03	09/2019 01/2020	01/2020
173	BARH STPP(3X660MW) NTPC - [180100242]	2/2005	8,692.97 -	15,095.67	15,932.41	01/2011 08/2021	08/2021
174	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	2/2014	12,532.44 -	13,740.53	9,101.85	08/2018 02/2020	02/2020
175	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	2/2014	14,366.58 -	15,164.05	8,617.47	02/2019 09/2021	09/2021
176	RAMMAM-III HEPP (3X40 MW) - [N18000178]	9/2014	1,381.84 -	1,381.84	429.14	09/2019 02/2022	02/2022
177	TANDA TPP STAGE-II (2X660 MW) - [N18000175]	9/2014	9,188.98 -	9,188.98	5,961.47	03/2019 03/2020	03/2020
	<u>North East Electric Power Corporation</u>						
178	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	7,419.34	7,131.10	12/2009 06/2019	06/2019
	<u>Power Grid Corporation Of India Limited</u>						
179	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	738.48	689.46	09/2010 04/2019	04/2019
180	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 -	14,719.10	12,733.20	08/2013 03/2022	03/2022
181	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]	12/2017	193.14 -	193.14	24.40	06/2019 09/2019	09/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
182	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]	11/2017	358.83 -	358.83	5.00	05/2020 05/2020	05/2020
183	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]	9/2017	198.49 -	198.49	41.70	09/2019 02/2020	02/2020
184	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	810.69	02/2020 02/2020	02/2020
185	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	5/2017	186.17 -	186.17	80.77	07/2019 07/2019	07/2019
186	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]	5/2017	175.64 -	175.64	83.54	09/2018 09/2019	09/2019
187	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	3/2017	3,500.00 3,500.00	3,500.00	1,051.50	07/2020 -	07/2020
188	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]	2/2017	322.30 -	322.30	127.38	02/2019 06/2019	06/2019
189	WESTERN REGION STRENGTHENING SCHEME XVIII - [N18000241]	2/2017	195.05 -	195.05	109.10	02/2020 02/2020	02/2020
190	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	408.46	221.54	01/2019 09/2019	09/2019
191	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]	3/2017	283.72 -	283.72	164.25	11/2019 11/2019	11/2019
192	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION - [N18000236]	3/2017	251.60 -	251.60	167.81	06/2019 06/2019	06/2019
193	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS - [N18000222]	4/2016	790.13 -	790.30	530.54	06/2019 06/2019	06/2019
194	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P - [N18000219]	5/2016	14,733.37 -	14,733.37	6,580.05	11/2019 11/2019	11/2019
195	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]	4/2016	454.11 -	454.11	270.92	04/2018 01/2020	01/2020
196	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]	3/2016	808.63 -	808.63	458.26	01/2018 12/2019	12/2019
197	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII - [N18000248]	3/2017	337.75 -	337.75	35.50	06/2019 06/2019	06/2019
198	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]	2/2017	5,070.13 -	5,070.13	1,773.41	04/2020 04/2020	04/2020
199	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	3/2017	379.95 -	379.95	28.42	12/2019 12/2019	12/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
200	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	84.89	06/2019 06/2019	06/2019
201	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	518.50	06/2014 09/2019	09/2019
202	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	1/2015	203.28 -	260.03	188.36	07/2017 06/2019	06/2019
203	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	1/2015	871.62 -	871.62	496.12	10/2017 09/2019	09/2019
204	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	3,063.80	03/2018 12/2019	12/2019
205	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	546.36	447.83	11/2016 12/2019	12/2019
206	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,230.98	04/2016 08/2019	08/2019
207	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,554.87	10/2012 12/2019	12/2019
	<u>Satluj Jal Vidyut Nigam Limited</u>						
208	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	648.33	207.87	12/2021 -	12/2021
	<u>Thdc India Limited</u>						
209	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	296.17	09/2020 -	09/2020
210	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]	3/2019	11,089.42 -	11,089.42	-	09/2023 -	09/2023
	Total		1,68,285.15 -	1,90,223.53	1,24,613.00		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
211	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29 -	3,168.29	1,108.46	03/2023 -	03/2023
212	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]	2/2016	637.95 -	637.95	36.16	03/2023 -	03/2023
213	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00 -	2,081.27	59.41	03/2023 -	03/2023
214	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47 3,627.00	3,627.47	510.70	03/2024 -	03/2024
215	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]	2/2015	2,449.91 -	2,449.91	125.72	03/2023 -	03/2023
216	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	2/2015	1,272.19 -	1,272.19	231.61	03/2022 -	03/2022
217	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	2/2016	2,750.00 -	3,438.51	-	03/2024 -	03/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
218	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024
219	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00 -	9,968.00	-	03/2024 -	03/2024
220	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	3,712.50	2,075.20	03/2021 -	03/2021
221	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]	4/2012	540.02 -	540.02	195.62	03/2022 -	03/2022
222	KALYAN-KASARA 3RD LINE - [N22000233]	4/2011	792.89 -	792.89	293.18	03/2021 -	03/2021
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>						
223	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	03/2020
	<u>East Central Railways</u>						
224	KOSI BRIDGE (NL), ECR - [220100304]	4/2002	499.41 -	516.02	640.78	03/2020 -	03/2020
225	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181]	4/2009	548.00 -	785.87	40.00	03/2020 -	03/2020
	<u>East Coast Railway</u>						
226	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	582.11	03/2020 -	03/2020
227	JAGDALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	205.59	03/2022 -	03/2022
228	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	209.89	03/2022 -	03/2022
229	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]	4/2016	5,200.00 -	5,200.00	-	03/2020 -	03/2020
230	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]	4/2015	2,361.74 -	2,361.74	87.60	03/2022 -	03/2022
231	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	3/2012	155.81 -	238.03	180.78	03/2020 -	03/2020
	<u>Eastern Railways</u>						
232	HANSDIHA-GODDA NL - [N22000236]	4/2011	542.18 -	542.18	374.20	03/2020 -	03/2020
233	PIRPAINTI-JASIDIH - [N22000219]	4/2013	915.98 -	915.96	322.47	03/2022 -	03/2022
	<u>North Central Railway</u>						
234	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	1.92	03/2022 -	03/2022
235	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]	3/2018	4,329.53 -	4,329.53	-	03/2023 -	03/2023
236	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	4/2015	668.70 668.00	668.00	-	03/2020 -	03/2020
237	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	-	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
238	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	4/2008	2,393.47 -	4,968.00	2,671.70	03/2014 12/2020	12/2020
239	DIMAPUR-TIZIT NL - [N22000196]	4/2013	4,274.00 -	4,274.00	-	03/2020 -	03/2020
240	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	4/2006	2,326.52 -	3,000.00	734.88	03/2015 10/2021	10/2021
241	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	4/2010	906.46 -	6,000.00	260.68	03/2021 -	03/2021
242	DIGARU-HOJAI (102 KM) - [N22000389]	4/2015	870.96 -	821.00	399.61	03/2021 -	03/2021
243	MURKONGSELEK-PASIGHAT NL - [N22000208]	4/2011	414.84 -	661.00	121.59	03/2020 -	03/2020
244	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	4/2010	242.22 -	471.00	67.41	03/2020 -	03/2020
	<u>North Eastern Railway</u>						
245	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]	4/2016	1,900.00 -	1,277.06	-	01/2022 -	01/2022
	<u>Northern Railway</u>						
246	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.00	229.95	03/2023 -	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
247	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	2,568.77	12/2023 12/2023	12/2023
	<u>Rail India Technical And Economic Service</u>						
248	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]	3/2015	636.38 -	636.38	169.16	03/2021 -	03/2021
	<u>Rail Vikas Nigam Ltd.</u>						
249	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99 -	7,000.00	363.94	12/2026 -	12/2026
250	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00 -	2,900.00	1,390.53	03/2023 -	03/2023
251	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,082.32	830.71	12/2021 -	12/2021
252	DHASA-JETALSAR (GC) - [N22000141]	4/2012	644.38 -	644.38	210.07	03/2021 -	03/2021
253	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	4/2013	1,548.66 -	1,548.66	1,061.88	12/2021 -	12/2021
254	BINA - KOTA DOUBLING WITH RE - [N22000414]	4/2011	1,485.85 -	1,485.85	960.26	12/2020 -	12/2020
255	RAIPUR - TITLAGARH - DOUBLING - [N22000411]	3/2007	1,402.02 -	958.09	970.78	03/2020 -	03/2020
256	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	1,103.00	1,132.87	03/2020 -	03/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
257	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	1/1991	2,335.67 -	2,335.67	441.95	12/2024 -	12/2024
258	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) [N22000407]	3/2009	713.48 -	1,750.00	1,773.46	03/2020 -	03/2020
259	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	773.94	284.16	12/2024 -	12/2024
260	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.67	633.52	12/2023 -	12/2023
	<u>South Central Railway</u>						
261	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	4/2010	704.31 -	704.31	139.69	03/2020 03/2020	03/2020
262	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	4/2017	119.73 185.00	184.97	-	03/2022 -	03/2022
263	KAZIPET-BALHRSHA - [N22000367]	4/2015	2,063.03 -	2,063.03	632.48	03/2021 -	03/2021
264	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	4/2008	2,132.77 -	2,132.77	214.54	03/2014 03/2023	03/2023
	<u>South East Central Railway</u>						
265	GONDIA-JABALPUR(GC),(SECR) - [220100186]	2/1997	511.86 -	1,756.00	967.96	04/2020 -	04/2020
266	GEVRA ROAD PENDRA ROAD - [N22000488]	2/2014	2,288.00 -	4,919.00	67.00	03/2022 -	03/2022
267	ANUPPUR-KATNI - [N22000485]	4/2015	1,370.00 -	1,370.00	101.00	12/2021 -	12/2021
268	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	1,973.00	78.00	03/2021 -	03/2021
269	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]	4/2008	872.00 -	1,279.00	-	12/2019 -	12/2019
270	KENDRI-DHARTARI INCLUDING ABHANPUR-RAJIM - [N22000482]	4/2011	1,471.93 -	543.00	-	03/2022 -	03/2022
271	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	403.00	36.28	12/2021 -	12/2021
272	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	2,686.63	-	03/2023 -	03/2023
	<u>South Eastern Railway</u>						
273	MM FROM BURAMARA-CHAKULIA - [N22000305]	4/2008	466.48 -	1,000.00	.83	- 12/2024	12/2024
274	MM FROM PANSKURA-GHATAL NL - [N22000309]	4/2011	276.69 -	426.00	-	- 03/2030	03/2030
275	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	4/2010	651.00 -	1,009.00	7.96	03/2015 03/2024	03/2024
276	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398]	4/1995	524.43 -	939.00	184.33	12/2021 12/2024	12/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
277	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]	4/1998	1,027.40 -	2,373.00	484.92	03/2003 03/2030	03/2030
278	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397]	1/1991	1,013.45 -	1,428.00	484.58	12/2021 12/2021	12/2021
279	BOWAICHANDI-ARAMBAGH - [N22000159]	4/2010	267.37 -	620.00	40.77	- 03/2025	03/2025
	<u>South Western Railway</u>						
280	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	4/2011	1,801.01 -	1,801.01	42.34	- 12/2023	12/2023
281	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	4/1996	1,382.78 -	1,382.78	7.35	03/2002 03/2024	03/2024
282	MARIKUPPAM - KUPPAM - [N22000308]	4/2012	279.54 -	279.54	26.28	03/2016 12/2023	12/2023
283	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	4/2013	327.25 -	367.77	.31	- 12/2023	12/2023
284	GADAG-WADI NL - [N22000299]	4/2013	2,841.84 -	2,841.84	92.75	12/2018 12/2024	12/2024
285	TORANAGALLU-RANJITPURA DL - [N22000298]	4/2011	146.75 -	167.50	.34	- 12/2023	12/2023
286	BAGALKOT-KUDACHI NL - [N22000258]	4/2010	986.30 -	986.30	295.49	03/2016 12/2023	12/2023
287	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	4/2013	558.00 -	692.43	-	- 12/2023	12/2023
288	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	4/2013	296.00 -	466.65	-	- 12/2023	12/2023
289	HOTGI-KUDGI-GADAG - [N22000333]	3/2015	1,614.59 -	1,870.41	880.72	03/2019 03/2021	03/2021
290	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	578.00	498.04	03/2020 03/2020	03/2020
291	YELAHANKA-PENUKONDA - [N22000328]	5/2015	860.43 -	860.43	677.98	03/2020 03/2020	03/2020
292	MIRAJ-LONDA - [N22000327]	3/2015	1,830.00 -	1,190.92	161.34	- 03/2021	03/2021
293	WHITE FIELD-KOLAR NL - [N22000280]	4/2011	348.85 -	348.85	.36	- 12/2023	12/2023
294	SHIMOGA-HARIHAR NL - [N22000278]	4/2011	832.47 -	832.47	.94	03/2016 03/2024	03/2024
	<u>Southern Railway</u>						
295	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]	2/2015	1,700.00 -	1,700.00	-	03/2022 -	03/2022
296	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	2/2015	760.00 -	1,182.31	-	03/2020 -	03/2020
	<u>West Central Railway</u>						
297	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,713.09	898.83	03/2021 -	03/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
298	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	8/2016	582.13 -	1,260.61	-	03/2022 -	03/2022
299	KATNI-BINA 3RD LINE (263 KM) - [N22000415]	6/2016	2,478.23 -	2,478.23	112.07	03/2022 -	03/2022
	<u>Western Railway</u>						
300	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	1,030.29	1,195.16	03/2022 -	03/2022
301	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	4/2017	691.84 -	691.84	54.87	03/2020 -	03/2020
302	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	700.00	47.80	06/2020 -	06/2020
303	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,347.26	679.79	03/2022 -	03/2022
304	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,640.04	645.15	03/2022 -	03/2022
305	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	385.60	629.92	03/2020 -	03/2020
	Total		2,64,386.82 -	3,29,128.43	57,432.45		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways</u>						
306	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]	12/2017	257.34 -	257.34	-	12/2019 -	12/2019
307	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]	12/2017	200.34 -	200.34	35.76	12/2019 -	12/2019
308	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]	6/2017	282.08 -	282.08	45.92	06/2019 -	06/2019
309	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51 -	284.00	86.43	11/2019 -	11/2019
310	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]	2/2018	418.88 -	418.88	74.52	02/2020 -	02/2020
311	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]	11/2017	257.34 -	238.00	41.09	11/2019 -	11/2019
312	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	29.43	11/2019 -	11/2019
313	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]	5/2018	248.00 -	248.00	-	05/2020 -	05/2020

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
314	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778	11/2017	266.52 -	266.52	78.85	11/2019 -	11/2019
315	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776	11/2017	232.81 -	232.81	40.04	11/2019 -	11/2019
316	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	57.01	12/2019 -	12/2019
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
317	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857	4/2017	519.09 -	519.09	-	09/2019 -	09/2019
318	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862	4/2017	537.82 -	537.82	-	09/2019 -	09/2019
319	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903	3/2019	306.28 -	306.28	-	05/2019 -	05/2019
320	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868	3/2018	253.44 -	253.44	-	07/2019 -	07/2019
321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	-	09/2019 -	09/2019
322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864	4/2017	404.29 -	404.29	-	09/2019 -	09/2019
323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863	4/2017	518.53 -	518.53	-	09/2019 -	09/2019
324	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861	4/2017	473.18 -	473.18	-	09/2019 -	09/2019
325	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858	4/2017	640.07 -	640.07	-	09/2019 -	09/2019
326	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859	4/2017	642.96 -	642.96	-	09/2019 -	09/2019
	<u>National Highways Authority Of India</u>						
327	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - [N24000425	7/2015	2,288.18 -	2,288.18	-	05/2019 -	05/2019
328	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449	7/2015	2,128.72 -	2,128.72	970.58	04/2019 -	04/2019
329	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541	1/2016	1,081.57 -	1,081.57	892.00	06/2019 -	06/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
330	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]	3/2016	1,587.49 -	1,587.49	274.39	04/2019 -	04/2019
331	NAGPUR RING ROAD PACKAGE-1 - [N24000558]	3/2016	546.00 -	546.00	463.21	07/2019 -	07/2019
332	4-LANNING OF BODHRE-DHULE SECTION (KM 390.000 TO 452.800) - [N24000656]	3/2017	744.64 -	982.00	-	03/2020 -	03/2020
333	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]	3/2017	848.45 -	848.45	44.06	03/2020 -	03/2020
334	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 - [N24000625]	9/2016	1,004.67 -	1,004.67	-	05/2019 -	05/2019
335	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]	9/2016	2,510.04 -	2,510.04	-	08/2019 -	08/2019
336	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]	8/2016	1,664.20 -	1,664.20	500.79	04/2020 -	04/2020
337	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199 (DESIGN CHAINAGE) - [N24000600]	8/2016	1,388.34 -	1,388.34	1,017.40	09/2019 -	09/2019
338	NAGPUR RING ROAD PACKAGE-2 - [N24000560]	3/2016	591.66 -	591.66	609.09	07/2019 -	07/2019
339	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]	3/2016	899.00 -	899.00	512.49	04/2019 -	04/2019
340	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]	3/2016	676.73 -	676.73	623.35	04/2019 -	04/2019
341	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	3/2018	1,532.62 -	1,532.62	-	03/2021 -	03/2021
342	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	3/2017	2,064.99 -	2,447.00	1,377.59	03/2020 -	03/2020
343	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]	3/2017	672.89 -	736.01	-	03/2020 -	03/2020
344	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]	12/2015	1,041.10 -	1,041.10	191.74	04/2019 -	04/2019
345	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]	7/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	05/2019
<u>Public Works Dept Of State</u>							
346	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 - [N24000879]	3/2017	202.69 -	202.69	-	11/2019 -	11/2019

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
347	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]	2/2018	426.18 -	426.18	-	09/2020 -	09/2020
348	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]	2/2018	218.70 -	218.70	-	11/2020 -	11/2020
349	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0+000 - [N24000910]	3/2018	170.57 -	170.57	8.14	11/2020 -	11/2020
350	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]	10/2017	1,069.59 -	1,069.59	629.87	10/2019 -	10/2019
351	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF - [N24000906]	3/2018	173.24 -	173.24	10.97	06/2020 -	06/2020
352	REHABILITATION & UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH-3 - [N24000905]	3/2018	322.48 -	322.48	48.73	07/2020 -	07/2020
353	WIDENING TO 2-LANE+PS WITH RECONSTRUCTION OF BRIDGES & CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]	1/2017	373.82 -	373.82	-	09/2019 -	09/2019
354	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP - [N24000884]	3/2018	191.21 -	191.21	-	11/2019 -	11/2019
355	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]	3/2018	254.30 -	254.30	-	10/2020 -	10/2020
	Total		36,216.42 -	36,880.26	10,299.47		
	<u>SHIPPING AND PORTS</u>						
	<u>Cochin Shipyard Ltd</u>						
356	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA - [N25000073]	7/2016	1,799.00 -	1,799.00	297.60	05/2021 -	05/2021
357	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES - [N25000074]	5/2016	970.00 -	970.00	272.73	05/2020 -	05/2020
	Total		2,769.00 -	2,769.00	570.33		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
358	NMDC INTEGRATED STEEL PLANT - [N12000086]	1/2010	15,525.00 -	22,542.00	15,401.64	05/2015 10/2019	10/2019
359	2 MTPA PELLET PLANT AT NAGARNAR - [N12000115]	11/2015	818.00 -	818.00	31.60	06/2020 -	06/2020
	<u>Steel Authority Of India Limited (SAIL)</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
360	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121	12/2018	263.36 -	263.36	-	09/2020 -	09/2020
	Total		16,606.36 -	23,623.36	15,433.24		
	<u>TELECOMMUNICATIONS</u>						
	<u>Bharat Sanchar Nigam Limited</u>						
361	MADHYA PRADESH ACCESS (LOT1) - [N26000110	8/2017	215.30 -	219.60	33.46	05/2018 05/2019	05/2019
362	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT - [N26000113	1/2018	231.80 -	240.10	117.63	10/2018 05/2019	05/2019
	Total		447.10 -	459.70	151.09		
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
363	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	6/2015	197.33 -	197.33	25.15	04/2019 06/2020	06/2020
364	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120	1/2018	430.00 -	430.00	46.28	05/2020 -	05/2020
365	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118	10/2017	271.90 -	271.90	17.39	11/2019 -	11/2019
366	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098	10/2016	209.84 -	209.84	27.18	03/2020 -	03/2020
367	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106	11/2017	238.56 -	238.56	33.40	05/2020 -	05/2020
368	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU - [N28000107	12/2017	188.00 -	188.00	131.55	06/2019 -	06/2019
369	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112	9/2017	150.29 -	150.29	2.58	03/2020 -	03/2020
370	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110	10/2016	422.00 -	422.00	-	- 12/2020	12/2020
371	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103	12/2016	246.31 -	246.31	51.14	02/2020 09/2020	09/2020
	<u>Maharashtra Metro Rail Corporation Ltd.</u>						
372	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121	12/2016	11,420.00 -	11,420.00	2,377.05	11/2021 -	11/2021
	<u>Nagpur Metro Rail Corporation Ltd</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(April 2019)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
373	NAGPUR METRO RAIL - [N28000085 <u>National Building Construcion Corporation Ltd</u>	8/2014	8,680.00 -	8,680.00	5,632.05	03/2018 12/2019	12/2019
374	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,439.23	3,936.53	11/2019 -	11/2019
	Total		26,718.23 -	26,893.46	12,280.30		
	Grand Total		7,88,706.61	8,84,475.82	3,02,896.06		

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Annexure - XIII

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	6,840.00	09/2010 -	10/2021	95.88
	Total		3,492.00 -	6,840.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073	10/2013	314.61 -	441.33	09/2018 -	06/2020	40.28
	Total		314.61 -	441.33			
	<u>COAL</u>						
	<u>Neyveli Lignite Corporation</u>						
3	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	07/2016	17,237.00 -	17,237.80	11/2021 -	11/2021	.00
	<u>South-Eastern Coal Fields Limited</u>						
4	JAGANNATHPOR OCP(3.00MTY) - [N06000075	09/2008	152.43 -	459.49	03/2015 -	03/2020	201.44
	Total		17,389.43 -	17,697.29			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
5	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	513.89	11/2013 -	10/2020	24.10
6	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011	09/2014	505.58 -	523.00	03/2018 -	-	3.45
7	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019	12/2017	156.56 -	156.65	- -	02/2020	.06
	Total		1,076.25 -	1,193.54			
	<u>HEAVY INDUSTRY</u>						
	<u>Natrip Implementation Society</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
8	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP) - [N20000001	04/2011	1,718.00 -	3,827.30	09/2011 -	-	122.78
	Total		1,718.00 -	3,827.30			
	<u>PETROLEUM</u>						
	<u>Gas Authority Of India Limited</u>						
9	GAIL GAS LTD BENGALURU CGD PROJECT - [N16000210	02/2015	749.00 -	842.00	02/2020 -	02/2020	12.42
10	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	3,049.47	12/2012 -	02/2022	4.61
	<u>Hindustan Petroleum Corporation Limited</u>						
11	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II - [N16000209	11/2011	310.00 -	370.00	03/2013 -	-	19.35
	<u>Indian Strategic Petroleum Reserves Ltd</u>						
12	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	-	70.49
	<u>Mangalore Refinery And Petrochemicals Limited</u>						
13	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU - [N16000255	05/2015	224.00 207.00	207.25	04/2019 -	-	.12
	<u>Oil & Natural Gas Corporation Limited</u>						
14	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,247.19	04/2018 -	05/2020	1.77
	<u>Oil India Limited</u>						
15	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	07/2011	352.56 -	438.84	03/2017 -	12/2019	24.47
16	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	-	37.72
17	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331	01/2018	543.91 -	682.90	02/2020 -	02/2020	25.55
	Total		10,149.51 -	11,730.65			
	<u>POWER</u>						
	<u>National Hydro-Electric Power Corporation</u>						
18	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	09/2002	3,919.59 -	9,394.80	09/2009 -	12/2021	139.69

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
19	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,496.34	09/2010 -	-	210.19
	<u>National Thermal Power Corporation</u>						
20	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]	03/2013	11,638.55 -	12,865.92	09/2017 -	03/2020	10.55
21	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	12/2020	29.14
22	DARLIPALLI STPP STAGE-I (2X800 MW) - [N18000176]	02/2014	12,532.44 -	13,740.53	08/2018 -	02/2020	9.64
23	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,164.05	02/2019 -	09/2021	5.55
24	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	7,998.00	05/2014 -	05/2019	49.41
25	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	13,731.26	01/2018 -	05/2020	5.91
26	KUDGI STPP STAGE 1 - [N18000131]	01/2012	15,166.19 -	16,934.65	01/2017 -	-	11.66
27	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]	12/2012	11,846.00 -	12,739.82	06/2017 -	03/2020	7.55
28	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	08/2017 -	-	17.95
29	KHARGONE STPP STAGE I (1320 MW) - [N18000205]	03/2015	9,870.51 -	11,148.86	09/2019 -	01/2020	12.95
30	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						
31	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]	03/2017	379.95 -	379.95	12/2019 -	12/2019	.00
32	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,072.36	12/2018 -	12/2019	90.82
33	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,880.36	12/2018 -	12/2020	34.61
	<u>Satluj Jal Vidyut Nigam Limited</u>						
34	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]	05/2015	436.68 -	602.44	12/2016 -	05/2019	37.96
	<u>Thdc India Limited</u>						
35	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	4,105.30	06/2013 -	12/2022	64.77
36	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	5,024.35	02/2016 -	06/2022	203.22
	Total		1,27,517.19 -	1,69,478.36			

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
37	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	298.70	03/2019 -	03/2019	62.28
38	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	3,712.50	03/2021 -	03/2021	63.44
39	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	663.01 175.30	858.96	06/1999 -	-	389.99
40	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28
41	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	03/2024	25.04
	<u>Container Corporation Of India</u>						
42	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	12/2020	.21
	<u>East Central Railways</u>						
43	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,020.94	- -	03/2021	192.42
44	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.77	- -	03/2023	290.95
45	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	749.00	03/2012 -	03/2020	163.78
46	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	04/1997	324.73 -	1,156.41	03/2012 -	03/2020	256.11
47	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	162.87 -	589.15	- -	03/2022	261.73
48	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	499.41 -	516.02	03/2020 -	03/2020	3.33
49	NAWADA-LAXMIPUR (NL) - [N22000167]	04/2008	620.57 -	2,626.98	- -	-	323.32
50	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	926.09	- -	-	338.91
51	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]	04/2008	678.62 -	2,393.23	- -	-	252.66
52	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]	04/2004	372.14 -	1,474.47	- -	03/2021	296.21
53	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	785.87	03/2020 -	03/2020	43.41
54	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	367.17	- -	-	72.37
55	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	559.91	07/2014 -	-	68.57
56	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2022	63.37

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
57	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2022	62.06
58	PATNA Ganga BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]	11/2001	624.47 -	3,550.00	02/2016 -	03/2021	468.48
59	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	04/1998	180.82 -	528.26	- -	-	192.15
60	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	566.41	- -	12/2021	71.96
	<u>East Coast Railway</u>						
61	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	810.78 -	1,928.07	06/2021 -	03/2023	137.80
62	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	2,923.13 -	3,798.80	03/2009 -	06/2021	29.96
63	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	03/2021	38.43
64	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	03/2020 -	03/2020	.07
65	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	03/2020 -	03/2020	52.77
66	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]	04/2008	445.25 -	2,860.55	- -	-	542.46
67	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26
68	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	-	818.15
69	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	325.00 -	729.92	- -	03/2021	124.59
70	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	2,614.36	- -	03/2022	590.61
71	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2021	15.45
	<u>Eastern Railways</u>						
72	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,620.01	03/2019 12/2009	03/2022	36.26
73	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	635.03	02/2013 -	-	4.60
74	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.59	02/2012 -	09/2016	105.61
75	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	-	44.46
76	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]	04/2003	337.96 -	355.44	- -	-	5.17

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
77	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	665.75	02/2012 -	12/2013	33.16
78	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244	04/2009	257.42 -	258.73	03/2014 -	-	.51
79	MONIGRAM- NIMTITA - [N22000301	04/2012	250.93 -	259.23	- -	-	3.31
80	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	- -	-	6.48
81	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	1,125.89 -	1,988.38	03/2016 -	03/2020	76.61
82	GHUTIASHARIF-CANNING (ER) - [N22000117	04/2009	193.08 -	612.45	12/2011 -	09/2012	217.20
83	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	544.72	03/2006 -	01/2006	33.84
84	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218	04/2010	172.03 -	260.10	- -	-	51.19
85	PIRPAINTI-BHAGALPUR - [N22000222	04/2011	261.38 -	332.14	- -	-	27.07
86	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227	04/2010	174.56 -	175.99	- -	-	.82
<u>Metropolitan Rapid Transport Projects</u>							
87	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37
88	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,973.73	03/2004 -	03/2020	500.22
89	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	06/2013 -	-	48.06
90	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,986.04	03/2014 -	-	50.68
<u>North Central Railway</u>							
91	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	634.48	03/1994 -	-	131.09
92	ETAWAH-MAINPURI (NL),NCR - [220100318	04/1997	120.00 -	245.39	12/2008 -	-	104.49
93	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	-	300.67
94	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	03/2022 -	03/2022	32.02
<u>North East Frontier Railway</u>							
95	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135	04/1983	297.32 -	614.00	03/2019 -	03/2020	106.51

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
96	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	792.46 -	1,320.00	12/2010 -	-	66.57
97	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	4,968.00	03/2014 -	12/2020	107.56
98	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	3,300.00	12/2008 -	03/2019	179.62
99	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	13,809.00	03/2011 -	03/2020	210.02
100	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,532.00	03/2019 -	03/2020	297.72
101	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2020	302.54
102	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	3,000.00	03/2015 -	10/2021	28.95
103	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	03/2020	7.86
104	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	4,084.69	12/2015 -	03/2020	204.95
105	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	03/2020	71.62
106	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]	04/1999	895.00 -	1,733.20	03/2007 -	04/2016	93.65
107	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	650.00	03/2020 -	10/2022	14.11
108	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	6,000.00	03/2021 -	03/2021	561.92
109	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	03/2020	94.45
110	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	394.28	- -	-	63.25
111	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	661.00	03/2020 -	03/2020	59.34
112	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	- -	-	128.39
113	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	551.00	03/2019 -	03/2019	75.48
114	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 -	612.00	12/2021 -	03/2020	1.62
<u>North Eastern Railway</u>							
115	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	413.56	06/2018 -	-	89.54

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
116	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	- -	-	60.34
117	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	230.03 -	770.08	12/2022 -	-	234.77
118	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	744.71 -	1,126.79	- -	-	51.31
119	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	- -	-	8.10
120	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99
121	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	12/2021 -	-	267.13
122	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]	03/2008	195.64 -	435.00	- -	-	122.35
123	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	199.75 -	378.26	08/2018 -	-	89.37
124	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	477.31	01/2019 -	01/2020	61.80
125	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	- -	-	.16
126	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW - [N22000455]	04/1997	233.00 -	318.42	04/1999 -	-	36.66
127	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	02/2020	.16
128	MANDHANA - BRAHMAWART NEW LINE PROJECT. - [N22000458]	04/1997	609.04 1,063.00	1,807.88	04/1999 -	03/2019	70.07
129	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,345.00	01/2018 -	-	.15
130	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	-	18.56
<u>North Western Railway</u>							
131	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	795.01	02/2019 -	12/2021	93.87
132	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	685.99	03/2020 -	04/2022	14.33
133	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	1,103.04	- -	-	26.25
134	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	04/2008	829.74 -	1,216.00	03/2015 -	10/2020	46.55
135	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	348.55	12/2019 -	06/2020	41.64
136	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,261.71	- -	-	104.62
137	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	294.90	10/2018 -	09/2019	24.47

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
138	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]	04/2013	822.00 -	1,099.54	-	-	33.76
139	PUSHKAR-MERTA - [N22000151]	04/2013	323.00 -	432.22	-	-	33.81
140	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	420.18	03/2020 -	06/2020	.00
141	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	244.02	11/2019 -	05/2020	14.35
142	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	349.00	02/2019 -	12/2019	44.16
	<u>Northern Railway</u>						
143	JIND-SONEPAT (NL),NR - [220100280]	01/2004	238.56 -	740.00	03/2012 -	-	210.19
144	GRADE SEPARATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	197.17	- -	-	25.87
145	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	625.00	12/2011 -	-	117.77
146	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68
147	CHANDIGARH-BADDI NL - [N22000296]	04/2007	328.14 -	1,540.00	- -	-	369.31
148	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,100.00	07/2012 -	-	366.67
149	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	11/2002 -	03/2021	1,017.96
150	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	876.10	06/2007 -	-	114.33
151	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	369.90 -	1,581.53	03/2010 -	-	327.56
152	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.00	03/2023 -	03/2023	369.31
153	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	845.58	03/2016 -	-	35.29
	<u>Rail Vikas Nigam Ltd.</u>						
154	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	03/2020	55.57
155	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	1,202.70	02/2015 -	12/2021	.00
156	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	385.00	03/2009 03/2009	03/2019	85.99
157	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	732.81 -	1,993.00	03/2008 -	03/2020	171.97
158	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	7,000.00	12/2026 -	12/2026	135.93

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
159	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	2,900.00	03/2023 -	03/2023	36.34
160	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	631.78 -	1,195.00	12/2012 -	03/2022	89.15
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
162	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
163	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,082.32	12/2021 -	12/2021	10.94
164	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	816.55	03/2016 -	12/2020	29.06
165	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.67	12/2023 -	12/2023	9.32
166	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,077.00	03/2019 -	03/2020	16.18
167	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	1,750.00	03/2020 -	03/2020	145.28
168	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	1,103.00	03/2020 -	03/2020	16.35
169	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,120.00	03/2019 -	03/2021	18.78
	<u>Railway Electrification</u>						
170	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
171	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2023	102.85
172	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	- -	-	161.86
173	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	2,200.00	03/2023 -	03/2024	18.47
174	BHADRACHALAM-KOVVUR - [N22000264]	04/2012	923.23 -	1,787.00	- -	-	93.56
175	CUMBUM-PRODDATUR - [N22000282]	04/2013	829.00 -	1,599.39	- -	-	92.93
176	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84
177	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	645.00	03/2000 -	03/2019	64,400.00
178	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	458.25 -	458.26	- -	-	.00
	<u>South East Central Railway</u>						

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
179	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,101.16	-	-	186.92
180	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	1,756.00	04/2020 -	04/2020	243.06
181	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	2,686.63	03/2023 -	03/2023	40.77
182	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	04/2010	585.93 -	1,420.39	02/2019 -	-	142.42
183	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	403.00	12/2021 -	12/2021	75.98
184	CHHINDWARA-MANDLA FORT GC - [N22000481	03/2011	556.54 -	1,342.46	03/2012 -	03/2020	141.22
185	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,279.00	12/2019 -	12/2019	46.67
186	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,919.00	03/2022 -	03/2022	114.99
	<u>South Eastern Railway</u>						
187	MM FROM BURAMARA-CHAKULIA - [N22000305	04/2008	466.48 -	1,000.00	- -	12/2024	114.37
188	MM FROM PANSKURA-GHATAL NL - [N22000309	04/2011	276.69 -	426.00	- -	03/2030	53.96
189	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	564.94
190	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	749.69	06/2005 -	-	155.02
191	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	09/2019	153.41
192	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	- -	03/2025	131.89
193	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	03/2015 -	03/2024	54.99
194	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161	04/2011	289.64 -	760.00	- -	-	162.39
195	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44
196	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164	04/2010	309.44 -	525.81	12/2015 -	02/2019	69.92
197	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	365.00	- -	01/2020	41.36
198	ARA-BHABHUA ROAD (NL) - [N22000166	04/2008	633.87 -	2,396.88	- -	-	278.13
199	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,151.81	03/2020 -	06/2020	18.76
200	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI - [N22000397	01/1991	1,013.45 -	1,428.00	12/2021 -	12/2021	40.90

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
201	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO - [N22000398	04/1995	524.43 -	939.00	12/2021 -	12/2024	79.05
202	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
203	SRINIVASA-PURA-MADANAPALLI NL - [N22000277	04/2013	296.00 -	466.65	- -	12/2023	57.65
	<u>Southern Railway</u>						
204	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	-	141.40
205	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	920.00	- -	-	491.45
206	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,122.00	- -	-	300.71
207	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,072.50	02/2019 -	-	185.98
208	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080	09/2006	343.17 -	1,065.00	- -	-	210.34
209	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084	09/2006	227.40 -	900.00	- -	-	295.78
210	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	2,300.00	- -	-	294.63
211	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	- -	-	79.80
212	ATTIPPATTU PUTTUR - [N22000184	04/2008	151.84 -	1,105.00	02/2019 -	-	627.74
213	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52 -	2,350.00	- -	-	348.88
214	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
215	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
216	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188	04/1998	271.24 -	520.00	- -	-	91.71
217	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	457.08	- -	-	69.20
218	ERODE-PALANI - [N22000199	04/2008	288.57 -	1,140.00	- -	-	295.05
219	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	03/2020	173.71
220	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	369.83	- -	-	92.90

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
221	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70	1,800.00	03/2019	-	1,391.30
222	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26	231.67	04/2014	03/2020	23.72
223	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87	302.02	03/2005	-	12.33
224	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION - [N22000446]	02/2005	600.00	645.54	03/2010	-	7.59
225	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING - [N22000450]	02/2003	199.55	330.32	03/2009	-	65.53
226	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00	1,182.31	03/2020	03/2020	55.57
	<u>West Central Railway</u>						
227	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60	2,713.09	03/2021	03/2021	538.98
228	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66	6,093.31	05/2008	03/2023	2,360.35
229	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13	1,260.61	03/2022	03/2022	116.55
	<u>Western Railway</u>						
230	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36	203.00	03/2011	-	3.07
231	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24	321.62	03/2012	03/2019	1.06
232	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66	858.96	03/2019	03/2022	167.87
	Total		1,40,356.34	3,10,082.41			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Dept Of Road Transport & Highways</u>						
233	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUDEM TO A) - [N24000262]	12/2014	201.12	201.12	02/2015	-	.06
	<u>Ministry Of Road Transport And Highways</u>						
234	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97	268.92	08/2015	-	3.84
235	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]	11/2017	283.51	284.00	11/2019	11/2019	.17

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
236	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06
237	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	11/2019	.08
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
238	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
239	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	05/2019	92.75
240	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	-	80.68
241	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	05/2019	4.99
242	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	331.23	07/2009 -	-	68.99
243	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	06/2019	106.50
244	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	12/2019	10.58
245	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	06/2019	21.90
246	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	2,945.00	04/2015 -	-	52.73
247	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494	05/2013	1,055.00 -	1,601.77	11/2015 -	12/2018	51.83
248	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW - [N24000609	09/2015	771.18 -	7,558.00	- -	-	880.06
249	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	08/2020	10.58
250	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	03/2020	31.88
251	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	05/2020	3.40
252	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	08/2020	5.56
253	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	11/2020	1.06
254	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	08/2020	5.70
255	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	04/2020	.23

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
256	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	03/2020	9.38
257	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	05/2020	13.97
258	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00) - [N24000669	03/2017	165.50 -	172.16	03/2020 -	06/2019	4.02
259	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	03/2021	10.24
260	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	03/2020 -	03/2020	18.50
261	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	07/2020	41.54
262	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	06/2020	44.39
	<u>Public Works Dept Of State</u>						
263	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR - [N24000247	10/2014	295.47 -	313.27	02/2017 -	-	6.02
264	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWES - [N24000249	03/2011	218.31 -	339.82	12/2015 -	-	55.66
265	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	.12
266	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50 - [N24000261	01/2014	267.16 352.00	352.05	11/2017 -	-	.01
267	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF - [N24000420	12/2009	104.00 -	201.00	09/2010 -	-	93.27
	Total		23,936.94 -	36,748.19			
	<u>SHIPPING AND PORTS</u>						
	<u>Kamarajar Port Limited</u>						
268	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - [N25000066	02/2015	244.50 258.00	275.98	12/2017 -	-	6.97
	<u>Mumbai Port Trust</u>						
269	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - [N25000063	01/2007	366.39 -	669.46	12/2010 -	-	82.72

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above					(April 2019)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Port Trust</u>						
270	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	-	300.00
	Total		760.89 -	1,545.44			
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
271	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	22,542.00	05/2015 -	10/2019	45.20
	<u>Rastriya Ispat Nigam Limited</u>						
272	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]	12/2009	343.00 -	488.40	10/2016 -	03/2020	42.39
	Total		15,868.00 -	23,030.40			
	<u>TELECOMMUNICATIONS</u>						
	<u>Department Of Telecommunication</u>						
273	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	07/2015 -	05/2020	84.97
	Total		13,334.00 -	24,664.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Central Public Works Department</u>						
274	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	1,592.00	10/2019 -	03/2020	30.58
275	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	10/2020	.60
276	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	- -	12/2020	.00
277	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]	10/2016	392.00 -	392.00	- -	03/2021	.00
278	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.49	07/2019 -	12/2019	1.85
	<u>Chennai Metro Rail Ltd</u>						
279	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	19,058.00	12/2015 -	-	30.53
	<u>Hindustan Steelwork Construction Limited</u>						
280	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA - [N12000101]	05/2005	768.88 1,070.97	1,113.34	02/2014 -	-	3.96

List of ongoing projects having cost overrun w.r.t. to Revised schedule

Costing Rs. 150 Crore and above (April 2019)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
281	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	175.94	12/2015 -	-	1.70
	<u>Kochi Metro Rail Corporation Ltd</u>						
282	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	5,687.79	07/2017 -	12/2019	9.77
	<u>National Building Construcion Corporation Ltd</u>						
283	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,439.23	11/2019 -	11/2019	4.11
	Total		28,043.10 -	33,938.78			
	Grand Total		3,83,956.26	6,41,217.69			

List of Delayed Projects w.r.t. Latest Schedule

Annexure-XIV

Costing Rs. 150 Crore and above						(April 2019)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 -	6,840.00	5,771.17	09/2010 -	10/2021	133	-
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 16,580.00	16,580.00	13,469.00	12/2015 11/2016	06/2020	54	43
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	12,320.00	10,749.00	12/2016 03/2017	12/2020	48	45
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	13,910.00	11/2020 -	11/2023	36	-
	Total		67,120.00 -	75,589.00	43,899.17				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	314.61 -	441.33	85.79	09/2018 -	06/2020	21	-
	Total		314.61 -	441.33	85.79				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
6	MOONIDIH XV SEAM UG - [N06000098]BCCL, JHARKHAND	08/2011	1,230.27 -	1,230.27	344.32	04/2015 -	04/2019	48	-
	<u>Central Coal Fields Limited</u>								
7	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL, JHARKHAND	08/2007	163.51 -	163.51	104.04	03/2011 -	03/2021	120	-
8	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	179.16	03/2012 -	03/2021	108	-
9	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL, JHARKHAND	12/2009	510.85 -	510.85	366.52	03/2016 -	03/2021	60	-
10	KARMA OCP (1.0 MTY) - [N06000088]CCL, JHARKHAND	06/2009	162.46 -	162.46	89.30	03/2014 -	03/2021	84	-
11	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, JHARKHAND	08/2008	706.40 -	706.40	185.62	07/2012 -	03/2022	116	-
	<u>Eastern Coal Fields Limited</u>								
12	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N060000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	434.55	03/2018 -	03/2020	24	-
	<u>Mahanadi Coal Fields Limited</u>								
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, ODISHA	01/2005	302.96 -	302.96	302.96	03/2010 -	03/2020	120	-
14	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL, ODISHA	12/2007	490.10 -	490.10	467.50	03/2017 -	03/2020	36	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	KULDA EXPN OC. (5.00 MTY) - [N06000115]MCL, ODISHA	06/2014	289.03 -	289.03	29.93	03/2018 -	03/2020	24	-
16	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL, ODISHA	08/2008	207.28 -	207.28	249.61	03/2012 -	03/2021	108	-
17	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	479.53	404.31	03/2013 -	03/2021	96	-
18	JAGANNATH RE-ORGANISATION OC.(6.00 MTY) - [N06000114]MCL, ODISHA	05/2014	337.66 -	337.66	70.05	03/2019 -	03/2021	24	-
19	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL, ODISHA	12/2007	457.77 -	457.77	619.13	03/2013 -	03/2022	108	-
20	BALRAM OCP EXTENSION, MCL 8.00 MTY - [N06000044]MCL, ODISHA	12/2007	172.08 -	172.08	345.12	03/2010 -	03/2022	144	-
21	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	194.57	03/2019 -	03/2024	60	-
	<u>Neyveli Lignite Corporation</u>								
22	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC, TAMIL NADU	06/2011	5,907.11 7,080.41	7,080.41	6,300.55	12/2015 06/2019	09/2019	45	3
	<u>Singareni Colliers Company Limited</u>								
23	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL, TELANGANA	07/2012	417.33 384.32	384.32	75.36	07/2016 -	03/2020	44	-
24	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 415.37	415.37	175.42	03/2016 03/2019	03/2020	48	12
25	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL, TELANGANA	05/2015	397.09 442.42	442.42	68.57	03/2019 03/2019	03/2020	12	12
26	KOYAGUDEM OPENCAST PROJECT - [N06000146]SCCL, TELANGANA	10/2015	426.79 -	426.79	.72	03/2018 -	03/2020	24	-
27	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL, TELANGANA	03/2017	413.84 -	413.84	50.72	03/2019 -	03/2022	36	-
	<u>South-Eastern Coal Fields Limited</u>								
28	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL, CHHATISGARH	09/2008	152.43 -	459.49	203.55	03/2015 -	03/2020	60	-
29	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, CHHATISGARH	07/2008	178.44 -	178.44	5.16	03/2014 -	03/2020	72	-
30	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, CHHATISGARH	12/2009	321.50 -	321.50	207.31	03/2014 -	03/2021	84	-
	<u>Western Coal Fields Limited</u>								
31	BHANEGAON OC - [N06000121]WCL, MAHARASHTRA	02/2015	187.94 409.68	409.68	101.05	03/2023 02/2017	03/2023	0	73
32	KAMPTEE DEEP OC MINE - [N06000141]WCL, MAHARASHTRA	11/2015	277.65 313.34	313.34	37.51	03/2021 09/2018	03/2024	36	66
	Total		16,419.35 -	18,154.38	11,612.61				
	<u>FERTILISERS</u>								
	<u>Rashtriya Chemical & Fertiliser Limited</u>								
33	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY - [N08000009]RCF, MAHARASHTRA	10/2014	197.79 209.44	209.44	161.24	11/2016 04/2019	05/2019	30	1
	Total		197.79 -	209.44	161.24				

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>STEEL</u>								
	<u>Rastriya Ispat Nigam Limited</u>								
34	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85 -	1,682.85	1,094.53	09/2018 -	06/2019	9	-
35	CENTRAL DISPATCH YARD - [N12000119]RINL,ANDHRA PRADESH	08/2015	320.66 -	320.66	190.91	08/2018 -	06/2019	10	-
36	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II) - [N12000120]RINL,ANDHRA PRADESH	07/2015	465.85 -	465.85	382.25	07/2018 -	06/2019	11	-
37	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00 -	2,500.00	1,207.76	12/2017 -	09/2019	21	-
38	REVAMPING OF SINTER MACHINES - 1 AND 2 - [N12000091]RINL,ANDHRA PRADESH	12/2009	343.00 -	488.40	249.30	10/2016 -	03/2020	41	-
	<u>Steel Authority Of India Limited (Sail)</u>								
39	INSTALLATION OF NEW HOT STRIP MILL AT RSP - [N12000094]SAIL,ODISHA	04/2015	3,127.30 -	3,127.30	2,749.95	04/2018 -	05/2019	13	-
40	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT - [N12000096]SAIL,JHARKHAND	05/2015	1,154.18 -	1,154.18	910.60	12/2017 -	06/2019	18	-
41	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	423.33	10/2017 -	06/2020	32	-
42	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	84.26	06/2019 -	06/2020	12	-
	Total		11,248.72 -	11,036.12	7,292.89				
	<u>PETROLEUM</u>								
	<u>Gas Authority Of India Limited</u>								
43	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	03/2015	3,957.00 3,561.00	3,397.00	2,543.54	12/2018 -	05/2019	5	-
44	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 -	225.54	-	01/2018 -	02/2021	37	-
45	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 3,030.00	3,049.47	2,112.19	12/2012 02/2019	02/2022	110	36
	<u>Indian Oil Corporation Limited</u>								
46	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY - [N16000248]IOCL,BIHAR	07/2015	822.66 -	822.66	822.02	11/2018 -	06/2019	7	-
47	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	423.00	256.37	08/2019 -	09/2019	1	-
48	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]IOCL,MADHYA PRADESH	08/2017	236.00 -	236.00	16.55	06/2020 -	08/2020	2	-
49	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	32.67	02/2020 -	10/2020	8	-

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
50	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	428.96	12/2018 -	02/2021	26	-
51	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 -	163.02	39.00	04/2020 -	03/2021	11	-
52	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00 -	212.00	20.65	01/2021 -	04/2021	3	-
53	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	5.39	04/2021 -	07/2021	3	-
54	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	4.04	10/2020 -	08/2021	10	-
55	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 -	348.00	14.73	01/2021 -	10/2021	9	-
56	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	30.32	08/2021 -	11/2021	3	-
57	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	8.03	04/2022 -	02/2023	10	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
58	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE - [N16000256]MANGALORE REFIN,KARNATAKA	10/2015	135.00 171.00	170.70	132.43	03/2019 -	05/2019	2	-
59	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	176.25	12/2019 -	02/2020	2	-
	<u>Oil & Natural Gas Corporation Limited</u>								
60	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,577.15	1,577.15	1,240.37	05/2013 03/2019	12/2019	79	9
61	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	390.52 390.52	390.52	221.40	03/2019 -	05/2020	14	-
	<u>Oil India Limited</u>								
62	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN - [N16000299]OIL,ASSAM	07/2011	350.00 -	350.00	2.06	01/2019 -	09/2019	8	-
63	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	07/2011	352.56 -	438.84	220.73	03/2017 -	12/2019	33	-
	Total		19,465.42 -	21,405.23	8,327.70				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
64	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	1,086.32	04/2020 -	12/2023	44	-
	<u>National Hydro-Electric Power Corporation</u>								
65	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	9,394.80	7,244.66	09/2009 -	12/2021	147	-
	<u>National Thermal Power Corporation</u>								
66	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 -	7,998.00	7,128.72	05/2014 -	05/2019	60	-
67	MUNPL-MEJA TPP - JV (2X660 MW) - [N18000193]NTPC,UTTAR PRADESH	04/2012	9,750.89 -	9,750.89	8,893.00	12/2016 -	08/2019	32	-
68	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 -	13,731.26	12,695.00	01/2018 -	05/2020	28	-
	<u>Power Grid Corporation Of India Limited</u>								
69	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 225.28	225.28	152.32	02/2016 04/2019	05/2019	39	1
70	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP - [N18000180]PGCIL,MULTI STATE	01/2015	268.80 340.88	340.88	248.10	03/2018 03/2019	05/2019	14	2
71	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	74.71	03/2018 03/2018	05/2019	14	14
72	SOUTHERN REGION STRENGTHENING SCHEME-XXI - [N18000233]PGCIL,MULTI STATE	09/2016	562.25 562.25	562.25	195.50	03/2019 03/2019	05/2019	2	2
73	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 608.24	608.24	388.00	04/2019 04/2019	05/2019	1	1
74	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 374.63	374.63	187.24	04/2016 12/2017	06/2019	38	18
75	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA - [N18000223]PGCIL,ODISHA	04/2016	844.64 844.64	844.64	341.30	04/2019 04/2019	06/2019	2	2
76	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	3,654.00	3,130.07	04/2019 -	06/2019	2	-
77	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 3,519.59	3,519.59	2,215.60	05/2019 05/2019	09/2019	4	4
78	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 1,394.52	1,394.52	338.19	05/2017 06/2019	12/2019	31	6
79	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 4,754.42	9,072.36	1,083.08	12/2018 12/2018	12/2019	12	12
80	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 5,111.33	6,880.36	1,143.65	12/2018 12/2018	12/2020	24	24
	<u>SatluJ Jal Vidyut Nigam Limited</u>								

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
81	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT) - [N18000235]SJVN,GUJARAT	11/2016	330.00 -	330.00	330.23	11/2017 -	04/2019	17	-
82	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT - [N18000194]SJVN,BIHAR	05/2015	436.68 533.50	602.44	557.22	12/2016 -	05/2019	29	-
	<u>Thdc India Limited</u>								
83	DHUKWAN SMALL HYDRO PROJECT - [N18000189]THDCIL,UTTAR PRADESH	05/2011	195.42 294.60	294.60	257.04	02/2014 02/2018	10/2019	68	20
84	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 2,978.86	5,024.35	2,809.51	02/2016 05/2021	06/2022	76	13
85	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 -	4,105.30	1,608.70	06/2013 -	12/2022	114	-
	Total		66,697.28 -	87,017.91	52,108.16				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
86	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	152.95	95.16	02/2018 -	06/2019	16	-
87	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	204.44	176.22	05/2017 -	07/2019	26	-
88	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	363.99	145.51	05/2018 -	09/2019	16	-
89	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	513.89	147.00	11/2013 -	10/2020	83	-
	Total		1,135.49 -	1,235.27	563.89				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
90	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]JCR,MAHARASHTRA	02/2016	1,035.16 1,035.16	1,035.16	51.24	03/2022 -	03/2023	12	-
	<u>Container Corporation Of India</u>								
91	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	305.00	259.28	03/2019 -	12/2019	9	-
92	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00 -	343.00	310.09	03/2019 -	12/2019	9	-
93	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	174.00	148.20	03/2019 -	02/2020	11	-
94	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	493.17	435.76	03/2018 -	03/2020	24	-
95	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	300.00	286.56	03/2019 -	03/2020	12	-
96	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50 -	235.00	5.59	03/2019 -	12/2020	21	-
	<u>East Central Railways</u>								
97	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH	08/2015	528.57 -	528.57	47.38	03/2019 -	12/2019	9	-
98	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]JECR,BIHAR	04/1997	324.73 -	1,156.41	876.49	03/2012 -	03/2020	96	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
99	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 283.95	749.00	495.40	03/2012 -	03/2020	96	-
100	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54 -	678.54	-	03/2019 -	03/2020	12	-
101	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	397.88	03/2020 -	03/2021	12	-
102	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM - [N22000474]ECR,BIHAR	11/2001	624.47 -	3,550.00	97.63	02/2016 -	03/2021	61	-
103	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20 -	1,200.20	-	03/2020 -	10/2021	19	-
104	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	-	03/2020 -	10/2021	19	-
105	SAGAU VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	1.81	03/2021 -	03/2022	12	-
106	MUZAFFARPUR SAGAU DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	-	03/2021 -	03/2022	12	-
	<u>East Coast Railway</u>								
107	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	765.60	02/2019 -	03/2021	25	-
108	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 -	843.04	81.26	10/2020 -	03/2021	5	-
109	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	88.04	11/2018 -	03/2021	28	-
110	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 -	1,172.92	245.16	12/2018 -	03/2021	27	-
111	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 -	3,798.80	1,123.73	03/2009 -	06/2021	147	-
112	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	1,928.07	574.98	06/2021 -	03/2023	21	-
	<u>Eastern Railways</u>								
113	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	1,125.89 -	1,988.38	2,040.42	03/2016 -	03/2020	48	-
114	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	266.52	137.85	03/2016 -	03/2020	48	-
115	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,620.01	849.73	03/2019 12/2009	03/2022	36	147
	<u>Metropolitan Rapid Transport Projects</u>								
116	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 1,781.98	2,973.73	1,362.86	03/2004 -	03/2020	192	-
	<u>North East Frontier Railway</u>								
117	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 200.34	614.00	274.82	03/2019 -	03/2020	12	-
118	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	13,809.00	9,672.60	03/2011 -	03/2020	108	-
119	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,532.00	581.00	03/2019 -	03/2020	12	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
120	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	932.38	03/2019 -	03/2020	12	-
121	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 -	4,084.69	383.92	12/2015 -	03/2020	51	-
122	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	650.00	-	03/2020 -	10/2022	31	-
	<u>North Eastern Railway</u>								
123	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	477.31	217.90	01/2019 -	01/2020	12	-
124	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	426.74	107.98	04/2017 -	01/2020	33	-
125	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	213.35	2.05	04/2016 -	02/2020	46	-
126	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	1,028.95	1.79	12/2019 -	04/2021	16	-
127	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
128	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00 -	150.00	-	04/2017 -	10/2022	66	-
	<u>North Western Railway</u>								
129	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	294.90	169.51	10/2018 -	09/2019	11	-
130	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	349.00	329.33	02/2019 -	12/2019	10	-
131	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	244.02	240.62	11/2019 -	05/2020	6	-
132	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	348.55	179.50	12/2019 -	06/2020	6	-
133	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18 295.02	420.18	118.27	03/2020 -	06/2020	3	-
134	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	1,216.00	805.25	03/2015 -	10/2020	67	-
135	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 780.98	795.01	493.64	02/2019 -	12/2021	34	-
136	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00 -	685.99	4.78	03/2020 -	04/2022	25	-
137	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85 -	808.85	12.41	08/2022 -	09/2022	1	-
	<u>Northern Railway</u>								
138	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 -	27,949.00	17,336.24	11/2002 -	03/2021	220	-
	<u>Rail Vikas Nigam Ltd.</u>								
139	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	1,844.47	1,603.22	12/2017 -	03/2020	27	-
140	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	732.81 -	1,993.00	2,121.12	03/2008 -	03/2020	144	-
141	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,077.00	1,052.21	03/2019 -	03/2020	12	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
142	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	816.55	666.41	03/2016 03/2017	12/2020	57	45
143	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,120.00	941.20	03/2019 -	03/2021	24	-
144	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,183.25	952.52	12/2020 -	03/2021	3	-
145	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 245.00	1,202.70	801.40	02/2015 -	12/2021	82	-
146	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	631.78 632.00	1,195.00	731.65	12/2012 -	03/2022	111	-
147	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	36,195.04	03/2020 -	03/2022	24	-
148	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	943.60	238.36	03/2022 -	12/2024	33	-
149	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	405.85	03/2023 -	12/2024	21	-
150	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,092.40	03/2016 -	03/2025	108	-
151	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 4,200.00	2,913.50	838.07	03/2016 -	03/2025	108	-
152	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.13	03/2014 -	12/2025	141	-
153	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	16,216.00	1,317.68	12/2024 -	03/2026	15	-
	<u>South Central Railway</u>								
154	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.47	222.40	03/2010 -	03/2022	144	-
155	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,288.70	506.48	03/2021 -	03/2022	12	-
156	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	289.91	03/2009 -	03/2023	168	-
157	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,631.00	305.25	03/2022 -	03/2023	12	-
158	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	2,200.00	278.36	03/2023 -	03/2024	12	-
	<u>South East Central Railway</u>								
159	CHHINDWARA-MANDLA FORT GC - [N22000481]SECR,MADHYA PRADESH	03/2011	556.54 -	1,342.46	396.00	03/2012 -	03/2020	96	-
	<u>South Eastern Railway</u>								
160	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	377.00	166.55	12/2016 08/2018	09/2019	33	13

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
161	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	365.00	224.01	- 12/2018	01/2020	-	13
162	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,151.81	450.25	03/2020 03/2020	06/2020	3	3
163	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 1,724.20	1,724.20	289.76	03/2021 03/2021	12/2021	9	9
	<u>South Western Railway</u>								
164	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.52	889.52	438.16	03/2017 -	03/2020	36	-
165	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 1,140.93	1,140.93	754.97	03/2020 03/2020	03/2021	12	12
	<u>Southern Railway</u>								
166	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	231.67	7.62	04/2014 -	03/2020	71	-
167	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
	<u>West Central Railway</u>								
168	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	1,763.93	-	03/2020 -	10/2021	19	-
169	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	6,093.31	972.82	05/2008 -	03/2023	178	-
	<u>Western Railway</u>								
170	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	858.96	534.00	03/2019 -	03/2022	36	-
	Total		96,201.32 -	1,62,211.37	98,380.73				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways</u>								
171	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 - [N24000298]MORTH,RAJASTHAN	02/2015	383.40 -	383.40	224.68	03/2015 -	06/2019	51	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
172	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	373.07	-	08/2016 -	08/2019	36	-
173	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	396.52	-	08/2016 -	08/2019	36	-
174	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	429.52	-	08/2016 -	08/2019	36	-

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
175	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 - [N24000676]NHAI,ASSAM	12/2016	138.93 155.00	155.00	-	01/2017 -	01/2020	36	-
	<u>National Highways Authority Of India</u>								
176	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	312.79	06/2008 -	04/2019	130	-
177	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	217.61	391.12	04/2010 -	04/2019	108	-
178	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	818.53	06/2018 -	04/2019	10	-
179	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	2,322.02	05/2013 -	04/2019	71	-
180	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	1,948.92	11/2016 -	04/2019	29	-
181	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN	10/2015	597.00 -	597.00	605.33	10/2017 -	04/2019	18	-
182	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 -	593.26	60.83	05/2018 -	04/2019	11	-
183	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	602.95	417.86	06/2016 -	04/2019	34	-
184	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	574.28	436.21	07/2018 -	04/2019	9	-
185	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	505.00	454.85	05/2018 -	04/2019	11	-
186	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR - [N24000604]NHAI,RAJASTHAN	08/2016	320.30 -	320.30	228.17	01/2019 -	04/2019	3	-
187	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	352.71	07/2016 -	04/2019	33	-
188	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	211.69	04/2009 -	05/2019	121	-
189	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	167.98	203.98	05/2008 -	05/2019	132	-
190	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	844.31	01/2014 -	05/2019	64	-
191	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	2,614.84	09/2014 -	05/2019	56	-
192	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	465.22	07/2014 -	05/2019	58	-
193	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50) - [N24000342]NHAI,KARNATAKA	05/2015	709.00 -	709.00	419.34	09/2017 -	05/2019	20	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
194	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	531.13	163.10	05/2018 -	05/2019	12	-
195	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH	01/2016	1,134.97 -	1,134.97	73.29	11/2018 -	05/2019	6	-
196	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 174.34	174.34	270.88	03/2008 -	06/2019	135	-
197	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,965.17	11/2011 -	06/2019	91	-
198	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,289.31	03/2013 -	06/2019	75	-
199	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	884.84	02/2013 -	06/2019	76	-
200	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	3,008.77	05/2014 -	06/2019	61	-
201	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	842.31	07/2013 -	06/2019	71	-
202	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,317.74	08/2013 -	06/2019	70	-
203	PANVEL-INDAPUR - [N24000216]NHAI,MAHARASHTRA	12/2011	942.69 -	942.69	704.56	06/2014 -	06/2019	60	-
204	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	06/2019	64	-
205	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,544.00	1,429.59	09/2016 -	06/2019	33	-
206	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	923.04	695.52	11/2016 -	06/2019	31	-
207	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	596.67	333.94	05/2018 -	06/2019	13	-
208	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - [N24000505]NHAI,MADHYA PRADESH	06/2015	1,583.79 -	1,583.79	1,568.11	01/2019 -	06/2019	5	-
209	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1) - [N24000510]NHAI,CHHATISGARH	12/2015	726.67 -	726.67	323.95	04/2018 -	06/2019	14	-
210	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI,MEGHALAYA	12/2015	479.20 -	479.20	475.02	05/2018 -	06/2019	13	-
211	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH	02/2016	273.20 -	273.20	256.25	02/2019 -	06/2019	4	-
212	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	581.84	77.43	05/2017 -	06/2019	25	-
213	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	478.00	409.17	10/2013 -	07/2019	69	-
214	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,423.96	605.35	11/2018 -	07/2019	8	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
215	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	244.90	189.17	05/2019 -	07/2019	2	-
216	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	1,387.11	956.75	11/2017 -	08/2019	21	-
217	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	563.92	97.07	12/2017 -	08/2019	20	-
218	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	323.72	77.31	08/2018 -	08/2019	12	-
219	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 - [N24000608]NHAI,HARYANA	08/2016	248.97 -	248.97	225.48	05/2019 -	08/2019	3	-
220	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	637.18	571.06	06/2019 -	09/2019	3	-
221	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	649.00	-	06/2019 -	09/2019	3	-
222	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	767.03	228.73	08/2018 -	09/2019	13	-
223	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	400.25	64.89	03/2019 -	09/2019	6	-
224	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	2,136.97	1,124.97	12/2018 -	10/2019	10	-
225	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR	08/2015	399.54 -	399.54	178.16	04/2019 -	10/2019	6	-
226	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	1,388.00	1,040.75	08/2018 -	11/2019	15	-
227	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	763.23	155.23	06/2019 -	11/2019	5	-
228	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	2,016.00	1,820.02	04/2019 -	11/2019	7	-
229	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	446.17	38.95	03/2019 -	11/2019	8	-
230	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40) - [N24000700]NHAI,ANDHRA PRADESH	06/2017	648.33 -	648.33	49.59	06/2017 -	11/2019	29	-
231	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	230.00	308.94	04/2008 -	12/2019	140	-

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
232	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	943.17	08/2012 -	12/2019	88	-
233	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,149.72	03/2014 -	12/2019	69	-
234	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	1,363.43	03/2013 -	12/2019	81	-
235	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 -	1,083.00	225.46	06/2018 -	12/2019	18	-
236	FOUR LANING OF CHANDIGARH - KHARAR - [N24000503]NHAI,PUNJAB	10/2015	447.29 -	447.29	189.15	12/2017 -	12/2019	24	-
237	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI,WEST BENGAL	03/2016	229.37 -	229.37	24.78	11/2018 -	12/2019	13	-
238	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	804.97	341.74	06/2018 -	12/2019	18	-
239	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	605.84	722.46	07/2018 -	12/2019	17	-
240	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	639.97	239.96	10/2017 -	01/2020	27	-
241	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	277.66	08/2018 -	03/2020	19	-
242	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 -	322.09	71.28	04/2018 -	04/2020	24	-
243	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	72.04	03/2020 -	04/2020	1	-
244	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	355.39	07/2018 -	05/2020	22	-
245	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 -	904.16	333.48	02/2020 -	05/2020	3	-
246	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	1,065.51	863.82	03/2020 -	05/2020	2	-
247	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	1,989.00	896.05	03/2020 -	05/2020	2	-
248	SIX LANNING OF RANASTALAM- ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	143.09	03/2020 -	05/2020	2	-
249	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,837.93	08/2013 -	06/2020	82	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
250	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	1,434.00	515.09	03/2020 -	06/2020	3	-
251	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	1,124.11	157.94	09/2017 -	06/2020	33	-
252	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	1,177.00	440.28	03/2020 -	07/2020	4	-
253	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	423.83	12/2009 -	08/2020	128	-
254	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	1,310.00	253.84	03/2020 -	08/2020	5	-
255	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	1,043.28	925.93	03/2020 -	08/2020	5	-
256	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	1,160.64	648.57	03/2020 -	08/2020	5	-
257	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	1,958.88	933.00	06/2020 -	08/2020	2	-
258	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	-	09/2017 -	08/2020	35	-
259	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	-	08/2017 -	09/2020	37	-
260	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	29.48	03/2019 -	11/2020	20	-
261	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	870.00	12.95	03/2019 -	11/2020	20	-
262	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	336.65	03/2020 -	11/2020	8	-
263	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	1,071.00	256.29	03/2017 -	11/2020	44	-
264	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	476.56	-	07/2017 -	11/2020	40	-
265	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	964.17	211.90	10/2017 -	11/2020	37	-
266	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	193.70	03/2019 -	12/2020	21	-
267	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	1,655.01	1,515.16	08/2016 -	12/2020	52	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
268	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	2,168.66	239.74	06/2019 -	12/2020	18	-
269	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 -	950.69	720.79	08/2019 -	12/2020	16	-
270	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	1,420.00	115.12	03/2020 -	03/2021	12	-
271	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	227.77	-	03/2020 -	05/2021	14	-
272	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	136.69	06/2020 -	09/2021	15	-
273	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	-	08/2017 -	02/2022	54	-
	<u>Public Works Dept Of State</u>								
274	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]PWD,MADHYA PRADESH	01/2017	205.05 -	205.05	-	03/2017 -	04/2019	25	-
275	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) - [N24000908]PWD,HARYANA	01/2017	276.01 -	276.01	155.40	03/2019 -	05/2019	2	-
276	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A - [N24000467]PWD,RAJASTHAN	09/2012	511.00 -	511.00	33.73	10/2013 -	06/2019	68	-
277	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O - [N24000873]PWD,WEST BENGAL	08/2014	823.20 937.76	937.76	-	11/2017 -	07/2019	20	-
278	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]PWD,WEST BENGAL	04/2014	279.70 398.22	398.22	-	08/2017 -	08/2019	24	-
279	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]PWD,HARYANA	01/2017	247.25 -	247.25	139.32	03/2019 -	09/2019	6	-
280	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]PWD,WEST BENGAL	03/2016	271.17 291.20	291.20	-	11/2018 -	11/2019	12	-
281	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID - [N24000878]PWD,MADHYA PRADESH	11/2017	235.91 -	235.91	-	02/2018 -	11/2019	21	-
282	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]PWD,MADHYA PRADESH	03/2018	233.04 -	233.04	-	03/2018 -	11/2019	20	-

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
283	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]PWD,MADHYA PRADESH	11/2017	254.17 -	254.17	-	02/2018 -	11/2019	21	-
284	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]PWD,MADHYA PRADESH	03/2016	877.79 -	877.79	-	06/2019 -	11/2019	5	-
285	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]PWD,MADHYA PRADESH	03/2018	162.56 -	162.56	-	03/2018 -	12/2019	21	-
286	REHABILITATION & UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHANDE - [N24000876]PWD, WEST BENGAL	01/2017	396.86 -	396.86	-	09/2019 -	12/2019	3	-
287	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]PWD,MADHYA PRADESH	11/2017	249.05 -	249.05	-	07/2018 -	01/2020	18	-
288	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]PWD,MADHYA PRADESH	02/2018	279.44 -	279.44	-	03/2018 -	04/2020	25	-
289	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]PWD,MADHYA PRADESH	03/2018	166.21 -	166.21	-	08/2018 -	06/2020	22	-
290	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]PWD,MADHYA PRADESH	03/2018	217.22 -	217.22	-	08/2018 -	06/2020	22	-
291	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]PWD,MADHYA PRADESH	01/2016	809.16 -	809.16	-	07/2018 -	06/2020	23	-
292	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]PWD,MADHYA PRADESH	02/2018	169.63 -	169.63	-	03/2018 -	07/2020	28	-
293	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]PWD,MADHYA PRADESH	11/2017	184.62 -	184.62	-	02/2018 -	11/2020	33	-
294	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]PWD,MADHYA PRADESH	03/2018	214.69 -	214.69	-	03/2018 -	11/2020	32	-
295	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]PWD, WEST BENGAL	03/2016	160.27 -	160.27	-	08/2019 -	08/2021	24	-
296	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]PWD, WEST BENGAL	06/2016	236.78 -	236.78	-	08/2019 -	08/2021	24	-
	Total		97,501.48 -	1,00,719.03	61,393.68				
	<u>SHIPPING AND PORTS</u>								
	<u>Kamarajar Port Limited</u>								
297	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT - [N25000070]KPL,TAMIL NADU	03/2016	600.00 258.00	257.90	1.45	12/2017 -	05/2020	29	-
	Total		600.00 -	257.90	1.45				

Costing Rs. 150 Crore and above

(April 2019)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
298	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 -	24,664.00	8,397.00	07/2015 -	05/2020	58	-
	Total		13,334.00 -	24,664.00	8,397.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Bangalore Metro Rail Corporation Limited</u>								
299	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRCL,KARNATAKA	02/2014	26,405.14 -	26,405.14	499.85	02/2019 -	03/2020	13	-
	<u>Central Public Works Department</u>								
300	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB - [N28000088]CPWD,PUNJAB	02/2014	388.00 488.28	488.28	410.91	05/2017 02/2019	06/2019	25	4
301	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA - [N28000062]CPWD, WEST BENGAL	02/2014	156.57 -	156.57	154.15	08/2016 -	07/2019	35	-
302	NSG AT KOLKATA - [N28000104]CPWD, WEST BENGAL	10/2014	162.88 -	162.88	115.59	04/2018 -	07/2019	15	-
303	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP - [N28000108]CPWD, ANDHRA PRADESH	01/2018	206.58 -	206.58	82.25	03/2019 -	08/2019	5	-
304	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD, UTTARAKHAND	12/2008	114.26 266.00	266.00	-	12/2013 -	10/2019	70	-
305	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB - [N28000102]CPWD, PUNJAB	08/2016	294.00 349.94	294.00	167.44	04/2019 09/2019	12/2019	8	3
306	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD, RAJASTHAN	12/2016	549.31 -	559.49	291.77	07/2019 -	12/2019	5	-
307	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	1,592.00	496.57	10/2019 -	03/2020	5	-
308	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD, KERALA	01/2010	165.23 -	165.23	77.70	10/2012 -	03/2020	89	-
309	C/O OF 152 NOS TYPE-II, 304 NOS, TYPE-III, 76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD, TAMIL NADU	12/2015	209.00 -	209.00	105.72	10/2019 -	03/2020	5	-
310	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD, JHARKHAND	09/2012	171.86 -	171.86	73.90	03/2016 -	09/2020	54	-
311	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD, MAHARASHTRA	01/2018	223.37 -	223.37	24.40	07/2020 -	09/2020	2	-
312	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR - [N28000092]CPWD, MANIPUR	02/2014	216.69 -	216.69	52.00	03/2015 -	10/2020	67	-

Costing Rs. 150 Crore and above

(April 2019)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
313	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD,BIHAR	02/2016	496.18 496.00	498.99	61.43	06/2017 07/2017	10/2020	40	39
314	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 250.00	392.00	11.91	- 08/2020	03/2021	-	7
	<u>Hindustan Steelwork Construction Limited</u>								
315	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	956.00	651.21	03/2015 -	03/2021	72	-
	<u>Kochi Metro Rail Corporation Ltd</u>								
316	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	5,687.79	5,188.50	07/2017 -	12/2019	29	-
	<u>Mumbai Metro Rail Corporation Ltd</u>								
317	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	23,136.00	-	01/2015 -	05/2020	64	-
	Total		60,644.07 -	61,787.87	8,465.30				
	Grand Total		4,50,879.53	5,64,728.85	3,00,689.61				

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12/2020	12320	48
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	11459	54
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492	133
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
6	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
7	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	03/2020	430.45	48
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	72
9	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2020	417.33	44
10	BALRAM OCP EXTENSION, MCL 8.00 MTY	MCL	12/2007	03/2010	03/2022	172.08	144
11	ANANTA OC EXPANSION PH-III (15.0 MTY)	MCL	08/2008	03/2012	03/2021	207.28	108
12	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2021	321.5	84
13	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
14	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	MCL	05/2014	03/2019	03/2021	337.66	24
15	KULDA EXPN OC. (5.00 MTY)	MCL	06/2014	03/2018	03/2020	289.03	24
16	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2020	397.09	12
17	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
18	KULDA OCP (MAHANADI COALFIELDS LTD)	MCL	01/2005	03/2010	03/2020	302.96	120
19	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2021	510.85	60
20	KANIHA OCP, MCL, (10.0 MTY)	MCL	12/2007	03/2013	03/2022	457.77	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
21	BHUBANESWARI OCP, MCL (20.0 MTY)	MCL	12/2007	03/2017	03/2020	490.1	36
22	KOYAGUDEM OPENCAST PROJECT	SCCL	10/2015	03/2018	03/2020	426.79	24
23	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	60
24	MAGADH OC 20 MTY (CCL)	CCL	08/2008	07/2012	03/2022	706.4	116
25	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
26	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2021	163.51	120
27	TAPIN OCP (2.5 MTY)	CCL	08/2008	03/2012	03/2021	264.68	108
28	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2021	162.46	84
29	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	144
30	KISTARAM OCP	SCCL	11/2010	03/2015	03/2021	242.29	72
31	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2020	178.44	72
32	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	09/2019	1458.17	51
33	KAMPTEE DEEP OC MINE	WCL	11/2015	03/2021	03/2024	277.65	36
34	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	03/2020	1055.05	24
35	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2021	479.53	96
36	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	04/2019	1230.27	48
37	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	09/2019	5907.11	45
38	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2021	447.06	72

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
39	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	RCF	10/2014	11/2016	05/2019	197.79	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
40	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	09/2019	363.99	16
41	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	HSCC	07/2016	02/2018	06/2019	152.95	16
42	AIIMS - MOTHER AND CHILD BLOCK	HSCC	12/2013	05/2017	07/2019	204.44	26
43	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	10/2020	414.11	83

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
44	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	01/2018	02/2021	225.54	37
45	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2020	906	8
46	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
47	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	08/2021	466.43	10
48	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	OIL	07/2011	01/2019	09/2019	350	8
49	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	IOCL	05/2016	01/2019	12/2019	429	11
50	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	348	9
51	FIELD DEVELOPMENT OF NBP BLOCK KG-ONN-2003, NAGAYALANKA-KG	ONGC	04/2017	09/2018	04/2019	420.76	7
52	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2020	690	27
53	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	ONGC	11/2014	04/2019	12/2019	6068.8	8
54	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	ONGC	08/2015	03/2019	05/2020	2818.88	14
55	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	70
56	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	79
57	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	57
58	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	58
59	HALDIA LPG IMPORT FACILITY	BPCL	03/2015	10/2018	06/2019	694	8
60	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	15
61	ENHANCED RECOVERY FROM BASSEIN FIELD	ONGC	01/2015	12/2017	03/2020	4619.94	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA						
62	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2020	3190.69	25
63	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2020	160.1	8
64	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
65	ASSAM RENEWAL PROJECT FOR GROUP A	ONGC	03/2009	03/2013	12/2019	2465.15	81
66	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	OIL	07/2011	03/2017	12/2019	352.56	33
67	POLYPROPYLENE PLANT AT PARADIP REFINERY	IOCL	03/2014	09/2017	06/2019	3150	21
68	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	05/2020	390.52	14
69	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	08/2021	34012	14
70	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	IOCL	07/2015	11/2018	06/2019	822.66	7
71	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497	26
72	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	BPCL	02/2016	02/2020	10/2020	3313	8
73	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	03/2021	163.02	11

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
74	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	24
75	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	PGCIL	03/2016	01/2018	12/2019	808.63	23
76	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	PGCIL	05/2017	09/2018	09/2019	175.64	12
77	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	09/2019	445.89	7
78	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	12964.6	28
79	MUNPL-MEJA TPP - JV (2X660 MW)	NTPC	04/2012	12/2016	08/2019	9750.89	32
80	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	147
81	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	04/2019	477.69	103
82	TR. SYSTEM ASSOCIATED WITH MUNDRA	PGCIL	10/2008	10/2012	12/2019	4824.12	86

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	ULTRA MEGA POWER PROJECT						
83	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	11130.19	103
84	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	40
85	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	06/2019	374.63	38
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	PGCIL	02/2014	06/2016	05/2019	539.82	35
87	EASTERN REGION STRENGTHENING SCHEME- XII	PGCIL	05/2014	11/2016	12/2019	522.29	37
88	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	93
89	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPSPS IN CHHATTISGARH	PGCIL	06/2014	03/2018	12/2019	5151.37	21
90	EASTERN REGION STRENGTHENING SCHEME - IX	PGCIL	02/2014	02/2016	05/2019	196.58	39
91	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	12/2023	8112.12	44
92	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	03/2020	11638.55	30
93	TANDA TPP STAGE-II (2X660 MW)	NTPC	09/2014	03/2019	03/2020	9188.98	12
94	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	02/2020	12532.44	18
95	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	09/2021	14366.58	31
96	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	02/2022	1381.84	29
97	TRANSMISSION SYSTEM ASSOCIATED WITH KISHENGANAGA HEP	PGCIL	01/2015	03/2018	05/2019	268.8	14
98	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP)	PGCIL	01/2015	10/2017	09/2019	871.62	23
99	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	PGCIL	01/2015	07/2017	06/2019	203.28	23
100	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	05/2019	436.68	29
101	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	114
102	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2019	2496.9	114
103	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657	76
104	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	63
105	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	05/2019	1779.29	126

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
106	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	08/2021	8692.97	127
107	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	03/2020	11846	33
108	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	07/2020	02/2021	10598.98	7
109	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	05/2019	197.4	14
110	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2019	1394.52	31
111	DHUKWAN SMALL HYDRO PROJECT	THDCIL	05/2011	02/2014	10/2019	195.42	68
112	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353	60
113	EASTERN REGION STRENGTHENING SCHEME- XV	PGCIL	04/2016	04/2018	01/2020	454.11	21
114	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	SJVN	11/2016	11/2017	04/2019	330	17
115	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	12
116	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	09/2019	408.46	8

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
117	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	36
118	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	96
119	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
120	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
121	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2021	1172.92	27
122	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2021	1724.2	9
123	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	36
124	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
125	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
126	LUCKNOW- PILIBHIT VIA SITAPUR,	RVNL	04/2011	03/2019	03/2020	927.01	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	LAKHIMPUR GC						
127	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
128	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	03/2026	16216	15
129	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	24
130	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295	12
131	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	6
132	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	36
133	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	09/2019	236.93	11
134	AJMER-BANGURGRAM	NWR	04/2011	11/2019	05/2020	213.39	6
135	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	12/2019	242.09	10
136	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651	108
137	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	10/2022	569.63	31
138	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	57
139	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2021	2436.21	12
140	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	12/2019	528.57	9
141	MULTI MODAL LOGISTICS PARK AT KATHUWAS	CCOI	01/2011	03/2018	03/2020	493.17	24
142	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	CCOI	10/2013	03/2019	12/2019	305	9
143	MULTI MODAL LOGISTICS PARK AT BARHI	CCOI	12/2015	03/2019	03/2020	346.32	12
144	MULTI MODAL LOGISTICS PARK AT TIHI	CCOI	12/2015	03/2019	02/2020	174	11
145	MULTI MODAL LOGISTICS PARK AT VARNAMA	CCOI	10/2013	03/2019	12/2019	343	9
146	MULTI MODAL LOGISTICS PARK AT KAKINADA	CCOI	08/2016	03/2019	12/2020	234.5	21
147	NEW BG RLY LINE FROM EKLAKHI- BALURGHAT INCLUDING GAZOLE- ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	297.32	12
148	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.2	168

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
149	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2022	1188.91	36
150	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	27
151	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	12/2021	1202.7	82
152	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	21
153	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	81
154	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	96
155	MANOHARABAD-KOTHPALL NEW LINE(SCR)	SCR	04/2006	03/2010	03/2022	1160.48	144
156	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	732.81	144
157	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
158	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2020	277.28	48
159	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2023	986.3	93
160	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
161	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
162	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2022	2288.7	12
163	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2023	2132.77	108
164	GADAG-WADI NL	SWR	04/2013	12/2018	12/2024	2841.84	72
165	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
166	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	192
167	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	03/2016	03/2020	1125.89	48
168	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	178
169	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	96
170	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	147
171	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
172	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.2	12
173	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	12
174	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	79
175	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	51
176	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	12/2021	410.08	34
177	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	03/2021	2500	220
178	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	111
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	108
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
181	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
182	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
183	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2021	1111.99	25
184	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	09/2019	148.77	33
185	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2021	1156.94	12
186	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	04/2022	600	25
187	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	24
188	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	03/2020	678.54	12
189	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	10/2020	829.74	67
190	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	10/2021	1200.2	19
191	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	10/2021	1491.47	19
192	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	10/2021	1763.93	19
193	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2023	1035.16	12
194	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2023	3631	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
195	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	03/2020	187.26	71
196	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	28
197	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
198	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	02/2020	213	46
199	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	NER	04/2017	04/2017	01/2020	622.5	33
200	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	NER	04/2016	12/2019	04/2021	1177.96	16
201	SAGauli VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	12
202	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	12
203	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	61

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
204	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	PWD	01/2017	03/2019	09/2019	247.25	6
205	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	NHAI	09/2010	06/2018	04/2019	946	10
206	HARIDWAR DEHRADUN APPROVED LENGTH 69	NHAI	11/2011	10/2013	07/2019	478.51	69
207	PANVEL-INDAPUR	NHAI	12/2011	06/2014	06/2019	942.69	60
208	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	NHAI	06/2015	12/2017	08/2019	563.92	20
209	2 LANING WITH PS OF GULABPURA - UNIARA	NHAI	10/2015	10/2017	04/2019	597	18
210	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	05/2019	531.13	12
211	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	04/2019	593.26	11
212	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	12/2020	649.5	21
213	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	NHAI	12/2015	06/2016	04/2019	602.95	34
214	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	NHAI	01/2016	07/2018	04/2019	574.28	9
215	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	NHAI	08/2015	05/2018	04/2019	505	11
216	4 LANING OF NH-31D FROM GHOSHPUKUR -	NHAI	12/2015	06/2018	12/2019	1083	18

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SALSALABARI (KM 0.00 TO KM . 83.785)						
217	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	04/2019	641.17	33
218	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
219	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	09/2020	1176.37	37
220	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	NHAI	07/2017	07/2017	11/2020	476.56	40
221	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	NHAI	06/2017	06/2017	11/2019	648.33	29
222	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	NHAI	10/2017	10/2017	01/2020	639.97	27
223	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	NHAI	10/2017	10/2017	11/2020	964.17	37
224	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	06/2020	1124.11	33
225	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	08/2020	1227.87	35
226	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	MORTH	02/2015	03/2015	06/2019	383.4	51
227	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	PWD	09/2012	10/2013	06/2019	511	68
228	GWALIOR-JHANSI, NH-75	NHAI	12/2003	12/2009	08/2020	604	128
229	PATNA-MUZZAFFARPUR	NHAI	08/2010	02/2013	06/2019	671.3	76
230	JORBAT - BARAPANI	NHAI	01/2011	01/2014	05/2019	536	64
231	4-LANNING OF CHAPRA-HAJIPUR	NHAI	01/2011	07/2013	06/2019	575	71
232	KRISHNANAGAR-BERHAMPUR	NHAI	02/2012	07/2014	05/2019	702.16	58
233	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108	91
234	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	NHAI	05/2013	02/2014	06/2019	1348.2	64
235	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	NHAI	02/2010	08/2012	12/2019	617	88
236	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	06/2019	1724.55	75
237	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	NHAI	11/2010	05/2013	04/2019	1585	71
238	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	NHAI	11/2013	11/2016	04/2019	1916.79	29
239	4 LANNING OF MH-KNT BORDER SANGAREDDY	NHAI	04/2014	09/2016	06/2019	1266.6	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	SECTION OF NH-9						
240	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2019	2848	69
241	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	NHAI	11/2011	05/2014	06/2019	1535	61
242	MUZAFFARNAGAR-HARIDWAR	NHAI	09/2011	03/2013	12/2019	754	81
243	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	06/2019	1078.84	70
244	4-LANING OF BRAHAMPUR-FARAKA	NHAI	02/2011	08/2013	06/2020	998.79	82
245	6-LANING OF DHANKUNI-KHARAGPUR SECTION	NHAI	04/2012	09/2014	05/2019	1396.18	56
246	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATAKA SECTION	NHAI	06/2014	11/2016	06/2019	923.04	31
247	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	NHAI	05/2014	08/2016	12/2020	1655.01	52
248	FOUR LANING OF HOSPET - CHITRADURGA	NHAI	03/2015	08/2018	11/2019	1388	15
249	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HONNABAD - SECTION OF NH-218 (NEW NH NO -50)	NHAI	05/2015	09/2017	05/2019	709	20
250	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	NHAI	05/2015	11/2017	08/2019	1387.11	21
251	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	NHAI	12/2015	06/2019	12/2020	2168.66	18
252	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	07/2019	1423.96	8
253	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	NHAI	12/2015	12/2018	10/2019	2136.97	10
254	FOUR LANING OF SIMGA - SARAGAON	NHAI	12/2015	05/2018	06/2019	596.67	13
255	FOUR LANING OF FORBESGANJ - JOGBANI	NHAI	08/2015	04/2018	04/2020	322.09	24
256	FOUR LANING OF CHANDIGARH - KHARAR	NHAI	10/2015	12/2017	12/2019	447.29	24
257	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	NHAI	12/2015	04/2018	06/2019	726.67	14
258	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	NHAI	12/2015	05/2018	06/2019	479.2	13
259	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	05/2019	199.81	121
260	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	NHAI	12/2003	05/2008	05/2019	160	132
261	REHABILITATION AND UPGRADE OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	PWD	01/2016	07/2018	06/2020	809.16	23

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
262	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	PWD	02/2018	03/2018	04/2020	279.44	25
263	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2019	254.17	21
264	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	PWD	11/2017	07/2018	01/2020	249.05	18
265	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2019	233.04	20
266	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	217.22	22
267	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	PWD	03/2018	03/2018	11/2020	214.69	32
268	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	08/2019	279.7	24
269	FOUR LANING OF BARHI-HAZARIBAGH NH-33	NHAI	08/2016	08/2018	08/2019	323.72	12
270	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	NHAI	08/2016	04/2019	11/2019	2016	7
271	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	NHAI	09/2016	08/2018	09/2019	767.03	13
272	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	12/2020	950.69	16
273	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	NHAI	11/2016	03/2019	09/2019	400.25	6
274	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	NHAI	11/2016	03/2019	11/2019	446.17	8
275	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	12/2019	605.84	17
276	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	11/2020	1373.28	8
277	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	NHAI	03/2017	03/2017	11/2020	1059.73	44
278	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	NHAI	03/2017	03/2020	05/2021	235.48	14
279	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	12
280	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	NHIDCL	12/2016	01/2017	01/2020	138.93	36
281	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	373.07	36
282	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	NHIDCL	03/2016	08/2016	08/2019	396.52	36
283	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	NHIDCL	03/2016	08/2016	08/2019	429.52	36
284	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
285	SONAPUR TO GUWAHTI (AS-3)	NHAI	12/2003	03/2008	06/2019	245	135
286	BRAHMPUTRA BRIDGE, NH NO-31	NHAI	12/2003	04/2010	04/2019	217.61	108
287	NALBARI T BIJNI (AS-7)	NHAI	12/2003	04/2008	12/2019	208	140
288	NALBARI TO BIJNI (AS-6)	NHAI	12/2003	06/2008	04/2019	225	130
289	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	NHAI	08/2015	04/2019	10/2019	399.54	6
290	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	NHAI	01/2016	11/2018	05/2019	1134.97	6
291	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	11/2020	701.4	20
292	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	NHAI	03/2016	11/2018	12/2019	229.37	13
293	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	NHAI	03/2016	03/2019	11/2020	870	20
294	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	03/2020	707.82	19
295	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	05/2020	641.17	22
296	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	NHAI	04/2016	06/2018	12/2019	804.97	18
297	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ	NHAI	05/2015	05/2017	06/2019	581.84	25
298	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	PWD	01/2017	03/2017	04/2019	205.05	25
299	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	PWD	06/2016	08/2019	08/2021	236.78	24
300	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	PWD	03/2016	08/2019	08/2021	160.27	24
301	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	PWD	11/2017	02/2018	11/2020	184.62	33
302	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	PWD	11/2017	02/2018	11/2019	235.91	21
303	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	PWD	02/2018	03/2018	07/2020	169.63	28
304	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	PWD	03/2016	11/2018	11/2019	271.17	12
305	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	PWD	03/2018	08/2018	06/2020	166.21	22
306	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	PWD	08/2014	11/2017	07/2019	823.2	20
307	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	PWD	03/2018	03/2018	12/2019	162.56	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

SHIPPING AND PORTS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
308	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	KPL	03/2016	12/2017	05/2020	600	29

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
309	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	RINL	07/2015	07/2018	06/2019	465.85	11
310	CENTRAL DISPATCH YARD	RINL	08/2015	08/2018	06/2019	320.66	10
311	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	09/2019	2858	21
312	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	SAIL	05/2015	12/2017	06/2019	1154.18	18
313	INSTALLATION OF NEW HOT STRIP MILL AT RSP	SAIL	04/2015	04/2018	05/2019	3127.3	13
314	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2019	15525	53
315	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2020	343	41
316	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	06/2020	1034.01	32
317	FORGED WHEEL PLANT	RINL	04/2014	09/2018	06/2019	1682.85	9
318	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	06/2020	262.87	12

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
319	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	13334	58
320	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	BSNL	01/2018	10/2018	05/2019	231.8	7
321	MADHYA PRADESH ACCESS (LOT1)	BSNL	08/2017	05/2018	05/2019	215.3	12

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
322	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	09/2020	246.31	7
323	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	CPWD	09/2012	03/2016	09/2020	171.86	54
324	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	CPWD	02/2014	03/2015	10/2020	216.69	67
325	NSG AT KOLKATA	CPWD	10/2014	04/2018	07/2019	162.88	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
326	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2020	26405.14	13
327	IRRIGATION WORK OF BAGMATI	HSCL	10/2005	03/2015	03/2021	956	72
328	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	06/2020	197.33	14
329	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	06/2019	388	25
330	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	CPWD	02/2014	08/2016	07/2019	156.57	35
331	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	CPWD	01/2010	10/2012	03/2020	165.23	89
332	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	29
333	NAGPUR METRO RAIL	NMRCL	08/2014	03/2018	12/2019	8680	21
334	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	01/2015	05/2020	23136	64
335	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	70
336	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	10/2020	496.18	40
337	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	CPWD	08/2016	04/2019	12/2019	294	8

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	314.61	441.33	126.72

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
5	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
6	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7080.41	1173.3
7	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
8	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	249.03	448.86	199.83

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
9	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	NATIS	04/2011	09/2011	1718	3827.3	2109.3

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
10	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	ISPRL	01/2006	01/2012	993	1693	700
11	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	714.25	107.19
12	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	202.94	330.35	127.41
13	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	543.91	682.9	138.99
14	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	3049.47	134.47
15	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
16	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	658.62	910.23	251.61
17	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
18	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	OIL	09/2012	03/2015	871.35	1200	328.65
19	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	309.81	723.4	413.59
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	2059.63	2665.65	606.02
21	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	1577.15	715.36
22	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	12/2020	1823	3027.9	1204.9
23	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
POWER							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
24	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9394.8	5475.21
25	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19496.34	13211.01
26	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	11638.55	12865.92	1227.37
27	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	477.69	738.48	260.79
29	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
30	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
31	KHARGONE STPP STAGE I (1320 MW)	NTPC	03/2015	09/2019	9870.51	11148.86	1278.35
32	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
33	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	11846	12739.82	893.82
34	KUDGI STPP STAGE 1	NTPC	01/2012	01/2017	15166.19	16934.65	1768.46
35	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	8692.97	15095.67	6402.7
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	1779.29	2187.32	408.03
37	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
38	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	5024.35	3367.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6880.36	1769.03
40	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9072.36	4317.94
41	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	2496.9	7419.34	4922.44
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	4105.3	1613.72
43	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	436.68	602.44	165.76
44	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	12964.6	13731.26	766.66
45	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	5353	7998	2645
46	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	14366.58	15164.05	797.47
47	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	12532.44	13740.53	1208.09
48	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	3846.3	867.82
49	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
50	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	NCR	04/1986	03/1994	158.77	634.48	475.71
51	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	297.32	614	316.68
52	CALICUT-MANGALORE (DL) (SR)	SR	02/1996	N.A.	240	579.37	339.37
53	KARUR-SALEM(NL),SR	SR	02/1997	N.A.	155.55	920	764.45
54	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	ECR	03/1999	N.A.	1033.07	3020.94	1987.87
55	KATI HAR - JOGBANI (GC)(NEFR)	NFR	09/2001	12/2010	792.46	1320	527.54
56	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	SR	03/1998	N.A.	280	1122	842
57	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	09/2006	N.A.	343.17	1065	721.83
58	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2072.5	1347.81
59	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
60	KHURDA ROAD - BARANG 3RD LINE (DL)	RVNL	04/2000	03/2009	133.41	385	251.59

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	(ECOR)						
61	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1101.16	717.37
62	HATHUA-BHATNI (N L) (NER)	NER	04/2005	12/2022	230.03	770.08	540.05
63	ETAWAH-MAINPURI (NL),NCR	NCR	04/1997	12/2008	120	245.39	125.39
64	MAHARAJGANJ-MASRAKH (NL) - NER	NER	04/2003	06/2018	218.19	413.56	195.37
65	RAMGANJMUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	2713.09	2288.49
66	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	732.81	1993	1260.19
67	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	749	271.12
68	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.77	1538.12
69	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	4968	2574.53
70	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
71	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	2300	1717.17
72	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	SR	09/2006	N.A.	227.4	900	672.6
73	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
74	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	1180.19	3300	2119.81
75	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	589.15	426.28
76	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	04/1999	12/2009	108	432.72	324.72
77	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	324.73	1156.41	831.68
78	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	6093.31	5845.65
79	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	ER	04/1995	03/2016	1125.89	1988.38	862.49
80	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2973.73	2478.29
81	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	3712.5	1441
82	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	2900	773

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
83	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	858.96	538.3
84	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1082.32	106.7
85	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	348.55	102.47
86	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	477.31	182.31
87	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	NER	03/2012	08/2018	199.75	378.26	178.51
88	BHOJIPUR TANAKPUR VIA PILIBHIT	NER	03/2008	N.A.	195.64	435	239.36
89	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
90	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
91	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	631.78	1195	563.22
92	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	403	174
93	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	566.41	237.02
94	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	528.26	347.44
95	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	624.47	3550	2925.53
96	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
97	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
98	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
99	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540	1211.86
100	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
101	MANDHANA - BRAHMAWART NEW LINE PROJECT.	NER	04/1997	04/1999	609.04	1807.88	1198.84
102	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1182.31	422.31
103	MADURAI-DINDIGUL (INCL. AMBADUTURAI-KODAIKANNAL ROAD) (62.05 KM) DOUBLING	SR	02/2003	03/2009	199.55	330.32	130.77
104	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1420.39	834.46
105	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	2686.63	778.12

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
106	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1260.61	678.48
107	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1120	177.05
108	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	1103	154.96
109	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	1750	1036.52
110	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1077	149.99
111	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
112	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	524.43	939	414.57
113	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	SER	01/1991	12/2021	1013.45	1428	414.55
114	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1151.81	181.98
115	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
116	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	559.91	227.76
117	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.67	302.41
118	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
119	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
120	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
121	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
122	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	544.72	137.73
123	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	1800	1679.3
124	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	816.55	183.87
125	LUMDING-HOJAI PATCH DOUBLING PROJECT	NFR	04/2012	03/2019	246.07	398.93	152.86
126	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	551	237
127	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
128	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	661	246.16

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
129	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	394.28	152.76
130	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
131	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	6000	5093.54
132	CHENGANNUR-CHINGAVANAM	SR	04/2006	N.A.	191.72	369.83	178.11
133	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	450	285.59
134	ERODE-PALANI	SR	04/2008	N.A.	288.57	1140	851.43
135	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	NFR	04/1999	03/2007	895	1733.2	838.2
136	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
137	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
138	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	SR	04/1998	N.A.	271.24	520	248.76
139	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	556.64	357.96
140	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	SR	04/2013	N.A.	839	1500	661
141	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	2350	1826.48
142	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	1105	953.16
143	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	367.17	154.16
144	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	785.87	237.87
145	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1474.47	1102.33
146	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	ECR	04/2008	N.A.	678.62	2393.23	1714.61
147	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	926.09	715.09
148	CHHAPRA-MUZAFFARPUR (NL)	ECOR	04/2006	N.A.	378.56	2614.36	2235.8
149	SAKRI-HASANPUR ROAD (NL)	ECOR	04/1999	N.A.	325	729.92	404.92
150	BIHTA-AURANGABAD (NL)	ECOR	04/2008	N.A.	326.2	2995.01	2668.81
151	GAYA-CHATRA (NL)	ECOR	04/2008	N.A.	415.67	549.75	134.08

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
152	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	ECOR	04/2008	N.A.	445.25	2860.55	2415.3
153	NAWADA-LAXMIPUR (NL)	ECR	04/2008	N.A.	620.57	2626.98	2006.41
154	ARA-BHABHUA ROAD (NL)	SER	04/2008	N.A.	633.87	2396.88	1763.01
155	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	N.A.	258.2	365	106.8
156	DANGOPOSI-RAJKHARSWAN 3RD LINE DOUBLING	SER	04/2010	12/2015	309.44	525.81	216.37
157	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	SER	04/2011	N.A.	289.64	760	470.36
158	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
159	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
160	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	349	106.91
161	PUSHKAR-MERTA	NWR	04/2013	N.A.	323	432.22	109.22
162	AJMER-KOTA (NASIRABAD-JAUNDRI)	NWR	04/2013	N.A.	822	1099.54	277.54
163	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
164	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4261.71	2178.96
165	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	845.58	220.58
166	GEVRA ROAD PENDRA ROAD	SECR	02/2014	03/2022	2288	4919	2631
167	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	644.78	889.52	244.74
168	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1279	407
169	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	556.54	1342.46	785.92
170	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	NR	04/2006	03/2010	369.9	1581.53	1211.63
171	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	NR	03/2002	06/2007	625.3	876.1	250.8
172	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
173	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2100	1650
174	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	795.01	384.93

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
175	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	04/1999	N.A.	744.71	1126.79	382.08
176	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	4084.69	2745.21
177	AGARTALA SABROOM, NL, NEFR	NFR	04/2008	03/2014	1142	3407	2265
178	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
179	AMRAVATI-NARKHER NL(CR)	CR	06/1994	06/1999	663.01	858.96	195.95
180	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	829.74	1216	386.26
181	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1870.41	255.82
182	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	1103.04	229.33
183	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
184	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
185	TAMLUK DIGHA, LINE DOUBLING (SER)	SER	03/1984	06/2005	293.97	749.69	455.72
186	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
187	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	1756	1244.14
188	NANDYAL-YERRAGUNTALA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64
189	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
190	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
191	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	M RTP	04/2008	03/2014	5300	7986.04	2686.04
192	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	3000	673.48
193	GHUTIASHARIF-CANNING (ER)	ER	04/2009	12/2011	193.08	612.45	419.37
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
195	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1532	1146.8
196	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	495.74	734.01	238.27
197	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	13809	9354.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
198	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3798.8	875.67
199	CHANDIGARH-BADDI NL	NR	04/2007	N.A.	328.14	1540	1211.86
200	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
201	CUMBUM-PRODDATUR	SCR	04/2013	N.A.	829	1599.39	770.39
202	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
203	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692.43	134.43
204	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	7000	4033.01
205	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	625	338
206	BHADRACHALAM-KOVVUR	SCR	04/2012	N.A.	923.23	1787	863.77
207	MM FROM PANSKURA-GHATAL NL	SER	04/2011	N.A.	276.69	426	149.31
208	MM FROM BURAMARA-CHAKULIA	SER	04/2008	N.A.	466.48	1000	533.52
209	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	1856.95	2200	343.05
210	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
211	MUNIRABAD (GINGERA) -RAICHUR NL	SWR	04/2007	N.A.	179.65	1350.91	1171.26
212	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	298.7	114.64
213	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRHAT-KULPI NL	ER	04/2009	02/2012	499.96	665.75	165.79
214	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
215	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	ER	04/2009	02/2012	259.51	533.59	274.08
216	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
217	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1620.01	431.1
218	JIND-SONEPAT (NL),NR	NR	01/2004	03/2012	238.56	740	501.44
219	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
220	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	385.13	185.32
221	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
222	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	1928.22	2945	1016.78
223	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	NHAI	09/2015	N.A.	771.18	7558	6786.82
224	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
225	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	279.7	398.22	118.52
226	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	PWD	08/2014	11/2017	823.2	937.76	114.56
227	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 & NH-10 0	PWD	08/2014	11/2017	600.87	720.97	120.1
228	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
229	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
230	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
231	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
232	SIX LANING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
233	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
234	FOUR LANING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
235	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH-202 UNDER LWE S	PWD	03/2011	12/2015	218.31	339.82	121.51
236	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	PWD	12/2011	02/2012	156.63	276	119.37
237	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	280.13	125.09
238	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
239	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	331.23	135.23
SHIPPING AND PORTS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
240	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	PORT TRUST	10/2002	03/2006	150	600	450
241	CONSTRUCTION OF OFFSHORE CONTAINER	MUMBAI PORT	01/2007	12/2010	366.39	669.46	303.07

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB						
STEEL							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
242	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	22542	7017
243	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	343	488.4	145.4
TELECOMMUNICATIONS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
244	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330
URBAN DEVELOPMENT							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
245	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	HSCL	05/2005	02/2014	768.88	1113.34	344.46
246	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74
247	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	19058	4458
248	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	5687.79	506
249	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4439.23	175.23
250	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	1592	372.79
251	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	388	488.28	100.28

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2019)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	06/2020	1,1459.00	1,6580.00	5121	54
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2021	3492.00	6840.00	3348	133

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
3	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2020	314.61	441.33	126.72	21

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2021	162.76	349.28	186.52	72
5	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2020	152.43	459.49	307.06	60
6	SHANTIKHANI LONGWALL PROJ-SCCL	SCCL	10/2006	03/2012	03/2024	249.03	448.86	199.83	144
7	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	09/2019	5907.11	7080.41	1173.3	45

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
8	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2021	4497.00	6025.00	1528	26
9	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	3049.47	134.47	110
10	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	11/2019	4588.29	5245.96	657.67	15
11	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	ONGC	06/2010	01/2014	11/2019	202.94	330.35	127.41	70
12	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	12/2019	861.79	1577.15	715.36	79
13	URAN CHAKAN SHIKRAPUR LPG PIPELINE	HPCL	12/2009	10/2014	08/2019	309.81	723.40	413.59	58
14	INTEGRATED DEVELOPMENT OF B-127 FIELDS	ONGC	12/2011	03/2015	12/2019	2059.63	2665.65	606.02	57

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	12/2020	5111.33	6880.36	1769.03	24
16	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	PGCIL	05/2005	11/2008	05/2019	1779.29	2187.32	408.03	126
17	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	12/2020	2978.48	3846.30	867.82	93
18	DARLIPALLI STPP STAGE-I (2X800 MW)	NTPC	02/2014	08/2018	02/2020	1,2532.44	1,3740.53	1208.09	18
19	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	02/2019	09/2021	1,4366.58	1,5164.05	797.47	31
20	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	05/2014	05/2019	5353.00	7998.00	2645	60
21	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	SJVN	05/2015	12/2016	05/2019	436.68	602.44	165.76	29
22	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	12/2022	2491.58	4105.30	1613.72	114
23	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	NEEPCO	12/2004	12/2009	06/2019	2496.90	7419.34	4922.44	114
24	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2022	1657.00	5024.35	3367.35	76
25	SYSTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	09/2019	487.49	639.46	151.97	63
26	NPGCL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	01/2018	05/2020	1,2964.60	1,3731.26	766.66	28
27	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	12/2021	3919.59	9394.80	5475.21	147
28	WESTERN REGION STRENGTHENING SCHEME-V	PGCIL	12/2007	09/2010	04/2019	477.69	738.48	260.79	103
29	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	12/2019	4824.12	5071.94	247.82	86
30	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	NTPC	03/2013	09/2017	03/2020	1,1638.55	1,2865.92	1227.37	30

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	03/2022	1,1130.19	1,4719.10	3588.91	103
32	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	08/2019	1364.52	1891.41	526.89	40
33	BARH STPP(3X660MW) NTPC	NTPC	02/2005	01/2011	08/2021	8692.97	1,5095.67	6402.7	127
34	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	12/2019	4754.42	9072.36	4317.94	12
35	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	NTPC	12/2012	06/2017	03/2020	1,1846.00	1,2739.82	893.82	33

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
36	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2020	644.78	889.52	244.74	36
37	CHHINDWARA-MANDLA FORT GC	SECR	03/2011	03/2012	03/2020	556.54	1342.46	785.92	96
38	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	ECR	11/2001	02/2016	03/2021	624.47	3550.00	2925.53	61
39	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	03/2021	942.95	1120.00	177.05	24
40	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
41	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2023	247.66	6093.31	5845.65	178
42	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	03/2020	324.73	1156.41	831.68	96
43	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	06/2021	2923.13	3798.80	875.67	147
44	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	03/2020	4454.17	1,3809.00	9354.83	108
45	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2020	385.20	1532.00	1146.8	12
46	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2020	532.87	2145.00	1612.13	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
47	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	10/2021	2326.52	3000.00	673.48	79
48	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	03/2020	1339.48	4084.69	2745.21	51
49	DAUSA-GANGAPUR CITY(NL),NWR	NWR	02/1997	02/2019	12/2021	410.08	795.01	384.93	34
50	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	NFR	04/1983	03/2019	03/2020	297.32	614.00	316.68	12
51	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2023	1045.20	2120.16	1074.96	168
52	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2022	1188.91	1620.01	431.1	36
53	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	03/2020	1185.64	1844.47	658.83	27
54	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2023	810.78	1928.07	1117.29	21
55	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	12/2020	2393.47	4968.00	2574.53	81
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	03/2020	477.88	749.00	271.12	96
57	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	RVNL	07/2006	03/2008	03/2020	732.81	1993.00	1260.19	144
58	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	2200.00	343.05	12
59	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2020	495.44	2973.73	2478.29	192
60	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	ER	04/1995	03/2016	03/2020	1125.89	1988.38	862.49	48
61	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	03/2021	2500.00	2,7949.00	25449	220
62	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR), NL, RVNL	RVNL	04/1995	12/2012	03/2022	631.78	1195.00	563.22	111
63	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2019)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	RAJARHAT (MTP)								
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
65	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	03/2021	1111.99	1539.28	427.29	25
66	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	09/2019	148.77	377.00	228.23	33
67	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2021	1614.59	1870.41	255.82	24
68	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	NWR	04/2008	03/2015	10/2020	829.74	1216.00	386.26	67
69	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	01/2020	295.00	477.31	182.31	12
70	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	06/2020	246.08	348.55	102.47	6
71	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2022	320.66	858.96	538.3	36
72	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	12/2019	242.09	349.00	106.91	10
73	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2024	651.00	1009.00	358	108
74	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2020	632.68	816.55	183.87	57
75	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2021	701.61	810.02	108.41	28
76	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	SER	04/1995	12/2021	12/2024	524.43	939.00	414.57	36
77	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	03/2020	927.01	1077.00	149.99	12
78	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2022	731.64	1185.73	454.09	12
79	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2022	744.04	1215.54	471.5	12

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(APRIL 2019)

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
80	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	PWD	04/2014	08/2017	08/2019	279.70	398.22	118.52	24
81	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A 0	PWD	08/2014	11/2017	07/2019	823.20	937.76	114.56	20
82	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	03/2021	1288.07	1420.00	131.93	12
83	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	05/2019	199.81	385.13	185.32	121
84	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	06/2019	1108.00	2288.00	1180	91
85	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	06/2019	1266.60	1544.00	277.4	33

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
86	REVAMPING OF SINTER MACHINES - 1 AND 2	RINL	12/2009	10/2016	03/2020	343.00	488.40	145.4	41
87	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	10/2019	1,5525.00	2,2542.00	7017	53

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
88	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	05/2020	1,3334.00	2,4664.00	11330	58

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
89	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	10/2019	114.26	266.00	151.74	70
90	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	12/2019	5181.79	5687.79	506	29
91	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	CPWD	02/2014	05/2017	06/2019	388.00	488.28	100.28	25

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

TOR -> Time Overrun

Details of Ongoing Projects Under -Public Private Partnership Mode

Annexure-XVIII

Costing Rs. 150 Crore and above					(April 2019)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
1	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36 -	291.36	01/2014 -	09/2018	.00	56
2	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00 -	325.00	05/2013 -	-	.00	0
3	2 LANNING OF MOKAMA-MUNGER - PPP (ANNUITY) - [N24000166]	05/2011	351.54 -	351.54	05/2013 -	-	.00	0
4	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - PPP (ANNUITY) - [N24000176]	05/2010	374.00 -	374.00	05/2013 -	-	.00	0
5	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - PPP (ANNUITY) - [N24000177]	09/2011	485.00 -	485.00	08/2013 -	12/2018	.00	64
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00 -	486.00	05/2010 -	10/2018	.00	101
7	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54 -	511.54	11/2013 -	12/2018	.00	61
8	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00 -	516.00	07/2008 -	-	.00	0
9	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07 -	530.07	08/2016 -	02/2019	.00	30
10	JORBAT - BARAPANI - PPP (ANNUITY) - [N24000180]	01/2011	536.00 -	536.00	01/2014 -	05/2019	.00	64
11	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00 -	571.00	10/2013 -	-	.00	0
12	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00 -	574.00	03/2014 -	-	.00	0
13	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00 -	575.00	07/2013 -	06/2019	.00	71
14	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00 -	604.00	12/2009 -	08/2020	.00	128
15	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00 -	617.00	08/2012 -	12/2019	.00	88
16	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00 -	624.00	04/2014 -	-	.00	0
17	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU PPP (BOT) - [N24000586]	06/2016	637.18 -	637.18	06/2019 -	09/2019	.00	3
18	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30 -	671.30	02/2013 -	06/2019	.00	76

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (April 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
19	KRISHNANAGAR-BERHAMPUR - PPP (ANNUITY) - [N24000209]	02/2012	702.16 -	702.16	07/2014 -	05/2019	.00	58
20	MUZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00 -	754.00	03/2013 -	12/2019	.00	81
21	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23 -	763.23	06/2019 -	11/2019	.00	5
22	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90 -	822.90	04/2018 -	03/2019	.00	11
23	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - PPP (BOT) - [N24000454]	06/2014	923.04 -	923.04	11/2016 -	06/2019	.00	31
24	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88 -	953.88	07/2013 -	12/2018	.00	65
25	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - PPP (BOT) - [N24000453]	01/2015	972.50 -	972.50	07/2017 -	12/2018	.00	17
26	4-LANING OF BRAHAMPUR-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79 -	998.79	08/2013 -	06/2020	.00	82
27	BAREILLY-SITAPUR (NH-24) - PPP (BOT) - [N24000200]	03/2011	1,046.00 -	1,046.00	09/2013 -	-	.00	0
28	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - PPP (BOT) - [N24000205]	12/2011	1,047.00 -	1,047.00	06/2014 -	-	.00	0
29	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84 -	1,078.84	08/2013 -	06/2019	.00	70
30	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70 -	1,100.70	06/2014 -	-	.00	0
31	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00 -	1,141.00	08/2013 -	-	.00	0
32	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00 -	1,175.00	04/2013 -	-	.00	0
33	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00 -	1,250.00	12/2013 -	-	.00	0
34	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - PPP (BOT) - [N24000230]	05/2013	1,348.20 -	1,348.20	02/2014 -	06/2019	.00	64
35	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00 -	1,388.00	08/2018 -	11/2019	.00	15
36	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18 -	1,396.18	09/2014 -	05/2019	.00	56
37	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00 -	1,410.00	09/2014 -	03/2019	.00	54
38	RANCHI-RARGA-JAMSETHPUR - PPP (ANNUITY) - [N24000215]	12/2012	1,479.00 -	1,479.00	06/2015 -	-	.00	0
39	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10 -	1,509.10	09/2012 -	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (April 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
40	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	06/2019	.00	61
41	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	06/2019	21.90	33
42	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
43	FOUR LANING OF BIAORA -DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR - PPP (BOT) - [N24000505]	06/2015	1,583.79	1,583.79	01/2019	06/2019	.00	5
44	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - PPP (BOT) - [N24000145]	11/2010	1,585.00	1,585.00	05/2013	04/2019	.00	71
45	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	12/2018	51.83	37
46	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
47	6 LANING OF AGRA - ETAWAH BYPASS - PPP (BOT) - [N24000452]	07/2015	1,657.20	1,657.20	01/2019	01/2019	.00	0
48	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00	1,665.00	-	03/2019	.00	0
49	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	03/2019	.00	89
50	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
51	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	06/2019	.00	75
52	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
53	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	02/2019	.00	13
54	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	04/2019	.00	29
55	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	03/2019	.00	44
56	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
57	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	04/2019	.00	0
58	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00	2,159.00	06/2015	-	.00	0
59	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00	2,288.00	11/2011	06/2019	106.50	91
60	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) - PPP (BOT) - [N24000425]	07/2015	2,288.18	2,288.18	05/2019	05/2019	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (April 2019)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
61	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76	2,498.76	08/2014	-	.00	0
62	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00	2,848.00	03/2014	12/2019	.00	69
63	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	2,945.00	04/2015	-	52.73	0
	Total		75,880.12	78,901.07				
	<u>SHIPPING AND PORTS</u>							
	<u>Kamarajar Port Limited</u>							
64	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED - PPP (ANNUITY) - [N25000066]	02/2015	244.50	275.98	12/2017	-	12.88	0
	<u>Mumbai Port Trust</u>							
65	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB - PPP (BOT) - [N25000063]	01/2007	366.39	669.46	12/2010	-	82.72	0
	Total		610.89	945.44				
	Grand Total		76,491.01	79,846.51				

State-wise Ongoing Project detail's

Annexure-XIX

Details of Central Sector Projects Costing Rs.150 crore and above (as on					30.04.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (-) [6/2020]	314.61 (-) [441.33]	85.79 (126.72) [21]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (-) [0/0]	409.85 (-) [409.85]	0.00 (0.00) [0]
3	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (-) [0/0]	277.17 (-) [277.17]	0.00 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (-) [0/0]	262.97 (-) [262.97]	0.00 (0.00) [0]
5	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	257.34 (-) [238.00]	41.09 (-19.34) [0]
6	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [0/0]	391.00 (-) [391.00]	0.00 (0.00) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (-) [0/0]	234.27 (-) [234.27]	0.00 (0.00) [0]
8	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (-) [11/2019]	237.80 (-) [238.00]	29.43 (0.20) [0]
	<u>ANDHRA PRADESH</u>				
	<u>Health And Family Welfare</u>				
9	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [2/2020]	601.02 (-) [601.02]	96.75 (0.00) [-]
10	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [0/0]	272.19 (-) [272.19]	111.92 (0.00) [0]
	<u>Petroleum</u>				
11	ADDITIONAL FACILITIES AT VIJAYWADA FOR CONVERSION TO TOP ON PARADEEP HYDERABAD PIPELINE	1/2015	3/2021 (-) [3/2021]	342.00 (-) [342.00]	0.00 (0.00) [0]
12	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (-) [7/2021]	466.00 (-) [466.00]	5.39 (0.00) [3]
13	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (-) [4/2021]	384.58 (-) [384.58]	66.38 (0.00) [0]

14	FIELD DEVELOPMENT OF NELL BLOCK KG-ONN-2003, NAGAYALANKA-KG	4/2017	9/2018 (4/2019) [4/2019]	420.76 (-) [420.76]	105.21 (0.00) [7]
15	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (8/2021) [8/2021]	34,012.00 (-) [34,012.00]	2,465.32 (0.00) [14]
16	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	8.03 (0.00) [10]
17	REVAMPING OF MARKETING TERMINAL AT VISHAKHAPATNAM	7/2014	3/2021 (-) [3/2021]	247.00 (-) [247.00]	0.00 (0.00) [0]
18	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (-) [10/2021]	316.20 (-) [316.20]	12.16 (0.00) [0]
19	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (-) [7/2020]	20,928.00 (-) [20,928.00]	4,501.16 (0.00) [0]
20	VVSPL CAPACITY EXPANSION AND OSTT-SS JETTY SUB SEA PIPELINE PROJECT	9/2016	9/2019 (-) [9/2019]	407.00 (-) [407.00]	328.48 (0.00) [0]
	<u>Railways</u>				
21	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [1,599.39]	0.94 (770.39) [0]
22	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.07 (0.00) [0]
23	GUDUR-DURGARAJPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
24	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2023]	3,631.00 (-) [3,631.00]	305.25 (0.00) [12]
25	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009 (-) [3/2023]	1,045.20 (-) [2,120.16]	289.91 (1,074.96) [168]
26	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	2,499.71 (-) [2,499.71]	209.89 (0.00) [0]
27	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [12/2020]	234.50 (-) [235.00]	5.59 (0.50) [21]
28	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [387.70]	323.91 (0.00) [0]
29	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2022]	2,288.70 (-) [2,288.70]	506.48 (0.00) [12]
30	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
31	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	7/2006	3/2008 (-) [3/2020]	732.81 (-) [1,993.00]	2,121.12 (1,260.19) [144]
32	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.67]	633.52 (302.41) [0]
33	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [1,503.71]	36,195.04 (0.00) [24]

	Road Transport And Highways				
34	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [6/2019]	328.67 (-) [328.67]	0.00 (0.00) [-]
35	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
36	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	0.00 (0.00) [0]
37	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [12/2020]	314.43 (-) [314.43]	0.00 (0.00) [-]
38	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	11/2010	5/2013 (-) [4/2019]	1,585.00 (-) [1,585.00]	2,322.02 (0.00) [71]
39	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C	10/2015	11/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
40	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	7/2015	12/2015 (-) [0/0]	333.21 (333.21) [333.21]	0.00 (0.00) [0]
41	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	7/2015	12/2015 (-) [0/0]	333.21 (-) [333.21]	0.00 (0.00) [0]
42	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (-) [3/2021]	1,532.62 (-) [1,532.62]	0.00 (0.00) [0]
43	FOUR LANNING OF AP/TN BORDER TO NALAGAMPALLI VILLAGE(KM 133.360 TO 172.00) OF NH-4 (NEW NH-40)	6/2017	6/2017 (-) [11/2019]	648.33 (-) [648.33]	49.59 (0.00) [29]
44	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [5/2019]	1,134.97 (-) [1,134.97]	73.29 (0.00) [6]
45	REHABILITATION AND UP-GRADATION OF NH-214 (NEW NH-216) FROM KM 0.0 TO 26.150(KATHIPUDI TO START OF K	10/2015	/ (-) [0/0]	480.21 (-) [480.21]	0.00 (0.00) [0]
46	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 0.0 TO 32.735(IBRAHIMPATNAM TO CHANDR	7/2015	/ (-) [0/0]	314.43 (-) [314.43]	0.00 (0.00) [0]
47	REHABILITATION AND UP-GRADATION OF NH-221 (NEW NH-30) FROM KM 32.735 TO KM 71.200 (CHANDRAGUEDEM TO A	12/2014	2/2015 (-) [0/0]	201.12 (201.00) [201.12]	0.00 (0.00) [0]
48	REHABILITATION AND UPGRADATION FROM KM.425 400 TO 509 400 NH-565 OF PENCHALAKONA TO YERPEDU CONTRAC	1/2014	7/2014 (-) [0/0]	361.30 (-) [207.40]	44.08 (-153.90) [0]
49	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 70/000 TO KM 125-150	2/2015	5/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
50	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
51	REHABILITATION AND UPGRADATION OF EXISTING NH-565 OF FROM KM.154.900 TO 198.694 OF DAVULAPALLY TO	2/2014	11/2014 (-) [0/0]	170.21 (-) [170.21]	5.65 (0.00) [0]
52	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [0/0]	565.09 (-) [565.09]	0.00 (0.00) [0]
53	REHABILITATION AND UPGRADATION OF NH -18 FROM KM 57/0 TO KM 108/850 PILERU TO RAYACHOTY SECTION TO T	3/2015	/ (-) [0/0]	175.03 (-) [175.00]	0.00 (-0.03) [0]

54	REHABILITATION AND UPGRADATION OF NH -67 FROM KM 589/0 TO 641/0 (MYDUKUR TO DORNALA T-JUNCTION)	2/2015	2/2017 (-) [0/0]	241.61 (-) [241.61]	7.71 (0.00) [0]
55	REHABILITATION AND UPGRADATION OF NH-167 FROM KM 70	2/2015	4/2015 (-) [0/0]	224.83 (-) [224.83]	0.00 (0.00) [0]
56	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (-) [0/0]	271.45 (-) [271.45]	0.00 (0.00) [0]
57	REHABILITATION AND UPGRADATION OF NH-4 FROM NALAGAMPALLI TO AP/KARNATAKA BORDER	3/2017	3/2020 (-) [11/2019]	648.32 (-) [503.10]	15.10 (-145.22) [-4]
58	REHABILITATION AND UPGRADATION OF NH-42 (OLD NO.205) FROM KM.134/0 TO 202/050 (MUDIGUBBA TO ANANTHAP	2/2015	/ (-) [0/0]	266.00 (-) [266.00]	0.00 (0.00) [0]
59	REHABILITATION AND UPGRADATION OF NH-42 FROM KM 4 to 350 TO KM 75 to 600 TO TWO LANE WITH PAVE SOLDOU	3/2015	9/2015 (-) [0/0]	309.01 (-) [309.01]	0.00 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF NH-565 FROM KM 294.00 TO 361.327 (VAGGAMPALLE- DORNALA T-JUNCTION)	2/2014	7/2014 (-) [0/0]	258.99 (-) [258.99]	16.54 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF NH-565 FROM KM.198/694 TO 294/0 (MARKAPURAM TO VAGGAMPALLE SECTION	2/2014	6/2014 (-) [0/0]	417.61 (-) [417.61]	0.00 (0.00) [0]
62	REHABILITATION AND UPGRADATION OF NH-67 FROM KM 695.000 TO KM 741.950 (ATMAKUR – NELLORE SECTION) IN	11/2014	2/2017 (-) [0/0]	297.78 (330.00) [330.00]	0.00 (32.22) [0]
63	REHABILITATION UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR SEC	7/2014	2/2015 (-) [0/0]	251.55 (-) [251.55]	7.74 (0.00) [0]
64	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [0/0]	1,959.00 (-) [1,959.00]	0.00 (0.00) [0]
65	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [0/0]	1,323.15 (-) [1,323.15]	0.00 (0.00) [0]
66	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [7/2021]	1,550.98 (-) [1,550.98]	0.00 (0.00) [-]
67	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [6/2019]	1,535.00 (-) [1,535.00]	3,008.77 (0.00) [61]
68	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [5/2020]	1,041.62 (-) [1,187.10]	143.09 (145.48) [2]
69	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.52 (0.00) [0]
70	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	54.13 (0.00) [0]
	<u>Steel</u>				
71	ADDITIONAL WATER STORAGE RESERVOIR(KBR-II)	7/2015	7/2018 (-) [6/2019]	465.85 (-) [465.85]	382.25 (0.00) [11]
72	CENTRAL DISPATCH YARD	8/2015	8/2018 (-) [6/2019]	320.66 (-) [320.66]	190.91 (0.00) [10]
73	COKE OVEN BATTERY-5	12/2011	12/2017 (-) [9/2019]	2,858.00 (-) [2,500.00]	1,207.76 (-358.00) [21]

74	REVAMPING OF SINTER MACHINES - 1 AND 2	12/2009	10/2016 (-) [3/2020]	343.00 (-) [488.40]	249.30 (145.40) [41]
	<u>Urban Development</u>				
75	CONSTRUCTION OF NIT AP PHASE 1A AT TADEPALLIGUIDEM AP	1/2018	3/2019 (-) [8/2019]	206.58 (-) [206.58]	82.25 (0.00) [5]
76	CONSTRUCTION OF 123 BLOCKS IN TELENGANA AND 167 BLOCKS IN A.P. FOR INDOOR SPORTS HALL UNDER RGKA	7/2014	/ (-) [0/0]	232.00 (-) [232.00]	0.00 (0.00) [0]
77	CONSTRUCTION OF SOUTHERN REGIONAL CENTER FOR NSG AT IBRAHIMPATNAM HYDERABAD	6/2014	3/2017 (-) [0/0]	157.84 (-) [157.84]	155.25 (0.00) [0]
78	REHABILITATION AND STRENGTHENING OF SEWERAGE SYSTEM IN OLD CITY AREA ON SOUTH OF MUSI IN ZONE 2	8/2007	/ (-) [0/0]	246.90 (-) [246.90]	0.00 (0.00) [0]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
79	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (6/2019) [6/2019]	2,496.90 (7,419.34) [7,419.34]	7,131.10 (4,922.44) [114]
80	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,723.47 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
81	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
82	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
83	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH- 229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
84	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	8.99 (0.00) [0]
85	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450.TO KM 605.600(EXISTING CHAINAGE FROM KM.583.450	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
86	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
87	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
88	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
89	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	38.50 (0.00) [0]
90	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
91	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
92	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]

93	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
94	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
95	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
96	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
97	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
98	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
99	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
100	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
101	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
102	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
103	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]
104	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
105	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
106	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
107	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
108	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
109	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
110	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
111	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,132.88 (-86.29) [81]
112	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	86.47

			(-) [2/2020]	(-) [557.00]	(0.00) [0]
113	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	403.95 (0.00) [0]
114	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
115	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	129.67 (127.41) [70]
116	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	256.37 (0.00) [1]
117	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [682.90]	2.40 (138.99) [0]
118	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,451.96 (0.00) [0]
119	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	145.01 (-5.15) [0]
120	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
121	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (486.96) [551.00]	660.21 (237.00) [0]
122	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	475.48 (-50.32) [-24]
123	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	399.61 (-49.96) [0]
124	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (614.81) [398.93]	413.64 (152.86) [0]
125	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	581.00 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
126	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
127	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
128	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	0.00 (-65.82) [0]
129	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
130	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
131	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	80.00 (0.00) [0]

132	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	0.00 (0.00) [0]
133	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
134	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
135	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
136	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2019]	217.61 (-) [217.61]	391.12 (0.00) [108]
137	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [5/2019]	160.00 (-) [167.98]	203.98 (7.98) [132]
138	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	59.85 (0.00) [0]
139	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	16.84 (0.00) [0]
140	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [818.00]	0.00 (0.00) [0]
141	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
142	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	0.00 (0.00) [0]
143	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
144	HARANGAJAO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [280.00]	422.51 (0.00) [0]
145	HARANGAJAO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
146	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
147	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [5/2019]	199.81 (-) [385.13]	211.69 (185.32) [121]
148	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [167.64]	268.94 (0.00) [0]
149	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2019]	208.00 (-) [230.00]	308.94 (22.00) [140]
150	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [4/2019]	225.00 (-) [225.00]	312.79 (0.00) [130]
151	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [6/2019]	245.00 (174.34) [174.34]	270.88 (-70.66) [135]
152	STRENGTHENING AND CONSTRUCTION OF PAVED	5/2011	2/2018	176.22	0.00

	SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM		(-) [0/0]	(-) [176.22]	(0.00) [0]
153	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>BIHAR</u>				
	<u>Petroleum</u>				
154	BRANCH PIPELINE FROM PATNA TO MOTIHARI BAITALPUR ON BKPL	5/2016	12/2020 (-) [2/2020]	664.00 (-) [664.00]	528.48 (0.00) [-10]
155	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	52.16 (0.00) [0]
156	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (-) [3/2021]	522.00 (-) [522.00]	16.56 (0.00) [0]
157	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (-) [10/2020]	199.36 (-) [199.36]	51.40 (0.00) [0]
158	FUEL QUALITY UPGRADATION (DHDT/PRIME G) PROJECT AT BARAUNI REFINERY	7/2015	11/2018 (-) [6/2019]	822.66 (-) [822.66]	822.02 (0.00) [7]
159	FUEL QUALITY UPGRADATION (NSU,NHT CCR NEW UNIT) PROJECT AT BARAUNI REFINERY	6/2017	10/2019 (-) [10/2019]	951.64 (-) [951.64]	246.28 (0.00) [0]
160	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (-) [1/2021]	189.00 (-) [189.00]	4.55 (0.00) [0]
161	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (-) [3/2021]	206.50 (-) [206.50]	0.00 (0.00) [0]
162	MOTIHARI AMLEKHGANJ PIPELINE	9/2015	6/2020 (-) [6/2020]	324.00 (-) [324.00]	143.56 (0.00) [0]
	<u>Power</u>				
163	ASSOCIATED TRANSMISSION SYSTEM FOR NABINAGAR-II TIPS	4/2016	6/2019 (6/2019) [6/2019]	790.13 (790.30) [790.30]	530.54 (0.17) [0]
164	BARH STPP(3X660MW) NTPC	2/2005	1/2011 (8/2021) [8/2021]	8,692.97 (15,095.67) [15,095.67]	15,932.41 (6,402.70) [127]
165	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	5/2014 (-) [5/2019]	5,353.00 (-) [7,998.00]	7,128.72 (2,645.00) [60]
166	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	1/2018 (-) [5/2020]	12,964.60 (-) [13,731.26]	12,695.00 (766.66) [28]
167	PRE-CONSTRUCTION ACTIVITIES OF 1320 MW BUXAR THERMAL POWER PLANT	5/2015	12/2016 (-) [5/2019]	436.68 (533.50) [602.44]	557.22 (165.76) [29]
	<u>Railways</u>				
168	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [2,396.88]	0.39 (1,763.01) [0]
169	ARARIA-SUPAUL (NL)	4/2008	/ (-) [3/2023]	1,605.17 (-) [1,605.17]	0.19 (0.00) [-]
170	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [0/0]	326.20 (-) [2,995.01]	1.68 (2,668.81) [0]
171	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/	378.56	111.71

			(-) [3/2022]	(-) [2,614.36]	(2,235.80) [-]
172	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/	406.92	200.00
			(-) [0/0]	(-) [339.00]	(-67.92) [0]
173	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/	205.00	5.21
			(-) [0/0]	(-) [205.00]	(0.00) [0]
174	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	4/1991	/	329.39	759.20
			(-) [12/2021]	(-) [566.41]	(237.02) [-]
175	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/	445.25	0.00
			(-) [0/0]	(-) [2,860.55]	(2,415.30) [0]
176	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/	213.01	13.00
			(-) [0/0]	(-) [367.17]	(154.16) [0]
177	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/	528.65	330.82
			(-) [3/2023]	(-) [2,066.77]	(1,538.12) [-]
178	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012	324.73	876.49
			(-) [3/2020]	(-) [1,156.41]	(831.68) [96]
179	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020	548.00	40.00
			(-) [3/2020]	(-) [785.87]	(237.87) [0]
180	KATIHAR - JOGBANI (GC)(NEFR)	9/2001	12/2010	792.46	944.77
			(-) [0/0]	(724.31) [1,320.00]	(527.54) [0]
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/	162.87	183.72
			(-) [3/2022]	(-) [589.15]	(426.28) [-]
182	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	4.98
			(-) [3/2020]	(-) [360.00]	(26.24) [-]
183	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020	1,200.20	0.00
			(-) [10/2021]	(-) [1,200.20]	(0.00) [19]
184	KOSI BRIDGE (NL), ECR	4/2002	3/2020	499.41	640.78
			(-) [3/2020]	(-) [516.02]	(16.61) [0]
185	KURSELA-BIHARIGANJ (NL)	4/2008	/	192.56	0.38
			(-) [0/0]	(-) [192.56]	(0.00) [0]
186	MAHARAJGANJ-MASRAKH (NL) - NER	4/2003	6/2018	218.19	379.47
			(-) [10/2018]	(-) [413.56]	(195.37) [0]
187	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012	477.88	495.40
			(-) [3/2020]	(283.95) [749.00]	(271.12) [96]
188	MOTIHARI-SITAMARHI (NL)	4/2006	/	211.00	4.41
			(-) [0/0]	(-) [926.09]	(715.09) [0]
189	MUZAFFARPUR SAGauli DOUBLING 100.60 KM	4/2016	3/2021	731.64	0.00
			(-) [3/2022]	(-) [1,185.73]	(454.09) [12]
190	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/	281.30	0.58
			(-) [0/0]	(-) [281.30]	(0.00) [0]
191	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/	228.05	1.52
			(-)	(-)	(0.00)

			[0/0]	[228.05]	[0]
192	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (-) [559.91]	538.21 (227.76) [0]
193	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	620.57 (-) [2,626.98]	0.00 (2,006.41) [0]
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2020]	532.87 (2,132.03) [2,145.00]	932.38 (1,612.13) [12]
195	PATNA GANGA BRIDGE WITH LINKING LINES BETWEEN PATNA AND HAJIPUR (RAIL CUM ROAD BRIDGE) 19 KM	11/2001	2/2016 (-) [3/2021]	624.47 (-) [3,550.00]	97.63 (2,925.53) [61]
196	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (-) [0/0]	180.82 (-) [528.26]	462.75 (347.44) [0]
197	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (-) [10/2021]	1,491.47 (-) [1,491.47]	0.00 (0.00) [19]
198	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (-) [3/2022]	744.04 (-) [1,215.54]	1.81 (471.50) [12]
199	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (-) [729.92]	253.10 (404.92) [-]
200	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2021]	372.14 (-) [1,474.47]	338.44 (1,102.33) [-]
201	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [0/0]	380.00 (-) [380.00]	0.00 (0.00) [0]
202	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [2,393.23]	17.17 (1,714.61) [0]
	<u>Road Transport And Highways</u>				
203	2 LANNING OF MOKAMA-MUNGER	5/2011	5/2013 (-) [0/0]	351.54 (-) [351.54]	329.40 (0.00) [0]
204	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [12/2018]	511.54 (-) [511.54]	565.81 (0.00) [0]
205	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014 (-) [0/0]	375.09 (-) [375.09]	494.33 (0.00) [0]
206	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (-) [6/2019]	575.00 (-) [575.00]	842.31 (0.00) [71]
207	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [6/2019]	581.84 (-) [581.84]	77.43 (0.00) [25]
208	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	8/2015	11/2015 (-) [0/0]	288.24 (-) [288.24]	0.00 (0.00) [0]
209	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (-) [0/0]	2,598.00 (-) [2,598.00]	0.00 (0.00) [0]
210	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	0.00 (-7.71) [14]
211	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH	3/2018	/ (-)	496.20 (-)	0.00 (0.00)

	PAVED SHOULDER		[0/0]	[496.20]	[0]
212	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (-) [683.83]	0.00 (0.00) [0]
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [178.85]	0.00 (0.00) [0]
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [553.30]	0.00 (0.00) [0]
215	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	6/2016 (-) [0/0]	369.77 (-) [369.77]	0.00 (0.00) [0]
216	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [12/2019]	1,167.45 (-) [1,167.45]	78.28 (0.00) [-]
217	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [10/2020]	642.41 (-) [642.41]	84.54 (0.00) [-]
218	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [4/2020]	322.09 (-) [322.09]	71.28 (0.00) [24]
219	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (-) [1,408.85]	0.00 (0.00) [0]
220	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [1/2020]	814.04 (-) [814.04]	328.86 (0.00) [-]
221	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-) [0/0]	556.07 (-) [556.07]	0.00 (0.00) [0]
222	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [4/2019]	1,041.10 (-) [1,041.10]	191.74 (0.00) [0]
223	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.73 (0.00) [0]
224	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [6/2019]	671.30 (-) [671.30]	884.84 (0.00) [76]
225	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	0.00 (0.00) [0]
226	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	0.00 (0.00) [0]
227	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2014	3/2014 (-) [0/0]	377.64 (-) [377.64]	0.00 (0.00) [0]
228	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	8/2014 (-) [0/0]	278.39 (-) [278.39]	0.00 (0.00) [0]
229	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	1/1991	/ (-) [0/0]	478.35 (-) [478.35]	0.00 (0.00) [0]
230	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [319.68]	0.00 (0.00) [0]
231	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	2/2014	7/2016 (-) [0/0]	665.50 (-) [665.50]	0.00 (0.00) [0]

232	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	8/2016 (-) [0/0]	282.41 (-) [282.41]	67.52 (0.00) [0]
233	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/2013	8/2014 (-) [0/0]	322.01 (-) [322.01]	0.00 (0.00) [0]
234	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG	1/1991	10/2016 (-) [0/0]	358.22 (-) [358.22]	188.71 (0.00) [0]
235	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (-) [675.00]	0.00 (0.00) [0]
236	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40	1/1991	/ (-) [0/0]	154.62 (-) [154.62]	0.00 (0.00) [0]
237	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
238	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	0.00 (0.00) [54]
239	STRENGTHENING & WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPROV	3/2015	7/2016 (-) [0/0]	206.80 (-) [206.80]	0.00 (0.00) [0]
240	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA	8/2015	4/2019 (-) [10/2019]	399.54 (-) [399.54]	178.16 (0.00) [6]
241	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [3/2019]	854.80 (-) [854.80]	575.71 (0.00) [0]
242	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [516.13]	410.36 (0.00) [0]
243	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [3/2020]	672.89 (-) [736.01]	0.00 (63.12) [0]
	<u>Urban Development</u>				
244	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (7/2017) [10/2020]	496.18 (496.00) [498.99]	61.43 (2.81) [40]
245	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [3/2021]	956.00 (-) [956.00]	651.21 (0.00) [72]
	<u>CHHATISGARH</u>				
	<u>Coal</u>				
246	AMERA OC RCE	2/2015	3/2018 (-) [0/0]	335.97 (-) [335.97]	51.96 (0.00) [0]
247	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2020]	316.10 (-) [316.10]	65.52 (0.00) [0]
248	AMLAI OC EXPANSION SECTOR B (1.50 MTY)	11/2009	3/2016 (-) [3/2019]	198.59 (-) [198.59]	169.59 (0.00) [0]
249	BAROUD OC EXPANSION (RCE)- 3MTY	4/2012	3/2016 (-) [3/2019]	258.56 (-) [258.56]	172.88 (0.00) [0]
250	BIJARI OC RCE (1.50 MTY)	5/2014	3/2020 (-) [3/2020]	164.49 (-) [164.49]	80.25 (0.00) [0]
251	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022	610.63	88.29

			(-) [3/2022]	(-) [610.63]	(0.00) [0]
252	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2023]	916.24 (-) [916.24]	3.94 (0.00) [0]
253	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (-) [3/2023]	11,816.40 (-) [11,816.40]	2,900.98 (0.00) [0]
254	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (-) [3/2020]	152.43 (-) [459.49]	203.55 (307.06) [60]
255	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]
256	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2020]	178.44 (-) [178.44]	5.16 (0.00) [72]
257	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,057.66 (0.00) [0]
258	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2024]	1,875.32 (-) [1,875.32]	0.00 (0.00) [0]
259	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	9.53 (0.00) [0]
260	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2021]	321.50 (-) [321.50]	207.31 (0.00) [84]
261	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	6.21 (0.00) [0]
262	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	75.96 (0.00) [0]
	<u>Petroleum</u>				
263	CONSTRUCTION OF NEW MARKETING TERMINAL AT BARADWAR, DISTT- JANJGIR- CHAMPA IN STATE OF CHHATTISGARH	12/2016	4/2021 (-) [4/2021]	300.00 (-) [300.00]	0.00 (0.00) [0]
	<u>Power</u>				
264	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	6/2017 (3/2020) [3/2020]	11,846.00 (-) [12,739.82]	11,850.13 (893.82) [33]
265	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [11/2019]	3,004.00 (-) [3,004.00]	1,420.87 (0.00) [0]
	<u>Railways</u>				
266	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (-) [12/2019]	872.00 (-) [1,279.00]	0.00 (407.00) [0]
267	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	4/1995	12/2012 (-) [3/2022]	631.78 (632.00) [1,195.00]	731.65 (563.22) [111]
268	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [3/2022]	2,288.00 (-) [4,919.00]	67.00 (2,631.00) [0]
269	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (-) [3/2021]	1,973.00 (-) [1,973.00]	78.00 (0.00) [0]
270	KENDRI-DHANTARI INCLUDING ABHANPUR-RAJIM	4/2011	3/2022 (-)	1,471.93 (-)	0.00 (-928.93)

			[3/2022]	[543.00]	[0]
271	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [0/0]	3,055.00 (-) [3,055.00]	600.00 (0.00) [0]
272	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (-) [3/2020]	1,160.00 (-) [1,160.83]	582.11 (0.83) [0]
273	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
274	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [3/2020]	1,402.02 (-) [958.09]	970.78 (-443.93) [0]
	Road Transport And Highways				
275	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/	1,029.96	0.00
			(-) [0/0]	(-) [1,029.96]	(0.00) [0]
276	CONSTRUCION OF 2 LANE ROAD FROM KM. 28700-292.00, 322.00-342.00 AND 352.00- 400.00 OF NH 63 (OLD NH-	12/2010	12/2012 (-) [0/0]	169.26 (-) [169.26]	0.00 (0.00) [0]
277	FOUR / SIX LANING OF RAIPUR - SIMGA (PKG-1)	12/2015	4/2018 (-) [6/2019]	726.67 (-) [726.67]	323.95 (0.00) [14]
278	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	7.21 (0.00) [0]
279	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [6/2019]	596.67 (-) [596.67]	333.94 (0.00) [13]
280	REHABILITATION AND UP GRADATION OF NH-43 FROM KM.81.500-KM 130.00 DHAMTARI- KANKER SECTION.	10/2014	3/2015 (-) [0/0]	213.47 (-) [213.47]	0.00 (0.00) [0]
281	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/	291.05	0.00
			(-) [0/0]	(-) [291.05]	(0.00) [0]
282	REHABILITATION AND UP GRADATION OF NH-12A FROM KM246.849-KM 317.406 KAWARDHA- SIMGA SECTION.	12/2014	/	394.20	0.00
			(-) [0/0]	(-) [394.20]	(0.00) [0]
283	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION	11/2015	12/2015 (-) [0/0]	485.44 (-) [485.44]	0.00 (0.00) [0]
284	REHABILITATION AND UPGRADATION OF NH-43 KM. 180.00 TO 241.00 (BEDMA-DAHAKONDA) UNDER NHDP-IV	10/2014	3/2015 (-) [0/0]	298.34 (-) [298.34]	0.00 (0.00) [0]
285	REHABILITATION AND UPGRADATION OF NH-43 KM. 241.000 TO 298.000 (DAHAKONDA TO JAGDALPUR) UNDER NHDP-I	11/2014	3/2015 (-) [0/0]	262.54 (-) [262.54]	0.00 (0.00) [0]
286	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.0.00 TO 28.110(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE I	3/2015	/	422.34	22.25
			(-) [0/0]	(-) [422.34]	(0.00) [0]
	Steel				
287	2 MTPA PELLET PLANT AT NAGARNAR	11/2015	6/2020 (-) [6/2020]	818.00 (-) [818.00]	31.60 (0.00) [0]
288	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	4/2015 (-) [0/0]	188.93 (-) [188.93]	132.20 (0.00) [0]
289	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (10/2019) [10/2019]	15,525.00 (-) [22,542.00]	15,401.64 (7,017.00) [53]
	D & N HAVELI				

	<u>Petroleum</u>				
290	DAMAN DEVELOPMENT PROJECT	8/2014	5/2019 (10/2019) [10/2019]	6,086.08 (5,842.31) [5,842.31]	4,778.58 (-243.77) [5]
	<u>DELHI</u>				
	<u>Health And Family Welfare</u>				
291	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [7/2019]	204.44 (-) [204.44]	176.22 (0.00) [26]
292	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [0/0]	293.65 (-) [293.65]	282.43 (0.00) [0]
293	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [2/2020]	156.56 (-) [156.65]	54.94 (0.09) [-]
294	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [10/2020]	414.11 (-) [513.89]	147.00 (99.78) [83]
	<u>Heavy Industry</u>				
295	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [9/2019]	1,554.00 (-) [1,554.00]	335.03 (0.00) [0]
	<u>Power</u>				
296	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (6/2019) [12/2019]	1,394.52 (1,394.52) [1,394.52]	338.19 (0.00) [31]
	<u>Railways</u>				
297	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [0/0]	295.68 (-) [295.68]	1.20 (0.00) [0]
298	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [0/0]	156.65 (-) [197.17]	56.10 (40.52) [0]
	<u>Road Transport And Highways</u>				
299	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-I)_NEW	9/2015	/ (-) [0/0]	771.18 (-) [7,558.00]	261.77 (6,786.82) [0]
	<u>Telecommunications</u>				
300	GSM-RF EXPANSION PROJECT, MTNL DELHI (3G)	6/2016	6/2017 (-) [0/0]	418.26 (-) [418.26]	367.03 (0.00) [0]
	<u>Urban Development</u>				
301	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (6/2020) [6/2020]	197.33 (-) [197.33]	25.15 (0.00) [14]
302	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	7/2012	12/2015 (-) [0/0]	884.30 (-) [884.30]	689.94 (0.00) [0]
303	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [11/2019]	271.90 (-) [271.90]	17.39 (0.00) [0]
304	CONSTRUCTION OF FLYOVER-UNDERPASS BETWEEN NORTHERN MAHIPALPUR BYPASS ROAD AND AIRPORT ROAD NEAR HANU	12/2017	6/2019 (-) [6/2019]	188.00 (-) [188.00]	131.55 (0.00) [0]
305	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [0/0]	38,585.00 (-) [38,585.00]	34,763.15 (0.00) [0]
306	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2020]	1,219.21 (-) [1,592.00]	496.57 (372.79) [5]
307	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO	11/2017	5/2020	238.56	33.40

	ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B		(-) [5/2020]	(-) [238.56]	(0.00) [0]
308	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [11/2019]	4,264.00 (-) [4,439.23]	3,936.53 (175.23) [0]
309	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	/ (8/2020) [3/2021]	392.00 (250.00) [392.00]	11.91 (0.00) [-]
310	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	/ (12/2020) [12/2020]	422.00 (250.00) [422.00]	0.00 (0.00) [-]
311	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [0/0]	2,694.00 (-) [2,694.00]	0.00 (0.00) [0]
312	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2016	4/2018 (-) [0/0]	248.20 (-) [248.20]	28.59 (0.00) [0]
	<u>GOA</u>				
	<u>Defence Production</u>				
313	CONSTRUCTION WORKS PHASE 3B	12/2016	8/2020 (-) [8/2020]	285.95 (286.00) [285.95]	74.55 (0.00) [0]
314	CONSTRUCTION WORKS PHASE 4	12/2016	5/2018 (3/2019) [0/0]	167.69 (168.00) [167.69]	127.00 (0.00) [0]
	<u>Health And Family Welfare</u>				
315	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [5/2020]	249.01 (-) [249.01]	46.28 (0.00) [-]
	<u>Road Transport And Highways</u>				
316	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [280.16]	16.06 (0.00) [0]
317	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	10.72 (0.00) [0]
318	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM- MANGALORE	10/2015	/ (-) [0/0]	936.40 (-) [936.40]	0.00 (0.00) [0]
319	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/ (-) [0/0]	298.33 (-) [298.33]	16.10 (0.00) [0]
320	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE	3/2015	4/2018 (-) [0/0]	297.00 (-) [297.00]	38.33 (0.00) [0]
321	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/ (-) [0/0]	773.98 (-) [773.98]	0.00 (0.00) [0]
322	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/ (-) [0/0]	819.95 (-) [819.95]	0.00 (0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
323	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015 (11/2016) [6/2020]	11,459.00 (16,580.00) [16,580.00]	13,469.00 (5,121.00) [54]
	<u>Petroleum</u>				
324	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/ (-) [0/0]	588.20 (-) [588.20]	0.00 (0.00) [0]
325	BS-VI PROJECT AT GUJARAT REFINERY	3/2018	9/2019	3,380.00	1,683.93

			(-) [9/2019]	(-) [3,380.00]	(0.00) [0]
326	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018 (-) [3/2019]	327.78 (-) [200.00]	141.46 (-127.78) [0]
327	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020 (10/2020) [10/2020]	906.00 (-) [906.00]	27.50 (0.00) [8]
328	INFRASTRUCTURE DEVELOPMENT TO FACILITATE GRID POWER IMPORT AT 220KV AT GUJARAT REFINERY	9/2016	7/2020 (-) [7/2020]	208.35 (-) [208.35]	96.96 (0.00) [0]
329	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026 (3/2026) [3/2026]	1,162.56 (1,162.56) [1,162.56]	338.79 (0.00) [0]
330	REPLACEMENT OF KV SECTION OF KSPL	10/2014	8/2018 (-) [0/0]	279.00 (-) [279.00]	200.05 (0.00) [0]
331	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	1/2018 (-) [2/2021]	225.54 (-) [225.54]	0.00 (0.00) [37]
	<u>Power</u>				
332	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (9/2019) [9/2019]	193.14 (193.14) [193.14]	24.40 (0.00) [3]
333	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (9/2019) [9/2019]	175.64 (175.64) [175.64]	83.54 (0.00) [12]
334	WIND POWER PROJECT AT SADLA IN DISTT. SURENDRANAGAR (GUJARAT)	11/2016	11/2017 (-) [4/2019]	330.00 (-) [330.00]	330.23 (0.00) [17]
	<u>Railways</u>				
335	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,082.32]	830.71 (106.70) [0]
336	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (-) [3/2020]	829.74 (-) [385.60]	629.92 (-444.14) [0]
337	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [203.00]	202.29 (85.64) [0]
338	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (-) [0/0]	551.51 (-) [551.51]	257.05 (0.00) [0]
339	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (-) [3/2019]	318.24 (-) [321.62]	125.76 (3.38) [0]
340	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (-) [3/2020]	691.84 (-) [691.84]	54.87 (0.00) [0]
341	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [3/2021]	644.38 (-) [644.38]	210.07 (0.00) [0]
342	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
343	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (-) [3/2023]	844.10 (-) [844.10]	79.08 (0.00) [-]
344	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [12/2019]	343.00 (-) [343.00]	310.09 (0.00) [9]

345	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
346	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [12/2021]	1,548.66 (-) [1,548.66]	1,061.88 (0.00) [0]
347	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (-) [3/2022]	320.66 (-) [858.96]	534.00 (538.30) [36]
348	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (-) [3/2020]	1,002.39 (-) [1,002.39]	324.69 (0.00) [-12]
349	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
	Road Transport And Highways				
350	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [9/2019]	417.19 (-) [417.19]	173.51 (0.00) [-]
351	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [1/2020]	829.97 (-) [829.97]	74.67 (0.00) [-]
352	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [8/2020]	1,958.88 (-) [1,958.88]	933.00 (0.00) [2]
353	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,659.71 (0.00) [0]
354	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [12/2019]	364.56 (-) [364.56]	56.16 (0.00) [-]
355	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
356	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [0/0]	1,437.64 (-) [1,437.64]	0.00 (0.00) [0]
357	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [0/0]	2,702.05 (-) [2,702.05]	0.00 (0.00) [0]
358	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [8/2019]	998.18 (-) [998.18]	263.46 (0.00) [-]
359	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [9/2019]	723.64 (-) [723.64]	174.10 (0.00) [-]
360	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [10/2019]	834.64 (-) [834.64]	81.26 (0.00) [-]
361	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [8/2019]	763.08 (-) [763.08]	207.06 (0.00) [-]
362	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,187.21 (0.00) [0]
363	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
364	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [12/2018]	953.88 (-) [953.88]	976.79 (0.00) [0]

365	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,052.21]	0.00 (0.00) [-]
366	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [1/2021]	1,251.11 (-) [1,251.11]	842.34 (0.00) [-]
367	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [3/2019]	425.60 (-) [425.60]	0.00 (0.00) [0]
368	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	346.60 (0.00) [0]
	<u>Urban Development</u>				
369	CONSTRUCTION OF CAMPUS AND BUILDING FOR NIPER AT GANDHINAGAR, GUJARAT	1/2013	/ (-) [0/0]	175.00 (-) [175.00]	1.83 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
370	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (-) [11/2019]	215.92 (-) [215.92]	67.89 (0.00) [0]
	<u>Health And Family Welfare</u>				
371	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [0/0]	505.58 (-) [523.00]	508.29 (17.42) [0]
	<u>Petroleum</u>				
372	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (-) [1/2021]	909.00 (-) [909.00]	9.93 (0.00) [0]
373	BS-VI PROJECT AT PANIPAT REFINERY	12/2017	7/2019 (-) [7/2019]	3,529.00 (-) [3,529.00]	1,238.56 (0.00) [0]
374	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (-) [2/2020]	206.63 (-) [206.63]	5.53 (0.00) [0]
375	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	11/2020 (-) [11/2020]	255.00 (-) [255.00]	47.50 (0.00) [0]
376	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (-) [2/2020]	598.00 (-) [598.00]	13.67 (0.00) [0]
377	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (-) [8/2020]	1,636.00 (-) [1,636.00]	144.71 (0.00) [0]
378	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (-) [8/2020]	286.42 (-) [286.42]	0.00 (0.00) [0]
	<u>Railways</u>				
379	HISSAR-SIRSA VIA AGROHA AND FATEHABAD	4/2013	/ (-) [0/0]	400.00 (-) [400.00]	0.00 (0.00) [0]
380	JIND-SONEPAT (NL),NR	1/2004	3/2012 (-) [0/0]	238.56 (-) [740.00]	722.65 (501.44) [0]
381	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [3/2020]	346.32 (-) [300.00]	286.56 (-46.32) [12]
382	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [0/0]	287.00 (-) [625.00]	4.38 (338.00) [0]
	<u>Road Transport And Highways</u>				

383	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [4/2019]	602.95 (-) [602.95]	417.86 (0.00) [34]
384	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [4/2019]	574.28 (-) [574.28]	436.21 (0.00) [9]
385	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL	3/2017	3/2020 (-) [6/2019]	639.79 (-) [552.90]	476.34 (-86.89) [-9]
386	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [4/2019]	2,128.72 (-) [2,128.72]	970.58 (0.00) [0]
387	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	1/2017	3/2019 (-) [5/2019]	276.01 (-) [276.01]	155.40 (0.00) [2]
388	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [9/2019]	247.25 (-) [247.25]	139.32 (0.00) [6]
389	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	8/2016	5/2019 (-) [8/2019]	248.97 (-) [248.97]	225.48 (0.00) [3]
390	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (-) [0/0]	1,484.30 (-) [1,484.30]	0.00 (0.00) [0]
391	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211	9/2016	5/2019 (-) [5/2019]	1,004.67 (-) [1,004.67]	0.00 (0.00) [0]
392	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [10/2018]	486.00 (-) [486.00]	470.00 (0.00) [0]
393	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -2	11/2015	5/2018 (-) [0/0]	867.66 (-) [867.66]	502.66 (0.00) [0]
394	FOUR LANING OF HISAR - DABWALI SECTION WITH PS - PACKAGE -I	8/2015	2/2018 (-) [0/0]	723.54 (-) [723.54]	530.94 (0.00) [0]
395	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011 (-) [6/2019]	1,108.00 (-) [2,288.00]	3,965.17 (1,180.00) [91]
396	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION & STRENGTHENING OF ROHNA/HASS	3/2018	/ (-) [0/0]	551.58 (-) [551.58]	0.00 (0.00) [0]
397	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/ (-) [3/2020]	275.12 (-) [275.12]	0.00 (0.00) [-]
398	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI	3/2018	/ (-) [3/2020]	307.79 (-) [307.79]	0.00 (0.00) [-]
399	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/ (-) [0/0]	181.78 (-) [181.78]	0.00 (0.00) [0]
400	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/ (-) [3/2020]	198.05 (-) [198.05]	0.00 (0.00) [-]
401	SIX LANING & STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) I	3/2018	/ (-) [0/0]	795.50 (-) [795.50]	0.00 (0.00) [0]
402	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/ (-) [0/0]	634.70 (-) [634.70]	0.00 (0.00) [0]
	HIMACHAL PRADESH				

	Petroleum				
403	BRANCH PIPELINE OF PAJPL TO UNA	2/2016	9/2019 (-) [2/2019]	151.00 (-) [151.00]	139.69 (0.00) [0]
	Power				
404	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009 (-) [12/2021]	3,919.59 (-) [9,394.80]	7,244.66 (5,475.21) [147]
	Railways				
405	BHANUPALI-BILASPUR BERI NL	4/2008	12/2026 (-) [12/2026]	2,966.99 (-) [7,000.00]	363.94 (4,033.01) [0]
	Road Transport And Highways				
406	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019 (-) [6/2019]	273.20 (-) [273.20]	256.25 (0.00) [4]
407	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020 (-) [9/2021]	2,485.93 (-) [2,485.93]	136.69 (0.00) [15]
408	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM)	11/2013	11/2016 (-) [4/2019]	1,916.79 (-) [1,916.79]	1,948.92 (0.00) [29]
409	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [3/2019]	934.46 (-) [934.46]	384.88 (0.00) [0]
410	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [5/2021]	478.74 (-) [478.74]	0.00 (0.00) [-]
411	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [7/2020]	1,273.71 (-) [1,273.71]	0.00 (0.00) [-]
412	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [11/2019]	447.75 (-) [447.75]	162.78 (0.00) [-]
413	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [9/2020]	1,583.18 (-) [1,583.18]	234.67 (0.00) [-]
	Urban Development				
414	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 (-) [0/0]	270.83 (-) [270.83]	163.97 (0.00) [0]
	JAMMU AND KASHMIR				
	Power				
415	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [12/2023]	8,112.12 (-) [8,112.12]	1,086.32 (0.00) [44]
	Railways				
416	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [3/2021]	2,500.00 (-) [27,949.00]	17,336.24 (25,449.00) [220]
	Road Transport And Highways				
417	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [0/0]	1,471.75 (-) [1,471.75]	274.09 (0.00) [0]
418	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [12/2020]	2,168.66 (-) [2,168.66]	239.74 (0.00) [18]
419	FOUR LANING OF UDHAMPUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [10/2019]	2,136.97 (-) [2,136.97]	1,124.97 (0.00) [10]
420	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013	1,813.76	2,393.99

			(-) [0/0]	(-) [1,813.76]	(0.00) [0]
421	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,159.00]	3,986.82 (0.00) [0]
422	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [3/2019]	1,987.00 (-) [1,987.00]	2,529.39 (0.00) [0]
423	SRINAGAR TO BANIHAI	6/2011	6/2014 (-) [0/0]	1,100.70 (-) [1,100.70]	2,075.87 (0.00) [0]
424	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [7/2019]	253.44 (-) [253.44]	0.00 (0.00) [0]
425	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [8/2018]	404.17 (-) [404.17]	0.00 (0.00) [0]
426	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [11/2018]	216.00 (-) [216.00]	0.00 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
427	AMRAPALI OC(12MTY)	2/2012	3/2020 (-) [3/2020]	858.11 (-) [858.11]	185.90 (0.00) [0]
428	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	78.84 (0.00) [0]
429	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2021]	163.51 (-) [163.51]	104.04 (0.00) [120]
430	HURA - C OC (3 MTY)	10/2015	3/2022 (-) [3/2022]	359.69 (-) [359.69]	46.93 (0.00) [0]
431	KAPURIA UG(PSLW)	8/2011	4/2017 (-) [0/0]	988.35 (-) [988.35]	45.26 (0.00) [0]
432	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2021]	162.46 (-) [162.46]	89.30 (0.00) [84]
433	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [4/2018]	289.45 (-) [289.45]	228.68 (0.00) [0]
434	MAGADH OC 20 MTY (CCL)	8/2008	7/2012 (-) [3/2022]	706.40 (-) [706.40]	185.62 (0.00) [116]
435	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [4/2019]	1,230.27 (-) [1,230.27]	344.32 (0.00) [48]
436	MURAIIDH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [10/2018]	339.88 (-) [339.88]	12.08 (0.00) [0]
437	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2021]	555.52 (-) [555.52]	5.24 (0.00) [0]
438	NORTH URIMARI OCP (3.0 MTY)	12/2007	3/2012 (-) [3/2019]	179.87 (-) [179.87]	175.21 (0.00) [0]
439	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2018]	269.82 (-) [269.82]	182.72 (0.00) [0]

440	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2021]	510.85 (-) [510.85]	366.52 (0.00) [60]
441	TAPIN OCP (2.5 MTY)	8/2008	3/2012 (-) [3/2021]	264.68 (-) [264.68]	179.16 (0.00) [108]
	<u>Petroleum</u>				
442	120 TMTPA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [6/2020]	161.50 (-) [161.50]	17.78 (0.00) [0]
443	CITY GAS DISTRIBUTION (CGD) NETWORK, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	36.75 (0.00) [0]
444	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	39.19 (0.00) [0]
445	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	658.62 (910.23) [910.23]	237.35 (251.61) [-12]
446	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND)	4/2011	5/2015 (-) [0/0]	191.96 (-) [191.96]	176.28 (0.00) [0]
	<u>Power</u>				
447	NORTH KARANPURA STPP (3X660 MW)	2/2014	2/2019 (9/2021) [9/2021]	14,366.58 (-) [15,164.05]	8,617.47 (797.47) [31]
448	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,152.58 (314.04) [0]
	<u>Railways</u>				
449	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (3/2021) [12/2021]	1,724.20 (1,724.20) [1,724.20]	289.76 (0.00) [9]
450	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING	4/2010	12/2015 (12/2018) [2/2019]	309.44 (-) [525.81]	525.93 (216.37) [0]
451	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [12/2020]	348.23 (-) [348.23]	136.13 (0.00) [-3]
452	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	3/1999	/ (-) [3/2021]	1,033.07 (-) [3,020.94]	0.00 (1,987.87) [-]
453	KODERMA-TILAIYA (NL), ECR	4/2002	/ (-) [0/0]	459.91 (-) [459.91]	221.54 (0.00) [0]
454	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	4/1995	3/2016 (-) [3/2020]	1,125.89 (-) [1,988.38]	2,040.42 (862.49) [48]
455	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	/ (12/2018) [1/2020]	258.20 (-) [365.00]	224.01 (106.80) [-]
456	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (8/2018) [9/2019]	148.77 (-) [377.00]	166.55 (228.23) [33]
	<u>Road Transport And Highways</u>				
457	4 LANING OF KUTCHERY CHOWK TO BIJU PARA SECTION (FROM KM 0.00 TO KM.34.00)	3/2017	3/2020 (-) [6/2019]	239.68 (-) [235.90]	84.03 (-3.78) [-9]
458	4 LANING OF PISKA MORE TO PALMA SECTION(FROM KM 2.9 TO KM 26.00)	3/2017	3/2020 (-) [6/2019]	165.50 (-) [172.16]	45.34 (6.66) [-9]

459	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (-) [0/0]	1,005.08 (-) [1,005.08]	0.00 (0.00) [0]
460	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	2/2016	3/2019 (-) [3/2019]	997.15 (-) [997.15]	392.99 (0.00) [0]
461	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [273.46]	0.00 (0.00) [0]
462	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [8/2019]	323.72 (-) [323.72]	77.31 (0.00) [12]
463	RANCHI-RARGA-JAMSETHPUR	12/2012	6/2015 (-) [0/0]	1,479.00 (-) [1,479.00]	740.26 (0.00) [0]
464	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	0.00 (0.00) [0]
465	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [12/2019]	458.03 (-) [458.03]	59.62 (0.00) [-]
	<u>Steel</u>				
466	EXPANSION OF GUA ORE MINES WITH BENEFICIATION FACILITIES AND INSTALLATION OF PELLET PLANT	2/2014	9/2017 (-) [0/0]	4,749.00 (-) [4,749.00]	109.06 (0.00) [0]
467	MODERNISATION OF STEEL MELTING SHOP NO.1 AT BOKARO STEEL PLANT	5/2015	12/2017 (-) [6/2019]	1,154.18 (-) [1,154.18]	910.60 (0.00) [18]
468	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (-) [6/2020]	1,034.01 (-) [1,034.01]	423.33 (0.00) [32]
469	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (-) [6/2020]	262.87 (-) [262.87]	84.26 (0.00) [12]
	<u>Urban Development</u>				
470	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [9/2020]	171.86 (-) [171.86]	73.90 (0.00) [54]
471	CONSTRUCTION OF ROAD AND BRIDGE IN GIRIDHI, KODERMA, HAZARIBAG, RAMGARH AND CHATRA DISTRICT	12/2007	3/2018 (-) [0/0]	200.00 (-) [200.00]	131.15 (0.00) [0]
472	CONSTRUCTION OF ROAD AND BRIDGE UNDER PMGSY	4/2013	4/2018 (-) [0/0]	170.00 (-) [170.00]	88.91 (0.00) [0]
473	CONSTRUCTION OF RURAL ROAD DEVELOPMENT AUTHORITY UNDER PHASE-XII	2/2014	12/2016 (-) [0/0]	787.29 (-) [787.29]	285.30 (0.00) [0]
474	CONSTRUCTION OF RURAL ROADS WITH FIVE YEAR MAINTAINANCE UNDER PMGSY-JHARKHAND	12/2007	6/2016 (-) [0/0]	253.92 (253.92) [253.92]	193.97 (0.00) [0]
	<u>KARNATAKA</u>				
	<u>Petroleum</u>				
475	BSVI UPGRADATION	9/2016	12/2019 (-) [2/2020]	1,810.00 (1,810.00) [1,810.00]	176.25 (0.00) [2]
476	CAPACITY ENHANCEMENT/ REVAMP OF NHT-2/PLATFORMER-2/CCR-2/PSA-2/RSU	5/2015	4/2019 (-) [4/2019]	224.00 (207.00) [207.25]	99.99 (-16.75) [0]
477	GAIL GAS LTD BENGALURU CGD PROJECT	2/2015	2/2020 (-) [2/2020]	749.00 (-) [842.00]	860.14 (93.00) [0]

478	RAILWAY SIDING PROJECT FOR EVACUATION OF PETCOKE	10/2015	3/2019 (-) [5/2019]	135.00 (171.00) [170.70]	132.43 (35.70) [2]
479	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [3/2021]	206.26 (-) [206.26]	0.00 (0.00) [0]
480	SEA WATER DESALINATION PLANT	11/2017	3/2020 (-) [3/2020]	581.00 (-) [581.00]	0.00 (0.00) [0]
481	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR	1/2006	1/2012 (-) [0/0]	993.00 (-) [1,693.00]	1,549.85 (700.00) [0]
	<u>Power</u>				
482	KUDGI STPP STAGE 1	1/2012	1/2017 (-) [0/0]	15,166.19 (-) [16,934.65]	15,364.00 (1,768.46) [0]
483	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (12/2019) [9/2019]	445.89 (445.89) [445.89]	258.66 (0.00) [7]
	<u>Railways</u>				
484	ARSIKERE-TUMKUR	3/2015	3/2020 (3/2020) [3/2020]	578.00 (578.00) [578.00]	498.04 (0.00) [0]
485	BAGALKOT-KUDACHI NL	4/2010	3/2016 (12/2023) [12/2023]	986.30 (986.30) [986.30]	295.49 (0.00) [93]
486	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (3/2024) [3/2024]	1,382.78 (1,382.78) [1,382.78]	7.35 (0.00) [264]
487	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (12/2023) [12/2023]	327.25 (367.77) [367.77]	0.31 (40.52) [-]
488	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (12/2023) [12/2023]	558.00 (692.43) [692.43]	0.00 (134.43) [-]
489	GADAG-WADI NL	4/2013	12/2018 (12/2024) [12/2024]	2,841.84 (2,841.84) [2,841.84]	92.75 (0.00) [72]
490	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [3/2023]	2,127.00 (-) [2,900.00]	1,390.53 (773.00) [0]
491	HUBLI- CHIKJAJUR	3/2015	3/2020 (3/2020) [3/2021]	1,156.94 (1,140.93) [1,140.93]	754.97 (-16.01) [12]
492	HUBLI-ANKOLA(NL),SWR	4/1997	/ (-) [12/2024]	2,315.00 (-) [2,135.00]	144.75 (-180.00) [-]
493	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2020]	644.78 (889.52) [889.52]	438.16 (244.74) [36]
494	MARIKUPPAM - KUPPAM	4/2012	3/2016 (12/2023) [12/2023]	279.54 (279.54) [279.54]	26.28 (0.00) [93]
495	MUNIRABAD (GINGERA) -RAICHUR NL	4/2007	/ (-) [12/2023]	179.65 (1,350.91) [1,350.91]	892.53 (1,171.26) [-]
496	SHIMOGA-HARIHAR NL	4/2011	3/2016 (3/2024) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
497	TORANAGALLU-RANJITPURA DL	4/2011	/ (12/2023)	146.75 (167.50)	0.34 (20.75)

			[12/2023]	[167.50]	[-]
498	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/	1,801.01	42.34
			(12/2023)	(1,801.01)	(0.00)
			[12/2023]	[1,801.01]	[-]
499	WHITE FIELD-KOLAR NL	4/2011	/	348.85	0.36
			(12/2023)	(348.85)	(0.00)
			[12/2023]	[348.85]	[-]
	Road Transport And Highways				
500	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019	1,167.42	237.03
			(-)	(-)	(0.00)
			[3/2019]	[1,167.42]	[0]
501	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/	486.78	0.00
			(-)	(-)	(0.00)
			[0/0]	[486.78]	[0]
502	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016	1,655.01	1,515.16
			(-)	(-)	(0.00)
			[12/2020]	[1,655.01]	[52]
503	4-LANING OF HOSKOTE-DOBBASPET	5/2014	/	720.69	99.03
			(-)	(-)	(0.00)
			[0/0]	[720.69]	[0]
504	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019	701.40	29.48
			(-)	(-)	(0.00)
			[11/2020]	[701.40]	[20]
505	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019	870.00	12.95
			(-)	(-)	(0.00)
			[11/2020]	[870.00]	[20]
506	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018	1,388.00	1,040.75
			(-)	(-)	(0.00)
			[11/2019]	[1,388.00]	[15]
507	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020	1,664.20	500.79
			(-)	(-)	(0.00)
			[4/2020]	[1,664.20]	[0]
508	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018	946.00	818.53
			(-)	(-)	(0.00)
			[4/2019]	[946.00]	[10]
509	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB	1/1991	1/2018	219.40	0.00
			(-)	(-)	(0.00)
			[0/0]	[219.40]	[0]
510	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020	993.16	515.09
			(-)	(-)	(440.84)
			[6/2020]	[1,434.00]	[3]
511	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020	831.58	440.28
			(-)	(-)	(345.42)
			[7/2020]	[1,177.00]	[4]
512	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/	2,177.80	0.00
			(-)	(-)	(0.00)
			[0/0]	[2,177.80]	[0]
513	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/	1,995.34	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,995.34]	[0]
514	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015	165.67	0.00
			(-)	(-)	(0.00)
			[0/0]	[165.67]	[0]
515	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU	3/2015	11/2015	159.12	0.00
			(-)	(-)	(0.00)
			[0/0]	[159.12]	[0]
516	TWO LANE WITH PAVED SHOULDERS OF BIJAPUR - GULBARGA - HOMNABAD - SECTION OF NH-218 (NEW NH NO -50)	5/2015	9/2017	709.00	419.34
			(-)	(-)	(0.00)
			[5/2019]	[709.00]	[20]
517	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-	9/2016	8/2019	950.69	720.79
			(-)	(-)	(0.00)

	209(EXISTING CHAINAGE FROM		[12/2020]	[950.69]	[16]
	<u>Urban Development</u>				
518	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2020]	26,405.14 (-) [26,405.14]	499.85 (0.00) [13]
519	CONSTRUCTION OF MEDICAL COLLEGE AND HOSPITAL AT GULBARGA	5/2005	2/2014 (-) [0/0]	768.88 (1,070.97) [1,113.34]	1,085.64 (344.46) [0]
520	CONSTRUCTION OF PARAMEDICAL AND ALLIED HEALTH INSTITUTE AT GULBARGA	7/2011	12/2015 (-) [0/0]	324.87 (324.87) [324.87]	262.93 (0.00) [0]
521	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (9/2020) [9/2020]	246.31 (-) [246.31]	51.14 (0.00) [7]
	<u>KERALA</u>				
	<u>Petroleum</u>				
522	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [6/2019]	1,112.00 (-) [1,112.00]	108.79 (0.00) [0]
523	LPG TERMINAL AT KOCHI	10/2015	10/2017 (-) [3/2019]	607.06 (714.25) [714.25]	354.58 (107.19) [0]
524	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY	2/2016	2/2020 (10/2020) [10/2020]	3,313.00 (3,288.96) [3,288.96]	718.31 (-24.04) [8]
525	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [11/2019]	4,588.29 (5,245.96) [5,245.96]	2,868.71 (657.67) [15]
526	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	12.63 (0.00) [0]
	<u>Railways</u>				
527	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/ (-) [0/0]	1,566.00 (-) [2,815.62]	254.53 (1,249.62) [0]
528	CHENGANNUR-CHINGAVANAM	4/2006	/ (-) [0/0]	191.72 (-) [369.83]	432.50 (178.11) [0]
529	ERNAKULAM-KUMBALAM	4/2010	/ (-) [0/0]	189.24 (-) [189.24]	6.70 (0.00) [0]
530	KUMBALAM-TURAVUR	4/2011	/ (-) [0/0]	252.96 (-) [252.96]	8.50 (0.00) [0]
531	MULANTURUTTI - KURUPPANTARA (24 KM) DOUBLING.	2/2005	3/2014 (-) [0/0]	241.00 (-) [241.00]	294.63 (0.00) [0]
532	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016 (-) [0/0]	550.00 (-) [550.00]	0.00 (0.00) [0]
533	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/ (-) [0/0]	1,431.90 (-) [1,431.90]	23.84 (0.00) [0]
534	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/ (-) [0/0]	1,000.00 (-) [828.50]	0.08 (-171.50) [0]
	<u>Road Transport And Highways</u>				
535	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/ (-) [10/2019]	845.24 (-) [845.24]	758.13 (0.00) [-]
536	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL	4/2016	6/2018	804.97	341.74

	NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T		(-) [12/2019]	(-) [804.97]	(0.00) [18]
537	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017 (-) [6/2020]	1,124.11 (-) [1,124.11]	157.94 (0.00) [33]
538	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/ (-) [0/0]	1,424.77 (-) [1,424.77]	0.00 (0.00) [0]
539	CONSTRUCTION OF 13.0 KM 2 LANE WITH PAVED SHOULDERS KOLLAM BYPASS ON NH47 (NEW NH 66) FROM KM 486/50	1/2014	11/2017 (-) [0/0]	267.16 (352.00) [352.05]	201.35 (84.89) [0]
540	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017 (-) [0/0]	255.75 (348.00) [348.43]	231.56 (92.68) [0]
541	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012 (-) [12/2019]	617.00 (-) [617.00]	943.17 (0.00) [88]
	<u>Shipping And Ports</u>				
542	INTERNATIONAL SHIP REPAIR FACILITY PROJECT AT COCHIN PORT TRUST PREMISES	5/2016	5/2020 (-) [5/2020]	970.00 (-) [970.00]	272.73 (0.00) [0]
543	NEW LARGE DRY DOCK AT COCHIN SHIPYARD LIMITED PREMISES AT KOCHI KERALA	7/2016	5/2021 (-) [5/2021]	1,799.00 (-) [1,799.00]	297.60 (0.00) [0]
	<u>Urban Development</u>				
544	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST	9/2017	3/2020 (-) [3/2020]	150.29 (-) [150.29]	2.58 (0.00) [0]
545	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-) [3/2020]	165.23 (-) [165.23]	77.70 (0.00) [89]
546	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (-) [12/2019]	5,181.79 (-) [5,687.79]	5,188.50 (506.00) [29]
	<u>MADHYA PRADESH</u>				
	<u>Coal</u>				
547	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2021]	869.44 (-) [869.44]	112.35 (0.00) [0]
548	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2023]	481.60 (-) [481.60]	0.00 (0.00) [0]
549	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2022]	231.92 (-) [231.92]	0.00 (0.00) [0]
550	BATURA OCP (2.0 MTY)	8/2015	3/2023 (-) [3/2021]	1,186.64 (-) [203.82]	117.55 (-982.82) [-24]
551	COAL PROJECT NAME JAMUNIA UG (0.84 MTY)	7/2016	3/2022 (-) [3/2022]	409.87 (-) [409.87]	18.23 (0.00) [0]
552	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2022]	1,255.17 (-) [1,255.17]	94.84 (0.00) [0]
553	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2021]	1,783.09 (-) [1,783.09]	250.33 (0.00) [0]
554	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2021]	371.04 (-) [371.04]	47.54 (0.00) [0]
555	MALACHUA OPENCAST PROJECT	10/2015	3/2023	488.33	24.29

			(-) [3/2023]	(-) [488.33]	(0.00) [0]
556	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (-) [3/2021]	357.80 (-) [357.80]	115.40 (0.00) [0]
	<u>Petroleum</u>				
557	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (-) [8/2020]	236.00 (-) [236.00]	16.55 (0.00) [2]
	<u>Power</u>				
558	AMELIA COAL MINE	1/2017	9/2020 (-) [9/2020]	2,104.21 (1,587.16) [1,587.16]	296.17 (-517.05) [0]
559	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	3/2013	9/2017 (3/2020) [3/2020]	11,638.55 (-) [12,865.92]	11,086.44 (1,227.37) [30]
560	KHARGONE STPP STAGE I (1320 MW)	3/2015	9/2019 (1/2020) [1/2020]	9,870.51 (-) [11,148.86]	7,697.03 (1,278.35) [4]
	<u>Railways</u>				
561	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2021]	1,370.00 (-) [1,370.00]	101.00 (0.00) [0]
562	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2020]	1,485.85 (-) [1,485.85]	960.26 (0.00) [0]
563	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (-) [0/0]	383.79 (-) [1,101.16]	194.91 (717.37) [0]
564	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (-) [0/0]	585.93 (-) [1,420.39]	104.10 (834.46) [0]
565	CHHINDWARA-MANDLA FORT GC	3/2011	3/2012 (-) [3/2020]	556.54 (-) [1,342.46]	396.00 (785.92) [96]
566	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (-) [6/2020]	700.00 (-) [700.00]	47.80 (0.00) [0]
567	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [10/2021]	1,763.93 (-) [1,763.93]	0.00 (0.00) [19]
568	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2022]	582.13 (-) [1,260.61]	0.00 (678.48) [0]
569	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2022]	2,478.23 (-) [2,478.23]	112.07 (0.00) [0]
570	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-) [2/2020]	174.00 (-) [174.00]	148.20 (0.00) [11]
571	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (-) [3/2021]	424.60 (-) [2,713.09]	898.83 (2,288.49) [0]
572	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (-) [3/2022]	3,503.69 (-) [1,030.29]	1,195.16 (-2,473.40) [0]
	<u>Road Transport And Highways</u>				
573	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	3/2018	11/2019 (-) [11/2019]	191.21 (-) [191.21]	0.00 (0.00) [0]
574	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018	249.05	0.00

			(-) [1/2020]	(-) [249.05]	(0.00) [18]
575	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/	950.27	0.00
			(-) [0/0]	(-) [950.27]	(0.00) [0]
576	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019	227.49	104.96
			(-) [3/2019]	(-) [227.49]	(0.00) [0]
577	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017	374.40	0.00
			(-) [0/0]	(-) [374.40]	(0.00) [0]
578	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017	990.61	0.00
			(-) [0/0]	(-) [990.61]	(0.00) [0]
579	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP	8/2015	/	257.80	12.38
			(-) [0/0]	(-) [257.00]	(-0.80) [0]
580	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/	390.51	43.25
			(-) [0/0]	(-) [390.51]	(0.00) [0]
581	BELA(RIWA)-MP/UP BORDER (4L) OF NH-7 IN MP	11/2011	2/2015	670.82	590.00
			(-) [0/0]	(-) [670.82]	(0.00) [0]
582	BHOPAL-BIORA (4L) OF NH-12 IN MP	11/2011	5/2015	704.26	5.21
			(-) [0/0]	(-) [704.26]	(0.00) [0]
583	BIORA-RAJASTHAN BORDER (2L) OF NH-12EXT IN MP	3/2013	2/2016	257.80	59.30
			(-) [0/0]	(-) [257.80]	(0.00) [0]
584	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017	205.05	0.00
			(-) [4/2019]	(-) [205.05]	(0.00) [25]
585	FOUR LANING OF BIAORA –DEWAS SECTION OF NH-3 FROM KM 426.100 TO KM 566.450 IN THE STATE OF MADHYA PR	6/2015	1/2019	1,583.79	1,568.11
			(-) [6/2019]	(-) [1,583.79]	(0.00) [5]
586	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	1/2018	/	960.24	0.00
			(-) [8/2020]	(-) [960.24]	(0.00) [-]
587	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016	1,012.90	439.07
			(-) [0/0]	(-) [1,012.90]	(0.00) [0]
588	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015	1,055.00	1,393.40
			(-) [12/2018]	(-) [1,601.77]	(546.77) [0]
589	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/	928.83	540.03
			(-) [3/2019]	(-) [928.83]	(0.00) [0]
590	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/	794.30	442.07
			(-) [5/2019]	(-) [794.30]	(0.00) [-]
591	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/	795.76	504.40
			(-) [3/2019]	(-) [795.76]	(0.00) [0]
592	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/	810.22	516.64
			(-) [6/2019]	(-) [810.22]	(0.00) [-]
593	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017	639.97	239.96
			(-) [1/2020]	(-) [639.97]	(0.00) [27]
594	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER FROM KM 66.00 TO KM 130.00 SECTION OF NH-12	1/2018	/	770.73	0.00
			(-)	(-)	(0.00)

	UNDE		[0/0]	[770.73]	[0]
595	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	6/2018 (-) [0/0]	927.54 (-) [927.54]	29.17 (0.00) [0]
596	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870	11/2013	5/2017 (-) [0/0]	497.05 (-) [497.05]	0.00 (0.00) [0]
597	INDORE-DEWAS(NH-3)	11/2010	5/2013 (-) [0/0]	325.00 (-) [325.00]	469.54 (0.00) [0]
598	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013 (-) [0/0]	1,175.00 (-) [1,175.00]	1,342.77 (0.00) [0]
599	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	3/2018 (-) [0/0]	628.45 (-) [628.45]	20.74 (0.00) [0]
600	JABALPUR-BARELA SECTION OF NH-12A IN MADHYA PRADESH KM 477/6 OF NH-7 TO KM 22/8 OF NH-12A	2/2015	5/2017 (-) [0/0]	327.32 (-) [327.32]	142.73 (0.00) [0]
601	KATNI TO UMARIYA SECTION OF NH-78 IN MADYA PRADESH KM 0 TO 68/4	2/2015	7/2017 (-) [0/0]	377.83 (-) [377.83]	57.42 (0.00) [0]
602	MANDLA-CHILPI SECTION OF NH-12A IN MADHYA PRADESH KM 89/6 TO KM 192/4 OF NH-12A	6/2015	12/2017 (-) [0/0]	641.02 (-) [641.02]	89.88 (0.00) [0]
603	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015 (-) [0/0]	381.86 (-) [381.86]	252.03 (0.00) [0]
604	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018 (-) [7/2020]	169.63 (-) [169.63]	0.00 (0.00) [28]
605	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	9/2016	1/2019 (-) [1/2019]	287.34 (-) [287.34]	0.00 (0.00) [0]
606	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019 (-) [11/2019]	877.79 (-) [877.79]	0.00 (0.00) [5]
607	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	2/2018 (-) [11/2019]	235.91 (-) [235.91]	0.00 (0.00) [21]
608	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018 (-) [6/2020]	809.16 (-) [809.16]	0.00 (0.00) [23]
609	SATANA-BELA SECTION OF NH-75(4L) IN MP	1/2012	8/2015 (-) [0/0]	320.48 (-) [320.48]	189.49 (0.00) [0]
610	SHAH DOL TO ANUPPUR-MP/CHATTISGARH BORDER SECTION OF NH-78 IN MADYA PRADESH KM 142/200 TO 245/0	6/2015	5/2017 (-) [0/0]	532.49 (-) [532.49]	137.08 (0.00) [0]
611	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP	11/2011	9/2015 (-) [0/0]	871.15 (-) [871.15]	332.25 (0.00) [0]
612	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017 (-) [0/0]	511.83 (-) [511.83]	40.87 (0.00) [0]
613	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2019]	254.17 (-) [254.17]	0.00 (0.00) [21]
614	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2019]	233.04 (-) [233.04]	0.00 (0.00) [20]

615	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (-) [4/2020]	279.44 (-) [279.44]	0.00 (0.00) [25]
616	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	166.21 (-) [166.21]	0.00 (0.00) [22]
617	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (-) [11/2020]	184.62 (-) [184.62]	0.00 (0.00) [33]
618	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (-) [11/2020]	214.69 (-) [214.69]	0.00 (0.00) [32]
619	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (-) [6/2020]	217.22 (-) [217.22]	0.00 (0.00) [22]
620	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (-) [12/2019]	162.56 (-) [162.56]	0.00 (0.00) [21]
621	WIDENING TO 2 LANE WITH PAVED SHOULDER AND STRENGTHENING FROM KM 88 TO 130 ON NH-86	3/2014	2/2015 (-) [2/2015]	170.00 (-) [170.00]	0.00 (0.00) [0]
622	WIDENING TO 2-LANE+PS WITH RECONSTRUCTION OF BRIDGES & CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (-) [9/2019]	373.82 (-) [373.82]	0.00 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Coal</u>				
623	ADASA UG TO OC	8/2015	3/2023 (3/2024) [3/2024]	288.90 (333.43) [333.43]	0.07 (44.53) [12]
624	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [0/0]	198.68 (-) [198.68]	254.72 (0.00) [0]
625	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (-) [483.69]	165.09 (0.00) [0]
626	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (-) [727.28]	239.42 (0.00) [0]
627	BHANEGAON OC	2/2015	3/2023 (2/2017) [3/2023]	187.94 (409.68) [409.68]	101.05 (221.74) [0]
628	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2019]	304.52 (-) [304.52]	130.28 (0.00) [0]
629	DINESH OCP	11/2014	3/2020 (-) [3/2020]	611.16 (-) [611.16]	409.85 (0.00) [0]
630	GOKUL	11/2014	3/2018 (-) [3/2018]	267.67 (-) [267.67]	208.29 (0.00) [0]
631	KAMPTTEE DEEP OC MINE	11/2015	3/2021 (9/2018) [3/2024]	277.65 (313.34) [313.34]	37.51 (35.69) [36]
632	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (-) [3/2020]	362.73 (-) [362.73]	279.61 (0.00) [0]
633	MAKARDHOKRA I OC	9/2014	3/2021 (-) [3/2021]	266.23 (-) [266.23]	144.38 (0.00) [0]
634	MUNGOLI NIORGUDA EXTENSION (DEEP) OC MINE	11/2015	3/2020 (-)	498.42 (-)	138.73 (0.00)

			[3/2020]	[498.42]	[0]
635	NEW MAJRI UG TO OC	5/2015	3/2019 (-) [3/2019]	295.56 (-) [295.56]	115.83 (0.00) [0]
636	PENGANGA OCP(REVISED)	9/2014	3/2020 (-) [3/2020]	441.82 (-) [441.82]	206.72 (0.00) [0]
637	SINGHORI OC MINE	6/2015	3/2020 (-) [3/2020]	205.49 (-) [205.49]	112.45 (0.00) [0]
	<u>Fertilisers</u>				
638	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (-) [4/2020]	426.72 (-) [426.72]	70.98 (0.00) [0]
639	NEW SEWAGE TREATMENT PLANT PACKAGE, RCF TROMBAY	10/2014	11/2016 (4/2019) [5/2019]	197.79 (209.44) [209.44]	161.24 (11.65) [30]
	<u>Health And Family Welfare</u>				
640	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	/ (-) [2/2020]	582.99 (-) [582.99]	61.17 (0.00) [-]
641	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASHTRA	8/2017	3/2019 (-) [0/0]	274.19 (-) [274.19]	125.36 (0.00) [0]
	<u>Petroleum</u>				
642	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [6/2020]	249.26 (-) [249.26]	58.33 (0.00) [0]
643	4TH PHASE DEVELOPMENT OF NBP FIELD	2/2017	11/2019 (11/2019) [11/2019]	968.61 (968.61) [968.61]	815.29 (0.00) [0]
644	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [1/2021]	261.00 (-) [261.00]	20.36 (0.00) [0]
645	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [4/2021]	212.00 (-) [212.00]	20.65 (0.00) [3]
646	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [10/2021]	348.00 (-) [348.00]	14.73 (0.00) [9]
647	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (3/2019) [12/2019]	861.79 (1,577.15) [1,577.15]	1,240.37 (715.36) [79]
648	DEVELOPMENT OF B-147 FIELD	2/2017	11/2019 (11/2019) [11/2019]	546.15 (546.15) [546.15]	366.12 (0.00) [0]
649	DEVELOPMENT OF BSE-11 BLOCK	2/2017	11/2019 (11/2019) [11/2019]	511.30 (511.30) [511.30]	358.81 (0.00) [0]
650	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,006.83) [4,006.83]	2,354.21 (0.00) [0]
651	ENHANCED RECOVERY FROM BASSEIN FIELD THROUGH INTEGRATED DEVELOPMENT OF MUKTA, BASSEIN AND PANNA	1/2015	12/2017 (3/2020) [3/2020]	4,619.94 (4,619.94) [4,619.94]	4,255.37 (0.00) [27]
652	INSTALLATION OF GASOLINE HYDRO TREATMENT UNIT TO PRODUCE 100% BSVI MS AT MUMBAI REFINERY	2/2016	2/2020 (-) [2/2020]	554.00 (-) [554.00]	260.09 (0.00) [0]
653	INTEGRATED DEVELOPMENT OF B-127 FIELDS	12/2011	3/2015 (12/2019) [12/2019]	2,059.63 (2,665.65) [2,665.65]	1,906.55 (606.02) [57]

654	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	8/2021 (-) [8/2021]	1,945.00 (-) [1,945.00]	834.52 (0.00) [0]
655	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2020) [5/2020]	3,190.69 (-) [3,247.19]	2,167.85 (56.50) [25]
656	MMPL PIPELINE REROUTING PROJECT	4/2013	12/2019 (-) [12/2019]	449.58 (-) [449.58]	142.34 (0.00) [0]
657	MUMBAI HIGH SOUTH (MHS) REDEVELOPMENT PHASE-III	11/2014	4/2019 (12/2019) [12/2019]	6,068.80 (6,068.80) [5,296.93]	4,731.48 (-771.87) [8]
658	MUMBAI REFINERY EXPANSION PROJECT	9/2015	3/2020 (-) [7/2019]	4,199.00 (-) [4,199.00]	194.97 (0.00) [-8]
659	NEELAM REDEVELOPMENT PLAN FOR EXPLOITATION OF BASSEIN AND MUKTA PAY	8/2015	3/2019 (5/2020) [5/2020]	2,818.88 (-) [2,818.88]	2,073.56 (0.00) [14]
660	NW B-173A DEVELOPMENT PLAN FOR EXPLOITATION OF MUKTA PAY	1/2017	5/2019 (5/2019) [5/2019]	474.15 (474.15) [474.15]	346.77 (0.00) [0]
661	PIPELINE REPLACEMENT PROJECT-V (OFFSHORE)	4/2018	12/2019 (-) [12/2019]	766.37 (-) [766.37]	345.40 (0.00) [0]
662	PUNE POL STORAGE DEPOT	8/2016	8/2020 (-) [8/2020]	282.64 (-) [282.64]	88.28 (0.00) [0]
	<u>Power</u>				
663	MOUDA STPP STAGE 2	3/2012	9/2016 (-) [0/0]	7,921.47 (-) [7,921.47]	5,302.00 (0.00) [0]
664	SOLAPUR STPP	3/2012	11/2016 (3/2019) [3/2019]	9,395.18 (-) [9,395.18]	9,363.22 (0.00) [0]
665	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	9/2010 (4/2019) [4/2019]	477.69 (738.48) [738.48]	689.46 (260.79) [103]
	<u>Railways</u>				
666	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [3/2019]	184.06 (199.12) [298.70]	255.25 (114.64) [0]
667	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2021]	2,271.50 (2,271.50) [3,712.50]	2,075.20 (1,441.00) [0]
668	AMRAVATI-NARKHER NL(CR)	6/1994	6/1999 (-) [0/0]	663.01 (668.34) [858.96]	718.23 (195.95) [0]
669	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2020]	495.44 (1,781.98) [2,973.73]	1,362.86 (2,478.29) [192]
670	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (2,081.27) [2,081.27]	59.41 (205.27) [0]
671	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [3/2020]	713.48 (-) [1,750.00]	1,773.46 (1,036.52) [0]
672	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.22 (0.00) [-9]
673	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-)	9,968.00 (-)	0.00 (0.00)

			[3/2024]	[9,968.00]	[0]
674	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2023]	2,449.91 (2,449.91) [2,449.91]	125.72 (0.00) [0]
675	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2021]	792.89 (792.89) [792.89]	293.18 (0.00) [0]
676	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2023]	1,035.16 (1,035.16) [1,035.16]	51.24 (0.00) [12]
677	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [12/2019]	305.00 (-) [305.00]	259.28 (0.00) [9]
678	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
679	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [7,986.04]	2,423.55 (2,686.04) [0]
680	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2024]	3,627.47 (3,627.47) [3,627.47]	510.70 (0.00) [0]
681	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
682	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (-) [3/2023]	1,908.51 (-) [2,686.63]	0.00 (778.12) [0]
683	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
684	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [3/2024]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
685	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
686	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (-) [12/2021]	229.00 (-) [403.00]	36.28 (174.00) [0]
687	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2023]	637.95 (637.95) [637.95]	36.16 (0.00) [0]
688	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2022]	1,272.19 (1,272.19) [1,272.19]	231.61 (0.00) [0]
689	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (3,168.29) [3,168.29]	1,108.46 (0.00) [0]
690	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2022]	540.02 (540.02) [540.02]	195.62 (0.00) [0]
	<u>Road Transport And Highways</u>				
691	4 LANING OF AMRAVATI - CHIKHLI (PKG-I)	7/2015	5/2019 (-) [5/2019]	2,288.18 (-) [2,288.18]	0.00 (0.00) [0]
692	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [5/2019]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
693	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-)	972.50 (-)	1,485.07 (0.00)

			[12/2018]	[972.50]	[0]
694	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/	607.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[607.00]	[0]
695	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/	621.00	0.00
			(-)	(-)	(0.00)
			[4/2021]	[621.00]	[-]
696	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016	923.04	695.52
			(-)	(-)	(0.00)
			[6/2019]	[923.04]	[31]
697	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020	744.64	0.00
			(-)	(-)	(237.36)
			[3/2020]	[982.00]	[0]
698	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/	1,071.61	0.00
			(-)	(-)	(0.00)
			[7/2021]	[1,071.61]	[-]
699	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019	446.17	38.95
			(-)	(-)	(0.00)
			[11/2019]	[446.17]	[8]
700	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020	1,098.06	648.57
			(-)	(-)	(62.58)
			[8/2020]	[1,160.64]	[5]
701	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/	1,142.62	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,142.62]	[0]
702	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/	1,101.58	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,101.58]	[0]
703	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019	400.25	64.89
			(-)	(-)	(0.00)
			[9/2019]	[400.25]	[6]
704	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/	1,064.88	0.00
			(-)	(-)	(0.00)
			[7/2021]	[1,064.88]	[-]
705	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017	1,059.73	256.29
			(-)	(-)	(11.27)
			[11/2020]	[1,071.00]	[44]
706	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020	1,030.44	863.82
			(-)	(-)	(35.07)
			[5/2020]	[1,065.51]	[2]
707	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020	988.34	925.93
			(-)	(-)	(54.94)
			[8/2020]	[1,043.28]	[5]
708	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018	505.00	454.85
			(-)	(-)	(0.00)
			[4/2019]	[505.00]	[11]
709	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018	197.69	22.27
			(-)	(-)	(0.00)
			[0/0]	[197.69]	[0]
710	BALANCE WORK OF 4-LANNING FROM KM 94.000 TO KM 123.000 OF NAGPUR- HYDERABAD SECTION NS-60	3/2016	7/2018	244.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[244.00]	[0]
711	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/	1,162.92	0.00
			(-)	(-)	(0.00)
			[7/2021]	[1,162.92]	[-]
712	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019	649.50	193.70
			(-)	(-)	(0.00)
			[12/2020]	[649.50]	[21]
713	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/	291.53	5.16
			(-)	(-)	(0.00)
			[11/2020]	[291.53]	[-]

714	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [7/2019]	244.90 (-) [244.90]	189.17 (0.00) [2]
715	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [11/2020]	289.21 (-) [289.21]	5.76 (0.00) [-]
716	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (-) [4/2019]	593.26 (-) [593.26]	60.83 (0.00) [11]
717	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION	12/2011	/ (-) [0/0]	156.26 (227.00) [156.26]	65.16 (0.00) [0]
718	CONSTRUCTION OF HL BRIDGE ACROSS GADAVARI RIVER AND ITS APPROACHES FOR MISSING LINK BETWEEN SIRONCHA	3/2011	/ (-) [0/0]	185.82 (292.00) [185.82]	205.97 (0.00) [0]
719	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (-) [5/2019]	531.13 (-) [531.13]	163.10 (0.00) [12]
720	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	13.43 (0.00) [0]
721	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	57.60 (0.00) [0]
722	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [2/2020]	247.02 (-) [157.49]	0.00 (-89.53) [-1]
723	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (-) [3/2019]	414.51 (-) [414.00]	514.02 (-0.51) [0]
724	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [6/2019]	296.19 (-) [254.00]	233.60 (-42.19) [-9]
725	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
726	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [12/2020]	642.13 (-) [642.13]	47.07 (0.00) [-]
727	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [2/2019]	1,871.34 (-) [1,871.34]	3,385.90 (0.00) [0]
728	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (-) [5/2020]	904.16 (-) [904.16]	333.48 (0.00) [3]
729	NAGPUR - KONDHALI	9/2005	6/2006 (-) [0/0]	168.00 (-) [168.00]	226.24 (0.00) [0]
730	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [7/2019]	546.00 (-) [546.00]	463.21 (0.00) [0]
731	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [7/2019]	591.66 (-) [591.66]	609.09 (0.00) [0]
732	PANVEL-INDAPUR	12/2011	6/2014 (-) [6/2019]	942.69 (-) [942.69]	704.56 (0.00) [60]
733	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [6/2019]	1,724.55 (-) [1,724.55]	2,289.31 (0.00) [75]
734	REHABILATION AND UPGRADATION OF NH-222(61) FOM	12/2013	11/2016	220.72	95.02

	KM 161.570 TO 211.00		(-) [0/0]	(-) [220.72]	(0.00) [0]
735	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 284 TO 337	6/2014	11/2016 (-) [0/0]	260.39 (-) [260.39]	87.43 (0.00) [0]
736	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	87.62 (0.00) [0]
737	REHABILITATION AND AUGMENTAION OF NH-222 FROM KM 101.00 TO 161.570 UNDER NHDP-IV ON EPC MODE. JOB NO	1/2014	11/2014 (-) [0/0]	292.98 (-) [292.98]	95.60 (0.00) [0]
738	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	6.50 (0.00) [0]
739	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (-) [10/2020]	404.94 (-) [404.94]	39.25 (0.00) [-]
740	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (-) [5/2019]	290.73 (-) [290.73]	159.04 (0.00) [-]
741	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/ (-) [0/0]	289.60 (-) [289.60]	0.00 (0.00) [0]
742	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [6/2019]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [64]
	<u>Shipping And Ports</u>				
743	CONSTRUCTION OF OFFSHORE CONTAINER BERTHS AND DEVELOPMENT OF CONTAINER TERMINAL ON BOT BASIS IN MUMB	1/2007	12/2010 (-) [0/0]	366.39 (-) [669.46]	411.12 (303.07) [0]
	<u>Telecommunications</u>				
744	MADHYA PRADESH ACCESS (LOT1)	8/2017	5/2018 (5/2019) [5/2019]	215.30 (219.60) [219.60]	33.46 (4.30) [12]
745	MAHARASTRA ACCESS LOT 2 GSM PHASE VIII.4 PROJECT	1/2018	10/2018 (5/2019) [5/2019]	231.80 (240.10) [240.10]	117.63 (8.30) [7]
	<u>Urban Development</u>				
746	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [9/2020]	223.37 (-) [223.37]	24.40 (0.00) [2]
747	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	1/2015 (-) [5/2020]	23,136.00 (-) [23,136.00]	0.00 (0.00) [64]
748	NAGPUR METRO RAIL	8/2014	3/2018 (12/2019) [12/2019]	8,680.00 (8,680.00) [8,680.00]	5,632.05 (0.00) [21]
749	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (-) [11/2021]	11,420.00 (-) [11,420.00]	2,377.05 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
750	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	9,672.60 (9,354.83) [108]
	<u>Road Transport And Highways</u>				
751	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2018]	517.57 (-) [517.57]	0.00 (0.00) [0]
	<u>Urban Development</u>				
752	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015	216.69	52.00

			(-) [10/2020]	(-) [216.69]	(0.00) [67]
	MEGHALAYA				
	Health And Family Welfare				
753	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	145.51 (0.00) [16]
	Railways				
754	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [6,000.00]	260.68 (5,093.54) [0]
	Road Transport And Highways				
755	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
756	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [5/2019]	306.28 (-) [306.28]	0.00 (0.00) [0]
757	JORBAT - BARAPANI	1/2011	1/2014 (-) [5/2019]	536.00 (-) [536.00]	844.31 (0.00) [64]
758	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [6/2019]	479.20 (-) [479.20]	475.02 (0.00) [13]
759	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	Urban Development				
760	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	MIZORAM				
	Railways				
761	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,968.00]	2,671.70 (2,574.53) [81]
	Road Transport And Highways				
762	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
763	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
764	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	519.09 (-) [519.09]	0.00 (0.00) [0]
765	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
766	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
767	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
768	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
769	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]

770	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
771	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
772	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
773	DHANKASA UG (1.00 MTY)	9/2016	3/2022 (-) [3/2022]	458.07 (-) [458.07]	20.86 (0.00) [0]
774	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [3/2021]	328.00 (-) [328.00]	98.04 (0.00) [0]
775	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (-) [319.76]	58.04 (0.00) [0]
	<u>Heavy Industry</u>				
776	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	4/2011	9/2011 (-) [0/0]	1,718.00 (-) [3,827.30]	2,289.00 (2,109.30) [0]
	<u>Petroleum</u>				
777	50MW WIND ENERGY POWER PROJECT	11/2015	6/2017 (-) [0/0]	500.00 (-) [500.00]	0.00 (0.00) [0]
778	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	12/2020 (-) [12/2020]	1,823.00 (3,027.90) [3,027.90]	670.40 (1,204.90) [0]
779	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [12/2019]	571.66 (-) [571.66]	112.73 (0.00) [0]
780	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (-) [3,308.00]	192.71 (0.00) [0]
781	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	3,437.00 (-) [3,437.00]	1,177.26 (0.00) [0]
782	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	6/2007	9/2011 (-) [0/0]	736.65 (-) [571.47]	543.05 (-165.18) [0]
783	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	2,433.00 (-) [2,433.00]	1,168.02 (0.00) [0]
784	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	3/2021 (-) [3/2021]	2,677.00 (-) [2,677.00]	358.80 (0.00) [0]
785	JAIPUR-PANIPAT NAPTHA PIPELINE ALONG WITH AUGMENTATION OF KOYALI-SANGANER PRODUCT PIPELINE	2/2015	10/2019 (-) [6/2019]	890.00 (-) [887.00]	591.29 (-3.00) [-4]
786	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2019) [2/2022]	2,915.00 (3,030.00) [3,049.47]	2,112.19 (134.47) [110]
787	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (12/2020) [12/2020]	2,881.40 (-) [2,000.00]	1,162.20 (-881.40) [0]
788	MDPL CAPACITY EXPANSION AND PALANPUR VADODARA PIPELINE EXTENSION	9/2016	6/2020 (-) [6/2020]	1,879.00 (-) [1,879.00]	1,308.78 (0.00) [0]

789	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (-) [8/2020]	2,321.00 (3,338.00) [3,338.00]	1,393.27 (1,017.00) [-4]
790	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (10/2020) [10/2020]	690.00 (-) [690.00]	236.57 (0.00) [27]
791	PARADIP-RAIPUR- RANCHI PIPELINE	8/2009	12/2016 (-) [0/0]	1,793.00 (-) [1,793.00]	1,788.86 (0.00) [0]
792	PHUPLUR-HALDIA PIPELINE PROJECT PHASE-I	3/2015	12/2018 (-) [5/2019]	3,957.00 (3,561.00) [3,397.00]	2,543.54 (-560.00) [5]
793	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [10/2020]	406.00 (-) [406.00]	63.20 (0.00) [0]
794	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	7/2011	3/2017 (-) [12/2019]	352.56 (-) [438.84]	220.73 (86.28) [33]
795	URAN CHAKAN SHIKRAPUR LPG PIPELINE	12/2009	10/2014 (8/2019) [8/2019]	309.81 (723.40) [723.40]	645.53 (413.59) [58]
	<u>Power</u>				
796	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (2/2020) [2/2020]	198.49 (198.49) [198.49]	41.70 (0.00) [5]
797	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (12/2018) [12/2019]	4,754.42 (4,754.42) [9,072.36]	1,083.08 (4,317.94) [12]
798	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (5/2020) [5/2020]	358.83 (358.83) [358.83]	5.00 (0.00) [0]
799	EASTERN REGION STRENGTHENING SCHEME -IX	2/2014	2/2016 (4/2019) [5/2019]	196.58 (225.28) [225.28]	152.32 (28.70) [39]
800	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (8/2019) [8/2019]	1,364.52 (1,891.41) [1,891.41]	1,230.98 (526.89) [40]
801	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (12/2019) [12/2019]	522.29 (546.36) [546.36]	447.83 (24.07) [37]
802	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (-) [7/2020]	3,500.00 (3,500.00) [3,500.00]	1,051.50 (0.00) [0]
803	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (6/2019) [6/2019]	235.53 (235.53) [235.53]	84.89 (0.00) [0]
804	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (6/2019) [6/2019]	322.30 (322.30) [322.30]	127.38 (0.00) [4]
805	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (3/2018) [5/2019]	197.40 (-) [197.40]	74.71 (0.00) [14]
806	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D	5/2016	5/2019 (5/2019) [9/2019]	3,519.59 (3,519.59) [3,519.59]	2,215.60 (0.00) [4]
807	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (4/2020) [4/2020]	5,070.13 (5,070.13) [5,070.13]	1,773.41 (0.00) [0]
808	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (11/2019) [11/2019]	14,733.37 (14,733.37) [14,733.37]	6,580.05 (0.00) [0]

809	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (2/2020) [2/2020]	1,931.39 (1,931.39) [1,931.39]	810.69 (0.00) [0]
810	INSTALLATION OF BUS REACTORS AT CUDDAPAH NELLORE KURNOOL RAICHUR AND TIRUVALAM SUB STATION	3/2017	6/2019 (6/2019) [6/2019]	251.60 (251.60) [251.60]	167.81 (0.00) [0]
811	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2018) [12/2020]	5,111.33 (5,111.33) [6,880.36]	1,143.65 (1,769.03) [24]
812	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (3/2022) [3/2022]	11,130.19 (14,719.10) [14,719.10]	12,733.20 (3,588.91) [103]
813	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX	2/2014	6/2016 (9/2019) [5/2019]	539.82 (575.67) [575.67]	426.83 (35.85) [35]
814	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (11/2019) [11/2019]	283.72 (283.72) [283.72]	164.25 (0.00) [0]
815	SOUTHERN REGION STRENGTHENING SCHEME-XXI	9/2016	3/2019 (3/2019) [5/2019]	562.25 (562.25) [562.25]	195.50 (0.00) [2]
816	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [6/2019]	3,654.00 (-) [3,654.00]	3,130.07 (0.00) [2]
817	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (4/2019) [5/2019]	608.24 (608.24) [608.24]	388.00 (0.00) [1]
818	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (6/2019) [6/2019]	203.28 (260.03) [260.03]	188.36 (56.75) [23]
819	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (12/2019) [12/2019]	379.95 (379.85) [379.95]	28.42 (0.00) [0]
820	SYSTEM STRENGTHENING SCHEME IN NORTHERN REGION XXXVIII	3/2017	6/2019 (6/2019) [6/2019]	337.75 (337.75) [337.75]	35.50 (0.00) [0]
821	SYSTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (9/2019) [9/2019]	487.49 (639.46) [639.46]	518.50 (151.97) [63]
822	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (12/2019) [12/2019]	4,824.12 (5,071.94) [5,071.94]	4,554.87 (247.82) [86]
823	TRANSMISSION SYSTEM ASSOCIATED WITH KISHANGANAGA HEP	1/2015	3/2018 (3/2019) [5/2019]	268.80 (340.88) [340.88]	248.10 (72.08) [14]
824	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (9/2019) [9/2019]	871.62 (871.62) [871.62]	496.12 (0.00) [23]
825	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (9/2019) [9/2019]	408.46 (408.46) [408.46]	221.54 (0.00) [8]
826	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (12/2019) [12/2019]	5,151.37 (5,151.37) [5,151.37]	3,063.80 (0.00) [21]
827	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (12/2019) [12/2019]	808.63 (808.63) [808.63]	458.26 (0.00) [23]
828	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [6/2019]	374.63 (374.63) [374.63]	187.24 (0.00) [38]
829	WESTERN REGION STRENGTHENING SCHEME XVIII	2/2017	2/2020	195.05	109.10

			(2/2020) [2/2020]	(195.05) [195.05]	(0.00) [0]
	<u>Railways</u>				
830	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (12/2023) [12/2023]	1,08,000.00 (-) [1,08,000.00]	2,568.77 (0.00) [0]
831	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH	4/2010	/ (-) [0/0]	338.54 (-) [338.54]	212.64 (0.00) [0]
832	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [0/0]	288.35 (-) [238.36]	273.54 (-49.99) [0]
833	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [0/0]	450.55 (-) [250.55]	19.82 (-200.00) [0]
834	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (3/2020) [3/2020]	704.31 (704.31) [704.31]	139.69 (0.00) [0]
835	BHADRACHALAM-KOVVUR	4/2012	/ (-) [0/0]	923.23 (-) [1,787.00]	2.46 (863.77) [0]
836	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [0/0]	175.80 (-) [173.91]	139.80 (-1.89) [0]
837	CALICUT-MANGALORE (DL) (SR)	2/1996	/ (-) [0/0]	240.00 (-) [579.37]	537.30 (339.37) [0]
838	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.00]	229.95 (1,211.86) [0]
839	CHANDIGARH-BADDI NL	4/2007	/ (-) [0/0]	328.14 (-) [1,540.00]	45.20 (1,211.86) [0]
840	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [0/0]	337.96 (-) [355.44]	72.84 (17.48) [0]
841	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [0/0]	523.52 (-) [2,350.00]	2.27 (1,826.48) [0]
842	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [1/2020]	295.00 (-) [477.31]	217.90 (182.31) [12]
843	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [0/0]	243.78 (-) [895.00]	104.79 (651.22) [0]
844	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [5/2010]	595.51 (-) [538.37]	110.00 (-57.14) [0]
845	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (-) [3/2022]	1,347.26 (-) [1,347.26]	679.79 (0.00) [0]
846	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (-) [3/2022]	1,640.04 (-) [1,640.04]	645.15 (0.00) [0]
847	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [0/0]	365.17 (-) [296.43]	118.48 (-68.74) [0]
848	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR	4/2013	/ (-) [0/0]	1,239.00 (-) [1,239.00]	0.00 (0.00) [0]
849	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/	336.91	143.18

			(-) [0/0]	(-) [336.91]	(0.00) [0]
850	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [0/0]	607.09 (-) [635.03]	635.24 (27.94) [0]
851	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [12/2022]	2,030.50 (-) [2,030.50]	10.34 (0.00) [-]
852	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (3/2024) [3/2024]	651.00 (-) [1,009.00]	7.96 (358.00) [108]
853	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
854	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	14.62 (134.08) [0]
855	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020 (-) [4/2020]	511.86 (-) [1,756.00]	967.96 (1,244.14) [0]
856	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/ (-) [0/0]	636.38 (-) [636.38]	0.00 (0.00) [0]
857	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	4/1986	3/1994 (-) [0/0]	158.77 (274.56) [634.48]	629.43 (475.71) [0]
858	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (-) [3/2022]	2,912.96 (-) [3,845.60]	1.92 (932.64) [0]
859	HAJIPUR - BACHAWARA	5/2015	3/2019 (-) [3/2020]	678.54 (-) [678.54]	0.00 (0.00) [12]
860	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2020]	542.18 (-) [542.18]	374.20 (0.00) [0]
861	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/ (-) [0/0]	172.03 (-) [260.10]	10.84 (88.07) [0]
862	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [5/2019]	230.03 (-) [770.08]	277.14 (540.05) [-43]
863	HOTGI-KUDGI-GADAG	3/2015	3/2019 (3/2021) [3/2021]	1,614.59 (1,870.41) [1,870.41]	880.72 (255.82) [24]
864	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [0/0]	157.94 (-) [157.94]	50.69 (0.00) [0]
865	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/ (-) [0/0]	166.89 (-) [166.89]	246.00 (0.00) [0]
866	JAKHAL-MANSA DOUBLING ON SPR SECTION	4/2008	/ (-) [0/0]	162.96 (-) [162.96]	153.31 (0.00) [0]
867	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [0/0]	625.00 (-) [845.58]	0.00 (220.58) [0]
868	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	3/2002	6/2007 (-) [0/0]	625.30 (408.76) [876.10]	841.57 (250.80) [0]
869	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (3/2023)	2,132.77 (-)	214.54 (0.00)

			[3/2023]	[2,132.77]	[108]
870	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (2/2010) [2/2010]	923.52 (-) [792.27]	506.12 (-131.25) [0]
871	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/ (-) [0/0]	174.56 (-) [175.99]	57.51 (1.43) [0]
872	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	4/1999	/ (-) [0/0]	744.71 (-) [1,126.79]	751.05 (382.08) [0]
873	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2021]	2,063.03 (-) [2,063.03]	632.48 (0.00) [0]
874	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [2,200.00]	278.36 (343.05) [12]
875	KURUPPANTHARA-CHINGAVANAM	4/2007	/ (-) [0/0]	270.14 (-) [457.08]	317.14 (186.94) [0]
876	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [1/2006]	406.99 (-) [544.72]	147.86 (137.73) [0]
877	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2023]	247.66 (-) [6,093.31]	972.82 (5,845.65) [178]
878	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [0/0]	257.42 (-) [258.73]	113.51 (1.31) [0]
879	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-) [3/2019]	120.70 (-) [1,800.00]	114.45 (1,679.30) [0]
880	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (12/2013) [12/2013]	499.96 (-) [665.75]	152.07 (165.79) [0]
881	MIRAJ-LONDA	3/2015	/ (3/2021) [3/2021]	1,830.00 (1,190.92) [1,190.92]	161.34 (-639.08) [-]
882	MM FROM BURAMARA-CHAKULIA	4/2008	0/0 (12/2024) [12/2024]	466.48 (-) [1,000.00]	0.83 (533.52) [-]
883	MONIGRAM- NIMTITA	4/2012	/ (-) [0/0]	250.93 (-) [259.23]	199.46 (8.30) [0]
884	MUNEERABAD-MAHABOONNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2019]	1,723.00 (1.00) [645.00]	838.33 (-1,078.00) [0]
885	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [3/2020]	414.84 (-) [661.00]	121.59 (246.16) [0]
886	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [0/0]	450.00 (-) [2,100.00]	484.14 (1,650.00) [0]
887	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI- BAHRAHAT NL	4/2010	3/2005 (-) [0/0]	494.54 (-) [492.68]	32.00 (-1.86) [0]
888	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [3/2020]	242.22 (-) [471.00]	67.41 (228.78) [0]
889	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (-) [0/0]	241.52 (-) [394.28]	148.33 (152.76) [0]

890	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [3/2019]	1,798.00 (-) [1,798.00]	0.00 (0.00) [0]
891	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
892	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [3/2019]	1,180.19 (2,531.34) [3,300.00]	3,165.68 (2,119.81) [0]
893	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [4/2022]	600.00 (-) [685.99]	4.78 (85.99) [25]
894	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [0/0]	261.38 (-) [332.14]	360.58 (70.76) [0]
895	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2022]	915.98 (-) [915.96]	322.47 (-0.02) [0]
896	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [0/0]	299.60 (-) [269.60]	1.12 (-30.00) [0]
897	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	3/1998	/ (-) [0/0]	280.00 (-) [1,122.00]	834.87 (842.00) [0]
898	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,261.71]	183.82 (2,178.96) [0]
899	RAYADURGA-TUMKUR NL	4/2007	/ (-) [3/2022]	2,062.30 (2,062.30) [2,062.20]	817.00 (-0.10) [-]
900	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE	4/2010	/ (-) [0/0]	268.52 (-) [268.52]	78.81 (0.00) [0]
901	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL	4/2000	/ (-) [0/0]	297.47 (-) [153.02]	52.10 (-144.45) [0]
902	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2020]	277.28 (-) [266.52]	137.85 (-10.76) [48]
903	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (12/2023) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]
904	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [0/0]	450.00 (-) [288.85]	9.31 (-161.15) [0]
905	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [0/0]	365.17 (-) [527.54]	1.73 (162.37) [0]
906	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [3/2020]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
907	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH	4/2013	/ (-) [0/0]	876.00 (-) [876.00]	0.00 (0.00) [0]
908	YELAHANKA-PENUKONDA	5/2015	3/2020 (3/2020) [3/2020]	860.43 (860.43) [860.43]	677.98 (0.00) [0]
<u>Road Transport And Highways</u>					
909	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]

910	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (-) [0/0]	1,928.22 (-) [2,945.00]	3,070.11 (1,016.78) [0]
911	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-III)	9/2015	3/2018 (-) [0/0]	788.51 (-) [788.51]	103.37 (0.00) [0]
912	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,294.47]	0.00 (0.00) [0]
913	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [998.70]	0.00 (0.00) [0]
914	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (-) [8/2020]	604.00 (-) [604.00]	423.83 (0.00) [128]
915	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [12/2019]	754.00 (-) [754.00]	1,363.43 (0.00) [81]
916	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [2/2020]	1,244.10 (-) [1,244.10]	85.00 (0.00) [-]
917	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,675.28 (0.00) [0]
918	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2019]	2,848.00 (-) [2,848.00]	1,149.72 (0.00) [69]
919	WIDENING AND STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF AMRTISA	3/2015	/ (-) [0/0]	789.83 (-) [789.83]	109.77 (0.00) [0]
	<u>Telecommunications</u>				
920	NETWORK FOR SPECTRUM	3/2012	7/2015 (-) [5/2020]	13,334.00 (-) [24,664.00]	8,397.00 (11,330.00) [58]
921	NETWORK FOR SPECTRUM (NFS) TO CONNECT DEFENCE STATIONS ACROSS COUNTRY	9/2014	9/2014 (-) [0/0]	2,111.17 (-) [2,011.17]	253.90 (-100.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
922	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
923	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [10/2021]	2,326.52 (2,446.57) [3,000.00]	734.88 (673.48) [79]
	<u>Road Transport And Highways</u>				
924	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
925	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
926	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	0.00 (0.00) [0]
927	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	0.00 (0.00) [0]
928	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]

929	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
930	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
931	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
932	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]
933	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	0.00 (0.00) [0]
934	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
935	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
936	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
937	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	0.00 (0.00) [0]
938	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	0.00 (0.00) [0]
939	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
940	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
941	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
942	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>ODISHA</u>				
	<u>Coal</u>				
943	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	249.61 (0.00) [108]
944	BALRAM OCP EXTENSION,MCL 8.00 MTY	12/2007	3/2010 (-) [3/2022]	172.08 (-) [172.08]	345.12 (0.00) [144]
945	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	194.57 (0.00) [60]
946	BHUBANESWARI OCP, MCL (20.0 MTY)	12/2007	3/2017 (-) [3/2020]	490.10 (-) [490.10]	467.50 (0.00) [36]
947	GARJANBAHAL OCP	11/2014	3/2021 (-) [3/2021]	1,375.38 (-) [1,375.38]	433.20 (0.00) [0]
948	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-)	479.53 (-)	404.31 (0.00)

			[3/2021]	[479.53]	[96]
949	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	79.92 (0.00) [0]
950	JAGANNATH RE-ORGANISATION OC.(6.00 MTY)	5/2014	3/2019 (-) [3/2021]	337.66 (-) [337.66]	70.05 (0.00) [24]
951	KANIHA OCP, MCL, (10.0 MTY)	12/2007	3/2013 (-) [3/2022]	457.77 (-) [457.77]	619.13 (0.00) [108]
952	KULDA EXPN OC. (5.00 MTY)	6/2014	3/2018 (-) [3/2020]	289.03 (-) [289.03]	29.93 (0.00) [24]
953	KULDA OCP (MAHANADI COALFIELDS LTD)	1/2005	3/2010 (-) [3/2020]	302.96 (-) [302.96]	302.96 (0.00) [120]
954	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,109.33 (0.00) [0]
955	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	1,174.58 (0.00) [0]
	<u>Mines</u>				
956	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (4/2021) [4/2021]	5,540.00 (5,540.00) [5,540.00]	96.98 (0.00) [0]
957	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [11/2020]	355.00 (-) [355.00]	31.92 (0.00) [0]
958	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (4/2021) [4/2021]	483.00 (483.00) [483.00]	0.00 (0.00) [0]
959	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (1/2020) [1/2020]	534.00 (534.00) [534.00]	315.25 (0.00) [0]
	<u>Petroleum</u>				
960	2G ETHANOL BIO REFINERY AT BARGARH	8/2017	12/2020 (-) [12/2020]	750.00 (-) [750.00]	29.15 (0.00) [0]
961	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (-) [12/2021]	315.00 (-) [315.00]	108.80 (0.00) [0]
962	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (243.53) [243.53]	45.20 (0.00) [0]
963	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [181.20]	25.90 (-1.00) [0]
964	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,933.00 (-) [1,933.00]	967.24 (0.00) [0]
965	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	235.99 (0.00) [0]
966	INSTALLATION OF ADDITIONAL CRUDE TANKS (7 NOS) AT PARADIP REFINERY	5/2016	1/2019 (12/2019) [12/2019]	429.00 (-) [429.00]	290.69 (0.00) [11]
967	LPG BP PROJECT KHORDHA	12/2016	12/2019 (-) [12/2019]	161.59 (-) [161.59]	34.33 (0.00) [0]
968	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021	1,297.50	7.01

			(-) [10/2021]	(-) [1,297.50]	(0.00) [0]
969	POLYPROPYLENE PLANT AT PARADIP REFINERY	3/2014	9/2017 (6/2019) [6/2019]	3,150.00 (-) [3,150.00]	2,589.31 (0.00) [21]
	<u>Power</u>				
970	DARLIPALLI STPP STAGE-I (2X800 MW)	2/2014	8/2018 (2/2020) [2/2020]	12,532.44 (-) [13,740.53]	9,101.85 (1,208.09) [18]
971	PG WORKS ASSOCIATED WITH COMMON TRANSMISSION SYSTEM FOR PHASE-II GENERATION PROJECT IN ODISHA	4/2016	4/2019 (4/2019) [6/2019]	844.64 (844.64) [844.64]	341.30 (0.00) [2]
	<u>Railways</u>				
972	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [3/2021]	942.95 (-) [1,120.00]	941.20 (177.05) [24]
973	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (-) [3/2021]	843.04 (-) [843.04]	81.26 (0.00) [5]
974	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	4/2015	12/2018 (-) [3/2021]	1,172.92 (-) [1,172.92]	245.16 (0.00) [27]
975	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.96 (80.10) [0]
976	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2020]	5,200.00 (-) [5,200.00]	0.00 (0.00) [0]
977	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [3/2020]	1,185.64 (-) [1,844.47]	1,603.22 (658.83) [27]
978	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (-) [3/2022]	1,547.38 (-) [1,547.38]	205.59 (0.00) [0]
979	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (-) [3/2021]	701.61 (-) [810.02]	88.04 (108.41) [28]
980	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [3/2019]	133.41 (207.00) [385.00]	384.55 (251.59) [0]
981	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (-) [6/2021]	2,923.13 (-) [3,798.80]	1,123.73 (875.67) [147]
982	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2022]	2,361.74 (-) [2,361.74]	87.60 (0.00) [0]
983	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (3/2020) [6/2020]	969.83 (-) [1,151.81]	450.25 (181.98) [3]
984	RUPSA BANGRIPOSI 90 KM WITH MM FOR UPGRADATION FROM RUPSA BURAMARA AND EXTENSION OF LINE FRO	4/1995	12/2021 (12/2024) [12/2024]	524.43 (-) [939.00]	184.33 (414.57) [36]
985	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2020]	155.81 (-) [238.03]	180.78 (82.22) [0]
986	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [3/2020]	948.04 (-) [1,103.00]	1,132.87 (154.96) [0]
987	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [3/2021]	1,111.99 (-) [1,539.28]	765.60 (427.29) [25]

988	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [12/2021]	1,202.70 (245.00) [1,202.70]	801.40 (0.00) [82]
989	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (-) [3/2023]	810.78 (-) [1,928.07]	574.98 (1,117.29) [21]
990	VIZIANAGARAM -SAMABALPUR 3RD LINE	1/1991	12/2024 (-) [12/2024]	2,335.67 (2,335.67) [2,335.67]	441.95 (0.00) [0]
	Road Transport And Highways				
991	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [4/2020]	1,282.94 (-) [1,282.94]	0.00 (0.00) [-]
992	DEVELOPMENT OF FOUR LANNING OF ANGUL- SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [8/2019]	2,510.04 (-) [2,510.04]	0.00 (0.00) [0]
993	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [11/2019]	752.28 (-) [752.28]	0.00 (0.00) [-]
994	IMPROVEMENT FROM KM 0 TO KM 68.0 (KANAKTORA TO JHARSUGUDA SECTION) TO 2 LANE CARRIAGEWAY WITH PAVED	12/2013	5/2016 (-) [0/0]	319.80 (320.00) [320.00]	0.00 (0.20) [0]
995	IMPROVEMENT FROM KM 0/0 TO 68/0	12/2013	10/2016 (-) [0/0]	319.80 (-) [319.80]	0.00 (0.00) [0]
996	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [6/2019]	1,069.65 (-) [1,069.65]	0.00 (0.00) [-]
997	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [3/2019]	1,410.00 (-) [1,410.00]	1,555.96 (0.00) [0]
998	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [7/2020]	1,008.96 (-) [1,008.96]	130.32 (0.00) [-]
999	REHABILITATION AND UP GRADATION OF EXISTING 2- LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [0/0]	564.66 (-) [564.66]	0.00 (0.00) [0]
1000	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [11/2020]	476.56 (-) [476.56]	0.00 (0.00) [40]
1001	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	0.00 (0.00) [0]
1002	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [0/0]	953.09 (-) [953.09]	0.00 (0.00) [0]
1003	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [5/2020]	668.86 (-) [668.86]	0.00 (0.00) [-]
1004	REHABILITATION AND UP-GRADATION OF EXISTING 2- LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [0/0]	614.48 (-) [614.48]	0.00 (0.00) [0]
1005	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH	7/2014	1/2017 (-) [0/0]	342.05 (-) [342.05]	0.00 (0.00) [0]
1006	REHABILITATION AND UP-GRADATION OF SIX-LANING OF CHANDIKHOLE - BHADRAK SECTION FROM KM. 62.000 TO KM	1/2018	/ (-) [0/0]	1,522.00 (-) [1,522.00]	0.00 (0.00) [0]
1007	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [6/2021]	503.88 (-) [503.88]	0.00 (0.00) [-]

1008	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [3/2021]	1,288.07 (-) [1,420.00]	115.12 (131.93) [12]
1009	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [7/2020]	686.65 (-) [686.65]	0.00 (0.00) [-]
1010	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/ (-) [3/2020]	686.65 (-) [686.65]	0.00 (0.00) [-]
1011	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/ (-) [0/0]	417.51 (-) [417.51]	0.00 (0.00) [0]
1012	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	7/2014	1/2017 (-) [0/0]	342.05 (342.00) [342.00]	0.00 (-0.05) [0]
1013	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141	1/2018	/ (-) [0/0]	999.00 (-) [999.00]	0.00 (0.00) [0]
1014	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016 (-) [0/0]	171.96 (172.00) [172.00]	0.00 (0.04) [0]
1015	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB	1/1991	10/2017 (-) [0/0]	218.63 (-) [218.63]	29.27 (0.00) [0]
1016	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	1/1991	5/2018 (-) [0/0]	229.41 (-) [229.41]	6.65 (0.00) [0]
1017	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014 (-) [0/0]	1,047.00 (-) [1,047.00]	1,633.88 (0.00) [0]
1018	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/ (-) [0/0]	806.11 (-) [806.11]	0.00 (0.00) [0]
1019	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM 256.8	3/2014	5/2016 (-) [0/0]	162.51 (163.00) [163.00]	0.00 (0.49) [0]
1020	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016 (-) [0/0]	191.50 (192.00) [192.00]	0.00 (0.50) [0]
1021	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	2/2015	10/2017 (-) [0/0]	239.91 (240.00) [240.00]	0.00 (0.09) [0]
1022	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	1/2015	4/2018 (-) [0/0]	326.63 (327.00) [327.00]	0.00 (0.37) [0]
1023	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	6/2016	6/2018 (-) [0/0]	157.30 (157.00) [157.00]	0.00 (-0.30) [0]
1024	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA	12/2011	11/2017 (-) [0/0]	159.39 (-) [159.39]	0.00 (0.00) [0]
1025	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA	12/2011	8/2015 (-) [0/0]	191.08 (-) [191.08]	0.00 (0.00) [0]
1026	WIDENING TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDERS AND STRENGTHENING FROM KM 162.010 TO KM 224.900	3/2015	10/2017 (-) [0/0]	226.31 (226.00) [226.00]	0.00 (-0.31) [0]
	<u>Steel</u>				
1027	INSTALLATION OF NEW HOT STRIP MILL AT RSP	4/2015	4/2018 (-) [5/2019]	3,127.30 (-) [3,127.30]	2,749.95 (0.00) [13]

	PUNJAB				
	Fertilisers				
1028	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (-) [11/2019]	218.83 (-) [218.83]	69.23 (0.00) [0]
1029	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (-) [11/2019]	239.81 (-) [239.81]	69.08 (0.00) [0]
	Health And Family Welfare				
1030	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [6/2020]	703.00 (-) [703.00]	272.00 (0.00) [0]
1031	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [6/2019]	152.95 (-) [152.95]	95.16 (0.00) [16]
	Railways				
1032	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL	4/2009	/ (-) [0/0]	396.04 (-) [369.00]	186.27 (-27.04) [0]
1033	QADIAN-BEAS	4/2011	/ (-) [0/0]	205.22 (-) [205.22]	3.18 (0.00) [0]
	Road Transport And Highways				
1034	4 LAINING WITH PAVED SHOULDERS OF DOGAL KALAN TO PUNJAB/HARYANA BORDER SEC.OF NH-71(NEW NH-52) FROM	11/2014	/ (-) [0/0]	573.96 (605.00) [605.00]	209.74 (31.04) [0]
1035	4 LANES WITH PAVED SIDE SHOULDERS OF END OF PATIALA BYPASS TO START OF SANGRUR BYEPASS SEC.OF NH-64(	2/2015	/ (-) [0/0]	486.74 (-) [486.74]	189.39 (0.00) [0]
1036	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [4/2020]	1,169.61 (-) [1,169.61]	361.32 (0.00) [-]
1037	4-LAINING WITH PAVED SHOULDERS OF SANGRUR TO DOGAL KALAN SEC.OF NH-71(NEW NH-52) FROM KM.181.805 TO	11/2014	/ (-) [0/0]	463.65 (546.00) [463.65]	280.16 (0.00) [0]
1038	4-LANES WITH PAVED SIDE SHOULDERS OF END OF SANGRUR BYPASS TO TAPA SEC,IF NH-64(NEW NH-07) FROM EXI	2/2015	/ (-) [0/0]	483.38 (-) [483.38]	65.76 (0.00) [0]
1039	4-LANES WITH PAVED SIDE SHOULDERS OF TAPA TO BATHINDA SEC.OF NH-64(NEW NH-07) FROM EXISING KM.168/0	2/2015	/ (-) [0/0]	616.36 (-) [616.36]	68.58 (0.00) [0]
1040	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600	11/2015	/ (-) [0/0]	847.02 (-) [847.02]	299.81 (0.00) [0]
1041	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [889.24]	389.64 (0.00) [0]
1042	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [9/2019]	1,388.34 (-) [1,388.34]	1,017.40 (0.00) [0]
1043	CONST.OF 4 LANES WITH PAVED SHOUDLERS OF HARIKE BYPASS FROM EXISTING KM.158.350 TO 166.925 OF NH-15(	3/2015	/ (-) [0/0]	312.79 (-) [312.79]	17.57 (0.00) [0]
1044	CONST.OF SANGRUR BYPASS(EXISTING KM.106.170 TO 116.950) AND DHANOULA BYPASS(EXISTING KM.138.030 TO K	7/2014	/ (-) [0/0]	319.80 (-) [319.80]	102.55 (0.00) [0]
1045	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [4/2020]	754.54 (-) [756.27]	72.04 (1.73) [1]
1046	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71	12/2015	/ (-)	766.36 (-)	99.86 (0.00)

	(NEW NH-52) FROM EXIS		[0/0]	[766.36]	[0]
1047	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF TALLEWAL-BARNALA SECTION OF NH-71 FROM EXISTING KM	12/2015	/ (-) [0/0]	578.38 (-) [578.38]	128.53 (0.00) [0]
1048	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	12/2017 (-) [12/2019]	447.29 (-) [447.29]	189.15 (0.00) [24]
1049	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [1/2021]	261.76 (-) [261.76]	7.90 (0.00) [-]
1050	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [6/2019]	479.00 (-) [479.00]	453.09 (0.00) [-]
1051	IMPROVEMENT OF AMRITSAR BYPASS BY CONSTRUCTION OF ADDITIONAL STRUCTURE AND SERVICE ROADS ON NH-1	9/2015	/ (-) [5/2019]	273.06 (-) [273.06]	199.72 (0.00) [-]
1052	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [10/2019]	1,069.59 (-) [1,069.59]	629.87 (0.00) [0]
1053	REHABILITATION & UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH-3	3/2018	7/2020 (-) [7/2020]	322.48 (-) [322.48]	48.73 (0.00) [0]
1054	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [1/2020]	196.05 (-) [196.05]	9.03 (0.00) [-]
1055	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	9.03 (0.00) [0]
1056	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	3/2018	6/2020 (-) [6/2020]	173.24 (-) [173.24]	10.97 (0.00) [0]
1057	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0+000	3/2018	11/2020 (-) [11/2020]	170.57 (-) [170.57]	8.14 (0.00) [0]
1058	REHABILITATION AND UPGRADATION OF NH-64 FROM KM.28.110 TO 50.000(ZIRAKPUR TO PATIALA SEC.) TO 4 LANE	3/2015	/ (-) [0/0]	435.90 (-) [435.90]	31.02 (0.00) [0]
1059	WIDENING AND REHABILITATION OF THE EXISTING PATIALA BYEPASS FROM EXISTING KM.50/0 TO 69/280) ON NH-6	1/2015	/ (-) [0/0]	279.68 (-) [279.68]	25.28 (0.00) [0]
1060	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF FARIDKOT-KO	6/2015	/ (-) [0/0]	899.21 (-) [899.21]	25.08 (0.00) [0]
1061	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA	6/2015	/ (-) [0/0]	892.17 (-) [892.17]	26.92 (0.00) [0]
	<u>Urban Development</u>				
1062	CONSTRUCTION OF DIFFERENT BUILDINGS UNDER PHASE-I FOR IIT ROPAR AT ROPAR, PUNJAB	2/2014	5/2017 (2/2019) [6/2019]	388.00 (488.28) [488.28]	410.91 (100.28) [25]
1063	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020 (-) [5/2020]	430.00 (-) [430.00]	46.28 (0.00) [0]
1064	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	8/2016	4/2019 (9/2019) [12/2019]	294.00 (349.94) [294.00]	167.44 (0.00) [8]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1065	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (3/2017) [12/2020]	12,320.00 (-) [12,320.00]	10,749.00 (0.00) [48]

	<u>Coal</u>				
1066	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [12/2019]	513.63 (-) [513.63]	176.87 (0.00) [0]
1067	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [9/2019]	522.45 (-) [522.45]	9.13 (0.00) [0]
	<u>Petroleum</u>				
1068	50 MW CAPACITY WIND POWER PROJECT UNDER PHASE II	11/2011	3/2013 (-) [0/0]	310.00 (-) [370.00]	17.84 (60.00) [0]
1069	LPG BP PROJECT JODHPUR	3/2018	/ (-) [3/2021]	229.80 (-) [229.80]	69.19 (0.00) [-]
	<u>Power</u>				
1070	TRANSMISSION SYSTEM FOR SOLAR PARK AT BHADLA RAJISTHAN	7/2016	1/2019 (7/2019) [6/2019]	1,429.38 (1,429.38) [1,429.38]	916.66 (0.00) [5]
	<u>Railways</u>				
1071	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [1,103.04]	2.69 (229.33) [0]
1072	AJMER-BANGURGRAM	4/2011	11/2019 (-) [5/2020]	213.39 (-) [244.02]	240.62 (30.63) [6]
1073	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [1,099.54]	0.00 (277.54) [0]
1074	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019 (-) [12/2019]	242.09 (-) [349.00]	329.33 (106.91) [10]
1075	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [6/2020]	246.08 (-) [348.55]	179.50 (102.47) [6]
1076	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [12/2021]	410.08 (780.98) [795.01]	493.64 (384.93) [34]
1077	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR)	4/2008	3/2015 (-) [10/2020]	829.74 (-) [1,216.00]	805.25 (386.26) [67]
1078	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [9/2022]	808.85 (-) [808.85]	12.41 (0.00) [1]
1079	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [6/2020]	420.18 (295.02) [420.18]	118.27 (0.00) [3]
1080	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [3/2020]	493.17 (-) [493.17]	435.76 (0.00) [24]
1081	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [432.22]	0.00 (109.22) [0]
1082	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [9/2019]	236.93 (-) [294.90]	169.51 (57.97) [11]
	<u>Road Transport And Highways</u>				
1083	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [4/2019]	597.00 (-) [597.00]	605.33 (0.00) [18]
1084	2-LANE WITH PAVED SHOULDER TONK-SAWAIMADHOPUR	8/2016	1/2019 (-)	320.30 (-)	228.17 (0.00)

			[4/2019]	[320.30]	[3]
1085	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [2/2019]	530.07 (-) [530.07]	675.73 (0.00) [0]
1086	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [11/2019]	688.70 (-) [688.70]	552.52 (0.00) [-]
1087	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [8/2020]	1,031.95 (-) [1,031.95]	367.00 (0.00) [-]
1088	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [3/2019]	822.90 (-) [822.90]	753.50 (0.00) [0]
1089	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	0.00 (0.00) [0]
1090	CONSTRUCTION/ UP-GRADATION OF 2LANE WITH PAVED SHOULDER OF NH FROM RAISINGHNAGAR-POOGAL (DESIGN CH.	2/2018	/ (-) [0/0]	716.76 (-) [716.76]	0.00 (0.00) [0]
1091	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	0.00 (0.00) [0]
1092	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [12/2020]	1,308.73 (-) [1,308.73]	0.00 (0.00) [-]
1093	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [11/2019]	763.23 (-) [763.23]	155.23 (0.00) [5]
1094	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM	6/2016	6/2019 (-) [9/2019]	649.00 (-) [649.00]	0.00 (0.00) [3]
1095	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [11/2020]	964.17 (-) [964.17]	211.90 (0.00) [37]
1096	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (9/2017) [3/2019]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1097	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING	9/2012	10/2013 (-) [0/0]	511.00 (-) [511.00]	0.00 (0.00) [0]
1098	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A	9/2012	10/2013 (-) [6/2019]	511.00 (-) [511.00]	33.73 (0.00) [68]
1099	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS	10/2013	5/2014 (-) [0/0]	278.87 (-) [278.87]	0.00 (0.00) [0]
1100	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF LALSOT-KARALI	1/1991	5/2016 (-) [0/0]	208.87 (-) [208.87]	206.78 (0.00) [0]
1101	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF PRATAPGARH-PADI	1/1991	10/2016 (-) [0/0]	269.26 (-) [269.26]	212.72 (0.00) [0]
1102	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O	1/1991	4/2014 (-) [0/0]	376.52 (-) [376.52]	0.00 (0.00) [0]
1103	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [12/2019]	1,100.19 (-) [1,100.19]	750.00 (0.00) [-]
1104	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [5/2020]	1,239.82 (-) [1,239.82]	795.68 (0.00) [-]

1105	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [11/2019]	894.00 (-) [894.00]	15.00 (0.00) [-5]
1106	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [3/2019]	425.19 (-) [425.19]	297.72 (0.00) [0]
1107	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [3/2019]	275.90 (-) [275.90]	256.10 (0.00) [0]
1108	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	261.25 (0.00) [0]
1109	TWO LANNING WITH PAVED SHOULDER OF SALASAR- NAGPUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	571.06 (0.00) [3]
1110	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (-) [0/0]	874.25 (-) [874.25]	0.00 (0.00) [0]
1111	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [9/2020]	1,103.88 (-) [1,103.88]	129.11 (0.00) [-]
1112	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING	10/2014	1/2015 (-) [0/0]	257.09 (-) [257.09]	14.80 (0.00) [0]
1113	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24	2/2015	3/2015 (-) [6/2019]	383.40 (-) [383.40]	224.68 (0.00) [51]
1114	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K	10/2014	1/2015 (-) [0/0]	269.22 (-) [269.22]	33.24 (0.00) [0]
1115	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH	12/2015	6/2018 (-) [0/0]	621.43 (-) [621.43]	0.00 (0.00) [0]
	<u>Urban Development</u>				
1116	CONSTRUCTION OF MEDICAL COLLEGE CAMPUS FOR 100 MBBS ADMISSION ANNUALLY AND UP-GRADATION OF GOVT. DIS	5/2015	3/2017 (-) [0/0]	189.00 (-) [189.00]	0.00 (0.00) [0]
1117	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (-) [12/2019]	549.31 (-) [559.49]	291.77 (10.18) [5]
	<u>SIKKIM</u>				
	<u>Railways</u>				
1118	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
1119	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
1120	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
1121	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
1122	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
1123	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	18.12 (0.00) [0]

1124	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
1125	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
1126	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TAMIL NADU</u>				
	<u>Atomic Energy</u>				
1127	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	13,910.00 (0.00) [36]
1128	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	9/2003	9/2010 (-) [10/2021]	3,492.00 (-) [6,840.00]	5,771.17 (3,348.00) [133]
	<u>Coal</u>				
1129	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (9/2019) [9/2019]	1,458.17 (709.06) [709.06]	430.69 (-749.11) [51]
1130	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (6/2019) [9/2019]	5,907.11 (7,080.41) [7,080.41]	6,300.55 (1,173.30) [45]
	<u>Mines</u>				
1131	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (-) [6/2019]	166.62 (-) [166.62]	134.98 (0.00) [0]
	<u>Petroleum</u>				
1132	AUGMENTATION OF CTMPL	12/2016	6/2020 (-) [6/2020]	228.00 (-) [228.00]	5.79 (0.00) [0]
1133	BS-VI PROJECTS	9/2017	12/2019 (-) [12/2019]	1,858.00 (-) [1,858.00]	757.22 (0.00) [0]
1134	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (-) [8/2021]	466.43 (-) [466.43]	4.04 (0.00) [10]
1135	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (-) [2/2021]	4,497.00 (6,025.00) [6,025.00]	428.96 (1,528.00) [26]
1136	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [6/2020]	711.00 (-) [711.00]	11.12 (0.00) [0]
1137	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (-) [5/2020]	390.52 (390.52) [390.52]	221.40 (0.00) [14]
1138	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (-) [0/0]	678.00 (-) [678.00]	5.53 (0.00) [0]
1139	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [8/2020]	421.00 (-) [421.00]	62.32 (0.00) [0]
1140	RESID UPGRADATION PROJECT	3/2013	11/2015 (-) [0/0]	3,110.36 (-) [3,110.36]	2,915.42 (0.00) [0]
	<u>Power</u>				
1141	KUNADANKULAM APP TRANS SYSTEM (PGCIL)	5/2005	11/2008 (6/2019) [5/2019]	1,779.29 (2,187.32) [2,187.32]	2,133.02 (408.03) [126]
1142	TRANSMISSION SYSTEM FOR EVACUTION OF POWER	5/2017	7/2019	186.17	80.77

	FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY		(7/2019) [7/2019]	(186.17) [186.17]	(0.00) [0]
	<u>Railways</u>				
1143	ATTIPPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [3/2018]	257.00 (-) [257.00]	0.00 (0.00) [0]
1144	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [1,105.00]	3.34 (953.16) [0]
1145	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	4/1998	/ (-) [0/0]	271.24 (-) [520.00]	468.18 (248.76) [0]
1146	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [0/0]	198.68 (-) [556.64]	303.72 (357.96) [0]
1147	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	9/2006	/ (-) [0/0]	343.17 (-) [1,065.00]	1,049.68 (721.83) [0]
1148	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [1,140.00]	1.63 (851.43) [0]
1149	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (-) [0/0]	495.74 (-) [734.01]	445.91 (238.27) [0]
1150	KARUR-SALEM(NL),SR	2/1997	/ (-) [0/0]	155.55 (-) [920.00]	856.94 (764.45) [0]
1151	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [3/2020]	760.00 (-) [1,182.31]	0.00 (422.31) [0]
1152	MADURAI - RAMESWARAM (161 KM) GAUGE CONVERSION	2/1997	3/2015 (-) [0/0]	458.63 (-) [458.63]	0.92 (0.00) [0]
1153	MADURAI-BODINAYAKKANUR	4/2008	/ (-) [3/2020]	164.41 (-) [450.00]	83.15 (285.59) [-]
1154	MADURAI-DINDIGUL (INCL. AMBADUTURAI- KODAIKANNAL ROAD) (62.05 KM) DOUBLING	2/2003	3/2009 (-) [0/0]	199.55 (-) [330.32]	2.12 (130.77) [0]
1155	MANAMADURAI - VIRUDHUNAGAR (66.55 KM) GAUGE CONVERSION.	2/2006	3/2012 (-) [0/0]	208.00 (-) [208.00]	3.58 (0.00) [0]
1156	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [3/2022]	1,700.00 (-) [1,700.00]	0.00 (0.00) [0]
1157	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [2/2019]	724.69 (-) [2,072.50]	1,188.90 (1,347.81) [0]
1158	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [3/2020]	187.26 (-) [231.67]	7.62 (44.41) [71]
1159	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [1,500.00]	0.61 (661.00) [0]
1160	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [0/0]	268.87 (-) [302.02]	304.07 (33.15) [0]
1161	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [0/0]	582.83 (-) [2,300.00]	237.73 (1,717.17) [0]
1162	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/	227.40	61.97

			(-) [0/0]	(-) [900.00]	(672.60) [0]
1163	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
1164	TRICHY - MANAMADURAI (150 KM) GAUGE CONVERSION	2/2000	3/2014 (-) [0/0]	200.84 (-) [200.84]	394.26 (0.00) [0]
1165	VILLUPURAM - KATPADI (161 KM) GAUGE CONVERSION	2/2005	3/2010 (-) [0/0]	600.00 (600.00) [645.54]	671.00 (45.54) [0]
Road Transport And Highways					
1166	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI	9/2011	8/2013 (-) [12/2018]	485.00 (-) [485.00]	406.68 (0.00) [0]
1167	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4/2012	4/2014 (-) [0/0]	624.00 (-) [624.00]	350.79 (0.00) [0]
1168	4-LANNING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	0.00 (0.00) [0]
1169	4-LANNING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [8/2020]	1,227.87 (-) [1,227.87]	0.00 (0.00) [35]
1170	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (-) [268.92]	0.00 (9.95) [0]
1171	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I-	11/2015	8/2015 (-) [0/0]	154.14 (-) [154.14]	0.00 (0.00) [0]
1172	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [0/0]	600.00 (-) [600.00]	325.55 (0.00) [0]
1173	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [0/0]	1,016.92 (-) [1,016.92]	0.00 (0.00) [0]
1174	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [8/2019]	1,387.11 (-) [1,387.11]	956.75 (0.00) [21]
1175	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICULAM (7/300)	3/2018	/ (-) [11/2020]	628.71 (-) [628.71]	31.45 (0.00) [-]
1176	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	3/2018	/ (-) [0/0]	2,065.96 (-) [2,065.96]	0.00 (0.00) [0]
1177	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [0/0]	1,166.26 (-) [1,166.26]	0.00 (0.00) [0]
1178	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [4/2019]	641.17 (-) [641.17]	352.71 (0.00) [33]
1179	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [11/2020]	505.35 (-) [505.35]	32.77 (0.00) [-]
1180	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [9/2020]	1,176.37 (-) [1,176.37]	0.00 (0.00) [37]
1181	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [3/2020]	707.82 (-) [707.82]	277.66 (0.00) [19]
1182	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM	3/2017	3/2020	848.45	44.06

	KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.		(-) [3/2020]	(-) [848.45]	(0.00) [0]
1183	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [5/2020]	641.17 (-) [641.17]	355.39 (0.00) [22]
1184	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO	3/2015	7/2015 (-) [0/0]	157.18 (162.00) [162.00]	0.00 (4.82) [0]
1185	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2020]	379.90 (-) [379.90]	62.24 (0.00) [-]
1186	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-) [0/0]	1,250.00 (-) [1,250.00]	1,330.22 (0.00) [0]
1187	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1188	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	627.47 (0.00) [0]
1189	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [0/0]	374.00 (-) [374.00]	237.00 (0.00) [0]
1190	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [633.55]	0.00 (0.00) [0]
1191	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [8/2019]	563.92 (-) [563.92]	97.07 (0.00) [20]
	Shipping And Ports				
1192	CAPITAL DREDGING PHASE-IV TO PROVIDE 18M DEEP DRAFT	3/2016	12/2017 (-) [5/2020]	600.00 (258.00) [257.90]	1.45 (-342.10) [29]
1193	CONSTRUCTION OF COAL BERTH-4 AT KAMARAJAR PORT LIMITED	2/2015	12/2017 (-) [0/0]	244.50 (258.00) [275.98]	275.98 (31.48) [0]
1194	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	3/2006 (-) [0/0]	150.00 (-) [600.00]	139.80 (450.00) [0]
1195	SETHUSAMUDRAM SHIP CHANNEL PROJECT	6/2005	10/2008 (-) [0/0]	2,427.40 (-) [2,427.40]	831.21 (0.00) [0]
	Urban Development				
1196	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [3/2020]	209.00 (-) [209.00]	105.72 (0.00) [5]
1197	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	0.00 (0.00) [0]
1198	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (-) [19,058.00]	16,352.77 (4,458.00) [0]
1199	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	/ (-) [11/2021]	348.77 (-) [348.77]	12.00 (0.00) [-]
	TELANGANA				
	Coal				
1200	KALYANIKHANI 6 INCLINE PROJECT	12/2015	3/2020 (-) [3/2020]	477.65 (-) [477.65]	2.11 (0.00) [0]
1201	KOYAGUDEM OPENCAST PROJECT	10/2015	3/2018	426.79	0.72

			(-) [3/2020]	(-) [426.79]	(0.00) [24]
1202	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (3/2021) [3/2021]	447.06 (473.22) [473.22]	417.24 (26.16) [72]
1203	KAKATIYA LONGWALL	12/2008	12/2012 (-) [0/0]	453.63 (-) [453.63]	121.91 (0.00) [0]
1204	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	50.72 (0.00) [36]
1205	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (3/2019) [3/2020]	397.09 (442.42) [442.42]	68.57 (45.33) [12]
1206	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2020]	417.33 (384.32) [384.32]	75.36 (-33.01) [44]
1207	KISTARAM OCP	11/2010	3/2015 (3/2021) [3/2021]	242.29 (164.04) [164.04]	104.08 (-78.25) [72]
1208	MANUGURU OC-II EXTENSION PHASE-II	3/2010	3/2012 (-) [0/0]	181.19 (-) [181.19]	159.87 (0.00) [0]
1209	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (3/2023) [3/2023]	418.97 (489.62) [489.62]	329.15 (70.65) [132]
1210	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (3/2021) [3/2021]	162.76 (349.28) [349.28]	2.82 (186.52) [72]
1211	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (3/2019) [3/2020]	430.45 (415.37) [415.37]	175.42 (-15.08) [48]
1212	RG OC -III EXTENSION (PHASE -II) PROJECT	6/2012	6/2015 (3/2019) [3/2019]	365.01 (-) [365.01]	192.63 (0.00) [0]
1213	RKP OCP PHASE-I	3/2010	3/2015 (3/2019) [3/2019]	209.78 (-) [209.78]	156.37 (0.00) [0]
1214	SHANTIKHANI LONGWALL PROJ-SCCL	10/2006	3/2012 (3/2024) [3/2024]	249.03 (448.86) [448.86]	203.77 (199.83) [144]
	<u>Petroleum</u>				
1215	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [4/2022]	611.00 (-) [611.00]	1.68 (0.00) [0]
	<u>Power</u>				
1216	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	7/2020 (2/2021) [2/2021]	10,598.98 (-) [10,598.98]	4,370.06 (0.00) [7]
	<u>Railways</u>				
1217	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (3/2017) [12/2020]	632.68 (-) [816.55]	666.41 (183.87) [57]
1218	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [3/2021]	636.38 (-) [636.38]	169.16 (0.00) [0]
1219	KONDAPALLI-KOTHAGUDEM	4/2013	/ (-) [0/0]	723.00 (-) [616.08]	0.00 (-106.92) [0]
1220	MACHERLA-NALGONDA(NL)(SCR)	7/1998	/ (-)	458.25 (-)	3.69 (0.01)

			[0/0]	[458.26]	[0]
1221	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [3/2022]	119.73 (185.00) [184.97]	0.00 (65.24) [0]
1222	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2022]	1,160.48 (-) [1,160.47]	222.40 (-0.01) [144]
1223	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1224	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [773.94]	284.16 (0.00) [0]
	Road Transport And Highways				
1225	REHABILITATION AND UPGRADATION OF NH -765 FROM KM 23.00 TO 108.00 (HYDERABAD TO DINDI SECTION) TO T	1/2014	3/2016 (-) [0/0]	340.00 (-) [340.00]	0.00 (0.00) [0]
1226	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [6/2019]	1,266.60 (-) [1,544.00]	1,429.59 (277.40) [33]
1227	CONSTRUCTION OF GODAVARI RIVER BRIDGE NEAR VENKATPURAM INCLUDING APPROACH ROAD ON NH- 202 UNDER LW E S	3/2011	12/2015 (-) [0/0]	218.31 (-) [339.82]	208.28 (121.51) [0]
1228	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	0.00 (0.00) [0]
1229	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1230	FOUR LANING OF NH-161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH-65) TO RAMSANPALLE (DESIGN KM 3	3/2018	/ (-) [0/0]	857.62 (-) [857.62]	0.00 (0.00) [0]
1231	FOUR LANING OF NH-161 FROM MANGLOOR (DESIGN KM 135.751/EXISTING KM 140.873) (DESIGN LENGTH =48.963 K	3/2018	/ (-) [0/0]	802.65 (-) [802.65]	0.00 (0.00) [0]
1232	FOUR LANING OF NH-161 FROM RAMSANPALLE (DESIGN KM 39.980/EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/ (-) [0/0]	950.63 (-) [950.63]	0.00 (0.00) [0]
1233	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/ (-) [0/0]	828.29 (-) [828.29]	0.00 (0.00) [0]
1234	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018 (-) [7/2019]	1,423.96 (-) [1,423.96]	605.35 (0.00) [8]
1235	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 154.00 TO 187.00 (MANGALWARPET TO MALLAPALLY SECTIO	12/2013	3/2016 (-) [0/0]	158.65 (-) [158.65]	103.50 (0.00) [0]
1236	REHABILITATION AND UPGRADATION OF NH -365 FROM KM 72.600 TO 121.00 (THANAMCHERLA TO JAMANDLAPALLY S	12/2013	3/2016 (-) [0/0]	177.18 (-) [177.18]	40.51 (0.00) [0]
1237	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016 (-) [0/0]	270.00 (-) [270.00]	19.84 (0.00) [0]
1238	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 121/0 TO 165/00 (OF VIJAYAWADA-JAGDALPUR RUDRAMPUR	10/2014	2/2017 (-) [0/0]	295.47 (-) [313.27]	0.00 (17.80) [0]
1239	REHABILITATION AND UPGRADATION OF NH-221 FROM KM 71/2 TO 121/0 (OF VIJAYAWADA-JAGDALPUR AP BORDER TO	10/2014	12/2016 (-) [0/0]	244.30 (-) [156.09]	0.00 (-88.21) [0]
1240	YAN TO NIRMAL SERE REHABILITATION AND UPGRADATION OF NH -222 FROM KM 615.00 TO 668.60 (KALCTION) TO	12/2013	3/2016 (-)	244.08 (-)	38.32 (0.00)

	TW		[0/0]	[244.08]	[0]
	<u>Urban Development</u>				
1241	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [3/2020]	209.84 (-) [209.84]	27.18 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Railways</u>				
1242	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (3,407.00) [3,407.00]	3,422.67 (2,265.00) [0]
1243	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
1244	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (984.97) [1,733.20]	1,563.33 (838.20) [0]
	<u>Road Transport And Highways</u>				
1245	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	288.63 (0.00) [0]
1246	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				
1247	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
1248	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
1249	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	<u>UTTAR PRADESH</u>				
	<u>Coal</u>				
1250	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (-) [11/2021]	17,237.00 (-) [17,237.80]	5,982.50 (0.80) [0]
	<u>Health And Family Welfare</u>				
1251	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [4/2020]	785.00 (-) [785.00]	39.35 (0.00) [0]
1252	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	/ (-) [4/2020]	268.84 (-) [268.84]	68.33 (0.00) [-]
	<u>Petroleum</u>				
1253	120 TMTA LPG BOTTLING PLANT AT GORAKHPUR UP	3/2014	9/2019 (-) [9/2019]	204.00 (-) [204.00]	0.00 (0.00) [0]
1254	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	12/2021 (-) [12/2021]	676.00 (-) [676.00]	8.18 (0.00) [0]
1255	BS-VI PROJECT AT MATHURA REFINERY	1/2018	9/2019 (-) [9/2019]	666.64 (-) [666.64]	323.69 (0.00) [0]
1256	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (-) [287.49]	117.30 (0.00) [0]
1257	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (-) [8/2020]	255.40 (-) [255.40]	0.31 (0.00) [0]

1258	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2021]	318.80 (-) [318.80]	30.32 (0.00) [3]
	<u>Power</u>				
1259	DHUKWAN SMALL HYDRO PROJECT	5/2011	2/2014 (2/2018) [10/2019]	195.42 (294.60) [294.60]	257.04 (99.18) [68]
1260	FGUTPP, UNCHAHAH STAGE-IV (1X500 MW)	7/2013	12/2016 (-) [0/0]	3,363.12 (-) [3,363.12]	2,244.00 (0.00) [0]
1261	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [9/2023]	11,089.42 (-) [11,089.42]	0.00 (0.00) [0]
1262	MUNPL-MEJA TPP - JV (2X660 MW)	4/2012	12/2016 (-) [8/2019]	9,750.89 (-) [9,750.89]	8,893.00 (0.00) [32]
1263	TANDA TPP STAGE-II (2X660 MW)	9/2014	3/2019 (3/2020) [3/2020]	9,188.98 (-) [9,188.98]	5,961.47 (0.00) [12]
	<u>Railways</u>				
1264	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	4/1999	12/2009 (-) [0/0]	108.00 (-) [432.72]	446.52 (324.72) [0]
1265	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/ (-) [0/0]	307.00 (-) [1,409.09]	0.00 (1,102.09) [0]
1266	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [1/2020]	600.00 (-) [366.71]	5.92 (-233.29) [-24]
1267	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP	3/2012	8/2018 (-) [1/2019]	199.75 (-) [378.26]	283.53 (178.51) [0]
1268	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [1/2022]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [0]
1269	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [3/2021]	1,183.25 (-) [1,183.25]	952.52 (0.00) [3]
1270	BHOJIPUR TANAKPUR VIA PILIBHIT	3/2008	/ (-) [3/2018]	195.64 (-) [435.00]	455.83 (239.36) [0]
1271	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/ (-) [0/0]	602.50 (-) [714.34]	4.62 (111.84) [0]
1272	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1273	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1274	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [245.39]	210.67 (125.39) [0]
1275	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI	4/2013	/ (-) [0/0]	654.00 (-) [654.00]	0.00 (0.00) [0]
1276	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/ (-) [0/0]	182.92 (-) [197.73]	0.00 (14.81) [0]
1277	GONDA - BAHRAICH (60 KIMS.) OF GONDA-BAHRAICH-SITAPUR-LUCKNOW	4/1997	4/1999 (-)	233.00 (-)	348.82 (85.42)

			[0/0]	[318.42]	[0]
1278	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [2/2020]	213.00 (-) [213.35]	2.05 (0.35) [46]
1279	JHANSI BINA DOUBLING	9/2016	3/2021 (-) [3/2021]	2,001.00 (-) [2,001.00]	0.00 (0.00) [0]
1280	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [3/2023]	4,329.53 (-) [4,329.53]	0.00 (0.00) [0]
1281	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/ (-) [0/0]	643.00 (-) [644.00]	0.00 (1.00) [0]
1282	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [12/2019]	528.57 (-) [528.57]	47.38 (0.00) [9]
1283	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [3/2020]	927.01 (-) [1,077.00]	1,052.21 (149.99) [12]
1284	MANDHANA - BRAHMAWART NEW LINE PROJECT.	4/1997	4/1999 (-) [3/2019]	609.04 (1,063.00) [1,807.88]	1,805.98 (1,198.84) [0]
1285	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020 (-) [3/2020]	668.70 (668.00) [668.00]	0.00 (-0.70) [0]
1286	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	405.85 (0.00) [21]
1287	MEERUT-MUZAFARNAGAR PATCH DL	4/2012	/ (-) [0/0]	377.44 (-) [377.44]	182.85 (0.00) [0]
1288	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [150.00]	0.00 (0.00) [66]
1289	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,345.00]	0.00 (2.00) [0]
1290	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [1/2020]	622.50 (427.00) [426.74]	107.98 (-195.76) [33]
1291	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2021]	2,436.21 (-) [2,436.21]	397.88 (0.00) [12]
1292	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [12/2019]	1,295.42 (-) [1,295.42]	183.61 (0.00) [-27]
1293	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	1.79 (-149.01) [16]
1294	UNCHAHAH-AMETHI	4/2012	/ (-) [0/0]	1,229.00 (-) [380.00]	4.12 (-849.00) [0]
1295	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	4/2006	3/2010 (-) [0/0]	369.90 (-) [1,581.53]	618.19 (1,211.63) [0]
1296	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [943.60]	238.36 (0.00) [33]
Road Transport And Highways					
1297	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-)	368.73 (-)	232.93 (0.00)

			[0/0]	[368.73]	[0]
1298	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30INTHE STATE	11/2010	3/2017 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
1299	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [351.34]	425.99 (0.00) [0]
1300	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [495.78]	617.93 (0.00) [0]
1301	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [9/2018]	291.36 (-) [291.36]	451.29 (0.00) [0]
1302	2-LANING WITH PS SITARGANJ BAREILY SECTION	6/2014	1/2016 (-) [0/0]	301.04 (-) [301.04]	207.94 (0.00) [0]
1303	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [11/2019]	2,016.00 (-) [2,016.00]	1,820.02 (0.00) [7]
1304	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,120.57]	0.00 (0.00) [0]
1305	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [2/2020]	1,668.00 (-) [1,668.00]	490.12 (0.00) [-]
1306	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	718.15 (0.00) [0]
1307	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [7/2020]	1,408.00 (-) [1,408.00]	5.71 (0.00) [-]
1308	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [4/2020]	1,737.00 (-) [1,737.00]	178.80 (0.00) [-]
1309	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)	3/2016	/ (-) [0/0]	1,404.50 (-) [1,404.50]	301.48 (0.00) [0]
1310	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [4/2019]	1,587.49 (-) [1,587.49]	274.39 (0.00) [0]
1311	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPU	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	225.06 (0.00) [0]
1312	6 LANING OF AGRA - ETAWAH BYPASS	7/2015	1/2019 (-) [1/2019]	1,657.20 (-) [1,657.20]	2,270.00 (0.00) [0]
1313	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [3/2020]	2,064.99 (-) [2,447.00]	1,377.59 (382.01) [0]
1314	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1315	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [4/2019]	676.73 (-) [676.73]	623.35 (0.00) [0]
1316	ALLAHABAD TO UP/MP BORDER SECTION OF NH-27 IN UTTAR PRADESH	6/2015	3/2018 (-) [0/0]	774.57 (-) [774.57]	0.00 (0.00) [0]
1317	BAHRAICH BYPASS TO RUPAIDHA SECTION NH-28C IN UTTAR PRADESH KM 99 TO150	1/2014	10/2016 (-) [0/0]	397.04 (-) [397.04]	0.00 (0.00) [0]

1318	BARABANKI TO JUNCTION WITH MDR 13 NEAR JARWAL SECTION OF NH-28C IN UTTAR PRADESH KM 0 TO 43	10/2013	3/2017 (-) [0/0]	317.76 (-) [317.76]	15.47 (0.00) [0]
1319	BAREILY-SITAPUR (NH-24)	3/2011	9/2013 (-) [0/0]	1,046.00 (-) [1,046.00]	805.19 (0.00) [0]
1320	CONSTN FOR FOUR LANING OF BABATPUR-VARANASI SECTION OF NH-56 (231) KM 263.00 TO 280.25 (EPC MODE)	3/2015	/ (-) [0/0]	629.74 (-) [629.74]	0.00 (0.00) [0]
1321	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	0.00 (0.00) [0]
1322	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [534.55]	361.36 (0.00) [0]
1323	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1324	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO	3/2018	/ (-) [0/0]	1,117.84 (-) [1,117.84]	0.00 (0.00) [0]
1325	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	350.99 (0.00) [0]
1326	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	0.00 (0.00) [0]
1327	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [6/2019]	1,081.57 (-) [1,081.57]	892.00 (0.00) [0]
1328	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [5/2020]	1,232.21 (-) [1,232.21]	637.48 (0.00) [-]
1329	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [5/2020]	1,989.00 (-) [1,989.00]	896.05 (0.00) [2]
1330	DEVELOPMENT OF SIX LANE EASTERN PERIPHERAL EXPRESSWAY (PKG-II)	9/2015	3/2018 (-) [0/0]	785.78 (-) [785.78]	839.63 (0.00) [0]
1331	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	1,998.25 (0.00) [0]
1332	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	0.00 (0.00) [0]
1333	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	0.00 (0.00) [0]
1334	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [925.40]	0.00 (0.00) [0]
1335	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	512.93 (0.00) [0]
1336	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-) [0/0]	667.00 (-) [667.00]	441.72 (0.00) [0]
1337	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	557.65 (0.00) [0]
1338	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018	815.28	478.12

			(-) [0/0]	(-) [815.28]	(0.00) [0]
1339	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1340	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (-) [11/2020]	1,373.28 (-) [1,373.28]	336.65 (0.00) [8]
1341	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [8/2020]	1,184.71 (-) [1,310.00]	253.84 (125.29) [5]
1342	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [4/2019]	899.00 (-) [899.00]	512.49 (0.00) [0]
1343	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.42 (0.00) [0]
1344	JUNCTION WITH MDR-13 NEAR JARWAL TO BAHRAICH SECTION OF NH-28C IN UTTAR PRADESH KM 43 TO 93	10/2013	10/2016 (-) [0/0]	283.45 (-) [283.45]	0.00 (0.00) [0]
1345	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [683.24]	565.33 (0.00) [0]
1346	R & U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [0/0]	326.99 (327.00) [326.99]	0.00 (0.00) [0]
1347	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [1,025.80]	0.00 (0.00) [0]
1348	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [1,115.28]	0.00 (0.00) [0]
1349	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270	10/2013	3/2017 (-) [0/0]	445.89 (-) [445.89]	0.00 (0.00) [0]
1350	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	0.00 (0.00) [0]
1351	SONOULI TO GORAKHPUR SECTION OF NH-29E IN UTTAR PRADESH KM 0/0 TO 80/0	10/2013	3/2017 (-) [0/0]	493.94 (-) [493.94]	0.00 (0.00) [0]
1352	STRENGTHENING WITH PROVISION OF PAVED SHOULDER IN KM. 0.00 TO 46.470 OF NH-96(330) EPC MODE	10/2014	10/2016 (-) [0/0]	227.74 (-) [227.74]	0.00 (0.00) [0]
1353	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1354	WIDENING AND STRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1355	WIDENING ANDSTRENGTHENING FROM KM.505.00 TO 538.00 OF NH-730 (EPC MODE)	12/2014	/ (-) [0/0]	207.88 (-) [207.88]	0.00 (0.00) [0]
1356	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	0.00 (0.00) [0]
	<u>Steel</u>				
1357	FORGED WHEEL PLANT	4/2014	9/2018 (-) [6/2019]	1,682.85 (-) [1,682.85]	1,094.53 (0.00) [9]
	<u>Urban Development</u>				

1358	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (7/2020) [3/2020]	171.72 (-) [171.72]	3.50 (0.00) [0]
1359	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [3/2019]	6,928.00 (6,928.00) [6,928.00]	2,536.77 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Petroleum</u>				
1360	SITARGANJ LPG PROJECT	2/2017	2/2020 (-) [10/2020]	160.10 (-) [160.10]	32.67 (0.00) [8]
	<u>Power</u>				
1361	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.16 (274.07) [0]
1362	NAITWAR MORI HEP	10/2017	12/2021 (-) [12/2021]	648.33 (-) [648.33]	207.87 (0.00) [0]
1363	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2020) [12/2020]	2,978.48 (-) [3,846.30]	3,938.20 (867.82) [93]
1364	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (5/2021) [6/2022]	1,657.00 (2,978.86) [5,024.35]	2,809.51 (3,367.35) [76]
1365	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (-) [12/2022]	2,491.58 (-) [4,105.30]	1,608.70 (1,613.72) [114]
	<u>Railways</u>				
1366	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	38.33 (126.80) [0]
1367	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1368	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2026]	16,216.00 (-) [16,216.00]	1,317.68 (0.00) [15]
	<u>Road Transport And Highways</u>				
1369	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [0/0]	403.36 (-) [403.36]	0.00 (0.00) [0]
1370	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [0/0]	417.24 (-) [417.24]	0.00 (0.00) [0]
1371	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	11/2012	7/2018 (-) [12/2019]	605.84 (-) [605.84]	722.46 (0.00) [17]
1372	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/ (-) [2/2020]	1,443.00 (-) [1,443.00]	275.21 (0.00) [-]
1373	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [0/0]	274.31 (-) [274.31]	0.00 (0.00) [0]
1374	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [7/2018]	1,383.78 (-) [1,383.78]	3.80 (0.00) [0]
1375	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (-) [5/2020]	248.00 (-) [248.00]	0.00 (0.00) [0]
1376	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO	3/2016	/ (-)	720.00 (-)	244.82 (0.00)

	KM 88		[10/2019]	[720.00]	[-]
1377	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [7/2019]	478.51 (-) [478.00]	409.17 (-0.51) [69]
1378	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (-) [11/2019]	232.81 (-) [232.81]	40.04 (0.00) [0]
1379	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (-) [11/2019]	283.51 (-) [284.00]	86.43 (0.49) [0]
1380	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	257.34 (-) [257.34]	0.00 (0.00) [0]
1381	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (-) [6/2019]	282.08 (-) [282.08]	45.92 (0.00) [0]
1382	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (-) [12/2019]	200.34 (-) [200.34]	35.76 (0.00) [0]
1383	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (-) [2/2020]	418.88 (-) [418.88]	74.52 (0.00) [0]
1384	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (-) [11/2019]	266.52 (-) [266.52]	78.85 (0.00) [0]
1385	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/ (-) [0/0]	293.68 (-) [293.68]	0.14 (0.00) [0]
1386	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/ (-) [0/0]	460.73 (-) [461.00]	0.74 (0.27) [0]
1387	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (-) [12/2019]	248.22 (-) [248.22]	57.01 (0.00) [0]
	<u>Urban Development</u>				
1388	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [10/2019]	114.26 (266.00) [266.00]	0.00 (151.74) [70]
	<u>WEST BENGAL</u>				
	<u>Coal</u>				
1389	JHANJRA COMBINED PR(3.50 MTY)	11/2015	3/2022 (-) [3/2022]	602.86 (-) [602.86]	307.30 (0.00) [0]
1390	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	0.00 (0.00) [0]
1391	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [0/0]	2,661.73 (-) [2,661.73]	215.58 (0.00) [0]
1392	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	0.00 (0.00) [0]
1393	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [3/2020]	1,055.05 (-) [1,055.05]	434.55 (0.00) [24]
	<u>Health And Family Welfare</u>				
1394	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [0/0]	244.00 (-) [244.00]	247.47 (0.00) [0]
1395	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-)	651.99 (-)	58.04 (0.00)

			[2/2020]	[651.99]	[-]
1396	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [0/0]	355.15 (-) [355.15]	122.43 (0.00) [0]
	<u>Petroleum</u>				
1397	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [6/2021]	3,712.00 (-) [3,696.00]	31.02 (-16.00) [-15]
1398	BS-VI PROJECT (PHASE-I) AT HALDIA REFINERY	5/2018	9/2019 (-) [9/2019]	2,934.40 (-) [2,934.40]	1,252.80 (0.00) [0]
1399	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020 (-) [12/2020]	1,740.00 (-) [1,740.00]	60.93 (0.00) [0]
1400	HALDIA BARAUNI PRODUCT PIPELINE	4/2016	12/2020 (-) [12/2020]	1,021.00 (-) [1,021.00]	4.45 (0.00) [0]
1401	HALDIA LPG IMPORT FACILITY	3/2015	10/2018 (6/2019) [6/2019]	694.00 (1,097.54) [694.00]	568.96 (0.00) [8]
1402	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (-) [3/2021]	163.02 (-) [163.02]	39.00 (0.00) [11]
	<u>Power</u>				
1403	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (1/2020) [1/2020]	454.11 (454.11) [454.11]	270.92 (0.00) [21]
1404	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (2/2022) [2/2022]	1,381.84 (-) [1,381.84]	429.14 (0.00) [29]
	<u>Railways</u>				
1405	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (3/2030) [3/2030]	1,027.40 (1,966.70) [2,373.00]	484.92 (1,345.60) [324]
1406	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [12/2017]	1,106.62 (-) [1,092.20]	671.23 (-14.42) [0]
1407	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [0/0]	255.64 (-) [272.20]	88.25 (16.56) [0]
1408	BHADUTOLA-JHARGRAM VIA LALGARH (NL)	4/2011	/ (-) [0/0]	289.64 (-) [760.00]	0.13 (470.36) [0]
1409	BOWAICHANDI-ARAMBAGH	4/2010	/ (3/2025) [3/2025]	267.37 (-) [620.00]	40.77 (352.63) [-]
1410	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [0/0]	573.78 (-) [268.52]	0.67 (-305.26) [0]
1411	DAKSHIN-BARASAL-LAKSHMIKANTAPUR	4/2009	2/2012 (-) [9/2016]	259.51 (-) [533.59]	145.59 (274.08) [0]
1412	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [4,874.58]	1,881.65 (0.00) [0]
1413	GHUTIASHARIF-CANNING (ER)	4/2009	12/2011 (-) [9/2012]	193.08 (-) [612.45]	156.24 (419.37) [0]
1414	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]

1415	MM FROM PANSKURA-GHATAL NL	4/2011	0/0 (3/2030) [3/2030]	276.69 (-) [426.00]	0.00 (149.31) [-]
1416	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [3/2020]	221.42 (-) [380.00]	102.82 (158.58) [-]
1417	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [3/2020]	297.32 (200.34) [614.00]	274.82 (316.68) [12]
1418	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [3/2020]	602.27 (-) [612.00]	93.63 (9.73) [-21]
1419	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.13 (435.44) [141]
1420	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (4,200.00) [2,913.50]	838.07 (-0.01) [108]
1421	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]
1422	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,092.40 (307.50) [108]
1423	TAMLUK DIGHA 88.9 KM WITH MM DESHPRAN NANDIGRAM 18.5 KM MM KANTHI EGRA 26.2 KM NADAKUMAR BOLAI	1/1991	12/2021 (12/2021) [12/2021]	1,013.45 (1,013.45) [1,428.00]	484.58 (414.55) [0]
1424	TAMLUK DIGHA,LINE DOUBLING (SER)	3/1984	6/2005 (-) [0/0]	293.97 (-) [749.69]	0.00 (455.72) [0]
1425	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2022]	1,188.91 (-) [1,620.01]	849.73 (431.10) [36]
1426	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,544.30 (2,355.23) [0]
	<u>Road Transport And Highways</u>				
1427	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [12/2019]	1,083.00 (-) [1,083.00]	225.46 (0.00) [18]
1428	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2020]	998.79 (-) [998.79]	1,837.93 (0.00) [82]
1429	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [6/2019]	1,078.84 (-) [1,078.84]	2,317.74 (0.00) [70]
1430	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [5/2019]	1,396.18 (-) [1,396.18]	2,614.84 (0.00) [56]
1431	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [1/2020]	361.15 (-) [361.15]	77.11 (0.00) [-]
1432	CONSTRUCTION OF MECHI BRIDGE AND APPROACHES ON INDIA-NEPAL BORDER LINKING KAKARVITTA AND PANITNAKI I	3/2017	6/2018 (-) [0/0]	158.65 (-) [158.65]	0.00 (0.00) [0]
1433	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (-) [11/2019]	271.17 (291.20) [291.20]	0.00 (20.03) [12]
1434	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [8/2021]	160.27 (-) [160.27]	0.00 (0.00) [24]

1435	CONSTRUCTION OF ROB –FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [12/2019]	229.37 (-) [229.37]	24.78 (0.00) [13]
1436	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (-) [8/2021]	236.78 (-) [236.78]	0.00 (0.00) [24]
1437	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (-) [10/2020]	254.30 (-) [254.30]	0.00 (0.00) [0]
1438	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [9/2019]	767.03 (-) [767.03]	228.73 (0.00) [13]
1439	KRISHNANAGAR-BERHAMPUR	2/2012	7/2014 (-) [5/2019]	702.16 (-) [702.16]	465.22 (0.00) [58]
1440	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 & NH-10 O	8/2014	11/2017 (-) [11/2017]	600.87 (720.97) [720.97]	0.00 (120.10) [0]
1441	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	8/2014	11/2017 (-) [7/2019]	823.20 (937.76) [937.76]	0.00 (114.56) [20]
1442	REHABILITATION & UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHANDE	1/2017	9/2019 (-) [12/2019]	396.86 (-) [396.86]	0.00 (0.00) [3]
1443	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (-) [1,261.98]	0.00 (0.00) [0]
1444	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (-) [8/2019]	279.70 (398.22) [398.22]	0.00 (118.52) [24]
1445	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	1/1991	3/2018 (-) [0/0]	322.00 (-) [322.00]	56.41 (0.00) [0]
1446	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [3/2019]	1,665.00 (-) [1,665.00]	1,901.17 (0.00) [0]
1447	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	3/2017	11/2019 (-) [11/2019]	202.69 (-) [202.69]	0.00 (0.00) [0]
1448	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (-) [11/2020]	218.70 (-) [218.70]	0.00 (0.00) [0]
1449	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (-) [9/2020]	426.18 (-) [426.18]	0.00 (0.00) [0]
	<u>Steel</u>				
1450	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (-) [9/2020]	263.36 (-) [263.36]	0.00 (0.00) [0]
	<u>Urban Development</u>				
1451	CONSTRUCTION OF PERMANENT CAMPUS OF IISER KOLKATA AT HARINGHANTA KALYANI NADIA	2/2014	8/2016 (-) [7/2019]	156.57 (-) [156.57]	154.15 (0.00) [35]
1452	CONSTRUCTION OF WORKSHOPS AND BUILDINGS FOR 24 NOS NEW INDUSTRIAL TRAINING INSTITUTES(ITI) WEST BENG	8/2012	3/2016 (-) [0/0]	185.37 (-) [185.37]	178.30 (0.00) [0]
1453	NSG AT KOLKATA	10/2014	4/2018 (-) [7/2019]	162.88 (-) [162.88]	115.59 (0.00) [15]
	Total			18,32,579.17 (3,99,900.79)	8,84,906.88 (3,28,734.01)

				[21,61,313.18]	

North-East Ongoing Project Detail's

Annexure-XX

Details of Central Sector Projects Costing Rs.150 crore and above (as on)					30.04.2019)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
1	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	12/2004	12/2009 (6/2019) [6/2019]	2,496.90 (7,419.34) [7,419.34]	7,131.10 (4,922.44) [114]
2	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (-) [0/0]	6,285.33 (-) [19,496.34]	10,723.47 (13,211.01) [0]
	<u>Road Transport And Highways</u>				
3	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [0/0]	394.00 (-) [394.00]	0.00 (0.00) [0]
4	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 0 TO KM 28	3/2015	5/2018 (-) [0/0]	235.08 (-) [235.08]	47.81 (0.00) [0]
5	2 LANING FROM PASIGHAT TO PANGIN SECTION OF NH-229 FROM KM 41.3 TO KM 58.42 (EXISTING KM 42 TO KM 59)	3/2015	5/2018 (-) [0/0]	194.11 (-) [194.11]	30.54 (0.00) [0]
6	2 LANING OF SINGER RIVER TO SIZOH NALA IN ARUNACHAL PRADESH ON EPC BASIS	10/2015	1/2019 (-) [0/0]	179.82 (-) [179.82]	8.99 (0.00) [0]
7	2-LANING WITH PAVED SHOULDER OF NH-52 FROM KM 583.450 TO KM 605.600 (EXISTING CHAINAGE FROM KM 583.450)	1/2016	11/2016 (-) [0/0]	183.65 (-) [183.65]	0.00 (0.00) [0]
8	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120	12/2016	1/2017 (-) [1/2020]	138.93 (155.00) [155.00]	0.00 (16.07) [36]
9	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (-) [0/0]	245.79 (-) [245.79]	0.00 (0.00) [0]
10	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM.	4/2016	10/2016 (-) [0/0]	198.00 (-) [198.00]	0.00 (0.00) [0]
11	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH	7/2015	10/2018 (-) [0/0]	197.16 (-) [197.16]	38.50 (0.00) [0]
12	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN	1/2017	3/2017 (-) [0/0]	1,253.10 (-) [1,253.10]	0.00 (0.00) [0]
13	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [0/0]	167.28 (-) [167.28]	0.00 (0.00) [0]
14	CONSTRUCTION OF TWOLANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXIS	2/2017	4/2017 (-) [0/0]	216.71 (-) [216.71]	0.00 (0.00) [0]

15	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
16	FOUR LANING OF ITANAGAR - HOLONGI SECTION OF NH-52A (19.26 KM) IN ARUNACHAL PRADESH UNDER PHASE 'A'	1/2011	/ (-) [0/0]	264.16 (-) [264.16]	0.00 (0.00) [0]
17	FUNDED) 2 LANING FROM CHANGLANG DISTRICT BOUNDARY -KHONSA (42.844KM) SECTION OF NH-52B IN THE STATE	1/2016	6/2016 (-) [0/0]	334.22 (-) [334.22]	0.00 (0.00) [0]
18	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH	11/2015	/ (-) [0/0]	434.06 (-) [434.06]	0.00 (0.00) [0]
19	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (-) [0/0]	284.09 (-) [284.09]	0.00 (0.00) [0]
20	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [0/0]	195.23 (-) [195.23]	0.00 (0.00) [0]
21	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [0/0]	203.36 (-) [203.36]	0.00 (0.00) [0]
22	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	194.66 (-) [194.66]	0.00 (0.00) [0]
23	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [0/0]	198.22 (-) [198.22]	0.00 (0.00) [0]
24	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR	3/2012	5/2012 (-) [0/0]	207.03 (-) [207.03]	0.00 (0.00) [0]
25	TWO LANING OF HOJ POTIN SECTION OF NH 229 (19.06 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PA	12/2009	9/2010 (-) [0/0]	165.00 (-) [165.00]	0.00 (0.00) [0]
26	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [0/0]	180.57 (-) [180.57]	0.00 (0.00) [0]
27	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 44+000 TO KM. 59+363 [EXIS	2/2017	4/2017 (-) [0/0]	168.32 (-) [168.32]	0.00 (0.00) [0]
28	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA	12/2011	2/2012 (-) [0/0]	156.63 (276.00) [276.00]	132.21 (119.37) [0]
29	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P	11/2010	3/2011 (-) [0/0]	305.49 (-) [305.49]	0.00 (0.00) [0]
30	TWO LANING OF YUPIA - HOJ SECTION (20.40 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH PACKAGE OF	12/2009	9/2010 (-) [0/0]	104.00 (-) [201.00]	0.00 (97.00) [0]
	<u>ASSAM</u>				
	<u>Health And Family Welfare</u>				
31	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (-) [5/2021]	875.00 (-) [875.00]	174.00 (0.00) [0]
32	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [0/0]	175.57 (-) [175.57]	113.50 (0.00) [0]
	<u>Petroleum</u>				
33	ASSAM RENEWAL PROJECT FOR GROUP A	3/2009	3/2013 (12/2019) [12/2019]	2,465.15 (-) [2,378.86]	2,132.88 (-86.29) [81]
34	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	86.47

			(-) [2/2020]	(-) [557.00]	(0.00) [0]
35	BS-VI PROJECT AT BONGAIGAON REFINERY	5/2018	9/2019 (-) [9/2019]	1,222.00 (-) [1,222.00]	403.95 (0.00) [0]
36	CONSTRUCTION OF GROUP GATHERING STATION AT BAGHJAN	7/2011	1/2019 (-) [9/2019]	350.00 (-) [350.00]	2.06 (0.00) [8]
37	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	6/2010	1/2014 (11/2019) [11/2019]	202.94 (341.70) [330.35]	129.67 (127.41) [70]
38	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (-) [9/2019]	423.00 (-) [423.00]	256.37 (0.00) [1]
39	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [2/2020]	543.91 (-) [682.90]	2.40 (138.99) [0]
40	INDMAX PROJECT AT BONGAIGAON REFINERY	2/2016	11/2019 (-) [11/2019]	2,582.00 (-) [2,582.00]	1,451.96 (0.00) [0]
41	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (5/2020) [5/2020]	249.85 (249.85) [244.70]	145.01 (-5.15) [0]
42	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE	9/2012	3/2015 (-) [0/0]	871.35 (-) [1,200.00]	565.63 (328.65) [0]
	<u>Railways</u>				
43	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [3/2019]	314.00 (486.96) [551.00]	660.21 (237.00) [0]
44	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2020]	2,232.32 (-) [2,182.00]	475.48 (-50.32) [-24]
45	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2021]	870.96 (-) [821.00]	399.61 (-49.96) [0]
46	LUMDING-HOJAI PATCH DOUBLING PROJECT	4/2012	3/2019 (-) [3/2019]	246.07 (614.81) [398.93]	413.64 (152.86) [0]
47	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2020]	385.20 (-) [1,532.00]	581.00 (1,146.80) [12]
	<u>Road Transport And Highways</u>				
48	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (-) [0/0]	268.08 (-) [268.08]	0.00 (0.00) [0]
49	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR	11/2010	2/2011 (-) [0/0]	470.20 (-) [470.20]	0.00 (0.00) [0]
50	4 LANING FROM END OF NAGAON BYPASS TO RANGAGARA (KM. 278.60 TO KM. 297.00) OF NH-37ON EPC BASIS	12/2015	12/2018 (-) [0/0]	225.02 (-) [159.20]	0.00 (-65.82) [0]
51	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	12/2015	6/2018 (-) [0/0]	223.30 (-) [223.30]	0.00 (0.00) [0]
52	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [0/0]	520.01 (-) [520.01]	0.00 (0.00) [0]
53	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [0/0]	588.95 (-) [588.95]	80.00 (0.00) [0]

54	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [0/0]	289.99 (-) [289.99]	0.00 (0.00) [0]
55	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [0/0]	252.00 (-) [252.00]	0.00 (0.00) [0]
56	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [0/0]	437.39 (-) [437.39]	21.86 (0.00) [0]
57	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [0/0]	294.17 (-) [294.17]	0.00 (0.00) [0]
58	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [4/2019]	217.61 (-) [217.61]	391.12 (0.00) [108]
59	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [5/2019]	160.00 (-) [167.98]	203.98 (7.98) [132]
60	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52	6/2016	1/2019 (-) [0/0]	829.00 (-) [829.00]	59.85 (0.00) [0]
61	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [0/0]	168.39 (-) [168.39]	16.84 (0.00) [0]
62	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [0/0]	818.00 (-) [818.00]	0.00 (0.00) [0]
63	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [0/0]	463.49 (-) [463.49]	9.26 (0.00) [0]
64	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [0/0]	829.00 (-) [829.00]	0.00 (0.00) [0]
65	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [0/0]	454.89 (-) [454.89]	22.74 (0.00) [0]
66	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [280.00]	422.51 (0.00) [0]
67	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [331.23]	340.12 (135.23) [0]
68	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [280.13]	195.35 (125.09) [0]
69	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [5/2019]	199.81 (-) [385.13]	211.69 (185.32) [121]
70	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [167.64]	268.94 (0.00) [0]
71	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [12/2019]	208.00 (-) [230.00]	308.94 (22.00) [140]
72	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [4/2019]	225.00 (-) [225.00]	312.79 (0.00) [130]
73	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [6/2019]	245.00 (174.34) [174.34]	270.88 (-70.66) [135]
74	STRENGTHENING AND CONSTRUCTION OF PAVED	5/2011	2/2018	176.22	0.00

	SHOULDERS INCLUDING REHABILITATION/REPAIRING OF BRIDGES FROM		(-) [0/0]	(-) [176.22]	(0.00) [0]
75	STRENGTHENING AND WIDENING OF NH-44 FROM KM.173.125 TO KM. 272.241 OF NH-44 AND ALONG THE KARIMGANJ	11/2014	2/2018 (-) [0/0]	218.31 (-) [218.31]	0.00 (0.00) [0]
	<u>MANIPUR</u>				
	<u>Railways</u>				
76	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [3/2020]	4,454.17 (-) [13,809.00]	9,672.60 (9,354.83) [108]
	<u>Road Transport And Highways</u>				
77	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2018]	517.57 (-) [517.57]	0.00 (0.00) [0]
	<u>Urban Development</u>				
78	NIT ACADEMIC BUILDING AT IMPHAL MANIPUR	2/2014	3/2015 (-) [10/2020]	216.69 (-) [216.69]	52.00 (0.00) [67]
	<u>MEGHALAYA</u>				
	<u>Health And Family Welfare</u>				
79	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [9/2019]	363.99 (-) [363.99]	145.51 (0.00) [16]
	<u>Railways</u>				
80	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [3/2021]	906.46 (1,202.33) [6,000.00]	260.68 (5,093.54) [0]
	<u>Road Transport And Highways</u>				
81	2 LANING OF SHILLONG NONGSTOIN SECTION OF NH 44 AND NONGSTOIN TURA STATE ROAD UNDER PHASE A OF SA	12/2010	2/2011 (-) [0/0]	1,494.48 (-) [1,494.48]	0.00 (0.00) [0]
82	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [5/2019]	306.28 (-) [306.28]	0.00 (0.00) [0]
83	JORBAT - BARAPANI	1/2011	1/2014 (-) [5/2019]	536.00 (-) [536.00]	844.31 (0.00) [64]
84	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [6/2019]	479.20 (-) [479.20]	475.02 (0.00) [13]
85	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (-) [0/0]	553.51 (-) [553.51]	159.00 (0.00) [0]
	<u>Urban Development</u>				
86	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [0/0]	151.33 (-) [151.33]	7.15 (0.00) [0]
	<u>MIZORAM</u>				
	<u>Railways</u>				
87	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (12/2020) [12/2020]	2,393.47 (2,393.48) [4,968.00]	2,671.70 (2,574.53) [81]
	<u>Road Transport And Highways</u>				
88	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (-) [0/0]	195.04 (-) [195.04]	130.82 (0.00) [0]
89	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (-) [0/0]	193.69 (-) [193.69]	0.00 (0.00) [0]
90	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC	4/2017	9/2019 (-)	519.09 (-)	0.00 (0.00)

	IMPROVEMENTS FRO		[9/2019]	[519.09]	[0]
91	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	404.29 (-) [404.29]	0.00 (0.00) [0]
92	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	428.11 (-) [428.11]	0.00 (0.00) [0]
93	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	518.53 (-) [518.53]	0.00 (0.00) [0]
94	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	640.07 (-) [640.07]	0.00 (0.00) [0]
95	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	642.96 (-) [642.96]	0.00 (0.00) [0]
96	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	473.18 (-) [473.18]	0.00 (0.00) [0]
97	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [9/2019]	537.82 (-) [537.82]	0.00 (0.00) [0]
98	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (-) [0/0]	624.41 (-) [624.41]	0.00 (0.00) [0]
	<u>NAGALAND</u>				
	<u>Railways</u>				
99	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [3/2020]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
100	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	4/2006	3/2015 (10/2021) [10/2021]	2,326.52 (2,446.57) [3,000.00]	734.88 (673.48) [79]
	<u>Road Transport And Highways</u>				
101	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [0/0]	239.30 (-) [239.30]	0.00 (0.00) [0]
102	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [0/0]	285.68 (-) [285.68]	0.00 (0.00) [0]
103	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [0/0]	282.98 (-) [282.98]	0.00 (0.00) [0]
104	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [0/0]	387.00 (-) [387.00]	0.00 (0.00) [0]
105	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [0/0]	500.09 (-) [500.09]	0.00 (0.00) [0]
106	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683	2/2017	4/2017 (-) [0/0]	507.68 (-) [507.68]	0.00 (0.00) [0]
107	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	339.57 (-) [339.57]	0.00 (0.00) [0]
108	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [0/0]	315.03 (-) [315.03]	0.00 (0.00) [0]
109	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	3/2018	9/2018 (-) [0/0]	240.64 (-) [240.64]	0.00 (0.00) [0]

110	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [0/0]	215.12 (-) [215.12]	0.00 (0.00) [0]
111	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [0/0]	215.79 (-) [215.79]	0.00 (0.00) [0]
112	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [0/0]	272.89 (-) [272.89]	0.00 (0.00) [0]
113	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [0/0]	323.98 (-) [323.98]	0.00 (0.00) [0]
114	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [0/0]	251.97 (-) [251.97]	0.00 (0.00) [0]
115	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [0/0]	237.72 (-) [237.72]	0.00 (0.00) [0]
116	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [8/2019]	373.07 (-) [373.07]	0.00 (0.00) [36]
117	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [8/2019]	396.52 (-) [396.52]	0.00 (0.00) [36]
118	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [8/2019]	429.52 (-) [429.52]	0.00 (0.00) [36]
119	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA	12/2010	2/2011 (-) [0/0]	1,296.00 (-) [1,296.00]	0.00 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
120	SEVOK RANGPO, NEFR	4/2008	12/2015 (-) [3/2020]	1,339.48 (-) [4,084.69]	383.92 (2,745.21) [51]
	<u>Road Transport And Highways</u>				
121	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (-) [0/0]	182.28 (-) [182.00]	24.36 (-0.28) [0]
122	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (-) [0/0]	151.59 (-) [151.59]	0.00 (0.00) [0]
123	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (-) [0/0]	166.27 (-) [166.27]	0.00 (0.00) [0]
124	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	0.00 (0.00) [0]
125	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [0/0]	290.05 (-) [290.05]	18.12 (0.00) [0]
126	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA	4/2017	11/2017 (-) [0/0]	318.42 (-) [318.42]	7.50 (0.00) [0]
127	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	0.00 (0.00) [0]
128	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	0.00 (59.37) [0]
	<u>TRIPURA</u>				

	<u>Railways</u>				
129	AGARTALA SABROOM, NL, NEFR	4/2008	3/2014 (12/2019) [3/2019]	1,142.00 (3,407.00) [3,407.00]	3,422.67 (2,265.00) [0]
130	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [10/2022]	569.63 (-) [650.00]	0.00 (80.37) [31]
131	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	4/1999	3/2007 (-) [4/2016]	895.00 (984.97) [1,733.20]	1,563.33 (838.20) [0]
	<u>Road Transport And Highways</u>				
132	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	288.63 (0.00) [0]
133	IMPROVEMENT/ WIDENING TO TWO LANING WITH PAVED SHOULDER OF UDAIPUR-SABROOM SECTION FROM KM 55.00 TO	5/2014	4/2017 (-) [0/0]	497.89 (-) [497.89]	70.47 (0.00) [0]
	<u>Urban Development</u>				
134	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [0/0]	149.73 (173.00) [175.94]	178.65 (26.21) [0]
135	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [0/0]	202.61 (227.00) [227.00]	199.95 (24.39) [0]
136	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [0/0]	175.49 (206.71) [206.71]	141.28 (31.22) [0]
	Total			79,059.82 (20,759.06) [1,23,470.91]	50,695.88 (44,411.09)
