


**290th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crores and above)
DECEMBER, 2009**



NHPC

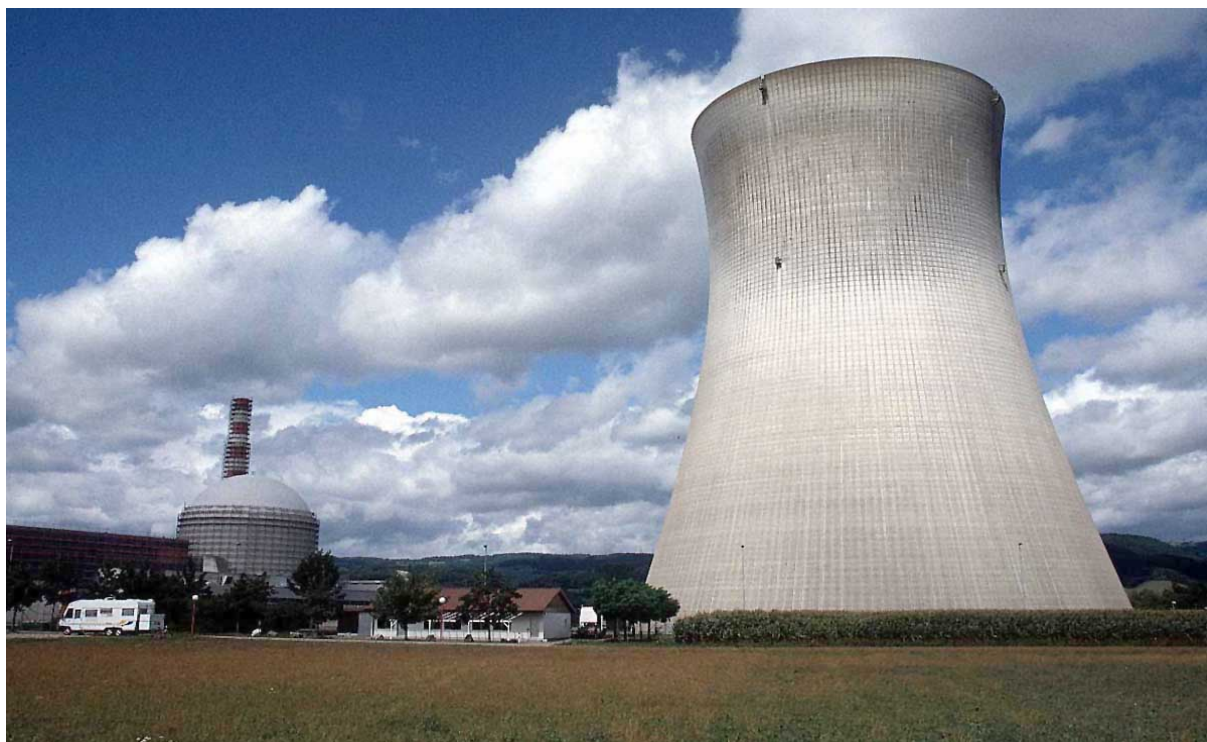

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -4
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2008-09	5-10
Summary of Projects	1-19
Sector wise analysis of projects	20-58

EXECUTIVE SUMMARY

The 290th Flash Report for December' 2009, that contains information on the status of 597 projects in the Central Sector, each costing Rs. 100 crores and above. During December' 2009, two projects reported completion and have been dropped from the monitor of this Ministry. During the month under reference, ten new projects have been added. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	152
2.	RAILWAYS	154
3.	POWER	85
4.	PETROLEUM	70
5.	COAL	43
6.	TELECOMMUNICATION	27
7.	STEEL	28
8.	SHIPPING & PORTS	18
9.	CIVIL AVIATION	9
10.	ATOMIC ENERGY	5
11.	URBAN DEVELOPMENT	3
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		597

2. Eighty one (81) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1-48 months in respect of projects relating to Civil Aviation, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways and Telecommunication sectors.

3. In the **Civil Aviation Sector**, 5 projects have shown additional delays of 1-11 months, however no specific reasons have been provided by the project authorities for such delays.
4. In the **Coal sector**, 4 projects have reported additional delays in the range of 2-6 months. Barsingsar Lignite Mine, Nevyeli Lignite Corporation (NLC), has reported additional delay of 2 months due to inadequate mobilization by the contractor. Thermal Power Station -II Expansion (1470 MW to 1970 MW) project of National Lignite Corporation, (NLC), has reported additional delay of 4 months due to delay in equipment erection and inadequate mobilization by the contractor. Kakatiya Laongwall project, has reported additional delay of 3 months however, no specific reason has been given by the project authorities. Barsingsar Thermal Power Station (2X125 MW) (NLC), has reported additional delay of 6 months due to delay in supply of indigenous equipments by Private and Public Sector and delay in equipment erection.
5. In the **Steel Sector**, 3 projects have reported additional delays in the range of 1-5 months. Rebuilding of coke oven battery No.4 has reported additional delay of one month due to delay in supply of equipments by the contractor. Rebuilding of Coke Oven Battery No. 1 & 2, Bokaro has reported additional delays of 2 months due to inadequate mobilization by the contractor. Pulverised Coal Injection System for Blast Furnace -1&2, has reported additional delay of 5 months due to delay in design & engineering works, and inadequate supplies & mobilization of resources for site activities by the contractor.
6. In the **Petroleum Sector**, 9 projects have reported additional delays in the range of 1-24 months. MSQ Upgradation Project at Panipat Refinery, Installation of FCCV at Mumbai Refinery and LPG Processing & Compression have reported additional delays of 1 month, 1 month, and 4 months , however, no specific reasons have been given by the concerned project authorities. Panipat Naphta Cracker Project has reported additional delay of 1 month due to delay in completion of Captive Power Plant by L&T. Installation of FCC Gasoline Desulphun Unit at Mathura Refinery has reported additional delay of 1 month, due to continuous delay in supply of compressor's piping and instrumentation items by BPCL. Chainsa-Jhajjar Pipeline Project has reported additional delay of 2 months due to delay in land acquisition. Revamping of WIN Platform at MH Asset has reported additional delay of 12 months due to high bid pricing. Development of C-Series field project has reported additional delay of 3 months due to late installation of well platforms

as two platforms capsized during transportation and needs to be re-fabricated and installed. Development of B-46 Cluster field has reported additional delay of 24 months due to revision of works.

7. In the **Power Sector**, 13 projects have reported additional delays in the range of 1-21 months. SEWA –II Hydro Electric Project of NHPC has reported additional delay of 1 month however no specific reason has been given by the project authorities. System Strengthening VII of Southern Region (PGCIL) has reported additional delay of 1 month due to delay in construction of 220 KV downstream bays by SEBs. SIPAT–II Supplementary Transmission System (PGCIL) project has reported additional delay of 1 month and Kudadankulam Atomic Power Project HEP Transmission Line (PGCIL) and Koldam Hydro Electric Project (PGCIL) have reported additional delay of 1 month, 1 month and 4 months respectively to match with the commissioning of linked Generation Projects. System Strengthening in South Western Part –B northern project has reported additional delay of 3 months due to non- availability of forest clearance. Enhancement of Transmission Capacity in East West Project of PGCIL, has reported additional delay of 2 months due to shutdown in switch yard. Farakka STPP Stage-III of NTPC has reported additional delay of 3 months due to delay in finalization of erection by M/s BHEL. Chamera, Stage III (NHPC) has reported additional delays of 4 months due to violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. NIMOO BAZGO Hydro Electric Project has reported additional delay of 4 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Korba STPP Stage III has reported additional delay of 6 months due to delay in various civil and structural works by M/s SPML. Parbati HEP stage III has reported additional delay of 7 months due to delay in award of E&M package on account of delay in receipt of decision from Government of India regarding participation of Chinese companies. Vishnugad Pipalkoti Hydro power Project (THDC) has reported additional delays of 21 months due to delay in land acquisition.

8. In the **Road Transport and Highways Sector**, 32 projects have reported additional delays in the range of 1-12 months. No specific reason has been reported by the project authorities for such additional delays.

9. In the **Railway Sector**, 8 projects have shown additional delays in the range of 1-48 months. Mansi-Purnia (Extension of Mansi-Saharsa) project, Tollyganj-Garia (MTP) project, Kurla-Bhandur, 5th and 6th P.I. Mumbai, Central Railways, Cuttack-Barang (LC), Palwal-Bhuteswar 3rd line doubling (NCR) and Mumbai Urban transport project phase-I have reported additional delays of 3 months, 3 months, 3 months, 6 months, 9 months and 22 months respectively, however, no specific reasons have been reported by the concerned project authorities. Rajatgarh-Barang (Line Doubling), ECoR has reported additional delay of 3 months due to slow progress of work by the contractor. Udhampur-Srinagar-Baramulla (NL), has reported additional delay of 48 months due to land acquisition of Army land.

10. In the **Telecommunication Sector**, 7 projects have reported additional delays in the range of 1-19 months. However, no specific reasons have been reported by the concerned project authorities.

Status as on 01.01.2010 in respect of completion of projects costing Rs.100 Crores and above in different sectors during 2009-10 is indicated in the following tables.



(Pankaj Jain)

Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	154	8
2	Road Transport & Highways	152	32
3	Power	85	13
4	Petroleum	70	9
5	Coal	43	4
6	Steel	28	3
7	Telecommunications	27	7
8	Shipping & Ports	18	0
9	Civil Aviation	9	5
10	Atomic Energy	5	0
11	Urban Development	3	0
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	597	81

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 100 Crore and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NHDP,P) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAVA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
14	PARADIP PORT, NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ, NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
July, 2009				
<u>Power</u>				
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
<u>Road Transport & Highways</u>				
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET, KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
<u>Telecommunications</u>				
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
August, 2009				
<u>Power</u>				
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
<u>Railways</u>				
26	MADURAI-DINDIGUL,(LD)(SR)(SR) - [N22000047]	73.19	-	181.81
<u>Road Transport & Highways</u>				
27	TIRUNELVEI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September,2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH- 7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR,NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
Shipping & Ports				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24
October,2009				
Petroleum				
40	DEVELOPMENT OF BASSEIN EAST (ONGCL)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100232]	985.17	03/2006	1,568.46
Railways				
41	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)(RAIL VIKAS NIGAM LTD.) - [220100221]	93.10	-	126.11
Telecommunications				
42	GSM EQUIPMENT OF 1015K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000044]	350.84	11/2008	182.06
43	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM(BHARAT SANCHAR NIGAM LIMITED) - [N26000059]	567.40	06/2009	241.85
November,2009				

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
44	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106272]	327.20	01/2009	457.60
45	HYDERABAD BANGALORE SECTION(NH-7)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106284]	611.44	03/2009	834.20
46	KADAL TO ARMUR, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000092]	271.73	11/2009	303.80
<u>Telecommunications</u>				
47	GSM BASED NETWORK PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000033]	174.36	11/2007	71.50
December,2009				
<u>Steel</u>				
48	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000024]	123.22	06/2009	77.00
<u>Telecommunications</u>				
49	GSM EQUIPMENT OF 1162K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000045]	325.00	12/2008	237.85

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2009				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95


Summary of projects on the Flash Report for the month of December, 2009

I. Project Implementation – Current Status:

Number of Projects Previous Month	593
Number of Projects Completed/Dropped/Frozen in Previous Month	4
Number of Projects Completed/Dropped/Frozen in Current month	2
Number of Projects Added in Current month	10
Number of Projects in Current Month	597

II. Brief Analysis


a) Project Status w.r.t Original Schedule: Out of 597 projects, 12 projects are ahead of schedule, 130 projects are on schedule and 330 projects are delayed. Of the balance, 82 projects do not have fixed dates of commissioning while 43 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

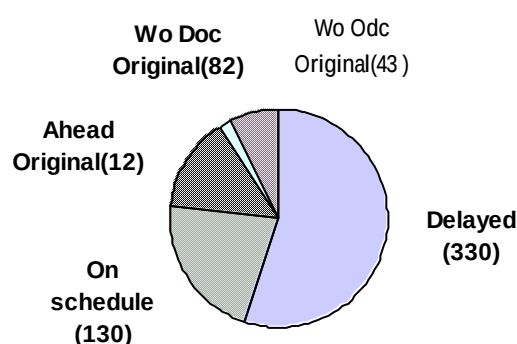

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 597 projects when sanctioned, was of the order of Rs. 574712.56 crore but this was subsequently revised to Rs. 621811.96 crore implying a cost overrun of 8.20%. The expenditure incurred on these projects till December, 2009 is Rs. 239577.46 crore, which is 38.53% of the revised cost of the projects.

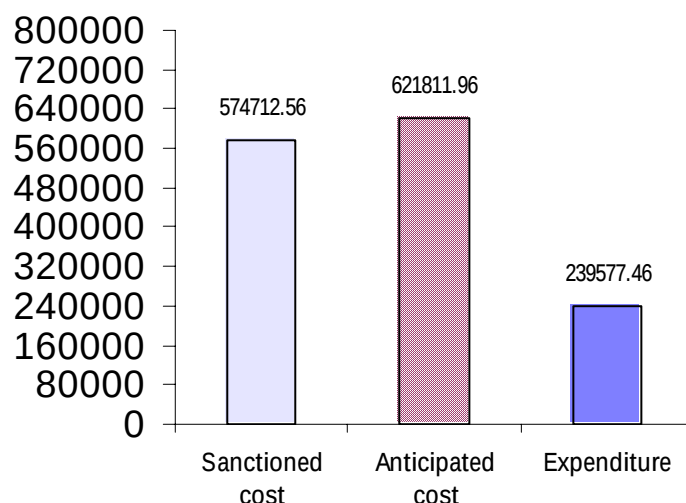

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	593
No of Projects Completed/Dropped/Frozen in Previous Month	4
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	10
No of Projects in Current Month	597

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original	330	12	130	43	82	597	55.28
Latest Approved	345	14	138	31	69	597	57.79

III. (A) Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Original	499	485,946.20	515,568.70	187,291.96	36.30	29,622.50	6.10
Latest Approved	98	88,766.36	106,243.26	52,285.50	49.20	17,476.90	19.70
Total	597	574,712.56	621,811.96	239,577.46	38.53	47099.4	8.20

III. (B) Delayed Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Original	330	328,346.44	381,716.85	180,823.07	47.40	53,370.41	16.30
Latest Approved	345	60,444.07	383,714.87	182,089.33	47.50	323,270.80	534.80

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				(Cost/ Expenditure in Rs. crore)	
		Sanctioned	Anticipated	Expenditure	%	Cost overrun (Rs. Crore)	%
Latest Approved	81	61,339.99	73,766.41	46,233.68	62.70	12,426.42	20.30
Total	81	61,339.99	73,766.41	46,233.68	62.68	12426.42	20.26

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Telecommunications</u>						
GSM EQUIPMENT OF 1162K LINES PH-4.5	03/2008	325.00	12/2008	325.00	12/2009	237.85
<u>Steel</u>						
INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA	07/2007	123.22	06/2009	123.22	12/2009	77.00

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Petroleum</u>					
CAPACITY EXP. CUM MODERNISATION PH-II	9/2009	2,591.80	12/2009	3,941.41	2/2010
<u>Railways</u>					
BHAIRABI SAIRONG	4/2008	619.34	4/2014	619.34	4/2014
<u>Petroleum</u>					
BINA KOTA PIPE LINE PROJECT	7/2007	405.82	12/2009	405.82	3/2010
<u>Railways</u>					
BHAKURA DAMODAR	3/1998	282.70	7/2008	325.17	7/2008
<u>Petroleum</u>					
SHORT TERM LOW COST MUMBAI REFINERY	12/2006	390.00	1/2010	230.00	1/2010
<u>Railways</u>					
TAMLUK DIGHA	3/1984	293.97	6/2005	293.97	4/2012
AGARTALA SABROOM	4/2008	813.34	3/2014	813.34	3/2014
<u>Petroleum</u>					
REFRIGERATED LPG STORAGE AT JNPT	6/2008	304.40	12/2010	304.40	12/2010
BINA DESPATCH TERMINAL	5/2007	490.71	12/2009	639.11	3/2010
HYDROCRACKER REVAMP & SETTING	2/2008	825.00	12/2011	825.00	12/2011

VII. Milestones (Cumulative due & achieved)

Total	1993
Achieved up to month	755

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Civil Aviation</u>						
CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	245.58	245.58	12/2008	11/2009	12/2009	1
C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE	135.60	135.60	10/2009	02/2010	03/2010	1
C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR	129.65	129.65	09/2009	12/2009	03/2010	3
C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA	135.04	135.04	09/2009	12/2009	03/2010	3
C/O INTEGERATED CARGO COMPLEX(PH-III) AT CHENNAI A	144.94	144.94	04/2010	01/2010	12/2010	11
<u>Coal</u>						
BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)	254.07	254.60	06/2009	12/2009	02/2010	2
KAKATIYA LAONGWALL	453.63	453.63	12/2012	12/2012	03/2013	3
TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	2,453.57	06/2009	02/2011	06/2011	4
BARSINGSAR TPS (2X125MW) (NLC)	1,114.18	1,626.09	06/2009	03/2010	09/2010	6
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO.-4	248.94	248.94	08/2009	12/2009	01/2010	1
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	04/2010	10/2010	12/2010	2
Pulverised coal injection system for bf-1&2	125.00	133.00	09/2009	03/2010	08/2010	5
<u>Petroleum</u>						
PANIPAT NAPHTA CRACKER PROJECT	12,138.00	14,439.00	09/2009	02/2010	03/2010	1
INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE	348.00	348.00	12/2009	01/2010	02/2010	1
MSQ UPGRADATION PROJECT AT PANIPAT REFINERY	1,131.00	1,131.00	12/2009	12/2009	01/2010	1
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	05/2010	06/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
CHAINSA-JHAJJAR PIPE LINE PROJECT	967.77	571.64	09/2009	12/2009	02/2010	2
DEVELOPMENT OF C-SERIES FIELDS	3,195.16	1,800.00	12/2008	12/2009	03/2010	3
LPG PROCESSING & COMPRESSION	142.00	139.07	10/2009	12/2009	04/2010	4
REVAMPING OF WIN PLATFORM AT MH ASSET	333.40	333.40	05/2010	05/2010	05/2011	12
DEVELOPMENT OF B-46 CLUSTER FIELD	1,436.21	1,436.21	07/2010	05/2010	05/2012	24
Power						
SEWA- II H.E.P (NHPC)	665.46	1,016.74	09/2007	12/2009	01/2010	1
SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL)	279.30	340.14	07/2009	11/2009	12/2009	1
SIPAT-II SUPP. TRANS. SYSTEM (PGCIL)	813.67	777.15	06/2008	11/2009	12/2009	1
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	1,779.29	1,896.65	11/2008	02/2010	03/2010	1
ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST	103.80	103.80	06/2009	12/2009	02/2010	2
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	08/2010	11/2010	3
SYSTEM STRENGTHENING IN SOUTH-WESTERN PART- B NORTHERN	150.26	153.24	10/2009	12/2009	03/2010	3
CHAMERA,STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	08/2010	12/2010	4
KOLDAM HEP TRANSMISSION LINE (PGCIL)	464.91	464.91	09/2008	11/2009	03/2010	4
NIMOO BAZGO HYDROELECTRIC PROJECT	611.01	611.02	08/2010	08/2010	12/2010	4
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	02/2010	08/2010	6
PARBATI H.E.P. STAGE -III (NHPC)	2,304.56	2,304.52	10/2010	11/2010	06/2011	7
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	2,491.58	06/2013	06/2013	03/2015	21
Railways						
TOLLYGANJ-GARIA(MTP)	907.69	1,032.76	12/2006	03/2010	06/2010	3
RAJATGARH-BARANG(LD),ECOR	166.16	243.40	N.A.	03/2010	06/2010	3
KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR	49.84	136.45	03/2002	12/2009	03/2010	3
MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN	114.01	322.87	N.A.	12/2009	03/2010	3
CUTTACK - BARANG (LD)	127.13	135.10	N.A.	06/2010	12/2010	6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	240.00	329.70	03/2009	06/2010	03/2011	9
MUMBAI URBAN TRANSPORT PROJECT PHASE-I	3,125.20	4,174.00	12/2010	12/2010	10/2012	22
UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	2,500.00	11,270.00	03/2001	12/2012	12/2016	48
Road Transport & Highways						
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7	407.60	407.60	06/2010	09/2010	06/2010	-3
ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2	440.93	440.93	12/2006	11/2009	12/2009	1
ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2	534.39	534.39	05/2007	11/2009	12/2009	1
NALBARI TO BIJNI (AS-8)	200.00	200.00	06/2008	06/2010	07/2010	1
NEW MANGALORE PORT NH-17 AND 48	196.50	196.50	06/2008	12/2009	01/2010	1
AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA	402.80	402.80	03/2009	11/2009	12/2009	1
PANIPAT TO PANCHI GUJRAN, NH-1	109.00	109.00	10/2008	11/2009	12/2009	1
SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS	110.00	110.00	07/2008	11/2009	12/2009	1
ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT	450.00	450.00	07/2008	11/2009	12/2009	1
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120	323.36	323.36	03/2008	11/2009	01/2010	2
SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47	469.80	469.80	12/2008	11/2009	01/2010	2
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5	480.00	480.00	11/2007	12/2009	03/2010	3
PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57	276.00	276.00	04/2008	12/2009	03/2010	3
PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57	310.00	310.00	04/2008	12/2009	03/2010	3
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	11/2009	02/2010	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)	261.00	261.00	08/2008	12/2009	03/2010	3
FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	09/2008	12/2010	03/2011	3
SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4)	100.50	100.50	04/2008	12/2009	03/2010	3
THANJAUR-TRICHY, NH-67(NHAI)	280.00	280.00	06/2009	03/2010	06/2010	3
PADALUR-TRICHY, NH-45	320.00	320.00	05/2009	11/2009	02/2010	3
GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)	399.75	399.75	03/2005	11/2009	03/2010	4
JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25	158.06	158.06	08/2005	12/2009	06/2010	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	227.00	227.00	12/2008	06/2010	12/2010	6
THRISSUR TO ANGAMALI (NH-47)	312.50	312.50	03/2009	12/2009	06/2010	6
NALBARI TO BIJNI (AS-9)	142.00	142.00	06/2008	06/2010	12/2010	6
TRICHY - DINDIGUAL NH-45	576.00	576.00	07/2010	07/2010	01/2011	6
GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	412.78	479.54	11/2007	11/2009	06/2010	7
KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A	110.00	110.00	12/2004	03/2010	12/2010	9
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	210.00	210.00	04/2007	12/2009	12/2010	12
GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	275.00	275.00	09/2007	12/2009	12/2010	12
HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	220.00	220.00	09/2007	12/2009	12/2010	12
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A	284.00	284.00	05/2008	12/2009	12/2010	12
Telecommunications						
GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G)	373.94	373.94	12/2008	12/2009	01/2010	1
GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN	335.91	335.91	03/2009	12/2009	01/2010	1
UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	149.15	149.15	06/2009	12/2009	01/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
Assam Telecom Circle, Phase-V.I, 2G & 3G	336.81	336.81	01/2009	11/2009	01/2010	2
EXPANSION OF 750K GSM LINES	278.16	278.16	12/2008	10/2009	01/2010	3
DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES	463.61	463.61	12/2009	12/2009	03/2010	3
500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB	134.25	133.75	06/2008	06/2008	01/2010	19

Number of projects reporting additional delay = 81

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	25,054.29	25,054.29	26,308.29
Civil Aviation	9	4,832.24	4,826.73	4,832.24
Coal	43	26,110.40	27,286.87	27,629.32
Mines	1	4,091.51	4,091.51	4,091.51
Steel	28	45,473.36	45,473.36	49,248.38
Petroleum	70	141,026.24	149,576.85	159,564.03
Power	85	165,980.96	167,795.04	168,458.49
Health & Family Welfare	1	71.18	422.60	443.15
Railways	154	52,042.12	65,037.64	96,970.60
Road Transport & Highways	152	44,015.85	44,015.85	44,240.60
Shipping & Ports	18	12,475.83	12,475.83	12,747.59
Telecommunications	27	11,266.06	11,266.06	10,884.73
Urban Development	3	14,596.67	16,847.03	15,206.03
Water Resources	1	542.90	542.90	1,187.00
Grand total	597	547,579.61	574,712.56	621,811.96


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	5
Number of Projects on schedule	2
Number of Projects Delayed	3

Brief Analysis


Project Status w.r.t Original Schedule: Out of 5 projects, 1 projects are on schedule and 4 projects are delayed.

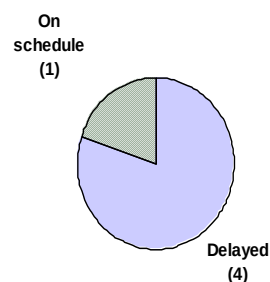

Investment Scenario

Figures are in Rs.

The total cost of implementation of 5 projects when sanctioned, was of the order of Rs. 25054.29 Crores but this was subsequently revised to Rs. 26308.29 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 19398.61 Crores.

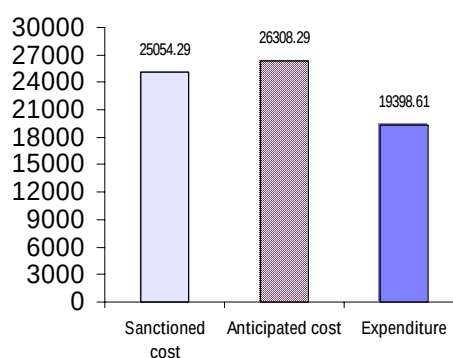


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	3
Number of Projects Delayed	6


Brief Analysis

Project Status w.r.t Original Schedule:
Out of 9 projects, 3 projects are on schedule, 5 projects are delayed and 1 project is ahead.



Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 4832.24 Crores but this was subsequently revised to Rs. 4832.24 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 1021.78 Crores.

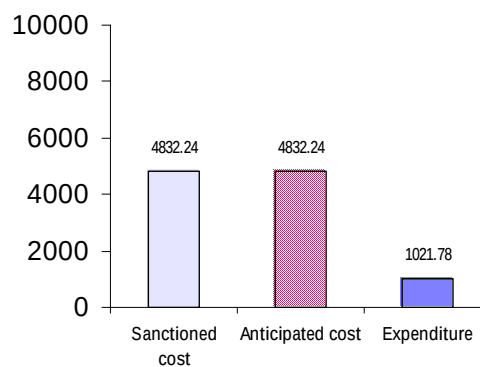


3. Sector: - Coal

Number of Projects	43
Number of Projects on schedule	16
Number of Projects Delayed	22
Number of Projects Ahead	4
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 43 projects, 16 projects are on schedule, 22 projects are delayed and 4 projects are ahead and 1 Project Wo_Doc.

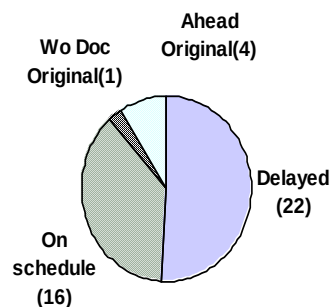

Investment Scenario

The total cost of implementation of 43 projects when sanctioned, was of the order of Rs. 26110.40 Crores but this was subsequently revised to Rs. 27629.32 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 10385.54 Crores

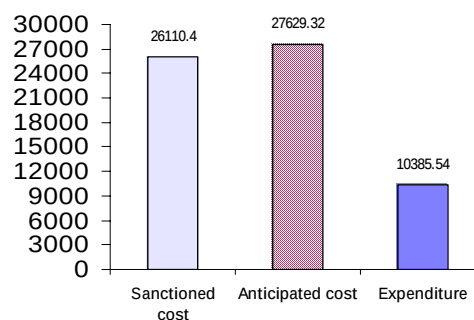


4. Sector: - Petroleum

Number of Projects	70
Number of Projects on schedule	29
Number of Projects Delayed	39
Number of Projects Ahead	2


Brief Analysis

Project Status w.r.t Original Schedule: Out of 70 projects, 29 projects are on schedule, 39 projects are delayed and 2 projects are ahead.



Investment Scenario

The total cost of implementation of 70 projects when sanctioned, was of the order of Rs. 141026.24 Crores but this was subsequently revised to Rs. 159524.03 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 44995.27 Crores.

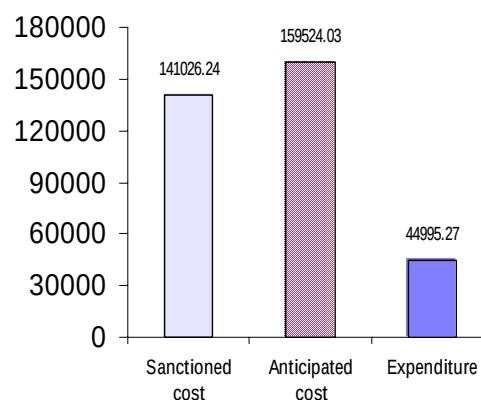


5. Sector: - Power

Number of Projects	85
Number of Projects on schedule	43
Number of Projects Delayed	40
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 85 projects, 43 projects are on schedule, 40 projects are delayed, 1 projects is Wo_Doc_Original and 1 projects is Wo_Odc_Original

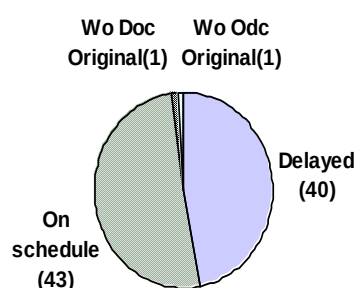

Investment Scenario

The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 165980.96 Crores but this was subsequently revised to Rs. 168458.49 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 50769.05 Crores.

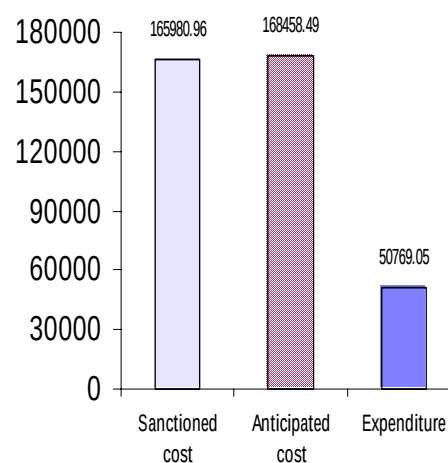


6. Sector: - Railways

Number of Projects	154
Number of Projects on schedule	9
Number of Projects Delayed	41
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	60
Number of Projects Wo_Odc_Original	43


Brief Analysis

Project Status w.r.t Original Schedule: Out of 154 projects, 9 projects are on schedule, 41 projects are delayed, 1 projects is ahead. 60 projects are Wo_Doc_Original and 43 projects are Wo_Odc_Original

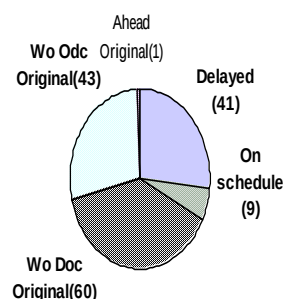

Investment Scenario

The total cost of implementation of 154 projects when sanctioned, was of the order of Rs. 52042.12 Crores but this was subsequently revised to Rs. 96694.33 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 40991.32 Crores.

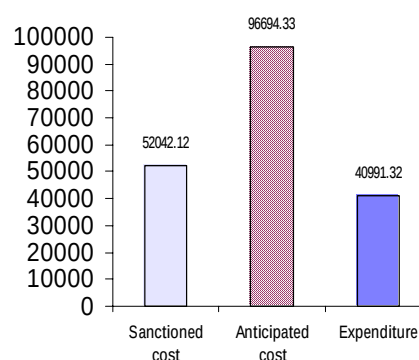


7. Sector: - Road Transport and Highways

Number of Projects	152
Number of Projects on schedule	14
Number of Projects Delayed	134
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 152 projects, 14 projects are on schedule, 134 projects are delayed, 3 projects are ahead and 1 projects is Wo_Doc_Original.

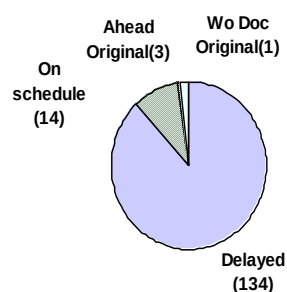

Investment Scenario

The total cost of implementation of 152 projects when sanctioned, was of the order of Rs. 44015.83 Crores but this was subsequently revised to Rs. 44240.60 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 31895.19 Crores.

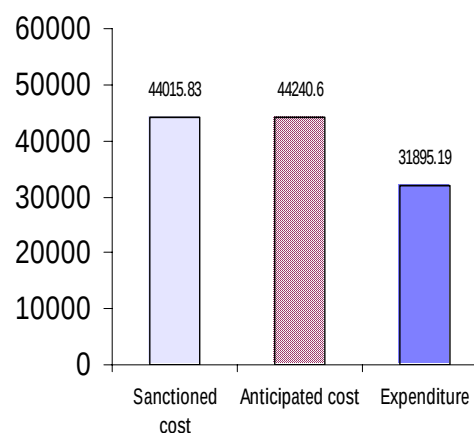


8. Sector: - Shipping and Ports

Number of Projects	18
Number of Projects on schedule	9
Number of Projects Delayed	5
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status w.r.t Original Schedule: Out of 18 projects, 9 projects are on schedule, 5 projects are delayed, 2 projects are ahead and 2 projects are Wo_Doc_Original.

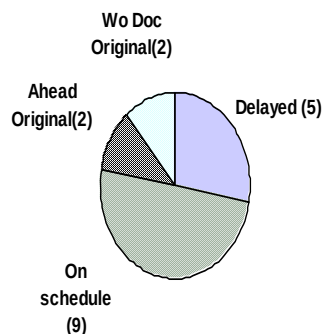

Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs.12475.83 Crores but this was subsequently revised to Rs. 12747.59 Crores. The expenditure incurred on these projects till September, 2009 is Rs. 2993.67 Crores.

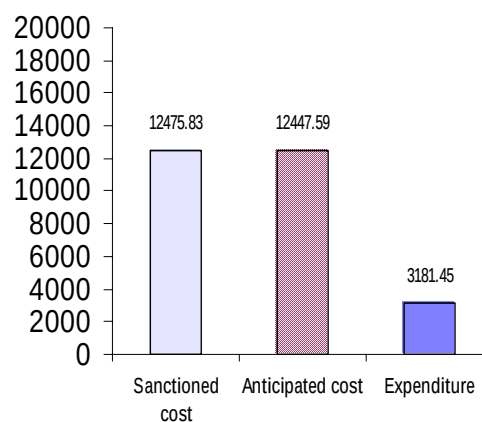


9. Sector: - Steel

Number of Projects	28
Number of Projects on schedule	4
Number of Projects Delayed	22
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status w.r.t Original Schedule: Out of 28 projects, 4 projects are on schedule, 22 projects are delayed and 2 projects are Wo_Doc_Original .

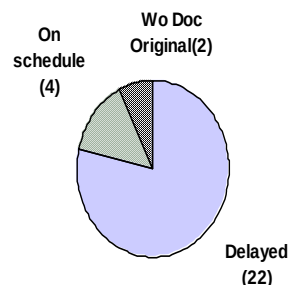

Investment Scenario

The total cost of implementation of 28 projects when sanctioned, was of the order of Rs. 45473.36 Crores but this was subsequently revised to Rs. 49248.38 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 15693.15 Crores.

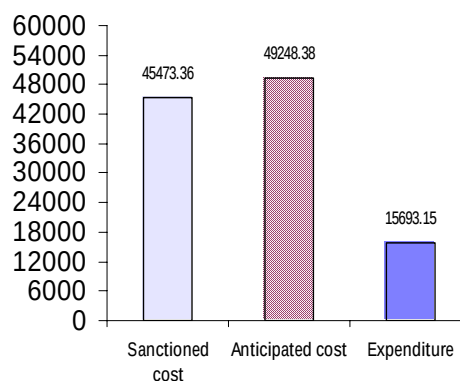


10. Sector: - Telecommunications

Number of Projects	27
Number of Projects on schedule	1
Number of Projects Delayed	23
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status w.r.t Original Schedule: Out of 27 projects, 1 projects are on schedule, 23 projects are delayed and 3 projects are Wo_Doc_Original .

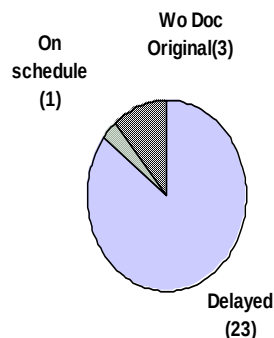

Investment Scenario

The total cost of implementation of 27 projects when sanctioned, was of the order of Rs. 11266.06 Crores but this was subsequently revised to Rs. 10884.73 Crores. The expenditure incurred on these projects till December, 2009 is Rs. 3552.56 Crores.

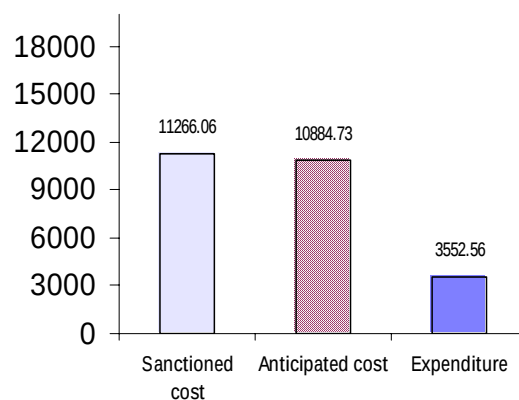

(Dec,2009)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL) - [020100042]	04/2002	3,072.00	3,072.00	2,070.00	02/2008	02/2010	24(O)	73/75
2	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,476.00	10/2009 09/2007	03/2010	30(R1)	71/75
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,446.00	12/2008	03/2011	27(O)	61/119
4	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	356.94	04/2011	04/2011	0(O)	0/0
5	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,049.67	09/2010	09/2011	12(O)	8/80
Total			25,054.29	26,308.29	19,398.61				213/349
<u>Civil Aviation</u>									
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	146.12	02/2009	10/2009	8(O)	1/24
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING - [N04000016]	10/2006	245.58 295.00	245.58	74.80	12/2008	12/2009	12(O)	1/28
8	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65 135.72	129.65	31.20	09/2009 03/2010	03/2010	0(R3)	0/0
9	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04	135.04	58.25	09/2009	03/2010	6(O)	0/0
10	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60	135.60	44.76	10/2009	03/2010	5(O)	0/0
11	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
12	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94	144.94	21.86	04/2010	12/2010	8(O)	0/1
13	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE - [N04000038]	08/2008	1,273.00 1,212.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
14	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	245.58	05/2011	05/2011	0(O)	0/0
Total			4,832.24	4,832.24	1,021.78				2/53
<u>Coal</u>									
15	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC) - [060100088]	10/2004	2,161.28 2,295.93	2,295.93	1,715.75	06/2009	02/2010	8(O)	29/23

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07 254.60	254.60	207.91	06/2009 -	02/2010	8(O)	18/21
17	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55 -	1,667.55	928.56	03/2010 -	03/2010	0(O)	3/7
18	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53 -	1,268.53	756.02	03/2010 -	03/2010	0(O)	2/6
19	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88 -	789.88	134.44	03/2010 -	03/2010	0(O)	0/1
20	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39 -	131.39	358.84	03/2010 -	03/2010	0(O)	0/0
21	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08 -	172.08	471.91	03/2009 -	03/2010	12(O)	0/0
22	KTK OC Sector-I - [N06000077]	01/2008	91.50 -	128.16	115.33	09/2010 -	03/2010	-6(O)	0/0
23	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18 1,626.09	1,626.09	1,347.66	06/2009 -	09/2010	15(O)	32/26
24	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74 -	116.54	246.00	03/2007 -	03/2011	48(O)	0/0
25	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 2,453.57	2,453.57	1,873.08	06/2009 -	06/2011	24(O)	23/24
26	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35 -	122.35	-	03/2010 12/2011	12/2011	0(R3)	0/0
27	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18 -	287.17	-	11/2009 -	01/2012	26(O)	0/0
28	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96 -	302.96	55.66	03/2010 -	03/2012	24(O)	0/4
29	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66 341.63	341.63	100.38	03/2011 -	03/2012	12(O)	0/0
30	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04 -	746.04	134.78	03/2012 -	03/2012	0(O)	0/1
31	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03 -	249.03	31.43	03/2012 -	03/2012	0(O)	0/0
32	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40 -	259.40	-	03/2012 -	03/2012	0(O)	0/0
33	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28 -	207.28	244.00	03/2012 -	03/2012	0(O)	0/0
34	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34 -	212.34	17.34	03/2013 -	09/2012	-6(O)	2/11
35	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54 -	4,904.54	502.63	08/2012 -	09/2012	1(O)	0/0
36	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65 -	1,188.31	590.59	03/2011 03/2013	03/2013	0(R3)	0/4
37	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	706.40	12.13	07/2012 -	03/2013	8(O)	0/1
38	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78 -	467.78	11.29	03/2013 -	03/2013	0(O)	0/7
39	KANIHA OCP - [N06000035]	12/2007	457.77 -	457.77	48.96	03/2012 -	03/2013	12(O)	0/0
40	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63 -	453.63	42.48	12/2012 -	03/2013	3(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	NARAYANKURI UG - [N06000059]	02/2009	149.06	149.06	-	03/2013	03/2013	0(O)	0/0
42	CHITRA EAST OCP - [N06000060]	08/2007	112.69	112.69	-	11/2010	03/2013	28(O)	0/0
43	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	172.00	03/2013	03/2013	0(O)	0/0
44	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	127.64	03/2014	11/2013	-4(O)	1/1
45	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,352.04	26.98	03/2014	03/2014	0(O)	1/1
46	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	-	06/2014	03/2014	-3(O)	0/0
47	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	3.00	03/2010	03/2014	48(O)	0/0
48	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	03/2014	03/2014	0(O)	0/0
49	KARTALI (EAST) OC - [N06000076]	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
50	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	23.23	03/2013	03/2015	24(O)	0/0
51	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
52	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
53	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58	135.58	-	03/2015	03/2015	0(O)	0/0
54	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
55	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	54.70	03/2014	03/2016	24(O)	0/0
56	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	12(O)	0/0
57	AUGMENTATION OF PRODUCTION AT SAPRI UG MINE - [N06000058]	09/1987	147.86	147.86	25.50	03/2012	-	-	0/0
Total			26,110.40	27,629.32	10,385.54				111/138
<u>Mines</u>									
58	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
<u>Steel</u>									
59	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	196.00	10/2009	10/2009	0(O)	2/21
60	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	157.00	08/2009	01/2010	5(O)	0/0
61	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	210.00	06/2009	01/2010	7(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
62	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	89.00	10/2009	01/2010	3(O)	0/0
63	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	54.00	01/2010	01/2010	0(O)	0/0
64	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88	119.88	38.00	12/2009	02/2010	2(O)	0/0
65	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73	133.92	84.77	05/2008	03/2010	22(O)	0/2
66	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	221.00	09/2009	03/2010	6(O)	0/0
67	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	477.00	08/2009	03/2010	7(O)	0/0
68	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,134.00	03/2010	06/2010	3(O)	0/0
69	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	42.02	06/2010	06/2010	0(O)	0/0
70	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00	133.00	36.47	09/2009	08/2010	11(O)	0/0
71	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	84.40	12/2009	08/2010	8(O)	0/0
72	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	80.00	02/2010	08/2010	6(O)	0/0
73	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	113.00	04/2010	12/2010	8(O)	0/0
74	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50	145.00	6.64	12/2010	12/2010	0(O)	0/0
75	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
76	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30	232.93	45.00	07/2009	05/2011	22(O)	0/0
77	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.33	10.00	08/2009	05/2011	21(O)	0/0
78	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	4,620.00	10/2009	06/2011	20(O)	0/126
79	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
80	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	4,981.00	07/2010	06/2011	11(O)	0/0
81	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,316.00	584.00	12/2010	10/2011	10(O)	0/0
82	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
83	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	6,171.00	884.00	02/2011	03/2012	13(O)	0/0
84	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	4,792.00	1,208.00	05/2011	09/2012	16(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
85	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91 -	134.32	103.00	03/2008 -	-	-	0/3
86	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02 -	143.02	104.49	11/2008 -	-	-	0/0
Total			45,473.36 -	49,248.38	15,693.15				2/152
<u>Petroleum</u>									
87	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00 2,869.00	2,869.00	2,410.45	04/2009 12/2009	12/2009	0(R1)	31/36
88	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL) - [160100281]	04/2003	1,635.00 -	2,147.79	2,095.36	05/2006 -	12/2009	43(O)	29/45
89	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 -	350.00	305.00	06/2008 -	12/2009	18(O)	0/0
90	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80 -	3,941.41	1,793.00	09/2009 -	12/2009	3(O)	0/0
91	CHENNAI-BANGALORE PIPELINE - [N16000029]	07/2007	232.11 -	273.00	206.00	07/2009 -	12/2009	5(O)	0/0
92	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00 -	6,898.00	4,299.00	01/2010 -	01/2010	0(O)	0/0
93	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00 -	1,131.00	710.17	12/2009 -	01/2010	1(O)	0/0
94	SHORT TERM LOW COST MUMBAI REFINERY - [N16000082]	12/2006	390.00 -	230.00	164.51	01/2010 -	01/2010	0(O)	0/0
95	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00 -	348.00	178.95	12/2009 -	02/2010	2(O)	0/0
96	CHAINSAR-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77 -	571.64	329.00	09/2009 -	02/2010	5(O)	0/0
97	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80 3,941.41	3,941.41	2,176.19	12/2009 -	02/2010	2(O)	0/0
98	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	429.38	483.40	03/2007 -	03/2010	36(O)	3/3
99	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	219.22	-	03/2006 -	03/2010	48(O)	6/6
100	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	12,138.00 -	14,439.00	10,656.87	09/2009 11/2009	03/2010	4(R1)	61/101
101	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	1,800.00	1,522.16	12/2008 -	03/2010	15(O)	0/0
102	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13 -	396.13	52.34	10/2009 -	03/2010	5(O)	0/0
103	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71 639.11	639.11	520.92	12/2009 -	03/2010	3(O)	0/0
104	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82 -	405.82	277.56	12/2009 -	03/2010	3(O)	0/0
105	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00 -	139.07	44.55	10/2009 -	04/2010	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
106	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	2,979.49	11/2009 04/2010	04/2010	0(R3)	0/0
107	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	78.02	04/2010	04/2010	0(O)	0/0
108	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	547.47	04/2009	05/2010	13(O)	0/0
109	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009	05/2010	14(O)	0/0
110	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	159.62	05/2010	05/2010	0(O)	0/0
111	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	96.17	05/2010	05/2010	0(O)	0/0
112	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,646.39	-	09/2009	06/2010	9(O)	0/0
113	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	1,339.25	1,144.30	06/2010 06/2010	06/2010	0(R1)	0/0
114	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	137.45	02/2010	06/2010	4(O)	0/0
115	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	137.05	02/2010	06/2010	4(O)	0/0
116	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	-	04/2010	06/2010	2(O)	0/0
117	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60	293.60	117.97	12/2009	06/2010	6(O)	0/0
118	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18	143.84	87.57	06/2010	06/2010	0(O)	0/0
119	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	490.20	09/2009	06/2010	9(O)	0/0
120	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	595.34	06/2006 05/2008	07/2010	26(R1)	0/2
121	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTA - [N16000017]	06/2005	806.00 1,007.83	1,007.83	563.52	03/2008 12/2009	08/2010	8(R1)	18/48
122	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	8.66	10/2010	10/2010	0(O)	0/0
123	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	1.13	10/2010	10/2010	0(O)	0/0
124	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38	3,000.00	176.96	10/2010	10/2010	0(O)	0/0
125	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00	1,212.85	18.46	10/2011	10/2010	-12(O)	0/0
126	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00	224.00	35.28	12/2010	12/2010	0(O)	0/0
127	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40 605.40	605.40	65.36	12/2010 12/2010	12/2010	0(R3)	0/0
128	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40	304.40	32.06	12/2010	12/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
129	CAPACITY AUGMENTATION OF AGRA& FERAZABAD REGION - [N16000074]	07/2009	199.57	199.57	-	01/2011	01/2011	0(O)	0/0
130	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	834.90	930.88	03/2007	03/2011	48(O)	6/6
131	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75	8,061.42	3,796.70	06/2009	04/2011	22(O)	0/0
132	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93	1,061.78	9.91	11/2011	04/2011	-7(O)	0/0
133	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	33.68	04/2011	04/2011	0(O)	0/0
134	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,230.10	03/2005	05/2011	74(O)	0/0
135	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	333.40	-	05/2010	05/2011	12(R3)	0/0
136	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00	349.00	2.00	08/2011	08/2011	0(O)	0/0
137	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	349.00	5.37	08/2011	08/2011	0(O)	0/0
138	Construction of Tanks and Blending Facility at Vad - [N16000077]	02/2009	267.00	349.00	-	08/2011	08/2011	0(O)	0/0
139	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	48.79	09/2011	09/2011	0(O)	0/0
140	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	47.57	09/2011	09/2011	0(O)	0/0
141	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	756.00	128.17	12/2011	12/2011	0(O)	0/0
142	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	-	12/2011	12/2011	0(O)	0/0
143	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	-	04/2011	12/2011	8(O)	0/0
144	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00	825.00	48.11	12/2011	12/2011	0(O)	0/0
145	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0(O)	0/0
146	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	266.65	03/2010	03/2012	0(R1)	0/0
147	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78	5,633.44	0.61	03/2010	03/2012	19(R1)	0/0
148	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	2,920.82	5.24	02/2009	04/2012	19(R1)	0/0
149	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29	6,326.40	160.84	05/2010	05/2012	24(O)	0/0
150	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2012	22(O)	0/0
151	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	-	09/2012	09/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
152	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	2,488.68	03/2012	11/2012	8(O)	0/0
153	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0(O)	0/0
154	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0(O)	0/0
155	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	-	01/2013	01/2013	0(O)	0/0
156	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	36.27	03/2013	03/2013	0(O)	0/0
	Total		141,026.24	159,564.03	44,995.27				154/247
	Power								
157	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL) - [180100253]	05/2005	279.30	340.14	282.50	07/2009	12/2009	5(O)	5/18
158	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL) - [180100257]	06/2005	813.67	777.15	780.09	06/2008	12/2009	18(O)	9/22
159	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,016.74	106.96	09/2007	01/2010	28(O)	8/36
160	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL) - [180100247]	01/2005	691.83	913.33	706.05	12/2007	02/2010	26(O)	13/20
161	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI - [N18000021]	01/2007	186.95	186.95	141.75	07/2009	02/2010	7(O)	2/21
162	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST - [N18000026]	10/2006	103.80	103.80	67.34	06/2009	02/2010	8(O)	0/0
163	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72	836.14	319.14	07/2006	03/2010	44(O)	2/5
164	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45	1,007.16	705.26	12/2007	03/2010	27(O)	7/18
165	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34	266.61	126.03	06/2008	03/2010	21(O)	6/20
166	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	1,896.65	1,465.48	11/2008	03/2010	16(O)	20/38
167	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.G.R.) - [180100260]	12/2005	3,779.46	3,779.46	3,178.77	09/2009	03/2010	6(O)	11/30
168	KOLDAM HEP TRANSMISSION LINE (PGCIL) - [180100263]	09/2005	464.91	464.91	159.34	09/2008	03/2010	18(R1)	9/22
169	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]	06/2006	803.70	803.76	529.73	06/2009	03/2010	9(O)	0/20
170	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96	975.96	498.78	10/2009	03/2010	5(O)	2/20
171	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-V - [N18000017]	06/2006	721.25	721.25	552.33	06/2009	03/2010	9(O)	6/19

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
172	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN - [N18000020]	10/2006	150.26 -	153.24	107.32	10/2009 -	03/2010	5(O)	5/20
173	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	205.91	04/2010 -	04/2010	0(O)	0/0
174	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	86.66	06/2010 -	06/2010	0(O)	0/0
175	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23 -	5,221.23	1,862.81	07/2010 -	07/2010	0(O)	2/20
176	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57 -	353.57	30.66	07/2010 -	07/2010	0(O)	0/0
177	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,736.00	02/2010 -	08/2010	6(O)	2/24
178	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	237.18	09/2010 -	09/2010	0(O)	0/0
179	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	126.06	09/2010 -	09/2010	0(O)	0/0
180	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	3,519.77	10/2010 -	10/2010	0(O)	8/40
181	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44 -	2,570.44	1,465.78	08/2010 -	11/2010	3(O)	10/26
182	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24 -	557.25	252.43	01/2010 -	11/2010	10(O)	0/22
183	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72 -	340.72	84.36	11/2010 -	11/2010	0(O)	0/0
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55 -	261.55	73.03	11/2010 -	11/2010	0(O)	0/0
185	SYSTEM STRAIGHTENING SCHEME-VIII OF SOUTHERN REGIO - [N18000070]	02/2008	105.84 -	105.84	45.86	11/2010 -	11/2010	0(O)	0/0
186	KOTESHWAR HEP(THDC) - [180100184]	04/2000	1,301.56 -	1,301.56	1,487.95	04/2005 -	12/2010	68(O)	0/0
187	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63 -	1,405.63	259.18	08/2010 -	12/2010	4(O)	0/0
188	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	611.02	113.37	08/2010 -	12/2010	4(O)	0/0
189	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76 -	417.76	199.46	12/2010 -	12/2010	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36 -	408.36	221.28	12/2010 -	12/2010	0(O)	0/0
191	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89 -	230.89	4.94	01/2011 -	01/2011	0(O)	0/0
192	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92 -	1,279.40	1,009.68	03/2007 -	02/2011	47(O)	1/25
193	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	1,724.79	229.41	11/2009 -	02/2011	15(O)	0/0
194	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26 -	621.28	93.96	02/2011 -	02/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
195	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]	10/2006	238.25	238.25	160.43	-	05/2011	-	0/0
196	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	2,242.87	05/2011	05/2011	0(O)	0/0
197	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	150.84	10/2010	06/2011	8(O)	0/0
198	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	32.40	06/2011	06/2011	0(O)	0/0
199	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	49.72	06/2011	06/2011	0(O)	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	254.27	07/2011	07/2011	0(O)	0/0
201	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	125.76	07/2011	07/2011	0(O)	0/0
202	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	6.86	07/2011	07/2011	0(O)	0/0
203	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,307.03	634.93	09/2009	08/2011	23(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19	132.19	9.62	08/2011	08/2011	0(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	5.13	08/2011	08/2011	0(O)	0/0
206	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	41.14	09/2011	09/2011	0(O)	0/0
207	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,502.01	12/2009	10/2011	22(O)	33/56
208	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	727.42	07/2011	11/2011	4(O)	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	90.43	11/2011	11/2011	0(O)	0/0
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	3.50	11/2011	11/2011	0(O)	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	2.51	11/2011	11/2011	0(O)	0/0
212	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	11.86	11/2011	11/2011	0(O)	0/0
213	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	2,943.39	04/2009	12/2011	32(O)	19/41
214	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	623.44	60.45	01/2012	01/2012	0(O)	0/0
215	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	18.55	02/2012	02/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
216	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50 -	409.50	-	02/2012 -	02/2012	0(O)	0/0
217	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29 -	410.29	18.97	02/2012 -	02/2012	0(O)	0/0
218	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGIONA - [N18000060]	02/2009	120.62 -	120.62	3.25	02/2012 -	02/2012	0(O)	0/0
219	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32 -	1,347.32	95.35	02/2012 -	02/2012	0(O)	0/0
220	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	2,047.03	710.65	01/2012 -	03/2012	2(O)	2/10
221	PARA HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	573.99	77.90	08/2012 -	08/2012	0(O)	0/0
222	MOUDA STPP - [N18000048]	11/2007	5,459.28 -	5,459.28	660.94	02/2012 -	08/2012	6(O)	0/0
223	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95 -	2,360.95	603.88	08/2012 -	08/2012	0(O)	0/0
224	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33 -	7,075.33	1,285.07	08/2012 -	08/2012	0(O)	0/0
225	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12 -	4,824.12	220.89	10/2012 -	10/2012	0(O)	0/0
226	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00 -	5,915.00	411.80	11/2012 -	11/2012	0(O)	0/0
227	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81 -	6,230.81	364.92	11/2012 -	11/2012	0(O)	0/0
228	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	6,285.33	512.55	09/2010 -	12/2012	27(O)	2/11
229	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42 -	358.42	-	12/2008 09/2010	12/2012	27(R1)	0/15
230	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10 -	721.25	552.33	11/2011 -	12/2012	13(O)	6/34
231	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88 -	7,031.88	307.14	12/2012 -	12/2012	0(O)	0/0
232	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	3,919.59	245.56	09/2009 -	03/2013	42(O)	1/20
233	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48 -	2,978.48	686.19	03/2013 -	03/2013	0(O)	5/31
234	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	1,657.60	252.91	07/2010 -	04/2013	33(O)	0/0
235	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	3,253.22	1,033.97	12/2009 -	05/2013	41(O)	37/165
236	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04 -	7,341.04	619.47	08/2013 -	08/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
237	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	321.66	08/2013	08/2013	0(O)	0/0
238	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,500.68	11/2010	10/2013	35(O)	15/51
239	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	93.25	06/2013	03/2015	21(O)	0/0
240	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67	3,642.04	14.69	07/2014	01/2016	18(O)	0/0
241	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			165,980.96	168,458.49	50,769.05				248/920
<u>Health & Family Welfare</u>									
242	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18	443.15	477.33	03/1999	-	-	7/16
Total			422.60	443.15	477.33	03/2005			7/16
<u>Railways</u>									
243	BHAKURA DAMODAR - [N22000098]	03/1998	282.70	325.17	274.56	07/2008	07/2008	0(O)	0/0
244	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64	106.64	139.06	03/2007	05/2008	14(O)	0/0
245	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00	103.57	106.47	03/2005	05/2009	8(R3)	0/0
246	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53	564.50	685.58	03/1996	08/2009	2(R1)	0/0
247	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50	246.50	298.52	03/2009	11/2009	8(R3)	0/0
248	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00	214.09	113.40	12/2009	12/2009	0(O)	0/0
249	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70	142.48	98.84	12/2008	12/2009	12(O)	0/0
250	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74	224.51	41.39	-	12/2009	-	0/0
251	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44	209.57	153.00	03/2009	02/2010	11(O)	0/0
252	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00	634.13	456.48	03/1995	03/2010	180(O)	0/0
253	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21	265.00	265.33	03/1998	03/2010	144(O)	0/0
254	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00	170.00	99.32	03/2002	03/2010	96(O)	0/0
255	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00	571.55	564.66	-	03/2010	-	0/0
256	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00	816.40	693.99	03/2001	03/2010	108(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 124.13	281.20	67.79	- -	03/2010	-	0/0
258	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	960.48	972.04	03/2003 -	03/2010	84(O)	0/0
259	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	501.69	278.12	- -	03/2010	-	0/0
260	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 356.90	425.90	122.22	- 11/2008	03/2010	16(R3)	0/0
261	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	502.14	453.51	- -	03/2010	-	0/0
262	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	753.18	06/2007 -	03/2010	33(O)	0/0
263	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	335.00	293.99	12/2006 12/2008	03/2010	15(R3)	0/0
264	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	219.00	111.14	- -	03/2010	-	0/0
265	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 546.49	610.07	526.24	- 02/2009	03/2010	13(R1)	0/0
266	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	456.48	- 03/2009	03/2010	12(R1)	0/0
267	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84 -	136.45	131.28	03/2002 -	03/2010	96(O)	0/0
268	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	4.77	- -	03/2010	-	0/0
269	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 -	227.52	222.70	03/2008 03/2009	03/2010	12(R1)	0/0
270	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	134.52	03/1998 08/2005	03/2010	55(R3)	0/0
271	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	-	- 03/2009	03/2010	12(R1)	0/0
272	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	322.87	33.00	- -	03/2010	-	0/0
273	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	126.50	03/2006 -	03/2010	48(O)	0/0
274	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	151.41	03/2008 06/2008	03/2010	21(R3)	0/0
275	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	158.95	204.77	- -	03/2010	-	0/0
276	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	73.85	03/2010 -	03/2010	0(O)	0/0
277	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 654.51	1,160.52	434.32	- -	06/2010	-	0/0
278	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	216.60	04/2003 03/2010	06/2010	3(R1)	0/0
279	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	1,006.89	12/2006 -	06/2010	42(O)	0/0
280	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 138.48	138.48	35.72	- -	06/2010	-	0/0
281	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	186.39	- 02/2009	06/2010	16(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
282	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62	221.90	87.07	12/2007 03/2010	07/2010	4(R1)	0/0
283	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09	881.19	86.35	- -	07/2010	-	0/0
284	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	86.57	- -	09/2010	-	0/0
285	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52	273.00	252.64	- 03/2009	11/2010	20(R1)	0/0
286	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23	638.00	6.31	02/2015 -	11/2010	-51(O)	0/0
287	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)- PH-I - [220100164]	03/1996	401.81	495.44	130.68	03/2004 -	12/2010	81(O)	0/0
288	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00	672.38	646.85	- -	12/2010	-	0/0
289	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	567.00	181.20	- 12/2009	12/2010	12(R1)	0/0
290	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13	135.10	116.58	- -	12/2010	-	0/0
291	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 716.64	718.30	-	03/2008 08/2008	12/2010	28(R1)	0/0
292	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	254.47	03/2009 12/2008	12/2010	24(R1)	0/0
293	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15	245.15	7.53	12/2010 -	12/2010	0(O)	0/0
294	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	323.40	02/2010 -	02/2011	12(O)	0/0
295	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38	1,000.00	79.07	- -	02/2011	-	0/0
296	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 810.78	810.78	32.36	- -	02/2011	-	0/0
297	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66	356.87	182.31	- 03/2010	03/2011	12(R1)	0/0
298	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	475.00	261.20	06/1999 -	03/2011	141(O)	0/0
299	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00	332.75	43.72	- -	03/2011	-	0/0
300	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	240.05	06/2004 -	03/2011	81(O)	0/0
301	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	334.52	- 06/2009	03/2011	21(R3)	0/0
302	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36	371.36	234.34	- -	03/2011	-	0/0
303	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	220.07	03/2009 12/2009	03/2011	15(R1)	0/0
304	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
305	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35	258.35	9.30	03/2011 -	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
306	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97	196.97	16.78	03/2011	03/2011	0(O)	0/0
307	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66	528.65	22.26	-	06/2011	-	0/0
308	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69	501.69	312.32	03/2010	06/2011	15(O)	0/0
309	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50	252.50	23.86	02/2010	11/2011	21(O)	0/0
310	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44	587.08	628.48	-	12/2011	-	0/0
311	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64	735.10	179.28	-	12/2011	27(R1)	0/0
312	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00	496.03	26.64	03/2010	12/2011	21(O)	0/0
313	LUMDING-SILCHAR(GC),NEFR - [220100170]	04/1996	648.00	4,074.10	1,936.85	03/2009	03/2012	36(O)	0/0
314	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54	141.40	103.18	03/2003	03/2012	108(O)	0/0
315	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81	234.45	56.22	-	03/2012	-	0/0
316	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41	322.95	32.59	-	03/2012	-	0/0
317	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59	495.74	53.06	-	03/2012	-	0/0
318	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90	324.90	57.58	03/2010	03/2012	24(O)	0/0
319	TAMLUK DIGHA - [N22000097]	03/1984	293.97	293.97	298.27	06/2005	04/2012	82(O)	0/0
320	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20	4,174.00	2,953.68	12/2010	10/2012	22(O)	0/0
321	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08	1,010.00	44.37	-	12/2012	-	0/0
322	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	921.00	236.87	03/2009	12/2012	45(O)	0/0
323	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
324	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20	687.20	44.22	03/2010	12/2012	33(O)	0/0
325	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84	410.08	88.28	-	03/2013	-	0/0
326	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00	899.42	534.95	-	03/2013	-	0/0
327	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70	1,556.23	132.38	-	03/2013	-	0/0
328	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00	3,087.44	1,652.70	04/2008	03/2014	27(R1)	0/0
329	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00	1,502.29	416.99	12/2008	03/2014	63(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
330	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]	09/1996	156.00 156.00	160.48	68.55	- -	03/2014	-	0/0
331	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00 200.00	546.47	0.48	- -	03/2014	-	0/0
332	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	5,300.00	60.00	03/2014 -	03/2014	0(O)	0/0
333	AGARTALA SABROOM - [N22000099]	04/2008	813.34 -	813.34	15.03	03/2014 -	03/2014	0(O)	0/0
334	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34 -	619.34	0.59	04/2014 -	04/2014	0(O)	0/0
335	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	2,492.53	125.88	03/2011 -	03/2016	60(O)	0/0
336	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 8,000.00	11,270.00	5,903.81	03/2001 -	12/2016	189(O)	0/0
337	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77 274.56	432.46	427.90	03/1994 -	-	-	0/0
338	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	617.63	310.54	- -	-	-	0/0
339	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
340	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	231.64	- -	-	-	0/0
341	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
342	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	39.76	- -	-	-	0/0
343	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
344	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
345	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	388.94	03/2004 03/2005	-	-	0/0
346	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	216.45	- -	-	-	0/0
347	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	71.76	- -	-	-	0/0
348	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.00	61.86	- -	-	-	0/0
349	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	245.60	02/2009 -	-	-	0/0
350	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	103.72	4.64	- -	-	-	0/0
351	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 -	268.00	275.41	12/1999 03/2008	-	-	0/0
352	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
353	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	55.86	- -	-	-	0/0
354	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	89.61	03/2007 03/2007	-	-	0/0
355	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	366.54	0.27	07/2008 -	-	-	0/0
356	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	540.09	07/2005 -	-	-	0/0
357	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	320.24	05/2008 -	-	-	0/0
358	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	- -	-	-	0/0
359	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	61.86	- -	-	-	0/0
360	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
361	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	123.21	- 05/2009	-	-	0/0
362	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
363	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
364	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	57.38	- -	-	-	0/0
365	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	374.06	- -	-	-	0/0
366	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
367	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	-	- -	-	-	0/0
368	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	325.17	278.36	03/2005 12/2008	-	-	0/0
369	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00 -	133.00	-	- -	-	-	0/0
370	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00 -	137.71	8.97	- -	-	-	0/0
371	REWARI-SADULPUR-HISSAR (GC),NWR - [220100290]	04/1997	198.96 364.19	410.00	377.20	- -	-	-	0/0
372	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	459.91	36.40	- -	-	-	0/0
373	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23 -	120.23	220.17	- -	-	-	0/0
374	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86 -	103.86	28.93	- -	-	-	0/0
375	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	104.79	34.13	- -	-	-	0/0
376	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	726.05	106.29	- -	-	-	0/0
378	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10 -	113.75	40.35	- -	-	-	0/0
379	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
380	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73 -	230.03	45.76	- -	-	-	0/0
381	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
382	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
383	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27 -	100.27	0.01	- -	-	-	0/0
384	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10 -	102.10	22.75	- -	-	-	0/0
385	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	670.00	0.74	- -	-	-	0/0
386	GAELKERA-MANOHPUR,(LD)(SER) - [N22000045]	03/1998	186.92 261.70	261.70	0.08	02/2006 -	-	-	0/0
387	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67 -	129.78	90.84	- -	-	-	0/0
388	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94 -	124.00	151.76	03/2004 07/2008	-	-	0/0
389	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]	09/2007	404.19 404.19	711.15	36.81	- -	-	-	0/0
390	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 343.17	639.00	158.61	- -	-	-	0/0
391	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00 170.00	255.96	65.75	- -	-	-	0/0
392	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 125.00	227.40	11.01	- -	-	-	0/0
393	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	22.05	- -	-	-	0/0
394	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	19.12	- -	-	-	0/0
395	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 254.07	676.00	283.91	- 12/2011	06/2011	-6(R3)	0/0
396	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	132.90	- 12/2012	12/2012	0(R1)	0/0
Total			52,042.12 -	96,970.60	40,991.32				0/0
<u>Road Transport & Highways</u>									
397	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00 -	229.00	-	05/2010 -	12/2009	-5(O)	0/0
398	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213 - [240106232]	03/2005	133.03 -	133.03	244.00	08/2005 -	10/2009	50(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
399	JAWAHARLAL NEHRU PORT PHASE-II, SH-54 - [N24000039]	04/2000	143.00	143.00	-	05/2007	10/2009	29(O)	0/0
400	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93	440.93	697.16	12/2006	12/2009	36(O)	0/0
401	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39	534.39	716.15	05/2007	12/2009	31(O)	0/0
402	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85	140.85	148.17	01/2004	12/2009	71(O)	0/0
403	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	417.47	03/2005	12/2009	57(O)	0/0
404	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40	372.40	380.72	07/2004	12/2009	65(O)	0/0
405	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73 - [240106231]	12/2003	266.00	288.06	312.79	08/2007	12/2009	28(O)	0/0
406	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	533.81	03/2009	12/2009	9(O)	0/0
407	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	-	03/2009	12/2009	9(O)	0/0
408	SAGAR - RAJMARG CHORAH, KM.255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	12/2009	14(O)	0/0
409	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]	04/2000	263.00	263.00	317.74	08/2008	12/2009	16(O)	0/0
410	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]	03/2005	168.00	168.00	227.70	12/2008	12/2009	12(O)	0/0
411	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80	402.80	-	03/2009	12/2009	9(O)	0/0
412	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	131.03	10/2008	12/2009	14(O)	0/0
413	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	29.89	04/2009	12/2009	8(O)	0/0
414	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00	110.00	107.90	07/2008	12/2009	17(O)	0/0
415	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00	450.00	868.21	07/2008	12/2009	17(O)	0/0
416	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	448.24	03/2005	01/2010	58(O)	0/0
417	MADURAI - KANIAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.80	03/2008	01/2010	22(O)	0/0
418	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	665.80	12/2008	01/2010	13(O)	0/0
419	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	749.60	11/2010	01/2010	-10(O)	0/0
420	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	-	06/2008	01/2010	19(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
421	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	301.37	03/2008	02/2010	23(O)	0/0
422	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	199.08	01/2009	02/2010	13(O)	0/0
423	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	636.10	05/2009	02/2010	9(O)	0/0
424	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	756.44	02/2010	02/2010	0(O)	0/0
425	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	395.85	03/2005	03/2010	60(O)	0/0
426	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	-	07/2004	03/2010	68(O)	0/0
427	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	760.60	11/2007	03/2010	28(O)	0/0
428	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00	144.00	95.12	07/2005	03/2010	56(O)	0/0
429	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00	110.00	105.70	06/2005	03/2010	57(O)	0/0
430	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	333.60	04/2008	03/2010	23(O)	0/0
431	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00	310.00	359.26	04/2008	03/2010	23(O)	0/0
432	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	349.71	02/2009	03/2010	13(O)	0/0
433	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	286.29	08/2008	03/2010	19(O)	0/0
434	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	137.10	06/2008	03/2010	21(O)	0/0
435	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	154.86	04/2008	03/2010	23(O)	0/0
436	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	432.03	11/2009	03/2010	4(O)	0/0
437	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00	445.00	664.82	07/2010	03/2010	-4(O)	0/0
438	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	92.90	08/2006	04/2010	44(O)	0/0
439	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	84.51	09/2006	04/2010	43(O)	0/0
440	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	83.56	03/2008	04/2010	25(O)	0/0
441	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	158.45	08/2009	04/2010	8(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
442	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	159.91	08/2009	04/2010	8(O)	0/0
443	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	211.04	08/2009	04/2010	8(O)	0/0
444	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	137.79	08/2009	04/2010	8(O)	0/0
445	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	143.38	08/2004	05/2010	69(O)	0/0
446	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	109.70	03/2008	05/2010	26(O)	0/0
447	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	-	04/2009	05/2010	13(O)	0/0
448	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	162.67	10/2008	05/2010	19(O)	0/0
449	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	64.42	05/2010	05/2010	0(O)	0/0
450	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	119.37	09/2007	06/2010	33(O)	0/0
451	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	47.34	08/2004	06/2010	70(O)	0/0
452	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	406.41	11/2007	06/2010	31(O)	0/0
453	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	140.95	08/2005	06/2010	58(O)	0/0
454	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	252.41	10/2008	06/2010	20(O)	0/0
455	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	282.20	10/2008	06/2010	20(O)	0/0
456	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	317.27	10/2008	06/2010	20(O)	0/0
457	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	231.47	10/2008	06/2010	20(O)	0/0
458	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	282.78	10/2008	06/2010	20(O)	0/0
459	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	395.12	04/2008	06/2010	26(O)	0/0
460	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	331.71	06/2008	06/2010	24(O)	0/0
461	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	353.40	06/2008	06/2010	24(O)	0/0
462	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	178.80	10/2008	06/2010	20(O)	0/0
463	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	139.61	07/2008	06/2010	23(O)	0/0
464	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	384.69	06/2008	06/2010	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
465	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	171.20	06/2009	06/2010	12(O)	0/0
466	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	06/2010	15(O)	0/0
467	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	150.40	11/2008	06/2010	19(O)	0/0
468	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	533.50	06/2009	06/2010	12(O)	0/0
469	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	186.88	02/2004	06/2010	76(O)	0/0
470	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	183.77	09/2009	06/2010	9(O)	0/0
471	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	180.00	09/2008	06/2010	21(O)	0/0
472	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	237.53	06/2010	06/2010	0(O)	0/0
473	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	223.00	03/2010	06/2010	3(O)	0/0
474	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]	12/2003	407.60	407.60	177.60	06/2010	06/2010	0(O)	0/0
475	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	238.40	09/2009	06/2010	9(O)	0/0
476	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	127.10	06/2010	06/2010	0(O)	0/0
477	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	44.98	08/2004	07/2010	71(O)	0/0
478	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	145.40	06/2008	07/2010	25(O)	0/0
479	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.60	07/2010	07/2010	0(O)	0/0
480	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	07/2010	0(O)	0/0
481	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	321.10	07/2010	07/2010	0(O)	0/0
482	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	563.64	07/2010	07/2010	0(O)	0/0
483	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	666.34	03/2010	07/2010	4(O)	0/0
484	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	-	04/2004	08/2010	76(O)	0/0
485	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	99.85	06/2008	08/2010	26(O)	0/0
486	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	245.20	08/2010	08/2010	0(O)	0/0
487	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52	111.78	0.52	06/2004	09/2010	75(O)	0/0
488	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	239.76	03/2005	09/2010	66(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
489	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00	198.00	96.34	11/2008	09/2010	22(O)	0/0
490	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	214.80	09/2009	09/2010	12(O)	0/0
491	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	183.20	09/2009	09/2010	12(O)	0/0
492	LUMDING TO DABOKA - [N24000110]	12/2003	130.00	130.00	38.36	08/2010	09/2010	1(O)	0/0
493	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
494	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	171.88	10/2009	10/2010	12(O)	0/0
495	KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A - [240102193]	04/2000	110.00	110.00	140.97	12/2004	12/2010	72(O)	0/0
496	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	579.82	04/2007	12/2010	44(O)	0/0
497	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	267.62	09/2007	12/2010	39(O)	0/0
498	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	120.46	09/2007	12/2010	39(O)	0/0
499	JAM-WADNER - [240106209]	12/2003	145.00	145.00	68.18	07/2005	12/2010	65(O)	0/0
500	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	90.65	06/2005	12/2010	66(O)	0/0
501	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	-	05/2008	12/2010	31(O)	0/0
502	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	195.16	10/2008	12/2010	26(O)	0/0
503	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	204.49	03/2008	12/2010	33(O)	0/0
504	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	112.36	02/2009	12/2010	22(O)	0/0
505	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	27.66	04/2009	12/2010	20(O)	0/0
506	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	-	11/2008	12/2010	25(O)	0/0
507	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	27.96	11/2008	12/2010	25(O)	0/0
508	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	55.40	04/2009	12/2010	20(O)	0/0
509	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00	225.00	86.47	06/2008	12/2010	30(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
510	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHA) - [240106290]	12/2003	195.00	195.00	85.35	06/2008	12/2010	30(O)	0/0
511	KASIA TO GORAKHPUR (NH-28)(NHA) - [240106291]	12/2003	242.00	242.00	286.24	12/2008	12/2010	24(O)	0/0
512	UP/BIHAR BORDER TO KASIA (NH-28)(NHA) - [240106292]	12/2003	227.00	227.00	248.09	12/2008	12/2010	24(O)	0/0
513	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHA) - [240106293]	12/2003	237.80	237.80	84.06	06/2008	12/2010	30(O)	0/0
514	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHA) - [240106301]	12/2003	151.30	151.30	94.72	10/2008	12/2010	26(O)	0/0
515	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHA) - [240106303]	12/2003	203.43	203.43	80.44	10/2008	12/2010	26(O)	0/0
516	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHA) - [240106304]	12/2003	251.03	251.03	62.13	10/2008	12/2010	26(O)	0/0
517	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	29.18	10/2008	12/2010	26(O)	0/0
518	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	52.29	04/2008	12/2010	32(O)	0/0
519	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	75.54	06/2008	12/2010	30(O)	0/0
520	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	226.02	03/2008	12/2010	33(O)	0/0
521	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	80.90	04/2008	12/2010	32(O)	0/0
522	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	108.74	06/2008	12/2010	30(O)	0/0
523	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	99.92	04/2008	12/2010	32(O)	0/0
524	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	53.00	05/2008	12/2010	31(O)	0/0
525	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	109.87	06/2008	12/2010	30(O)	0/0
526	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	78.52	06/2008	12/2010	30(O)	0/0
527	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.11	09/2007	12/2010	39(O)	0/0
528	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.32	07/2009	12/2010	17(O)	0/0
529	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	61.01	04/2010	12/2010	8(O)	0/0
530	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	176.32	02/2010	12/2010	10(O)	0/0
531	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	368.34	10/2009	12/2010	14(O)	0/0
532	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	189.26	12/2009	12/2010	12(O)	0/0
533	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	0.41	02/2004	12/2010	82(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
534	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	172.90	07/2010	01/2011	6(O)	0/0
535	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	266.60	01/2011	01/2011	0(O)	0/0
536	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	169.30	01/2011	01/2011	0(O)	0/0
537	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	102.45	09/2007	02/2011	41(O)	0/0
538	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	179.05	07/2005	03/2011	68(O)	0/0
539	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	197.32	07/2005	03/2011	68(O)	0/0
540	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	145.49	10/2008	03/2011	29(O)	0/0
541	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	129.64	09/2008	03/2011	30(O)	0/0
542	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	214.44	09/2008	03/2011	30(O)	0/0
543	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	80.12	09/2010	03/2011	6(O)	0/0
544	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	363.70	05/2010	05/2011	12(O)	0/0
545	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	45.32	09/2008	06/2011	33(O)	0/0
546	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40	117.40	29.83	11/2008	06/2011	31(O)	0/0
547	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
548	DEVDHARI-WADNER - [240106208]	12/2003	145.00	145.00	24.71	07/2005	-	-	0/0
Total			44,015.85	44,240.60	31,895.19				0/0
<u>Shipping & Ports</u>									
549	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00	100.00	0.50	01/2010	01/2010	0(O)	0/0
550	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	-	12/2005	03/2010	51(O)	0/0
551	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	129.44	06/2007 01/2009	03/2010	14(R1)	0/0
552	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	342.92	03/2010	03/2010	0(O)	0/0
553	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	368.23	07/2010	07/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
554	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	809.61	10/2008	11/2010	25(O)	0/0
555	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	274.01	04/2009	11/2010	19(O)	0/0
556	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	241.64	11/2010	11/2010	0(O)	0/0
557	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
558	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
559	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	882.00	0.16	02/2011	02/2011	0(O)	0/0
560	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	702.00	0.73	03/2011	03/2011	0(O)	0/0
561	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	200.91	04/2011	04/2011	0(O)	0/0
562	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	341.48	04/2011	12/2011	8(O)	0/0
563	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
564	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
565	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.24	10/2008	-	-	0/0
566	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
Total			12,475.83	12,747.59	3,181.45				0/0
<u>Telecommunications</u>									
567	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
568	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
569	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007	11/2009	33(O)	0/0
570	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	-	02/2007	12/2009	34(O)	0/0
571	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	92.61	10/2007	12/2009	26(O)	0/0
572	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	12/2009	20(O)	0/0
573	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
574	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	422.85	12/2008	12/2009	12(O)	0/0
575	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	97.35	03/2009	12/2009	9(O)	0/0
576	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	470.24	12/2008	12/2009	12(O)	0/0
577	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	180.93	03/2009	12/2009	9(O)	0/0
578	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	12/2009	3(O)	0/0
579	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	9.86	12/2009	12/2009	0(O)	0/0
580	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25	133.75	34.05	06/2008 12/2009	01/2010	1(R3)	0/0
581	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	169.33	12/2008	01/2010	13(O)	0/0
582	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	278.16	278.16	175.77	12/2008 12/2009	01/2010	1(R3)	0/0
583	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	110.83	03/2009	01/2010	10(O)	0/0
584	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15	149.15	40.87	06/2009	01/2010	7(O)	0/0
585	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	336.81	64.50	01/2009	01/2010	12(O)	0/0
586	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.16	12/2004	02/2010	62(O)	0/0
587	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	104.60	12/2009 12/2009	03/2010	3(R3)	0/0
588	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	161.35	02/2008	05/2010	27(O)	0/0
589	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	73.54	09/2009	06/2010	9(O)	0/0
590	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	10(O)	0/0
591	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
592	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
593	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
	Total		11,266.06	10,884.73	3,552.56				0/0
<u>Urban Development</u>									
594	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67	135.03	-	02/2010	02/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
595	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00 8,605.36	8,676.00	12,228.48	06/2010 -	10/2010	4(O)	0/7
596	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 8,158.00	6,395.00	1,636.24	12/2011 09/2012	12/2011	-9(R3)	0/0
	Total		14,596.67 -	15,206.03	13,864.72				0/7
Water Resources									
597	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			547,579.61	621,811.96	239,577.46				755/1993
