

**292th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crores and above)
February, 2010**



Karol Bagh Metro



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary	1 -6
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2008-09	7-11
Summary of Projects	1-19
Sector wise analysis of projects	20-59

EXECUTIVE SUMMARY

The 292nd Flash Report for February' 2010, that contains information on the status of 618 projects in the Central Sector, each costing Rs. 100 Crores and above. During February' 2010, two projects reported completion and have been dropped from the monitor of this Ministry. During February' 2010, six projects of Coal (2), Steel (1), Railways (1), Road Transport & Highways (1) and Shipping & Port (1) Sectors have shown considerable improvement over the completion schedule reported earlier. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	151
2.	RAILWAYS	157
3.	POWER	84
4.	PETROLEUM	78
5.	COAL	43
6.	TELECOMMUNICATION	29
7.	STEEL	28
8.	SHIPPING & PORTS	20
9.	CIVIL AVIATION	17
10.	ATOMIC ENERGY	5
11.	URBAN DEVELOPMENT	3
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		618

2. Eighty three (83) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of -15-60 months in respect of projects relating to Atomic Energy, Civil Aviation, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways and Shipping & Ports sectors.

3. In the **Atomic Energy sector**, 2 projects have shown additional delays of 3 months each, however no specific reasons have been provided by the project authorities for such delays.
4. In the **Civil Aviation Sector**, 2 projects have shown additional delays of 3 months each, however no specific reasons have been provided by the project authorities for such delays.
5. In the **Coal sector**, 2 projects have reported additional delays in the range of 1-48 months while two projects namely, Jhanjra Continuous Miner for Jhanjra UG-II and Tuticorin Thermal Power Project, have reported considerable improvement over the completion schedule by 15 months and 1 month respectively. Expansion of Mine-II (10.5 MIPA to 15.0 MTPA) project of National Lignite Corporation, (NLC) has reported additional delay of 1 month due to acquisition of private land, delay in supply of indigenous equipment by private sector and delay in equipment erection. DIPKA Expansion OCP, 20 MTY of SECL has reported additional delays of 48 months due to finalization of tender and award of work for construction of workshop.
6. In the **Steel Sector**, 9 projects have reported additional delays in the range of 1-12 months while Power Plant-1 has reported considerable improvement over the completion schedule by 5 months. Rebuilding of Blast Furnace No 2, Bokaro Steel Plant and Coal Dust Injection in BF-2 and 3 have reported additional delays of two month each, due to relocation of Coal Handling & Storage site for SMS-III. Simultaneous Blowing of BOF Converter of SMS-II has reported additional delay of 2 months, due to slow progress of work. Rebuilding of coke oven battery No.10 has reported additional delay of 3 months due to poor performance by the contractor. Enhancement of Loading Capacity at Bolani Iron ore has reported additional delay of 4 months due to slow progress of design engineering & fabrication work by M/s TECPRO. Pulverised Coal Injection System for Blast Furnace -1&2, has reported additional delay of 5 months due to delay in design & engineering work and inadequate supplies & mobilization of resources for site activities by the contractor. Installation of 700 TPD Oxygen Plant, Rourkela has reported additional delay of 6 months, due to delay in supply of booster air compressor. Rebuilding of coke oven

battery No. 1 & 2 Bokaro Steel Plant, Expansion of Bhilai Steel Plant and Rourkela Steel Plant have reported additional delay of 6 months, 6 months and 12 months respectively due to inadequate mobilization of resources by the respective contractors.

7. In the **Petroleum Sector**, 10 projects have reported additional delays in the range of 1-24 months. Panipat Naphta Cracker Project has reported additional delay of 1 month due to delay in completion of Captive Power Plant by L&T. Installation of FCCV at Mumbai Refinery has reported additional delay of one month however no specific reason has been given by the project authority. MSQ Upgradation project at Guwahati, DIGBOI and MS/HSD Quality Improvement has reported additional delays of 1 month each without assigning any specific reason to such delays. IOR Lakwa-Lakhmani (ONGC) has reported additional delay of 12 months, however no specific reason has been reported by the project authority. IOR, Rudrasagar (ONGC) has reported additional delay of 12 months, due to re-prioritization of wells. Revamping of Win Platform at MH Asset has reported additional delay of 12 months, due to process of retendering process. Development of B-46 Cluster Field has reported additional delay of 24 months, due to revision of works.
8. In the **Power Sector**, 15 projects have reported additional delays in the range of 1-21 months. Parbati Hydro Electric Project Stage-III 4x130 MW (NHPC) has reported additional delay of 7 months due to delay in land acquisition for Sainj bypass and delay in award of E&M contract. Chamera, Hydro Electric Project Stage III (NHPC) has reported additional delays of 4 months due to violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. NIMOO BAZGO Hydro Electric Project has reported additional delay of 4 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Bongaigaon Thermal Power Project (NTPC) has reported additional delay of 3 months due to delay in slow progress by civil agency. Korba STPP Stage-III, 1x500 MW (NTPC) has reported additional delay of 6 months due to delay in civil and structural work by M/s SPML. Farakka STPP Stage-III (NTPC) has reported additional delay of 3 months due to delay in finalization of erection by M/s BHEL. Transmission system associated with Parbati

HEP stage III, 543 CKM has reported additional delay of 7 months due to court cases. Kaiga 3 & 4 Transmission System (PGCIL) has reported additional delay of 3 months due to revision of works in 50 km Karnataka portion. Kunadankulam Atomic Power Project HEP Transmission Line 1838 CKM (PGCIL) has reported additional delay of one month, to match with the commissioning of linked Generation Projects. Neyveli Transmission System-II 838 CKM (PGCIL) has reported additional delay of 1 month due to court cases. Transmission System for Startup Power to DVC & Maithon RB Generation project (PGCIL) has report additional delay of 2 months due to delay in forest clearance. Northern Region System Strengthening Scheme-VI 54 CKM (PGCIL) has reported additional delay of one month due to revision of works. Vishnugad-Pipalkoti Hydro Electric Project (THDCL) has reported additional delays of 21 months due to delay in acquisition of forest land. Western Region Strengthening Scheme-II has reported additional delays of 5 months , however, no specific reason has been provided by the project authority for such delays.

9. In the **Road Transport and Highways Sector**, 17 projects have reported additional delays in the range of 1-9 months. No specific reasons have been reported by the project authorities for such additional delays.

10. In the **Railway Sector**, 8 projects have shown additional delays in the range of 3-60 months while Hajipur- Sugauli Via Vaishali New Line Project of ECR has reported considerable improvement of three months over the completion schedule reported earlier. Udhampur-Srinagar-Baramulla (NL), NR has reported additional delays of 60 months due to delay in land acquisition of Army Land. Tollyganj-Garia (MTP) project, Sitamarhi- Raxaul- Narkataiganj (GC) and Palwal-Bhuteswar 3rd line doubling (NCR), have reported additional delays of 3 months, 9 months and 9 months, respectively, however, no specific reasons have been reported by the concerned project authorities. Rajatgarh-Barang (Line Doubling) ECoR, and Cuttack-Barang (Line Doubling), ECoR of RVNL has reported additional delays of 3 months and 6 months due to inadequate mobilization by the contractor. Deograh-Dumka New BG Line (LD) ER of RVNL has reported additional delays of 8 months due to Maoists movement. New Guwahati- Digaru Patch (LD) Phase-I has reported additional delays of 12 months due to ban on cutting of hills.

11. **In the Road Transport & Highways sector**, 29 projects have shown additional delays in the range of 3-60 months while Lakhnaadon to MP/MH Border, Km 596.75 – 653 (NS-1/BOT/Mp-2), of National Highways-7 has reported considerable improvement of three months over the completion schedule reported earlier. However, no specific reasons have been provided by the project authorities for such delays.
12. In the **Shipping & Ports Sector**, Deepening of Channel at Paradip Port has reported additional delay of 1 month, while rail connectivity to ICTT at Vallarpadam has shown considerable improvement over the completion schedule reported earlier, however, no specific reason has been reported by the concerned project authority.

Status as on 01.03.2010 in respect of completion of projects costing Rs.100 Crores and above in different sectors during 2010-11 is indicated in the following tables.



(Pankaj Jain)

Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	157	9
2	Road Transport & Highways	151	29
3	Power	84	15
4	Petroleum	78	10
5	Coal	43	4
6	Telecommunications	29	0
7	Steel	28	10
8	Shipping & Ports	20	2
9	Civil Aviation	17	2
10	Atomic Energy	5	2
11	Urban Development	3	0
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	618	83

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAHA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60
	<u>Road Transport & Highways</u>			
14	PARADIP PORT,NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ,NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
	July,2009			
	<u>Power</u>			
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
	<u>Road Transport & Highways</u>			
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET,KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
	<u>Telecommunications</u>			
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
	August,2009			
	<u>Power</u>			
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
	<u>Railways</u>			
26	MADURAI-DINDIGUL,(LD)(SR)(SOUTHERN RAILWAY) - [N22000047]	73.19	-	181.81
	<u>Road Transport & Highways</u>			

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
27	TIRUNELVEI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September, 2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
Shipping & Ports				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24
October, 2009				
Petroleum				
40	DEVELOPMENT OF BASSEIN EAST (ONGCL)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100232]	985.17	03/2006	1,568.46
Railways				
41	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)(RAIL VIKAS NIGAM LTD.) - [220100221]	93.10	-	126.11
Telecommunications				
42	GSM EQUIPMENT OF 1015K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000044]	350.84	11/2008	182.06
43	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM(BHARAT SANCHAR NIGAM LIMITED) - [N26000059]	567.40	06/2009	241.85
November, 2009				

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
44	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106272]	327.20	01/2009	457.60
45	HYDERABAD BANGALORE SECTION(NH-7)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106284]	611.44	03/2009	834.20
46	KADAL TO ARMUR, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000092]	271.73	11/2009	303.80
<u>Telecommunications</u>				
47	GSM BASED NETWORK PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000033]	174.36	11/2007	71.50
December,2009				
<u>Steel</u>				
48	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000024]	123.22	06/2009	77.00
<u>Telecommunications</u>				
49	GSM EQUIPMENT OF 1162K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000045]	325.00	12/2008	237.85
January,2010				
<u>Road Transport & Highways</u>				
50	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106231]	266.00	08/2007	.00
51	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106232]	133.03	08/2005	.00
February,2010				
<u>Civil Aviation</u>				
52	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000016]	245.58	12/2008	260.35
<u>Power</u>				
53	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100257]	813.67	06/2008	784.58

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 100 Crore and above during
2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95

Summary of projects on the Flash Report for the month of February, 2010


I. Project Implementation – Current Status:

Number of Projects Previous Month	622
Number of Projects Completed/Dropped/Frozen in Previous Month	2
Number of Projects Completed/Dropped/Frozen in Current month	2
Number of Projects Added in Current month	0
Number of Projects in Current Month	618

II. Brief Analysis

a) Project Status w.r.t


Original Schedule: Out of 618 projects, 12 projects are ahead of schedule, 128 projects are on schedule and 323 projects are delayed. Of the balance, 112 projects do not have fixed dates of commissioning while 43 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

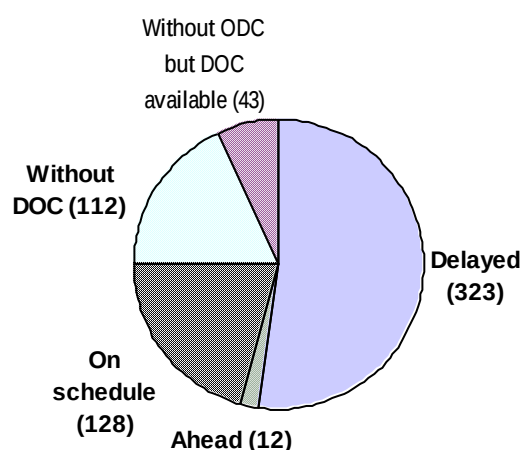

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 618 projects when sanctioned, was of the order of Rs. 596070.73 crore but this was subsequently revised to Rs. 652941.56 crore implying a cost overrun of 7.50%. The expenditure incurred on these projects till February, 2010 is Rs. 265596.20 crore, which is 39.00% of the revised cost of the projects.

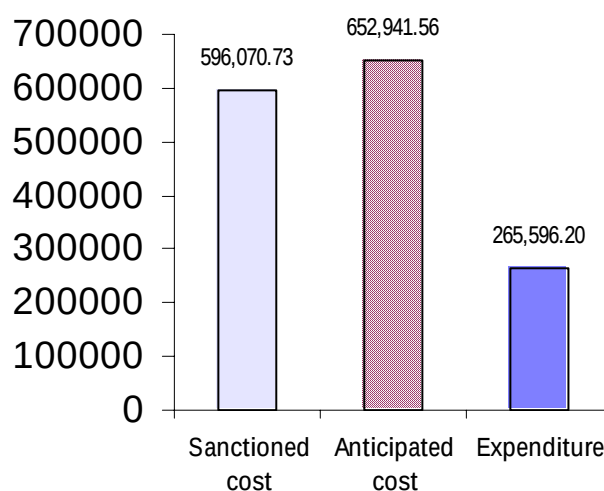

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	622
No of Projects Completed/Dropped/Frozen in Previous Month	2
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects added in Current Month	0
No of Projects in Current Month	618

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original	323	12	128	43	112	618	52.27
Latest Approved	353	14	140	31	80	618	57.12

III. (A) Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	514	503,128.75	540,722.85	210,983.41	39.00	37,594.10	7.50
Latest Approved	104	92,941.98	112,218.71	54,612.79	48.70	19,276.73	20.70
Total	618	596,070.73	652,941.56	265,596.20	40.68	56870.83	9.54

III. (B) Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	323	328,889.60	387,662.14	198,313.72	51.20	58,772.54	17.90
Latest Approved	353	65,346.92	403,032.14	207,140.79	51.40	337,685.22	516.80

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Latest Approved	83	91,929.65	107,853.16	53,665.12	49.80	15,923.51	17.30
Total	83	91,929.65	107,853.16	53,665.12	49.76	15923.51	17.32

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
SIPAT-II SUPP. TRANS. SYSTEM (PGCIL)	06/2005	813.67	06/2008	777.15	11/2009	784.58
<u>Civil Aviation</u>						
CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	10/2006	245.58	12/2008	295.00	12/2009	260.35

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC

VII. Milestones (Cumulative due & achieved)

Total	1958
Achieved up to month	748

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL)	3,072.00	3,072.00	02/2008	02/2010	03/2010	1
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	03/2010	05/2010	2
<u>Civil Aviation</u>						
C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE	135.60	113.02	10/2009	02/2010	05/2010	3
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	1,942.51	1,942.51	05/2011	05/2011	08/2011	3
<u>Coal</u>						
JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II	122.35	122.35	03/2010	03/2013	12/2011	-15
TUTICORIN THERMAL POWER PROJECT	4,904.54	4,904.54	08/2012	09/2012	08/2012	-1
EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC)	2,161.28	2,295.93	06/2009	02/2010	03/2010	1
DIPKA EXPANSION OCP (SECL) (20 MTY)	1,268.53	1,943.66	03/2010	03/2010	03/2014	48
<u>Steel</u>						
POWER PLANT-I	462.00	350.00	12/2009	01/2011	08/2010	-5
REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL	892.32	892.32	08/2009	03/2010	04/2010	1
COAL DUST INJECTION IN BF-2 and 3	132.73	133.92	05/2008	03/2010	05/2010	2
EXPANSION OF BOKARO STEEL PLANT	3,316.00	3,534.00	12/2010	10/2011	12/2011	2
REBUILDING OF COKE OVEN BATTERY-10	416.50	416.50	09/2009	03/2010	06/2010	3
ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE	124.88	119.88	12/2009	02/2010	06/2010	4
Pulverised coal injection system for bf-1&2	125.00	133.00	09/2009	03/2010	08/2010	5
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	04/2010	10/2010	04/2011	6
EXPANSION OF BHILAI STEEL PLANT	5,185.00	6,146.00	05/2011	09/2012	03/2013	6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
EXPENSION OF ROURKELA STEEL PLANT	6,133.00	8,128.00	02/2011	03/2012	03/2013	12
<u>Petroleum</u>						
PANIPAT NAPHTHA CRACKER PROJECT	12,138.00	14,439.00	09/2009	02/2010	03/2010	1
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY	372.00	372.00	02/2010	06/2010	07/2010	1
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY	356.00	356.00	02/2010	06/2010	07/2010	1
MSQ IMPROVMENT PROJECT	293.60	293.60	12/2009	06/2010	07/2010	1
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	05/2010	06/2010	1
BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA	349.00	349.00	08/2011	08/2011	12/2011	4
IOR LAKWA - LAKHMANI (ONGCL)	345.10	600.00	03/2007	03/2010	03/2011	12
IOR, RUDRASAGAR (ONGCL)	113.90	219.22	03/2006	03/2010	03/2011	12
REVAMPING OF WIN PLATFORM AT MH ASSET	333.40	333.40	05/2010	05/2010	05/2011	12
DEVELOPMENT OF B-46 CLUSTER FIELD	1,436.21	1,436.21	07/2010	05/2010	05/2012	24
<u>Power</u>						
NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL)	691.83	913.33	12/2007	02/2010	03/2010	1
KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	1,779.29	1,896.65	11/2008	02/2010	03/2010	1
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI	186.95	186.95	07/2009	02/2010	03/2010	1
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G	290.49	290.49	04/2010	04/2010	06/2010	2
KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL)	596.45	1,007.16	12/2007	03/2010	06/2010	3
EASTERN REGION STRENGTHENING SCHEME-I	975.96	975.96	10/2009	03/2010	06/2010	3
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	08/2010	11/2010	3
BONGAIGAON THERMAL POWER PROJECT	4,375.35	4,375.35	07/2011	11/2011	02/2012	3
CHAMERA, STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	08/2010	12/2010	4
NIMOO BAZGO HYDROELECTRIC PROJECT	611.01	611.02	08/2010	08/2010	12/2010	4

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
WESTERN REGION STRENGTHENING SCHEME- II	5,221.23	5,221.23	07/2010	07/2010	12/2010	5
KORBA STPP STAGE-III	2,448.50	2,448.49	02/2010	02/2010	08/2010	6
PARBATI H.E.P. STAGE -III (NHPC)	2,304.56	2,304.52	10/2010	11/2010	06/2011	7
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE	557.24	557.25	01/2010	11/2010	06/2011	7
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	2,491.58	06/2013	06/2013	03/2015	21
<u>Railways</u>						
HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	324.66	528.65	N.A.	06/2011	03/2011	-3
TOLLYGANJ-GARIA(MTP)	907.69	1,032.76	12/2006	03/2010	06/2010	3
RAJATGARH- BARANG(LD),ECOR	166.16	243.40	N.A.	03/2010	06/2010	3
CUTTACK - BARANG (LD)	127.13	135.10	N.A.	06/2010	12/2010	6
DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	180.73	335.00	12/2006	03/2010	11/2010	8
PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	240.00	329.70	03/2009	06/2010	03/2011	9
SITAMARHI-RAXAUL- NARKATIAGANJ (GC)	501.69	501.69	03/2010	06/2011	03/2012	9
NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I	99.84	110.94	03/2010	03/2010	03/2011	12
UDHAMPUR-SRINAGAR- BARAMULLA (NL),NR	2,500.00	11,270.00	03/2001	12/2012	12/2017	60
<u>Road Transport & Highways</u>						
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS- 1/BOT/MP-2),NH7	407.60	407.60	06/2010	09/2010	06/2010	-3
NALBARI TO BIJNI (AS-8)	200.00	200.00	06/2008	06/2010	07/2010	1
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	05/2010	07/2010	2
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31	205.73	205.73	07/2004	03/2010	06/2010	3
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	04/2010	07/2010	3
AURANG-RAIPUR, NH-6, KM.232 TO KM.281	190.00	190.00	01/2009	02/2010	05/2010	3
FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	332.94	332.94	09/2008	12/2010	03/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
THANJAUR-TRICHY,NH-67(NHAI)	280.00	280.00	06/2009	03/2010	06/2010	3
GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID	600.24	600.24	10/2009	12/2010	03/2011	3
JHANSI TO LALITPUR, NH-25,26	355.06	355.06	09/2009	06/2010	09/2010	3
AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2	193.00	193.00	10/2008	06/2010	10/2010	4
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	217.00	217.00	10/2008	06/2010	10/2010	4
GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00	239.00	239.00	10/2008	06/2010	10/2010	4
GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00	205.00	205.00	10/2008	06/2010	10/2010	4
AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075	212.00	212.00	10/2008	06/2010	10/2010	4
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	05/2010	10/2010	5
TRICHY - KORUR NH-67	516.00	516.00	07/2010	07/2010	12/2010	5
KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7	120.00	120.00	09/2006	04/2010	10/2010	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	227.00	227.00	12/2008	06/2010	12/2010	6
LALITPUR TO SAGAR, NH-26 (NHAI)	198.00	198.00	11/2008	09/2010	03/2011	6
RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	251.03	251.03	10/2008	12/2010	06/2011	6
RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	229.91	229.91	10/2008	12/2010	06/2011	6
SITAPUR-LUCKNOW	322.00	322.00	06/2009	06/2010	12/2010	6
NALBARI TO BIJNI (AS-9)	142.00	142.00	06/2008	06/2010	12/2010	6
TRICHY - DINDIGUAL NH-45	576.00	576.00	07/2010	07/2010	01/2011	6
KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A	110.00	110.00	12/2004	03/2010	12/2010	9
JHAJHARPUR TO DARBANGA (BR-7)	340.00	340.00	09/2008	03/2011	12/2011	9
NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	557.00	557.00	02/2010	02/2010	12/2010	10
KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN	418.04	418.04	03/2010	06/2010	06/2011	12

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	11/2010	03/2010	-8
DEEPENING OF CHEENEL AT PARADIP PORT	154.84	253.36	06/2007	03/2010	04/2010	1
Number of projects reporting additional delay = 83						

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	25,054.29	25,054.29	26,308.29
Civil Aviation	17	7,839.47	7,784.54	7,816.89
Coal	43	26,110.40	27,853.79	28,858.54
Mines	1	4,091.51	4,091.51	4,091.51
Steel	28	45,473.36	45,473.36	52,777.38
Petroleum	78	150,389.80	160,317.67	171,409.05
Power	84	165,167.29	166,981.37	169,829.85
Health & Family Welfare	1	71.18	422.60	443.15
Railways	157	53,764.93	67,170.85	100,933.14
Road Transport & Highways	151	43,916.82	43,916.82	44,119.51
Shipping & Ports	20	18,154.63	18,154.63	18,426.49
Telecommunications	29	11,637.90	11,459.37	11,534.73
Urban Development	3	14,596.67	16,847.03	15,206.03
Water Resources	1	542.90	542.90	1,187.00
Grand total	618	566,811.15	596,070.73	652,941.56


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	5
Number of Projects on schedule	1
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are on schedule and 4 projects are delayed.



Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 5 projects when sanctioned, was of the order of Rs. 25054.29 Crores but this was subsequently revised to Rs. 26308.29 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 20036.73 Crores.

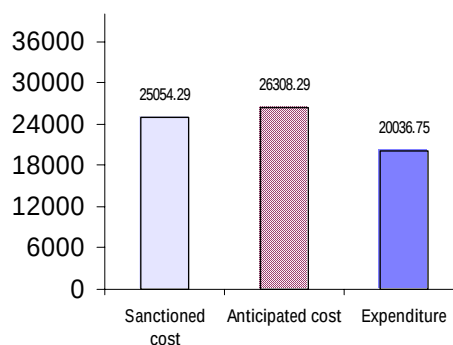


2. Sector: - Civil Aviation

Number of Projects	18
Number of Projects on schedule	3
Number of Projects Delayed	8
Number of Projects Wo_Doc_Original	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are on schedule, 8 projects are delayed and 7 projects are original date of



Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs. 7839.47 Crores but this was subsequently revised to Rs. 7816.89 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs 2149.19 Crores.

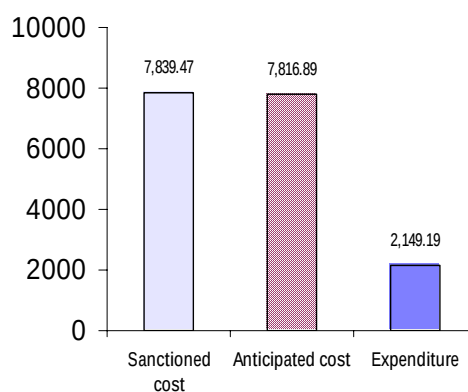


3. Sector: - Coal

Number of Projects	43
Number of Projects on schedule	18
Number of Projects Delayed	20
Number of Projects Ahead	4
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 43 projects, 18 projects are on schedule, 20 projects are delayed and 4 projects are ahead and 1 Project without original date of commissioning.



Investment Scenario

The total cost of implementation of 43 projects when sanctioned, was of the order of Rs. 26110.40 Crores but this was subsequently revised to Rs. 28854.58 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 11027.73 Crores

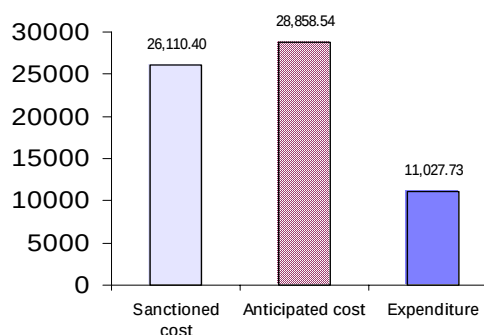


4. Sector: - Petroleum

Number of Projects	78
Number of Projects on schedule	34
Number of Projects Delayed	37
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	3
Number of Projects Without original date of commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 34 projects are on schedule, 37 projects are delayed and 3 projects are ahead and 3 projects are without date of commissioning and 1 Project is Without original date of commissioning.

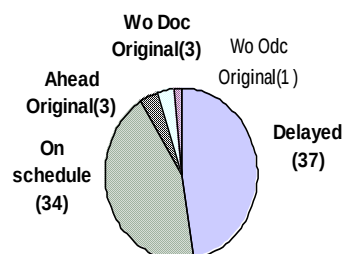

Investment Scenario

The total cost of implementation of 78 projects when sanctioned, was of the order of Rs. 150389.80 Crores but this was subsequently revised to Rs. 171409.05 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 50793.21 Crores.

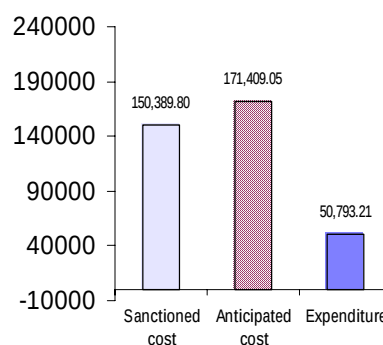


5. Sector: - Power

Number of Projects	85
Number of Projects on schedule	43
Number of Projects Delayed	39
Number of Projects Wo_Doc_Original	2
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 85 projects, 43 projects are on schedule, 39 projects are delayed, 2 projects is without date of commissioning and 1 projects is without original date of commissioning



Investment Scenario

The total cost of implementation of 85 projects when sanctioned, was of the order of Rs. 165167.29 Crores but this was subsequently revised to Rs. 169829.85 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 63058.96 Crores.

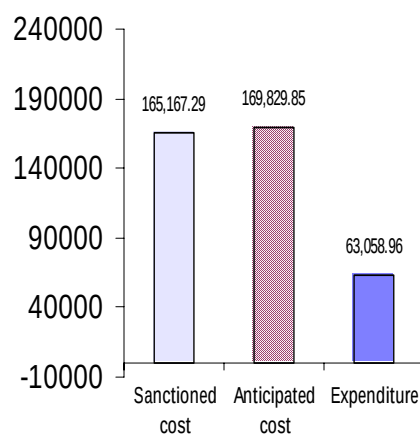


6. Sector: - Railways

Number of Projects	157
Number of Projects on schedule	9
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	67
Number of Projects Wo_Odc_Original	41


Brief Analysis

Project Status with out respect Original Schedule: Out of 157 projects, 9 projects are on schedule, 39 projects are delayed, 1 projects is ahead. 67 projects are Without date of commissioning and 41 projects are without original date of commissioning.

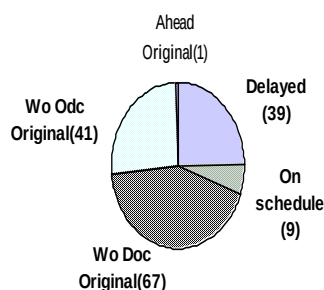

Investment Scenario

The total cost of implementation of 157 projects when sanctioned, was of the order of Rs. 53764.93 Crores but this was subsequently revised to Rs. 100933.14 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 38662.17 Crores.

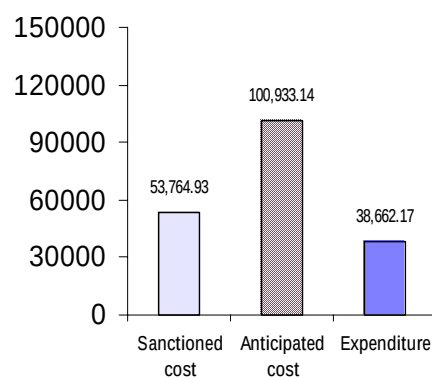


7. Sector: - Road Transport and Highways

Number of Projects	151
Number of Projects on schedule	13
Number of Projects Delayed	127
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	9


Brief Analysis

Project Status with respect to Original Schedule: Out of 151 projects, 13 projects are on schedule, 127 projects are delayed, 2 projects are ahead and 9 projects is with out date of commissioning .

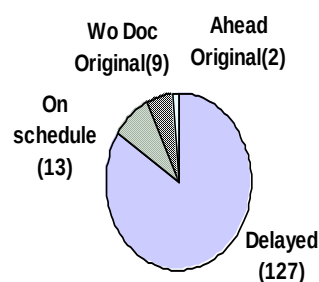

Investment Scenario

The total cost of implementation of 151 projects when sanctioned, was of the order of Rs 43916.82 Crores but this was subsequently revised to Rs. 44119.51 Crores. The expenditure incurred on these projects till January, 2010 is Rs. 34939.24 Crores.

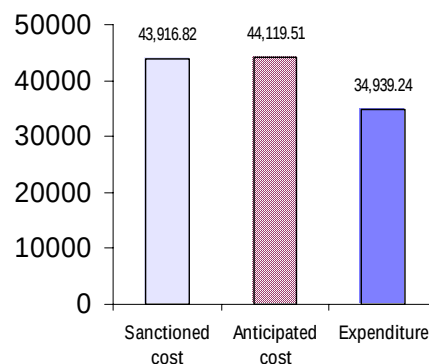


8. Sector: - Shipping and Ports

Number of Projects	20
Number of Projects on schedule	9
Number of Projects Delayed	7
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	2


Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 9 projects are on schedule, 7 projects are delayed, 2 projects are ahead and 2 projects are without date of commissioning.



Investment Scenario

The total cost of implementation of 20 projects when sanctioned, was of the order of Rs.18154.63 Crores but this was subsequently revised to Rs. 18426.49 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 3943.71 Crores.

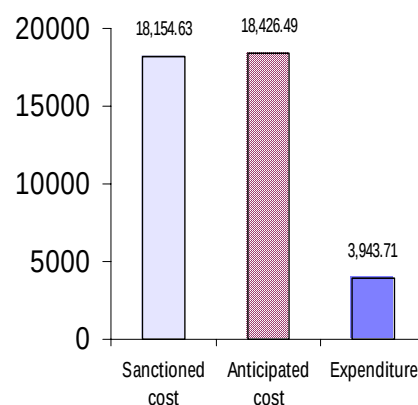


9. Sector: - Steel

Number of Projects	28
Number of Projects on schedule	3
Number of Projects Delayed	22
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 3 projects are on schedule, 22 projects are delayed and 3 projects are without date of commissioning.



Investment Scenario

The total cost of implementation of 28 projects when sanctioned, was of the order of Rs. 45473.36 Crores but this was subsequently revised to Rs. 52777.38 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs. 19585.98 Crores.

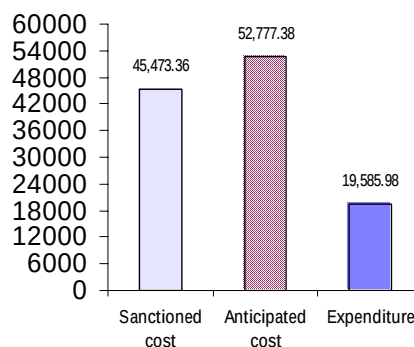


10. Sector: - Telecommunications

Number of Projects	29
Number of Projects Delayed	12
Number of Projects Wo_Doc_Original	17


Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 12 projects are delayed and 17 projects are with our date of commissioning.



Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs 11637.90 Crores but this was subsequently revised to Rs. 11534.73 Crores. The expenditure incurred on these projects till Feb, 2010 is Rs 3705.76 Crores.

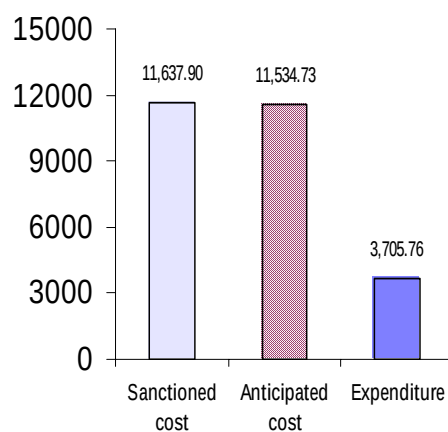

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL) - [020100042]	04/2002	3,072.00	3,072.00	2,133.00	02/2008	03/2010	25(O)	73/75
2	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,515.00	10/2009 09/2007	05/2010	32(R1)	71/75
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,614.00	12/2008	03/2011	27(O)	61/119
4	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	486.37	04/2011	04/2011	0(O)	0/0
5	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,288.38	09/2010	09/2011	12(O)	8/80
Total			25,054.29	26,308.29	20,036.75				213/349
Civil Aviation									
6	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65	129.65	35.92	09/2009 03/2010	03/2010	0(R3)	0/0
7	Construction of New Integrated Passenger Terminal - [N04000042]	03/2006	129.38	129.38	13.49	04/2009 10/2009	03/2010	5(R2)	0/0
8	Construction of New Expandable Modular Integrated - [N04000047]	03/2008	135.72	135.72	10.94	09/2009 12/2009	03/2010	3(R2)	0/0
9	Construction of New Integrated terminal building - [N04000051]	04/2007	128.96	128.96	20.90	02/2009 06/2009	03/2010	9(R2)	0/0
10	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60	113.02	44.76	10/2009	05/2010	7(O)	0/0
11	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	233.51	02/2009	06/2010	16(O)	1/24
12	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04	135.04	58.25	09/2009	06/2010	9(O)	0/0
13	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
14	C/o new Integrated terminal Bldg. at Birsamunda - [N04000049]	01/2009	137.79	137.79	7.50	01/2010 02/2010	06/2010	4(R2)	0/0
15	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94	144.94	26.13	04/2010	12/2010	8(O)	0/1
16	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE - [N04000038]	08/2008	1,273.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
17	DEV. OF KAMARAJ DOMESTIC CHENNAI AIRPORT - [N04000056]	08/2008	1,808.00	1,808.00	523.27	01/2011	01/2011	0(O)	0/0
18	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	539.43	05/2011	08/2011	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	C/o new Airport-SH: E/W in cutting and filling geogrid - [N04000050]	01/2009	264.29	264.29	10.02	01/2011	-	-	0/0
20	Construction of New Integrated Terminal Building - [N04000052]	10/2006	147.00	147.00	46.43	09/2008 02/2009	-	-	0/0
21	C/O PASSENGER LOUNGE BIRSI AIRPORT - [N04000057]	03/2006	108.07	108.07	19.14	08/2008	-	-	0/0
22	GAGAN PROJECT - [N04000065]	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
	Total		7,839.47	7,816.89	2,149.19				1/25
Coal									
23	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07	254.60	212.95	06/2009	02/2010	8(O)	18/21
24	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC) - [060100088]	10/2004	2,161.28	2,295.93	1,789.91	06/2009	03/2010	9(O)	29/23
25	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	961.42	03/2010	03/2010	0(O)	3/7
26	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	789.88	134.46	03/2010	03/2010	0(O)	0/1
27	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39	131.39	382.90	03/2010	03/2010	0(O)	0/0
28	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	473.97	03/2009	03/2010	12(O)	0/0
29	KTK OC Sector-I - [N06000077]	01/2008	91.50	115.33	115.33	09/2010	03/2010	-6(O)	0/0
30	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,385.97	06/2009	09/2010	15(O)	32/26
31	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74	116.54	247.82	03/2007	03/2011	48(O)	0/0
32	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,919.29	06/2009	06/2011	24(O)	23/24
33	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35	122.35	-	03/2010 12/2011	12/2011	0(R3)	0/0
34	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009 01/2012	01/2012	0(R3)	0/0
35	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	57.90	03/2010	03/2012	24(O)	0/4
36	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	341.63	100.57	03/2011	03/2012	12(O)	0/0
37	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	746.04	134.83	03/2012	03/2012	0(O)	0/1
38	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	35.65	03/2012	03/2012	0(O)	0/0
39	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	-	03/2012	03/2012	0(O)	0/0
40	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	249.85	03/2012	03/2012	0(O)	0/0
41	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	572.16	08/2012	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34 779.26	779.26	38.38	03/2013 -	09/2012	-6(O)	2/11
43	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63 -	453.63	46.22	12/2012 -	12/2012	0(O)	0/0
44	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65 -	1,188.31	582.38	03/2011 03/2013	03/2013	0(R3)	0/4
45	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	706.40	12.12	07/2012 -	03/2013	8(O)	0/1
46	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78 -	467.78	11.29	03/2013 -	03/2013	0(O)	0/7
47	KANIHA OCP - [N06000035]	12/2007	457.77 -	457.77	48.96	03/2012 -	03/2013	12(O)	0/0
48	NARAYANKURI UG - [N06000059]	02/2009	149.06 -	149.06	-	03/2013 -	03/2013	0(O)	0/0
49	CHITRA EAST OCP - [N06000060]	08/2007	112.69 -	112.69	-	11/2010 -	03/2013	28(O)	0/0
50	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93 -	479.53	175.35	03/2013 -	03/2013	0(O)	0/0
51	BINA EXTN. PROJ - [N06000019]	11/2006	168.97 -	168.97	137.88	03/2014 -	11/2013	-4(O)	1/1
52	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53 -	1,943.66	765.78	03/2010 -	03/2014	48(O)	2/6
53	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04 -	1,352.04	26.99	03/2014 -	03/2014	0(O)	1/1
54	CHURCHA UG - [N06000046]	06/2008	462.35 -	462.35	270.87	06/2014 -	03/2014	-3(O)	0/0
55	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08 -	153.82	3.14	03/2010 -	03/2014	48(O)	0/0
56	PENGANGA OC - [N06000066]	10/2008	339.77 -	339.77	-	03/2014 -	03/2014	0(O)	0/0
57	KARTALI (EAST) OC - [N06000076]	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/0
58	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87 -	395.87	22.73	03/2013 -	03/2015	24(O)	0/0
59	PELMA OC - [N06000045]	07/2008	448.32 -	448.32	-	03/2012 -	03/2015	36(O)	0/0
60	Batura OC - [N06000049]	09/2008	203.82 -	203.82	-	03/2013 -	03/2015	24(O)	0/0
61	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58 -	135.58	23.32	03/2015 -	03/2015	0(O)	0/0
62	JAGANNATHPOR OC - [N06000075]	09/2008	152.43 -	152.43	-	03/2015 -	03/2015	0(O)	0/0
63	BHUBANESWARI OCP - [N06000034]	12/2007	490.10 -	490.10	56.52	03/2014 -	03/2016	24(O)	0/0
64	TALABIRA OCP - [N06000043]	03/2008	447.72 -	447.72	5.32	03/2015 -	03/2016	12(O)	0/0
65	AUGMENTATION OF PRODUCTION AT SAPRI UG MINE - [N06000058]	09/1987	147.86 -	147.86	25.50	03/2012 -	-	-	0/0
Total			26,110.40 -	28,858.54	11,027.73				111/138

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Mines</u>								
66	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	11(O)	18/111
	Total		4,091.51	4,091.51	3,316.00				18/111
	<u>Steel</u>								
67	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89	607.17	206.09	10/2009	10/2009	0(O)	2/21
68	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	164.48	08/2009	02/2010	6(O)	0/0
69	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	103.09	10/2009	03/2010	5(O)	0/0
70	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	527.00	08/2009	04/2010	8(O)	0/0
71	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73	133.92	87.24	05/2008	05/2010	24(O)	0/2
72	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	244.28	09/2009	06/2010	9(O)	0/0
73	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88	119.88	47.03	12/2009	06/2010	6(O)	0/0
74	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,358.80	03/2010	06/2010	3(O)	0/0
75	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	74.27	01/2010	06/2010	5(O)	0/0
76	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	42.02	06/2010	06/2010	0(O)	0/0
77	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	227.50	06/2009	07/2010	13(O)	0/0
78	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00	133.00	36.47	09/2009	08/2010	11(O)	0/0
79	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	84.40	12/2009	08/2010	8(O)	0/0
80	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	80.00	02/2010	08/2010	6(O)	0/0
81	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50	145.00	6.64	12/2010	12/2010	0(O)	0/0
82	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	114.32	02/2010	01/2011	11(O)	0/0
83	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	165.99	04/2010	04/2011	12(O)	0/0
84	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30	232.93	50.18	07/2009	05/2011	22(O)	0/0
85	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.33	12.97	08/2009	05/2011	21(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
86	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	5,523.00	10/2009	06/2011	20(O)	0/126
87	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
88	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	6,545.80	07/2010	06/2011	11(O)	0/0
89	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
90	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,534.00	932.87	12/2010	12/2011	12(O)	0/0
91	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	8,128.00	1,253.17	02/2011	03/2013	25(O)	0/0
92	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	6,146.00	1,474.84	05/2011	03/2013	22(O)	0/0
93	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91	134.32	103.00	03/2008	-	-	0/3
94	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02	143.02	104.49	11/2008	-	-	0/0
Total			45,473.36	52,777.38	19,585.98				2/152
Petroleum									
95	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	29/45
96	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.00	09/2009	12/2009	3(O)	0/0
97	MSQ UPGRADEATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	750.71	12/2009	01/2010	1(O)	0/0
98	SHORT TERM LOW COST MUMBAI REFINERY - [N16000082]	12/2006	390.00	230.00	164.51	01/2010	01/2010	0(O)	0/0
99	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00	2,869.00	2,550.34	04/2009	02/2010	2(R1)	31/36
100	INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	186.58	12/2009	02/2010	2(O)	0/0
101	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80	3,941.41	2,176.19	12/2009	02/2010	2(O)	0/0
102	PANIPAT NAPHTA CRACKER PROJECT - [160100292]	04/2006	12,138.00	14,439.00	11,284.00	09/2009	03/2010	4(R1)	61/101
103	CHENNAI-BANGALORE PIPELINE - [N16000029]	07/2007	232.11	273.00	239.08	07/2009	03/2010	8(O)	0/0
104	CHAINSANGAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77	565.00	382.13	09/2009	03/2010	6(O)	0/0
105	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13	396.13	-	10/2009	03/2010	5(O)	0/0
106	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71	639.11	520.92	12/2009	03/2010	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
107	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82	405.82	277.56	12/2009	03/2010	3(O)	0/0
108	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 350.00	389.00	331.87	06/2008	04/2010	22(O)	0/0
109	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00	139.07	57.04	10/2009	04/2010	6(O)	0/0
110	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	3,114.04	11/2009 04/2010	04/2010	0(R3)	0/0
111	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70 706.70	706.70	102.23	04/2010	04/2010	0(O)	0/0
112	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	2,800.00	1,557.81	12/2008	05/2010	17(O)	0/0
113	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	576.32	04/2009	05/2010	13(O)	0/0
114	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009	05/2010	14(O)	0/0
115	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	173.95	05/2010	05/2010	0(O)	0/0
116	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	306.39	05/2010	05/2010	0(O)	0/0
117	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,675.72	1,218.02	09/2009	06/2010	9(O)	0/0
118	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00	6,898.00	5,086.94	01/2010	06/2010	5(O)	0/0
119	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	2,305.30	1,144.34	06/2010 06/2010	06/2010	0(R1)	0/0
120	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	795.50	04/2010	06/2010	2(O)	0/0
121	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18	143.84	87.57	06/2010	06/2010	0(O)	0/0
122	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	493.93	09/2009	06/2010	9(O)	0/0
123	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	595.34	06/2006 05/2008	07/2010	26(R1)	0/2
124	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	184.43	02/2010	07/2010	5(O)	0/0
125	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	170.70	02/2010	07/2010	5(O)	0/0
126	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60	293.60	158.44	12/2009	07/2010	7(O)	0/0
127	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]	06/2005	806.00 1,007.83	1,007.83	593.33	03/2008 12/2009	08/2010	8(R1)	18/48
128	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	-	10/2010	10/2010	0(O)	0/0
129	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	-	10/2010	10/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
130	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38	3,000.00	-	10/2010	10/2010	0(O)	0/0
131	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00	1,212.85	-	10/2011	10/2010	-12(O)	0/0
132	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00	224.00	39.43	12/2010	12/2010	0(O)	0/0
133	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40	605.40	132.32	12/2010	12/2010	0(R3)	0/18
134	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40	304.40	32.06	12/2010	12/2010	0(O)	0/0
135	CAPACITY AUGMENTATION OF AGRA& FERIZABAD REGION - [N16000074]	07/2009	199.57	199.57	-	01/2011	01/2011	0(O)	0/0
136	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	600.00	523.08	03/2007	03/2011	12(R3)	3/3
137	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	1,200.00	987.26	03/2007	03/2011	0(R3)	6/6
138	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90	219.22	142.38	03/2006	03/2011	60(O)	6/6
139	NORTH TAPTI GAS FIELD DEV. - [N16000085]	07/2008	589.70	589.70	-	03/2011	03/2011	0(O)	0/0
140	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75	8,061.42	3,818.71	06/2009	04/2011	22(O)	0/0
141	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93	1,061.78	-	11/2011	04/2011	-7(O)	0/0
142	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	33.68	04/2011	04/2011	0(O)	0/0
143	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,231.40	03/2005	05/2011	74(O)	0/0
144	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	333.40	0.35	05/2010	05/2011	12(R3)	0/0
145	BNPL superlines(Uttaranchal & Punjab) - [N16000091]	12/2009	540.92	540.92	-	05/2011	05/2011	0(O)	0/0
146	VKPL Upgradation and Laying of Superlines - [N16000092]	12/2009	463.32	463.32	-	05/2011	05/2011	0(O)	0/0
147	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	267.00	26.70	08/2011	08/2011	0(O)	0/0
148	Construction of Tanks and Blending Facility at Vad - [N16000077]	02/2009	267.00	349.00	57.75	08/2011	08/2011	0(O)	0/0
149	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	49.88	09/2011	09/2011	0(O)	0/0
150	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	54.39	09/2011	09/2011	0(O)	0/0
151	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	756.00	170.08	12/2011	12/2011	0(O)	0/0
152	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00	349.00	4.85	08/2011	12/2011	4(O)	0/0
153	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	-	12/2011	12/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	-	04/2011	12/2011	8(O)	0/0
155	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00	825.00	48.11	12/2011	12/2011	0(O)	0/0
156	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	06/2007	736.65	736.65	0.01	12/2011	12/2011	0(O)	0/0
157	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64	2,163.64	-	12/2011	12/2011	0(O)	0/0
158	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT. - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0(O)	0/0
159	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	266.78	03/2010 03/2012	03/2012	0(R1)	0/0
160	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 5,633.44	5,633.44	0.61	03/2010 08/2010	03/2012	19(R1)	0/0
161	Integrated crude Oil handling facilities at Paradip - [N16000090]	12/2009	1,492.33	1,492.33	18.70	06/2012	03/2012	-3(O)	0/0
162	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	2,920.82	5.24	02/2009 09/2010	04/2012	19(R1)	0/0
163	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29 6,326.40	6,326.40	188.14	05/2010	05/2012	24(O)	0/0
164	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2012	22(O)	0/0
165	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	478.71	09/2012	09/2012	0(O)	0/0
166	Paradip-Sambalpur-Raipur-Ranchi Pipeline - [N16000088]	08/2009	1,793.00	1,793.00	5.76	09/2012	09/2012	0(O)	0/0
167	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	3,212.29	03/2012	11/2012	8(O)	0/0
168	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0(O)	0/0
169	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0(O)	0/0
170	De-bottlenecking of SMPL - [N16000089]	12/2009	1,584.00	1,584.00	1.51	-	12/2012	-	0/0
171	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	-	01/2013	01/2013	0(O)	0/0
172	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	36.27	03/2013	03/2013	0(O)	0/0
Total			150,389.80	171,409.05	50,793.21				154/265
Power									
173	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72	836.14	319.71	07/2006	03/2010	44(O)	2/5
174	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,016.74	950.76	09/2007	03/2010	30(O)	8/36
175	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL) - [180100247]	01/2005	691.83	913.33	722.72	12/2007	03/2010	27(O)	13/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL) - [180100253]	05/2005	279.30 -	340.14	287.27	07/2009 -	03/2010	8(O)	5/18
177	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34 -	241.27	131.85	06/2008 -	03/2010	21(O)	6/20
178	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	1,896.65	1,511.39	11/2008 -	03/2010	16(O)	20/38
179	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]	12/2005	3,779.46 -	3,779.46	3,257.17	09/2009 -	03/2010	6(O)	11/30
180	KOLDAM HEP TRANSMISSION LINE (PGCIL) - [180100263]	09/2005	464.91 -	464.91	163.05	09/2008 09/2008	03/2010	18(R1)	9/22
181	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]	06/2006	803.70 -	803.76	558.13	06/2009 -	03/2010	9(O)	0/20
182	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-V - [N18000017]	06/2006	721.25 -	721.25	558.63	06/2009 -	03/2010	9(O)	6/19
183	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN - [N18000020]	10/2006	150.26 -	153.24	109.54	10/2009 -	03/2010	5(O)	5/20
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI - [N18000021]	01/2007	186.95 -	186.95	146.76	07/2009 -	03/2010	8(O)	2/21
185	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST - [N18000026]	10/2006	103.80 -	103.80	70.93	06/2009 -	03/2010	9(O)	0/0
186	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	725.60	12/2007 -	06/2010	30(O)	7/18
187	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96 -	975.96	531.89	10/2009 -	06/2010	8(O)	2/20
188	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	94.18	06/2010 -	06/2010	0(O)	0/0
189	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	226.45	04/2010 -	06/2010	2(O)	0/0
190	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57 -	353.57	47.43	07/2010 -	07/2010	0(O)	0/0
191	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,805.10	02/2010 -	08/2010	6(O)	3/24
192	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	268.75	09/2010 -	09/2010	0(O)	0/0
193	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	131.18	09/2010 -	09/2010	0(O)	0/0
194	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	3,676.30	10/2010 -	10/2010	0(O)	9/40
195	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44 -	2,570.44	1,529.40	08/2010 -	11/2010	3(O)	11/26
196	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72 -	340.72	102.99	11/2010 -	11/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55 -	261.55	90.39	11/2010 -	11/2010	0(O)	0/0
198	SYSTEM STRAIGHTENING SCHEME-VIII OF SOUTHERN REGION - [N18000070]	02/2008	105.84 -	105.84	52.53	11/2010 -	11/2010	0(O)	0/0
199	KOTESHWAR HEP (THDC) - [180100184]	04/2000	1,301.56 -	1,301.56	1,667.43	04/2005 -	12/2010	68(O)	0/0
200	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63 -	1,405.63	1,112.84	08/2010 -	12/2010	4(O)	0/0
201	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	611.02	416.75	08/2010 -	12/2010	4(O)	0/0
202	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23 -	5,221.23	2,027.32	07/2010 -	12/2010	5(O)	2/20
203	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76 -	417.76	210.60	12/2010 -	12/2010	0(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36 -	408.36	254.53	12/2010 -	12/2010	0(O)	0/0
205	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89 -	230.89	11.38	01/2011 -	01/2011	0(O)	0/0
206	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92 -	1,279.40	1,064.60	03/2007 -	02/2011	47(O)	1/25
207	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	1,724.79	1,021.16	11/2009 -	02/2011	15(O)	0/0
208	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26 -	621.28	364.48	02/2011 -	02/2011	0(O)	0/0
209	URI-II - [N18000023]	10/2006	238.25 -	238.25	171.08	-	05/2011	-	0/0
210	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39 -	5,038.53	2,529.30	05/2011 -	05/2011	0(O)	0/0
211	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,304.52	942.29	10/2010 -	06/2011	8(O)	0/0
212	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24 -	557.25	285.68	01/2010 -	06/2011	17(O)	0/22
213	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07 -	204.07	56.59	06/2011 -	06/2011	0(O)	0/0
214	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61 -	276.61	71.87	06/2011 -	06/2011	0(O)	0/0
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14 -	525.14	279.90	07/2011 -	07/2011	0(O)	0/0
216	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37 -	297.37	140.93	07/2011 -	07/2011	0(O)	0/0
217	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10 -	196.10	9.96	07/2011 -	07/2011	0(O)	0/0
218	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,307.03	670.98	09/2009 -	08/2011	23(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
219	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19 -	132.19	9.62	08/2011 -	08/2011	0(O)	0/0
220	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79 -	210.79	34.64	08/2011 -	08/2011	0(O)	0/0
221	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97 -	328.97	57.44	09/2011 -	09/2011	0(O)	0/0
222	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39 -	8,323.39	6,571.00	12/2009 -	10/2011	22(O)	33/56
223	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48 -	520.48	110.02	11/2011 -	11/2011	0(O)	0/0
224	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66 -	509.66	13.69	11/2011 -	11/2011	0(O)	0/0
225	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69 -	317.69	2.51	11/2011 -	11/2011	0(O)	0/0
226	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19 -	184.19	17.24	11/2011 -	11/2011	0(O)	0/0
227	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	4,527.15	3,008.50	04/2009 -	12/2011	32(O)	19/41
228	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	16.58	01/2012 -	01/2012	0(O)	0/0
229	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	4,375.35	831.30	07/2011 -	02/2012	7(O)	0/0
230	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96 -	664.96	18.54	02/2012 -	02/2012	0(O)	0/0
231	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50 -	409.50	-	02/2012 -	02/2012	0(O)	0/0
232	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29 -	410.29	33.31	02/2012 -	02/2012	0(O)	0/0
233	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGION - [N18000060]	02/2009	120.62 -	120.62	10.78	02/2012 -	02/2012	0(O)	0/0
234	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32 -	1,347.32	163.56	02/2012 -	02/2012	0(O)	0/0
235	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	2,047.03	771.30	01/2012 -	03/2012	2(O)	2/10
236	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]	12/2008	573.99 -	573.99	82.52	08/2012 -	08/2012	0(O)	0/0
237	MOUDA STPP - [N18000048]	11/2007	5,459.28 -	5,459.28	764.60	02/2012 -	08/2012	6(O)	0/0
238	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95 -	2,360.95	765.72	08/2012 -	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
239	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	1,526.62	08/2012	08/2012	0(O)	0/0
240	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	304.68	10/2012	10/2012	0(O)	0/0
241	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	484.80	11/2012	11/2012	0(O)	0/0
242	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	425.23	11/2012	11/2012	0(O)	0/0
243	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33	6,285.33	3,751.11	09/2010	12/2012	27(O)	2/11
244	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	6.09	12/2008 09/2010	12/2012	27(R1)	0/15
245	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
246	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	440.03	12/2012	12/2012	0(O)	0/0
247	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	2,710.83	09/2009	03/2013	42(O)	1/20
248	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	733.50	03/2013	03/2013	0(O)	5/31
249	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	243.51	07/2010	04/2013	33(O)	0/0
250	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,077.81	05/2013	05/2013	0(O)	37/161
251	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	658.40	08/2013	08/2013	0(O)	0/0
252	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	482.60	08/2013	08/2013	0(O)	0/0
253	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,626.50	11/2010	10/2013	35(O)	15/51
254	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	98.10	06/2013	03/2015	21(O)	0/0
255	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	245.85	07/2014	01/2016	18(O)	0/0
256	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			165,167.29	169,829.85	63,058.96				242/894
Health & Family Welfare									
257	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	477.33	03/1999 03/2005	-	-	7/16
Total			71.18	443.15	477.33				7/16
Railways									

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
258	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00 107.29	103.57	106.47	03/2005 09/2008	05/2009	8(R3)	0/0
259	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	-	03/2009 03/2009	11/2009	8(R3)	0/0
260	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00 214.09	214.09	113.40	12/2009 -	12/2009	0(O)	0/0
261	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70 129.70	142.48	98.84	12/2008 -	12/2009	12(O)	0/0
262	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74 -	224.51	41.39	- -	12/2009	-	0/0
263	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44 -	209.57	174.22	03/2009 -	02/2010	11(O)	0/0
264	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	456.48	03/1995 -	03/2010	180(O)	0/0
265	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998 -	03/2010	144(O)	0/0
266	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 142.98	170.00	99.32	03/2002 -	03/2010	96(O)	0/0
267	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 459.55	571.55	567.85	- -	03/2010	-	0/0
268	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	693.99	03/2001 -	03/2010	108(O)	0/0
269	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 124.13	281.20	264.03	- -	03/2010	-	0/0
270	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	960.48	976.28	03/2003 -	03/2010	84(O)	0/0
271	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	501.69	278.12	- -	03/2010	-	0/0
272	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 356.90	425.90	-	- 11/2008	03/2010	16(R3)	0/0
273	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	502.14	459.07	- -	03/2010	-	0/0
274	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	746.02	06/2007 -	03/2010	33(O)	0/0
275	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	228.09	140.67	- -	03/2010	-	0/0
276	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 546.49	610.07	552.23	- 02/2009	03/2010	13(R1)	0/0
277	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	-	- 03/2009	03/2010	12(R1)	0/0
278	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84 -	136.45	131.28	03/2002 -	03/2010	96(O)	0/0
279	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	4.77	- -	03/2010	-	0/0
280	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 -	227.52	227.54	03/2008 03/2009	03/2010	12(R1)	0/0
281	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	134.52	03/1998 08/2005	03/2010	55(R3)	0/0
282	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	-	- 03/2009	03/2010	12(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
283	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	322.87	35.59	- -	03/2010	-	0/0
284	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	126.50	03/2006 -	03/2010	48(O)	0/0
285	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	-	03/2008 06/2008	03/2010	21(R3)	0/0
286	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	158.95	218.78	- -	03/2010	-	0/0
287	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 654.51	1,160.52	434.32	- -	06/2010	-	0/0
288	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	-	04/2003 03/2010	06/2010	3(R1)	0/0
289	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	1,006.89	12/2006 -	06/2010	42(O)	0/0
290	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 138.48	138.48	35.75	- -	06/2010	-	0/0
291	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	-	- 02/2009	06/2010	16(R1)	0/0
292	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	221.90	-	12/2007 03/2010	07/2010	4(R1)	0/0
293	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
294	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	-	- -	09/2010	-	0/0
295	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	335.00	299.15	12/2006 12/2008	11/2010	23(R3)	0/0
296	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 -	273.00	-	- 03/2009	11/2010	20(R1)	0/0
297	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	-	02/2015 -	11/2010	-51(O)	0/0
298	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	263.09	03/2004 -	12/2010	81(O)	0/0
299	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	672.38	650.02	- -	12/2010	-	0/0
300	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	567.00	204.13	- 12/2009	12/2010	12(R1)	0/0
301	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	135.10	-	- -	12/2010	-	0/0
302	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 716.64	718.30	-	03/2008 08/2008	12/2010	28(R1)	0/0
303	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
304	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	450.00	6.25	12/2010 -	12/2010	0(O)	0/0
305	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,174.00	3,182.58	12/2010 -	12/2010	0(O)	0/0
306	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	-	02/2010 -	02/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
307	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38 -	1,000.00	79.07	- -	02/2011	-	0/0
308	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 810.78	810.78	32.36	- -	02/2011	-	0/0
309	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	375.21	186.15	- 03/2010	03/2011	12(R1)	0/0
310	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	475.00	276.51	06/1999 -	03/2011	141(O)	0/0
311	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	50.70	- -	03/2011	-	0/0
312	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	240.05	06/2004 -	03/2011	81(O)	0/0
313	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	381.10	05/2008 -	03/2011	34(O)	0/0
314	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	341.81	- 06/2009	03/2011	21(R3)	0/0
315	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	25.89	- -	03/2011	-	0/0
316	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	371.36	234.34	- -	03/2011	-	0/0
317	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
318	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	77.17	03/2010 -	03/2011	12(O)	0/0
319	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
320	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.30	03/2011 -	03/2011	0(O)	0/0
321	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	33.29	03/2011 -	03/2011	0(O)	0/0
322	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	-	02/2010 -	11/2011	21(O)	0/0
323	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	1,121.50	642.30	- -	12/2011	-	0/0
324	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
325	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	496.03	27.08	03/2010 -	12/2011	21(O)	0/0
326	LUMDING-SILCHAR(GC),NEFR - [220100170]	04/1996	648.00 1,676.31	4,074.10	1,965.78	03/2009 -	03/2012	36(O)	0/0
327	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54 -	141.40	103.18	03/2003 -	03/2012	108(O)	0/0
328	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	385.95	61.74	- -	03/2012	-	0/0
329	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	322.95	40.56	- -	03/2012	-	0/0
330	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59 -	495.74	61.49	- -	03/2012	-	0/0
331	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 324.90	324.90	57.58	03/2010 -	03/2012	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
332	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69	501.69	45.90	03/2010	03/2012	24(O)	0/0
333	TAMLUK DIGHA - [N22000097]	03/1984	293.97	293.97	1.91	06/2005	04/2012	82(O)	0/0
334	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00	921.00	236.87	03/2009	12/2012	45(O)	0/0
335	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47	1,480.71	445.84	10/2007	12/2012	62(O)	0/0
336	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
337	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84	410.08	88.28	-	03/2013	-	0/0
338	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00	899.42	535.46	-	03/2013	-	0/0
339	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70	1,556.23	158.87	-	03/2013	-	0/0
340	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00	3,087.44	1,682.94	04/2008	03/2014	27(R1)	0/0
341	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00	1,502.29	424.34	12/2008	03/2014	63(O)	0/0
342	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00	160.48	72.47	-	03/2014	-	0/0
343	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00	546.47	0.54	-	03/2014	-	0/0
344	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00	5,300.00	120.00	03/2014	03/2014	0(O)	0/0
345	AGARTALA SABROOM - [N22000099]	04/2008	813.34	813.34	13.89	03/2014	03/2014	0(O)	0/0
346	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34	619.34	0.01	04/2014	04/2014	0(O)	0/0
347	SEVOK RANGPO - [N22000102]	04/2008	1,339.48	1,339.48	-	12/2015	12/2015	0(O)	0/0
348	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56	2,492.53	129.76	03/2011	03/2016	60(O)	0/0
349	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00	11,270.00	5,956.55	03/2001	12/2017	201(O)	0/0
350	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77	432.46	433.90	03/1994	-	-	0/0
351	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43	617.63	312.05	-	-	-	0/0
352	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53	464.50	477.15	03/1996	-	-	0/0
353	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00	318.66	452.61	03/1999	-	-	0/0
354	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80	285.93	231.68	-	-	-	0/0
355	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00	968.60	0.43	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	353.58	- -	-	-	0/0
357	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
358	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
359	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	681.07	03/2004 03/2005	-	-	0/0
360	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	226.48	- -	-	-	0/0
361	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	71.76	- -	-	-	0/0
362	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	290.22	- -	-	-	0/0
363	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	247.05	02/2009 -	-	-	0/0
364	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	103.72	49.48	- -	-	-	0/0
365	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 -	268.00	-	12/1999 03/2008	-	-	0/0
366	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
367	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	55.86	- -	-	-	0/0
368	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	89.61	03/2007 03/2007	-	-	0/0
369	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
370	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	540.09	07/2005 -	-	-	0/0
371	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	- -	-	-	0/0
372	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	62.05	- -	-	-	0/0
373	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
374	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	129.05	- 05/2009	-	-	0/0
375	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
376	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
377	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	3.99	- -	-	-	0/0
378	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	374.84	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
379	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00	695.00	9.41	-	-	-	0/0
380	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00	901.62	0.28	-	-	-	0/0
381	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	325.17	278.36	03/2005 12/2008	-	-	0/0
382	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00	133.00	-	-	-	-	0/0
383	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00	137.71	9.71	-	-	-	0/0
384	REWARI-SADULPUR-HISSAR (GC),NWR - [220100290]	04/1997	198.96 364.19	410.00	377.20	-	-	-	0/0
385	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91	459.91	36.40	-	-	-	0/0
386	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23	120.23	220.17	-	-	-	0/0
387	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86	103.86	28.93	-	-	-	0/0
388	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79	104.79	34.13	-	-	-	0/0
389	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006	-	-	0/0
390	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	1,225.00	109.16	-	-	-	0/0
391	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10	113.75	40.35	-	-	-	0/0
392	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67	165.67	0.15	-	-	-	0/0
393	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73	230.03	45.76	-	-	-	0/0
394	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	585.93	102.78	-	-	-	0/0
395	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45	573.12	555.49	-	-	-	0/0
396	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27	100.27	0.01	-	-	-	0/0
397	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10	102.10	22.75	-	-	-	0/0
398	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56	670.00	0.74	-	-	-	0/0
399	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92 261.70	261.70	0.08	02/2006	-	-	0/0
400	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67	129.78	90.84	-	-	-	0/0
401	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94	124.00	151.76	03/2004 07/2008	-	-	0/0
402	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]	09/2007	404.19 404.19	711.15	38.83	-	-	-	0/0
403	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 343.17	639.00	163.05	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
404	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00 170.00	255.96	75.34	- -	-	-	0/0
405	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 125.00	227.40	11.32	- -	-	-	0/0
406	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	24.27	- -	-	-	0/0
407	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	20.46	- -	-	-	0/0
408	BHAKURA DAMODAR - [N22000098]	03/1998	282.70 -	325.17	24.32	07/2008 -	-	-	0/0
409	KISHANGANJ JALALGARH - [N22000101]	04/2008	282.92 -	359.86	-	- -	-	-	0/0
410	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]	04/1993	100.41 -	949.22	15.65	12/2009 -	-	-	0/0
411	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 254.07	676.00	294.21	- 12/2011	06/2011	-6(R3)	0/0
412	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08 353.08	1,010.00	45.16	- 12/2012	12/2012	0(R3)	0/0
413	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	166.35	- 12/2012	12/2012	0(R1)	0/0
414	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64 117.31	106.64	139.37	03/2007 05/2008	-	-	0/0
Total			53,764.93 -	100,933.14	38,662.17				
Road Transport & Highways									
415	JAWAHARLAL NEHRU PORT PHASE-II,SH-54 - [N24000039]	04/2000	143.00 -	143.00	120.30	05/2007 -	10/2009	29(O)	0/0
416	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93 -	440.93	641.40	12/2006 -	12/2009	36(O)	0/0
417	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39 -	534.39	716.15	05/2007 -	12/2009	31(O)	0/0
418	TOVARAMKURCHI-MADURAI,NH45B (NHAI) - [N24000054]	04/2000	263.00 -	263.00	317.74	08/2008 -	12/2009	16(O)	0/0
419	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80 -	402.80	453.70	03/2009 -	12/2009	9(O)	0/0
420	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00 -	450.00	-	07/2008 -	01/2010	18(O)	0/0
421	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85 -	140.85	149.17	01/2004 -	03/2010	74(O)	0/0
422	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75 -	399.75	402.95	03/2005 -	03/2010	60(O)	0/0
423	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00 -	144.00	121.40	07/2005 -	03/2010	56(O)	0/0
424	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00 -	110.00	105.70	06/2005 -	03/2010	57(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
425	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	343.50	04/2008	03/2010	23(O)	0/0
426	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00	310.00	371.65	04/2008	03/2010	23(O)	0/0
427	MADURAI -KANIYAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.90	03/2008	03/2010	24(O)	0/0
428	MADURAI -KANNIYAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	321.30	03/2008	03/2010	24(O)	0/0
429	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	568.50	03/2009	03/2010	12(O)	0/0
430	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	367.74	02/2009	03/2010	13(O)	0/0
431	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	665.80	12/2008	03/2010	15(O)	0/0
432	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	286.30	08/2008	03/2010	19(O)	0/0
433	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	245.40	06/2008	03/2010	21(O)	0/0
434	SAGAR - RAJMARG CHORAH,KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	03/2010	17(O)	0/0
435	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	161.00	04/2008	03/2010	23(O)	0/0
436	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	636.10	05/2009	03/2010	10(O)	0/0
437	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00	110.00	113.84	07/2008	03/2010	20(O)	0/0
438	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	457.70	11/2009	03/2010	4(O)	0/0
439	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00	445.00	752.22	07/2010	03/2010	-4(O)	0/0
440	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	115.01	08/2006	04/2010	44(O)	0/0
441	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40	372.40	399.29	07/2004	04/2010	69(O)	0/0
442	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]	03/2005	168.00	168.00	227.74	12/2008	04/2010	16(O)	0/0
443	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	169.40	08/2009	04/2010	8(O)	0/0
444	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	177.40	08/2009	04/2010	8(O)	0/0
445	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	232.50	08/2009	04/2010	8(O)	0/0
446	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	149.80	08/2009	04/2010	8(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
447	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	151.46	08/2004	05/2010	69(O)	0/0
448	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	199.18	01/2009	05/2010	16(O)	0/0
449	GONDE-VADAPPE (THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	510.08	04/2009	05/2010	13(O)	0/0
450	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	64.42	05/2010	05/2010	0(O)	0/0
451	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	127.20	09/2007	06/2010	33(O)	0/0
452	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	61.79	08/2004	06/2010	70(O)	0/0
453	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	450.31	03/2005	06/2010	63(O)	0/0
454	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	241.10	07/2004	06/2010	71(O)	0/0
455	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	774.10	11/2007	06/2010	31(O)	0/0
456	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	406.80	11/2007	06/2010	31(O)	0/0
457	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	144.43	08/2005	06/2010	58(O)	0/0
458	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	425.90	04/2008	06/2010	26(O)	0/0
459	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	533.81	03/2009	06/2010	15(O)	0/0
460	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	797.58	11/2010	06/2010	-5(O)	0/0
461	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	353.70	06/2008	06/2010	24(O)	0/0
462	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	359.65	06/2008	06/2010	24(O)	0/0
463	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	189.13	10/2008	06/2010	20(O)	0/0
464	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	144.10	07/2008	06/2010	23(O)	0/0
465	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	399.70	06/2008	06/2010	24(O)	0/0
466	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	06/2010	15(O)	0/0
467	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.44	06/2008	06/2010	24(O)	0/0
468	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	159.60	11/2008	06/2010	19(O)	0/0
469	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	550.82	06/2009	06/2010	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
470	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	196.59	02/2004	06/2010	76(O)	0/0
471	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	30.89	04/2009	06/2010	14(O)	0/0
472	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	200.00	09/2009	06/2010	9(O)	0/0
473	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	214.80	09/2008	06/2010	21(O)	0/0
474	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	301.43	06/2010	06/2010	0(O)	0/0
475	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	177.60	06/2010	06/2010	0(O)	0/0
476	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	164.02	06/2010	06/2010	0(O)	0/0
477	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	58.86	08/2004	07/2010	71(O)	0/0
478	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	111.60	03/2008	07/2010	28(O)	0/0
479	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	83.56	03/2008	07/2010	28(O)	0/0
480	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	152.10	06/2008	07/2010	25(O)	0/0
481	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.55	07/2010	07/2010	0(O)	0/0
482	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	415.64	07/2010	07/2010	0(O)	0/0
483	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	727.76	07/2010	07/2010	0(O)	0/0
484	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	666.80	03/2010	07/2010	4(O)	0/0
485	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	173.40	06/2008	08/2010	26(O)	0/0
486	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	250.80	08/2010	08/2010	0(O)	0/0
487	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52	111.78	0.52	06/2004	09/2010	75(O)	0/0
488	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	265.59	03/2005	09/2010	66(O)	0/0
489	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	214.80	09/2009	09/2010	12(O)	0/0
490	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	242.30	09/2009	09/2010	12(O)	0/0
491	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
492	LUMDING TO DABOKA - [N24000110]	12/2003	130.00	130.00	45.56	08/2010	09/2010	1(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
493	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
494	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	118.20	09/2006	10/2010	49(O)	0/0
495	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	262.59	10/2008	10/2010	24(O)	0/0
496	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	287.70	10/2008	10/2010	24(O)	0/0
497	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	332.80	10/2008	10/2010	24(O)	0/0
498	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	244.70	10/2008	10/2010	24(O)	0/0
499	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	292.10	10/2008	10/2010	24(O)	0/0
500	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	172.90	10/2008	10/2010	24(O)	0/0
501	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	172.18	10/2009	10/2010	12(O)	0/0
502	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	418.65	03/2005	12/2010	69(O)	0/0
503	KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A - [240102193]	04/2000	110.00	110.00	142.24	12/2004	12/2010	72(O)	0/0
504	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	617.30	04/2007	12/2010	44(O)	0/0
505	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00	275.00	-	09/2007	12/2010	39(O)	0/0
506	JAM-WADNER - [240106209]	12/2003	145.00	145.00	71.49	07/2005	12/2010	65(O)	0/0
507	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	92.79	06/2005	12/2010	66(O)	0/0
508	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00	284.00	276.40	05/2008	12/2010	31(O)	0/0
509	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00	227.00	212.10	10/2008	12/2010	26(O)	0/0
510	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68	340.68	227.10	03/2008	12/2010	33(O)	0/0
511	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00	280.00	118.60	02/2009	12/2010	22(O)	0/0
512	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81	199.81	27.66	04/2009	12/2010	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
513	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
514	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04	155.04	27.96	11/2008	12/2010	25(O)	0/0
515	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00	200.00	55.40	04/2009	12/2010	20(O)	0/0
516	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00	225.00	165.70	06/2008	12/2010	30(O)	0/0
517	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00	195.00	86.50	06/2008	12/2010	30(O)	0/0
518	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	289.40	12/2008	12/2010	24(O)	0/0
519	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	262.00	12/2008	12/2010	24(O)	0/0
520	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]	12/2003	237.80	237.80	89.74	06/2008	12/2010	30(O)	0/0
521	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	100.10	10/2008	12/2010	26(O)	0/0
522	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	102.80	10/2008	12/2010	26(O)	0/0
523	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	254.27	06/2009	12/2010	18(O)	0/0
524	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	54.47	04/2008	12/2010	32(O)	0/0
525	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	132.00	06/2008	12/2010	30(O)	0/0
526	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	227.20	03/2008	12/2010	33(O)	0/0
527	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	86.08	04/2008	12/2010	32(O)	0/0
528	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	117.50	06/2008	12/2010	30(O)	0/0
529	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	116.30	04/2008	12/2010	32(O)	0/0
530	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	54.05	05/2008	12/2010	31(O)	0/0
531	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	117.30	06/2008	12/2010	30(O)	0/0
532	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	126.20	06/2008	12/2010	30(O)	0/0
533	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.11	09/2007	12/2010	39(O)	0/0
534	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.53	07/2009	12/2010	17(O)	0/0
535	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	63.87	04/2010	12/2010	8(O)	0/0
536	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	142.40	10/2008	12/2010	26(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	176.32	02/2010	12/2010	10(O)	0/0
538	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	189.50	12/2009	12/2010	12(O)	0/0
539	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
540	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	808.79	02/2010	12/2010	10(O)	0/0
541	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	-	02/2004	12/2010	82(O)	0/0
542	TRICHY - DINDIGUL NH-45 - [N24000099]	03/2005	576.00	576.00	254.40	07/2010	01/2011	6(O)	0/0
543	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	526.99	01/2011	01/2011	0(O)	0/0
544	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	207.70	01/2011	01/2011	0(O)	0/0
545	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	107.80	09/2007	02/2011	41(O)	0/0
546	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	182.61	07/2005	03/2011	68(O)	0/0
547	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	207.19	07/2005	03/2011	68(O)	0/0
548	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	153.18	10/2008	03/2011	29(O)	0/0
549	FORBESGANJ TO SIMRAHI (NH-57)(NHA) - [240106294]	12/2003	332.94	332.94	134.40	09/2008	03/2011	30(O)	0/0
550	LALITPUR TO SAGAR, NH-26 (NHA) - [240106299]	12/2003	198.00	198.00	105.20	11/2008	03/2011	28(O)	0/0
551	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	420.90	10/2009	03/2011	17(O)	0/0
552	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	84.04	09/2010	03/2011	6(O)	0/0
553	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	453.26	05/2010	05/2011	12(O)	0/0
554	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	129.10	09/2007	06/2011	45(O)	0/0
555	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	53.32	09/2008	06/2011	33(O)	0/0
556	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40	117.40	35.41	11/2008	06/2011	31(O)	0/0
557	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHA) - [240106304]	12/2003	251.03	251.03	62.13	10/2008	06/2011	32(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
558	RAJMARG CHORAH TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA - [240106305]	12/2003	229.91	229.91	29.18	10/2008	06/2011	32(O)	0/0
559	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	228.00	03/2010	06/2011	15(O)	0/0
560	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	-	04/2004	10/2011	90(O)	0/0
561	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	243.50	09/2008	12/2011	39(O)	0/0
562	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
563	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	6.05	05/2010	08/2012	27(O)	0/0
564	DEVDHARI-WADNER - [240106208]	12/2003	145.00	145.00	24.71	07/2005	-	-	0/0
565	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]	12/2003	300.00	300.00	-	10/2008	-	-	0/0
Total			43,916.82	44,119.51	34,939.24				0/0
<u>Shipping & Ports</u>									
566	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00	100.00	0.50	01/2010	01/2010	0(O)	0/0
567	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00	165.00	72.76	12/2005	03/2010	51(O)	0/0
568	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32	411.32	406.28	03/2010	03/2010	0(O)	0/0
569	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67	298.17	290.01	04/2009	03/2010	11(O)	0/0
570	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84	253.36	129.62	06/2007 01/2009	04/2010	15(R1)	0/0
571	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59	1,658.59	318.24	07/2010	07/2010	0(O)	0/0
572	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	813.75	10/2008	11/2010	25(O)	0/0
573	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58	586.58	241.64	11/2010	11/2010	0(O)	0/0
574	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
575	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
576	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	882.00	0.16	02/2011	02/2011	0(O)	0/0
577	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	702.00	0.73	03/2011	03/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
578	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	211.21	04/2011	04/2011	0(O)	0/0
579	Acquisition of two nos. of 120 B.P - [N25000042]	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
580	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	374.36	04/2011	12/2011	8(O)	0/0
581	Acquisition of Two nos. of 3060 DWT - [N25000043]	04/2009	2,770.32	2,770.42	554.06	09/2011	12/2011	3(O)	0/0
582	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
583	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
584	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0
585	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
	Total		18,154.63	18,426.49	3,943.71				0/0
	Telecommunications								
586	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	10/2009	46(O)	0/0
587	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	34(O)	0/0
588	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	12/2009	20(O)	0/0
589	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	15(O)	0/0
590	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	422.85	12/2008	12/2009	12(O)	0/0
591	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	113.34	03/2009	12/2009	9(O)	0/0
592	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	483.54	470.24	12/2008	12/2009	12(O)	0/0
593	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	180.93	03/2009	12/2009	9(O)	0/0
594	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	12/2009	3(O)	0/0
595	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	169.33	12/2008	01/2010	13(O)	0/0
596	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	0.00	278.16	175.77	12/2008 12/2009	01/2010	1(R3)	0/0
597	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	110.83	03/2009	01/2010	10(O)	0/0
598	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15	149.15	40.87	06/2009	01/2010	7(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
599	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	336.81	64.50	01/2009	01/2010	12(O)	0/0
600	NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.24	12/2004	02/2010	62(O)	0/0
601	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007 12/2009	03/2010	3(R3)	0/0
602	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	94.13	10/2007 12/2009	03/2010	3(R3)	0/0
603	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25	133.75	34.05	06/2008 02/2010	03/2010	1(R3)	0/0
604	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	104.60	12/2009 12/2009	03/2010	3(R3)	0/0
605	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	161.35	02/2008	05/2010	27(O)	0/0
606	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	73.54	09/2009	06/2010	9(O)	0/0
607	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	10(O)	0/0
608	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53 2.00	180.53	25.97	12/2009	06/2010	6(O)	0/0
609	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007 11/2009	12/2010	13(R3)	0/0
610	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
611	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
612	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
613	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]	11/2008	350.00	350.00	-	-	-	-	0/0
614	CENTRALISED TRANSMISSION NMS - [N26000064]	08/2009	300.00	300.00	-	-	-	-	0/0
Total			11,637.90	11,534.73	3,705.76				0/0
<u>Urban Development</u>									
615	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67	135.03	-	02/2010	02/2010	0(O)	0/0
616	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00 8,605.36	8,676.00	12,228.48	06/2010	10/2010	4(O)	0/7
617	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 8,158.00	6,395.00	1,636.20	12/2011 09/2012	12/2011	-9(R3)	0/1
Total			14,596.67	15,206.03	13,864.68				0/8
<u>Water Resources</u>									

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
618	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			566,811.15	652,941.56	265,596.20				748/1958
