

**304th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
February, 2011**



NPCIL - Kudankulam



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for February 2011 (the 304th Flash Report) contains information on the status of the 565 projects in the Central Sector costing ` 150 Crores and above. During February 2011, 5 projects reported completion (which have now been dropped from the monitor of this Ministry) and one project namely Loharinag – Pal HEP has been frozen. Five new projects have been added during the month under reference.

The online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably and all projects reported online during the current month. This has been mainly due to the continued effort/persuasion by this Ministry. During February 2011, forty (40) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 12 months in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and . Highways, Telecommunications, Shipping & Ports, Urban Development and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	122	12
2.	RAILWAYS	145	2
3.	POWER	82	8
4.	PETROLEUM	70	12
5.	COAL	45	1
6.	TELECOMMUNICATION	41	1
7.	STEEL	14	1
8.	SHIPPING & PORTS	25	1
9.	CIVIL AVIATION	7	0
10.	FERTILISERS	6	0
11.	ATOMIC ENERGY	3	1
12.	URBAN DEVELOPMENT	3	1
13.	MINES	1	0
14.	WATER RESOURCES	1	0
Total		565	40

3. The total original cost of implementation of the 565 projects was about ` 604245.71 Crores and their anticipated completion cost is likely to be ` 726336.99 Crores, which reflects an overall cost overrun of 20.20%. The expenditure incurred on these projects till February, 2011 is ` 313088.62 Crores.

4. Out of the 565 projects, 9 projects are ahead of schedule, 123 are on schedule and 285 projects are delayed and 61 projects have been sanctioned without any commissioning schedule/date .. Further in case of 87 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month the project reporting delays have marginally decreased to 285 from 289 in January'2011. The overall cost overrun has also reduced to 20% from 21 % in January 2011. Out of 285 delayed projects, at the end of February, 2011, 69 projects had overall delay in the range of 1 to 12 months, 67 projects had delay in the range of 13 to 24 months, 112 projects had delay in the range of 25 to 60 months and 37 projects had delay of 61 months and above.

The Sector-wise details of delays are as under:-

i) In the **Coal sector**, the TPS-II Expansion (1470MW To 1970MW) NLC Project has reported additional delay of two months (an overall delay of 30 months) due to delay in delivery of boiler equipments and delay in erection by BHEL.

ii) In the **Steel sector**, rebuilding of Coke Oven Battery No-6 (Bokaro Steel Plant) SAIL has reported an additional delay of 2 months (an overall delay of 16 months) due to delay in supply of fireclay & silica brick by the contractor.

iii) In the **Petroleum Sector**, 12 projects have reported additional delays in the range of 1-7 months. Diesel Hydro Treatment Project Dhaligaon BRPL, Residue Upgradation and MS/HSD Quality Improvement project of IOCL and BNPL Superlines (Uttanchal & Punjab) of GAIL have reported additional delay of one month each (an overall delay of 8 months) due to slow progress by the contractors. C2-C3 and LPG Recovery from LNG, Dahej, ONGC has reported an additional delay of 2 months due to delay in LSTK contract works. MSQ

Improvement Project IOCL has reported delay of 2 months due to delay in supply of equipment by BHEL. Sultanpur Neemrana Pipeline Project (Superline to CJPL) GAIL and Dahej -Vijaypur Pipe Line Project (Phase-II) GAIL have reported an additional delay of 2 months each due to high land compensation demanded by the farmers. BNPL superlines (Uttaranchal and Punjab) GAIL has reported an additional delay of 2 months due to pending court cases. Compressor Stations (Kailaras & Chainsa) GAIL has reported additional delay of three months due to delay in electrical and instrumental work by the contractors. Bawana Nangal Pipe Line Project GAIL has reported an additional delay of 4 months due to additional financial implication of Rs. 276 crores above DFR provision. VKPL Upgradation and Laying of Spurline (Bhilwara and Chittore) GAIL has reported an additional delay of 4 months due to delay in submitting the final survey report. Compressor Stations (Vijaypur and Jhabua) Phase - 1 GAIL has an additional delay of 6 months (overall delay of 6 months) due to delay in supply of equipment. Heera and South Heera Re-development Project ONGC, has reported an additional delay of 7 months, however no specific reason has been reported by the Project authority.

iv) In the **Power Sector**, 8 projects have reported additional delays in the range of 1-6 months. Koteswar Transmission System (PGCIL) has reported an additional delay of 1 month due to delay in generation project. Farakka STPP Stage III NTPC has reported an additional delay of 1 month, for which no specific reason has been reported. System Strengthening in NR GRID for Karcham Wangto PGCIL and Transmission System for Phase -1 generation project PGCIL have reported an additional delay of one month each and no specific reason for delay has been reported. Teesta Low Dam Phase-III & Phase IV Hydro Electric Power Project NHPC have reported an additional delay of 2 months each due to delay in forest clearance , award of E &M contract and strike by GJMM activities. Transmission System Associated with Barh Generation Project PGCIL has reported an additional delay of four months due to delay in generation project. Bongaigaon Thermal Power Project (NTPC) has reported an additional delay of 6 months due to slow progress by civil agency and delay in erection of Turbo Generator.

v) In the **Road Transport and Highways Sector**, 12 projects have reported additional delay in the range of 1-9 months. 5 projects have reported additional delay of one month each due to slow progress of work by the contractor. Gagodhar – Garamore (Phase -IV, NH-15) KM 245 to 281.3 and 308 to 254 NHA has reported additional delay of 3 months due to change of

scope. Ayodhya-Lucknow , NH-28 of NHAI has reported additional delay of 3 months due to disruptions by the locals in the execution of works at various places. Ayodhya –Lucknow (LMNHP-II) KM 93.075 to KM 45, NH-28 NHAI has reported an additional delay of 3 months due to delay in finalization of drawings for Major Bridge at River Saryu. Aurang-Raipur NH-6, KM 232 to KM 281 NHAI has reported an additional delay of 3 months due to delay in land acquisition and ROB issues. Ganga Bridge to Ramdevi Crossing Phase II NH -25, KM 75 - 80.06 NHAI and Kosi Bridge including approaches NHAI have reported an additional delay of 6 months each due to delay in forest clearance and acquisition of land. Agra Shikohabad (GQ) KM 199.66-KM 250.50 (NH-2) NHAI has reported an additional delay of 9 months due to delay in construction of ROB at Tundla.

vi) In the Urban Development Sector, Delhi MRTS Phase –II Project DMRC has reported an additional delay of four months (overall delay of 12 months) due to slow progress by the contractor.

vii) In the Railway Sector, 2 projects namely, Muzaffarpur Sitamarhi (NL) ECR and Mansi-Purnia (Extension of Mansi – Saharsa) ECR have reported additional delay of 12 months each due to slow progress by contractors.

viii) In the Telecommunication Sector, convergent Billing and CRM (Mumbai of MTNL) has reported additional delay of 5 months (overall delay of 54 months) due to delay in supply of equipment.

ix) In the Shipping & Ports Sector, acquisition of 4 of Anchor Handling Cum Supply SCI, has shown additional delays of 2 months (overall delay of 2 months) due to slow progress by the contractor.

x) In the Atomic Energy Sector, Kudankulam APP(NPCIL has an additional delay of 3 months (overall 39 months) for which there is no specific reason has been reported.

The status as on 01.03.2011 in respect of completion of projects costing ` 150 Crores and above in different sectors during 2010-11 is indicated in the Report.



(T.C.A. Anant)
Secretary

Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	145	2
2	Road Transport & Highways	122	12
3	Power	82	8
4	Petroleum	70	12
5	Coal	45	1
6	Telecommunications	41	1
7	Shipping & Ports	25	1
8	Steel	14	1
9	Civil Aviation	7	0
10	Fertilisers	6	0
11	Atomic Energy	3	1
12	Urban Development	3	1
13	Mines	1	0
14	Water Resources	1	0
	Total	565	40

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	168.33	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93
September,2010				
<u>Coal</u>				
8	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)(NEYVELI LIGNITE CORPORATION) - [060100090]	254.07	06/2009	1,687.78
<u>Steel</u>				
9	REBUILDING OF COKE OVEN BATTERY-10(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000016]	416.50	09/2009	305.14
<u>Petroleum</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
10	PANIPAT NAPHTA CRACKER PROJECT(INDIAN OIL CORPORATION LIMITED) - [160100292]	12,138.00	09/2009	12,054.37
11	DADRI- PANIPAT R-LNG SPUR PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000018]	250.66	06/2008	350.96
12	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000026]	638.90	04/2009	796.21
13	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE(INDIAN OIL CORPORATION LIMITED) - [N16000034]	348.00	12/2009	186.58
14	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000035]	1,131.00	12/2009	750.71
15	CHAINSAR-JHAJJAR PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000047]	967.77	09/2009	416.90
16	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000067]	643.46	-	726.45
17	Construction of Tank and Blending Facility at Vadi(INDIAN OIL CORPORATION LIMITED) - [N16000075]	267.00	-	72.99
18	BINA DESPATCH TERMINAL(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000078]	490.71	12/2009	590.52
<u>Railways</u>				
19	HOSPET-GUNTAKAL(LD),SCR(RAIL VIKAS NIGAM LTD.) - [220100195]	105.22	12/1999	283.49
20	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100224]	536.85	03/2003	1,005.50
21	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR)(RAIL VIKAS NIGAM LTD.) - [220100244]	223.00	-	586.85
22	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000033]	352.00	03/2008	616.44
23	ABOHAR- FAZILKA, NR, NL(NORTHERN RAILWAY) - [N22000055]	86.44	03/2009	201.79
<u>Road Transport & Highways</u>				
24	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100203]	440.93	12/2006	641.40
25	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100204]	534.39	05/2007	716.15
26	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101178]	372.40	07/2004	406.05
27	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101181]	467.93	03/2005	453.64
28	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101187]	399.75	03/2005	424.96
29	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106227]	276.00	04/2008	360.00
30	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106228]	310.00	04/2008	392.26
31	MADURAI - KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106241]	507.49	03/2008	342.80
32	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106257]	556.00	03/2009	568.50

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
33	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106273]	469.80	12/2008	665.80
34	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106285]	261.00	08/2008	286.30
35	TOVARAMKURCHI-MADURAI,NH45B (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000054]	263.00	08/2008	317.74
36	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000060]	402.80	03/2009	453.70
37	PADALUR-TRICHY, NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000083]	320.00	05/2009	636.10
38	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000093]	360.42	11/2009	478.40
39	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000105]	450.00	07/2008	876.61
40	ISLAM NAGAR TO KADTAL(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000109]	546.83	03/2010	667.80
41	WAINGANGA BRIDGE -CHHATISGARH-MAHARASHTRA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000120]	424.00	09/2010	298.40
Shipping & Ports				
42	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS(SHIPPING corp. of india) - [N25000013]	411.32	03/2010	406.28
43	DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA(PORT TRUST) - [N25000046]	2,118.00	11/2004	.00
Telecommunications				
44	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I(DEPARTMENT OF TELECOMMUNICATION) - [260100051]	279.97	12/2004	136.24
45	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA(BHARAT SANCHAR NIGAM LIMITED) - [260100095]	1,174.75	03/2006	371.41
46	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000026]	741.77	10/2007	151.37
47	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH-(BHARAT SANCHAR NIGAM LIMITED) - [N26000028]	364.52	-	51.44
48	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000042]	409.21	12/2008	470.24
49	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000061]	180.53	12/2009	25.97
October,2010				
Health & Family Welfare				
50	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS(HEALTH & FAMILY WELFARE) - [210100001]	71.18	03/1999	547.78
Railways				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
51	DHARMAVARAM-PAKALA (GC), SCR(SOUTH CENTRAL RAILWAY) - [220100282]	200.00	-	567.49
Road Transport & Highways				
52	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106268]	263.00	02/2009	420.80
53	AMRITSAR-WAGHA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000121]	205.88	06/2010	214.90
Shipping & Ports				
54	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE(SHIPPING crp. of india) - [N25000029]	1,658.59	07/2010	1,657.45
Telecommunications				
55	GSM BASED NETWORK EXPANSION PLAN PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000034]	239.19	04/2008	96.97
56	Provision of data network for CWG delhi(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000076]	488.76	10/2010	198.65
57	Expn of existing 2G & 3G GSM N/W by 750k(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000077]	180.53	06/2010	40.92
58	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph(BHARAT SANCHAR NIGAM LIMITED) - [N26000079]	577.35	09/2010	40.76
November,2010				
Petroleum				
59	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL)(INDIAN OIL CORPORATION LIMITED) - [160100289]	1,876.00	04/2009	2,747.34
60	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA(INDIAN OIL CORPORATION LIMITED) - [N16000017]	806.00	03/2008	840.06
Power				
61	SEWA- II H.E.P (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100220]	665.46	09/2007	982.76
62	NORTHERN REGION SYSTEM STRENGTHENING-XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000034]	417.76	12/2010	266.87
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000036]	408.36	12/2010	304.83
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000039]	261.55	11/2010	143.36
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000055]	525.14	07/2011	354.99
Railways				
66	RAJGIR-TILAIYA (NL), ECR(EAST CENTRAL RAILWAYS) - [220100312]	180.82	03/2006	272.46

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
67	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000079]	205.92	08/2009	204.50
68	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000080]	243.64	08/2009	256.40
<u>Telecommunications</u>				
69	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M(BHARAT SANCHAR NIGAM LIMITED) - [N26000051]	908.30	08/2009	211.83
70	CENTRALISED TRANSMISSION NMS(BHARAT SANCHAR NIGAM LIMITED) - [N26000064]	300.00	-	.00
December,2010				
<u>Petroleum</u>				
71	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000036]	372.00	-	229.04
72	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000037]	356.00	-	222.69
73	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY(INDIAN OIL CORPORATION LIMITED) - [N16000038]	1,492.00	04/2010	1,113.09
<u>Road Transport & Highways</u>				
74	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106302]	206.96	10/2008	281.90
75	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000078]	243.38	09/2008	286.40
76	BANGALORE-NEELAMANGALALA NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000104]	445.00	07/2010	803.40
<u>Shipping & Ports</u>				
77	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS(SHIPPING corp. of india) - [N25000030]	586.58	11/2010	634.09
<u>Telecommunications</u>				
78	KOLKATA TELECOM DISTRICT PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000036]	208.50	09/2008	146.00
January,2011				
<u>Atomic Energy</u>				
79	KAIGA 3 and 4 UNITS (NPCIL)(NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100041]	4,213.00	10/2009	2,610.00
<u>Steel</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
80	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000025]	302.70	06/2009	244.97
81	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000035]	892.32	-	616.57
82	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS- II(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000036]	197.66	11/2009	130.32
83	POWER PLANT-I(RASTRIYA ISPAT NIGAM LIMITED) - [N12000039]	462.00	12/2009	84.40
84	EXPANSION OF SALEM STEEL PLANT(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000050]	1,902.00	06/2011	1,754.78
<u>Petroleum</u>				
85	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000048]	5,595.31	11/2009	3,326.01
<u>Power</u>				
86	KORBA STPP STAGE-III(NATIONAL THERMAL POWER CORPORATION) - [N18000011]	2,448.50	02/2010	2,119.00
87	National Capital Thermal Power Project Stage-II(NATIONAL THERMAL POWER CORPORATION) - [N18000013]	5,135.33	10/2010	4,062.00
88	WESTERN REGION STRENGTHENING SCHEME-VI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000038]	340.72	11/2010	164.37
<u>Railways</u>				
89	HOTGI-GADAG(GC),SWR(SOUTH WESTERN RAILWAY) - [220100125]	180.00	03/1999	360.21
90	BHILDI-SAMDARI (GC)(RAIL VIKAS NIGAM LTD.) - [220100291]	244.74	-	476.85
91	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN(GAUGE CONVERSION) - [N22000103]	100.41	12/2009	911.24
<u>Road Transport & Highways</u>				
92	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100206]	106.00	08/2006	141.70
93	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106202]	480.00	11/2007	846.20
94	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251- 293(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000076]	208.46	08/2009	197.80
95	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4- 3(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000077]	239.19	09/2009	224.80
96	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211- 251(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000081]	194.80	08/2009	179.70
February,2011				
<u>Civil Aviation</u>				
97	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000017]	290.92	01/2011	266.53

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2010-2011**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
98	MIRAJ-LATUR ROAD(GC),CR(CENTRAL RAILWAYS) - [220100162]	225.00	03/2001	845.26
<u>Road Transport & Highways</u>				
99	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106245]	239.00	10/2008	396.30
100	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106249]	451.97	04/2008	533.70
101	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106296]	291.80	06/2008	455.00
<u>Shipping & Ports</u>				
102	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM(PORT TRUST) - [N25000015]	245.67	04/2009	304.01

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
September,2011				
<u>Road Transport & Highways</u>				
1	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N16000082]	300.00	10/2008	.00
November,2011				
<u>Civil Aviation</u>				
2	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N12000021]	535.00	06/2010	331.80


Summary of projects in the Flash Report for the month of February, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	582
Number of Projects completed/dropped/frozen in Previous Month	19
Number of Projects completed/dropped/frozen in Current Month	7
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	4
Number of Projects Added in Current Month	5
Number of Projects in Current Month	565

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 565 projects, 9 projects are ahead of schedule, 123 projects are on schedule and 285 projects are delayed. Of the balance, 87 projects do not have fixed dates of commissioning while 61 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

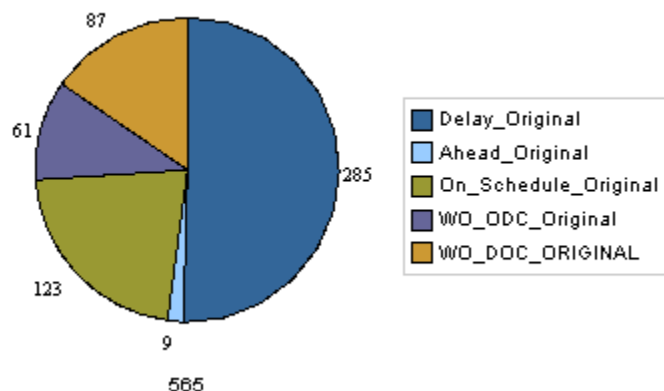

III. Investment Scenario

The Total Original cost of implementation of 565 projects when sanctioned, was of the order of Rs. 604245.71 crore but this was subsequently revised to Rs. 726336.99 crore implying a cost overrun of 20.2%. The expenditure incurred on these projects till February, 2011 is Rs. 313088.62 crore, which is 43.1% of the revised cost of the projects.

Figures are in Rs. Crore

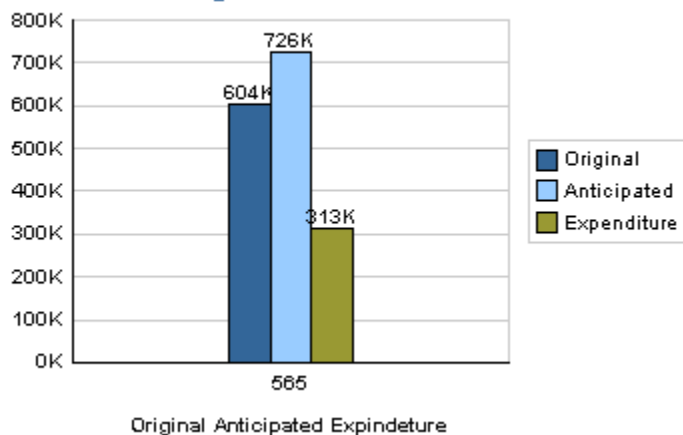

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	582
No of Projects Completed/Dropped/Frozen in Previous Month	19
No of Projects Completed/Dropped/Frozen in Current Month	7
No. of projects with Cost Anticipated greater than Rs. 150 Cr in Current Months	4
No of Projects added in Current Month	5
No of Projects in Current Month	565

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	285	9	123	61	87	565	50.44
Latest Approved (Date)	298	10	153	47	58	565	52.74

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	482	521,223.11	566,662.21	226,069.39	39.90	45,439.10	8.70
Latest Approved (RCE)	83	138,144.93	159,674.78	87,019.23	54.50	21,529.85	15.60
Total (RCE)	565	659,368.04	726,336.99	313,088.62	43.11	66968.95	10.16
Original Cost of All Projects							
Original Cost	565	604,245.71	726,336.99	313,088.62	43.10	122,091.28	20.20

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	285	305,138.32	380,182.27	217,009.65	57.10	75,043.95	24.60
Latest Approved (RCE)	298	322,733.78	367,619.64	208,287.60	56.70	44,885.86	13.90
Total	583	627,872.10	747,801.91	425,297.25	56.87	119929.81	19.10

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	40	64,965.59	76,434.18	63,226.90	82.70	11,468.59	17.70

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Railways</u>						
MIRAJ-LATUR ROAD(GC),CR	04/1993	225.00	03/2001	816.40	02/2011	845.26
<u>Road Transport & Highways</u>						
GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00	12/2003	239.00	10/2008	239.00	02/2011	396.30
ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0	12/2003	451.97	04/2008	451.97	03/2011	533.70
DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI)	12/2003	291.80	06/2008	291.80	02/2011	455.00
<u>Power</u>						
LOHARINAG-PAL HEP(4X150MW)	06/2006	2,895.10	11/2011	2,895.10	12/2012	552.33
<u>Civil Aviation</u>						
CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A	02/2007	290.92	01/2011	290.92	02/2011	266.53
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	03/2007	245.67	04/2009	298.17	02/2011	304.01

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Shipping & Ports</u>					
MARINE LIQUID TERMINALS	10/2004	196.25	6/2006	196.25	9/2011
<u>Petroleum</u>					
Polypropylene unit	5/2009	1,803.78	7/2012	1,803.78	7/2012
MRPL Phase-III Expansion	8/2008	12,412.00	1/2012	12,160.00	1/2012
<u>Shipping & Ports</u>					
DEVELOPMENT OF IRON ORE TERMINAL	9/2006	370.00	8/2010	370.00	4/2011
DEVELOPMENT OF COAL TERMINAL	9/2006	399.13	8/2010	399.13	3/2011

VII. Milestones (Cumulative due & achieved)

Total	1986
Achieved up to month	879

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	12/2011	03/2012	3
<u>Coal</u>						
TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	2,453.57	06/2009	10/2011	12/2011	2
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) SAIL	172.78	172.78	01/2010	02/2011	04/2011	2
<u>Petroleum</u>						
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON BRPL	1,431.91	1,690.13	09/2009	03/2011	04/2011	1
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT IOCL	5,693.00	6,898.00	N.A.	02/2011	03/2011	1
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) ONGC	900.92	976.08	06/2006	02/2011	04/2011	2
MSQ IMPROVMENT PROJECT IOCL	293.60	293.60	12/2009	03/2011	05/2011	2
SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) GAIL	396.13	266.00	10/2009	01/2011	03/2011	2
DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) GAIL	4,429.38	2,500.00	10/2011	04/2011	06/2011	2
BNPL superlines(Uttranchal & Punjab) GAIL	540.92	375.00	05/2011	11/2011	01/2012	2
COMPRESSOR STATIONS (KAILARAS &CHAINS) GAIL	1,167.00	810.00	04/2011	06/2011	09/2011	3
BAWANA NANGAL PIPE LINE PROJECT GAIL	1,816.07	1,200.00	N.A.	06/2011	10/2011	4
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	375.00	06/2011	08/2011	12/2011	4
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I GAIL	1,512.00	975.00	N.A.	04/2011	10/2011	6
HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT ONGC	2,305.30	2,305.30	06/2010	03/2011	10/2011	7

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Power</u>						
KOTESWAR TRANSMISSION SYSTEM (PGCIL) PGCIL	260.34	241.27	06/2008	02/2011	03/2011	1
Farakka STPP Stage-III NTPC	2,570.44	2,570.44	08/2010	02/2011	03/2011	1
SYSTEM STRENGHTENING IN NR GRID FOR KARCHAM WANGTO PGCIL	328.97	328.97	09/2011	02/2011	03/2011	1
Transmission System for phase-1 generation project PGCIL	2,074.86	2,074.86	02/2013	02/2013	03/2013	1
TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT NHPC	768.92	768.92	03/2007	12/2011	02/2012	2
TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,061.38	09/2009	08/2012	10/2012	2
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) PGCIL	3,779.46	3,725.13	09/2009	06/2011	10/2011	4
BONGAIGAON THERMAL POWER PROJECT (NTPC) NTPC	4,375.35	4,375.35	07/2011	10/2012	04/2013	6
<u>Railways</u>						
MUZAFFARPUR-SITAMARHI(NL),ECR ECR	100.00	329.29	N.A.	03/2011	03/2012	12
MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR ECR	114.01	348.78	N.A.	03/2011	03/2012	12
<u>Road Transport & Highways</u>						
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS NHAI	210.00	210.00	04/2007	02/2011	03/2011	1
MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	02/2011	03/2011	1
KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	02/2011	03/2011	1
THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	02/2011	03/2011	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	03/2011	04/2011	1
GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 NHAI	412.78	479.54	11/2007	03/2011	06/2011	3
AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 NHAI	193.00	193.00	10/2008	03/2011	06/2011	3

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 NHAI	217.00	217.00	10/2008	03/2011	06/2011	3
AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	03/2011	06/2011	3
GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 NHAI	155.00	201.66	09/2008	06/2011	12/2011	6
KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN NHAI	418.04	418.04	03/2010	06/2011	12/2011	6
AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	03/2011	12/2011	9
<u>Shipping & Ports</u>						
ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY SHIPP.	359.44	359.44	04/2011	04/2011	06/2011	2
<u>Telecommunications</u>						
CONVERGENT BILLING AND CRM-MTNL(DELHI) MTNL	249.00	229.41	02/2007	03/2011	08/2011	5
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT DMRC	8,676.00	18,894.36	06/2010	02/2011	06/2011	4
Number of projects reporting additional delay = 40						

List of Projects Without Date of Commissioning as on 01.03.2011

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
Civil Aviation				
1	C/o new Airport at Pakyong(Sikkim) Airport	01/2011	N.A.	01/2011
2	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TER BLDG(K1)	01/2011	N.A.	01/2011
Petroleum				
1	CAPACITY EXP. CUM MODERNISATION PH-II	12/2009	N.A.	12/2010
2	De-bottlenecking of SMPL	N.A.	N.A.	N.A.
3	Guru Govind Singh Refinery Products Evacuation Project	12/2010	12/2010	12/2010
4	INSTALLATION OF FCCV AT MUMBAI REFINERY	09/2009	N.A.	12/2010
5	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	12/2010	N.A.	01/2011
6	JHAJJAR HISSAR PIPE LINE PROJECT	10/2010	N.A.	N.A.
Power				
1	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	12/2007	N.A.	N.A.
Railways				
1	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	N.A.	N.A.	N.A.
2	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	N.A.	11/2010	N.A.
3	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	03/2009	12/2008	12/2010
4	AMBALA-MORADABAD(RE)	03/1998	N.A.	N.A.
5	ANGAMALI-SABARIMALA (N.L.)(SR)	N.A.	N.A.	N.A.
6	BANGLORE - SATYAMANGALAM (NL)(SWR)	N.A.	N.A.	N.A.
7	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	03/2004	N.A.	N.A.
8	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	N.A.	N.A.	12/2010
9	CALICUT-MANGALORE (DL) (SR)	N.A.	N.A.	N.A.
10	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT	N.A.	N.A.	N.A.
11	DALLIRAJHARA-JAGDALPUR,NL,SECR	N.A.	N.A.	N.A.
12	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	N.A.	N.A.	N.A.
13	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	03/1995	N.A.	N.A.
14	GONDIA-JABALPUR(GC),(SECR)	03/1998	N.A.	N.A.
15	GULBARGA-BIDAR,SCR(NL)	N.A.	05/2009	N.A.
16	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)	N.A.	N.A.	N.A.
17	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU	N.A.	N.A.	N.A.
18	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	N.A.	N.A.	N.A.
19	HOWRAH-AMTA-CHAMPADANGA NL (SER)	03/2007	03/2007	N.A.
20	HUBLI-ANKOLA(NL),SWR	N.A.	N.A.	N.A.
21	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	06/2007	N.A.	N.A.
22	KARUR-SALEM(NL),SR	N.A.	N.A.	N.A.
23	KATIHAR - JOGBANI (GC)(NEFR)	N.A.	12/2010	12/2010
24	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	N.A.	N.A.	N.A.

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
25	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	N.A.	03/2009	12/2010
26	KICHHA-KHATIMA (NL) - NER	N.A.	N.A.	N.A.
27	KISHANGANJ JALALGARH, NEFR	N.A.	N.A.	N.A.
28	KODERMA GIRIDH (NL), ECR	N.A.	N.A.	N.A.
29	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR	07/2005	N.A.	N.A.
30	KODERMA-TILAIYA (NL), ECR	N.A.	N.A.	N.A.
31	KOTLPALLI-NARASAPUR (NL) (SCR)	N.A.	N.A.	N.A.
32	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR)	N.A.	N.A.	N.A.
33	MACHERLA-NALGONDA(NL)(SCR)	07/2008	N.A.	N.A.
34	MANOHARABAD-KOTHPALL NEW LINE(SCR)	N.A.	N.A.	N.A.
35	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTHAMPALLI	N.A.	N.A.	N.A.
36	MUNEERABAD-MAHABOONNAGAR(NL),SCR	N.A.	N.A.	N.A.
37	NANDYAL-YERRAGUNTALA(NL),SCR	02/2009	N.A.	N.A.
38	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	N.A.	N.A.	N.A.
39	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	N.A.	N.A.	N.A.
40	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR	N.A.	N.A.	N.A.
41	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	03/2008	06/2008	N.A.
42	Pandabeswar-Chinpai doubling (ER)	12/2010	12/2010	12/2010
43	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	N.A.	N.A.	N.A.
44	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	03/2008	10/2010	10/2010
45	PURNA-AKOLA (G.C), SCR	N.A.	N.A.	N.A.
46	RAICHUR-GUNTAKAL(DL)(SCR)	12/2007	03/2010	12/2010
47	RAJATGARH-BARANG(LD),ECOR	N.A.	02/2009	12/2010
48	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	03/1996	06/2009	N.A.
49	RAMGANJMUNDI-BHOPAL (NL),WCR	N.A.	N.A.	N.A.
50	RENIGUNTA-GUNTAKAL(RE)	04/2003	03/2010	N.A.
51	SURENDRANAGAR-BHAVNAGAR(GC),WR	03/2004	03/2010	N.A.
52	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	N.A.	12/2009	N.A.
53	TIDIVANAM-NAGARI (NL)	N.A.	N.A.	N.A.
54	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	N.A.	N.A.	N.A.
55	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	N.A.	N.A.	N.A.
56	VALLAPARPADM-IDAPALLY,(NL)(RVNL)	03/2009	N.A.	N.A.
57	VILLUPURAM-KATPADI (GC)(SR)	N.A.	N.A.	N.A.
Shipping & Ports				
1	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND JN PORT C	10/2008	N.A.	N.A.
2	SETHUSAMUDRAM SHIP CHANNEL PROJECT	10/2008	N.A.	11/2010
Steel				
1	AIR SEPARATION PLANT (ASU-4)	06/2010	N.A.	10/2010
Telecommunications				
1	Execution of telecom network requirement of defence forces	03/2009	N.A.	N.A.



SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
2	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06	10/2007	N.A.	N.A.
3	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3G) PH-5.1	09/2009	N.A.	02/2010
4	GSM equipment of 375000Lines (2G) 75000lines 3(G) Kolkatta Phase V.1 Telecom Circle	06/2009	N.A.	01/2011
5	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle	03/2009	N.A.	01/2011
6	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment	03/2010	N.A.	10/2010
7	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant	03/2010	N.A.	10/2010
8	MANAGED LEASED LINE NETWORK PH-VI	N.A.	N.A.	N.A.
9	NIB-II PROJECT RURAL BROADBAND	02/2008	N.A.	12/2010
10	Procurement of 10G (40 chl) DWDM equipment	03/2009	N.A.	N.A.
11	Procurement of 10G 40 CHL (12 chi equipped) DWDM equipment (SDCA level)	03/2010	N.A.	12/2010
12	Procurement of 2.5G DWDM equipment	03/2009	N.A.	12/2010
13	Procurement of DXC equipment	03/2010	N.A.	11/2010
14	Procurement of STM-1 SDH equipment	03/2010	N.A.	12/2010
15	Procurement of STM-16 ADM equipment	03/2010	N.A.	12/2010
16	Procurement of STM-16 MADM equipment	03/2010	N.A.	12/2010
17	PROJ.III OF NIB-II OF MESSAGING STORAGE	12/2005	N.A.	10/2010
Urban Development				
1	C/o office building for IDBI at bandra Kurla Complex,Mumbai	04/2009	N.A.	01/2011

List of Projects Without Original Date of Commissioning as on 01.03.2011


SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
Atomic Energy				
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALLE	N.A.	N.A.	04/2011
Coal				
1	RANAGUNDAM OC-II EXTENSION	N.A.	N.A.	03/2012
2	Kistaram OCP	N.A.	N.A.	03/2015
3	RKP OCP PHASE-I	N.A.	N.A.	03/2015
4	MANUGURU OC-II EXTENSION PHASE-II	N.A.	N.A.	03/2012
5	KAKATIYA LAONGWALL	N.A.	12/2012	03/2015
6	JALLARAM SHAFT PROJECT	N.A.	N.A.	03/2013
7	RAJMAHAL OC EXP.	N.A.	N.A.	03/2014
8	KANIHA OCP	N.A.	N.A.	03/2013
9	BHUBANESWARI OCP	N.A.	N.A.	03/2017
Fertilisers				
1	THAL AMMONIA REVAMP PROJECT	N.A.	11/2011	11/2011
Petroleum				
1	PARADIP REFINERY PROJECT	N.A.	N.A.	11/2012
2	EURO-IV DHDT	N.A.	N.A.	12/2011
3	CDU/VDU-II	N.A.	N.A.	03/2012
4	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I & II	N.A.	N.A.	10/2011
5	Paradip-Sambalpur-Raipur-Ranchi Pipeline	N.A.	N.A.	09/2012
6	BAWANA NANGAL PIPE LINE PROJECT	N.A.	04/2011	10/2011
7	HYDROCRACKER REVAMP & SETTING	N.A.	N.A.	12/2011
8	Assam gas Cracker project	N.A.	N.A.	04/2012
9	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT PROJECT AT GUJRAT	N.A.	06/2010	03/2011
Power				
1	Transmission system associated with Uri-II HEP	N.A.	N.A.	05/2011
Railways				
1	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	N.A.	N.A.	03/2011
2	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	N.A.	12/2010	06/2011
3	SHIMOGA-TALAGUPPA (SWR), GC	N.A.	N.A.	02/2011
4	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	N.A.	N.A.	03/2012
5	SRIGANGANAGAR-SARUPSAR (GC), NWR	N.A.	N.A.	03/2011
6	DAUSA-GANGAPUR CITY(NL),NWR	N.A.	N.A.	03/2013
7	VIRAMGAM-BHILDI(WR),GC	N.A.	03/2013	03/2013
8	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	N.A.	03/2011	03/2012
9	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	N.A.	N.A.	03/2015
10	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	N.A.	N.A.	03/2012
11	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR	N.A.	N.A.	03/2011

SN	NAME	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
12	TALCHER-BIMALAGARH(NL)(ECOR)	N.A.	N.A.	02/2011
13	CHHINDWARA - NAGPUR (GC)(SECR)	N.A.	N.A.	12/2013
14	BILASPUR-URKURA (DL)	N.A.	03/2009	03/2011
15	HATHUA-BHATNI (N L) (NER)	N.A.	N.A.	03/2011
16	MAHARAJGANJ-MASRAKH (NL) - NER	N.A.	N.A.	03/2011
17	RANGIA-MURKONGSELEK, (GC) NEFR	N.A.	N.A.	03/2013
18	KOSI BRIDGE (NL), ECR	N.A.	N.A.	03/2012
19	HARIDASPUR-PARADEEP(NL)	N.A.	09/2009	12/2011
20	KHURDA ROAD-BOLANGIR(NL)ECOR	N.A.	N.A.	03/2011
21	JIND-SONEPAT (NL),NR	N.A.	03/2012	12/2012
22	DEOGHAR - SULTANGANJ (INL), ER	N.A.	12/2012	N.A.
23	GADWAL - RAICHUR (NL), SCR	N.A.	N.A.	02/2011
24	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR)	N.A.	N.A.	03/2011
25	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	N.A.	N.A.	03/2013
26	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	N.A.	N.A.	03/2013
27	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	N.A.	N.A.	12/2012
28	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	N.A.	N.A.	03/2012
29	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	N.A.	N.A.	12/2012
30	KOTTUR-HARIHAR(NL),(SWR)	N.A.	N.A.	03/2011
31	KANPUR-KASGANJ-MATHURA(GC),NER	N.A.	N.A.	02/2012
32	MUZAFFARPUR-SITAMARHI(NL),ECR	N.A.	N.A.	03/2012
33	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	N.A.	03/2012	03/2012
34	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	N.A.	12/2011	12/2011
Steel				
1	EXPANSION OF BOKARO STEEL PLANT	N.A.	12/2011	12/2011
2	EXPANSION OF BHILAI STEEL PLANT	N.A.	03/2013	03/2013
3	INSTALLATION OF 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI	N.A.	N.A.	05/2011
4	Bailadila Iron Ore Deposit- II(B)(NMDC)	N.A.	N.A.	10/2011
5	330 TPH BOILER-6 AND AUXILIARY SYSTEM	N.A.	N.A.	06/2011
Telecommunications				
1	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	N.A.	03/2011	02/2011


Trend and Graphical Analysis of All Projects

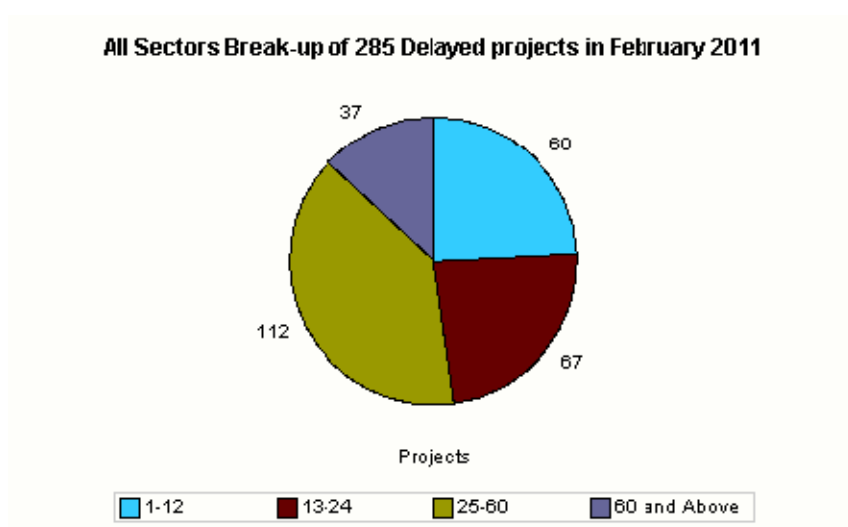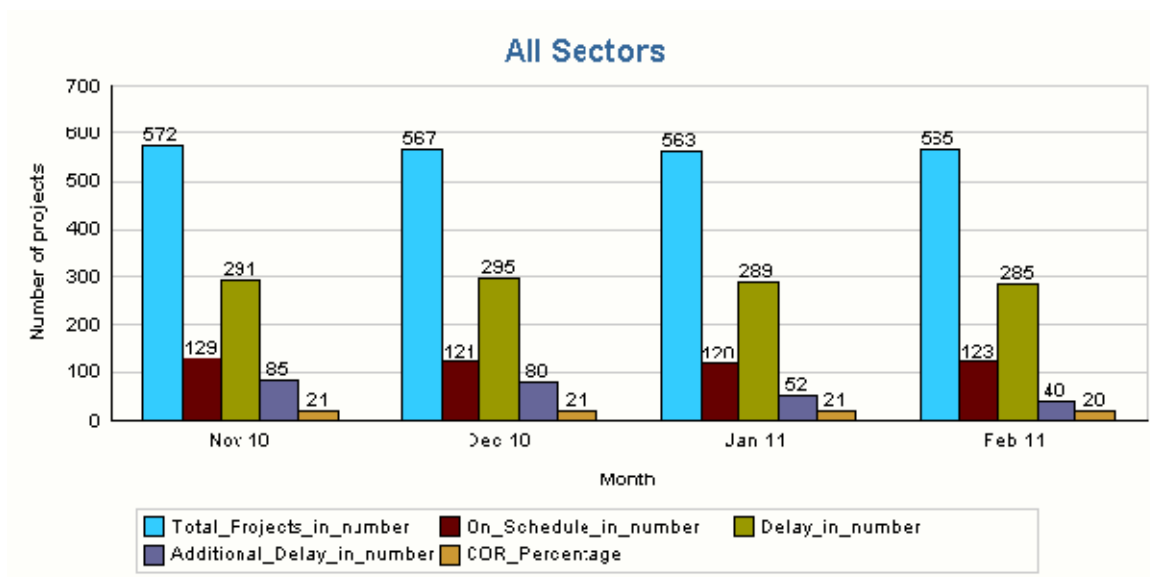


Trend and Graphical Analysis of Urban Development Sector

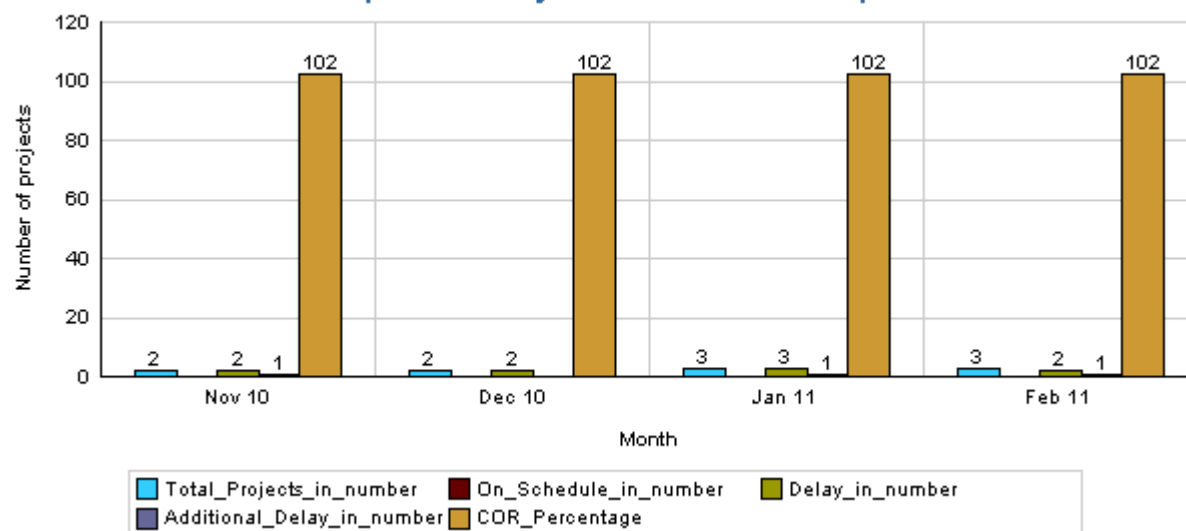


Urban Development Sector Break-up of 2 Delayed projects in February 2011

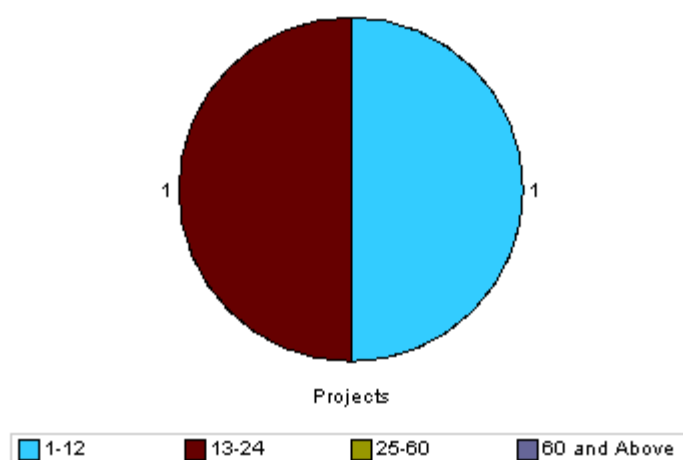


Trend and Graphical Analysis of Telecommunications Sector

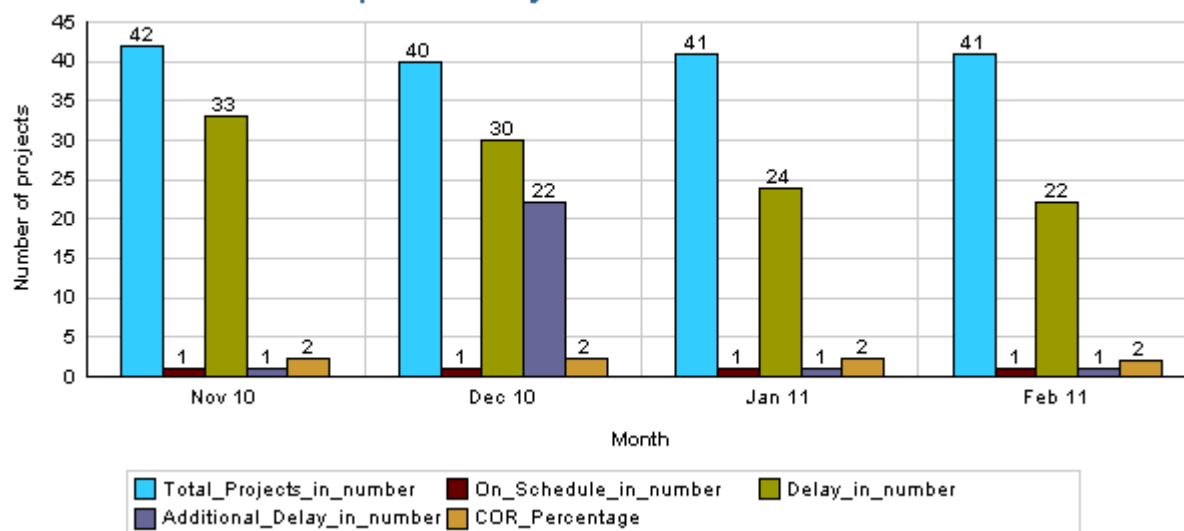


Telecommunications Sector Break-up of 22 Delayed projects in February 2011

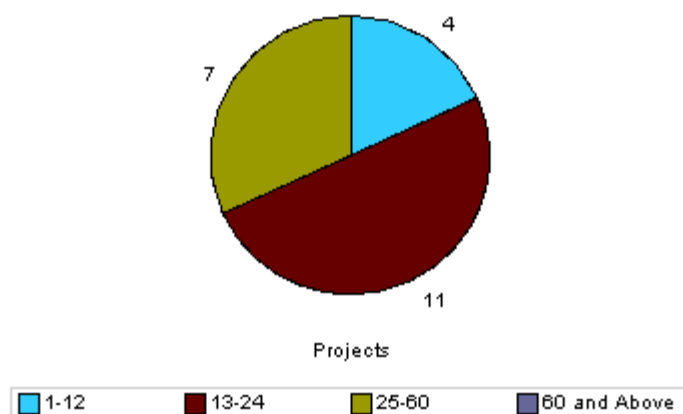


Trend and Graphical Analysis of Shipping and Ports Sector

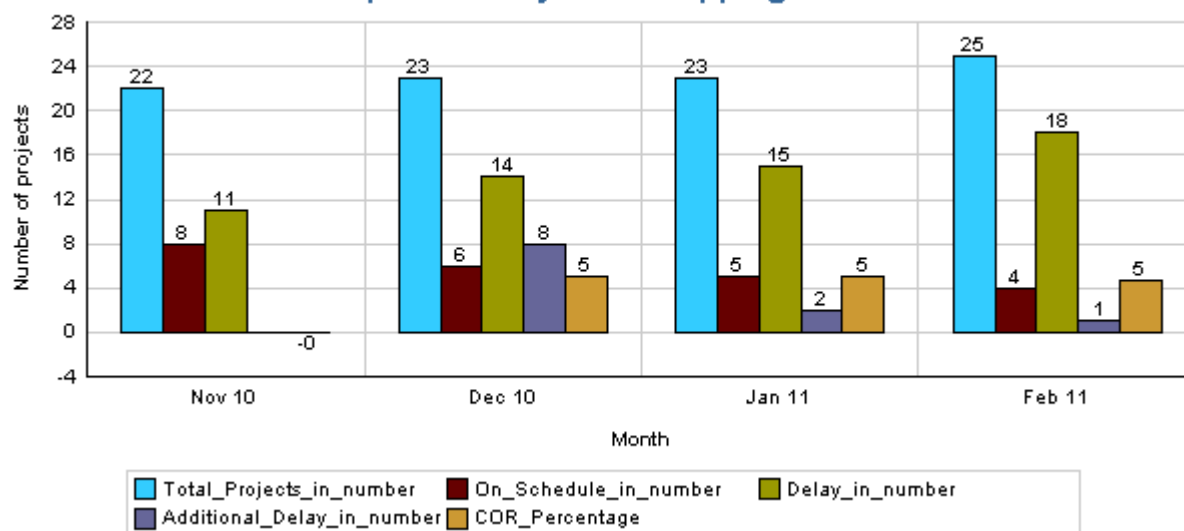


Sector Break-up of 18 Delayed projects in February 2011

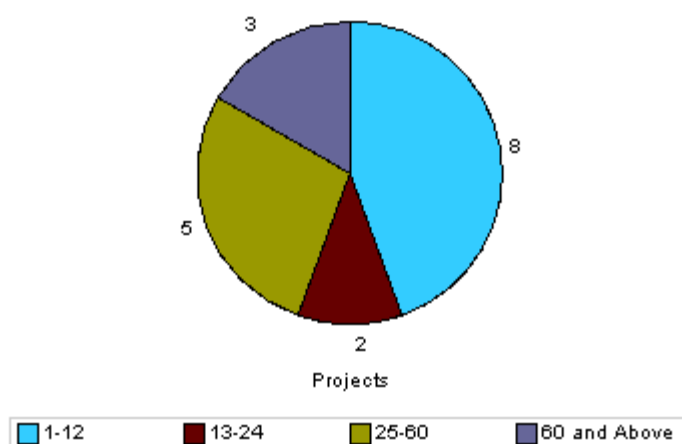


Trend and Graphical Analysis of Road Transport and Highways Sector

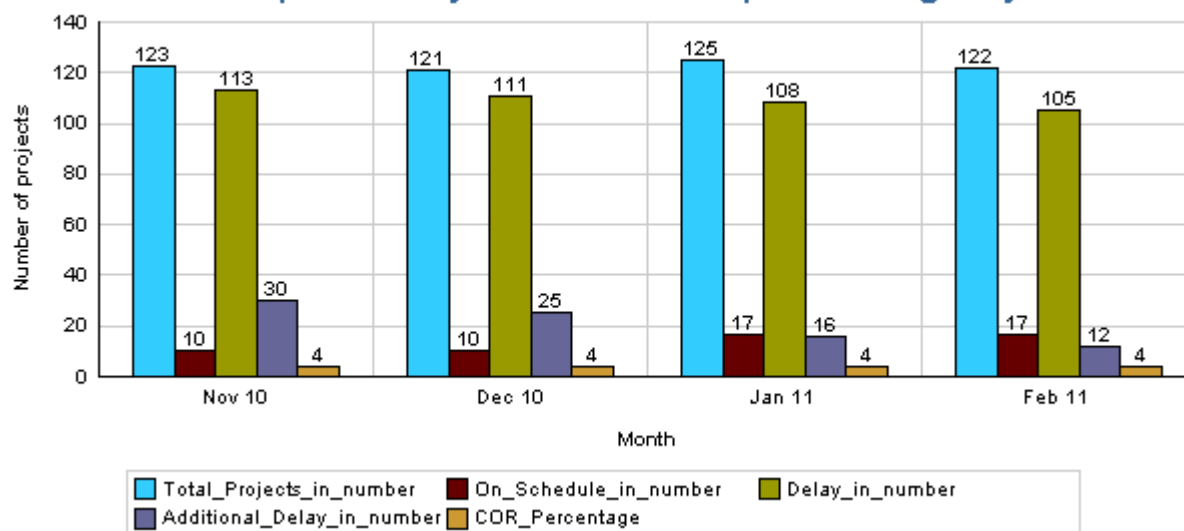


Sector Break-up of 105 Delayed projects in February 2011

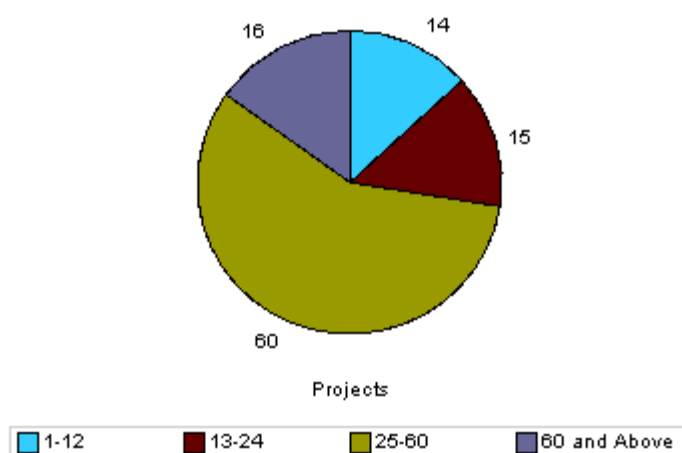


Trend and Graphical Analysis of Railways Sector

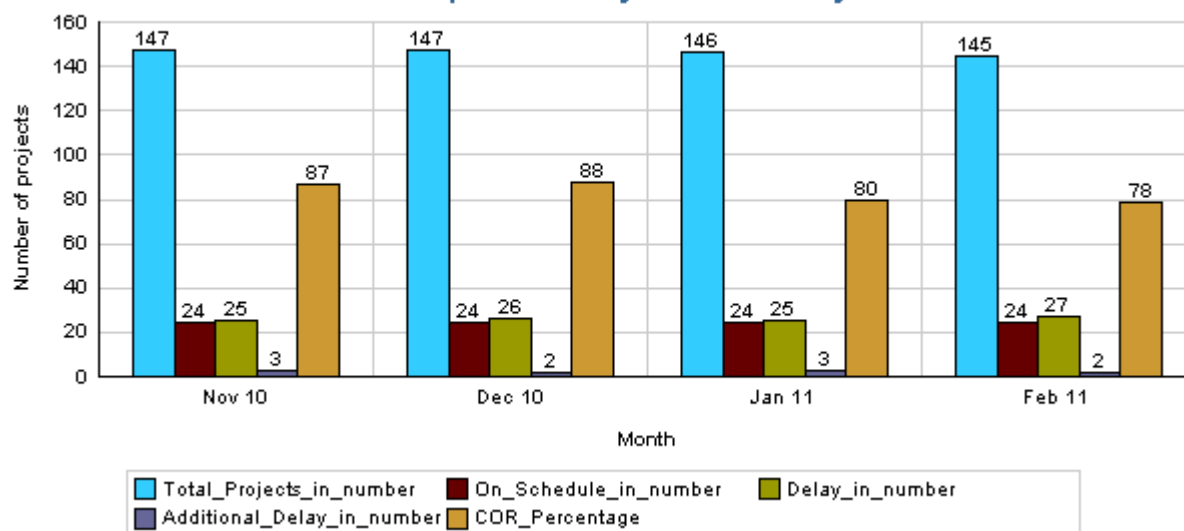


Railways Sector Break-up of 27 Delayed projects in February 2011

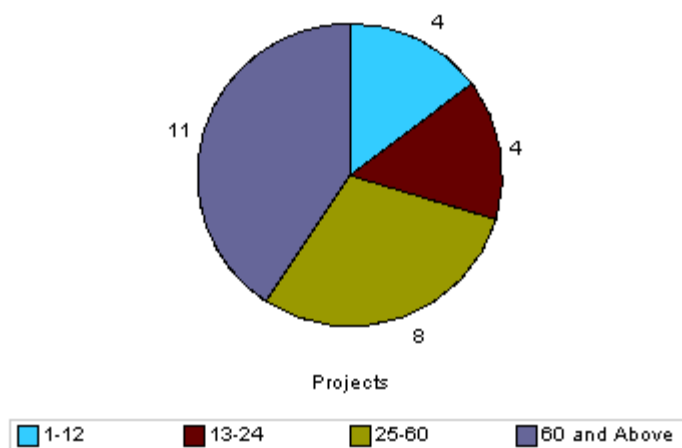


Trend and Graphical Analysis of Power Sector

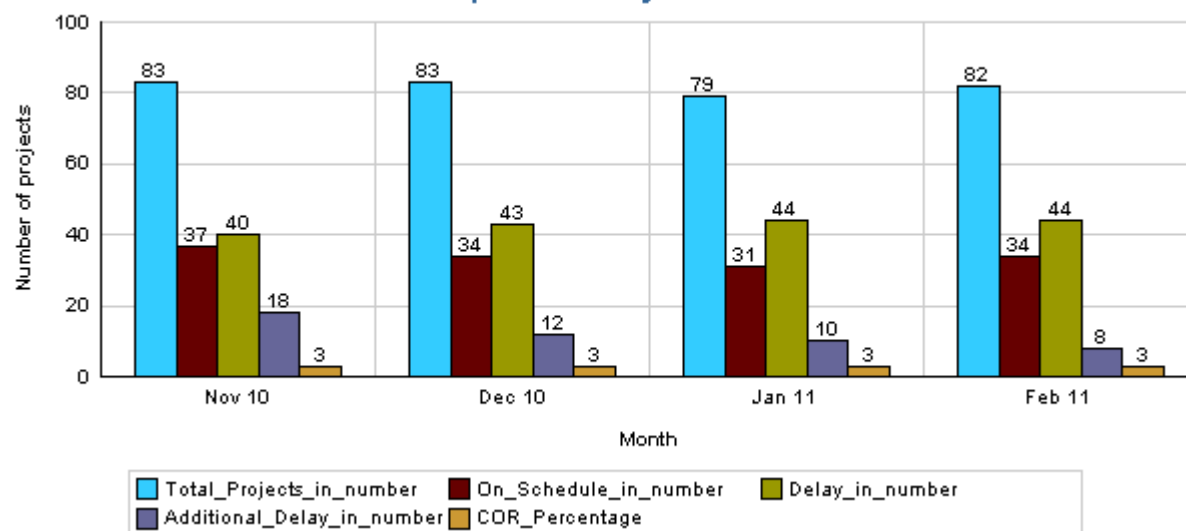


Power Sector Break-up of 44 Delayed projects in February 2011

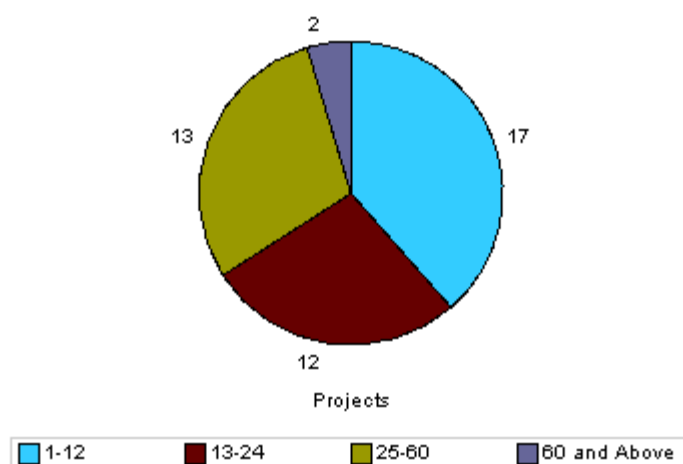


Trend and Graphical Analysis of Petroleum Sector

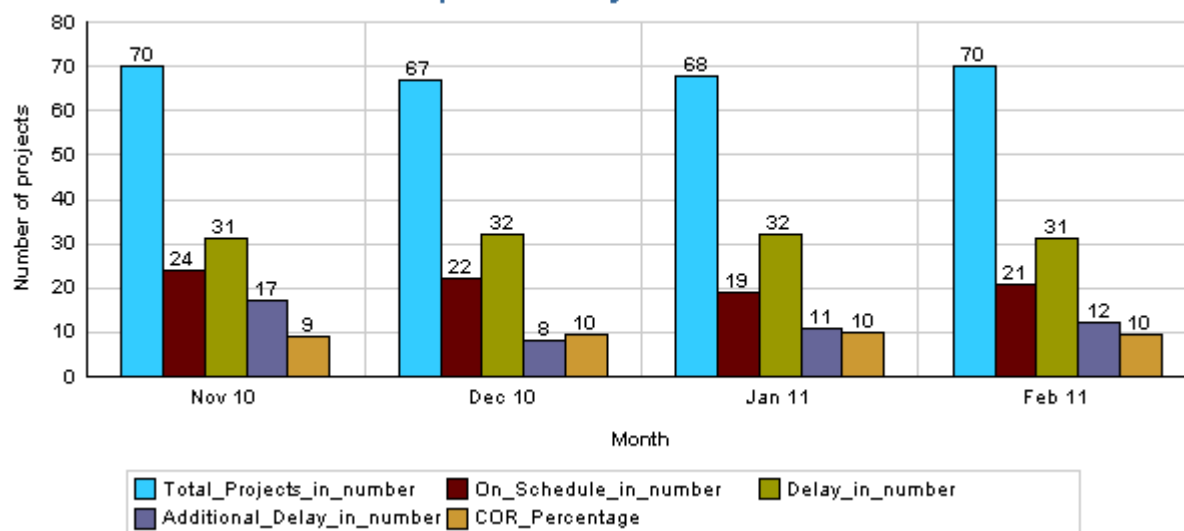


Petroleum Sector Break-up of 31 Delayed projects in February 2011

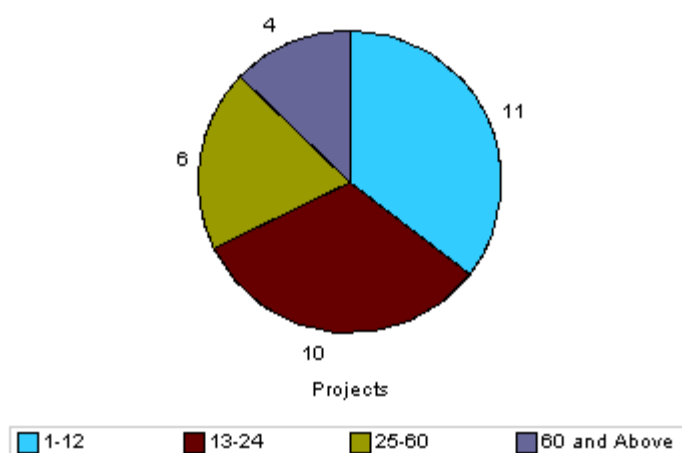


Trend and Graphical Analysis of Steel Sector

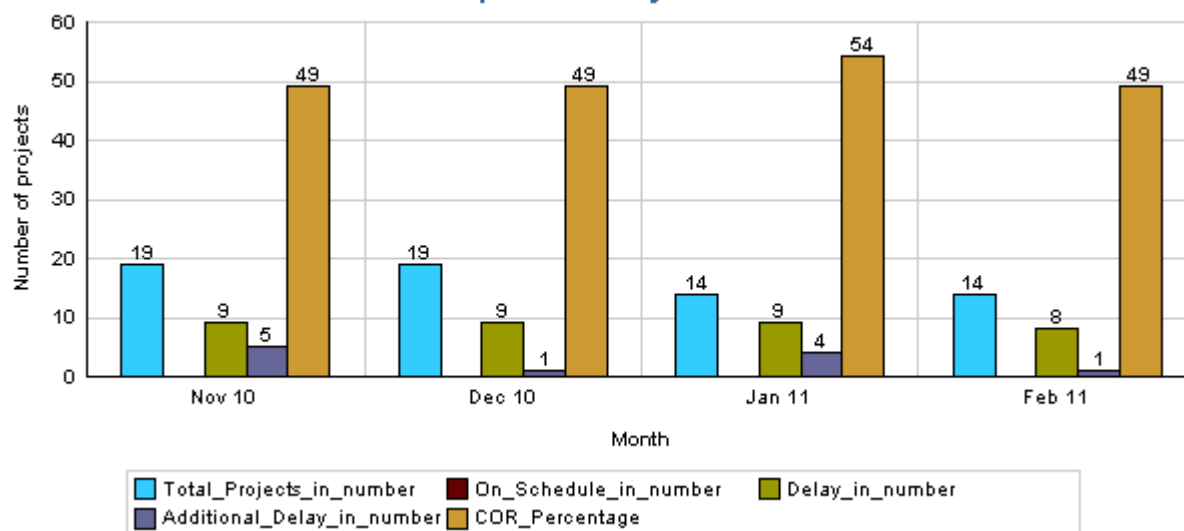

Steel Sector Break-up of 8 Delayed projects in February 2011

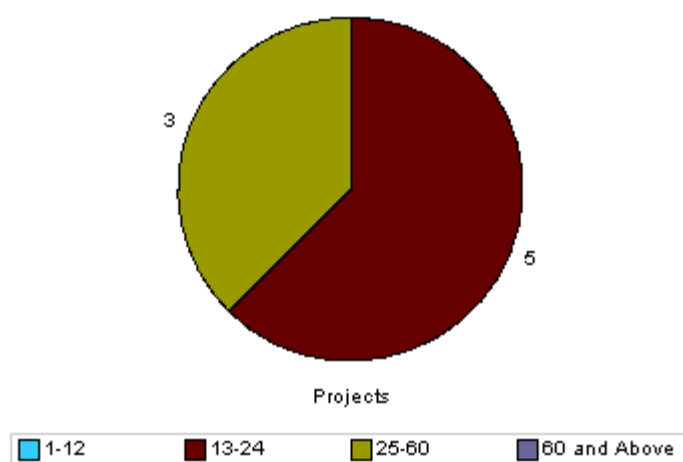


Trend and Graphical Analysis of Fertilisers Sector

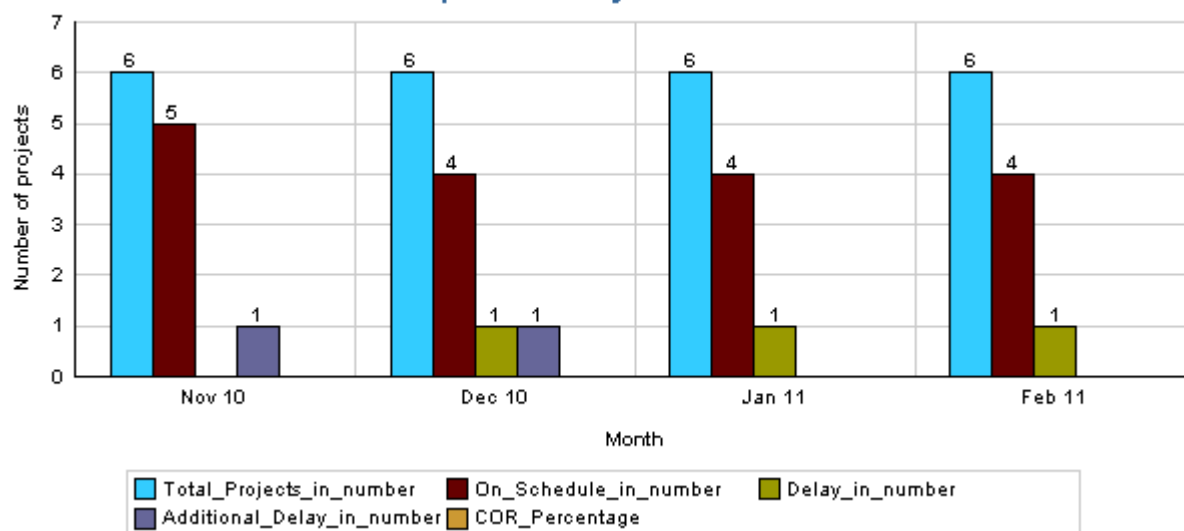


Fertilisers Sector Break-up of 1 Delayed projects in February 2011




Trend and Graphical Analysis of Coal Sector

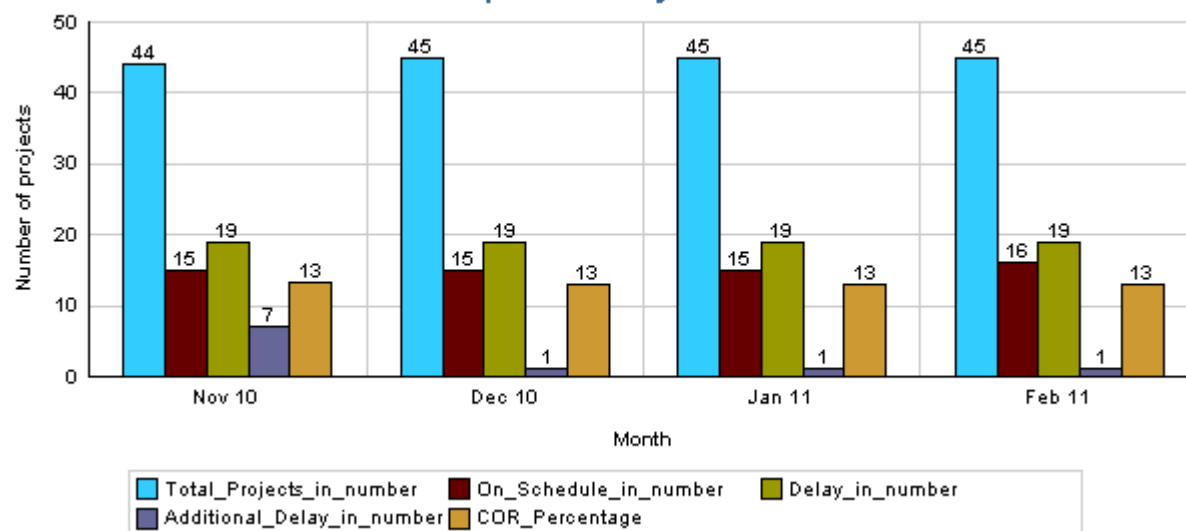


Coal Sector Break-up of 19 Delayed projects in February 2011

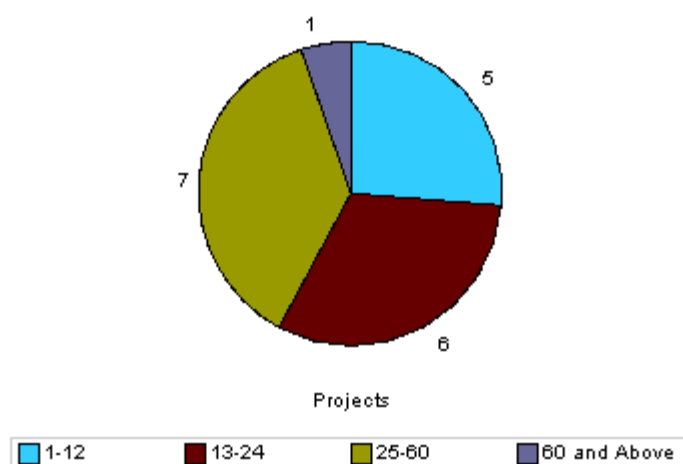


Trend and Graphical Analysis of Civil Aviation Sector

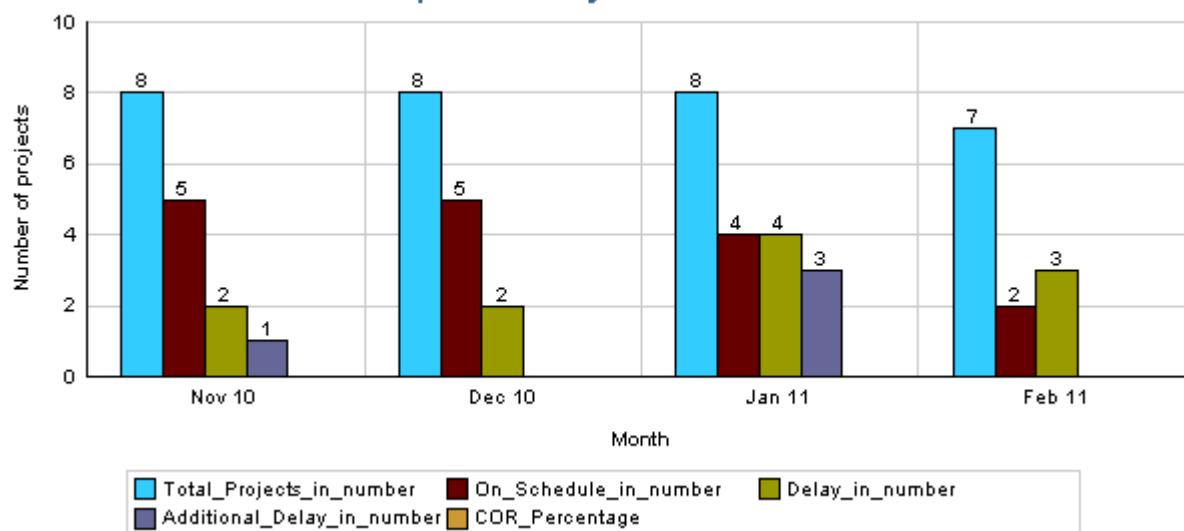


Civil Aviation Sector Break-up of 3 Delayed projects in February 2011

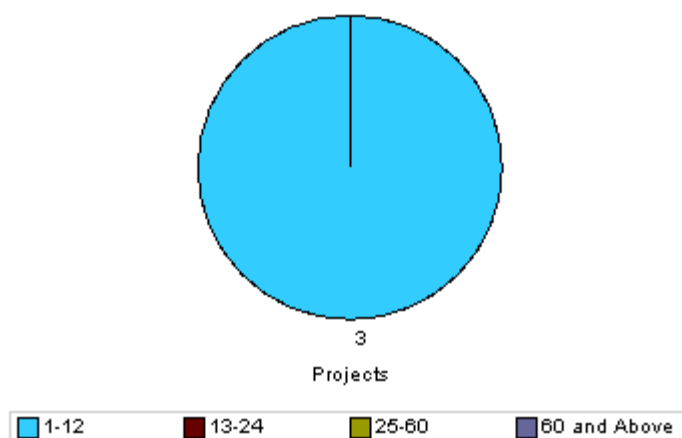

Trend and Graphical Analysis of Atomic Energy Sector

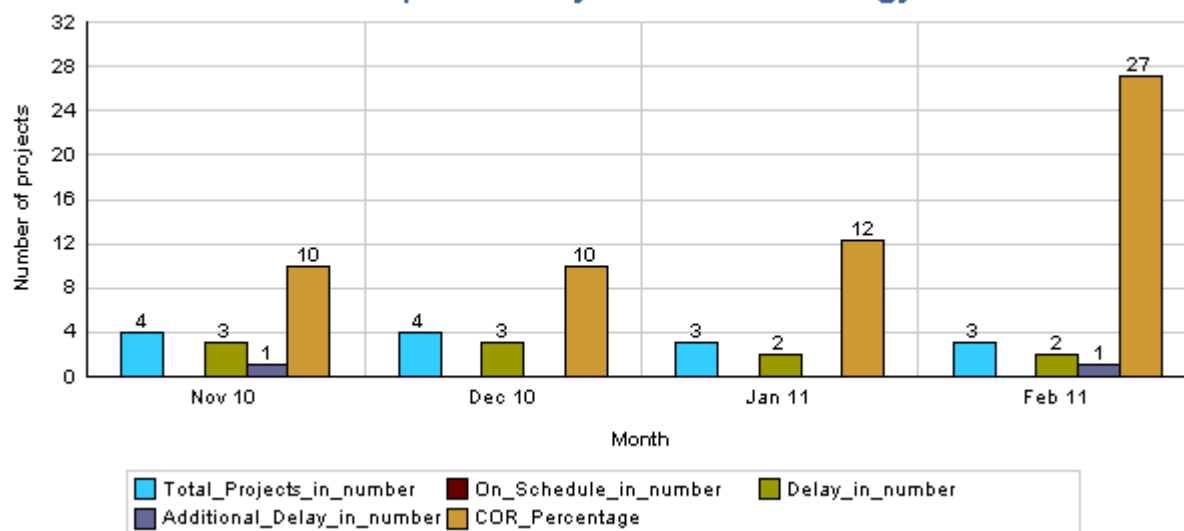

Atomic Energy Sector Break-up of 2 Delayed projects in February 2011

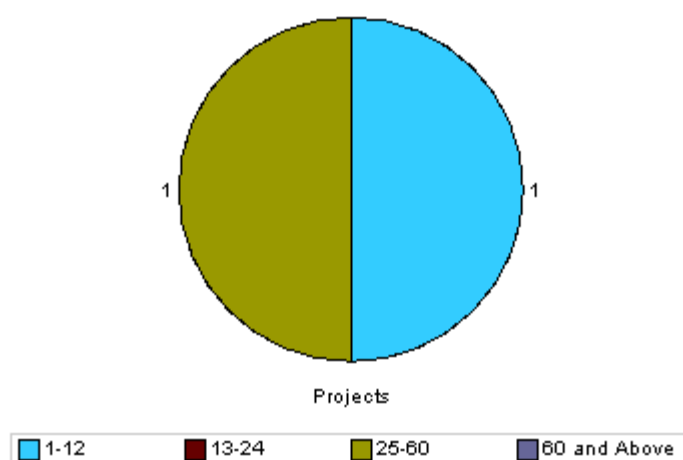

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	3	17,769.29	17,769.29	22,607.29
Civil Aviation	7	4,521.48	4,521.48	4,521.48
Coal	45	25,452.49	27,069.30	28,789.58
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	14	40,023.85	55,234.50	59,739.88
Petroleum	70	159,424.34	183,140.07	174,919.99
Power	82	173,813.00	174,223.71	179,065.68
Railways	145	68,682.72	82,031.02	122,500.87
Road Transport & Highways	122	50,323.24	50,323.24	52,221.65
Shipping & Ports	25	19,072.31	19,620.83	19,955.57
Telecommunications	41	20,025.99	19,999.09	20,424.17
Urban Development	3	15,185.18	15,173.44	30,684.66
Water Resources	1	542.90	542.90	1,187.00
Grand total	565	604,245.71	659,368.04	726,336.99

(Feb,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	891.59	- -	04/2011	-	0/1
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	2,832.35	09/2010 -	09/2011	12(O)	8/80
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,504.00	12/2008 -	03/2012	39(O)	61/119
	Total		17,769.29 -	22,607.29	17,227.94				69/200
	<u>Civil Aviation</u>								
4	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00 -	230.00	232.94	01/2011 -	03/2011	2(O)	0/0
5	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 -	1,273.00	714.65	01/2011 -	01/2011	0(O)	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29 -	264.29	85.64	01/2011 -	01/2011	0(O)	0/0
7	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35 -	213.35	211.18	09/2010 -	03/2011	6(O)	0/0
8	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	945.06	05/2011 -	08/2011	3(O)	0/0
9	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	25.64	05/2012 -	05/2012	0(O)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	262.69	06/2013 -	06/2013	0(O)	0/0
	Total		4,521.48 -	4,521.48	2,477.80				0/0
	<u>Coal</u>								
11	BARSINGAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,560.35	06/2009 -	03/2011	21(O)	59/26
12	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.48	03/2011 -	03/2011	0(O)	0/2
13	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,116.35	06/2009 -	12/2011	30(O)	41/24
14	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	75.87	03/2010 -	03/2012	24(O)	0/4
15	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	102.87	03/2011 03/2012	03/2012	0(R3)	0/2
16	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	39.34	03/2012 -	03/2012	0(O)	12/42

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya Pradesh	10/2007	259.40	259.40	1.24	03/2012	03/2012	0(O)	0/1
18	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08	172.08	108.56	03/2009	03/2012	36(O)	0/2
19	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28	207.28	55.95	03/2012	03/2012	0(O)	0/0
20	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,	12/2009	418.57	418.97	79.60	-	03/2012	-	18/27
21	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,	03/2010	181.91	181.19	0.90	-	03/2012	-	6/34
22	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	68.39	03/2012	03/2012	0(O)	0/2
23	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	78.88	03/2012	03/2012	0(O)	0/2
24	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	1,430.21	08/2012	08/2012	0(O)	0/3
25	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya Pradesh	05/2006	789.88	741.56	137.22	03/2010	03/2013	36(O)	0/2
26	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	556.04	03/2011	03/2013	24(O)	0/4
27	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	16.25	07/2012	03/2013	0(R3)	0/2
28	JALLARAM SHAFT PROJECT - [N06000025]SCCL,	03/2013	467.78	467.78	11.86	-	03/2013	-	0/83
29	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77	457.77	69.11	-	03/2013	-	0/2
30	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	29.59	03/2013	03/2013	0(O)	0/2
31	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98	210.98	22.83	03/2013	03/2013	0(O)	0/2
32	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34	779.26	149.09	03/2013	06/2013	11(R3)	2/22
33	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,028.90	03/2010	03/2014	48(O)	3/10
34	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	942.37	03/2010	03/2014	48(O)	2/8
35	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97	168.97	143.61	03/2014	03/2014	0(O)	1/1
36	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	255.83	06/2014	03/2014	-3(O)	0/0
37	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	02/2006	50.08	153.82	-	-	03/2014	-	0/1
38	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77	339.77	0.05	03/2014	03/2014	0(O)	0/2
39	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
40	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	213.92	03/2013	03/2014	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	25.13	03/2014	03/2014	0(O)	0/0
42	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	437.34	137.63	03/2012	03/2015	36(O)	0/1
43	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	11/2009	03/2015	64(O)	1/1
44	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	24.33	03/2013	03/2015	24(O)	0/3
45	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
46	KAKATIYA LAONGWALL - [N06000048]SCCL,	12/2008	453.63	453.63	57.12	-	03/2015	27(R3)	11/44
47	Batura OC - [N06000049]BCCL,Madhya pradesh	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
48	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
49	RKP OCP PHASE-I - [N06000079]SCCL,	03/2010	201.58	209.78	15.56	-	03/2015	-	4/31
50	Kistaram OCP - [N06000089]SCCL,	11/2010	242.29	242.29	-	-	03/2015	-	0/28
51	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	47.77	03/2014	03/2016	24(O)	1/2
52	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	6.04	03/2015	03/2016	12(O)	0/2
53	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	158.59	198.59	108.56	03/2016	03/2016	0(O)	0/0
54	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	291.12	03/2016	03/2016	0(O)	0/2
55	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.00	490.10	71.47	-	03/2017	-	0/1
Total			25,452.49	28,789.58	10,113.39				161/427
Fertilisers									
56	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	18.28	07/2011	07/2011	0(O)	0/0
57	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	33.62	07/2011	07/2011	0(O)	0/0
58	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	41.51	-	11/2011	0(R3)	2/22
59	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	88.70	01/2013	01/2013	0(O)	0/5
60	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	89.41	01/2013	01/2013	0(O)	0/5
61	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	73.75	12/2012	01/2013	1(O)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			5,317.41	5,317.41	345.27				2/40
<u>Mines</u>									
62	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa	10/2004	4,091.51 4,401.76	4,401.76	3,942.55	12/2008 01/2011	03/2011	2(R3)	117/110
Total			4,091.51	4,401.76	3,942.55				117/110
<u>Steel</u>									
63	AIR SEPARATION PLANT (ASU-4) - [N12000060]RINL, Andhra Pradesh	03/2008	96.00	170.00	74.39	06/2010	10/2010	4(O)	0/0
64	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL, Jharkhand	07/2008	172.78	172.78	123.06	01/2010	04/2011	15(O)	0/1
65	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Madhya Pradesh	07/2007	111.28 232.93	232.93	-	-	05/2011	-	0/1
66	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00	350.00	203.24	-	06/2011	-	0/1
67	Rebuilding of coke oven battery No.1 & 2 (Bokaro S) - [N12000033]SAIL, Jharkhand	10/2007	500.90	500.90	268.63	04/2010	08/2011	16(O)	0/2
68	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00	343.58	210.57	02/2010	08/2011	18(O)	0/0
69	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDCL) - [N12000018]NMDCL, Chhattisgarh	01/2003	295.89	607.17	259.44	-	10/2011	-	2/21
70	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	14,443.00	10,400.59	09/2010 12/2011	12/2011	0(R3)	0/6
71	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	3,316.00 6,325.00	6,325.00	1,757.92	- 12/2011	12/2011	0(R3)	0/7
72	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,499.00	7,958.00	10/2009	03/2012	29(O)	5/16
73	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Andhra Pradesh	05/2008	480.00	480.84	67.07	09/2010	05/2012	20(O)	0/0
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00	216.68	32.41	10/2009	10/2012	36(O)	0/0
75	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00	6,133.00	1,253.17	02/2011	03/2013	25(O)	0/0
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhattisgarh	09/2008	5,185.00 17,265.00	17,265.00	2,110.51	- 03/2013	03/2013	0(R3)	0/8
Total			40,023.85	59,739.88	24,719.00				7/63
<u>Petroleum</u>									

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
77	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra	03/2007	900.47	900.47	750.98	09/2009	12/2010	15(O)	0/0
78	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab	01/2009	605.40 605.40	510.00	364.55	12/2010 12/2010	12/2010	0(R3)	17/17
79	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80 3,941.41	3,941.41	-	12/2009	12/2010	12(O)	0/0
80	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	425.52	12/2010	01/2011	1(O)	0/0
81	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	224.00	160.55	12/2010 02/2011	02/2011	0(R3)	0/0
82	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat	01/2007	5,693.00 6,898.00	6,898.00	5,997.40	- 06/2010	03/2011	9(R3)	96/42
83	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	12/2008 12/2008	03/2011	27(R3)	0/0
84	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13	266.00	187.41	10/2009	03/2011	17(O)	0/0
85	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	190.93	12/2010	03/2011	3(O)	0/0
86	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 1,493.49	976.08	765.80	06/2006 07/2010	04/2011	9(R3)	0/2
87	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,529.40	09/2009	04/2011	19(O)	0/0
88	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	706.70	551.47	04/2010	04/2011	12(O)	0/0
89	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	305.08	142.98	04/2011	04/2011	0(O)	0/0
90	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	03/2005 05/2011	05/2011	0(R3)	0/0
91	MSQ IMPROVMENT PROJECT - [N16000040]IOCL,Assam	04/2008	293.60	293.60	210.80	12/2009	05/2011	17(O)	0/0
92	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	58.26	03/2009	05/2011	26(O)	0/0
93	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	01/2010	589.70 755.76	755.76	181.20	03/2011 05/2011	05/2011	0(R3)	0/0
94	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28 3,796.21	3,796.21	3,310.00	05/2011	05/2011	0(O)	0/0
95	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 4,403.00	2,500.00	1,991.94	10/2011 04/2011	06/2011	2(R3)	0/2
96	COMPRESSOR STATIONS (KAILARAS &CHAINS) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	810.00	297.80	04/2011 04/2011	09/2011	5(R3)	0/2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	3,597.00	236.66	09/2011	09/2011	0(O)	0/0
98	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	3,284.00	-	09/2011	09/2011	0(O)	0/0
99	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30	2,305.30	2,061.15	06/2010 06/2010	10/2011	16(R3)	0/0
100	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	07/2011	1,816.07 1,816.07	1,200.00	668.25	- 04/2011	10/2011	6(R3)	0/1
101	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Madhya pradesh	11/2007	1,512.00	975.00	822.32	- -	10/2011	-	0/3
102	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	540.92	1.35	06/2011	11/2011	5(O)	7/9
103	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	756.00	547.25	12/2011	12/2011	0(O)	0/0
104	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	349.00	349.00	150.80	08/2011	12/2011	4(O)	0/0
105	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	348.00 348.00	260.00	90.63	03/2012	12/2011	-3(O)	6/12
106	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL,Maharashtra	02/2008	825.00	825.00	102.62	- -	12/2011	-	0/203
107	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	180.36	12/2011	12/2011	0(O)	0/0
108	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	375.00	12.54	06/2011	12/2011	6(O)	3/9
109	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,422.87	- -	12/2011	-	0/116
110	BNPL superlines(Uttranchal & Punjab) - [N16000091]GAIL,Multi State	12/2009	540.92	375.00	1.35	05/2011	01/2012	8(O)	0/0
111	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	12,160.00	5,100.00	01/2012	01/2012	0(O)	0/0
112	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	411.64	03/2010 03/2012	03/2012	0(R1)	0/0
113	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	0.65	01/2013	03/2012	-10(O)	0/0
114	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	147.99	03/2012	03/2012	0(O)	11/10
115	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	22.45	- -	03/2012	-	5/36

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	Assam gas Cracker project - [N16000106]BCPL, Assam	04/2006	5,460.61 -	5,460.61	1,391.19	- -	04/2012	-	0/2
117	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	2,240.84	05/2010 05/2012	05/2012	0(R3)	0/0
118	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	356.98	02/2009 03/2012	05/2012	2(R3)	0/0
119	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	3.25	05/2010 04/2012	05/2012	1(R3)	0/0
120	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 05/2012	05/2012	0(R3)	0/0
121	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	442.36	03/2010 03/2012	06/2012	3(R3)	0/0
122	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	214.37	12/2011 -	06/2012	6(O)	0/0
123	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL, Orissa	12/2009	1,492.33 -	1,492.33	297.49	06/2012 -	06/2012	0(O)	0/0
124	Additional Development of D-1 Field - [N16000097]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	317.67	12/2011 06/2012	06/2012	0(R3)	0/0
125	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	19.42	04/2011 -	07/2012	15(O)	0/0
126	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	150.84	07/2012 -	07/2012	0(O)	0/0
127	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	34.30	08/2012 -	08/2012	0(O)	0/0
128	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	6,855.93 -	6,855.93	1,392.75	09/2012 -	09/2012	0(O)	0/0
129	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL, Multi State	08/2009	1,793.00 -	1,793.00	159.02	- -	09/2012	-	0/15
130	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC, Gujarat	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
131	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00 -	29,777.00	5,602.41	- -	11/2012	-	107/103
132	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	1,797.35	20.86	12/2011 -	01/2013	13(O)	0/0
133	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL, Uttar Pradesh	07/2010	1,000.00 -	1,000.00	8.57	01/2013 -	01/2013	0(O)	0/0
134	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]IOCL, Haryana	11/2009	341.50 -	341.50	1.38	02/2013 -	02/2013	0(O)	0/0
135	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	212.30	03/2006 03/2013	03/2013	0(R3)	6/6

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
136	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	06/2007	1,252.75 8,813.41	8,813.41	5,986.74	06/2009 03/2013	03/2013	0(R3)	0/0
137	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	263.44	03/2013 -	03/2013	0(O)	0/0
138	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
139	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
140	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
141	Wax Project - [N16000101]NRL,Assam	08/2010	576.60 -	576.60	6.95	02/2014 -	02/2014	0(O)	0/0
142	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	-	02/2014 -	02/2014	0(O)	0/0
143	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	559.61	03/2007 03/2014	03/2014	0(R3)	3/3
144	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,180.74	03/2007 03/2017	03/2017	0(R3)	6/6
145	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	2.44	10/2010 -	-	-	0/0
146	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	1.60	- -	-	-	0/0
	Total		159,424.34 -	174,919.99	53,723.91				267/599
Power									
147	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34 -	241.27	163.44	06/2008 -	03/2011	33(O)	9/20
148	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70 -	803.76	643.11	06/2009 -	03/2011	21(O)	1/20
149	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	894.26	638.59	10/2009 -	03/2011	17(O)	2/20
150	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44 -	2,570.44	1,862.00	08/2010 -	03/2011	7(O)	13/26
151	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	119.66	06/2010 -	03/2011	9(O)	0/0
152	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49 -	299.08	316.82	04/2010 -	03/2011	11(O)	0/0
153	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10 -	262.10	154.42	09/2010 -	03/2011	6(O)	0/0
154	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State	12/2008	328.97 -	328.97	175.54	09/2011 -	03/2011	-6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
155	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	67.41	01/2011	03/2011	2(O)	0/1
156	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	271.32	07/2011	03/2011	-4(O)	0/0
157	Transmission system associated with Uri-II HEP - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	204.64	-	05/2011	-	0/0
158	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,661.21	11/2008	06/2011	31(O)	25/38
159	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	422.03	01/2010	06/2011	17(O)	0/22
160	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,750.83	07/2010	06/2011	11(O)	3/20
161	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	98.36	06/2011	06/2011	0(O)	0/0
162	TRANSMISSION SYSTEM ASSOCIATED WITH CORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	182.75	06/2011	06/2011	0(O)	0/0
163	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	48.10	07/2011	07/2011	0(O)	0/0
164	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,501.13	08/2010	08/2011	12(O)	0/0
165	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.26	621.28	593.43	02/2011	08/2011	6(O)	0/1
166	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	124.50	08/2011	08/2011	0(O)	0/0
167	NIMOO BAZGO HYDROELECTRIC PROJECT (NHPC) - [N18000006]NHPC,J & K	08/2006	611.01	611.02	595.11	08/2010	09/2011	13(O)	0/0
168	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,430.00	09/2009 06/2011	10/2011	4(R3)	15/30
169	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,729.29	1,724.79	1,361.70	11/2009	11/2011	24(O)	0/0
170	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	212.63	11/2011	11/2011	0(O)	0/0
171	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	206.28	11/2011	11/2011	0(O)	0/0
172	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	42.13	11/2011	11/2011	0(O)	0/0
173	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	99.52	11/2011	11/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
174	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,304.52	1,312.04	10/2010	12/2011	14(O)	0/0
175	SIMHADRI STPP STAGE -II (NTPC) - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.53	3,602.00	05/2011	12/2011	7(O)	0/0
176	TESSTA LOW DAM - III HYDROELECTRIC POWER PROJECT - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,259.95	03/2007 12/2011	02/2012	2(R3)	1/25
177	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	192.28	02/2012	02/2012	0(O)	0/0
178	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	17.13	02/2012	02/2012	0(O)	0/0
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	108.13	02/2012	02/2012	0(O)	0/0
180	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	187.39	07/2010	02/2012	19(O)	0/0
181	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	642.90	02/2012	02/2012	0(O)	0/0
182	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,246.21	04/2005	03/2012	83(O)	2/1
183	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	6,852.00	12/2009	03/2012	27(O)	33/56
184	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	20.34	04/2012	04/2012	0(O)	0/0
185	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	159.97	05/2012	05/2012	0(O)	0/0
186	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	50.84	06/2012	06/2012	0(O)	0/0
187	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	66.05	06/2012	06/2012	0(O)	0/0
188	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	6.19	06/2012	06/2012	0(O)	0/0
189	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,511.86	08/2012	08/2012	0(O)	0/0
190	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,151.10	08/2012	08/2012	0(O)	0/0
191	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	176.79	08/2012	08/2012	0(O)	0/0
192	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	883.64	09/2009 08/2012	10/2012	2(R3)	0/0
193	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,938.00	02/2012 08/2012	10/2012	2(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
194	TRANSMISSION SYSTEM ASSOCIATED WITH MUNDRA ULTRA M - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,290.52	10/2012	10/2012	0(O)	0/0
195	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	46.12	10/2012	10/2012	0(O)	0/0
196	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF I - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	1.11	10/2012	10/2012	0(O)	0/0
197	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	44.12	11/2012	11/2012	0(O)	0/0
198	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	127.28	11/2012	11/2012	0(O)	0/0
199	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	14.74	12/2008 09/2010	12/2012	27(R1)	0/15
200	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,863.17	12/2012	12/2012	0(O)	0/0
201	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	1,453.00	11/2012	12/2012	1(O)	0/0
202	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,367.00	11/2012	12/2012	1(O)	0/0
203	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	123.72	12/2012	12/2012	0(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	-	01/2013	01/2013	0(O)	0/0
205	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,475.00	04/2009	03/2013	47(O)	19/41
206	Transmission System for phase-1 generation project - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	0.48	02/2013	03/2013	1(O)	0/0
207	BONGAIGAON THERMAL POWER PROJECT (NTPC) - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,749.00	07/2011 10/2012	04/2013	6(R3)	0/0
208	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	61.27	01/2012	07/2013	18(O)	0/0
209	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	167.08	08/2012 08/2013	08/2013	0(R3)	8/17
210	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,956.32	08/2013	08/2013	0(O)	0/0
211	Transmission system associated with krishnapatnam-part-A - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	-	08/2013	08/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
212	Northern Region system strengthening scheme-XXII - [N18000091]PGCIL, Multi State	12/2010	209.78	209.78	-	08/2013	08/2013	0(O)	0/0
213	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL, Chhatisgarh	12/2010	1,719.52	1,719.52	-	08/2013	08/2013	0(O)	0/0
214	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,090.27	01/2012	09/2013	20(O)	2/10
215	BARH STPP STAGE -II (NTPC) - [N18000047]NTPC, Bihar	02/2008	7,341.04	7,341.04	1,610.00	08/2013	10/2013	2(O)	0/0
216	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33	6,285.33	4,629.01	09/2010	12/2013	39(O)	2/11
217	Transmission system for phase-I generation project - [N18000093]PGCIL, Orissa	12/2010	2,743.19	2,743.19	-	12/2013	12/2013	0(O)	0/0
218	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72	913.63	219.54	07/2006	01/2014	90(O)	2/5
219	Tapovan-Vishnugad HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttarakhand	11/2006	2,978.48	2,978.48	999.00	03/2013	02/2014	11(O)	5/31
220	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59	3,919.59	3,060.19	09/2009	07/2014	58(O)	1/20
221	BARH STPP(3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97	8,693.00	5,327.00	11/2010	09/2014	46(O)	15/51
222	Transm System for development of Pooling stn. in N - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
223	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttarakhand	07/2006	1,657.00	2,978.86	251.65	07/2010	03/2015	56(O)	0/0
224	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67	3,642.04	560.56	07/2014	01/2016	18(O)	0/0
225	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttarakhand	08/2008	2,491.58	2,491.58	145.21	07/2014	03/2016	20(O)	0/8
226	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90	2,496.90	1,365.57	05/2013 06/2016	06/2016	0(R3)	78/22
227	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	947.96	797.17	12/2007	-	-	14/18
228	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra	12/2007	477.69	477.69	332.32	09/2010 06/2011	06/2011	0(R3)	0/0
Total			173,813.00	179,065.68	76,458.89				250/529
<u>Railways</u>									
229	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23	638.00	-	02/2015	02/2015	0(O)	0/0
230	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	218.52	- 02/2009	12/2010	22(R1)	0/0
231	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41 207.00	211.90	172.50	- 03/2009	12/2010	21(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
232	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	-	12/2007 03/2010	12/2010	9(R1)	0/0
233	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	284.59	03/2009 12/2008	12/2010	24(R1)	0/0
234	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	-	- -	12/2010	-	0/0
235	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]ER,Jharkhandd	02/1999	180.73 -	358.00	339.64	12/2006 12/2008	02/2011	26(R1)	0/0
236	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 -	228.09	207.45	- -	02/2011	-	0/0
237	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.16	438.26	02/2010 -	02/2011	12(O)	0/0
238	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 -	810.78	71.39	- -	02/2011	-	0/0
239	SHIMOGA-TALAGUPPA (SWR), GC - [N22000056]SWR,Karnataka	12/1992	46.00 -	218.00	239.95	- -	02/2011	-	0/0
240	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	399.63	06/1999 -	03/2011	141(O)	0/0
241	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 119.29	170.00	170.38	03/2002 -	03/2011	108(O)	0/0
242	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	281.20	320.53	- -	03/2011	-	0/0
243	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	193.78 -	456.45	255.16	06/2004 -	03/2011	81(O)	0/0
244	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	493.70	05/2008 -	03/2011	34(O)	0/0
245	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 -	214.09	185.80	12/2009 -	03/2011	15(O)	0/0
246	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	522.56	328.71	- -	03/2011	-	0/1
247	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh	05/2002	304.50 -	306.00	341.81	- -	03/2011	-	0/0
248	TOLLYGANJ-GARIA with extension to Dum Dum-Naopara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,040.89	2,668.40	12/2006 08/2010	03/2011	7(R3)	0/0
249	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 -	700.00	137.08	- -	03/2011	-	0/0
250	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/1997	143.92 -	258.60	221.05	- -	03/2011	-	0/0
251	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	104.10 -	218.19	79.22	- -	03/2011	-	0/0
252	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	200.73 -	230.03	132.93	- -	03/2011	-	0/0
253	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
254	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
255	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	272.11	278.34	- -	03/2011	-	0/0
256	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	118.92	12/2010 -	03/2011	3(O)	0/0
257	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
258	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0
259	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	137.02	03/2011 -	03/2011	0(O)	0/0
260	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	743.87	03/2011 -	03/2011	0(O)	0/0
261	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	153.43	03/2011 -	03/2011	0(O)	0/0
262	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,087.96	- 12/2010	06/2011	6(R3)	0/1
263	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	128.36	02/2010 -	11/2011	21(O)	0/0
264	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	188.82	- 09/2009	12/2011	27(R1)	0/0
265	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	42.24	12/2011 -	12/2011	0(O)	0/0
266	Ghutarisharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	36.66	12/2011 -	12/2011	0(O)	0/0
267	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1998	186.92 -	283.10	1.86	02/2006 -	01/2012	71(O)	0/0
268	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,548.95	1,222.25	- -	02/2012	-	0/0
269	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 -	262.82	160.62	- 03/2012	03/2012	0(R3)	0/0
270	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	03/1997	100.00 322.29	329.29	387.08	- -	03/2012	-	0/0
271	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	727.52	509.74	- -	03/2012	-	0/0
272	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	201.73	- -	03/2012	-	0/0
273	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	326.87	- 03/2011	03/2012	12(R3)	0/0
274	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	415.59 -	495.74	104.00	- -	03/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	163.82	03/2010	03/2012	24(O)	0/0
276	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	160.48	125.76	-	03/2012	-	0/0
277	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73	167.73	34.15	03/2012	03/2012	0(O)	0/0
278	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	603.04	27.65	03/2012	03/2012	0(O)	0/0
279	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]ER,Gujarat	04/2008	318.24	318.24	-	03/2012	03/2012	0(O)	0/0
280	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68	730.00	301.05	-	07/2012	-	0/0
281	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77	540.96	514.70	03/1994	12/2012	225(O)	0/0
282	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67	1,653.00	536.02	-	12/2012	-	0/0
283	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1997	248.44	1,103.47	729.17	-	12/2012	-	0/0
284	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	325.17	368.83	03/2005 12/2008	12/2012	48(R1)	0/0
285	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81	234.45	180.49	-	12/2012	9(R3)	0/0
286	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	981.00	440.88	03/2009	12/2012	45(O)	0/0
287	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.00	811.67	10/2007	12/2012	62(O)	0/0
288	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	266.36	03/2010	12/2012	33(O)	0/0
289	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52	207.52	97.16	12/2012	12/2012	0(O)	0/0
290	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90	227.90	79.56	12/2012	12/2012	0(O)	0/0
291	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	132.64	-	03/2013	0(R3)	0/0
292	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84	410.08	131.95	-	03/2013	-	0/0
293	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	383.15	863.23	347.35	-	03/2013	-	0/0
294	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00	1,029.00	645.76	-	03/2013	-	0/0
295	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70	1,556.23	476.12	-	03/2013	-	0/0
296	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13	394.13	0.03	03/2013	03/2013	0(O)	0/0
297	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	585.93	146.61	-	12/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
298	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.00	161.12	03/2013 -	12/2013	9(O)	0/0
299	Lumding-silchar jiribam, badarpur-baraigram kumarghat - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	3,909.49	2,518.67	03/2009 -	12/2013	57(O)	0/0
300	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	04/1996	1,000.00 1,500.00	3,230.02	2,068.45	04/2008 12/2011	03/2014	27(R1)	0/0
301	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	02/2000	733.00 -	1,655.80	661.88	12/2008 -	03/2014	63(O)	0/0
302	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	138.93	03/2014 -	03/2014	0(O)	0/0
303	BHAIRABI SAIRONG, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	1.61	04/2014 -	03/2014	-1(O)	0/0
304	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.16	03/2014 -	03/2014	0(O)	0/0
305	Jaipur - Ringus - Churu and Sikar - Lohatu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	3.01	03/2014 -	03/2014	0(O)	0/0
306	Suratpura - Hanumangarh - Sriganganagar Guage Canv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	3.29	03/2014 -	03/2014	0(O)	0/0
307	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	105.60	03/2014 -	03/2014	0(O)	0/0
308	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	96.46	03/2010 -	06/2014	51(O)	0/0
309	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	141.20	- -	03/2015	-	0/0
310	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	171.00	03/2014 -	03/2015	12(O)	0/0
311	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.91	12/2015 -	03/2015	-9(O)	0/0
312	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	0.09	03/2015 -	03/2015	0(O)	0/0
313	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	5.96	03/2015 -	03/2015	0(O)	0/0
314	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	328.32	03/2011 -	03/2016	60(O)	0/0
315	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	12.04	03/2016 -	03/2016	0(O)	0/0
316	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	1.36	03/2016 -	03/2016	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	2,619.02	1.11	03/2016 -	03/2016	0(O)	0/0
318	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00 8,000.00	11,270.00	6,844.11	03/2001 -	12/2017	201(O)	0/0
319	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 422.79	634.13	526.02	03/1995 -	-	-	0/0
320	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 -	617.63	455.49	- -	-	-	0/0
321	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR, Gujarat	04/1992	112.53 320.66	464.50	502.85	03/1996 06/2009	-	-	0/0
322	AMBALA-MORADABAD(RE) - [220100131]RE, Multi State	03/1993	152.21 157.76	265.00	265.33	03/1998 -	-	-	0/0
323	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	01/1986	36.80 274.41	285.93	232.84	- -	-	-	0/0
324	DALLIRAJHARA-JAGDALPUR, NL, SECR - [220100149]SECR, Chhatisgarh	04/1995	369.00 968.60	1,317.24	50.08	- -	-	-	0/0
325	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	587.00	- -	-	-	0/0
326	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	1,010.00	92.12	- -	-	-	0/0
327	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 -	412.91	444.91	- -	-	-	0/0
328	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	356.00 -	1,038.00	501.08	03/1998 -	-	-	0/0
329	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 -	712.00	488.70	- -	-	-	0/0
330	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1997	155.74 164.36	429.49	389.85	02/2009 -	-	-	0/0
331	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	997.58	58.20	- -	-	-	0/0
332	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1996	377.32 236.41	497.47	76.24	- -	-	-	0/0
333	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 154.30	154.30	128.54	03/2007 03/2007	-	-	0/0
334	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
335	KODERMA-RANCHI VIA BARKAKHANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 -	1,099.20	907.40	07/2005 -	-	-	0/0
336	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR, Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0
337	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR, Tamil Nadu	02/2000	175.00 -	513.16	535.95	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
338	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	68.13	- -	-	-	0/0
339	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
340	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	169.57	- 05/2009	-	-	0/0
341	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23 -	162.87	82.12	- -	-	-	0/0
342	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 408.76	639.54	799.22	06/2007 -	-	-	0/0
343	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	-	04/2003 03/2010	-	-	0/0
344	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	448.67	- -	-	-	0/0
345	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
346	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 240.59	607.09	269.75	- 12/2012	-	-	0/0
347	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
348	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 -	418.17	66.81	- -	-	-	0/0
349	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	177.07	- -	-	-	0/0
350	KICHHA-KHATIMA (NL) - NER - [220100317]NER,Uttaranchal	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
351	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR,Andhra Pradesh	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
352	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0
353	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]RVNL,Kerala	07/2006	246.50 -	246.50	-	03/2009 -	-	-	0/0
354	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	267.82	03/2008 06/2008	-	-	0/0
355	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 -	224.51	41.39	- -	-	-	0/0
356	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 -	881.19	86.35	- -	-	-	0/0
357	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	120.35	- -	-	-	0/0
358	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	350.57	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
359	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	19.77	- -	-	-	0/0
360	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	66.55	- -	-	-	0/0
361	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	29.96	- -	-	-	0/0
362	KISHANGANJ JALALGARH, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	333.76	0.71	- -	-	-	0/0
363	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 -	495.44	159.86	03/2004 -	-	-	0/0
364	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 -	675.00	395.96	- 12/2011	12/2011	0(R3)	0/0
365	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	545.16	- 11/2010	-	-	0/0
366	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 -	563.25	544.15	03/2004 03/2010	-	-	0/0
367	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	724.31	701.80	- 12/2010	12/2010	0(R3)	0/0
368	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 -	762.33	413.15	- 12/2009	-	-	0/0
369	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	313.04	- -	-	-	0/0
370	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	255.30	03/2008 10/2010	10/2010	0(R3)	0/0
371	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	0.93	- -	-	-	0/0
372	TAMLUK DIGHA - [N22000097]LD,West Bengal	03/1984	293.97 -	293.97	361.97	06/2005 -	04/2012	82(O)	0/0
373	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	118.93	12/2010 12/2010	12/2010	0(R3)	0/0
	Total		68,682.72 -	122,500.87	50,816.36				0/2
<u>Road Transport & Highways</u>									
374	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	157.30	09/2007 -	03/2011	42(O)	0/0
375	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	120.81	08/2004 -	03/2011	79(O)	0/0
376	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	131.71	08/2004 -	03/2011	79(O)	0/0
377	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	247.70	07/2004 -	03/2011	80(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	669.80	04/2007 -	03/2011	47(O)	0/0
379	GARMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	286.80	09/2007 -	03/2011	42(O)	0/0
380	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI,Uttar Pradesh	12/2003	158.06 -	158.06	163.50	08/2005 -	03/2011	67(O)	0/0
381	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00 -	239.00	304.60	07/2005 -	03/2011	68(O)	0/0
382	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI,Bihar	12/2003	275.00 -	275.00	334.70	07/2005 -	03/2011	68(O)	0/0
383	MADURAI -KANIYAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36 -	323.36	192.70	03/2008 -	03/2011	36(O)	0/0
384	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	228.60	10/2008 -	03/2011	29(O)	0/0
385	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00 -	205.00	351.30	10/2008 -	03/2011	29(O)	0/0
386	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00 -	212.00	388.50	10/2008 -	03/2011	29(O)	0/0
387	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	328.00	03/2008 -	03/2011	36(O)	0/0
388	MEERUT-MUZZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	772.80	03/2009 -	03/2011	24(O)	0/0
389	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00 -	579.00	737.70	04/2009 -	03/2011	23(O)	0/0
390	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	03/2011	4(O)	0/0
391	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI,Assam	12/2003	225.00 -	225.00	220.50	06/2008 -	03/2011	33(O)	0/0
392	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	268.20	10/2008 -	03/2011	29(O)	0/0
393	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	198.00	167.50	11/2008 -	03/2011	28(O)	0/0
394	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	232.80	10/2008 -	03/2011	29(O)	0/0
395	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	527.00	06/2008 -	03/2011	33(O)	0/0
396	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	235.10	06/2008 -	03/2011	33(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	03/2011	21(O)	0/0
398	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI, Kerala	12/2003	312.50	312.50	575.20	03/2009	03/2011	24(O)	0/0
399	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	219.30	06/2008	03/2011	33(O)	0/0
400	THANJAVUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	578.90	06/2009	03/2011	21(O)	0/0
401	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI, Uttar Pradesh	12/2003	465.00	465.00	607.80	04/2009	03/2011	23(O)	0/0
402	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI, Punjab	03/2005	309.00	309.00	549.60	06/2010	03/2011	9(O)	0/0
403	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	286.50	10/2009	03/2011	17(O)	0/0
404	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.30	09/2009	03/2011	18(O)	0/0
405	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	276.09	294.80	09/2009	03/2011	18(O)	0/0
406	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	759.20	07/2010	03/2011	8(O)	0/0
407	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI, Karnataka	03/2005	565.00	565.00	1,007.00	07/2010	03/2011	8(O)	0/0
408	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	121.06	02/2004	03/2011	85(O)	0/0
409	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI, Assam	12/2003	230.00	230.00	308.70	06/2008	04/2011	34(O)	0/0
410	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	234.24	02/2004	04/2011	86(O)	0/0
411	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	613.30	07/2010	04/2011	9(O)	0/0
412	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	355.80	07/2010	04/2011	9(O)	0/0
413	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	415.40	01/2011	04/2011	3(O)	0/0
414	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00	242.00	348.10	12/2008	05/2011	29(O)	0/0
415	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	622.70	08/2010	05/2011	9(O)	0/0
416	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI, Madhya Pradesh	11/2008	549.00	549.00	697.00	05/2010	05/2011	12(O)	0/0
417	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	475.40	05/2010	05/2011	12(O)	0/0
418	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	367.70	03/2005	06/2011	75(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
419	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	192.30	09/2007 -	06/2011	45(O)	0/0
420	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	435.00	11/2007 -	06/2011	43(O)	0/0
421	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	307.30	10/2008 -	06/2011	32(O)	0/0
422	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	343.70	10/2008 -	06/2011	32(O)	0/0
423	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	162.40	03/2008 -	06/2011	39(O)	0/0
424	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	193.10	132.00	03/2008 -	06/2011	39(O)	0/0
425	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	327.20	10/2008 -	06/2011	32(O)	0/0
426	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	06/2011	29(O)	0/0
427	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	332.80	12/2008 -	06/2011	30(O)	0/0
428	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	242.90	09/2008 -	06/2011	33(O)	0/0
429	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	205.60	10/2008 -	06/2011	32(O)	0/0
430	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	153.20	10/2008 -	06/2011	32(O)	0/0
431	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	620.40	10/2009 -	06/2011	20(O)	0/0
432	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	396.40	12/2009 -	06/2011	18(O)	0/0
433	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	548.70	07/2010 -	06/2011	11(O)	0/0
434	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,803.00	01/2011 -	06/2011	5(O)	0/0
435	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	385.30	12/2008 -	08/2011	32(O)	0/0
436	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	1,900.00	08/2011 -	08/2011	0(O)	0/0
437	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	203.80	11/2008 -	09/2011	34(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	50.95	04/2004	10/2011	90(O)	0/0
439	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	232.30	06/2008	10/2011	40(O)	0/0
440	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	170.00	10/2011	10/2011	0(O)	0/0
441	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	300.50	10/2011	10/2011	0(O)	0/0
442	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar	12/2003	305.00	305.00	497.20	06/2008	11/2011	41(O)	0/0
443	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	155.90	10/2008	11/2011	37(O)	0/0
444	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	1,990.00	11/2011	11/2011	0(O)	0/0
445	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
446	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	73.58	09/2008	12/2011	39(O)	0/0
447	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	181.60	06/2005	12/2011	78(O)	0/0
448	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	200.40	02/2009	12/2011	34(O)	0/0
449	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	70.70	04/2009	12/2011	32(O)	0/0
450	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	146.80	06/2008	12/2011	42(O)	0/0
451	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	178.40	06/2008	12/2011	42(O)	0/0
452	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	176.70	10/2008	12/2011	38(O)	0/0
453	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	393.90	09/2008	12/2011	39(O)	0/0
454	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	213.90	06/2008	12/2011	42(O)	0/0
455	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	280.00	03/2008	12/2011	45(O)	0/0
456	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	160.90	06/2008	12/2011	42(O)	0/0
457	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	173.60	04/2008	12/2011	44(O)	0/0
458	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	98.01	05/2008	12/2011	43(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
459	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	165.50	06/2008	12/2011	42(O)	0/0
460	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	274.20	03/2010	12/2011	21(O)	0/0
461	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	247.30	02/2012	02/2012	0(O)	0/0
462	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	101.70	04/2008	03/2012	47(O)	0/0
463	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	157.20	04/2008	03/2012	47(O)	0/0
464	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	113.50	04/2010	03/2012	23(O)	0/0
465	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.20	02/2010	03/2012	25(O)	0/0
466	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	926.10	02/2010	05/2012	27(O)	0/0
467	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	490.70	05/2012	05/2012	0(O)	0/0
468	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	492.00	05/2012	05/2012	0(O)	0/0
469	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	183.30	05/2012	05/2012	0(O)	0/0
470	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	143.80	10/2008	06/2012	44(O)	0/0
471	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	157.00	09/2010	06/2012	21(O)	0/0
472	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	289.50	06/2012	06/2012	0(O)	0/0
473	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,475.00	10/2011	06/2012	8(O)	0/0
474	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	254.70	07/2012	07/2012	0(O)	0/0
475	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	80.12	05/2008	08/2012	51(O)	0/0
476	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	359.00	80.12	05/2010	08/2012	27(O)	0/0
477	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	183.30	06/2010	10/2012	28(O)	0/0
478	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	232.50	09/2009	10/2012	37(O)	0/0
479	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
480	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	469.00	09/2012	10/2012	1(O)	0/0
481	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	512.10	10/2012	10/2012	0(O)	0/0
482	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	173.00	07/2008	12/2012	53(O)	0/0
483	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	302.50	12/2012	12/2012	0(O)	0/0
484	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	132.60	01/2013	01/2013	0(O)	0/0
485	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	15.07	09/2010	03/2013	30(O)	0/0
486	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
487	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
488	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	109.40	09/2007	06/2013	69(O)	0/0
489	New 4 Lane elevated road from Chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
490	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	0.23	11/2013	11/2013	0(O)	0/0
491	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.60	04/2009	12/2013	56(O)	0/0
492	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
493	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	29.12	11/2008	12/2013	61(O)	0/0
494	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	38.55	09/2007	12/2013	75(O)	0/0
495	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	27.54	07/2009	12/2013	53(O)	0/0
	Total		50,323.24	52,221.65	41,629.79				0/0
Shipping & Ports									
496	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40	2,427.40	820.38	10/2008	11/2010	25(O)	0/0
497	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00	165.00	112.04	12/2005 01/2008	03/2011	38(R3)	0/0
498	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 253.36	253.36	223.37	06/2007 07/2009	03/2011	20(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
499	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	335.00	08/2010 -	03/2011	7(O)	0/0
500	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	356.12	08/2010 -	04/2011	8(O)	0/0
501	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	354.81	04/2011 -	06/2011	2(O)	0/0
502	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	230.00	219.00	12/2010 -	06/2011	6(O)	0/0
503	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	290.85 -	290.85	72.59	03/2011 -	06/2011	3(O)	0/0
504	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	290.00	06/2006 09/2011	09/2011	0(R2)	0/0
505	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12 -	1,168.42	1,078.17	04/2011 -	12/2011	8(O)	0/0
506	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 -	277.03	55.40	09/2011 -	12/2011	3(O)	0/0
507	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 -	1,061.96	240.52	03/2012 -	03/2012	0(O)	0/0
508	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	09/2005 -	03/2012	78(O)	0/0
509	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,512.00	1,778.00	01/2012 01/2012	03/2012	2(R3)	0/0
510	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	08/2012	-1(O)	0/0
511	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	448.69	12/2010 -	09/2012	21(O)	0/0
512	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
513	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 -	612.72	61.31	12/2012 -	12/2012	0(O)	0/0
514	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.38	02/2011 -	03/2013	25(O)	0/0
515	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	1.02	03/2011 -	03/2013	24(O)	0/0
516	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 -	272.50	-	01/2009 -	05/2013	52(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	1,028.10	202.04	12/2013	12/2013	0(O)	0/0
518	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	966.46	189.92	02/2014	02/2014	0(O)	0/0
519	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2015	36(O)	0/0
520	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.57	10/2008	-	-	0/0
	Total		19,072.31	19,955.57	7,134.28				0/0
Telecommunications									
521	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	225.78	09/2009	02/2010	5(O)	0/0
522	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	10/2010	58(O)	0/0
523	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
524	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
525	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
526	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	234.24	02/2008	12/2010	34(O)	0/0
527	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
528	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
529	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
530	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
531	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
532	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.42	06/2009	01/2011	19(O)	0/0
533	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	01/2011	22(O)	0/0
534	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.88	03/2009	02/2011	23(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
535	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	176.33	12/2008	02/2011	26(O)	0/0
536	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	308.13	03/2009	02/2011	23(O)	0/0
537	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	88.17	06/2009	02/2011	20(O)	0/0
538	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	02/2011	25(O)	0/0
539	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	02/2011	12(O)	0/0
540	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	223.06	10/2008	02/2011	28(O)	0/0
541	GSM equipment of 1900000Lines (2G) 401700 lines 3(-) - [N26000091]BSNL,Tamil Nadu	01/2009	760.20	810.37	759.33	01/2010 03/2011	02/2011	-1(R3)	0/0
542	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.88	01/2010	02/2011	13(O)	0/0
543	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	513.15	01/2010	02/2011	13(O)	0/0
544	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	112.11	01/2010	02/2011	13(O)	0/0
545	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	03/2011	49(O)	0/0
546	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	480.57	12/2008	03/2011	27(O)	0/0
547	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	169.43	03/2009	03/2011	24(O)	0/0
548	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	93.24	09/2009	03/2011	18(O)	0/0
549	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	31.26	10/2009	03/2011	17(O)	0/0
550	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	74.65	09/2010	03/2011	6(O)	0/0
551	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	395.77	02/2009	03/2011	25(O)	0/0
552	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	331.72	08/2009	03/2011	19(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	211.83	11/2010	03/2011	4(O)	0/0
554	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	395.06	10/2009	03/2011	17(O)	0/0
555	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	138.65	10/2010	04/2011	6(O)	0/0
556	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007	08/2011	54(O)	0/0
557	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	-	09/2011	09/2011	0(O)	0/0
558	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
559	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
560	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
561	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
Total			20,025.99	20,424.17	7,246.49				0/0
<u>Urban Development</u>									
562	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	93.80	04/2009	01/2011	21(O)	0/0
563	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	17,123.66	06/2010	06/2011	12(O)	0/10
564	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	-	12/2011	03/2013	15(O)	6/6
Total			15,185.18	30,684.66	17,217.46				6/16
<u>Water Resources</u>									
565	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
Total			542.90	1,187.00	35.49				0/0
Grand Total			604,245.71	726,336.99	313,088.62				879/1986

Sector wise current status of projects on the Flash Report

Urban Development

I. Current Status:


Number of Projects **3**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **1**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed .1 project do not have fixed dates of commissioning.

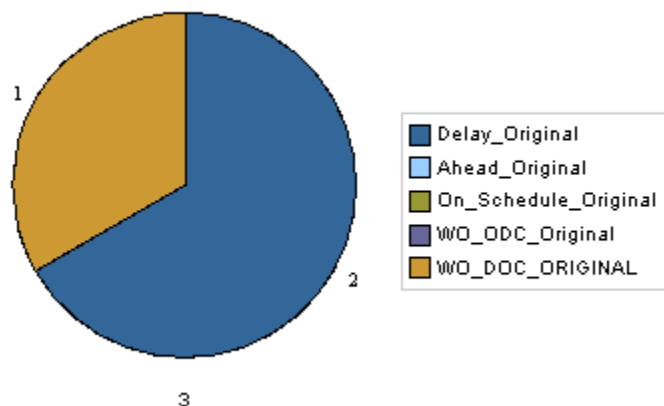

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15185.18 crore but this was subsequently revised to Rs. 30684.66 crore implying a cost overrun of 102.1%. The expenditure incurred on these projects till February, 2011 is Rs. 17217.46 crore, which is 56.1% of the revised cost of the projects.

Figures are in Rs. Crore

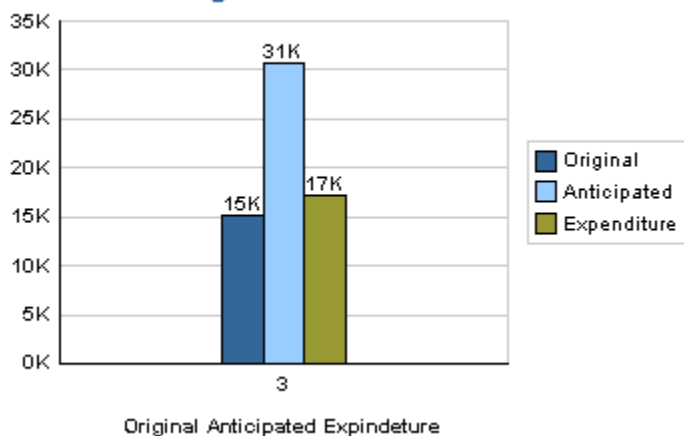

Sector wise current status of projects on the Flash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	23

Number of Projects Without Date Of Commissioning 17

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 23 projects are delayed .17 projects do not have fixed dates of commissioning.

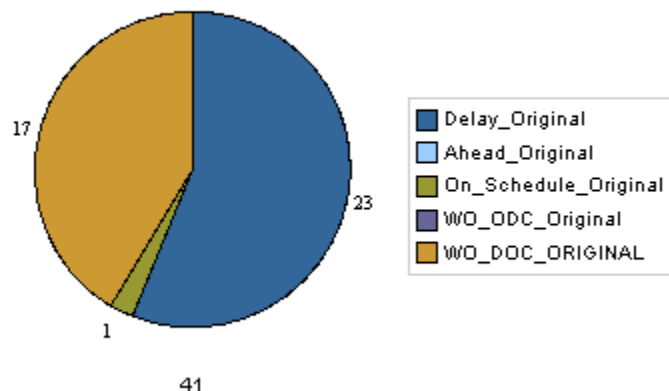

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 20424.17 crore implying a cost overrun of 2%. The expenditure incurred on these projects till February, 2011 is Rs. 7246.49 crore, which is 35.5% of the revised cost of the projects.

Figures are in Rs. Crore

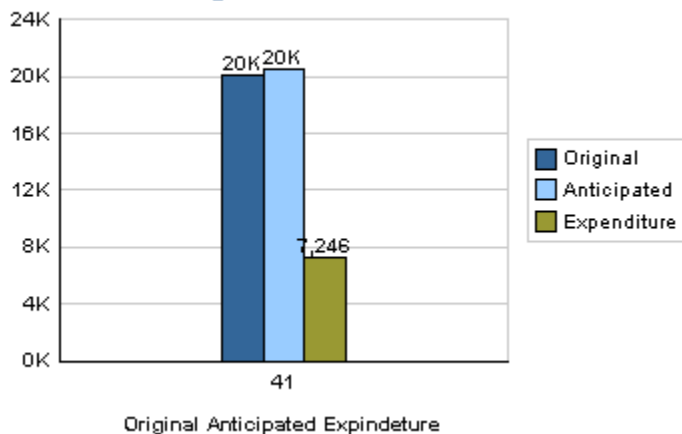

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	25
Number of Projects On Schedule	4
Number of Projects Delayed	18
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 1 project are ahead of schedule, 4 projects are on schedule and 18 projects are delayed .2 projects do not have fixed dates of commissioning.

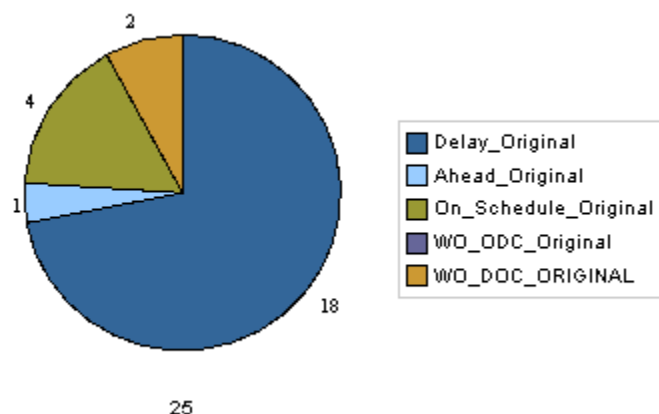

III. Investment Scenario

The Total Original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 19072.31 crore but this was subsequently revised to Rs. 19955.57 crore implying a cost overrun of 4.6%. The expenditure incurred on these projects till February, 2011 is Rs. 7134.28 crore, which is 35.8% of the revised cost of the projects.

Figures are in Rs. Crore

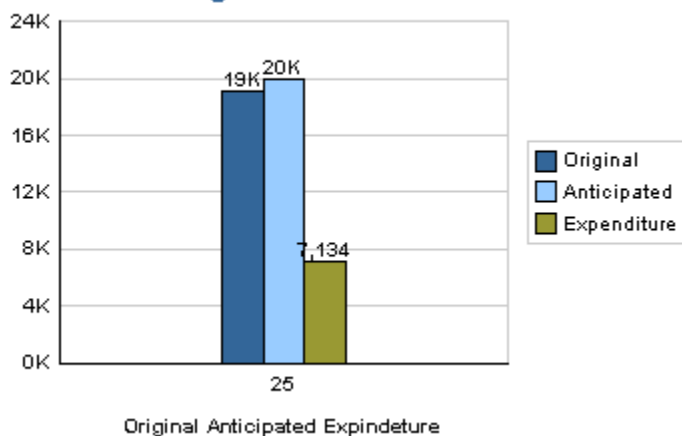

Sector wise current status of projects on the Flash Report


Road Transport & Highways

I. Current Status:

Number of Projects	122
Number of Projects On Schedule	17
Number of Projects Delayed	105

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 122 projects, 17 projects are on schedule and 105 projects are delayed .

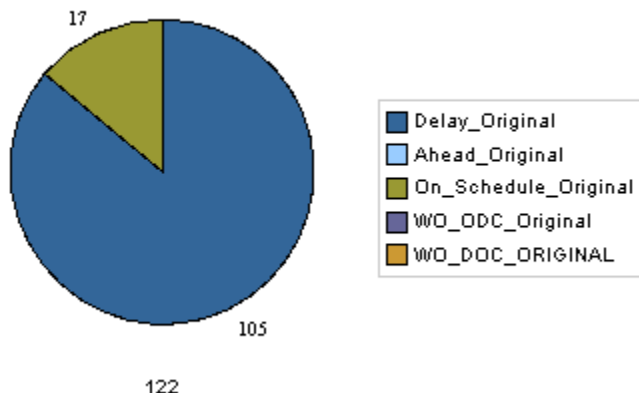

III. Investment Scenario

The Total Original cost of implementation of 122 projects when sanctioned, was of the order of Rs. 50323.24 crore but this was subsequently revised to Rs. 52221.65 crore implying a cost overrun of 3.8%. The expenditure incurred on these projects till February, 2011 is Rs. 41629.79 crore, which is 79.7% of the revised cost of the projects.

Figures are in Rs. Crore

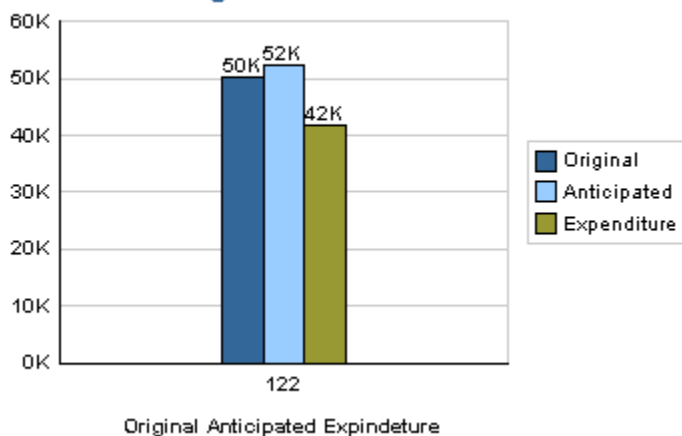

Sector wise current status of projects on the Flash Report


Railways

I. Current Status:

Number of Projects	145
Number of Projects On Schedule	24
Number of Projects Delayed	27
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	35
Number of Projects Without Date Of Commissioning	57

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 145 projects, 2 projects are ahead of schedule, 24 projects are on schedule and 27 projects are delayed .57 projects do not have fixed dates of commissioning.35 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

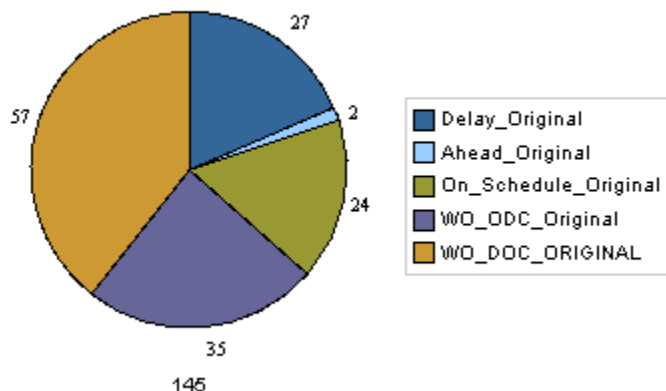

III. Investment Scenario

The Total Original cost of implementation of 145 projects when sanctioned, was of the order of Rs. 68682.72 crore but this was subsequently revised to Rs. 122500.87 crore implying a cost overrun of 78.4%. The expenditure incurred on these projects till February, 2011 is Rs. 50816.36 crore, which is 41.5% of the revised cost of the projects.

Figures are in Rs. Crore

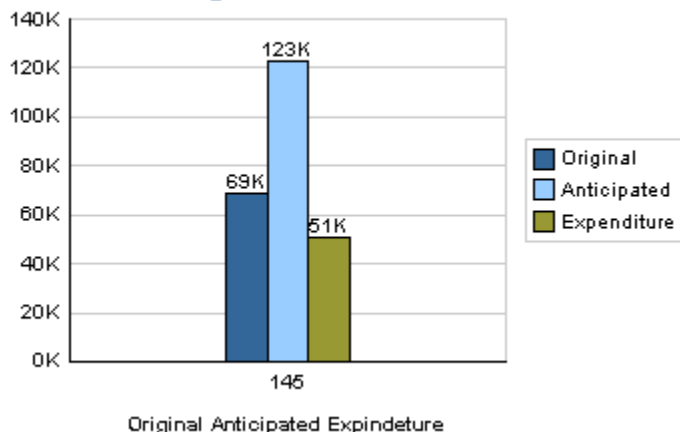

Sector wise current status of projects on the Flash Report


Power

I. Current Status:

Number of Projects	82
Number of Projects On Schedule	34
Number of Projects Delayed	44
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 82 projects, 2 projects are ahead of schedule, 34 projects are on schedule and 44 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

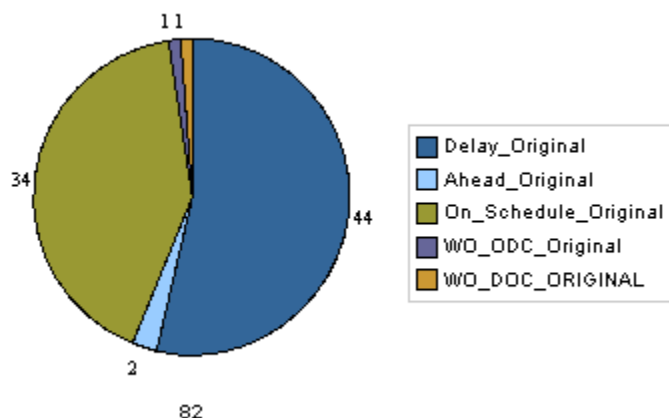

III. Investment Scenario

The Total Original cost of implementation of 82 projects when sanctioned, was of the order of Rs. 173813 crore but this was subsequently revised to Rs. 179065.68 crore implying a cost overrun of 3%. The expenditure incurred on these projects till February, 2011 is Rs. 76458.89 crore, which is 42.7% of the revised cost of the projects.

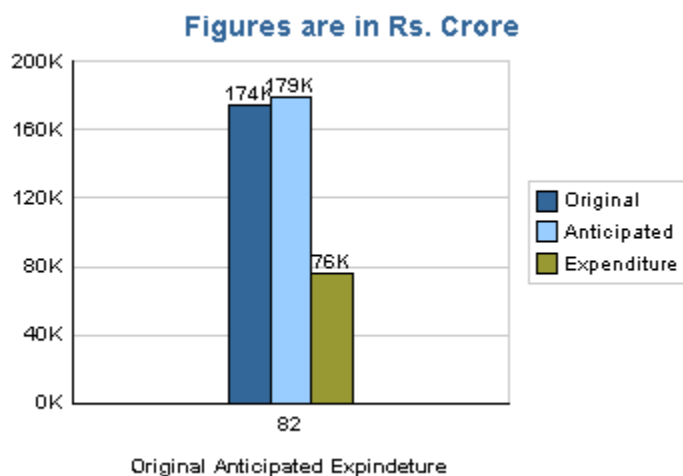

Sector wise current status of projects on the Flash Report


Petroleum

I. Current Status:

Number of Projects	70
Number of Projects On Schedule	21
Number of Projects Delayed	31
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	9
Number of Projects Without Date Of Commissioning	6

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 70 projects, 3 projects are ahead of schedule, 21 projects are on schedule and 31 projects are delayed .6 projects do not have fixed dates of commissioning.9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

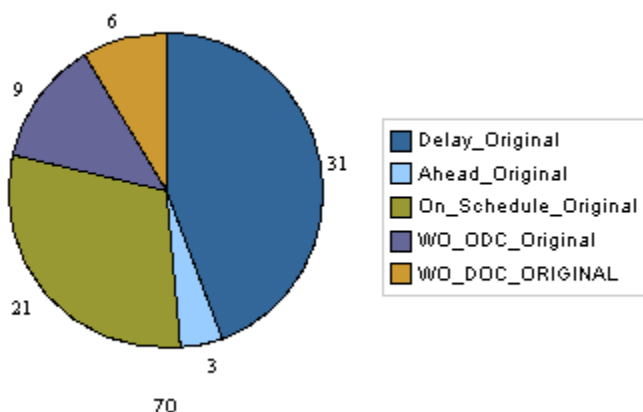

III. Investment Scenario

The Total Original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 159424.34 crore but this was subsequently revised to Rs. 174919.99 crore implying a cost overrun of 9.7%. The expenditure incurred on these projects till February, 2011 is Rs. 53723.91 crore, which is 30.7% of the revised cost of the projects.

Figures are in Rs. Crore

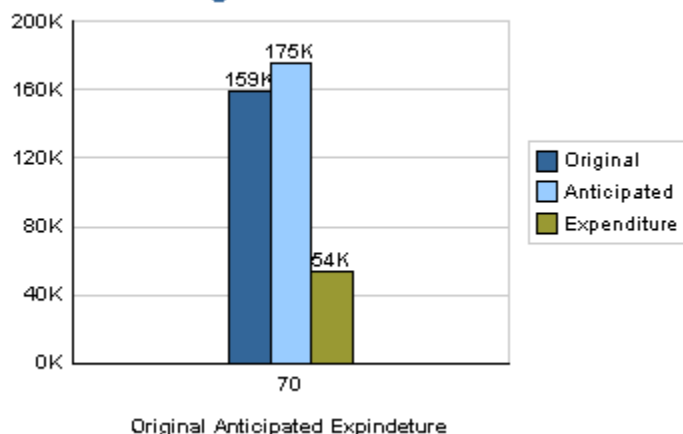

Sector wise current status of projects on the Flash Report


Steel

I. Current Status:

Number of Projects	14
Number of Projects Delayed	8
Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 14 projects, 8 projects are delayed .1 project do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

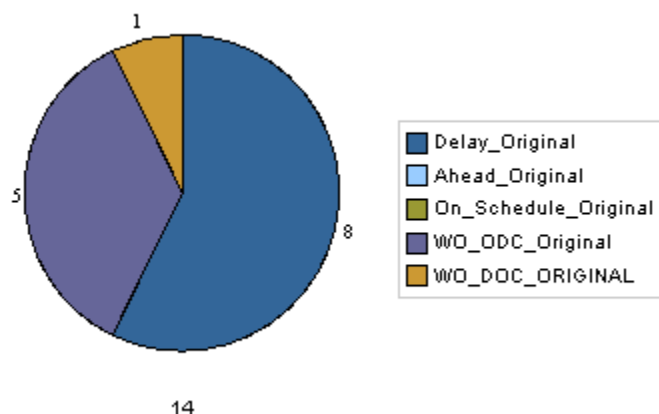

III. Investment Scenario

The Total Original cost of implementation of 14 projects when sanctioned, was of the order of Rs. 40023.85 crore but this was subsequently revised to Rs. 59739.88 crore implying a cost overrun of 49.3%. The expenditure incurred on these projects till February, 2011 is Rs. 24719 crore, which is 41.4% of the revised cost of the projects.

Figures are in Rs. Crore

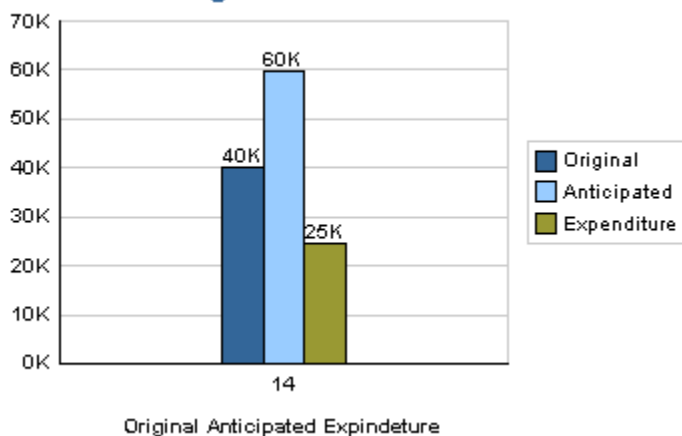

Sector wise current status of projects on the Flash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	1

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule and 1 project are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

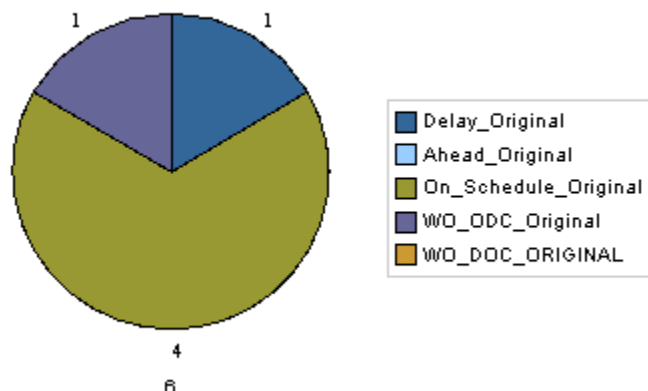

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till February, 2011 is Rs. 345.27 crore, which is 6.5% of the revised cost of the projects.

Figures are in Rs. Crore

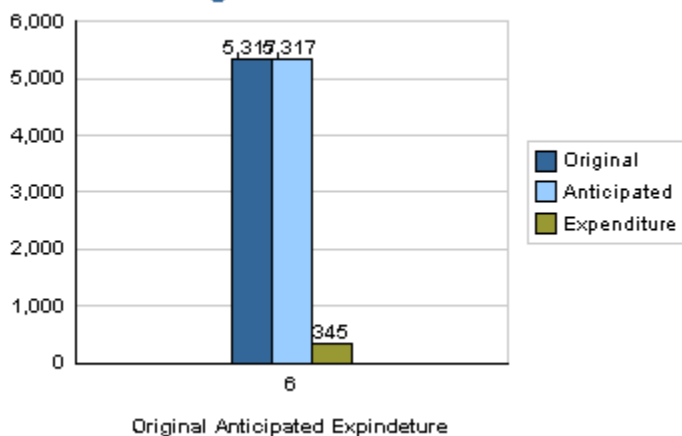

Sector wise current status of projects on the Flash Report


Coal

I. Current Status:

Number of Projects	45
Number of Projects On Schedule	16
Number of Projects Delayed	19
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 45 projects, 1 project are ahead of schedule, 16 projects are on schedule and 19 projects are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

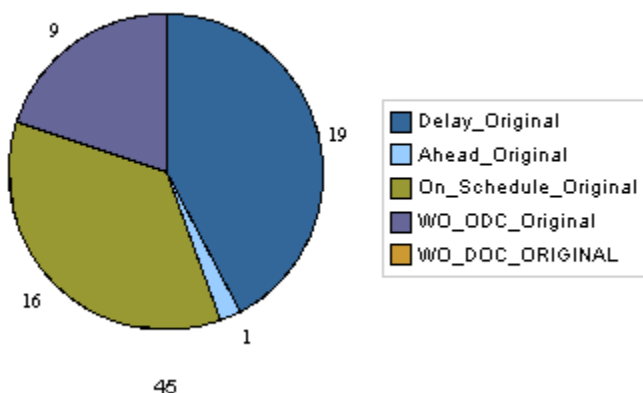

III. Investment Scenario

The Total Original cost of implementation of 45 projects when sanctioned, was of the order of Rs. 25452.49 crore but this was subsequently revised to Rs. 28789.58 crore implying a cost overrun of 13.1%. The expenditure incurred on these projects till February, 2011 is Rs. 10113.39 crore, which is 35.1% of the revised cost of the projects.

Figures are in Rs. Crore

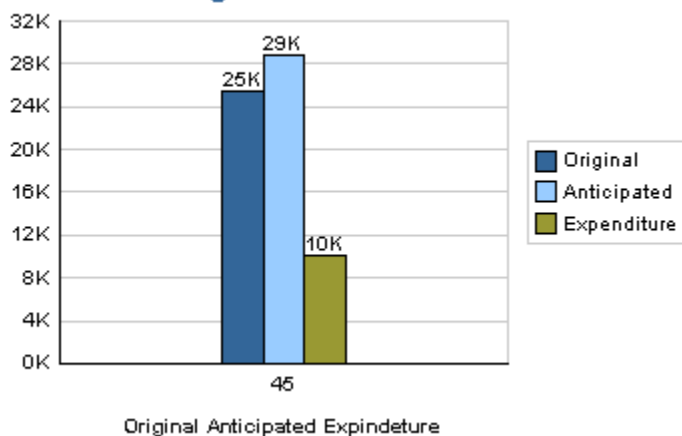

Sector wise current status of projects on the Flash Report

Civil Aviation


I. Current Status:

Number of Projects	7
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 7 projects, 2 projects are on schedule and 3 projects are delayed .2 projects do not have fixed dates of commissioning.

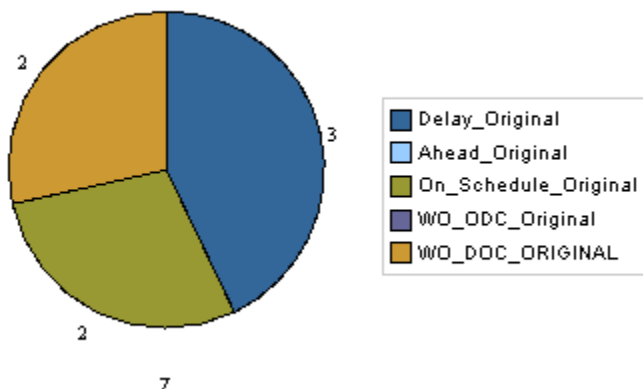

III. Investment Scenario

The Total Original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 4521.48 crore but this was subsequently revised to Rs. 4521.48 crore implying a cost overrun of 0%. The expenditure incurred on these projects till February, 2011 is Rs. 2477.8 crore, which is 54.8% of the revised cost of the projects.

Figures are in Rs. Crore

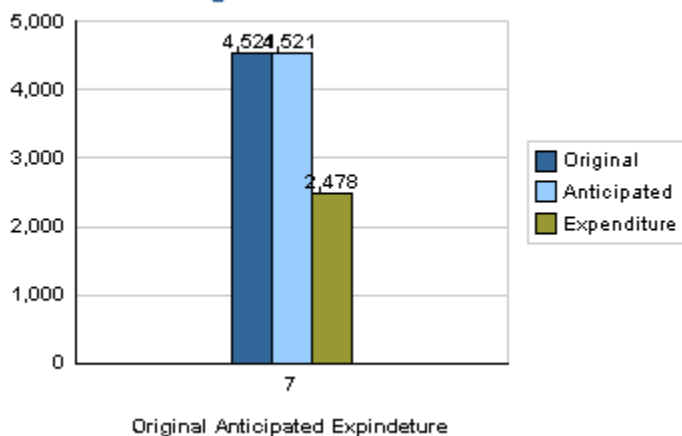

Sector wise current status of projects on the Flash Report


Atomic Energy

I. Current Status:

Number of Projects	3
Number of Projects Delayed	2
Number of Projects Without Original Date of Commissioning	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 3 projects, 2 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

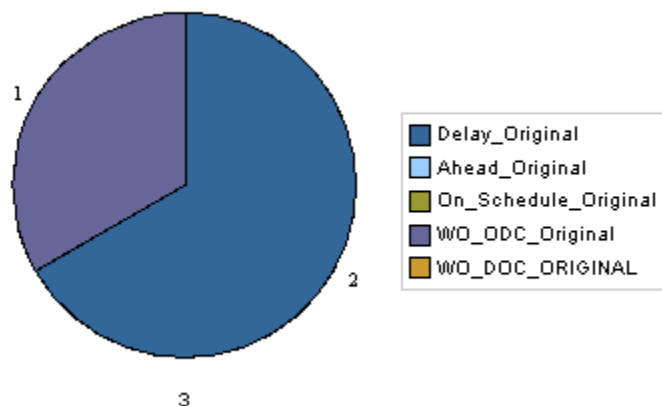

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 17769.29 crore but this was subsequently revised to Rs. 22607.29 crore implying a cost overrun of 27.2%. The expenditure incurred on these projects till February, 2011 is Rs. 17227.94 crore, which is 76.2% of the revised cost of the projects.

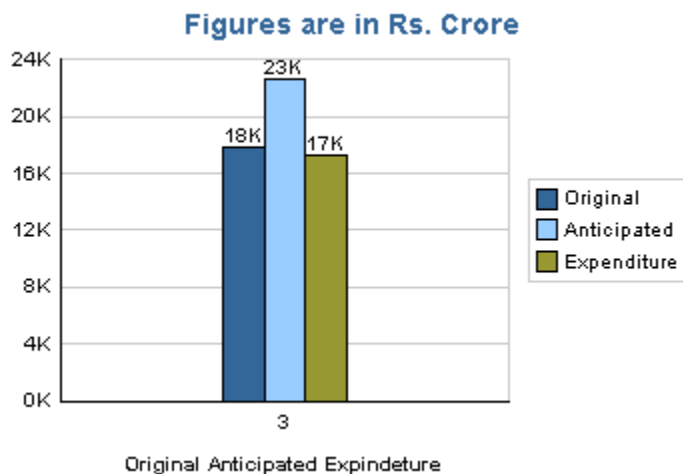

Summary of Central Sector Projects in Various States/UTs
(Status of projects as on 28.2.2011)

(Rs.Crores)					
Sr N.	State Name	No of Projects	Cost Original	Cost Anticipated	Expenditure
1	Andhra Pradesh	30	29391.54	36190.06	17622.65
2	Arunachal Pr.	4	9512.22	9516.70	6287.42
3	Assam	38	22765.13	28230.29	12954.65
4	Bihar	29	27979.21	31020.00	17415.15
5	Chhatisgarh	18	22418.50	38053.49	13183.87
6	Delhi	2	8925.00	19123.77	17189.86
7	Goa	1	204.73	204.73	25.64
8	Gujarat	21	15679.35	17894.09	9981.00
9	Haryana	10	4821.32	6379.33	3645.88
10	Himachal Pr.	8	15381.72	15463.96	11029.82
11	J & K	8	8297.84	18455.56	10453.95
12	Jharkhandd	22	9662.37	14556.07	5399.76
13	Karnataka	21	27223.84	34697.18	10470.35
14	Kerala	9	9160.26	10460.55	4051.07
15	Madhya pradesh	26	19050.00	18769.14	6137.15
16	Maharashtra	52	66816.16	86411.00	31060.56
17	Mizoram	2	988.06	3343.04	221.15
18	Multi State	98	120872.92	129246.83	40350.37
19	Nagaland	1	850.00	850.00	5.96
20	Orissa	25	51919.66	53891.16	13364.35
21	Punjab	9	5064.09	6028.72	2236.29
22	Rajasthan	15	12485.03	13574.15	7805.57
23	Sikkim	2	1603.77	3644.86	138.55
24	Tamil Nadu	36	42829.04	51468.15	35025.64
25	Tripura	3	1522.39	2053.24	234.50
26	Uttar Pradesh	34	16941.25	18941.70	11388.99
27	Uttaranchal	7	9003.78	11412.97	3893.83
28	West Bengal	28	40910.77	44482.61	21349.60
28		6	1965.76	1973.64	165.04
TOTAL		565	604245.71	726336.99	313088.62

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
