

**327th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
January 2013**



NPCIL - RAJASTHAN ATOMIC POWER PROJECT



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

जनवरी, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 571 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जनवरी, 2013 के दौरान 4 परियोजनाओं (उर्वरक तथा रेलवे क्षेत्र प्रत्येक की 2 परियोजनाएं) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 571 परियोजनाओं में से 278 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 82 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 82 परियोजनाओं में से, 23 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। नागर विमानन, रेलवे, पेट्रोलियम, विद्युत, कोयला तथा सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 36 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	126	37	7	4
2.	सड़क परिवहन एवं राजमार्ग	149	89	37	1
3.	विद्युत	101	53	10	6
4.	पेट्रोलियम	74	38	7	5
5.	कोयला	51	25	11	2
6.	दूरसंचार	15	8	0	0
7.	पोत परिवहन एवं पत्तन	20	5	0	0
8.	इस्पात	17	11	8	5
9.	उर्वरक	1	1	0	0
10.	नागर विमानन	6	3	2	0
11.	परमाणु ऊर्जा	5	3	0	0
12.	शहरी विकास	4	1	0	0
13.	जल संसाधन	1	0	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		571	274	82	23

3. 571 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,98,960.65 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,40,983.81 करोड़ रुपए होने की संभावना है जो 1,42,023.16 करोड़ रुपए (मूल लागत का 17.78%) की समग्र लागत वृद्धि को दर्शाता है। जनवरी, 2013 तक इन परियोजनाओं पर किया गया व्यय 4,41,396.08 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 46.30% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.01.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. 571 परियोजनाओं में से, 5 परियोजनाएं समय से पहले चल रही हैं, 173 समय पर तथा 274 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या 287 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है। इसके अलावा, 28 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 92 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है। 274 विलंबित परियोजनाओं में से, 75 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 62 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 87 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 50 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.01.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावा बारास्ता शिवपुरी-ग्वालियर-भिंड एनएलए(एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
2	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	01/2013	132

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

5. विभिन्न परियोजना कार्यान्वयनकर्ता एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी स्वीकृति में विलंब, सामग्री की आपूर्ति में विलंब, निविदा देने में विलंब, एमओईएफ के पास लंबित ईएमपी अनुमति, विक्रेताओं के चयन को अंतिम रूप देने में विलंब, भारी वर्षा के कारण देरी, काम देने में विलंब, मृदा संबंधी समस्या, विद्युत संबंधी तथा ऑटोमेशन प्रणाली की जांच एवं सुदृढीकरण में विलंब, कार्य की धीमी गति, आरओयू/आरओडब्ल्यू समस्याएं आदि शामिल हैं ।

6. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.01.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

7. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.01.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
				मूल	अनुमानित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.01.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) नागर विमानन क्षेत्र में, 6 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । माह के दौरान 2 परियोजनाओं के संबंध में 3 से 8 माह तक के अतिरिक्त विलंब की सूचना दी गई है । वेंडरों के चयन में विलंब के कारण 'नवीन अंतराष्ट्रीय भवन, एएआई' परियोजना में 3 माह तथा कार्य सौंपने तथा अत्यधिक वर्षा के कारण 'पाकयोंग (सिक्किम) हवाई अड्डा एएआई' स्थित 'नवीन हवाई अड्डा के निर्माण' में 8 माह के अतिरिक्त विलंब की सूचना दी गई है । इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वयन एजेंसी ने कोई विशेष कारण नहीं बताया गया है ।

(ii) रेलवे क्षेत्र में, 126 परियोजनाओं में से 37 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में प्रत्येक में 1-31 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 4 बड़ी परियोजनाएं हैं । 7 परियोजनाओं में से, 1 परियोजना के संबंध में 1 माह के अतिरिक्त विलंब की सूचना दी गई है तथा 1 परियोजना के संबंध में 11 माह तथा 2 परियोजनाओं में 12 माह के अतिरिक्त विलंब की सूचना दी गई है/भूमि अधिग्रहण तथा वन संबंधी मंजूरी नहीं मिलने के कारण 'गुना-इटावा V-ए शिवपुरी-ग्वालियर-भिंड एन एल परियोजना' में 22 माह के अतिरिक्त विलंब की सूचना दी गई है । मुंगेर एनएल, एनसीआर में 'रेल-सह-सड़कपुल' तथा आगरा-इटावा V-ए फतेहाबाद तथा बीएचए, एनएस, एनसीआर परियोजना में क्रमशः 24 तथा 31 माह के अतिरिक्त विलंब की सूचना दी गई है । तथापि, परियोजना प्राधिकारियों द्वारा इन परियोजनाओं में विलंब के लिए कोई विशेष कारण नहीं बताया गया है ।

(iii) पेट्रोलियम क्षेत्र में, 74 परियोजनाओं में से 38 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 1-14 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 5 बड़ी परियोजनाएं हैं । इन 7 परियोजनाओं में से, 1 परियोजनाओं के संबंध में प्रत्येक में 1 माह के 2 परियोजनाओं में प्रत्येक में 2 माह तथा 1 परियोजना में 4 माह के अतिरिक्त विलंब की सूचना दी गई है । यूरान, ओएनजीसी स्थित 'एडिशनल गैस प्रोसेसिंग यूनिट' परियोजना में कार्य सौंपने में विलंब के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'रेवाड़ी कानपुर पाइपलाइन परियोजना, एचपीसीएल' में भूमि अधिग्रहण में विलंब के कारण 6 माह के अतिरिक्त विलंब तथा 'कोच्ची-कूटानंद बंगलौर मंगलोर पाइपलाइन परियोजना, जीएआईएल' में आरओयू समस्या के कारण 14 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(iv) **इस्पात क्षेत्र में,** 17 परियोजनाओं में से 11 परियोजनाएं विलंबित हैं। माह के दौरान 8 परियोजनाओं के संबंध में 1-9 माह तक के अतिरिक्त विलंब की सूचना दी है जिनमें से 5 मेगा परियोजनाएं हैं। इन 8 परियोजनाओं में 1 परियोजना में 1 माह के अतिरिक्त विलंब, 1 परियोजना में 3 माह के अतिरिक्त विलंब तथा 1 परियोजना में 4 माह के अतिरिक्त विलंब की सूचना दी गई है। 'II एससीओ इस्पात संयंत्र, सेल का विस्तार परियोजना' में 6 माह के अतिरिक्त विलंब तथा 'बोकारो इस्पात संयंत्र, सेल का विस्तार परियोजना' में 6 माह के अतिरिक्त विलंब की सूचना दी गई है। इन दोनों ही परियोजनाओं में विलंब का कारण मृदा संबंधी समस्या तथा इलेक्ट्रिकल एवं ऑटोमेशन प्रणाली की टेस्टिंग व स्टेबिलाइजेशन में विलंब बताया गया है। 'राउरकेला इस्पात संयंत्र, सेल का विस्तार परियोजना, तथा भिलाई इस्पात संयंत्र, सेल का विस्तार परियोजना' में प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना दी गई है। एवं 'दुर्गापुर इस्पात संयंत्र, सेल का विस्तार परियोजना' में 9 माह के अतिरिक्त विलंब की सूचना दी गई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों ने कोई विशेष कारण नहीं बताया है।

(v) **विद्युत क्षेत्र में,** 102 परियोजनाओं में से 53 परियोजनाएं विलंबित हैं। माह के दौरान 10 परियोजनाओं के संबंध में 1-11 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 6 परियोजनाएं बड़ी परियोजनाएं हैं। इन 10 परियोजनाओं में से 2 परियोजना के संबंध में क्रमशः प्रत्येक में 1 माह के विलंब की सूचना प्राप्त हुई है तथा 1 परियोजना के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 5 परियोजनाओं में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। आरओयू समस्या के कारण 'नॉदर्न रिजन सिस्टम स्ट्रैथनिंग स्कीम-XX, पीजीसीआईएल' परियोजना में 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। उपस्कर की आपूर्ति में विलंब के कारण 'बाढ़ एसटीपीपी स्टेजI (3X660 मेगावाट), एनटीपीसी परियोजना में 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है

(vi) **कोयला क्षेत्र में,** 51 परियोजनाओं में से 25 परियोजनाएं विलंबित हैं। माह के दौरान 11 परियोजनाओं के संबंध में 12-36 माह के अतिरिक्त विलंब की सूचना दी है जिनमें से 2 मेगा परियोजनाएं हैं। इन 11 परियोजनाओं के संबंध में प्रत्येक 2 में 12 माह के अतिरिक्त विलंब की सूचना दी गई है। निविदा प्रक्रिया में विलंब के कारण 'जीवरा विस्तार ओसीपी (25-35) एमटीवाई, एसईसीएल', 'दिपका विस्तार ओसीपी (20-25) एमटीवाई, एसईसीएल', 'राजमहल ओसी विस्तार, ईसीएल' तथा चुड़ी बेंती यूजी (0.81 एमटीवाई), सीसीएल' परियोजना के संबंध में प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना दी गई है। पर्यावरण प्रबंधन योजना (ईएमपी) की स्वीकृति में विलंबके कारण 'कारतली (पूर्व) ओसीपी (2.50 एमटीवाई), एसईसीएल' तथा 'मणिकपुर ओसी विस्तार (3.5 एमटीवाई), एसईसीएल' परियोजनाओं के संबंध में प्रत्येक में 24 माह के अतिरिक्त विलंब की सूचना दी गई है। भूमि अधिग्रहण के कारण 'पुरनाडीह ओसीपी (3.0 एमटीवाई), सीसीएल' परियोजनाओं में 24 माह के अतिरिक्त विलंब की सूचना दी गई है। वन संबंधी स्वीकृति में विलंब के कारण तापिन ओसीपी (2.5 एमटीवाई), सीसीएल तथा (3.0 एमटीवाई), सीसीएल' परियोजनाओं के संबंध में प्रत्येक में क्रमशः 24 तथा 36 माह के अतिरिक्त विलंब की सूचना दी गई है।

(vii) **सड़क परिवहन एवं राजमार्ग क्षेत्र में,** 149 परियोजनाओं में से 89 परियोजनाएं विलंबित हैं। माह के दौरान 37 परियोजनाओं के संबंध में 1-21 माह के अतिरिक्त विलंब की सूचना प्राप्त दी गई है, जिनमें से 1

बड़ी परियोजना है । इन 37 परियोजनाओं में से 8 परियोजनाओं के संबंध में प्रत्येक में 1 माह, 6 परियोजनाओं में से प्रत्येक में 2 माह, 5 परियोजनाओं में से प्रत्येक में 3 माह, 1 परियोजना में से प्रत्येक में 4 माह, 2 परियोजनाओं में से प्रत्येक में 5 माह, 3 परियोजनाओं में से प्रत्येक में 6 माह, 1 परियोजना में 8 माह, 2 परियोजनाओं में से प्रत्येक में 9 माह तथा 4 परियोजनाओं में से प्रत्येक में 11 माह के अतिरिक्त विलंब की सूचना दी गई है । परियोजनाएं क्रमश 'बिजनी से असम/पश्चिम बंगाल सीमा पीएच-II, एनएच-31 एनएचएआई तथा बिजनी से असम/पश्चिम बंगाल बंगाल सीमा (एनएच-31 सी) (1), एनएचएआई' के संबंध में 12 माह के अतिरिक्त विलंब की सूचना दी गई है । 'हारनगाजो से मैबांग (एएस-23), 126.450 से 140.700 किमी., एनएचएआई' तथा मैबांग से लुंडिंग (एएस-25), 83.400 किमी से 111.000 किमी एनएचएआई' परियोजनाओं के संबंध में क्रमश: 14 तथा 17 माह के अतिरिक्त विलंब की सूचना दी गई है । 'मैबांग से लुंडिंग (एएस-27), 40.000 किमी से 60.500 किमी, एनएचएआई' परियोजना के संबंध में 21 माह के अतिरिक्त विलंब की सूचना दी गई है । इन परियोजनाओं में विलंब के लिए परियोजना कार्यान्वयन एजेंसी ने कोई विशेष कारण नहीं बताया है । तथापि, इन परियोजनाओं में विलंब के कारणों में साधारणतः भूमि अधिग्रहण में विलंब, वन तथा पर्यावरण संबंधी स्वीकृति में विलंब, जन सुविधाएं स्थानांतरित करने की समस्या तथा संविदाकार का खराब कार्य-निष्पादन आदि शामिल हैं ।

9. दिनांक 30.01.2012 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपए तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में दर्शाई गई है ।

10. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for January 2013 contains information on the status of the 571 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During January 2013, 4 projects (2 projects each in Fertilizers and Railways Sector) have reported completion.

2. During the reference month, out of 571 projects, 274 projects are delayed with respect to latest schedule and 82 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 82 projects, 23 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 36 months in respect of projects relating to Civil Aviation, Railways, Petroleum, Steel, Power, Coal and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	126	37	7	4
2.	ROAD TRANSPORT & HIGHWAYS	149	89	37	1
3.	POWER	101	53	10	6
4.	PETROLEUM	74	38	7	5
5.	COAL	51	25	11	2
6.	TELECOMMUNICATION	15	8	0	0
7.	SHIPPING & PORTS	20	5	0	0
8.	STEEL	17	11	8	5
9.	FERTILISERS	1	1	0	0
10.	CIVIL AVIATION	6	3	2	0
11.	ATOMIC ENERGY	5	3	0	0
12.	URBAN DEVELOPMENT	4	1	0	0
13.	WATER RESOURCES	1	0	0	0
14.	PETROCHEMICALS	1	0	0	0
Total		571	274	82	23

3. Total original cost of implementation of the 571 projects was about ₹ 7,98,960.65 crore and their anticipated completion cost is likely to be ₹ 9,40,983.81 crore, which reflects an overall cost overruns of ₹ 1,42,023.16 crore (17.78 % of original cost). The expenditure incurred on these projects till January 2013 is ₹ 4,41,396.08 crore, which is 46.30 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-01-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Out of the 571 projects, 5 projects are ahead of schedule, 173 are on schedule and 274 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 287 if delay is calculated on the basis of original schedule of completion. Further, 28 projects have been sanctioned without any commissioning schedule/date and for 92 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 274 delayed projects, 75 projects have overall delay in the range of 1 to 12 months, 62 projects have a delay in the range of 13 to 24 months, 87 projects have a delay in the range of 25 to 60 months and 50 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-01-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI- GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
3	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
5	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

5. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of material, delay in tendering process, EMP clearance is pending with MOEF, delay in finalization of vendors, delay due to heavy rain, delay in award of work, soil related problem, delay in testing and stabilization of electrical & automation system, slow progress of work, ROU/ROW problems, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-01-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		EXPENDITURE CUMULATIVE (₹ ; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

7. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-01-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.01.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

8. The Sector-wise details of delays/additional delays are as under:-

i) In the **Civil Aviation Sector**, out of 6 projects, 3 projects are delayed. During the month 2 projects have reported additional delays of 3 & 8 months. The projects 'Construction of New International Terminal Building, AAI' has reported additional delay of 3 months due to delay in finalization of vendors and 'Construction of New Airport at Pakyong (Sikkim) Airport, AAI' has reported additional delay of 8 months due to delay in award of work and heavy rain.

ii) In the **Railways Sector**, out of 126 projects, 37 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-31 months, out of which 4 are Mega project. Of these 7 projects, 1 project has reported additional delay of 1 month, 1 project has reported additional delay 11 months and 2 projects have reported additional delay of 12 months each. The project 'Guna-Etawah VI-A Shivpuri-Gwalior-Bhind NL, NCR' has reported additional delay of 22 months due to delay in land acquisition and forest clearance. The projects 'Rail-Cum-Road Bridge at Munger NL, ECR' and 'Agra-Etawah VI-A Fatehabad and BAH NL, NCR' have reported additional delay of 24 and 31 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

iii) In the **Petroleum Sector**, out of 74 projects, 38 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-14 months, out of which 5 are Mega projects. Of these 7 projects, 1 project has reported additional delay of 1 month, 2 projects have reported additional delay of 2 months each and 1 project has reported additional delay of 4 months. The project 'Additional Gas Processing Units at Uran, ONGC' has reported additional delay of 6 months due to delay in award of works. The projects 'Rewari Kanpur Pipeline Project, HPCL' has reported additional delay of 8 months due to delay in land acquisition and 'Kochi-Kootanad Bangalore Mangalore Pipeline Project, GAIL' has reported additional of 14 months due to ROU problem.

iv) In the **Steel Sector**, out of 17 projects, 11 projects are delayed. During the month 8 projects have reported additional delays in the range of 6-9 months. The projects 'Expansion of II SCO Steel Plant, SAIL' and 'Expansion of Bokaro Steel Plant, SAIL'

have reported additional delay of 6 months each due to soil related problem and delay in testing and stabilization of electrical & automation system. The project 'Expansion of Rourkela Steel Plant, SAIL' and 'Expansion of Bhilai Steel Plant, SAIL' have reported additional delay of 6 months each and 'Expansion of Durgapur Steel Plant, SAIL' has reported additional delay of 9 months. However, no specific reasons have been reported by the project authorities for delay in these projects.

v) In the **Power Sector**, out of 102 projects, 53 projects are delayed. During the month 10 projects have reported additional delays in the range of 1-11 months, out of which 6 are Mega projects. Of these 10 projects, 2 projects have reported additional delay of 1 month each, 1 project has reported additional delay of 2 months and 5 projects have reported additional delay of 3 months each. The project 'Northern Region System Strengthening Scheme- XXI, PGCIL' has reported additional delay of 5 months due to ROU problem. The project 'Barh STPP STAGE I (3X660MW), NTPC' has reported additional delay of 11 months due to delay in supply of equipment.

vi) In the **Coal Sector**, out of 51 projects, 25 projects are delayed. During the month 11 projects have reported additional delays in the range of 12-36 months, out of which 2 are Mega project. Of these 11 projects, 2 projects have reported additional delay of 12 months each. The projects 'Gevra Expansion OCP (25-35) MTY, SECL', 'Dipka Expansion OCP (20-25) MTY, SECL', 'Rajmahal OC Expansion, ECL' and 'Churi Benti UG (0.81 MTY), CCL' have reported additional delay of 24 months each due to delay in tendering process. The projects 'Kartali (East) OCP (2.50 MTY), SECL' and 'Manikpur OC Expansion (3.5 MTY), SECL' have reported additional delay of 24 months each due to delay in Environment Management Plan (EMP) clearance. The projects 'Purnadih OCP (3.0 MTY), CCL' has reported additional delay of 24 months due to land acquisition. The projects 'Tapin OCP (2.5 MTY), CCL' and 'North Urimari OCP (3.0 MTY), CCL' has reported additional delay of 24 and 36 months respectively due to delay in forest clearance.

vii) In the **Road Transport & Highways Sector**, out of 149 projects, 89 are delayed. During the month 37 projects have reported additional delays in the range of 1-21 months, out of which 1 is a Mega Projects. Of these 37 projects, 8 projects have reported additional delay of 1 month each, 6 projects have reported additional delay of 2 months each, 5 projects have reported additional delay of 3 months each, 1 project has reported additional delay of 4 months, 2 projects have reported additional delay of 5 months each, 3 projects have reported additional delay of 6 months each, 1 project has reported additional delay of 8 months, 2 projects have reported additional delay of 9 months each and 4 projects have

reported additional delay of 11 months each . The projects 'Bijni to Assam/WB Border PH.II, NH-31 C NHAI' and 'Bijni to Assam/WB Border (NH-31.C) (1), NHAI' have reported additional delay of 12 months respectively. The projects 'Harangajo to Maibang (AS-23), KM.126.450 to KM.140.700, NHAI' and 'Maibang to Lunding (AS-25), KM.83.400 to KM.111.000, NHAI' have reported additional delay of 14 and 17 months respectively. The project 'Maibang to Lunding (AS-27), KM.40.000 to KM.60.500, NHAI' has reported additional delay of 21 months. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

9. The status as on 31.01.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

10. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Road Transport & Highways	149	37
2	Railways	126	7
3	Power	101	10
4	Petroleum	74	7
5	Coal	51	11
6	Shipping & Ports	20	0
7	Steel	17	8
8	Telecommunications	15	0
9	Civil Aviation	6	2
10	Atomic Energy	5	0
11	Urban Development	4	0
12	Fertilisers	1	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	571	82

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	1438
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
	June,2012			
	<u>Steel</u>			
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
	<u>Power</u>			
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	3779.46
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
	<u>Railways</u>			
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
	<u>Road Transport & Highways</u>			
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300] July,2012	225.00	10/2008	261.9
	<u>Power</u>			
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096] August,2012	196.97	03/2011	218.66
	<u>Steel</u>			
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
	<u>Power</u>			
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
	<u>Road Transport & Highways</u>			
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235] September,2012	193.09	03/2008	189.15
	<u>Petroleum</u>			
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
	<u>Telecommunications</u>			
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
October,2012				
<u>Road Transport & Highways</u>				
37	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106204]	275.00	09/2007	306.65
38	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106301]	151.30	10/2008	190.61
November,2012				
<u>Petroleum</u>				
39	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC(GAS AUTHORITY OF INDIA LIMITED) - [N16000071]	348.00	03/2012	203.31
December,2012				
<u>Fertilisers</u>				
40	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS(NATIONAL FERTILISER LIMITED) - [N08000007]	325.00	07/2011	185.1
41	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ(NATIONAL FERTILISER LIMITED) - [N08000008]	438.00	07/2011	239.93
<u>Power</u>				
42	WESTERN REGION STRENGTHENING SCHEME-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000022]	5,221.23	07/2010	3175.3
<u>Railways</u>				
43	MUMBAI URBAN TRANSPORT PROJECT PHASE-I(METROPOLITAN RAPID TRANSPORT PROJECTS) - [N22000093]	3,125.20	06/2011	4334
<u>Road Transport & Highways</u>				
44	DAKOB TO NAGAON (NH-36)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106288]	225.00	06/2008	285.2
45	JHAJHARPUR TO DARBANGA (BR-7)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000031]	340.00	09/2008	575.32
46	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000118]	464.00	01/2011	535.62
47	Hyderabad-yadgiri N.H no-202(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000142]	388.00	05/2012	537.91
<u>Shipping & Ports</u>				
48	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA(SHIPPING crp. of india) - [N25000031]	1,066.91	09/2012	1027.12
January,2013				

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Fertilisers</u>				
49	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE(NATIONAL FERTILISER LIMITED) - [N08000004]	1,292.84	01/2013	987.72
50	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ(NATIONAL FERTILISER LIMITED) - [N08000005]	1,294.19	01/2013	972.95
<u>Railways</u>				
51	REWARI-ROHTAK (NL),NR(NORTHERN RAILWAY) - [220100279]	149.38	02/2010	508.76
52	PODAPAHAR-BANSPANI,(LD)(SER)(SOUTH EASTERN RAILWAY) - [N22000046]	129.74	03/2006	162.27


Summary of projects in the Flash Report for the month of January, 2013

I. Project Implementation - Current Status:

Number of Projects in Previous Month	577
Number of Projects completed/dropped/frozen in Previous Month	9
Number of Projects completed/dropped/frozen in Current Month	4
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	1
Number of Projects Added in Current Month	7
Number of Projects in Current Month	571


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 571 projects, 4 projects are ahead of schedule, 160 projects are on schedule and 287 projects are delayed. Of the balance, 92 projects do not have fixed dates of commissioning while 28 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

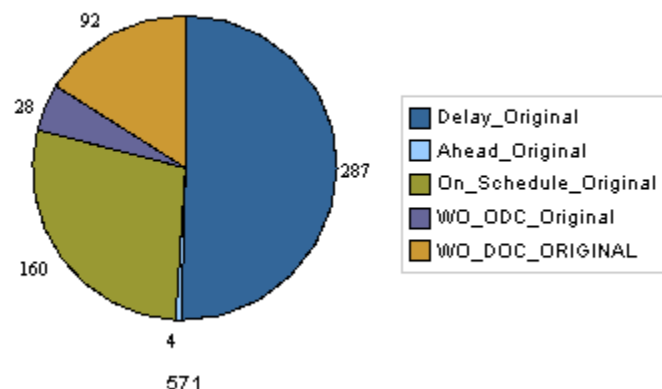

III. Investment Scenario

The Total Original cost of implementation of 571 projects when sanctioned, was of the order of Rs. 798960.65 crore but this was subsequently revised to Rs. 940983.81 crore implying a cost overrun of 17.8%. The expenditure incurred on these projects till January, 2013 is Rs. 440674.08 crore, which is 46.8% of the revised cost of the projects.

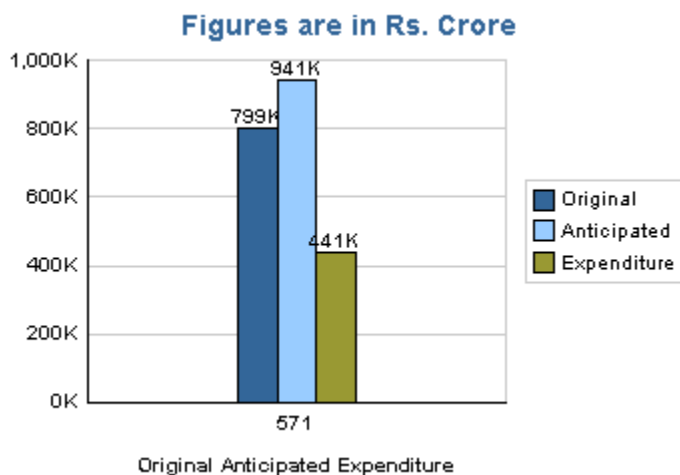

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	577
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	1
No of Projects added in Current Month	6
No of Projects in Current Month	571

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	287	4	160	28	92	571	50.26
Latest Approved (Date)	274	5	172	28	92	571	47.99

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	421	669,144.37	705,026.18	302,728.23	42.90	35,881.81	5.40
Latest Approved (RCE)	150	188,091.53	235,957.63	137,945.85	58.50	47,866.10	25.40
Total (RCE)	571	857,235.90	940,983.81	440,674.08	46.83	83747.91	9.77
Original Cost of All Projects							
Original Cost	571	798,960.65	940,983.81	440,674.08	46.80	142,023.16	17.80

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	287	458,307.11	554,356.36	333,389.66	60.10	96,049.25	21.00
Latest Approved (RCE)	274	460,000.72	519,707.79	312,952.18	60.20	59,707.07	13.00

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	82	140,383.73	150,712.53	100,799.54	66.90	10,328.80	7.40

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,510.5	4.0	7	8,579.5	10,631.3	23.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	74	177,600.6	188,903.2	6.4	16	54,264.0	73,426.2	35.3
8	Power	101	239,851.9	255,682.1	6.6	19	46,019.4	61,849.6	34.4
9	Railways	126	61,373.8	148,389.9	141.8	109	42,670.2	129,732.9	204.0
10	Road Transport & Highways	149	97,021.8	98,960.5	2.0	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	20	15,908.0	18,174.9	14.3	9	8,629.0	11,218.5	30.0
12	Telecommunications	15	7,113.1	6,920.2	-2.7	2	477.3	550.9	15.4
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		571	798,960.7	940,983.8	17.8	187	220,918.6	372,247.0	68.5

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,097.3	38,721.1	24.5	14	12,420.0	20,910.9	68.4
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	2	6,441.3	11,073.4	71.9
3	Assam	34	22,035.9	35,405.4	60.7	12	10,491.8	23,955.3	128.3
4	Bihar	30	26,917.6	34,877.4	29.6	14	12,668.3	20,628.1	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	8	4,054.4	5,741.1	41.6	2	1,298.8	2,985.5	129.9
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	26	46,344.4	55,830.8	20.5	9	8,598.8	18,491.8	115.1
11	Kerala	7	20,376.7	21,818.2	7.1	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	22	18,978.9	19,259.5	1.5	2	1,110.9	1,810.9	63.0
13	Maharashtra	52	93,207.4	108,066.8	15.9	15	28,256.2	45,605.8	61.4
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Odisha	31	57,664.0	62,099.1	7.7	12	32,671.6	37,106.7	13.6
19	Punjab	6	3,542.0	4,483.8	26.6	2	532.4	1,474.2	176.9
20	Rajasthan	14	21,115.8	20,928.0	-0.9	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	33	51,458.8	62,238.6	20.9	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	24	18,952.6	23,241.3	22.6	9	3,628.2	7,965.2	119.5
25	West Bengal	27	42,286.1	54,919.8	29.9	17	25,617.0	38,250.7	49.3
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	25	58,429.8	59,712.9	2.2	6	1,548.3	2,831.4	82.9
28	Jharkhand	23	14,447.4	18,493.0	28.0	7	2,225.5	6,442.8	189.5
29	Uttarakhand	4	6,097.2	7,037.6	15.4	2	2,640.7	3,581.2	35.6
30	Multi State	112	147,454.2	156,976.8	6.5	22	10,740.0	24,294.2	126.2
Total		571	798,960.7	940,983.8	17.8	187	220,918.6	372,247.0	68.5

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	13 - 35
3	Coal	51	36,056.5	37,510.5	4.0	25	22,863.2	24,736.8	16 - 60
4	Fertilisers	1	1,478.6	1,478.6	0.0	1	1,478.6	1,478.6	2 - 2
5	Steel	17	65,285.9	71,443.4	9.4	11	51,228.4	57,386.0	4 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	74	177,600.6	188,903.2	6.4	43	115,637.2	126,836.3	1 - 120
8	Power	101	239,851.9	255,682.1	6.6	53	133,184.7	148,401.8	1 - 102
9	Railways	126	61,373.8	148,389.9	141.8	43	27,831.3	73,163.8	2 - 235
10	Road Transport & Highways	149	97,021.8	98,960.5	2.0	89	44,536.0	46,474.6	2 - 109
11	Shipping & Ports	20	15,908.0	18,174.9	14.3	6	6,413.2	7,718.8	5 - 87
12	Telecommunications	15	7,113.1	6,920.2	-2.7	8	3,741.4	3,611.6	11 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		571	798,960.7	940,983.8	17.8	287	458,307.1	554,356.4	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,097.3	38,721.1	24.5	12	16,856.0	20,665.4	5 - 41
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	3	9,356.2	13,737.9	25 - 78
3	Assam	34	22,035.9	35,405.4	60.7	31	20,716.4	33,256.6	12 - 120
4	Bihar	30	26,917.6	34,877.4	29.6	12	19,613.9	23,190.2	2 - 86
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	13 - 13
6	Gujarat	22	31,111.6	31,313.5	0.6	7	16,101.7	16,093.9	6 - 24
7	Haryana	8	4,054.4	5,741.1	41.6	4	2,216.6	3,396.6	1 - 50
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	25 - 102
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	9	13,826.3	33,724.9	10 - 201
10	Karnataka	26	46,344.4	55,830.8	20.5	10	23,407.9	28,392.5	9 - 102
11	Kerala	7	20,376.7	21,818.2	7.1	4	5,356.0	6,006.0	5 - 58
12	Madhya pradesh	22	18,978.9	19,259.5	1.5	12	9,884.2	9,884.2	5 - 60
13	Maharashtra	52	93,207.4	108,066.8	15.9	24	50,822.7	60,375.3	6 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	72 - 72
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 35
17	Nagaland	1	850.0	850.0	0.0	1	850.0	850.0	24 - 24
18	Odisha	31	57,664.0	62,099.1	7.7	13	35,397.6	36,359.9	3 - 132
19	Punjab	6	3,542.0	4,483.8	26.6	4	2,716.1	3,657.8	2 - 58
20	Rajasthan	14	21,115.8	20,928.0	-0.9	6	15,563.1	15,116.8	3 - 56
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	35 - 51
22	Tamil Nadu	33	51,458.8	62,238.6	20.9	11	30,528.8	36,459.4	9 - 87
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,101.4	1,395.4	9 - 21
24	Uttar Pradesh	24	18,952.6	23,241.3	22.6	13	11,872.8	14,293.5	7 - 95
25	West Bengal	27	42,286.1	54,919.8	29.9	16	27,379.4	34,549.5	3 - 135
26	Delhi	4	38,214.4	38,194.8	-0.1	2	478.4	458.8	11 - 72
27	Chhatisgarh	25	58,429.8	59,712.9	2.2	8	23,022.5	23,333.9	12 - 59
28	Jharkhand	23	14,447.4	18,493.0	28.0	13	9,731.2	10,692.6	5 - 94
29	Uttarakhand	4	6,097.2	7,037.6	15.4	4	6,097.2	7,037.6	5 - 45
30	Multi State	112	147,454.2	156,976.8	6.5	55	87,810.2	92,404.2	1 - 235
Total		571	798,960.7	940,983.8	17.8	287	458,307.1	554,356.4	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	13 - 35
3	Coal	51	36,056.5	37,510.5	4.0	25	22,863.2	24,736.8	16 - 60
4	Fertilisers	1	1,478.6	1,478.6	0.0	1	1,478.6	1,478.6	2 - 2
5	Steel	17	65,285.9	71,443.4	9.4	11	51,228.4	57,386.0	4 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	74	177,600.6	188,903.2	6.4	38	105,879.9	111,555.9	1 - 86
8	Power	101	239,851.9	255,682.1	6.6	53	133,184.7	148,401.8	1 - 102
9	Railways	126	61,373.8	148,389.9	141.8	37	19,509.3	63,315.7	2 - 235
10	Road Transport & Highways	149	97,021.8	98,960.5	2.0	89	44,536.0	46,474.6	2 - 109
11	Shipping & Ports	20	15,908.0	18,174.9	14.3	5	6,263.2	7,118.8	5 - 34
12	Telecommunications	15	7,113.1	6,920.2	-2.7	8	3,741.4	3,611.6	11 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		571	798,960.7	940,983.8	17.8	274	434,617.2	519,707.8	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,510.5	1.3	6	7,115.6	7,603.7	6.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	74	193,120.4	188,903.2	-2.2	2	30,602.0	32,253.0	5.4
8	Power	101	243,659.0	255,682.1	4.9	13	39,029.6	51,052.7	30.8
9	Railways	126	91,434.1	148,389.9	62.3	79	46,008.2	103,446.3	124.8
10	Road Transport & Highways	149	97,188.3	98,960.5	1.8	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	20	17,661.9	18,174.9	2.9	6	3,312.5	4,036.9	21.9
12	Telecommunications	15	7,113.1	6,920.2	-2.7	2	477.3	550.9	15.4
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		571	857,235.9	940,983.8	9.8	128	164,702.8	255,657.9	55.2

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	0	0.00	0.00	0- 0
3	Coal	51	36,056.46	37,510.52	4.03	0	0.00	0.00	0- 0
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	0	0.00	0.00	0- 0
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	74	177,600.55	188,903.21	6.36	3	3,930.35	6,028.17	52- 120
8	Power	101	239,851.89	255,682.13	6.60	1	1,657.00	2,978.86	76- 76
9	Railways	126	61,373.80	148,389.93	141.78	2	1,189.97	5,627.03	23- 92
10	Road Transport & Highways	149	97,021.84	98,960.46	2.00	0	0.00	0.00	0- 0
11	Shipping & Ports	20	15,907.97	18,174.92	14.25	1	150.00	600.00	87- 87
12	Telecommunications	15	7,113.08	6,920.16	-2.71	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		571	798960.65	940983.81	17.78	8	12387.93	24154.06	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	22- 22
3	Coal	51	36,056.46	37,510.52	4.03	5	7,938.86	9,942.56	16- 51
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	8- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	74	177,600.55	188,903.21	6.36	13	52,458.98	70,307.15	12- 120
8	Power	101	239,851.89	255,682.13	6.60	17	45,001.89	60,218.99	7- 102
9	Railways	126	61,373.80	148,389.93	141.78	33	17,023.65	61,056.12	2- 235
10	Road Transport & Highways	149	97,021.84	98,960.46	2.00	11	3,324.28	5,445.20	21- 106
11	Shipping & Ports	20	15,907.97	18,174.92	14.25	4	5,580.00	6,965.50	13- 87
12	Telecommunications	15	7,113.08	6,920.16	-2.71	2	477.28	550.85	45- 46
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		571	798960.65	940983.81	17.78	95	182802.95	284826.8	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Fertilisers</u>							
1	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE	01/2010	1,292.84	01/2013	1,292.84	01/2013	987.72
2	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ	01/2010	1,294.19	01/2013	1,294.19	01/2013	972.95
<u>Railways</u>							
3	REWARI-ROHTAK (NL),NR	01/2004	149.38	02/2010	602.78	02/2011	508.76
4	PODAPAHAR-BANSPANI,(LD)(SER)	04/2006	129.74	03/2006	163.00	N.A.	162.27

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
<u>Petroleum</u>						
1	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli	4/2011	152.89	6/2013	152.89	6/2013
<u>Power</u>						
2	LARA STPP STAGE-I	11/2012	11,846.00	5/2017	11,846.00	5/2017
<u>Road Transport & Highways</u>						
3	RANCHI-RARGA-JAMSETHPUR	12/2012	1,479.00	6/2015	1,479.00	6/2015
4	PANVEL-INDAPUR	12/2011	942.69	6/2014	942.69	6/2014
5	TUTICORIN-PORT	4/2010	182.25	2/2013	182.25	2/2013
<u>Telecommunications</u>						
6	Supply Installation testing and commissioning of Rural Wimax	7/2010	1,148.19	5/2011	964.37	6/2013

VII. Milestones (Cumulative due & achieved)

Total	3496
Achieved up to month	1317

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Civil Aviation</u>						
1	Construction of New International Terminal Building AAI	335.61	335.61	05/2012	03/2013	06/2013	3
2	C/o new Airport at Pakyong(Sikkim) Airport AAI	309.46	309.46	01/2011	04/2013	12/2013	8
	<u>Coal</u>						
3	ASHOK EXPN.OCP -CCL (10 MTY) CCL	471.66	341.63	03/2011	03/2013	03/2014	12
4	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
5	GEVRA EXPANSION OCP (SECL) (25-35) MTY SECL	2,675.67	2,675.67	03/2014	03/2014	03/2016	24
6	DIPKA EXPANSION OCP (SECL) (20-25) MTY SECL	1,943.66	1,943.66	03/2014	03/2014	03/2016	24
7	RAJMAHAL OC EXP. ECL	153.82	153.82	03/2014	03/2014	03/2016	24
8	KARTALI (EAST) OCP (2.50 MTY) SECL	178.44	178.44	03/2014	03/2014	03/2016	24
9	MANIKPUR OC EXPANSION (3.5 MTY) SECL	321.42	321.50	03/2014	03/2014	03/2016	24
10	Churi Benti UG (0.81 MTY) CCL	163.51	163.51	03/2011	03/2014	03/2016	24
11	Purnadih OCP (3.0 MTY) CCL	210.98	210.98	03/2013	03/2013	03/2015	24
12	Tapin OCP (2.5 MTY) CCL	264.68	264.68	03/2012	03/2014	03/2016	24
13	North Urimari OCP (3.0 MTY) CCL	179.87	179.87	03/2012	03/2014	03/2017	36
	<u>Steel</u>						
14	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	01/2013	02/2013	1
15	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	10/2012	03/2013	06/2013	3
16	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON SAIL	254.55	254.55	11/2013	11/2013	03/2014	4
17	EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	12/2012	06/2013	6
18	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	12/2012	06/2013	6
19	Expansion of Rourkela Steel Plant SAIL	11,812.00	11,812.00	11/2013	03/2013	09/2013	6
20	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	09/2013	03/2014	6
21	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	03/2013	12/2013	9
	<u>Petroleum</u>						
22	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA ONGC	370.11	370.11	04/2011	01/2013	02/2013	1
23	PARADIP REFINERY PROJECT IOCL	29,777.00	30,426.00	11/2012	09/2013	11/2013	2
24	Fluidized catalytic cracking unit(FCCU) revamp IOCL	1,000.00	1,000.00	01/2013	06/2013	08/2013	2
25	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	2,174.00	09/2011	02/2013	06/2013	4
26	ADDITIONAL GAS PROCESSING UNITS AT URAN ONGC	1,797.35	977.00	12/2011	01/2013	07/2013	6

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
27	REWARI KANPUR PIPELINE PROJECT HPCL	1,210.64	1,210.64	11/2015	03/2015	11/2015	8
28	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC GAIL	2,915.00	2,915.00	12/2012	03/2013	05/2014	14
Power							
29	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	758.75	01/2010	02/2013	03/2013	1
30	765 KV POOLING STATION AND NETWORK WITH DVC AND MA PGCIL	7,075.33	7,075.33	08/2012	12/2013	01/2014	1
31	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	386.32	07/2011	01/2013	03/2013	2
32	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	12/2013	03/2014	3
33	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	03/2013	06/2013	3
34	System Strengthening in NR for SASAN & MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	12/2013	03/2014	3
35	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI PGCIL	2,074.86	2,074.86	03/2013	03/2013	06/2013	3
36	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX PGCIL	182.68	182.68	01/2013	03/2013	06/2013	3
37	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI PGCIL	1,677.57	1,677.57	04/2013	10/2013	03/2014	5
38	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	03/2016	02/2017	11
Railways							
39	CHANDIGARH-LUDHIANA(NEW BG LINE),NR NR	248.44	1,115.21	12/2012	01/2013	02/2013	1
40	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) RVNL	133.41	225.00	03/2009	04/2013	03/2014	11
41	KHURDA ROAD-BOLANGIR(NL)ECOR ECOR	355.38	1,995.25	N.A.	03/2013	03/2014	12
42	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) NEFR	727.56	4,444.00	03/2011	03/2016	03/2017	12
43	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) NCR	158.77	580.83	03/1994	12/2011	10/2013	22
44	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR ECR	921.00	2,363.00	03/2009	12/2012	12/2014	24
45	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR NCR	108.00	432.72	12/2009	03/2011	10/2013	31
Road Transport & Highways							
46	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH- 4) NHAI	241.00	196.65	08/2004	01/2013	02/2013	1
47	HARIHAR-CHITRADURGA (GQ) KM.284- KM.207 (NH-4) NHAI	318.00	207.56	08/2004	01/2013	02/2013	1
48	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	01/2013	02/2013	1
49	AGRA-SHIKOHABAD (GQ) KM.199.66- KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	01/2013	02/2013	1


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
50	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA NHAI	229.91	229.91	10/2008	01/2013	02/2013	1
51	HARANGAJO TO MAIBANG, NH-54 NHAI	196.00	363.74	07/2009	04/2014	05/2014	1
52	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	01/2013	02/2013	1
53	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	01/2013	02/2013	1
54	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	01/2013	03/2013	2
55	NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	03/2013	05/2013	2
56	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	03/2013	05/2013	2
57	THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	01/2013	03/2013	2
58	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	01/2013	03/2013	2
59	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	01/2013	03/2013	2
60	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) NHAI	237.80	237.80	06/2008	12/2013	03/2014	3
61	NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2011	01/2013	04/2013	3
62	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	03/2013	06/2013	3
63	JHANSI TO LALITPUR, NH-25,26 NHAI	355.06	355.06	09/2009	03/2013	06/2013	3
64	SALEM - U / UNDRUPET(BOT -1/TN-06) NH - 68 NHAI	941.00	941.00	01/2011	02/2013	05/2013	3
65	KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	02/2013	06/2013	4
66	NALBARI T BIJNI (AS-7) NHAI	208.00	208.00	04/2008	12/2013	05/2014	5
67	Hazaribagh-Ranchi NHAI	625.07	625.07	01/2013	01/2013	06/2013	5
68	NALBARI TO BIJNI (AS-8) NHAI	200.00	200.00	06/2008	03/2013	09/2013	6
69	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	03/2013	09/2013	6
70	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE NHAI	232.45	232.45	09/2010	06/2013	12/2013	6
71	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	217.61	04/2010	03/2014	11/2014	8
72	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) NHAI	160.00	160.00	05/2008	03/2013	12/2013	9
73	SAMAIKHALI - GANDHIDHAM NHAI	805.39	805.39	03/2013	03/2013	12/2013	9
74	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	01/2013	12/2013	11
75	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 NHAI	167.64	167.64	11/2008	01/2014	12/2014	11
76	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 NHAI	155.04	280.13	11/2008	07/2013	06/2014	11
77	kandla - Mundra port NHAI	953.88	953.88	07/2013	07/2013	06/2014	11
78	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C NHAI	230.00	230.00	06/2005	03/2013	03/2014	12
79	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) NHAI	195.00	195.00	06/2008	03/2013	03/2014	12
80	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 NHAI	280.00	280.00	02/2009	03/2013	05/2014	14
81	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 NHAI	199.81	385.13	04/2009	07/2013	12/2014	17


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
82	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 NHAI	200.00	200.00	04/2009	03/2013	12/2014	21


Graphical Analysis of All Projects w.r.t. Original Schedule

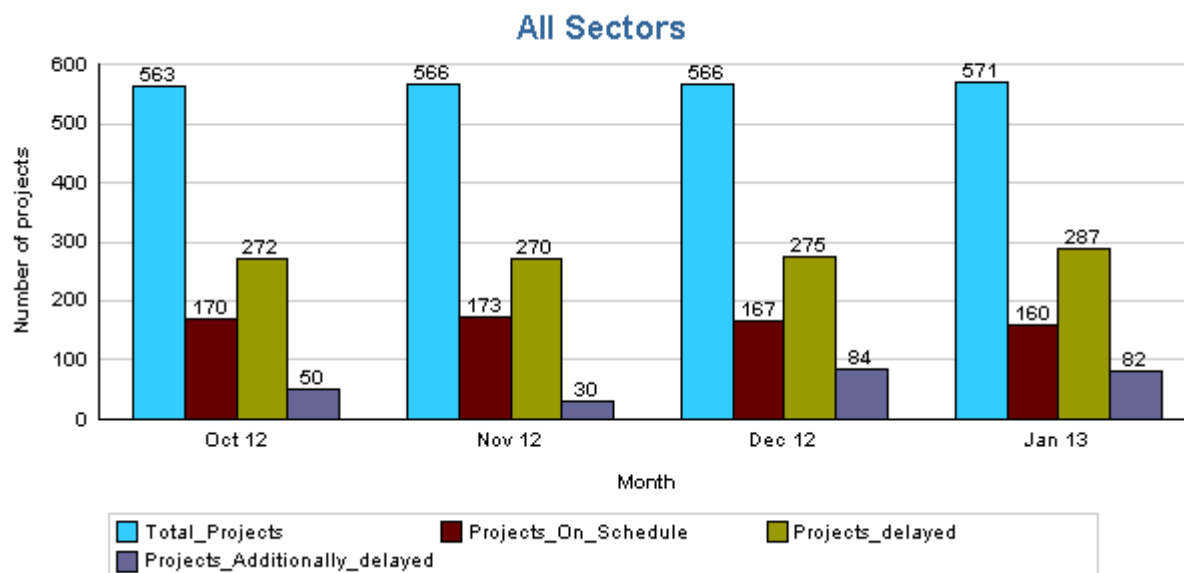


All Sectors Break-up of 287 Delayed projects in January 2013

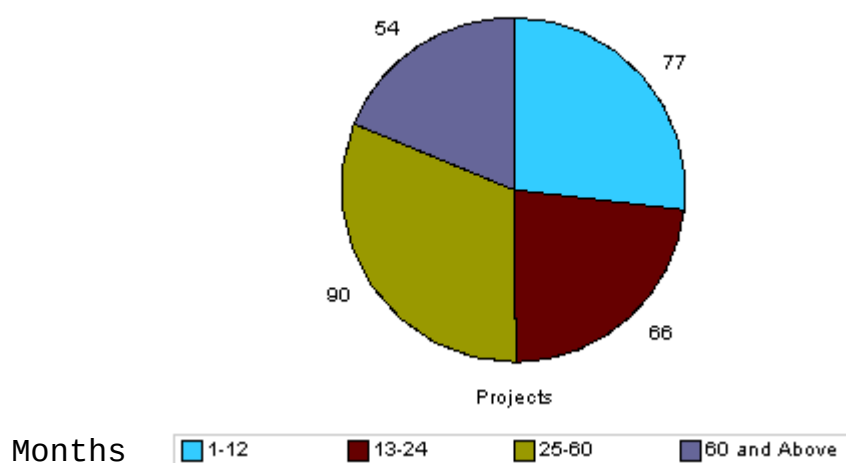

Graphical Analysis of All Projects w.r.t. Revised Schedule

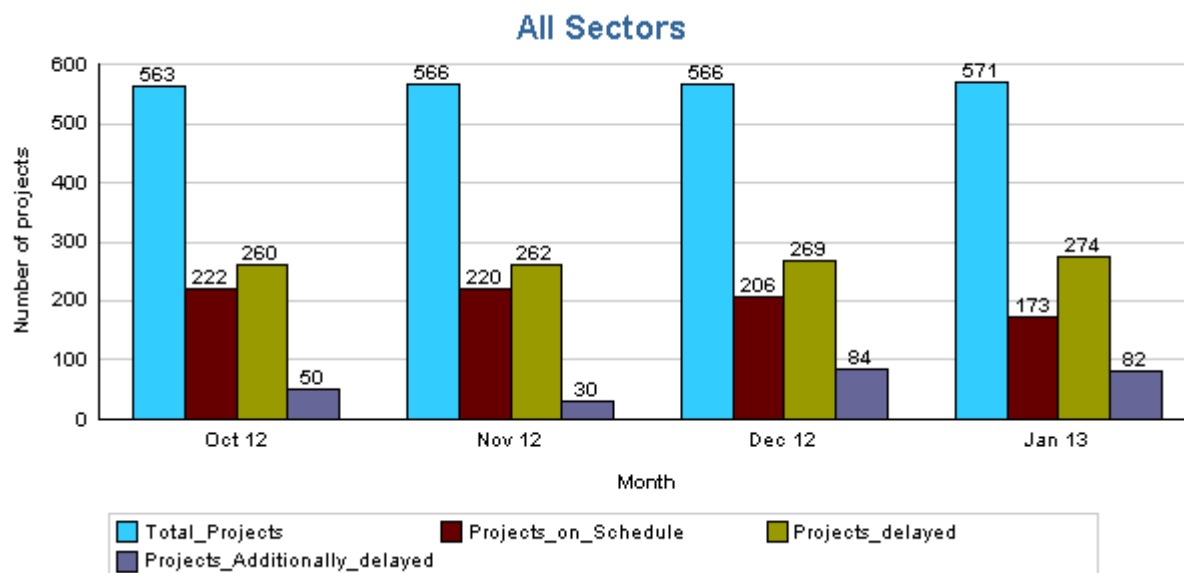

All Sectors Break-up of 274 Delayed projects in January 2013

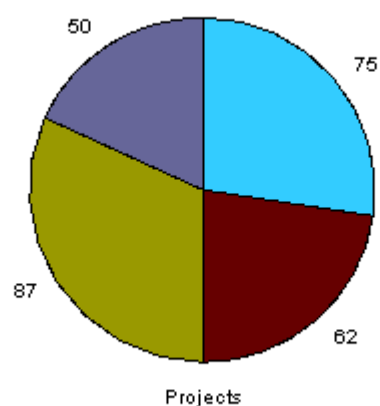


Months




Trend and Graphical Analysis

Urban Development Sector

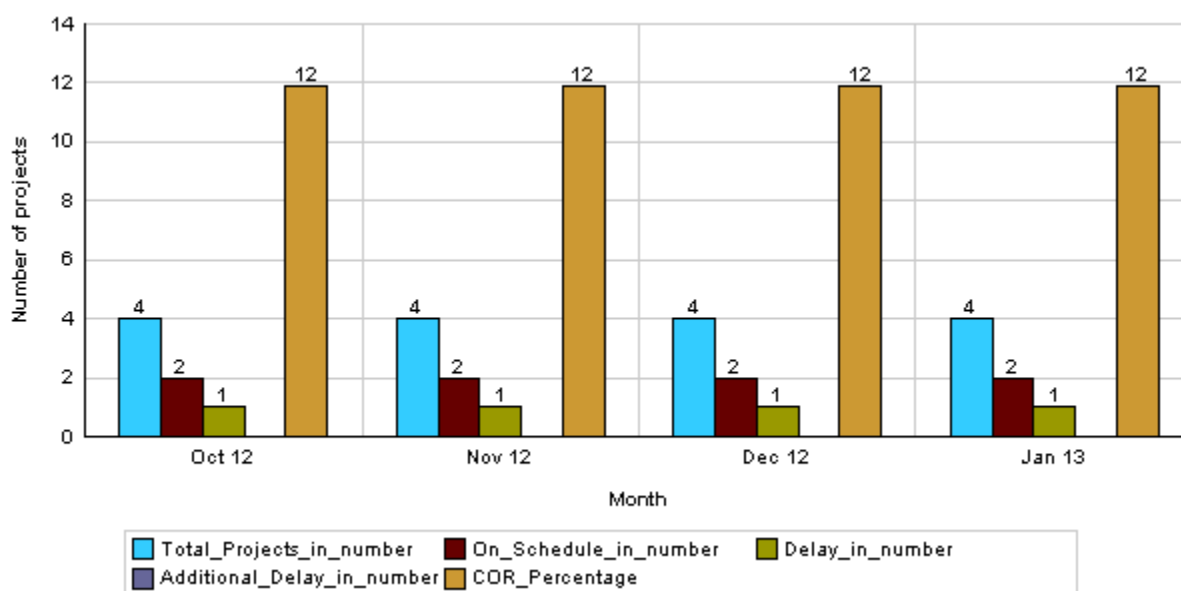


Urban Development Sector Break-up of 1 Delayed projects in January 2013

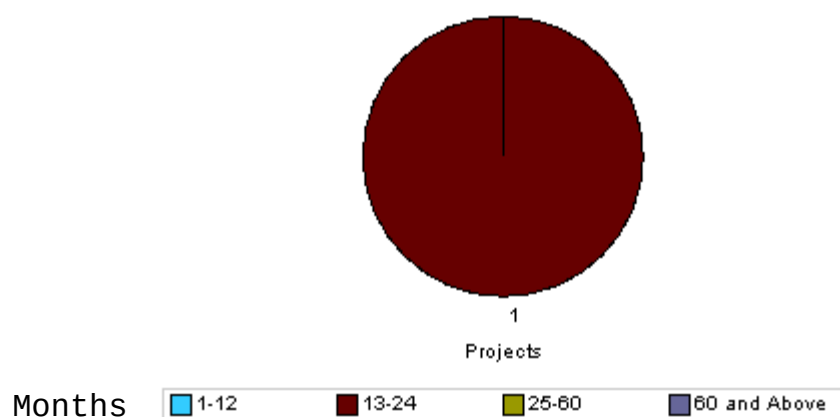


Trend and Graphical Analysis


Telecommunications Sector

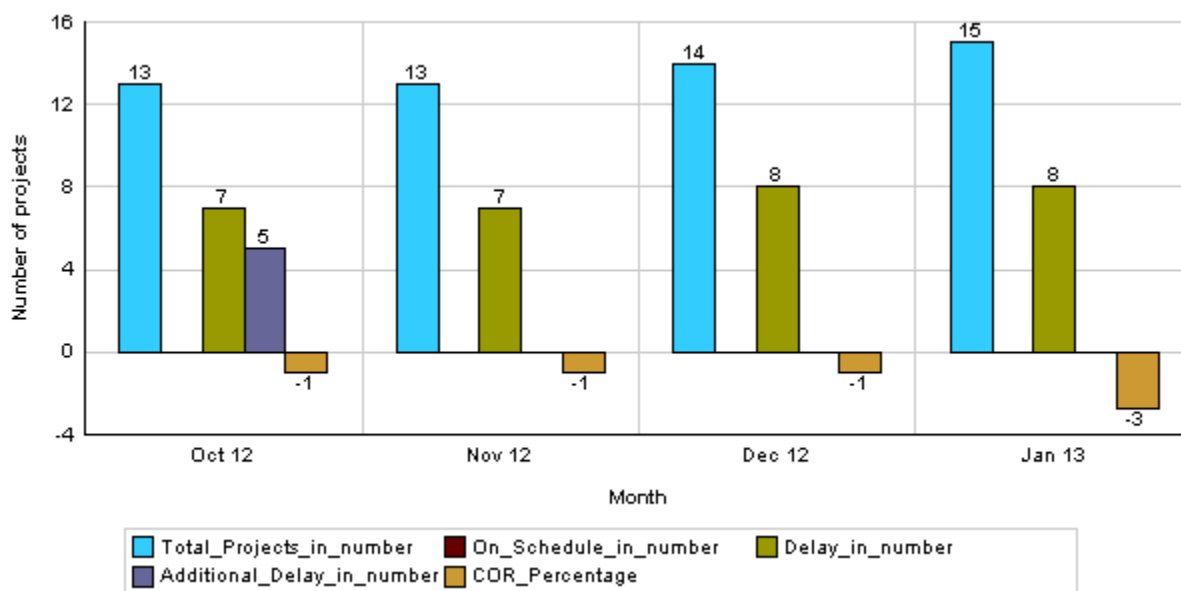


Telecommunications Sector Break-up of 8 Delayed projects in January 2013

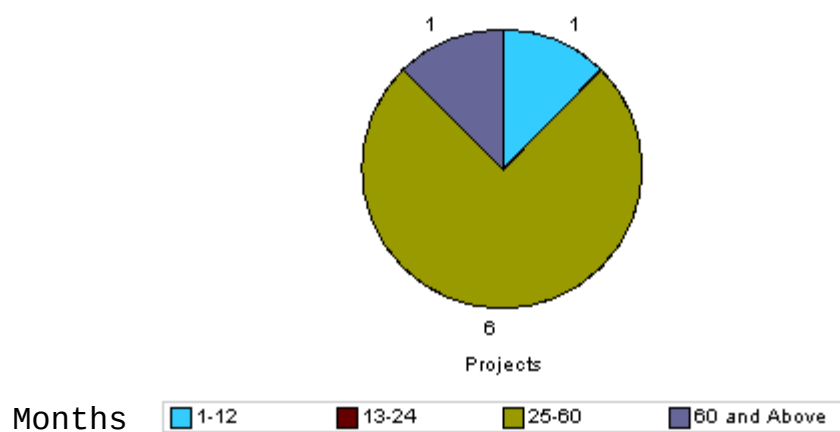


Trend and Graphical Analysis Shipping and Ports Sector

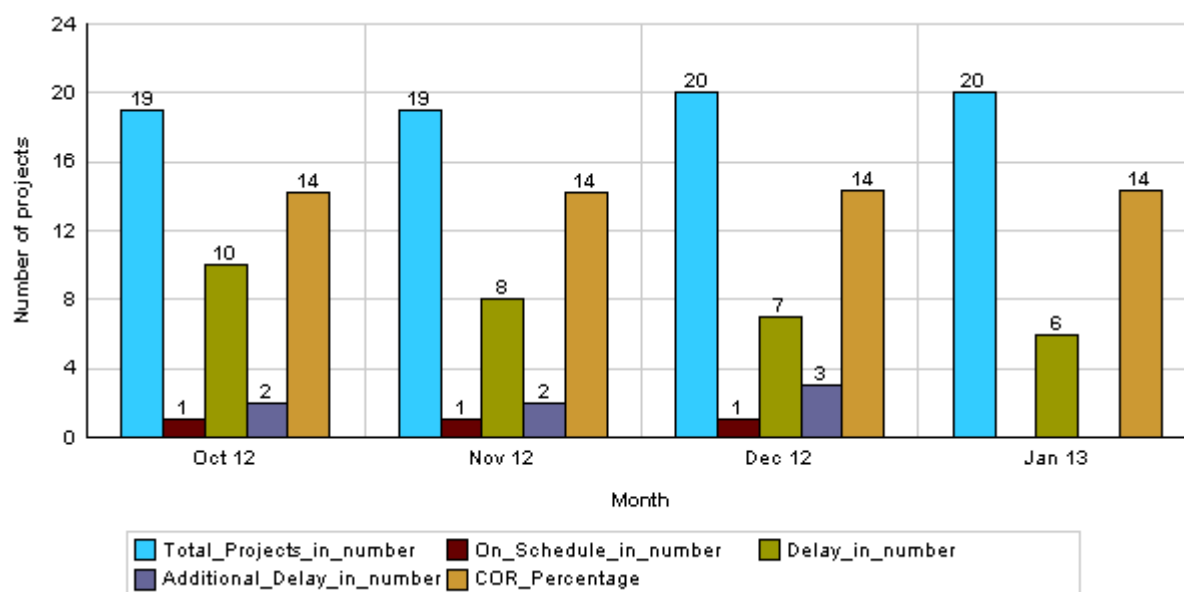


Sector Break-up of 6 Delayed projects in January 2013

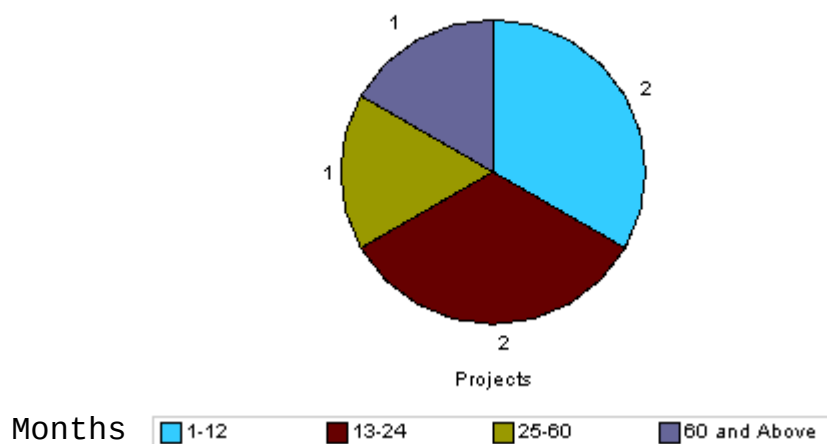

Trend and Graphical Analysis Road Transport and Highways Sector

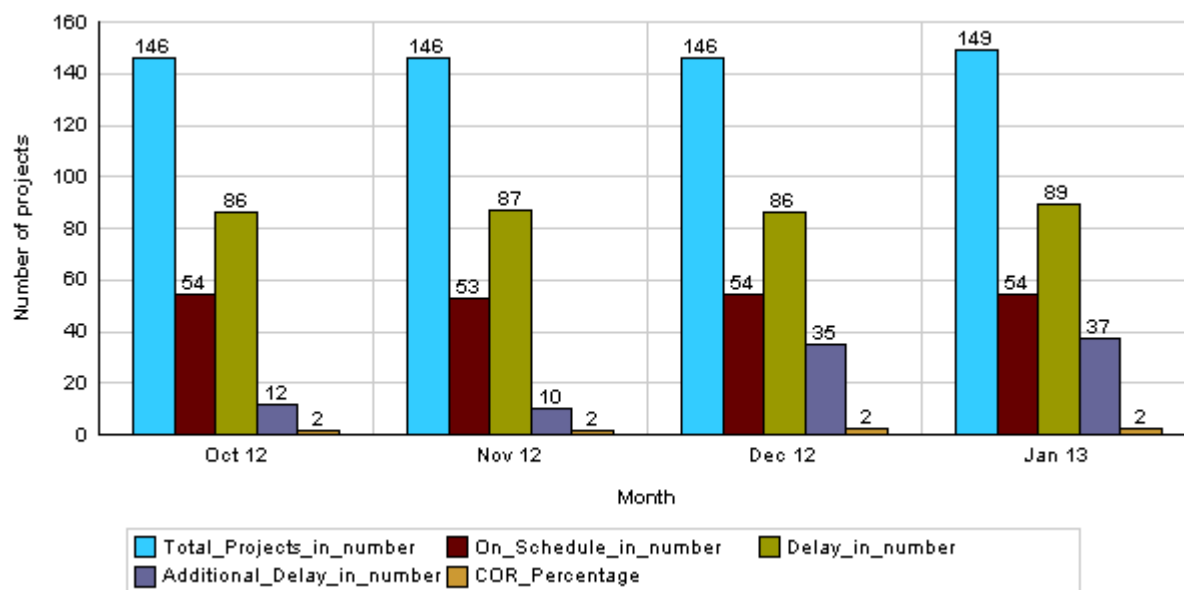


Sector Break-up of 89 Delayed projects in January 2013

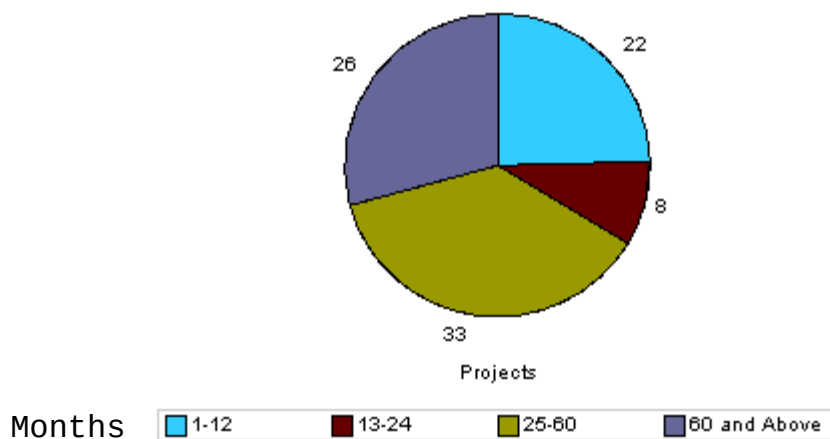


Trend and Graphical Analysis


Railways Sector

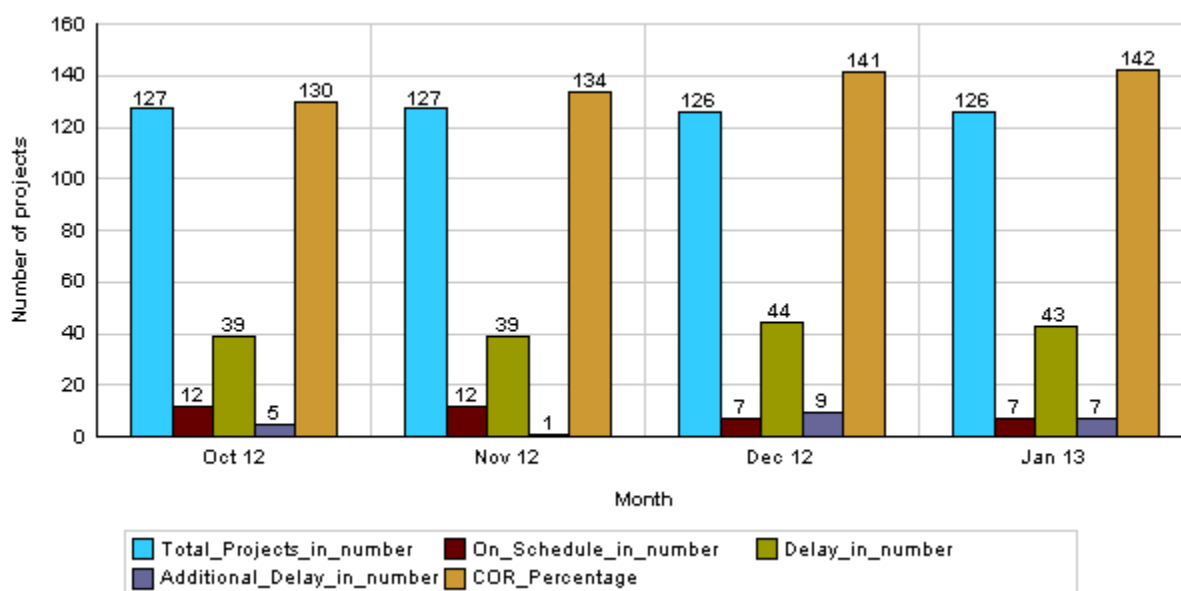


Railways Sector Sector Break-up of 43 Delayed projects in January 2013

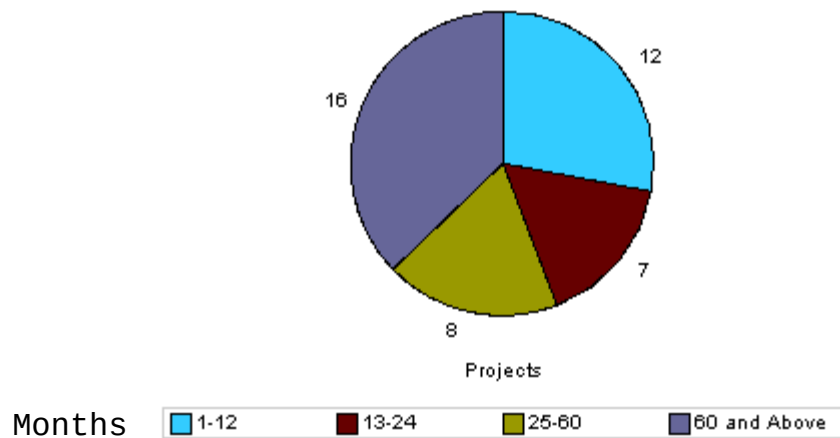

Graphical Analysis of Power Sector

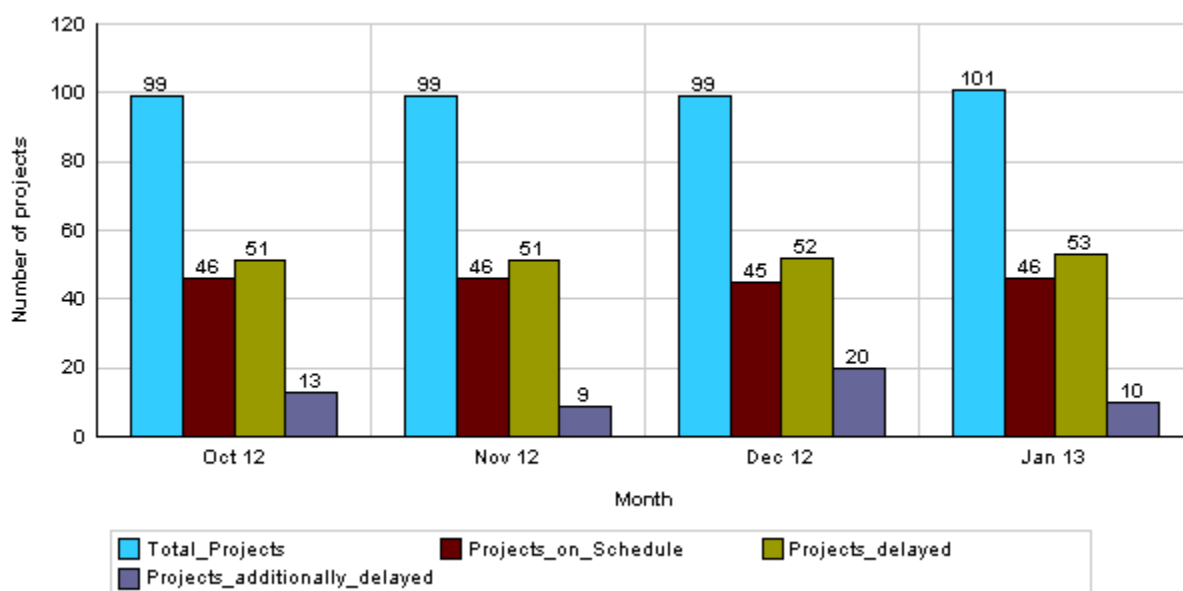


Power Sector Break-up of 53 Delayed projects in January 2013

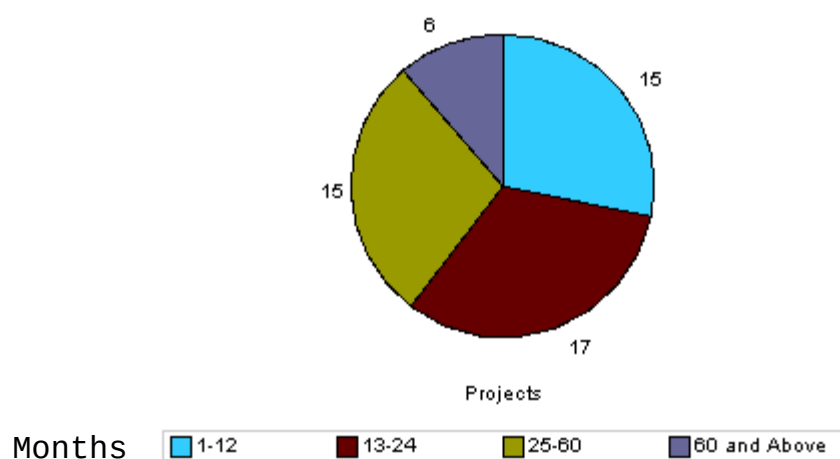


Trend and Graphical Analysis

Petroleum Sector

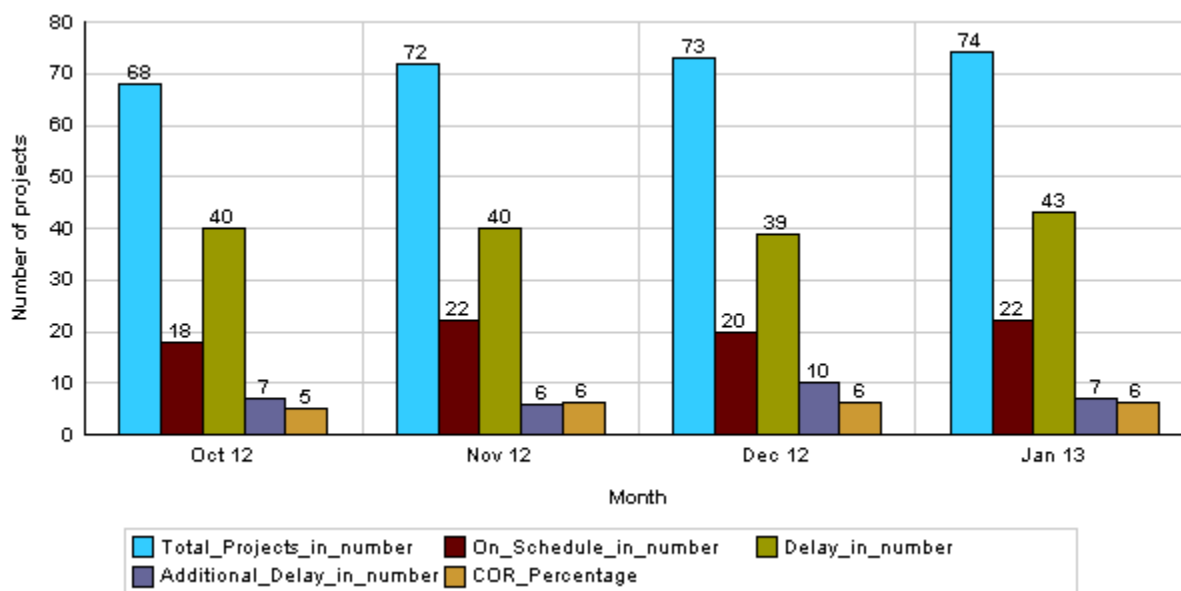


Petroleum Sector Sector Break-up of 43 Delayed projects in January 2013

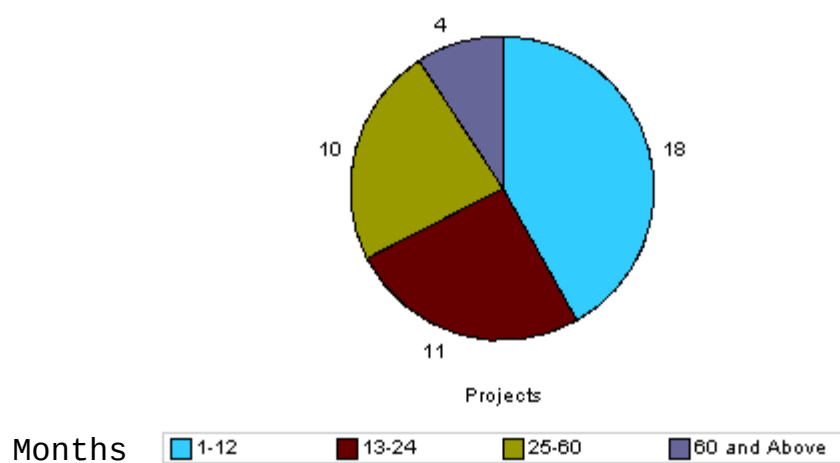


Trend and Graphical Analysis

Steel Sector

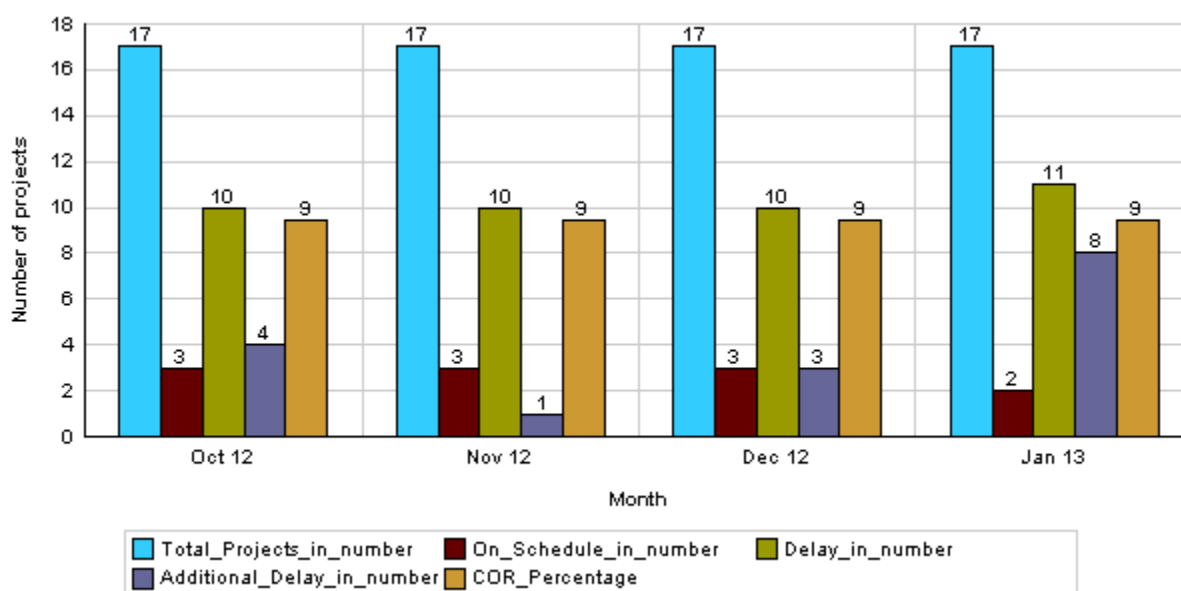


Steel Sector Break-up of 11 Delayed projects in January 2013

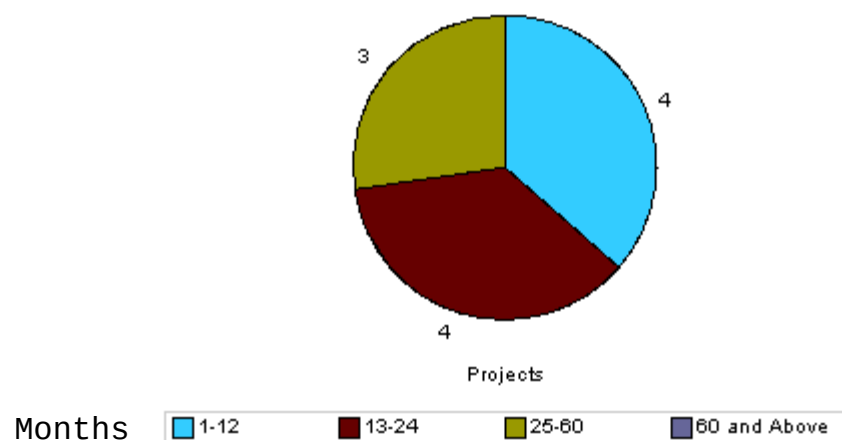


Trend and Graphical Analysis

Coal Sector

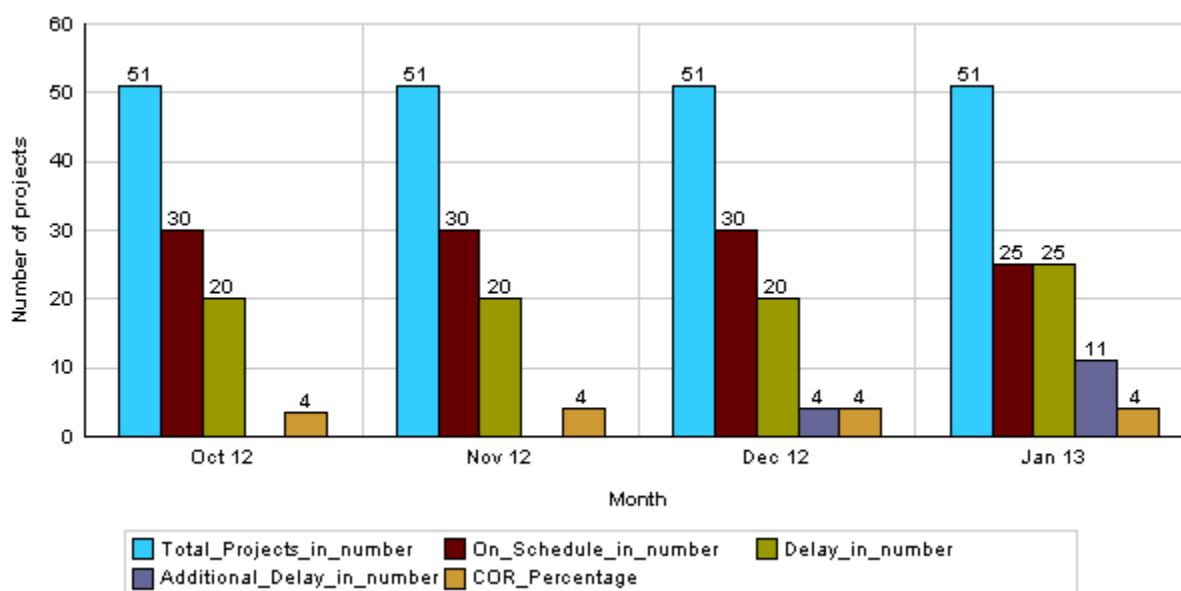


Coal Sector Sector Break-up of 25 Delayed projects in January 2013

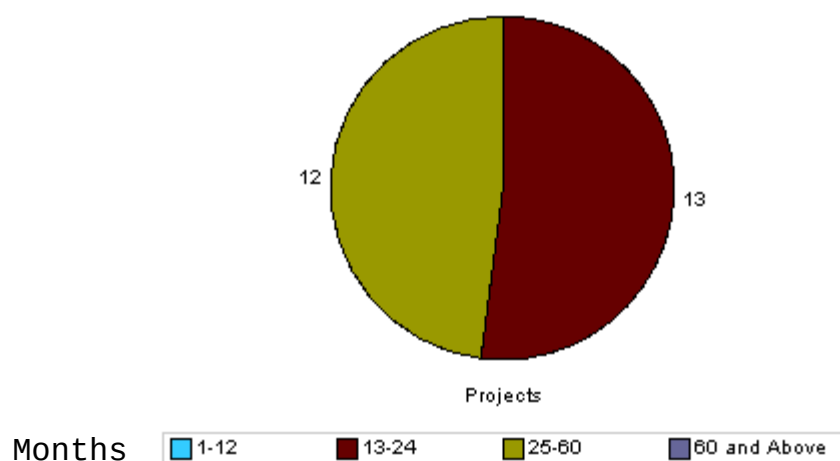


Trend and Graphical Analysis

Civil Aviation Sector

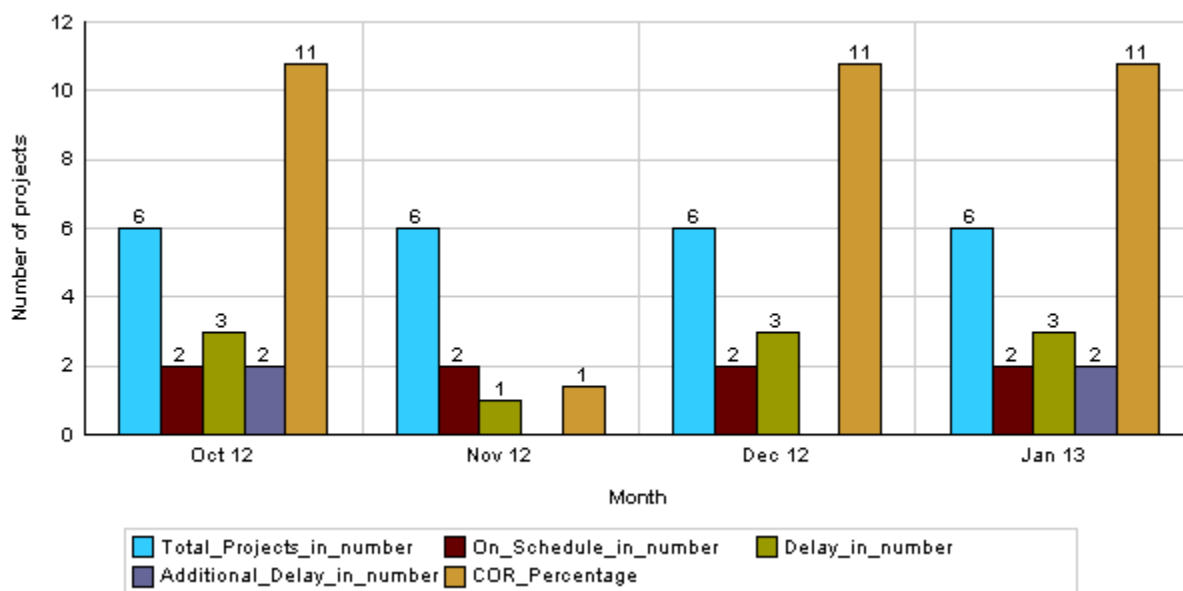


Civil Aviation Sector Break-up of 3 Delayed projects in January 2013

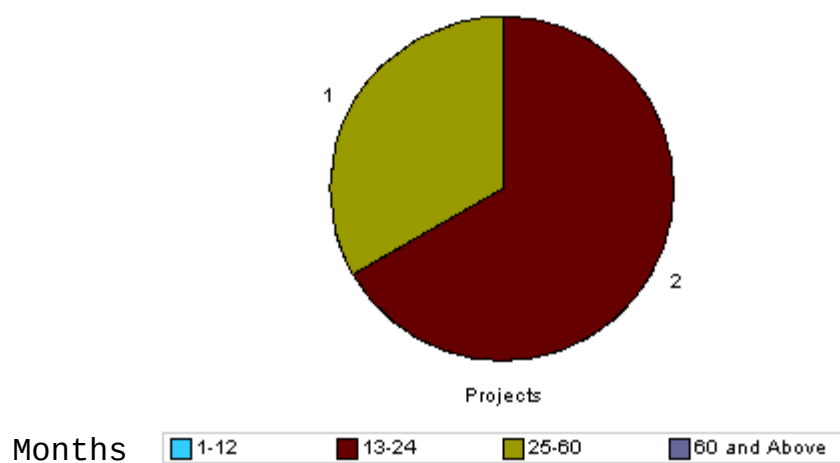


Trend and Graphical Analysis

Atomic Energy Sector

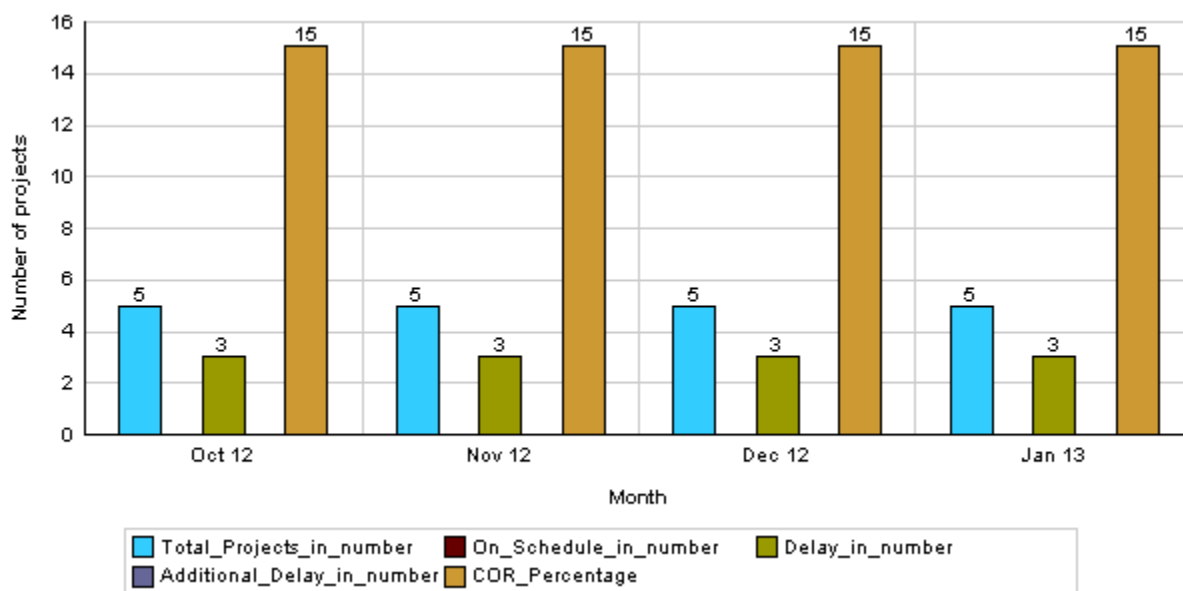

Atomic Energy Sector Break-up of 3 Delayed projects in January 2013

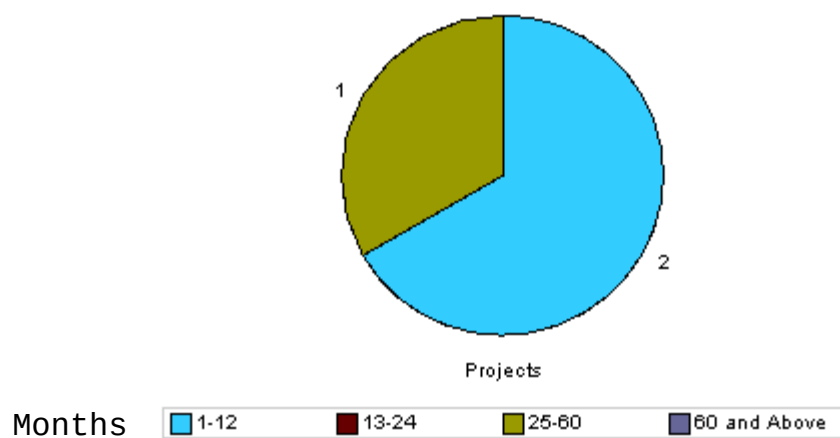

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	24,323.57
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,833.48
Coal	51	36,056.46	37,022.46	37,510.52	13,622.25
Fertilisers	1	1,478.63	1,478.63	1,478.63	1,064.53
Steel	17	65,285.87	67,562.15	71,443.41	46,958.93
Petrochemicals	1	5,460.61	8,920.00	8,920.00	6,077.01
Petroleum	74	177,600.55	193,120.42	188,903.21	84,299.81
Power	101	239,851.89	243,658.99	255,682.13	112,805.94
Railways	126	61,373.80	91,434.05	148,389.93	61,928.21
Road Transport & Highways	149	97,021.84	97,188.34	98,960.46	70,848.16
Shipping & Ports	20	15,907.97	17,661.93	18,174.92	8,239.52
Telecommunications	15	7,113.08	7,113.08	6,920.16	1,688.15
Urban Development	4	44,245.18	44,304.08	49,518.08	3,949.03
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	571	798,960.65	857,235.90	940,983.81	440,674.08

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/R evised (in months)	Milestone s Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,335.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,373.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,960.33	09/2010	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,571.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011	-	-	0/0
Total			41,548.29	47,832.29	24,323.57				47/327
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,259.45	05/2011	03/2013	22(O)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	207.52	01/2011	12/2013	35(O)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	183.67	04/2013	06/2013	8(R)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	2,015.00	1,749.61	05/2012	02/2012	13(O)	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	452.00	56.26	02/2012	03/2015	-	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	376.97	03/2015	03/2015	0(O)	0/0
Total			5,473.58	6,063.07	4,833.48	06/2013	06/2013	0(O)	0/0
<u>Coal</u>									
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34	977.53	421.73	03/2013	07/2014	16(O)	7/22
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	779.26	198.59	94.86	09/2012	03/2016	22(R)	2/6
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	150.59	1,143.54	405.07	03/2016	03/2016	0(O)	2/4
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	1,352.04	207.28	100.37	03/2016	03/2014	0(R)	5/9
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	207.28	341.63	143.73	03/2012	03/2014	24(O)	0/4
			471.66			-		36(O)	
			341.63					-	

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08	172.08	119.20	03/2010	03/2015	60(O)	4/5
18	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	258.56	39.95	03/2016	03/2016	0(O)	0/1
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00	490.10	119.73	03/2017	03/2017	0(O)	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.86	03/2014	03/2014	0(O)	1/4
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04	535.10	165.54	03/2015	03/2015	0(O)	0/3
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	1/2
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	264.84	03/2014	03/2014	0(O)	2/7
24	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.71	03/2011	03/2016	60(O)	0/2
25	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66	1,943.66	1,258.59	03/2014	03/2016	24(O)	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67	2,675.67	1,404.76	03/2014	03/2016	24(O)	10/15
27	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87	395.87	71.92	03/2015	03/2015	0(O)	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63	479.63	116.35	03/2013	03/2013	0(O)	5/10
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24(O)	1/7
30	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	3.02	03/2015	03/2015	0(O)	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78	467.78	12.31	03/2013	03/2013	0(O)	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.82	03/2011	03/2015	48(O)	0/2
33	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63	453.63	81.40	12/2012	03/2016	39(O)	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77	457.77	114.85	03/2013	03/2013	0(O)	6/11
35	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46	162.46	34.89	03/2014	03/2014	0(O)	0/3
36	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24(O)	1/7
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	3.87	03/2018	03/2018	0(O)	0/3
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88	741.62	342.83	03/2013	03/2013	0(O)	2/5
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96	302.96	108.96	03/2010	03/2014	48(O)	7/10
40	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31	1,188.31	691.64	03/2013	03/2013	0(O)	0/9
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78	706.40	19.23	07/2012	03/2016	44(O)	1/5
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42	321.50	204.97	03/2014	03/2016	24(O)	1/6
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	39.77	03/2012	03/2014	24(O)	7/20
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	25.98	12/2015	08/2017	20(O)	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	3.27	03/2012	03/2015	36(O)	0/2
49	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87	179.87	60.74	03/2012	03/2017	60(O)	0/4
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.88	03/2014	03/2016	24(O)	0/1
52	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98	210.98	91.35	03/2013	03/2015	24(O)	2/4
53	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82	153.82	24.39	03/2014	03/2016	24(O)	0/2
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	123.02	03/2012	03/2015	36(O)	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	2.48	03/2015	03/2015	0(O)	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78	209.78	30.19	03/2015	03/2015	0(O)	4/31
57	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85	510.85	269.00	03/2016	03/2016	0(O)	1/4
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	49.91	03/2012	-	-	11/42
59	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72	447.72	43.29	03/2016	03/2016	0(O)	0/10
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78	3,027.59	2,580.27	06/2009	09/2013	51(O)	19/24
61	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,748.36	03/2012	03/2014	24(O)	0/39
62	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	108.35	03/2012	03/2016	48(O)	0/4
Total			36,056.46	37,510.52	13,622.25				161/661
Fertilisers									
63	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	1,064.53	01/2013	03/2013	2(O)	0/8

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			1,478.63	1,478.63	1,064.53				0/8
<u>Steel</u>									
64	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	234.32	-	04/2013	-	15/19
65	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	251.61	08/2010	02/2013	30(O)	0/1
66	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	254.28	02/2011	03/2013	25(O)	2/3
67	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	188.57	-	11/2013	-	11/21
68	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	231.16	05/2012	06/2013	13(O)	1/2
69	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	345.58	12/2011	03/2013	15(O)	16/21
70	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	136.13	10/2012	06/2013	8(O)	3/4
71	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	332.65	18.30	08/2014	08/2014	0(O)	0/0
72	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55	254.55	14.78	11/2013	03/2014	4(O)	1/1
73	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	7,638.68	03/2013	03/2014	12(O)	22/27
74	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00	6,325.00	3,244.03	12/2011	06/2013	18(O)	15/16
75	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00	2,875.00	1,364.11	12/2012	12/2013	12(O)	10/12
76	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	14,219.38	12/2011	06/2013	18(O)	19/19
77	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	10,103.53	10/2009	03/2013	41(O)	62/64
78	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00	11,812.00	8,691.36	11/2013	09/2013	-2(O)	9/14
79	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33	187.33	22.69	-	12/2013	-	0/1
80	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90	254.90	0.42	12/2014	12/2014	0(O)	0/0
Total			65,285.87	71,443.41	46,958.93				186/225
<u>Petrochemicals</u>									
81	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61	8,920.00	6,077.01	04/2012	12/2013	20(O)	19/29
Total			5,460.61	8,920.00	6,077.01				19/29
<u>Petroleum</u>									

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
82	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	678.02	-	06/2012	03/2014	21(O)	0/0
83	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	2,163.64	1,147.97	06/2012	06/2013	12(O)	0/0
84	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	271.67	04/2011	02/2013	22(O)	0/0
85	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	658.19	12/2011	07/2013	19(O)	0/0
86	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	1,244.96	03/2013	03/2014	12(O)	0/0
87	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00	586.00	4.28	07/2015	07/2015	0(O)	0/0
88	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	711.28	12/2014	12/2014	0(O)	0/0
89	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014	12/2014	0(O)	0/0
90	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	204.96	07/2012 07/2012	-	-	0/17
91	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	149.24	02/2013	03/2013	1(O)	38/42
92	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00	190.00	25.91	03/2014	03/2014	0(O)	0/24
93	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	228.26	-	10/2012	-	36/36
94	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	715.73	04/2011	02/2013	22(O)	2/2
95	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	344.83	09/2011	12/2013	27(O)	0/0
96	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,585.41	05/2010 05/2012	01/2013	32(O) 8(R)	0/0
97	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	379.22	-	-	-	21/22
98	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	756.65	84.94	05/2013	11/2013	6(O)	0/0
99	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89	152.89	-	06/2013	06/2013	0(O)	0/0
100	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	27.13	08/2013	01/2014	5(O)	0/0
101	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	240.95	65.20	09/2012	09/2013	12(O)	0/0
102	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
103	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	223.48	09/2012	-	-	0/0
104	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	1,709.62	03/2012	02/2013	11(O)	0/21
105	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00	486.00	35.11	09/2013	09/2013	0(O)	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
106	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	215.51	- -	-	-	0/0
107	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86(O) 12(R)	0/0
108	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,136.61	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
109	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
110	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
111	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
112	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,280.22	09/2011 05/2012	06/2013	21(O) 13(R)	0/76
113	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,488.99	09/2011 03/2012	03/2013	18(O) 12(R)	0/0
114	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	143.95	03/2013 -	04/2013	1(O) -	0/0
115	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
116	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	841.62	03/2013 -	04/2014	13(O) -	0/0
117	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	94.39	11/2012 -	10/2013	11(O) -	0/0
118	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	486.20	01/2014 -	01/2014	0(O) -	0/0
119	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
120	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,981.03	- -	01/2013	-	116/116
121	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	373.62	01/2013 -	08/2013	7(O) -	18/18
122	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	-	04/2013 -	04/2013	0(O) -	0/167
123	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	32.66	05/2015 -	05/2015	0(O) -	0/0
124	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Odisha	12/2009	1,492.33 -	1,492.33	1,219.12	06/2012 -	03/2013	9(O) -	8/8
125	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
126	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
127	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	03/2014	0(O) -	0/0
128	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
129	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015	0(O) -	0/0
130	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	2,059.63	51.17	03/2015 -	03/2015	0(O) -	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	7,596.18	2.54	01/2013 -	07/2015	30(O) -	0/0
132	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	-	10/2010 -	12/2014	50(O) -	0/0
133	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 312.00	312.00	276.60	01/2012 01/2012	01/2013	12(O) 12(R)	0/1
134	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	2,915.00	765.59	12/2012 -	05/2014	17(O) -	0/21
135	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL, Karnataka	11/2012	666.00 -	666.00	-	11/2015 -	11/2015	0(O) -	0/0
136	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 -	12,160.26	8,727.48	01/2012 -	03/2013	14(O) -	0/108
137	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	4,524.89	09/2012 -	09/2013	12(O) -	0/0
138	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,154.22	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
139	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00 -	3,823.00	701.82	04/2015 -	04/2015	0(O) -	0/0
140	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
141	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	612.76	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
142	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL, Multi State	02/2011	913.00 -	913.00	21.84	07/2015 -	07/2015	0(O) -	0/0
143	PARADIP REFINERY PROJECT - [N16000058]IOCL, Odisha	02/2009	29,777.00 -	30,426.00	20,012.00	11/2012 -	11/2013	12(O) -	60/100
144	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, Multi State	08/2009	1,793.00 -	1,793.00	-	09/2012 -	-	- -	0/11
145	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00 -	8,140.00	1,701.79	02/2014 -	02/2014	0(O) -	0/0
146	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL, Maharashtra	08/2009	246.81 -	246.81	-	04/2012 -	-	- -	0/0
147	Pipeline Replacement Project-3 - [N16000137]ONGC, Multi State	04/2012	2,547.26 -	1,417.00	105.57	05/2014 -	05/2014	0(O) -	0/0
148	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	566.69	07/2012 -	10/2013	15(O) -	0/31
149	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 898.00	898.00	913.94	- -	-	- -	51/53
150	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL, Multi State	02/2012	1,210.64 -	1,210.64	39.62	11/2015 -	11/2015	0(O) -	1/25
151	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL, Maharashtra	01/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014	0(O) -	0/0
152	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin, Karnataka	07/2010	1,043.57 -	1,043.57	1,024.65	04/2012 -	01/2013	9(O) -	0/0
153	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	253.66	165.66	08/2012 -	05/2013	9(O) -	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
154	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	199.91	03/2012 -	03/2013	12(O) -	13/20
155	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	-	12/2013 -	12/2013	0(O) -	0/0
Total			177,600.55 -	188,903.21	84,299.81				379/934
<u>Power</u>									
156	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,563.20	08/2012 -	01/2014	17(O) -	0/11
157	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,161.90	02/2012 -	03/2013	13(O) -	0/7
158	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	718.60	05/2012 -	06/2013	13(O) -	0/11
159	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,108.30	06/2012 -	03/2013	9(O) -	0/4
160	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/0
161	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,975.00	08/2013 -	09/2014	13(O) -	7/19
162	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,806.00	12/2009 -	02/2017	86(O) -	26/47
163	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,525.00	07/2011 -	10/2015	51(O) -	4/28
164	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	913.00	775.32	02/2011 10/2012	01/2013	23(O) 3(R)	2/4
165	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	447.60	08/2014 -	08/2014	0(O) -	0/20
166	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	33.70	06/2014 -	06/2014	0(O) -	0/20
167	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	-	10/2014 -	10/2014	0(O) -	0/0
168	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	552.20	09/2014 -	09/2014	0(O) -	8/19
169	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	870.70	10/2009 -	06/2013	44(O) -	20/20
170	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	519.10	11/2012 -	03/2014	16(O) -	3/11
171	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
172	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	579.80	05/2014 -	05/2014	0(O) -	0/16

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
173	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	813.70	08/2013 -	08/2013	0(O) -	0/14
174	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	117.80	08/2014 -	08/2014	0(O) -	0/21
175	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	697.50	12/2013 -	12/2013	0(O) -	0/13
176	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	58.80	10/2012 -	03/2013	5(O) -	5/14
177	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [N180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	871.03	12/2007 12/2009	-	-	0/10
178	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [N180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	2,496.90	2,148.54	05/2013 06/2016	03/2017	46(O) 9(R)	6/22
179	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,012.53	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
180	KOLDAM HEP (NTPC) - [N180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	4,735.00	04/2009 -	09/2014	65(O) -	0/9
181	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,217.00	12/2016 -	12/2016	0(O) -	5/5
182	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [N180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,844.91	09/2008 -	03/2013	54(O) -	17/37
183	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	722.00	05/2017 -	05/2017	0(O) -	0/2
185	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,733.00	08/2012 -	03/2013	7(O) -	11/16
186	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	661.00	09/2016 -	09/2016	0(O) -	12/13
187	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	823.90	08/2010 01/2013	06/2013	34(O) 5(R)	0/3
188	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,430.70	08/2013 -	09/2014	13(O) -	0/17
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	251.00	02/2012 -	12/2013	22(O) -	0/14
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	337.80	11/2011 -	12/2013	25(O) -	0/11
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	348.20	11/2011 -	12/2013	25(O) -	0/14
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	46.20	01/2013 -	06/2013	5(O) -	0/7
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	233.80	07/2013 -	07/2013	0(O) -	0/12
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	686.00	04/2013 -	03/2014	11(O) -	0/12
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	110.60	08/2013 -	08/2013	0(O) -	0/16
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	67.90	11/2014 -	11/2014	0(O) -	0/0
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	14.90	04/2015 -	05/2015	1(O) -	0/0
199	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	511.10	11/2012 -	12/2013	13(O) -	0/10
200	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,011.21	10/2010 01/2013	09/2013	35(O) 8(R)	0/6
201	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,735.11	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
202	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	573.99	410.24	08/2012 08/2013	09/2014	25(O) 13(R)	16/22
203	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,180.90	01/2012 -	02/2014	25(O) -	0/27
204	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,909.00	10/2012 -	11/2013	13(O) -	11/16
205	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,137.00	11/2016 -	11/2016	0(O) -	0/13
206	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	5,897.12	09/2010 08/2014	03/2017	78(O) 31(R)	11/11
207	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	68.50	04/2013 -	04/2013	0(O) -	0/15
208	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	2,005.70	08/2012 -	12/2013	16(O) -	0/7
209	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016	0(O) -	0/0
210	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014	0(O) -	0/0
211	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/0
212	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	65.60	08/2014 -	08/2014	0(O) -	0/20
213	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	162.20	02/2015 -	02/2015	0(O) -	0/0
214	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	183.60	11/2014 -	11/2014	0(O) -	0/0
215	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	159.40	01/2015 -	01/2015	0(O) -	0/19
216	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	46.40	08/2014 -	08/2014	0(O) -	0/20
217	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	85.30	06/2014 -	06/2014	0(O) -	0/19
218	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	169.80	04/2012 -	03/2013	11(O) -	0/0
219	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	132.88	06/2012 -	03/2013	9(O) -	0/9
220	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	823.00	08/2012 -	03/2014	19(O) -	0/11

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48	2,978.48	1,670.00	03/2013	09/2015	30(O)	2/15
222	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,270.70	09/2009 06/2013	03/2014	54(O) 9(R)	0/0
223	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,649.72	03/2007 09/2012	02/2013	71(O) 5(R)	25/25
224	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	440.48	07/2010 02/2016	11/2016	76(O) 9(R)	1/10
225	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	52.90	01/2014	01/2014	0(O)	0/17
226	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	145.50	08/2014	08/2014	0(O)	0/0
227	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - [N18000129]PGCIL,Multi State	02/2012	3,201.44	3,201.44	226.90	10/2014	10/2014	0(O)	0/21
228	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	335.93	07/2011	03/2013	20(O)	0/5
229	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	3,213.20	10/2012	12/2013	14(O)	0/12
230	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	338.20	01/2015	01/2015	0(O)	0/20
231	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	1,082.80	03/2014	03/2014	0(O)	0/15
232	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	717.80	08/2013	08/2013	0(O)	0/14
233	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33	324.33	2.40	08/2014	08/2014	0(O)	0/20
234	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16	1,927.16	63.90	10/2014	10/2014	0(O)	0/20
235	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24	758.75	596.30	01/2010	03/2013	38(O)	0/22
236	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	155.80	11/2011	09/2013	22(O)	0/7
237	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	4,221.80	12/2012	06/2013	6(O)	0/11
238	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44	552.44	142.70	02/2014	02/2014	0(O)	0/20
239	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51	425.51	200.70	10/2013	10/2013	0(O)	0/18
240	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	65.40	07/2013	07/2013	0(O)	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
241	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34	1,366.34	386.20	12/2013	12/2013	0(O)	0/18
242	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26	558.26	93.30	11/2013	11/2013	0(O)	0/20
243	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86	2,074.86	827.20	03/2013	06/2013	3(O)	0/14
244	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19	2,743.19	1,187.50	12/2013	12/2013	0(O)	0/13
245	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	2,011.20	11/2012	03/2014	16(O)	0/15
246	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51	2,127.51	402.20	07/2014	07/2014	0(O)	0/19
247	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	428.37	-	07/2013	-	6/29
248	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63	913.63	378.42	07/2014	02/2015	7(O)	0/16
249	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	1,128.20	12/2012	12/2013	12(O)	0/11
250	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	673.30	11/2013	11/2013	0(O)	0/15
251	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	60.30	01/2013	11/2013	10(O)	0/16
252	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29	2,081.00	1,880.57	11/2009	03/2013	40(O)	0/4
253	VINDHYACHAL STTP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40	3,180.40	154.00	08/2015	08/2015	0(O)	5/5
254	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	4,145.00	10/2012	03/2013	5(O)	11/15
255	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58	3,422.44	335.86	07/2014	05/2016	22(O)	1/1
256	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	426.00	09/2010	03/2013	30(O)	0/9
257	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76	9,569.76	380.90	06/2015	06/2015	0(O)	0/24
Total			239,851.89	255,682.13	112,805.94				216/1324
Railways									
258	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.75	448.95	03/2014	12/2015	21(O)	0/0
259	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00	432.72	366.38	12/2009	10/2013	46(O)	0/0
260	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08	2,820.00	224.48	-	03/2013	-	0/0
261	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00	453.04	396.44	03/2011	03/2011	-	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
262	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	541.95	06/1999 03/2011	03/2011	-	0/0
263	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
264	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	404.39	15.67	03/2013 -	03/2013	0(O) -	0/0
265	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.29	- -	-	-	0/0
266	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	463.65	03/2005 12/2008	06/2016	135(O) 90(R)	0/0
267	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	213.77	12/2010 03/2011	03/2011	-	0/0
268	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	202.80	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
269	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	32.05	04/2014 -	03/2017	35(O) -	0/0
270	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20 -	687.20	682.45	03/2010 -	-	-	0/0
271	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	350.00	330.65	- 03/2009	-	-	0/0
272	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	5,016.00	2,623.90	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
273	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	156.35	12/2012 -	12/2013	12(O) -	0/0
274	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	194.27	03/2011 -	-	-	0/0
275	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.52	03/2012 -	-	-	0/0
276	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
277	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	933.54	12/2012 01/2013	02/2013	2(O) 1(R)	0/0
278	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
279	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya Pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
280	CHURCHGATE-VIRAR.CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
281	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	287.63	- -	06/2013	-	0/0
282	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	118.37	12/2012 -	-	-	0/0
283	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	88.88	- -	-	-	0/0
284	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	209.11	- -	03/2013	-	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
285	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	460.04	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
286	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	577.76	- -	12/2012	-	0/0
287	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	94.30	12/2011 02/2012	02/2012	-	0/0
288	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
289	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
290	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	204.65	12/2008 -	09/2014	69(O) -	0/0
291	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	169.13	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
292	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
293	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	266.03	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
294	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013	94(O) -	0/0
295	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	623.58	- -	03/2012	-	0/0
296	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
297	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	484.97	- 05/2009	05/2009	-	0/0
298	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	548.65	03/1994 -	10/2013	235(O) -	0/0
299	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	119.46	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
300	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	183.55	- -	-	-	0/0
301	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 1,185.64	735.10	222.32	- 09/2009	-	-	0/0
302	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
303	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	573.49	- -	01/2013	- -	0/0
304	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	143.26	- -	03/2014	- -	0/0
305	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	176.52	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
306	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	71.41	- -	-	-	0/0
307	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	13.85	03/2015 -	03/2015	0(O) -	0/0
308	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	835.70	06/2007 -	06/2007	-	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
309	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	694.57	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
310	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	697.50	432.22	03/2012 03/2012	12/2012	-	0/0
311	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,155.87	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
312	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	224.26	03/2014 -	03/2014	0(O) -	0/0
313	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	269.64	03/2012 03/2012	03/2013	12(O) 12(R)	0/0
314	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,708.41	1,399.73	- -	03/2013	- -	0/0
315	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	504.45	- -	03/2014	- -	1/1
316	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	756.42	- -	10/2012	-	0/0
317	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	736.40	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
318	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	102.37	- -	03/2013	- -	0/0
319	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	225.00	235.15	03/2009 03/2009	03/2014	60(O) 60(R)	0/0
320	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	235.15	- -	03/2014	- -	0/0
321	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
322	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	446.13	- 03/2010	03/2010	-	0/0
323	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,369.97	07/2005 -	-	-	0/0
324	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	131.25	- -	-	-	0/0
325	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	282.26	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
326	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
327	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	344.29	- -	12/2012	-	0/0
328	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	116.33	12/2012 -	03/2015	27(O) -	0/0
329	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	349.77	05/2008 03/2011	03/2011	-	0/0
330	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	211.19	03/2002 -	03/2013	132(O) -	0/0
331	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,316.95	03/2009 -	12/2014	69(O) -	0/0
332	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
333	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.44	- -	02/2013	- -	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
334	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	650.85	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
335	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
336	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	408.83	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
337	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDY'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	295.24	- -	-	-	0/0
338	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	1,008.73	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
339	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	148.03	- -	03/2012	-	0/0
340	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	635.20	02/2009 -	03/2012	-	0/0
341	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	353.41	07/2012 -	-	-	0/0
342	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
343	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	122.83	- -	03/2016	-	0/0
344	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,336.31	12/2008 -	03/2014	63(O) -	0/0
345	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	247.74	- -	03/2015	-	0/0
346	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24(O) -	0/0
347	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	222.22	03/2016 -	03/2016	0(O) -	0/0
348	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	44.12	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
349	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	57.91	03/2016 -	03/2016	0(O) -	0/0
350	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	33.08	03/2016 -	06/2016	3(O) -	0/0
351	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	429.24	03/2008 06/2008	-	-	0/0
352	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	355.00	378.12	03/2009 11/2012	-	-	0/0
353	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	246.13	02/2010 11/2012	12/2015	70(O) 37(R)	0/0
354	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,636.65	10/2007 12/2012	12/2012	-	0/0
355	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	597.99	- -	03/2012	-	0/0
356	Pandabeswar-Chinai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	133.95	12/2010 12/2010	12/2010	-	0/0
357	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	785.32	- -	03/2013	-	0/6

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
358	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	243.30	12/2007 03/2010	12/2010	-	0/0
359	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	917.84	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
360	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
361	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	226.78	- -	-	-	0/0
362	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	320.60	06/2004 -	12/2012	-	0/0
363	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,632.12	- -	03/2014	-	0/0
364	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	344.50	04/2003 03/2010	-	-	0/0
365	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	639.97	175.25	03/1998 08/2005	08/2005	-	0/0
366	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	416.24	03/2013 -	03/2014	12(O) -	0/0
367	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	152.51	03/2012 -	03/2013	12(O) -	0/0
368	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	229.47	03/2010 -	-	-	0/0
369	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.94	12/2015 -	03/2020	51(O) -	0/0
370	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	76.45	02/2015 -	-	-	0/0
371	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	324.23	03/2014 -	03/2014	0(O) -	0/0
372	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	139.61	- -	03/2013	-	0/0
373	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	433.89	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
374	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	577.90	- 12/2009	02/2012	-	0/0
375	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	141.39	- -	-	-	0/0
376	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	40.36	- -	-	-	0/0
377	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	527.63	- -	-	-	0/0
378	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,249.42	12/2006 08/2010	08/2010	-	0/0
379	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	64.23	03/2012 -	02/2013	11(O) -	0/0
380	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,549.43	03/2001 -	12/2017	201(O) -	0/0
381	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	194.44	03/2010 03/2017	06/2014	51(O) -33(R)	0/0
382	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	487.20	03/2014 -	03/2013	-12(O) -	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
383	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	176.44	- 03/2010	-	-	0/0
	Total		61,373.80	148,389.93	61,928.21				1/7
			-						
	<u>Road Transport & Highways</u>								
384	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	391.89	05/2013 -	03/2014	10(O) -	0/0
385	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	275.17	11/2013 -	11/2013	0(O) -	0/0
386	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	105.22	04/2014 -	04/2014	0(O) -	0/0
387	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
388	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	44.34	01/2014 -	01/2014	0(O) -	0/0
389	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	275.35	02/2014 -	02/2014	0(O) -	0/0
390	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	320.95	02/2014 -	04/2014	2(O) -	0/0
391	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	45.59	04/2014 -	04/2014	0(O) -	0/0
392	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	160.02	05/2014 -	05/2014	0(O) -	0/0
393	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,150.90	08/2014 -	08/2014	0(O) -	0/0
394	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,115.60	06/2013 -	06/2013	0(O) -	0/0
395	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	34.97	09/2013 -	07/2014	10(O) -	0/0
396	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	678.92	08/2013 -	08/2013	0(O) -	0/0
397	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	480.66	07/2013 -	07/2013	0(O) -	0/0
398	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	398.00	305.59	02/2014 -	02/2014	0(O) -	0/0
399	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	640.19	08/2013 -	08/2013	0(O) -	0/0
400	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	859.60	08/2013 -	08/2013	0(O) -	0/0
401	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	218.49	08/2013 -	08/2013	0(O) -	0/0
402	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	1,396.18	529.67	09/2014 -	09/2014	0(O) -	0/0
403	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	199.82	09/2007 -	03/2014	78(O) -	0/0
404	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	02/2013	95(O) -	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
405	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,250.80	11/2012	06/2013	7(O)	0/0
406	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	298.66	11/2008	03/2013	52(O)	0/0
407	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	260.71	01/2009	12/2013	59(O)	0/0
408	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	02/2013	12(O)	0/0
409	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70	228.70	194.51	02/2004	03/2013	109(O)	0/0
410	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	1,046.00	236.09	09/2013	09/2013	0(O)	0/0
411	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00	2,388.00	760.82	06/2014	06/2014	0(O)	0/0
412	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	425.02	-	10/2013	-	2/2
413	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	209.00	3.82	01/2013	10/2013	9(O)	0/0
414	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29	500.29	449.35	08/2013	08/2013	0(O)	0/0
415	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	259.55	06/2008	03/2014	69(O)	0/0
416	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	220.64	06/2008	03/2014	69(O)	0/0
417	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	230.82	06/2005	03/2014	105(O)	0/0
418	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	240.89	04/2010	11/2014	55(O)	0/0
419	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
420	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	776.82	03/2013	03/2013	0(O)	0/0
421	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	499.70	-	12/2013	-	0/1
422	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013	0(O)	0/0
423	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	389.95	10/2011	03/2014	29(O)	0/0
424	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	727.14	10/2011	06/2013	20(O)	0/0
425	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	175.59	10/2008	01/2014	63(O)	0/0
426	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	637.97	05/2010	03/2013	34(O)	0/0
427	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00	593.00	463.70	07/2013	07/2013	0(O)	0/0
428	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.82	06/2013	06/2013	0(O)	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
429	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	434.06	-	06/2013	-	1/1
430	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	239.89	06/2008	05/2013	59(O)	0/0
431	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	193.25	05/2008	12/2013	67(O)	0/0
432	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	280.71	09/2010	12/2013	39(O)	0/0
433	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	295.04	08/2013	08/2013	0(O)	0/0
434	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	417.74	09/2008	05/2013	56(O)	0/0
435	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00	682.00	-	10/2013	03/2014	5(O)	0/0
436	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	12/2013	30(O)	0/0
437	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	137.44	09/2008	03/2013	54(O)	0/0
438	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27	263.27	272.24	02/2004	03/2013	109(O)	0/0
439	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	1,032.00	08/2013	08/2013	0(O)	0/0
440	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	223.89	04/2008	03/2014	71(O)	0/0
441	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	164.00	04/2008	03/2014	71(O)	0/0
442	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	303.02	10/2009	02/2013	40(O)	0/0
443	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	495.37	12/2009	07/2013	43(O)	0/0
444	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,675.00	09/2012	03/2013	6(O)	0/0
445	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,776.70	10/2011	06/2013	20(O)	0/0
446	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	282.68	09/2007	03/2013	66(O)	0/0
447	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	290.15	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
448	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	96.33	07/2009	05/2014	58(O)	0/0
449	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	39.52	09/2007	04/2014	79(O)	0/0
450	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00	478.00	229.47	10/2013	03/2014	5(O)	0/0
451	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	189.88	08/2004	02/2013	102(O)	0/0
452	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	187.97	08/2004 07/2010	02/2013	102(O) 31(R)	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
453	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	911.93	01/2013	06/2013	5(O)	0/0
			-			-		-	
454	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
			-			-		-	
455	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,939.30	10/2012	03/2013	5(O)	0/0
			-			-		-	
456	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	431.35	05/2013	02/2014	9(O)	0/0
			-			-		-	
457	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
			-			-		-	
458	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	267.81	559.34	02/2013	02/2013	0(O)	0/0
			-			-		-	
459	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
			-			-		-	
460	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	500.75	09/2009	06/2013	45(O)	0/0
			-			-		-	
461	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	446.54	01/2014	01/2014	0(O)	0/0
			-			-		-	
462	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	1,628.50	12/2012	03/2013	3(O)	0/0
			-			-		-	
463	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.68	10/2008	06/2013	56(O)	0/0
			-			-		-	
464	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.50	10/2008	03/2013	53(O)	0/0
			-			-		-	
465	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16	702.16	235.27	07/2014	07/2014	0(O)	0/0
			-			-		-	
466	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
			-			-		-	
467	Kishangarh-Ajmer-Beaver - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,055.70	05/2012	02/2013	9(O)	0/0
			-			-		-	
468	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	186.18	06/2010	12/2013	42(O)	0/0
			-			-		-	
469	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
			-			-		-	
470	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
			-			-		-	
471	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	105.66	11/2008	06/2014	67(O)	0/0
			-			-		-	
472	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	69.30	04/2009	12/2014	68(O)	0/0
			-			-		-	
473	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	27.54	11/2008	12/2014	73(O)	0/0
			-			-		-	
474	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	127.03	04/2009	12/2014	68(O)	0/0
			-			-		-	
475	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	03/2013	9(O)	0/0
			-			-		-	
476	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	1,269.90	06/2013	06/2013	0(O)	0/0
			-			-		-	

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
477	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00	754.00	482.60	03/2013	03/2014	12(O)	0/0
478	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	269.32	11/2013	11/2013	0(O)	0/0
479	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	296.49	06/2008	05/2013	59(O)	0/0
480	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2013	54(O)	0/0
481	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19	484.19	34.07	10/2014	10/2014	0(O)	0/0
482	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	282.11	04/2008	05/2014	73(O)	0/0
483	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	255.40	06/2008	09/2013	63(O)	0/0
484	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	276.18	06/2008	09/2013	63(O)	0/0
485	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
486	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	266.34	06/2011	04/2013	22(O)	0/2
487	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	932.27	02/2010	12/2014	58(O)	0/0
488	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
489	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	475.44	09/2013	09/2013	0(O)	0/0
490	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	393.93	03/2008	03/2013	60(O)	0/0
491	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00	1,410.00	152.77	09/2014	09/2014	0(O)	0/0
492	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	995.04	10/2014	10/2014	0(O)	0/0
493	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69	942.69	-	06/2014	06/2014	0(O)	0/0
494	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	256.85	05/2008	03/2013	58(O)	0/0
495	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00	574.00	479.47	03/2014	03/2014	0(O)	0/0
496	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	671.30	599.93	02/2013	02/2013	0(O)	0/0
497	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	1,222.60	07/2012	06/2013	11(O)	0/0
498	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	1,059.70	03/2013	03/2013	0(O)	0/0
499	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	835.00	116.75	01/2014	01/2014	0(O)	0/0
500	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,465.90	11/2011	08/2013	21(O)	0/0
501	Pune-sholapur, pkg 1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
502	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11(O)	0/0
503	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	221.77	10/2008	06/2013	56(O)	0/0
504	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91	229.91	289.80	10/2008	02/2013	52(O)	0/0
505	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00	1,479.00	-	06/2015	06/2015	0(O)	0/0
506	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	852.97	11/2013	11/2013	0(O)	0/0
507	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	248.22	10/2008	02/2013	52(O)	0/0
508	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2013	28(O)	0/0
509	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	426.52	03/2013	12/2013	9(O)	0/0
510	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
511	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	218.94	09/2007	03/2013	66(O)	0/0
512	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	189.58	07/2008	03/2013	56(O)	0/0
513	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
514	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	14.58	12/2013	12/2013	0(O)	0/0
515	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
516	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2015	31(O)	0/0
517	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
518	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	06/2013	63(O)	0/0
519	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00	241.53	156.85	04/2004	02/2013	106(O)	0/0
520	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,677.20	08/2011	02/2013	18(O)	0/0
521	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	03/2013	45(O)	0/0
522	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	03/2013	32(O)	0/0
523	TUTICORIN-PORT - [N24000217]NHAI,Multi State	04/2010	182.25	182.25	-	02/2013	02/2013	0(O)	0/0
524	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	817.78	11/2013	11/2013	0(O)	0/0
525	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
526	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	83.75	05/2013	05/2013	0(O)	0/0
			-			-		-	
527	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	180.34	-	04/2013	-	2/2
			-			-		-	
528	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	730.14	03/2014	03/2014	0(O)	0/0
			-			-		-	
529	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27	193.10	163.57	03/2008	03/2013	60(O)	0/0
			-			-		-	
530	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	37.77	11/2012	12/2013	13(O)	0/0
			-			-		-	
531	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	487.64	07/2013	06/2014	11(O)	0/0
			-			-		-	
532	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	149.40	06/2014	06/2014	0(O)	0/0
			-			-		-	
	Total		97,021.84	98,960.46	70,848.16				10/14
			-						
Shipping & Ports									
533	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011	11/2012	-	0/0
			-			-			
534	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49	220.49	98.31	01/2013	06/2013	5(O)	0/0
			-			-		-	
535	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87	511.87	107.56	03/2014	-	-	0/0
			-			-			
536	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	532.83	364.52	12/2012	10/2013	10(O) 10(R)	0/0
			532.83			12/2012			
537	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03	277.03	294.87	12/2011	10/2012	-	0/0
			280.00			10/2012			
538	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	272.50	194.14	06/2011	09/2012	-	0/0
			272.50			-			
539	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	306.12	02/2014	-	-	0/0
			-			-			
540	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	1,012.23	433.54	12/2013	10/2013	-2(O) -2(R)	0/0
			1,012.23			12/2013			
541	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	1,460.00	917.60	12/2010	10/2013	34(O) 13(R)	0/0
			1,460.00			09/2012			
542	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24(O)	0/0
			-			-		-	
543	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.93	02/2011	12/2012	-	0/0
			-			-			
544	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	1,571.60	5.75	10/2008	10/2008	-	0/0
			1,571.60			-			
545	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84	253.36	-	-	01/2009	-	0/1
			-			01/2009			

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
546	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	137.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
547	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
548	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
549	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
550	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	830.81	10/2008 11/2010	-	-	0/0
551	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,644.30	01/2012 09/2012	02/2013	13(O) 5(R)	0/0
552	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
	Total		15,907.97 -	18,174.92	8,239.52				0/1
<u>Telecommunications</u>									
552	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53(O) -	0/0
553	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	-	02/2007 12/2010	-	-	0/0
554	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	-	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
555	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	-	03/2012 -	02/2013	11(O) -	0/0
556	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 -	06/2013	32(O) -	0/0
557	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
558	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
559	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013	45(O) -	0/0
560	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	12/2012	-	0/0
561	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	818.09	11/2010 -	03/2013	28(O) -	0/0
562	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	-	-	0/0
563	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	46(O) -	0/0
564	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
565	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0

Sector Wise Details

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original/Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
566	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19	964.37	170.25	05/2011	06/2013	25(O)	0/0
			-			-		-	
	Total		7,113.08	6,920.16	1,688.15				0/0
			-						
	<u>Urban Development</u>								
567	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	06/2011	03/2013	21(O)	6/6
			-			-		-	
568	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
			173.08			-			
569	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	1,515.23	03/2016	03/2016	0(O)	0/0
			-			-		-	
570	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	166.23	09/2014	09/2014	0(O)	0/0
			-			-		-	
	Total		44,245.18	49,518.08	3,949.03				6/6
			-						
	<u>Water Resources</u>								
571	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	-	0/0
			-			-			
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			798,960.65	940,983.81	440,674.08				1025/3536

Sector wise current status of projects on the Flash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

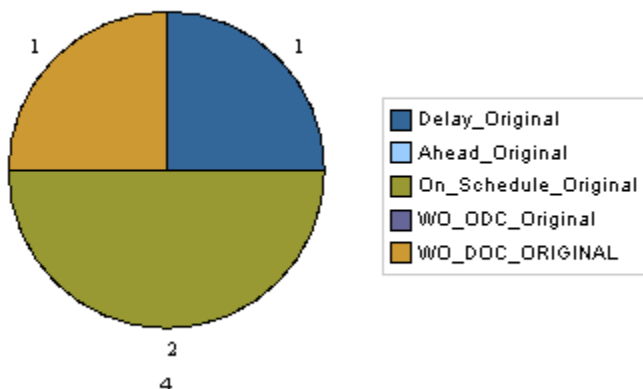

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till January, 2013 is Rs. 3949.03 crore, which is 8% of the revised cost of the projects.

Figures are in Rs. Crore

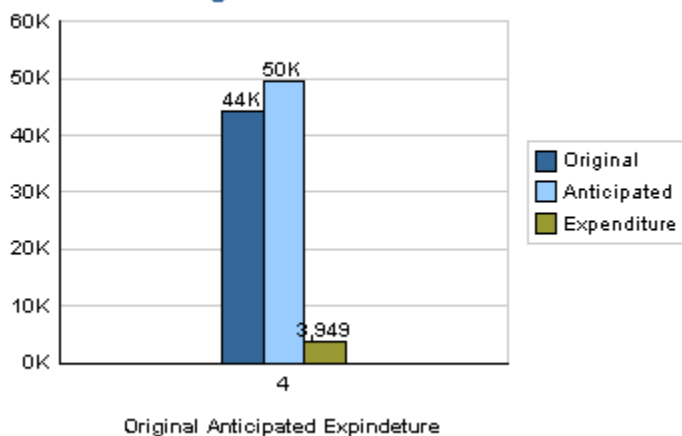

Sector wise current status of projects on the Flash Report


Telecommunications

I. Current Status:

Number of Projects	15
Number of Projects Delayed	8
Number of Projects Without Date Of Commissioning	7

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 8 projects are delayed .7 projects do not have fixed dates of commissioning.

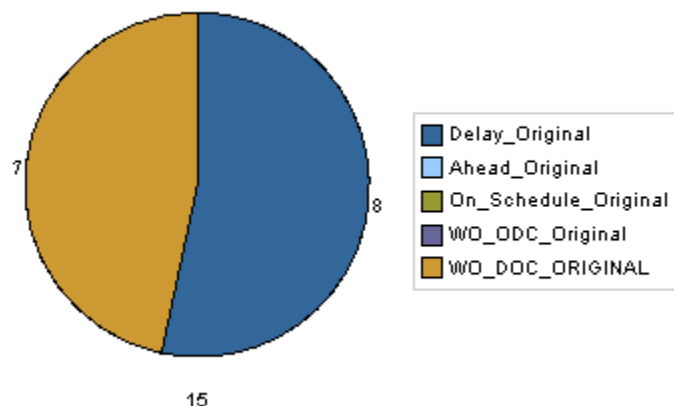

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 7113.08 crore but this was subsequently revised to Rs. 6920.16 crore implying a cost overrun of -2.7%. The expenditure incurred on these projects till January, 2013 is Rs. 1688.15 crore, which is 24.4% of the revised cost of the projects.

Figures are in Rs. Crore

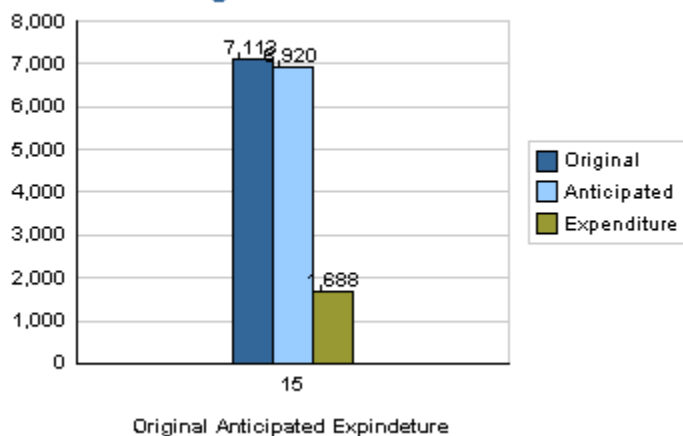

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	20
Number of Projects Delayed	6
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	12


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 2 projects are ahead of schedule, 6 projects are delayed .12 projects do not have fixed dates of commissioning.

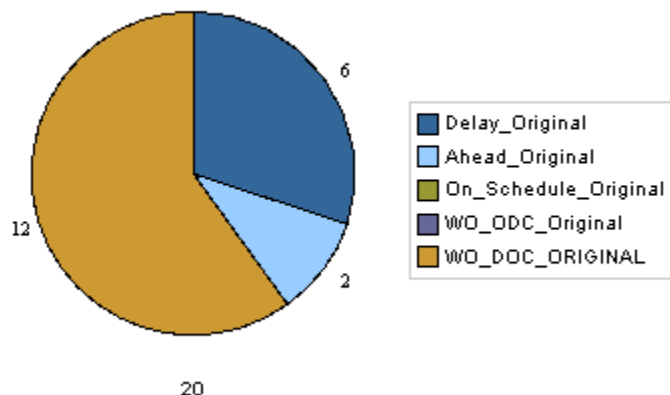

III. Investment Scenario

The Total Original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 15907.97 crore but this was subsequently revised to Rs. 18174.92 crore implying a cost overrun of 14.3%. The expenditure incurred on these projects till January, 2013 is Rs. 8239.52 crore, which is 45.3% of the revised cost of the projects.

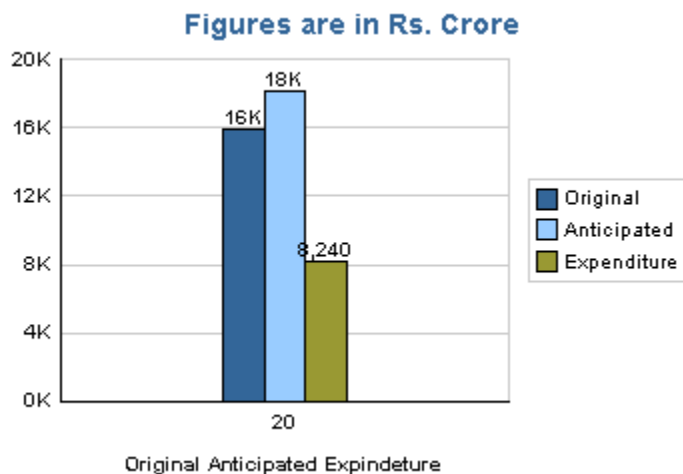

Sector wise current status of projects on the Flash Report

Road Transport & Highways


I. Current Status:

Number of Projects	149
Number of Projects On Schedule	54
Number of Projects Delayed	89

Number of Projects Without Original Date of Commissioning	6
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 149 projects, 54 projects are on schedule and 89 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

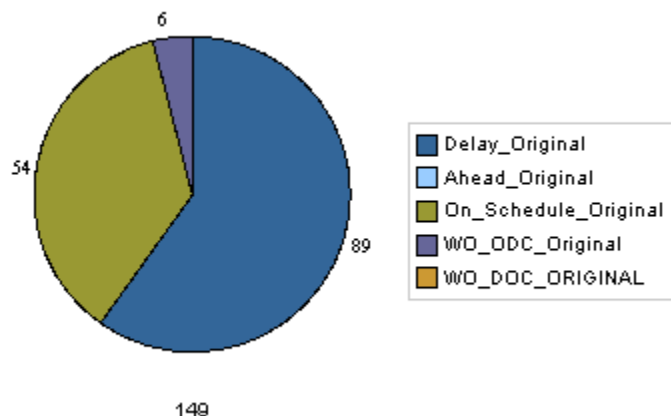

III. Investment Scenario

The Total Original cost of implementation of 149 projects when sanctioned, was of the order of Rs. 97021.84 crore but this was subsequently revised to Rs. 98960.46 crore implying a cost overrun of 2%. The expenditure incurred on these projects till January, 2013 is Rs. 70848.16 crore, which is 71.6% of the revised cost of the projects.

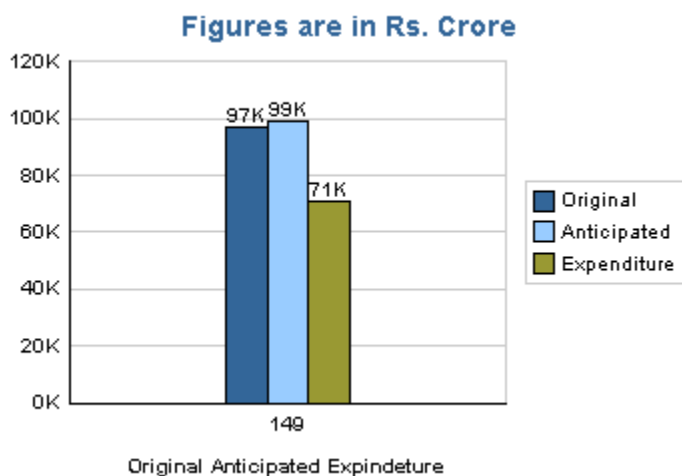

Sector wise current status of projects on the Flash Report


Railways

I. Current Status:

Number of Projects	126
Number of Projects On Schedule	7
Number of Projects Delayed	43
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	17
Number of Projects Without Date Of Commissioning	58

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 126 projects, 1 project are ahead of schedule, 7 projects are on schedule and 43 projects are delayed .58 projects do not have fixed dates of commissioning.17 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

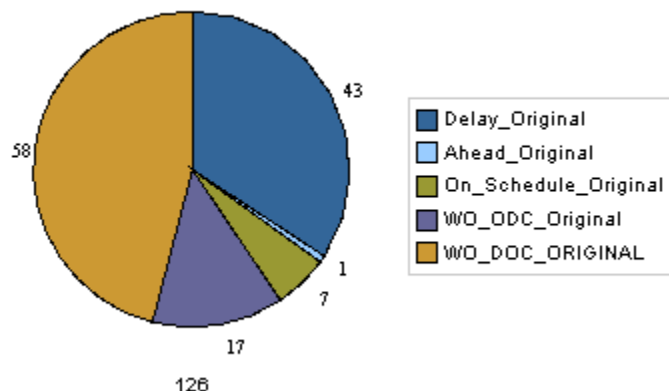

III. Investment Scenario

The Total Original cost of implementation of 126 projects when sanctioned, was of the order of Rs. 61373.8 crore but this was subsequently revised to Rs. 148389.93 crore implying a cost overrun of 141.8%. The expenditure incurred on these projects till January, 2013 is Rs. 61928.21 crore, which is 41.7% of the revised cost of the projects.

Figures are in Rs. Crore

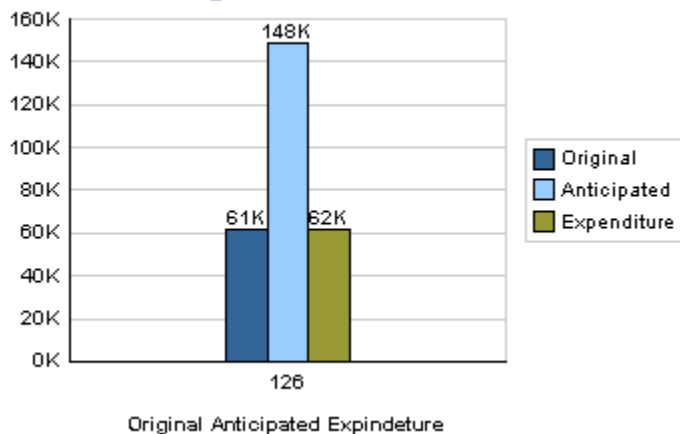

Sector wise current status of projects on the Flash Report

Power


I. Current Status:

Number of Projects	102
Number of Projects On Schedule	46
Number of Projects Delayed	53

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 101 projects, 46 projects are on schedule and 53 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

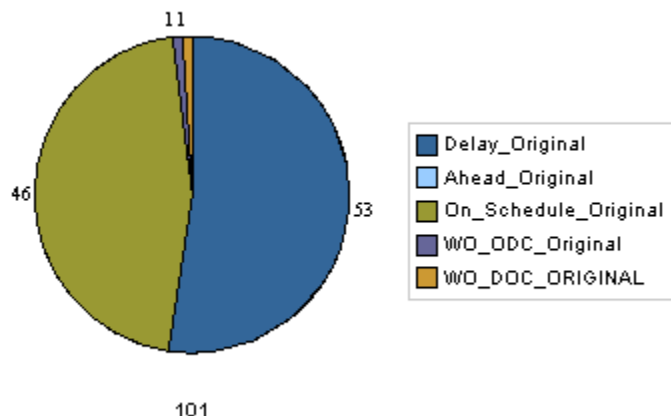

III. Investment Scenario

The Total Original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 239851.89 crore but this was subsequently revised to Rs. 255682.13 crore implying a cost overrun of 6.6%. The expenditure incurred on these projects till January, 2013 is Rs. 112805.94 crore, which is 44.1% of the revised cost of the projects.

Figures are in Rs. Crore

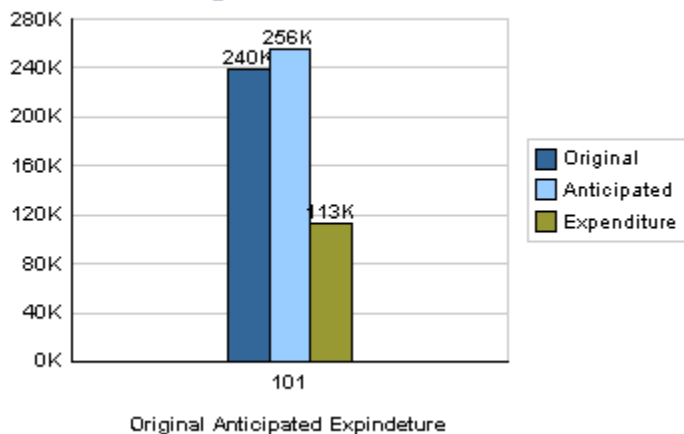

Sector wise current status of projects on the Flash Report

Petroleum


I. Current Status:

Number of Projects	74
Number of Projects On Schedule	22
Number of Projects Delayed	43

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	8


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 74 projects, 22 projects are on schedule and 43 projects are delayed .8 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

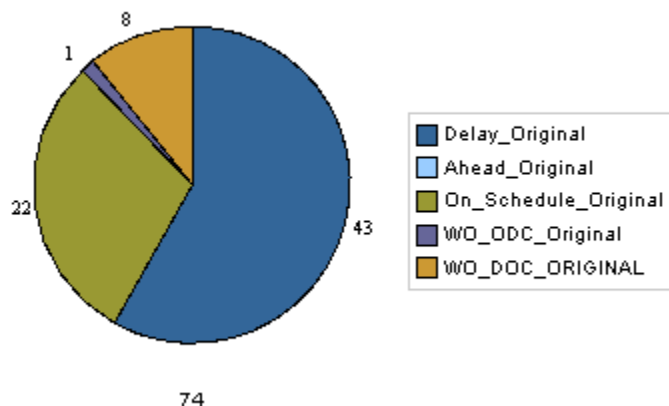

III. Investment Scenario

The Total Original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 177600.55 crore but this was subsequently revised to Rs. 188903.21 crore implying a cost overrun of 6.4%. The expenditure incurred on these projects till January, 2013 is Rs. 84299.81 crore, which is 44.6% of the revised cost of the projects.

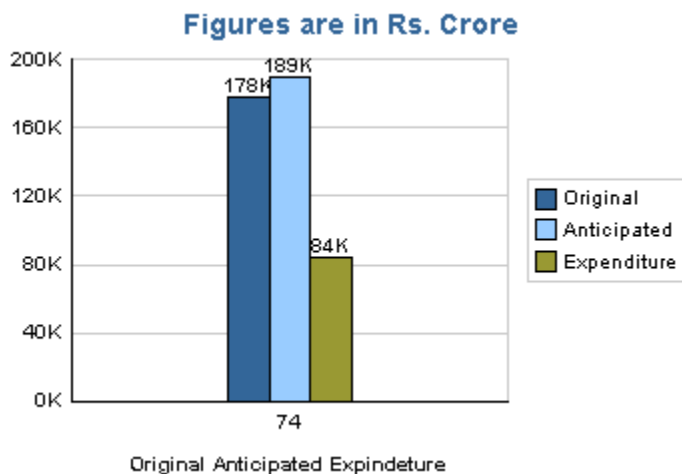

Sector wise current status of projects on the Flash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	2
Number of Projects Delayed	11
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 2 projects are on schedule and 11 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

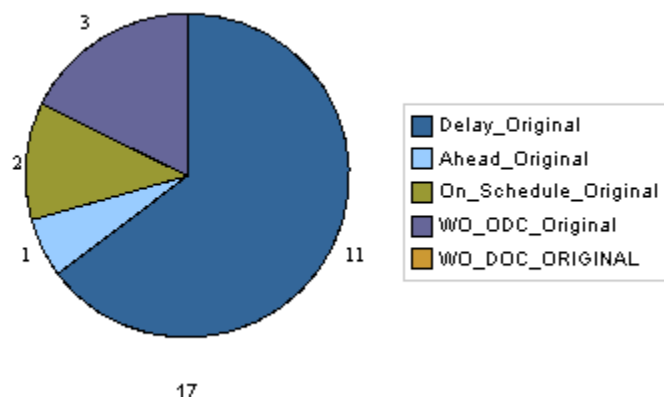

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till January, 2013 is Rs. 46958.93 crore, which is 65.7% of the revised cost of the projects.

Figures are in Rs. Crore

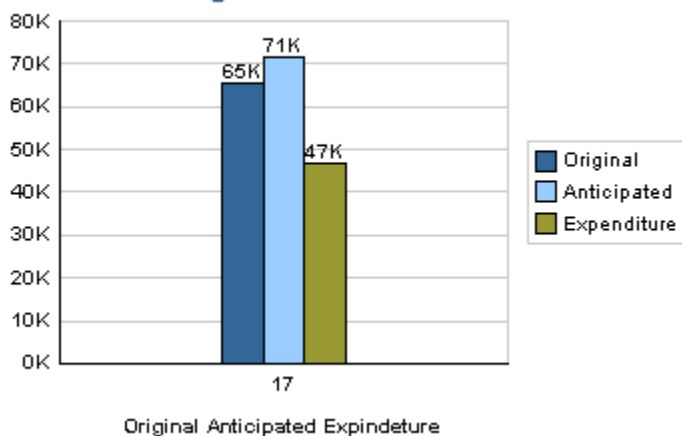

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	25
Number of Projects Delayed	25

Number of Projects Without Date Of Commissioning 1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 51 projects, 25 projects are on schedule and 25 projects are delayed .1 project do not have fixed dates of commissioning.

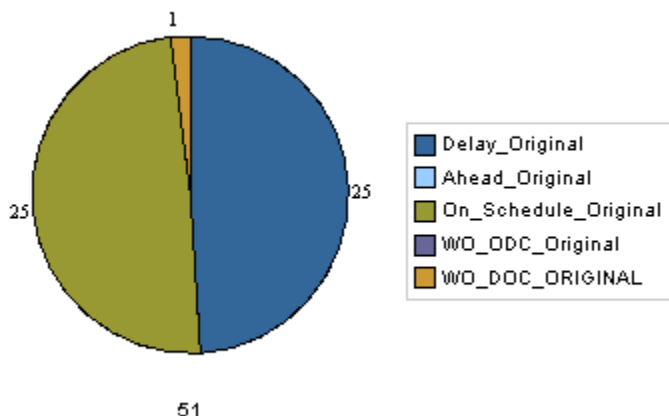

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37510.52 crore implying a cost overrun of 4%. The expenditure incurred on these projects till January, 2013 is Rs. 13622.25 crore, which is 36.3% of the revised cost of the projects.

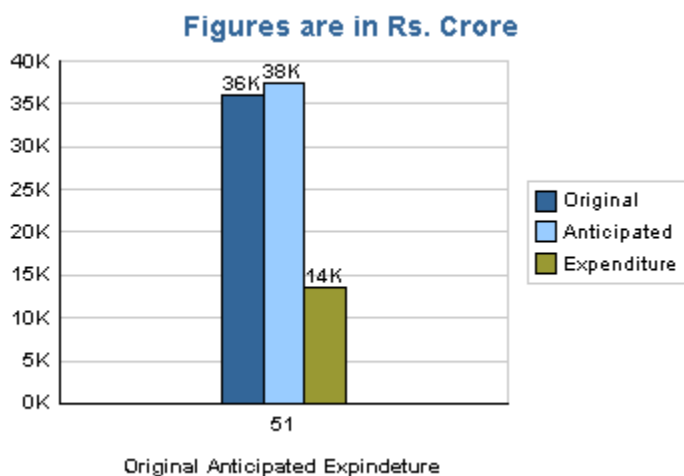

Sector wise current status of projects on the Flash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

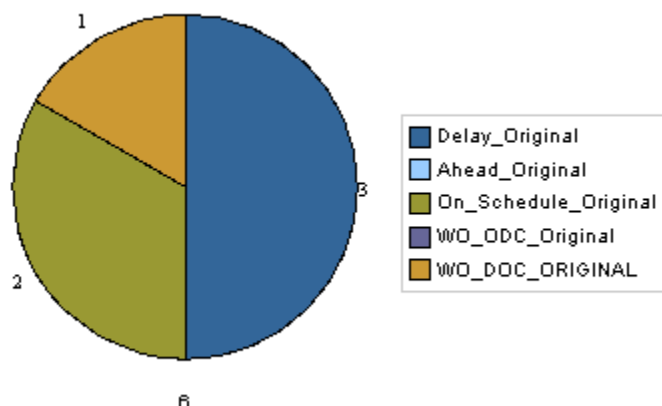

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till January, 2013 is Rs. 4833.48 crore, which is 79.7% of the revised cost of the projects.

Figures are in Rs. Crore

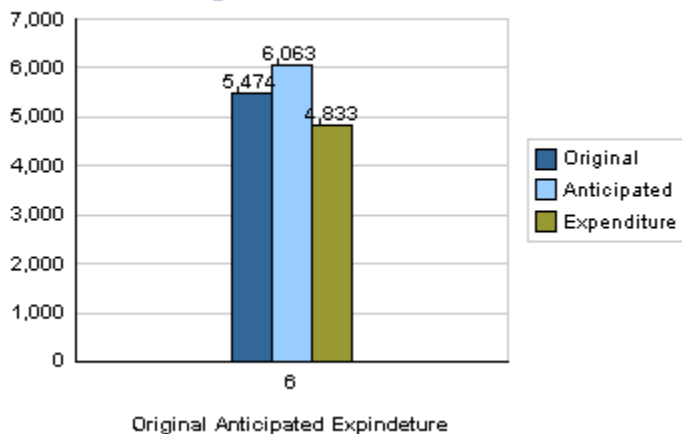

Sector wise current status of projects on the Flash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

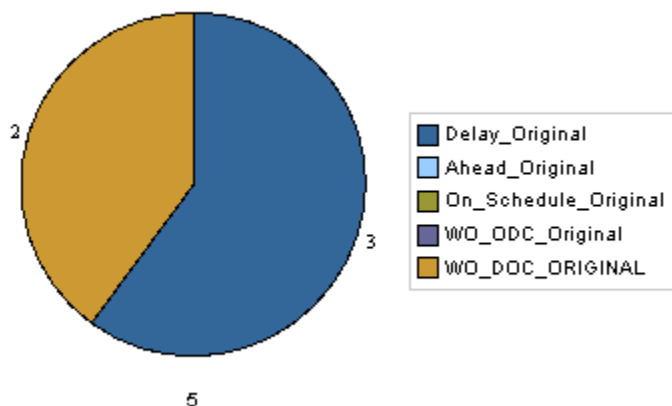

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till January, 2013 is Rs. 24323.57 crore, which is 50.9% of the revised cost of the projects.

Figures are in Rs. Crore

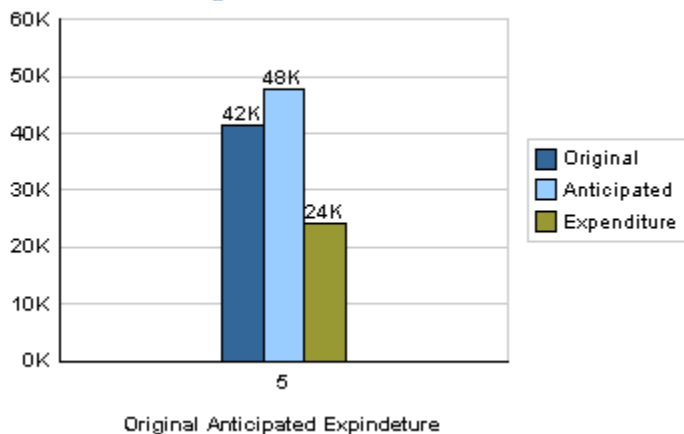

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31097.25	38721.12	23601.50
2	Arunachal Pradesh	4	9512.22	14144.29	8743.53
3	Assam	34	22035.93	35405.41	24059.74
4	Bihar	30	26917.64	34877.43	23301.68
5	Chhatisgarh	25	58429.84	59712.92	16722.47
6	Delhi	4	38214.41	38194.82	1681.46
7	Goa	1	335.61	335.61	183.67
8	Gujarat	22	31111.55	31313.49	9811.37
9	Haryana	8	4054.38	5741.07	6559.25
10	Himachal Pradesh	5	13355.57	17246.69	13258.52
11	Jammu and Kashmir	10	14926.96	34825.56	14205.32
12	Jharkhand	23	14447.40	18492.99	8594.55
13	Karnataka	26	46344.40	55830.82	21607.86
14	Kerala	7	20376.67	21818.22	5163.34
15	Madhya pradesh	22	18978.92	19259.49	9204.92
16	Maharashtra	52	93207.43	108066.84	48881.40
17	Manipur	1	727.56	4444.00	1155.87
18	Meghalaya	2	762.00	762.00	721.89
19	Mizoram	2	1532.97	3307.11	410.47
20	Multi State	112	147454.21	156976.75	68607.46
21	Nagaland	1	850.00	850.00	8.45
22	Odisha	31	57663.96	62099.12	36608.31
23	Punjab	6	3542.01	4483.78	3793.98
24	Rajasthan	14	21115.76	20927.99	7269.42
25	Sikkim	2	1648.94	3690.04	266.46
26	Tamil Nadu	33	51458.75	62238.62	41252.87
27	Tripura	3	1522.39	2018.85	1042.98
28	Uttar Pradesh	24	18952.60	23241.31	12813.99
29	Uttarakhand	4	6097.21	7037.64	2315.38
30	West Bengal	27	42286.11	54919.83	28825.97
TOTAL		571	798960.65	940983.81	440674.08

List of Ongoing Projects More than Cost

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	0.00	15373.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492.00	0.00	3960.33
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0.00	2259.45
4	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756.00	898.00	913.94
5	KOLDAM HEP (NTPC)	Power	10/2002	4527.15	0.00	4735.00
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	10/2003	768.92	0.00	1649.72
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0.00	1270.70
8	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	0.00	1880.57
9	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	611.01	0.00	823.90
10	CHUTAK HYDRO-ELECTRIC PROJECT	Power	08/2006	621.26	0.00	775.32
11	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	Power	07/2006	557.24	0.00	596.30
12	RAMPUR HEP(412 MW)	Power	01/2007	2047.03	0.00	2180.90
13	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
14	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
15	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
16	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
17	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240.00	0.00	600.41
18	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	02/1997	295.00	412.91	573.49
19	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	04/1996	157.00	262.82	269.64
20	KARUR-SALEM(NL),SR	Railways	02/1997	155.55	155.00	756.42
21	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	03/1996	155.74	429.49	635.20
22	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	03/1997	395.00	1062.36	1399.73
23	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	1500.00	2623.90
24	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29
25	RANCHI-LOHARDAGA(GC),SER	Railways	04/1997	194.07	194.07	320.60
26	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	04/1997	233.00	501.69	694.57
27	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	07/1998	248.44	576.27	933.54
28	KATI HAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100.00	492.98	736.40
29	GULBARGA-BIDAR,SCR(NL)	Railways	02/1998	242.42	369.70	484.97

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
30	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	03/2002	381.17	381.17	623.58
31	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.40	323.40	504.45
32	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	03/2002	409.00	625.30	835.70
33	RENIGUNTA-GUNTAKAL(RE)	Railways	06/2000	168.34	0.00	344.50
34	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100.00	100.00	527.63
35	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	733.00	733.00	1336.31
36	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	03/2000	907.69	3156.32	3249.42
37	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	266.03
38	JIND-SONEPAT (NL),NR	Railways	01/2004	190.81	238.56	432.22
39	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	166.16	0.00	258.82
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	727.53	1155.87
41	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.70	915.70	1632.12
42	BILASPUR-URKURA (DL)	Railways	04/1997	151.52	0.00	330.65
43	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	04/2000	133.41	207.00	235.15
44	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	04/2003	136.62	0.00	243.30
45	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	408.83
46	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	577.76
47	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170.00	170.00	396.44
48	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156.00	156.00	287.63
49	ELECTRIFICATION OF MORADABAD-ROZA	Railways	12/2004	129.17	0.00	227.48
50	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3316.95
51	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	12/2003	157.47	0.00	218.94
52	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	04/2000	367.49	0.00	453.68

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
53	HAPUR-GARH Mukteswar (Others) KM.58-93, NH-24	Road Transport & Highways	03/2005	220.00	0.00	282.68
54	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport & Highways	12/2003	230.00	0.00	230.82
55	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	12/2003	240.00	0.00	294.50
56	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	12/2003	340.68	0.00	393.93
57	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	03/2005	190.00	0.00	260.71
58	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport & Highways	12/2003	280.00	0.00	290.15
59	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	12/2003	195.00	0.00	220.64
60	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	12/2003	237.80	0.00	259.55
61	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	12/2003	332.94	0.00	417.74

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
62	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	12/2003	275.00	0.00	279.68
63	SAGAR - RAJMARG CHORAHHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	12/2003	203.43	0.00	248.22
64	RAJMARG CHORAHHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	12/2003	229.91	0.00	289.80
65	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	12/2003	200.00	0.00	276.18
66	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	12/2003	264.72	0.00	296.49
67	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	12/2003	245.00	0.00	491.21
68	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	12/2003	221.82	0.00	298.66
69	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	12/2003	198.16	0.00	223.89
70	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	12/2003	225.00	0.00	255.40

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
71	NALBARI T BIJNI (AS-7)	Road Transport & Highways	12/2003	208.00	0.00	282.11
72	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	12/2003	160.00	0.00	193.25
73	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	12/2003	200.00	0.00	239.89
74	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	03/2005	168.00	0.00	457.30
75	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	03/2005	280.00	0.00	581.49
76	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	04/2000	263.27	0.00	272.24
77	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport & Highways	12/2003	217.61	0.00	240.89
78	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	12/2003	300.93	0.00	303.02
79	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	12/2003	355.06	0.00	500.75

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
80	TRICHY - KORUR NH-67	Road Transport & Highways	03/2005	516.00	0.00	760.07
81	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	03/2005	941.00	0.00	1901.00
82	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	03/2005	557.00	0.00	932.27
83	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	12/2003	232.45	0.00	280.71
84	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	04/2007	486.00	0.00	637.97
85	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	03/2005	940.00	0.00	1222.60
86	Gujarat/Maharashtra Border Surat-Hazira Port Section	Road Transport & Highways	03/2010	1509.10	0.00	1675.00
87	MP/Maharashtra Border-Dhula	Road Transport & Highways	12/2009	835.00	0.00	1068.70
88	Pune-sholapur, pkg1	Road Transport & Highways	11/2009	1110.00	0.00	1802.10

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
89	Kishangarh-Ajmer-Beawer	Road Transport & Highways	11/2009	795.00	0.00	1055.70
90	Chennai-Tada(Six lane)	Road Transport & Highways	04/2009	353.37	0.00	389.95
91	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	04/2009	1673.70	0.00	2776.70
92	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	02/2009	1693.75	0.00	2677.20
93	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	05/2009	572.30	0.00	727.14
94	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	05/2009	1108.00	0.00	3465.90
95	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	04/2010	1740.00	0.00	1939.30
96	Jaipur-Tonk-Deoli	Road Transport & Highways	06/2010	792.06	0.00	1628.50
97	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	09/2010	946.00	0.00	1394.40

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
98	Talegaon-amravati	Road Transport & Highways	11/2009	567.00	0.00	817.78
99	Hazaribagh-Ranchi	Road Transport & Highways	08/2010	625.07	0.00	911.93
100	Armur to kadloor yellareddy	Road Transport & Highways	02/2010	390.56	0.00	631.65
101	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	09/2010	671.00	0.00	737.54
102	AMRITSAR-PATHANKOT	Road Transport & Highways	05/2010	705.00	0.00	1250.80
103	PANIPAT-ROHTAK	Road Transport & Highways	04/2011	807.00	0.00	995.04
104	MURADABAD-BAREILY	Road Transport & Highways	04/2010	1267.00	0.00	1269.90
105	INDORE-DEWAS(NH-3)	Road Transport & Highways	11/2010	325.00	0.00	431.35
106	2 LANNING OF MOKAMA-MUNGER	Road Transport & Highways	05/2011	351.54	0.00	391.89

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
107	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	12/2010	1008.50	0.00	1115.60
108	ROHTAK-BAWAL	Road Transport & Highways	05/2011	650.00	0.00	852.97
109	2-LANNING OF SHILONG BYPASS	Road Transport & Highways	02/2011	226.00	0.00	275.35
110	JAIPUR-REENGUS	Road Transport & Highways	08/2010	267.81	0.00	559.34
111	Acquisition of Two nos. of 3060 DWT	Shipping & Ports	04/2009	277.03	280.00	294.87
112	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	03/2007	245.67	298.17	326.08
113	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	Steel	10/2005	8692.00	0.00	10103.53
114	COKE OVEN BATTERY NO. 4 PHASE-II	Steel	08/2007	108.00	0.00	136.13
115	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	07/2007	230.00	0.00	254.28

List of Projects Ahead of Schedule

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Steel</u>						
1	Expansion of Rourkela Steel Plant - [N12000056	9/2008	11,812.00 11,812.00	11,812.00	8,691.36	11/2013 -	09/2013
	Total		11,812.00 -	11,812.00	8,691.36		
	<u>Railways</u>						
2	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	487.20	03/2014 -	03/2013
	Total		1,389.62 -	1,389.62	487.20		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	433.54	12/2013 12/2013	10/2013
4	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,633.76	433.54		
	Grand Total		15,059.72	14,835.38	9,612.10		

Sectorwise Summary of Project Without Original Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Petroleum	1	2,615.69	.00	2,615.69	1,981.03
Power	1	421.01	623.44	623.44	428.37
Railways	17	5,382.32	7,782.21	15,237.90	6,968.86
Road Transport & Highways	6	4,069.00	.00	4,069.00	3,671.06
Steel	3	1,657.88	.00	1,657.88	445.58
Grand total	28	14,145.90	8,405.65	24,203.91	13,494.90

List of project Without Original Date of Commissioning

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
1	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	234.32	- -	04/2013	-	15/19
2	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	188.57	- 11/2013	11/2013	0(R3)	17/21
3	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	22.69	- -	12/2013	-	0/1
	Total		1,657.88 -	1,657.88	445.58				32/41
	<u>Petroleum</u>								
4	EURO-IV DHD T - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,981.03	- -	01/2013	-	118/116
	Total		2,615.69 -	2,615.69	1,981.03				118/116
	<u>Power</u>								
5	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	428.37	- -	07/2013	-	6/29
	Total		421.01 -	623.44	428.37				6/29
	<u>Railways</u>								
6	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	573.49	- -	01/2013	-	0/0
7	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.44	- -	02/2013	-	0/0
8	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	209.11	- -	03/2013	-	0/0
9	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,708.41	1,399.73	- -	03/2013	-	0/0
10	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	785.32	- -	03/2013	-	0/6
11	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	287.63	- -	06/2013	-	0/0
12	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
13	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	504.45	- -	03/2014	-	0/1

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	235.15	- -	03/2014	-	0/0
15	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,632.12	- -	03/2014	-	0/0
16	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	143.26	- -	03/2014	-	0/0
17	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	247.74	- -	03/2015	-	0/0
18	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
19	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	122.83	- -	03/2016	-	0/0
20	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	224.48	- -	03/2013	-	0/0
21	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	102.37	- -	03/2013	-	0/0
22	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	139.61	- -	03/2013	-	0/0
	Total		5,382.32 -	15,237.90	6,968.86				0/7
Road Transport & Highways									
23	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
24	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
25	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	180.34	- -	04/2013	-	2/2
26	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	434.06	- -	06/2013	-	1/1
27	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	425.02	- -	10/2013	-	2/2
28	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	499.70	- -	12/2013	-	0/1
	Total		4,069.00 -	4,069.00	3,671.06				10/12
Grand Total			14,145.90	24,203.91	13,494.90				166/205

Sectorwise Summary Without Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	2	4,598.29	.00	6,783.29	5,044.57
Civil Aviation	1	1,808.00	2,015.00	2,015.00	1,749.61
Coal	1	249.03	.00	249.03	49.91
Petroleum	8	5,745.72	1,292.00	5,977.50	2,165.37
Power	1	596.45	1,007.16	1,007.16	871.03
Railways	58	17,152.42	30,186.41	48,027.14	23,370.77
Shipping & Ports	12	7,636.66	2,422.27	8,822.34	2,425.25
Telecommunications	7	3,371.69	.00	3,308.61	267.75
Urban Development	1	114.18	173.08	173.08	0.00
Water Resources	1	542.90	.00	1,187.00	35.49
Grand total	92	41,815.34	37,095.92	77,550.15	35,979.75

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	09/2010	-
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-
	Total		4,598.29		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
	Total		2,015.00	02/2012	
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	-
	Total		249.03		
<u>Petroleum</u>					
5	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	-	10/2012
6	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	-	-
7	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	898.00	-	-
8	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	01/2008	224.00	-	-
9	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	08/2009	394.00	09/2012	-
10	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	1,793.00	-	-
11	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	12/2009	1,584.00	07/2012	-
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	02/2009	540.92	07/2012	-
	Total		267.00	09/2012	-
			246.81	04/2012	-
			5,745.72		
<u>Power</u>					
13	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	08/2009	596.45	12/2007	-
	Total		1,007.16	12/2009	
<u>Railways</u>					

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
14	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005
15	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
16	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
17	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
18	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
19	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRT,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
20	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
21	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
22	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
23	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
24	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
25	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
26	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
27	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
28	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
29	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
30	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
31	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
32	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
33	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
34	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
35	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
36	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
37	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
38	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
39	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
40	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
41	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
42	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	12/2012 -	-
43	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
44	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
45	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
46	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 1,185.64	- 09/2009	-
47	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
48	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	-
49	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	-
50	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-
51	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
52	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	-
53	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
54	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
55	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
56	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
57	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
58	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
59	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
60	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
61	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
62	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
63	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
64	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
65	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
66	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
67	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
68	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
69	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
70	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
71	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		17,152.42 -		
Shipping & Ports					
72	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
73	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 -	- 01/2009	01/2009
74	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
75	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
76	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 272.50	06/2011 -	09/2012
77	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
78	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012
79	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
80	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
81	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	-
82	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
83	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	-
	Total		7,636.66 -		
Telecommunications					
84	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
85	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
86	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
87	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
88	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
89	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
90	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	-
	Total		3,371.69 -		
<u>Urban Development</u>					
91	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
<u>Water Resources</u>					
92	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
Grand Total			41,815.34		

Sectorwise Summary On Schedule

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Civil Aviation	2	1,078.00	.00	1,078.00	433.23
Coal	25	12,944.28	.00	12,524.68	2,867.49
Petroleum	22	53,601.98	.00	53,473.72	3,932.37
Power	47	117,495.76	.00	117,495.76	15,201.20
Railways	7	9,618.14	654.51	10,571.43	1,467.11
Road Transport & Highways	54	48,416.87	.00	48,416.87	23,318.09
Steel	2	587.55	.00	587.55	18.72
Urban Development	2	37,736.00	.00	37,736.00	1,681.46
Grand total	161	281,478.58	654.51	281,884.01	48,919.67

List of On schedule Projects w.r.t. original

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	376.97	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	56.26	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	433.23		
	<u>Coal</u>						
3	KRISHNASHILA (NCL) (4MTY) - [N06000007	6/2011	789.88 -	741.62	342.83	03/2013 -	03/2013
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	165.54	03/2015 03/2015	03/2015
5	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.86	03/2014 03/2014	03/2014
6	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	119.73	03/2017 -	03/2017
7	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	71.92	03/2015 -	03/2015
8	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
9	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
10	JALAGAM VENGALA RAO OCP-II - [N06000094	7/2011	447.06 -	447.06	3.02	03/2015 -	03/2015
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
12	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	3.87	03/2018 03/2018	03/2018
13	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
14	KARMA OCP (1.0MTY) - [N06000088	6/2009	162.46 -	162.46	34.89	03/2014 -	03/2014
15	Rajrappa RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016
16	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	94.86	03/2016 -	03/2016
17	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	30.19	03/2015 -	03/2015
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	116.35	03/2013 -	03/2013
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	39.95	03/2016 -	03/2016

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
20	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
21	Muraidih UG Turn-key Project - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
22	CHURCHA ROUG(1.35MTY) - [N06000046	6/2008	462.35 -	462.35	264.84	03/2014 -	03/2014
23	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	43.29	03/2016 -	03/2016
24	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	114.85	03/2013 -	03/2013
25	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
26	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	405.07	03/2016 03/2016	03/2016
27	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008	6/2008	1,188.31 -	1,188.31	691.64	03/2013 -	03/2013
	Total		12,944.28 -	12,524.68	2,867.49		
<u>Petroleum</u>							
28	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	-	04/2013 -	04/2013
29	Wax Project - [N16000101	6/2010	576.60 -	576.60	-	12/2013 -	12/2013
30	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	486.20	01/2014 -	01/2014
31	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	711.28	12/2014 -	12/2014
32	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014
33	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	32.66	05/2015 -	05/2015
34	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
35	DABHOL BANGALORE PIPELINE PROJECT PHASE-II [N16000147	6/2009	486.00 -	486.00	35.11	09/2013 -	09/2013
36	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	666.00	-	11/2015 -	11/2015
37	REWARI KANPUR PIPELINE PROJECT - [N16000145	2/2012	1,210.64 -	1,210.64	39.62	11/2015 -	11/2015
38	Integrated Refinery Expansion Project - [N16000143	1/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015
39	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014
40	IOR of B-173A Field - [N16000140	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
41	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	25.91	03/2014 -	03/2014

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
42	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	105.57	05/2014 -	05/2014
43	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
44	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline [N16000153	4/2011	152.89 -	152.89	-	06/2013 -	06/2013
45	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE [N16000149	8/2011	586.00 -	586.00	4.28	07/2015 -	07/2015
46	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	21.84	07/2015 -	07/2015
47	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,059.63	51.17	03/2015 -	03/2015
48	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	701.82	04/2015 -	04/2015
49	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA [N16000112	8/2010	8,140.00 -	8,140.00	1,701.79	02/2014 -	02/2014
	Total		53,601.98 -	53,473.72	3,932.37		
<u>Power</u>							
50	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID [N16000144	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
51	Transmission system for phase-I generation projects in orissa-part B - [N18000093	12/2010	2,743.19 -	2,743.19	1,187.50	12/2013 -	12/2013
52	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) [N18000140	11/2012	11,846.00 -	11,846.00	722.00	05/2017 -	05/2017
53	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139	1/2013	182.80 -	182.80	-	10/2014 -	10/2014
54	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A [N18000138	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
55	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137	9/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI [N18000136	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
57	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV [N18000115	12/2011	297.33 -	297.33	46.40	08/2014 -	08/2014
58	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	142.70	02/2014 -	02/2014
59	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113	12/2011	2,422.66 -	2,422.66	145.50	08/2014 -	08/2014

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112	11/2011	2,127.51 -	2,127.51	402.20	07/2014 -	07/2014
61	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	447.60	08/2014 -	08/2014
62	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	85.30	06/2014 -	06/2014
63	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	697.50	12/2013 -	12/2013
64	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106	8/2011	425.51 -	425.51	200.70	10/2013 -	10/2013
65	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	386.20	12/2013 -	12/2013
66	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	380.90	06/2015 -	06/2015
67	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
68	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
69	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122	2/2012	1,927.16 -	1,927.16	63.90	10/2014 -	10/2014
70	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	2.40	08/2014 -	08/2014
71	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	162.20	02/2015 -	02/2015
72	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	52.90	01/2014 -	01/2014
73	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117	1/2012	1,422.85 -	1,422.85	159.40	01/2015 -	01/2015
74	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	1,746.65	65.60	08/2014 -	08/2014
75	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	154.00	08/2015 -	08/2015
76	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	1,137.00	11/2016 -	11/2016
77	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	661.00	09/2016 -	09/2016
78	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	1,217.00	12/2016 -	12/2016

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID [N18000130]	6/2012	1,263.26 -	1,263.26	183.60	11/2014 -	11/2014
80	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B [N18000129]	2/2012	3,201.44 -	3,201.44	226.90	10/2014 -	10/2014
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV [N18000128]	11/2011	723.63 -	723.63	67.90	11/2014 -	11/2014
82	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	117.80	08/2014 -	08/2014
83	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	33.70	06/2014 -	06/2014
84	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]	10/2011	558.26 -	558.26	93.30	11/2013 -	11/2013
85	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	552.20	09/2014 -	09/2014
86	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]	7/2011	181.93 -	181.93	65.40	07/2013 -	07/2013
87	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	579.80	05/2014 -	05/2014
88	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B [N18000099]	3/2011	1,585.12 -	1,585.12	673.30	11/2013 -	11/2013
89	Supplementary transmission associated with vellur TPS - [N18000097]	8/2010	170.36 -	170.36	68.50	04/2013 -	04/2013
90	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	1,082.80	03/2014 -	03/2014
91	Northern region system strengthening scheme XVI - [N18000094]	7/2010	752.64 -	752.64	233.80	07/2013 -	07/2013
92	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]	12/2010	1,719.52 -	1,719.52	813.70	08/2013 -	08/2013
93	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	338.20	01/2015 -	01/2015
94	Northern Region system strengthening scheme-XXII - [N18000091]	12/2010	209.78 -	209.78	110.60	08/2013 -	08/2013
95	Transmission system associated with krishnapatnam- Part-A - [N18000090]	12/2010	779.21 -	779.21	717.80	08/2013 -	08/2013
	Total		105,649.76 -	105,649.76	14,479.20		
Railways							
96	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	7/1996	653.84 654.51	1,302.12	608.97	06/2013 06/2013	06/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
97	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	4/2008	653.19 -	653.46	224.26	03/2014 -	03/2014
98	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	4/2008	394.14 -	404.39	15.67	03/2013 -	03/2013
99	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114]	4/2008	516.23 -	516.23	324.23	03/2014 -	03/2014
100	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]	4/2008	829.74 -	829.74	13.85	03/2015 -	03/2015
101	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	57.91	03/2016 -	03/2016
102	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	222.22	03/2016 -	03/2016
	Total		9,618.14 -	10,571.43	1,467.11		
Road Transport & Highways							
103	Indore-Jhabua-Gujrat/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
104	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]	9/2010	852.00 -	852.00	776.82	03/2013 -	03/2013
105	DEOLI-KOTA - [N24000148]	1/2011	593.00 -	593.00	463.70	07/2013 -	07/2013
106	MURADABAD-BAREILY - [N24000154]	4/2010	1,267.00 -	1,267.00	1,269.90	06/2013 -	06/2013
107	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	1,059.70	03/2013 -	03/2013
108	4-laning of Raiganj-Dalkola - [N24000204]	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
109	4-laning of Brahampore-Faraka - [N24000203]	2/2011	998.79 -	998.79	640.19	08/2013 -	08/2013
110	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84 -	1,078.84	859.60	08/2013 -	08/2013
111	BAREILY-SITAPUR - [N24000200]	3/2011	1,046.00 -	1,046.00	236.09	09/2013 -	09/2013
112	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	760.82	06/2014 -	06/2014
113	JAIPUR-REENGUS - [N24000198]	8/2010	267.81 -	267.81	559.34	02/2013 -	02/2013
114	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014
115	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
116	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	449.35	08/2013 -	08/2013
117	TUTICORIN-PORT - [N24000217]	4/2010	182.25 -	182.25	-	02/2013 -	02/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	-	06/2014 -	06/2014
119	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	-	06/2015 -	06/2015
120	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213	4/2012	624.00 -	624.00	105.22	04/2014 -	04/2014
121	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
122	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	34.07	10/2014 -	10/2014
123	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	235.27	07/2014 -	07/2014
124	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	44.34	01/2014 -	01/2014
125	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	529.67	09/2014 -	09/2014
126	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	149.40	06/2014 -	06/2014
127	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
128	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	116.75	01/2014 -	01/2014
129	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	305.59	02/2014 -	02/2014
130	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	160.02	05/2014 -	05/2014
131	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
132	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	275.17	11/2013 -	11/2013
133	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	480.66	07/2013 -	07/2013
134	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
135	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.82	06/2013 -	06/2013
136	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	14.58	12/2013 -	12/2013
137	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
138	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,032.00	08/2013 -	08/2013
139	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	852.97	11/2013 -	11/2013
140	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	678.92	08/2013 -	08/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,115.60	06/2013 -	06/2013
142	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	599.93	02/2013 -	02/2013
143	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	45.59	04/2014 -	04/2014
144	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	479.47	03/2014 -	03/2014
145	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
146	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	730.14	03/2014 -	03/2014
147	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	275.35	02/2014 -	02/2014
148	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	446.54	01/2014 -	01/2014
149	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
150	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	295.04	08/2013 -	08/2013
151	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	83.75	05/2013 -	05/2013
152	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	1,150.90	08/2014 -	08/2014
153	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	995.04	10/2014 -	10/2014
154	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM [N24000145	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013
155	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	817.78	11/2013 -	11/2013
156	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 [N24000139	9/2010	1,655.00 -	1,655.00	475.44	09/2013 -	09/2013
	Total		48,416.87 -	48,416.87	23,318.09		
Steel							
157	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	18.30	08/2014 -	08/2014
158	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	0.42	12/2014 -	12/2014
	Total		587.55 -	587.55	18.72		
Urban Development							
159	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	1,515.23	03/2016 -	03/2016
160	FARIDABAD EXTENSION - [N28000057	9/2011	2,494.00 -	2,494.00	166.23	09/2014 -	09/2014



(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		37,736.00 -	37,736.00	1,681.46		
	Grand Total		269,632.58	270,038.01	48,197.67		

Sectorwise Summary of Project Without Milestone

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	1	1,106.29	.00	1,106.29	1,084.24
Civil Aviation	6	5,473.58	2,015.00	6,063.07	4,833.48
Coal	2	1,570.15	.00	1,570.15	0.00
Petroleum	50	108,824.18	41,267.50	120,150.20	42,040.55
Power	15	12,763.40	.00	13,203.77	2,080.00
Railways	124	60,770.40	64,831.16	146,610.04	60,638.44
Road Transport & Highways	142	92,756.34	.00	94,694.96	66,910.76
Shipping & Ports	19	15,753.13	9,886.33	17,921.56	8,239.52
Steel	2	587.55	.00	587.55	18.72
Telecommunications	15	7,113.08	.00	6,920.16	1,688.15
Urban Development	3	37,850.18	173.08	37,909.08	1,681.46
Water Resources	1	542.90	.00	1,187.00	35.49
Grand total	380	345,111.18	118,173.07	447,923.83	189,250.81

List of Projects Without Milestones

(Jan,2013)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-	0/0
	Total		1,106.29			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	03/2013	0/0
4	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	06/2013	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011 04/2013	12/2013	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	03/2015	03/2015	0/0
	Total		5,473.58			0/0
<u>Coal</u>						
8	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88	04/2014	04/2014	0/0
9	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27	04/2015	04/2015	0/0
	Total		1,570.15			0/0
<u>Steel</u>						
10	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	08/2014	08/2014	0/0
11	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL,Odisha	01/2012	254.90	12/2014	12/2014	0/0
	Total		587.55			0/0
<u>Petroleum</u>						
12	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57	04/2012	01/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
13	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
14	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	01/2013	0/0
15	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	02/2013	0/0
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
17	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	03/2013	0/0
18	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
19	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
20	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
21	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
22	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
23	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
24	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	05/2013	0/0
25	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
27	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
28	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	07/2013	0/0
29	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
30	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
31	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
32	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0
34	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2013	0/0
36	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
37	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
38	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
39	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
40	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
41	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
42	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	03/2014	0/0
43	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 -	04/2014	0/0
44	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
45	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
46	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
47	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
48	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
49	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
50	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
51	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
52	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
53	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
54	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
55	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
56	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	07/2015	0/0
57	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
58	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	12/2015	0/0
59	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
60	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 -	-	0/0
61	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 -	04/2012 -	-	0/0
	Total		108,824.18 -			0/0
Power						
62	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	03/2013	0/0
63	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
64	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	03/2014	0/0
65	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
66	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
67	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
68	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	10/2014 -	10/2014	0/0
69	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
71	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
72	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	12/2014	0/0
73	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	03/2015 -	03/2015	0/0
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	04/2015 -	05/2015	0/0
76	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	06/2016 -	06/2016	0/0
	Total		12,763.40 -			0/0

Railways

77	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
78	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
79	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
80	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
81	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
82	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
83	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
84	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
85	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
86	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
87	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
88	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
89	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
90	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
91	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
92	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
93	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
94	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
95	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
96	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
97	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
98	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
99	KARUR-SALEM(NL), SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
100	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
101	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
102	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
103	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012	0/0
104	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
105	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
106	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	02/2013	0/0
107	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
108	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
109	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
110	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
111	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
112	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	03/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
113	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
114	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
115	KADUR-CHIKMAGALUR-SAKLHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
116	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2013	0/0
117	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
118	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
119	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
120	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2013	06/2013	0/0
121	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	06/2013	0/0
122	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
123	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
124	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
125	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
126	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	12/2013	0/0
127	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
128	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
129	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
130	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
131	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
132	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
133	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	03/2014	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
134	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
135	Ramanagaram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
136	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
137	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
138	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
139	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
140	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2014	0/0
141	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
143	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
144	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
145	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
146	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
147	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
148	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 11/2012	12/2015	0/0
149	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
150	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2016	0/0
151	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
152	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
153	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
154	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
155	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
156	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
157	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
158	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	04/2014 -	03/2017	0/0
160	New Line from Dimapur to Zubza (Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
161	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
162	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	12/2015 -	03/2020	0/0
163	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
164	GONDIA-JABALPUR (GC), (SECR) - [220100186]SECR, Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
165	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	- -	-	0/0
166	REINGUNTA-GUNTAKAL (RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
167	HARIDASPUR-PARADEEP (NL) - [220100285]RVNL, Odisha	04/1996	301.64 1,185.64	- 09/2009	-	0/0
168	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-	0/0
169	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	- 03/2009	-	0/0
170	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Odisha	04/1998	183.23 -	02/2015 -	-	0/0
171	PALWAL-BHUTESWAR 3RD LINE DOUBLING (NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 380.00	03/2009 11/2012	-	0/0
172	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
173	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya pradesh	09/2007	687.20 -	03/2010 -	-	0/0
174	VIRAMGAM-BHILDI (WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
175	AHMEDNAGAR-PARLI VAJNATH (NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 1,010.00	- -	03/2013	0/0
176	NANGALDAM-TALWARA (NL), NR - [220100188]NR, Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
177	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
178	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
179	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
180	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
182	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
183	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
184	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
185	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
186	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
187	RAMGANJIMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
188	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	03/2013	0/0
189	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
190	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
191	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
192	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
193	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
194	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
195	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	06/2014	0/0
196	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
197	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
198	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
199	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
200	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		60,770.40 -			0/0
Road Transport & Highways						
201	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	02/2013	0/0
202	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	02/2013	0/0
203	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	02/2013	0/0
204	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	02/2013	0/0
205	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	02/2013	0/0
206	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	02/2013	0/0
207	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	02/2013	0/0
208	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	02/2013	0/0
209	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	02/2013	0/0
210	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	02/2013	0/0
211	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
212	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
213	TUTICORIN-PORT - [N24000217]NHAI,Multi State	04/2010	182.25 -	02/2013 -	02/2013	0/0
214	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2013	0/0
215	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	03/2013	0/0
216	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
217	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	03/2013	0/0
218	PATHANKOT- BHOGPUR, KM.26- KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	03/2013	0/0
219	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
220	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	03/2013	0/0
221	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
222	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	03/2013	0/0
223	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	03/2013	0/0
224	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	03/2013	0/0
225	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
226	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	03/2013	0/0
227	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	03/2013	0/0
228	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	03/2013	0/0
229	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	03/2013	0/0
230	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	03/2013	0/0
231	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	03/2013	0/0
232	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
233	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
234	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
235	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	05/2013	0/0
236	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	05/2013	0/0
237	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	05/2013	0/0
238	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	05/2013	0/0
239	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
240	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	05/2013	05/2013	0/0
241	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	10/2008	06/2013	0/0
242	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	10/2008	06/2013	0/0
243	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	03/2008	06/2013	0/0
244	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	12/2008	06/2013	0/0
245	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	09/2009	06/2013	0/0
246	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	07/2012	06/2013	0/0
247	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	06/2013	0/0
248	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	10/2011	06/2013	0/0
249	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	01/2013	06/2013	0/0
250	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	11/2012	06/2013	0/0
251	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	06/2013	06/2013	0/0
252	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	06/2013	06/2013	0/0
253	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	06/2013	06/2013	0/0
254	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	12/2009	07/2013	0/0
255	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00	07/2013	07/2013	0/0
256	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	07/2013	07/2013	0/0
257	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	11/2011	08/2013	0/0
258	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0
259	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
260	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
261	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29	08/2013	08/2013	0/0
262	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
263	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
264	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
265	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	06/2008 -	09/2013	0/0
266	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	09/2013	0/0
267	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
268	BAREILY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
269	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
270	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
271	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0
272	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
273	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
274	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
275	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
276	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2013	0/0
277	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	12/2013	0/0
278	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	02/2010 -	12/2013	0/0
279	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	06/2010 -	12/2013	0/0
280	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	09/2010 -	12/2013	0/0
281	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	06/2011 -	12/2013	0/0
282	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	11/2012 -	12/2013	0/0
283	SIX LANNING OF HOSUR-KRISHNAGIRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
284	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
285	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	12/2013	0/0
286	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	10/2008 -	01/2014	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
287	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
288	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
289	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	01/2014	0/0
290	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
291	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
292	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
293	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
294	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
295	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
296	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
297	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
298	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
299	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
300	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
301	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
302	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
303	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
304	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
305	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
306	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	03/2014	0/0
307	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
308	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
309	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
310	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
311	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
312	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
313	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
314	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
315	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
316	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
317	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
318	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
319	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
320	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
321	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
322	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
323	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
324	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
325	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
326	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
327	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
328	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
329	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
330	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	09/2014	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
331	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
332	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
333	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
334	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
335	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
336	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
337	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
338	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
339	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
340	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
341	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
342	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		92,756.34 -			0/0
Shipping & Ports						
343	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST, Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
344	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
345	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
346	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP., Maharashtra	04/2009	290.85 272.50	06/2011 -	09/2012	0/0
347	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP., Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
348	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44 -	04/2011 -	11/2012	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
349	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
350	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
351	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	02/2013	0/0
352	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
353	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0
354	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
355	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 -	06/2013	0/0
356	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2013	0/0
357	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 12/2012	10/2013	0/0
358	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 12/2013	10/2013	0/0
359	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	-	0/0
360	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
361	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	-	0/0
	Total		15,753.13 -			0/0
Telecommunications						
362	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
363	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
364	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
365	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	02/2013	0/0
366	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	03/2013	0/0
367	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 -	03/2013	0/0
368	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2013	0/0
369	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 -	06/2013	0/0
370	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	06/2013	0/0
371	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
372	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
373	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
374	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
375	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
376	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	-	0/0
	Total		7,113.08 -			0/0
Urban Development						
377	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
378	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
379	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
380	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0

(Jan,2013)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
Grand Total			345,111.18			0/0

List of Delay Project w.r.t. original and revised

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,373.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,335.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,571.00	12/2016	03/2017	3	-
Total			36,950.00	41,049.00	19,279.00				
<u>Civil Aviation</u>									
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,259.45	05/2011	03/2013	22	-
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	183.67	05/2012	06/2013	13	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	207.52	01/2011 04/2013	12/2013	35	8
Total			2,587.58	2,970.07	2,650.64				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,580.27	06/2009	09/2013	51	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96	302.96	108.96	03/2010	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	143.73	03/2011	03/2014	36	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,748.36	03/2012	03/2014	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	100.37	03/2012 -	03/2014	24	-
12	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.77	03/2012 -	03/2014	24	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	421.73	03/2013 09/2012	07/2014	16	22
14	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48	-
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	3.27	03/2012 -	03/2015	36	-
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	119.20	03/2010 -	03/2015	60	-
17	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	123.02	03/2012 -	03/2015	36	-
18	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	91.35	03/2013 -	03/2015	24	-
19	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,404.76	03/2014 -	03/2016	24	-
20	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,258.59	03/2014 -	03/2016	24	-
21	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44	-
22	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	81.40	12/2012 -	03/2016	39	-
23	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2016	24	-
24	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.88	03/2014 -	03/2016	24	-
25	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
26	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	204.97	03/2014 -	03/2016	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
27	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.71	03/2011	03/2016	60	-
28	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	108.35	03/2012	03/2016	48	-
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
30	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87	179.87	60.74	03/2012	03/2017	60	-
31	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	25.98	12/2015	08/2017	20	-
Total			22,863.15	24,736.81	10,704.85				
<u>Fertilisers</u>									
32	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	1,064.53	01/2013	03/2013	2	-
Total			1,478.63	1,478.63	1,064.53				
<u>Steel</u>									
33	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	251.61	08/2010	02/2013	30	-
34	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	10,103.53	10/2009	03/2013	41	-
35	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	345.58	12/2011 03/2012	03/2013	15	12
36	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	254.28	02/2011	03/2013	25	-
37	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	136.13	10/2012	06/2013	8	-
38	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,219.38	12/2011	06/2013	18	-

(Jan, 2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
39	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	450.00	231.16	05/2012 -	06/2013	13	-
40	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00 -	6,325.00	3,244.03	12/2011 -	06/2013	18	-
41	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	1,364.11	12/2012 -	12/2013	12	-
42	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhattisgarh	09/2008	17,265.00 -	17,265.00	7,638.68	03/2013 -	03/2014	12	-
43	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL, Odisha	11/2011	254.55 -	254.55	14.78	11/2013 -	03/2014	4	-
Total			51,228.44 -	57,385.98	37,803.27				
<u>Petrochemicals</u>									
44	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	6,077.01	04/2012 12/2013	12/2013	20	0
Total			5,460.61 -	8,920.00	6,077.01				
<u>Petroleum</u>									
45	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin, Karnataka	07/2010	1,043.57 -	1,043.57	1,024.65	04/2012 -	01/2013	9	-
46	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	199.91	03/2012 -	03/2013	12	-
47	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 -	12,160.26	8,727.48	01/2012 -	03/2013	14	-
48	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,585.41	05/2010 05/2012	01/2013	32	8
49	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 312.00	312.00	276.60	01/2012 01/2012	01/2013	12	12
50	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	715.73	04/2011 -	02/2013	22	-

(Jan, 2013)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
51	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	271.67	04/2011 -	02/2013	22	-
52	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,500.00	1,709.62	03/2012 -	02/2013	11	-
53	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	03/2013	84	0
54	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,154.22	05/2010 03/2013	03/2013	34	0
55	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,488.99	09/2011 03/2012	03/2013	18	12
56	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL, Odisha	12/2009	1,492.33 -	1,492.33	1,219.12	06/2012 -	03/2013	9	-
57	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	03/2013	24	22
58	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50 -	341.50	149.24	02/2013 -	03/2013	1	-
59	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
60	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
61	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	372.11	143.95	03/2013 -	04/2013	1	-
62	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	612.76	03/2010 03/2012	05/2013	38	14
63	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12

(Jan,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
64	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	165.66	08/2012 -	05/2013	9	-
65	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12
66	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,280.22	09/2011 05/2012	06/2013	21	13
67	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12	-
68	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	658.19	12/2011 -	07/2013	19	-
69	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	373.62	01/2013 -	08/2013	7	-
70	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	4,524.89	09/2012 -	09/2013	12	-
71	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	65.20	09/2012 -	09/2013	12	-
72	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	566.69	07/2012 -	10/2013	15	-
73	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	94.39	11/2012 -	10/2013	11	-
74	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	30,426.00	20,012.00	11/2012 -	11/2013	12	-
75	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
76	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	84.94	05/2013 -	11/2013	6	-
77	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,136.61	08/2010 03/2012	12/2013	40	21

(Jan,2013)

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
78	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.83	09/2011 -	12/2013	27	-	
79	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	27.13	08/2013 -	01/2014	5	-	
80	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84	0	
81	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,244.96	03/2013 -	03/2014	12	-	
82	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	-	06/2012 -	03/2014	21	-	
83	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	841.62	03/2013 -	04/2014	13	-	
84	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	765.59	12/2012 -	05/2014	17	-	
85	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	-	10/2010 -	12/2014	50	-	
86	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.54	01/2013 -	07/2015	30	-	
87	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120	0	
Total			115,637.16 -	126,836.30	76,221.04					
Power										
88	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	913.00	775.32	02/2011 10/2012	01/2013	23	3	
89	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,649.72	03/2007 09/2012	02/2013	71	5	
90	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,880.57	11/2009 02/2013	03/2013	40	1	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
91	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,844.91	09/2008 -	03/2013	54	-
92	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	758.75	596.30	01/2010 -	03/2013	38	-
93	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	426.00	09/2010 -	03/2013	30	-
94	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,733.00	08/2012 -	03/2013	7	-
95	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.32	386.32	335.93	07/2011 -	03/2013	20	-
96	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,161.90	02/2012 -	03/2013	13	-
97	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	4,145.00	10/2012 -	03/2013	5	-
98	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,108.30	06/2012 -	03/2013	9	-
99	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	132.88	06/2012 -	03/2013	9	-
100	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	169.80	04/2012 -	03/2013	11	-
101	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	58.80	10/2012 -	03/2013	5	-
102	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	870.70	10/2009 -	06/2013	44	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	5
103	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, Jammu and Kashmir	08/2006	611.01 -	936.00	823.90	08/2010 01/2013	06/2013	34	5
104	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88 -	7,031.88	4,221.80	12/2012 -	06/2013	6	-
105	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL, Multi State	11/2009	1,075.12 -	1,075.12	718.60	05/2012 -	06/2013	13	-
106	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Odisha	09/2010	2,074.86 -	2,074.86	827.20	03/2013 -	06/2013	3	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL, Multi State	10/2010	182.68 -	182.68	46.20	01/2013 -	06/2013	5	-
108	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,011.21	10/2010 01/2013	09/2013	35	8
109	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL, Multi State	02/2009	184.19 -	184.19	155.80	11/2011 -	09/2013	22	-
110	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,909.00	10/2012 -	11/2013	13	-
111	Transmission system for transfer of power from Gen. - [N18000098]PGCIL, Multi State	05/2010	250.03 -	250.03	60.30	01/2013 -	11/2013	10	-
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State	02/2009	520.48 -	520.48	337.80	11/2011 -	12/2013	25	-
113	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66 -	509.66	348.20	11/2011 -	12/2013	25	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	251.00	02/2012 -	12/2013	22	-
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,213.20	10/2012 -	12/2013	14	-
116	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	2,005.70	08/2012 -	12/2013	16	-
117	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,128.20	12/2012 -	12/2013	12	-
118	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	511.10	11/2012 -	12/2013	13	-
119	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,563.20	08/2012 -	01/2014	17	-
120	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,180.90	01/2012 -	02/2014	25	-
121	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	1,501.75	1,270.70	09/2009 06/2013	03/2014	54	9
122	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,011.20	11/2012 -	03/2014	16	-
123	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	823.00	08/2012 -	03/2014	19	-
124	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	686.00	04/2013 -	03/2014	11	-

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
125	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	519.10	11/2012 -	03/2014	16	-
126	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	4,735.00	04/2009 -	09/2014	65	-
127	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	573.99	410.24	08/2012 08/2013	09/2014	25	13
128	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,975.00	08/2013 -	09/2014	13	-
129	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,430.70	08/2013 -	09/2014	13	-
130	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	378.42	07/2014 -	02/2015	7	-
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	14.90	04/2015 -	05/2015	1	-
132	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,670.00	03/2013 -	09/2015	30	-
133	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,525.00	07/2011 -	10/2015	51	-
134	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	335.86	07/2014 -	05/2016	22	-
135	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	440.48	07/2010 02/2016	11/2016	76	9
136	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,012.53	01/2016 01/2016	11/2016	10	10
137	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,806.00	12/2009 -	02/2017	86	-
138	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	5,897.12	09/2010 08/2014	03/2017	78	31

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	9	
139	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pradesh	12/2004	2,496.90	2,496.90	2,148.54	05/2013 06/2016	03/2017	46	9	
140	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pradesh	09/2002	3,919.59	5,366.00	3,735.11	09/2009 07/2014	03/2018	102	44	
Total			133,184.67	148,401.77	97,027.34					
<u>Railways</u>										
141	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	933.54	12/2012 01/2013	02/2013	2	1	
142	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	266.03	02/2011 02/2011	02/2013	24	24	
143	DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	460.04	12/2012 12/2012	02/2013	2	2	
144	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	64.23	03/2012 -	02/2013	11	-	
145	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-	
146	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	211.19	03/2002 -	03/2013	132	-	
147	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	650.85	12/2011 12/2011	03/2013	15	15	
148	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	269.64	03/2012 03/2012	03/2013	12	12	
149	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	282.26	03/2012 03/2013	03/2013	12	0	
150	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	408.83	03/2012 03/2013	03/2013	12	0	
151	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013	50	50	
152	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	548.65	03/1994 -	10/2013	235	-	

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
153	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	366.38	12/2009 03/2011	10/2013	46	31
154	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	119.46	12/2011 11/2013	11/2013	23	0
155	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013	94	-
156	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	156.35	12/2012 -	12/2013	12	-
157	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	202.80	03/2004 12/2010	03/2014	120	39
158	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,336.31	12/2008 -	03/2014	63	-
159	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	225.00	235.15	03/2009 03/2009	03/2014	60	60
160	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	169.13	06/2013 06/2013	03/2014	9	9
161	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	416.24	03/2013 -	03/2014	12	-
162	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	204.65	12/2008 -	09/2014	69	-
163	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	917.84	03/2009 12/2012	12/2014	69	24
164	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,316.95	03/2009 -	12/2014	69	-
165	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	176.52	03/2007 03/2007	03/2015	96	96
166	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	736.40	12/2010 12/2010	03/2015	51	51

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
167	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90 227.90	223.01	116.33	12/2012 -	03/2015	27	-	
168	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	5,016.00	2,623.90	04/2008 03/2014	12/2015	92	21	
169	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 529.23	529.23	246.13	02/2010 11/2012	12/2015	70	37	
170	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura	04/2008	813.34 813.34	1,141.75	448.95	03/2014 -	12/2015	21	-	
171	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	5,300.00	1,008.73	03/2014 03/2016	03/2016	24	0	
172	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,298.42	44.12	03/2014 03/2016	03/2016	24	0	
173	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	1,423.98	463.65	03/2005 12/2008	06/2016	135	90	
174	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,074.47	433.89	06/2005 07/2011	06/2016	132	59	
175	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	33.08	03/2016 -	06/2016	3	-	
176	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	4,444.00	1,155.87	03/2011 03/2014	03/2017	72	36	
177	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 619.34	2,393.48	32.05	04/2014 -	03/2017	35	-	
178	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24	-	
179	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,549.43	03/2001 -	12/2017	201	-	
180	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	58.94	12/2015 -	03/2020	51	-	
181	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 501.69	1,043.56	694.57	03/2012 08/2012	02/2013	11	6	

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
182	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	194.44	03/2010 03/2017	06/2014	51	-33	
183	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	152.51	03/2012 -	03/2013	12	-	
Total			27,831.30	73,163.84	29,634.27					
<u>Road Transport & Highways</u>										
184	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	187.97	08/2004 07/2010	02/2013	102	31	
185	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	189.88	08/2004 -	02/2013	102	-	
186	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	156.85	04/2004 -	02/2013	106	-	
187	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	02/2013	95	-	
188	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	248.22	10/2008 -	02/2013	52	-	
189	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	289.80	10/2008 -	02/2013	52	-	
190	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	02/2013	40	-	
191	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,055.70	05/2012 -	02/2013	9	-	
192	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,677.20	08/2011 -	02/2013	18	-	
193	Amur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	02/2013	12	-	
194	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	218.94	09/2007 -	03/2013	66	-	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
195	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	282.68	09/2007 -	03/2013	66	-
196	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	137.44	09/2008 -	03/2013	54	-
197	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, Jammu and Kashmir	12/2003	166.27 -	193.10	163.57	03/2008 -	03/2013	60	-
198	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	256.85	05/2008 -	03/2013	58	-
199	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	294.50	10/2008 -	03/2013	53	-
200	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	340.68	393.93	03/2008 -	03/2013	60	-
201	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	189.58	07/2008 -	03/2013	56	-
202	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	298.66	11/2008 -	03/2013	52	-
203	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	03/2013	45	-
204	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI, Odisha	04/2000	263.27 -	263.27	272.24	02/2004 -	03/2013	109	-
205	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
206	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	03/2013	109	-
207	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	637.97	05/2010 -	03/2013	34	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
208	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	03/2013	6	-
209	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	03/2013	9	-
210	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,939.30	10/2012 -	03/2013	5	-
211	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,628.50	12/2012 -	03/2013	3	-
212	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	266.34	06/2011 06/2011	04/2013	22	22
213	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	417.74	09/2008 -	05/2013	56	-
214	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	296.49	06/2008 -	05/2013	59	-
215	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	239.89	06/2008 -	05/2013	59	-
216	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	05/2013	28	-
217	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.68	10/2008 -	06/2013	56	-
218	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	221.77	10/2008 -	06/2013	56	-
219	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	06/2013	63	-
220	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54	-
221	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	500.75	09/2009 -	06/2013	45	-
222	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,222.60	07/2012 -	06/2013	11	-

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
223	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	-	1,673.70	2,776.70	10/2011	06/2013	20	-
224	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	-	572.30	727.14	10/2011	06/2013	20	-
225	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	-	625.07	911.93	01/2013	06/2013	5	-
226	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	-	705.00	1,250.80	11/2012	06/2013	7	-
227	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	-	604.00	495.37	12/2009	07/2013	43	-
228	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	-	2,288.00	3,465.90	11/2011	08/2013	21	-
229	NALBARI TO BIJUNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	-	200.00	276.18	06/2008	09/2013	63	-
230	NALBARI TO BIJUNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	-	225.00	255.40	06/2008	09/2013	63	-
231	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	-	1,110.00	1,802.10	05/2012	10/2013	17	-
232	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00	-	209.00	3.82	01/2013	10/2013	9	-
233	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	-	190.00	260.71	01/2009	12/2013	59	-
234	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	-	160.00	193.25	05/2008	12/2013	67	-
235	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	-	281.31	179.23	02/2010	12/2013	46	-
236	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	-	407.60	186.18	06/2010	12/2013	42	-
237	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	-	232.45	280.71	09/2010	12/2013	39	-
238	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	-	1,170.52	4.41	06/2011	12/2013	30	-

S.No Project		Date of Approval	Original / Revised Cost		Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
239	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	37.77	11/2012 -	12/2013	13	-
240	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	805.39	426.52	03/2013 -	12/2013	9	-
241	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	01/2014	63	-
242	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	431.35	05/2013 -	02/2014	9	-
243	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	230.82	06/2005 -	03/2014	105	-
244	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	220.64	06/2008 -	03/2014	69	-
245	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	259.55	06/2008 -	03/2014	69	-
246	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	164.00	04/2008 -	03/2014	71	-
247	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	223.89	04/2008 -	03/2014	71	-
248	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	199.82	09/2007 -	03/2014	78	-
249	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	389.95	10/2011 -	03/2014	29	-
250	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	391.89	05/2013 -	03/2014	10	-
251	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	482.60	03/2013 -	03/2014	12	-
252	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, Uttarakhand	11/2011	478.00 -	478.00	229.47	10/2013 -	03/2014	5	-
253	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5	-

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9		
254	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	39.52	09/2007	04/2014	79	-	
255	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00	664.00	320.95	02/2014	04/2014	2	-	
256	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	290.15	02/2009 03/2014	05/2014	63	2	
257	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	282.11	04/2008	05/2014	73	-	
258	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	96.33	07/2009	05/2014	58	-	
259	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	105.66	11/2008	06/2014	67	-	
260	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, Jammu and Kashmir	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11	-	
261	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	953.88	487.64	07/2013	06/2014	11	-	
262	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	34.97	09/2013	07/2014	10	-	
263	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24	-	
264	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60	-	
265	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	240.89	04/2010	11/2014	55	-	
266	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	69.30	04/2009	12/2014	68	-	
267	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	27.54	11/2008	12/2014	73	-	
268	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	127.03	04/2009	12/2014	68	-	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
269	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	932.27	02/2010 -	12/2014	58	-
270	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31	-
271	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
272	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	-	07/2015 -	06/2016	11	-
Total			44,535.97 -	46,474.59	43,859.01				
<u>Shipping & Ports</u>									
273	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,644.30	01/2012 09/2012	02/2013	13	5
274	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
275	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00 309.00	600.00	137.00	03/2006 06/2013	06/2013	87	0
276	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP., Multi State	07/2011	220.49 -	220.49	98.31	01/2013 -	06/2013	5	-
277	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	917.60	12/2010 09/2012	10/2013	34	13
278	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Mahara shtra	08/2010	612.72 532.83	532.83	364.52	12/2012 12/2012	10/2013	10	10
Total			6,413.21 -	7,718.82	5,380.73				

Telecommunications

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9		
279	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N260000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	46	-	
280	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	-	02/2007 03/2012	02/2013	72	11	
281	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N260000099]MTNL,Delhi	02/2006	229.41 -	229.41	-	03/2012 -	02/2013	11	-	
282	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N260000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013	45	-	
283	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N260000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	818.09	11/2010 -	03/2013	28	-	
284	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N260000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53	-	
285	ERP implementation in BSNL on Turnkey basis - [N260000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 -	06/2013	32	-	
286	Supply Installation testing and commissioning of Rural Wimax - [N260000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	170.25	05/2011 -	06/2013	25	-	
Total			3,741.39 -	3,611.55	1,420.40					
<u>Urban Development</u>										
287	BANGALORE METRO RAIL PROJECT - [N280000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21	-	
Total			6,395.00 -	11,609.00	2,267.57					
Grand Total			458,307.11	554,356.36	333,389.66					

List of ongoing projects having cost overrun w.r.to original

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	15,373.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	3,960.33	09/2010 -	-
	Total		16,663.00 -	22,947.00	19,333.33		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,259.45	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038]	08/2008	1,808.00 -	2,015.00	1,749.61	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	23,342.39		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,580.27	06/2009 -	09/2013
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	421.73	03/2013 -	07/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	119.73	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	4,909.54	3,748.36	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	204.97	03/2014 -	03/2016
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.86	03/2016 -	03/2016
	Total		8,579.45 -	37,918.25	30,531.54		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	6,077.01	04/2012 -	12/2013
	Total		5,460.61 -	46,838.25	36,608.55		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	637.21	03/2007 -	03/2014

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.44	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	296.85	03/2006 -	03/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,585.41	05/2010 -	01/2013
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,136.61	08/2010 03/2012	12/2013
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,154.22	05/2010 -	03/2013
22	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	913.94	- -	-
23	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	20,012.00	11/2012 -	11/2013
24	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	379.22	- -	-
25	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	276.60	01/2012 -	01/2013
26	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	-	04/2013 -	04/2013
27	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	03/2013
28	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	841.62	03/2013 -	04/2014
	Total		54,263.98 -	120,264.40	85,639.99		
Power							
29	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,735.11	09/2009 -	03/2018
30	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,735.00	04/2009 -	09/2014
31	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,897.12	09/2010 -	03/2017
32	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,649.72	03/2007 -	02/2013
33	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,806.00	12/2009 -	02/2017
34	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,270.70	09/2009 -	03/2014

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	871.03	12/2007 -	-
36	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	2,011.21	10/2010 -	09/2013
37	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,880.57	11/2009 -	03/2013
38	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,844.91	09/2008 -	03/2013
39	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	823.90	08/2010 -	06/2013
40	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	775.32	02/2011 -	01/2013
41	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	440.48	07/2010 -	11/2016
42	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	596.30	01/2010 -	03/2013
43	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	2,012.53	01/2016 -	11/2016
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	335.86	07/2014 -	05/2016
45	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,733.00	08/2012 -	03/2013
46	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.32	335.93	07/2011 -	03/2013
47	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	428.37	- -	07/2013
	Total		46,019.35 -	182,113.99	127,823.05		
<u>Railways</u>							
48	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	548.65	03/1994 -	10/2013
49	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
50	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	176.44	- 03/2010	-
51	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	597.99	- -	03/2012
52	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	541.95	06/1999 -	03/2011
53	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,549.43	03/2001 -	12/2017
54	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	247.74	- -	03/2015
55	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	211.19	03/2002 -	03/2013
56	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	118.37	12/2012 -	-

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	202.80	03/2004 -	03/2014
59	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	650.85	12/2011 12/2010	03/2013
60	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	224.48	- -	-
61	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	573.49	- -	01/2013
62	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	209.11	- -	03/2013
63	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
64	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	353.41	07/2012 -	-
65	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	269.64	03/2012 -	03/2013
66	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	756.42	- -	10/2012
67	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	635.20	02/2009 -	03/2012
68	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	71.41	- -	-
69	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	1,399.73	- -	03/2013
70	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	5,016.00	2,623.90	04/2008 12/2011	12/2015
71	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	148.03	- -	03/2012
72	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	176.52	03/2007 03/2007	03/2015
73	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	344.29	- -	12/2012
74	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	320.60	06/2004 -	12/2012
75	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
76	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,369.97	07/2005 -	-
77	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	349.77	05/2008 -	-
78	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2013
79	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	694.57	03/2012 -	-
80	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	933.54	12/2012 -	02/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	366.38	12/2009 -	10/2013
82	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	736.40	12/2010 -	03/2015
83	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-
84	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	484.97	- 05/2009	05/2009
85	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	623.58	- -	03/2012
86	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	504.45	- -	03/2014
87	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	102.37	- -	-
88	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	835.70	06/2007 -	06/2007
89	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	344.50	04/2003 03/2010	-
90	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	527.63	- -	-
91	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	785.32	- -	03/2013
92	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
93	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,336.31	12/2008 -	03/2014
94	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,249.42	12/2006 -	08/2010
95	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	266.03	02/2011 -	02/2013
96	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	577.90	- 12/2009	02/2012
97	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	460.04	12/2012 12/2012	02/2013
98	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
99	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	463.65	03/2005 12/2008	06/2016
100	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	697.50	432.22	03/2012 -	12/2012
101	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	235.15	- -	03/2014
102	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	735.10	222.32	- 09/2009	-
103	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	258.82	02/2009 02/2009	04/2013
104	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	1,155.87	03/2011 -	03/2017

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	183.55	- -	-
106	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	282.26	03/2012 -	03/2013
107	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	446.13	- -	03/2010
108	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	917.84	03/2009 -	12/2014
109	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,636.65	10/2007 -	12/2012
110	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	88.88	- -	-
111	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	226.78	- -	-
112	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	1,717.29	1,632.12	- -	03/2014
113	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	204.65	12/2008 -	09/2014
114	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	330.65	- 03/2009	-
115	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	175.25	03/1998 08/2005	08/2005
116	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
117	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	76.45	02/2015 -	-
118	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	235.15	03/2009 03/2009	03/2014
119	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	139.61	- -	-
120	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	243.30	12/2007 03/2010	12/2010
121	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	408.83	03/2012 -	03/2013
122	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027	04/2005	240.00 -	355.00	378.12	03/2009 12/2009	-
123	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.60	0.76	- -	-
124	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	105.70	02/2006 -	12/2013
125	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	429.24	03/2008 06/2008	-
126	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N22000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
127	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
128	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075	09/2006	324.90 -	385.54	229.47	03/2010 -	-

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 -	529.23	246.13	02/2010 -	12/2015
130	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N22000079]	09/2007	404.19 -	900.00	295.24	- -	-
131	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N22000080]	09/2006	343.17 -	900.00	577.76	- -	12/2012
132	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	453.04	396.44	03/2011 -	03/2011
133	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	406.40	287.63	- -	06/2013
134	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	40.36	- -	-
135	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	141.39	- -	-
136	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	200.00 -	385.20	122.83	- -	03/2016
137	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	40.88	- -	-
138	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	819.40	194.44	03/2010 -	-
139	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	213.77	12/2010 -	03/2011
140	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012
141	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	433.89	06/2005 -	06/2016
142	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	448.95	03/2014 -	12/2015
143	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	32.05	04/2014 -	03/2017
144	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
145	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	58.94	12/2015 -	03/2020
146	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	416.24	03/2013 -	03/2014
147	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) [N22000109]	04/2010	2,069.60 -	2,298.42	44.12	03/2014 -	03/2016
148	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	222.22	03/2016 -	03/2016
149	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	224.26	03/2014 -	03/2014
150	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	94.30	12/2011 -	02/2012
151	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	119.46	12/2011 -	11/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	Pandabeswar-Chinpai doubling (ER) - [N22000118	04/2004	225.68 -	293.74	133.95	12/2010 -	12/2010
153	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	04/2008	394.14 -	404.39	15.67	03/2013 -	-
154	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123	04/2008	318.24 -	468.62	1.52	03/2012 -	-
155	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125	04/2006	117.36 196.95	196.95	194.27	03/2011 -	-
156	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127	04/1996	1,676.31 -	4,255.37	3,316.95	03/2009 -	12/2014
	Total		42,670.15 -	311,846.90	185,895.31		
Road Transport & Highways							
157	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	156.85	04/2004 -	02/2013
158	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	137.44	09/2008 -	03/2013
159	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.57	03/2008 -	03/2013
160	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	256.85	05/2008 -	03/2013
161	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	69.30	04/2009 -	12/2014
162	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	105.66	11/2008 -	06/2014
163	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	39.52	09/2007 -	04/2014
164	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	96.33	07/2009 -	05/2014
165	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
166	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	199.82	09/2007 -	03/2014
167	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	08/2013
	Total		3,324.28 -	317,292.10	190,765.78		
Shipping & Ports							
168	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	5.75	10/2008 -	10/2008
169	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
170	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016	11/2007	1,228.00 -	1,460.00	917.60	12/2010 -	10/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	137.00	03/2006 -	06/2013
172	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
173	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
174	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,644.30	01/2012 -	02/2013
175	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy [N25000053]	10/2010	966.46 -	994.82	306.12	02/2014 -	-
176	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	326.08	04/2009 -	02/2011
	Total		8,628.97 -	328,510.60	196,322.56		
<u>Steel</u>							
177	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10,103.53	10/2009 -	03/2013
178	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	345.58	12/2011 06/2010	03/2013
179	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	136.13	10/2012 -	06/2013
180	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	14,219.38	12/2011 -	06/2013
181	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	230.00 -	343.58	254.28	02/2011 -	03/2013
182	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	350.00	251.61	08/2010 -	02/2013
	Total		24,028.89 -	358,727.03	221,633.07		
<u>Telecommunications</u>							
183	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013
184	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle [N26000088]	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013
	Total		477.28 -	359,277.88	221,877.70		
<u>Urban Development</u>							
185	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013

(Jan,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
186	C/o office building for IDBI at bandra Kurla Complex, Mumbai [N28000048]	11/2006	114.18 173.08	173.08	-	04/2009	-
	Total		6,509.18	371,059.96	224,145.27		
			-				
	<u>Water Resources</u>						
187	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	Total		542.90	372,246.96	224,180.76		
			-				
	Grand Total		220,918.55	2,856,330.32	1,788,099.30		
