

**297th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
JULY, 2010**



Unloading of Metro Coaches by DMRC



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-6
Summary of Projects	7-14
Sector wise Trend and Graphicalf Analysis	15-24
Sector wise analysis of projects	25-56
Graph	57-66
List of All Ongoing Projects	67-67
List of Abbreviations	68-69

EXECUTIVE SUMMARY

The 297th Flash Report for July' 2010, that contains information on the status of 597 projects in the Central Sector, each costing Rs. 150 Crores and above. Since April' 2010, Flash report is prepared for the central sector projects costing Rs 150 Crores and above. During July' 2010, two projects have reported completion and have been dropped from the monitor of this Ministry. During July' 2010, total five projects, three projects of Petroleum sector, one in Power sector and one in Urban Development sector have shown considerable improvement over the completion schedule reported earlier.

The online submission of the implementation Status Report of the ongoing projects has not been provided/updated regularly by some of the project agencies leading to under utilization of online computerized monitoring system (OCMS) developed by this Ministry for effective monitoring. Out of 597 ongoing projects on the monitor of this Ministry, 435 projects were updated either by the concerned project agencies online or the data has been entered locally by the staff of this Ministry. The information regarding 162 projects were not updated/received by this Ministry. Sector-wise number of ongoing projects along with status of online reporting is given below:

S. No.	Sector	Projects on monitor	Reported Online	Additional delays
1.	ROAD TRANSPORT & HIGHWAYS	135	120	12
2.	RAILWAYS	135	75	6
3.	POWER	85	78	7
4.	PETROLEUM	79	60	19
5.	COAL	39	38	3
6.	TELECOMMUNICATION	58	32	15
7.	STEEL	20	12	5
8.	SHIPPING & PORTS	22	13	3
9.	CIVIL AVIATION	9	1	-
10.	FERTILISERS	6	-	-
11.	ATOMIC ENERGY	4	4	-
12.	URBAN DEVELOPMENT	2	2	2
13.	MINES	1	-	-
14.	HEALTH & FW	1	-	-
15.	WATER RESOURCES	1	-	-
Total		597	435	72

2. Seventy two (72) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1 to 24 months in

respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports, Telecommunications and Urban Development sectors.

3. Out of 597 projects, 10 projects are ahead of schedule, 107 are on schedule and 296 projects are delayed. Of the balance, 115 projects do not have fixed dates of commissioning while 69 projects were sanctioned without any commissioning date.
4. The total cost of implementation of 597 projects when sanctioned, was of the order of Rs. 649088.41 crore but this was subsequently revised to Rs. 731525.23 Crores implying a cost overrun of 12.7% the expenditure incurred on these projects till July, 2010 is Rs. 292193.35 Crores which is 40% of the revised cost of the projects.
5. In the **Coal sector**, 3 projects have reported additional delays in the range of 1-24 months. Barsingsar TPS (NLC) has reported additional delay of 1 month due to delay in supply of indigenous equipment by private sector and delay in equipment erection. Bina Extension Project has reported additional delay of 4 months due to delay in possession and clearance of forest land. Gevea Expansion OCD (SECL) has reported additional delay of 24 months due to delay in acquisition of land and delay in construction of approach road
6. In the **Steel Sector**, 5 projects have reported additional delay of 1-5 months. Installation of 700 TPD Oxygen Plant, Rourkela and Simultaneous Blowing of BOF Converter of SMS-II have reported additional delay of 1 month each, however, no reason has been provided by the project authorities for such delay. Rebuilding of Coke Oven Battery – 10 has reported additional delay of 2 months due to increase in civil work based on revised design engineering by Mecon Ltd. & termination of contract with HSCL for civil work due to poor performance. Expansion of Salem Steel Plant has reported additional delay of 2 months due to delay in equipment supply by the contractor. Rebuilding of Coke Oven Battery has reported additional delay of 5 months due to delay in supply of fireclay bricks.
7. In the **Petroleum Sector**, 19 projects have reported additional delays in the range of 1-23 months, whereas three projects have shown considerable improvement over the completion schedule reported earlier. Jagdishpur-Haldia pipeline project of GAIL has reported improvement of 10 months due to revival of fertilizer plants and availability of gas at Haldia landfall point. Installation of FCCV at Mumbai refinery has reported improvement of 2 months due to availability of raw material. Kochi-Kanjirkod-Bangalore-Mangalore Pipeline Project Phase-I has reported improvement of 9 months due to availability of gas. Additional Gas Processing Facility at Hazira has reported additional delay of 1 month due to late issue of Notice inviting tenders (NIT). VKPL up gradation and Laying of Spurline to Bhilwara has reported additional delay of 1 month due to delay in tender process, inclement weather conditions and queries by vendors. MSQ Improvement project has reported additional delay of 3 months due to delay in installation and drilling work by the contractor. Additional Gas processing units at (ONGC) Uran, Mumbai has reported additional delay of 2 months due to delay in tender process. MSQ Upgradation Project at Gawahati Refinery and Upgradation Project at Digboi Refinery have reported additional delay of 2 months each due to poor response to consultancy bids, frequent bands and

insufficient transportation of material/equipment. MSQ Upgradation Project at Barauni Refinery has reported additional delay of 3 months due to backing out of reputed PSU consultants in last moment, slow progress by M/S BHEL in power plant jobs and delay by BPCL in supply of compressor package by 11 month. Integrated offshore crude Oil handling facilities at Paradip has reported additional delay of 3 months due to slow progress of the work by the contractor. Bawana-Nangal Pipeline Project has reported additional delays of 6 months due to abnormally high demand of land and crops compensation by farmers of UP and Punjab. Residue upgradation and MS/HSD quality improvement project, BNPL Spurline (Uttaranchal & UP), Compressor Stations (Vijaypur & Jhabua) Phase-I, Diesel Hydro Treatment Project BRPL Dhaligaon and Dahej-Vijaypur Pipe Line Project (Phase-II) – have reported additional delay of 2 months, 3 months, 1 month, 6 months and 6 months respectively, however no reasons have been provided by the project authorities.

8. In the **Power Sector**, 6 projects have reported additional delays in the range of 3-12 months. Koteswar HEP (THDC) has shown considerable improvement over the completion schedule reported earlier. Koteswar Transmission System (PGCIL) has reported additional delay of 3 months due to transmission work slowed down. East – West Transmission Corridor Strengthening Scheme has reported additional delay of 3 months due to delay in final forest clearance for Rourkela- Raipur Line & Ranchi-Rourkela is awaited. Western Region Strengthening Scheme II & V have reported additional delay of 3 months and 6 months respectively due to severe ROW problems. Teesta Low Dam State-II, III and IV have reported additional delay of 10 and 12 months respectively due to delay in forest clearance and delay in decision regarding participation of Chinese firm and strike by GJMM.
9. In the **Road Transport and Highways Sector**, 12 projects have reported additional delay in the range of 1-24 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, utility shifting, Termination of contracts due to poor performance and delay in getting the forest clearance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such delays.
10. In the **Railway Sector**, 6 projects have shown additional delays in the range of 3-12 months. Tollyganj-Garia (MTP), Jind-Sonepat (NL), Chandigarh-Ludhiana (New BG Line), (NR) and Utratia – Zafrabad (LD) have reported additional delays of 3 months, 9 months, 12 months and 12 months respectively, however, no specific reasons have been given by the project authorities. Kottur-Harhar (NL) project of SWR has reported additional delay of 6 months due to delay in link between Telgi and Amaraithy stations held up by the farmers demanding parallel road on railway land. Shimoga-Talguppa has reported additional delay of 9 months due to slow progress by the contractor and frequent rains.
11. In the **Shipping & Ports Sector**, 2 projects have shown additional delays in the range of 2-8 months. However, no specific reason has been given by the project authorities.

12. In the **Telecommunication Sector**, 15 projects have shown additional delays of 1 – 3 months. General reasons of delay in meeting the completion schedule include delay in land acquisition, Termination of contracts due to poor performance, slow progress of work by the contractor, local constraints, inclement weather conditions and revision of scope of works. However, the project authorities have not mentioned any specific reason for such delays.
- 13 In the **Urban Development Sector**, Bangalore Metro Rail Project has reported additional delay of 9 months due to delay in demolition of structures/building etc. Delhi Metro Rail Project Phase-II has shown considerable improvement over the completion schedule reported earlier, however, no specific reason has been reported by the concerned project authority.
- 14 Out of 597 projects, presently on the monitor at the end of July, 2010, 106 projects were on schedule (17.8%), excluding 80 projects without date of commissioning and those have not reported during the month, 296 projects were delayed (50%). During the month, 72 projects have reported additional delays in the range of 2-19 months. The analysis of pictorial presentation shows that since April, 2010 there is a continuous increase in projects reporting additional delays. The overall cost overrun is also on the rise continuously since April, 2010. The overall cost overrun has increases from 17.6 % in June to 20% in July 2010 due to substantial increase in the completion costs of Expansion of Bokaro Steel Plant and Bhilai Steel Plant by Rs 15089 Crores. It may be seen that out of 296 delayed projects, at the end of July, 2010, 89 projects had overall delay in the range of 1 to 12 months, 80 projects had delay in the range of 13 to 24 months, 58 projects had delay in the range of 25 to 26 months and 69 projects had time overrun of 37 months and above.

Status as on 01.07.2010 in respect of completion of projects costing Rs.150 Crores and above in different sectors during 2010-11 is indicated in the following tables.



(Pankaj Jain)
08.10.2010

**Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation**

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	135	6
2	Road Transport & Highways	135	12
3	Power	85	7
4	Petroleum	79	19
5	Telecommunications	58	15
6	Coal	39	3
7	Shipping & Ports	22	3
8	Steel	20	5
9	Civil Aviation	9	0
10	Fertilisers	6	0
11	Atomic Energy	4	0
12	Urban Development	2	2
13	Mines	1	0
14	Health & Family Welfare	1	0
15	Water Resources	1	0
	Total	597	72

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2010-2011

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Petroleum</u>				
1	SHORT TERM LOW COST MUMBAI REFINERY(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000082]	390.00	01/2010	188.43
June,2010				
<u>Steel</u>				
2	REBUILDING OF COKE OVEN BATTERY NO.-4(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000021]	248.94	08/2009	164.48
<u>Petroleum</u>				
3	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL)(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100281]	1,635.00	05/2006	2,095.36
<u>Telecommunications</u>				
4	EXPANSION OF 750K GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000049]	.00	12/2008	175.77
5	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N26000052]	463.61	12/2009	106.13
July,2010				
<u>Petroleum</u>				
6	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000055]	289.60	05/2010	198.16
7	BINA KOTA PIPE LINE PROJECT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000079]	405.82	12/2009	354.93

Summary of projects on the Flash Report for the month of July, 2010


I. Project Implementation – Current Status:

Number of Projects Cost (Rs. 150 Cr. & above) Previous Month	599
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Previous Month	4
Number of Projects Completed/Dropped/Frozen Cost (Rs. 150 Cr. & above) in Current month	2
Number of Projects Dropped (duplicate) in Current month	3
Number of Projects Cost (Rs. 150 Cr. & above) Added in Current month	7
Number of Projects Cost (Rs. 150 Cr. & above) in Current Month	597

II. Brief Analysis

a) Project Status w.r.t


Original Schedule: Out of 597 projects, 10 projects are ahead of schedule, 107 projects are on schedule and 296 projects are delayed. Of the balance, 115 projects do not have fixed dates of commissioning while 69 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

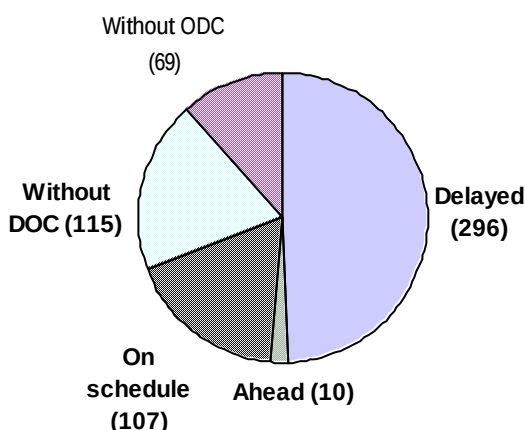

III. Investment Scenario

Figures are in Rs. Crore

The total Original cost of implementation of 597 projects when sanctioned, was of the order of Rs. 609603.35 crore but this was subsequently revised to Rs. 731525.23 crore implying a cost overrun of 20.00%. The expenditure incurred on these projects till July, 2010 is Rs. 292193.35 crore, which is 39.94% of the revised cost of the projects.

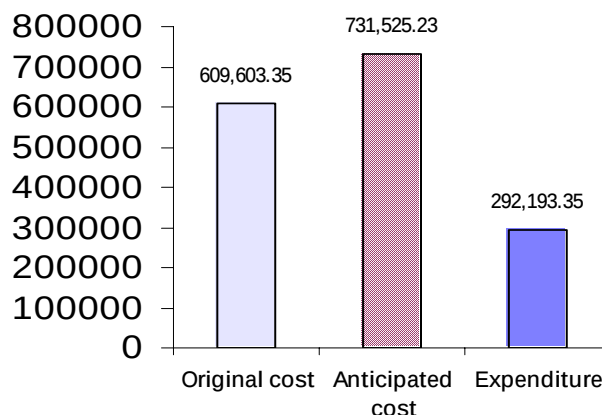

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	599
No of Projects Completed/Dropped/Frozen in Previous Month	4
No of Projects Completed/Dropped/Frozen in Current Month	2
Number of Projects Dropped (duplicate) in Current month	3
No of Projects added in Current Month	7
No of Projects in Current Month	597

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original	296	10	107	69	115	597	49.58
Latest Approved	319	13	122	56	90	597	53.43

III. (A) Project cost w.r.t Sanctioned Cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	510	512,564.88	571,494.51	226,930.34	39.70	58,929.63	11.50
Latest Approved	87	136,523.53	160,030.72	65,263.01	40.80	23,507.19	17.20
Total	597	649,088.41	731,525.23	292,193.35	39.94	82436.82	12.70

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Latest Approved	72	85,757.84	104,272.33	54,956.55	52.70	18,514.49	21.60
Total	72	85,757.84	104,272.33	54,956.55	52.70	18514.49	21.59

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>						
BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT	05/2008	289.60	05/2010	289.60	05/2010	198.16
BINA KOTA PIPE LINE PROJECT	07/2007	405.82	12/2009	405.82	07/2010	354.93

VI. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Telecommunications</u>					
UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	1/2009	149.15	6/2009	158.72	9/2010
<u>Petroleum</u>					
Development of WO-16 Cluster Fields	6/2010	2,523.00	1/2014	2,523.00	1/2014
<u>Civil Aviation</u>					
Construction of New International Terminal Building	5/2010	204.73	5/2012	204.73	5/2012
<u>Petroleum</u>					
Construction of one Multipurpose Support Vessel	1/2010	723.64	3/2013	723.64	3/2013
Development of Cluster-7 Fields	3/2010	3,241.03	3/2013	3,241.03	3/2013
Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli	6/2009	613.54	12/2010	727.88	12/2010
ASSAM GAS CRACKER PROJECT	4/2006	5,460.61	4/2012	5,460.61	4/2012

VII. Milestones (Cumulative due & achieved)

Total	2093
Achieved up to month	807

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Coal</u>						
BARSINGSAR TPS (2X125MW) (NLC)	1,114.18	1,626.09	06/2009	09/2010	10/2010	1
BINA EXTN. PROJ	168.97	168.97	03/2014	11/2013	03/2014	4
GEVRA EXPANSION OCP (SECL) (25 MTY)	1,667.55	2,675.67	03/2010	03/2012	03/2014	24
<u>Steel</u>						
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA	302.70	302.70	06/2009	07/2010	08/2010	1
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II	197.66	197.66	N.A.	07/2010	08/2010	1
REBUILDING OF COKE OVEN BATTERY-10	416.50	436.54	N.A.	06/2010	08/2010	2
EXPANSION OF SALEM STEEL PLANT	1,902.00	1,902.00	N.A.	06/2010	08/2010	2
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)	172.78	191.00	N.A.	06/2010	11/2010	5
<u>Petroleum</u>						
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I	7,596.18	6,652.22	01/2013	01/2013	03/2012	-10
KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I	3,032.00	348.00	N.A.	12/2012	03/2012	-9
INSTALLATION OF FCCV AT MUMBAI REFINERY	900.47	900.47	09/2009	12/2010	10/2010	-2
LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY	638.90	1,030.00	04/2009	06/2010	07/2010	1
ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA	370.11	370.11	04/2011	06/2012	07/2012	1
VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI	463.32	463.32	N.A.	05/2011	06/2011	1
BNPL SPURLINE (UTTRANCHAL & PUNJAB)	540.92	540.92	N.A.	05/2011	06/2011	1
RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT	5,693.00	6,898.00	01/2010	08/2010	10/2010	2
DEVELOPMENT OF B-193 CLUSTER FIELDS	3,248.78	5,633.44	03/2010	04/2012	06/2012	2

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY	372.00	325.00	02/2010	07/2010	09/2010	2
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY	356.00	300.00	02/2010	07/2010	09/2010	2
ADDITIONAL GAS PROCESSING UNITS AT URAN	1,797.35	1,797.35	12/2011	09/2012	11/2012	2
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)	900.92	1,493.49	06/2006	07/2010	10/2010	3
MSQ UPGRADATION PROJECT AT BARAUNI REFINERY	1,492.00	1,505.00	04/2010	07/2010	10/2010	3
MSQ IMPROVMENT PROJECT	293.60	293.60	12/2009	07/2010	10/2010	3
Integrated offshore crude Oil handling facilities at Paradip	1,492.33	1,492.33	06/2012	03/2012	06/2012	3
BAWANA NANGAL PIPE LINE PROJECT	1,816.07	1,816.07	N.A.	10/2010	04/2011	6
DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)	4,429.38	2,800.00	N.A.	10/2010	04/2011	6
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I	1,512.00	975.00	N.A.	10/2010	04/2011	6
Power						
KOTESHWAR HEP(THDC)	1,301.56	2,398.39	04/2005	10/2011	12/2010	-10
KOTESWAR TRANSMISSION SYSTEM (PGCIL)	260.34	241.27	06/2008	08/2010	11/2010	3
EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME	803.70	803.76	06/2009	09/2010	12/2010	3
WESTERN REGION STRENGTHENING SCHEME-II	5,221.23	4,978.56	07/2010	12/2010	03/2011	3
WESTERN REGION STRENGTHENING SCHEME-V	477.69	477.69	09/2010	09/2010	03/2011	6
TESSTA LOW DAM STAGE - II, III (NHPC)	768.92	845.46	03/2007	02/2011	12/2011	10
TEESTA LOW DAM HEP, STAGE-IV (NHPC)	1,061.38	1,061.38	09/2009	08/2011	08/2012	12
Railways						
TOLLYGANJ-GARIA(MTP)	907.69	1,032.76	12/2006	06/2010	09/2010	3
KOTTUR-HARIHAR(NL),(SWR)	65.94	325.00	N.A.	03/2010	09/2010	6
JIND-SONEPAT (NL),NR	190.81	234.45	N.A.	03/2012	12/2012	9
SHIMOGA-TALAGUPPA	46.00	218.00	N.A.	03/2010	12/2010	9

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
CHANDIGARH- LUDHIANA(NEW BG LINE),NR	248.44	1,103.47	N.A.	12/2011	12/2012	12
UTRATIA-ZAFRABAD (LINE DOUBLING)	325.00	496.03	03/2010	12/2011	12/2012	12
<u>Road Transport & Highways</u>						
ISLAM NAGAR TO KADTAL	546.83	546.83	03/2010	07/2010	08/2010	1
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	10/2010	12/2010	2
SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	151.30	151.30	10/2008	12/2010	03/2011	3
PONDICHERY - TINDIVANAU NH-66	285.00	285.00	07/2010	07/2010	10/2010	3
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	565.00	565.00	07/2010	07/2010	10/2010	3
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	07/2010	12/2010	5
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	07/2010	12/2010	5
DELHI/ HARYANA BORDER TO ROHTAK	486.00	486.00	05/2010	12/2010	05/2011	5
DHARAMTUL TO SONAPUR,KM 205-183 (AS- 20)	160.00	160.00	05/2008	06/2011	12/2011	6
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI	441.00	441.00	07/2010	07/2010	03/2011	8
BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	230.00	230.00	06/2005	12/2010	12/2011	12
MAIBANG TO LUNDING (AS- 24), KM.111.000 TO KM.126.450	155.04	155.04	11/2008	12/2010	12/2012	24
<u>Shipping & Ports</u>						
DEV. & OPRATION OF AN INTERNATIONAL CONTAINER TRA	2,118.00	2,118.00	11/2004	08/2010	10/2010	2
ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS	586.58	586.58	11/2010	11/2010	03/2011	4
ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE	1,658.59	1,658.59	07/2010	07/2010	03/2011	8
<u>Telecommunications</u>						


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GSM equipment of 900000Lines (2G) PunjabPhase V.2	241.49	241.49	09/2009	09/2010	10/2010	1
GSM equipment of 1867000Lines (2G) 383000 lines 3(	868.00	868.00	08/2009	09/2010	10/2010	1
GSM equipment of 1625000Lines (2G) 325000 lines 3(	916.70	916.70	11/2010	08/2010	09/2010	1
GSM equipment of 1900000Lines (2G) 401700 lines 3(	760.20	810.37	01/2010	08/2010	09/2010	1
GSM equipment of 1700000Lines (2G) 234100 lines 3(	677.75	719.90	10/2009	09/2010	10/2010	1
GSM equipment of 1900000Lines (2G) 335500lines 3(G	848.70	848.70	01/2010	09/2010	10/2010	1
GSM equipment of 4,50,000 Lines (2G) Haryana (Phas	216.54	216.54	09/2009	08/2010	10/2010	2
GSM equipment of 200000Lines (2G) UP(West)Phase V.	336.84	336.84	10/2009	08/2010	10/2010	2
GSM equipment of 975000Lines (2G) 325000 lines 3(G	625.53	625.53	02/2010	08/2010	10/2010	2
GSM equipment of 1100000Lines (2G) UP East Phase	624.75	624.75	09/2010	08/2010	10/2010	2
GSM equipment of 375000Lines (2G) 75000lines 3(G)	170.23	167.20	06/2009	08/2010	10/2010	2
GSM equipment of 945000Lines (2G) 225000lines 3(G)	366.00	529.32	10/2008	08/2010	10/2010	2
GSM equipment of 799000Lines (2G) 101000 lines 3(G	328.13	392.44	03/2009	08/2010	10/2010	2
GSM equipment of 1500000Lines (2G) 264700lines 3(G	922.91	922.91	01/2010	08/2010	10/2010	2
CONVERGENT BILLING AND CRM-MTNL(DELHI)	249.00	229.41	02/2007	12/2010	03/2011	3
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT	8,676.00	18,894.36	06/2010	11/2010	09/2010	-2
BANGALORE METRO RAIL PROJECT	6,395.00	11,609.00	12/2011	06/2012	03/2013	9


VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
Number of projects reporting additional delay = 72						

Sector wise Trend and Graphical Analysis (April'10, May'10, June'10 ,July'10)

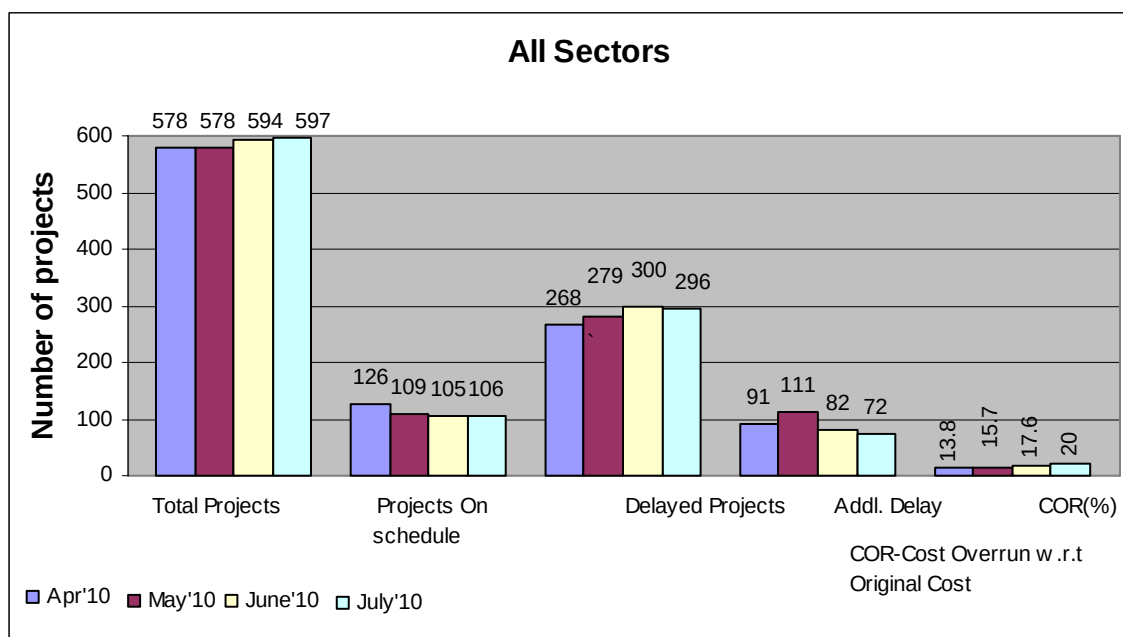



Break-up of Delayed projects in the month of July'10

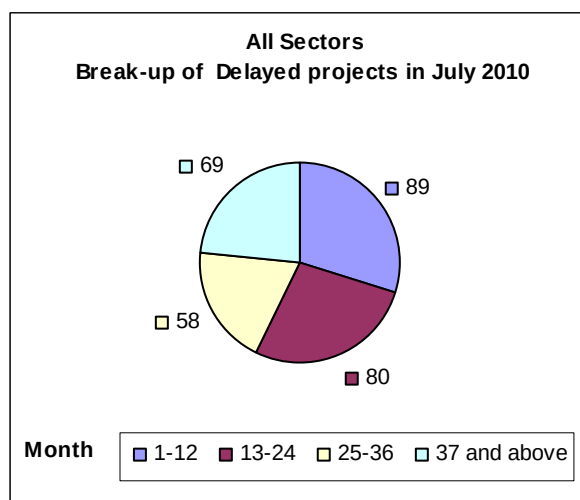

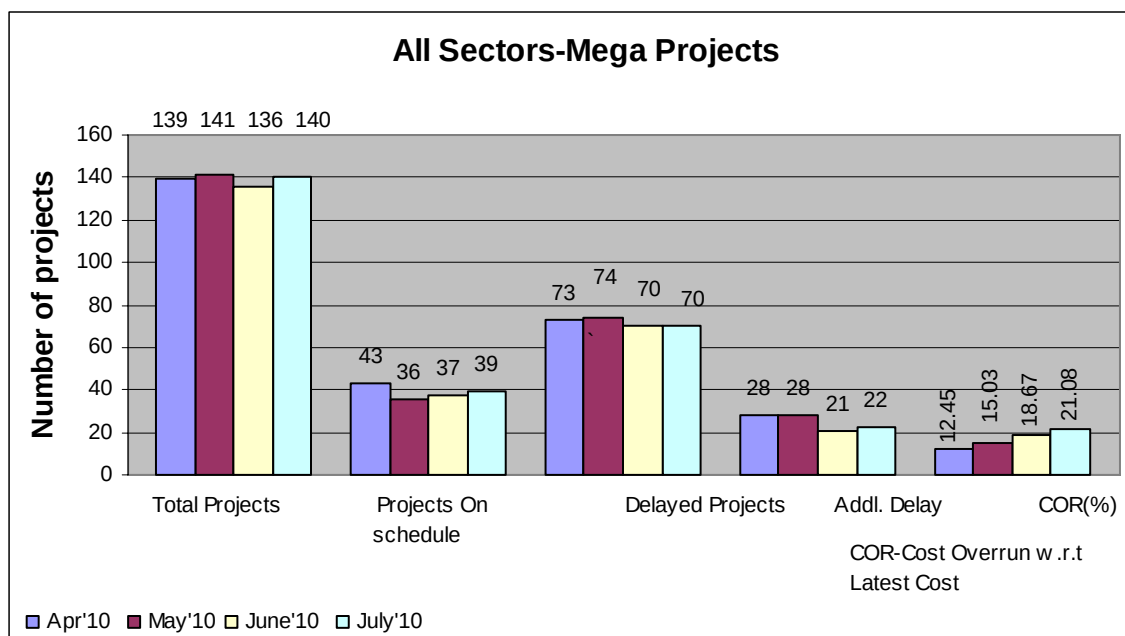



Break-up of Delayed projects in the month of July'10

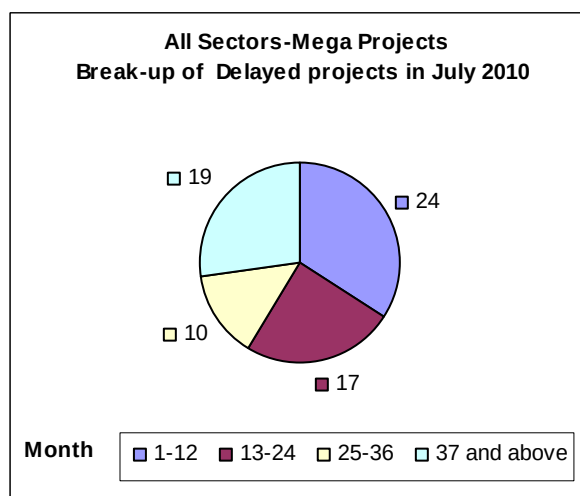

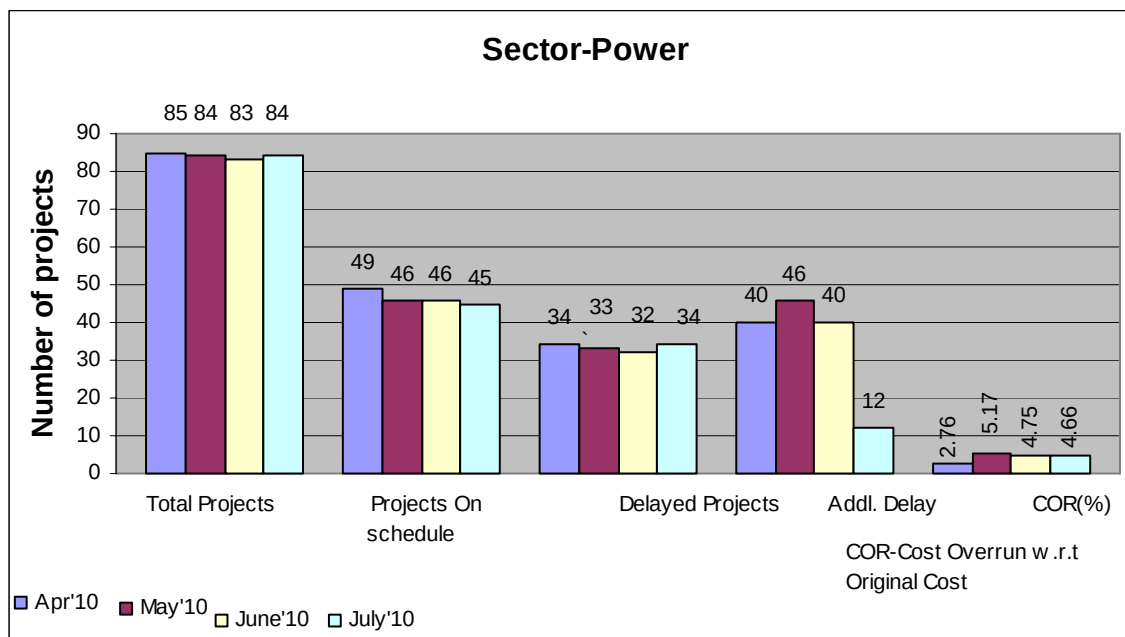



Break-up of Delayed projects in the month of July'10

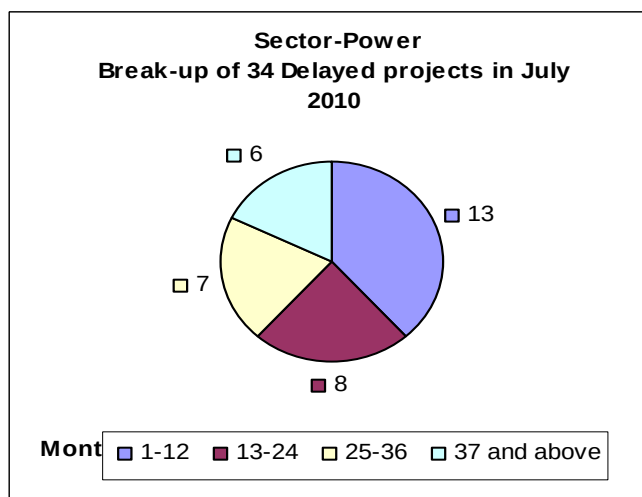

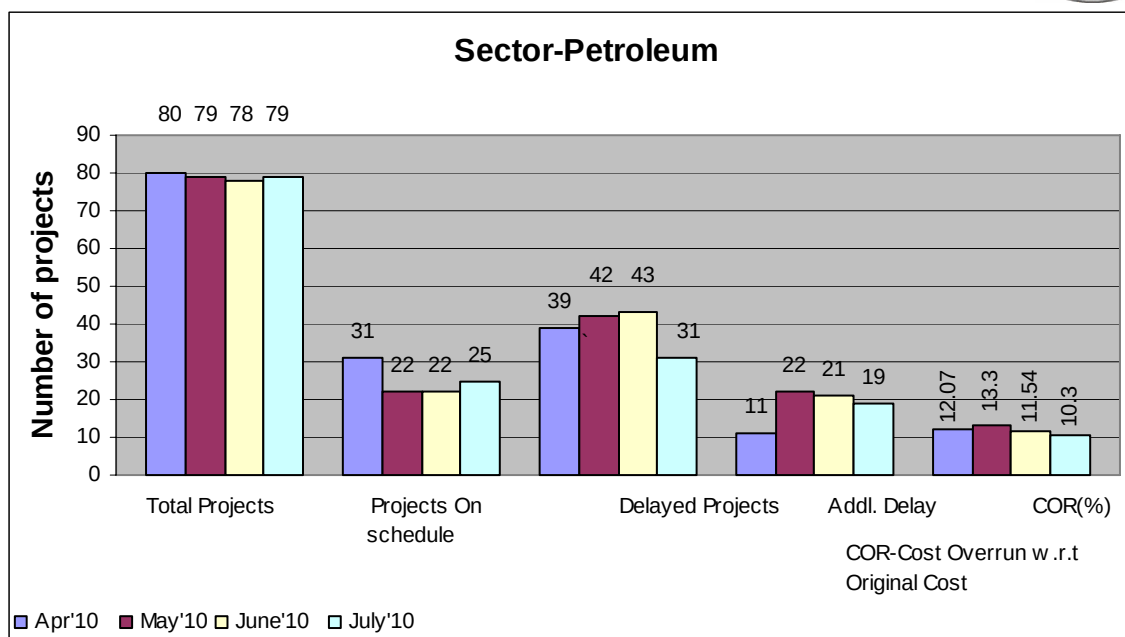



Break-up of Delayed projects in the month of July'10

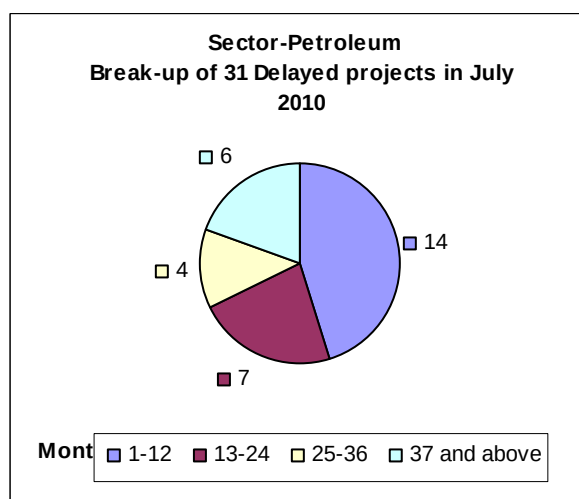

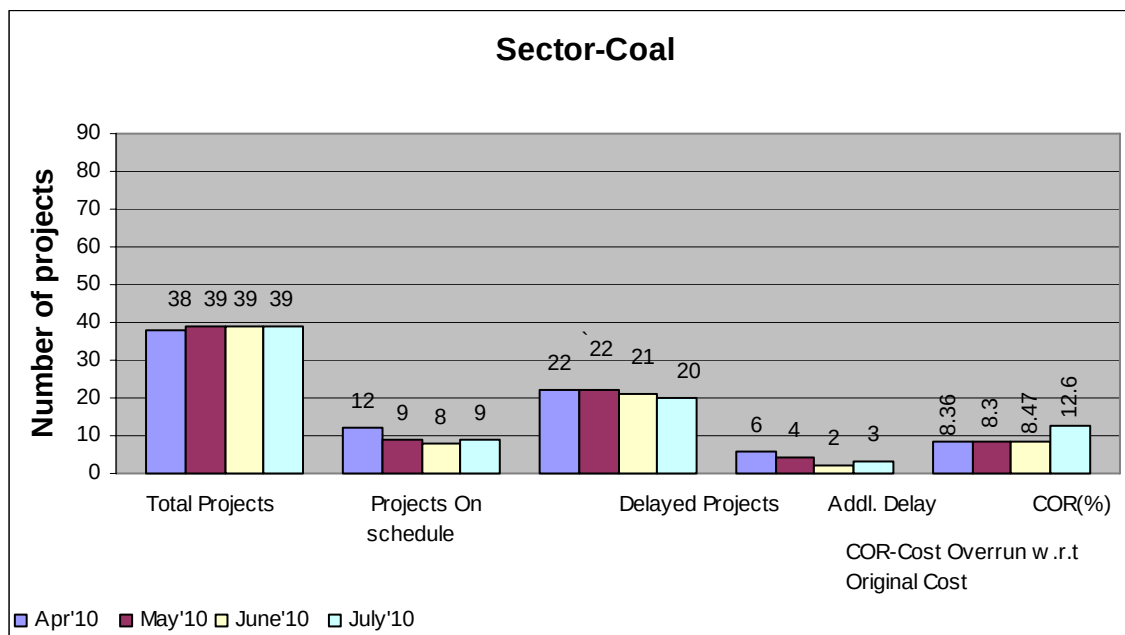



Break-up of Delayed projects in the month of July'10

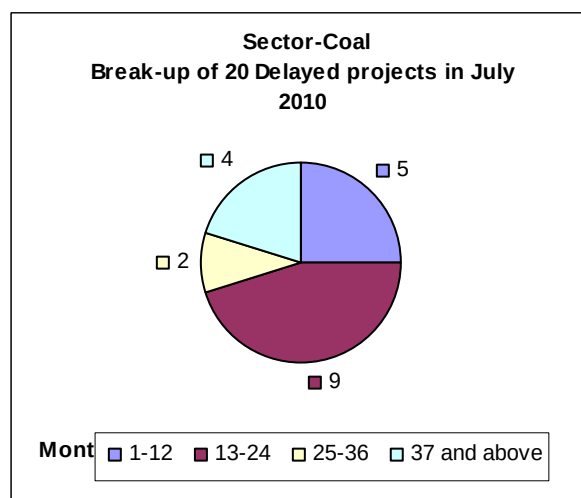

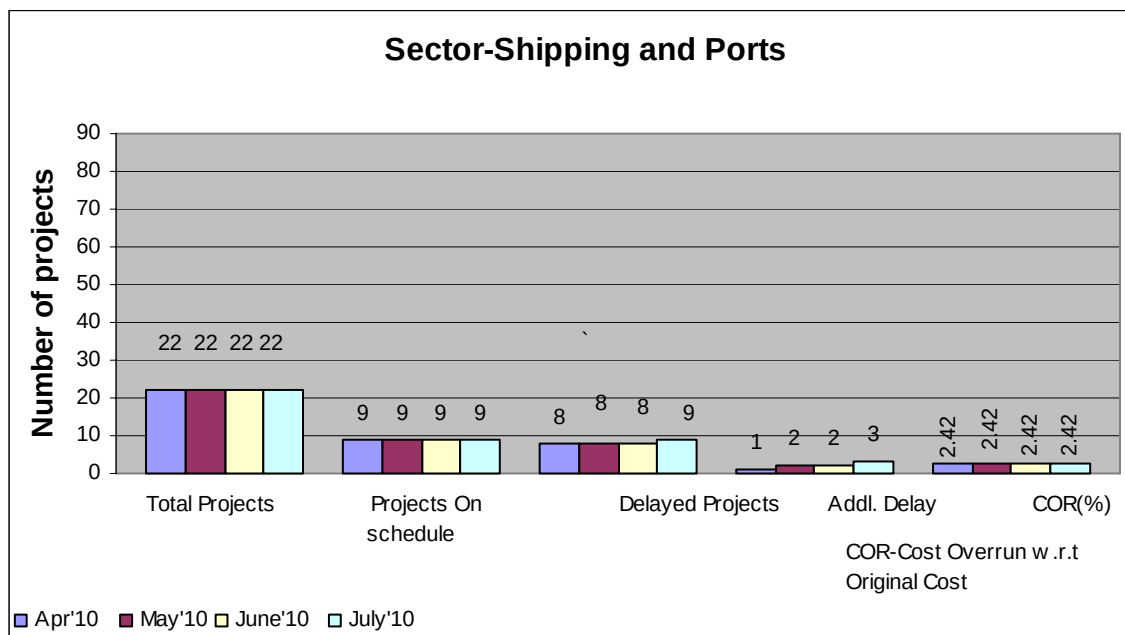



Break-up of Delayed projects in the month of July'10

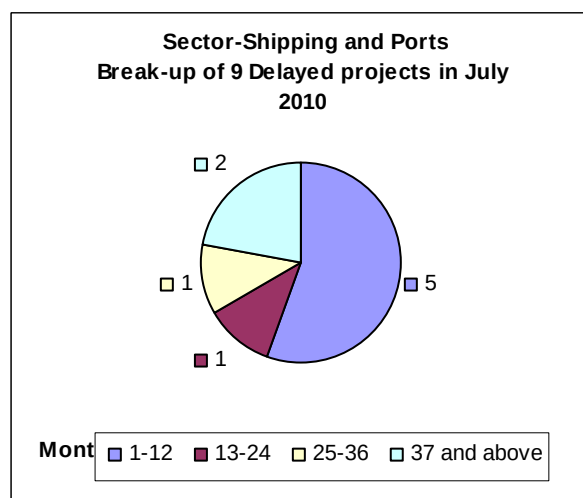

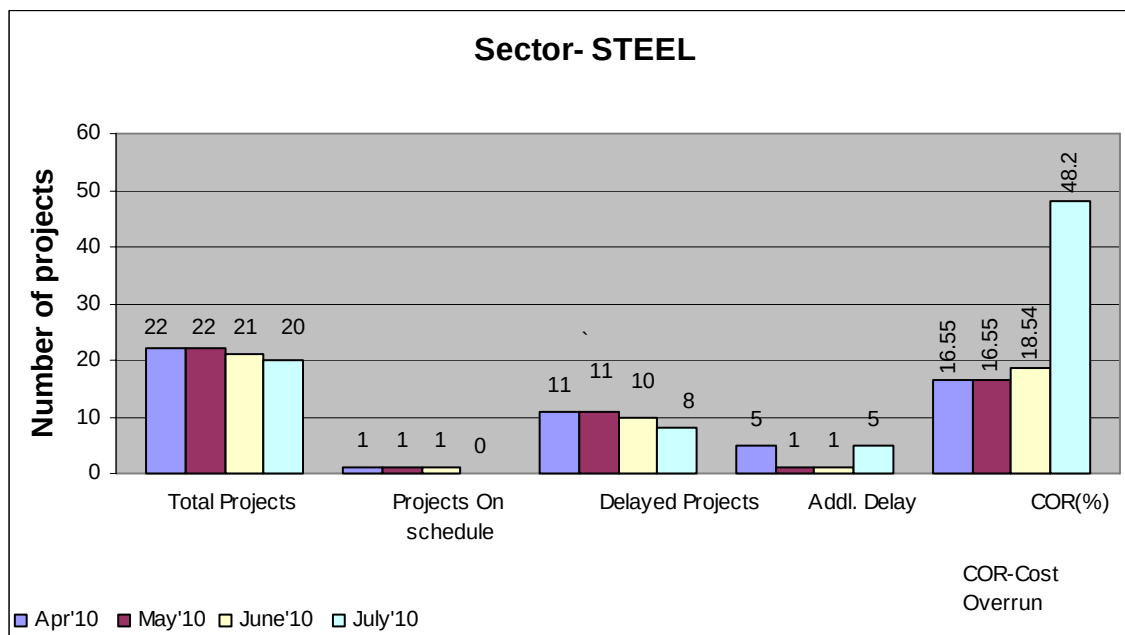



Break-up of Delayed projects in the month of July'10

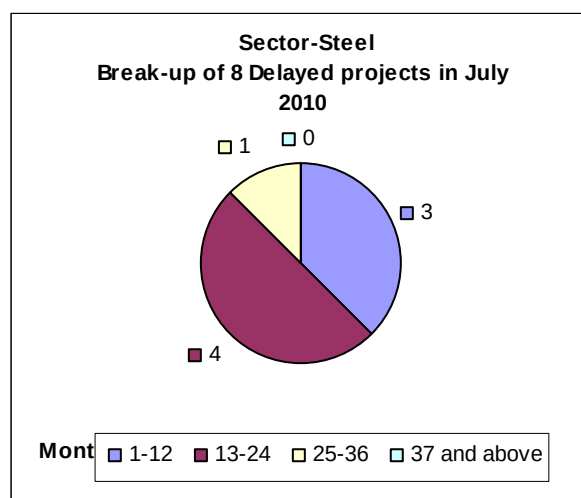

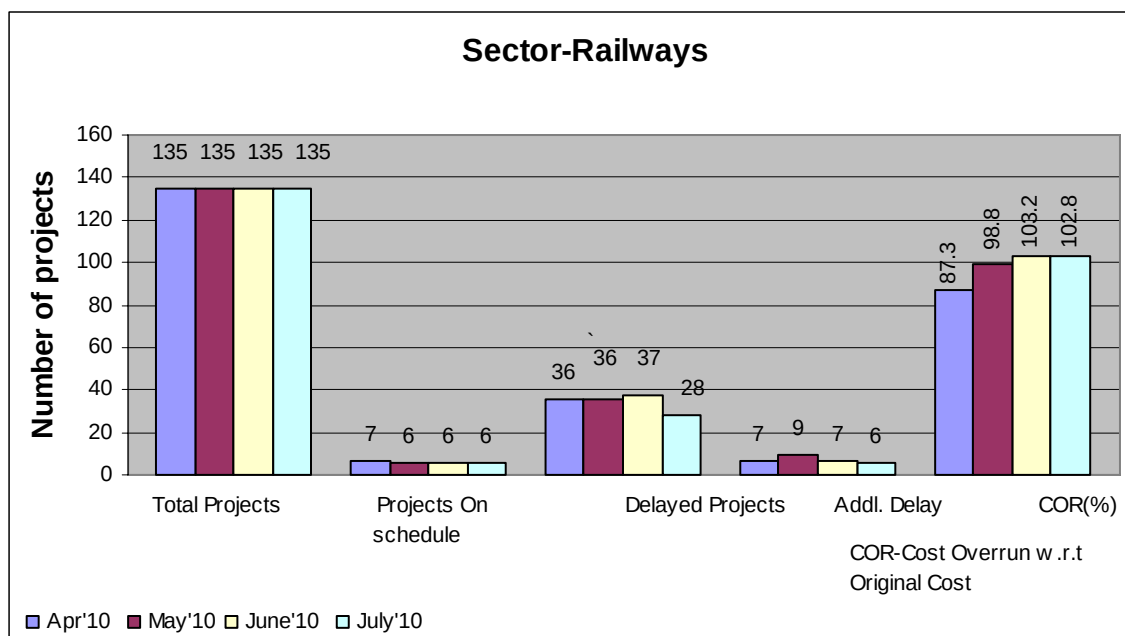



Break-up of Delayed projects in the month of July'10

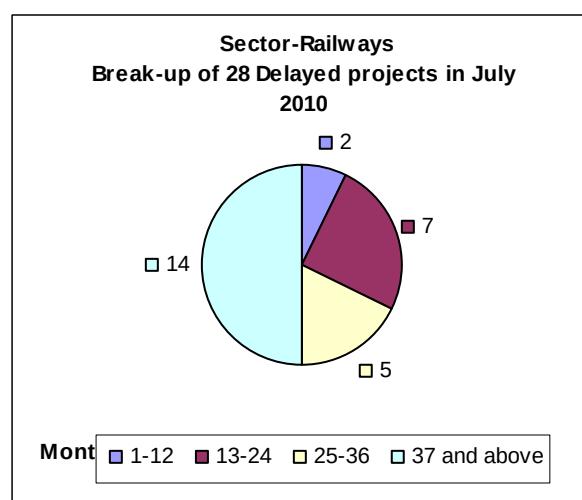

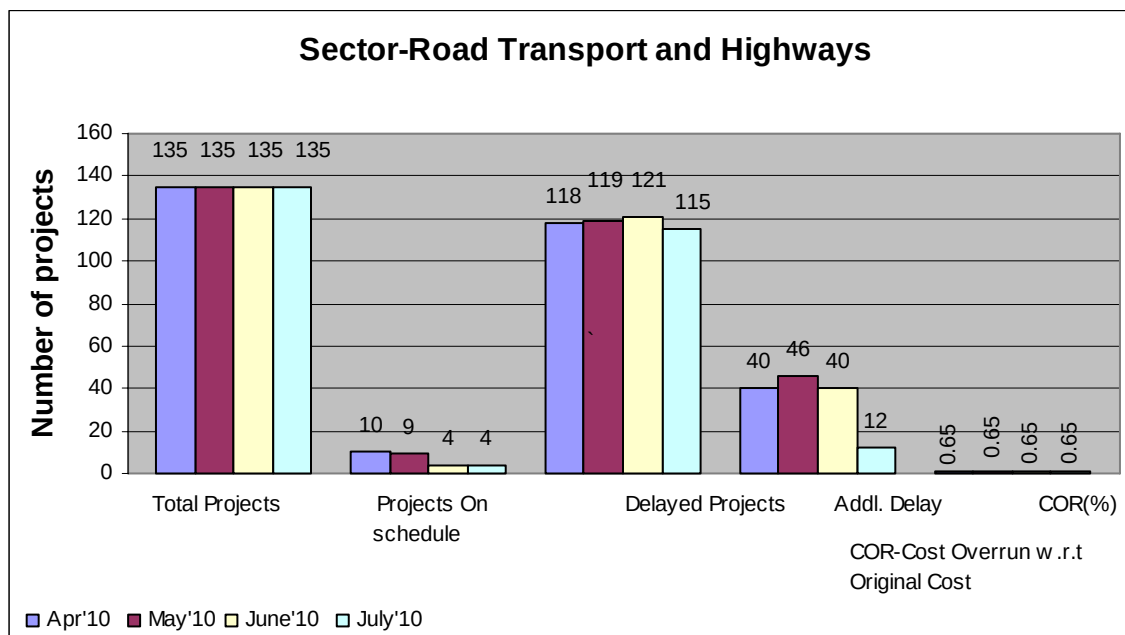


Break-up of Delayed projects in the month of July'10

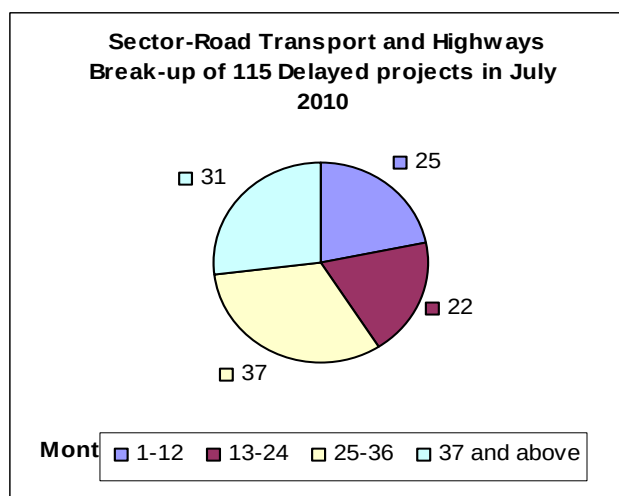

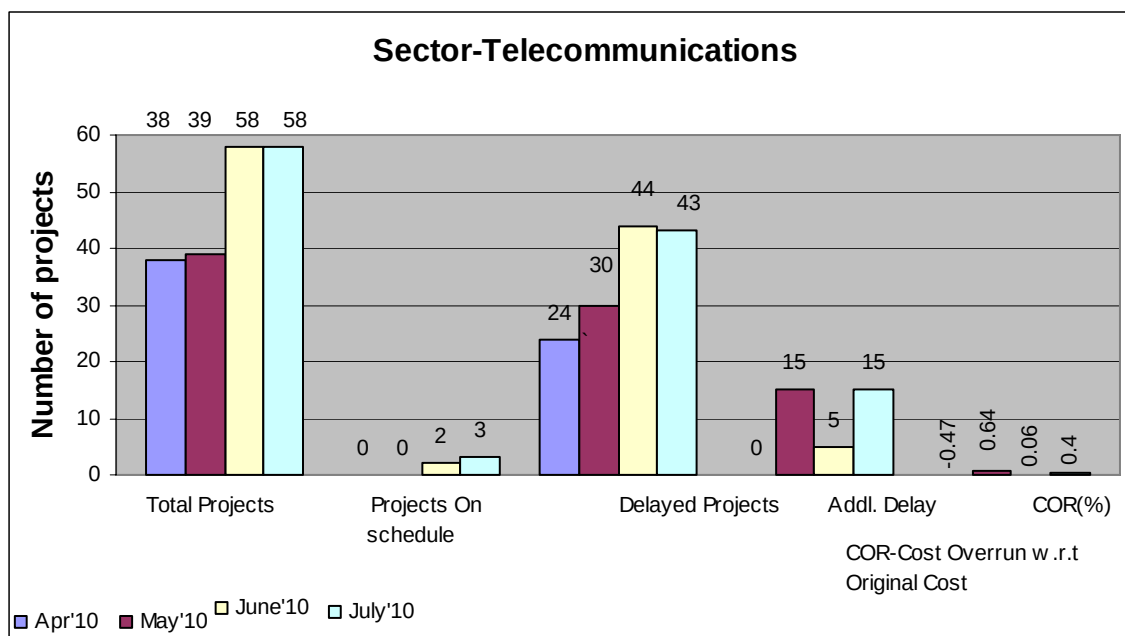

Break-up of Delayed projects in the month of July'10

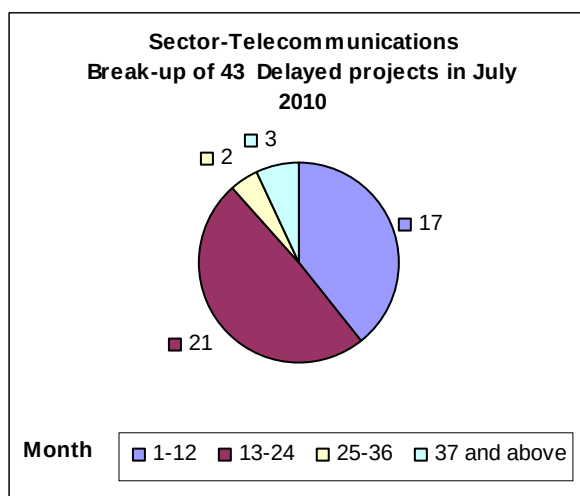

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	23,236.29
Civil Aviation	9	5,347.40	5,347.40	5,347.40
Coal	39	24,242.02	25,614.14	27,304.44
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,091.51	4,091.51
Steel	20	44,197.03	59,286.03	65,533.01
Petroleum	79	165,180.90	178,839.57	182,291.63
Power	85	179,619.98	181,434.06	188,867.08
Health & Family Welfare	1	71.18	422.60	443.15
Railways	135	51,007.64	56,356.00	103,480.09
Road Transport & Highways	135	41,863.55	41,863.55	42,136.98
Shipping & Ports	22	24,047.63	24,047.63	24,630.99
Telecommunications	58	27,020.91	27,179.96	27,154.89
Urban Development	2	15,071.00	16,763.36	30,503.36
Water Resources	1	542.90	542.90	1,187.00
Grand total	597	609,603.35	649,088.41	731,525.23

(Jul,2010)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]NPCIL,Karnataka	05/2001	4,213.00	3,282.00	2,564.00	10/2009 09/2007	08/2010	35(R1)	71/75
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	732.55	-	04/2011	-	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	13,171.00	13,113.00	12/2008	06/2011	30(O)	61/119
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	2,592.29	09/2010	09/2011	12(O)	8/80
Total			21,982.29	23,236.29	19,001.84				140/275
<u>Civil Aviation</u>									
5	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]AAI,Tamil Nadu	06/2009	213.35	213.35	112.00	09/2010	11/2010	2(O)	0/0
6	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
7	Extension of Secondary Runway(K2) - [N04000056]AAI,Tamil Nadu	08/2008	230.00	230.00	188.12	01/2011	01/2011	0(O)	0/0
8	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	1,942.51	579.26	05/2011	08/2011	3(O)	0/0
9	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73	204.73	5.97	05/2012	05/2012	0(O)	0/0
10	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]AAI,Gujarat	02/2007	290.92	290.92	239.59	-	-	-	1/24
11	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]AAI,Tamil Nadu	01/2008	535.00	535.00	143.97	06/2010	-	-	0/0
12	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	264.29	264.29	10.02	01/2011	-	-	0/0
13	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
Total			5,347.40	5,347.40	1,694.46				1/24
<u>Coal</u>									
14	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]NLC,Rajasthan	12/2004	254.07 254.60	254.60	215.84	06/2009	05/2010	11(O)	36/21
15	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,457.96	06/2009	10/2010	16(O)	59/26
16	BALRAM OCP EXTENSION - [N06000044]JMCL,Orissa	12/2007	172.08	172.08	484.90	03/2009	03/2011	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	1,998.81	06/2009 -	06/2011	24(O)	41/24
18	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	59.35	03/2010 -	03/2012	24(O)	0/4
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,	04/2006	471.66 341.63	341.63	101.48	03/2011 -	03/2012	12(O)	0/0
20	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,	10/2006	249.03 -	249.03	37.99	03/2012 -	03/2012	0(O)	8/42
21	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	529.40 -	259.40	0.63	03/2012 -	03/2012	0(O)	0/0
22	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	251.79	03/2012 -	03/2012	0(O)	0/0
23	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.57 -	418.97	90.05	- -	03/2012	-	7/27
24	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.91 -	181.19	0.07	- -	03/2012	-	2/34
25	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,904.54	914.50	08/2012 -	08/2012	0(O)	0/0
26	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,	09/2006	212.34 779.26	779.26	120.75	03/2013 09/2012	09/2012	0(R3)	2/22
27	KAKATIYA LAONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	-	- 12/2012	12/2012	0(R3)	7/44
28	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.56	136.15	03/2010 -	03/2013	36(O)	0/1
29	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	554.13	03/2011 03/2013	03/2013	0(R3)	0/4
30	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 -	437.34	136.45	03/2012 -	03/2013	12(O)	0/1
31	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 -	706.40	16.21	07/2012 -	03/2013	8(O)	0/1
32	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	11.40	- -	03/2013	-	0/83
33	KANIHA OCP - [N06000035]MCL,	12/2007	457.77 -	457.77	51.40	- -	03/2013	-	0/2
34	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.53	183.34	03/2013 -	03/2013	0(O)	0/0
35	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	999.31	03/2010 -	03/2014	48(O)	3/7
36	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	886.90	03/2010 -	03/2014	48(O)	2/6
37	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	137.48	03/2014 -	03/2014	0(O)	1/1
38	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	246.83	06/2014 -	03/2014	-3(O)	0/0
39	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	02/2006	50.08 -	153.82	3.74	03/2010 -	03/2014	48(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
40	PENGANGA OC - [N06000066]WCL,Andhra Pradesh	10/2008	339.77	339.77	-	-	03/2014	-	0/1
41	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2014	0(O)	0/0
42	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	211.51	03/2013	03/2014	12(O)	0/0
43	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	11/2009 01/2012	03/2015	38(R3)	0/0
44	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	24.33	03/2013	03/2015	24(O)	0/0
45	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2012	03/2015	36(O)	0/0
46	Batura OC - [N06000049]BCCL,Madhya pradesh	09/2008	203.82	203.82	-	03/2013	03/2015	24(O)	0/0
47	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/0
48	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	201.58	209.78	0.18	-	03/2015	-	0/31
49	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	27.23	03/2014	03/2016	24(O)	1/1
50	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.10	490.10	57.73	03/2014	03/2016	24(O)	0/0
51	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	6.04	03/2015	03/2016	12(O)	0/0
52	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	158.59	198.59	90.80	03/2016	03/2016	0(O)	0/0
Total			24,242.02	27,304.44	9,515.28				169/383
Fertilisers									
53	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,	01/2009	488.75	488.75	-	-	03/2011	-	0/1
54	CAPACITY ENHANCEMENT OF VIJAIPUR-I - [N08000007]FACT,Madhya pradesh	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
55	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]FACT,Madhya pradesh	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
56	PANIPATH - AMMONIA PLANT FEEDSTOCK PLANT - [N08000004]FACT,Haryana	01/2010	1,292.84	1,292.84	-	10/2012	10/2012	0(O)	0/0
57	BATHINDA - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000005]FACT,Punjab	01/2010	1,294.19	1,294.19	-	10/2012	10/2012	0(O)	0/0
58	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]FACT,Punjab	01/2010	1,478.63	1,478.63	-	10/2012	10/2012	0(O)	0/0
Total			5,317.41	5,317.41	.00				0/1
Mines									

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO,	10/2004	4,091.51 -	4,091.51	3,316.00	12/2008 -	-	-	18/111
	Total		4,091.51 -	4,091.51	3,316.00				18/111
<u>Steel</u>									
60	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]NMDC, Andhra Pradesh	01/2003	295.89 -	607.17	220.32	- -	06/2010	-	2/21
61	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]SAIL, Jharkhandd	10/2007	892.32 -	892.32	611.02	- -	07/2010	-	2/1
62	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]SAIL, West Bengal	03/2007	416.50 -	436.54	292.63	- -	08/2010	-	2/1
63	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]SAIL, Orissa	07/2007	302.70 -	302.70	240.29	06/2009 -	08/2010	14(O)	0/0
64	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]SAIL, Orissa	01/2008	197.66 -	197.66	123.91	- -	08/2010	-	0/0
65	POWER PLANT-I - [N12000039]RINL, Andhra Pradesh	09/2007	462.00 -	350.00	84.40	12/2009 -	08/2010	8(O)	0/0
66	EXPANSION OF SALEM STEEL PLANT - [N12000050]SAIL, Tamil Nadu	01/2008	1,902.00 -	1,902.00	5,279.38	- -	08/2010	-	2/6
67	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	353.00	80.00	02/2010 -	08/2010	6(O)	0/0
68	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL, Jharkhandd	07/2008	172.78 -	191.00	101.32	- -	11/2010	-	0/1
69	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	358.00	114.32	02/2010 -	01/2011	11(O)	0/0
70	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL, Jharkhandd	10/2007	500.90 -	500.90	203.11	- -	04/2011	-	0/2
71	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Madhya Pradesh	07/2007	111.28 -	232.93	60.23	- -	05/2011	-	0/1
72	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,228.00	6,203.00	10/2009 -	06/2011	20(O)	0/126
73	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	168.95	12.00	10/2009 -	06/2011	20(O)	0/0
74	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 -	14,443.00	8,292.02	- -	06/2011	-	0/6
75	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Andhra Pradesh	05/2008	480.00 -	480.84	4.04	09/2010 -	12/2011	15(O)	0/0
76	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhandd	01/2008	3,316.00 6,325.00	6,325.00	1,197.43	- 12/2011	12/2011	0(R3)	0/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
77	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	8,128.00	2,506.34	02/2011	03/2013	25(O)	0/0
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	1,241.83	- 03/2013	03/2013	0(R3)	0/8
79	AIR SEPARATION PLANT (ASU-4) - [N12000060]RINL,Andhra Pradesh	03/2008	96.00	170.00	42.02	06/2010	-	-	0/0
	Total		44,197.03	65,533.01	26,909.61				8/180
	Petroleum								
80	CHAINSA-JHAJJAR PIPE LINE PROJECT - [N16000047]GAIL,Haryana	11/2007	967.77	571.64	11.82	09/2009	03/2010	6(O)	0/0
81	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]IOCL,	04/2006	14,439.00	15,292.00	12,054.37	11/2009 11/2009	05/2010	6(R1)	61/101
82	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]IOCL,West Bengal	11/2005	1,876.00 2,869.00	3,154.00	2,728.21	04/2009 12/2009	02/2010	2(R1)	41/36
83	BINA DESPATCH TERMINAL - [N16000078]BPCL,Madhya pradesh	05/2007	490.71 639.11	639.11	581.93	12/2009 03/2010	03/2010	0(R3)	0/0
84	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]IOCL,Haryana	06/2005	250.66 350.00	389.00	350.96	06/2008	05/2010	23(O)	0/0
85	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]HPCL,Andhra Pradesh	11/2008	643.46	643.46	489.52	-	05/2010	-	0/2
86	LUBE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI REFINERY - [N16000026]HPCL,Maharashtra	10/2006	638.90 1,030.00	1,030.00	734.16	04/2009	07/2010	15(O)	0/0
87	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]GAIL,Multi State	11/2007	5,595.31 4,803.00	3,760.00	3,239.40	11/2009 04/2010	08/2010	4(R3)	0/0
88	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]IOCL,Assam	04/2008	372.00	325.00	213.94	02/2010	09/2010	7(O)	0/0
89	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]IOCL,Assam	04/2008	356.00	300.00	-	02/2010	09/2010	7(O)	0/0
90	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL) - [N16000049]GAIL,Multi State	11/2007	396.13	396.13	153.15	10/2009 06/2010	09/2010	3(R3)	0/0
91	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80 3,941.41	3,941.41	-	12/2009	09/2010	9(O)	0/0
92	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92	1,493.49	705.27	06/2006 07/2010	10/2010	3(R3)	0/2
93	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,	06/2006	1,431.91 1,646.39	1,676.00	1,403.15	09/2009 05/2008	10/2010	29(R3)	0/0
94	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]IOCL,Haryana	06/2005	1,007.83	1,087.00	740.43	12/2009 12/2009	10/2010	10(R1)	18/49

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
95	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]IOCL,Gujarat	01/2007	5,693.00 6,898.00	6,898.00	5,529.75	01/2010 06/2010	10/2010	4(R3)	0/0
96	MSQ UPGRADE PROJECT AT BARAUNI REFINERY - [N16000038]IOCL,Bihar	04/2008	1,492.00 -	1,505.00	975.54	04/2010 -	10/2010	6(O)	0/0
97	MSQ IMPROVEMENT PROJECT - [N16000040]BRPL,Assam	04/2008	293.60 -	293.60	175.60	12/2009 -	10/2010	10(O)	0/0
98	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	1.13	10/2010 -	10/2010	0(O)	0/0
99	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]HPCL,Maharashtra	03/2007	900.47 -	900.47	652.84	09/2009 -	10/2010	13(O)	0/0
100	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 -	224.00	99.55	12/2010 -	12/2010	0(O)	0/0
101	Guru Govind Singh Refinery Products Evacuation Project - [N16000076]HPCL,Punjab	01/2009	605.40 605.40	605.40	246.17	12/2010 12/2010	12/2010	0(R3)	12/17
102	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	120.30	12/2010 -	12/2010	0(O)	0/0
103	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	5.58	12/2010 -	12/2010	0(O)	0/0
104	CAPACITY AUGMENTATION OF AGRA& FEROSABAD REGION - [N16000074]GAIL,Uttar Pradesh	07/2009	199.57 -	199.57	1.00	- -	01/2011	-	9/7
105	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 -	600.00	525.82	03/2007 -	03/2011	48(O)	3/3
106	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 834.90	1,200.00	1,067.54	03/2007 03/2011	03/2011	0(R3)	6/6
107	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 -	219.22	162.17	03/2006 -	03/2011	60(O)	6/6
108	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.62	12/2008 12/2008	03/2011	27(R3)	0/0
109	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 -	2,305.30	2,056.13	06/2010 06/2010	03/2011	9(R3)	0/0
110	NORTH TAPTI GAS FIELD DEV. - [N16000085]ONGC,Gujarat	07/2008	589.70 -	589.70	-	03/2011 -	03/2011	0(O)	0/0
111	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	01/2010	589.70 755.56	755.56	-	03/2011 -	03/2011	0(O)	0/0
112	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	10/2010	1,816.07 1,816.07	1,816.07	289.93	- 04/2011	04/2011	0(R3)	0/2
113	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Gujarat	11/2007	4,429.38 4,403.00	2,800.00	1,270.91	- 04/2011	04/2011	0(R3)	0/2
114	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Multi State	11/2007	1,512.00 1,434.00	975.00	622.65	- 04/2011	04/2011	0(R3)	0/2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
115	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,061.93 1,167.00	1,167.00	20.09	- 04/2011	04/2011	0(R3)	0/2
116	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70 -	706.70	450.36	04/2010 -	04/2011	12(O)	0/0
117	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08 -	305.08	69.38	04/2011 -	04/2011	0(O)	0/0
118	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,234.69	03/2005 05/2011	05/2011	0(R3)	0/0
119	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 -	330.40	-	05/2010 -	05/2011	12(O)	0/0
120	MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21 -	162.12	-	03/2009 -	05/2011	26(O)	0/0
121	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	463.32	-	- -	06/2011	-	3/9
122	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	540.92	-	- -	06/2011	-	7/9
123	Construction of Tank and Blending Facility at Vadi - [N16000075]IOCL, Gujarat	02/2009	267.00 -	267.00	72.99	- -	08/2011	-	0/1
124	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 -	3,597.00	110.15	09/2011 -	09/2011	0(O)	0/0
125	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
126	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 -	756.00	387.28	12/2011 -	12/2011	0(O)	0/0
127	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL, Gujarat	02/2009	349.00 -	349.00	40.73	08/2011 -	12/2011	4(O)	0/0
128	HYDROCRACKER REVAMP & SETTING - [N16000081]BPCL, Maharashtra	02/2008	825.00 -	825.00	72.80	12/2011 -	12/2011	0(O)	0/0
129	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	154.37	12/2011 -	12/2011	0(O)	0/0
130	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	-	12/2011 -	12/2011	0(O)	0/0
131	Additional Development of D-1 Field - [N16000097]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	-	12/2011 -	12/2011	0(O)	0/0
132	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	411.41	03/2010 03/2012	03/2012	0(R1)	0/0
133	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL, Uttar Pradesh	06/2009	3,032.00 348.00	348.00	6.52	- -	03/2012	-	6/12

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
134	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Gujarat	07/2009	7,596.18 6,652.22	6,652.22	0.65	01/2013 -	03/2012	-10(O)	0/0
135	ASSAM GAS CRACKER PROJECT - [N16000100]BCPL,Assam	04/2006	5,460.61 -	5,460.61	954.64	04/2012 -	04/2012	0(O)	0/0
136	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 -	6,326.40	889.65	05/2010 -	05/2012	24(O)	0/0
137	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	1,552.63 2,920.82	2,920.82	78.13	02/2009 09/2010	05/2012	20(R1)	0/0
138	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	-	07/2010 -	05/2012	22(O)	0/0
139	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	0.61	03/2010 08/2010	06/2012	22(R1)	0/0
140	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]IOCL,Maharashtra	12/2009	1,492.33 -	1,492.33	22.57	06/2012 -	06/2012	0(O)	0/0
141	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	8.53	04/2011 -	07/2012	15(O)	0/0
142	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	-	08/2012 -	08/2012	0(O)	0/0
143	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	6,855.93 -	6,855.93	632.36	09/2012 -	09/2012	0(O)	0/0
144	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]IOCL,Maharashtra	08/2009	1,793.00 -	1,793.00	9.39	09/2012 -	09/2012	0(O)	0/0
145	Construction of six Effluent Treatment Plants (ETP) - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	234.78	-	09/2012 -	09/2012	0(O)	0/0
146	PARADIP REFINERY PROJECT - [N16000058]IOCL,	02/2009	29,777.00 -	29,777.00	3,843.04	- -	11/2012	-	0/82
147	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	9.77	12/2011 -	11/2012	11(O)	0/0
148	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	4,508.38	6.97	- -	12/2012	-	11/10
149	De-bottlenecking of SMPL - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	1.55	- -	12/2012	-	0/0
150	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	06/2007	1,252.75 8,813.41	8,813.41	4,791.34	06/2009 03/2013	03/2013	0(R3)	0/0
151	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	211.94	03/2013 -	03/2013	0(O)	0/0
152	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
153	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
154	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
155	CAPACITY EXPANSION AND MODERNISATION OF KOCHI REFINERY - [N16000028]BPCL,Kerala	04/2006	2,591.80	3,941.41	1,793.00	09/2009	-	-	0/0
156	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]IOCL,Uttar Pradesh	01/2008	348.00	348.00	186.58	12/2009	-	-	0/0
157	MSQ UPGRADE PROJECT AT PANIPAT REFINERY - [N16000035]IOCL,Haryana	01/2008	1,131.00	1,131.00	750.71	12/2009	-	-	0/0
158	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68	238.68	-	-	-	-	1/8
Total			165,180.90	182,291.63	56,951.74				184/368
Power									
159	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72	913.63	215.96	07/2006	03/2010	44(O)	2/5
160	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	947.96	767.27	12/2007	06/2010	30(O)	14/18
161	SEWA- II H.E.P (NHPC) - [180100220]NHPC,J & K	09/2003	665.46	1,016.74	982.76	09/2007	07/2010	34(O)	8/36
162	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]NHPC,Multi State	12/2007	227.52	227.52	114.42	06/2010	09/2010	3(O)	0/0
163	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]PGCIL,Haryana	04/2008	290.49	299.08	269.78	04/2010	09/2010	5(O)	0/0
164	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]NHPC,Himachal Pr.	09/2007	262.10	262.10	137.79	09/2010	09/2010	0(O)	0/0
165	KORBA STPP STAGE-III - [N18000011]NTPC,Madhya pradesh	08/2006	2,448.50	2,448.49	2,008.00	02/2010	10/2010	8(O)	5/24
166	National Capital Thermal Power Project Stage-II - [N18000013]NTPC,Uttar Pradesh	10/2006	5,135.33	5,135.33	4,062.00	10/2010	10/2010	0(O)	11/40
167	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34	241.27	148.40	06/2008	11/2010	29(O)	8/20
168	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]PGCIL,Gujarat	02/2008	340.72	340.72	134.01	11/2010	11/2010	0(O)	0/0
169	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]PGCIL,Haryana	02/2008	261.55	261.55	136.99	11/2010	11/2010	0(O)	0/0
170	KOTESHWAR HEP(THDC) - [180100184]THDC,Uttaranchal	04/2000	1,301.56	2,398.39	1,955.04	04/2005	12/2010	68(O)	2/22
171	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,477.56	08/2010	12/2010	4(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
172	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,402.62	09/2009	12/2010	15(O)	15/30
173	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70	803.76	601.69	06/2009	12/2010	18(O)	1/20
174	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Uttar Pradesh	10/2006	975.96	894.26	609.70	10/2009	12/2010	14(O)	2/20
175	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.01	611.02	643.73	08/2010	12/2010	4(O)	0/0
176	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]PGCIL,Multi State	12/2007	417.76	417.76	258.97	12/2010	12/2010	0(O)	0/0
177	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]PGCIL,Uttar Pradesh	12/2007	408.36	408.36	287.54	12/2010	12/2010	0(O)	0/0
178	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	30.85	01/2011	01/2011	0(O)	0/0
179	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,729.29	1,724.79	1,158.15	11/2009	02/2011	15(O)	0/0
180	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]NHPC,J & K	08/2006	621.26	621.28	466.15	02/2011	02/2011	0(O)	0/1
181	Farakka STPP Stage-III - [N18000016]NTPC,West Bengal	07/2006	2,570.44	2,570.44	1,766.00	08/2010	02/2011	6(O)	13/26
182	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,472.97	07/2010	03/2011	8(O)	3/20
183	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	296.07	09/2010	03/2011	6(O)	0/0
184	URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	1,724.79	1,141.80	-	05/2011	-	0/0
185	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.53	3,133.00	05/2011	05/2011	0(O)	0/0
186	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,304.52	1,077.57	10/2010	06/2011	8(O)	0/0
187	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	353.56	01/2010	06/2011	17(O)	0/22
188	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	77.53	06/2011	06/2011	0(O)	0/0
189	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	127.57	06/2011	06/2011	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]PGCIL,Multi State	07/2008	525.14	525.14	340.02	07/2011	07/2011	0(O)	0/0
191	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	193.00	07/2011	07/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
192	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	17.93	07/2011	07/2011	0(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	80.16	08/2011	08/2011	0(O)	0/0
194	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,591.86	11/2008	09/2011	34(O)	25/38
195	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]PGCIL,Multi State	12/2008	328.97	328.97	134.72	09/2011	09/2011	0(O)	0/0
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	178.82	11/2011	11/2011	0(O)	0/0
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	79.48	11/2011	11/2011	0(O)	0/0
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	13.89	11/2011	11/2011	0(O)	0/0
199	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	41.48	11/2011	11/2011	0(O)	0/0
200	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]NHPC,West Bengal	10/2003	768.92	845.46	1,162.32	03/2007	12/2011	57(O)	1/25
201	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	6,835.00	12/2009	12/2011	24(O)	33/56
202	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	54.44	01/2012	01/2012	0(O)	0/0
203	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	63.03	02/2012	02/2012	0(O)	0/0
204	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	4.51	02/2012	02/2012	0(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	81.86	02/2012	02/2012	0(O)	0/0
206	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	112.99	07/2010	02/2012	19(O)	0/0
207	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	331.52	02/2012	02/2012	0(O)	0/0
208	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,238.00	04/2009	03/2012	35(O)	19/41
209	RAMPUR HEP(412 MW) - [N18000024]SJVN,	01/2007	2,047.03	2,047.03	909.61	01/2012	03/2012	2(O)	2/10
210	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	1,235.00	07/2011	03/2012	8(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
211	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	14.62	04/2012	04/2012	0(O)	0/0
212	765KV System for central part of Northern Region Grid - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	78.26	05/2012	05/2012	0(O)	0/0
213	765KV System for Central part of Northern Region G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	-	06/2012	06/2012	0(O)	0/0
214	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	4.56	06/2012	06/2012	0(O)	0/0
215	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38	1,061.38	769.48	09/2009	08/2012	35(O)	0/0
216	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,	12/2008	573.99	573.99	99.48	08/2012	08/2012	0(O)	4/21
217	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,139.98	08/2012	08/2012	0(O)	0/0
218	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	2,126.58	08/2012	08/2012	0(O)	0/0
219	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	87.87	08/2012	08/2012	0(O)	0/0
220	MOUDA STPP - [N18000048]NTPC,Maharashtra	11/2007	5,459.28	6,010.89	1,244.00	02/2012	10/2012	8(O)	0/0
221	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	654.25	10/2012	10/2012	0(O)	0/0
222	MAUDA Transmission System - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	9.84	10/2012	10/2012	0(O)	0/0
223	VINDHYACHAL STTP STAGE-IV - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	833.00	11/2012	11/2012	0(O)	0/0
224	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	723.00	11/2012	11/2012	0(O)	0/0
225	Transmission System of Vindhuachal -IV & Rihand -I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	11.89	11/2012	11/2012	0(O)	0/0
226	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2012	965.58	965.58	64.67	11/2012	11/2012	0(O)	0/0
227	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	7,451.99	4,124.79	09/2010	12/2012	27(O)	2/11
228	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]PGCIL,Himachal Pr.	12/2005	358.42	358.42	6.57	12/2008 09/2010	12/2012	27(R1)	0/15
229	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
230	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	1,070.07	12/2012	12/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
231	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	63.57	12/2012	12/2012	0(O)	0/0
232	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	2,846.67	09/2009	03/2013	42(O)	1/20
233	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	894.00	03/2013	03/2013	0(O)	5/31
234	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	3,253.22	1,217.03	05/2013	05/2013	0(O)	77/54
235	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	1,097.00	08/2013	08/2013	0(O)	0/0
236	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	1,225.49	08/2013	08/2013	0(O)	0/0
237	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,692.97	4,826.00	11/2010	04/2014	41(O)	15/51
238	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00	3,124.76	246.74	07/2010	12/2014	53(O)	0/0
239	Transm System for development of Pooling stn. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
240	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	2,491.58	115.17	07/2014	03/2015	8(O)	0/8
241	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	332.60	07/2014	01/2016	18(O)	0/0
242	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,Manipur	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
243	Immsdiate evacuation system for NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	10.12	06/2012	-	-	0/0
Total			179,619.98	188,867.08	73,533.05				274/719
Health & Family Welfare									
244	NORTH EAST INDIRA GANDHI INST-ITUTE OF HEALTH & MS - [210100001]H&FW,Meghalaya	05/1986	71.18	443.15	477.33	03/1999	-	-	7/16
			422.60			03/2005			
Total			71.18	443.15	477.33				7/16
Railways									
245	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	576.17	-	03/2010	-	0/0
			-			-			
246	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00	503.16	489.98	-	03/2010	-	0/0
			-			-			
247	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09	881.19	86.35	-	07/2010	-	0/0
			-			-			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
248	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]RVNL,Kerala	07/2006	246.50 246.50	246.50	-	03/2009 03/2009	11/2009	8(R3)	0/0
249	RAJGIR-TILAIYA (NL), ECR - [220100312]ECR,Bihar	04/2001	180.82 180.82	180.82	264.46	03/2006 -	01/2010	46(O)	0/0
250	MIRAJ-LATUR ROAD(GC),CR - [220100162]CR,Maharashtra	04/1993	225.00 360.63	816.40	793.83	03/2001 -	03/2010	108(O)	0/0
251	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]NEFR,Multi State	11/1998	536.85 -	1,010.00	1,002.75	03/2003 -	03/2010	84(O)	0/0
252	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]RVNL,Tamil Nadu	10/2001	223.00 -	665.00	-	- 11/2008	03/2010	16(R1)	0/0
253	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	639.54	767.52	06/2007 -	03/2010	33(O)	0/0
254	BHILDI-SAMDARI (GC) - [220100291]RVNL,Gujarat	04/1999	244.74 479.00	479.00	-	- 03/2009	03/2010	12(R1)	0/0
255	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	235.19	03/2008 03/2009	03/2010	12(R1)	0/0
256	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 732.80	732.80	-	03/2008 06/2008	03/2010	21(R3)	0/0
257	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	501.12	03/1996 06/2009	06/2010	12(R1)	0/0
258	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	-	04/2003 03/2010	06/2010	3(R1)	0/0
259	ABOHAR- FAZILKA - [N22000055]NL,Punjab	09/2001	86.44 -	209.57	197.85	03/2009 -	08/2010	17(O)	0/0
260	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	325.00	300.18	- -	09/2010	-	0/0
261	TOLLYGANJ-GARIA(MTP) - [220100268]MRTP,West Bengal	03/2000	907.69 -	1,032.76	834.19	12/2006 -	09/2010	45(O)	0/0
262	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]ER,Jharkhand	02/1999	180.73 -	358.00	309.87	12/2006 12/2008	11/2010	23(R1)	0/0
263	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	11/2010	-51(O)	0/0
264	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]MRTP,Maharashtra	03/1996	401.81 -	495.44	308.10	03/2004 -	12/2010	81(O)	0/0
265	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	724.31	685.33	- -	12/2010	-	0/0
266	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 -	762.33	244.42	- 12/2009	12/2010	12(R1)	0/0
267	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	-	- 02/2009	12/2010	22(R1)	0/0
268	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	-	- 03/2009	12/2010	21(R1)	0/0
269	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	-	12/2007 03/2010	12/2010	9(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
270	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]RVNL,Rajasthan	04/2005	352.00 716.64	718.30	-	03/2008 08/2008	12/2010	28(R1)	0/0
271	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
272	SHIMOGA-TALAGUPPA - [N22000056]GC,Karnataka	12/1992	46.00 -	218.00	219.28	- -	12/2010	-	0/0
273	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 200.80	200.80	-	- -	12/2010	-	0/0
274	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]JMRT,Maharashtra	04/2003	3,125.20 -	4,103.20	3,736.36	- -	12/2010	-	0/1
275	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 -	465.00	112.11	- -	02/2011	-	0/0
276	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	03/1997	100.00 -	332.75	362.39	- -	02/2011	-	0/0
277	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.17	391.42	02/2010 -	02/2011	12(O)	0/0
278	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECR,Orissa	04/2005	726.96 -	810.78	52.00	- 03/2011	02/2011	-1(R3)	0/0
279	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	356.87	121.93	- 03/2010	03/2011	12(R1)	0/0
280	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	306.62	06/1999 -	03/2011	141(O)	0/0
281	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECR,Orissa	04/1993	100.00 119.29	170.00	128.00	03/2002 -	03/2011	108(O)	0/0
282	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	193.78 -	456.45	247.29	06/2004 -	03/2011	81(O)	0/0
283	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	467.10	05/2008 -	03/2011	34(O)	0/0
284	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 -	214.09	134.90	12/2009 -	03/2011	15(O)	0/0
285	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]SCR,Andhra Pradesh	05/2002	304.50 -	306.00	341.81	- -	03/2011	-	0/0
286	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECR,Orissa	04/1994	355.38 -	700.00	99.00	- -	03/2011	-	0/0
287	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	266.35	- -	03/2011	-	0/0
288	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/1997	143.92 -	168.80	70.43	- -	03/2011	-	0/0
289	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
290	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]ECR,Bihar	04/1996	114.01 283.95	348.78	315.34	- -	03/2011	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
291	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 329.70	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
292	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]NEFR,Multi State	12/2006	170.00 -	272.11	180.55	- -	03/2011	-	0/0
293	BARDHAMAN-KATWA (GC) - [N22000091]GC,West Bengal	04/2007	245.15 -	245.15	34.57	12/2010 -	03/2011	3(O)	0/0
294	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
295	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0
296	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]GC,Gujarat	04/2006	196.97 -	196.97	114.91	03/2011 -	03/2011	0(O)	0/0
297	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 252.50	252.50	73.00	02/2010 -	11/2011	21(O)	0/0
298	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
299	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	727.52	470.54	- -	03/2012	-	0/0
300	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	174.67	- -	03/2012	-	0/0
301	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]MRTP,Tamil Nadu	04/2006	415.59 -	495.74	74.69	- -	03/2012	-	0/0
302	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	-	03/2010 -	03/2012	24(O)	0/0
303	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]GC,Bihar	04/1997	501.69 -	501.69	45.90	03/2010 -	03/2012	24(O)	0/0
304	TAMLUK DIGHA - [N22000097]LD,West Bengal	03/1984	293.97 -	293.97	313.13	06/2005 -	04/2012	82(O)	0/0
305	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	278.10	- -	07/2012	-	0/0
306	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 274.56	540.96	475.20	03/1994 -	12/2012	225(O)	0/0
307	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 654.51	1,160.52	484.07	- -	12/2012	-	0/0
308	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1997	248.44 576.27	1,103.47	669.40	- -	12/2012	-	0/0
309	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	234.45	151.77	- -	12/2012	-	0/0
310	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	340.69	03/2009 -	12/2012	45(O)	0/0
311	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,480.71	445.84	10/2007 -	12/2012	62(O)	0/0
312	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
313	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]LD, Uttar Pradesh	04/2006	325.00 -	496.03	88.06	03/2010 -	12/2012	33(O)	0/0
314	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 -	410.08	105.58	- -	03/2013	-	0/0
315	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	567.11	- -	03/2013	-	0/0
316	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]NEFR,Multi State	01/2004	912.70 915.70	1,556.23	261.35	- -	03/2013	-	0/0
317	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	04/1996	1,000.00 1,500.00	3,230.01	1,906.42	04/2008 12/2011	03/2014	27(R1)	0/0
318	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]NEFR,Multi State	02/2000	733.00 733.00	1,655.80	512.55	12/2008 -	03/2014	63(O)	0/0
319	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	160.48	97.39	- -	03/2014	-	0/0
320	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]NEFR,Assam	09/2006	200.00 -	390.00	0.78	- -	03/2014	-	0/0
321	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	110.99	03/2014 -	03/2014	0(O)	0/0
322	AGARTALA SABROOM - [N22000099]NL,Tripura	04/2008	813.34 -	813.34	85.97	03/2014 -	03/2014	0(O)	0/0
323	BHAIRABI SAIRONG - [N22000100]NL,Mizoram	04/2008	619.34 -	2,429.41	0.78	04/2014 -	03/2014	-1(O)	0/0
324	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	131.29	- -	03/2015	-	0/0
325	SEVOK RANGPO - [N22000102]LD,Sikkim	04/2008	1,339.48 -	1,339.48	1.42	12/2015 -	12/2015	0(O)	0/0
326	JIRIBAM TO IMPHAL (TUPUI)(NL),(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,123.52	205.04	03/2011 -	03/2016	60(O)	0/0
327	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 -	16,000.00	-	03/2001 -	12/2017	201(O)	0/0
328	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	556.48	03/1995 -	-	-	0/0
329	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 -	617.63	386.41	- -	-	-	0/0
330	HOTGI-GADAG(GC),SWR - [220100125]SWR,Multi State	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
331	AMBALA-MORADABAD(RE) - [220100131]RE,Multi State	03/1993	152.21 157.76	265.00	265.33	03/1998 -	-	-	0/0
332	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]NEFR,West Bengal	01/1986	36.80 274.41	285.93	231.74	- -	-	-	0/0
333	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]SECR,Chhatisgarh	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
334	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 -	675.00	315.61	- 12/2010	-	-	0/0
335	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	880.00	421.71	- -	-	-	0/0
336	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
337	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
338	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 -	563.25	539.91	03/2004 03/2010	-	-	0/0
339	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	712.00	363.60	- -	-	-	0/0
340	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1997	155.74 164.36	429.49	363.58	02/2009 -	-	-	0/0
341	HUBLI-AKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	337.82	49.69	- -	-	-	0/0
342	HOSPET-GUNTAKAL(LD),SCR - [220100195]RVNL,Multi State	03/1996	105.22 -	268.00	283.49	12/1999 03/2008	-	-	0/0
343	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
344	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1996	377.32 236.41	497.47	82.45	- -	-	-	0/0
345	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	154.30	106.79	03/2007 03/2007	-	-	0/0
346	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
347	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 -	1,099.20	711.79	07/2005 -	-	-	0/0
348	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]SR,Kerala	03/2001	178.76 177.34	219.94	190.49	- -	-	-	0/0
349	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	63.65	- -	-	-	0/0
350	PURNA-AKOLA (G.C), SCR - [220100253]SCR,Maharashtra	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
351	BIDAR-GULBARGA,SCR(NL) - [220100254]SCR,Karnataka	02/1999	242.42 369.70	369.70	151.69	- 05/2009	-	-	0/0
352	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
353	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	09/2001	320.10 -	320.10	108.05	- -	-	-	0/1
354	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	03/1997	78.23 -	162.87	72.45	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 -	548.96	407.73	- -	-	-	0/0
356	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
357	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, Multi State	04/1998	92.63 -	228.09	198.33	- -	-	-	0/0
358	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, Multi State	04/2000	138.00 240.59	607.09	194.84	- 12/2012	-	-	0/0
359	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 -	1,300.00	0.29	- -	-	-	0/0
360	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 -	325.17	311.98	03/2005 12/2008	-	-	0/0
361	DHARMAVARAM-PAKALA (GC), SCR - [220100282]SCR, Andhra Pradesh	04/1997	200.00 294.99	610.07	724.45	- 02/2009	-	-	0/0
362	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 -	418.17	52.53	- -	-	-	0/0
363	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	144.20	- -	-	-	0/0
364	KICHHA-KHATIMA (NL) - NER - [220100317]NER, Uttaranchal	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
365	HATHUA-BHATNI (N L) (NER) - [220100319]NER, Multi State	04/2005	200.73 -	230.03	45.76	- -	-	-	0/0
366	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
367	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]SCR, Andhra Pradesh	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
368	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 -	671.82	1.05	- -	-	-	0/0
369	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER, Jharkhand	03/1998	186.92 -	261.70	0.08	02/2006 -	-	-	0/0
370	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 -	224.51	41.39	- -	-	-	0/0
371	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR, Tamil Nadu	09/2007	404.19 -	900.00	60.44	- -	-	-	0/0
372	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, Tamil Nadu	09/2006	343.17 -	900.00	219.40	- -	-	-	0/0
373	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, Tamil Nadu	09/2006	125.00 -	227.40	14.30	- -	-	-	0/0
374	TIDIVANAM-NAGARI (NL) - [N22000085]SR, Tamil Nadu	09/2006	456.00 -	582.83	28.22	- -	-	-	0/0
375	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR, Bihar	09/2006	300.00 300.00	529.88	25.52	- -	-	-	0/0
376	BHAKURA DAMODAR - [N22000098]LD, West Bengal	03/1998	282.70 -	325.17	48.64	07/2008 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
377	KISHANGANJ JALALGARH - [N22000101]SR(NL),Bihar	04/2008	282.92	333.76	0.71	-	-	-	0/0
378	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]GC,Assam	04/1993	100.41	949.22	15.65	12/2009	-	-	0/0
379	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08	1,010.00	65.02	-	-	-	0/0
			353.08			12/2012			
	Total		51,007.64	103,480.09	34,362.24				0/2
			-						
Road Transport & Highways									
380	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]NHAI,Uttar Pradesh	04/2000	372.40	372.40	-	07/2004	06/2010	71(O)	0/0
			-			-			
381	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]NHAI,Jharkhand	04/2000	399.75	399.75	-	03/2005	06/2010	63(O)	0/0
			-			-			
382	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	-	11/2007	06/2010	31(O)	0/0
			-			-			
383	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	-	02/2004	06/2010	76(O)	0/0
			-			-			
384	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	-	08/2004	07/2010	71(O)	0/0
			-			-			
385	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]NHAI,Bihar	12/2003	310.00	310.00	392.26	04/2008	07/2010	27(O)	0/0
			-			-			
386	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]NHAI,Andhra Pradesh	12/2003	360.42	360.42	478.40	11/2009	07/2010	8(O)	0/0
			-			-			
387	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]NHAI,Kerala	04/2000	106.00	193.00	141.71	08/2006	08/2010	48(O)	0/0
			-			-			
388	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]NHAI,Multi State	04/2000	467.93	467.93	453.64	03/2005	08/2010	65(O)	0/0
			-			-			
389	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]NHAI,Tamil Nadu	12/2003	480.00	480.00	825.00	11/2007	08/2010	33(O)	0/0
			-			-			
390	MADURAI -KANIYAKUMARI SECTION (NS-41/TN) NH-7, KM.80 TO KM.120 - [240106240]NHAI,Tamil Nadu	12/2003	323.36	323.36	189.90	03/2008	08/2010	29(O)	0/0
			-			-			
391	MADURAI -KANNIYAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]NHAI,Tamil Nadu	12/2003	507.49	507.49	342.80	03/2008	08/2010	29(O)	0/0
			-			-			
392	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]NHAI,Punjab	03/2005	263.00	263.00	411.80	02/2009	08/2010	18(O)	0/0
			-			-			
393	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]NHAI,Assam	12/2003	225.00	225.00	196.40	06/2008	08/2010	26(O)	0/0
			-			-			
394	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	196.11	06/2008	08/2010	26(O)	0/0
			-			-			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
395	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]NHAI,Andhra Pradesh	12/2003	205.92	205.92	198.10	08/2009	08/2010	12(O)	0/0
396	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]NHAI,Andhra Pradesh	12/2003	243.64	243.64	254.50	08/2009	08/2010	12(O)	0/0
397	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]NHAI,Andhra Pradesh	12/2003	194.80	194.80	174.60	08/2009	08/2010	12(O)	0/0
398	BANGALORE-NEELAMANGALALA NH-4 - [N24000104]NHAI,Karnataka	03/2005	445.00	445.00	798.60	07/2010	08/2010	1(O)	0/0
399	ISLAM NAGAR TO KADTAL - [N24000109]NHAI,Andhra Pradesh	12/2003	546.83	546.83	667.80	03/2010	08/2010	5(O)	0/0
400	AMRITSAR-WAGHA BORDER - [N24000121]NHAI,Punjab	06/2008	205.88	205.88	212.20	06/2010	08/2010	2(O)	0/0
401	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	-	08/2004	09/2010	73(O)	0/0
402	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	317.24	03/2005	09/2010	66(O)	0/0
403	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	876.90	11/2010	09/2010	-2(O)	0/0
404	NAGAON BYPASS (NH-37)(NHAI) - [240106289]NHAI,Assam	12/2003	230.00	230.00	282.50	06/2008	09/2010	27(O)	0/0
405	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	240.50	10/2008	09/2010	23(O)	0/0
406	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]NHAI,Andhra Pradesh	12/2003	239.19	239.19	216.60	09/2009	09/2010	12(O)	0/0
407	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	232.50	09/2009	09/2010	12(O)	0/0
408	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	243.10	09/2009	09/2010	12(O)	0/0
409	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
410	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]NHAI,Multi State	03/2008	424.00	424.00	298.38	09/2010	09/2010	0(O)	0/0
411	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00	193.00	284.10	10/2008	10/2010	24(O)	0/0
412	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00	217.00	310.30	10/2008	10/2010	24(O)	0/0
413	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]NHAI,Uttar Pradesh	12/2003	239.00	239.00	373.70	10/2008	10/2010	24(O)	0/0
414	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]NHAI,Uttar Pradesh	12/2003	205.00	205.00	300.10	10/2008	10/2010	24(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]NHAI,Uttar Pradesh	12/2003	212.00 -	212.00	330.60	10/2008 -	10/2010	24(O)	0/0
416	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]NHAI,Uttar Pradesh	12/2003	451.97 -	451.97	485.80	04/2008 -	10/2010	30(O)	0/0
417	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]NHAI,Andhra Pradesh	12/2003	208.46 -	208.46	191.30	08/2009 -	10/2010	14(O)	0/0
418	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]NHAI,Andhra Pradesh	12/2003	243.38 -	243.38	249.80	09/2008 -	10/2010	25(O)	0/0
419	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00 -	309.00	473.20	06/2010 -	10/2010	4(O)	0/0
420	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	232.00	10/2009 -	10/2010	12(O)	0/0
421	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	238.30	07/2010 -	10/2010	3(O)	0/0
422	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00 -	565.00	842.30	07/2010 -	10/2010	3(O)	0/0
423	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	425.61	03/2005 -	12/2010	69(O)	0/0
424	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	244.30	07/2004 -	12/2010	77(O)	0/0
425	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	-	04/2007 -	12/2010	44(O)	0/0
426	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	-	09/2007 -	12/2010	39(O)	0/0
427	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	193.09	129.40	03/2008 -	12/2010	33(O)	0/0
428	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	166.27	96.05	03/2008 -	12/2010	33(O)	0/0
429	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	284.00	296.00	05/2008 -	12/2010	31(O)	0/0
430	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	-	03/2008 -	12/2010	33(O)	0/0
431	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	560.71	03/2009 -	12/2010	21(O)	0/0
432	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	204.70	01/2009 -	12/2010	23(O)	0/0
433	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	199.81	28.39	04/2009 -	12/2010	20(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
434	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	39.49	11/2008	12/2010	25(O)	0/0
435	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	318.70	12/2008	12/2010	24(O)	0/0
436	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	300.60	12/2008	12/2010	24(O)	0/0
437	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]NHAI,Bihar	12/2003	305.00	305.00	445.00	06/2008	12/2010	30(O)	0/0
438	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]NHAI,Bihar	12/2003	291.80	291.80	412.70	06/2008	12/2010	30(O)	0/0
439	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	178.00	10/2008	12/2010	26(O)	0/0
440	SAGAR - RAJMARG CHORAHA,KM 255-297, NH-26 (NHAI) - [240106302]NHAI,Madhya pradesh	12/2003	206.96	206.96	281.90	10/2008	12/2010	26(O)	0/0
441	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	108.10	10/2008	12/2010	26(O)	0/0
442	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	166.00	07/2008	12/2010	29(O)	0/0
443	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	474.00	06/2008	12/2010	30(O)	0/0
444	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	275.40	06/2009	12/2010	18(O)	0/0
445	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI, Kerala	12/2003	312.50	312.50	477.00	03/2009	12/2010	21(O)	0/0
446	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	183.10	11/2008	12/2010	25(O)	0/0
447	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	305.42	12/2008	12/2010	24(O)	0/0
448	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	565.50	06/2009	12/2010	18(O)	0/0
449	BARA TO ORAI, NH-2, 25 - [N24000069]NHAI, Uttar Pradesh	12/2003	465.00	465.00	33.65	04/2009	12/2010	20(O)	0/0
450	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	256.80	12/2009	12/2010	12(O)	0/0
451	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	182.00	06/2010	12/2010	6(O)	0/0
452	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
453	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	505.00	02/2010	12/2010	10(O)	0/0
454	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	177.15	02/2004	12/2010	82(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
455	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	444.80	08/2010	12/2010	4(O)	0/0
456	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]NHAI,Maharashtra	03/2005	579.00	579.00	678.70	04/2009	01/2011	21(O)	0/0
457	NALBARI TO BIJINI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	181.40	06/2008	01/2011	31(O)	0/0
458	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	316.20	07/2010	01/2011	6(O)	0/0
459	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	526.99	01/2011	01/2011	0(O)	0/0
460	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	334.80	01/2011	01/2011	0(O)	0/0
461	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	108.30	09/2007	02/2011	41(O)	0/0
462	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	-	09/2007	03/2011	42(O)	0/0
463	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]NHAI,Uttar Pradesh	12/2003	158.06	158.06	155.60	08/2005	03/2011	67(O)	0/0
464	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00	239.00	230.10	07/2005	03/2011	68(O)	0/0
465	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]NHAI,Bihar	12/2003	275.00	275.00	269.50	07/2005	03/2011	68(O)	0/0
466	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	190.60	10/2008	03/2011	29(O)	0/0
467	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	250.50	10/2008	03/2011	29(O)	0/0
468	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	139.40	02/2009	03/2011	25(O)	0/0
469	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	147.10	09/2008	03/2011	30(O)	0/0
470	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	110.90	11/2008	03/2011	28(O)	0/0
471	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	104.00	10/2008	03/2011	29(O)	0/0
472	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	245.60	03/2008	03/2011	36(O)	0/0
473	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	139.20	06/2008	03/2011	33(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
474	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	513.10	10/2009	03/2011	17(O)	0/0
475	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	563.70	07/2010	03/2011	8(O)	0/0
476	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	121.50	09/2010	03/2011	6(O)	0/0
477	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	62.95	04/2009	04/2011	24(O)	0/0
478	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]NHAI,Madhya pradesh	11/2008	549.00	549.00	604.80	05/2010	05/2011	12(O)	0/0
479	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	287.00	05/2010	05/2011	12(O)	0/0
480	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	-	09/2007	06/2011	45(O)	0/0
481	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	61.17	09/2008	06/2011	33(O)	0/0
482	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	205.60	10/2008	06/2011	32(O)	0/0
483	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	150.30	10/2008	06/2011	32(O)	0/0
484	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	249.70	03/2010	06/2011	15(O)	0/0
485	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	225.00	-	04/2004	10/2011	90(O)	0/0
486	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	190.90	06/2008	10/2011	40(O)	0/0
487	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	115.30	06/2005	12/2011	78(O)	0/0
488	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	123.70	06/2008	12/2011	42(O)	0/0
489	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	114.20	06/2008	12/2011	42(O)	0/0
490	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	322.80	09/2008	12/2011	39(O)	0/0
491	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	183.00	06/2008	12/2011	42(O)	0/0
492	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	161.40	04/2008	12/2011	44(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
493	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	81.55	05/2008	12/2011	43(O)	0/0
494	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	145.60	06/2008	12/2011	42(O)	0/0
495	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	94.67	04/2008	03/2012	47(O)	0/0
496	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	133.10	04/2008	03/2012	47(O)	0/0
497	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	177.20	02/2010	03/2012	25(O)	0/0
498	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
499	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	229.00	40.81	05/2010	08/2012	27(O)	0/0
500	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	155.04	28.27	11/2008	12/2012	49(O)	0/0
501	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	35.04	09/2007	12/2012	63(O)	0/0
502	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	25.11	07/2009	12/2012	41(O)	0/0
503	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	74.47	04/2010	12/2012	32(O)	0/0
504	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]NHAI, Uttar Pradesh	04/2000	440.93	440.93	641.40	12/2006	-	-	0/0
505	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]NHAI, Uttar Pradesh	04/2000	534.39	534.39	716.15	05/2007	-	-	0/0
506	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]NHAI, Bihar	12/2003	276.00	276.00	360.00	04/2008	-	-	0/0
507	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	-	10/2008	-	-	0/0
508	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]NHAI, Maharashtra	03/2005	556.00	556.00	568.50	03/2009	-	-	0/0
509	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]NHAI, Tamil Nadu	12/2003	469.80	469.80	665.80	12/2008	-	-	0/0
510	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]NHAI, Tamil Nadu	03/2005	261.00	261.00	286.30	08/2008	-	-	0/0
511	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]NHAI, Tamil Nadu	04/2000	263.00	263.00	317.74	08/2008	-	-	0/0
512	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]NHAI, Karnataka	12/2003	402.80	402.80	453.70	03/2009	-	-	0/0
513	PADALUR-TRICHY, NH-45 - [N24000083]NHAI, Tamil Nadu	03/2005	320.00	320.00	636.10	05/2009	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
514	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]NHAI,Karnataka	03/2005	450.00	450.00	876.61	07/2008	-	-	0/0
	Total		41,863.55	42,136.98	35,984.87				0/0
Shipping & Ports									
515	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	221.26	06/2007 01/2009	09/2010	20(R1)	0/0
516	DEV. & OPERATION OF AN INTERNATIONAL CONTAINER TRA - [N25000046]PORT TRUST,Kerala	11/2004	2,118.00	2,118.00	-	11/2004	10/2010	71(O)	0/0
517	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	816.12	10/2008	11/2010	25(O)	0/0
518	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
519	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
520	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00	165.00	12.54	12/2005	01/2011	61(O)	0/0
521	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,140.00	0.16	02/2011	02/2011	0(O)	0/0
522	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]SHIPP.,Maharashtra	10/2006	1,658.59	1,658.59	792.37	07/2010	03/2011	8(O)	0/0
523	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]SHIPP.,Maharashtra	08/2007	586.58	586.58	307.02	11/2010	03/2011	4(O)	0/0
524	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	0.73	03/2011	03/2011	0(O)	0/0
525	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SCI,Maharashtra	10/2007	359.44	359.44	262.97	04/2011	04/2011	0(O)	0/0
526	Acquisition of two nos. of 120 B.P - [N25000042]PORT TRUST,Maharashtra	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
527	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]SHIPP.,Maharashtra	08/2008	1,108.12	1,168.42	503.24	04/2011	12/2011	8(O)	0/0
528	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	2,770.32	2,770.42	55.40	09/2011	12/2011	3(O)	0/0
529	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
530	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	01/2012	0(O)	0/0
531	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
532	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0
533	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]SCI,Maharashtra	12/2006	411.32	411.32	406.28	03/2010	-	-	0/0
534	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]MUMBAI PORT TRU,Kerala	03/2007	245.67	298.17	297.76	04/2009	-	-	0/0
535	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SCIL,Tamil Nadu	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
536	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00	375.00	-	01/2009	-	-	0/0
	Total		24,047.63	24,630.99	4,206.24				0/0
Telecommunications									
537	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]BSNL,Maharashtra	11/2006	364.52	364.52	51.44	12/2006	08/2009	32(O)	0/0
538	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	109.31	12/2005	07/2010	55(O)	0/0
539	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]BSNL,Chhatisgarh	02/2007	239.19	239.19	96.97	04/2008	07/2010	27(O)	0/0
540	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	231.12	02/2008	07/2010	29(O)	0/0
541	GSM equipment of 2,00,000Lines (2G) Rajasthan (Ph - [N26000079]BSNL,Rajasthan	09/2009	577.35	577.35	39.70	09/2010	07/2010	-2(O)	0/0
542	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	377.04	02/2009	08/2010	18(O)	0/0
543	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	68.99	01/2010	08/2010	7(O)	0/0
544	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]BSNL,West Bengal	09/2006	208.50	208.50	146.00	09/2008	09/2010	24(O)	0/0
545	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	157.24	03/2009	09/2010	18(O)	0/0
546	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	158.72	88.17	06/2009	09/2010	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
547	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	09/2010	18(O)	0/0
548	Expn of existing 2G & 3G GSM N/W by 750k - [N26000077]MTNL,Maharashtra	10/2008	180.53	180.53	30.30	06/2010	09/2010	3(O)	0/0
549	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	185.06	11/2010	09/2010	-2(O)	0/0
550	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	810.37	685.28	01/2010	09/2010	8(O)	0/0
551	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	467.21	12/2008	10/2010	22(O)	0/0
552	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.82	03/2009	10/2010	19(O)	0/0
553	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	64.49	09/2009	10/2010	13(O)	0/0
554	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	277.34	292.21	03/2009	10/2010	19(O)	0/0
555	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]BSNL,Bihar	04/2007	366.00	529.32	202.66	09/2009	10/2010	13(O)	0/0
556	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	10/2010	21(O)	0/0
557	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
558	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
559	Provision of data network for CWG delhi - [N26000076]MTNL,Delhi	11/2009	488.76	488.76	-	10/2010	10/2010	0(O)	0/0
560	GSM equipment of 4,50,000 Lines (2G) Haryana (Phas - [N26000080]BSNL,Haryana	09/2008	216.54	216.54	51.39	09/2009	10/2010	13(O)	0/0
561	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	89.66	09/2009	10/2010	13(O)	0/0
562	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	22.23	10/2009	10/2010	12(O)	0/0
563	GSM equipment of 975000Lines (2G) 325000 lines 3(G - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	242.56	02/2010	10/2010	8(O)	0/0
564	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	75.25	09/2010	10/2010	1(O)	0/0
565	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	167.20	127.33	06/2009	10/2010	16(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
566	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	202.66	10/2008	10/2010	24(O)	0/0
567	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 392.44	392.44	149.92	03/2009	10/2010	19(O)	0/0
568	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	234.87	08/2009	10/2010	14(O)	0/0
569	GSM equipment of 1700000Lines (2G) 234100 lines 3(-) [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	282.08	10/2009	10/2010	12(O)	0/0
570	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	202.14	01/2010	10/2010	9(O)	0/0
571	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	445.52	01/2010	10/2010	9(O)	0/0
572	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	12.64	10/2010	10/2010	0(O)	0/0
573	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	176.33	12/2008	11/2010	23(O)	0/0
574	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]BSNL,Madhya pradesh	06/2008	908.30	916.70	185.06	08/2009	11/2010	15(O)	0/0
575	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
576	Procurement of 24 F OF cable. - [N26000075]BSNL,Multi State	02/2008	199.00	199.00	-	03/2010	11/2010	8(O)	0/0
577	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	-	02/2007	12/2010	46(O)	0/0
578	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
579	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
580	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
581	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
582	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
583	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
584	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	-	02/2007	03/2011	49(O)	0/0
585	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	09/2011	389.86	389.86	2.09	09/2011	09/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
586	NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]DOT, Delhi	08/2000	279.97	172.04	136.24	12/2004	-	-	0/0
587	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]BSNL, Maharashtra	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
588	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]BSNL, Multi State	10/2004	160.00	160.00	94.77	06/2006	-	-	0/0
589	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]MTNL, Delhi	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
590	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
591	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]BSNL, Tamil Nadu	06/2008	409.21	483.54	470.24	12/2008	-	-	0/0
592	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]MTNL, Delhi	10/2008	180.53	180.53	25.97	12/2009	-	-	0/0
593	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL, Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
594	CENTRALISED TRANSMISSION NMS - [N26000064]BSNL, Multi State	08/2009	300.00	300.00	-	-	-	-	0/0
	Total		27,020.91	27,154.89	8,196.03				0/0
	Urban Development								
595	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,	08/2005	8,676.00	18,894.36	15,054.58	06/2010	09/2010	3(O)	0/8
596	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00	11,609.00	2,954.59	12/2011	03/2013	0(R3)	6/6
	Total		15,071.00	30,503.36	18,009.17				6/14
	Water Resources								
597	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			609,603.35	731,525.23	292,193.35				807/2093


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.

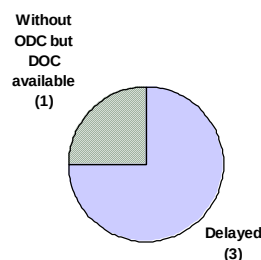

Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 19001.84 Crores.

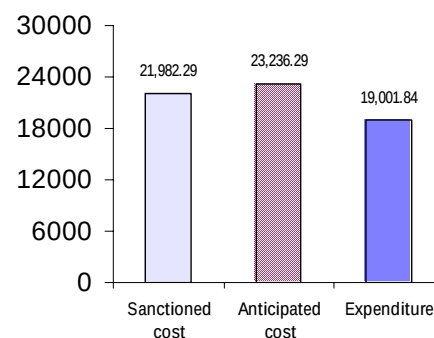


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	3
Number of Projects Delayed	2
Number of Projects Wo_Doc_Original	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule, 2 projects are delayed and 4 projects are original date of commissioning.

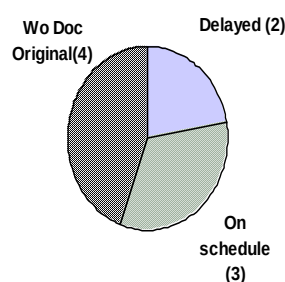

Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 5347.40 Crores but this was subsequently revised to Rs. 5347.40 Crores. The expenditure incurred on these projects till July, 2010 is Rs 1694.46 Crores.

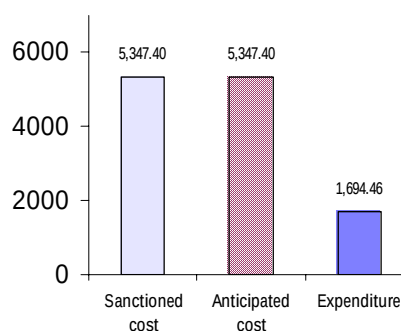


3. Sector: - Coal

Number of Projects	39
Number of Projects on schedule	9
Number of Projects Delayed	22
Number of Projects Ahead	2
Number of Projects Wo_ODC_Original	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 39 projects, 9 projects are on schedule, 22 projects are delayed and 2 projects are ahead and 6 Project W_Odc_Original .



Investment Scenario

The total cost of implementation of 39 projects when sanctioned, was of the order of Rs. 24242.02 Crores but this was subsequently revised to Rs. 27304.44 Crores. The expenditure incurred on these projects till July, 2010 is Rs 9515.28 Crores

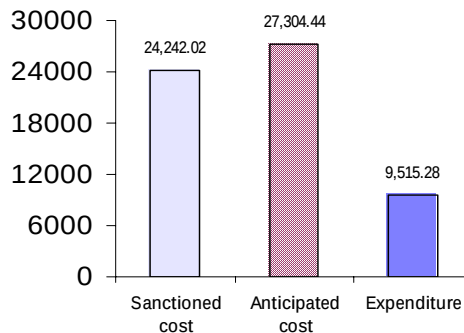


4. Sector: - Petroleum

Number of Projects	79
Number of Projects on schedule	25
Number of Projects Delayed	37
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	4
Number of Projects Without original date of commissioning	12


Brief Analysis

Project Status with respect to Original Schedule: Out of 79 projects, 25 projects are on schedule, 37 projects are delayed and 1 projects are ahead and 4 projects is without date of commissioning and 12 Project is Without original date of commissioning.

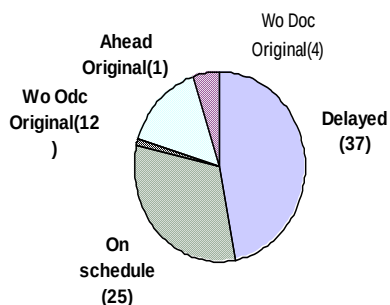

Investment Scenario

The total cost of implementation of 79 projects when sanctioned, was of the order of Rs. 165180.90 Crores but this was subsequently revised to Rs. 182291.63 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 56951.74 Crores.

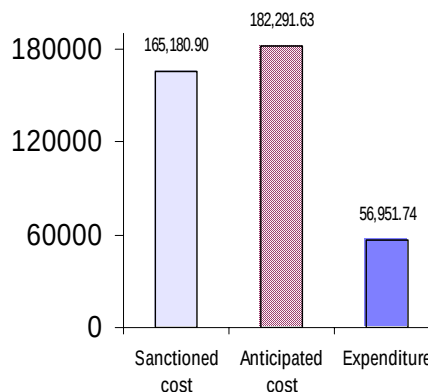


5. Sector: - Power


Number of Projects	85
Number of Projects on schedule	45
Number of Projects Delayed	34
Number of Projects Wo_Doc_Original	4
Number of Projects Wo_Odc_Original	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 84 projects, 45 projects are on schedule, 36 projects are delayed, 2 projects are without date of commissioning and 1 projects is with out original date of commissioning



Investment Scenario

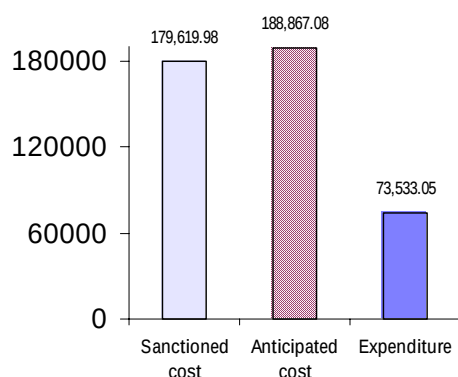


The total cost of implementation of 84 projects when sanctioned, was of the order of Rs. 179619.98 Crores but this was subsequently revised to Rs. 188867.08 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 73533.05 Crores.

6. Sector: - Railways

Number of Projects	135
Number of Projects on schedule	6
Number of Projects Delayed	36
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	50
Number of Projects Wo_Odc_Original	41


Brief Analysis

Project Status with out respect Original Schedule: Out of 135 projects, 6 projects are on schedule, 36 projects are delayed, 2 projects is ahead. 50 projects are Without date of commissioning and 41 projects are without original date of commissioning.

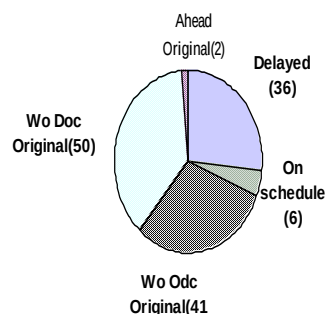

Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs. 51007.64 Crores but this was subsequently revised to Rs. 103480.09 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 34362.24 Crores.

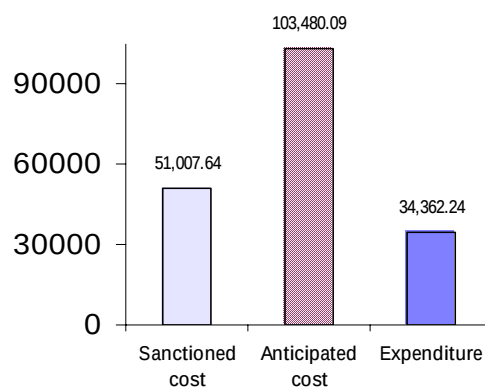


7. Sector: - Road Transport and Highways

Number of Projects	135
Number of Projects on schedule	4
Number of Projects Delayed	119
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	11


Brief Analysis

Project Status with respect to Original Schedule: Out of 135 projects, 4 projects are on schedule, 119 projects are delayed, 1 projects are ahead and 11 projects is with out date of commissioning .

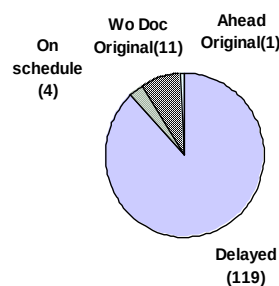

Investment Scenario

The total cost of implementation of 135 projects when sanctioned, was of the order of Rs 41863.55 Crores but this was subsequently revised to Rs. 42136.98 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 35984.87 Crores.

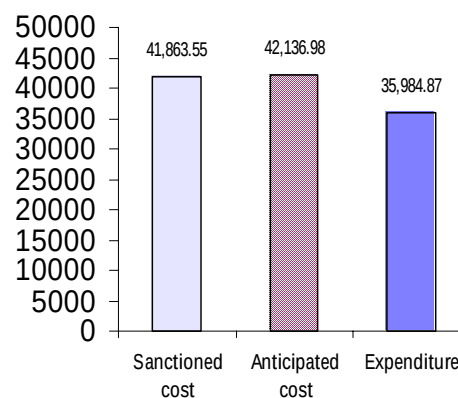


8. Sector: - Shipping and Ports

Number of Projects	22
Number of Projects on schedule	9
Number of Projects Delayed	6
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 22 projects, 9 projects are on schedule, 6 projects are delayed, 2 projects are ahead and 5 projects are without date of commissioning.

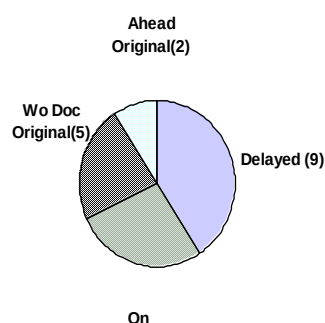

Investment Scenario

The total cost of implementation of 22 projects when sanctioned, was of the order of Rs.24047.63 Crores but this was subsequently revised to Rs. 24630.99 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 4206.24 Crores.

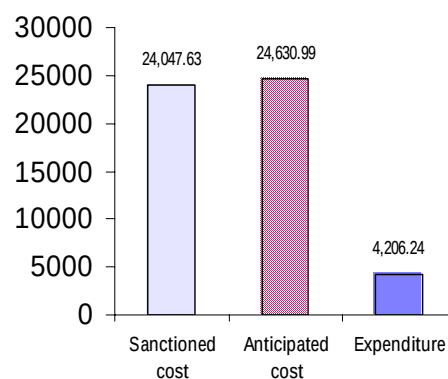


9. Sector: - Steel

Number of Projects	20
Number of Projects Delayed	8
Number of Projects Wo_Odc_Original	11
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 20 projects, 8 projects are delayed and 11 projects are Wo_Odc_Original and 1 projects are Wo_Doc_Original..



Investment Scenario

The total cost of implementation of 20 projects when sanctioned, was of the order of Rs.44197.03 Crores but this was subsequently revised to Rs. 65533.01 Crores. The expenditure incurred on these projects till July, 2010 is Rs. 26909.61 Crores.

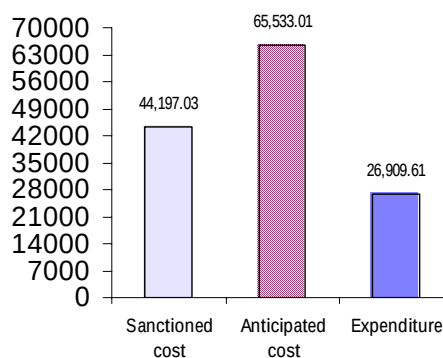


10. Sector: - Telecommunications

Number of Projects	58
Number of Projects Delayed	43
Number of Projects Ahead	2
Number of Projects on Schedule	3
Number of Projects Wo_Doc_Original	10


Brief Analysis

Project Status with respect to Original Schedule: Out of 58 projects, 43 projects are delayed and 10 projects are with out date of commissioning, 2 Projects are ahead and 3 projects are on schedule.

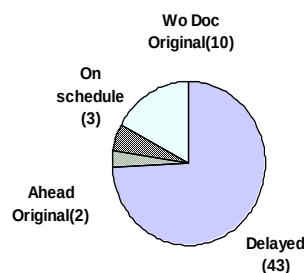

Investment Scenario

The total cost of implementation of 58 projects when sanctioned, was of the order of Rs 27020.91 Crores but this was subsequently revised to Rs. 27154.89 Crores. The expenditure incurred on these projects till July, 2010 is Rs 8196.03 Crores.

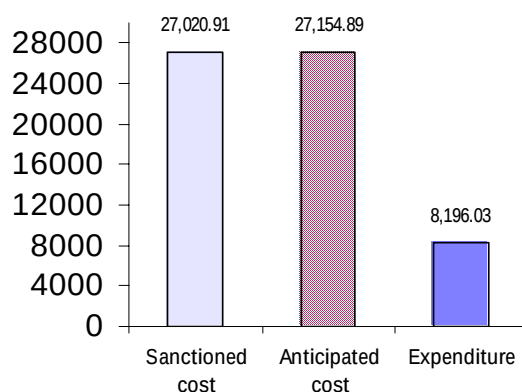

STATE WISE SUMMARY OF ONGOING PROJECTS AS ON					31.07.2010
S.No.	State	No. Of Projects	Original Cost (In Crores)	Anticipated Cost (In Crores)	Cummulative Expenditure (In Crores)
1	Andhra Pradesh	40	30,443.25	37,429.71	16,888.57
2	Arunachal Pr.	4	12,009.12	14,692.90	6,755.72
3	Assam	39	22,789.04	27,923.99	10,834.94
4	Bihar	35	31,293.42	34,491.58	17,237.78
5	Chhatisgarh	17	20,642.28	35,617.35	11,703.21
6	Delhi	6	10,616.03	20,243.26	15,368.16
7	Goa	1	204.73	204.73	5.97
8	Gujarat	22	25,432.54	25,826.02	9,641.86
9	Haryana	14	21,157.42	22,209.82	15,308.59
10	Himachal Pr.	8	15,381.72	15,463.96	10,047.33
11	J & K	9	8,963.30	25,700.02	4,950.64
12	Jharkhandd	16	8,669.29	13,624.13	4,287.75
13	Karnataka	20	16,342.86	23,588.89	11,553.91
14	Kerala	13	14,221.73	17,101.63	3,914.13
15	Madhya pradesh	27	20,084.43	20,227.36	6,814.39
16	Maharashtra	56	74,231.37	93,292.50	26,356.63
17	Manipur	1	578.62	578.62	28.33
18	Meghalaya	1	71.18	443.15	477.33
19	Mizoram	2	988.06	3,343.04	216.74
20	Multi State	97	99,456.48	108,608.36	26,853.96
21	Orissa	24	46,109.74	49,749.26	12,066.68
22	Punjab	12	5,619.41	6,597.57	2,813.42
23	Rajasthan	12	9,438.87	10,533.76	5,798.18
24	Sikkim	2	1,603.77	1,603.77	11.44
25	Tamil Nadu	39	42,276.11	48,472.55	36,011.80
26	Tripura	3	1,522.39	1,724.82	140.41
27	Uttar Pradesh	44	28,079.16	26,070.75	14,217.24
28	Uttaranchal	9	12,100.46	14,663.75	4,000.18
29	West Bengal	24	31,773.47	34,751.20	19,105.09
Total	All States	597	612,100.25	734,778.45	293,410.38

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
