

**309th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
July, 2011**



BCPL – Assam Gas Cracker



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for July 2011 (the 309th Flash Report) contains information on the status of the 558 projects in the Central Sector costing — 150 Crores and above. During July 2011, nine projects have reported completion (which has now been dropped from the monitor of this Ministry).

The online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month, due to the continuous effort/persuasion by this Ministry. However, NHAI, which has the second largest number of projects is not reporting online in spite of repeated persuasion .During July 2011, forty (40) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 21 months, in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports, Civil Aviation and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays	The total
1.	RAILWAYS	134	1	
2.	ROAD TRANSPORT & HIGHWAYS	123	15	
3.	POWER	84	6	
4.	PETROLEUM	70	8	
5.	COAL	47	1	
6.	TELECOMMUNICATION	41	0	
7.	SHIPPING & PORTS	26	1	
8.	STEEL	13	5	
9.	FERTILISERS	6	0	
10.	CIVIL AVIATION	5	2	
11.	ATOMIC ENERGY	4	1	
12.	URBAN DEVELOPMENT	3	0	
13.	MINES	1	0	
14.	WATER RESOURCES	1	0	
Total		558	40	

original cost of implementation of the 558 projects was about — 6,30,041.22 Crores and their anticipated completion cost is likely to be — 7,55,975.99 Crores, which reflects an overall cost overrun of 20.00%. The expenditure incurred on these projects till July, 2011 is — 3,32,554.55 Crores.

4. Out of the 558 projects, 7 projects are ahead of schedule, 140 are on schedule, 241 projects are delayed and 116 projects have been sanctioned without any commissioning schedule/date. Further, in case of 54 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month under reference the projects reporting delays have marginally decreased to 241 from 250 in June'2011. Out of 241 delayed projects, at the end of July, 2011, 47 projects had overall delay in the range of 1 to 12 months, 59 projects had delay in the range of 13 to 24 months, 103 projects had delay in the range of 25 to 60 months and 32 projects had delay of 61 months and above.

The Sector-wise details of delays are as under:-

i) In the **Coal sector**, Adriyala Shaft Project SCCL has reported additional delay of six months overall delay of 15 months due to the under program of Revised feasibility report (RFR) in view of geological disturbance.

ii) In the **Steel sector**, 5 projects have reported additional delays in the range of 2-6 months. 700 TPD ARI Separation Unit-4 at Oxygen Plant-II, Bhilai SAIL has reported an additional delay of two months due to retendering of the main package. 67.5 MW TG-5 Auxiliary System Emergency Power Requirement project, RINL and 330 TPH Boiler-6 and Auxiliary System RINL have reported an additional delay of two months each due to delay in supply of equipments by BHEL. Rebuilding of Coke Oven Battery No. 1 & 2, Bokaro SAIL has reported an additional delay of 3 months due to delay in chimney repair and piping works for start of heating of COB 1. Expansion of IISCO Steel Plant SAIL has reported an additional delay of 6 months (over all delay of 36 months) due to delay in design engineering by MECON.

iii) In the **Petroleum Sector**, 8 projects have reported additional delays in the range of 2-16 months. Diesel Hydro Treatment Project Dhaligaon, BRPL has reported additional delay of two months (overall delay of 22 months) due to north east problem. MSQ Quality up- Gradation Project at Bongaigaon Refinery, IOCL has reported additional delay of two months (over all delay of 20 months) due to the project being primarily a modification of an existing running plant and delay by BHEL in delivery of accessories. Karanpur Moradabad Kashipur Rudrapur Pipeline Project, GAIL has reported additional delay of three months due to farmers and land owners are demanding for re-routing the pipeline and also high compensation is being demanded. Refrigerated LPG Storage at JNPT BPCL has reported an additional delay of three months (over all delay of 35 months) due to delay in clearance from JHPI and Railway and ban on sand mining in Maharashtra. Hydrocracker Revamp Setting up a New CCR at Mumbai BPCL has reported additional delay of 16 months due to poor mobilization by the main contractor. Resitment of Marketing Instalation at Visakhapatnam HPCL, Heera Reconstruction, ONGC and Neelam Reconstruction, ONGC have reported an additional delay of 3 months, 6 months and 6 months respectively, however no specific reason has been reported by the project authorities.

iv) In the **Power Sector**, 6 projects have reported additional delays in the range of 1-9 months. Chamera Stage-III, NHPC has reported an additional delay of one month overall delay of 14 months due to heavy leakage due to extensive scouring of sill beam concrete. Chutak Hydro Electric Project, NHPC has reported an additional delay of one month (over all delay of 8 months) due to delay in man power of ejection contractor needs improvement. Simhadri STPP Stage-II, NTPC has reported an additional delay of 3 months (over all delay of 17 months) due to structural area progress is slow and the issue is continuously taken up with M/sERA at highest level. Kundankulam- APP Transmission System, PGCIL has reported an additional delay of 9 months (over all delay of 27 months) due to severe ROW problem with state problem in kerala. Tehri Pumped Storage Plant, THDCL and Transmission System Associated with Farakka-III, PGCIL have reported an additional delay of one month and 2 months (over all delay of 22 months) respectively, however no specific reason has been reported by the project authorities.

In the **Road Transport and Highways Sector**, 15 projects have reported additional delay in the range of 1-14 months. 6 projects have reported additional delay of one month each due to slow progress of work by the contractor. Vijayapur to Pathankot (J&K) NH-1A KM 16.35 to KM 50, NHAI and Vijayapur to Pathankot (NS-35/J&K) NH-1A KM 50 to KM 80, NHAI have reported an additional delay of 2 months each due to delay in utility shifting by the state departments. Ringbunds to Jhajhanpur (BR-6), NHAI and Thrissur to Angamali, NHAI have an additional delay of 2 months each due to delay in slow mobilization of contractor. Neelamangalar Junction on NH-4 Smith NH-48 to Devi NHAI has an additional delay of two months due to slow progress by the contractor. New Mangalore Port NH-17 and 48 NHAI has an additional delay of 5 months due to delay in shifting of utilities. End of Durg Bypass – Chhatisgarh/Maharashtra Border NHAI, Amritsar – Pathankot NHAI and Six Lanning of Vadakkancherry Thrissuresection NHAI have an additional delay of 3 months, 7 months and 14 months respectively. However no specific reason has been reported by the project authorities.

vi) In the Railway Sector, Rangia – Murkongselek (GC) Along with Linked Finger NEFR has reported an additional delay of 12 months (overall delay of 12 months) due to land acquisition and slow progress by the contractor.

vii) In the Civil Aviation Sector, 2 projects have reported additional delay in the range of 2-3 months. Development of Kamaraj Domestic Terminal Phase-II and Expansion Anna International Airport, AAI has reported an additional delay of two months due to the commissioning of technological works are going to be delayed. Construction of Integrated Passenger Terminal Building NSCBI, Airport, AAI has reported an additional delay of three months (overall delay of 7 months), due to lack of skilled worker.

viii) In the Atomic Energy Sector, Kudankulam APP, NPCIL has reported an additional delay of one month. However reasons have not been specified.

ix) In the Shipping Sector, Ennore Manali Express Way, F/O Special Purpose Vehicle Shipping has reported an additional delay of 21 months due to delay in tender by NHAI at an estimated cost of ₹ 150 crore. The tender document was revised twice for improving the connectivity of Chennai port trust.

The status as on 01.07.2011 in respect of completion of projects costing ₹150 Crores and above in different sectors during 2011-12 is indicated in the Report.



(Pankaj Jain)
Additional Secretary

Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	134	1
2	Road Transport & Highways	123	15
3	Power	84	6
4	Petroleum	70	8
5	Coal	47	1
6	Telecommunications	41	0
7	Shipping & Ports	26	1
8	Steel	13	5
9	Fertilisers	6	0
10	Civil Aviation	5	2
11	Atomic Energy	4	1
12	Urban Development	3	0
13	Mines	1	0
14	Water Resources	1	0
	Total	558	40

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
	<u>Road Transport & Highways</u>			
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
	June,2011			
	<u>Petroleum</u>			
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
	<u>Power</u>			
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
	<u>Railways</u>			
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
	<u>Road Transport & Highways</u>			
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00
	July,2011			
	<u>Steel</u>			
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
	<u>Petroleum</u>			

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
30	KURALI-KIRATPUR, NH-21(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000087]	309.00	06/2010	553.56

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2011				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97


Summary of projects in the Flash Report for the month of July, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	572
Number of Projects completed/dropped/frozen in Previous Month	9
Number of Projects completed/dropped/frozen in Current Month	7
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	1
Number of Projects Added in Current Month	3
Number of Projects in Current Month	558


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 558 projects, 7 projects are ahead of schedule, 140 projects are on schedule and 241 projects are delayed. Of the balance, 116 projects do not have fixed dates of commissioning while 54 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

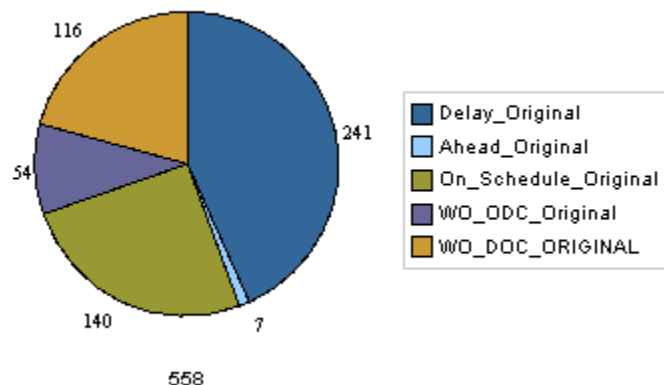

III. Investment Scenario

The Total Original cost of implementation of 558 projects when sanctioned, was of the order of Rs. 630041.22 crore but this was subsequently revised to Rs. 755975.99 crore implying a cost overrun of 20%. The expenditure incurred on these projects till July, 2011 is Rs. 332554.55 crore, which is 44% of the revised cost of the projects.

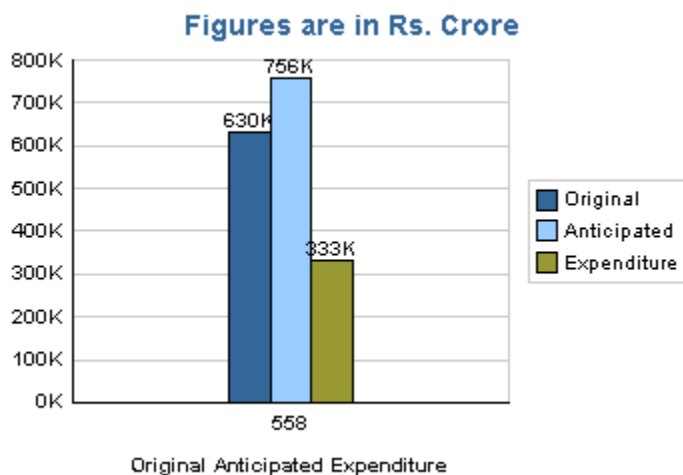

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	572
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	7
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	1
No of Projects added in Current Month	3
No of Projects in Current Month	558

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	241	7	140	54	116	558	43.19
Latest Approved (Date)	261	8	173	35	80	558	46.77

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	449	489,296.87	531,845.45	210,404.57	39.60	42,548.58	8.70
Latest Approved (RCE)	109	195,901.35	224,130.54	122,149.98	54.50	28,229.19	14.40
Total (RCE)	558	685,198.22	755,975.99	332,554.55	43.99	70777.77	10.33
Original Cost of All Projects							
Original Cost	558	630,041.22	755,975.99	332,554.55	44.00	125,934.77	20.00

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	241	292,393.24	354,507.89	190,058.56	53.60	62,114.65	21.20
Latest Approved (RCE)	261	321,398.82	371,553.42	209,919.40	56.50	50,154.60	15.60

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	39	54,226.92	64,349.25	48,343.97	75.10	10,122.33	18.70

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	4,123.2	4,820.1	16.9	1	1,273.0	2,015.0	58.3
3	Coal	47	27,763.0	31,150.0	12.2	11	13,421.4	17,406.1	29.7
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	13	40,724.7	67,781.9	66.4	10	38,774.2	65,851.4	69.8
7	Petroleum	70	158,287.8	166,089.8	4.9	15	21,740.3	37,650.3	73.2
8	Power	84	180,274.3	186,358.4	3.4	11	25,563.8	32,102.3	25.6
9	Railways	134	65,747.6	122,300.1	86.0	101	36,869.9	93,479.2	153.5
10	Road Transport & Highways	123	60,277.9	61,741.3	2.4	11	3,482.9	5,515.4	58.4
11	Shipping & Ports	26	18,451.4	19,434.9	5.3	11	6,524.5	7,709.1	18.2
12	Telecommunications	41	20,026.0	20,650.7	3.1	6	2,427.3	3,134.7	29.1
13	Urban Development	3	15,185.2	30,676.4	102.0	3	15,185.2	30,676.4	102.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		558	630,041.2	755,976.0	20.0	184	186,559.8	322,629.6	72.9

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	3	28,122.0	32,960.0	11 - 42
2	Civil Aviation	5	4,123.2	4,820.1	16.9	3	3,524.9	4,221.8	10 - 17
3	Coal	47	27,763.0	31,150.0	12.2	17	11,824.7	14,752.2	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	0	0.0	0.0	-
6	Steel	13	40,724.7	67,781.9	66.4	2	14,825.0	24,103.0	25 - 36
7	Petroleum	70	158,287.8	166,089.8	4.9	29	42,699.9	53,394.9	3 - 120
8	Power	84	180,274.3	186,358.4	3.4	49	118,652.3	124,449.4	2 - 90
9	Railways	134	65,747.6	122,300.1	86.0	26	22,639.0	43,214.0	2 - 213
10	Road Transport & Highways	123	60,277.9	61,741.3	2.4	92	31,476.3	32,119.7	1 - 106
11	Shipping & Ports	26	18,451.4	19,434.9	5.3	12	8,569.7	9,394.8	2 - 93
12	Telecommunications	41	20,026.0	20,650.7	3.1	3	880.0	860.4	17 - 54
13	Urban Development	3	15,185.2	30,676.4	102.0	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		558	630,041.2	755,976.0	20.0	241	292,393.2	354,507.9	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	2	16,663.00	21,501.00	16- 42
2	Civil Aviation	5	4,123.24	4,820.13	16.90	1	1,273.00	2,015.00	11- 11
3	Coal	47	27,763.01	31,149.96	12.20	7	6,813.24	10,338.47	9- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	13	40,724.72	67,781.91	66.44	2	14,825.00	24,103.00	25- 36
7	Petroleum	70	158,287.81	166,089.80	4.93	14	20,915.26	35,823.31	3- 120
8	Power	84	180,274.32	186,358.39	3.37	10	24,967.32	31,154.36	3- 90
9	Railways	134	65,747.63	122,300.11	86.01	19	10,934.02	31,857.69	12- 213
10	Road Transport & Highways	123	60,277.85	61,741.26	2.43	10	2,374.90	3,227.40	19- 90
11	Shipping & Ports	26	18,451.36	19,434.85	5.33	7	3,728.52	4,751.17	6- 93
12	Telecommunications	41	20,025.99	20,650.68	3.12	3	1,104.24	1,256.16	17- 23
13	Urban Development	3	15,185.18	30,676.44	102.02	2	15,071.00	30,503.36	12- 15
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		558	630041.22	755975.99	19.99	79	123303.91	202119.68	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Railways</u>						
SURENDRANAGAR-BHAVNAGAR(GC),WR	03/1997	437.40	03/2004	563.25	02/2005	544.35
<u>Road Transport & Highways</u>						
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	12/2003	210.00	04/2007	210.00	07/2011	672.97
KURALI-KIRATPUR, NH-21	03/2005	309.00	06/2010	309.00	07/2011	553.56
<u>Steel</u>						
REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)	07/2008	172.78	01/2010	172.78	06/2011	131.95
<u>Petroleum</u>						
C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)	12/2003	900.92	05/2008	976.08	04/2011	774.32
Pipeline Replacement project-2	12/2007	2,553.28	05/2011	3,796.21	05/2011	3,614.84
COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I	11/2007	1,512.00	04/2011	975.00	07/2011	846.61

VI. List of projects added

(All Cost in Rs. crore)

		Original		Anticipated	
Project	DOA	Cost	DOC	Cost	DOC
<u>Power</u>					
TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV	7/2011	181.93	7/2013	181.93	7/2013
<u>Coal</u>					
KHADIA EXPANSION OPENCAST PROJECT	6/2011	1,131.28	3/2018	1,131.28	3/2018
KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT	6/2011	1,131.28	3/2018	1,131.28	3/2018

VII. Milestones (Cumulative due & achieved)

Total	2269
Achieved up to month	917

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	05/2012	06/2012	1
<u>Civil Aviation</u>						
D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. AAI	1,273.00	2,015.00	01/2011	10/2011	12/2011	2
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT AAI	1,942.51	1,942.51	05/2011	12/2011	03/2012	3
<u>Coal</u>						
ADRIYALA SHAFT PROJECT SCCL	212.34	779.26	03/2013	06/2013	12/2013	6
<u>Steel</u>						
700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT- II, BHILLAI SAIL	111.28	232.93	N.A.	08/2011	10/2011	2
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	10/2011	12/2011	2
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	09/2011	11/2011	2
Rebuilding of coke oven battery No.1 & 2 (Bokaro S SAIL	500.90	500.90	04/2010	09/2011	12/2011	3
EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	N.A.	12/2011	06/2012	6
<u>Petroleum</u>						
DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON BRPL	1,431.91	1,690.13	09/2009	06/2011	08/2011	2
MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF IOCL	293.60	261.75	12/2009	07/2011	09/2011	2
RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT HPCL	756.00	756.00	12/2011	09/2011	12/2011	3
KARANPUR MORADABAD- KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- GAIL	238.68	204.00	N.A.	07/2011	10/2011	3

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
REFRIGERATED LPG STORAGE AT JNPT BPCL	304.40	304.40	12/2010	06/2011	09/2011	3
HEERA RECONSTRUCTION ONGC	706.70	706.70	04/2010	06/2011	12/2011	6
NEELAM RECONSTRUCTION ONGC	305.08	305.08	04/2011	06/2011	12/2011	6
HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB BPCL	825.00	1,827.00	N.A.	12/2011	04/2013	16
Power						
CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	1,405.63	08/2010	09/2011	10/2011	1
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.28	621.28	02/2011	10/2011	11/2011	1
TEHRI PUMPED STORAGE PLANT(1000MW) THDCL	1,657.00	2,978.86	07/2010	01/2016	02/2016	1
TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III PGCIL	204.07	204.07	06/2011	06/2011	08/2011	2
SIMHADRI STPP STAGE -II NTPC	5,103.39	5,038.83	N.A.	12/2011	03/2012	3
KUDANKULAM-APP TRANS. SYSTEM (PGCIL) PGCIL	1,779.29	1,946.85	11/2008	03/2012	12/2012	9
Railways						
RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER NEFR	915.70	1,717.29	N.A.	03/2013	03/2014	12
Road Transport & Highways						
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 NHAI	359.00	359.00	03/2009	07/2011	08/2011	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	07/2011	08/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	07/2011	08/2011	1
TRICHY - KORUR NH-67 NHAI	516.00	516.00	07/2010	12/2011	01/2012	1
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	07/2011	08/2011	1
DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	11/2011	12/2011	1
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 NHAI	193.09	166.30	03/2008	07/2011	09/2011	2

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	07/2011	09/2011	2
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	07/2011	09/2011	2
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	07/2011	09/2011	2
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	07/2010	07/2011	09/2011	2
END OF DURG BYPASS- CHHATISGARH/MAHARASHT RA BORDER NHAI	464.00	464.00	01/2011	07/2011	10/2011	3
NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2008	07/2011	12/2011	5
AMRITSAR-PATHANKOT NHAI	705.00	705.00	11/2012	11/2012	06/2013	7
SIX LANNING OF VADAKKANCHERRY THRISSURESECTION NHAI	617.00	617.00	08/2012	08/2012	10/2013	14
Shipping & Ports						
ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI SHIPP.	150.00	600.00	03/2006	03/2012	12/2013	21

Number of projects reporting additional delay = 40

Trend and Graphical Analysis of All Projects

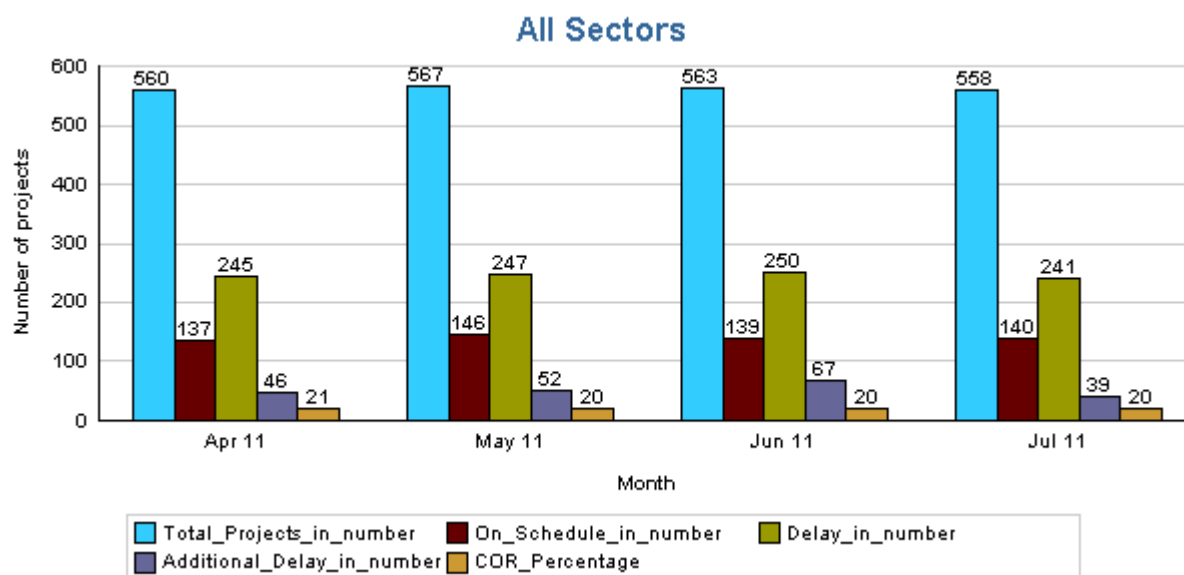


All Sectors Break-up of 241 Delayed projects in July 2011

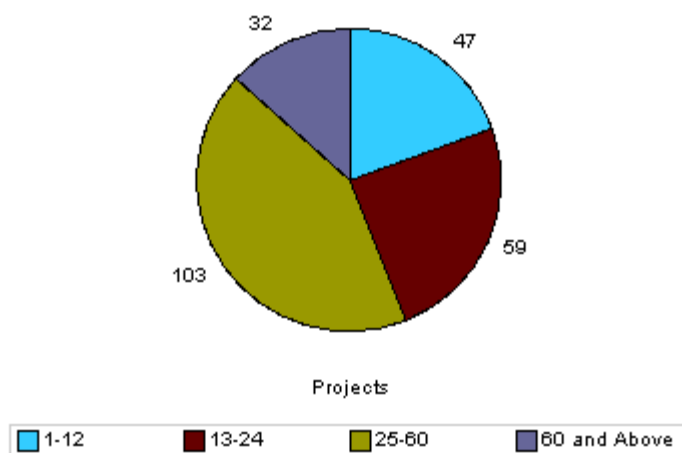


Trend and Graphical Analysis


Urban Development Sector

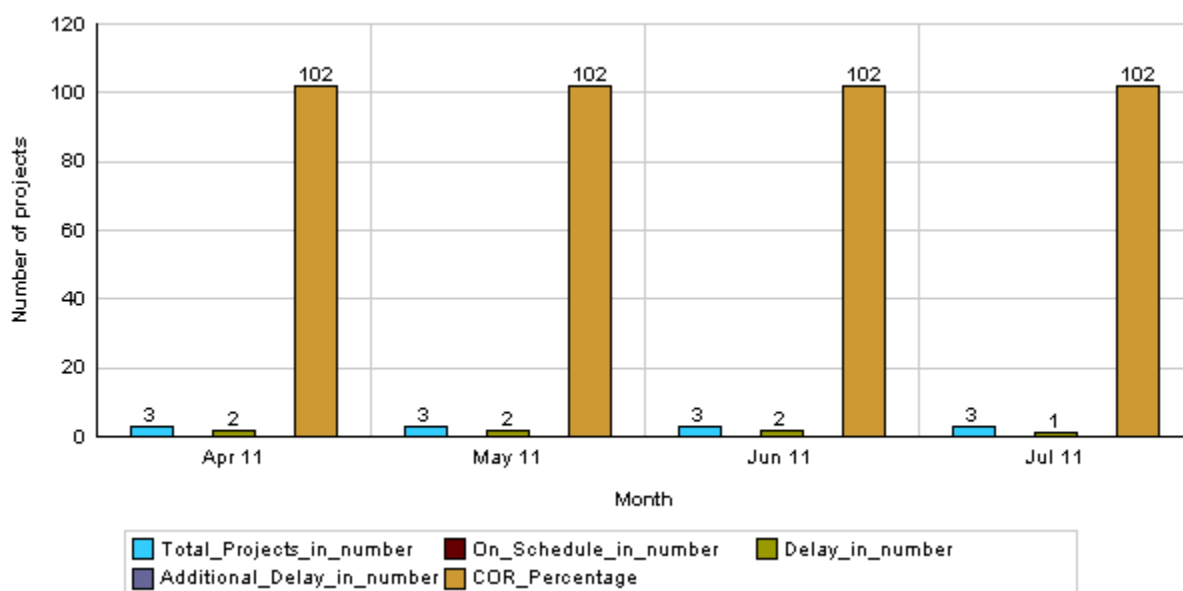


Urban Development Sector Sector Break-up of 1 Delayed projects in July 2011

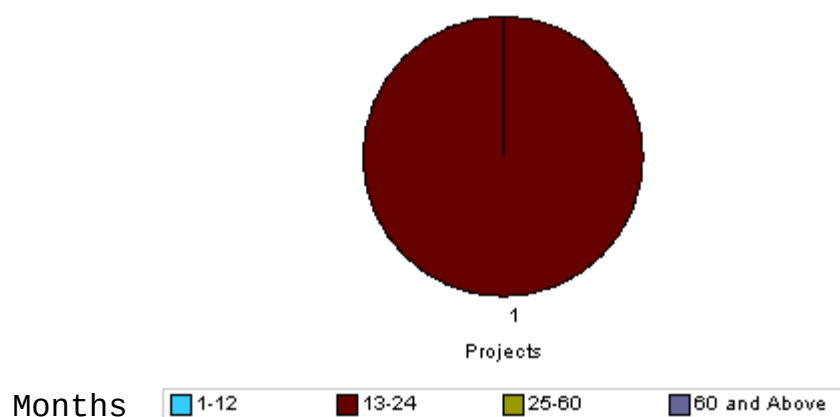

Trend and Graphical Analysis Telecommunications Sector

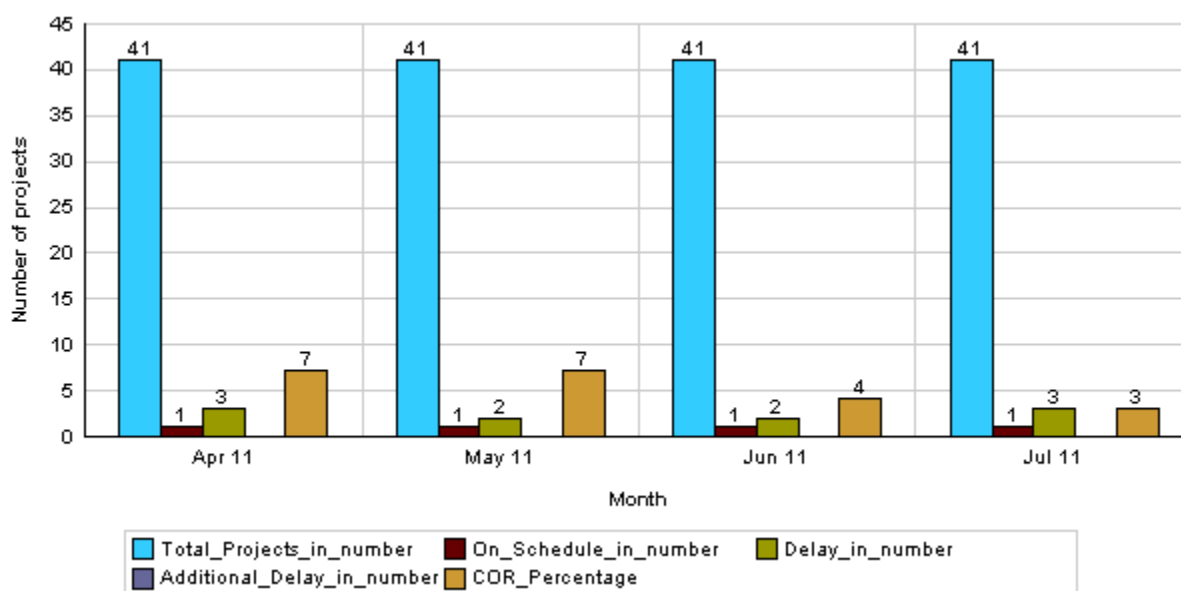


Telecommunications Sector Sector Break-up of 3 Delayed projects in July 2011




Months



Trend and Graphical Analysis Shipping and Ports Sector

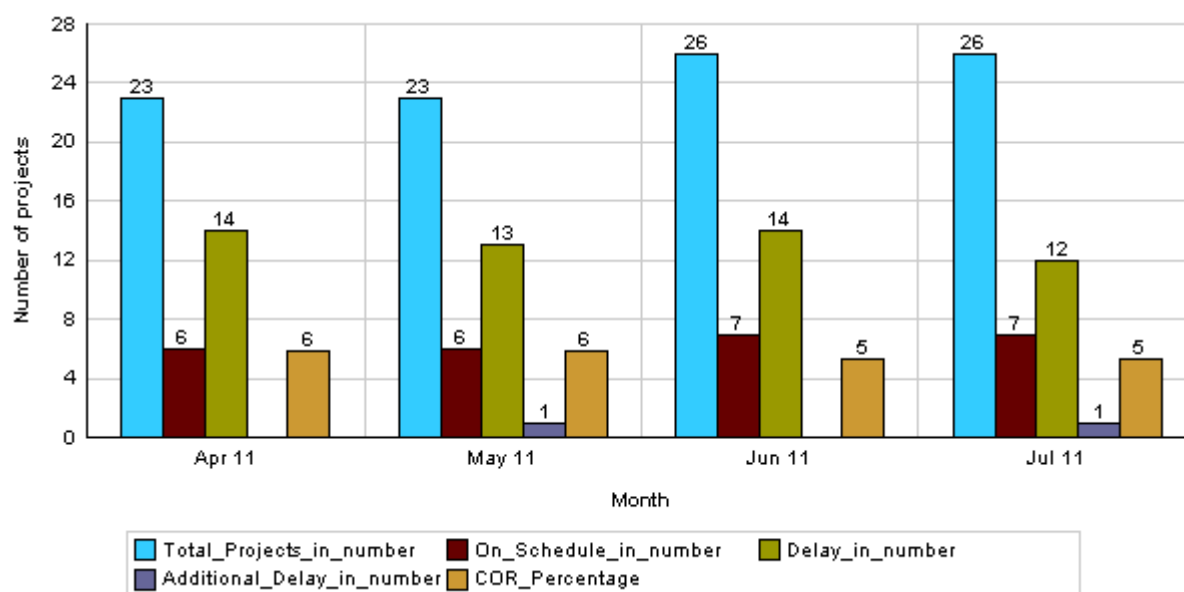


Sector Break-up of 12 Delayed projects in July 2011

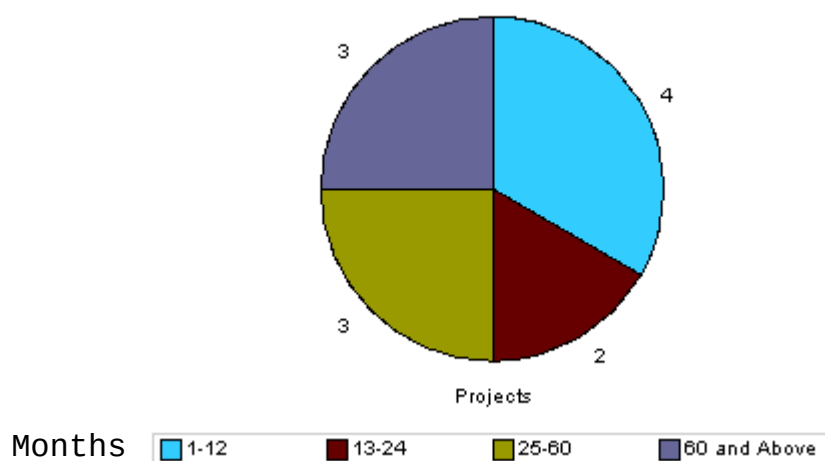


Trend and Graphical Analysis

Road Transport and Highways Sector

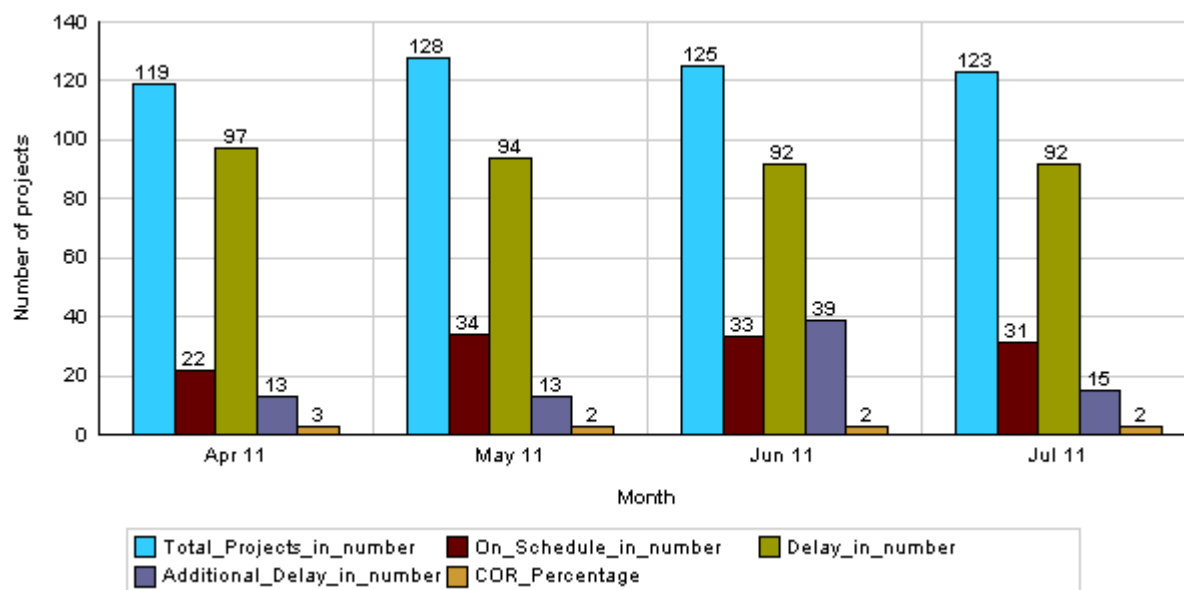


Sector Break-up of 92 Delayed projects in July 2011

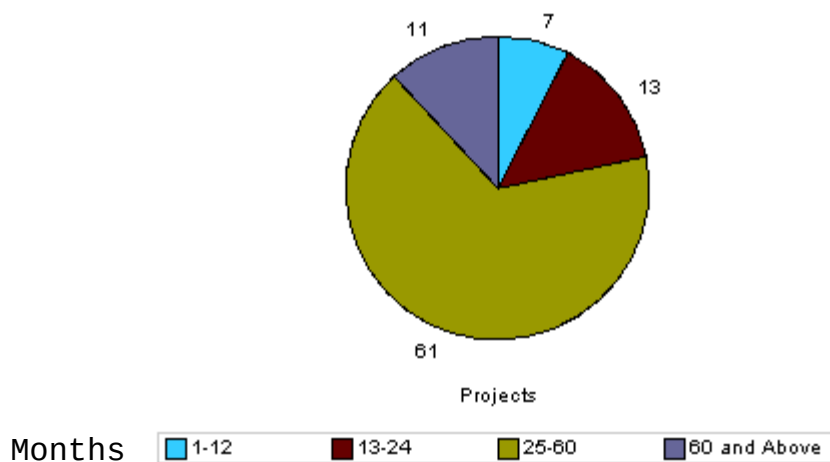


Trend and Graphical Analysis

Railways Sector

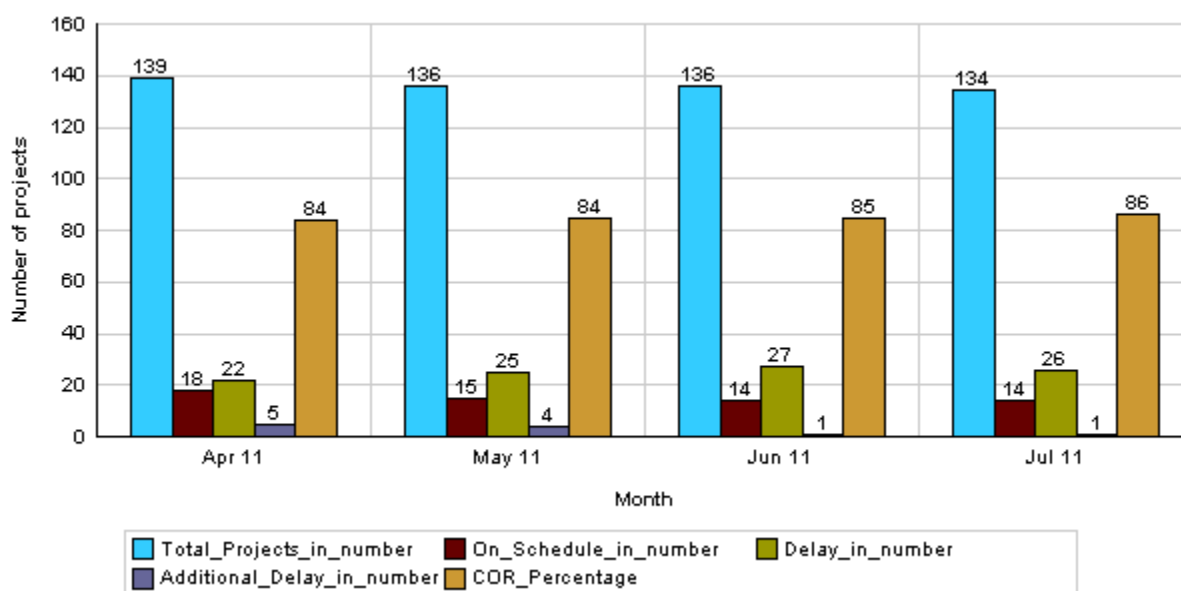


Railways Sector Sector Break-up of 26 Delayed projects in July 2011

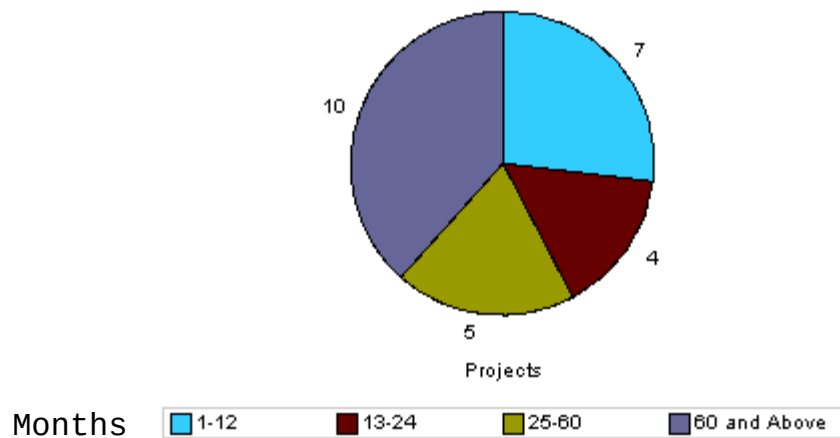


Trend and Graphical Analysis

Power Sector

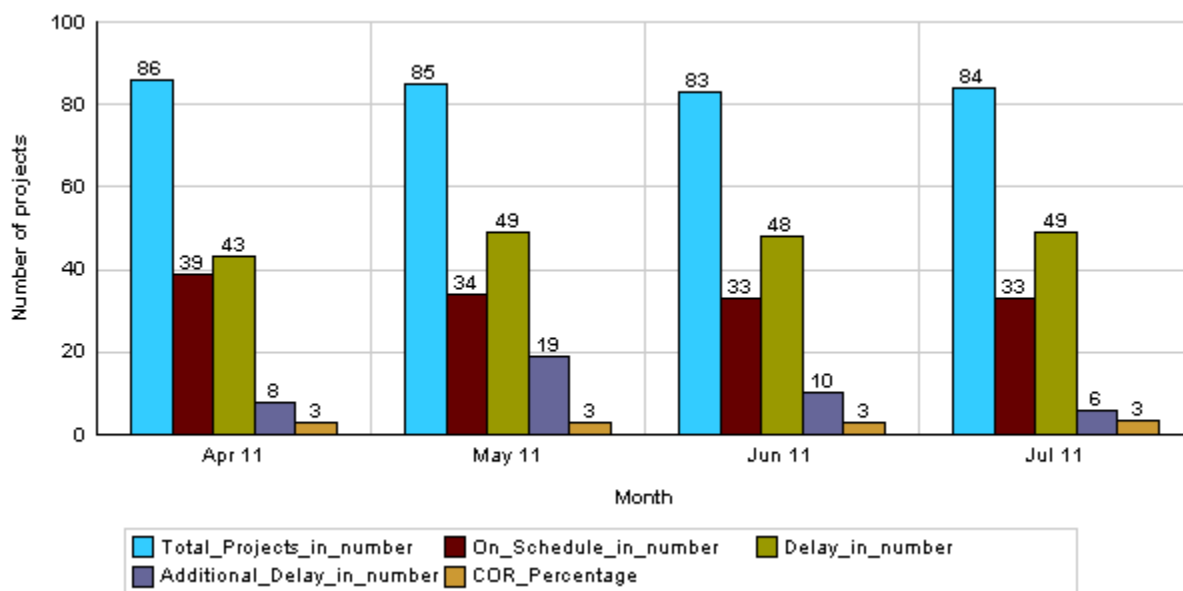


Power Sector Sector Break-up of 49 Delayed projects in July 2011

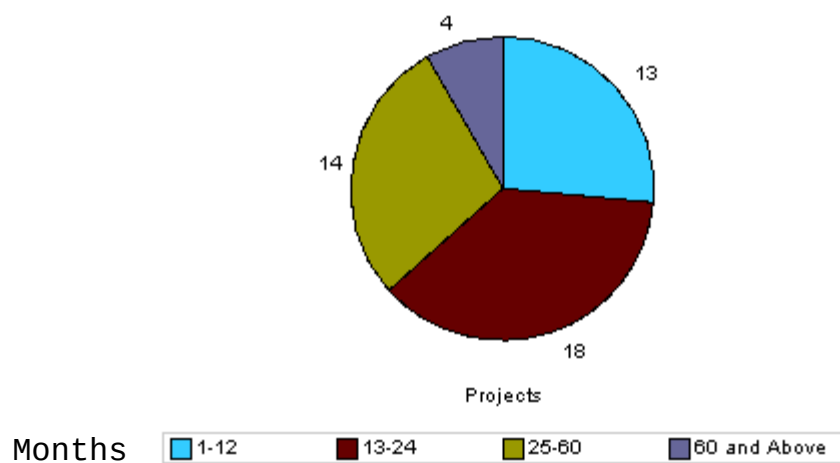


Trend and Graphical Analysis

Petroleum Sector

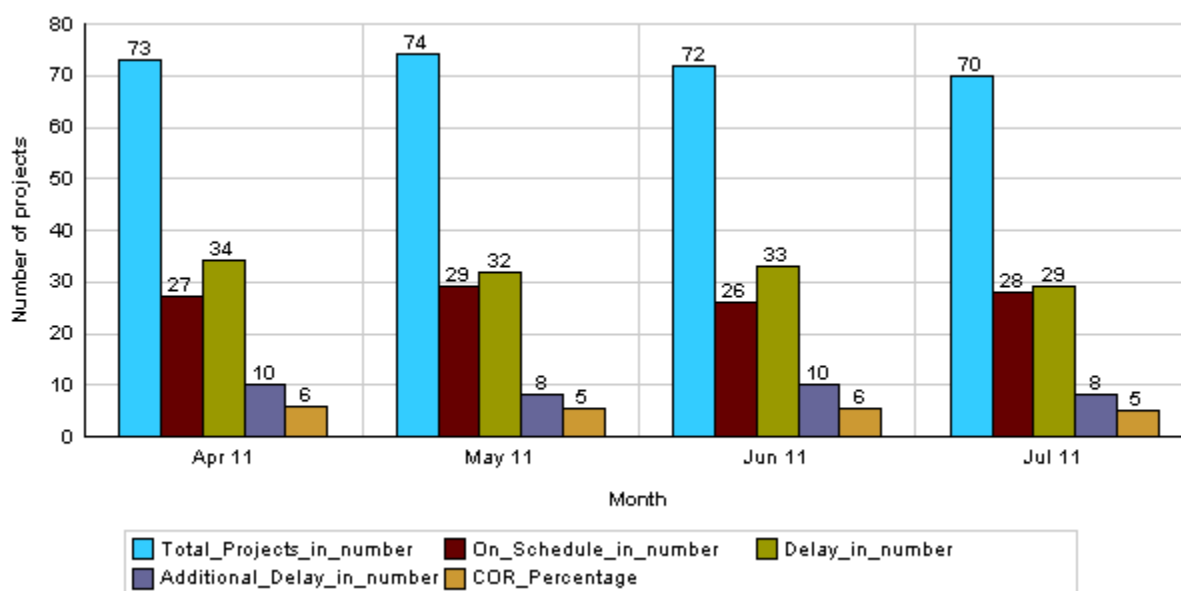


Petroleum Sector Sector Break-up of 29 Delayed projects in July 2011

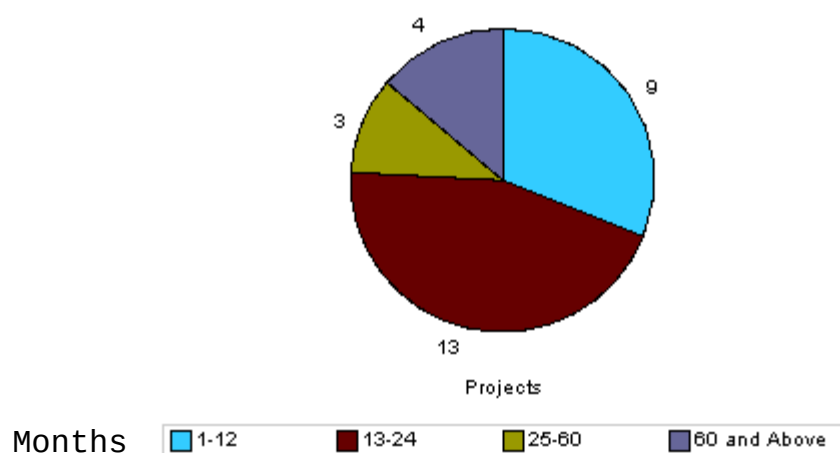

Trend and Graphical Analysis

Steel Sector

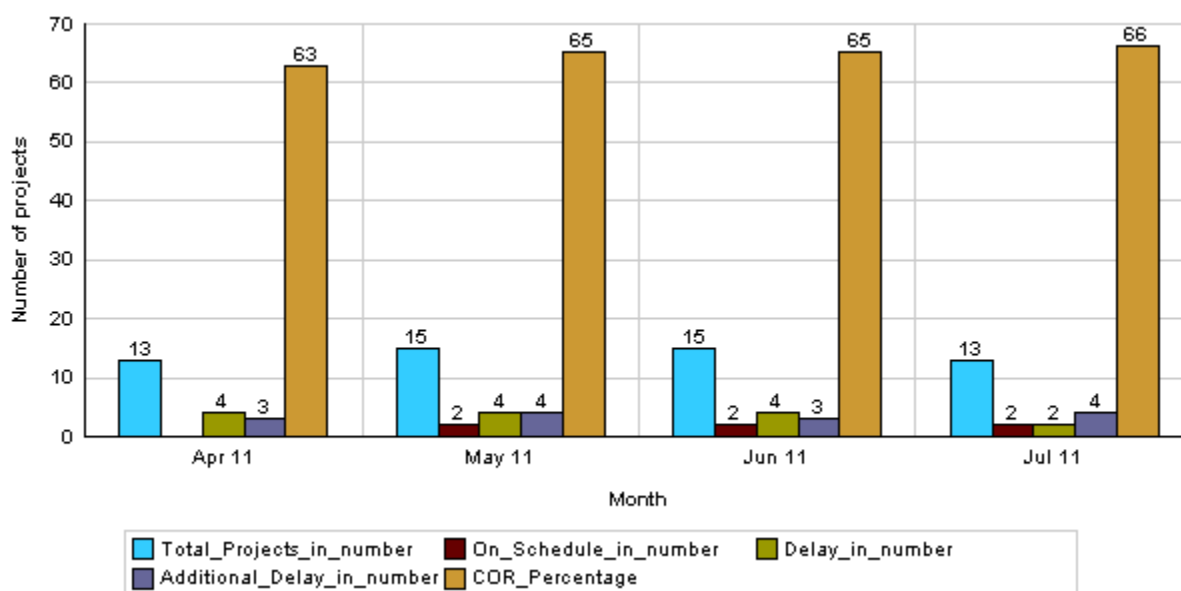

Steel Sector Break-up of 2 Delayed projects in July 2011




Months




Trend and Graphical Analysis

Fertilisers Sector

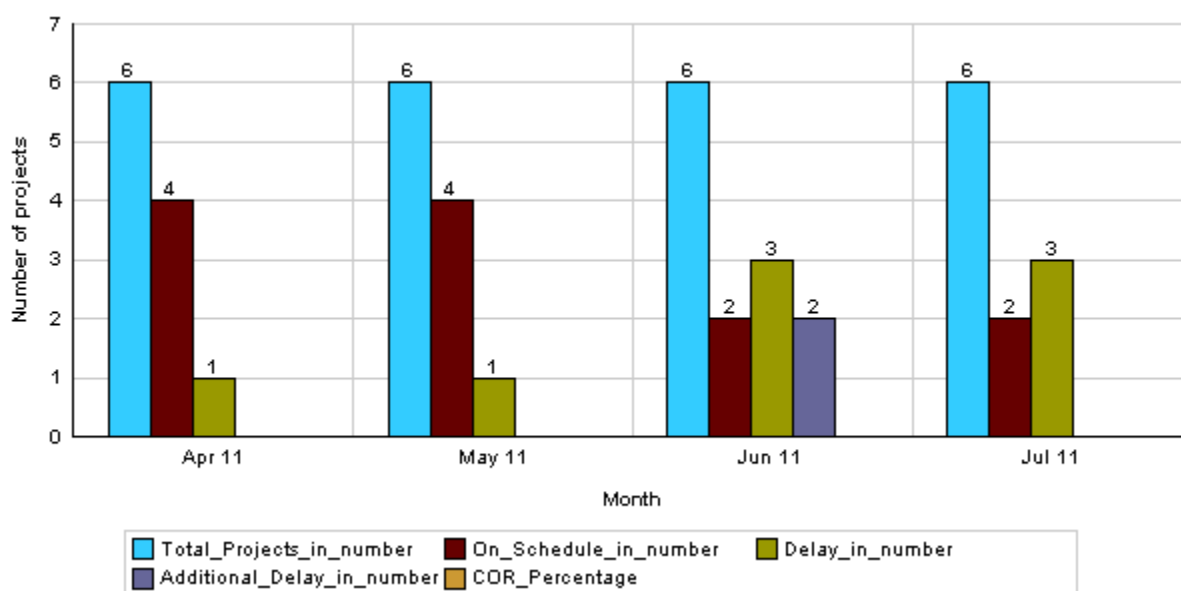


Fertilisers Sector Break-up of 3 Delayed projects in July 2011

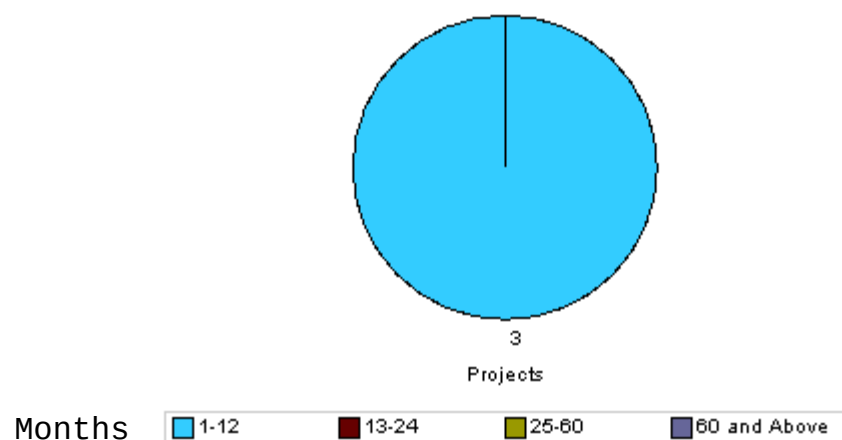


Trend and Graphical Analysis

Coal Sector

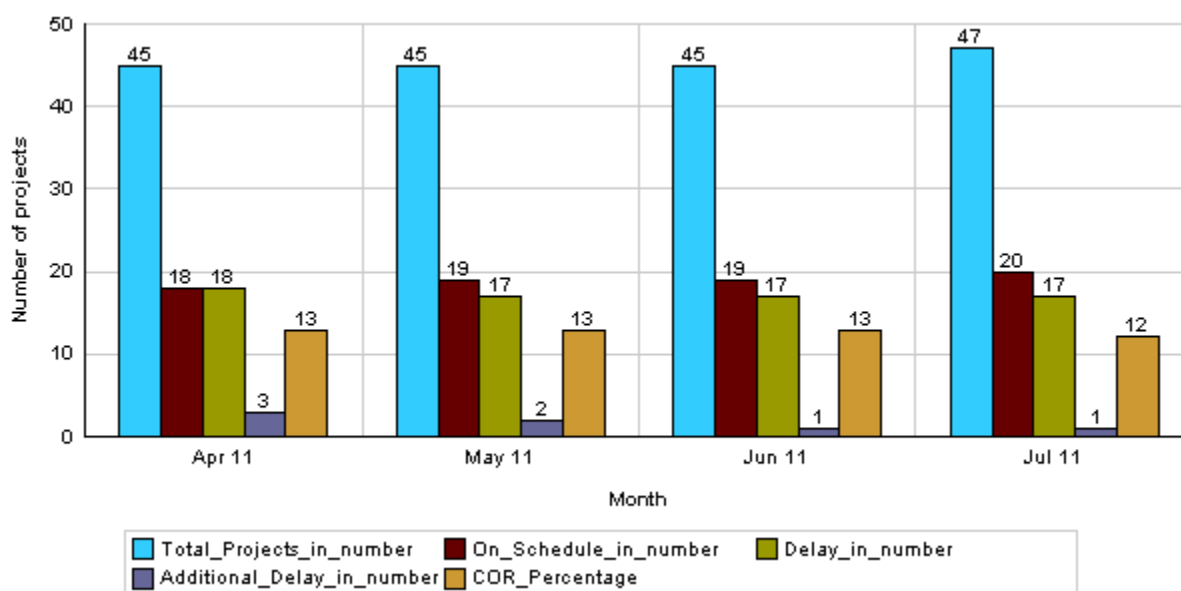


Coal Sector Sector Break-up of 17 Delayed projects in July 2011

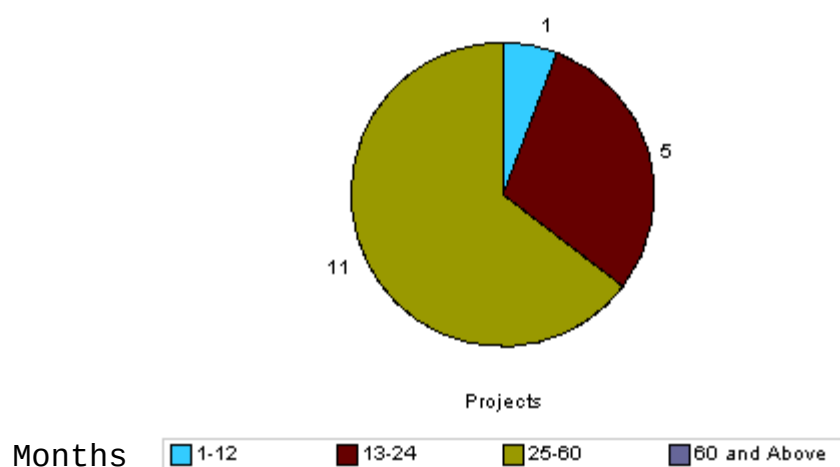


Trend and Graphical Analysis

Civil Aviation Sector

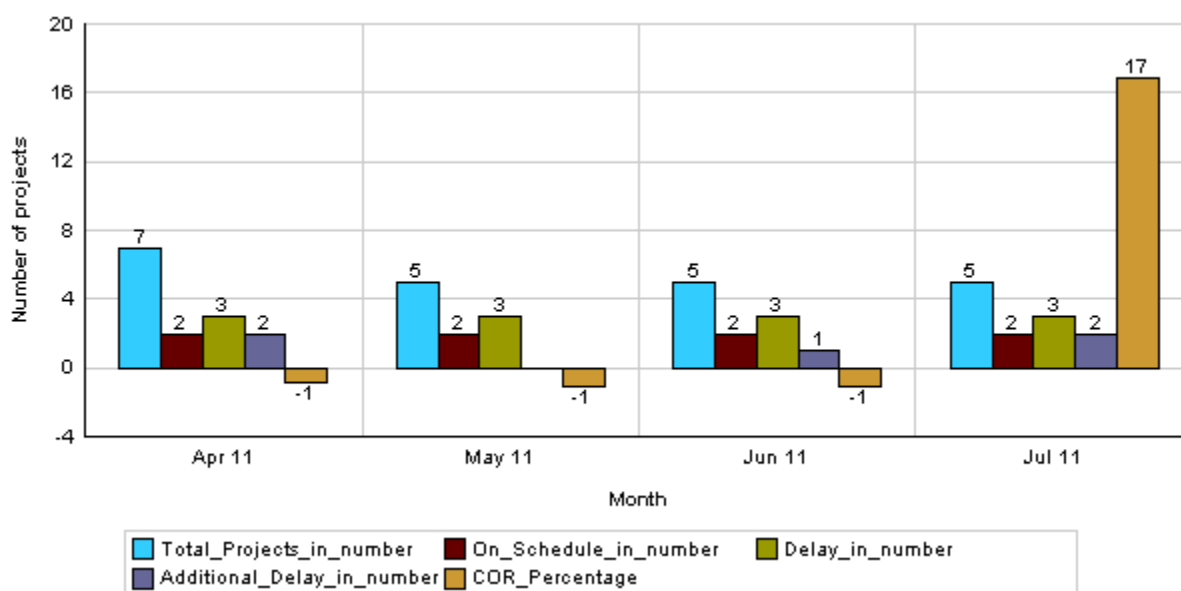


Civil Aviation Sector Break-up of 3 Delayed projects in July 2011

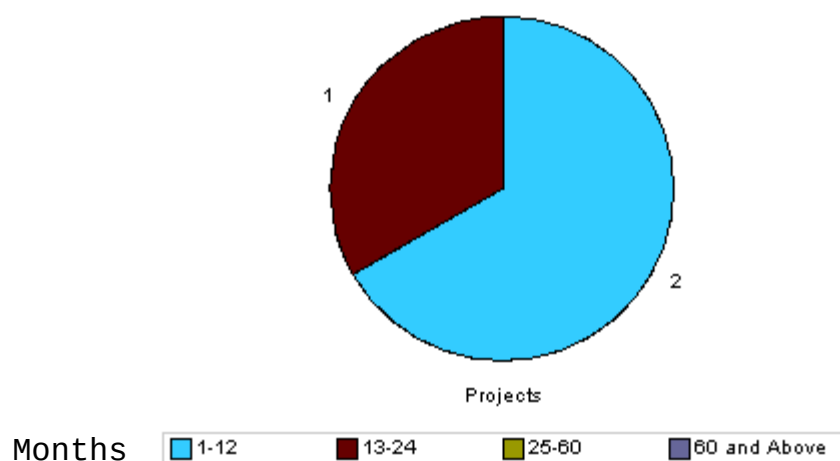


Trend and Graphical Analysis

Atomic Energy Sector

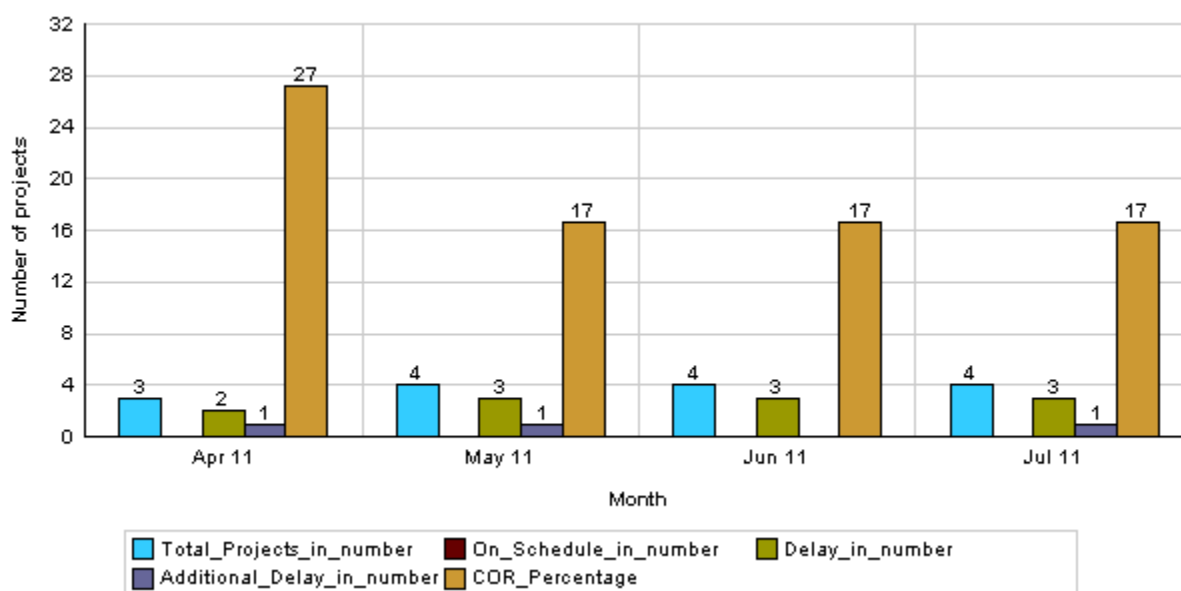

Atomic Energy Sector Sector Break-up of 3 Delayed projects in July 2011

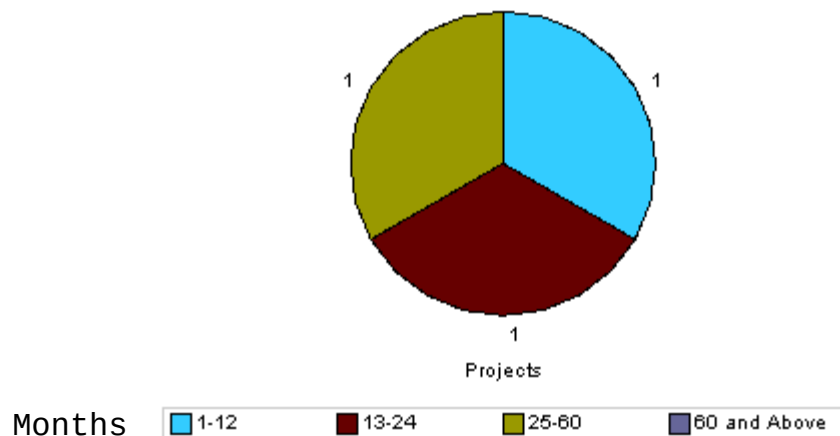

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	29,228.29	29,228.29	34,066.29
Civil Aviation	5	4,123.24	4,865.24	4,820.13
Coal	47	27,763.01	29,012.26	31,149.96
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	13	40,724.72	61,810.65	67,781.91
Petroleum	70	158,287.81	169,937.51	166,089.80
Power	84	180,274.32	182,088.40	186,358.39
Railways	134	65,747.63	83,653.72	122,300.11
Road Transport & Highways	123	60,277.85	60,277.85	61,741.26
Shipping & Ports	26	18,451.36	18,830.67	19,434.85
Telecommunications	41	20,025.99	20,058.12	20,650.68
Urban Development	3	15,185.18	15,173.44	30,676.44
Water Resources	1	542.90	542.90	1,187.00
Grand total	558	630,041.22	685,198.22	755,975.99

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,103.67	09/2010 -	01/2012	16(O)	8/80
2	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	980.87	- 04/2011	04/2012	12(R3)	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,940.00	12/2008 -	06/2012	42(O)	61/119
4	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	899.00	12/2015 05/2016	11/2016	6(R1)	0/70
	Total		29,228.29 -	34,066.29	18,923.54				69/270
	<u>Civil Aviation</u>								
5	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 2,015.00	2,015.00	881.21	01/2011 -	12/2011	11(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	1,282.55	05/2011 -	03/2012	10(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	39.57	05/2012 -	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40 -	264.29	141.91	01/2011 -	06/2012	17(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	323.65	06/2013 -	06/2013	0(O)	0/0
	Total		4,123.24 -	4,820.13	2,668.89				0/0
	<u>Coal</u>								
10	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,628.27	06/2009 -	08/2011	26(O)	59/26
11	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,230.62	06/2009 -	03/2012	33(O)	60/24
12	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	81.25	03/2010 -	03/2012	24(O)	0/11
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.51	03/2012 03/2012	03/2012	0(R3)	0/1
14	BALRAM OCP EXTENSION - [N06000044]MCL,	12/2007	172.08 -	172.08	97.15	- -	03/2012	-	4/4
15	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	40.43	- -	03/2012	-	5/7
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	74.13	03/2012 -	03/2012	0(O)	28/27

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	21.20	03/2012 -	03/2012	0(O)	10/34
18	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	1,903.33	- -	10/2012	-	0/6
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	102.17	03/2011 03/2013	03/2013	0(R3)	0/2
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhy Pradesh	05/2006	789.88 741.62	741.62	139.06	03/2010 03/2013	03/2013	0(R3)	0/2
21	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	631.78	03/2013 -	03/2013	0(O)	0/3
22	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O)	0/83
23	KANIHA OCP - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	103.11	- -	03/2013	-	0/11
24	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	31.67	- -	03/2013	-	5/7
25	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	24.99	03/2013 -	03/2013	0(O)	0/2
26	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	191.01	03/2013 09/2012	12/2013	15(R3)	2/22
27	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,065.27	03/2010 -	03/2014	48(O)	3/2
28	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,118.14	03/2010 -	03/2014	48(O)	2/3
29	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	183.63	03/2014 -	03/2014	0(O)	1/2
30	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	256.46	03/2014 -	03/2014	0(O)	0/2
31	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.50	03/2011 -	03/2014	36(O)	0/3
32	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
33	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.50 -	321.50	223.01	03/2014 -	03/2014	0(O)	0/1
34	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.64	03/2011 03/2012	03/2014	24(R3)	0/2
35	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.51	03/2012 -	03/2014	24(O)	0/2
36	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	76.12	03/2012 03/2013	03/2014	12(R3)	0/2
37	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	27.33	03/2014 -	03/2014	0(O)	0/0
38	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77 -	339.77	0.10	- -	10/2014	-	1/1
39	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhy Pradesh	06/2006	746.04 535.10	535.10	139.84	03/2012 -	03/2015	36(O)	0/2
40	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48(O)	1/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	49.16	-	03/2015	-	0/12
42	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
43	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	67.16	12/2012	03/2015	27(O)	11/44
44	Batura OC - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
45	JAGANNATHPUR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/1
46	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	17.63	03/2015	03/2015	0(O)	4/31
47	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
48	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	83.44	03/2014	03/2016	24(O)	1/2
49	MAGADH OC (CCL) - [N06000015]JCL,Jharkhandd	07/2006	469.78	706.40	16.27	07/2012 03/2014	03/2016	24(R3)	0/2
50	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.20	-	03/2016	-	0/12
51	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	115.56	03/2016	03/2016	0(O)	0/1
52	Rajrappa RCE OCP - [N06000087]JCL,Jharkhandd	12/2009	510.85	510.85	291.29	03/2016	03/2016	0(O)	0/2
53	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.00	490.10	-	-	03/2017	-	0/12
54	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0
55	KHADIA EXPANSION OPENCAST PROJECT - [N06000092]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0
56	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	39.92	03/2012	-	-	13/42
Total			27,763.01	31,149.96	11,239.17				210/491
Fertilisers									
57	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	141.65	- 11/2011	11/2011	0(R3)	2/22
58	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4(O)	0/0
59	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8(O)	0/0
60	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	163.27	01/2013	01/2013	0(O)	0/5

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	165.49	01/2013	01/2013	0(O)	0/5
62	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	197.03	12/2012	01/2013	1(O)	0/8
	Total		5,317.41	5,317.41	857.54				2/40
	Mines								
63	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51	4,401.76	4,074.00	12/2008 01/2011	06/2011	5(R3)	117/110
	Total		4,091.51	4,401.76	4,074.00				117/110
	Steel								
64	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	111.28	232.93	165.28	-	10/2011	-	0/1
65	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	217.06	-	11/2011	-	1/2
66	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	3,316.00	6,325.00	2,078.49	-	12/2011	0(R3)	0/11
67	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	222.78	-	12/2011	-	2/3
68	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	289.11	-	03/2012	3(R3)	18/21
69	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	460.00	112.74	-	05/2012	0(R3)	1/2
70	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	11,272.00	-	06/2012	6(R3)	1/14
71	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	8,588.49	10/2009 10/2012	10/2012	0(R3)	47/59
72	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	43.90	-	10/2012	0(R3)	3/4
73	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	11,812.00	1,253.17	02/2011	03/2013	25(O)	0/0
74	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	2,935.85	-	03/2013	0(R3)	2/20
75	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	-	04/2013	04/2013	0(O)	0/0
76	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	-	05/2013	05/2013	0(O)	0/0
	Total		40,724.72	67,781.91	27,178.87				75/137
	Petroleum								

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
77	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	519.93	03/2011 05/2011	06/2011	1(R3)	0/0
78	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
79	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
80	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	229.13	12/2010 08/2011	08/2011	0(R3)	0/0
81	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60 -	261.75	227.94	12/2009 -	09/2011	21(O)	0/0
82	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,403.26 -	2,340.00	2,200.48	10/2011 09/2011	09/2011	0(R2)	0/2
83	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
84	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	245.01	12/2010 07/2011	09/2011	2(R3)	0/0
85	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
86	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	204.00	116.54	- -	10/2011	-	1/8
87	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
88	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 -	1,385.00	884.80	- 12/2011	12/2011	0(R3)	0/1
89	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	798.00	616.86	04/2011 12/2011	12/2011	0(R3)	0/2
90	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	696.82	12/2011 -	12/2011	0(O)	0/0
91	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	190.04	03/2013 03/2013	12/2011	-15(R1)	0/0
92	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	618.58	04/2010 -	12/2011	20(O)	0/0
93	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	245.78	04/2011 -	12/2011	8(O)	0/0
94	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	-	09/2011 -	12/2011	3(O)	0/0
95	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,599.82	05/2011 -	12/2011	7(O)	0/116
96	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	169.06	09/2012 -	12/2011	-9(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	6,378.01	01/2012 -	01/2012	0(O)	0/0
98	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	02/2012	35(O)	0/0
99	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
100	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	137.35	03/2012 08/2012	03/2012	-5(R3)	6/12
101	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	132.59	06/2011 03/2012	03/2012	0(R3)	3/9
102	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
103	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	2,533.49	- -	04/2012	-	0/30
104	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
105	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,310.99	05/2010 05/2012	05/2012	0(R3)	0/0
106	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,094.03	09/2010 03/2012	05/2012	2(R3)	0/0
107	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	19.28	05/2010 04/2012	05/2012	1(R3)	0/0
108	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	81.57	07/2010 05/2012	05/2012	0(R3)	0/0
109	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	44.78	05/2012 -	05/2012	0(O)	9/36
110	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,354.04	08/2010 03/2012	06/2012	3(R3)	0/0
111	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	485.72	06/2012 -	06/2012	0(O)	0/0
112	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	664.26	06/2012 -	06/2012	0(O)	6/9
113	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
114	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	58.95	04/2011 -	07/2012	15(O)	0/0
115	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	116.07	06/2011 07/2012	07/2012	0(R3)	7/9
116	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	354.31	07/2012 -	07/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
117	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	877.46	03/2012 08/2012	08/2012	0(R3)	11/10
118	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	105.00	08/2012 -	08/2012	0(O)	0/0
119	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,249.00	09/2012 -	09/2012	0(O)	0/0
120	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	402.43	09/2012 09/2012	09/2012	0(R3)	0/15
121	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	15.78	09/2012 -	09/2012	0(O)	0/0
122	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	29,777.00	8,332.32	11/2012 -	11/2012	0(O)	107/100
123	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	64.67	12/2011 -	01/2013	13(O)	0/0
124	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	13.84	01/2013 -	01/2013	0(O)	12/18
125	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	01/2013 -	01/2013	0(O)	0/0
126	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	13.29	02/2013 -	02/2013	0(O)	15/42
127	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	231.94	03/2006 03/2013	03/2013	0(R3)	6/6
128	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,709.86	05/2010 03/2013	03/2013	0(R3)	0/0
129	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	359.45	03/2013 -	03/2013	0(O)	0/0
130	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
131	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
132	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
133	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	02/2008	825.00 1,827.00	1,827.00	160.16	- 04/2013	04/2013	0(R3)	0/203
134	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	2.33	- -	08/2013	-	0/0
135	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
136	Wax Project - [N16000101]NRL,Assam	08/2010	576.60 -	576.60	9.71	02/2014 -	12/2013	-2(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
138	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	167.70	02/2014	02/2014	0(O)	0/0
139	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	592.78	03/2007 03/2014	03/2014	0(R3)	3/3
140	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
141	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
142	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
143	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,375.28	03/2007 03/2017	03/2017	0(R3)	6/6
144	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
145	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	2,730.00	696.82	09/2011 03/2012	03/2012	0(R3)	0/0
146	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	1.63	03/2012	-	-	0/0
Total			158,287.81	166,089.80	56,625.81				192/637
Power									
147	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.72	09/2010	08/2011	11(O)	0/0
148	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	111.27	06/2011	08/2011	2(O)	0/0
149	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	211.19	05/2011 05/2011	09/2011	4(R3)	0/0
150	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.79	06/2010	09/2011	15(O)	0/0
151	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,639.93	08/2010	10/2011	14(O)	0/0
152	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	90.47	01/2011	10/2011	9(O)	0/1
153	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	664.47	02/2011	11/2011	9(O)	0/1
154	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	465.07	01/2010	11/2011	22(O)	0/22
155	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	52.66	11/2011	11/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,500.13	11/2009	12/2011	25(O)	0/0
157	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,483.30	09/2009	12/2011	27(O)	15/30
158	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,916.88	07/2010	12/2011	17(O)	3/20
159	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	292.95	07/2011	12/2011	5(O)	0/0
160	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	304.39	02/2012	02/2012	0(O)	0/0
161	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	35.25	02/2012	02/2012	0(O)	0/0
162	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	144.29	08/2011	02/2012	6(O)	0/0
163	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	205.53	07/2010 02/2012	02/2012	0(R3)	0/0
164	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	69.47	07/2011	02/2012	7(O)	0/0
165	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,283.69	2,466.65	04/2005	03/2012	83(O)	6/11
166	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,213.00	12/2009	03/2012	27(O)	33/60
167	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,515.05	10/2010	03/2012	17(O)	0/0
168	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	687.20	10/2009	03/2012	29(O)	2/20
169	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.83	3,991.00	-	03/2012	-	0/6
170	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	70.81	04/2012	04/2012	0(O)	0/0
171	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,334.24	03/2007	05/2012	62(O)	1/25
172	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	314.22	06/2012	06/2012	0(O)	0/0
173	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	108.33	06/2012	06/2012	0(O)	0/0
174	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	9.05	06/2012	06/2012	0(O)	0/0
175	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,650.16	08/2012	08/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
176	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,791.31	08/2012	08/2012	0(O)	0/0
177	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	315.35	08/2012	08/2012	0(O)	0/0
178	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,871.81	10/2012	10/2012	0(O)	0/0
179	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	156.20	10/2012	10/2012	0(O)	0/0
180	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	11.32	10/2012	10/2012	0(O)	0/0
181	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	651.69	08/2010	11/2012	27(O)	0/0
182	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	2,624.00	08/2012	11/2012	3(O)	1/16
183	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	296.64	11/2012	11/2012	0(O)	0/0
184	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	236.41	11/2012	11/2012	0(O)	0/0
185	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	86.27	11/2012	11/2012	0(O)	0/0
186	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	989.23	09/2009	12/2012	39(O)	0/0
187	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,715.27	11/2008	12/2012	49(O)	25/38
188	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	693.00	11/2011	12/2012	13(O)	6/34
189	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,469.21	12/2012	12/2012	0(O)	0/0
190	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	2,044.00	10/2012	12/2012	2(O)	2/15
191	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	1,953.00	10/2012	12/2012	2(O)	3/16
192	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	287.17	12/2012	12/2012	0(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	25.54	01/2013	01/2013	0(O)	0/0
194	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	18.23	01/2013	01/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
195	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,739.00	04/2009	03/2013	47(O)	19/9
196	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	339.93	09/2010	03/2013	30(O)	0/0
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	254.83	11/2011	03/2013	16(O)	0/0
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	242.11	11/2011	03/2013	16(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	128.43	02/2012	03/2013	13(O)	0/0
200	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	812.27	02/2012	03/2013	13(O)	0/0
201	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	244.42	05/2012	03/2013	10(O)	0/0
202	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	119.72	03/2013	03/2013	0(O)	0/0
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	76.35	04/2013	04/2013	0(O)	0/0
204	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	8.71	04/2013	04/2013	0(O)	0/0
205	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	80.58	01/2012	07/2013	18(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	37.78	07/2013	07/2013	0(O)	0/0
207	TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
208	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	199.44	08/2013 08/2013	08/2013	0(R3)	8/17
209	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	60.02	08/2013	08/2013	0(O)	0/0
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	15.15	08/2013	08/2013	0(O)	0/0
211	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	125.65	08/2013	08/2013	0(O)	0/0
212	RAMPUR HEP(412 MW) - [N18000024]SJVN,Himachal Pr.	01/2007	2,047.03	2,047.03	1,280.36	01/2012	09/2013	20(O)	2/10

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total	
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
213	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	126.43	11/2011 -	09/2013	22(O)	0/0	
214	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,232.00	06/2011 -	10/2013	28(O)	0/29	
215	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	2,378.00	08/2013 -	10/2013	2(O)	1/18	
216	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	57.32	11/2013 -	11/2013	0(O)	0/0	
217	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	210.01	12/2013 -	12/2013	0(O)	0/0	
218	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 -	913.63	246.20	07/2006 -	01/2014	90(O)	2/5	
219	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014	0(O)	0/0	
220	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,142.00	03/2013 -	06/2014	15(O)	5/13	
221	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,239.34	09/2009 -	07/2014	58(O)	1/20	
222	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	6,285.33	5,004.42	09/2010 -	08/2014	47(O)	2/11	
223	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,015.00	12/2009 -	09/2014	57(O)	15/70	
224	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	2,755.04	08/2013 -	09/2014	13(O)	0/0	
225	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	-	01/2015 -	01/2015	0(O)	0/0	
226	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67 3,642.04	3,642.04	801.63	07/2014 -	01/2016	18(O)	0/0	
227	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00 -	2,978.86	261.62	07/2010 -	02/2016	67(O)	1/1	
228	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	164.91	07/2014 -	05/2016	22(O)	0/7	
229	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,532.51	05/2013 06/2016	06/2016	0(R3)	79/22	
230	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	821.10	12/2007 12/2009	-	-	14/18	
Total			180,274.32 -	186,358.39	86,831.40					246/565
Railways										
231	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	202.69	-	03/1996 06/2009	03/2008	-15(R1)	0/0	

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
232	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	-	03/2011	03/2011	0(O)	0/0
233	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	550.00	-	-	03/2012	-	0/0
234	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	-	03/2010	03/2013	36(R1)	0/0
235	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	-	-	07/2011	-	0/0
236	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	-	03/2008 03/2009	10/2010	19(R1)	0/0
237	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	232.29	- 02/2009	12/2010	22(R1)	0/0
238	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	186.55	- 03/2009	12/2010	21(R1)	0/0
239	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	151.94	12/2007 03/2010	12/2010	9(R1)	0/0
240	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	290.88	03/2009 12/2008	12/2010	24(R1)	0/0
241	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	251.88	- -	12/2010	-	0/0
242	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	-	- 03/2009	03/2011	24(R1)	0/0
243	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	329.70	257.15	03/2009 12/2009	03/2011	15(R1)	0/0
244	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,241.30	- 12/2010	06/2011	6(R3)	0/1
245	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	154.13	- -	08/2011	-	0/0
246	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.99	03/2002 -	09/2011	114(O)	0/0
247	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50	252.50	158.67	02/2010 -	11/2011	21(O)	0/0
248	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	553.70	03/1994 -	12/2011	213(O)	0/0
249	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	466.70	02/2009 -	12/2011	34(O)	0/0
250	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64	735.10	197.09	- 09/2009	12/2011	27(R1)	0/0
251	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	76.41	- -	12/2011	-	0/0
252	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00	482.70	218.31	03/2013 -	12/2011	-15(O)	0/0
253	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,139.38	- -	02/2012	-	0/0
254	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	402.11	- 12/2009	02/2012	26(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
255	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	61.97	12/2011 -	02/2012	2(O)	0/0
256	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	542.24	03/1995 -	03/2012	204(O)	0/0
257	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	497.96	- -	03/2012	-	0/0
258	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	437.13	- 12/2011	03/2012	3(R3)	0/0
259	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	202.08	- 03/2012	03/2012	0(R3)	0/0
260	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	418.31	- -	03/2012	-	0/0
261	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.53	- -	03/2012	-	0/0
262	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	334.14	- 03/2011	03/2012	12(R3)	0/0
263	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	183.09	- -	03/2012	-	0/0
264	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	883.35	- -	03/2012	-	0/0
265	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	-	03/2010 -	03/2012	24(O)	0/0
266	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	174.33	- -	03/2012	-	0/0
267	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	134.93	03/2012 -	03/2012	0(O)	0/0
268	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	217.12	03/2011 -	03/2012	12(O)	0/0
269	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	376.53	06/2005 07/2011	03/2012	8(R3)	0/0
270	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	784.01	03/2011 -	03/2012	12(O)	0/0
271	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	44.35	03/2012 -	03/2012	0(O)	0/0
272	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	142.00	03/2007 03/2007	06/2012	63(R1)	0/0
273	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	320.95	- 07/2012	07/2012	0(R3)	0/0
274	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	570.01	- -	12/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	761.65	12/2012 -	12/2012	0(O)	0/0
276	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	385.44	03/2005 12/2008	12/2012	48(R1)	0/0
277	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	261.90	- 03/2012	12/2012	9(R3)	0/0
278	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	233.17	- -	12/2012	-	0/0
279	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	526.28	03/2009 -	12/2012	45(O)	0/0
280	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	949.38	10/2007 -	12/2012	62(O)	0/0
281	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33(O)	0/0
282	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	102.82	12/2012 -	12/2012	0(O)	0/0
283	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	147.14	- -	03/2013	-	0/0
284	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	-	- -	03/2013	-	0/0
285	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	41.02	03/2012 -	03/2013	12(O)	0/0
286	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.13	-	03/2013 -	03/2013	0(O)	0/0
287	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,Tamil Nadu	04/2006	495.74 495.74	495.74	121.20	- 06/2013	06/2013	0(R3)	0/0
288	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	57.75	12/2011 -	11/2013	23(O)	0/0
289	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0
290	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	82.70	12/2012 -	12/2013	12(O)	0/0
291	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,712.15	03/2009 -	12/2013	57(O)	0/0
292	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,208.23	04/2008 03/2014	03/2014	0(R3)	0/0
293	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	740.96	12/2008 -	03/2014	63(O)	0/0
294	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	654.95	- -	03/2014	-	0/0
295	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	186.25	03/2014 -	03/2014	0(O)	0/0
296	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	3.55	04/2014 -	03/2014	-1(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
297	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	6.29	03/2014 -	03/2014	0(O)	0/0
298	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	48.14	03/2014 -	03/2014	0(O)	0/0
299	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	-	03/2014 -	03/2014	0(O)	0/0
300	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	163.35	- -	03/2015	-	0/0
301	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	277.24	03/2014 -	03/2015	12(O)	0/0
302	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	03/2015	-9(O)	0/0
303	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
304	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
305	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	449.44	03/2011 03/2014	03/2016	24(R3)	0/0
306	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.21	03/2014 -	03/2016	24(O)	0/0
307	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	1.42	03/2016 -	03/2016	0(O)	0/0
308	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	23.10	03/2016 -	03/2016	0(O)	0/0
309	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	-	03/2016 -	06/2016	3(O)	0/0
310	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
311	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.28	- -	-	-	0/0
312	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
313	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	94.54	- -	-	-	0/0
314	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	464.70	- -	-	-	0/0
315	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
316	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	945.73	572.91	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	64.46	- -	-	-	0/0
318	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	85.68	- -	-	-	0/0
319	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
320	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,046.57	07/2005 -	-	-	0/0
321	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	554.55	378.41	- 05/2009	-	-	0/0
322	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	84.76	- -	-	-	0/0
323	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	808.81	06/2007 -	-	-	0/0
324	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	300.19	04/2003 03/2010	-	-	0/0
325	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	-	- -	-	-	0/0
326	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
327	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	301.92	- 12/2012	-	-	0/0
328	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
329	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	73.49	- -	-	-	0/0
330	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	209.49	- -	-	-	0/0
331	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	171.52	03/1998 08/2005	-	-	0/0
332	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	25.01	02/2015 -	-	-	0/0
333	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
334	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	261.70	18.10	02/2006 -	-	-	0/0
335	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	303.08	03/2008 06/2008	-	-	0/0
336	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	-	- -	-	-	0/0
337	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	396.44	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
338	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	-	- -	-	-	0/0
339	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83		- -	-	-	0/0
340	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	35.45	- -	-	-	0/0
341	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
342	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	-	03/2011 -	-	-	0/0
343	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	444.63	06/1999 03/2011	-	-	0/0
344	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	165.49	03/2004 -	-	-	0/0
345	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	548.49	- 11/2010	-	-	0/0
346	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	323.24	- 03/2011	-	-	0/0
347	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	263.34	06/2004 04/2005	-	-	0/0
348	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	499.50	05/2008 03/2011	-	-	0/0
349	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	243.20	12/2009 03/2011	-	-	0/0
350	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	718.90	- 12/2010	-	-	0/0
351	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	383.68	- -	-	-	0/0
352	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	402.51	- -	-	-	0/1
353	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,058.65	12/2006 08/2010	-	-	0/0
354	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	227.75	- 02/2011	-	-	0/0
355	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	460.27	02/2010 02/2011	-	-	0/0
356	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	364.24	- -	-	-	0/0
357	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	233.72	- 03/2011	-	-	0/0
358	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	117.60	- -	-	-	0/0
359	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	130.85	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
360	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	358.41	- 03/2011	-	-	0/0
361	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.42	- -	-	-	0/0
362	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	154.42	12/2010 03/2011	-	-	0/0
363	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	128.39	- 12/2010	-	-	0/0
364	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.41	03/2012 -	03/2012	0(O)	0/0
Total			65,747.63 -	122,300.11					0/2
<u>Road Transport & Highways</u>									
365	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	436.30	11/2007 -	08/2011	45(O)	0/0
366	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	351.20	10/2008 -	08/2011	34(O)	0/0
367	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	870.60	03/2009 -	08/2011	29(O)	0/0
368	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	08/2011	9(O)	0/0
369	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09 -	276.09	295.20	09/2009 -	08/2011	23(O)	0/0
370	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	657.60	07/2010 -	08/2011	13(O)	0/0
371	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	359.00	07/2010 -	08/2011	13(O)	0/0
372	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	165.14	02/2004 -	08/2011	90(O)	0/0
373	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,478.00	08/2011 -	08/2011	0(O)	0/0
374	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	147.83	08/2004 -	09/2011	85(O)	0/0
375	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	157.70	08/2004 -	09/2011	85(O)	0/0
376	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	09/2011	78(O)	0/0
377	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	338.70	10/2008 -	09/2011	35(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	179.10	03/2008	09/2011	42(O)	0/0
379	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	147.70	03/2008	09/2011	42(O)	0/0
380	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	253.50	10/2008	09/2011	35(O)	0/0
381	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	557.10	06/2008	09/2011	39(O)	0/0
382	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	598.90	03/2009	09/2011	30(O)	0/0
383	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	236.50	11/2008	09/2011	34(O)	0/0
384	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	876.70	07/2010	09/2011	14(O)	0/0
385	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	75.70	04/2004	10/2011	90(O)	0/0
386	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.60	01/2009	10/2011	33(O)	0/0
387	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	251.80	06/2008	10/2011	40(O)	0/0
388	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	10/2011	34(O)	0/0
389	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	10/2011	9(O)	0/0
390	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	194.70	10/2011	10/2011	0(O)	0/0
391	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	277.00	10/2008	11/2011	37(O)	0/0
392	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	171.70	10/2008	11/2011	37(O)	0/0
393	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,569.00	11/2011	11/2011	0(O)	0/0
394	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
395	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	293.80	09/2007	12/2011	51(O)	0/0
396	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	231.10	09/2007	12/2011	51(O)	0/0
397	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	85.40	09/2008	12/2011	39(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
398	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	203.00	06/2005 -	12/2011	78(O)	0/0
399	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	257.20	10/2008 -	12/2011	38(O)	0/0
400	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	394.10	10/2008 -	12/2011	38(O)	0/0
401	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	347.80	03/2008 -	12/2011	45(O)	0/0
402	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	223.50	02/2009 -	12/2011	34(O)	0/0
403	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	77.24	04/2009 -	12/2011	32(O)	0/0
404	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	169.50	06/2008 -	12/2011	42(O)	0/0
405	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	242.00	393.20	12/2008 -	12/2011	36(O)	0/0
406	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	363.20	12/2008 -	12/2011	36(O)	0/0
407	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	196.00	06/2008 -	12/2011	42(O)	0/0
408	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	261.50	09/2008 -	12/2011	39(O)	0/0
409	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	198.00	186.10	11/2008 -	12/2011	37(O)	0/0
410	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	275.70	10/2008 -	12/2011	38(O)	0/0
411	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	217.40	10/2008 -	12/2011	38(O)	0/0
412	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	420.30	09/2008 -	12/2011	39(O)	0/0
413	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	254.20	06/2008 -	12/2011	42(O)	0/0
414	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00 -	322.00	553.70	06/2009 -	12/2011	30(O)	0/0
415	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	232.40	06/2008 -	12/2011	42(O)	0/0
416	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	242.00	06/2008 -	12/2011	42(O)	0/0
417	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	468.80	03/2008 -	12/2011	45(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	161.30	06/2008	12/2011	42(O)	0/0
419	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	204.90	04/2008	12/2011	44(O)	0/0
420	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	118.60	05/2008	12/2011	43(O)	0/0
421	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	186.90	06/2008	12/2011	42(O)	0/0
422	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.30	06/2009	12/2011	30(O)	0/0
423	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	692.70	10/2009	12/2011	26(O)	0/0
424	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	313.40	03/2010	12/2011	21(O)	0/0
425	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.60	09/2009	12/2011	27(O)	0/0
426	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
427	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	336.50	05/2010	12/2011	19(O)	0/0
428	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16(O)	0/0
429	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	523.50	05/2010	12/2011	19(O)	0/0
430	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	01/2012	18(O)	0/0
431	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	375.10	02/2012	02/2012	0(O)	0/0
432	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	176.00	09/2007	03/2012	54(O)	0/0
433	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya pradesh	12/2003	203.43	203.43	206.80	10/2008	03/2012	41(O)	0/0
434	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	115.70	04/2008	03/2012	47(O)	0/0
435	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	175.60	04/2008	03/2012	47(O)	0/0
436	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	138.30	04/2010	03/2012	23(O)	0/0
437	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.60	02/2010	03/2012	25(O)	0/0
438	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
439	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,205.00	05/2012	05/2012	0(O)	0/0
440	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	804.30	05/2012	05/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
441	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	328.60	05/2012	05/2012	0(O)	0/0
442	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	165.50	10/2008	06/2012	44(O)	0/0
443	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
444	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.20	12/2009	06/2012	30(O)	0/0
445	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	157.00	09/2010	06/2012	21(O)	0/0
446	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	396.40	06/2012	06/2012	0(O)	0/0
447	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,519.00	10/2011	06/2012	8(O)	0/0
448	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	315.90	07/2012	07/2012	0(O)	0/0
449	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	115.60	05/2008	08/2012	51(O)	0/0
450	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	506.30	10/2011	08/2012	10(O)	0/0
451	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	183.70	06/2010	10/2012	28(O)	0/0
452	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.30	09/2009	10/2012	37(O)	0/0
453	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
454	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	813.80	09/2012	10/2012	1(O)	0/0
455	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	937.90	10/2012	10/2012	0(O)	0/0
456	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
457	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
458	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	175.60	07/2008	12/2012	53(O)	0/0
459	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	247.90	02/2004	12/2012	106(O)	0/0
460	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	374.70	12/2012	12/2012	0(O)	0/0
461	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
462	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	831.50	09/2010	03/2013	30(O)	0/0
463	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
464	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	267.80	03/2013	03/2013	0(O)	0/0
465	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
466	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
467	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
468	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	180.80	05/2013	05/2013	0(O)	0/0
469	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	105.10	05/2013	05/2013	0(O)	0/0
470	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
471	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	111.20	09/2007	06/2013	69(O)	0/0
472	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	822.60	11/2012	06/2013	7(O)	0/0
473	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
474	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0
475	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.60	04/2009	07/2013	51(O)	0/0
476	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
477	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	593.00	65.94	07/2013	07/2013	0(O)	0/0
478	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
479	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
480	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	0.99	09/2013	09/2013	0(O)	0/0
481	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
482	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
483	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
484	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	212.00	40.29	09/2007	12/2013	75(O)	0/0
485	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	27.94	07/2009	12/2013	53(O)	0/0
486	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
487	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	300.10	10/2014	10/2014	0(O)	0/0
	Total		60,277.85	61,741.26	44,168.09				0/0
Shipping & Ports									
488	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	293.57	04/2009	02/2011	22(O)	0/0
489	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
490	MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
491	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	241.50	48.10	09/2011	09/2011	0(O)	0/0
492	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	117.28	12/2005 01/2008	10/2011	45(R3)	0/0
493	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
494	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
495	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	320.74	03/2012	03/2012	0(O)	0/0
496	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2(O)	0/0
497	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2012	0(O)	0/0
498	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.40	12/2011 05/2012	05/2012	0(R3)	0/0
499	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	1,460.00	545.85	12/2010	09/2012	21(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012	09/2012	0(O)	0/0
501	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
502	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	83.51	12/2012	12/2012	0(O)	0/0
503	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25(O)	0/0
504	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	-	03/2011	03/2013	24(O)	0/0
505	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009	05/2013	52(O)	0/0
506	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006	12/2013	93(O)	0/0
507	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013	12/2013	0(O)	0/0
508	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	189.92	02/2014	02/2014	0(O)	0/0
509	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.92	10/2008	-	-	0/0
510	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	-	12/2007 01/2009	-	-	0/0
511	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	-	08/2010	-	-	0/0
512	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	-	-	0/0
513	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	821.02	10/2008	-	-	0/0
	Total		18,451.36	19,434.85	3,633.73				0/0
Telecommunications									
514	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	243.30	09/2009	02/2010	5(O)	0/0
515	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
516	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	119.42	03/2009	02/2011	23(O)	0/0
517	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	194.39	12/2008	02/2011	26(O)	0/0
518	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	308.13	03/2009	02/2011	23(O)	0/0
519	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	75.31	06/2009	02/2011	20(O)	0/0
520	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	155.71	01/2009	02/2011	25(O)	0/0
521	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	366.00	225.42	10/2008	02/2011	28(O)	0/0
522	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,100.00	812.08	- 03/2011	02/2011	-1(R3)	0/1
523	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	02/2011	13(O)	0/0
524	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	675.35	01/2010	02/2011	13(O)	0/0
525	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	132.24	01/2010	02/2011	13(O)	0/0
526	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	494.68	12/2008	03/2011	27(O)	0/0
527	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
528	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	106.69	09/2009	03/2011	18(O)	0/0
529	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
530	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	398.08	02/2009	03/2011	25(O)	0/0
531	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	352.89	08/2009	03/2011	19(O)	0/0
532	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	280.72	11/2010	03/2011	4(O)	0/0
533	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	395.08	10/2009	03/2011	17(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
534	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
535	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
536	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
537	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	20.90	10/2010 -	03/2012	17(O)	0/0
538	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	-	12/2005 -	-	-	0/0
539	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
540	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 -	353.00	-	02/2008 -	-	-	0/0
541	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
542	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
543	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	-	-	0/0
544	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
545	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	-	-	0/0
546	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	-	-	0/0
547	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	-	-	0/0
548	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	-	-	0/0
549	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
550	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	-	-	0/0
551	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53 -	625.53	-	02/2010 -	-	-	0/0
552	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75 -	624.75	-	09/2010 -	-	-	0/0
553	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	-	06/2009 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
554	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
	Total		20,025.99	20,650.68	5,865.22				0/1
			-						
	<u>Urban Development</u>								
555	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00	18,894.36	18,127.83	06/2010	06/2011	12(O)	0/10
			8,605.36			-			
556	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15(O)	6/6
			-			-			
557	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
			173.08			-			
	Total		15,185.18	30,676.44	20,395.40				6/16
			-						
	<u>Water Resources</u>								
558	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-			
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			630,041.22	755,975.99					917/2269

Sector wise current status of projects on theFlash Report

Urban Development

I. Current Status:


Number of Projects **3**

Number of Projects Delayed **1**

Number of Projects Without Date Of Commissioning **2**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 3 projects, 1 project are delayed .2 projects do not have fixed dates of commissioning.

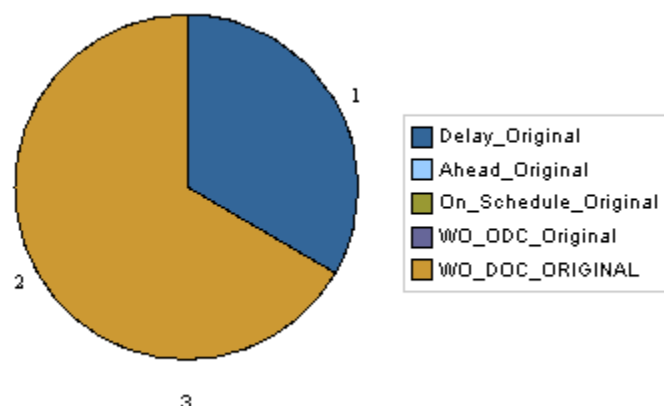

III. Investment Scenario

The Total Original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 15185.18 crore but this was subsequently revised to Rs. 30676.44 crore implying a cost overrun of 102%. The expenditure incurred on these projects till July, 2011 is Rs. 20395.4 crore, which is 66.5% of the revised cost of the projects.

Figures are in Rs. Crore

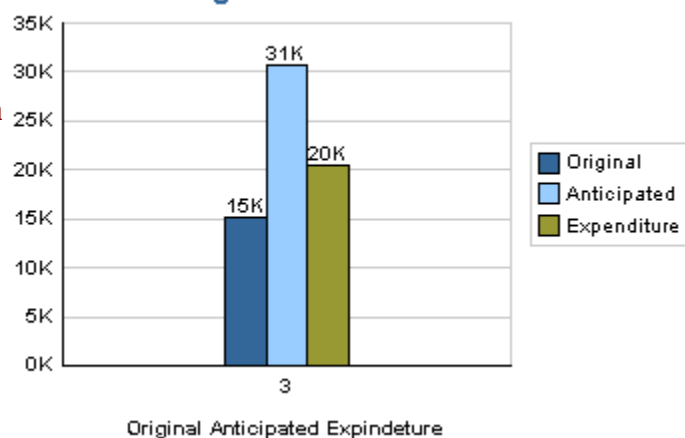

Sector wise current status of projects on theFlash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning 37

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 3 projects are delayed .37 projects do not have fixed dates of commissioning.

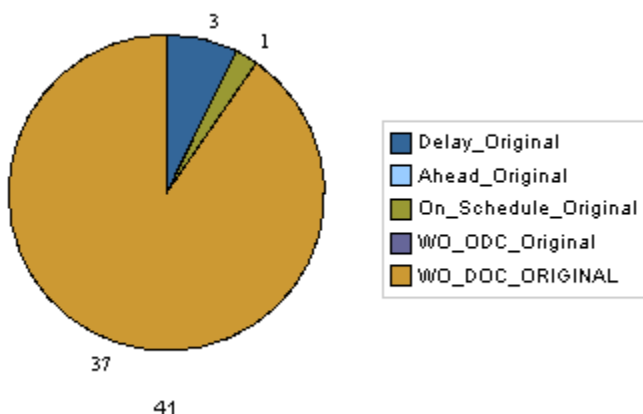

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 20650.68 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till July, 2011 is Rs. 5865.22 crore, which is 28.4% of the revised cost of the projects.

Figures are in Rs. Crore

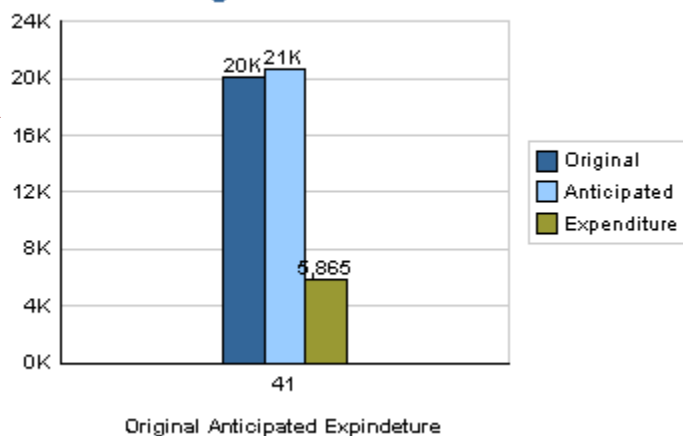

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	26
Number of Projects On Schedule	7
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	7
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 26 projects, 7 projects are on schedule and 12 projects are delayed .7 projects do not have fixed dates of commissioning.

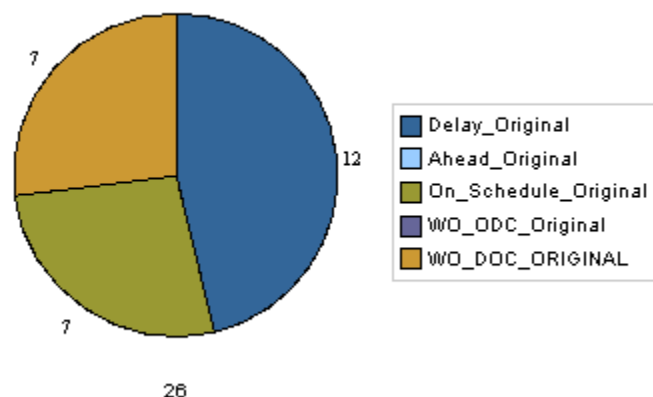

III. Investment Scenario

The Total Original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 18451.36 crore but this was subsequently revised to Rs. 19434.85 crore implying a cost overrun of 5.3%. The expenditure incurred on these projects till July, 2011 is Rs. 3633.73 crore, which is 18.7% of the revised cost of the projects.

Figures are in Rs. Crore

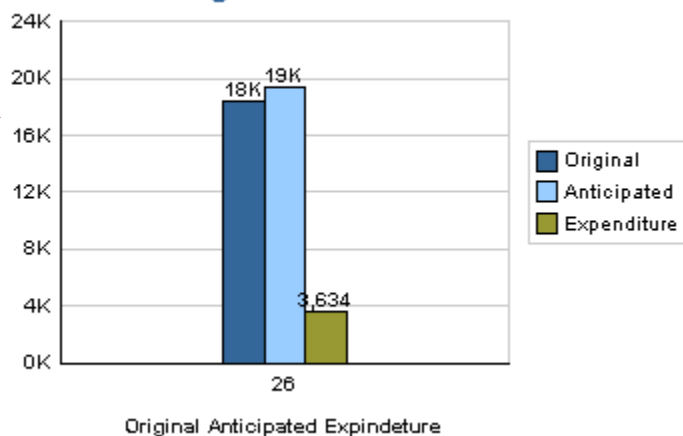

Sector wise current status of projects on theFlash Report


Road Transport & Highways

I. Current Status:

Number of Projects	123
Number of Projects On Schedule	31
Number of Projects Delayed	92

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 123 projects, 31 projects are on schedule and 92 projects are delayed .

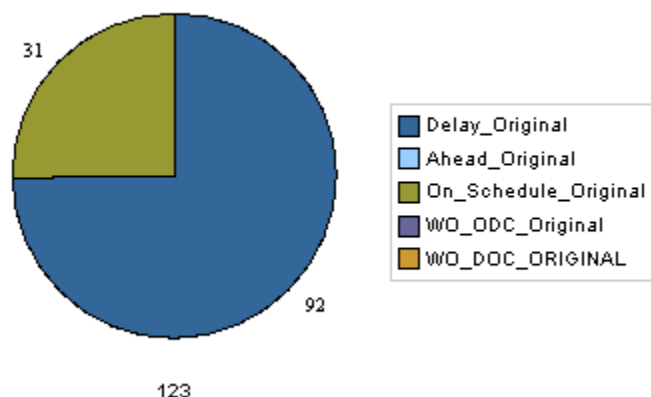

III. Investment Scenario

The Total Original cost of implementation of 123 projects when sanctioned, was of the order of Rs. 60277.85 crore but this was subsequently revised to Rs. 61741.26 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till July, 2011 is Rs. 44168.09 crore, which is 71.5% of the revised cost of the projects.

Figures are in Rs. Crore

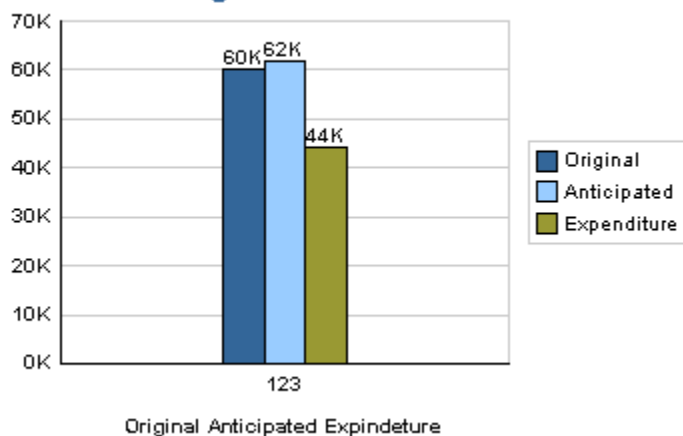

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	134
Number of Projects On Schedule	14
Number of Projects Delayed	26
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	28
Number of Projects Without Date Of Commissioning	63

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 134 projects, 3 projects are ahead of schedule, 14 projects are on schedule and 26 projects are delayed. 63 projects do not have fixed dates of commissioning. 28 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

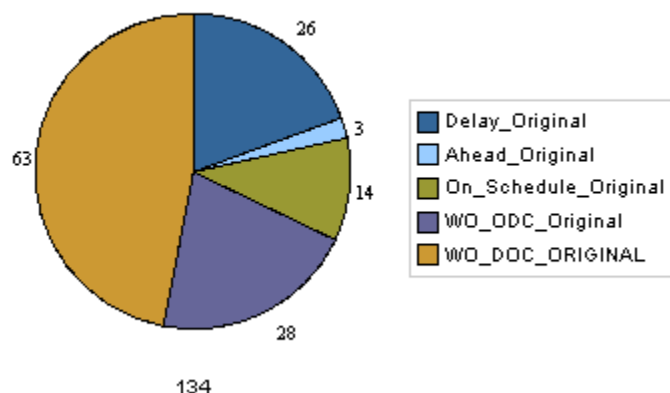

III. Investment Scenario

The Total Original cost of implementation of 134 projects when sanctioned, was of the order of Rs. 65747.63 crore but this was subsequently revised to Rs. 122300.11 crore implying a cost overrun of 86%. The expenditure incurred on these projects till July, 2011 is Rs. 50057.4 crore, which is 40.9% of the revised cost of the projects.

Figures are in Rs. Crore

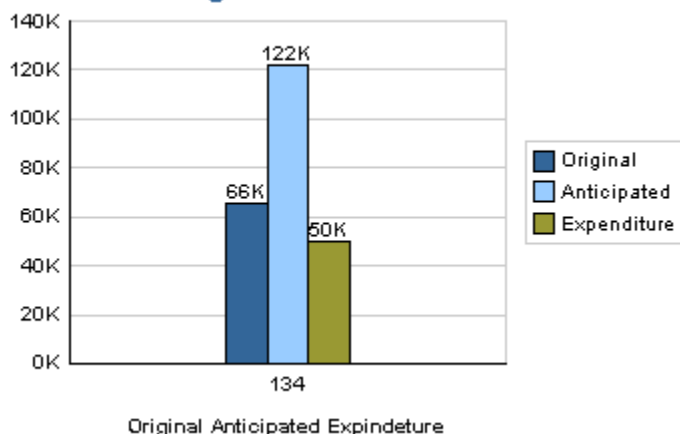

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	84
Number of Projects On Schedule	33
Number of Projects Delayed	49

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 84 projects, 33 projects are on schedule and 49 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

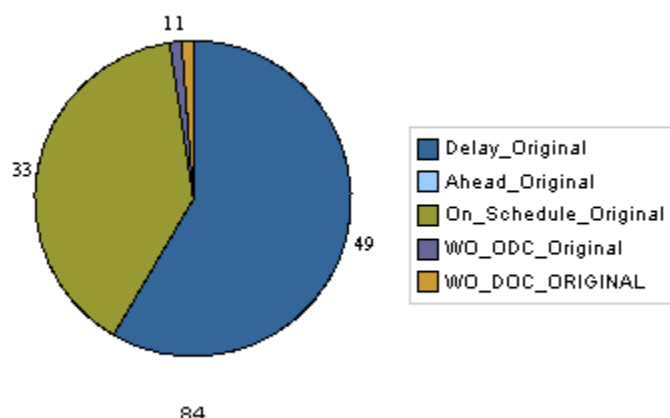

III. Investment Scenario

The Total Original cost of implementation of 84 projects when sanctioned, was of the order of Rs. 180274.32 crore but this was subsequently revised to Rs. 186358.39 crore implying a cost overrun of 3.4%. The expenditure incurred on these projects till July, 2011 is Rs. 86831.4 crore, which is 46.6% of the revised cost of the projects.

Figures are in Rs. Crore

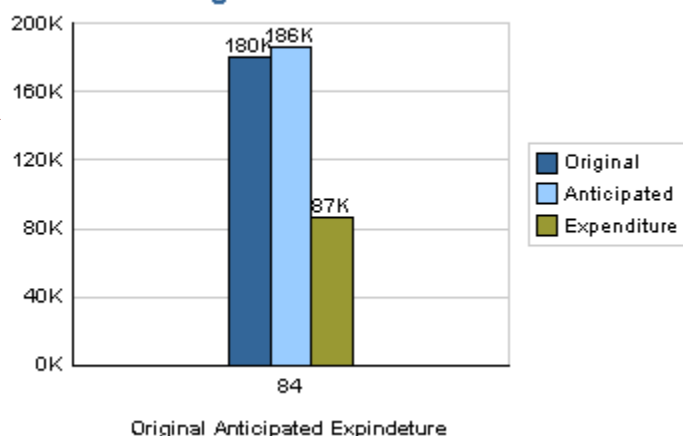

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	70
Number of Projects On Schedule	28
Number of Projects Delayed	29
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 70 projects, 4 projects are ahead of schedule, 28 projects are on schedule and 29 projects are delayed. 4 projects do not have fixed dates of commissioning. 5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

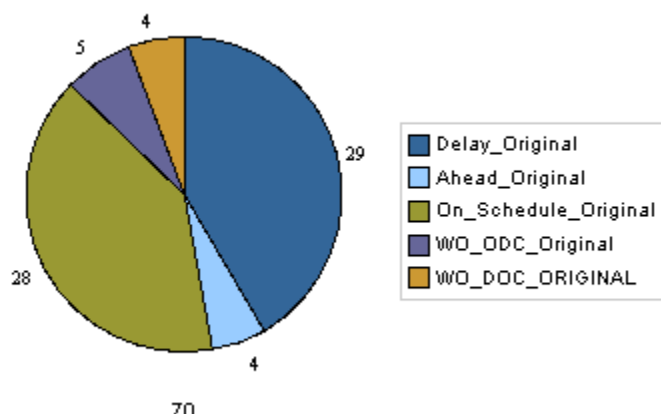

III. Investment Scenario

The Total Original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 158287.81 crore but this was subsequently revised to Rs. 166089.8 crore implying a cost overrun of 4.9%. The expenditure incurred on these projects till July, 2011 is Rs. 56625.81 crore, which is 34.1% of the revised cost of the projects.

Figures are in Rs. Crore

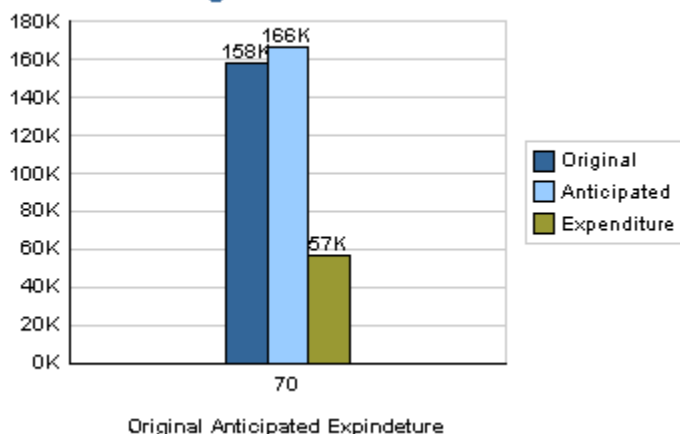

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	14
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Original Date of Commissioning	9
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 2 projects are on schedule and 2 projects are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

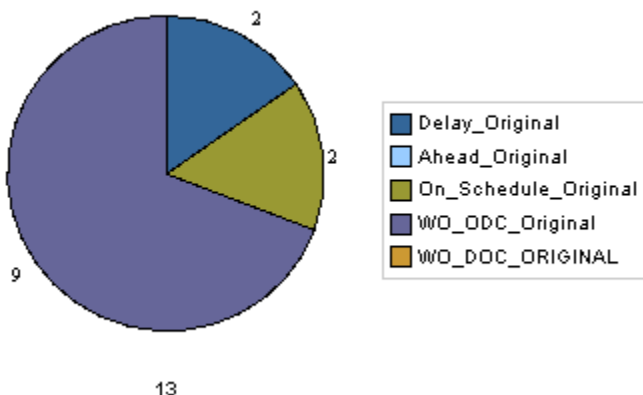

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 40724.72 crore but this was subsequently revised to Rs. 67781.91 crore implying a cost overrun of 66.4%. The expenditure incurred on these projects till July, 2011 is Rs. 27178.87 crore, which is 40.1% of the revised cost of the projects.

Figures are in Rs. Crore

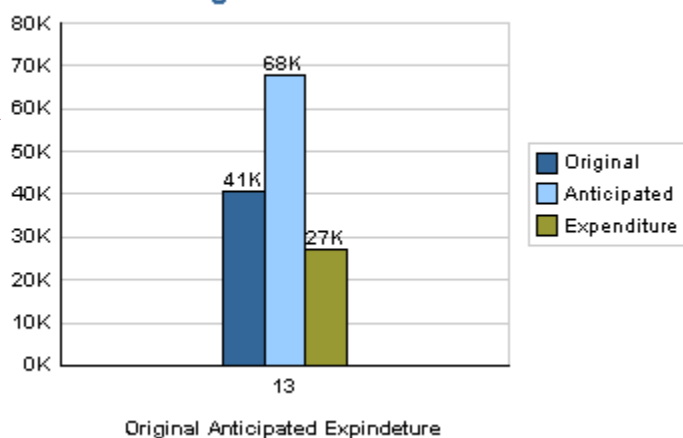

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

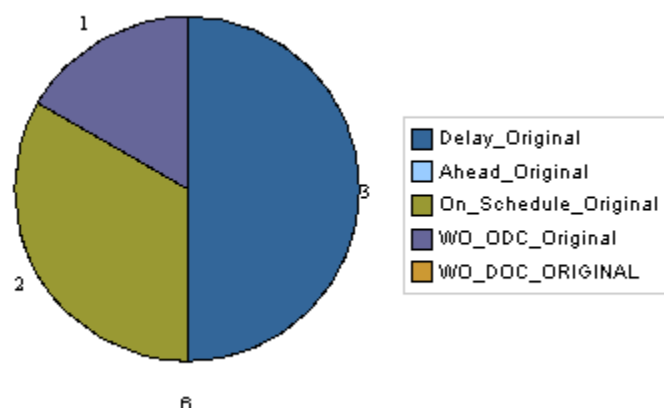

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till July, 2011 is Rs. 857.54 crore, which is 16.1% of the revised cost of the projects.

Figures are in Rs. Crore

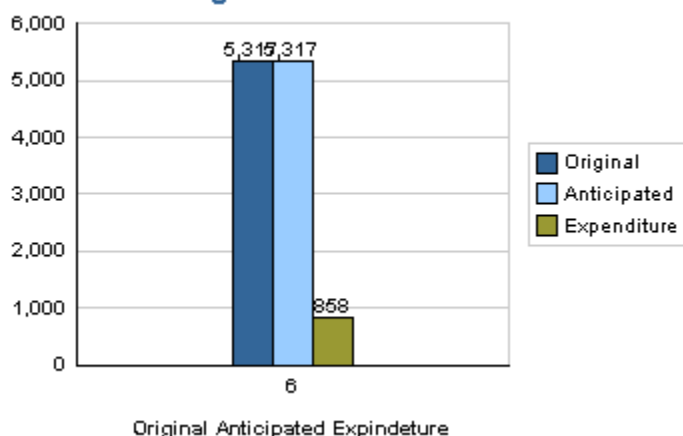

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	47
Number of Projects On Schedule	20
Number of Projects Delayed	17

Number of Projects Without Original Date of Commissioning	9
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 47 projects, 20 projects are on schedule and 17 projects are delayed .1 project do not have fixed dates of commissioning.9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

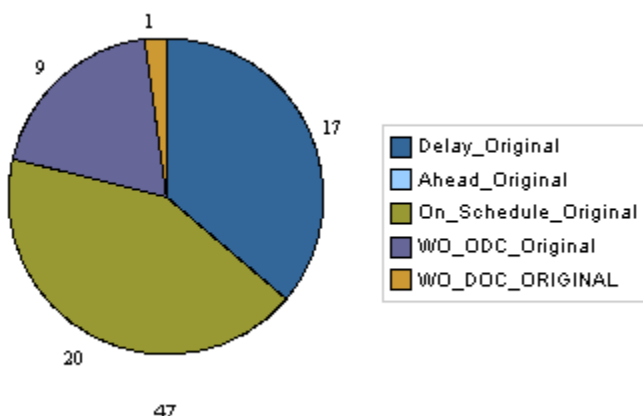

III. Investment Scenario

The Total Original cost of implementation of 47 projects when sanctioned, was of the order of Rs. 27763.01 crore but this was subsequently revised to Rs. 31149.96 crore implying a cost overrun of 12.2%. The expenditure incurred on these projects till July, 2011 is Rs. 11239.17 crore, which is 36.1% of the revised cost of the projects.

Figures are in Rs. Crore

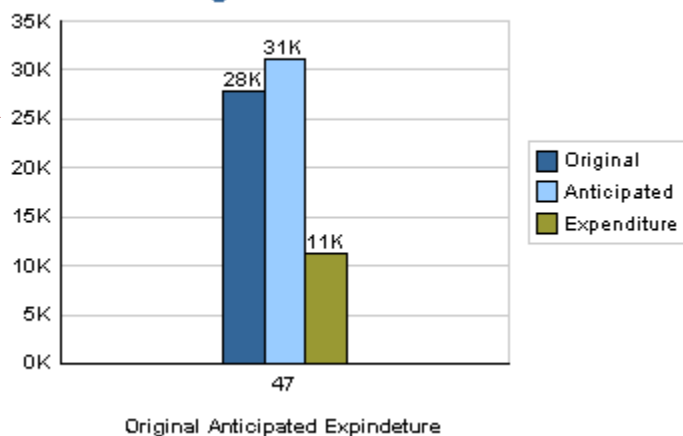

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 3 projects are delayed.

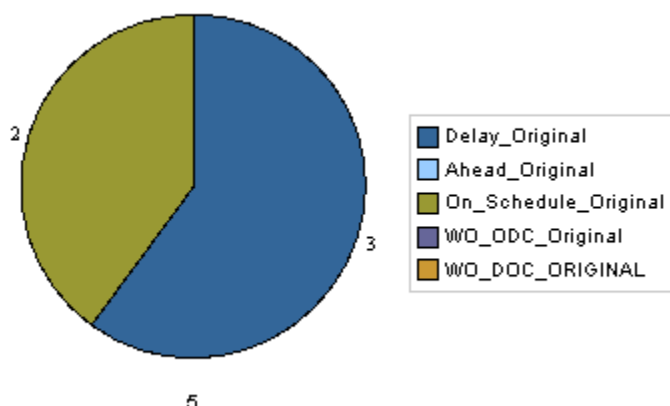

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4123.24 crore but this was subsequently revised to Rs. 4820.13 crore implying a cost overrun of 16.9%. The expenditure incurred on these projects till July, 2011 is Rs. 2668.89 crore, which is 55.4% of the revised cost of the projects.

Figures are in Rs. Crore

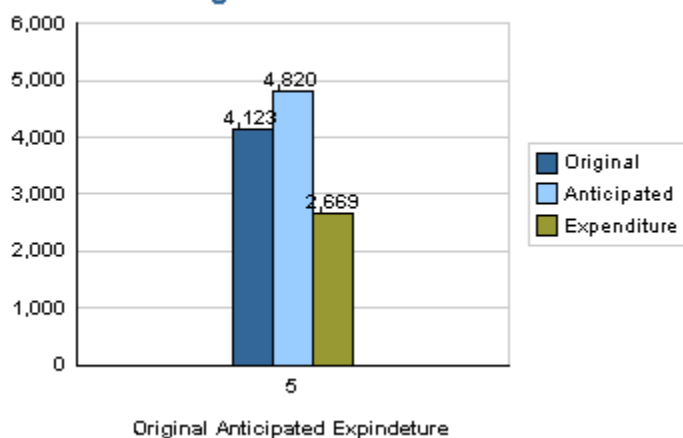

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

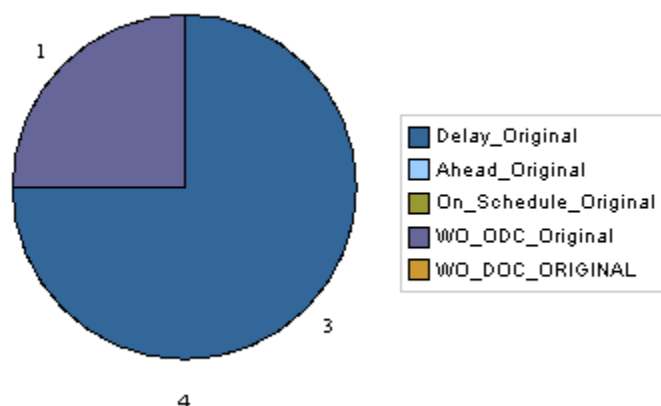

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till July, 2011 is Rs. 18923.54 crore, which is 55.5% of the revised cost of the projects.

Figures are in Rs. Crore

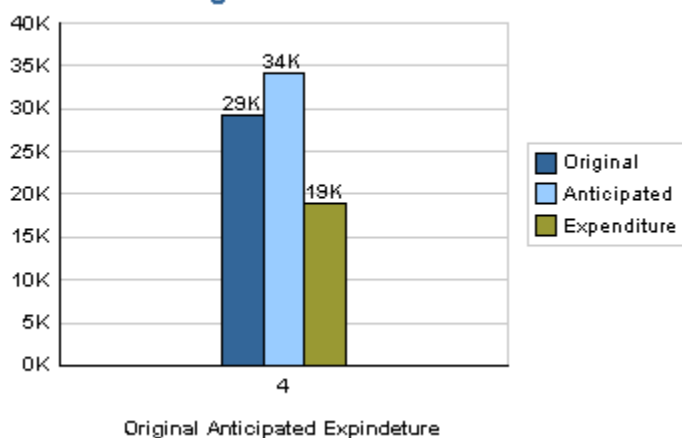

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	30	30608.05	36249.13	20242.27
2	Arunachal Pr.	4	9512.22	9610.51	6910.70
3	Assam	37	23986.44	31829.87	17971.23
4	Bihar	26	27168.57	31861.52	20031.59
5	Chhatisgarh	19	22504.86	37937.78	14786.61
6	Delhi	2	8925.00	19123.77	18194.03
7	Goa	1	204.73	204.73	39.57
8	Gujarat	23	28271.24	28968.54	3306.59
9	Haryana	10	5337.83	7054.75	4555.69
10	Himachal Pr.	7	15023.26	15105.54	12042.47
11	J & K	8	8293.37	18455.56	11324.44
12	Jharkhandd	18	8758.17	13349.17	5794.61
13	Karnataka	27	31565.39	39116.07	14611.98
14	Kerala	9	7247.37	7197.37	2701.32
15	Madhya pradesh	23	16926.11	17158.42	5417.12
16	Maharashtra	51	71609.01	86785.84	35321.05
17	Manipur	1	727.56	3056.85	449.44
18	Mizoram	2	988.06	3343.04	249.75
19	Multi State	103	124581.80	127299.85	38419.18
20	Nagaland	1	850.00	850.00	8.44
21	Orissa	28	52775.14	60641.39	17113.41
22	Punjab	8	4854.69	5840.65	2699.95
23	Rajasthan	17	14544.03	15273.15	8652.45
24	Sikkim	2	1648.88	3644.86	194.54
25	Tamil Nadu	32	42609.48	52170.64	34035.50
26	Tripura	3	1522.39	2053.24	371.83
27	Uttar Pradesh	32	18974.59	21064.79	10836.11
28	Uttaranchal	7	11682.65	14927.07	4821.12
29	West Bengal	27	38340.33	45801.89	21451.56
TOTAL		558	630041.22	755975.99	332554.55

List of project Without Date of Commissioning

(Jul,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Coal</u>									
1	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	39.92	03/2012 -	-	-	13/42
	Total		249.03 -	249.03	39.92				13/42
<u>Mines</u>									
2	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51 4,401.76	4,401.76	4,074.00	12/2008 01/2011	06/2011	5(R3)	117/110
	Total		4,091.51 -	4,401.76	4,074.00				117/110
<u>Petroleum</u>									
3	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	519.93	03/2011 05/2011	06/2011	1(R3)	0/0
4	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
5	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.29	10/2010 -	-	-	0/0
6	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 6,652.22	6,652.22	1.63	03/2012 -	-	-	0/0
	Total		9,080.49 -	8,416.93	1,196.37				0/0
<u>Power</u>									
7	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	821.10	12/2007 12/2009	-	-	14/18
	Total		596.45 -	947.96	821.10				14/18
<u>Railways</u>									
8	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	202.69	-	03/1996 06/2009	03/2008	-15(R1)	0/0
9	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	-	03/2011 -	03/2011	0(O)	0/0
10	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	-	03/2008 03/2009	10/2010	19(R1)	0/0
11	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	232.29	- 02/2009	12/2010	22(R1)	0/0
12	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	186.55	- 03/2009	12/2010	21(R1)	0/0
13	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	151.94	12/2007 03/2010	12/2010	9(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	290.88	03/2009 12/2008	12/2010	24(R1)	0/0
15	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	251.88	- -	12/2010	-	0/0
16	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
17	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	257.15	03/2009 12/2009	03/2011	15(R1)	0/0
18	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]JMRT,Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,241.30	- 12/2010	06/2011	6(R3)	0/1
19	New BG line Rly line from Eklakhi-Balughat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.28	- -	-	-	0/0
20	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD) - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
21	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	94.54	- -	-	-	0/0
22	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	464.70	- -	-	-	0/0
23	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
24	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	945.73	572.91	- -	-	-	0/0
25	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	64.46	- -	-	-	0/0
26	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	85.68	- -	-	-	0/0
27	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
28	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	1,099.20	1,046.57	07/2005 -	-	-	0/0
29	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	554.55	378.41	- 05/2009	-	-	0/0
30	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	84.76	- -	-	-	0/0
31	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	808.81	06/2007 -	-	-	0/0
32	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	300.19	04/2003 03/2010	-	-	0/0
33	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	-	- -	-	-	0/0
34	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
35	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
36	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91	418.17	73.49	-	-	-	0/0
37	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13	1,225.00	209.49	-	-	-	0/0
38	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	173.49	171.52	03/1998 08/2005	-	-	0/0
39	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	25.01	02/2015	-	-	0/0
40	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	791.60	0.76	-	-	-	0/0
41	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92	261.70	18.10	02/2006	-	-	0/0
42	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	303.08	03/2008 06/2008	-	-	0/0
43	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	-	-	-	-	0/0
44	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	396.44	-	-	-	0/0
45	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	-	-	-	-	0/0
46	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	-	-	-	-	0/0
47	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	529.88	35.45	-	-	-	0/0
48	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
49	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	196.95	-	03/2011	-	-	0/0
50	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90	488.76	444.63	06/1999 03/2011	-	-	0/0
51	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	495.44	165.49	03/2004	-	-	0/0
52	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00	567.23	548.49	-	-	-	0/0
53	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94	302.23	323.24	-	-	-	0/0
54	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07	456.45	263.34	06/2004 04/2005	-	-	0/0
55	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00	925.00	499.50	05/2008 03/2011	-	-	0/0
56	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00	227.42	243.20	12/2009 03/2011	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
57	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	718.90	- 12/2010	-	-	0/0
58	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	383.68	- -	-	-	0/0
59	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	402.51	- -	-	-	0/1
60	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,058.65	12/2006 08/2010	-	-	0/0
61	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	227.75	- 02/2011	-	-	0/0
62	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	460.27	02/2010 02/2011	-	-	0/0
63	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	364.24	- -	-	-	0/0
64	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	233.72	- 03/2011	-	-	0/0
65	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	117.60	- -	-	-	0/0
66	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	130.85	- -	-	-	0/0
67	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	358.41	- 03/2011	-	-	0/0
68	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.42	- -	-	-	0/0
69	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	154.42	12/2010 03/2011	-	-	0/0
70	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	128.39	- 12/2010	-	-	0/0
	Total		19,502.35 -	38,895.34					0/2
Shipping & Ports									
71	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -	298.17	293.57	04/2009 -	02/2011	22(O)	0/0
72	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	272.50	219.00	12/2010 -	06/2011	6(O)	0/0
73	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.92	10/2008 -	-	-	0/0
74	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
75	DEVELOPMENT OF COAL TERMINAL - [N25000055]JENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
76	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	-	-	0/0
77	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	821.02	10/2008	-	-	0/0
	Total		4,627.04	4,820.56	1,339.51				0/0
Telecommunications									
78	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	243.30	09/2009	02/2010	5(O)	0/0
79	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
80	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	119.42	03/2009	02/2011	23(O)	0/0
81	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	194.39	12/2008	02/2011	26(O)	0/0
82	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	308.13	03/2009	02/2011	23(O)	0/0
83	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	75.31	06/2009	02/2011	20(O)	0/0
84	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	155.71	01/2009	02/2011	25(O)	0/0
85	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	366.00	225.42	10/2008	02/2011	28(O)	0/0
86	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,100.00	812.08	- 03/2011	02/2011	-1(R3)	0/1
87	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	02/2011	13(O)	0/0
88	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	675.35	01/2010	02/2011	13(O)	0/0
89	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	132.24	01/2010	02/2011	13(O)	0/0
90	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	494.68	12/2008	03/2011	27(O)	0/0
91	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
92	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	106.69	09/2009	03/2011	18(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
94	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	398.08	02/2009	03/2011	25(O)	0/0
95	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	352.89	08/2009	03/2011	19(O)	0/0
96	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	280.72	11/2010	03/2011	4(O)	0/0
97	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75	719.90	395.08	10/2009	03/2011	17(O)	0/0
98	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	-	12/2005	-	-	0/0
99	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
100	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	-	02/2008	-	-	0/0
101	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
102	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
103	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0
104	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
105	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	-	-	0/0
106	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	-	-	0/0
107	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	-	-	0/0
108	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	-	-	0/0
109	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
110	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	-	-	0/0
111	GSM equipment of 975000Lines (2G) 325000 lines 3(G - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	-	-	0/0
112	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	-	-	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
113	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL, West Bengal	06/2008	170.23	170.23	-	06/2009	-	-	0/0
114	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL, Jharkhand	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
	Total		18,756.13	19,400.41	5,699.17				0/1
	Urban Development								
115	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC, Delhi	08/2005	8,676.00 8,605.36	18,894.36	18,127.83	06/2010	06/2011	12(O)	0/10
116	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
	Total		8,790.18	19,067.44	18,127.83				0/10
Grand Total			65,693.18	96,199.43					144/183

List of project Without Original Date of Commissioning

(Jul,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	980.87	- 04/2011	04/2012	12(R3)	0/1
	Total		1,106.29 -	1,106.29	980.87				0/1
	<u>Coal</u>								
2	BALRAM OCP EXTENSION - [N06000044]MCL,	12/2007	172.08 -	172.08	97.15	- -	03/2012	-	4/4
3	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	40.43	- -	03/2012	-	5/7
4	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	1,903.33	- -	10/2012	-	0/6
5	KANIHA OCP - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	103.11	- -	03/2013	-	0/11
6	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	31.67	- -	03/2013	-	5/7
7	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77 -	339.77	0.10	- -	10/2014	-	1/1
8	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	49.16	- -	03/2015	-	0/12
9	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	447.72	35.20	- -	03/2016	-	0/12
10	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	-	- -	03/2017	-	0/12
	Total		7,890.96 -	7,899.76	2,260.15				15/72
	<u>Fertilisers</u>								
11	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	141.65	- 11/2011	11/2011	0(R3)	2/22
	Total		488.75 -	488.75	141.65				2/22
	<u>Steel</u>								
12	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	111.28 232.93	232.93	165.28	- -	10/2011	-	0/1
13	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	217.06	- -	11/2011	-	1/2
14	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	3,316.00 6,325.00	6,325.00	2,078.49	- 12/2011	12/2011	0(R3)	0/11

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	222.78	- -	12/2011	-	2/3
16	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC, Chhattisgarh	01/2007	295.89 607.17	607.17	289.11	- 12/2011	03/2012	3(R3)	18/21
17	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	460.00	112.74	- 05/2012	05/2012	0(R3)	1/2
18	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	11,272.00	- 12/2011	06/2012	6(R3)	1/14
19	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	43.90	- 10/2012	10/2012	0(R3)	3/4
20	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhattisgarh	09/2008	5,185.00 17,265.00	17,265.00	2,935.85	- 03/2013	03/2013	0(R3)	2/20
Total			24,429.17 -	42,208.36	17,337.21				28/78
<u>Petroleum</u>									
21	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 -	204.00	116.54	- -	10/2011	-	1/8
22	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	11/2007	1,816.07 -	1,385.00	884.80	- 12/2011	12/2011	0(R3)	0/1
23	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 -	5,460.61	2,533.49	- -	04/2012	-	0/30
24	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL, Maharashtra	02/2008	825.00 1,827.00	1,827.00	160.16	- 04/2013	04/2013	0(R3)	0/203
25	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	2.33	- -	08/2013	-	0/0
Total			9,924.36 -	10,460.61	3,697.32				1/242
<u>Power</u>									
26	SIMHADRI STPP STAGE -II - [N18000032]NTPC, Andhra Pradesh	08/2007	5,103.39 -	5,038.83	3,991.00	- -	03/2012	-	0/6
Total			5,103.39 -	5,038.83	3,991.00				0/6
<u>Railways</u>									
27	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	550.00	-	- -	03/2012	-	0/0
28	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 -	356.87	-	- 03/2010	03/2013	36(R1)	0/0
29	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	-	- -	07/2011	-	0/0
30	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, Orissa	04/1994	355.38 470.21	700.00	154.13	- -	08/2011	-	0/0
31	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 -	735.10	197.09	- 09/2009	12/2011	27(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
32	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	76.41	- -	12/2011	-	0/0
33	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,139.38	- -	02/2012	-	0/0
34	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	402.11	- 12/2009	02/2012	26(R1)	0/0
35	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	497.96	- -	03/2012	-	0/0
36	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	437.13	- 12/2011	03/2012	3(R3)	0/0
37	KADUR-CHIKMAGALUR-SAKLHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	202.08	- 03/2012	03/2012	0(R3)	0/0
38	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	418.31	- -	03/2012	-	0/0
39	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.53	- -	03/2012	-	0/0
40	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	334.14	- 03/2011	03/2012	12(R3)	0/0
41	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	183.09	- -	03/2012	-	0/0
42	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	883.35	- -	03/2012	-	0/0
43	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	174.33	- -	03/2012	-	0/0
44	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	320.95	- 07/2012	07/2012	0(R3)	0/0
45	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	570.01	- -	12/2012	-	0/0
46	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	261.90	- 03/2012	12/2012	9(R3)	0/0
47	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	233.17	- -	12/2012	-	0/0
48	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	147.14	- -	03/2013	-	0/0
49	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	-	- -	03/2013	-	0/0
50	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	121.20	- 06/2013	06/2013	0(R3)	0/0
51	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70	1,717.29	654.95	-	03/2014	-	0/0
53	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	163.35	-	03/2015	-	0/0
54	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00	607.09	301.92	-	-	-	0/0
			519.67			12/2012			
	Total		8,035.17	19,433.01	8,560.57				0/0
			-						
Grand Total			56,978.09	86,635.61	36,968.77				46/421

List of Dealy Project

(Jul,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,103.67	09/2010 -	01/2012	16(O)	8/80
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,940.00	12/2008 -	06/2012	42(O)	61/119
3	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	899.00	12/2015 05/2016	11/2016	6(R1)	0/70
Total			28,122.00 -	32,960.00	17,942.67				69/269
<u>Civil Aviation</u>									
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 2,015.00	2,015.00	881.21	01/2011 -	12/2011	11(O)	0/0
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	1,282.55	05/2011 -	03/2012	10(O)	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40 -	264.29	141.91	01/2011 -	06/2012	17(O)	0/0
Total			3,524.91 -	4,221.80	2,305.67				0/0
<u>Coal</u>									
7	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,628.27	06/2009 -	08/2011	26(O)	59/26
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,230.62	06/2009 -	03/2012	33(O)	60/24
9	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	81.25	03/2010 -	03/2012	24(O)	0/11
10	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	102.17	03/2011 03/2013	03/2013	0(R3)	0/2
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 741.62	741.62	139.06	03/2010 03/2013	03/2013	0(R3)	0/2
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	191.01	03/2013 09/2012	12/2013	15(R3)	2/22
13	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,065.27	03/2010 -	03/2014	48(O)	3/2
14	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,118.14	03/2010 -	03/2014	48(O)	2/3
15	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.50	03/2011 -	03/2014	36(O)	0/3
16	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.64	03/2011 03/2012	03/2014	24(R3)	0/2
17	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.51	03/2012 -	03/2014	24(O)	0/2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
18	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	76.12	03/2012 03/2013	03/2014	12(R3)	0/2
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	139.84	03/2012 -	03/2015	36(O)	0/2
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011 -	03/2015	48(O)	1/5
21	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	67.16	12/2012 -	03/2015	27(O)	11/44
22	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	83.44	03/2014 -	03/2016	24(O)	1/2
23	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.27	07/2012 03/2014	03/2016	24(R3)	0/2
	Total		11,824.69	14,752.18	7,058.27				139/156
			-						
	Fertilisers								
24	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011 -	11/2011	4(O)	0/0
25	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011 -	03/2012	8(O)	0/0
26	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	197.03	12/2012 -	01/2013	1(O)	0/8
	Total		2,241.63	2,241.63	387.13				0/8
			-						
	Steel								
27	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	8,588.49	10/2009 10/2012	10/2012	0(R3)	47/59
28	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00	11,812.00	1,253.17	02/2011 -	03/2013	25(O)	0/0
	Total		14,825.00	24,103.00	9,841.66				47/59
			-						
	Petroleum								
29	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
30	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	229.13	12/2010 08/2011	08/2011	0(R3)	0/0
31	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60	261.75	227.94	12/2009 -	09/2011	21(O)	0/0
32	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	245.01	12/2010 07/2011	09/2011	2(R3)	0/0
33	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
34	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
35	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	798.00	616.86	04/2011 12/2011	12/2011	0(R3)	0/2
36	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	618.58	04/2010 -	12/2011	20(O)	0/0
37	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	245.78	04/2011 -	12/2011	8(O)	0/0
38	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	-	09/2011 -	12/2011	3(O)	0/0
39	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,599.82	05/2011 -	12/2011	7(O)	0/116
40	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	02/2012	35(O)	0/0
41	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
42	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	132.59	06/2011 03/2012	03/2012	0(R3)	3/9
43	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
44	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,310.99	05/2010 05/2012	05/2012	0(R3)	0/0
45	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,094.03	09/2010 03/2012	05/2012	2(R3)	0/0
46	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	19.28	05/2010 04/2012	05/2012	1(R3)	0/0
47	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	81.57	07/2010 05/2012	05/2012	0(R3)	0/0
48	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,354.04	08/2010 03/2012	06/2012	3(R3)	0/0
49	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	58.95	04/2011 -	07/2012	15(O)	0/0
50	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	116.07	06/2011 07/2012	07/2012	0(R3)	7/9
51	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	877.46	03/2012 08/2012	08/2012	0(R3)	11/10
52	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	64.67	12/2011 -	01/2013	13(O)	0/0
53	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	231.94	03/2006 03/2013	03/2013	0(R3)	6/6

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
54	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,709.86	05/2010 03/2013	03/2013	0(R3)	0/0
55	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	592.78	03/2007 03/2014	03/2014	0(R3)	3/3
56	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,375.28	03/2007 03/2017	03/2017	0(R3)	6/6
57	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	03/2012	0(R3)	0/0
	Total		42,699.87 -	53,394.92	28,742.77				36/161
Power									
58	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10 -	262.10	163.72	09/2010 -	08/2011	11(O)	0/0
59	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07 -	204.07	111.27	06/2011 -	08/2011	2(O)	0/0
60	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25 -	227.03	211.19	05/2011 05/2011	09/2011	4(R3)	0/0
61	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	132.79	06/2010 -	09/2011	15(O)	0/0
62	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,639.93	08/2010 -	10/2011	14(O)	0/0
63	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89 -	230.89	90.47	01/2011 -	10/2011	9(O)	0/1
64	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28 -	621.28	664.47	02/2011 -	11/2011	9(O)	0/1
65	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	639.52	465.07	01/2010 -	11/2011	22(O)	0/22
66	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	1,724.79	1,500.13	11/2009 -	12/2011	25(O)	0/0
67	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,725.13	3,483.30	09/2009 -	12/2011	27(O)	15/30
68	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	4,978.56	2,916.88	07/2010 -	12/2011	17(O)	3/20
69	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.37	292.95	07/2011 -	12/2011	5(O)	0/0
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	144.29	08/2011 -	02/2012	6(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
71	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	205.53	07/2010 02/2012	02/2012	0(R3)	0/0
72	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	69.47	07/2011 -	02/2012	7(O)	0/0
73	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,283.69	2,466.65	04/2005 -	03/2012	83(O)	6/11
74	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,213.00	12/2009 -	03/2012	27(O)	33/60
75	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52 -	2,304.52	1,515.05	10/2010 -	03/2012	17(O)	0/0
76	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	894.26	687.20	10/2009 -	03/2012	29(O)	2/20
77	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	768.92	1,334.24	03/2007 -	05/2012	62(O)	1/25
78	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	651.69	08/2010 -	11/2012	27(O)	0/0
79	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	2,624.00	08/2012 -	11/2012	3(O)	1/16
80	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	989.23	09/2009 -	12/2012	39(O)	0/0
81	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,946.85	1,715.27	11/2008 -	12/2012	49(O)	25/38
82	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	693.00	11/2011 -	12/2012	13(O)	6/34
83	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,044.00	10/2012 -	12/2012	2(O)	2/15
84	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	1,953.00	10/2012 -	12/2012	2(O)	3/16
85	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,739.00	04/2009 -	03/2013	47(O)	19/9
86	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	339.93	09/2010 -	03/2013	30(O)	0/0
87	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	254.83	11/2011 -	03/2013	16(O)	0/0
88	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	242.11	11/2011 -	03/2013	16(O)	0/0
89	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	128.43	02/2012 -	03/2013	13(O)	0/0
90	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	812.27	02/2012 -	03/2013	13(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	244.42	05/2012	03/2013	10(O)	0/0
92	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	80.58	01/2012	07/2013	18(O)	0/0
93	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03	2,047.03	1,280.36	01/2012	09/2013	20(O)	2/10
94	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	126.43	11/2011	09/2013	22(O)	0/0
95	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	2,232.00	06/2011	10/2013	28(O)	0/29
96	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	2,378.00	08/2013	10/2013	2(O)	1/18
97	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72	913.63	246.20	07/2006	01/2014	90(O)	2/5
98	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,142.00	03/2013	06/2014	15(O)	5/13
99	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	3,919.59	3,239.34	09/2009	07/2014	58(O)	1/20
100	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	6,285.33	5,004.42	09/2010	08/2014	47(O)	2/11
101	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	6,015.00	12/2009	09/2014	57(O)	15/70
102	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	2,755.04	08/2013	09/2014	13(O)	0/0
103	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	801.63	07/2014	01/2016	18(O)	0/0
104	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00	2,978.86	261.62	07/2010	02/2016	67(O)	1/1
105	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	3,422.44	164.91	07/2014	05/2016	22(O)	0/7
106	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90	2,496.90	1,532.51	05/2013 06/2016	06/2016	0(R3)	79/22
Total			118,652.28	124,449.40	68,998.82				224/524
Railways									
107	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.99	03/2002	09/2011	114(O)	0/0
108	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50	252.50	158.67	02/2010	11/2011	21(O)	0/0
109	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	553.70	03/1994	12/2011	213(O)	0/0
110	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	466.70	02/2009	12/2011	34(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51	259.51	61.97	12/2011	02/2012	2(O)	0/0
112	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	542.24	03/1995	03/2012	204(O)	0/0
113	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	-	03/2010	03/2012	24(O)	0/0
114	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17	220.00	217.12	03/2011	03/2012	12(O)	0/0
115	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97	723.27	376.53	06/2005 07/2011	03/2012	8(R3)	0/0
116	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36	803.39	784.01	03/2011	03/2012	12(O)	0/0
117	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	142.00	03/2007 03/2007	06/2012	63(R1)	0/0
118	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	1,211.22	385.44	03/2005 12/2008	12/2012	48(R1)	0/0
119	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	981.00	526.28	03/2009	12/2012	45(O)	0/0
120	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.98	949.38	10/2007	12/2012	62(O)	0/0
121	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	-	03/2010	12/2012	33(O)	0/0
122	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	603.04	41.02	03/2012	03/2013	12(O)	0/0
123	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97	189.97	57.75	12/2011	11/2013	23(O)	0/0
124	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90	223.01	82.70	12/2012	12/2013	12(O)	0/0
125	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31	4,091.33	2,712.15	03/2009	12/2013	57(O)	0/0
126	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,208.23	04/2008 03/2014	03/2014	0(R3)	0/0
127	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00	1,655.80	740.96	12/2008	03/2014	63(O)	0/0
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	277.24	03/2014	03/2015	12(O)	0/0
129	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	449.44	03/2011 03/2014	03/2016	24(R3)	0/0
130	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	0.21	03/2014	03/2016	24(O)	0/0
131	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	-	03/2016	06/2016	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
132	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
	Total		22,639.01	43,214.04	19,084.26				0/0
			-						
<u>Road Transport & Highways</u>									
133	GAGODHAR-GARAMORE(PK-IV,NH15) KM.245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	436.30	11/2007 -	08/2011	45(O)	0/0
134	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	351.20	10/2008 -	08/2011	34(O)	0/0
135	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	870.60	03/2009 -	08/2011	29(O)	0/0
136	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	08/2011	9(O)	0/0
137	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09 -	276.09	295.20	09/2009 -	08/2011	23(O)	0/0
138	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	657.60	07/2010 -	08/2011	13(O)	0/0
139	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	359.00	07/2010 -	08/2011	13(O)	0/0
140	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	165.14	02/2004 -	08/2011	90(O)	0/0
141	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	147.83	08/2004 -	09/2011	85(O)	0/0
142	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	157.70	08/2004 -	09/2011	85(O)	0/0
143	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	09/2011	78(O)	0/0
144	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	338.70	10/2008 -	09/2011	35(O)	0/0
145	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	179.10	03/2008 -	09/2011	42(O)	0/0
146	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	193.10	147.70	03/2008 -	09/2011	42(O)	0/0
147	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	253.50	10/2008 -	09/2011	35(O)	0/0
148	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	557.10	06/2008 -	09/2011	39(O)	0/0
149	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	598.90	03/2009 -	09/2011	30(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	236.50	11/2008	09/2011	34(O)	0/0
151	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	876.70	07/2010	09/2011	14(O)	0/0
152	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	75.70	04/2004	10/2011	90(O)	0/0
153	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.60	01/2009	10/2011	33(O)	0/0
154	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	251.80	06/2008	10/2011	40(O)	0/0
155	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	385.30	12/2008	10/2011	34(O)	0/0
156	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	10/2011	9(O)	0/0
157	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	277.00	10/2008	11/2011	37(O)	0/0
158	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30	151.30	171.70	10/2008	11/2011	37(O)	0/0
159	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
160	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	293.80	09/2007	12/2011	51(O)	0/0
161	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	231.10	09/2007	12/2011	51(O)	0/0
162	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	85.40	09/2008	12/2011	39(O)	0/0
163	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	203.00	06/2005	12/2011	78(O)	0/0
164	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	257.20	10/2008	12/2011	38(O)	0/0
165	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	227.00	394.10	10/2008	12/2011	38(O)	0/0
166	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	347.80	03/2008	12/2011	45(O)	0/0
167	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	223.50	02/2009	12/2011	34(O)	0/0
168	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	77.24	04/2009	12/2011	32(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
169	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	169.50	06/2008	12/2011	42(O)	0/0
170	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	393.20	12/2008	12/2011	36(O)	0/0
171	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	363.20	12/2008	12/2011	36(O)	0/0
172	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	196.00	06/2008	12/2011	42(O)	0/0
173	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	261.50	09/2008	12/2011	39(O)	0/0
174	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	186.10	11/2008	12/2011	37(O)	0/0
175	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	275.70	10/2008	12/2011	38(O)	0/0
176	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	217.40	10/2008	12/2011	38(O)	0/0
177	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	420.30	09/2008	12/2011	39(O)	0/0
178	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	254.20	06/2008	12/2011	42(O)	0/0
179	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	12/2011	30(O)	0/0
180	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	232.40	06/2008	12/2011	42(O)	0/0
181	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	242.00	06/2008	12/2011	42(O)	0/0
182	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	468.80	03/2008	12/2011	45(O)	0/0
183	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	161.30	06/2008	12/2011	42(O)	0/0
184	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	204.90	04/2008	12/2011	44(O)	0/0
185	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	118.60	05/2008	12/2011	43(O)	0/0
186	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	186.90	06/2008	12/2011	42(O)	0/0
187	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	580.30	06/2009	12/2011	30(O)	0/0
188	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	692.70	10/2009	12/2011	26(O)	0/0
189	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	313.40	03/2010	12/2011	21(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
190	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.60	09/2009	12/2011	27(O)	0/0
191	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
192	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	336.50	05/2010	12/2011	19(O)	0/0
193	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16(O)	0/0
194	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	523.50	05/2010	12/2011	19(O)	0/0
195	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	01/2012	18(O)	0/0
196	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	176.00	09/2007	03/2012	54(O)	0/0
197	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	206.80	10/2008	03/2012	41(O)	0/0
198	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	115.70	04/2008	03/2012	47(O)	0/0
199	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	175.60	04/2008	03/2012	47(O)	0/0
200	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	138.30	04/2010	03/2012	23(O)	0/0
201	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	178.60	02/2010	03/2012	25(O)	0/0
202	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
203	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	165.50	10/2008	06/2012	44(O)	0/0
204	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
205	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.20	12/2009	06/2012	30(O)	0/0
206	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	157.00	09/2010	06/2012	21(O)	0/0
207	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,519.00	10/2011	06/2012	8(O)	0/0
208	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	115.60	05/2008	08/2012	51(O)	0/0
209	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	506.30	10/2011	08/2012	10(O)	0/0
210	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	183.70	06/2010	10/2012	28(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
211	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.30	09/2009	10/2012	37(O)	0/0
212	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
213	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	813.80	09/2012	10/2012	1(O)	0/0
214	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	175.60	07/2008	12/2012	53(O)	0/0
215	GANJAM-ICCHAPURUM, NH-5 (NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	247.90	02/2004	12/2012	106(O)	0/0
216	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	831.50	09/2010	03/2013	30(O)	0/0
217	AGRA-BYPASS (NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	111.20	09/2007	06/2013	69(O)	0/0
218	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	822.60	11/2012	06/2013	7(O)	0/0
219	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.60	04/2009	07/2013	51(O)	0/0
220	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
221	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
222	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
223	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	40.29	09/2007	12/2013	75(O)	0/0
224	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	27.94	07/2009	12/2013	53(O)	0/0
	Total		31,476.28	32,119.69	32,004.30				0/0
Shipping & Ports									
225	MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK, Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
226	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00 165.00	165.00	117.28	12/2005 01/2008	10/2011	45(R3)	0/0
227	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
228	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
229	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2(O)	0/0
230	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03	277.03	55.40	12/2011	05/2012	0(R3)	0/0
231	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	1,460.00	545.85	12/2010	09/2012	21(O)	0/0
232	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
233	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.16	02/2011	03/2013	25(O)	0/0
234	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	-	03/2011	03/2013	24(O)	0/0
235	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00	272.50	-	01/2009	05/2013	52(O)	0/0
236	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00	600.00	67.00	03/2006	12/2013	93(O)	0/0
	Total		8,569.67	9,394.82	1,226.96				0/0
	Telecommunications								
237	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007	08/2011	54(O)	0/0
238	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
239	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	20.90	10/2010	03/2012	17(O)	0/0
	Total		880.00	860.41	162.99				0/0
	Urban Development								
240	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	03/2013	15(O)	6/6
	Total		6,395.00	11,609.00	2,267.57				6/6
	Water Resources								
241	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Grand Total			292,393.24	354,507.89	190,058.56				521/1183

LIST OF DELAYED PROJECTS W.R.T. REVISED

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
	Atomic Energy						
1	KAKRAPAR ATOMIC POWER PROJECT - 3&4	10/2009	05/2016	11/2016	11459.00	11459.00	899.00
2	KUDANKULAM APP (NPCIL)	12/2001	12/2008	06/2012	13171.00	15824.00	13940.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	01/2012	3492.00	5677.00	3103.67
4	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPALLE	09/2007	04/2011	04/2012	1106.29	1106.29	980.87
	Civil Aviation						
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	08/2008	05/2011	03/2012	1942.51	1942.51	1282.55
6	C/o new Airport at Pakyong(Sikkim) Airport	01/2009	01/2011	06/2012	309.40	264.29	141.91
7	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1)	08/2008	01/2011	12/2011	1273.00	2015.00	881.21
	Coal						
8	ADRIYALA SHAFT PROJECT	09/2006	09/2012	12/2013	212.34	779.26	191.01
9	AMLOHRI EPR (NCL) (6 MTY)	05/2006	03/2014	03/2016	1352.04	1143.54	83.44
10	BARSINGSAR TPS (2X125MW) (NLC)	12/2004	06/2009	08/2011	1114.18	1626.09	1628.27
11	BLOCK-B OCP NCL (3.5 MTY)	06/2006	03/2012	03/2015	746.04	535.10	139.84
12	Churi Benti UG	06/2007	03/2012	03/2014	163.51	163.51	33.64
13	DIPKA EXPANSION OCP (SECL) (20 MTY)	07/2005	03/2010	03/2014	1268.53	1943.66	1118.14
14	GEVRA EXPANSION OCP (SECL) (25 MTY)	07/2005	03/2010	03/2014	1667.55	2675.67	1065.27
15	JHANJRA R-VI SEAM PSLW	11/2006	03/2011	03/2015	287.18	287.17	0.00
16	KAKATIYA LAONGWALL	12/2008	12/2012	03/2015	453.63	453.63	67.16
17	KULDA OCP (MAHANADI COALFIELDS LTD.)	01/2005	03/2010	03/2012	302.96	302.96	81.25
18	MAGADH OC (CCL)	07/2006	03/2014	03/2016	469.78	706.40	16.27
19	North Urimari OCP	12/2007	03/2012	03/2014	179.87	179.87	66.51
20	RAJMAHAL OC EXP.	02/2006	03/2011	03/2014	50.08	153.82	19.50
21	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	10/2004	06/2009	03/2012	2030.78	2453.57	2230.62
22	Tapin OCP	08/2008	03/2013	03/2014	264.68	264.68	76.12
	Fertilisers						
23	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJAIPUR-II	09/2008	07/2011	03/2012	438.00	438.00	105.79
24	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS	09/2008	07/2011	11/2011	325.00	325.00	84.31

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
25	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	01/2010	12/2012	01/2013	1478.63	1478.63	197.03
	Mines						
26	SECOND PHASE EXPANSION OF NALCO MINE, REFINERY, SMELTER AND CAPTIVE POWER PLANT	10/2004	01/2011	06/2011	4091.51	4401.76	4074.00
	Petroleum						
27	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA	02/2008	04/2011	07/2012	370.11	370.11	58.95
28	ADDITIONAL GAS PROCESSING UNITS AT URAN	10/2008	12/2011	01/2013	1797.35	1797.35	64.67
29	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	06/2007	09/2011	12/2011	736.65	736.65	0.00
30	DEVELOPMENT OF B-193 CLUSTER FIELDS	06/2007	03/2012	06/2012	3248.78	5633.44	1354.04
31	DEVELOPMENT OF B-22 CLUSTER FIELDS	01/2007	03/2012	05/2012	2323.40	2920.82	1094.03
32	DEVELOPMENT OF C-SERIES FIELDS	08/2006	12/2008	11/2011	3195.16	2800.00	2520.91
33	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON	06/2006	09/2009	08/2011	1431.91	1690.13	1596.80
34	EURO-IV DHDT	09/2008	05/2011	12/2011	2615.69	2615.69	1599.82
35	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	09/2006	06/2010	10/2011	2305.30	3005.30	2416.96
36	HEERA RECONSTRUCTION	05/2008	04/2010	12/2011	706.70	706.70	618.58
37	INTEGRATED DEV OF G1 and GS-15 (ONGCL)	04/2003	05/2011	05/2012	429.82	2218.01	1237.61
38	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	06/2009	12/2010	06/2011	613.54	727.88	671.52
39	MNW-NF BRIDGE PROJECT	05/2008	03/2009	02/2012	175.21	162.12	58.26
40	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REFINERY	04/2008	12/2009	09/2011	293.60	261.75	227.94
41	NEELAM RECONSTRUCTION	05/2008	04/2011	12/2011	305.08	305.08	245.78
42	North Tapti Gas Field Development	07/2008	05/2011	06/2011	589.70	755.76	519.93
43	REFRIGERATED LPG STORAGE AT JNPT	06/2008	07/2011	09/2011	304.40	304.40	245.01
44	REVAMPING OF WIN PLATFORM AT MH ASSET	05/2008	04/2012	05/2012	333.40	656.51	19.28
	Power						
45	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I	02/2009	02/2012	03/2013	1347.32	1347.32	812.27
46	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-III	11/2009	05/2012	03/2013	1075.12	1075.12	244.42
47	BARH STPP STAGE -II	02/2008	08/2013	10/2013	7341.04	7341.04	2378.00
48	BARH STPP(3X660MW) NTPC	12/2003	12/2009	09/2014	8692.97	8693.00	6015.00
49	BONGAIGAON THERMAL POWER PROJECT	01/2008	06/2011	10/2013	4375.35	4375.35	2232.00
50	CHAMERA, STAGE-III (NHPC)	08/2005	08/2010	10/2011	1405.63	1405.63	1639.93
51	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	08/2006	02/2011	11/2011	621.28	621.28	664.47

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
52	EASTERN REGION STRENGTHENING SCHEME-I	10/2006	10/2009	03/2012	975.96	894.26	687.20
53	EASTERN REGION STRENGTHENING SCHEME-II	12/2007	06/2010	09/2011	227.52	227.52	132.79
54	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMERA-II HEP	09/2007	09/2010	08/2011	262.10	262.10	163.72
55	KISHANGANGA HEP	07/2007	07/2014	01/2016	2238.67	3642.04	801.63
56	KOLDAM HEP (NTPC)	10/2002	04/2009	03/2013	4527.15	4527.15	3739.00
57	KOTESHWAR HEP (THDC)	04/2000	04/2005	03/2012	1301.56	2283.69	2466.65
58	KUDANKULAM-APP TRANS. SYSTEM (PGCIL)	05/2005	11/2008	12/2012	1779.29	1946.85	1715.27
59	LOHARINAG-PAL HEP(4X150MW)	06/2006	11/2011	12/2012	2895.10	2895.10	693.00
60	MOUDA STPP	11/2008	08/2012	11/2012	5459.28	6010.89	2624.00
61	NIMOO BAZGO HYDROELECTRIC PROJECT	08/2006	08/2010	11/2012	611.02	611.02	651.69
62	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	02/2009	08/2013	09/2014	11130.19	11130.19	2755.04
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	02/2009	02/2012	03/2013	410.29	410.29	128.43
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV	02/2009	11/2011	03/2013	520.48	520.48	254.83
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII	02/2009	08/2011	02/2012	210.79	210.79	144.29
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	02/2009	11/2011	03/2013	509.66	509.66	242.11
67	PARBATI H.E.P. STAGE -III (NHPC)	10/2005	10/2010	03/2012	2304.52	2304.52	1515.05
68	PARBATI HEP (NHPC) II	09/2002	09/2009	07/2014	3919.59	3919.59	3239.34
69	RAMPUR HEP(412 MW)	01/2007	01/2012	09/2013	2047.03	2047.03	1280.36
70	RIHAND STTP STAGE-III (2X500MW)	01/2009	10/2012	12/2012	6230.81	6230.81	1953.00
71	SIPAT STPP STAGE - I (NTPC)	12/2003	12/2009	03/2012	8323.39	8323.39	7213.00
72	SUBANSIRI LOWER H.E.P (NHPC)	09/2003	09/2010	08/2014	6285.33	6285.33	5004.42
73	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION	03/2009	07/2011	02/2012	196.10	196.10	69.47
74	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	09/2005	09/2009	12/2012	1061.38	1061.38	989.23
75	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	10/2003	03/2007	05/2012	768.92	768.92	1334.24
76	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	07/2010	02/2016	1657.00	2978.86	261.62
77	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	04/2008	07/2011	12/2011	297.37	297.37	292.95
78	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)	12/2005	09/2009	12/2011	3779.46	3725.13	3483.30
79	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III	12/2008	06/2011	08/2011	204.07	204.07	111.27
80	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	07/2006	01/2010	11/2011	557.24	639.52	465.07
81	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP	02/2009	11/2011	09/2013	184.19	184.19	126.43

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
82	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II	10/2006	05/2011	09/2011	238.25	227.03	211.19
83	TRIPURA GAS BASED POWER PROJECT	07/2009	01/2012	07/2013	421.01	623.44	80.58
84	TUIRIAL HE PROJECT(NEEPCO)	07/1998	07/2006	01/2014	368.72	913.63	246.20
85	Tapovan-Vishnugad HEP (4x130MW)	11/2006	03/2013	06/2014	2978.48	2978.48	1142.00
86	URI H.E.P STAGE -II (NHPC)	08/2005	11/2009	12/2011	1724.79	1724.79	1500.13
87	VINDHYACHAL STTP STAGE-IV	01/2009	10/2012	12/2012	5915.00	5915.00	2044.00
88	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	07/2014	05/2016	2491.58	3422.44	164.91
89	WESTERN REGION STRENGTHENING SCHEME-IX	04/2008	01/2011	10/2011	230.89	230.89	90.47
90	WESTERN REGION STRENGTHENING SCHEME-II	07/2006	07/2010	12/2011	5221.23	4978.56	2916.88
91	WESTERN REGION STRENGTHENING SCHEME-V	12/2007	09/2010	03/2013	477.69	477.69	339.93
	Railways						
92	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	04/2003	12/2008	12/2010	230.73	399.50	290.88
93	BANKURA - DAMODAR (GC) (SER)	03/1998	12/2008	12/2012	111.90	1211.22	385.44
94	BHOPAL BINA 3D LINE DOUBLING	09/2007	03/2010	12/2012	687.20	687.20	0.00
95	BILASPUR-URKURA (DL)	04/1997	03/2009	03/2011	151.52	273.00	0.00
96	Dakshin-barasat-lakshmikantapur (ER)	04/2009	12/2011	02/2012	259.51	259.51	61.97
97	ELECTRIFICATION OF MORADABAD-ROZA	12/2004	03/2011	03/2012	129.17	220.00	217.12
98	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	03/1984	03/1995	03/2012	520.00	634.13	542.24
99	GUNA-ETAWAH(NCR), NL	04/1985	03/1994	12/2011	158.77	540.96	553.70
100	Ghutiasharif-Canning (ER)	04/2009	12/2011	11/2013	189.97	189.97	57.75
101	HARIDASPUR-PARADEEP(NL)	04/1996	09/2009	12/2011	301.64	735.10	197.09
102	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	06/2012	31.42	499.16	142.00
103	JIND-SONEPAT (NL),NR	01/2004	03/2012	12/2012	190.81	401.83	261.90
104	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	03/2014	03/2016	727.56	3056.85	449.44
105	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	04/2000	03/2009	12/2010	133.41	211.90	186.55
106	Katakhal to Bhairabi	04/1998	12/2012	12/2013	227.90	223.01	82.70
107	LANJHIGARH-JUNAGARH NL(ECOR)	04/1993	03/2002	09/2011	100.00	170.00	181.99
108	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	04/1996	03/2009	12/2013	1676.31	4091.33	2712.15
109	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	04/1995	12/2011	03/2012	184.00	675.00	437.13
110	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	04/1996	03/2011	03/2012	114.01	427.89	334.14
111	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	04/2003	12/2010	06/2011	3125.20	4501.80	4241.30
112	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP	04/2008	03/2014	03/2015	5300.00	5300.00	277.24

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
113	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	02/2009	12/2011	155.74	429.49	466.70
114	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	04/2000	12/2008	03/2014	733.00	1655.80	740.96
115	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP)	04/2010	03/2014	03/2016	2069.60	2069.60	0.21
116	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbander (MTP)	04/2010	03/2016	06/2016	2397.72	2397.72	0.00
117	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	04/2005	12/2009	03/2011	240.00	329.70	257.15
118	PANSPURA-KHARAGPUR 3D LINE	09/2007	02/2010	11/2011	252.50	252.50	158.67
119	PATNA GANGA BRIDGE (NL), ECR	04/2001	10/2007	12/2012	624.47	1389.98	949.38
120	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	04/2005	03/2009	10/2010	148.61	227.52	0.00
121	RAICHUR-GUNTAKAL(DL)(SCR)	04/2003	03/2010	12/2010	136.62	221.90	151.94
122	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	04/2002	03/2009	12/2012	921.00	981.00	526.28
123	RAJATGARH-BARANG(LD),ECOR	04/1999	02/2009	12/2010	166.16	243.40	232.29
124	Ratlam-Mhow-Khandwa-Akola (GC)	04/2008	03/2012	03/2013	603.04	603.04	41.02
125	SALKA ROAD -ANUPNAGAR LINE DOUBLING	09/2006	03/2010	03/2012	324.90	324.90	0.00
126	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	04/2007	03/2011	03/2012	643.36	803.39	784.01
127	TAMLUK DIGHA,LINE DOUBLING (SER)	03/1984	07/2011	03/2012	293.97	723.27	376.53
128	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	04/2000	12/2009	02/2012	157.96	762.33	402.11
129	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	03/2001	12/2017	2500.00	11270.00	7168.53
130	VIRAMGAM-BHILDI(WR),GC	04/1990	03/2010	03/2013	155.66	356.87	0.00
	Road Transport & Highways						
131	AGRA-BYPASS(NS-1/UP-1), NH-2,3	12/2003	09/2007	06/2013	348.16	348.16	111.20
132	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	04/2000	03/2005	12/2011	367.49	367.49	453.68
133	AMRITSAR-PATHANKOT	05/2010	11/2012	06/2013	705.00	705.00	822.60
134	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	12/2003	11/2008	09/2011	221.82	221.82	236.50
135	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	03/2005	01/2009	10/2011	190.00	190.00	227.60
136	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	12/2003	10/2008	09/2011	193.00	193.00	338.70
137	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	12/2003	10/2008	08/2011	217.00	217.00	351.20
138	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5	04/2000	02/2004	08/2011	228.70	228.70	165.14
139	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI)	12/2003	06/2008	12/2011	237.80	237.80	196.00
140	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	12/2003	06/2008	12/2011	195.00	195.00	169.50

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
141	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	12/2003	06/2005	12/2011	230.00	230.00	203.00
142	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	04/2010	03/2012	217.61	217.61	138.30
143	Bijapur-Hungund Section	09/2010	09/2010	03/2013	748.00	748.00	831.50
144	CHAMBAL BRIDGE, NH-76 (RJ-5)	12/2003	02/2010	03/2012	275.00	281.31	178.60
145	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	05/2009	10/2011	08/2012	572.30	572.30	506.30
146	DAKOBA TO NAGAON (NH-36)(NHAI)	12/2003	06/2008	10/2011	225.00	225.00	251.80
147	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	12/2003	10/2008	06/2012	300.00	300.00	165.50
148	DELHI/ HARYANA BORDER TO ROHTAK	04/2007	05/2010	12/2011	486.00	486.00	523.50
149	DHARAMTUL TO SONAPUR (AS-19)	12/2003	06/2008	12/2011	200.00	200.00	186.90
150	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	05/2008	12/2011	160.00	160.00	118.60
151	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	12/2003	09/2010	06/2012	232.45	232.45	157.00
152	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	01/2008	01/2011	10/2011	464.00	464.00	419.90
153	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	12/2003	09/2008	12/2011	332.94	332.94	261.50
154	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass	04/2010	06/2011	10/2012	1170.52	1170.52	4.41
155	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	12/2003	11/2007	08/2011	412.78	479.54	436.30
156	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	12/2003	09/2008	12/2011	155.00	201.66	85.40
157	GANJAM-ICCHAPURUM,NH-5(NHAI)	04/2000	02/2004	12/2012	263.27	263.27	247.90
158	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	12/2003	09/2007	12/2011	275.00	275.00	293.80
159	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	12/2003	10/2009	12/2011	600.24	600.24	692.70
160	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	12/2003	10/2008	12/2011	227.00	227.00	394.10
161	GUWAHATI TO NALBARI (AS-5)	12/2003	04/2008	03/2012	198.16	198.16	175.60
162	GUWHATI TO NALBARI (AS-4)	12/2003	04/2008	03/2012	175.96	175.96	115.70
163	GWALIOR BYPASS, NH-75,3	12/2003	10/2009	06/2012	300.93	300.93	294.10
164	GWALIOR-JHANSI, NH-75	12/2003	12/2009	06/2012	604.00	604.00	412.20
165	Gujarat/Maharashtra BorderSurat-Hazira Port Section	03/2010	09/2012	10/2012	1509.10	1509.10	813.80
166	Gurgaon-Kotputli Km 42.70 to 54.4 Km	04/2009	10/2011	06/2012	1673.70	1673.70	1519.00
167	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	04/2000	03/2005	09/2011	273.00	522.00	475.60
168	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	03/2005	09/2007	12/2011	220.00	220.00	231.10

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
169	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	02/2009	12/2011	280.00	280.00	223.50
170	HARANGAJO TO MAIBANG, NH-54	12/2003	07/2009	12/2013	196.00	196.00	27.94
171	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54	12/2003	09/2007	12/2013	212.00	212.00	40.29
172	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	04/2000	08/2004	09/2011	318.00	207.56	157.70
173	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4)	04/2000	08/2004	09/2011	241.00	196.65	147.83
174	JHAJHARPUR TO DARBANGA (BR-7)	12/2003	09/2008	12/2011	340.00	340.00	420.30
175	JHANSI TO LALITPUR, NH-25,26	12/2003	09/2009	12/2011	355.06	355.06	294.60
176	JHANSI TO LALITPUR, NH-26	12/2003	09/2009	08/2011	276.09	276.09	295.20
177	KASIA TO GORAKHPUR (NH-28)(NHAI)	12/2003	12/2008	12/2011	242.00	242.00	393.20
178	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AND AFFLUX-BOND (BR-5)	12/2003	03/2010	12/2011	418.04	418.04	313.40
179	KOTA BYPASS,RJ-4, NH-76 (NHAI)	12/2003	10/2008	11/2011	275.00	250.39	277.00
180	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	12/2003	10/2008	12/2011	240.00	240.00	257.20
181	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7	12/2003	06/2010	10/2012	407.60	407.60	183.70
182	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7	12/2003	09/2009	10/2012	263.17	263.17	233.30
183	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	12/2003	10/2008	09/2011	225.00	225.00	253.50
184	LALITPUR TO SAGAR, NH-26 (NHAI)	12/2003	11/2008	12/2011	198.00	198.00	186.10
185	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	03/2005	11/2010	08/2011	629.00	629.00	910.00
186	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008	07/2013	155.04	280.13	39.26
187	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000	12/2003	04/2009	07/2013	199.81	385.13	29.60
188	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008	12/2013	167.64	167.64	40.71
189	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500	12/2003	04/2009	12/2011	200.00	200.00	77.24
190	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	03/2005	03/2009	08/2011	359.00	359.00	870.60
191	NAGAON TO DHARAMTUL (AS-2)	12/2003	06/2008	12/2011	264.72	264.72	242.00
192	NAGPUR-KONDHALI,NH-6(NHAI)	03/2005	12/2008	10/2011	168.00	168.00	385.30
193	NALBARI T BIJNI (AS-7)	12/2003	04/2008	12/2011	208.00	208.00	204.90
194	NALBARI TO BIJNI (AS-6)	12/2003	06/2008	12/2011	225.00	225.00	161.30
195	NALBARI TO BIJNI (AS-8)	12/2003	06/2008	12/2011	200.00	200.00	254.20
196	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	03/2005	07/2010	09/2011	441.00	441.00	876.70

[illegible]

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
223	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS	10/2007	06/2011	11/2011	359.44	359.44	354.81
224	C/O Berthing and Allied Facilities off tekra near TUNA	04/2005	02/2011	03/2013	882.00	1060.00	0.16
225	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	11/2007	12/2010	09/2012	1228.00	1460.00	545.85
226	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	12/2005	03/2011	03/2013	702.00	755.50	0.00
227	Construction & License out the OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR COAL HANDELLING	06/2006	12/2010	06/2011	230.00	272.50	219.00
228	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	10/2002	03/2006	12/2013	150.00	600.00	67.00
229	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH	01/2002	01/2008	10/2011	165.00	165.00	117.28
230	Mechanization of coal handling facilities to 200000 DWT Vessels on DBFOT basis	02/2010	06/2010	11/2012	444.10	444.10	0.00
231	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	03/2007	04/2009	02/2011	245.67	298.17	293.57
232	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT COCHIN	03/2008	01/2009	05/2013	375.00	272.50	0.00
233	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN	03/2009	01/2012	03/2012	3500.00	3500.00	0.00
	Steel						
234	Bailadila Iron Ore Deposit- II(B)(NMDC)	01/2007	12/2011	03/2012	295.89	607.17	289.11
235	EXPANSION OF IISCO STEEL PLANT	02/2008	12/2011	06/2012	14443.00	16408.00	11272.00
236	EXPENSION OF ROURKELA STEEL PLANT	09/2008	02/2011	03/2013	6133.00	11812.00	1253.17
	Telecommunications						
237	Assam Telecom Circle, Phase-V.I, 2G & 3G	06/2007	01/2009	02/2011	336.81	336.81	155.71
238	CONVERGENT BILLING AND CRM(MUMBAI)	01/2006	02/2007	08/2011	247.00	247.00	75.89
239	CONVERGENT BILLING AND CRM-MTNL(DELHI)	12/2005	02/2007	08/2011	249.00	229.41	66.20
240	ERP implementation in BSNL on Turnkey basis	10/2009	10/2010	03/2012	384.00	384.00	20.90
241	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	01/2008	03/2009	02/2011	192.48	192.48	119.42
242	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3G) PH-5.1	09/2008	09/2009	02/2010	1799.94	1799.94	243.30
243	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1	02/2008	12/2008	02/2011	373.94	373.94	194.39

SN	PROJECTS NAME	DOA	DOC ORIGINAL	DOC REVISED/ ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
244	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	11/2007	03/2009	02/2011	277.34	377.54	308.13
245	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)PH-5	06/2007	12/2008	03/2011	601.49	601.49	494.68
246	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN UP(W)-PH-V.I	05/2007	03/2009	03/2011	335.91	335.91	182.45
247	GSM equipment of 1500000Lines (2G) 264700lines 3(G)Andhra Pradesh Phase V.1 Telecom Circle	01/2009	01/2010	02/2011	922.91	922.91	346.90
248	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle	11/2009	11/2010	03/2011	916.70	916.70	280.72
249	GSM equipment of 1700000Lines (2G) 234100 lines 3(G)Karnataka Phase V.1 Telecom Circle	10/2008	10/2009	03/2011	677.75	719.90	395.08
250	GSM equipment of 1867000Lines (2G) 383000 lines 3(G) GujaratPhase V.1 Telecom Circle	08/2008	08/2009	03/2011	868.00	868.00	352.89
251	GSM equipment of 1900000Lines (2G) 335500lines 3(G)kerala Phase V.1 Telecom Circle	01/2009	01/2010	02/2011	848.70	848.70	675.35
252	GSM equipment of 200000Lines (2G) UP(West)Phase V.2 Telecom Circle	10/2008	10/2009	03/2011	336.84	336.84	35.75
253	GSM equipment of 614000Lines (2G) 150000lines 3(G) Chennai TD Phase V.1 Telecom Circle	01/2009	01/2010	02/2011	315.19	315.19	132.24
254	GSM equipment of 849862Lines (2G) 150138 lines 3(G) West Bengal Phase V.1 Telecom Circle	02/2008	02/2009	03/2011	584.33	584.33	398.08
255	GSM equipment of 900000Lines (2G) PunjabPhase V.2 Telecom Circle	09/2008	09/2009	03/2011	241.49	241.49	106.69
256	GSM equipment of 945000Lines (2G) 225000lines 3(G) Bihar Phase V.1 Telecom Circle	10/2007	10/2008	02/2011	366.00	366.00	225.42
257	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant	12/2007	03/2010	10/2010	952.88	952.88	0.00
258	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	01/2009	06/2009	02/2011	149.15	158.72	75.31
	Urban Development						
259	BANGALORE METRO RAIL PROJECT	05/2006	12/2011	03/2013	6395.00	11609.00	2267.57
260	DELHI MRTS PHASE-II PROJECT	08/2005	06/2010	06/2011	8676.00	18894.36	18127.83
261	PAGLADIYA DAM PROJECT	01/2001	12/2007	12/2012	542.90	1187.00	35.49

List of Projects Without Milestones

(Jul,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Civil Aviation</u>									
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 2,015.00	2,015.00	881.21	01/2011 -	12/2011	11(O)	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	1,282.55	05/2011 -	03/2012	10(O)	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	39.57	05/2012 -	05/2012	0(O)	0/0
4	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40 -	264.29	141.91	01/2011 -	06/2012	17(O)	0/0
5	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	323.65	06/2013 -	06/2013	0(O)	0/0
	Total		4,123.24 -	4,820.13	2,668.89				0/0
<u>Coal</u>									
6	KARMA OCP - [N06000088]JCL,Jharkhandd	06/2009	162.46 -	162.46	27.33	03/2014 -	03/2014	0(O)	0/0
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 -	1,131.28	-	03/2018 -	03/2018	0(O)	0/0
8	KHADIA EXPANSION OPENCAST PROJECT - [N06000092]NCL,Uttar Pradesh	06/2011	1,131.28 -	1,131.28	-	03/2018 -	03/2018	0(O)	0/0
	Total		2,425.02 -	2,425.02	27.33				0/0
<u>Fertilisers</u>									
9	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	84.31	07/2011 -	11/2011	4(O)	0/0
10	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	105.79	07/2011 -	03/2012	8(O)	0/0
	Total		763.00 -	763.00	190.10				0/0
<u>Steel</u>									
11	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	6,133.00 -	11,812.00	1,253.17	02/2011 -	03/2013	25(O)	0/0
12	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
13	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		7,603.55 -	13,282.55	1,253.17				0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Petroleum									
14	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	519.93	03/2011 05/2011	06/2011	1(R3)	0/0
15	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
16	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
17	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	229.13	12/2010 08/2011	08/2011	0(R3)	0/0
18	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60 -	261.75	227.94	12/2009 -	09/2011	21(O)	0/0
19	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
20	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	245.01	12/2010 07/2011	09/2011	2(R3)	0/0
21	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
22	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
23	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	696.82	12/2011 -	12/2011	0(O)	0/0
24	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	190.04	03/2013 03/2013	12/2011	-15(R1)	0/0
25	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	618.58	04/2010 -	12/2011	20(O)	0/0
26	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	245.78	04/2011 -	12/2011	8(O)	0/0
27	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	-	09/2011 -	12/2011	3(O)	0/0
28	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	169.06	09/2012 -	12/2011	-9(O)	0/0
29	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	6,378.01	01/2012 -	01/2012	0(O)	0/0
30	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	02/2012	35(O)	0/0
31	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
32	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
33	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
34	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,310.99	05/2010 05/2012	05/2012	0(R3)	0/0
35	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,094.03	09/2010 03/2012	05/2012	2(R3)	0/0
36	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	19.28	05/2010 04/2012	05/2012	1(R3)	0/0
37	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	81.57	07/2010 05/2012	05/2012	0(R3)	0/0
38	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,354.04	08/2010 03/2012	06/2012	3(R3)	0/0
39	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	485.72	06/2012 -	06/2012	0(O)	0/0
40	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
41	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	58.95	04/2011 -	07/2012	15(O)	0/0
42	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	354.31	07/2012 -	07/2012	0(O)	0/0
43	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	105.00	08/2012 -	08/2012	0(O)	0/0
44	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,249.00	09/2012 -	09/2012	0(O)	0/0
45	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	15.78	09/2012 -	09/2012	0(O)	0/0
46	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	64.67	12/2011 -	01/2013	13(O)	0/0
47	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	01/2013 -	01/2013	0(O)	0/0
48	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,709.86	05/2010 03/2013	03/2013	0(R3)	0/0
49	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	359.45	03/2013 -	03/2013	0(O)	0/0
50	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
51	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
52	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]OCL,Maharashtra	12/2009	1,584.00	1,584.00	2.33	-	08/2013	-	0/0
54	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	331.20	-	08/2013	08/2013	0(O)	0/0
55	Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	9.71	02/2014	12/2013	-2(O)	0/0
56	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
57	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	167.70	02/2014	02/2014	0(O)	0/0
58	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
59	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
60	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
61	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
62	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	2,730.00	696.82	09/2011 03/2012	03/2012	0(R3)	0/0
63	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	1.63	03/2012	-	-	0/0
Total			100,278.92	110,392.86	35,579.27				0/0
Power									
64	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.72	09/2010	08/2011	11(O)	0/0
65	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	111.27	06/2011	08/2011	2(O)	0/0
66	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	211.19	05/2011 05/2011	09/2011	4(R3)	0/0
67	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.79	06/2010	09/2011	15(O)	0/0
68	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,639.93	08/2010	10/2011	14(O)	0/0
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	52.66	11/2011	11/2011	0(O)	0/0
70	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,500.13	11/2009	12/2011	25(O)	0/0
71	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	292.95	07/2011	12/2011	5(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
72	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96 -	664.96	304.39	02/2012 -	02/2012	0(O)	0/0
73	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	35.25	02/2012 -	02/2012	0(O)	0/0
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	144.29	08/2011 -	02/2012	6(O)	0/0
75	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	205.53	07/2010 02/2012	02/2012	0(R3)	0/0
76	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	69.47	07/2011 -	02/2012	7(O)	0/0
77	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52 -	2,304.52	1,515.05	10/2010 -	03/2012	17(O)	0/0
78	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	70.81	04/2012 -	04/2012	0(O)	0/0
79	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	314.22	06/2012 -	06/2012	0(O)	0/0
80	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	215.86	108.33	06/2012 -	06/2012	0(O)	0/0
81	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	9.05	06/2012 -	06/2012	0(O)	0/0
82	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,650.16	08/2012 -	08/2012	0(O)	0/0
83	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	3,791.31	08/2012 -	08/2012	0(O)	0/0
84	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	315.35	08/2012 -	08/2012	0(O)	0/0
85	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	1,871.81	10/2012 -	10/2012	0(O)	0/0
86	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	469.38	156.20	10/2012 -	10/2012	0(O)	0/0
87	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	11.32	10/2012 -	10/2012	0(O)	0/0
88	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	651.69	08/2010 -	11/2012	27(O)	0/0
89	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	296.64	11/2012 -	11/2012	0(O)	0/0
90	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	236.41	11/2012 -	11/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	86.27	11/2012 -	11/2012	0(O)	0/0
92	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	989.23	09/2009 -	12/2012	39(O)	0/0
93	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	2,469.21	12/2012 -	12/2012	0(O)	0/0
94	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	287.17	12/2012 -	12/2012	0(O)	0/0
95	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	25.54	01/2013 -	01/2013	0(O)	0/0
96	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	18.23	01/2013 -	01/2013	0(O)	0/0
97	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	339.93	09/2010 -	03/2013	30(O)	0/0
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	254.83	11/2011 -	03/2013	16(O)	0/0
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	242.11	11/2011 -	03/2013	16(O)	0/0
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	128.43	02/2012 -	03/2013	13(O)	0/0
101	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	812.27	02/2012 -	03/2013	13(O)	0/0
102	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	244.42	05/2012 -	03/2013	10(O)	0/0
103	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	119.72	03/2013 -	03/2013	0(O)	0/0
104	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	76.35	04/2013 -	04/2013	0(O)	0/0
105	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	8.71	04/2013 -	04/2013	0(O)	0/0
106	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	80.58	01/2012 -	07/2013	18(O)	0/0
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	37.78	07/2013 -	07/2013	0(O)	0/0
108	TRANSMISSION SYSTEM OF ESTABLISHMENT OF 400/220KV - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
109	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	60.02	08/2013	08/2013	0(O)	0/0
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	15.15	08/2013	08/2013	0(O)	0/0
111	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	125.65	08/2013	08/2013	0(O)	0/0
112	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	126.43	11/2011	09/2013	22(O)	0/0
113	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	57.32	11/2013	11/2013	0(O)	0/0
114	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	210.01	12/2013	12/2013	0(O)	0/0
115	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	-	03/2014	03/2014	0(O)	0/0
116	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	2,755.04	08/2013	09/2014	13(O)	0/0
117	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
118	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	801.63	07/2014	01/2016	18(O)	0/0
	Total		82,759.94	84,354.52	26,233.95				0/0
	Railways								
119	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53	202.69	-	03/1996	03/2008	-15(R1)	0/0
120	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	-	03/2011	03/2011	0(O)	0/0
121	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	550.00	-	-	03/2012	-	0/0
122	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	-	-	03/2013	36(R1)	0/0
123	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	-	-	07/2011	-	0/0
124	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	-	03/2008	10/2010	19(R1)	0/0
125	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	232.29	-	12/2010	22(R1)	0/0
126	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41	211.90	186.55	-	12/2010	21(R1)	0/0
127	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	151.94	12/2007	12/2010	9(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	290.88	03/2009 12/2008	12/2010	24(R1)	0/0
129	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	251.88	- -	12/2010	-	0/0
130	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	-	- 03/2009	03/2011	24(R1)	0/0
131	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	257.15	03/2009 12/2009	03/2011	15(R1)	0/0
132	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	154.13	- -	08/2011	-	0/0
133	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.99	03/2002 -	09/2011	114(O)	0/0
134	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	158.67	02/2010 -	11/2011	21(O)	0/0
135	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	553.70	03/1994 -	12/2011	213(O)	0/0
136	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	466.70	02/2009 -	12/2011	34(O)	0/0
137	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	197.09	- 09/2009	12/2011	27(R1)	0/0
138	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	76.41	- -	12/2011	-	0/0
139	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	218.31	03/2013 -	12/2011	-15(O)	0/0
140	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,139.38	- -	02/2012	-	0/0
141	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	402.11	- 12/2009	02/2012	26(R1)	0/0
142	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	61.97	12/2011 -	02/2012	2(O)	0/0
143	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	542.24	03/1995 -	03/2012	204(O)	0/0
144	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	497.96	- -	03/2012	-	0/0
145	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	437.13	- 12/2011	03/2012	3(R3)	0/0
146	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	202.08	- 03/2012	03/2012	0(R3)	0/0
147	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	418.31	- -	03/2012	-	0/0
148	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.53	- -	03/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
149	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	334.14	- 03/2011	03/2012	12(R3)	0/0
150	HARNOUT -SET,UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	183.09	- -	03/2012	-	0/0
151	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	883.35	- -	03/2012	-	0/0
152	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	-	03/2010 -	03/2012	24(O)	0/0
153	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	174.33	- -	03/2012	-	0/0
154	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	134.93	03/2012 -	03/2012	0(O)	0/0
155	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	217.12	03/2011 -	03/2012	12(O)	0/0
156	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	376.53	06/2005 07/2011	03/2012	8(R3)	0/0
157	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	784.01	03/2011 -	03/2012	12(O)	0/0
158	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	44.35	03/2012 -	03/2012	0(O)	0/0
159	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	142.00	03/2007 03/2007	06/2012	63(R1)	0/0
160	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	320.95	- 07/2012	07/2012	0(R3)	0/0
161	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	570.01	- -	12/2012	-	0/0
162	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	761.65	12/2012 -	12/2012	0(O)	0/0
163	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	385.44	03/2005 12/2008	12/2012	48(R1)	0/0
164	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	261.90	- 03/2012	12/2012	9(R3)	0/0
165	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	233.17	- -	12/2012	-	0/0
166	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	526.28	03/2009 -	12/2012	45(O)	0/0
167	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	949.38	10/2007 -	12/2012	62(O)	0/0
168	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	-	03/2010 -	12/2012	33(O)	0/0
169	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	102.82	12/2012 -	12/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
170	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	147.14	- -	03/2013	-	0/0
171	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	-	- -	03/2013	-	0/0
172	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	41.02	03/2012 -	03/2013	12(O)	0/0
173	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.13	-	03/2013 -	03/2013	0(O)	0/0
174	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]M RTP,Tamil Nadu	04/2006	495.74 495.74	495.74	121.20	- 06/2013	06/2013	0(R3)	0/0
175	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	57.75	12/2011 -	11/2013	23(O)	0/0
176	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0
177	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	82.70	12/2012 -	12/2013	12(O)	0/0
178	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,712.15	03/2009 -	12/2013	57(O)	0/0
179	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,208.23	04/2008 03/2014	03/2014	0(R3)	0/0
180	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	740.96	12/2008 -	03/2014	63(O)	0/0
181	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	654.95	- -	03/2014	-	0/0
182	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	186.25	03/2014 -	03/2014	0(O)	0/0
183	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	3.55	04/2014 -	03/2014	-1(O)	0/0
184	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	6.29	03/2014 -	03/2014	0(O)	0/0
185	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	48.14	03/2014 -	03/2014	0(O)	0/0
186	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	-	03/2014 -	03/2014	0(O)	0/0
187	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	163.35	- -	03/2015	-	0/0
188	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]M RTP,Maharashtra	04/2008	5,300.00 -	5,300.00	277.24	03/2014 -	03/2015	12(O)	0/0
189	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	03/2015	-9(O)	0/0
190	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
191	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
192	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	449.44	03/2011 03/2014	03/2016	24(R3)	0/0
193	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.21	03/2014 -	03/2016	24(O)	0/0
194	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	1.42	03/2016 -	03/2016	0(O)	0/0
195	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	23.10	03/2016 -	03/2016	0(O)	0/0
196	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	-	03/2016 -	06/2016	3(O)	0/0
197	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
198	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.28	- -	-	-	0/0
199	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
200	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	94.54	- -	-	-	0/0
201	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	464.70	- -	-	-	0/0
202	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
203	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	945.73	572.91	- -	-	-	0/0
204	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	64.46	- -	-	-	0/0
205	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	85.68	- -	-	-	0/0
206	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
207	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,046.57	07/2005 -	-	-	0/0
208	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	554.55	378.41	- 05/2009	-	-	0/0
209	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	84.76	- -	-	-	0/0
210	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	808.81	06/2007 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
211	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	300.19	04/2003 03/2010	-	-	0/0
212	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	-	-	-	-	0/0
213	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	695.00	9.44	-	-	-	0/0
214	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	301.92	- 12/2012	-	-	0/0
215	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
216	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91	418.17	73.49	-	-	-	0/0
217	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	209.49	-	-	-	0/0
218	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	173.49	171.52	03/1998 08/2005	-	-	0/0
219	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	25.01	02/2015	-	-	0/0
220	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	-	-	-	0/0
221	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92	261.70	18.10	02/2006	-	-	0/0
222	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	303.08	03/2008 06/2008	-	-	0/0
223	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	-	-	-	-	0/0
224	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	396.44	-	-	-	0/0
225	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	-	-	-	-	0/0
226	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	-	-	-	-	0/0
227	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	35.45	-	-	-	0/0
228	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
229	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	-	03/2011	-	-	0/0
230	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	444.63	06/1999 03/2011	-	-	0/0
231	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	165.49	03/2004	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
232	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	548.49	- 11/2010	-	-	0/0
233	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	323.24	- 03/2011	-	-	0/0
234	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	263.34	06/2004 04/2005	-	-	0/0
235	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	499.50	05/2008 03/2011	-	-	0/0
236	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	243.20	12/2009 03/2011	-	-	0/0
237	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	718.90	- 12/2010	-	-	0/0
238	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	383.68	- -	-	-	0/0
239	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,058.65	12/2006 08/2010	-	-	0/0
240	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	227.75	- 02/2011	-	-	0/0
241	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	460.27	02/2010 02/2011	-	-	0/0
242	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	364.24	- -	-	-	0/0
243	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	233.72	- 03/2011	-	-	0/0
244	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	117.60	- -	-	-	0/0
245	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	130.85	- -	-	-	0/0
246	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	358.41	- 03/2011	-	-	0/0
247	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.42	- -	-	-	0/0
248	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	154.42	12/2010 03/2011	-	-	0/0
249	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	128.39	- 12/2010	-	-	0/0
250	Bhuj-Naliya(GC) with extension from naliyate vayar - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.41	03/2012 -	03/2012	0(O)	0/0
	Total		62,299.03 -	117,275.75					0/0
Road Transport & Highways									
251	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	436.30	11/2007 -	08/2011	45(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
252	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00	217.00	351.20	10/2008	08/2011	34(O)	0/0
253	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00	359.00	870.60	03/2009	08/2011	29(O)	0/0
254	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	910.00	11/2010	08/2011	9(O)	0/0
255	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	295.20	09/2009	08/2011	23(O)	0/0
256	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	657.60	07/2010	08/2011	13(O)	0/0
257	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	359.00	07/2010	08/2011	13(O)	0/0
258	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	165.14	02/2004	08/2011	90(O)	0/0
259	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,478.00	08/2011	08/2011	0(O)	0/0
260	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00	196.65	147.83	08/2004	09/2011	85(O)	0/0
261	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	157.70	08/2004	09/2011	85(O)	0/0
262	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.60	03/2005	09/2011	78(O)	0/0
263	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00	193.00	338.70	10/2008	09/2011	35(O)	0/0
264	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	179.10	03/2008	09/2011	42(O)	0/0
265	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	147.70	03/2008	09/2011	42(O)	0/0
266	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	253.50	10/2008	09/2011	35(O)	0/0
267	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	557.10	06/2008	09/2011	39(O)	0/0
268	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50	312.50	598.90	03/2009	09/2011	30(O)	0/0
269	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	236.50	11/2008	09/2011	34(O)	0/0
270	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	876.70	07/2010	09/2011	14(O)	0/0
271	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	75.70	04/2004	10/2011	90(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
272	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.60	01/2009	10/2011	33(O)	0/0
273	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	251.80	06/2008	10/2011	40(O)	0/0
274	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	385.30	12/2008	10/2011	34(O)	0/0
275	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	10/2011	9(O)	0/0
276	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	194.70	10/2011	10/2011	0(O)	0/0
277	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	277.00	10/2008	11/2011	37(O)	0/0
278	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30	151.30	171.70	10/2008	11/2011	37(O)	0/0
279	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	2,569.00	11/2011	11/2011	0(O)	0/0
280	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
281	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	293.80	09/2007	12/2011	51(O)	0/0
282	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	231.10	09/2007	12/2011	51(O)	0/0
283	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	85.40	09/2008	12/2011	39(O)	0/0
284	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	203.00	06/2005	12/2011	78(O)	0/0
285	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	257.20	10/2008	12/2011	38(O)	0/0
286	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	227.00	394.10	10/2008	12/2011	38(O)	0/0
287	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	347.80	03/2008	12/2011	45(O)	0/0
288	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	223.50	02/2009	12/2011	34(O)	0/0
289	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00	200.00	77.24	04/2009	12/2011	32(O)	0/0
290	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00	195.00	169.50	06/2008	12/2011	42(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
291	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	242.00	393.20	12/2008 -	12/2011	36(O)	0/0
292	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	363.20	12/2008 -	12/2011	36(O)	0/0
293	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	196.00	06/2008 -	12/2011	42(O)	0/0
294	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	261.50	09/2008 -	12/2011	39(O)	0/0
295	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	198.00	186.10	11/2008 -	12/2011	37(O)	0/0
296	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	275.70	10/2008 -	12/2011	38(O)	0/0
297	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	217.40	10/2008 -	12/2011	38(O)	0/0
298	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	420.30	09/2008 -	12/2011	39(O)	0/0
299	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	254.20	06/2008 -	12/2011	42(O)	0/0
300	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00 -	322.00	553.70	06/2009 -	12/2011	30(O)	0/0
301	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	232.40	06/2008 -	12/2011	42(O)	0/0
302	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	242.00	06/2008 -	12/2011	42(O)	0/0
303	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	468.80	03/2008 -	12/2011	45(O)	0/0
304	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	161.30	06/2008 -	12/2011	42(O)	0/0
305	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	204.90	04/2008 -	12/2011	44(O)	0/0
306	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	118.60	05/2008 -	12/2011	43(O)	0/0
307	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	186.90	06/2008 -	12/2011	42(O)	0/0
308	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	580.30	06/2009 -	12/2011	30(O)	0/0
309	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	692.70	10/2009 -	12/2011	26(O)	0/0
310	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04 -	418.04	313.40	03/2010 -	12/2011	21(O)	0/0
311	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	294.60	09/2009 -	12/2011	27(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
312	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2011	11(O)	0/0
313	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00 -	284.00	336.50	05/2010 -	12/2011	19(O)	0/0
314	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00 -	295.00	624.30	08/2010 -	12/2011	16(O)	0/0
315	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	523.50	05/2010 -	12/2011	19(O)	0/0
316	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	594.20	07/2010 -	01/2012	18(O)	0/0
317	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	375.10	02/2012 -	02/2012	0(O)	0/0
318	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	176.00	09/2007 -	03/2012	54(O)	0/0
319	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	206.80	10/2008 -	03/2012	41(O)	0/0
320	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	115.70	04/2008 -	03/2012	47(O)	0/0
321	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	175.60	04/2008 -	03/2012	47(O)	0/0
322	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	138.30	04/2010 -	03/2012	23(O)	0/0
323	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	178.60	02/2010 -	03/2012	25(O)	0/0
324	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27(O)	0/0
325	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,205.00	05/2012 -	05/2012	0(O)	0/0
326	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	804.30	05/2012 -	05/2012	0(O)	0/0
327	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	388.00	328.60	05/2012 -	05/2012	0(O)	0/0
328	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	165.50	10/2008 -	06/2012	44(O)	0/0
329	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	294.10	10/2009 -	06/2012	32(O)	0/0
330	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	412.20	12/2009 -	06/2012	30(O)	0/0
331	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	157.00	09/2010 -	06/2012	21(O)	0/0
332	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	835.00	396.40	06/2012 -	06/2012	0(O)	0/0
333	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	1,519.00	10/2011 -	06/2012	8(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
334	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	315.90	07/2012	07/2012	0(O)	0/0
335	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	115.60	05/2008	08/2012	51(O)	0/0
336	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	506.30	10/2011	08/2012	10(O)	0/0
337	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	183.70	06/2010	10/2012	28(O)	0/0
338	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.30	09/2009	10/2012	37(O)	0/0
339	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
340	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	813.80	09/2012	10/2012	1(O)	0/0
341	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	937.90	10/2012	10/2012	0(O)	0/0
342	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
343	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
344	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	175.60	07/2008	12/2012	53(O)	0/0
345	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	247.90	02/2004	12/2012	106(O)	0/0
346	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	374.70	12/2012	12/2012	0(O)	0/0
347	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0
348	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	831.50	09/2010	03/2013	30(O)	0/0
349	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
350	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	267.80	03/2013	03/2013	0(O)	0/0
351	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
352	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
353	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
354	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	180.80	05/2013	05/2013	0(O)	0/0
355	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	105.10	05/2013	05/2013	0(O)	0/0
356	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
357	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	111.20	09/2007	06/2013	69(O)	0/0
358	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	822.60	11/2012	06/2013	7(O)	0/0
359	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
360	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0
361	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	29.60	04/2009	07/2013	51(O)	0/0
362	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
363	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	65.94	07/2013	07/2013	0(O)	0/0
364	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
365	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
366	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	0.99	09/2013	09/2013	0(O)	0/0
367	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
368	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
369	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
370	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	212.00	40.29	09/2007	12/2013	75(O)	0/0
371	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	196.00	27.94	07/2009	12/2013	53(O)	0/0
372	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
373	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	300.10	10/2014	10/2014	0(O)	0/0
	Total		60,277.85	61,741.26	44,168.09				0/0

Shipping & Ports

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
374	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -	298.17	293.57	04/2009 -	02/2011	22(O)	0/0
375	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	272.50	219.00	12/2010 -	06/2011	6(O)	0/0
376	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
377	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	241.50	48.10	09/2011 -	09/2011	0(O)	0/0
378	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	117.28	12/2005 01/2008	10/2011	45(R3)	0/0
379	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
380	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
381	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	320.74	03/2012 -	03/2012	0(O)	0/0
382	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
383	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
384	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	55.40	12/2011 05/2012	05/2012	0(R3)	0/0
385	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	545.85	12/2010 -	09/2012	21(O)	0/0
386	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
387	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
388	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	83.51	12/2012 -	12/2012	0(O)	0/0
389	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
390	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	-	03/2011 -	03/2013	24(O)	0/0
391	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
392	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
393	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
394	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0
395	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.92	10/2008 -	-	-	0/0
396	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
397	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	-	0/0
398	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
399	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.02	10/2008 -	-	-	0/0
Total			18,451.36 -	19,434.85	3,633.73				0/0
<u>Telecommunications</u>									
400	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	243.30	09/2009 -	02/2010	5(O)	0/0
401	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
402	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	192.48	119.42	03/2009 -	02/2011	23(O)	0/0
403	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	194.39	12/2008 -	02/2011	26(O)	0/0
404	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
405	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	75.31	06/2009 -	02/2011	20(O)	0/0
406	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
407	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	225.42	10/2008 -	02/2011	28(O)	0/0
408	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	02/2011	13(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
409	GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	675.35	01/2010	02/2011	13(O)	0/0
410	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	132.24	01/2010	02/2011	13(O)	0/0
411	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	494.68	12/2008	03/2011	27(O)	0/0
412	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
413	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	106.69	09/2009	03/2011	18(O)	0/0
414	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
415	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	398.08	02/2009	03/2011	25(O)	0/0
416	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	352.89	08/2009	03/2011	19(O)	0/0
417	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	280.72	11/2010	03/2011	4(O)	0/0
418	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	395.08	10/2009	03/2011	17(O)	0/0
419	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0
420	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
421	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
422	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	20.90	10/2010	03/2012	17(O)	0/0
423	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	-	12/2005	-	-	0/0
424	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
425	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	-	02/2008	-	-	0/0
426	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
427	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
428	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0
429	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
430	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	-	-	0/0
431	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	-	-	0/0
432	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	-	-	0/0
433	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	-	-	0/0
434	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
435	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	-	-	0/0
436	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	-	-	0/0
437	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	-	-	0/0
438	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	-	06/2009	-	-	0/0
439	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
Total			19,265.79	19,550.68	5,053.14				0/0
<u>Urban Development</u>									
440	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
Total			114.18	173.08	.00				0/0
<u>Water Resources</u>									
441	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
Total			542.90	1,187.00	35.49				0/0
Grand Total			358,904.78	435,400.70					0/0

List of Projects in which Expenditure is more than cost

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	13940.00
2	BINA EXTN. PROJ	Coal	NCL	168.97	0.00	183.63
3	BARSINGSAR TPS (2X125MW) (NLC)	Coal	NLC	1114.18	1626.09	1628.27
4	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	HPCL	613.54	0.00	671.52
5	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	Petroleum	ONGC	2305.30	700.00	2416.96
6	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	Power	NHPC	621.28	0.00	664.47
7	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.02	0.00	651.69
8	CHAMERA,STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1639.93
9	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1334.24
10	KOTESHWAR HEP(THDC)	Power	THDCL	1301.56	0.00	2466.65
11	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	SER	293.97	0.00	376.53
12	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	2712.15
13	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	217.12
14	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	FOIS	520.00	422.79	542.24
15	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	402.51
16	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	Railways	NWR	643.36	0.00	784.01
17	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	174.33
18	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	170.00	358.41
19	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	RVNL	200.80	0.00	251.88
20	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	396.44
21	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	RVNL	240.00	0.00	257.15
22	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	283.95	334.14
23	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	RVNL	136.62	0.00	151.94
24	RUPSA-BANGRIPOSI (GC)(SER)	Railways	SER	57.94	0.00	171.52
25	PATNA GANGA BRIDGE (NL), ECR	Railways	ECR	624.47	0.00	949.38
26	RAJATGARH-BARANG(LD),ECOR	Railways	RVNL	166.16	0.00	232.29
27	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	261.90
28	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	460.27
29	BANKURA - DAMODAR (GC) (SER)	Railways	SER	111.90	0.00	385.44
30	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	108.91	227.75
31	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	M RTP	907.69	1032.76	3058.65
32	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	740.96
33	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	300.19
34	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	808.81

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMUL ATIVE EXPENDI TURE
35	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	Railways	ECR	78.23	0.00	84.76
36	GULBARGA-BIDAR,SCR(NL)	Railways	SCR	242.42	369.70	378.41
37	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	718.90
38	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	243.20
39	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	761.65
40	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	335.77	526.53
41	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	263.34
42	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	281.20	323.24
43	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2208.23
44	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1139.38
45	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	ECR	100.00	322.29	418.31
46	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	164.36	466.70
47	KARUR-SALEM(NL),SR	Railways	SR	155.55	0.00	572.91
48	GONDIA-JABALPUR(GC),(SECR)	Railways	SECR	386.30	0.00	524.23
49	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	Railways	NWR	262.00	456.00	548.49
50	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR	Railways	SWR	295.00	0.00	464.70
51	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	ER	184.00	254.07	437.13
52	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.90	181.99
53	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	444.63
54	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	407.78	497.96
55	GUNA-ETAWAH(NCR), NL	Railways	NCR	158.77	432.46	553.70
56	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	666.00
57	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2478.00
58	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	176.00
59	Bijapur-Hungund Section	Road Transport & Highways	NHAI	748.00	0.00	831.50
60	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	822.60
61	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	804.30

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
62	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	2569.00
63	Pune-sholapur, pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1205.00
64	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	NHAI	229.00	0.00	336.50
65	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.90
66	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	236.50
67	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	468.80
68	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	254.20
69	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	420.30
70	RINGBUNDS TO JHAJHANPUR (BR-6)	Road Transport & Highways	NHAI	340.00	0.00	557.10
71	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	275.70
72	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	206.80
73	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	171.70
74	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	253.50

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMUL ATIVE EXPENDI TURE
75	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	277.00
76	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	363.20
77	KASIA TO GORAKHPUR (NH-28)(NHAI)	Road Transport & Highways	NHAI	242.00	0.00	393.20
78	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	251.80
79	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	227.60
80	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	347.80
81	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	Road Transport & Highways	NHAI	227.00	0.00	394.10
82	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE- II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	257.20
83	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	Road Transport & Highways	NHAI	217.00	0.00	351.20
84	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	Road Transport & Highways	NHAI	193.00	0.00	338.70
85	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	NHAI	412.78	0.00	436.30
86	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	231.10
87	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	293.80

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMUL ATIVE EXPENDI TURE
88	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
89	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	523.50
90	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	NHAI	295.00	0.00	624.30
91	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH- 48 TO DEVIHALLI	Road Transport & Highways	NHAI	441.00	0.00	876.70
92	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
93	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	594.20
94	PONDICHERY - TINDIVANAU NH-66	Road Transport & Highways	NHAI	285.00	0.00	359.00
95	TRICHY - DINDIGUAL NH-45	Road Transport & Highways	NHAI	576.00	0.00	657.60
96	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	580.30
97	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	385.30
98	THRISSUR TO ANGAMALI (NH-47)	Road Transport & Highways	NHAI	312.50	0.00	598.90
99	SITAPUR-LUCKNOW	Road Transport & Highways	NHAI	322.00	0.00	553.70
100	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	Road Transport & Highways	NHAI	629.00	0.00	910.00

SN	PROJ_TITLE	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
101	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	Road Transport & Highways	NHAI	359.00	0.00	870.60
102	JHANSI TO LALITPUR, NH-26	Road Transport & Highways	NHAI	276.09	0.00	295.20
103	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	NHAI	600.24	0.00	692.70
104	NEW MANGALORE PORT NH-17 AND 48	Road Transport & Highways	NHAI	196.50	0.00	232.40
105	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	NHAI	273.00	0.00	475.60
106	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	0.00	293.57
107	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	Telecommunications	BSNL	760.20	0.00	812.08
108	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	Telecommunications	BSNL	277.34	0.00	308.13
109	DELHI MRTS PHASE-II PROJECT	Urban Development	DMRC	8676.00	8605.36	18127.83

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
