

**319th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
June, 2012**



ASSAM GAS CRACKER PROJECTS (ASSAM)



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	6-9
Summary of Projects	9-23
Trend and Graphical Analysis of Mega Projects	24-36
Sector wise analysis of projects	37-37
List of All Ongoing Projects	38-68
Sector wise Graph	69-80
ANNEXURE	81-81
Central Sector Projects	82-82
List of Projects Having Expenditure More than cost	83-86
List of Projects Ahead of Schedule	87-87
List of Projects with out Original date of Commissioning	88-92
List of Projects with out date of Commissioning	93-97
List of On schedule Projects	98-103
List of Delayed Projects w.r.t Original and Revised	104-123
List of Projects without Milestones	124-142
Abbreviations	143-145

EXECUTIVE SUMMARY

The Flash Report for June, 2012 contains information on the status of the 555 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During, June, 2012, 8 projects (3 projects of Power, 2 projects each of Road Transport & Highways and Railway and one project of Steel Sector) have reported completion.

During the reference month, out of 555 projects 275 projects are delayed and 51 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 39 months, in respect of projects relating to Road Transport and Highways, Railways, Power, Petroleum, Coal, Shipping & Ports, Steel and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects	Additionally delayed during the month under report
1.	RAILWAYS	127	41	10
2.	ROAD TRANSPORT & HIGHWAYS	144	82	8
3.	POWER	96	51	10
4.	PETROLEUM	65	39	8
5.	COAL	52	27	2
6.	TELECOMMUNICATION	15	9	7
7.	SHIPPING & PORTS	19	10	2
8.	STEEL	16	7	4
9.	FERTILISERS	5	1	0
10.	CIVIL AVIATION	5	3	0
11.	ATOMIC ENERGY	5	3	0
12.	URBAN DEVELOPMENT	4	1	0
13.	WATER RESOURCES	1	1	0
14.	PETROCHEMICALS	1	0	0
Total		555	275	51

3. The total original cost of implementation of the 555 projects was about ₹ 7,23,971.96 Crores and their anticipated completion cost is likely to be ₹ 8, 67,266.90 Crores, which reflects an overall cost overrun of ₹ 1,43,294.94 Crores (19.8 % of original cost). The expenditure incurred on these projects till June, 2012 is ₹ 3,91,541.42 Crores, which is 45.1 % of the anticipated cost of the projects.

4. Out of the 555 projects, 4 projects are ahead of schedule, 160 are on schedule, 275 projects are delayed, and 36 projects have been sanctioned without any commissioning schedule/date. Further, in case of 80 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. Out of 275 delayed projects, 83 projects had overall delay in the range of 1 to 12 months, 50 projects had a delay in the range of 13 to 24 months, 105 projects had a delay in the range of 25 to 60 months and 37 projects had a delay of 61 months and above.

5. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

6. The brief reasons for time overruns as reported by various projects implementing agencies are law & order problem, delay in land acquisitions, revision in scope of work, delay in supply of equipment & non-development of modern equipment, ROU/ROW problem, delay in municipal permission, fund constraint, delay in start of project, delay in equipment erection and forest and environment clearances, etc

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedule for many projects, which suggest that time/cost overrun figures are underreported.

8. The Sector-wise details of delays/additional delays are as under:-

i) In the **Shipping and Ports sector**, out of 19 projects, 10 projects are delayed. During the month 2 projects have reported additional delays in the range of 1-3 months. The project 'Setting up of LNG Regasification Terminal at Puthu, Port Trust' and 'Construction & Development of 2 offshore Container Berths & Terminal, Mumbai Port' have reported additional delay of 1 and 3 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

ii) In the **Telecommunications sector**, out of 15 projects, 9 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-5 months. Two projects have reported additional delays of one month each. The project 'GSM Equipment of 390 K Lines (2G) and 130 K Lines (3G), BSNL' and 'GSM Equipment of 283000 Lines (2G) and 75000 lines, BSNL' have reported additional delay of 3 months each due to delay in municipal permission, 'Assam Telecom Circle, Phase-V.I 2G & 3G, BSNL' and 'GSM Equipment of 1625000 Lines (2G) 325000 Lines 3, BSNL' have reported additional delay 3 months each due to delay in non-availability of suitable sites and delay in permission from local bodies regarding to lay optical fibers respectively. The project 'ERP Implementation in BSNL on Turnkey basis, BSNL' has reported additional delay of 5 months due to delay in change of business process.

iii) In the **Petroleum Sector**, out of 65 projects, 39 projects are delayed. During the month 8 projects have reported additional delays in the range of 1-12 months. Three projects have reported additional delays of 2 months each. The project 'Upgradation of Konaban GGS and Pipeline Grid Project, ONGC' has reported additional delay of 4 months due to ROU issues, 'Development of SB-14 field, ONGC' has reported additional delay of 5 months due to clubbing of tendering process with WO-16 cluster development project, 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' has reported additional delay of 8 months due to delay in shortage of skilled manpower, 'Development of B-46 Cluster Field, ONGC' has reported additional delay of 10 months due to delay in completion of the linked project and 'Development of Cluster-7 Fields, ONGC' has reported additional delay of 12 months due to delay in award of work for installation of four well platform associated pipelines under two packages.

iv) In the **Power Sector**, out of 96 projects, 51 projects are delayed. During the month 10 projects have reported additional delays in the range of 1-4 months. Two projects have reported additional delays of one month each, three projects have reported additional delay of 2 months each and three projects have reported additional delay of 3 months each.. The project ‘System Strengthening in NR for Sasan & Mundra (UMPP), PGCIL’ and ‘Northern Region System Strengthening Scheme- XXI, PGCIL’ have reported additional delay of 4 months each due to change of ownership of executing agency and delay in acquisition of land for bareilly substation respectively.

v) In **Steel sector**, out of 16 projects, 7 projects are delayed. During the month 4 projects have reported additional delays in the range of 2-4 months. The project ‘330 TPH Boiler-6 and Auxiliary System, RINL’ has reported additional delay of 2 months due to delay in erection activities, ‘Expansion of Bhilai Steel Plant, SAIL’ and ‘Expansion of Durgapur Steel Plant, SAIL’ have reported additional delay of 3 months each due to lack of skilled manpower & non-development of modern equipment and change of scope of works respectively. The project ‘Enhancement of Production Capacity at bolani I/O Mines, SAIL’ has reported of additional delay of 4 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vi) In the **Road Transport and Highways Sector**, out of 144 projects, 82 projects are delayed. During the month 8 projects of NHAI have reported additional delays in the range of 1-10 months. Two projects have reported additional delays of one and two months respectively, two projects have reported additional delay of 3 months each, one projects has reported additional delay of 5 months. The project ‘Aurang-Raipur, NH-6, Km.232 to Km.281, NHAI’ and ‘Gurgaon-Kotputli Km 42.70 to 54.4 Km, NHAI’ have reported additional delay of 6 months each and ‘4 Lanning of Belgum-Khanpur Section and 2 Laning of Khanpur-KNT/Goa Border, NHAI’ has reported additional delay of 10 months. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

vii) In the **Coal Sector**, out of 52 projects, 27 projects are delayed. During the month 2 projects have reported additional delays in the range of 12-24 months. The project 'Penganga OC, WCL' has reported additional delay of 12 months due to agitation by locals as the villagers are demanding the rehabilitation site of their choice and 'Kartali (EAST) OCP (2.50 MTY), SECL' has reported additional delay of 24 months due to delay in start of project

viii) In the **Railways Sector**, out of 127 projects, 41 projects are delayed. During the month 10 projects have been reported additional delays in the range of 1-39 months. One project has additional delay of 1 month and two projects have additional delay of 2 months each. The project 'Gadwal - Raichur (NL), SCR' has reported additional delay of 11 months due to fund constraints, 'Lanjigarh-Junagarh NL, ECOR' and 'Khurda Road-Bolangir NL, ECOR' have reported additional delay of 12 months each due to fund constraints, 'Howrah-Amta-Champadanga NL, SER' has reported additional delay of 12 months due to law & order problem 'Belapur-Seawood-Uran Electrified Double Line, MRTP has reported additional delay of 39 months due to delay in land acquisition. The project 'Bankura - Damodar (GC), SER' and 'Mandarhill-Dumka-Rampurhat (NL), ER' have reported additional delay of 6 and 12 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects. Regarding 74 projects of Railways for which either original/anticipated date of commissioning schedule is not available, M/o Railways has clarified that they have huge throwforward of ongoing projects with limited availability of resources, as a result funds are thinly spreaded prolonging period of completion. Targets are therefore, fixed on annual basis depending upon availability of resources and progress achieved on individual projects, therefore by implication fixing of completion dates is difficult to finalize/report.

9. The status as on 01.07.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.

(Pankaj Jain)
Special Secretary
Ministry of Statistics and Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	144	8
2	Railways	127	10
3	Power	96	10
4	Petroleum	65	8
5	Coal	52	2
6	Shipping & Ports	19	2
7	Steel	16	4
8	Telecommunications	15	7
9	Atomic Energy	5	0
10	Civil Aviation	5	0
11	Fertilisers	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	555	51


ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	N.A.
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
<u>Road Transport & Highways</u>				
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
<u>Shipping & Ports</u>				
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
June,2012				
<u>Steel</u>				
19	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
<u>Power</u>				
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	N.A.
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
<u>Railways</u>				
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
<u>Road Transport & Highways</u>				
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9

9


Summary of projects in the Flash Report for the month of June, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	574
Number of Projects completed/dropped/frozen in Previous Month	10
Number of Projects completed/dropped/frozen in Current Month	9
Number of Projects Removed the System in Cur. Month	1
Number of Projects Added in Current Month	1
Number of Projects in Current Month	555


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 555 projects, 4 projects are ahead of schedule, 160 projects are on schedule and 275 projects are delayed. Of the balance, 80 projects do not have fixed dates of commissioning while 36 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

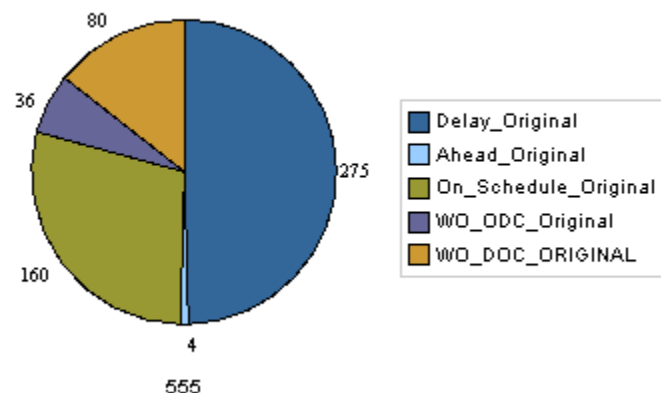

III. Investment Scenario

The Total Original cost of implementation of 555 projects when sanctioned, was of the order of Rs. 723971.96 crore but this was subsequently revised to Rs. 867266.9 crore implying a cost overrun of 19.8%. The expenditure incurred on these projects till June, 2012 is Rs. 391541.42 crore, which is 45.1% of the revised cost of the projects.

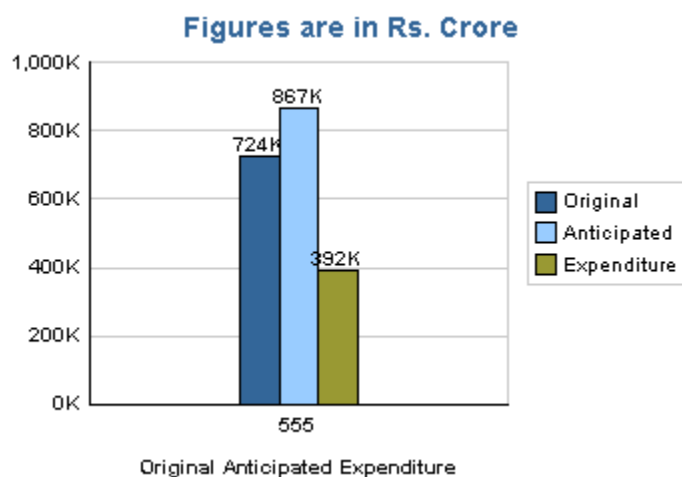

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	574
No of Projects Completed/Dropped/Frozen in Previous Month	10
No of Projects Completed/Dropped/Frozen in Current Month	9
No of Projects Removed the System in Current Month	1
No of Projects added in Current Month	1
No of Projects in Current Month	555

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	275	4	160	36	80	555	49.55
Latest Approved (Date)	255	3	225	45	27	555	45.95

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	435	586,441.56	663,776.77	265,555.07	40.00	77,335.21	13.20
Latest Approved (RCE)	120	191,614.88	203,490.13	125,986.35	61.90	11,875.25	6.20
Total (RCE)	555	778,056.44	867,266.90	391,541.42	45.15	89210.46	11.47
Original Cost of All Projects							
Original Cost	555	723,971.96	867,266.90	391,541.42	45.10	143,294.94	19.80

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	275	392,540.61	476,574.30	269,256.94	56.50	84,033.69	21.40
Latest Approved (RCE)	255	369,223.45	425,276.59	236,080.45	55.50	56,053.14	15.20

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	51	43,917.22	65,304.33	27,525.44	42.10	21,387.11	48.70

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	52	33,950.7	37,570.8	10.7	13	12,914.8	17,132.6	32.7
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	16	50,110.2	71,356.8	42.4	8	32,529.9	53,806.4	65.4
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	65	156,993.5	165,178.0	5.2	16	51,356.4	68,035.0	32.5
8	Power	96	203,091.9	216,802.4	6.8	17	40,935.0	54,645.5	33.5
9	Railways	127	64,610.9	141,720.1	119.3	105	41,996.8	119,152.7	183.7
10	Road Transport & Highways	144	91,164.1	92,882.4	1.9	12	3,520.8	5,808.2	65.0
11	Shipping & Ports	19	16,242.5	17,757.5	9.3	10	8,732.5	10,579.5	21.2
12	Telecommunications	15	6,161.0	6,101.8	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		555	723,972.0	867,266.9	19.8	191	225,978.2	379,425.5	67.9

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Proj- ects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	14	12,420.0	20,714.4	66.8
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	36	22,463.9	33,865.5	50.8	12	10,491.8	21,987.5	109.6
4	Bihar	29	26,796.5	31,471.7	17.4	12	12,238.8	16,914.1	38.2
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	23	31,308.5	31,536.5	0.7	4	2,019.6	2,481.1	22.8
7	Haryana	9	5,306.6	7,177.2	35.2	3	1,448.2	3,318.8	129.2
8	Himachal Pr.	5	13,355.6	15,213.4	13.9	2	6,224.2	8,082.0	29.8
9	J and K	11	15,120.1	34,993.9	131.4	6	7,866.5	27,767.1	253.0
10	Karnataka	23	29,468.6	37,913.5	28.7	10	8,795.3	17,646.7	100.6
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	23	16,561.5	16,856.0	1.8	3	2,027.6	2,741.5	35.2
13	Maharashtra	50	78,266.3	93,478.4	19.4	18	31,818.4	49,505.1	55.6
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,405.4	61,206.5	6.6	13	33,147.5	37,141.0	12.0
19	Punjab	6	4,384.2	5,326.0	21.5	2	532.4	1,474.2	176.9
20	Rajasthan	14	26,544.1	26,138.3	-1.5	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	61,960.8	20.8	14	29,143.5	39,828.4	36.7
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	23	18,321.9	22,159.7	20.9	8	3,498.5	7,384.5	111.1
25	West Bengal	25	40,187.8	52,557.1	30.8	16	23,547.4	35,916.8	52.5
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	26	40,960.3	56,580.2	38.1	11	10,542.6	26,162.6	148.2
28	Jharkhandd	23	11,785.5	16,601.5	40.9	7	5,213.3	10,201.2	95.7
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	35.6
30	Multi State	104	137,462.2	142,739.7	3.8	21	6,624.0	16,429.4	148.0
Total		555	723,972.0	867,266.9	19.8	191	225,978.2	379,425.5	67.9

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	3	2,587.6	2,970.1	3 - 27
3	Coal	52	33,950.7	37,570.8	10.7	27	18,122.5	21,240.1	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	1	438.0	438.0	12 - 12
5	Steel	16	50,110.2	71,356.8	42.4	7	13,020.2	17,104.1	2 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	65	156,993.5	165,178.0	5.2	39	108,597.6	118,456.5	1 - 120
8	Power	96	203,091.9	216,802.4	6.8	51	135,028.3	148,125.8	2 - 99
9	Railways	127	64,610.9	141,720.1	119.3	41	26,157.8	66,046.2	1 - 216
10	Road Transport & Highways	144	91,164.1	92,882.4	1.9	82	33,091.2	35,142.7	2 - 101
11	Shipping & Ports	19	16,242.5	17,757.5	9.3	10	8,446.1	10,038.7	5 - 87
12	Telecommunications	15	6,161.0	6,101.8	-1.0	9	3,163.3	3,167.1	22 - 79
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		555	723,972.0	867,266.9	19.8	275	392,540.6	476,574.3	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	38,459.0	23.9	11	15,386.5	18,889.0	3 - 36
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	25 - 75
3	Assam	36	22,463.9	33,865.5	50.8	31	11,648.4	19,405.4	12 - 120
4	Bihar	29	26,796.5	31,471.7	17.4	14	20,578.4	23,672.8	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	3 - 3
6	Gujarat	23	31,308.5	31,536.5	0.7	6	13,912.3	14,143.8	3 - 24
7	Haryana	9	5,306.6	7,177.2	35.2	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	5	13,355.6	15,213.4	13.9	5	13,355.6	15,213.4	20 - 99
9	J and K	11	15,120.1	34,993.9	131.4	7	9,707.1	29,554.1	10 - 201
10	Karnataka	23	29,468.6	37,913.5	28.7	9	22,364.3	27,444.8	3 - 96
11	Kerala	5	5,469.7	6,911.2	26.4	3	4,674.0	5,324.0	9 - 58
12	Madhya pradesh	23	16,561.5	16,856.0	1.8	16	13,107.5	12,702.0	5 - 50
13	Maharashtra	50	78,266.3	93,478.4	19.4	25	47,453.8	58,653.6	2 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 11
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,405.4	61,206.5	6.6	10	31,575.9	32,538.2	7 - 132
19	Punjab	6	4,384.2	5,326.0	21.5	4	1,611.4	2,553.2	1 - 51
20	Rajasthan	14	26,544.1	26,138.3	-1.5	6	19,992.2	19,687.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	61,960.8	20.8	10	24,621.7	30,552.3	9 - 87
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	4 - 4
24	Uttar Pradesh	23	18,321.9	22,159.7	20.9	12	11,215.4	13,148.4	5 - 91
25	West Bengal	25	40,187.8	52,557.1	30.8	15	12,936.4	17,877.2	3 - 135
26	Delhi	3	37,985.0	37,965.4	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	26	40,960.3	56,580.2	38.1	10	13,138.2	15,255.7	10 - 48
28	Jharkhandd	23	11,785.5	16,601.5	40.9	9	2,442.6	3,602.4	12 - 102
29	Uttaranchal	3	5,619.2	6,559.6	16.7	3	5,619.2	6,559.6	22 - 39
30	Multi State	104	137,462.2	142,739.7	3.8	55	82,335.2	83,590.1	1 - 216
Total		555	723,972.0	867,266.9	19.8	275	392,540.6	476,574.3	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	5	41,548.3	47,832.3	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	2,278.1	2,660.6	3 - 17
3	Coal	52	33,950.7	37,570.8	10.7	25	16,024.5	19,561.5	12 - 60
4	Fertilisers	5	4,828.7	4,828.7	0.0	2	763.0	763.0	9 - 12
5	Steel	16	50,110.2	71,356.8	42.4	6	4,328.2	4,813.1	2 - 24
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	65	156,993.5	165,178.0	5.2	32	93,948.9	100,615.1	1 - 80
8	Power	96	203,091.9	216,802.4	6.8	42	119,593.5	129,987.2	2 - 99
9	Railways	127	64,610.9	141,720.1	119.3	40	17,565.2	57,121.8	0 - 216
10	Road Transport & Highways	144	91,164.1	92,882.4	1.9	83	33,257.5	35,335.8	2 - 101
11	Shipping & Ports	19	16,242.5	17,757.5	9.3	7	9,429.2	10,670.2	9 - 29
12	Telecommunications	15	6,161.0	6,101.8	-1.0	9	3,116.1	3,120.0	17 - 79
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	15 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		555	723,972.0	867,266.9	19.8	255	348,790.4	425,276.6	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	52	34,916.7	37,570.8	7.6	11	10,671.7	13,325.8	24.9
4	Fertilisers	5	4,828.7	4,828.7	0.0	0	0.0	0.0	0.0
5	Steel	16	55,985.5	71,356.8	27.5	5	9,099.0	24,500.3	169.3
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	65	170,819.1	165,178.0	-3.3	2	30,533.0	31,324.0	2.6
8	Power	96	206,810.0	216,802.4	4.8	12	34,242.5	44,235.0	29.2
9	Railways	127	89,053.1	141,720.1	59.1	76	37,791.7	90,667.6	139.9
10	Road Transport & Highways	144	91,330.6	92,882.4	1.7	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	17,604.0	17,757.5	0.9	7	4,306.6	4,770.0	10.8
12	Telecommunications	15	6,164.9	6,101.8	-1.0	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		555	778,056.4	867,266.9	11.5	129	155,512.1	252,335.9	62.3

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,808.00	2,015.00	13- 13
3	Coal	52	33,950.69	37,570.81	10.66	0	0.00	0.00	0- 0
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	16	50,110.22	71,356.76	42.40	2	8,987.89	12,898.17	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	65	156,993.49	165,177.98	5.21	12	20,971.88	35,745.22	19- 120
8	Power	96	203,091.86	216,802.42	6.75	2	2,253.45	3,986.02	0- 67
9	Railways	127	64,610.86	141,720.12	119.34	15	8,021.50	21,091.97	1- 141
10	Road Transport & Highways	144	91,164.10	92,882.43	1.88	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	17,757.49	9.33	6	6,013.42	7,487.89	5- 87
12	Telecommunications	15	6,161.00	6,101.79	-0.96	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		555	723971.96	867266.9	19.79	38	48056.14	83224.27	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,942.51	2,325.00	17- 17
3	Coal	52	33,950.69	37,570.81	10.66	8	10,739.18	14,454.50	12- 48
4	Fertilisers	5	4,828.66	4,828.66	0.00	0	0.00	0.00	0- 0
5	Steel	16	50,110.22	71,356.76	42.40	4	9,477.89	13,591.75	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	65	156,993.49	165,177.98	5.21	12	49,312.67	64,735.01	7- 120
8	Power	96	203,091.86	216,802.42	6.75	15	39,917.50	53,014.92	7- 99
9	Railways	127	64,610.86	141,720.12	119.34	32	13,972.11	53,865.40	1- 216
10	Road Transport & Highways	144	91,164.10	92,882.43	1.88	11	3,354.51	5,615.10	18- 99
11	Shipping & Ports	19	16,242.52	17,757.49	9.33	7	7,365.57	8,958.14	5- 87
12	Telecommunications	15	6,161.00	6,101.79	-0.96	2	1,065.85	1,089.32	22- 39
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	15- 15
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		555	723971.96	867266.9	19.79	95	157256.69	247715.14	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final
			Cost	DOC	Cost	DOC	Expenditure
	<u>Power</u>						
1	LOHARINAG-PAL HEP(4X150MW)	06/2006	2,895.10	11/2011	2,895.10	12/2012	690.00
2	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS	02/2010	215.86	06/2012	215.86	06/2012	179.70
3	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)	12/2005	3,779.46	09/2009	3,725.13	06/2012	.00
4	CHAMERA,STAGE-III (NHPC)	08/2005	1,405.63	08/2010	2,084.00	06/2012	1,842.24
	<u>Railways</u>						
5	MUZAFFARPUR-SITAMARHI(NL),ECR	04/1997	100.00	03/2012	484.03	06/2012	466.70
6	SRIGANGANAGAR-SARUPSAR (GC), NWR	04/2001	143.92	03/2011	279.59	06/2012	235.37
	<u>Road Transport & Highways</u>						
7	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	12/2003	227.00	12/2008	227.00	05/2012	383.20
8	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	12/2003	225.00	10/2008	225.00	05/2012	261.90
	<u>Steel</u>						
9	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI	07/2007	232.93	05/2011	232.93	05/2012	191.83

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	<u>Power</u>					
1	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID	6/2012	1,263.26	11/2014	1,263.26	11/2014

VII. Milestones (Cumulative due & achieved)

Total	3309
Achieved up to month	1177

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Coal</u>						
1	PENGANGA OC WCL	339.77	339.77	03/2014	03/2015	03/2016	12
2	KARTALI (EAST) OCP(2.50 MTY) SECL	178.44	178.44	03/2014	03/2014	03/2016	24
	<u>Steel</u>						
3	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	06/2012	08/2012	2
4	EXPANSION OF BHILAI STEEL PLANT SAIL	5,185.00	17,265.00	N.A.	06/2013	09/2013	3
5	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2012	03/2013	3
6	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES SAIL	254.55	254.55	N.A.	11/2013	03/2014	4
	<u>Petroleum</u>						
7	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2013	05/2013	2
8	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-GAIL	238.68	276.00	N.A.	07/2012	09/2012	2
9	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	330.47	03/2012	06/2012	08/2012	2
10	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	288.04	08/2012	08/2012	12/2012	4
11	Development of SB-14 field ONGC	410.44	410.44	11/2012	05/2013	10/2013	5
12	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2012	08/2013	8
13	DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,436.21	07/2010	07/2012	05/2013	10
14	Development of Cluster-7 Fields ONGC	3,241.03	3,241.03	03/2013	04/2013	04/2014	12
	<u>Power</u>						
15	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI PGCIL	409.50	409.50	02/2012	06/2012	07/2012	1
16	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII PGCIL	317.69	317.69	11/2011	06/2012	07/2012	1
17	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	06/2013	08/2013	2
18	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION PGCIL	196.10	196.10	07/2011	06/2012	08/2012	2
19	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	06/2012	08/2012	2
20	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE NHPC	768.92	1,628.00	03/2007	09/2012	12/2012	3
21	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND PGCIL	2,360.95	2,360.95	08/2012	12/2012	03/2013	3


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
22	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I PGCIL	4,672.99	4,672.99	11/2012	03/2013	06/2013	3
23	System Strengthening in NR for SASAN & MUNDRA (UMPP) PGCIL	1,216.83	1,216.83	08/2012	08/2012	12/2012	4
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI PGCIL	1,677.57	1,677.57	04/2013	06/2013	10/2013	4
<u>Railways</u>							
25	KANPUR-KASGANJ-MATHURA(GC),NER NER	395.00	1,577.46	N.A.	02/2012	03/2012	1
26	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR ECR	233.00	1,043.56	03/2012	06/2012	08/2012	2
27	DEOGHAR - SULTANGANJ (INL), ER ER	138.00	607.09	12/2012	12/2012	02/2013	2
28	BANKURA - DAMODAR (GC) (SER) SER	111.90	1,412.74	03/2005	12/2015	06/2016	6
29	GADWAL - RAICHUR (NL), SCR SCR	92.63	270.00	02/2011	03/2012	02/2013	11
30	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	03/2012	03/2013	12
31	MANDARHILL-DUMKA-RAMPURHAT (NL),ER ER	184.00	900.05	12/2011	03/2012	03/2013	12
32	HOWRAH-AMTA-CHAMPADANGA NL (SER) SER	31.42	499.16	03/2007	03/2014	03/2015	12
33	KHURDA ROAD-BOLANGIR(NL)ECOR ECOR	355.38	1,100.00	N.A.	03/2012	03/2013	12
34	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) MRTF	401.81	1,512.86	03/2004	12/2010	03/2014	39
<u>Road Transport & Highways</u>							
35	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	06/2012	07/2012	1
36	Hyderabad-yadgiri N.H no-202 NHAI	388.00	388.00	05/2012	06/2012	08/2012	2
37	ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	06/2012	09/2012	3
38	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	06/2012	09/2012	3
39	BHOPAL-SANCHI NHAI	209.00	209.00	01/2013	01/2013	06/2013	5
40	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	06/2012	12/2012	6
41	Gurgaon-Kotputli Km 42.70 to 54.4 Km NHAI	1,673.70	1,673.70	10/2011	06/2012	12/2012	6
42	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING NHAI	359.00	359.00	09/2013	09/2013	07/2014	10
<u>Shipping & Ports</u>							
43	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	09/2012	10/2012	1
44	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER MUMBAI PORT TRU	1,228.00	1,460.00	12/2010	12/2012	03/2013	3
<u>Telecommunications</u>							
45	PROJ.III OF NIB-II OF MESSAGING STORAGE BSNL	250.00	250.00	12/2005	06/2012	07/2012	1
46	NIB Project Capacity Expansion BSNL	175.52	175.52	12/2008	06/2012	07/2012	1


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
47	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) BSNL	373.94	373.94	12/2008	06/2012	09/2012	3
48	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES BSNL	149.15	158.72	06/2009	06/2012	09/2012	3
49	Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	06/2012	09/2012	3
50	GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	930.60	11/2010	06/2012	09/2012	3
51	ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	07/2012	12/2012	5


Trend and Graphical Analysis of All Projects

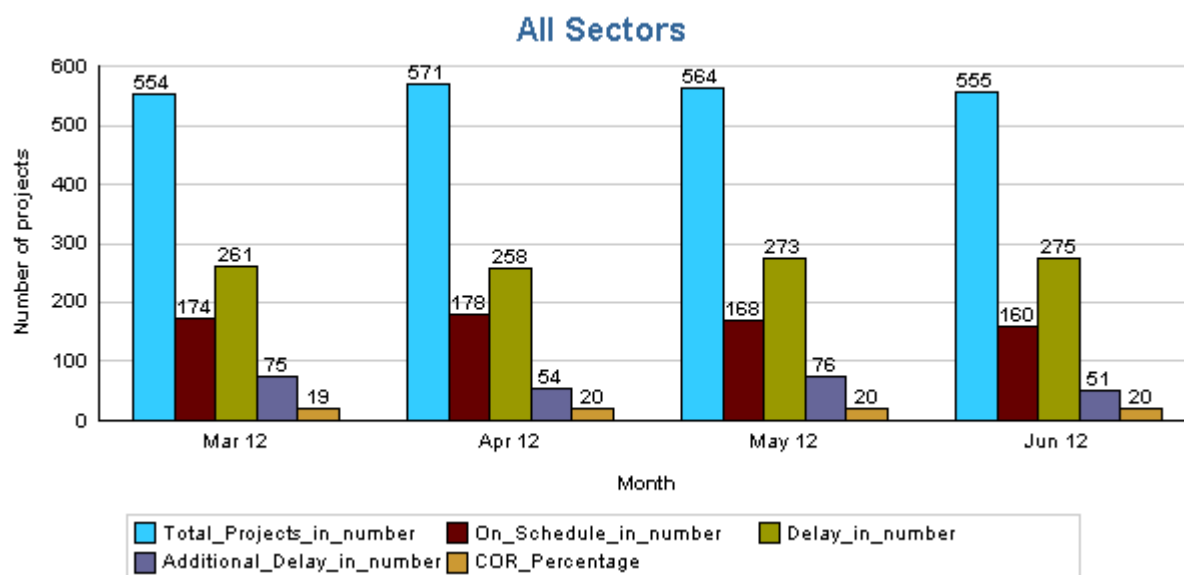


All Sectors Break-up of 275 Delayed projects in June 2012

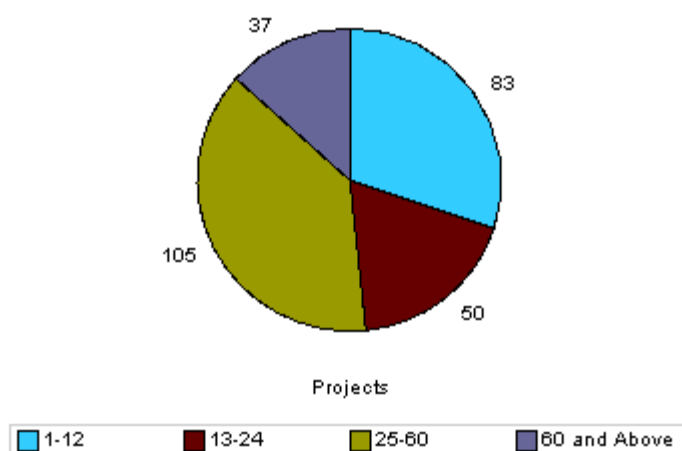


Trend and Graphical Analysis Telecommunications Sector

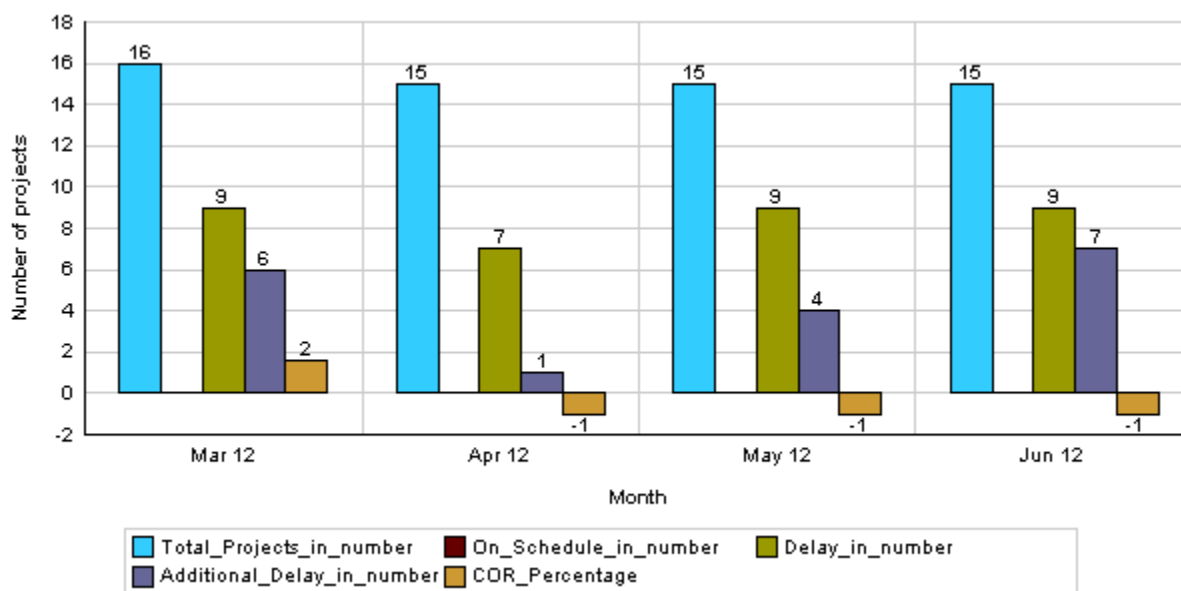


Telecommunications Sector Sector Break-up of 9 Delayed projects in June 2012

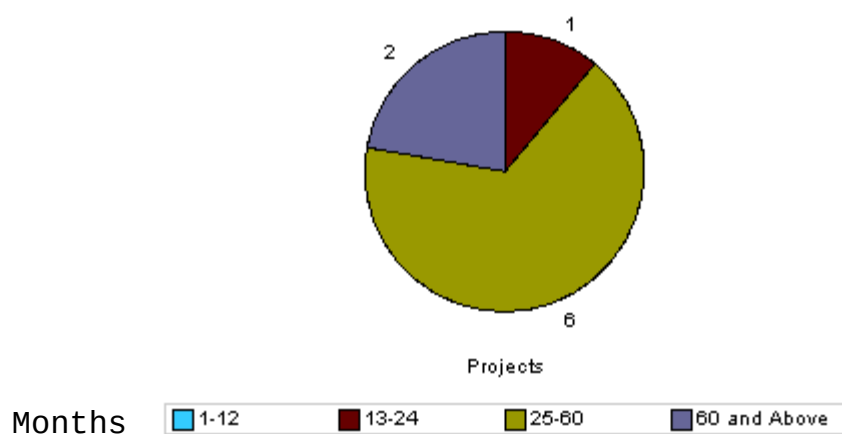

Trend and Graphical Analysis Shipping and Ports Sector

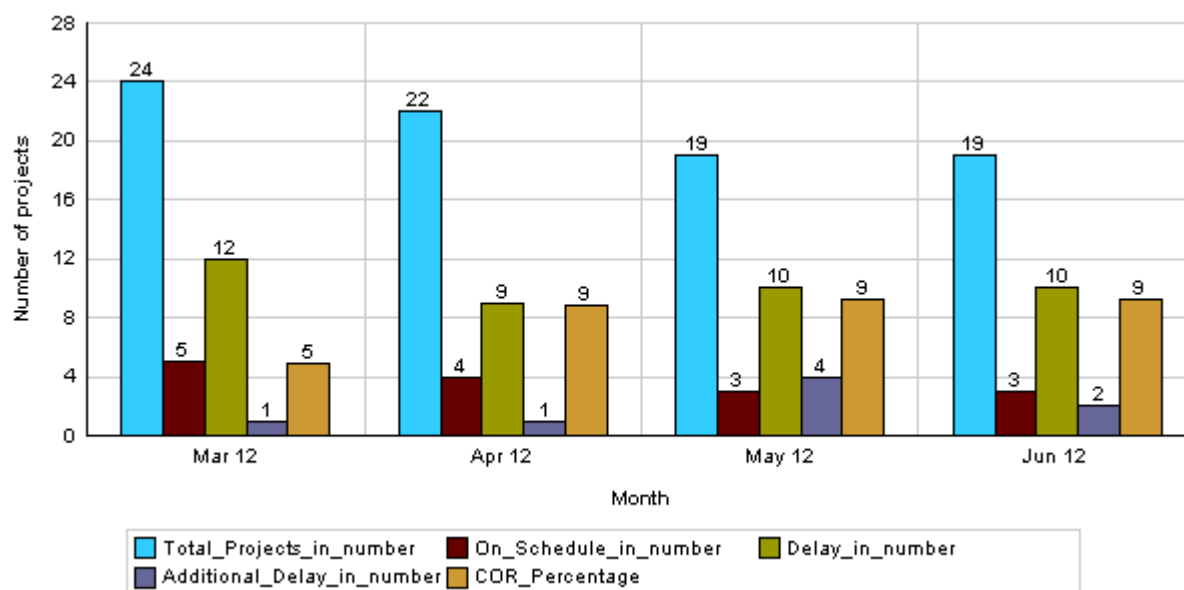


Sector Break-up of 10 Delayed projects in June 2012

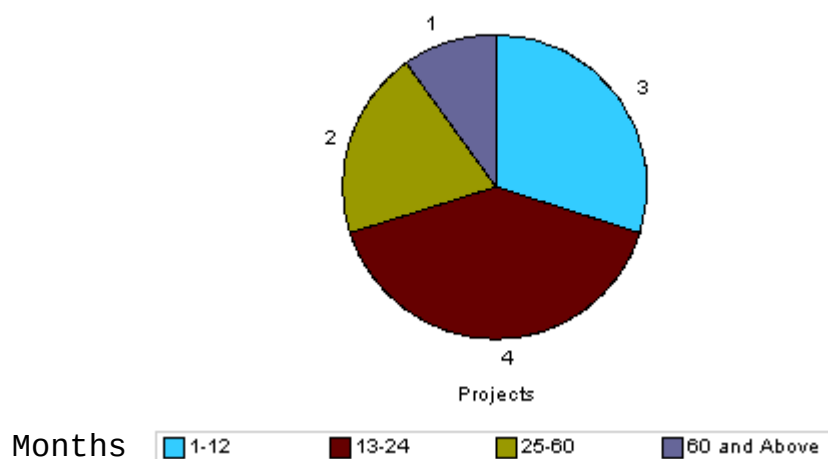


Trend and Graphical Analysis

Road Transport and Highways Sector

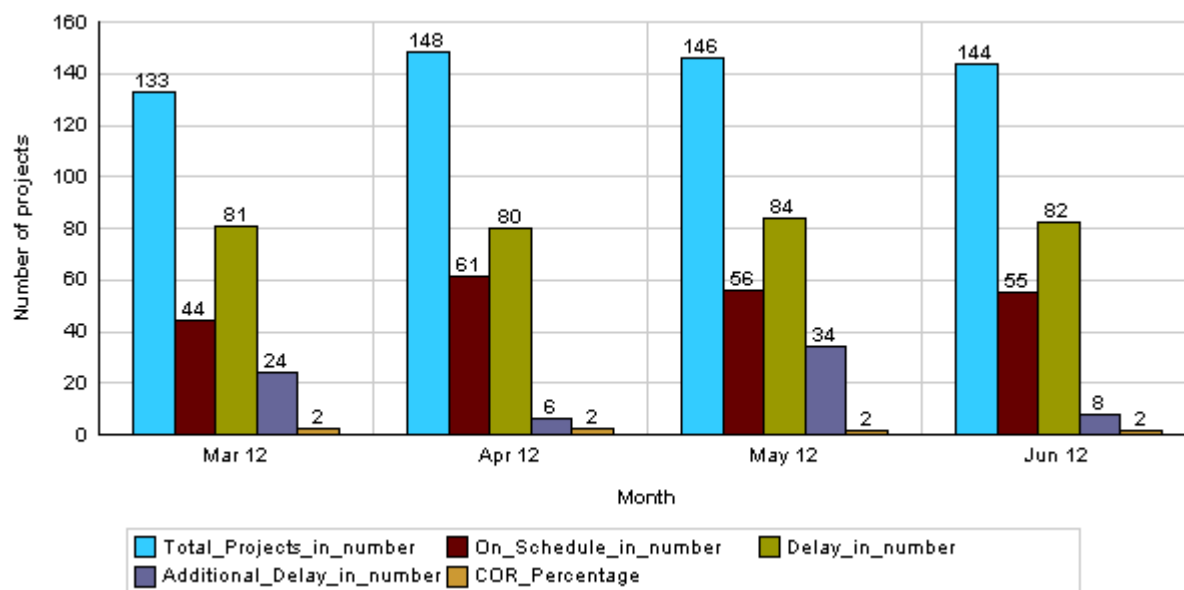


Sector Break-up of 82 Delayed projects in June 2012

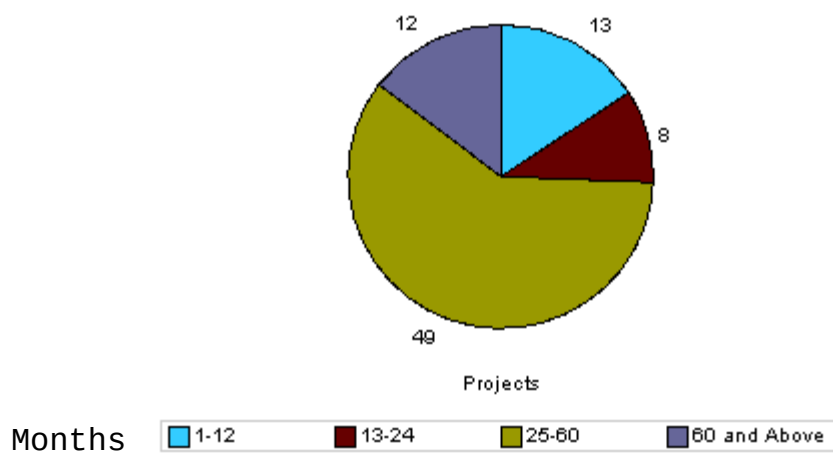


Trend and Graphical Analysis

Railways Sector

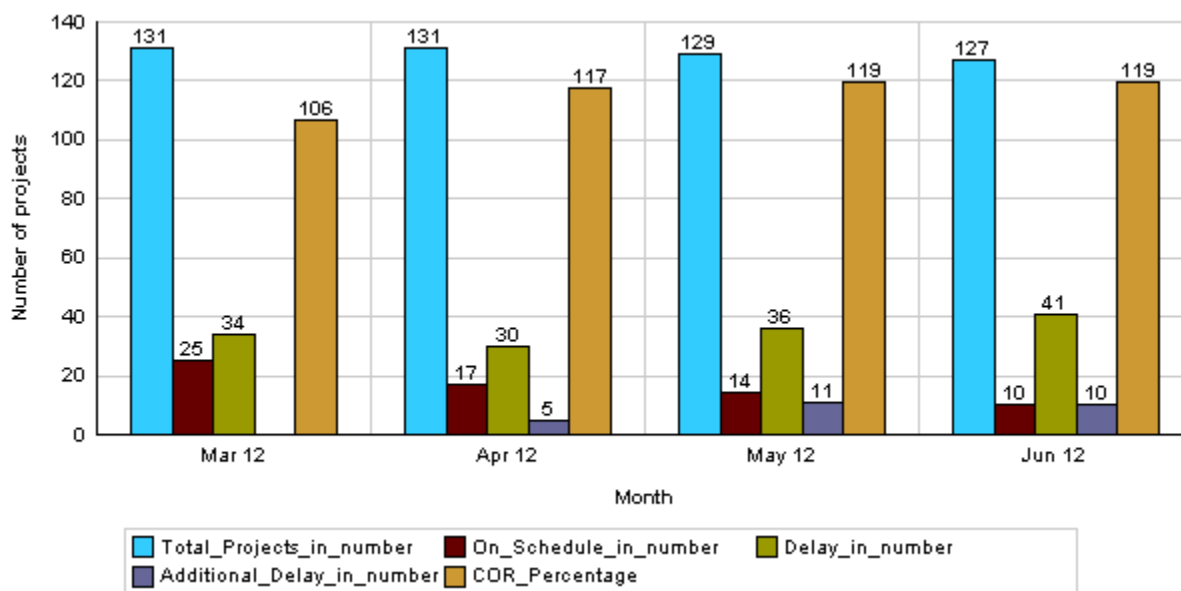


Railways Sector Sector Break-up of 41 Delayed projects in June 2012

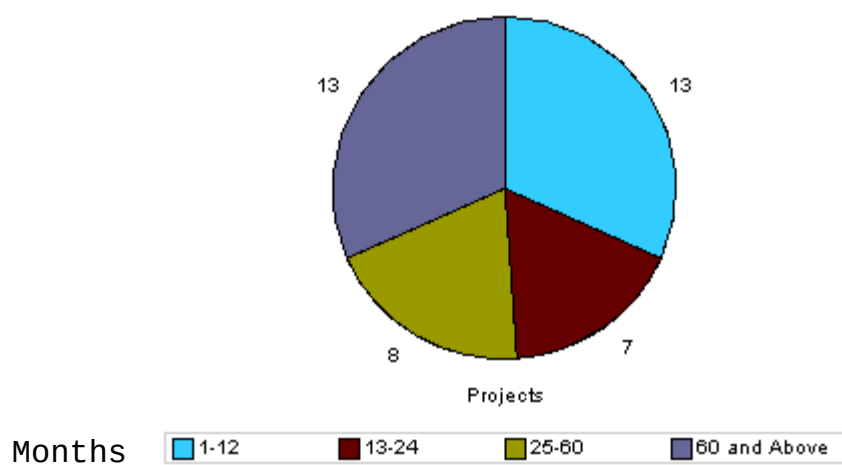


Trend and Graphical Analysis

Power Sector

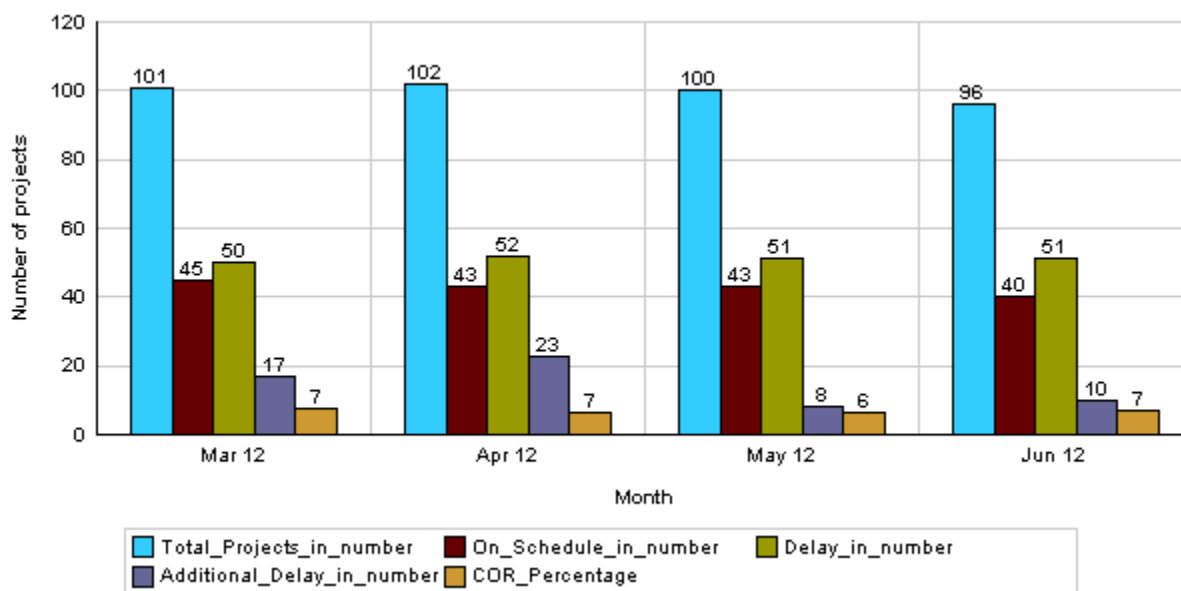


Power Sector Sector Break-up of 51 Delayed projects in June 2012

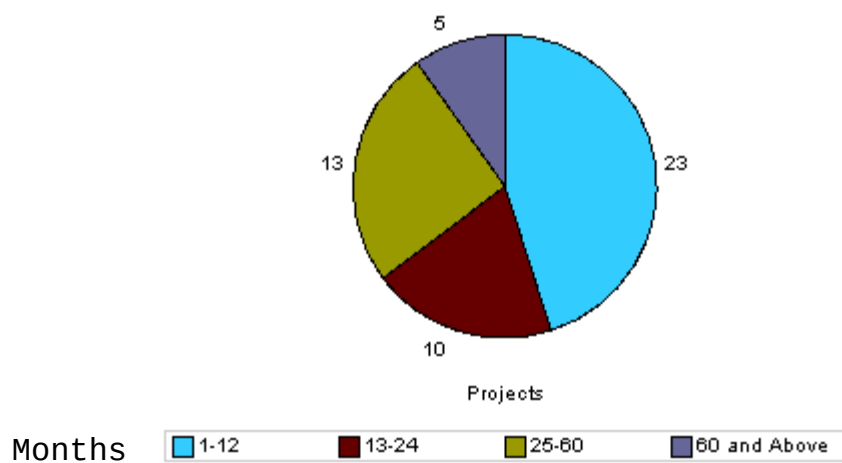


Trend and Graphical Analysis

Petroleum Sector

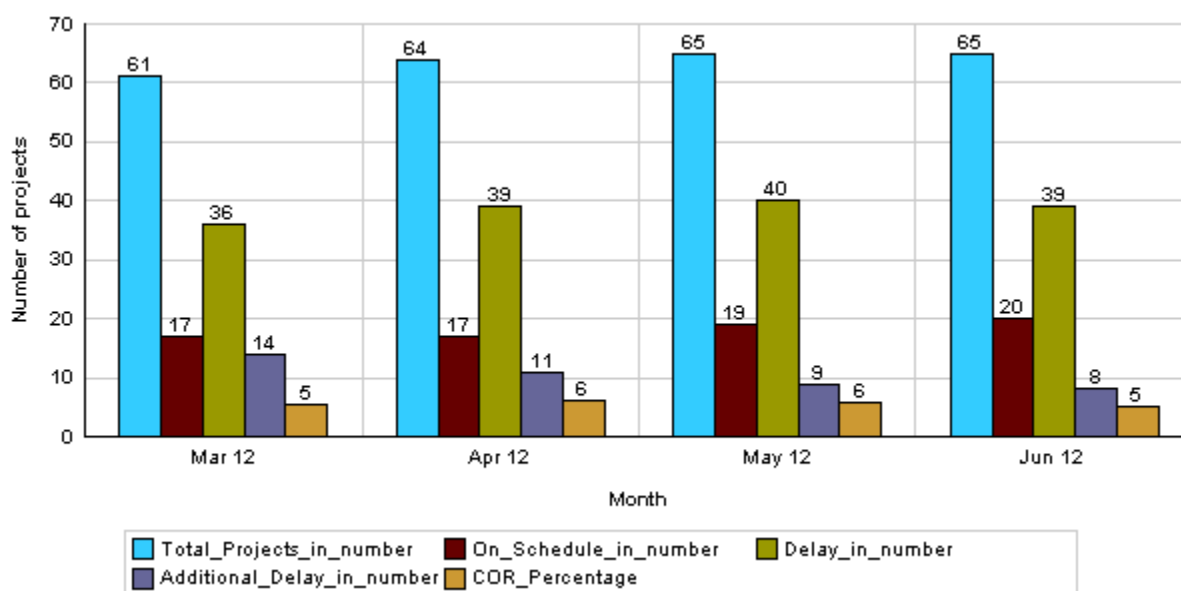


Petroleum Sector Sector Break-up of 39 Delayed projects in June 2012

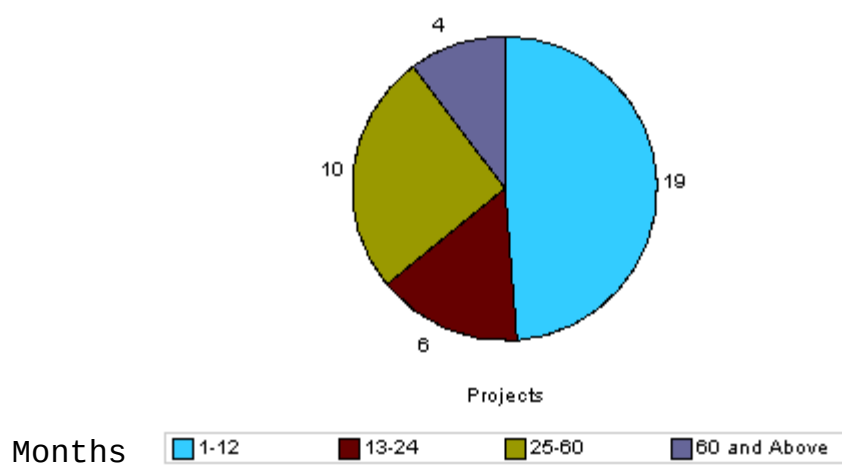


Trend and Graphical Analysis

Steel Sector

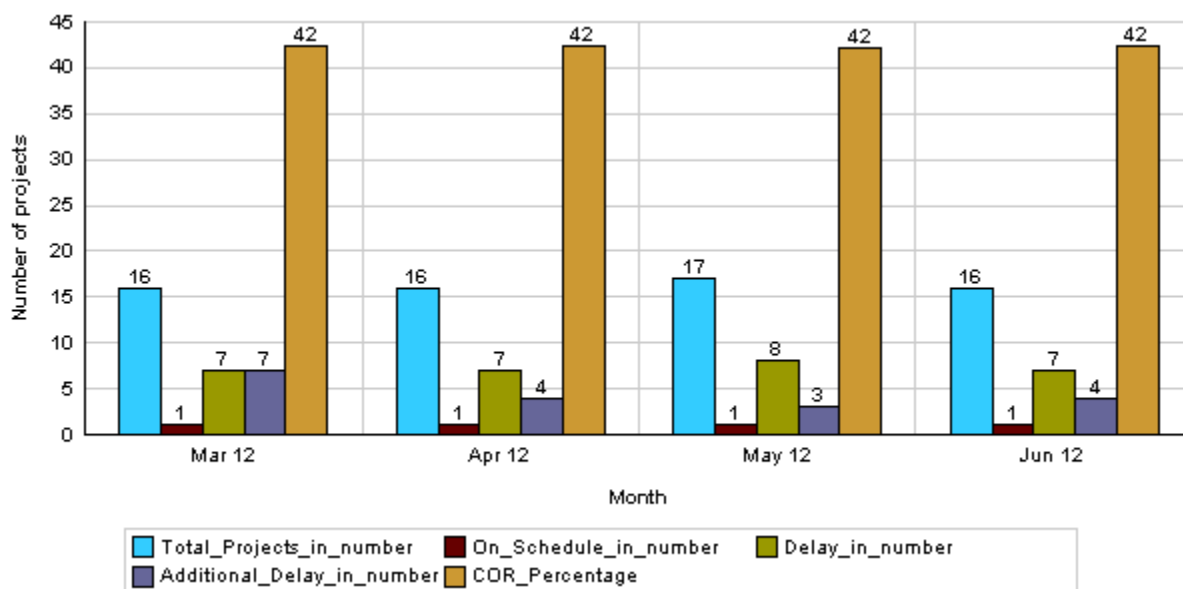


Steel Sector Sector Break-up of 7 Delayed projects in June 2012

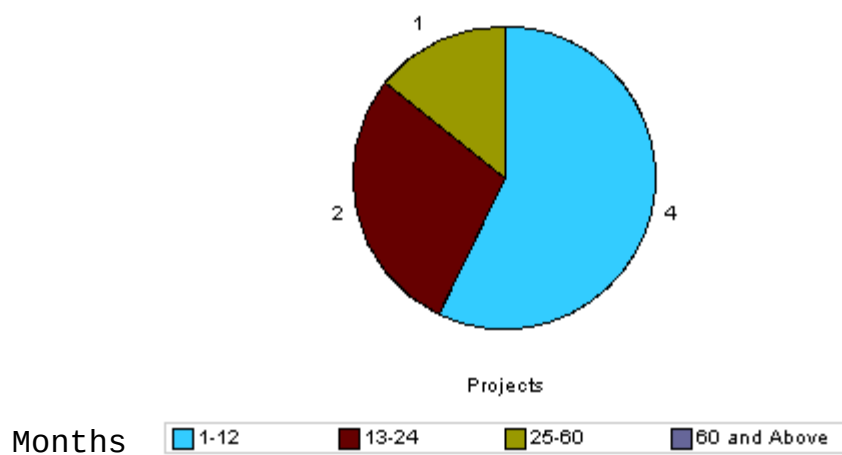


Trend and Graphical Analysis

Fertilisers Sector

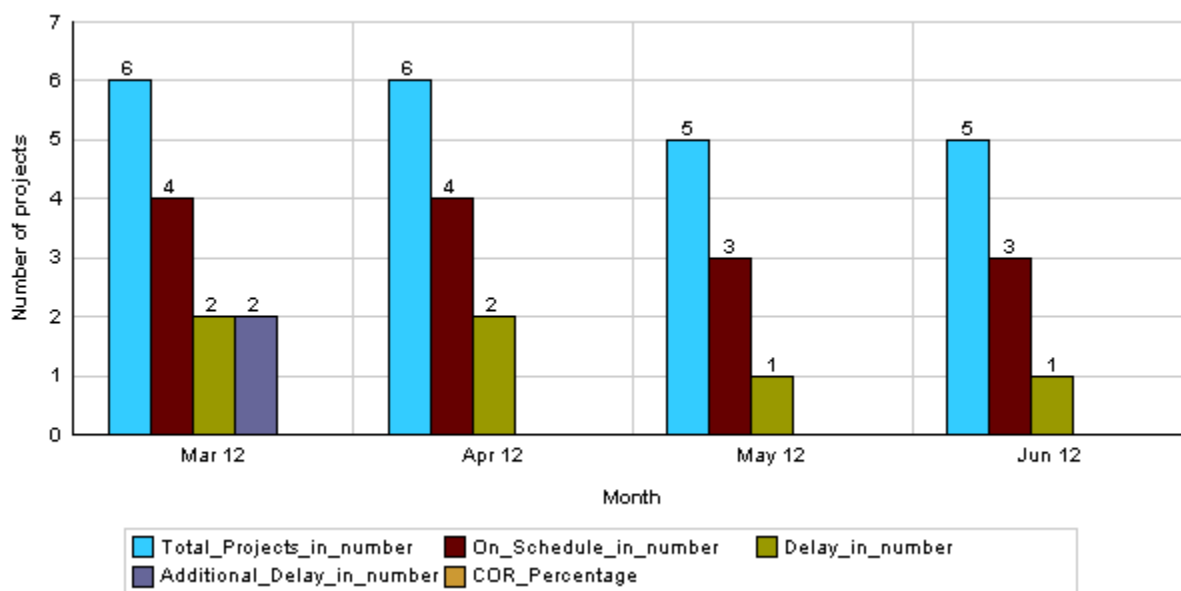


Fertilisers Sector Sector Break-up of 1 Delayed projects in June 2012

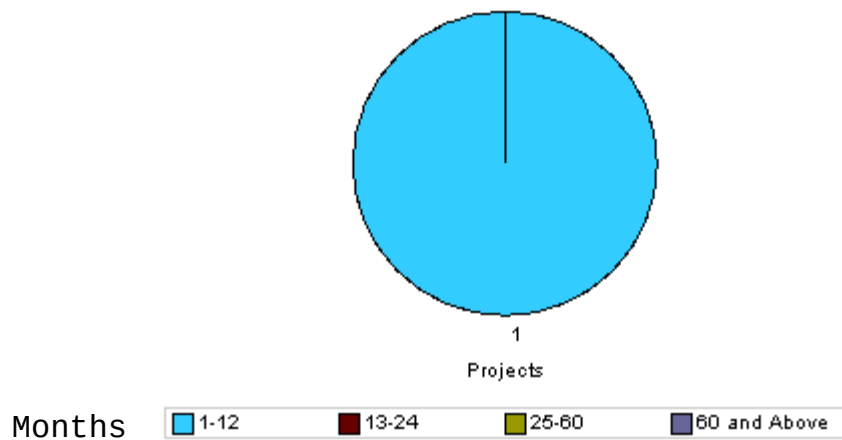


Trend and Graphical Analysis

Coal Sector

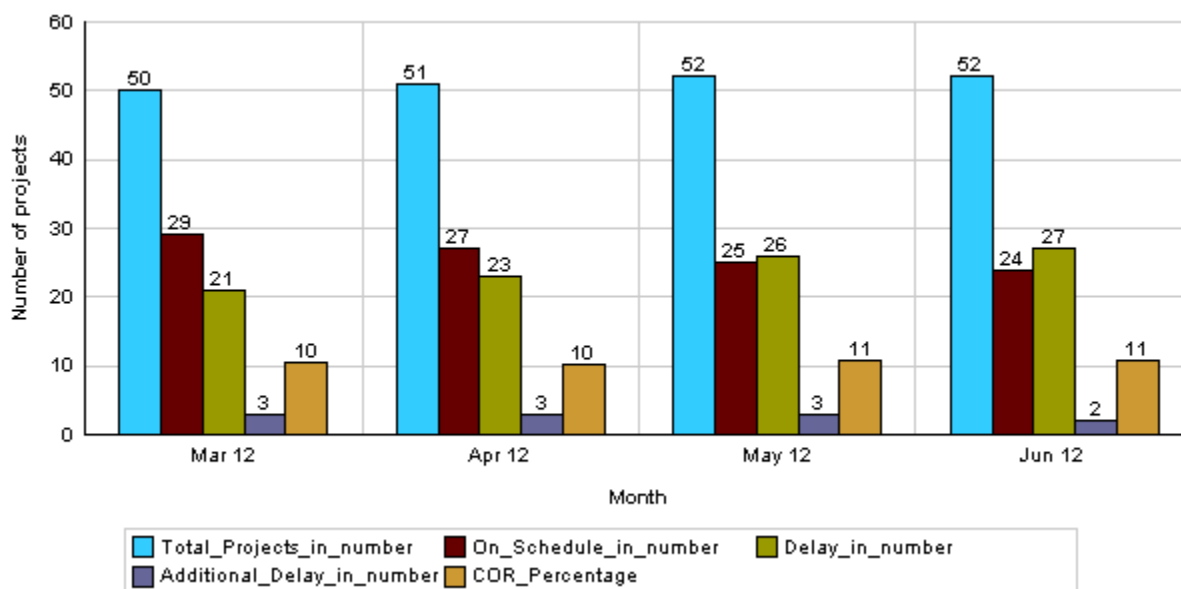


Coal Sector Sector Break-up of 27 Delayed projects in June 2012

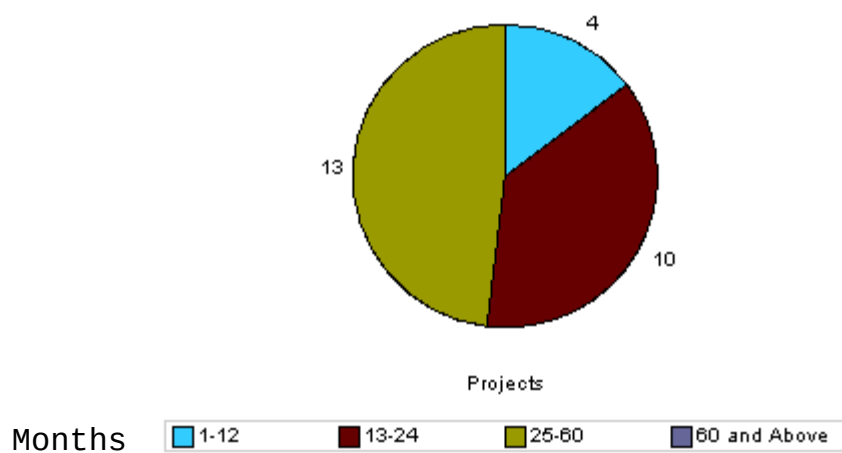


Trend and Graphical Analysis

Civil Aviation Sector

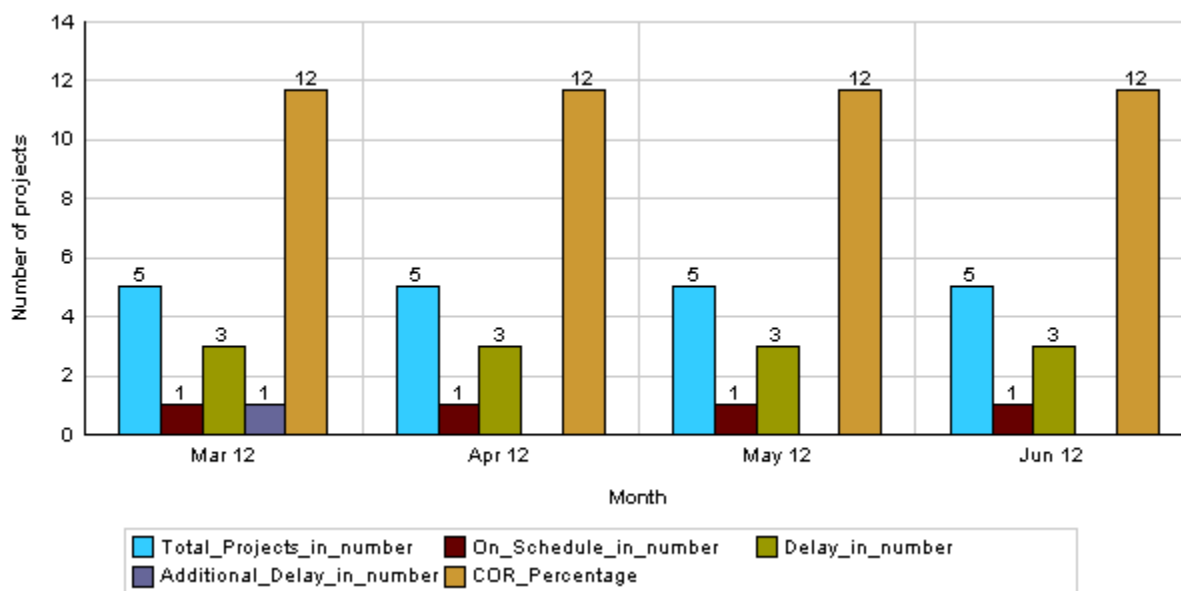


Civil Aviation Sector Break-up of 3 Delayed projects in June 2012

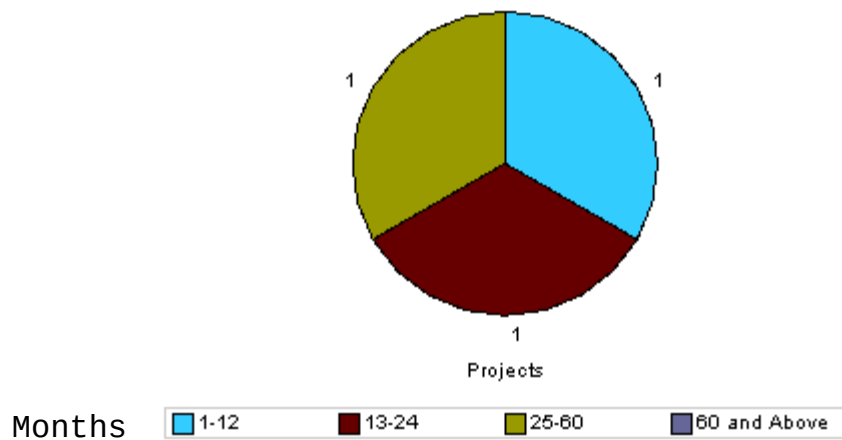


Trend and Graphical Analysis

Atomic Energy Sector

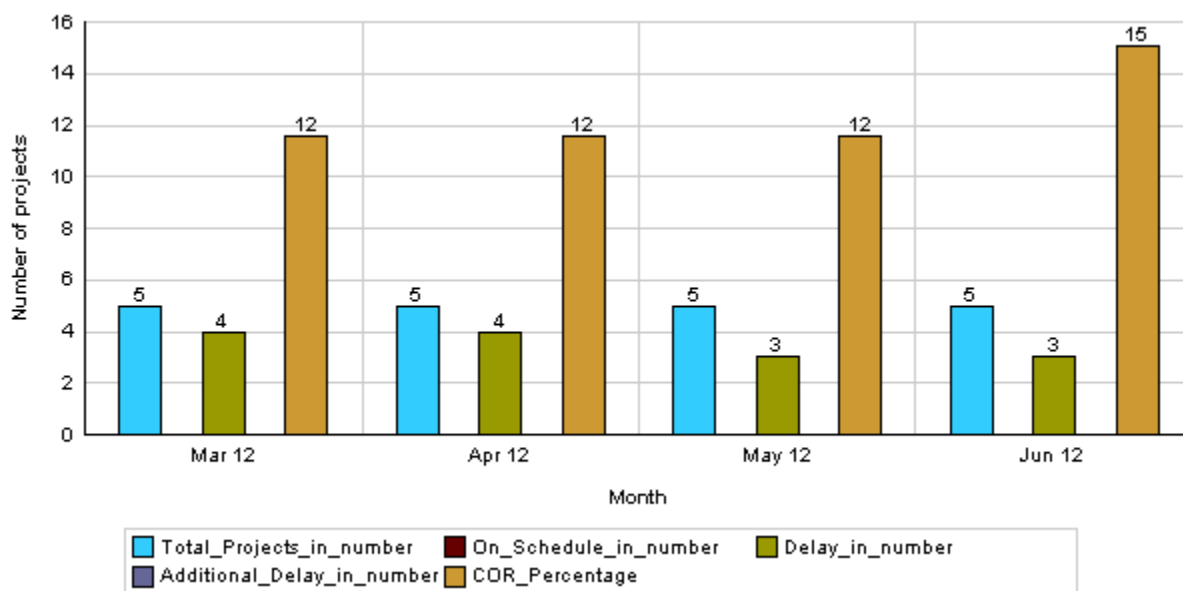


Atomic Energy Sector Sector Break-up of 3 Delayed projects in June 2012

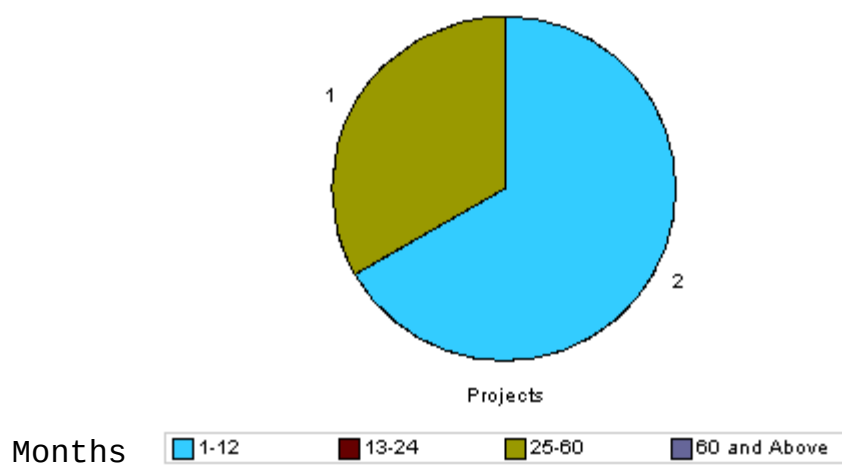


Trend and Graphical Analysis

Urban Development Sector

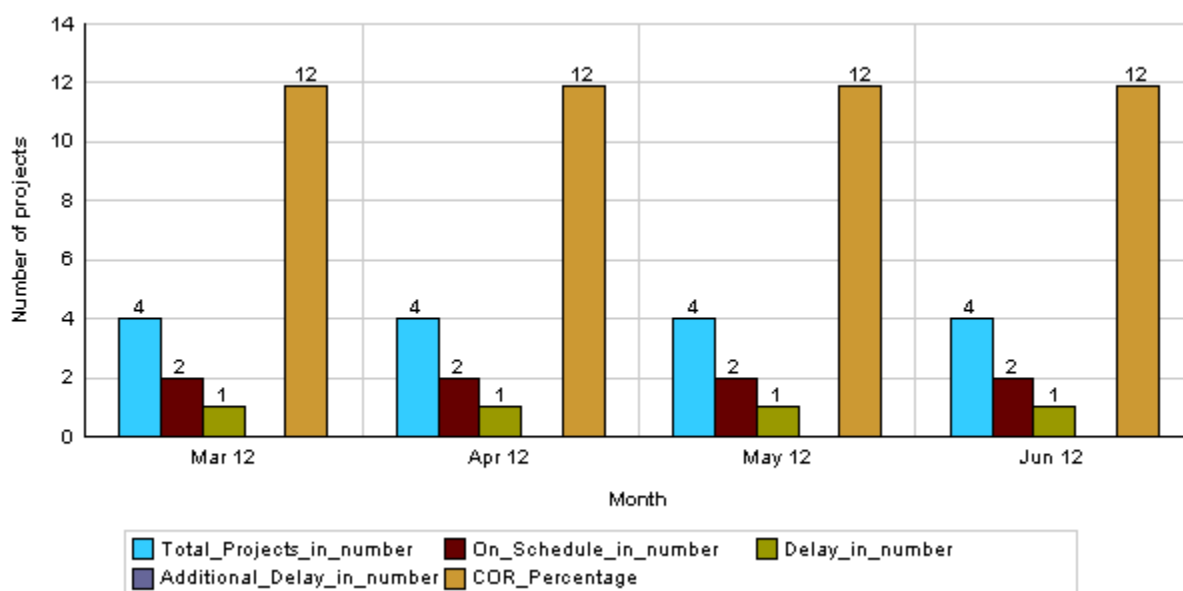

Urban Development Sector Break-up of 1 Delayed projects in June 2012

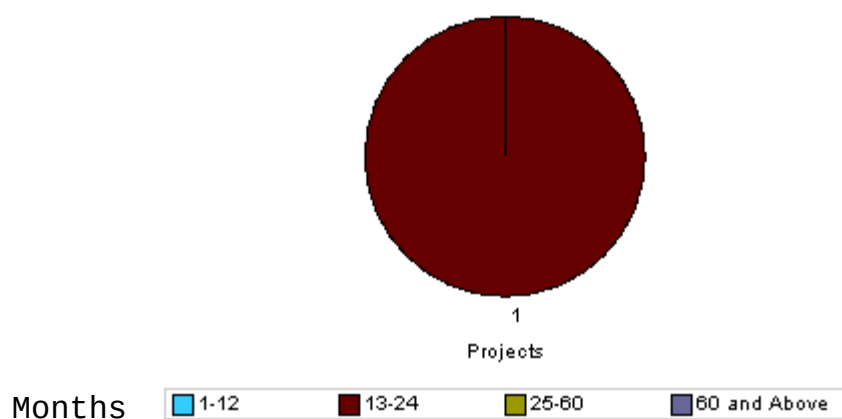

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	22,351.84
Civil Aviation	5	5,021.58	5,228.58	5,611.07	4,322.91
Coal	52	33,950.69	34,916.69	37,570.81	11,622.74
Fertilisers	5	4,828.66	4,828.66	4,828.66	2,453.98
Steel	16	50,110.22	55,985.50	71,356.76	35,770.64
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,657.21
Petroleum	65	156,993.49	170,819.14	165,177.98	73,785.97
Power	96	203,091.86	206,810.01	216,802.42	103,013.01
Railways	127	64,610.86	89,053.07	141,720.12	60,108.07
Road Transport & Highways	144	91,164.10	91,330.60	92,882.43	61,639.75
Shipping & Ports	19	16,242.52	17,604.04	17,757.49	7,363.49
Telecommunications	15	6,161.00	6,164.88	6,101.79	1,777.04
Urban Development	4	44,245.18	44,304.08	49,518.08	2,639.28
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	555	723,971.96	778,056.44	867,266.90	391,541.42

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,761.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	14,798.00	12/2008 -	03/2013	51(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,641.60	09/2010 -	01/2012	-	6/80
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,067.00	12/2016 -	03/2017	3(O) -	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,084.24	04/2011 04/2011	04/2012	-	0/0
Total			41,548.29 -	47,832.29	22,351.84				45/325
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,999.95	05/2011 03/2012	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	182.98	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	122.40	05/2012 -	08/2012	3(O) -	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,668.54	01/2011 02/2012	02/2012	-	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	349.04	06/2013 -	06/2013	0(O) -	0/0
Total			5,021.58 -	5,611.07	4,322.91				0/0
<u>Coal</u>									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	-	03/2013 09/2012	10/2014	19(O) 25(R)	7/22
12	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	70.19	03/2016 -	03/2016	0(O) -	2/6
13	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	338.98	03/2014 03/2016	03/2016	24(O) 0(R)	2/2

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	100.73	03/2012	03/2014	24(O)	5/7
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66	341.63	108.35	03/2011	03/2013	24(O)	0/2
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	103.13	03/2010	03/2015	60(O)	4/4
17	BAROUD OC EXPANSION - [N06000065]SECL,Chhatisgarh	07/2008	135.58	258.56	39.29	03/2015	03/2016	12(O)	0/0
18	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	258.56	-	03/2016	03/2016	0(O)	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	111.38	03/2017	03/2017	0(O)	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.35	03/2014	03/2014	0(O)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	161.87	03/2012	03/2015	36(O)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	261.91	03/2014	03/2016	24(O)	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	34.01	03/2011	03/2014	36(O)	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53	1,943.66	1,163.52	03/2010	03/2014	48(O)	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55	2,675.67	1,365.66	03/2010	03/2014	48(O)	10/15
27	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	70.56	03/2015	03/2015	0(O)	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	100.15	03/2013	03/2013	0(O)	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	9.93	03/2015	03/2017	24(O)	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015	03/2015	0(O)	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78	467.78	-	03/2013	03/2013	0(O)	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	0/1
33	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	71.37	12/2012	03/2015	27(O)	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	119.67	03/2013	03/2013	0(O)	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	30.55	03/2014	03/2014	0(O)	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24(O)	1/6
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	332.94	03/2010 -	03/2013	36(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	93.78	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	644.50	03/2013 03/2013	03/2013	0(O) 0(R)	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 -	706.40	18.16	07/2012 -	03/2016	44(O) -	1/2
43	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	203.55	03/2014 -	03/2014	0(O) -	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	-	03/2012 -	03/2013	12(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	19.70	12/2015 -	12/2015	0(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.20	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	62.45	03/2012 -	03/2014	24(O) -	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	33.74	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	-	03/2011 -	03/2014	36(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	-	03/2012 -	03/2013	12(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	-	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	-	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	266.45	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	-	03/2012 -	03/2012	-	11/42
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72 -	447.72	84.57	03/2016 -	03/2016	0(O) -	1/12

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,427.49	06/2009 -	03/2013	45(O) -	19/24
61	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	3,035.03	03/2012 -	03/2014	24(O) -	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	96.76	03/2012 -	03/2013	12(O) -	0/2
	Total		33,950.69 -	37,570.81	11,622.74				166/634
Fertilisers									
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	639.95	01/2013 -	01/2013	0(O) -	0/5
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	239.93	07/2011 -	07/2012	12(O) -	0/0
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	185.10	07/2011 -	04/2012	-	0/0
66	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	718.00	01/2013 01/2013	01/2013	0(O) 0(R)	8/8
67	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	671.00	01/2013 -	01/2013	0(O) -	0/5
	Total		4,828.66 -	4,828.66	2,453.98				8/18
Steel									
68	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	137.92	- -	04/2013	- -	1/19
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	243.84	08/2010 08/2010	08/2012	24(O) 24(R)	0/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	247.54	02/2011 02/2011	09/2012	19(O) 19(R)	2/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	80.90	- -	05/2013	- -	8/21
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	204.03	05/2012 05/2012	02/2013	9(O) 9(R)	1/2
73	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	331.15	12/2011 03/2012	10/2012	10(O) 7(R)	16/21
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	91.25	10/2012 10/2012	10/2012	0(O) 0(R)	3/4
75	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55 -	254.55	6.32	- -	03/2014	- -	0/1

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	-	-	09/2013	-	18/27
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	2,758.59	-	10/2012	-	10/16
78	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00	2,875.00	951.58	12/2012	03/2013	3(O)	6/12
79	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	13,470.28	-	12/2012	-	16/19
80	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	9,605.58	10/2009	10/2012	36(O) 0(R)	59/64
81	EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,Orissa	09/2008	11,812.00	11,812.00	7,286.45	11/2013	03/2013	-8(O)	6/14
82	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL,Maharashtra	12/2011	187.33	187.33	-	10/2013	12/2013	2(O)	0/0
83	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	500.90	355.21	-	02/2012	-	3/3
Total			50,110.22	71,356.76	35,770.64				149/227
Petrochemicals									
84	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61	8,920.00	4,657.21	12/2013	12/2013	0(O) 0(R)	10/30
Total			5,460.61	8,920.00	4,657.21				10/30
Petroleum									
85	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00	820.00	-	06/2012	04/2013	10(O)	0/0
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	2,163.64	1,017.31	06/2012	12/2012	6(O)	0/0
87	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	227.95	04/2011	07/2012	15(O)	0/0
88	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	362.81	12/2011	01/2013	13(O)	0/0
89	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	819.82	03/2013	03/2014	12(O)	0/0
90	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	5.57	12/2014	12/2014	0(O)	0/0
91	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014	12/2014	0(O)	0/0
92	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	460.70	247.03	07/2012	03/2013	8(O) 8(R)	0/16
93	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	89.83	02/2013	02/2013	0(O)	34/42

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	148.03	-	09/2012	-	28/36
95	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	719.92	04/2011 12/2011	09/2012	17(O) 9(R)	2/2
96	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	287.21	09/2011	08/2013	23(O)	0/0
97	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,525.33	05/2010 05/2012	07/2012	26(O) 2(R)	0/0
98	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	331.64	- 08/2011	08/2011	-	0/22
99	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94	202.94	0.20	01/2014	01/2014	0(O)	0/0
100	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	756.65	5.73	05/2013	05/2013	0(O)	0/0
101	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	-	08/2013	01/2014	5(O)	0/0
102	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	302.26	40.21	09/2012	12/2012	3(O)	0/0
103	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
104	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	198.44	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
105	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,775.82	03/2012 08/2012	08/2012	5(O) 0(R)	0/17
106	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	15.47	-	-	-	0/0
107	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	12/2012	80(O) 6(R)	0/0
108	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,596.34	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
109	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,279.74	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
110	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	837.12	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
111	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
112	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	966.53	09/2012 09/2012	09/2012	0(O) 0(R)	0/76
113	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,277.45	09/2011 03/2012	09/2012	12(O) 6(R)	0/0
114	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	49.65	03/2013 -	04/2013	1(O) -	0/0
115	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
116	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	288.30	03/2013 -	04/2014	13(O) -	0/0
117	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	7.33	11/2012 -	10/2013	11(O) -	0/0
118	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	48.25	01/2014 -	01/2014	0(O) -	0/0
119	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
120	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,908.40	- -	08/2012	- -	114/116
121	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	133.00	01/2013 -	01/2013	0(O) -	16/18
122	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	611.55	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
123	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015	0(O) -	0/0
124	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	1,141.82	06/2012 06/2012	06/2012	0(O) 0(R)	8/8
125	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
126	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
127	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
128	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015	0(O) -	0/0
129	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30(O) -	0/0
130	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.48	10/2010 -	12/2014	50(O) -	0/0
131	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 276.00	276.00	180.54	- -	09/2012	- -	0/1
132	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	987.59	12/2012 12/2012	04/2013	4(O) 4(R)	0/21

Sector Wise Details

(Jun,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
133	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	194.79	03/2012 08/2012	08/2012	5(O) 0(R)	2/4
134	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,763.03	01/2012 -	09/2012	8(O) -	0/0
135	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,896.72	09/2012 -	09/2013	12(O) -	0/0
136	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,987.33	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
137	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	5.67	04/2015 -	04/2015	0(O) -	0/0
138	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19(O) 17(R)	0/0
139	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
140	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	16,295.00	11/2012 -	06/2013	7(O) -	57/100
141	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,400.00	647.04	09/2012 09/2012	09/2012	0(O) 0(R)	0/11
142	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	1,292.50	02/2014 -	02/2014	0(O) -	0/0
143	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	-	05/2014 -	05/2014	0(O) -	0/0
144	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	584.47	07/2012 -	10/2012	3(O) -	0/0
145	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	898.00	857.41	- -	08/2012	- -	0/53
146	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	635.11	05/2010 04/2012	07/2012	26(O) 3(R)	0/0
147	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	148.32	08/2012 -	12/2012	4(O) -	0/0
148	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	213.91	03/2012 03/2012	08/2012	5(O) 5(R)	0/20
149	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	47.04	12/2013 12/2013	12/2013	0(O) 0(R)	0/0
Total			156,993.49 -	165,177.98	73,785.97				276/745
Power									
150	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,196.70	08/2012 -	03/2013	7(O) -	0/11

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,042.40	02/2012	10/2012	8(O)	0/7
152	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	601.60	05/2012	12/2012	7(O)	0/11
153	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	952.10	06/2012	12/2012	6(O)	0/4
154	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	4,312.00	08/2013	06/2014	10(O)	5/19
155	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,053.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
156	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,168.00	-	11/2014	-	4/28
157	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	743.22	02/2011 10/2012	10/2012	20(O) 0(R)	2/4
158	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	190.40	08/2014	08/2014	0(O)	0/20
159	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44	206.44	21.90	06/2014	06/2014	0(O)	0/20
160	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	203.20	09/2014	09/2014	0(O)	0/20
161	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	862.00	10/2009	12/2012	38(O)	20/20
162	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	315.70	11/2012	09/2013	10(O)	0/13
163	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
164	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	318.10	05/2014	05/2014	0(O)	0/16
165	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	497.30	08/2013	08/2013	0(O)	0/14
166	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77	901.77	52.80	08/2014	08/2014	0(O)	0/21
167	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	182.10	12/2013	12/2013	0(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL, Chhatisgarh	08/2011	1,391.97 -	1,391.97	214.90	12/2013 -	12/2013	0(O) -	0/13
169	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL, Multi State	10/2010	160.32 -	160.32	41.50	10/2012 -	03/2013	5(O) -	0/15
170	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	1,007.16	837.83	12/2007 12/2009	-	-	0/10
171	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,890.97	05/2013 03/2017	03/2017	46(O) 0(R)	4/22
172	KISHANGANGA HEP - [N18000031]NHPC, J and K	07/2007	2,238.67 3,642.04	3,642.00	1,514.73	01/2016 01/2016	11/2016	10(O) 10(R)	0/2
173	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,322.00	04/2009 03/2014	03/2014	59(O) 0(R)	0/9
174	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,825.01	09/2008 -	12/2012	51(O) -	17/37
175	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL, Madhya Pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/0
176	MOUDA STPP (NTPC) - [N18000048]NTPC, Maharashtra	11/2008	5,459.28 -	6,010.89	4,186.00	08/2012 -	03/2013	7(O) -	10/16
177	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, J and K	08/2006	611.01 -	936.00	765.72	08/2010 01/2013	01/2013	29(O) 0(R)	0/3
178	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	4,595.90	08/2013 -	09/2014	13(O) -	0/17
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL, Multi State	02/2009	317.69 -	317.69	183.20	11/2011 11/2011	07/2012	8(O) 8(R)	0/7
180	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, Multi State	02/2009	410.29 -	410.29	227.50	02/2012 -	03/2013	13(O) -	0/14
181	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State	02/2009	520.48 -	520.48	-	11/2011 -	12/2012	13(O) -	0/11
182	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66 -	509.66	325.40	11/2011 -	03/2013	16(O) -	0/14
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL, Multi State	10/2010	182.68 -	182.68	45.00	01/2013 -	01/2013	0(O) -	0/7
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, Multi State	07/2010	752.64 -	752.64	173.00	07/2013 -	07/2013	0(O) -	0/12
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL, Multi State	08/2010	1,677.57 -	1,677.57	443.90	04/2013 -	10/2013	6(O) -	0/12

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	61.10	08/2013 -	08/2013	0(O) -	0/16
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	40.40	11/2014 -	11/2014	0(O) -	0/0
188	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	399.40	11/2012 -	03/2013	4(O) -	0/10
189	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,853.81	10/2010 01/2013	01/2013	27(O) 0(R)	0/1
190	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,480.52	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
191	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	348.15	08/2012 09/2014	09/2014	25(O) 0(R)	13/19
192	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,827.31	01/2012 -	09/2013	20(O) -	0/0
193	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,263.00	10/2012 -	03/2013	5(O) -	10/16
194	SIPAT STTP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	8,230.00	12/2009 12/2011	06/2012	30(O) 6(R)	59/60
195	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,687.49	09/2010 08/2014	12/2016	75(O) 28(R)	11/11
196	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	38.20	04/2013 -	04/2013	0(O) -	0/15
197	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,922.90	08/2012 -	03/2013	7(O) -	0/7
198	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	133.30	07/2011 -	08/2012	13(O) -	0/5
199	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	47.90	08/2014 -	08/2014	0(O) -	0/20
200	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	93.20	02/2015 -	02/2015	0(O) -	0/0
201	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014	0(O) -	0/0
202	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	95.30	01/2015 -	01/2015	0(O) -	0/19
203	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	21.80	08/2014 -	08/2014	0(O) -	0/20

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
204	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	52.00	06/2014	06/2014	0(O)	0/19
205	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	134.40	04/2012	04/2012	-	0/0
206	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	96.08	06/2012	08/2012	2(O)	0/9
207	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	723.80	08/2012	12/2012	4(O)	0/11
208	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,474.00	03/2013	09/2015	30(O)	2/13
209	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,149.76	09/2009 06/2013	08/2013	47(O) 2(R)	0/0
210	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,518.60	03/2007 09/2012	12/2012	69(O) 3(R)	25/25
211	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	330.61	07/2010 02/2016	02/2016	67(O) 0(R)	1/10
212	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N180000118]PGCIL,Gujarat	01/2012	259.28	259.28	14.60	01/2014	01/2014	0(O)	0/17
213	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N180000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	72.60	08/2014	08/2014	0(O)	0/0
214	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N180000129]PGCIL,Multi State	02/2012	3,201.44	3,201.44	-	10/2014	10/2014	0(O)	0/21
215	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N180000064]PGCIL,Multi State	04/2008	297.37	297.91	326.43	07/2011	09/2012	14(O)	0/5
216	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N180000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,738.40	10/2012	09/2013	11(O)	0/12
217	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N180000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	255.10	01/2015	01/2015	0(O)	0/20
218	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N180000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	474.50	03/2013	03/2014	12(O)	0/15
219	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N180000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	406.40	08/2013	08/2013	0(O)	0/14
220	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N180000121]PGCIL,Andhra Pradesh	02/2012	324.33	324.33	1.40	08/2014	08/2014	0(O)	0/20

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16	1,927.16	17.30	10/2014	10/2014	0(O)	0/20
222	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	557.24	549.20	01/2010	02/2013	37(O)	0/22
223	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	149.70	11/2011	03/2013	16(O)	0/7
224	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	3,674.80	12/2012	12/2012	0(O)	0/11
225	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44	552.44	38.50	02/2014	02/2014	0(O)	0/20
226	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51	425.51	65.30	10/2013	10/2013	0(O)	0/18
227	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	45.30	07/2013	07/2013	0(O)	0/0
228	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34	1,366.34	156.00	12/2013	12/2013	0(O)	0/18
229	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26	558.26	62.90	11/2013	11/2013	0(O)	0/20
230	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	573.70	03/2013	03/2013	0(O)	0/14
231	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	638.40	12/2013	12/2013	0(O)	0/13
232	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	1,222.50	11/2012	06/2013	7(O)	0/15
233	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51	2,127.51	183.50	07/2014	07/2014	0(O)	0/19
234	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	295.71	- 07/2013	07/2013	- 0(R)	3/29
235	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63	913.63	334.77	07/2014 02/2015	02/2015	7(O) 0(R)	0/16
236	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	810.70	12/2012	03/2013	3(O)	0/11

Sector Wise Details

(Jun,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
237	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	295.80	11/2013 -	11/2013	0(O) -	0/15	
238	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	51.40	01/2013 -	01/2013	0(O) -	0/16	
239	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,083.00	1,744.34	11/2009 02/2013	02/2013	39(O) 0(R)	0/4	
240	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,510.00	10/2012 -	03/2013	5(O) -	9/15	
241	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	308.54	07/2014 -	05/2016	22(O) -	1/3	
242	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,133.60	07/2010 -	12/2012	29(O) -	20/20	
243	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	402.60	09/2010 -	-	-	0/9	
244	WESTERN REGION SYSTEM STRENGHTENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	112.31	02/2012 02/2012	07/2012	5(O) 5(R)	0/3	
245	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	18.60	06/2015 -	06/2015	0(O) -	0/24	
Total			203,091.86 -	216,802.42	103,013.01					243/1308
Railways										
246	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	356.57	03/2014 -	03/2014	0(O) -	0/0	
247	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	-	0/0	
248	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	165.33	- -	03/2013	- -	0/0	
249	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	453.04	391.98	03/2011 03/2011	03/2011	-	0/0	
250	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	523.76	06/1999 03/2011	03/2011	-	0/0	
251	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0	
252	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 -	394.14	0.49	03/2013 -	03/2013	0(O) -	0/0	
253	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0	
254	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	441.54	03/2005 12/2008	06/2016	135(O) 90(R)	0/0	

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
255	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	199.16	12/2010 03/2011	03/2011	-	0/0
256	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	189.02	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
257	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.48	4.57	04/2014 -	03/2015	11(O) -	0/0
258	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20 -	687.20	595.56	03/2010 -	12/2012	33(O) -	0/0
259	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhattisgarh	04/1997	151.52 -	350.00	319.07	- 03/2009	03/2011	-	0/0
260	BPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
261	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52 -	207.52	129.95	12/2012 -	05/2013	5(O) -	0/0
262	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36 196.95	196.95	179.41	03/2011 -	03/2011	-	0/0
263	Bhuj-Naliya (GC) with extension from naliya to Vayo - [N22000123]WR, Gujarat	04/2008	318.24 -	468.62	0.99	03/2012 -	03/2012	-	0/0
264	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
265	CHANDIGARH-LUDHIANA (NEW BG LINE), NR - [220100241](NR), Punjab	07/1998	248.44 576.27	1,115.21	877.21	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
266	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
267	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
268	CHURCHGATE-VIRAR: CONV. OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2012	06/2012	-12(O) 0(R)	0/0
269	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR, Arunachal Pr.	09/1996	156.00 -	415.73	240.93	- -	03/2012	-	0/0
270	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD) - [220100149]RVNL, Chhattisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
271	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, Rajasthan	02/1997	151.84 410.08	410.08	184.87	- -	03/2013	-	0/0
272	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, Multi State	04/2000	138.00 607.09	607.09	381.76	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
273	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, Tamil Nadu	09/2006	343.17 -	900.00	519.00	- -	12/2012	-	0/0
274	Dakshin-barasal-lakshmikanthapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	533.38	80.01	12/2011 02/2012	02/2012	-	0/0
275	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE, Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
276	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE, Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
277	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, Tamil Nadu	04/2006	495.74 -	495.74	154.63	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
278	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00 634.13	634.13	551.77	03/1995 -	03/2013	216(O) -	0/0
279	GADWAL - RAICHUR (NL), SCR - [220100270]SCR, Multi State	04/1998	92.63 228.09	270.00	260.76	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
280	GOELKERA-MANOHARPUR, (LD)(SER) - [N22000045]SER, Jharkhand	03/1997	186.92 261.70	261.70	39.12	02/2006 -	12/2013	94(O) -	0/0
281	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, Uttar Pradesh	03/2002	381.17 -	863.23	548.53	- -	03/2012	-	0/0
282	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
283	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	776.00	315.68	- 05/2009	05/2009	-	0/0
284	Ghutiasharif-Canning (ER) - [N22000117]ER, West Bengal	04/2009	189.97 611.03	611.03	94.82	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
285	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66 528.65	324.66	178.54	- -	03/2015	-	0/0
286	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 1,185.00	1,185.00	219.18	- 09/2009	12/2011	-	0/0
287	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO 50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
288	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 412.91	944.55	496.59	- -	01/2013	-	0/0
289	HATHUA-BHATNI (N L) (NER) - [220100319]NER, Multi State	04/2005	230.03 -	230.03	145.31	- -	03/2014	-	0/0
290	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 393.46	499.16	165.13	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
291	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	997.58	69.57	- -	-	-	0/0
292	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR, Rajasthan	04/2008	829.74 -	829.74	4.59	03/2015 -	03/2015	0(O) -	0/0
293	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00 625.30	847.76	833.20	06/2007 -	06/2007	-	0/0
294	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 501.69	1,043.56	641.56	03/2012 08/2012	08/2012	5(O) 0(R)	0/0
295	JIND-SONEPAT (NL), NR - [220100280](NR), Haryana	01/2004	190.81 238.56	500.00	414.03	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
296	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 -	4,444.00	797.35	03/2011 03/2014	03/2016	60(O) 24(R)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
297	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.46	107.79	03/2014 -	03/2014	0(O) -	0/0
298	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	231.34	03/2012 03/2012	10/2012	7(O) 7(R)	0/0
299	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,299.58	- -	03/2012	-	0/0
300	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	750.89	488.98	- -	03/2014	- -	1/1
301	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	724.88	- -	10/2012	- -	0/0
302	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	728.94	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
303	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	90.86	- -	03/2013	- -	0/0
304	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	206.19	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
305	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	208.82	- -	03/2013	- -	0/0
306	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	- -	0/0
307	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	408.37	- 03/2010	03/2010	-	0/0
308	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,261.28	07/2005 -	07/2005	-	0/0
309	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	118.67	- -	-	-	0/0
310	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	264.07	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
311	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.20	1,047.00	9.41	- -	-	-	0/0
312	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	341.37	- -	03/2011	-	0/0
313	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	105.81	12/2012 -	03/2014	15(O) -	0/0
314	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	-	0/0
315	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
316	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	201.64	03/2002 -	03/2013	132(O) -	0/0
317	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,073.53	3,083.48	03/2009 -	12/2013	57(O) -	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
318	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
319	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	158.62	- -	02/2013	- -	0/0
320	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	528.06	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
321	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
322	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	384.07	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
323	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	240.64	- -	-	-	0/0
324	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,334.00	06/2011 03/2012	03/2012	-	0/0
325	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	698.48	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
326	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	126.31	- -	03/2012	-	0/0
327	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	613.36	02/2009 -	03/2012	-	0/0
328	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	-	07/2012 07/2012	07/2012	0(O) 0(R)	0/0
329	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	532.87	39.45	- -	-	-	0/0
330	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	385.20	100.31	- -	03/2014	- -	0/0
331	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.81	1,141.55	12/2008 -	03/2014	63(O) -	0/0
332	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	- -	0/0
333	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O) -	0/0
334	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	2,913.51	135.97	03/2016 -	03/2016	0(O) -	0/0
335	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	27.66	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
336	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	16.68	03/2016 -	03/2016	0(O) -	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
337	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72	2,397.72	22.34	03/2016	06/2016	3(O)	0/0
338	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00	1,117.11	396.21	03/2008 06/2008	-	-	0/0
339	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	355.00	390.18	03/2009 12/2009	03/2011	-	0/0
340	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 529.23	529.23	212.25	02/2010 -	12/2015	70(O) -	0/0
341	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 1,389.98	1,389.98	1,445.12	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
342	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	568.11	- -	03/2012	-	0/0
343	Pandabeswar-Chinrai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	136.04	12/2010 12/2010	12/2010	-	0/0
344	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.00	741.64	- -	03/2013	-	0/0
345	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	221.90	223.67	12/2007 03/2010	12/2010	-	0/0
346	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00	1,115.63	725.62	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
347	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	248.61	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
348	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR, Gujarat	04/2006	196.97	196.97	218.04	03/2011 -	06/2012	15(O) -	0/0
349	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	232.01	- -	-	-	0/0
350	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, Jharkhand	04/1997	194.07	456.45	292.01	06/2004 -	12/2012	102(O) -	0/0
351	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70	1,717.29	1,190.08	- -	03/2013	-	0/0
352	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34	370.00	343.10	04/2003 03/2010	-	-	0/0
353	REWARI-ROHTAK (NL), NR - [220100279](NR), Haryana	01/2004	149.38 330.23	530.76	486.96	02/2010 02/2011	02/2011	-	0/0
354	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	639.97	173.67	03/1998 08/2005	08/2005	-	0/0
355	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	329.78	03/2013 -	03/2014	12(O) -	0/0
356	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04	603.04	84.85	03/2012 -	03/2013	12(O) -	0/0
357	SALKA ROAD - ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhattisgarh	09/2006	324.90	385.54	224.35	03/2010 -	03/2012	-	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
358	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	3,380.58	52.63	12/2015	12/2015	0(O)	0/0
359	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	818.29	67.86	02/2015	-	-	0/0
360	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23	516.23	200.11	03/2014	03/2014	0(O)	0/0
361	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96	810.78	112.49	-	03/2013	-	0/0
362	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97	1,086.41	419.38	06/2005	06/2016	132(O)	0/0
363	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96	1,188.91	500.49	07/2011	02/2012	59(R)	0/0
364	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	129.43	-	-	-	0/0
365	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	35.30	-	-	-	0/0
366	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	497.68	-	-	-	0/0
367	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69	3,176.10	3,009.20	12/2006	08/2010	-	0/0
368	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73	167.73	43.22	03/2012	03/2012	-	0/0
369	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00	20,000.00	7,947.68	03/2001	12/2017	201(O)	0/0
370	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00	820.40	150.01	03/2010	06/2014	51(O)	0/0
371	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62	1,389.62	287.90	03/2014	03/2013	-12(O)	0/0
372	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66	356.87	163.33	-	-	-	0/0
	Total		64,610.86	141,720.12	60,108.07	03/2010			1/1
Road Transport & Highways									
373	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	163.93	05/2013	03/2014	10(O)	0/0
374	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
375	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00	226.00	199.49	02/2014	02/2014	0(O)	0/0
376	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00	664.00	15.10	02/2014	04/2014	2(O)	0/0
377	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09	375.09	20.75	04/2014	04/2014	0(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00	325.00	115.63	05/2014	05/2014	0(O)	0/0
379	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	364.02	08/2014	08/2014	0(O)	0/0
380	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	1,008.50	1,097.80	06/2013	06/2013	0(O)	0/0
381	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	33.22	09/2013	07/2014	10(O)	0/0
382	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	785.50	507.92	08/2013	08/2013	0(O)	0/0
383	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00	575.00	366.62	07/2013	07/2013	0(O)	0/0
384	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00	398.00	150.00	02/2014	02/2014	0(O)	0/0
385	4-laning of Brahampore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79	998.79	498.45	08/2013	08/2013	0(O)	0/0
386	4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State	02/2011	1,078.84	1,078.84	594.39	08/2013	08/2013	0(O)	0/0
387	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
388	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	465.50	162.31	09/2007	06/2013	69(O)	0/0
389	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	10/2012	91(O)	0/0
390	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	1,038.80	11/2012	06/2013	7(O)	0/0
391	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	281.86	11/2008	09/2012	46(O)	0/0
392	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	256.42	01/2009	12/2012	47(O)	0/0
393	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	07/2012	5(O)	0/0
394	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	188.72	02/2004	07/2012	101(O)	0/0
395	BAREILY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00	1,046.00	87.11	09/2013	09/2013	0(O)	0/0
396	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan	12/2011	2,388.00	2,388.00	155.04	06/2014	06/2014	0(O)	0/0
397	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	386.83	-	10/2013	-	2/2
398	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00	209.00	3.77	01/2013	06/2013	5(O)	0/0
399	BHUBANESWAR TO PURI - [N24000195]NHAI, Orissa	03/2011	500.29	500.29	329.47	08/2013	08/2013	0(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
400	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	243.92	06/2008	12/2012	54(O)	0/0
401	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	201.47	06/2008	03/2013	57(O)	0/0
402	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	225.24	06/2005	09/2012	87(O)	0/0
403	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	201.07	04/2010	12/2012	32(O)	0/0
404	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
405	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	634.99	03/2013	03/2013	0(O)	0/0
406	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	97.49	-	12/2013	-	0/1
407	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	05/2013	0(O)	0/0
408	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	339.37	10/2011	03/2014	29(O)	0/0
409	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	663.32	10/2011	06/2013	20(O)	0/0
410	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	278.06	06/2008	12/2012	54(O)	0/0
411	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.23	10/2008	03/2014	65(O)	0/0
412	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	578.08	05/2010	12/2012	31(O)	0/0
413	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	339.12	07/2013	07/2013	0(O)	0/0
414	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
415	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	351.33	-	06/2013	-	1/1
416	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	227.95	06/2008	03/2013	57(O)	0/0
417	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	172.56	05/2008	03/2013	58(O)	0/0
418	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	252.87	09/2010	12/2012	27(O)	0/0
419	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	56.11	08/2013	08/2013	0(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
420	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	535.16	01/2011 -	12/2012	23(O) -	0/0
421	FORBESGANJ TO SIMRAHI (NH- 57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	371.68	09/2008 -	12/2012	51(O) -	0/0
422	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16(O) -	0/0
423	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	118.85	09/2008 -	03/2013	54(O) -	0/0
424	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27 -	263.27	265.81	02/2004 -	07/2012	101(O) -	0/0
425	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	275.00	304.29	09/2007 -	09/2012	60(O) -	0/0
426	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00 -	1,141.00	662.22	08/2013 -	08/2013	0(O) -	0/0
427	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	204.40	04/2008 -	12/2012	56(O) -	0/0
428	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	145.60	04/2008 -	12/2012	56(O) -	0/0
429	GWALIOR BYPASS, NH-75, 3 - [N24000088]NHAI, Madhya pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38(O) -	0/0
430	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	12/2012	36(O) -	0/0
431	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	1,299.10	09/2012 -	09/2012	0(O) -	0/0
432	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,488.40	10/2011 -	12/2012	14(O) -	0/0
433	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	273.84	09/2007 -	09/2012	60(O) -	0/0
434	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	264.82	02/2009 -	03/2013	49(O) -	0/0
435	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	43.39	07/2009 -	04/2014	57(O) -	0/0
436	HARANGAJO TO MAIBANG, km 164.08- 190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	23.66	09/2007 -	04/2014	79(O) -	0/0
437	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	184.41	08/2004 -	08/2012	96(O) -	0/0
438	HAVERI-HARIHAR (GQ) KM.340- KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	179.10	08/2004 07/2010	08/2012	96(O) 25(R)	0/0
439	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	625.07	779.14	01/2013 -	01/2013	0(O) -	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
440	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
441	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,744.70	10/2012	10/2012	0(O)	0/0
442	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	506.40	05/2012	08/2012	3(O)	0/0
443	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	369.11	05/2013	02/2014	9(O)	0/0
444	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
445	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81	267.81	452.55	02/2013	02/2013	0(O)	0/0
446	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
447	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	521.77	09/2008	12/2012	51(O)	0/0
448	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	468.34	09/2009	12/2012	39(O)	0/0
449	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	536.00	376.37	01/2014	01/2014	0(O)	0/0
450	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	1,214.20	12/2012	12/2012	0(O)	0/0
451	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.34	10/2008	09/2012	47(O)	0/0
452	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	285.56	10/2008	03/2013	53(O)	0/0
453	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
454	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,003.30	05/2012	09/2012	4(O)	0/0
455	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	185.64	06/2010	10/2012	28(O)	0/0
456	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	10/2012	37(O)	0/0
457	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	87.37	11/2008	07/2013	56(O)	0/0
458	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	56.76	04/2009	07/2013	51(O)	0/0
459	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	15.49	11/2008	01/2014	62(O)	0/0
460	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	108.63	04/2009	03/2013	47(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
461	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6(O)	0/0
462	MURADABAD-BAREILY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	1,264.30	06/2013	06/2013	0(O)	0/0
463	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00	754.00	335.29	03/2013	03/2013	0(O)	0/0
464	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	65.78	11/2013	11/2013	0(O)	0/0
465	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	266.72	06/2008	03/2013	57(O)	0/0
466	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48(O)	0/0
467	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	262.54	04/2008	12/2012	56(O)	0/0
468	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	231.87	06/2008	03/2013	57(O)	0/0
469	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	273.71	06/2008	12/2012	54(O)	0/0
470	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
471	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	363.00	248.66	06/2011	12/2012	18(O)	0/2
472	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
473	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00	586.00	162.45	01/2014	01/2014	0(O)	0/0
474	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	393.71	09/2013	09/2013	0(O)	0/0
475	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	379.89	03/2008	12/2012	57(O)	0/0
476	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00	1,410.00	120.31	09/2014	09/2014	0(O)	0/0
477	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	797.01	10/2014	10/2014	0(O)	0/0
478	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	205.95	05/2008	08/2012	51(O)	0/0
479	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	574.00	66.26	03/2014	03/2014	0(O)	0/0
480	PATNA-MUZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	580.92	02/2013	02/2013	0(O)	0/0
481	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,141.10	07/2012	12/2012	5(O)	0/0
482	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	874.76	03/2013	03/2013	0(O)	0/0
483	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	835.00	-	01/2014	01/2014	0(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
484	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,459.20	11/2011	08/2013	21(O)	0/0
485	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,906.80	05/2012	10/2012	5(O)	0/0
486	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
487	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	303.96	10/2008	12/2012	50(O)	0/0
488	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	255.82	10/2008	09/2012	47(O)	0/0
489	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	734.10	11/2013	11/2013	0(O)	0/0
490	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	231.38	10/2008	12/2012	50(O)	0/0
491	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	187.27	10/2008	08/2012	46(O)	0/0
492	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25(O)	0/0
493	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	228.54	03/2013	03/2013	0(O)	0/0
494	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
495	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	198.29	09/2007	03/2013	66(O)	0/0
496	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	180.10	07/2008	12/2012	53(O)	0/0
497	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
498	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	4.93	12/2013	12/2013	0(O)	0/0
499	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
500	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2014	19(O)	0/0
501	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
502	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60(O)	0/0

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
503	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	116.80	04/2004	07/2012	99(O)	0/0
504	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,649.60	08/2011	09/2012	13(O)	0/0
505	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41(O)	0/0
506	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	03/2013	32(O)	0/0
507	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	471.21	11/2013	11/2013	0(O)	0/0
508	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
509	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	55.89	05/2013	05/2013	0(O)	0/0
510	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	34.70	-	04/2013	-	2/2
511	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	497.30	03/2014	03/2014	0(O)	0/0
512	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09	166.30	189.15	03/2008	07/2012	52(O)	0/0
513	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	-	03/2008	05/2012	-	0/0
514	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.71	11/2012	11/2012	0(O)	0/0
515	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	314.98	07/2013	07/2013	0(O)	0/0
516	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00	1,047.00	148.11	06/2014	06/2014	0(O)	0/0
Total			91,164.10	92,882.43	61,639.75				10/14
Shipping & Ports									
517	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 10/2012	10/2012	18(O) 0(R)	0/0
518	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	501.89	09/2012	09/2012	0(O)	0/0
519	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	187.07	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
520	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8(O) 0(R)	0/0

Sector Wise Details

(Jun,2012)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	
521	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 09/2012	09/2012	15(O) 0(R)	0/0	
522	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O) -	0/0	
523	Acquistion of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O) -	0/0	
524	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	792.12	12/2010 09/2012	03/2013	27(O) 6(R)	0/0	
525	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0	
526	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0	
527	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	10/2008	-	0/0	
528	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1	
529	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0	
530	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0	
531	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	252.00	0.21	03/2012 -	03/2012	-	0/0	
532	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0	
533	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.32	10/2008 -	11/2010	-	0/0	
534	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,345.60	01/2012 09/2012	10/2012	9(O) 1(R)	0/0	
535	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0	
Total			16,242.52 -	17,757.49	7,363.49					0/1

Telecommunications

Sector Wise Details

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
536	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	09/2012	44(O) -	0/0
537	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
538	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
539	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	21.93	10/2010 12/2012	12/2012	26(O) 0(R)	0/0
540	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
541	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
542	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	09/2012	39(O) -	0/0
543	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94 -	373.94	231.79	12/2008 -	09/2012	45(O) -	0/0
544	GSM equipment of 1625000 Lines (2G) 325000 lines 3(-) - [N26000090]BSNL, Madhya Pradesh	11/2009	916.70 930.60	930.60	804.06	11/2010 -	09/2012	22(O) -	0/0
545	GSM equipment of 200000 Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	-	0/0
546	GSM equipment of 799000 Lines (2G) 101000 lines 3(G) - [N26000088]BSNL, Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39(O) -	0/0
547	Implementation of FTTH, the state of the art Access - [N26000073]BSNL, Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
548	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
549	NIB Project Capacity Expansion - [N26000098]BSNL, Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	07/2012	43(O) -	0/0
550	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL, Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	07/2012	79(O) 52(R)	0/0
	Total		6,161.00 -	6,101.79	1,777.04				0/0
Urban Development									
551	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15(O) -	6/6
552	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0

Sector Wise Details

(Jun,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	345.26	03/2016	03/2016	0(O)	0/0
554	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	26.45	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	2,639.28				6/6
			-						
	<u>Water Resources</u>								
555	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			723,971.96	867,266.90	391,541.42				914/3309

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **15**

Number of Projects Delayed **9**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 9 projects are delayed .6 projects do not have fixed dates of commissioning.

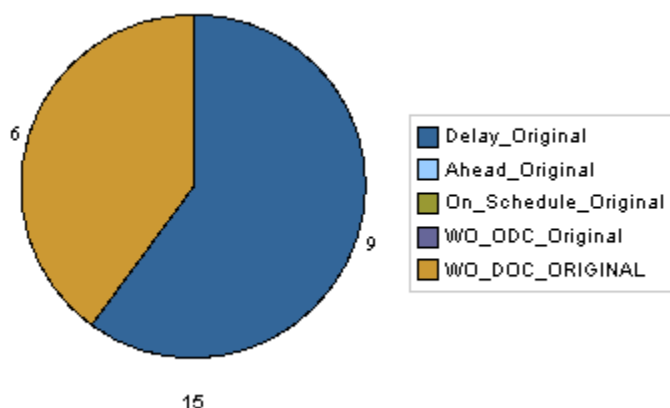

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 6161 crore but this was subsequently revised to Rs. 6101.79 crore implying a cost overrun of -1%. The expenditure incurred on these projects till June, 2012 is Rs. 1777.04 crore, which is 29.1% of the revised cost of the projects.

Figures are in Rs. Crore

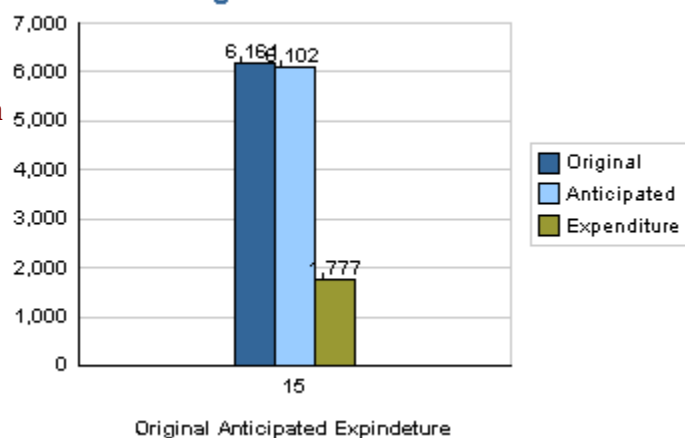

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	5

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .5 projects do not have fixed dates of commissioning.

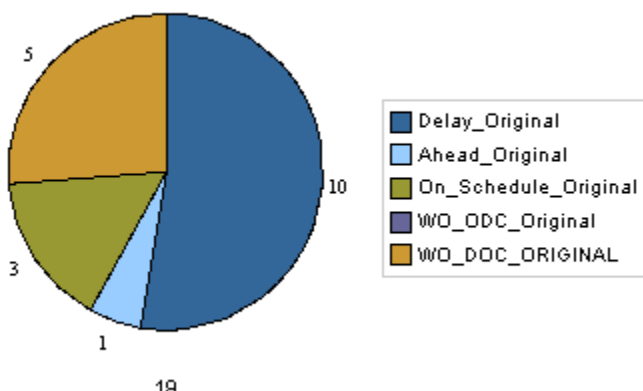

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 17757.49 crore implying a cost overrun of 9.3%. The expenditure incurred on these projects till June, 2012 is Rs. 7363.49 crore, which is 41.5% of the revised cost of the projects.

Figures are in Rs. Crore

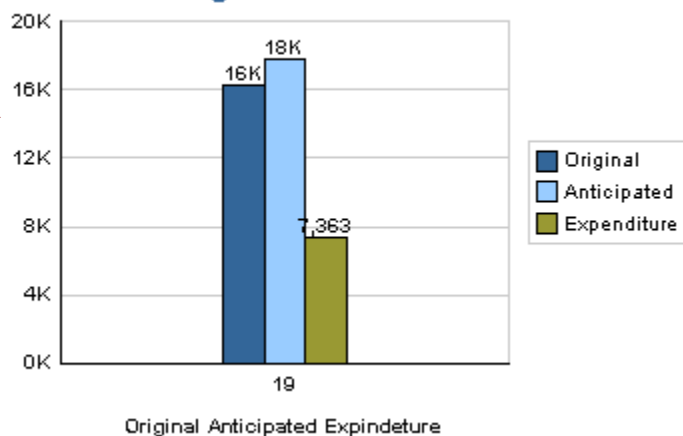

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	144
Number of Projects On Schedule	55
Number of Projects Delayed	82

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 144 projects, 55 projects are on schedule and 82 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

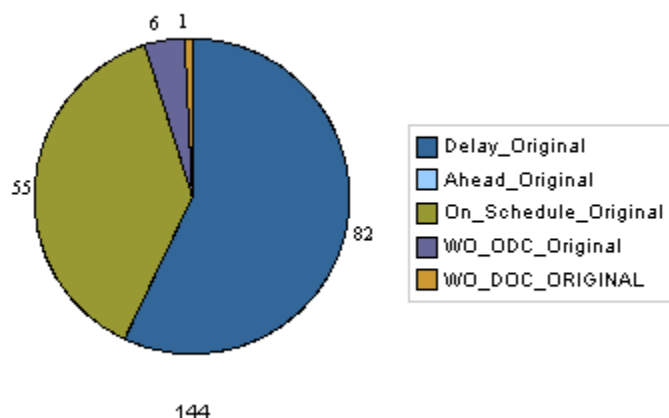

III. Investment Scenario

The Total Original cost of implementation of 144 projects when sanctioned, was of the order of Rs. 91164.1 crore but this was subsequently revised to Rs. 92882.43 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till June, 2012 is Rs. 61639.75 crore, which is 66.4% of the revised cost of the projects.

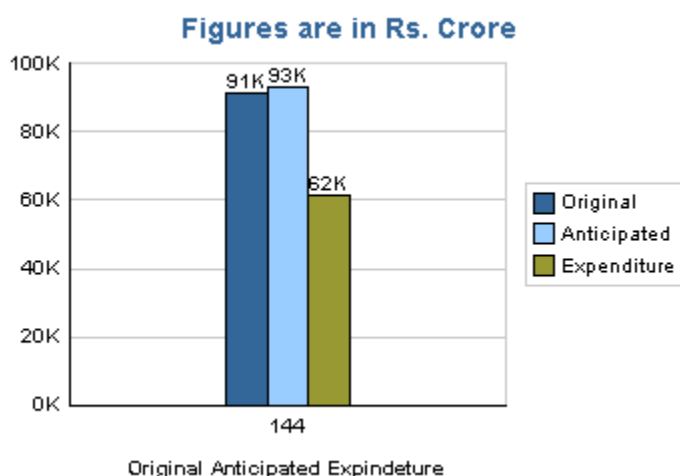

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	127
Number of Projects On Schedule	10
Number of Projects Delayed	41
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	18
Number of Projects Without Date Of Commissioning	56

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 2 projects are ahead of schedule, 10 projects are on schedule and 41 projects are delayed. 56 projects do not have fixed dates of commissioning. 18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

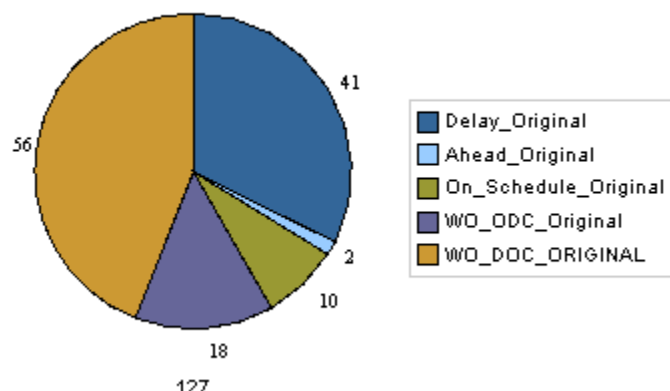

III. Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 64610.86 crore but this was subsequently revised to Rs. 141720.12 crore implying a cost overrun of 119.3%. The expenditure incurred on these projects till June, 2012 is Rs. 60108.07 crore, which is 42.4% of the revised cost of the projects.

Figures are in Rs. Crore

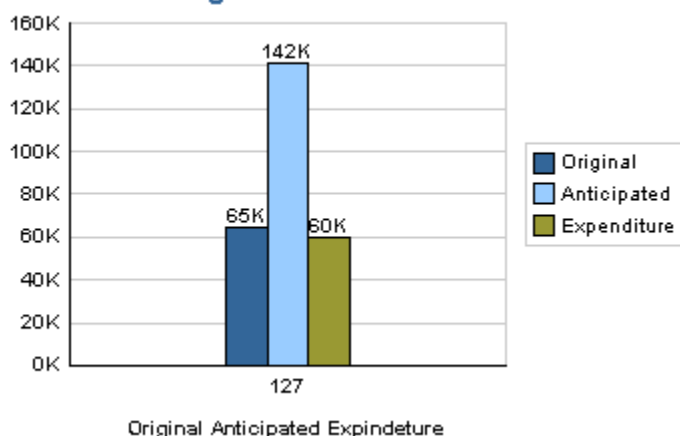

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	96
Number of Projects On Schedule	40
Number of Projects Delayed	51

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 96 projects, 40 projects are on schedule and 51 projects are delayed .3 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

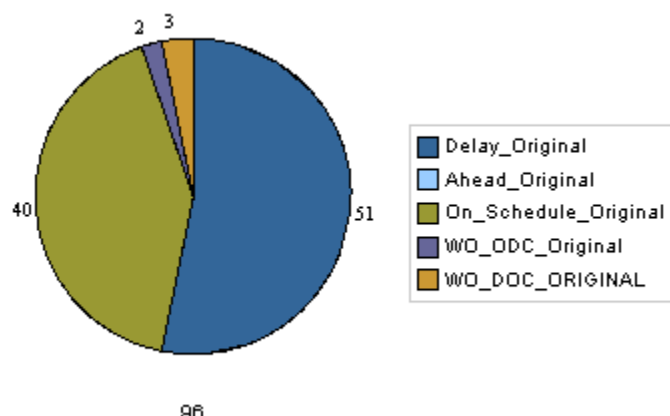

III. Investment Scenario

The Total Original cost of implementation of 96 projects when sanctioned, was of the order of Rs. 203091.86 crore but this was subsequently revised to Rs. 216802.42 crore implying a cost overrun of 6.8%. The expenditure incurred on these projects till June, 2012 is Rs. 103013.01 crore, which is 47.5% of the revised cost of the projects.

Figures are in Rs. Crore

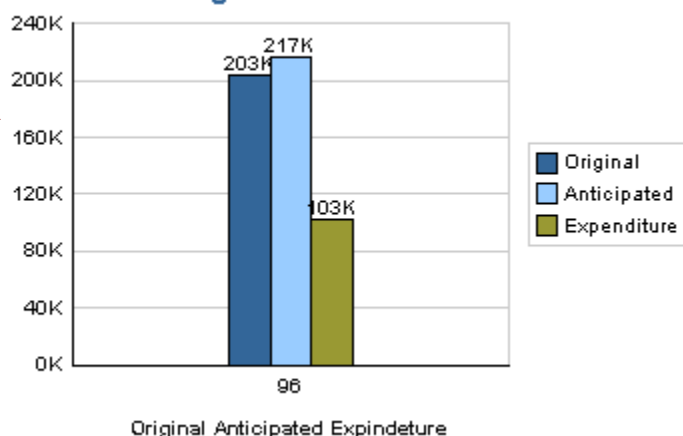

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	65
Number of Projects On Schedule	20
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 65 projects, 20 projects are on schedule and 39 projects are delayed .2 projects do not have fixed dates of commissioning.4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

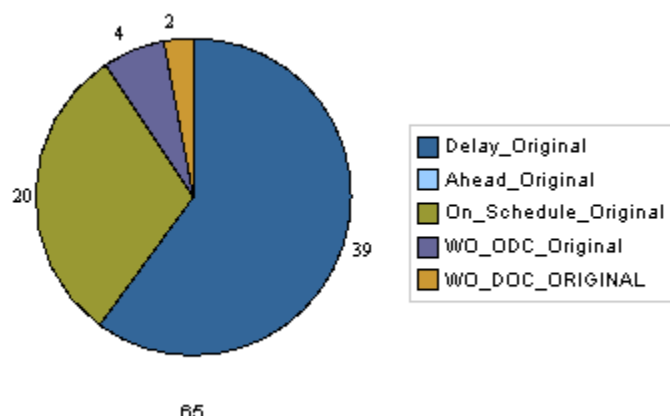

III. Investment Scenario

The Total Original cost of implementation of 65 projects when sanctioned, was of the order of Rs. 156993.49 crore but this was subsequently revised to Rs. 165177.98 crore implying a cost overrun of 5.2%. The expenditure incurred on these projects till June, 2012 is Rs. 73785.97 crore, which is 44.7% of the revised cost of the projects.

Figures are in Rs. Crore

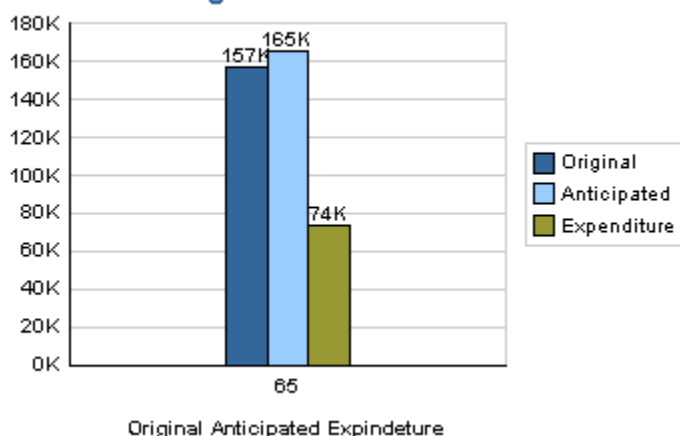

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	16
Number of Projects On Schedule	1
Number of Projects Delayed	7
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 1 project are ahead of schedule, 1 project are on schedule and 7 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

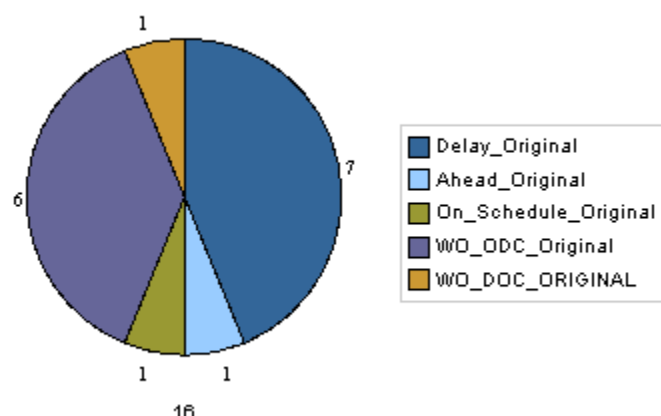

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 50110.22 crore but this was subsequently revised to Rs. 71356.76 crore implying a cost overrun of 42.4%. The expenditure incurred on these projects till June, 2012 is Rs. 35770.64 crore, which is 50.1% of the revised cost of the projects.

Figures are in Rs. Crore

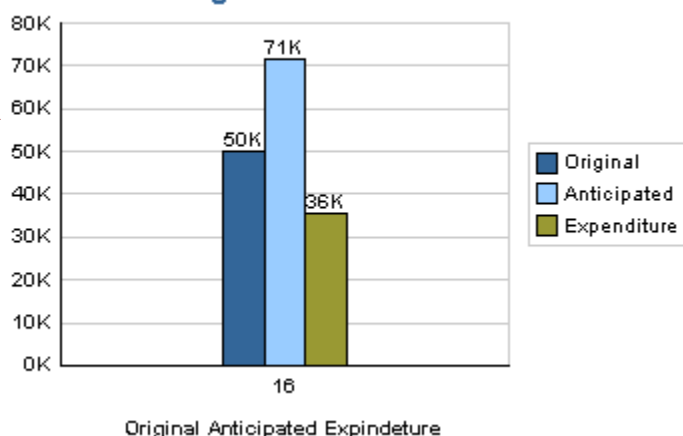

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	3
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

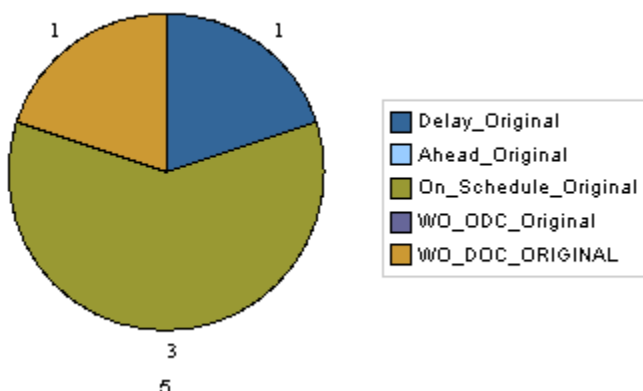

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4828.66 crore but this was subsequently revised to Rs. 4828.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till June, 2012 is Rs. 2453.98 crore, which is 50.8% of the revised cost of the projects.

Figures are in Rs. Crore

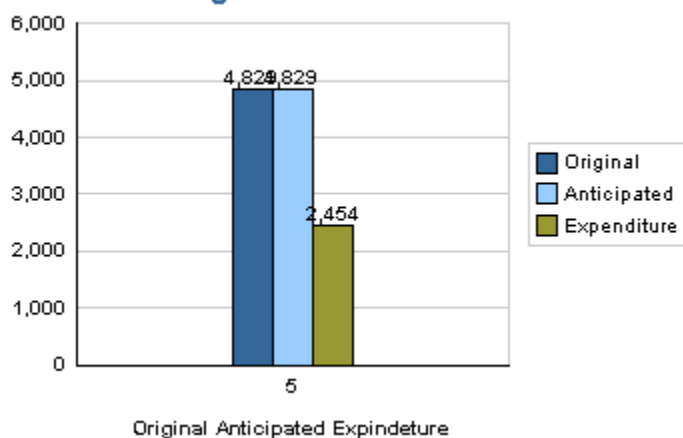

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	52
Number of Projects On Schedule	24
Number of Projects Delayed	27

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 52 projects, 24 projects are on schedule and 27 projects are delayed .1 project do not have fixed dates of commissioning.

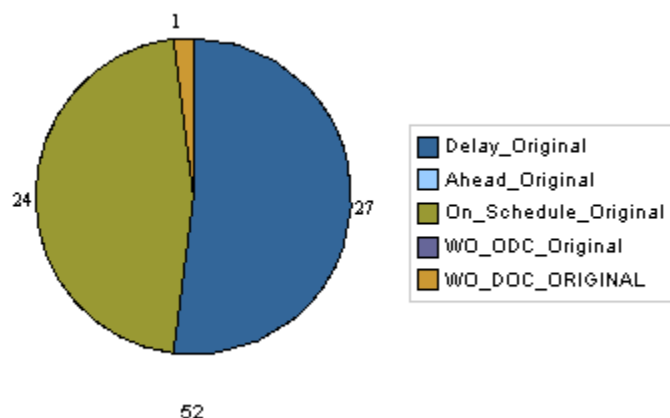

III. Investment Scenario

The Total Original cost of implementation of 52 projects when sanctioned, was of the order of Rs. 33950.69 crore but this was subsequently revised to Rs. 37570.81 crore implying a cost overrun of 10.7%. The expenditure incurred on these projects till June, 2012 is Rs. 11622.74 crore, which is 30.9% of the revised cost of the projects.

Figures are in Rs. Crore

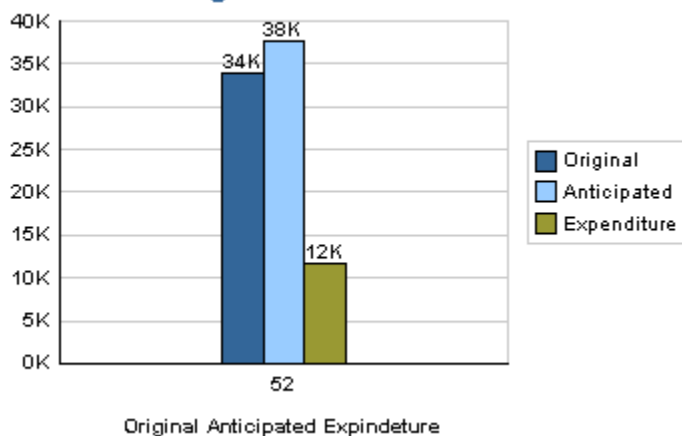

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

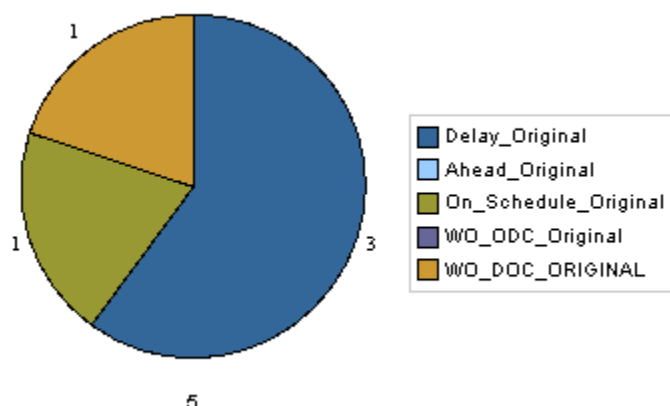

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till June, 2012 is Rs. 4322.91 crore, which is 77% of the revised cost of the projects.

Figures are in Rs. Crore

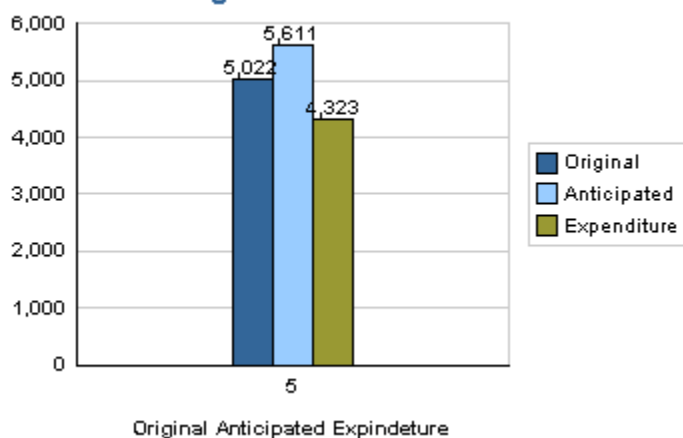

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

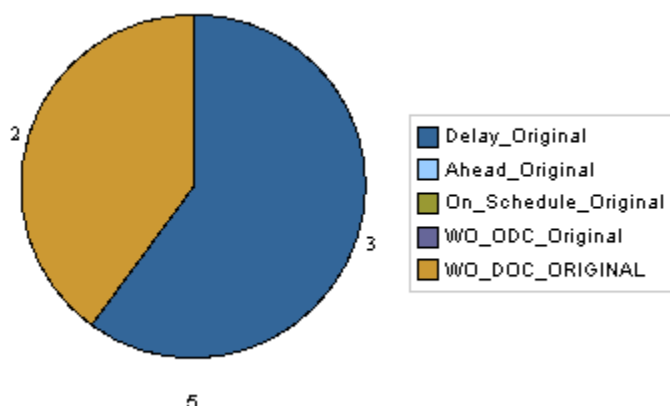

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till June, 2012 is Rs. 22351.84 crore, which is 46.7% of the revised cost of the projects.

Figures are in Rs. Crore

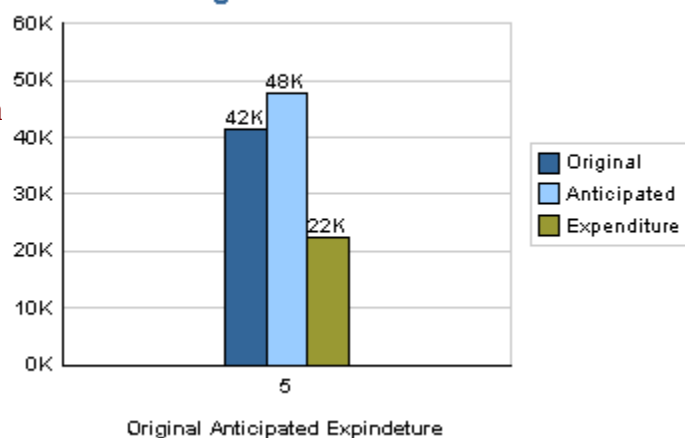

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

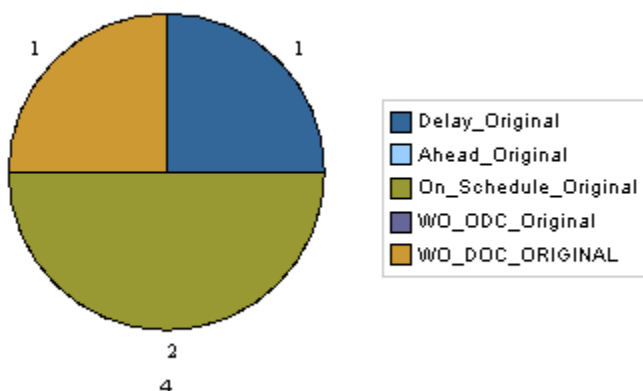

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till June, 2012 is Rs. 2639.28 crore, which is 5.3% of the revised cost of the projects.

Figures are in Rs. Crore

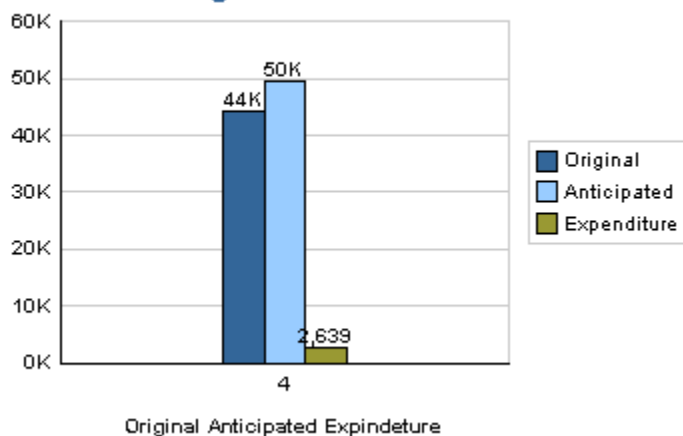

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31031.62	38459.02	21526.46
2	Arunachal Pr.	4	9512.22	14153.62	8167.54
3	Assam	36	22463.87	33865.52	21149.49
4	Bihar	29	26796.45	31471.73	20119.04
5	Chhatisgarh	26	40960.25	56580.22	15030.30
6	Delhi	3	37985.00	37965.41	438.91
7	Goa	1	335.61	335.61	122.40
8	Gujarat	23	31308.52	31536.52	6652.09
9	Haryana	9	5306.60	7177.17	7233.69
10	Himachal Pr.	5	13355.57	15213.42	12032.84
11	J and K	11	15120.05	34993.86	12904.84
12	Jharkhandd	23	11785.48	16601.53	7611.62
13	Karnataka	23	29468.64	37913.46	18104.02
14	Kerala	5	5469.67	6911.22	4854.08
15	Madhya pradesh	23	16561.52	16855.99	8438.61
16	Maharashtra	50	78266.29	93478.43	47572.51
17	Manipur	1	727.56	4444.00	797.35
18	Meghalaya	2	762.00	762.00	575.86
19	Mizoram	2	1532.97	3307.11	339.34
20	Multi State	104	137462.21	142739.67	58019.36
21	Nagaland	1	850.00	850.00	8.44
22	Orissa	30	57405.36	61206.54	30191.73
23	Punjab	6	4384.20	5325.97	3711.70
24	Rajasthan	14	26544.10	26138.31	8320.74
25	Sikkim	2	1648.94	3690.04	235.61
26	Tamil Nadu	32	51275.95	61960.82	38007.93
27	Tripura	3	1522.39	2053.23	800.60
28	Uttar Pradesh	23	18321.94	22159.71	11075.37
29	Uttaranchal	3	5619.21	6559.64	1859.09
30	West Bengal	25	40187.77	52557.13	25639.86
TOTAL		555	723971.96	867266.90	391541.42

LIST OF PROJECTS IN WHICH EXPENDITURE MORE THAN COST as on 30-06-2012

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	BHAVNI	3492.00	0.00	3641.60
2	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14798.00
3	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT	Civil Aviation	AAI	1942.51	0.00	1999.95
4	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Petroleum	HPCL	224.00	299.00	331.64
5	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	HPCL	756.00	0.00	857.41
6	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1518.60
7	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	NHPC	1061.38	0.00	1149.76
8	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	0.00	326.43
9	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	765.72
10	CHUTAK HYDRO-ELECTRIC PROJECT	Power	NHPC	621.26	0.00	743.22
11	URI H.E.P STAGE -II (NHPC)	Power	NHPC	1729.29	0.00	1744.34
12	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	NCR	158.77	432.46	558.07
13	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	600.41
14	KARUR-SALEM(NL),SR	Railways	SR	155.55	229.88	724.88
15	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	ECR	491.19	1099.20	1261.28
16	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	248.44	576.27	877.21
17	BILASPUR-URKURA (DL)	Railways	RVNL	151.52	0.00	319.07
18	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	RVNL	136.62	0.00	223.67
19	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	NEFR	733.00	0.00	1141.55
20	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
21	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	233.00	501.69	641.56
22	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	NEFR	1000.00	1500.00	2408.10
23	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	408.37
24	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	100.00	142.98	201.64
25	MANSI-PURNIA (EXTENSION OF MANSI SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	384.07
26	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	519.00
27	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	RVNL	240.00	0.00	390.18
28	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	(NR)	409.00	625.30	833.20
29	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	(NR)	2500.00	0.00	7947.68
30	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	488.98
31	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	NER	395.00	1062.36	1299.58

32	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	3083.48
33	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	240.93
34	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	391.98
35	PATNA GANGA BRIDGE (NL), ECR	Railways	ECR	624.47	1389.98	1445.12
36	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	NEFR	727.56	0.00	797.35
37	RAJPIPLA-ANKELASHWAR, WR (GC)	Railways	WR	196.97	0.00	218.04
38	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	523.76
39	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	495.68	568.11
40	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	497.68
41	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	496.59
42	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	341.37
43	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	292.01
44	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	429.49	613.36
45	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
46	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	343.10
47	RAJATGARH-BARANG(LD),ECOR	Railways	RVNL	166.16	0.00	248.61
48	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	486.96
49	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	NEFR	915.70	0.00	1190.08
50	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	728.94
51	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	548.53
52	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	260.76
53	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	414.03
54	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.56
55	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	198.29
56	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
57	JAIPUR-REENGUS	Road Transport & Highways	NHAI	267.81	0.00	452.55
58	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	NHAI	671.00	0.00	737.54
59	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.92
60	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	663.32
61	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2649.60

62	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	NHAI	1673.70	0.00	2488.40
63	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	760.07
64	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.49
65	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
66	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	792.06	0.00	1214.20
67	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	1038.80
68	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	NHAI	237.80	0.00	243.92
69	ROHTAK-BAWAL	Road Transport & Highways	NHAI	650.00	0.00	734.10
70	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	1008.50	0.00	1097.80
71	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	NHAI	946.00	0.00	1394.40
72	Pune-sholapur, pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1906.80
73	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	940.00	0.00	1141.10
74	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	835.00	0.00	1068.70
75	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	779.14
76	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	256.42
77	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	NHAI	464.00	0.00	535.16
78	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	NHAI	263.27	0.00	265.81
79	INDORE-DEWAS(NH-3)	Road Transport & Highways	NHAI	325.00	0.00	369.11
80	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	NHAI	198.16	0.00	204.40

81	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	NHAI	1740.00	0.00	1744.70
82	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	3459.20
83	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	1003.30
84	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	506.40
85	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	457.30
86	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	NHAI	232.45	0.00	252.87
87	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	NHAI	300.93	0.00	302.72
88	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	631.65
89	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	255.82
90	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	231.38
91	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	187.27
92	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	NHAI	355.06	0.00	468.34
93	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	279.34
94	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	379.89
95	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	521.77
96	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	281.86
97	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	NHAI	195.00	0.00	201.47
98	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	273.71
99	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	NHAI	225.00	0.00	231.87

100	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	262.54
101	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	491.21
102	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	NHAI	200.00	0.00	227.95
103	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	NHAI	264.72	0.00	266.72
104	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	NHAI	332.94	0.00	371.68
105	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	303.96
106	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	278.06
107	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	NHAI	160.00	0.00	172.56
108	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	578.08
109	GARH Mukteswar-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	304.29
110	HAPUR-GARH Mukteswar (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	273.84
111	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	298.17	326.08
112	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	RINL	230.00	0.00	247.54

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065]	9/2008	626.00 -	626.00	349.04	06/2013 -	06/2013
	Total		626.00 -	626.00	349.04		
	<u>Coal</u>						
2	Purnadih OCP - [N06000085]	7/2008	210.98 -	210.98	33.74	03/2013 -	03/2013
3	KARMA OCP - [N06000088]	6/2009	162.46 -	162.46	30.55	03/2014 -	03/2014
4	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
5	JALLARAM SHAFT PROJECT - [N06000025]	9/2007	467.78 -	467.78	-	03/2013 -	03/2013
6	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	6/2006	737.65 -	1,188.31	644.50	03/2013 03/2013	03/2013
7	Rajrappa RCE OCP - [N06000087]	12/2009	510.85 -	510.85	266.45	03/2016 -	03/2016
8	MANIKPUR OC EXPANTION - [N06000081]	11/2009	321.42 -	321.50	203.55	03/2014 -	03/2014
9	GOPAL PRASAD OCP - [N06000042]	2/2008	395.87 -	395.87	70.56	03/2015 -	03/2015
10	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	475.93 -	479.63	100.15	03/2013 -	03/2013
11	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	-	03/2016 -	03/2016
12	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	-	03/2015 -	03/2015
13	JALAGAM VENGALA RAO OCP - [N06000094]	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
14	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]	6/2011	5,907.11 -	5,907.11	19.70	12/2015 -	12/2015
15	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
16	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
17	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	-	03/2015 -	03/2015
18	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	40.35	03/2014 03/2014	03/2014
19	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	84.57	03/2016 -	03/2016

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
20	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	111.38	03/2017 -	03/2017
21	KANIHA OCP, MCL, (10.0 Mty) - [N06000035	12/2007	457.77 -	457.77	119.67	03/2013 -	03/2013
22	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091	6/2011	1,131.28 -	1,131.28	-	03/2018 03/2018	03/2018
23	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
24	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	70.19	03/2016 -	03/2016
25	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
	Total		15,579.12 -	16,707.66	2,144.40		
	<u>Fertilisers</u>						
26	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT - [N08000005	1/2010	1,294.19 -	1,294.19	639.95	01/2013 -	01/2013
27	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT [N08000006	1/2010	1,478.63 -	1,478.63	718.00	01/2013 01/2013	01/2013
28	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT - [N08000004	1/2010	1,292.84 -	1,292.84	671.00	01/2013 -	01/2013
	Total		4,065.66 -	20,773.32	4,173.35		
	<u>Petrochemicals</u>						
29	Assam gas Cracker project - [N16000106	4/2006	5,460.61 -	8,920.00	4,657.21	12/2013 12/2013	12/2013
	Total		5,460.61 -	29,693.32	8,830.56		
	<u>Petroleum</u>						
30	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY [N16000069	3/2009	3,284.00 -	2,174.00	966.53	09/2012 09/2012	09/2012
31	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014
32	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	5.67	04/2015 -	04/2015
33	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127	6/2010	202.94 -	202.94	0.20	01/2014 -	01/2014
34	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107	7/2010	1,000.00 -	1,000.00	133.00	01/2013 -	01/2013

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	Construction of tanks and blending facility at Vadinar - [N16000115]	2/2009	267.00 -	267.00	198.44	09/2012 09/2012	09/2012
36	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	-	05/2014 -	05/2014
37	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
38	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
39	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015
40	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015
41	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	4/2008	825.00 -	1,827.00	611.55	04/2013 04/2013	04/2013
42	Integrated crude Oil handling facilities at Paradip(2nd SPM) - [N16000090]	12/2009	1,492.33 -	1,300.00	1,141.82	06/2012 06/2012	06/2012
43	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE [N16000088]	8/2009	1,793.00 -	1,400.00	647.04	09/2012 09/2012	09/2012
44	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108]	11/2009	341.50 -	341.50	89.83	02/2013 -	02/2013
45	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	756.65	5.73	05/2013 -	05/2013
46	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	1,292.50	02/2014 -	02/2014
47	Wax Project - [N16000101]	6/2010	576.60 -	576.60	47.04	12/2013 12/2013	12/2013
48	Development of WO-16 Cluster Fields - [N16000105]	6/2010	2,523.00 -	2,523.00	48.25	01/2014 -	01/2014
49	Ahmedabad Redevelopment - [N16000120]	11/2010	1,916.10 -	1,916.10	5.57	12/2014 -	12/2014
	Total		42,643.52 -	70,408.11	14,028.57		
	<u>Power</u>						
50	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT - [N18000046]	12/2008	7,031.88 -	7,031.88	3,674.80	12/2012 -	12/2012
51	Transmission system associated with krishnapatnam-Part-A - [N18000090]	12/2010	779.21 -	779.21	406.40	08/2013 -	08/2013
52	Transmission system for phase-I generation projects in orissa-part B - [N18000093]	12/2010	2,743.19 -	2,743.19	638.40	12/2013 -	12/2013
53	Transmission System for phase-1 generation projects in orissa - [N18000087]	9/2010	2,074.86 -	2,074.86	573.70	03/2013 -	03/2013

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]	10/2010	182.68 -	182.68	45.00	01/2013 -	01/2013
55	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]	12/2010	1,719.52 -	1,719.52	497.30	08/2013 -	08/2013
56	Transm System for development of Pooling strn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	255.10	01/2015 -	01/2015
57	Northern Region system strengthening scheme-XXII - [N18000091]	12/2010	209.78 -	209.78	61.10	08/2013 -	08/2013
58	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B [N18000099]	3/2011	1,585.12 -	1,585.12	295.80	11/2013 -	11/2013
59	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	156.00	12/2013 -	12/2013
60	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	203.20	09/2014 -	09/2014
61	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A - [N18000104]	10/2011	558.26 -	558.26	62.90	11/2013 -	11/2013
62	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]	7/2011	181.93 -	181.93	45.30	07/2013 -	07/2013
63	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A - [N18000113]	12/2011	2,422.66 -	2,422.66	72.60	08/2014 -	08/2014
64	Supplementary transmission associated with vellur TPS - [N18000097]	8/2010	170.36 -	170.36	38.20	04/2013 -	04/2013
65	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A [N18000098]	5/2010	250.03 -	250.03	51.40	01/2013 -	01/2013
66	Northern region system strengthening scheme XVI - [N18000094]	7/2010	752.64 -	752.64	173.00	07/2013 -	07/2013
67	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]	5/2011	1,961.87 -	1,961.87	318.10	05/2014 -	05/2014
68	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	17.30	10/2014 -	10/2014
69	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	1.40	08/2014 -	08/2014
70	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	93.20	02/2015 -	02/2015
71	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	14.60	01/2014 -	01/2014

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
72	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	95.30	01/2015 -	01/2015
73	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	47.90	08/2014 -	08/2014
74	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	21.80	08/2014 -	08/2014
75	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	38.50	02/2014 -	02/2014
76	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	183.50	07/2014 -	07/2014
77	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	190.40	08/2014 -	08/2014
78	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000110]	8/2011	1,391.97 -	1,391.97	182.10	12/2013 -	12/2013
79	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	52.00	06/2014 -	06/2014
80	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	214.90	12/2013 -	12/2013
81	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	65.30	10/2013 -	10/2013
82	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	-	11/2014 -	11/2014
83	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	-	10/2014 -	10/2014
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	40.40	11/2014 -	11/2014
85	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	52.80	08/2014 -	08/2014
86	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	21.90	06/2014 -	06/2014
87	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	18.60	06/2015 -	06/2015
88	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS ASSOCIATED WITH SYSTEM STRENGTHENING COMMO - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
89	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
	Total		61,916.42 -	132,324.53	22,948.77		
	<u>Railways</u>						
90	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	4/2010	2,619.02 -	2,913.51	135.97	03/2016 -	03/2016
91	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	4/2006	850.00 -	850.00	8.44	03/2015 -	03/2015
92	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	4/2008	653.19 -	653.46	107.79	03/2014 -	03/2014
93	AGARTALA SABROOM, NL, NEFR - [N22000099]	4/2008	813.34 -	1,141.75	356.57	03/2014 -	03/2014
94	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114]	4/2008	516.23 -	516.23	200.11	03/2014 -	03/2014
95	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110]	4/2010	3,951.98 -	3,951.98	16.68	03/2016 -	03/2016
96	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	4/2008	394.14 -	394.14	0.49	03/2013 -	03/2013
97	NANGALDAM-TALWARA(NL),NR - [220100188]	3/1981	37.68 -	730.00	-	07/2012 07/2012	07/2012
98	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]	4/2008	829.74 -	829.74	4.59	03/2015 -	03/2015
99	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
	Total		12,004.80 -	147,685.92	23,832.04		
	<u>Road Transport & Highways</u>						
100	Talegaon-amravati - [N24000140]	11/2009	567.00 -	567.00	471.21	11/2013 -	11/2013
101	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]	2/2011	193.45 -	193.45	29.71	11/2012 -	11/2012
102	MURADABAD-BAREILY - [N24000154]	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013
103	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	874.76	03/2013 -	03/2013
104	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]	11/2010	1,585.00 -	1,585.00	957.76	05/2013 -	05/2013
105	Hazaribagh-Ranchi - [N24000141]	8/2010	625.07 -	625.07	779.14	01/2013 -	01/2013

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
106	Jaipur-Tonk-Deoli - [N24000135]	6/2010	792.06 -	792.06	1,214.20	12/2012 -	12/2012
107	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
108	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	366.62	07/2013 -	07/2013
109	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	20.75	04/2014 -	04/2014
110	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	66.26	03/2014 -	03/2014
111	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
112	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	497.30	03/2014 -	03/2014
113	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	199.49	02/2014 -	02/2014
114	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	376.37	01/2014 -	01/2014
115	Kandla - Mundra port - [N24000175]	1/2011	953.88 -	953.88	314.98	07/2013 -	07/2013
116	JAIPUR-REENGUS - [N24000198]	8/2010	267.81 -	267.81	452.55	02/2013 -	02/2013
117	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	120.31	09/2014 -	09/2014
118	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196]	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
119	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	329.47	08/2013 -	08/2013
120	NIROLI-ROXY-RAJAMUNDA - [N24000194]	7/2011	586.00 -	586.00	162.45	01/2014 -	01/2014
121	PUNE-SHOLAPUR,Pkg-II - [N24000193]	9/2011	835.00 -	835.00	-	01/2014 -	01/2014
122	4-laning of Barhi-Hazaribagh - [N24000191]	2/2012	398.00 -	398.00	150.00	02/2014 -	02/2014
123	2laning with PS Gopalganj-Chappra - [N24000190]	12/2011	325.00 -	325.00	115.63	05/2014 -	05/2014
124	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
125	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]	12/2011	1,047.00 -	1,047.00	148.11	06/2014 -	06/2014
126	4-laning of Raiganj-Dalkola - [N24000204]	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
127	4-laning of Brahampore-Faraka - [N24000203]	2/2011	998.79 -	998.79	498.45	08/2013 -	08/2013
128	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84 -	1,078.84	594.39	08/2013 -	08/2013

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	MUZAFFARNAGAR-HARIDWAR - [N24000201	9/2011	754.00 -	754.00	335.29	03/2013 -	03/2013
130	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	87.11	09/2013 -	09/2013
131	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	155.04	06/2014 -	06/2014
132	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
133	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
134	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	4.93	12/2013 -	12/2013
135	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
136	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	662.22	08/2013 -	08/2013
137	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	734.10	11/2013 -	11/2013
138	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168	3/2011	785.50 -	785.50	507.92	08/2013 -	08/2013
139	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013
140	SAMAIKHIALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	228.54	03/2013 -	03/2013
141	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
142	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	56.11	08/2013 -	08/2013
143	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	55.89	05/2013 -	05/2013
144	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	580.92	02/2013 -	02/2013
145	NASHRI CHANANI - [N24000162	6/2010	2,159.00 -	2,159.00	-	06/2015 -	06/2015
146	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161	7/2010	1,987.00 -	1,987.00	-	07/2015 -	07/2015
147	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	393.71	09/2013 -	09/2013
148	Indore-Jhabua-Gujrat/MP - [N24000136	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
149	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125	3/2010	1,509.10 -	1,509.10	1,299.10	09/2012 -	09/2012
150	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM - [N24000144	9/2010	852.00 -	852.00	634.99	03/2013 -	03/2013

List of On schedule Projects

(Jun,2012)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
151	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	364.02	08/2014 -	08/2014
152	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	797.01	10/2014 -	10/2014
153	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]	4/2010	1,740.00 -	1,740.00	1,744.70	10/2012 -	10/2012
154	DEOLI-KOTA - [N24000148]	1/2011	953.00 -	593.00	339.12	07/2013 -	07/2013
	Total		53,837.59 -	201,163.51	46,146.34		
	<u>Shipping & Ports</u>						
155	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS - [N25000031]	8/2008	1,066.91 -	968.35	501.89	09/2012 -	09/2012
156	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052]	10/2010	1,028.10 -	1,028.10	371.96	12/2013 -	12/2013
157	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014
	Total		3,061.47 -	204,154.78	47,210.11		
	<u>Steel</u>						
158	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	8/2007	108.00 -	216.68	91.25	10/2012 10/2012	10/2012
	Total		108.00 -	204,371.46	47,301.36		
	<u>Urban Development</u>						
159	DELHI MRTS PHASE-III - [N28000056]	9/2011	35,242.00 -	35,242.00	345.26	03/2016 -	03/2016
160	FARIDABAD EXTENSION - [N28000057]	9/2011	2,494.00 -	2,494.00	26.45	09/2014 -	09/2014
	Total		37,736.00 -	242,107.46	47,673.07		
	Grand Total		237,039.19	1,270,016.07	264,637.61		

List of project Without Original Date of Commissioning

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Steel</u>									
1	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	3,316.00	6,325.00	2,758.59	-	10/2012	-	3/16
2	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	13,470.28	-	12/2012	-	10/19
3	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	137.92	-	04/2013	-	1/19
4	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	80.90	-	05/2013	-	14/21
5	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	5,185.00	17,265.00	-	-	09/2013	-	9/27
6	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL,Orissa	11/2011	254.55	254.55	6.32	-	03/2014	-	0/1
Total			24,669.10	41,723.10	16,454.01				37/103
<u>Petroleum</u>									
7	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	898.00	857.41	-	08/2012	-	0/53
8	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,908.40	-	08/2012	-	116/116
9	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68	276.00	180.54	-	09/2012	-	1/1
10	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	148.03	-	09/2012	-	28/36
Total			3,944.36	4,123.68	3,094.38				145/206
<u>Power</u>									
11	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	295.71	-	07/2013	0(R3)	3/29
12	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,168.00	-	11/2014	-	4/28
Total			4,796.36	4,998.79	3,463.71				7/57
<u>Railways</u>									
13	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55	712.00	724.88	-	10/2012	-	0/0
14	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	519.00	-	12/2012	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
15	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	496.59	- -	01/2013	-	0/0
16	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	158.62	- -	02/2013	-	0/0
17	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,200.00	165.33	- -	03/2013	-	0/0
18	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	184.87	- -	03/2013	-	0/0
19	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	90.86	- -	03/2013	-	0/0
20	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	741.64	- -	03/2013	-	0/0
21	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	208.82	- -	03/2013	-	0/0
22	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	1,190.08	- -	03/2013	-	0/0
23	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	112.49	- -	03/2013	-	0/0
24	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
25	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	750.89	488.98	- -	03/2014	-	0/1
26	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	145.31	- -	03/2014	-	0/0
27	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	385.20	100.31	- -	03/2014	-	0/0
28	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.01	- -	03/2015	-	0/0
29	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	178.54	- -	03/2015	-	0/0
30	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	-	0/0
	Total		5,654.70 -	13,544.50	5,944.46				0/1
<u>Road Transport & Highways</u>									
31	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
32	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
33	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	34.70	- -	04/2013	-	2/2
34	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	351.33	- -	06/2013	-	1/1

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
35	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	386.83	-	10/2013	-	2/2
36	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	97.49	-	12/2013	-	0/1
	Total		4,069.00	4,069.00	3,002.29				10/12
Grand Total			43,133.52	68,459.07	31,958.85				199/379

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	09/2010	01/2012
			-	-	
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	04/2012
			-	04/2011	
	Total		4,598.29		
			-		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	02/2012	
	Total		1,808.00		
			-		
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	03/2012
			-	-	
	Total		249.03		
			-		
<u>Fertilisers</u>					
5	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	04/2012
			-	-	
	Total		325.00		
			-		
<u>Steel</u>					
6	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	-	02/2012
			-	-	
	Total		500.90		
			-		
<u>Petroleum</u>					
7	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
			-	-	
8	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	-	08/2011
			299.00	08/2011	
	Total		1,808.00		
			-		
<u>Power</u>					
9	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	04/2012
			-	-	
10	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	12/2007	-
			1,007.16	12/2009	
11	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	09/2010	-
			-	-	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
	Total		1,350.75		
			-		
	<u>Railways</u>				
12	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 1,099.20	07/2005 -	07/2005
13	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
14	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
15	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
16	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
17	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 -	- 03/2010	03/2010
18	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010
19	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
20	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
21	REWARI-ROHTAK (NL), NR - [220100279](NR), Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
22	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
23	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR, Karnataka	04/1995	65.94 302.23	- -	03/2011
24	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
25	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
26	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
27	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
28	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011
29	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
30	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR, Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011
31	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
32	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011
33	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012
34	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
35	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
36	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
37	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
38	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012
39	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
40	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	03/2012
41	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
42	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
43	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
44	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012
45	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	06/2011 03/2012	03/2012
46	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
47	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
48	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	03/2012 -	03/2012
49	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012
50	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
51	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
52	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
53	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
54	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,045.20	- -	-
55	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
56	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	-
57	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
58	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
59	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-
60	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
61	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
62	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-
63	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
64	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
65	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
66	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 227.40	- -	-
67	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
	Total		18,750.10 -		
<u>Road Transport & Highways</u>					
68	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	05/2012
	Total		166.27 -		
<u>Shipping & Ports</u>					
69	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008
70	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
71	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
72	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	03/2012 -	03/2012
73	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	11/2010
	Total		3,904.91 -		
<u>Telecommunications</u>					
74	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
75	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
76	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
77	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
78	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
79	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
	Total		2,997.75 -		
<u>Urban Development</u>					
80	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
Grand Total			36,573.18		

List of Delay Project

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	14,798.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,761.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,067.00	12/2016	03/2017	3	-
Total			36,950.00	41,049.00	17,626.00				
<u>Civil Aviation</u>									
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	122.40	05/2012	08/2012	3	-
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,999.95	05/2011 03/2012	10/2012	17	7
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	182.98	01/2011 04/2013	04/2013	27	0
Total			2,587.58	2,970.07	2,305.33				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,427.49	06/2009	03/2013	45	-
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	04/2006	471.66 341.63	341.63	108.35	03/2011	03/2013	24	-
9	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	332.94	03/2010	03/2013	36	-
10	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	-	03/2012	03/2013	12	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19 -	-	03/2012 -	03/2013	12	-
12	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68 -	96.76	03/2012 -	03/2013	12	-
13	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96 -	93.78	03/2010 -	03/2014	48	-
14	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67 -	1,365.66	03/2010 -	03/2014	48	-
15	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66 -	1,163.52	03/2010 -	03/2014	48	-
16	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54 -	3,035.03	03/2012 -	03/2014	24	-
17	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82 -	-	03/2011 -	03/2014	36	-
18	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28 -	100.73	03/2012 -	03/2014	24	-
19	Churi Benti UG - [N06000083]CCL,Jharkhand	06/2007	163.51 -	163.51 -	34.01	03/2011 -	03/2014	36	-
20	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87 -	62.45	03/2012 -	03/2014	24	-
21	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	-	03/2013 09/2012	10/2014	19	25
22	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	161.87	03/2012 03/2015	03/2015	36	0
23	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17 -	-	03/2011 -	03/2015	48	-
24	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40 -	1.20	03/2012 -	03/2015	36	-
25	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08 -	103.13	03/2010 -	03/2015	60	-
26	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63 -	71.37	12/2012 -	03/2015	27	-

(Jun,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
27	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	338.98	03/2014 03/2016	03/2016	24	0
28	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	07/2006	469.78 -	706.40	18.16	07/2012 -	03/2016	44	-
29	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	261.91	03/2014 -	03/2016	24	-
30	BAROUD OC EXPANSION - [N06000065]SECL,Chhatisgarh	07/2008	135.58 -	258.56	39.29	03/2015 -	03/2016	12	-
31	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2016	24	-
32	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
33	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	9.93	03/2015 -	03/2017	24	-
Total			18,122.54 -	21,240.12	9,827.38				
<u>Fertilisers</u>									
34	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	239.93	07/2011 -	07/2012	12	-
Total			438.00 -	438.00	239.93				
<u>Steel</u>									
35	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	243.84	08/2010 08/2010	08/2012	24	24
36	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	247.54	02/2011 02/2011	09/2012	19	19
37	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	9,605.58	10/2009 10/2012	10/2012	36	0

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
38	Bailadila Iron Ore Deposit-IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	331.15	12/2011 03/2012	10/2012	10	7
39	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	204.03	05/2012 05/2012	02/2013	9	9
40	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	951.58	12/2012 -	03/2013	3	-
41	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	-	10/2013 -	12/2013	2	-
Total			13,020.22	17,104.08	11,583.72				
Petroleum									
42	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,525.33	05/2010 05/2012	07/2012	26	2
43	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	635.11	05/2010 04/2012	07/2012	26	3
44	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	227.95	04/2011 -	07/2012	15	-
45	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	194.79	03/2012 08/2012	08/2012	5	0
46	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,775.82	03/2012 08/2012	08/2012	5	0
47	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	213.91	03/2012 03/2012	08/2012	5	5
48	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	719.92	04/2011 12/2011	09/2012	17	9
49	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,277.45	09/2011 03/2012	09/2012	12	6

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
50	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,763.03	01/2012 -	09/2012	8	-
51	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	549.84	03/2011 05/2011	10/2012	19	17
52	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	584.47	07/2012 -	10/2012	3	-
53	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	12/2012	80	6
54	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,017.31	06/2012 -	12/2012	6	-
55	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	148.32	08/2012 -	12/2012	4	-
56	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	40.21	09/2012 -	12/2012	3	-
57	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	362.81	12/2011 -	01/2013	13	-
58	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	265.66	03/2006 03/2013	03/2013	84	0
59	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,987.33	05/2010 03/2013	03/2013	34	0
60	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	247.03	07/2012 07/2012	03/2013	8	8
61	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
62	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,279.74	09/2010 03/2012	04/2013	31	13
63	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	49.65	03/2013 -	04/2013	1	-
64	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	04/2013	10	-

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
65	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	2,915.00	987.59	12/2012 12/2012	04/2013	4	4
66	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	479.11	03/2010 03/2012	05/2013	38	14
67	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	837.12	07/2010 05/2012	05/2013	34	12
68	PARADIP REFINERY PROJECT - [N16000058]IOCL, Orissa	02/2009	29,777.00 -	30,426.00	16,295.00	11/2012 -	06/2013	7	-
69	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	287.21	09/2011 -	08/2013	23	-
70	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	3,896.72	09/2012 -	09/2013	12	-
71	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	7.33	11/2012 -	10/2013	11	-
72	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
73	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,596.34	08/2010 03/2012	12/2013	40	21
74	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
75	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC, Assam	09/2001	345.10 663.69	663.69	594.10	03/2007 03/2014	03/2014	84	0
76	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	819.82	03/2013 -	03/2014	12	-
77	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 -	3,241.03	288.30	03/2013 -	04/2014	13	-
78	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	3.48	10/2010 -	12/2014	50	-

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
79	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.20	01/2013	07/2015	30	-
80	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,481.56	03/2007 03/2017	03/2017	120	0
	Total		108,597.61	118,456.51	65,146.47				
	Power								
81	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	8,230.00	12/2009 12/2011	06/2012	30	6
82	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	112.31	02/2012 02/2012	07/2012	5	5
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	183.20	11/2011 11/2011	07/2012	8	8
84	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	133.30	07/2011	08/2012	13	-
85	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	96.08	06/2012	08/2012	2	-
86	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.91	326.43	07/2011	09/2012	14	-
87	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	913.00	743.22	02/2011 10/2012	10/2012	20	0
88	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	1,042.40	02/2012	10/2012	8	-
89	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,518.60	03/2007 09/2012	12/2012	69	3

(Jun,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
90	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,825.01	09/2008 -	12/2012	51	-
91	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	862.00	10/2009 -	12/2012	38	-
92	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,133.60	07/2010 -	12/2012	29	-
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	-	11/2011 -	12/2012	13	-
94	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	952.10	06/2012 -	12/2012	6	-
95	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	601.60	05/2012 -	12/2012	7	-
96	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	723.80	08/2012 -	12/2012	4	-
97	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,853.81	10/2010 01/2013	01/2013	27	0
98	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	765.72	08/2010 01/2013	01/2013	29	0
99	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,083.00	1,744.34	11/2009 02/2013	02/2013	39	0
100	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	549.20	01/2010 -	02/2013	37	-
101	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,186.00	08/2012 -	03/2013	7	-

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	325.40	11/2011 -	03/2013	16	-
103	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	227.50	02/2012 -	03/2013	13	-
104	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	149.70	11/2011 -	03/2013	16	-
105	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,922.90	08/2012 -	03/2013	7	-
106	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,196.70	08/2012 -	03/2013	7	-
107	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,510.00	10/2012 -	03/2013	5	-
108	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,263.00	10/2012 -	03/2013	5	-
109	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	810.70	12/2012 -	03/2013	3	-
110	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	399.40	11/2012 -	03/2013	4	-
111	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	41.50	10/2012 -	03/2013	5	-
112	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,222.50	11/2012 -	06/2013	7	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
113	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,149.76	09/2009 06/2013	08/2013	47	2
114	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,827.31	01/2012 -	09/2013	20	-
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, Multi State	10/2008	4,824.12 -	4,824.12	2,738.40	10/2012 -	09/2013	11	-
116	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL, Multi State	07/2010	1,272.80 -	1,272.80	315.70	11/2012 -	09/2013	10	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL, Multi State	08/2010	1,677.57 -	1,677.57	443.90	04/2013 -	10/2013	6	-
118	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,322.00	04/2009 03/2014	03/2014	59	0
119	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25 -	2,569.25	474.50	03/2013 -	03/2014	12	-
120	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04 -	7,341.04	4,312.00	08/2013 -	06/2014	10	-
121	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]NEEPCO, Arunachal Pr.	12/2008	573.99 -	573.99	348.15	08/2012 09/2014	09/2014	25	0
122	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	4,595.90	08/2013 -	09/2014	13	-
123	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO, Mizoram	01/2011	913.63 -	913.63	334.77	07/2014 02/2015	02/2015	7	0
124	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttarakhand	11/2006	2,978.48 -	2,978.48	1,474.00	03/2013 -	09/2015	30	-
125	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	330.61	07/2010 02/2016	02/2016	67	0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
126	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	7,053.00	12/2009 12/2014	03/2016	75	15
127	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaran chal	08/2008	2,491.58 2,491.58	3,422.44	308.54	07/2014 -	05/2016	22	-
128	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,514.73	01/2016 01/2016	11/2016	10	10
129	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunacha I Pr.	09/2003	6,285.33 -	10,667.00	5,687.49	09/2010 08/2014	12/2016	75	28
130	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Aruna chal Pr.	12/2004	2,496.90 -	2,496.90	1,890.97	05/2013 03/2017	03/2017	46	0
131	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,480.52	09/2009 07/2014	12/2017	99	41
Total			135,028.33	148,125.75	89,254.27				
<u>Railways</u>									
132	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	218.04	03/2011 -	06/2012	15	-
133	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]JECR,Bihar	04/1997	233.00 501.69	1,043.56	641.56	03/2012 08/2012	08/2012	5	0
134	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	231.34	03/2012 03/2012	10/2012	7	7
135	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	292.01	06/2004 -	12/2012	102	-
136	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	414.03	03/2012 03/2012	12/2012	9	9
137	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]JECR,Bihar	04/2002	921.00 -	1,115.63	725.62	03/2009 12/2012	12/2012	45	0
138	PATNA GANGA BRIDGE (NL), ECR - [220100308]JECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,445.12	10/2007 12/2012	12/2012	62	0
139	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	595.56	03/2010 -	12/2012	33	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
140	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	877.21	12/2012 01/2013	01/2013	1	0
141	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.76	02/2011 02/2011	02/2013	24	24
142	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	381.76	12/2012 12/2012	02/2013	2	2
143	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	551.77	03/1995 -	03/2013	216	-
144	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	201.64	03/2002 -	03/2013	132	-
145	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	528.06	12/2011 12/2011	03/2013	15	15
146	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	264.07	03/2012 03/2013	03/2013	12	0
147	MANSI-PURNA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	384.07	03/2012 03/2013	03/2013	12	0
148	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	84.85	03/2012 -	03/2013	12	-
149	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	248.61	02/2009 02/2009	04/2013	50	50
150	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	206.19	03/2009 03/2009	04/2013	49	49
151	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	129.95	12/2012 -	05/2013	5	-
152	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	94.82	12/2011 11/2013	11/2013	23	0
153	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	39.12	02/2006 -	12/2013	94	-
154	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,073.53	3,083.48	03/2009 -	12/2013	57	-
155	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	189.02	03/2004 12/2010	03/2014	120	39

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
156	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.81	1,141.55	12/2008 -	03/2014	63	-
157	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	154.63	06/2013 06/2013	03/2014	9	9
158	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	329.78	03/2013 -	03/2014	12	-
159	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	105.81	12/2012 -	03/2014	15	-
160	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	820.40	150.01	03/2010 06/2014	06/2014	51	0
161	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	165.13	03/2007 03/2007	03/2015	96	96
162	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	728.94	12/2010 12/2010	03/2015	51	51
163	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.48	4.57	04/2014 -	03/2015	11	-
164	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,408.10	04/2008 03/2014	12/2015	92	21
165	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	212.25	02/2010 -	12/2015	70	-
166	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	4,444.00	797.35	03/2011 03/2014	03/2016	60	24
167	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	698.48	03/2014 03/2016	03/2016	24	0
168	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	27.66	03/2014 03/2016	03/2016	24	0
169	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	441.54	03/2005 12/2008	06/2016	135	90

(Jun,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Antici- pated Cost	Cumm. Expendi- ture	Original / Revised	Antici- pated		
1	2	3	4	5	6	7	8	9	
170	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	419.38	06/2005 07/2011	06/2016	132	59
171	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	22.34	03/2016 -	06/2016	3	-
172	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 -	20,000.00	7,947.68	03/2001 -	12/2017	201	-
Total			26,157.80 -	66,046.20	27,843.86				
<u>Road Transport & Highways</u>									
173	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	116.80	04/2004 -	07/2012	99	-
174	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	166.30	189.15	03/2008 -	07/2012	52	-
175	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	265.81	02/2004 -	07/2012	101	-
176	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	188.72	02/2004 -	07/2012	101	-
177	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	07/2012	5	-
178	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	179.10	08/2004 07/2010	08/2012	96	25
179	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	184.41	08/2004 -	08/2012	96	-
180	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	205.95	05/2008 -	08/2012	51	-
181	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	187.27	10/2008 -	08/2012	46	-
182	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	388.00	506.40	05/2012 -	08/2012	3	-

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
183	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	304.29	09/2007 -	09/2012	60	-
184	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	273.84	09/2007 -	09/2012	60	-
185	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	225.24	06/2005 -	09/2012	87	-
186	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.34	10/2008 -	09/2012	47	-
187	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	255.82	10/2008 -	09/2012	47	-
188	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	281.86	11/2008 -	09/2012	46	-
189	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,003.30	05/2012 -	09/2012	4	-
190	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,649.60	08/2011 -	09/2012	13	-
191	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	10/2012	91	-
192	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	185.64	06/2010 -	10/2012	28	-
193	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	10/2012	37	-
194	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	-
195	Pune-sholapur,pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,906.80	05/2012 -	10/2012	5	-

(Jun,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
196	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41	-
197	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	379.89	03/2008 -	12/2012	57	-
198	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	256.42	01/2009 -	12/2012	47	-
199	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	278.06	06/2008 -	12/2012	54	-
200	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	243.92	06/2008 -	12/2012	54	-
201	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	371.68	09/2008 -	12/2012	51	-
202	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	231.38	10/2008 -	12/2012	50	-
203	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	303.96	10/2008 -	12/2012	50	-
204	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	180.10	07/2008 -	12/2012	53	-
205	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	521.77	09/2008 -	12/2012	51	-
206	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	273.71	06/2008 -	12/2012	54	-
207	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	145.60	04/2008 -	12/2012	56	-
208	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	363.00	248.66	06/2011 06/2011	12/2012	18	18
209	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	204.40	04/2008 -	12/2012	56	-
210	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	262.54	04/2008 -	12/2012	56	-

(Jun, 2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
211	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055] NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	12/2012	48	-
212	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063] NHAI, Assam	12/2003	217.61 -	217.61	201.07	04/2010 -	12/2012	32	-
213	GWALIOR BYPASS, NH-75, 3 - [N24000088] NHAI, Madhya Pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38	-
214	GWALIOR-JHANSI, NH-75 - [N24000089] NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	12/2012	36	-
215	JHANSI TO LALITPUR, NH-25, 26 - [N24000096] NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	468.34	09/2009 -	12/2012	39	-
216	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108] NHAI, Multi State	12/2003	232.45 -	232.45	252.87	09/2010 -	12/2012	27	-
217	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118] NHAI, Chhatisgarh	01/2008	464.00 -	464.00	535.16	01/2011 -	12/2012	23	-
218	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122] NHAI, Haryana	04/2007	486.00 -	486.00	578.08	05/2010 -	12/2012	31	-
219	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123] NHAI, Maharashtra	03/2005	940.00 -	940.00	1,141.10	07/2012 -	12/2012	5	-
220	MP/Maharashtra Border-Dhula - [N24000126] NHAI, Maharashtra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	12/2012	6	-
221	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130] NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,488.40	10/2011 -	12/2012	14	-
222	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102] NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25	-
223	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207] NHAI, Assam	12/2003	157.47 -	154.57	198.29	09/2007 -	03/2013	66	-

(Jun,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
224	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	118.85	09/2008 -	03/2013	54	-
225	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	285.56	10/2008 -	03/2013	53	-
226	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	264.82	02/2009 -	03/2013	49	-
227	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	108.63	04/2009 -	03/2013	47	-
228	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	201.47	06/2008 -	03/2013	57	-
229	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	266.72	06/2008 -	03/2013	57	-
230	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60	-
231	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	231.87	06/2008 -	03/2013	57	-
232	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	172.56	05/2008 -	03/2013	58	-
233	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	227.95	06/2008 -	03/2013	57	-
234	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
235	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	162.31	09/2007 -	06/2013	69	-
236	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	663.32	10/2011 -	06/2013	20	-
237	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	1,038.80	11/2012 -	06/2013	7	-
238	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	3.77	01/2013 -	06/2013	5	-
239	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	56.76	04/2009 -	07/2013	51	-

(Jun,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
240	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	87.37	11/2008 -	07/2013	56	-
241	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,459.20	11/2011 -	08/2013	21	-
242	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-
243	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	15.49	11/2008 -	01/2014	62	-
244	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	369.11	05/2013 -	02/2014	9	-
245	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	170.23	10/2008 -	03/2014	65	-
246	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	339.37	10/2011 -	03/2014	29	-
247	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19	-
248	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	163.93	05/2013 -	03/2014	10	-
249	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	23.66	09/2007 -	04/2014	79	-
250	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	43.39	07/2009 -	04/2014	57	-
251	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	15.10	02/2014 -	04/2014	2	-
252	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
253	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANNING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	33.22	09/2013 -	07/2014	10	-
254	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
Total			33,091.24 -	35,142.74	36,323.16				

(Jun,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Shipping & Ports									
255	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	0
256	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 09/2012	09/2012	15	0
257	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18	0
258	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,345.60	01/2012 09/2012	10/2012	9	1
259	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
260	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
261	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	792.12	12/2010 09/2012	03/2013	27	6
262	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
263	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	187.07	12/2012 05/2013	05/2013	5	0
264	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 06/2013	06/2013	87	0
Total			8,446.14 -	10,038.71	5,138.36				
Telecommunications									
265	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39	-

(Jun, 2012)

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
266	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	250.00	80.47	12/2005 03/2008	07/2012	79	52	
267	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	175.52	60.84	12/2008 -	07/2012	43	-	
268	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	231.79	12/2008 -	09/2012	45	-	
269	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	09/2012	39	-	
270	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	09/2012	44	-	
271	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	804.06	11/2010 -	09/2012	22	-	
272	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.93	10/2010 12/2012	12/2012	26	0	
273	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11	
Total			3,163.25 -	3,167.12	1,665.40					
<u>Urban Development</u>										
274	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15	-	
Total			6,395.00 -	11,609.00	2,267.57					
<u>Water Resources</u>										
275	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-	
Total			542.90 -	1,187.00	35.49					
Grand Total			392,540.61	476,574.30	269,256.94					

List of Projects Without Milestones

(Jun,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011 04/2011	04/2012	0/0
	Total		1,106.29			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	08/2012	0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011 03/2012	10/2012	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
	Total		5,021.58			0/0
<u>Coal</u>						
7	KARMA OCP - [N06000088]JCL,Jharkhandd	06/2009	162.46	03/2014	03/2014	0/0
8	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	04/2014	04/2014	0/0
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	03/2012 03/2015	03/2015	0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	04/2015	04/2015	0/0
11	BAROUD OC EXPANSION - [N06000065]SECL,Chhatisgarh	07/2008	135.58	03/2015	03/2016	0/0
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	03/2016	03/2016	0/0
13	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		4,004.07			0/0
<u>Fertilisers</u>						
14	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	04/2012	0/0
15	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	07/2011	07/2012	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		763.00			0/0
			-			
	<u>Steel</u>					
16	INSTALLATION OF 1x 45MVA SAF AT CHANDRAPUR FERRO P - [N12000076]SAIL,Maharashtra	12/2011	187.33	10/2013	12/2013	0/0
			-	-		
	Total		187.33			0/0
			-			
	<u>Petroleum</u>					
17	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29	05/2010	07/2012	0/0
			6,326.40	05/2012		
18	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40	05/2010	07/2012	0/0
			837.54	04/2012		
19	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	04/2011	07/2012	0/0
			-	-		
20	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00	09/2011	09/2012	0/0
			2,730.00	03/2012		
21	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	01/2012	09/2012	0/0
			12,160.26	-		
22	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00	09/2012	09/2012	0/0
			-	09/2012		
23	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70	03/2011	10/2012	0/0
			755.76	05/2011		
24	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	07/2012	10/2012	0/0
			-	-		
25	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82	04/2006	12/2012	0/0
			2,735.65	06/2012		
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64	06/2012	12/2012	0/0
			-	-		
27	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04	08/2012	12/2012	0/0
			288.04	-		
28	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	09/2012	12/2012	0/0
			-	-		
29	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	12/2011	01/2013	0/0
			-	-		
30	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	05/2010	03/2013	0/0
			8,813.41	03/2013		
31	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	12/2008	04/2013	0/0
			3,690.37	04/2013		
32	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40	09/2010	04/2013	0/0
			2,920.82	03/2012		
33	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	03/2013	04/2013	0/0
			-	-		

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
34	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	04/2013	0/0
35	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
36	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
37	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
38	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
39	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
40	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
41	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
42	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
43	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
44	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
45	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
46	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
47	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
48	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
49	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	04/2014	0/0
50	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
51	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
52	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
53	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
54	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
55	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
56	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
57	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
58	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
59	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
60	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
Total			103,485.54 -			0/0
Power						
61	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	04/2012	0/0
62	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
63	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	08/2013	0/0
64	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013	0/0
65	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	12/2013	0/0
66	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
67	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
68	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
70	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0
71	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		11,091.73	-		0/0
	<u>Railways</u>					
72	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, Jharkhandd	03/1999	491.19 1,099.20	07/2005 -	07/2005	0/0
73	RUPSA-BANGRIPOSI (GC)(SER) - [220100323] SER, Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
74	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258] (NR), Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
75	MACHERLA-NALGONDA (NL)(SCR) - [220100220] SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
76	GULBARGA-BIDAR, SCR(NL) - [220100254] SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
77	KODERMA GIRIDH (NL), ECR - [220100306] ECR, Jharkhandd	04/1996	371.36 -	- 03/2010	03/2010	0/0
78	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268] MRTP, West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010	0/0
79	RAICHUR-GUNTAKAL (DL)(SCR) - [220100329] RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
80	Pandabeswar-Chinpa doubling (ER) - [N22000118] ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
81	REWARI-ROHTAK (NL), NR - [220100279] (NR), Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
82	AMRAVATI-NARKHER NL(CR) - [220100118] CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
83	KOTTUR-HARIHAR (NL), (SWR) - [220100212] SWR, Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
84	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232] NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
85	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243] NCR, Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
86	BILASPUR-URKURA (DL) - [220100321] RVNL, Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
87	PALWAL-BHUTESWAR 3RD LINE DOUBLING (NCR)(RVNL) - [N22000027] RVNL, Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
88	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082] NEFR, Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011	0/0
89	BARDHAMAN-KATWA (GC) - [N22000091] ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
90	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125] WR, Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011	0/0
91	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007] NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
92	HARIDASPUR-PARADEEP (NL) - [220100285] RVNL, Orissa	04/1996	301.64 1,185.00	- 09/2009	12/2011	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
93	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
94	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
95	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
96	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
97	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
98	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2012	0/0
99	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
100	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	03/2012	0/0
101	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
102	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
103	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
104	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
105	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	06/2011 03/2012	03/2012	0/0
106	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
107	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
108	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	03/2012 -	03/2012	0/0
109	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0
110	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012	0/0
111	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	06/2012	0/0
112	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
113	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	08/2012	0/0
114	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	10/2012	0/0
115	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	10/2012	0/0
116	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	06/2004 -	12/2012	0/0
117	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
118	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 12/2012	12/2012	0/0
119	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012	0/0
120	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
121	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	12/2012	0/0
122	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
123	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
124	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
125	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
126	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	02/2013	0/0
127	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
128	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2013	0/0
129	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
130	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	03/2013	0/0
131	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
132	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
133	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
134	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
135	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	03/2012 03/2013	03/2013	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
136	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013	0/0
137	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
138	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
139	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2013	0/0
140	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 -	03/2013 -	03/2013	0/0
141	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
142	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
143	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
144	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	05/2013	0/0
145	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
146	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
147	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	02/2006 -	12/2013	0/0
148	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013	0/0
149	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
150	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014	0/0
151	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	03/2014	0/0
152	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
153	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	03/2014	0/0
154	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014	0/0
155	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
156	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
157	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014	0/0
158	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	03/2014	0/0
159	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
160	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
161	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
162	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
163	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
164	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2015	0/0
165	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	03/2015	0/0
166	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	03/2015 -	03/2015	0/0
167	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	03/2015 -	03/2015	0/0
168	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
169	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015	0/0
170	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
171	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016	0/0
172	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
173	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
174	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
175	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	03/2016 -	03/2016	0/0
176	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
177	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
178	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
179	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 -	03/2001 -	12/2017	0/0
180	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
181	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
182	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
183	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
184	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 1,045.20	- -	-	0/0
185	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-	0/0
186	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	02/2015 -	-	0/0
187	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
188	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
189	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR, Bihar	09/2006	300.00 -	- -	-	0/0
190	VIRAMGAM-BHILDI(WR),GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
191	HUBLI-ANKOLA(NL),SWR - [220100193]SWR, Karnataka	04/1995	227.00 -	- -	-	0/0
192	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 -	- -	-	0/0
193	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 -	- -	-	0/0
194	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	- -	-	0/0
195	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR, Tamil Nadu	09/2007	404.19 -	- -	-	0/0
196	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, Tamil Nadu	09/2006	125.00 227.40	- -	-	0/0
197	TIDIVANAM-NAGARI (NL) - [N22000085]SR, Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
	Total		64,287.46 -			0/0

Road Transport & Highways

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
198	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	05/2012	0/0
199	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	07/2012	0/0
200	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09 -	03/2008 -	07/2012	0/0
201	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	07/2012	0/0
202	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	07/2012	0/0
203	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	07/2012	0/0
204	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	08/2012	0/0
205	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	08/2012	0/0
206	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	08/2012	0/0
207	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	10/2008 -	08/2012	0/0
208	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	05/2012 -	08/2012	0/0
209	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	09/2007 -	09/2012	0/0
210	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	09/2012	0/0
211	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	09/2012	0/0
212	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2012	0/0
213	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	09/2012	0/0
214	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	09/2012	0/0
215	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012	0/0
216	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	09/2012	0/0
217	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	09/2012	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
218	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	10/2012	0/0
219	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0
220	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	10/2012	0/0
221	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
222	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2012	0/0
223	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
224	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
225	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
226	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	12/2012	0/0
227	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2012	0/0
228	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	06/2008 -	12/2012	0/0
229	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
230	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
231	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
232	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
233	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
234	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	12/2012	0/0
235	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2012	0/0
236	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
237	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
238	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
239	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	12/2012	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
240	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
241	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
242	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2012	0/0
243	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2012	0/0
244	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
245	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	12/2012	0/0
246	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
247	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	12/2012	0/0
248	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	12/2012	0/0
249	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2012	0/0
250	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
251	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	01/2013	0/0
252	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	02/2013	0/0
253	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
254	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
255	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2013	0/0
256	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
257	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
258	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 -	03/2013	0/0
259	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
260	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2013	0/0
261	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2013	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
262	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	03/2013	0/0
263	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	03/2013	0/0
264	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
265	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
266	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
267	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
268	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
269	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
270	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	03/2013 -	03/2013	0/0
271	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
272	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
273	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
274	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	09/2007 -	06/2013	0/0
275	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
276	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
277	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
278	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
279	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
280	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	01/2013 -	06/2013	0/0
281	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
282	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
283	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
284	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
285	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
286	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
287	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
288	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
289	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
290	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29 -	08/2013 -	08/2013	0/0
291	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
292	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
293	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
294	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
295	BAREILLY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
296	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
297	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
298	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
299	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
300	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
301	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	12/2013	0/0
302	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
303	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
304	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014	0/0
305	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
306	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
307	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Orissa	07/2011	586.00 -	01/2014 -	01/2014	0/0
308	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
309	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
310	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhandd	02/2012	398.00 -	02/2014 -	02/2014	0/0
311	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	03/2014	0/0
312	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
313	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2014	0/0
314	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
315	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
316	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
317	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
318	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
319	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
320	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
321	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
322	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
323	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
324	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
325	SNG toBANL - [N24000189]NHAI,J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
326	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
327	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
328	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
329	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
330	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
331	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
332	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
333	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00	06/2015	06/2015	0/0
334	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	07/2015	07/2015	0/0
	Total		86,898.60			0/0
			-			
	Shipping & Ports					
335	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	10/2008	10/2008	0/0
336	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
337	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 252.00	03/2012	03/2012	0/0
338	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 08/2012	08/2012	0/0
339	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	09/2012	09/2012	0/0
340	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	06/2011 09/2012	09/2012	0/0
341	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	04/2011 10/2012	10/2012	0/0
342	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	10/2012	0/0
343	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	06/2010	11/2012	0/0
344	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	02/2011	12/2012	0/0
345	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2013	0/0
346	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	03/2011	03/2013	0/0
347	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00	05/2013	03/2013	0/0
348	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 05/2013	05/2013	0/0
349	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 600.00	03/2006 06/2013	06/2013	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
350	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013	0/0
351	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
352	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	11/2010	0/0
	Total		16,087.68 -			0/0
Telecommunications						
353	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
354	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	06/2012	0/0
355	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 03/2008	07/2012	0/0
356	NIB Project Capacity Expansion - [N26000098]BSNL,Multi State	06/2007	175.52 -	12/2008 -	07/2012	0/0
357	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	09/2012	0/0
358	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	09/2012	0/0
359	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	09/2012	0/0
360	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	09/2012	0/0
361	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 12/2012	12/2012	0/0
362	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2012	02/2013	0/0
363	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
364	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
365	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
366	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0

(Jun,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
367	Implementation of FTTH, the state of the art access, upon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
	Total		6,161.00 -			0/0
<u>Urban Development</u>						
368	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
369	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
370	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
<u>Water Resources</u>						
371	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			337,487.36			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
