

**332nd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
June 2013**



MUMBAI PORT - CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in Hindi	1 -9
Executive Summary in English	10-18
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	19-19
Summary of Projects	20-33
Trend and Graphical Analysis of Projects	34-46
Sector wise analysis of projects	47-47
List of All Ongoing Projects	48-77
Sector wise Graph	78-88
ANNEXURE	89-89
Central Sector Projects	90-90
List of Projects Having Expenditure More than cost	91-97
List of Projects Ahead of Schedule	98-98
List of Projects with out Original date of Commissioning	99-100
List of Projects with out date of Commissioning	101-106
List of On schedule Projects Original Schedule	107-115
List of Delayed Projects w.r.t Original and Revised	116-134
List of Projects Having cost overrun w.r.t original	135-146
List of Projects Having cost and time overrun w.r.t original	147-151
List of Projects without Milestones	152-168
List of Delayed Projects w.r.t Latest Schedule	169-190
List of On schedule Projects w.r.t. Latest Schedule	191-199

कार्यकारी सारांश

जून, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 573 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। जून, 2013 के दौरान रेलवे क्षेत्र की 2 परियोजनाओं के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 573 परियोजनाओं में से 275 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 53 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 53 परियोजनाओं में से, 21 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। परमाणु ऊर्जा, शहरी विकास, कोयला, रेलवे, इस्पात, विद्युत, पेट्रोलियम तथा सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 30 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	सड़क परिवहन एवं राजमार्ग	148	94	24	4
2.	रेलवे	127	32	3	1
3.	विद्युत	103	52	5	2
4.	पेट्रोलियम	74	42	15	9
5.	कोयला	55	28	1	1
6.	पोत परिवहन एवं पत्तन	19	2	0	0
7.	इस्पात	17	13	3	2
8.	दूरसंचार	13	5	0	0
9.	नागर विमानन	7	2	0	0
10.	परमाणु ऊर्जा	4	4	1	1
11.	शहरी विकास	4	1	1	1
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		573	275	53	21

3. 573 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग ` 7,98,677.21 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत ` 9,57,383.14 करोड़ रुपए होने की संभावना है जो 1,58,705.93 करोड़ (मूल लागत का 19.90%) की समग्र लागत वृद्धि को दर्शाता है। जून, 2013 तक इन परियोजनाओं पर किया गया व्यय ` 4,72,210.50 करोड़ है जो परियोजनाओं की अनुमानित लागत का 49.30% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (30.06.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (` करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची (30.06.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
3	सुबानश्री लोअर एचईपी (एनपीसीआईएल)	विद्युत	09/2003	6285.33	10667.00	4381.67
4	कुंडकुलम एपीपी (एनपीसीआईएल)	परमाणु ऊर्जा	12/2001	13171.00	17270.00	4099.00
5	बोगीबिल एंड लिंक लाईन पर ब्रह्मपुत्र पुल एनईएफआर	रेलवे	09/1997	1000.00	4996.65	3996.65

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 573 परियोजनाओं में से, 3 परियोजनाएं समय से पहले चल रही हैं, 156 समय पर तथा 275 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्या 286 तक और बढ़ जाती है यदि विलंब की गणना समापन की मूल समय-सारणी के आधार पर की जाती है । इसके अलावा, 17 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 122 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अंतरिम रूप से पूरा होने की अवधि सूचित की गई है । 275 विलंबित परियोजनाओं में से, 65 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 73 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 75 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 62 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (30.06.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएलए(एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
2	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	03/2013	132

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी मामले, उपस्करों की आपूर्ति में विलंब, उपस्कर संस्थापना में विलंब, निधि संबंधी बाधाएं, भू वैज्ञानिक गतिविधियां, कुशल जनशक्ति की कमी, सिविल कार्य में विलंब, कार्य-क्षेत्र में वृद्धि, राज्य सरकार द्वारा जनोपयोगी सेवाओं को अन्यत्र ले जाने में विलंब तथा बोलियों के खोलने और मूल्यांकन करने में विलंब, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति आदि शामिल हैं ।

7. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (30.06.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (30.06.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (30.06.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल),	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

	(एसडब्ल्यूआर)					
--	---------------	--	--	--	--	--

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

एन.आर.: सूचित नहीं।

9. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- I. **कोयला क्षेत्र** में 55 परियोजनाओं में से 28 परियोजनाएं विलंबित हैं। माह के दौरान, 'नेयवेली न्यू थर्मल पावर प्रोजेक्ट (2X600 मेगावाट), एनएलसी' (मेगा परियोजना) के संबंध में बोली खोलने तथा मूल्यांकन करने में विलंब के कारण 2 माह के अतिरिक्त विलंब की सूचना दी गई है।
- II. **परमाणु ऊर्जा क्षेत्र** में सभी 5 परियोजनाएं विलंबित हैं। माह के दौरान, "कुंदनकुलम एपीपी", एनपीसीआईएल' (मेगा परियोजना) के संबंध में उपस्करों की आपूर्ति तथा संस्थापन में विलंब के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।
- III. **शहरी विकास क्षेत्र** में 4 परियोजनाओं में से 1 परियोजना विलंबित है। माह के दौरान, 'फरीदाबाद विस्तार डीएमआरसी' (मेगा परियोजना) परियोजना के संबंध में 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इस योजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।
- IV **रेलवे क्षेत्र** में 127 परियोजनाओं में से 32 परियोजनाएं विलंबित हैं। माह के दौरान, 3 परियोजनाओं के संबंध में 6-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'हरमाती से ईटानगर/एनएआर, एनईएफआर' तक नई लाइन का निर्माण, एनईएफआर' परियोजना के संबंध में निधि की कमी के कारण 6 माह के अतिरिक्त विलंब की सूचना दी गई है; 'बाडानगर से बैरकपुर तथा दक्षिणेश्वर तक मेट्रो रेलवे के निर्माण के लिए नए कार्य, आरवीएनएल' परियोजना में राज्य सरकार द्वारा जनोपयोगी सेवाओं के अंतरण में विलम्ब के कारण 24 माह के अतिरिक्त विलंब की सूचना दी गई है; तथा 'फ्रेट ऑपरेशन इन्फॉर्मेशन सिस्टम, एफओआईएस' परियोजना में 24 माह के अतिरिक्त विलंब की सूचना दी गई है (तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।
- V **इस्पात क्षेत्र** में 17 परियोजनाओं में से 14 परियोजनाएं विलंबित हैं। माह के दौरान 3 परियोजनाओं के संबंध में 1-6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 2 मेगा परियोजनाएं हैं। 'दुर्गापुर इस्पात संयंत्र का विस्तार, सेल' परियोजना के संबंध में कार्य के क्षेत्र में वृद्धि के कारण 3 माह के अतिरिक्त विलंब की सूचना दी गई है तथा '1X5 एमवीए सबमर्ज्ड

आर्क फर्नेस की संस्थापना, सेल' तथा 'भिलाई इस्पात संयंत्र का विस्तार सेल' के संबंध में क्रमशः 1 तथा 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

V. विद्युत क्षेत्र में, 103 परियोजनाओं में से 52 परियोजनाएं विलंबित हैं । माह के दौरान, 5 परियोजनाओं के संबंध में 1-10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 2 मेगा परियोजनाएं हैं । 'यूआरआई एच.ई.पी. चरण-II, एनएचपीसी' परियोजना के संबंध में झेलम नदी में बाढ़ के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; '400/220 के, पीजीसीआईएल की स्थापना के लिए पारेषण प्रणाली, पीजीसीआईएल' परियोजना के संबंध में वन संबंधी अनुमति में विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'तीस्ता लो डैम एचईपी, चरण-IV एनएचपीसी' परियोजना के संबंध में सिविल कार्यों में विलंब के 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 'पार्वती-III एचईपी से संबद्ध पारेषण प्रणाली, पीजीसीआईएल' तथा 'त्रिपुरा गैस बेस्ड पावर प्रोजेक्ट, एनईईपीसीओ' परियोजनाओं के संबंध में क्रमशः 1 तथा 10 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

VI. पट्रोलियम क्षेत्र में 74 परियोजनाओं में से 42 परियोजनाएं विलंबित हैं । माह के दौरान, 15 परियोजनाओं के संबंध में 1-30 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 9 मेगा परियोजनाएं हैं । 'पारादीप रिफाइनरी परियोजना, आईओसीएल' परियोजना के संबंध में स्थल पर कानून और व्यवस्था की समस्या एवं वन संबंधी अनुमति उपलब्ध न होने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, "उरान चाकन/शिक्रापुर एलपीजी, एचपीसीएल" परियोजना के संबंध में आरओयू मामलों के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'मुंबई हाई में ऑफशोर ग्रीड इंटरकनेक्टिविटी प्रोजेक्ट, ओएनजीसी' तथा 'बी-193 कलस्टर फील्ड का विकास, ओएनजीसी' के संबंध में क्रमशः संशोधित कार्य क्षेत्र तथा संविदा संबंधी मामलों के कारण प्रत्येक में 5 माह के अतिरिक्त विलंब की सूचना दी गई है; 'आईओआर रूद्रसागर, ओएनजीसी' तथा 'बीएचई और बीएच-35 एरिया का विकास, ओएनजीसी' परियोजनाओं के संबंध में क्रमशः कार्य क्षेत्र में वृद्धि एवं अच्छे प्लेटफार्म व पाइप लाइन के संस्थापन में विलंब के कारण प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'बी-46 कलस्टर फील्ड, ओएनजीसी' का विकास परियोजना के संबंध में कार्य प्रदान करने में विलंब तथा कुओं को ड्रिल करने में विलंब के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'सी-सीरिज फील्ड्स का विकास, ओएनजीसी', 'मुम्बई हाई साउथ रिडेवलपमेंट पीएच-2, ओएनजीसी', तथा 'अपग्रेडेशन ऑफ कोनावन जीएसएस एंड पाइप लाइन ग्रीड प्रोजेक्ट, ओएनजीसी' परियोजनाओं के संबंध में क्रमशः डेक के पुनर्निर्माण, पैकेजों के अलग हो जाने तथा आरओयू मामलों के कारण प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'डी-1 फील्ड का अतिरिक्त विकास, ओएनजीसी', के संबंध में उपस्करों की आपूर्ति में विलंब के कारण

11 माह के अतिरिक्त विलंब की सूचना दी गई है; '12 ऑफशोर सप्लाई वेसल्स (ओएसवी) का निर्माण, ओएनजीसी' परियोजना के संबंध में जनशक्ति में कमी के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'बी-22 कलस्टर फील्ड का विकास, ओएनजीसी' परियोजना के संबंध में भूवैज्ञानिक गतिविधियों के कारण 30 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'विशाख रिफाइनरी में डीजल हाइड्रोट्रीटर परियोजना, एचपीसीएल' एवं 'मुम्बई रिफाइनरी में डीजल हाइड्रोट्रीटर परियोजना' नामक परियोजनाओं के संबंध में क्रमशः 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

VII. सड़क परिवहन तथा राजमार्ग क्षेत्र में 148 परियोजनाओं में से 94 विलंबित हैं। माह के दौरान, 2 परियोजनाओं के संबंध में 1-20 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 4 मेगा परियोजनाएं हैं। 'तंजोर-त्रिची, एनएच-67. एनएचएआई' हुंगुंद-सूरतकल व मंगलौर-कर्नाटक/केरल सीमा, एनएचएआई' एवं 'देवीहल्ली-हसन एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'न्यू मंगलौर पोर्ट एनएच-17 तथा एनएच-48, एनएचएआई' 'पिपलगांव-नासिक-गोंडे, एनएच-3 (एनएचडीपी-चरण-III), एनएचएआई', 'जयपुर-टांक-देवली, एनएचएआई' तथा 'जयपुर-उदरबांद (चरण-II) एनएच-54, 309 कि.मी. से 275 किमी., एनएचएआई', 'धरमतुल से सोनापुर (एस-19), एनएचएआई', 'किशनगढ़-अजमेर-बैवर, एनएचएआई' तथा 'अहमदाबाद से गोधरा को 4 लाइन बनाना, एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'दिल्ली/हरियाणा सीमा के रोहतक, एनएचएआई', 'चेंगापल्ली से कोयम्बटूर बाईपास 102.035 किमी. से 144.740 किमी., एनएचएआई' एवं 'त्रिची बाईपास, एनएचएआई' परियोजनाओं के संबंध में क्रमशः 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'झांसी से ललितपुर, एनएच-25, एनएच-26, एनएचएआई', 'सूरत-दहीसार (6 लाइन) 263 किमी से 502 किमी, एनएचएआई', 'अमृतसर-पठानकोट, एनएचएआई', तथा 'चेन्नई को पर्याप्त सड़क कनेक्टिविटी का विकास, एनएचएआई', के संबंध में प्रत्येक के 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'धोलपुर-मोरेना खण्ड (चंबोल पुल सहित), एनएचएआई; परियोजना के संबंध में 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; 'राजमार्ग चौराहा से लखनन्दन, 297 किमी. से 351 किमी, एनएच-26, एनएचएआई' तथा 'मुरादाबाद-बरेली, एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है एवं 'चिल्कालुरीपेट-विजयवाड़ा 6 लेन (355 किमी. से 434.1 किमी.), एनएचएआई; 'पानीखोली-रिमोली, एनएचएआई तथा 'वालायार-वादक्कनचेरी खण्ड को चार लेन बनाना, एनएचएआई' परियोजनाओं के संबंध में क्रमशः 12, 13 तथा 20 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। परियोजना कार्यान्वयन एजेंसी ने इन परियोजनाओं में विलंब के लिए किसी विशेष कारण का कोई उल्लेख नहीं किया है। तथापि, इन परियोजनाओं में विलंब के सामान्य कारण-भूमि अधिग्रहण, वन तथा पर्यावरण संबंधी अनुमति में विलंब, जनोपयोगी सुविधाओं के अंतरण में विलंब, ठेकेदारों का घटिया कार्य निष्पादन, आदि हैं।

10. दिनांक 30.06.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में ` 150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।
11. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for June 2013 contains information on the status of the 573 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During June 2013, 2 projects of Railways sector have reported completion.

2. During the reference month, out of 573 projects, 275 projects are delayed with respect to latest schedule and 53 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 53 projects, 21 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 30 months in respect of projects relating to Atomic Energy, Urban Development, Coal, Railways, Steel, Power, Petroleum and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Road Transport & Highways	148	94	24	4
2.	Railways	127	32	3	1
3.	Power	103	52	5	2
4.	Petroleum	74	42	15	9
5.	Coal	55	28	1	1
6.	Shipping & Ports	19	2	0	0
7.	Steel	17	13	3	2
8.	Telecommunications	13	5	0	0
9.	Civil Aviation	7	2	0	0
10.	Atomic Energy	4	4	1	1
11.	Urban Development	4	1	1	1
12.	Petrochemicals	1	0	0	0
13.	Water Resources	1	0	0	0
Total		573	275	53	21

3. Total original cost of implementation of the 573 projects was about ₹ 7,98,677.21 crore and their anticipated completion cost is likely to be ₹ 9,57,383.14 crore, which reflects overall cost overruns of ₹ 1,58,705.93 crore (19.90 % of original cost). The expenditure incurred on these projects till June 2013 is ₹ 4,72,210.50 crore, which is 49.30 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 30-06 -2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 30-06-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 573 projects, 3 projects are ahead of schedule, 156 are on schedule and 275 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 286 if delay is calculated on the basis of original schedule of completion. Further, 17 projects have been sanctioned without any commissioning schedule/date and for 122 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 275 delayed projects, 65 projects have overall delay in the range of 1 to 12 months, 73 projects have a delay in the range of 13 to 24 months, 75 projects have a delay in the range of 25 to 60 months and 62 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-06-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI- GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
3	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
5	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, delay in equipment erection, fund constraints, geological surprises, shortage of skill manpower, delay in civil work, increase in scope of work, delay in shifting of utility by State Government, delay in opening and evaluation of bids, ROU/ROW problems, law and order situation, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 30-06-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADAN GANL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30-06-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 30.06.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Coal Sector**, out of 55 projects, 28 projects are delayed. During the month the project 'Neyveli New Thermal Power Project (2x500 MW), NLC' (Mega Project) has reported additional delay of 2 months due to delay in opening and evaluation of bids.

ii) In the **Atomic Energy Sector**, all 4 projects are delayed. During the month the project 'Kudankulam APP, NPCIL' (Mega Project) has reported additional delay of 12 months due to delay in supply and erection of equipments.

iii) In the **Urban Development Sector**, out of 4 projects, 1 project is delayed. During the month the project 'Faridabad Extension, DMRC' (Mega Project) has reported additional delay of 8 months (however, no specific reasons have been reported by the project authorities for the delay in this project).

iv) In the **Railways Sector**, out of 127 projects, 32 projects are delayed. During the month 3 projects have reported additional delays in the range of 6-24 months. The project 'Construction of New Line From Harmati-Itanagar/NAR, NEFR' has reported additional delay of 6 months due to fund constraints; the project 'New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar, RVNL' has reported additional delay of 24 months due to delay in shifting of utilities by the State Government; and the project 'Freight Operations Information System, FOIS' has reported additional delay of 24 months (however, no specific reasons have been reported by the project authority for the delay in this project).

v) In the **Steel Sector**, out of 17 projects, 14 projects are delayed. During the month 3 projects have reported additional delays in the range of 1-6 months, out of which 2 are Mega projects. The project 'Expansion of Durgapur Steel Plant, SAIL' has reported additional delay of 3 months due to increase in scope of work; and the Projects 'Installation of 1x45 MVA Submerged Arc Furnace, SAIL' and 'Expansion of Bhilai Steel Plant, SAIL' have reported additional delays of 1 and 6 months respectively (however, no specific reasons have been reported by the project authority for the delay in these projects).

vi) In the **Power Sector**, out of 103 projects, 52 projects are delayed. During the month 5 projects have reported additional delays in the range of 1-10 months, out of which 2 are Mega project. The project 'URI H.E.P Stage –II, NHPC' has reported additional delay of 3 months due to flood in the river Jhelam; the project 'Transmission System for Establishment of 400/220 K, PGCIL' has reported additional delay of 5 months due to delay in forest clearance; and the project 'Teesta Low Dam HEP, Stage-IV, NHPC' has reported additional delay of 6 months due to delay in civil works. The projects 'Transmission System Associated with Parbati-III HEP, PGCIL' and 'Tripura Gas Based Power Project, NEEPCO' have reported additional delays of 1 and 10 months respectively (however, no specific reasons have been reported by the project authorities for the delay in these projects).

vii) In the **Petroleum Sector**, out of 74 projects, 42 projects are delayed. During the month 15 projects have reported additional delays in the range of 1-30 months, out of which 9 are Mega projects. The project 'Paradip Refinery Project, IOCL' has reported additional delay of 1 month due to law and order problem at site and non-availability of forest clearance; the project 'Uran Chakan/Shikrapur LPG Pipeline, HPCL' has reported additional delay of 2 months due to ROU issues; the projects 'Offshore Grid Interconnectivity Project in Mumbai High, ONGC' and 'Development of B-193 Cluster Fields, ONGC' have reported additional delay of 5 months each due to revised scope of work and contractual issues respectively; the projects 'IOR Rudrasagar, ONGC' and 'Development of BHE and BH-35 Area, ONGC' have reported additional delay of 6 months each due to increase in scope of work and delay in installation of well platform & pipeline respectively; the project 'Development of B-46 Cluster Field, ONGC' has reported additional delay of 7 months due to delay in award of work and delay in drilling of wells; the projects 'Development of C-Series Fields, ONGC', 'Mumbai High South Redevelopment PH-2, ONGC' and 'Up-Gradation of Konaban GGS and Pipeline Grid Project, ONGC' have reported additional delay of 9 months each due to re-fabrication of deck, splitting of packages and ROU issues respectively; the project 'Additional Development of D-1 Field, ONGC' has reported additional delay of 11 months due to delay in supply of equipments; the project 'Construction of 12 Offshore Supply Vessels (OSV), ONGC' has reported additional delay of 12 months due to shortage of manpower; and the project 'Development of B-22 Cluster Fields, ONGC' has reported additional delay of 30 months due to geological surprises. The projects 'Diesel Hydrotreator Project at Visakh Refinery, HPCL' and 'Diesel Hydrotreator Project at Mumbai Refinery, HPCL' have reported additional delays of 2 and 3 months respectively (however, no specific reasons have been reported by the project authority for the delay in these projects).

viii) In the **Road Transport & Highways Sector**, out of 148 projects, 94 are delayed. During the month 24 projects have reported additional delays in the range of 1-20 months, out of which 4 are Mega projects. The projects ‘Thanjaur-Trichy, NH-67, NHAI’ , ‘Hungund-Surathkal and Mangalore-Karnataka/Kerala Border, NHAI’ and ‘Devihalli-Hassan, NHAI’ have reported additional delay of 1 month each; the projects ‘New Mangalore Port NH-17 and NH-48, NHAI’ , ‘Pimpalgaon-Nasik-Gonde, NH-3 (NHDP-Phase-III), NHAI’ , ‘Jaipur-Tonk-Deoli, NHAI’ and ‘Jaipur-Reengus, NHAI’ have reported additional delay of 2 months each; the projects ‘Silchar-Udarband (PH.II) NH-54, KM.309 to KM.275, NHAI’ , ‘Dharamtul to Sonapur (AS-19), NHAI’ , ‘Kishangarh-Ajmer-Beawer, NHAI’ and ‘4 Lanning of Ahmedabad to Godhara, NHAI’ have reported additional delay of 3 months each; the projects ‘Delhi/ Haryana Border to Rohtak, NHAI’ , ‘Chengapalli to Coimbatore Bypass KM-102.035-144.740 KM NHAI’ and ‘Trichy Bypass, NHAI’ have reported additional delay of 4 months each; the projects ‘Jhansi to Lalitpur, NH-25, NH-26, NHAI’ , ‘ Surat- Dahisar (Six Lane) KM 263 to KM 502, NHAI’ , ‘Amritsar-Pathankot, NHAI’ and ‘Development of adequate Road Connectivity to Chennai, NHAI’ have reported additional delay of 6 months each; the project ‘Dholpur - Morena Section (Including Chambol Bridge), NHAI’ has reported additional delay of 7 months; ; the projects ‘Rajmarg Choraha to Lakhnandon, KM 297 to KM 351, NH-26, NHAI’ and ‘Muradabad-Bareilly, NHAI’ have reported additional delay of 9 months each; and the projects ‘Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1), NHAI’ , ‘Panikholi-Rimoli, NHAI’ and ‘Four Lanning of Walayar-Vadakkancherry Section, NHAI’ have reported additional delays of 12, 13 and 20 months respectively. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, delay in shifting of utility, poor performance of contractor, etc.


10. The status as on 30.06.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Road Transport & Highways	148	24
2	Railways	127	3
3	Power	103	5
4	Petroleum	74	15
5	Coal	55	1
6	Shipping & Ports	19	0
7	Steel	17	3
8	Telecommunications	13	0
9	Civil Aviation	7	0
10	Atomic Energy	4	1
11	Urban Development	4	1
12	Petrochemicals	1	0
13	Water Resources	1	0
	Total	573	53

Sectoral break up of on-going infrastructure projects.

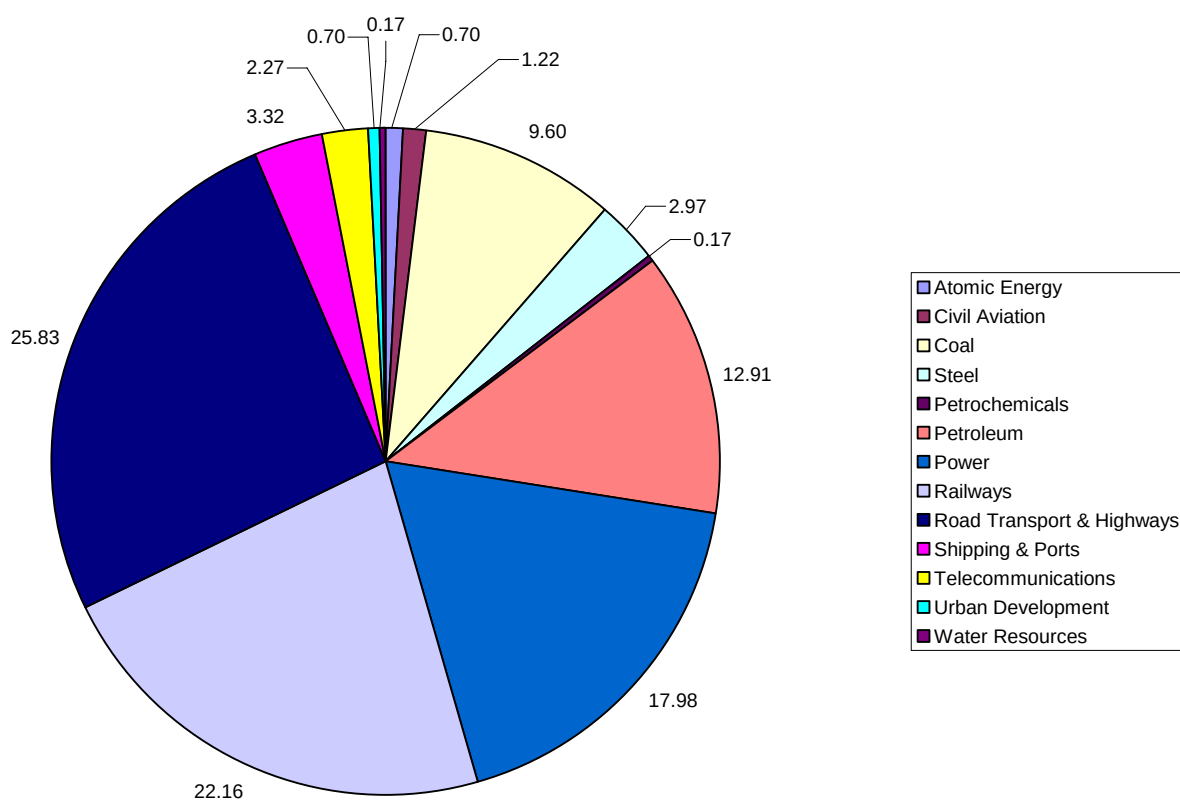

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>Power</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>Railways</u>			
2	REINGUNTA-GUNTAKAL(RE)(RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL)(RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>Fertilisers</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT(NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>Power</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>Road Transport & Highways</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>Railways</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE(RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36


Summary of projects in the Flash Report for the month of June, 2013

Project Implementation - Current Status:

Number of Projects in Previous Month	569
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects elevated to the status of Major project during the current month	4
Number of Projects Added in Current Month	2
Number of Projects in Current Month	573

Brief Analysis


Project Status with respect to Original Schedule: Out of 573 projects, 3 projects are ahead of schedule, 145 projects are on schedule and 286 projects are delayed. Of the balance, 122 projects do not have fixed dates of commissioning while 17 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

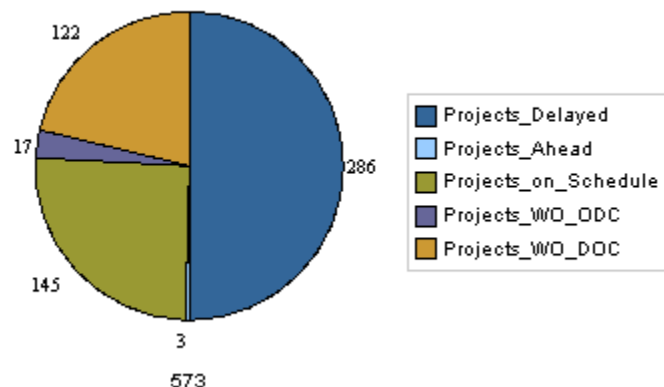

Investment Scenario

The Total Original cost of implementation of 573 projects when sanctioned, was of the order of Rs. 798677.21 crore but this was subsequently revised to Rs. 957383.14 crore implying a cost overrun of 19.9%. The expenditure incurred on these projects till June, 2013 is Rs. 472210.5 crore, which is 49.3% of the revised cost of the projects.

Figures are in Rs. Crore

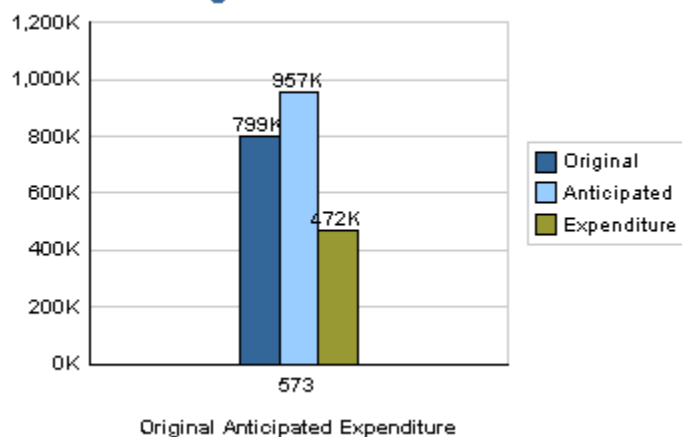

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	569
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects elevated to the status of Major Project during the current months	4
No of Projects added in Current Month	2
No of Projects in Current Month	573

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	286	3	145	17	122	573	49.91
Latest Approved (Date)	275	3	156	17	122	573	47.99

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	426	675,969.15	720,371.73	339,410.30	47.10	44,402.58	6.60
Latest Approved (RCE)	147	180,627.78	237,011.41	132,800.20	56.00	56,383.63	31.20
Total (RCE)	573	856,596.93	957,383.14	472,210.50	49.32	100786.21	11.77
Original Cost of All Projects							
Original Cost	573	798,677.21	957,383.14	472,210.50	49.30	158,705.93	19.90

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	53	121,411.57	135,312.24	99,033.98	73.20	13,900.67	11.40

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of Projects				Projects with cost overrun			
			Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	7	5,691.2	6,280.7	10.4	2	3,750.5	4,340.0	15.7
3	Coal	55	38,127.1	41,212.5	8.1	7	8,579.5	12,262.6	42.9
4	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	Petroleum	74	166,849.7	182,105.2	9.1	23	58,495.4	78,469.3	34.1
7	Power	103	243,029.0	262,286.4	7.9	23	51,424.0	70,681.4	37.4
8	Railways	127	66,498.3	161,153.6	142.3	108	46,392.6	141,094.5	204.1
9	Road Transport & Highways	148	101,189.1	103,127.7	1.9	11	3,324.3	5,445.2	63.8
10	Shipping & Ports	19	15,617.1	17,902.4	14.6	9	8,629.0	11,218.5	30.0
11	Telecommunications	13	5,699.2	5,520.2	-3.1	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		573	798,677.2	957,383.1	19.9	198	235,193.7	400,045.5	70.1

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

Sl.No	State	No. of Projects				Projects with cost overrun			
			Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Andhra Pradesh	37	31,097.1	38,953.4	25.3	14	12,923.7	21,646.9	67.5
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	4	9,512.2	17,330.3	82.2
3	Assam	39	23,597.3	37,785.7	60.1	14	10,762.0	25,044.4	132.7
4	Bihar	30	26,917.6	35,131.2	30.5	15	12,886.5	21,100.1	63.7
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	25	34,101.3	35,197.0	3.2	6	2,648.5	4,014.0	51.6
7	Haryana	8	4,054.4	5,737.0	41.5	2	1,298.8	2,981.4	129.5
8	Himachal Pradesh	5	13,355.6	17,263.2	29.3	4	11,308.5	15,216.2	34.6
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	27	47,076.4	56,474.7	20.0	11	9,996.8	19,888.1	98.9
11	Kerala	7	20,376.7	22,170.2	8.8	3	4,295.7	6,089.2	41.8
12	Madhya pradesh	20	18,545.6	18,953.8	2.2	4	2,714.8	3,542.4	30.5
13	Maharashtra	48	88,574.5	102,190.1	15.4	16	32,355.5	47,617.5	47.2
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	512.1
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	2,441.5	187.2	1	850.0	2,441.5	187.2
18	Odisha	30	56,171.6	63,436.9	12.9	12	32,671.6	39,936.9	22.2
19	Punjab	5	2,063.4	3,005.2	45.6	2	532.4	1,474.2	176.9
20	Rajasthan	14	21,115.8	21,356.0	1.1	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	48,788.1	61,732.8	26.5	14	29,143.5	42,088.3	44.4
23	Tripura	3	1,522.4	2,652.5	74.2	2	1,234.4	2,364.4	91.6
24	Uttar Pradesh	27	21,281.9	25,861.1	21.5	10	3,831.0	8,458.5	120.8
25	West Bengal	26	46,686.4	58,814.5	26.0	15	23,294.9	35,423.1	52.1
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
28	Jharkhand	24	15,305.5	19,509.0	27.5	7	2,225.5	6,600.7	196.6
29	Uttarakhand	5	7,624.2	8,564.6	12.3	2	2,640.7	3,581.2	35.6
30	Multi State	110	143,632.6	157,891.0	9.9	23	15,037.0	31,387.4	108.7
Total		573	798,677.2	957,383.1	19.9	198	235,193.7	400,045.5	70.1

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No	Sector	No. of Projects				Projects with time overruns			
			Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 63
2	Civil Aviation	7	5,691.2	6,280.7	10.4	2	645.1	645.1	13 - 47
3	Coal	55	38,127.1	41,212.5	8.1	28	24,633.8	28,090.6	12 - 72
4	Steel	17	65,285.9	71,443.4	9.4	15	64,698.3	70,855.9	6 - 45
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
6	Petroleum	74	166,849.7	182,105.2	9.1	44	119,651.5	135,241.8	1 - 120
7	Power	103	243,029.0	262,286.4	7.9	52	120,984.2	137,546.2	1 - 102
8	Railways	127	66,498.3	161,153.6	142.3	34	26,613.4	75,687.2	3 - 240
9	Road Transport & Highways	148	101,189.1	103,127.7	1.9	94	54,711.3	56,623.1	2 - 112
10	Shipping & Ports	19	15,617.1	17,902.4	14.6	6	6,223.1	7,475.2	5 - 87
11	Telecommunications	13	5,699.2	5,520.2	-3.1	5	2,934.9	2,774.5	28 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		573	798,677.2	957,383.1	19.9	286	469,492.1	573,079.5	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

Sl.No	State	No. of Projects				Projects with time overruns			
			Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Andhra Pradesh	37	31,097.1	38,953.4	25.3	12	16,954.0	21,129.5	4 - 45
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	3	9,356.2	16,923.9	25 - 87
3	Assam	39	23,597.3	37,785.7	60.1	34	21,203.5	34,562.6	12 - 120
4	Bihar	30	26,917.6	35,131.2	30.5	11	20,239.3	24,919.6	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	13 - 13
6	Gujarat	25	34,101.3	35,197.0	3.2	7	16,272.9	16,294.5	3 - 15
7	Haryana	8	4,054.4	5,737.0	41.5	4	2,216.6	3,396.6	5 - 50
8	Himachal Pradesh	5	13,355.6	17,263.2	29.3	5	13,355.6	17,263.2	26 - 102
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	7	13,038.7	32,618.8	10 - 201
10	Karnataka	27	47,076.4	56,474.7	20.0	11	19,058.4	19,061.1	6 - 108
11	Kerala	7	20,376.7	22,170.2	8.8	5	19,581.0	20,231.0	5 - 58
12	Madhya pradesh	20	18,545.6	18,953.8	2.2	10	4,795.0	4,921.7	8 - 69
13	Maharashtra	48	88,574.5	102,190.1	15.4	25	44,363.0	52,970.1	2 - 144
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	72 - 72
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 35
17	Nagaland	1	850.0	2,441.5	187.2	1	850.0	2,441.5	24 - 24
18	Odisha	30	56,171.6	63,436.9	12.9	18	51,393.9	54,735.8	3 - 136
19	Punjab	5	2,063.4	3,005.2	45.6	2	989.0	1,064.0	13 - 64
20	Rajasthan	14	21,115.8	21,356.0	1.1	7	15,830.9	15,812.6	3 - 59
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 47
22	Tamil Nadu	32	48,788.1	61,732.8	26.5	15	34,552.5	43,919.7	6 - 87
23	Tripura	3	1,522.4	2,652.5	74.2	2	1,101.4	2,029.0	19 - 21
24	Uttar Pradesh	27	21,281.9	25,861.1	21.5	14	13,392.6	16,137.5	8 - 84
25	West Bengal	26	46,686.4	58,814.5	26.0	11	23,968.7	29,391.6	3 - 141
26	Delhi	4	38,214.4	38,194.8	-0.1	1	2,494.0	2,494.0	8 - 8
27	Chhatisgarh	24	58,278.3	59,362.9	1.9	9	23,484.9	23,796.2	18 - 59
28	Jharkhand	24	15,305.5	19,509.0	27.5	10	9,422.6	9,529.2	5 - 60
29	Uttarakhand	5	7,624.2	8,564.6	12.3	4	6,097.2	7,037.6	5 - 54
30	Multi State	110	143,632.6	157,891.0	9.9	52	81,235.1	88,612.0	1 - 240
Total		573	798,677.2	957,383.1	19.9	286	469,492.1	573,079.5	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No	Sector	No. of Projects				Projects with time overruns			
			Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 63
2	Civil Aviation	7	5,691.2	6,280.7	10.4	2	645.1	645.1	13 - 47
3	Coal	55	38,127.1	41,212.5	8.1	28	24,633.8	28,090.6	12 - 72
4	Steel	17	65,285.9	71,443.4	9.4	13	63,227.8	69,385.3	7 - 45
5	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	Petroleum	74	166,849.7	182,105.2	9.1	42	118,916.3	132,904.0	1 - 94
7	Power	103	243,029.0	262,286.4	7.9	52	120,984.2	137,546.2	1 - 102
8	Railways	127	66,498.3	161,153.6	142.3	32	26,098.4	73,959.6	3 - 240
9	Road Transport & Highways	148	101,189.1	103,127.7	1.9	94	54,711.3	56,623.1	2 - 112
10	Shipping & Ports	19	15,617.1	17,902.4	14.6	2	4,728.0	5,610.0	18 - 39
11	Telecommunications	13	5,699.2	5,520.2	-3.1	5	2,934.9	2,774.5	28 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		573	798,677.2	957,383.1	19.9	275	459,815.7	556,758.4	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of projects				Projects with cost overruns			
			Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	44,541.0	46,726.0	4.9	1	3,492.0	5,677.0	62.6
2	Civil Aviation	7	5,898.2	6,280.7	6.5	1	1,942.5	2,325.0	19.7
3	Coal	55	40,729.4	41,212.5	1.2	5	2,211.1	2,694.1	21.8
4	Steel	17	65,597.2	71,443.4	8.9	5	23,733.0	29,609.3	24.8
5	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
6	Petroleum	74	180,741.2	182,105.2	0.8	6	32,051.3	36,177.5	12.9
7	Power	103	245,222.9	262,286.4	7.0	20	46,809.6	63,873.2	36.5
8	Railways	127	95,557.4	161,153.6	68.6	81	48,955.9	114,558.8	134.0
9	Road Transport & Highways	148	101,355.6	103,127.7	1.7	11	3,324.3	5,445.2	63.8
10	Shipping & Ports	19	17,488.0	17,902.4	2.4	5	3,157.6	3,783.5	19.8
11	Telecommunications	13	5,699.2	5,520.2	-3.1	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		573	856,596.9	957,383.1	11.8	140	174,009.1	278,421.1	60.0

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of projects				Projects with time & cost overruns			
			Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	7	5,691.18	6,280.67	10.36	1	1,808.00	2,015.00	13- 13
3	Coal	55	38,127.05	41,212.50	8.09	0	0.00	0.00	0- 0
4	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	24- 24
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	74	166,849.67	182,105.16	9.14	11	21,026.22	34,896.99	13- 120
7	Power	103	243,028.99	262,286.39	7.92	1	596.45	1,007.16	0- 0
8	Railways	127	66,498.32	161,153.59	142.34	15	5,839.02	22,637.54	0- 144
9	Road Transport & Highways	148	101,189.08	103,127.70	1.92	0	0.00	0.00	0- 0
10	Shipping & Ports	19	15,617.12	17,902.42	14.63	5	5,400.70	6,860.25	10- 87
11	Telecommunications	13	5,699.24	5,520.22	-3.14	0	0.00	0.00	0- 0
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		573	798677.21	957383.14	19.87	35	40426.89	76944.11	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of projects				Projects with time & cost overruns			
			Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 63
2	Civil Aviation	7	5,691.18	6,280.67	10.36	0	0.00	0.00	0- 0
3	Coal	55	38,127.05	41,212.50	8.09	5	7,938.86	11,573.95	19- 55
4	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	10- 45
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	74	166,849.67	182,105.16	9.14	17	53,961.35	72,524.90	2- 120
7	Power	103	243,028.99	262,286.39	7.92	17	41,777.81	58,339.86	10- 102
8	Railways	127	66,498.32	161,153.59	142.34	29	21,214.91	70,293.58	12- 240
9	Road Transport & Highways	148	101,189.08	103,127.70	1.92	10	3,158.01	5,252.10	21- 110
10	Shipping & Ports	19	15,617.12	17,902.42	14.63	3	4,878.00	6,210.00	18- 87
11	Telecommunications	13	5,699.24	5,520.22	-3.14	2	1,065.85	1,089.32	34- 54
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		573	798677.21	957383.14	19.87	92	180147.29	287367.14	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>Railways</u>						
1	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	04/2005	240.00	03/2009	355.00	N.A.	334.59
2	PANSPURA-KHARAGPUR 3D LINE	09/2007	252.50	02/2010	529.23	12/2015	249.36

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl. No	Project	DOA	Cost	DOC	Cost	DOC
	<u>Civil Aviation</u>					
1	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS	10/2012	217.60	3/2015	217.60	3/2015
	<u>Coal</u>					
2	AMRAPALI OC	2/2012	858.11	3/2020	858.11	3/2020

Milestones (Cumulative due & achieved)

Total	3560
Achieved up to month	1334


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) NPCIL	13,171.00	17,270.00	12/2008	03/2013	03/2014	12
	<u>Coal</u>						
2	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) NLC	5,907.11	5,907.11	12/2015	12/2017	02/2018	2
	<u>Steel</u>						
3	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT SAIL	187.33	187.33	10/2013	04/2014	05/2014	1
4	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2013	03/2014	3
5	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	03/2014	09/2014	6
	<u>Petroleum</u>						
6	PARADIP REFINERY PROJECT IOCL	29,777.00	32,710.00	11/2012	03/2014	04/2014	1
7	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	06/2013	08/2013	2
8	URAN CHAKAN/SHIKRAPUR LPG PIPELINE HPCL	309.81	309.82	08/2014	08/2014	10/2014	2
9	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY HPCL	3,284.00	2,174.00	09/2011	06/2013	09/2013	3
10	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	07/2013	12/2013	5
11	DEVELOPMENT OF B-193 CLUSTER FIELDS ONGC	3,248.78	5,633.44	08/2010	12/2013	05/2014	5
12	IOR, RUDRASAGAR (ONGCL) ONGC	113.90	438.85	03/2006	06/2013	12/2013	6
13	Development of BHE and BH-35 Area. ONGC	372.11	372.11	03/2013	06/2013	12/2013	6
14	DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,436.21	07/2010	07/2013	02/2014	7
15	DEVELOPMENT OF C-SERIES FIELDS ONGC	3,195.16	3,690.37	12/2008	06/2013	03/2014	9
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 ONGC	5,713.03	8,813.41	05/2010	06/2013	03/2014	9
17	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	288.04	08/2012	06/2013	03/2014	9
18	ADDITIONAL DEV. OF D-1 FIELD ONGC	2,163.64	2,331.62	06/2012	06/2013	05/2014	11
19	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2013	12/2014	12
20	DEVELOPMENT OF B-22 CLUSTER FIELDS ONGC	2,323.40	2,920.82	09/2010	06/2013	12/2015	30
	<u>Power</u>						

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
21	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	775.25	01/2010	06/2013	07/2013	1
22	URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	2,081.00	11/2009	07/2013	10/2013	3
23	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K PGCIL	181.93	181.93	07/2013	07/2013	12/2013	5
24	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	05/2014	11/2014	6
25	TRIPURA GAS BASED POWER PROJECT NEEPCO	421.01	623.44	N.A.	07/2013	05/2014	10
	<u>Railways</u>						
26	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR NEFR	156.00	406.40	N.A.	06/2013	12/2013	6
27	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) FOIS	520.00	835.04	03/1995	03/2013	03/2015	24
28	New Work for Construction of Metro railway from Ba RVNL	2,069.60	2,069.60	03/2014	03/2014	03/2016	24
	<u>Road Transport & Highways</u>						
29	THANJAUR-TRICHY, NH-67(NHAI) NHAI	280.00	280.00	06/2009	06/2013	07/2013	1
30	Hungund-Surathkal and Mangalore-Knt/Kerala Border NHAI	946.00	946.00	N.A.	06/2013	07/2013	1
31	DEVIHALLI-HASSAN NHAI	453.00	453.00	N.A.	06/2013	07/2013	1
32	NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2011	06/2013	08/2013	2
33	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) NHAI	940.00	940.00	07/2012	06/2013	08/2013	2
34	Jaipur-Tonk-Deoli NHAI	792.06	792.06	12/2012	06/2013	08/2013	2
35	JAIPUR-REENGUS NHAI	267.81	267.81	02/2013	07/2013	09/2013	2
36	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHAI	157.47	154.57	09/2007	12/2013	03/2014	3
37	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	09/2013	12/2013	3
38	Kishangarh-Ajmer-Beawer NHAI	795.00	795.00	05/2012	06/2013	09/2013	3
39	4 LANNING OF AHMEDABAD TO GODHARA NHAI	1,008.50	1,008.50	06/2013	06/2013	09/2013	3
40	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	06/2013	10/2013	4
41	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM NHAI	852.00	852.00	03/2013	08/2013	12/2013	4
42	Trichy Bypass NHAI	374.00	374.00	05/2013	08/2013	12/2013	4
43	JHANSI TO LALITPUR, NH-25,26 NHAI	355.06	355.06	09/2009	06/2013	12/2013	6
44	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	06/2013	12/2013	6
45	AMRITSAR-PATHANKOT NHAI	705.00	705.00	11/2012	06/2013	12/2013	6
46	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN NHAI	600.00	600.00	06/2013	06/2013	12/2013	6
47	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE NHAI	232.45	232.45	09/2010	01/2014	08/2014	7

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
48	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) NHAI	251.03	251.03	10/2008	06/2013	03/2014	9
49	MURADABAD-BAREILY NHAI	1,267.00	1,267.00	06/2013	06/2013	03/2014	9
50	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) NHAI	572.30	572.30	10/2011	06/2013	06/2014	12
51	PANIKHOLI-RIMOLI NHAI	1,410.00	1,410.00	09/2014	09/2014	10/2015	13
52	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION NHAI	682.00	682.00	10/2013	03/2014	11/2015	20
	<u>Urban Development</u>						
53	FARIDABAD EXTENSION DMRC	2,494.00	2,494.00	09/2014	09/2014	05/2015	8
	53						

Graphical Analysis of All Projects w.r.t. Original Schedule

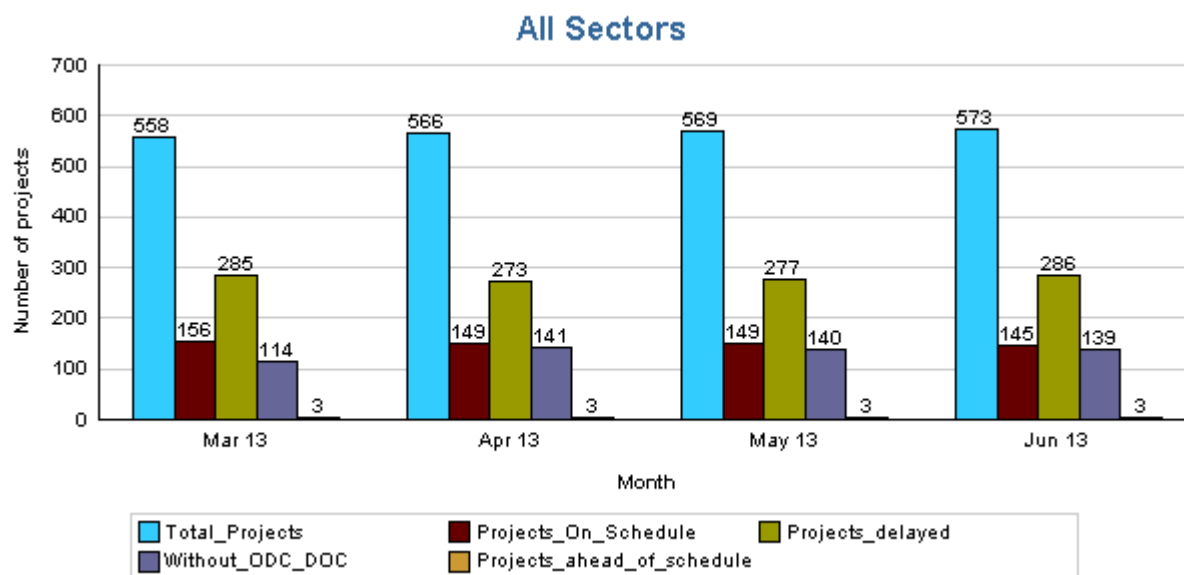


Break-up of 286 Delayed projects in June 2013

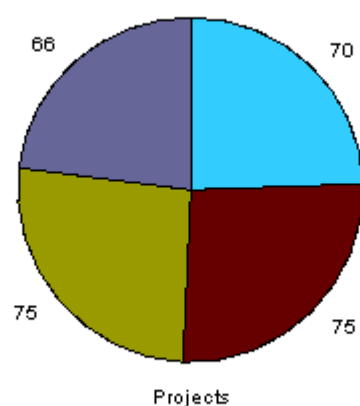


Delay in Months



Graphical Analysis of All Projects w.r.t. Revised Schedule

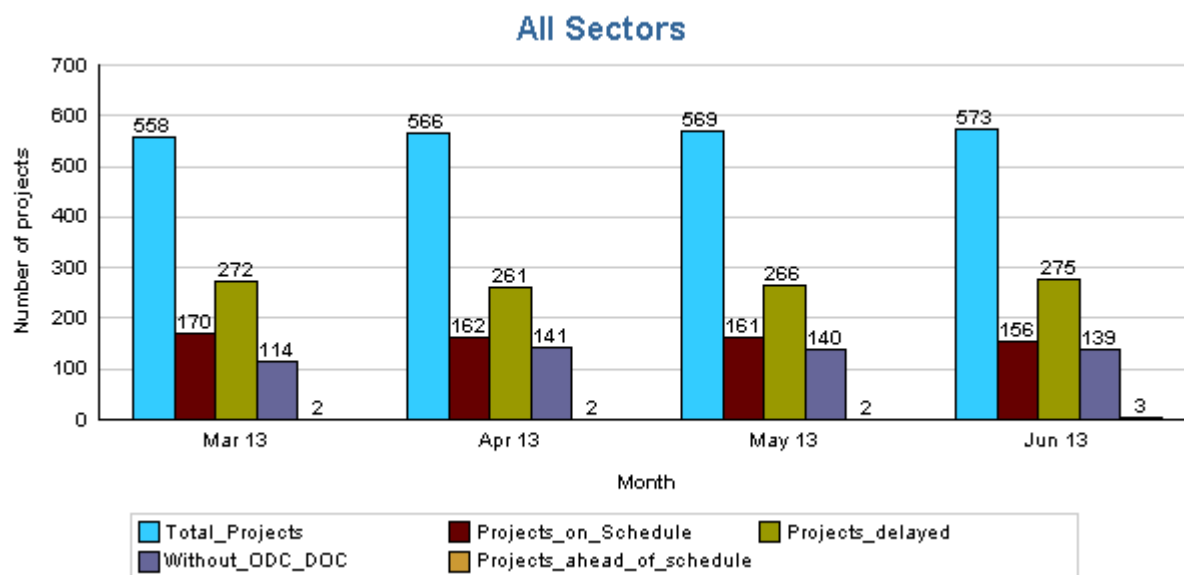


Break-up of 275 Delayed projects in June 2013

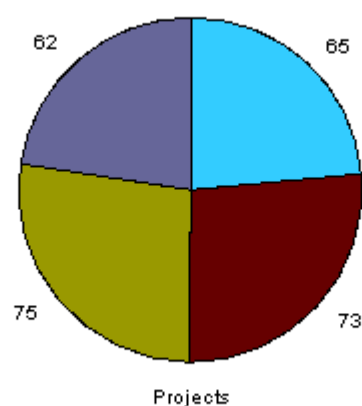


Delay in Months



Graphical Presentation of Urban Development Sector

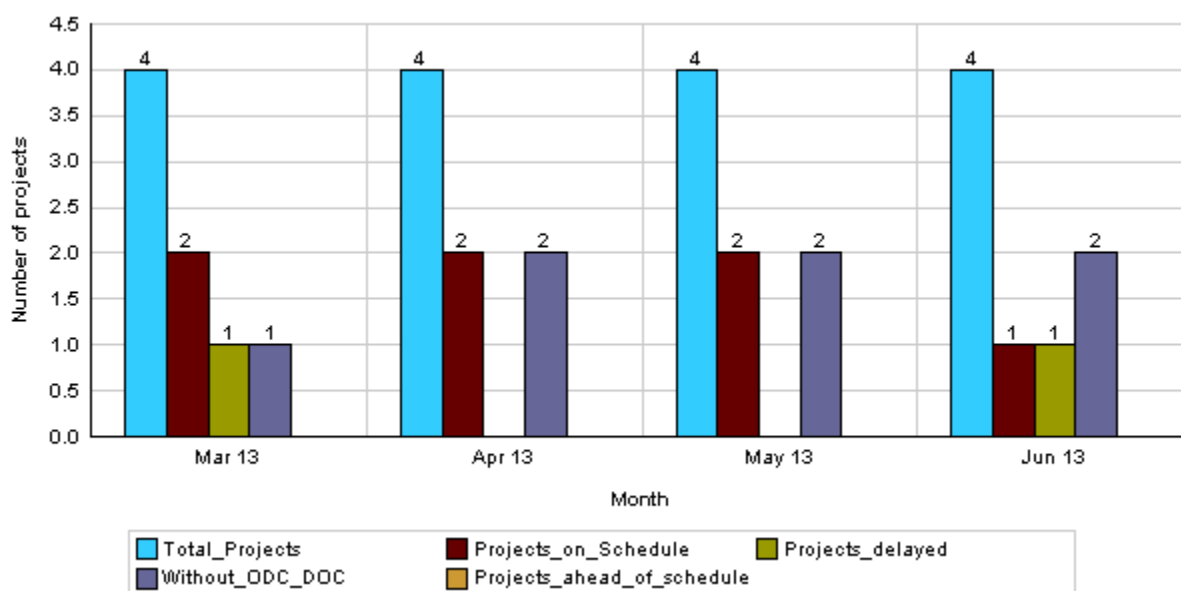


Break-up of 1 Delayed projects in June 2013



Delay in Months



Graphical Presentation of Telecommunications Sector

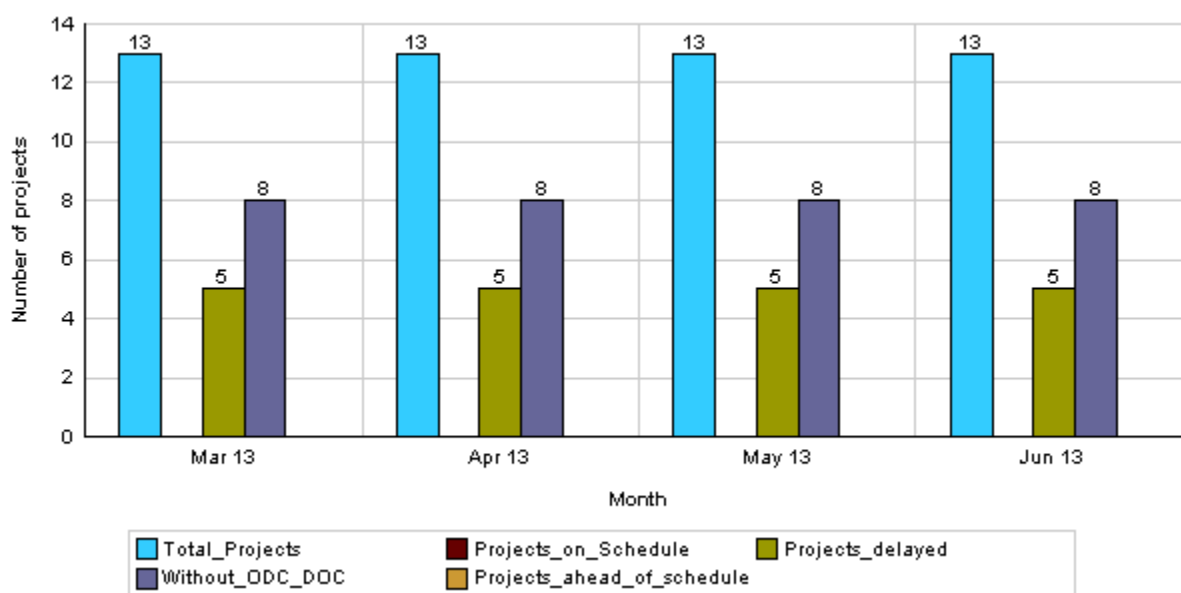


Break-up of 5 Delayed projects in June 2013




Delay in Months



Graphical Presentation of Shipping & Ports Sector

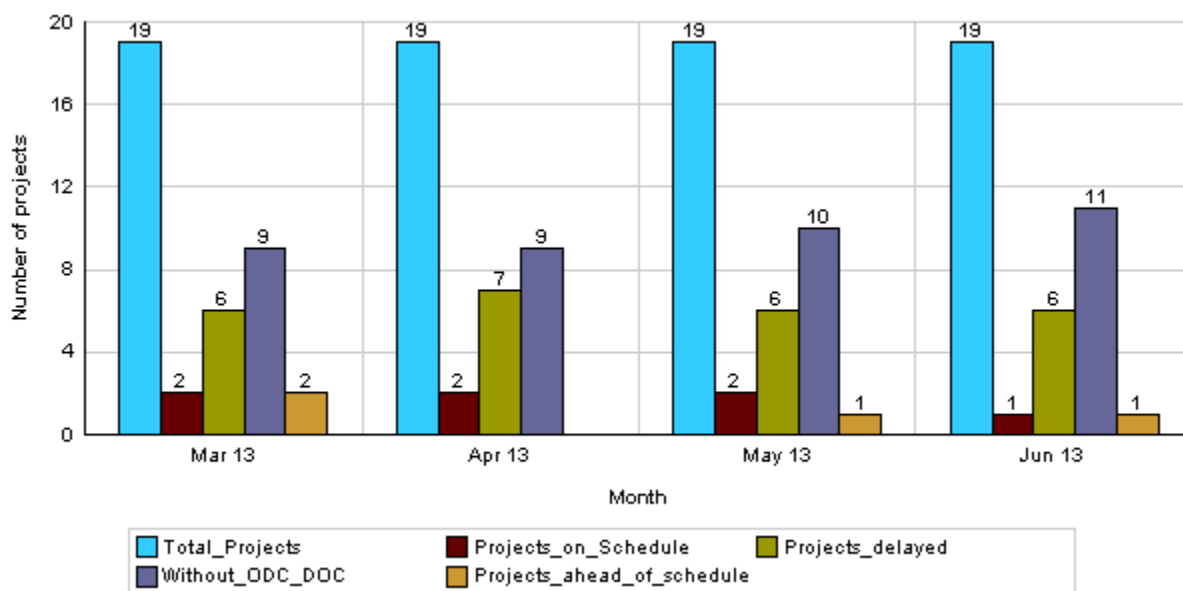


Break-up of 6 Delayed projects in June 2013

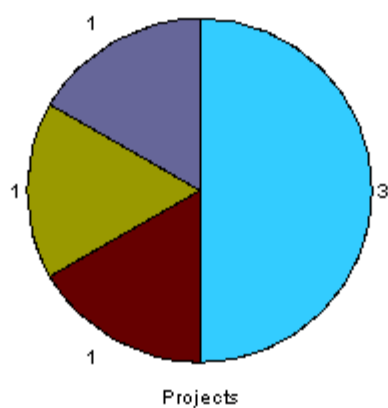


Delay in Months



Graphical Presentation of Road Transport & Highways Sector

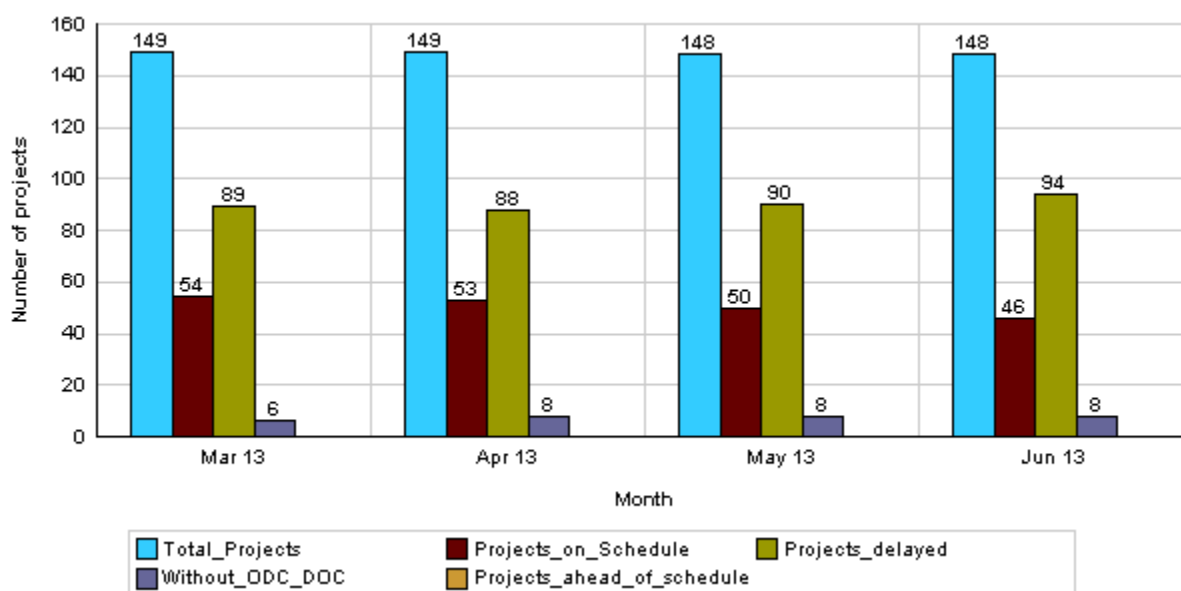


Break-up of 94 Delayed projects in June 2013

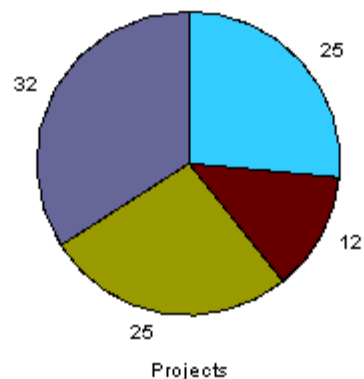


Delay in Months



Graphical Presentation of Railways Sector

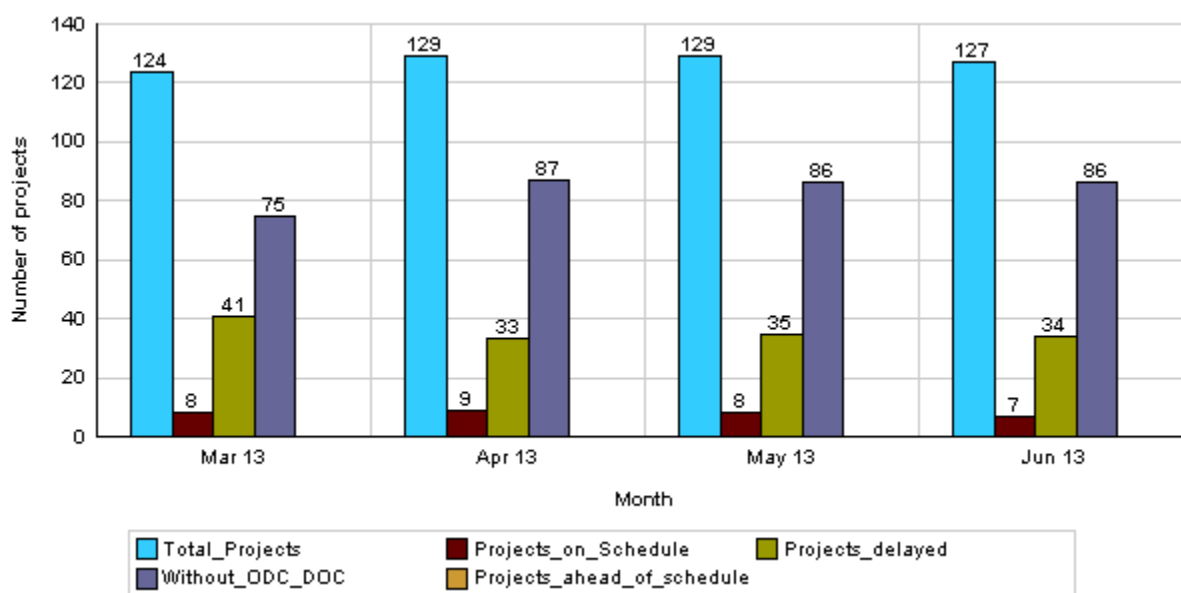


Break-up of 34 Delayed projects in June 2013

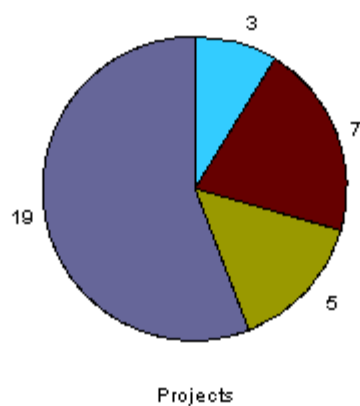


Delay in Months



Graphical Presentation of Power Sector

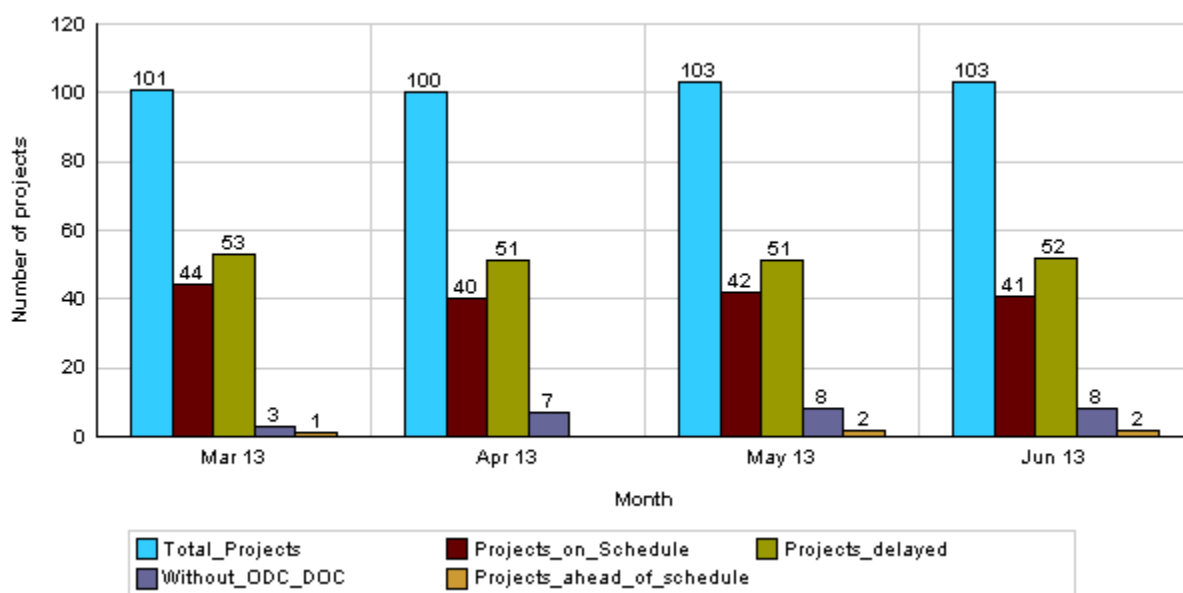


Break-up of 52 Delayed projects in June 2013

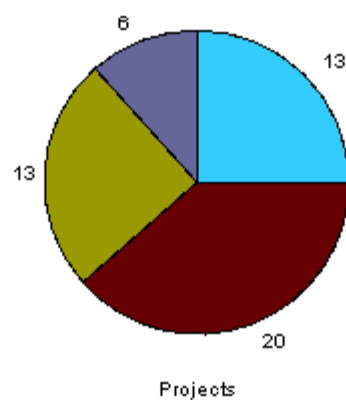


Delay in Months



Graphical Presentation of Petroleum Sector

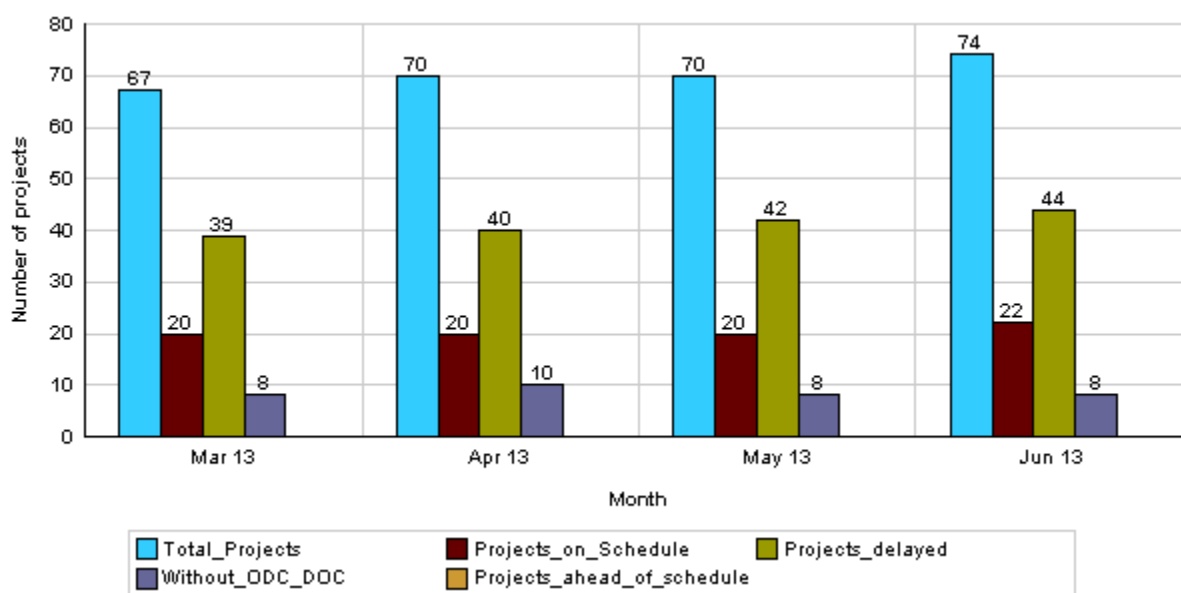


Break-up of 44 Delayed projects in June 2013

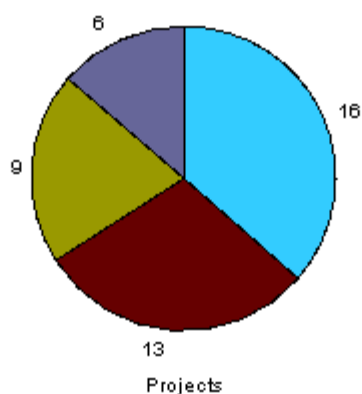


Delay in Months



Graphical Presentation of Steel Sector

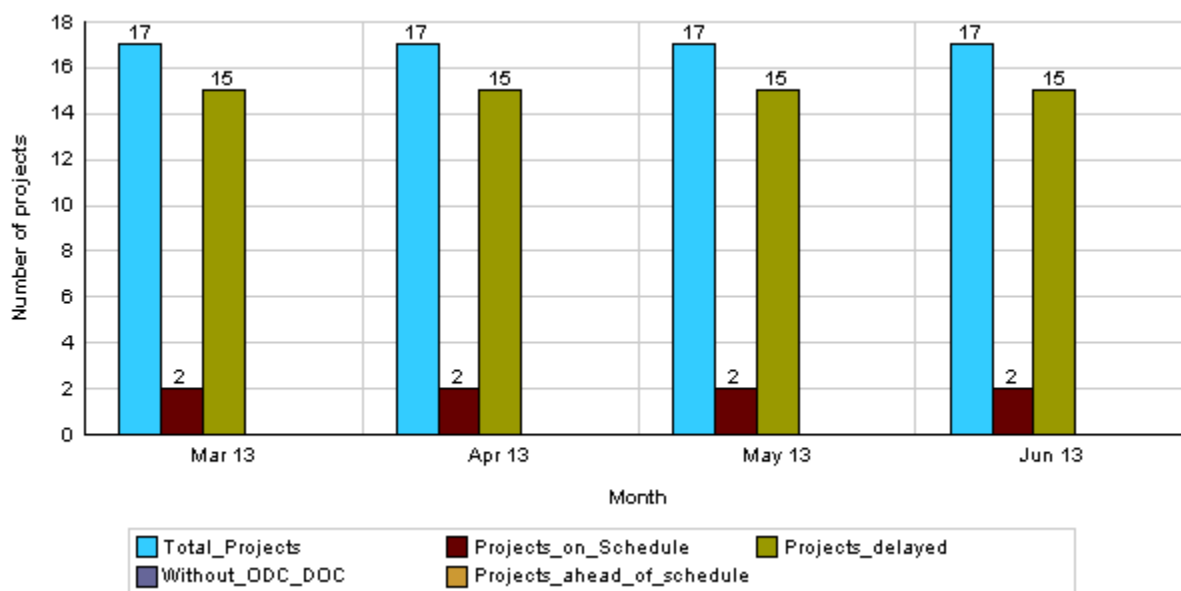


Break-up of 15 Delayed projects in June 2013

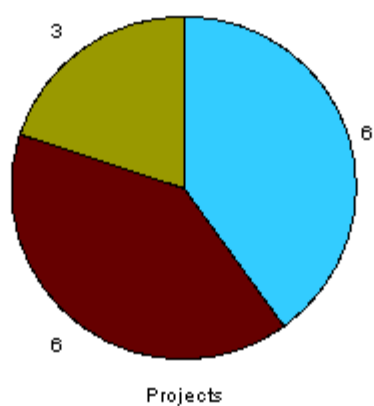


Delay in Months



Graphical Presentation of Coal Sector

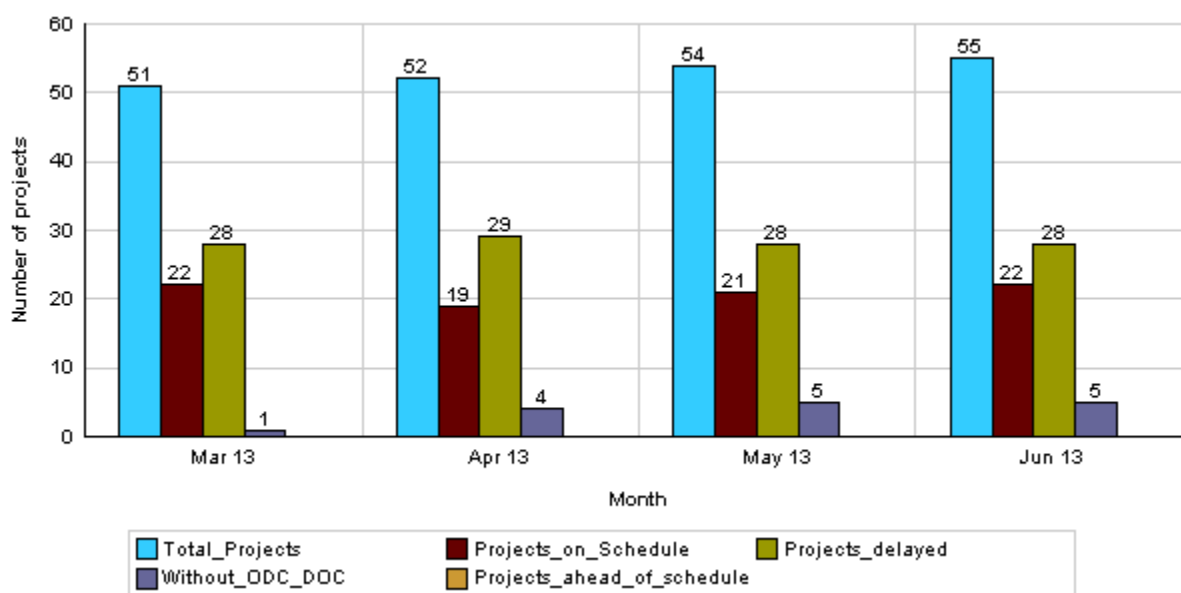


Break-up of 28 Delayed projects in June 2013

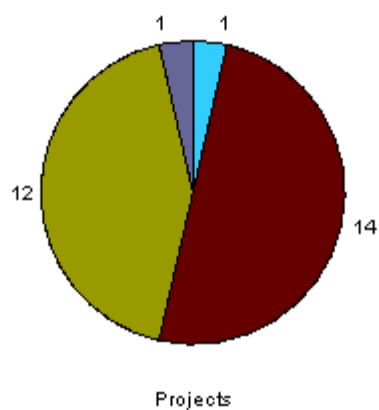


Delay in Months



Graphical Presentation of Civil Aviation Sector

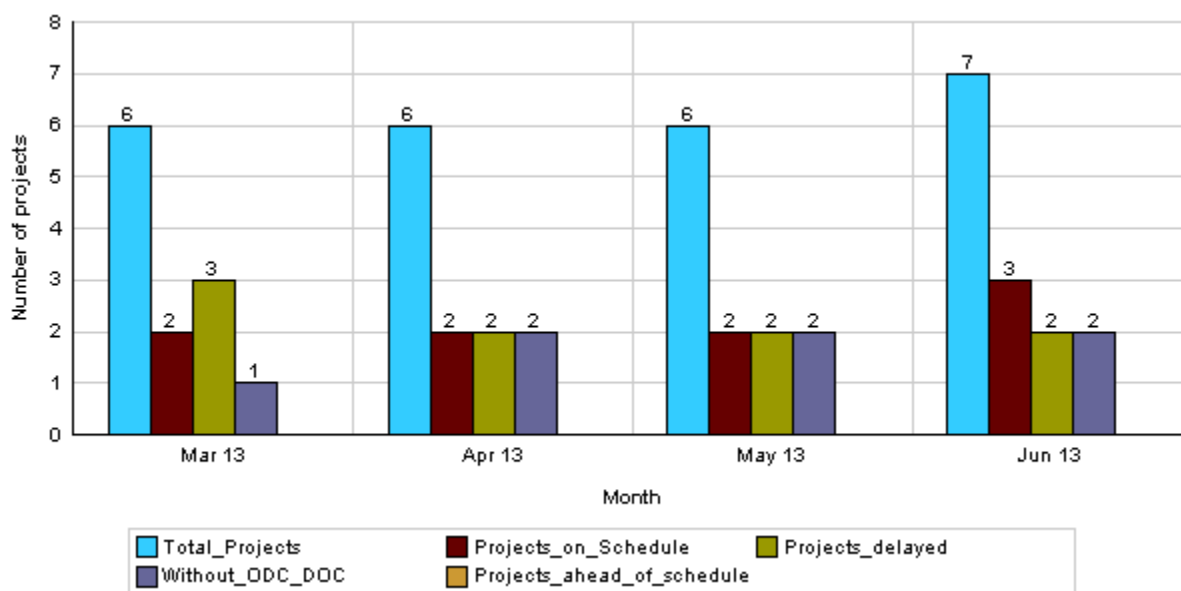


Break-up of 2 Delayed projects in June 2013

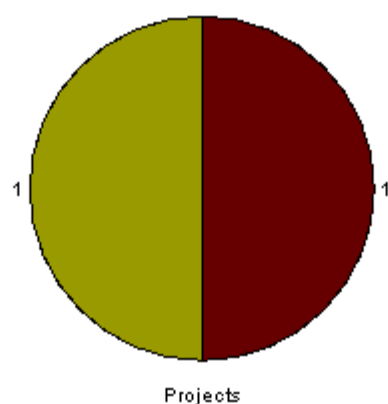


Delay in Months



Graphical Presentation of Atomic Energy Sector

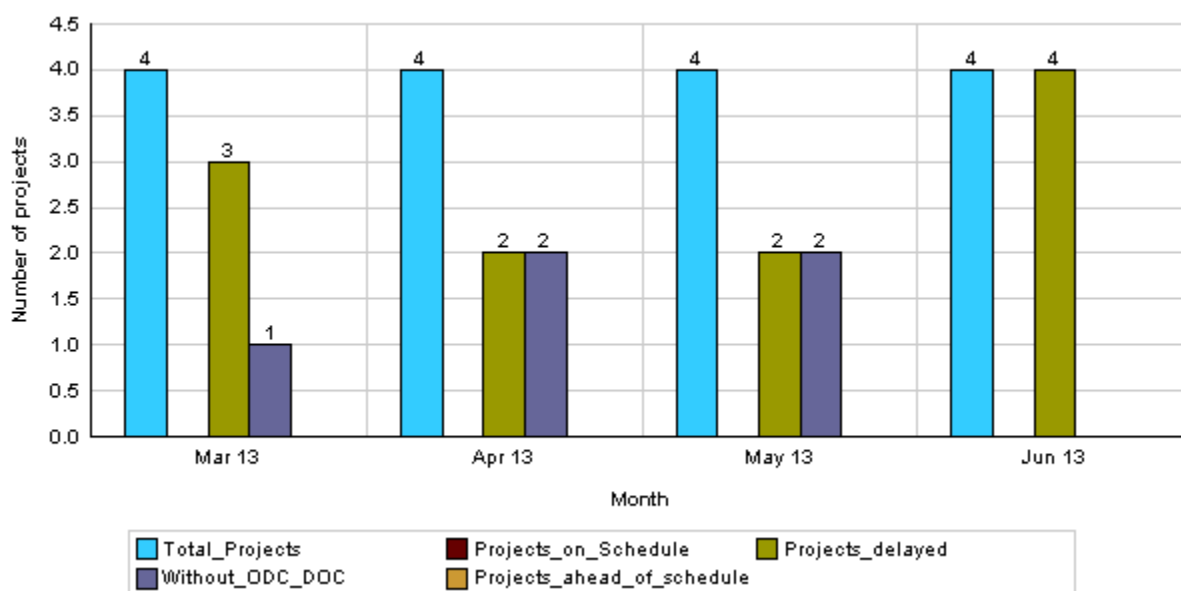

Break-up of 4 Delayed projects in June 2013

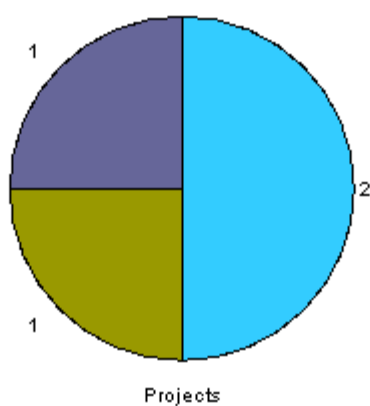

Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
Atomic Energy	4	40,442.00	44,541.00	46,726.00	25,369.48
Civil Aviation	7	5,691.18	5,898.18	6,280.67	5,408.64
Coal	55	38,127.05	40,729.44	41,212.50	15,064.77
Steel	17	65,285.87	65,597.15	71,443.41	51,276.24
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	74	166,849.67	180,741.21	182,105.16	88,364.70
Power	103	243,028.99	245,222.85	262,286.39	122,367.53
Railways	127	66,498.32	95,557.35	161,153.59	64,175.31
Road Transport & Highways	148	101,189.08	101,355.58	103,127.70	78,731.84
Shipping & Ports	19	15,617.12	17,487.95	17,902.42	8,603.74
Telecommunications	13	5,699.24	5,699.24	5,520.22	1,970.84
Urban Development	4	44,245.18	44,304.08	49,518.08	6,331.41
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	573	798,677.21	856,596.93	957,383.14	472,210.50

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(Jun,2013)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,940.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,262.00	12/2008 -	03/2014	63(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,140.48	09/2010 -	03/2015	54(O) -	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,027.00	12/2016 -	03/2017	3(O) -	0/69
	Total		40,442.00 -	46,726.00	25,369.48				47/327
	<u>Civil Aviation</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,471.11	05/2011 -	03/2013	-	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.80	01/2011 04/2013	12/2014	47(O) 20(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	242.98	05/2012 -	06/2013	13(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,904.73	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	452.00	108.03	03/2015 -	03/2015	0(O) -	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	449.97	06/2013 -	06/2013	0(O) -	0/0
11	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015	0(O) -	0/0
	Total		5,691.18 -	6,280.67	5,408.64				0/0
	<u>Coal</u>								
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	701.71	03/2013 09/2012	10/2014	19(O) 25(R)	18/22
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016	0(O) -	2/6
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	445.14	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
15	AMRAPALI OC - [N06000103]CCL,Jharkhand	02/2012	858.11 -	858.11	49.30	03/2020 -	03/2020	0(O) -	0/0
16	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	112.08	03/2012 -	03/2014	24(O) -	7/9
17	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.36	03/2011 -	03/2014	36(O) -	0/2

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.28	03/2010 -	03/2015	60(O) -	3/4
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	52.18	03/2016 -	03/2016	0(O) -	0/6
20	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00 -	490.10	149.34	03/2017 -	03/2017	0(O) -	4/12
21	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	45.02	03/2014 03/2014	03/2014	0(O) 0(R)	0/2
22	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	159.80	03/2015 03/2015	03/2015	0(O) 0(R)	0/3
23	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/2
24	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.36	03/2014 -	03/2016	24(O) -	2/8
25	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60(O) -	0/2
26	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,246.22	03/2014 -	03/2016	24(O) -	6/12
27	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,408.71	03/2014 -	03/2016	24(O) -	10/15
28	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87 -	395.87	84.50	03/2015 -	03/2015	0(O) -	1/13
29	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	113.75	03/2013 -	03/2015	24(O) -	5/10
30	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
31	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	14.02	03/2015 -	03/2015	0(O) -	4/31
32	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
33	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72(O) -	0/2
34	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	87.20	12/2012 -	03/2015	27(O) -	9/44
35	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,Andhra Pradesh	07/2012	417.33 -	417.33	0.02	07/2016 -	07/2016	0(O) -	0/39
36	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.74	03/2013 -	03/2015	24(O) -	5/10
37	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46 -	162.46	38.62	03/2014 -	03/2014	0(O) -	0/2
38	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
39	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	4.88	03/2018 03/2018	03/2018	0(O) 0(R)	0/4
40	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.81	03/2013 -	03/2014	12(O) -	0/2
41	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	114.77	03/2010 -	03/2014	48(O) -	9/10
42	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	702.44	03/2013 -	03/2013	-	0/9
43	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016	44(O) -	0/3
45	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24(O) -	1/6
46	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.29	03/2012 -	03/2015	36(O) -	11/20
47	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
48	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
49	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	30.75	12/2015 -	02/2018	26(O) -	1/33
50	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.66	03/2012 -	03/2015	36(O) -	0/2
51	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60(O) -	0/2
52	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
53	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.91	03/2014 -	03/2016	24(O) -	0/1
54	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.20	03/2013 -	03/2015	24(O) -	0/3
55	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24(O) -	0/2
56	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	228.82	03/2012 -	-	-	24/27
57	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
58	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.85	-	-	-	4/48
59	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,Andhra Pradesh	06/2012	365.01 -	365.01	-	06/2015 -	06/2015	0(O) -	0/51
60	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	36.82	03/2015 -	03/2015	0(O) -	6/31
61	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85 -	510.85	259.21	03/2016 -	03/2016	0(O) -	0/2
62	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	50.37	03/2012 -	-	-	16/42
63	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72 -	447.72	44.50	03/2016 -	03/2016	0(O) -	0/12
64	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,726.15	06/2009 -	01/2014	55(O) -	19/23
65	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,409.33	03/2012 -	03/2014	24(O) -	20/39
66	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	127.50	03/2012 -	03/2016	48(O) -	0/2
	Total		38,127.05 -	41,212.50	15,064.77				201/789
	Steel								

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
67	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	304.07	04/2013 12/2013	12/2013	8(O) 0(R)	17/19
68	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	253.47	08/2010 -	06/2013	34(O) -	0/1
69	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	260.49	02/2011 -	06/2013	28(O) -	2/3
70	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	200.10	05/2013 11/2013	11/2013	6(O) 0(R)	12/21
71	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	248.98	05/2012 -	08/2013	15(O) -	0/1
72	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	351.04	12/2011 03/2012	12/2013	24(O) 21(R)	16/21
73	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	145.98	10/2012 -	08/2013	10(O) -	3/4
74	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	332.65	57.57	08/2014 -	08/2014	0(O) -	0/0
75	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	63.20	11/2013 -	06/2014	7(O) -	1/1
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	9,540.32	03/2013 -	09/2014	18(O) -	22/27
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,628.95	12/2011 -	12/2013	24(O) -	16/16
78	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,642.51	12/2012 -	03/2014	15(O) -	10/12
79	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	14,671.22	12/2011 -	12/2013	24(O) -	19/19
80	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 -	12,291.00	10,417.06	10/2009 -	07/2013	45(O) -	65/67
81	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,413.47	03/2013 -	12/2013	9(O) -	11/14
82	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	74.71	10/2013 -	05/2014	7(O) -	0/1
83	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	254.90	3.10	12/2014 -	12/2014	0(O) -	0/0
	Total		65,285.87 -	71,443.41	51,276.24				194/227
	<u>Petrochemicals</u>								
84	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20(O) 0(R)	19/29
	Total		5,460.61 -	8,920.00	4,510.51				19/29
	<u>Petroleum</u>								
85	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	28.10	06/2012 -	03/2014	21(O) -	0/0
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23(O) -	0/0
87	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	726.73	12/2011 -	07/2013	19(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	1,494.50	03/2013 -	03/2014	12(O) -	0/0
89	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00 -	586.00	5.55	07/2015 -	08/2015	1(O) -	0/0
90	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014	0(O) -	0/0
91	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014	0(O) -	0/0
92	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	540.92	279.66	07/2012 07/2012	-	-	0/17
93	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50 -	341.50	187.51	02/2013 -	07/2013	5(O) -	38/42
94	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00 -	190.00	54.18	03/2014 -	03/2014	0(O) -	0/24
95	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	344.95	09/2011 -	12/2014	39(O) -	0/0
96	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 394.00	394.00	312.61	- -	03/2013	-	18/19
97	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94 -	202.94	4.12	01/2014 -	01/2014	0(O) -	0/0
98	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	761.68	275.07	05/2013 -	11/2013	6(O) -	0/0
99	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL, Rajasthan	04/2011	152.89 -	152.89	3.79	06/2013 -	06/2013	0(O) -	0/0
100	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	331.20	57.39	08/2013 -	01/2014	5(O) -	0/0
101	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	240.95	96.88	09/2012 -	09/2013	12(O) -	0/0
102	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]ONGC, Gujarat	10/2011	200.69 -	200.69	2.96	07/2014 -	07/2014	0(O) -	0/0
103	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
104	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC, Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12(O) -	0/0
105	Construction of three ETPs, Mehsana - [N16000135]ONGC, Gujarat	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2014	0(O) -	0/0
106	DBPL-II - [N16000147]GAIL, Multi State	06/2009	486.00 -	486.00	52.43	09/2013 -	09/2013	0(O) -	0/0
107	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	388.71	- -	-	-	0/0
108	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94(O) 20(R)	0/0
109	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,478.23	08/2010 03/2012	05/2014	45(O) 26(R)	0/0
110	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,881.73	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	920.79	07/2010 05/2012	02/2014	43(O) 21(R)	0/0
112	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63(O) 11(R)	0/0
113	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24(O) 16(R)	6/76

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
114	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	23(O) 17(R)	56/59
115	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	221.02	03/2013 -	12/2013	9(O) -	0/0
116	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
117	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,347.71	03/2013 03/2014	04/2014	13(O) 1(R)	0/0
118	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	217.08	11/2012 -	10/2013	11(O) -	0/0
119	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	955.50	01/2014 -	01/2014	0(O) -	0/0
120	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	61.34	12/2014 -	12/2014	0(O) -	0/0
121	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	594.83	01/2013 -	09/2013	8(O) -	18/18
122	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013	2(O) -	0/167
123	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	741.77	05/2015 -	05/2015	0(O) -	0/0
124	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,727.13	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
125	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	711.61	03/2007 03/2014	12/2013	81(O) -3(R)	3/3
126	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1(O) -	0/0
127	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	399.30	03/2006 03/2013	12/2013	93(O) 9(R)	6/6
128	IREF - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	20.90	12/2015 -	05/2016	5(O) -	0/0
129	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	2,665.65	145.57	03/2015 -	03/2015	0(O) -	0/0
130	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35(O) -	0/0
131	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
132	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	289.64	01/2012 -	-	-	0/1
133	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	1,219.17	12/2012 -	-	-	0/21
134	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015	0(O) -	0/0
135	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,371.54	01/2012 -	07/2013	18(O) -	0/108
136	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,124.72	09/2012 -	09/2013	12(O) -	0/0
137	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46(O) 12(R)	0/0
138	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015	0(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
139	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	279.00	-	12/2014 -	12/2014	0(O) -	0/0
140	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 973.79	973.79	729.51	03/2011 05/2011	05/2013	-	0/0
141	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	728.30	03/2010 03/2012	12/2013	45(O) 21(R)	0/0
142	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	913.00	31.35	07/2015 -	07/2015	0(O) -	0/0
143	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	22,254.00	11/2012 -	04/2014	17(O) -	60/100
144	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	834.74	09/2012 -	-	-	5/11
145	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	4,763.44	02/2014 -	02/2014	0(O) -	0/0
146	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	176.83	04/2012 -	06/2013	14(O) -	0/0
147	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	409.63	05/2014 -	05/2014	0(O) -	0/0
148	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	719.20	07/2012 -	10/2013	15(O) -	0/31
149	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	- -	52/53
150	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64 -	1,210.64	63.36	11/2015 -	11/2015	0(O) -	6/25
151	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	4.89	12/2014 -	12/2014	0(O) -	0/0
152	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	682.23	04/2012 -	07/2013	15(O) -	0/0
153	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26(O) -	0/0
154	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26(O) -	0/0
155	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014	2(O) -	0/0
156	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	184.41	08/2012 -	03/2014	19(O) -	0/0
157	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	247.86	03/2012 -	12/2013	21(O) -	13/20
158	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	34.77	12/2013 -	12/2013	0(O) -	0/0
	Total		166,849.67 -	182,105.16	88,364.70				287/807
	<u>Power</u>								
159	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,820.52	08/2012 -	03/2014	19(O) -	0/11
160	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	824.07	05/2012 -	09/2013	16(O) -	0/8
161	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/7

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
162	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,069.00	08/2013 -	09/2014	13(O) -	10/19
163	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,499.00	12/2009 -	02/2017	86(O) -	27/47
164	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,886.00	07/2011 -	10/2015	51(O) -	5/28
165	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	121.80	06/2012 -	09/2013	15(O) -	0/0
166	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	913.00	731.93	02/2011 10/2012	01/2013	-	2/4
167	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015	0(O) -	0/20
168	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	1,909.24	115.30	06/2015 -	06/2015	0(O) -	0/0
169	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	757.21	08/2014 -	08/2014	0(O) -	7/20
170	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	39.74	06/2014 -	06/2014	0(O) -	0/20
171	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
172	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	3.60	10/2014 -	10/2014	0(O) -	0/0
173	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	53.95	06/2012 -	09/2013	15(O) -	0/0
174	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	903.15	09/2014 -	09/2014	0(O) -	7/20
175	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	884.11	10/2009 -	12/2013	50(O) -	5/15
176	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	667.95	11/2012 -	09/2014	22(O) -	2/13
177	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
178	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	982.34	05/2014 -	05/2014	0(O) -	1/11
179	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,142.61	08/2013 -	08/2013	0(O) -	1/12
180	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	149.92	10/2011 -	07/2013	21(O) -	0/0
181	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	260.49	08/2014 -	08/2014	0(O) -	1/16
182	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	970.31	12/2013 -	12/2013	0(O) -	1/12
183	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	81.80	10/2012 -	07/2013	9(O) -	4/14
184	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	900.71	12/2007 12/2009	-	-	2/11
185	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,330.55	05/2013 05/2013	03/2017	46(O) 46(R)	7/22

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
186	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,606.19	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
187	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	5,000.00	04/2009 -	09/2014	65(O) -	0/9
188	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,629.00	12/2016 -	12/2016	0(O) -	12/15
189	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,869.99	09/2008 -	03/2013	-	15/23
190	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	1,083.00	05/2017 -	05/2017	0(O) -	5/5
191	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017	0(O) -	0/15
192	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
193	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	1,008.00	09/2016 -	09/2016	0(O) -	14/14
194	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	747.88	08/2010 01/2013	10/2013	38(O) 9(R)	0/3
195	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,045.64	08/2013 -	06/2015	22(O) -	0/17
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	267.02	02/2012 -	12/2013	22(O) -	1/13
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	355.02	11/2011 -	07/2014	32(O) -	0/11
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	363.76	11/2011 -	12/2013	25(O) -	1/14
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	130.78	01/2013 -	09/2013	8(O) -	1/6
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	277.02	07/2013 -	03/2014	8(O) -	1/11
201	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	826.24	04/2013 -	03/2014	11(O) -	0/11
202	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	153.17	11/2014 -	11/2014	0(O) -	1/12
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	78.99	03/2015 -	03/2015	0(O) -	0/15
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	23.88	04/2015 -	05/2015	1(O) -	0/16
205	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	572.28	11/2012 -	03/2014	16(O) -	0/11
206	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,819.66	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
207	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,479.78	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
208	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	1,117.92	605.07	08/2012 08/2013	09/2014	25(O) 13(R)	17/22
209	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,534.87	01/2012 -	03/2014	26(O) -	0/27
210	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,342.00	10/2012 -	11/2013	13(O) -	14/16

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
211	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,508.00	11/2016 -	11/2016	0(O) -	15/15
212	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,279.31	09/2010 08/2014	12/2017	87(O) 40(R)	11/11
213	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	85.91	04/2013 -	09/2013	5(O) -	4/15
214	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,580.90	2,051.68	08/2012 -	03/2014	19(O) -	0/5
215	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	50.32	06/2016 -	04/2015	-14(O) -	0/20
216	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	190.02	12/2014 -	11/2014	-1(O) -	0/0
217	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/7
218	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	93.67	08/2014 -	08/2014	0(O) -	2/19
219	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	347.09	02/2015 -	02/2015	0(O) -	0/14
220	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	171.52	11/2014 -	11/2014	0(O) -	0/16
221	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	305.71	01/2015 -	01/2015	0(O) -	3/19
222	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	105.63	08/2014 -	08/2014	0(O) -	7/20
223	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	161.99	06/2014 -	06/2014	0(O) -	7/20
224	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	149.64	06/2012 -	07/2013	13(O) -	0/3
225	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	887.88	08/2012 -	06/2014	22(O) -	0/11
226	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,841.00	03/2013 -	03/2016	36(O) -	2/15
227	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,147.32	09/2009 06/2013	11/2014	62(O) 17(R)	0/0
228	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,467.53	03/2007 09/2012	04/2013	-	25/25
229	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 -	2,978.86	489.19	07/2010 -	11/2016	76(O) -	1/10
230	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	92.22	01/2014 -	01/2014	0(O) -	3/18
231	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	349.64	08/2014 -	08/2014	0(O) -	2/19
232	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	712.82	10/2014 -	10/2014	0(O) -	2/18
233	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,423.42	10/2012 -	03/2014	17(O) -	0/11
234	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	384.67	01/2015 -	01/2015	0(O) -	0/20

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
235	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,639.56	03/2014 -	03/2014	0(O) -	4/15
236	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	24.22	08/2014 -	08/2014	0(O) -	7/20
237	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	298.14	10/2014 -	10/2014	0(O) -	3/16
238	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	775.25	641.00	01/2010 -	07/2013	42(O) -	2/11
239	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.88	11/2011 -	09/2013	22(O) -	0/4
240	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,493.74	12/2012 -	12/2013	12(O) -	0/9
241	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	281.72	02/2014 -	02/2014	0(O) -	3/17
242	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	297.45	10/2013 -	10/2013	0(O) -	2/13
243	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	123.44	07/2013 -	12/2013	5(O) -	0/13
244	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	669.25	12/2013 -	12/2013	0(O) -	2/13
245	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	149.57	11/2013 -	09/2014	10(O) -	7/20
246	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,058.95	03/2013 -	03/2014	12(O) -	4/15
247	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,562.41	12/2013 -	03/2014	3(O) -	0/13
248	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,511.10	11/2012 -	03/2015	28(O) -	0/15
249	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	759.70	07/2014 -	07/2014	0(O) -	2/14
250	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	572.96	- -	05/2014	- -	10/29
251	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	425.99	07/2014 -	02/2015	7(O) -	1/16
252	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,304.52	12/2012 -	03/2014	15(O) -	0/11
253	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	910.47	11/2013 -	12/2014	13(O) -	5/16
254	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.74	01/2013 -	12/2014	23(O) -	5/18
255	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	03/2015	0(O) -	0/0
256	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,750.74	11/2009 02/2013	10/2013	47(O) 8(R)	0/4
257	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	318.00	08/2015 -	08/2015	0(O) -	11/12

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
258	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
259	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	353.24	07/2014 -	05/2016	22(O) -	1/1
260	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	443.49	09/2010 -	-	-	0/5
261	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	721.59	06/2015 -	06/2015	0(O) -	3/28
	Total		243,028.99 -	262,286.39	122,367.53				352/1356
	<u>Railways</u>								
262	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	483.50	03/2014 -	12/2015	21(O) -	0/0
263	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	383.48	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
264	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,820.00	120.53	- -	-	-	0/0
265	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	396.76	03/2011 03/2011	03/2011	-	0/0
266	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	725.00	553.35	06/1999 03/2011	03/2011	-	0/0
267	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	307.00	-	- -	-	-	0/0
268	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,566.00	117.90	- -	-	-	0/0
269	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	199.75	30.73	- -	-	-	0/0
270	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	1,215.30	17.21	03/2013 -	03/2013	-	0/0
271	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.35	- -	-	-	0/0
272	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	477.57	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
273	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	225.88	12/2010 03/2011	03/2011	-	0/0
274	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	244.66	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
275	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.48	91.59	04/2014 -	03/2017	35(O) -	0/0
276	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	195.64	64.18	- -	-	-	0/0
277	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	735.19	03/2010 -	12/2015	69(O) -	0/0
278	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,762.83	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
279	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	169.89	12/2012 -	12/2013	12(O) -	0/0
280	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	191.35	03/2011 -	-	-	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
281	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.72	03/2012 -	-	-	0/0
282	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
283	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	954.23	12/2012 01/2013	04/2013	-	0/0
284	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	295.00	0.06	- -	-	-	0/0
285	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
286	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
287	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	243.78	25.79	- -	-	-	0/0
288	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	338.72	- -	12/2013	-	0/0
289	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	130.98	12/2012 -	-	-	0/0
290	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	100.07	- -	-	-	0/0
291	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	218.54	- -	03/2014	-	0/0
292	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	492.47	12/2012 12/2012	02/2013	-	0/0
293	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	914.98	642.65	- -	12/2012	-	0/0
294	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	96.22	12/2011 02/2012	02/2012	-	0/0
295	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
296	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
297	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	221.58	12/2008 -	09/2014	69(O) -	0/0
298	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	248.49	06/2013 06/2013	12/2014	18(O) 18(R)	0/0
299	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240(O) -	0/0
300	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	281.25	02/2011 02/2011	03/2013	-	0/0
301	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	280.00	116.78	02/2006 -	-	-	0/0
302	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	688.17	- -	03/2012	-	0/0
303	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
304	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	343.64	- 05/2009	05/2009	-	0/0
305	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	569.78	03/1994 -	10/2013	235(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
306	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	126.50	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
307	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	186.95	- -	-	-	0/0
308	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	217.64	- 09/2009	-	-	0/0
309	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
310	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	412.91	651.15	- -	01/2013	-	0/0
311	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	149.24	- -	03/2014	-	0/0
312	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.01	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
313	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	101.17	- -	-	-	0/0
314	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	26.54	03/2015 -	03/2015	0(O) -	0/0
315	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	836.10	06/2007 -	06/2007	-	0/0
316	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	708.64	03/2012 08/2012	-	-	0/0
317	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	693.39	442.99	03/2012 03/2012	12/2012	-	0/0
318	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,503.51	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
319	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	246.75	03/2014 -	03/2014	0(O) -	0/0
320	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	294.32	03/2012 03/2012	03/2013	-	0/0
321	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,461.89	- -	03/2013	-	0/0
322	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	643.00	-	- -	-	-	0/0
323	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	511.26	- -	03/2014	-	1/1
324	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	775.36	760.65	- -	10/2012	-	0/0
325	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	754.13	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
326	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	117.78	- -	-	-	0/0
327	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	244.34	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
328	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	255.10	- -	03/2014	-	0/0
329	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
330	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	483.81	- 03/2010	03/2010	-	0/0
331	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,562.12	07/2005 -	-	-	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
332	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	163.01	- -	-	-	0/0
333	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	288.18	03/2012 03/2013	03/2013	-	0/0
334	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
335	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	352.23	- -	12/2012	-	0/0
336	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.26	12/2012 -	03/2015	27(O) -	0/0
337	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	384.00	05/2008 03/2011	-	-	0/0
338	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	222.78	03/2002 -	07/2013	136(O) -	0/0
339	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,582.57	03/2009 -	03/2015	72(O) -	0/0
340	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.56	07/2008 -	07/2008	-	0/0
341	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	472.00	172.72	- -	02/2013	-	0/0
342	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	688.14	12/2011 12/2011	03/2013	-	0/0
343	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0
344	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	437.86	03/2012 03/2013	03/2013	-	0/0
345	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	1,190.05	314.06	- -	-	-	0/0
346	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,209.40	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
347	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	190.51	- -	03/2012	-	0/0
348	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	658.93	02/2009 -	03/2012	-	0/0
349	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	356.76	07/2012 -	-	-	0/0
350	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
351	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	136.92	- -	03/2015	-	0/0
352	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,446.69	12/2008 -	03/2015	75(O) -	0/0
353	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.22	- -	03/2015	-	0/0
354	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24(O) -	0/0
355	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	2,913.51	302.71	03/2016 -	03/2016	0(O) -	0/0
356	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	56.57	03/2014 -	03/2016	24(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
357	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	157.91	03/2016 -	03/2016	0(O) -	0/0
358	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	47.45	03/2016 -	06/2016	3(O) -	0/0
359	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	453.72	03/2008 06/2008	-	-	0/0
360	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,802.56	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
361	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	610.14	- -	03/2012	-	0/0
362	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	139.99	12/2010 12/2010	12/2010	-	0/0
363	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.92	808.27	- -	03/2013	-	0/6
364	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	289.93	264.04	12/2007 03/2010	-	-	0/0
365	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,076.75	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
366	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	279.07	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
367	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.90	227.75	- -	-	-	0/0
368	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.00	329.21	06/2004 -	12/2012	-	0/0
369	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,000.00	1,952.57	- -	03/2014	-	0/0
370	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	639.97	175.75	03/1998 08/2005	08/2005	-	0/0
371	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	478.76	03/2013 -	03/2014	12(O) -	0/0
372	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	222.76	03/2012 -	-	-	0/0
373	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	234.30	03/2010 -	-	-	0/0
374	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15(O) -	0/0
375	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	103.44	02/2015 -	-	-	0/0
376	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	378.80	03/2014 -	03/2014	0(O) -	0/0
377	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	126.92	- -	-	-	0/0
378	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	439.86	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
379	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	623.46	- 12/2009	02/2012	-	0/0
380	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	172.82	- -	-	-	0/0
381	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	57.70	- -	-	-	0/0
382	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	714.05	546.88	- -	-	-	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
383	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	3,176.10	3,440.96	12/2006 08/2010	08/2010	-	0/0
384	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 167.73	167.73	43.17	03/2012 -	02/2013	-	0/0
385	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201(O) -	0/0
386	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, Uttar Pradesh	04/2006	325.00 325.00	1,116.53	205.54	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
387	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62 -	1,389.62	575.05	03/2014 -	03/2014	0(O) -	0/0
388	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	589.43	198.99	- 03/2010	-	-	0/0
	Total		66,498.32 -	161,153.59	64,175.31				1/7
	Road Transport & Highways								
389	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, Uttar Pradesh	10/2012	250.50 -	250.50	127.10	10/2014 -	10/2014	0(O) -	0/0
390	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, Uttar Pradesh	01/2013	373.47 -	373.47	38.90	07/2014 -	07/2014	0(O) -	0/0
391	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	393.00	05/2013 -	03/2014	10(O) -	0/0
392	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, Bihar	05/2011	511.54 -	511.54	616.00	11/2013 -	11/2013	0(O) -	0/0
393	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI, Multi State	04/2012	624.00 -	624.00	211.60	04/2014 -	04/2014	0(O) -	0/0
394	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI, Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
395	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, Uttar Pradesh	07/2012	291.36 -	291.36	74.37	01/2014 -	01/2014	0(O) -	0/0
396	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	226.00	288.50	02/2014 -	02/2014	0(O) -	0/0
397	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	464.10	02/2014 -	04/2014	2(O) -	0/0
398	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014	0(O) -	0/0
399	2laning with PS Gopalganj-Chhapra - [N24000190]NHAI, Bihar	12/2011	325.00 -	325.00	160.90	05/2014 -	05/2014	0(O) -	0/0
400	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	1,725.00	08/2014 -	07/2015	11(O) -	0/0
401	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	1,008.50	1,325.00	06/2013 -	09/2013	3(O) -	0/0
402	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	39.02	09/2013 -	07/2014	10(O) -	0/0
403	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50 -	785.50	812.30	08/2013 -	08/2013	0(O) -	0/0
404	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	575.00	714.20	07/2013 -	07/2013	0(O) -	0/0
405	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhand	02/2012	398.00 -	398.00	431.00	02/2014 -	02/2014	0(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
406	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,126.00	08/2013 -	08/2013	0(O) -	0/0
407	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,162.00	08/2013 -	08/2013	0(O) -	0/0
408	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	256.50	08/2013 -	08/2013	0(O) -	0/0
409	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	1,396.18	943.90	09/2014 -	09/2014	0(O) -	0/0
410	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	233.00	09/2007 -	03/2014	78(O) -	0/0
411	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	2,125.24	30.19	12/2015 -	12/2015	0(O) -	0/0
412	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,063.00	11/2012 -	12/2013	13(O) -	0/0
413	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.30	01/2009 -	12/2013	59(O) -	0/0
414	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	16(O) -	0/0
415	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	06/2013	112(O) -	0/0
416	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	325.70	09/2013 -	09/2013	0(O) -	0/0
417	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	2,388.00	1,208.00	06/2014 -	06/2014	0(O) -	0/0
418	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	547.80	-	10/2013	-	2/2
419	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	13.80	01/2013 -	10/2013	9(O) -	0/0
420	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	504.20	08/2013 -	08/2013	0(O) -	0/0
421	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	281.40	06/2008 -	03/2014	69(O) -	0/0
422	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	242.60	06/2008 -	03/2014	69(O) -	0/0
423	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	237.30	06/2005 -	03/2014	105(O) -	0/0
424	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	280.50	04/2010 -	11/2014	55(O) -	0/0
425	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53(O) -	0/0
426	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	803.40	03/2013 -	12/2013	9(O) -	0/0
427	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	638.90	-	12/2013	-	0/1
428	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	09/2013	4(O) -	0/0
429	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	410.00	10/2011 -	03/2014	29(O) -	0/0
430	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	795.20	10/2011 -	06/2014	32(O) -	0/0
431	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
432	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015	0(O) -	0/0
433	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	646.60	05/2010 -	10/2013	41(O) -	0/0
434	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	538.10	07/2013 -	07/2013	0(O) -	0/0
435	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6(O) -	0/0
436	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	693.70	- -	07/2013	- -	1/1
437	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	246.20	06/2008 -	12/2013	66(O) -	0/0
438	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	204.80	05/2008 -	12/2013	67(O) -	0/0
439	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	295.40	09/2010 -	08/2014	47(O) -	0/0
440	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	313.50	08/2013 -	02/2015	18(O) -	0/0
441	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	1,573.00	13.50	09/2015 -	09/2015	0(O) -	0/0
442	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	461.60	09/2008 -	12/2013	63(O) -	0/0
443	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	1,232.00	119.60	08/2015 -	08/2015	0(O) -	0/0
444	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	42.90	10/2013 -	11/2015	25(O) -	0/0
445	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0
446	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014	66(O) -	0/0
447	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	06/2013	112(O) -	0/0
448	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,320.00	08/2013 -	08/2013	0(O) -	0/0
449	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	259.90	04/2008 -	03/2014	71(O) -	0/0
450	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	199.40	04/2008 -	03/2014	71(O) -	0/0
451	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	06/2013	44(O) -	0/0
452	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	12/2014	60(O) -	0/0
453	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	12/2013	15(O) -	0/0
454	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26(O) -	0/0
455	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74(O) -	0/0
456	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	314.80	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
457	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	141.70	07/2009 -	05/2014	58(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
458	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79(O) -	0/0
459	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	259.70	10/2013 -	03/2014	5(O) -	0/0
460	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.15	08/2004 -	08/2013	108(O) -	0/0
461	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.52	08/2004 07/2010	08/2013	108(O) 37(R)	0/0
462	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	946.20	01/2013 -	06/2013	5(O) -	0/0
463	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,720.00	- -	07/2013	- -	3/3
464	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	447.50	05/2013 -	02/2014	9(O) -	0/0
465	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8(O) -	0/0
466	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	640.10	02/2013 -	09/2013	7(O) -	0/0
467	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
468	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	506.20	09/2009 -	12/2013	51(O) -	0/0
469	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	536.00	501.60	01/2014 -	01/2014	0(O) -	0/0
470	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,967.00	12/2012 -	08/2013	8(O) -	0/0
471	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	276.90	10/2008 -	09/2013	59(O) -	0/0
472	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.90	10/2008 -	12/2013	62(O) -	0/0
473	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	702.16	450.80	07/2014 -	07/2014	0(O) -	0/0
474	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.50	- -	06/2014	- -	2/3
475	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	09/2013	16(O) -	0/0
476	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42(O) -	0/0
477	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.80	09/2009 -	09/2014	60(O) -	0/0
478	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	101.10	07/2012 -	07/2014	24(O) -	0/0
479	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014	67(O) -	0/0
480	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68(O) -	0/0
481	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73(O) -	0/0
482	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	146.30	04/2009 -	12/2014	68(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
483	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,431.00	06/2013 -	03/2014	9(O) -	0/0
484	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	512.70	03/2013 -	03/2014	12(O) -	0/0
485	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
486	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	299.20	06/2008 -	12/2013	66(O) -	0/0
487	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54(O) -	0/0
488	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	484.19	281.30	10/2014 -	10/2014	0(O) -	0/0
489	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	300.90	04/2008 -	05/2014	73(O) -	0/0
490	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	262.60	06/2008 -	09/2013	63(O) -	0/0
491	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	283.80	06/2008 -	09/2013	63(O) -	0/0
492	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
493	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	268.60	06/2011 06/2011	08/2013	26(O) 26(R)	0/2
494	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,127.00	02/2010 -	12/2014	58(O) -	0/0
495	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11(O) -	0/0
496	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013	0(O) -	0/0
497	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13(O) -	0/0
498	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	1,262.00	10/2014 -	10/2014	0(O) -	0/0
499	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	942.69	184.10	06/2014 -	06/2014	0(O) -	0/0
500	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	301.70	05/2008 -	09/2013	64(O) -	0/0
501	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	574.00	621.40	03/2014 -	03/2014	0(O) -	0/0
502	PATNA-MUZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.20	02/2013 -	10/2013	8(O) -	0/0
503	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,293.00	07/2012 -	08/2013	13(O) -	0/0
504	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	04/2014	13(O) -	0/0
505	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	835.00	122.70	01/2014 -	01/2014	0(O) -	0/0
506	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013	21(O) -	0/0
507	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17(O) -	0/0
508	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	881.20	07/2015 -	06/2016	11(O) -	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
509	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	333.30	10/2008 -	03/2014	65(O) -	0/0
510	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	1,479.00	188.90	06/2015 -	06/2015	0(O) -	0/0
511	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	1,026.00	11/2013 -	11/2013	0(O) -	0/0
512	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31(O) -	0/0
513	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	563.30	03/2013 -	12/2013	9(O) -	0/0
514	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	805.39	543.70	12/2013 -	12/2013	0(O) -	0/0
515	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	909.00	904.30	05/2014 -	05/2014	0(O) -	0/0
516	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	238.00	09/2007 -	03/2014	78(O) -	0/0
517	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	191.10	07/2008 -	03/2013	-	0/0
518	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
519	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013	0(O) -	0/0
520	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	1,535.00	1,117.00	05/2014 -	05/2014	0(O) -	0/0
521	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31(O) -	0/0
522	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
523	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	08/2013	65(O) -	0/0
524	SUNAKHALA-GANJAM (GO) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013	110(O) -	0/0
525	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,688.00	08/2011 -	12/2013	28(O) -	0/0
526	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	07/2013	49(O) -	0/0
527	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	856.30	07/2010 -	03/2014	44(O) -	0/0
528	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	1,124.00	11/2013 -	11/2013	0(O) -	0/0
529	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	0(O) -	0/0
530	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.70	05/2013 -	12/2013	7(O) -	0/0
531	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	-	04/2013	-	2/2
532	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	845.00	03/2014 -	03/2014	0(O) -	0/0
533	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	194.80	03/2008 -	02/2008	-	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
534	WADNER-DEV DHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	53.80	11/2012 -	03/2014	16(O) -	0/0
535	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	649.90	07/2013 -	06/2014	11(O) -	0/0
536	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	201.90	06/2014 -	06/2014	0(O) -	0/0
	Total		101,189.08 -	103,127.70	78,731.84				10/14
	<u>Shipping & Ports</u>								
537	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 09/2011	09/2011	-	0/0
538	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	5(O) 0(R)	0/0
539	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
540	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	418.64	12/2012 10/2013	10/2013	10(O) 0(R)	0/0
541	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
542	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014	0(O) -	0/0
543	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-1(O) 0(R)	0/0
544	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	956.18	12/2010 09/2012	03/2014	39(O) 18(R)	0/0
545	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
546	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
547	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	08/2012	-	0/0
548	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
549	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
550	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
551	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
552	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
553	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
554	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	07/2013	18(O) 10(R)	0/0
555	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		15,617.12 -	17,902.42	8,603.74				0/1
	<u>Telecommunications</u>								
556	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59(O) -	0/0
557	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
558	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00 -	229.41	67.20	02/2007 03/2012	02/2013	-	0/0
559	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL, Delhi	02/2006	229.41 -	229.41	67.21	03/2012 02/2013	-	-	0/0
560	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38(O) 21(R)	0/0
561	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL, Maharashtra	06/2006	231.38 -	168.30	86.11	10/2007 -	-	-	0/0
562	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttarakhand	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013	54(O) -	0/0
563	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
564	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL, Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34(O) 9(R)	0/0
565	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL, Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
566	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL, Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
567	Implementation of FTTH, the state of the art access , gpon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
568	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL, Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28(O) -	0/0
	Total		5,699.24 -	5,520.22	1,970.84				0/0
	<u>Urban Development</u>								
569	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP, Karnataka	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013	-	3/3
570	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
571	DELHI MRTS PHASE-III - [N28000056]DMRC, Delhi	09/2011	35,242.00 -	35,242.00	3,548.47	03/2016 -	03/2016	0(O) -	0/0
572	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	300.76	09/2014 -	05/2015	8(O) -	0/0
	Total		44,245.18 -	49,518.08	6,331.41				3/3
	<u>Water Resources</u>								
573	PAGLADIYA DAM PROJECT - [300100001]MoWR, Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0

Sector Wise Details

(Jun,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Grand Total		798,677.21	957,383.14	472,210.50				1114/3560

Sector wise current status of projects on the Flash Report

Urban Development


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

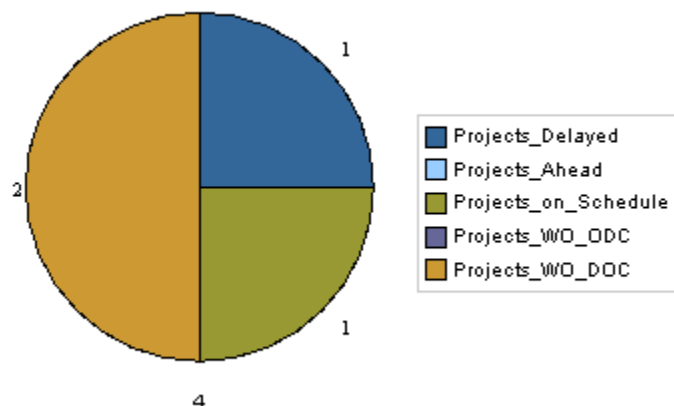

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till June, 2013 is Rs. 6331.41 crore, which is 12.8% of the revised cost of the projects.

Figures are in Rs. Crore

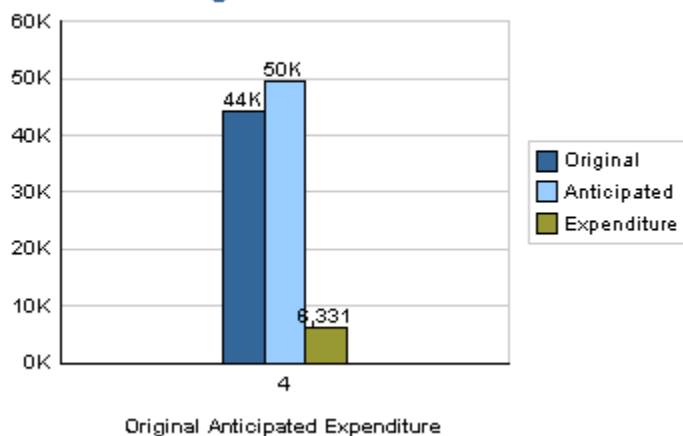

Sector wise current status of projects on the Flash Report

Telecommunications

Current Status:


Number of Projects **13**

Number of Projects Delayed **5**

Number of Projects Without Date Of Commissioning **8**

Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are delayed .8 projects do not have fixed dates of commissioning.

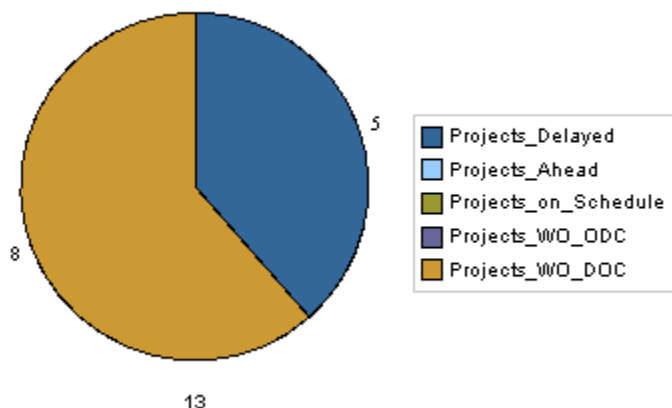

Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5520.22 crore implying a cost overrun of -3.1%. The expenditure incurred on these projects till June, 2013 is Rs. 1970.84 crore, which is 35.7% of the revised cost of the projects.

Figures are in Rs. Crore

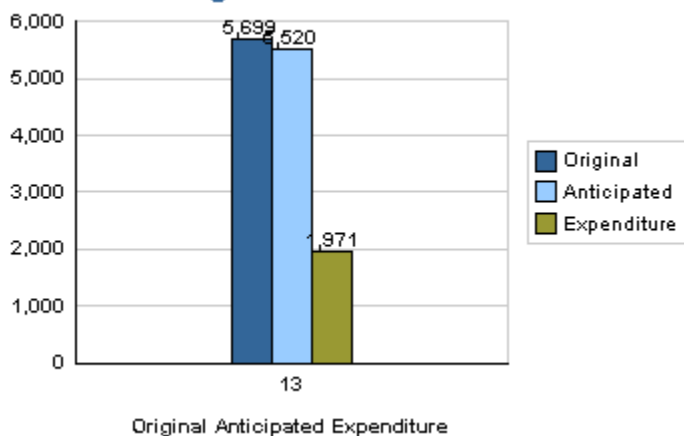

Sector wise current status of projects on the Flash Report


Shipping & Ports

Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	6
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	11

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 1 project are on schedule and 6 projects are delayed .11 projects do not have fixed dates of commissioning.

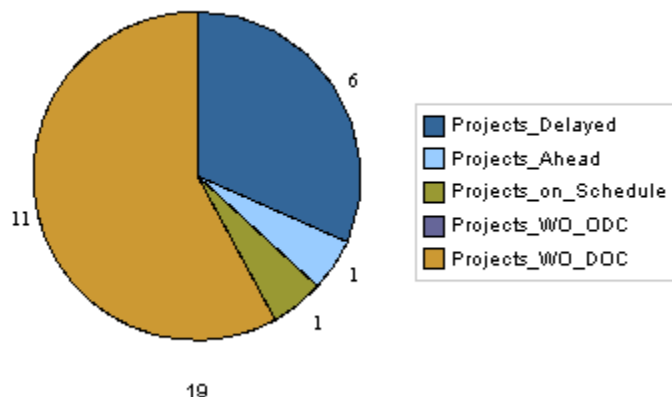

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till June, 2013 is Rs. 8603.74 crore, which is 48.1% of the revised cost of the projects.

Figures are in Rs. Crore

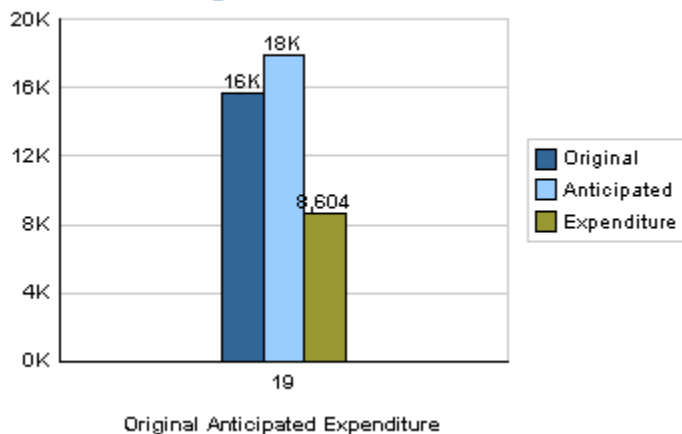

Sector wise current status of projects on the Flash Report

Road Transport & Highways


Current Status:

Number of Projects	148
Number of Projects On Schedule	46
Number of Projects Delayed	94

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 148 projects, 46 projects are on schedule and 94 projects are delayed .3 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

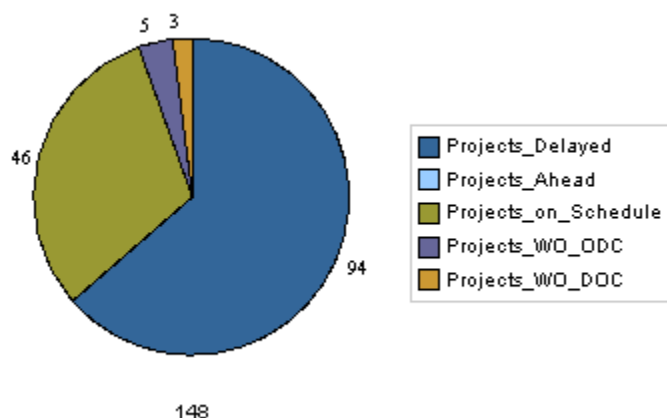

Investment Scenario

The Total Original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 101189.08 crore but this was subsequently revised to Rs. 103127.7 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till June, 2013 is Rs. 78731.84 crore, which is 76.3% of the revised cost of the projects.

Figures are in Rs. Crore

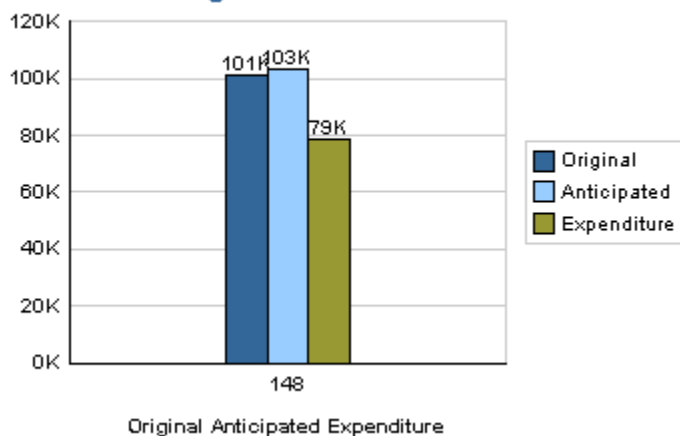

Sector wise current status of projects on the Flash Report

Railways


Current Status:

Number of Projects	127
Number of Projects On Schedule	7
Number of Projects Delayed	34

Number of Projects Without Original Date of Commissioning	10
Number of Projects Without Date Of Commissioning	76

Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 7 projects are on schedule and 34 projects are delayed .76 projects do not have fixed dates of commissioning.10 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

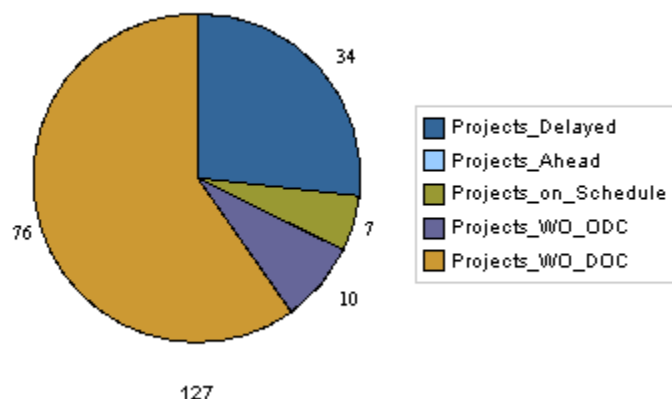

Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 66498.32 crore but this was subsequently revised to Rs. 161153.59 crore implying a cost overrun of 142.3%. The expenditure incurred on these projects till June, 2013 is Rs. 64175.31 crore, which is 39.8% of the revised cost of the projects.

Figures are in Rs. Crore

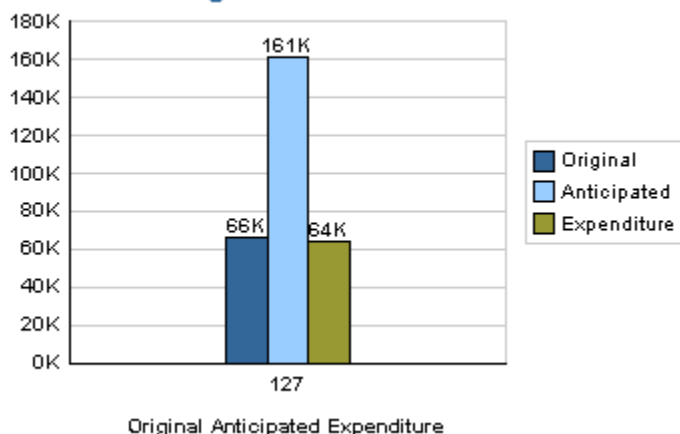

Sector wise current status of projects on the Flash Report


Power

Current Status:

Number of Projects	103
Number of Projects On Schedule	41
Number of Projects Delayed	52
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 103 projects, 2 projects are ahead of schedule, 41 projects are on schedule and 52 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

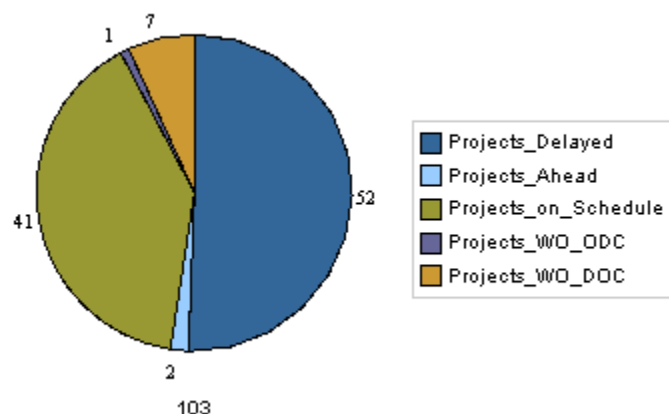

Investment Scenario

The Total Original cost of implementation of 103 projects when sanctioned, was of the order of Rs. 243028.99 crore but this was subsequently revised to Rs. 262286.39 crore implying a cost overrun of 7.9%. The expenditure incurred on these projects till June, 2013 is Rs. 122367.53 crore, which is 46.7% of the revised cost of the projects.

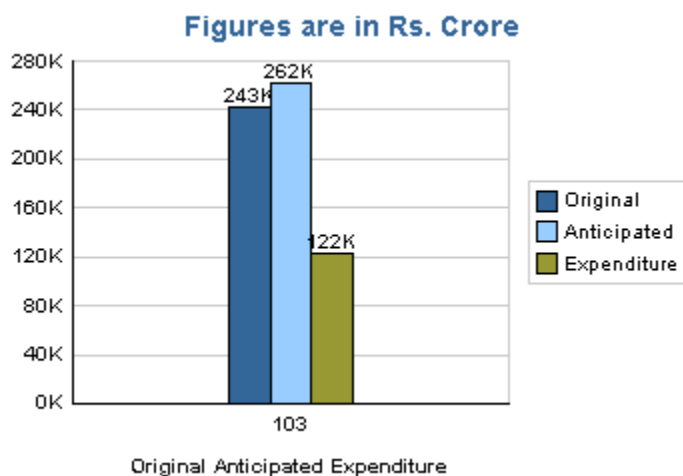

Sector wise current status of projects on the Flash Report

Petroleum


Current Status:

Number of Projects	74
Number of Projects On Schedule	22
Number of Projects Delayed	44

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 74 projects, 22 projects are on schedule and 44 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

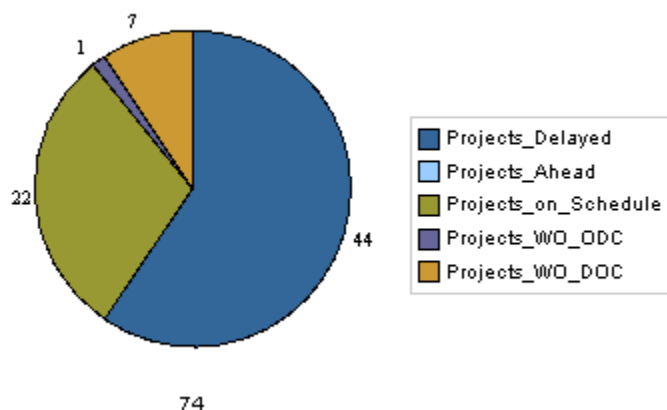

Investment Scenario

The Total Original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 166849.67 crore but this was subsequently revised to Rs. 182105.16 crore implying a cost overrun of 9.1%. The expenditure incurred on these projects till June, 2013 is Rs. 88364.7 crore, which is 48.5% of the revised cost of the projects.

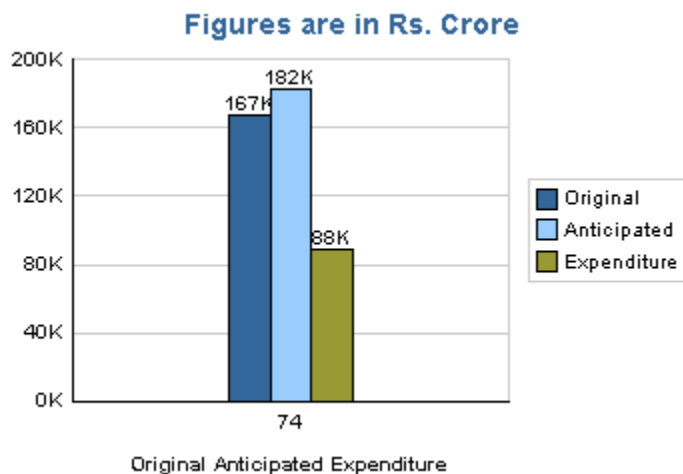

Sector wise current status of projects on the Flash Report


Steel

Current Status:

Number of Projects	17
Number of Projects On Schedule	2
Number of Projects Delayed	15

Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 2 projects are on schedule and 15 projects are delayed.

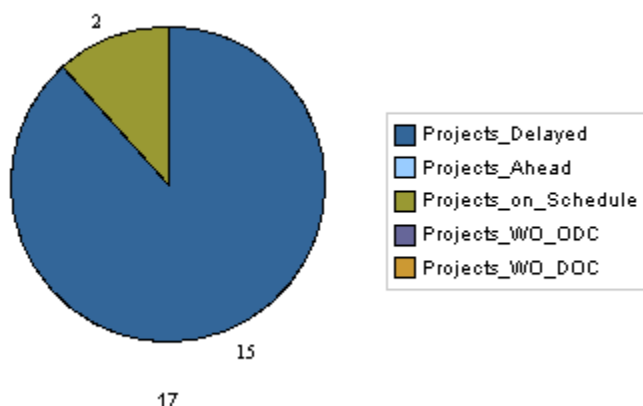

Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till June, 2013 is Rs. 51276.24 crore, which is 71.8% of the revised cost of the projects.

Figures are in Rs. Crore

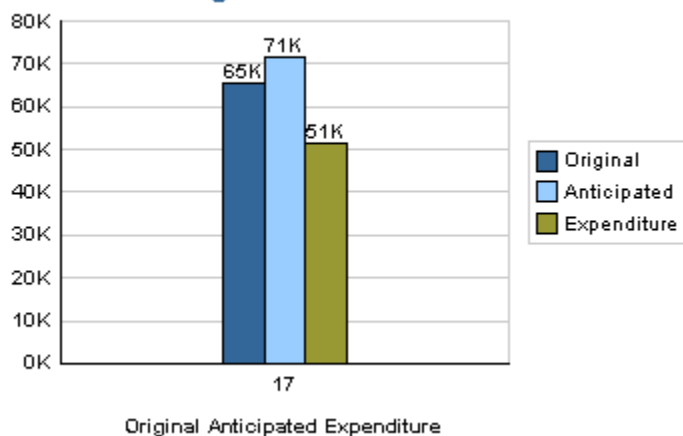

Sector wise current status of projects on the Flash Report

Coal


Current Status:

Number of Projects	55
Number of Projects On Schedule	22
Number of Projects Delayed	28

Number of Projects Without Date Of Commissioning 5

Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 22 projects are on schedule and 28 projects are delayed .5 projects do not have fixed dates of commissioning.

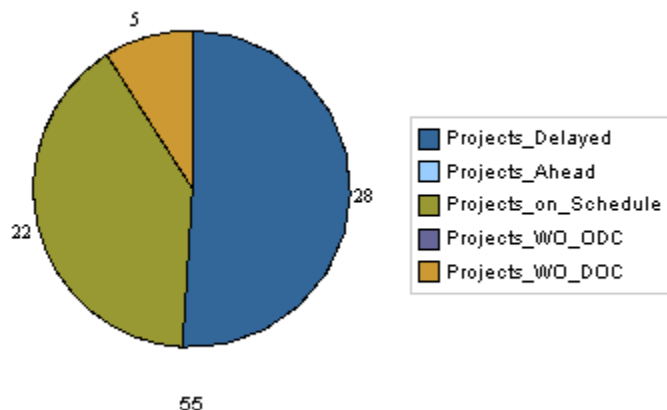

Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41212.5 crore implying a cost overrun of 8.1%. The expenditure incurred on these projects till June, 2013 is Rs. 15064.77 crore, which is 36.6% of the revised cost of the projects.

Figures are in Rs. Crore

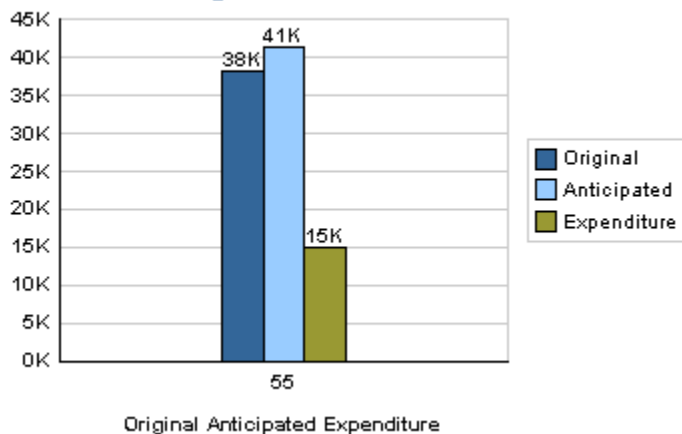

Sector wise current status of projects on the Flash Report

Civil Aviation


Current Status:

Number of Projects	7
Number of Projects On Schedule	3
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 7 projects, 3 projects are on schedule and 2 projects are delayed .2 projects do not have fixed dates of commissioning.

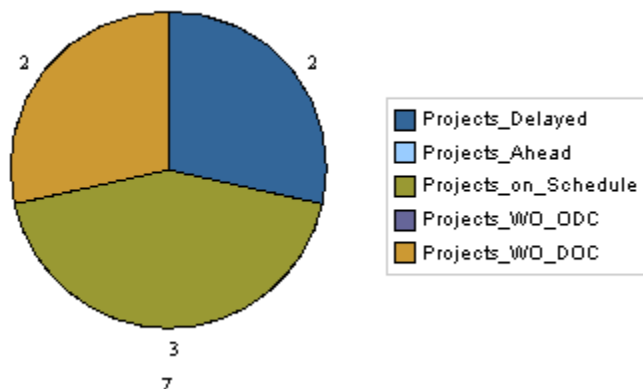

Investment Scenario

The Total Original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 5691.18 crore but this was subsequently revised to Rs. 6280.67 crore implying a cost overrun of 10.4%. The expenditure incurred on these projects till June, 2013 is Rs. 5408.64 crore, which is 86.1% of the revised cost of the projects.

Figures are in Rs. Crore

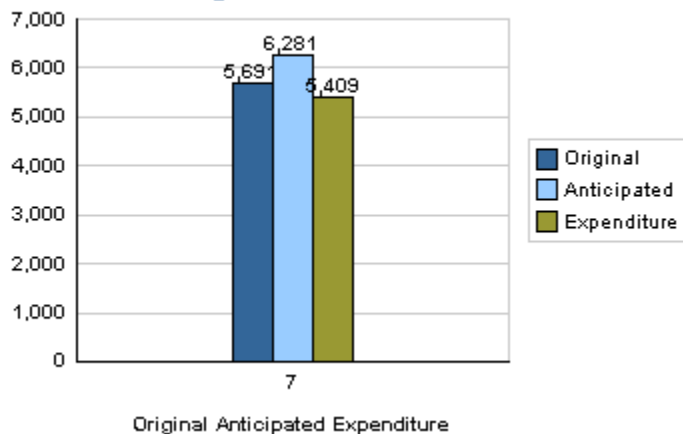

Sector wise current status of projects on the Flash Report


Atomic Energy

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

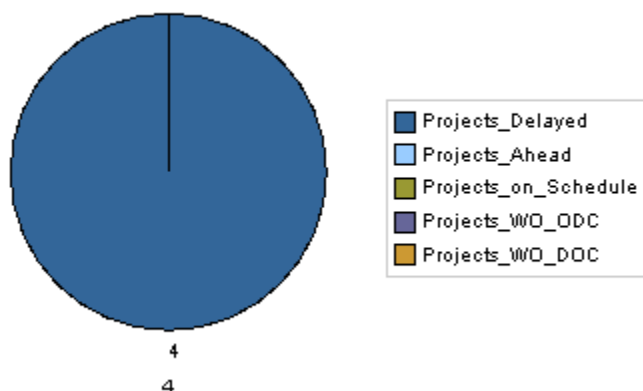

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till June, 2013 is Rs. 25369.48 crore, which is 54.3% of the revised cost of the projects.

Figures are in Rs. Crore

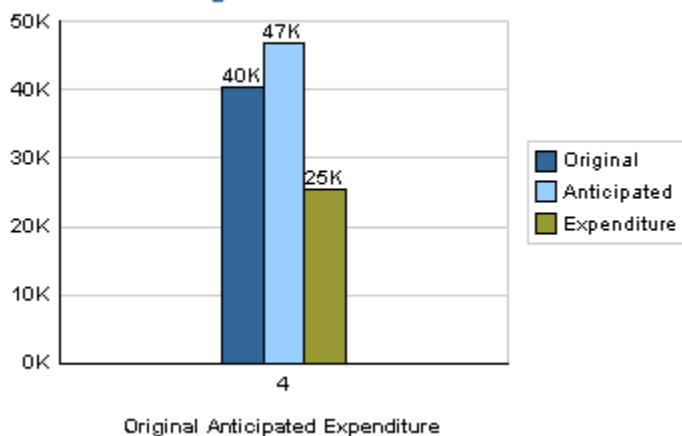

ANNEXURES

LIST OF CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	37	31097.13	38953.36	21789.51
2	Arunachal Pradesh	4	9512.22	17330.32	9553.65
3	Assam	39	23597.30	37785.69	24636.84
4	Bihar	30	26917.64	35131.24	26517.71
5	Chhatisgarh	24	58278.32	59362.92	20610.93
6	Delhi	4	38214.41	38194.82	3983.64
7	Goa	1	335.61	335.61	242.98
8	Gujarat	25	34101.28	35196.99	12640.71
9	Haryana	8	4054.38	5736.96	7089.70
10	Himachal Pradesh	5	13355.57	17263.19	13475.31
11	Jammu and Kashmir	10	14926.96	34825.56	14735.24
12	Jharkhand	24	15305.51	19508.95	9518.60
13	Karnataka	27	47076.40	56474.71	24563.40
14	Kerala	7	20376.67	22170.22	5496.33
15	Madhya pradesh	20	18545.58	18953.75	8494.08
16	Maharashtra	48	88574.45	102190.06	46360.72
17	Manipur	1	727.56	4453.50	1503.51
18	Meghalaya	2	762.00	762.00	790.10
19	Mizoram	2	1532.97	3307.11	517.58
20	Multi State	110	143632.58	157891.01	78097.99
21	Nagaland	1	850.00	2441.48	8.94
22	Odisha	30	56171.63	63436.93	39489.83
23	Punjab	5	2063.38	3005.15	3654.54
24	Rajasthan	14	21115.76	21355.97	8865.85
25	Sikkim	2	1648.94	3690.04	290.59
26	Tamil Nadu	32	48788.07	61732.81	41743.98
27	Tripura	3	1522.39	2652.48	1240.87
28	Uttar Pradesh	27	21281.92	25861.13	13592.50
29	Uttarakhand	5	7624.21	8564.64	2601.59
30	West Bengal	26	46686.37	58814.54	30103.28
TOTAL		573	798677.21	957383.14	472210.50

List of projects without Original Date of Commissioning

(Jun,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Petroleum</u>								
1	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	-	52/53
	Total		756.00 -	898.00	913.72				52/53
	<u>Power</u>								
2	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	572.96	- -	05/2014	-	10/29
	Total		421.01 -	623.44	572.96				10/29
	<u>Railways</u>								
3	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
4	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	338.72	- -	12/2013	-	0/0
5	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	218.54	- -	03/2014	-	0/0
6	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	511.26	- -	03/2014	-	0/1
7	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	255.10	- -	03/2014	-	0/0
8	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,000.00	1,952.57	- -	03/2014	-	0/0
9	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	149.24	- -	03/2014	-	0/0
10	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.22	- -	03/2015	-	0/0
11	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	136.92	- -	03/2015	-	0/0
12	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
	Total		3,035.86 -	8,826.81	4,008.70				0/1
	<u>Road Transport & Highways</u>								
13	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,720.00	- -	07/2013	-	3/3
14	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	693.70	- -	07/2013	-	1/1

(Jun,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Antici pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	547.80	- -	10/2013	-	2/2
16	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	638.90	- -	12/2013	-	0/1
17	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.50	- -	06/2014	-	2/3
	Total		3,389.00 -	3,389.00	4,337.90				8/10
	Grand Total		7,601.87	13,737.25	9,833.28				70/93

List of projects without Date of Commissioning

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Civil Aviation</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013
	Total		3,750.51 -		
	<u>Coal</u>				
3	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	03/2013 -	03/2013
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
5	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	03/2013 -	-
6	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	03/2012 -	-
7	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	- -	-
	Total		2,754.23 -		
	<u>Petroleum</u>				
8	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	- -	03/2013
9	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 973.79	03/2011 05/2011	05/2013
10	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 -	01/2012 -	-
11	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	09/2012 -	-
12	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
13	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	07/2012 07/2012	-
14	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	12/2012 -	-
	Total		7,885.30 -		
	<u>Power</u>				
15	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	02/2011 10/2012	01/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
17	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	08/2012 -	03/2013
18	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	10/2012 -	03/2013
19	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	03/2007 09/2012	04/2013
20	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	-
21	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		15,617.89 -		
	<u>Railways</u>				
22	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005
23	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
24	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
25	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
26	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
27	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
28	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
29	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011
30	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
31	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
32	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
33	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
34	Dakshin-barasal-Iakshmikanapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
35	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
36	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
37	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
38	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
39	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
40	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
41	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
42	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
43	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
44	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
45	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
46	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
47	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
48	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013
49	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
50	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013
51	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013
52	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013
53	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
54	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013
55	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013
57	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013
58	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013
59	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
60	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
61	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
62	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
63	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
64	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	-
65	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
66	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-
67	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
68	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
69	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-
70	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-
71	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-
72	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-
73	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-
74	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-
75	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
76	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-
77	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
78	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
79	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
80	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
81	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
82	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
83	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
84	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
85	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
86	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
87	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
88	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
89	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
90	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
91	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
92	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
93	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
94	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
95	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-
96	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
97	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		22,014.71 -		
	<u>Road Transport & Highways</u>				
98	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008
99	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013
100	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	- -	04/2013
	Total		1,071.27 -		
	<u>Shipping & Ports</u>				
101	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	- 01/2009	12/2010
102	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
103	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 09/2011	09/2011
104	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
105	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	08/2012
106	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
107	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
108	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
109	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
110	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013
111	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		7,399.48 -		
	<u>Telecommunications</u>				
112	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
113	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
114	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013
115	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
116	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
117	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
118	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
119	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 02/2013	-
	Total		2,764.39 -		
	<u>Urban Development</u>				
120	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	06/2011 -	03/2013
121	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>Water Resources</u>				
122	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		70,309.86		

List of Projects Ahead of Schedule w.r.t. Original Schedule

						(Jun,2013)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	50.32	06/2016 -	04/2015
2	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	190.02	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	240.34		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		1,028.10 -	1,012.23	554.60		
	Grand Total		4,472.19	4,456.32	794.94		

List of on schedule Projects w.r.t. Original Schedule

(Jun,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065]	9/2008	626.00 -	626.00	449.97	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	108.03	03/2015 -	03/2015
3	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		1,295.60 -	1,295.60	558.02		
	<u>Coal</u>						
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	159.80	03/2015 03/2015	03/2015
5	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	445.14	03/2016 03/2016	03/2016
6	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	45.02	03/2014 03/2014	03/2014
7	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	149.34	03/2017 -	03/2017
8	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	84.50	03/2015 -	03/2015
9	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	44.50	03/2016 -	03/2016
10	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
11	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
12	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	36.82	03/2015 -	03/2015
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016
14	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	259.21	03/2016 -	03/2016
15	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	38.62	03/2014 -	03/2014
16	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
17	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.88	03/2018 03/2018	03/2018
18	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
19	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.02	03/2015 -	03/2015
20	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
22	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	52.18	03/2016 -	03/2016
23	RAMAGUNDUM OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
24	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.02	07/2016 -	07/2016
25	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.30	03/2020 -	03/2020
	Total		10,739.01 -	10,367.67	1,474.54		
	<u>Petroleum</u>						
26	Wax Project - [N16000101]	6/2010	576.60 -	576.60	34.77	12/2013 -	12/2013
27	Development of WO-16 Cluster Fields - [N16000105]	6/2010	2,523.00 -	2,523.00	955.50	01/2014 -	01/2014
28	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	4,763.44	02/2014 -	02/2014
29	Mehesana Redevelopment - [N16000121]	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
30	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	202.94	4.12	01/2014 -	01/2014
31	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	741.77	05/2015 -	05/2015
32	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]	10/2011	200.69 -	200.69	2.96	07/2014 -	07/2014
33	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	61.34	12/2014 -	12/2014
34	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
35	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]	4/2011	152.89 -	152.89	3.79	06/2013 -	06/2013
36	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	31.35	07/2015 -	07/2015
37	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]	6/2009	486.00 -	486.00	52.43	09/2013 -	09/2013
38	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
39	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	63.36	11/2015 -	11/2015
40	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	4.89	12/2014 -	12/2014
41	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	54.18	03/2014 -	03/2014
42	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	409.63	05/2014 -	05/2014
43	Construction of three ETps, Mehsana - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
45	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	145.57	03/2015 -	03/2015
46	Ankleswar Redevelopment - [N16000122]	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014
47	Ahmedabad Redevelopment - [N16000120]	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014
	Total		38,556.86 -	38,067.62	9,870.85		
	<u>Power</u>						
48	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	384.67	01/2015 -	01/2015
49	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	669.25	12/2013 -	12/2013
50	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	970.31	12/2013 -	12/2013
51	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	2.26	03/2015 -	03/2015
52	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	115.30	06/2015 -	06/2015
53	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
54	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
55	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017
56	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,083.00	05/2017 -	05/2017
57	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
58	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	92.22	01/2014 -	01/2014
59	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	305.71	01/2015 -	01/2015
60	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	93.67	08/2014 -	08/2014
61	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	105.63	08/2014 -	08/2014
62	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	281.72	02/2014 -	02/2014

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
63	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	349.64	08/2014 -	08/2014
64	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	759.70	07/2014 -	07/2014
65	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	757.21	08/2014 -	08/2014
66	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	161.99	06/2014 -	06/2014
67	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	78.99	03/2015 -	03/2015
69	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	318.00	08/2015 -	08/2015
70	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,508.00	11/2016 -	11/2016
71	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,008.00	09/2016 -	09/2016
72	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	1,629.00	12/2016 -	12/2016
73	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	171.52	11/2014 -	11/2014
74	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	712.82	10/2014 -	10/2014
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	153.17	11/2014 -	11/2014
76	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	260.49	08/2014 -	08/2014
77	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	39.74	06/2014 -	06/2014
78	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	721.59	06/2015 -	06/2015
79	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
80	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
81	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	298.14	10/2014 -	10/2014
82	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	24.22	08/2014 -	08/2014
83	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	347.09	02/2015 -	02/2015
84	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	297.45	10/2013 -	10/2013
85	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	903.15	09/2014 -	09/2014

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
86	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	1,142.61	08/2013 -	08/2013
87	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	1,639.56	03/2014 -	03/2014
88	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	982.34	05/2014 -	05/2014
	Total		102,561.85 -	102,561.85	18,437.68		
	<u>Railways</u>						
89	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	157.91	03/2016 -	03/2016
90	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	575.05	03/2014 -	03/2014
91	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
92	Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	378.80	03/2014 -	03/2014
93	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111	4/2010	2,619.02 -	2,913.51	302.71	03/2016 -	03/2016
94	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112	4/2008	829.74 -	829.74	26.54	03/2015 -	03/2015
95	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113	4/2008	653.19 -	653.46	246.75	03/2014 -	03/2014
	Total		14,834.36 -	15,129.12	1,687.76		
	<u>Road Transport & Highways</u>						
96	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
97	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168	3/2011	785.50 -	785.50	812.30	08/2013 -	08/2013
98	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,320.00	08/2013 -	08/2013
99	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
100	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	281.30	10/2014 -	10/2014
101	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	450.80	07/2014 -	07/2014
102	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	74.37	01/2014 -	01/2014
103	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	943.90	09/2014 -	09/2014
104	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	201.90	06/2014 -	06/2014
105	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	256.50	08/2013 -	08/2013
106	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	1,126.00	08/2013 -	08/2013

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84 -	1,078.84	1,162.00	08/2013 -	08/2013
108	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]	1/2011	575.00 -	575.00	714.20	07/2013 -	07/2013
109	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	30.19	12/2015 -	12/2015
110	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	38.90	07/2014 -	07/2014
111	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	127.10	10/2014 -	10/2014
112	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	13.50	09/2015 -	09/2015
113	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	119.60	08/2015 -	08/2015
114	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	184.10	06/2014 -	06/2014
115	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	188.90	06/2015 -	06/2015
116	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENGTH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	211.60	04/2014 -	04/2014
117	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
118	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
119	SAMAIKHIALI GANDHIDHAM - [N24000223]	9/2010	805.39 -	805.39	543.70	12/2013 -	12/2013
120	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
121	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]	9/2011	574.00 -	574.00	621.40	03/2014 -	03/2014
122	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]	11/2011	1,535.00 -	1,535.00	1,117.00	05/2014 -	05/2014
123	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	9/2011	2,848.00 -	2,848.00	845.00	03/2014 -	03/2014
124	2-LANNING OF SHILONG BYPASS - [N24000181]	2/2011	226.00 -	226.00	288.50	02/2014 -	02/2014
125	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	501.60	01/2014 -	01/2014
126	Tirupati - Tiruthani - Chennai - [N24000178]	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
127	2 Laning of Muzaffarpur - Sonbarsa - [N24000174]	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
128	BAREILY-SITAPUR - [N24000200]	3/2011	1,046.00 -	1,046.00	325.70	09/2013 -	09/2013
129	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,208.00	06/2014 -	06/2014
130	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	904.30	05/2014 -	05/2014
131	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	504.20	08/2013 -	08/2013

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
132	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	122.70	01/2014 -	01/2014
133	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	431.00	02/2014 -	02/2014
134	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	160.90	05/2014 -	05/2014
135	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
136	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	616.00	11/2013 -	11/2013
137	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
138	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,026.00	11/2013 -	11/2013
139	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,262.00	10/2014 -	10/2014
140	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	1,124.00	11/2013 -	11/2013
141	DEOLI-KOTA - [N24000148	1/2011	593.00 -	593.00	538.10	07/2013 -	07/2013
	Total		42,017.52 -	42,017.52	21,349.89		
	<u>Shipping & Ports</u>						
142	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
	Total		966.46 -	994.82	363.20		
	<u>Steel</u>						
143	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	57.57	08/2014 -	08/2014
144	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	3.10	12/2014 -	12/2014
	Total		587.55 -	587.55	60.67		
	<u>Urban Development</u>						
145	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	3,548.47	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	3,548.47		
	Grand Total		246,801.21	246,263.75	57,351.08		

List of Delayed Projects w.r.t. Original and Revised Schedule

(Jun,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,262.00	12/2008 -	03/2014	63	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,140.48	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,940.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,027.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	25,369.48				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	242.98	05/2012 -	06/2013	13	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.80	01/2011 04/2013	12/2014	47	20
	Total		645.07 -	645.07	474.78				
	<u>Coal</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,726.15	06/2009 -	01/2014	55	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	114.77	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.36	03/2011 -	03/2014	36	-
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.81	03/2013 -	03/2014	12	-
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,409.33	03/2012 -	03/2014	24	-
12	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	112.08	03/2012 -	03/2014	24	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	701.71	03/2013 09/2012	10/2014	19	25
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.66	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.74	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.28	03/2010 -	03/2015	60	-
17	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	87.20	12/2012 -	03/2015	27	-
18	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	113.75	03/2013 -	03/2015	24	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SECL, Andhra Pradesh	03/2010	181.19 -	181.19	34.29	03/2012 -	03/2015	36	-
20	Purnadih OCP (3.0 MTY) - [N06000085]CCL, Jharkhand	07/2008	210.98 -	210.98	89.20	03/2013 -	03/2015	24	-
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,408.71	03/2014 -	03/2016	24	-
22	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,246.22	03/2014 -	03/2016	24	-
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, Jharkhand	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016	44	-
24	CHURCHA ROUG (1.35MTY) - [N06000046]SECL, Chhatisgarh	06/2008	462.35 -	462.35	265.36	03/2014 -	03/2016	24	-
25	RAJMAHAL OC EXP. - [N06000056]ECL, Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL, Maharashtra	10/2008	339.77 -	339.77	0.91	03/2014 -	03/2016	24	-
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24	-
29	Churi Benti UG (0.81 MTY) - [N06000083]CCL, Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
30	Tapin OCP (2.5 MTY) - [N06000086]CCL, Jharkhand	08/2008	264.68 -	264.68	127.50	03/2012 -	03/2016	48	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72	-
32	JAGANNATHPUR OCP (3.00 MTY) - [N06000075]SECL, Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
33	North Urimari OCP (3.0 MTY) - [N06000084]CCL, Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT (2x500 MW) - [N06000095]NLC, Tamil Nadu	06/2011	5,907.11 -	5,907.11	30.75	12/2015 -	02/2018	26	-
	Total		24,633.81 -	28,090.60	12,537.44				
	<u>Steel</u>								
35	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREM - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	260.49	02/2011 -	06/2013	28	-
36	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	253.47	08/2010 -	06/2013	34	-
37	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	10,417.06	10/2009 -	07/2013	45	-
38	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	145.98	10/2012 -	08/2013	10	-
39	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	450.00	248.98	05/2012 -	08/2013	15	-
40	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	351.04	12/2011 03/2012	12/2013	24	21
41	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 -	16,408.00	14,671.22	12/2011 -	12/2013	24	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,628.95	12/2011 -	12/2013	24	-
43	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,413.47	03/2013 -	12/2013	9	-
44	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	304.07	04/2013 12/2013	12/2013	8	0
45	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	200.10	05/2013 11/2013	03/2014	10	4
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,642.51	12/2012 -	03/2014	15	-
47	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	74.71	10/2013 -	05/2014	7	-
48	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	63.20	11/2013 -	06/2014	7	-
49	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	9,540.32	03/2013 -	09/2014	18	-
	Total		64,698.32 -	70,855.86	51,215.57				
	<u>Petrochemicals</u>								
50	ASSAM GAS CRACKER PROJECT - [N16000106]BPCL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	4,510.51				
	<u>Petroleum</u>								
51	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013	2	-
52	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	176.83	04/2012 -	06/2013	14	-
53	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	726.73	12/2011 -	07/2013	19	-
54	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	187.51	02/2013 -	07/2013	5	-
55	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,371.54	01/2012 -	07/2013	18	-
56	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	682.23	04/2012 -	07/2013	15	-
57	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	23	17
58	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,124.72	09/2012 -	09/2013	12	-
59	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24	16
60	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12	-
61	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	594.83	01/2013 -	09/2013	8	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	96.88	09/2012 -	09/2013	12	-
63	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	719.20	07/2012 -	10/2013	15	-
64	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	217.08	11/2012 -	10/2013	11	-
65	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
66	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	275.07	05/2013 -	11/2013	6	-
67	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	711.61	03/2007 03/2014	12/2013	81	-3
68	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	399.30	03/2006 03/2013	12/2013	93	9
69	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	728.30	03/2010 03/2012	12/2013	45	21
70	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	247.86	03/2012 -	12/2013	21	-
71	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	221.02	03/2013 -	12/2013	9	-
72	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26	-
73	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26	-
74	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	57.39	08/2013 -	01/2014	5	-
75	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
76	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	920.79	07/2010 05/2012	02/2014	43	21
77	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
78	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
79	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,494.50	03/2013 -	03/2014	12	-
80	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	184.41	08/2012 -	03/2014	19	-
81	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	28.10	06/2012 -	03/2014	21	-
82	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	22,254.00	11/2012 -	04/2014	17	-
83	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,347.71	03/2013 03/2014	04/2014	13	1
84	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1	-
85	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,478.23	08/2010 03/2012	05/2014	45	26
86	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014	2	-
88	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
89	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.95	09/2011 -	12/2014	39	-
90	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	586.00	5.55	07/2015 -	08/2015	1	-
91	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,881.73	09/2010 03/2012	12/2015	63	45
92	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35	-
93	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	20.90	12/2015 -	05/2016	5	-
94	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,727.13	03/2007 03/2017	03/2017	120	0
	Total		119,651.51 -	135,241.83	73,526.09				
	<u>Power</u>								
95	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	775.25	641.00	01/2010 -	07/2013	42	-
96	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	149.64	06/2012 -	07/2013	13	-
97	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	81.80	10/2012 -	07/2013	9	-
98	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	149.92	10/2011 -	07/2013	21	-
99	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.88	11/2011 -	09/2013	22	-
100	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	824.07	05/2012 -	09/2013	16	-
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	130.78	01/2013 -	09/2013	8	-
102	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	85.91	04/2013 -	09/2013	5	-
103	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	121.80	06/2012 -	09/2013	15	-
104	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	53.95	06/2012 -	09/2013	15	-
105	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,750.74	11/2009 02/2013	10/2013	47	8
106	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	747.88	08/2010 01/2013	10/2013	38	9
107	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,342.00	10/2012 -	11/2013	13	-
108	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	884.11	10/2009 -	12/2013	50	-
109	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,493.74	12/2012 -	12/2013	12	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	363.76	11/2011 -	12/2013	25	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	267.02	02/2012 -	12/2013	22	-
112	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	123.44	07/2013 -	12/2013	5	-
113	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,819.66	10/2010 01/2013	03/2014	41	14
114	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,534.87	01/2012 -	03/2014	26	-
115	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,423.42	10/2012 -	03/2014	17	-
116	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,580.90	2,051.68	08/2012 -	03/2014	19	-
117	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,820.52	08/2012 -	03/2014	19	-
118	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,304.52	12/2012 -	03/2014	15	-
119	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	572.28	11/2012 -	03/2014	16	-
120	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,058.95	03/2013 -	03/2014	12	-
121	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,562.41	12/2013 -	03/2014	3	-
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	277.02	07/2013 -	03/2014	8	-
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	826.24	04/2013 -	03/2014	11	-
124	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	887.88	08/2012 -	06/2014	22	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	355.02	11/2011 -	07/2014	32	-
126	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	5,000.00	04/2009 -	09/2014	65	-
127	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	1,117.92	605.07	08/2012 08/2013	09/2014	25	13
128	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,069.00	08/2013 -	09/2014	13	-
129	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	667.95	11/2012 -	09/2014	22	-
130	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	149.57	11/2013 -	09/2014	10	-
131	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,147.32	09/2009 06/2013	11/2014	62	17
132	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.74	01/2013 -	12/2014	23	-
133	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	910.47	11/2013 -	12/2014	13	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
134	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	425.99	07/2014 -	02/2015	7	-
135	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,511.10	11/2012 -	03/2015	28	-
136	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	23.88	04/2015 -	05/2015	1	-
137	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,045.64	08/2013 -	06/2015	22	-
138	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,886.00	07/2011 -	10/2015	51	-
139	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,841.00	03/2013 -	03/2016	36	-
140	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	353.24	07/2014 -	05/2016	22	-
141	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 -	2,978.86	489.19	07/2010 -	11/2016	76	-
142	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,606.19	01/2016 01/2016	11/2016	10	10
143	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,499.00	12/2009 -	02/2017	86	-
144	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,330.55	05/2013 05/2013	03/2017	46	46
145	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,279.31	09/2010 08/2014	12/2017	87	40
146	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,479.78	09/2009 07/2014	03/2018	102	44
	Total		120,984.15 -	137,546.20	90,245.90				
	<u>Railways</u>								
147	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	222.78	03/2002 -	07/2013	136	-
148	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	569.78	03/1994 -	10/2013	235	-
149	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	383.48	12/2009 03/2011	10/2013	46	31
150	Ghutiasarif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	126.50	12/2011 11/2013	11/2013	23	0
151	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	169.89	12/2012 -	12/2013	12	-
152	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
153	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	478.76	03/2013 -	03/2014	12	-
154	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	279.07	02/2009 02/2009	08/2014	66	66
155	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	244.34	03/2009 03/2009	08/2014	65	65
156	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	221.58	12/2008 -	09/2014	69	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
157	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,076.75	03/2009 12/2012	12/2014	69	24
158	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	248.49	06/2013 06/2013	12/2014	18	18
159	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
160	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.01	03/2007 03/2007	03/2015	96	96
161	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	754.13	12/2010 12/2010	03/2015	51	51
162	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,446.69	12/2008 -	03/2015	75	-
163	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.26	12/2012 -	03/2015	27	-
164	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,582.57	03/2009 -	03/2015	72	-
165	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,762.83	04/2008 03/2014	12/2015	92	21
166	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,802.56	10/2007 12/2012	12/2015	98	36
167	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	735.19	03/2010 -	12/2015	69	-
168	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	483.50	03/2014 -	12/2015	21	-
169	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	244.66	03/2004 12/2010	03/2016	144	63
170	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	56.57	03/2014 -	03/2016	24	-
171	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	439.86	06/2005 07/2011	06/2016	132	59
172	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	47.45	03/2016 -	06/2016	3	-
173	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	477.57	03/2005 12/2008	12/2016	141	96
174	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,209.40	03/2014 03/2016	12/2016	33	9
175	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,503.51	03/2011 03/2014	03/2017	72	36
176	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	205.54	03/2010 03/2017	03/2017	84	0
177	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.48	91.59	04/2014 -	03/2017	35	-
178	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15	-
179	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24	-
180	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201	-
	Total		26,613.39 -	75,687.17	29,800.27				

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Road Transport & Highways</u>								
181	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013	110	-
182	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54	-
183	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	06/2013	112	-
184	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya Pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	06/2013	44	-
185	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	06/2013	112	-
186	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	946.20	01/2013 -	06/2013	5	-
187	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	16	-
188	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	07/2013	49	-
189	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.52	08/2004 07/2010	08/2013	108	37
190	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.15	08/2004 -	08/2013	108	-
191	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	268.60	06/2011 06/2011	08/2013	26	26
192	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	08/2013	65	-
193	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31	-
194	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,293.00	07/2012 -	08/2013	13	-
195	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013	21	-
196	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,967.00	12/2012 -	08/2013	8	-
197	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	301.70	05/2008 -	09/2013	64	-
198	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	276.90	10/2008 -	09/2013	59	-
199	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	283.80	06/2008 -	09/2013	63	-
200	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	262.60	06/2008 -	09/2013	63	-
201	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	09/2013	16	-
202	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	09/2013	4	-
203	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,325.00	06/2013 -	09/2013	3	-
204	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	640.10	02/2013 -	09/2013	7	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
205	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	646.60	05/2010 -	10/2013	41	-
206	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
207	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.20	02/2013 -	10/2013	8	-
208	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00 -	209.00	13.80	01/2013 -	10/2013	9	-
209	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
210	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.90	10/2008 -	12/2013	62	-
211	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	264.30	01/2009 -	12/2013	59	-
212	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	461.60	09/2008 -	12/2013	63	-
213	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	299.20	06/2008 -	12/2013	66	-
214	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	204.80	05/2008 -	12/2013	67	-
215	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	246.20	06/2008 -	12/2013	66	-
216	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42	-
217	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	506.20	09/2009 -	12/2013	51	-
218	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
219	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	12/2013	15	-
220	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26	-
221	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,688.00	08/2011 -	12/2013	28	-
222	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
223	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	852.00	803.40	03/2013 -	12/2013	9	-
224	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	2,063.00	11/2012 -	12/2013	13	-
225	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
226	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	374.00	114.70	05/2013 -	12/2013	7	-
227	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	805.39	563.30	03/2013 -	12/2013	9	-
228	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	447.50	05/2013 -	02/2014	9	-
229	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	238.00	09/2007 -	03/2014	78	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
230	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014	66	-
231	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	237.30	06/2005 -	03/2014	105	-
232	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	242.60	06/2008 -	03/2014	69	-
233	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	281.40	06/2008 -	03/2014	69	-
234	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	333.30	10/2008 -	03/2014	65	-
235	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	199.40	04/2008 -	03/2014	71	-
236	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	259.90	04/2008 -	03/2014	71	-
237	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	233.00	09/2007 -	03/2014	78	-
238	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	856.30	07/2010 -	03/2014	44	-
239	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	410.00	10/2011 -	03/2014	29	-
240	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	53.80	11/2012 -	03/2014	16	-
241	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,431.00	06/2013 -	03/2014	9	-
242	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	393.00	05/2013 -	03/2014	10	-
243	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	512.70	03/2013 -	03/2014	12	-
244	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	259.70	10/2013 -	03/2014	5	-
245	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79	-
246	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	04/2014	13	-
247	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	464.10	02/2014 -	04/2014	2	-
248	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	314.80	02/2009 03/2014	05/2014	63	2
249	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	300.90	04/2008 -	05/2014	73	-
250	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	141.70	07/2009 -	05/2014	58	-
251	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68	-
252	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014	67	-
253	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	795.20	10/2011 -	06/2014	32	-
254	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
255	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	649.90	07/2013 -	06/2014	11	-
256	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-
257	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.02	09/2013 -	07/2014	10	-
258	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	101.10	07/2012 -	07/2014	24	-
259	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	295.40	09/2010 -	08/2014	47	-
260	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.80	09/2009 -	09/2014	60	-
261	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	280.50	04/2010 -	11/2014	55	-
262	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68	-
263	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73	-
264	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	146.30	04/2009 -	12/2014	68	-
265	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	12/2014	60	-
266	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,127.00	02/2010 -	12/2014	58	-
267	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
268	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	313.50	08/2013 -	02/2015	18	-
269	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
270	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,725.00	08/2014 -	07/2015	11	-
271	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13	-
272	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	42.90	10/2013 -	11/2015	25	-
273	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
274	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	881.20	07/2015 -	06/2016	11	-
	Total		54,711.29 -	56,623.08	52,658.15				
	<u>Shipping & Ports</u>								
275	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2013	06/2013	87	0
276	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	5	0

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
277	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	07/2013	18	10
278	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	418.64	12/2012 10/2013	10/2013	10	0
279	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	956.18	12/2010 09/2012	03/2014	39	18
280	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
	Total		6,223.08 -	7,475.19	5,381.60				
	<u>Telecommunications</u>								
281	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9
282	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28	-
283	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013	54	-
284	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
285	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
	Total		2,934.85 -	2,774.50	1,282.27				
	<u>Urban Development</u>								
286	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	300.76	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	300.76				
	Grand Total		469,492.08	573,079.50	347,302.82				

List of ongoing projects having time and cost overrun w.r.t original schedule

(Jun,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	16,262.00	12/2008 -	03/2014
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	4,140.48	09/2010 -	03/2015
	Total		16,663.00 -	22,947.00	20,402.48		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,726.15	06/2009 -	01/2014
4	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	701.71	03/2013 -	10/2014
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	4,409.33	03/2012 -	03/2014
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016
	Total		7,938.86 -	34,520.95	28,473.86		
	<u>Petrochemicals</u>						
8	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	4,510.51	04/2012 -	12/2013
	Total		5,460.61 -	43,440.95	32,984.37		
	<u>Petroleum</u>						
9	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	711.61	03/2007 -	12/2013
10	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	1,727.13	03/2007 -	03/2017
11	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	399.30	03/2006 -	12/2013
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	02/2014
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	03/2014
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	2,323.40 -	2,920.82	1,881.73	09/2010 03/2012	12/2015
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	5,633.44	4,478.23	08/2010 03/2012	05/2014
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	10/2007	5,713.03 -	8,813.41	7,204.61	05/2010 -	03/2014

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
17	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	32,710.00	22,254.00	11/2012 -	04/2014
18	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013
19	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64 -	2,331.62	1,557.08	06/2012 -	05/2014
20	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013
21	Development of Cluster-7 Fields - [N16000104]	03/2010	3,241.03 -	5,916.65	1,347.71	03/2013 -	04/2014
22	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	176.83	04/2012 -	06/2013
23	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014
24	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	-	10/2011 -	12/2013
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	-	10/2011 -	12/2013
	Total		53,961.35 -	115,965.85	80,086.67		
	<u>Power</u>						
26	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	3,479.78	09/2009 -	03/2018
27	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,358.91	5,000.00	04/2009 -	09/2014
28	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	6,279.31	09/2010 -	12/2017
29	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	2,330.55	05/2013 05/2013	03/2017
30	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	8,499.00	12/2009 -	02/2017
31	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	1,147.32	09/2009 -	11/2014
32	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	1,819.66	10/2010 -	03/2014
33	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	1,750.74	11/2009 -	10/2013
34	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	747.88	08/2010 -	10/2013
35	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	489.19	07/2010 -	11/2016
36	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]	07/2006	557.24 -	775.25	641.00	01/2010 -	07/2013
37	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	1,606.19	01/2016 -	11/2016

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
38	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,422.44	353.24	07/2014 -	05/2016
39	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	605.07	08/2012 -	09/2014
40	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	2,051.68	08/2012 -	03/2014
41	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	121.80	06/2012 -	09/2013
42	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	53.95	06/2012 -	09/2013
	Total		41,777.81 -	174,305.71	117,063.03		
	<u>Railways</u>						
43	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	580.83	569.78	03/1994 -	10/2013
44	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	602.18	03/1995 -	03/2015
45	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	8,822.50	03/2001 -	12/2017
46	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	222.78	03/2002 -	07/2013
47	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,814.48	244.66	03/2004 -	03/2016
48	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	4,996.65	2,762.83	04/2008 12/2011	12/2015
49	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	535.40	177.01	03/2007 03/2007	03/2015
50	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	383.48	12/2009 -	10/2013
51	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	1,041.79	754.13	12/2010 -	03/2015
52	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	2,350.00	1,446.69	12/2008 -	03/2015
53	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	477.57	03/2005 12/2008	12/2016
54	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	279.07	02/2009 02/2009	08/2014
55	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	4,453.50	1,503.51	03/2011 -	03/2017
56	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	1,076.75	03/2009 -	12/2014
57	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	1,802.56	10/2007 -	12/2015
58	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70 -	245.39	221.58	12/2008 -	09/2014
59	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	244.34	03/2009 03/2009	08/2014

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
60	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	735.19	03/2010 -	12/2015
61	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	205.54	03/2010 -	03/2017
62	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	1,209.40	03/2014 -	12/2016
63	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	141.55	03/2012 -	03/2014
64	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	439.86	06/2005 -	06/2016
65	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	483.50	03/2014 -	12/2015
66	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	91.59	04/2014 -	03/2017
67	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017
68	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	478.76	03/2013 -	03/2014
69	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	126.50	12/2011 -	11/2013
70	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,441.48	8.94	03/2015 -	03/2017
71	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	5,000.00	3,582.57	03/2009 -	03/2015
	Total		21,214.91 -	244,599.29	146,216.64		
	<u>Road Transport & Highways</u>						
72	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013
73	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014
74	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	301.70	05/2008 -	09/2013
75	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014
76	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014
77	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014
78	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	141.70	07/2009 -	05/2014
79	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
80	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	233.00	09/2007 -	03/2014
81	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs.crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		3,158.01	249,851.39	151,101.00		
			-				
	<u>Shipping & Ports</u>						
82	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00	1,460.00	956.18	12/2010	03/2014
83	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00	600.00	139.80	03/2006	06/2013
84	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]	03/2009	3,500.00	4,150.00	3,661.95	01/2012	07/2013
	Total		4,878.00	256,061.39	155,858.93		
			-				
	<u>Steel</u>						
85	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00	12,291.00	10,417.06	10/2009	07/2013
86	Bailadilla Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89	607.17	351.04	12/2011 06/2010	12/2013
87	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	216.68	145.98	10/2012	08/2013
88	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	16,408.00	14,671.22	12/2011	12/2013
89	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	230.00	343.58	260.49	02/2011	06/2013
90	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	350.00	253.47	08/2010	06/2013
	Total		24,028.89	286,277.82	181,958.19		
			-				
	<u>Telecommunications</u>						
91	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15	158.72	81.73	06/2009	12/2013
92	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]	11/2009	916.70	930.60	828.80	11/2010	09/2013
	Total		1,065.85	287,367.14	182,868.72		
			-				
	Grand Total		180,147.29	1,715,337.49	1,097,013.89		

List of ongoing projects having cost overrun w.r.t. to original schedule

(Jun,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	16,262.00	12/2008 -	03/2014
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	4,140.48	09/2010 -	03/2015
	Total		16,663.00 -	22,947.00	20,402.48		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,471.11	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	1,904.73	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	24,778.32		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,726.15	06/2009 -	01/2014
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	701.71	03/2013 -	10/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	149.34	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	4,409.33	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016
	Total		8,579.45 -	39,549.64	33,087.75		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	4,510.51	04/2012 -	12/2013
	Total		5,460.61 -	48,469.64	37,598.26		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	711.61	03/2007 -	12/2013

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,727.13	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	399.30	03/2006 -	12/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	02/2014
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	03/2014
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,881.73	09/2010 03/2012	12/2015
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,478.23	08/2010 03/2012	05/2014
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,204.61	05/2010 -	03/2014
21	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057	01/2009	756.00 -	898.00	913.72	- -	08/2013
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	22,254.00	11/2012 -	04/2014
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066	01/2008	224.00 -	394.00	312.61	- -	03/2013
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	289.64	01/2012 -	-
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	1,557.08	06/2012 -	05/2014
27	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	973.79	729.51	03/2011 -	05/2013
28	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013
29	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	1,347.71	03/2013 -	04/2014
30	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	145.57	03/2015 -	03/2015
31	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	176.83	04/2012 -	06/2013
32	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
33	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	-	10/2011 -	12/2013
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	-	10/2011 -	12/2013
	Total		58,495.36 -	126,938.98	87,108.17		
	<u>Power</u>						
36	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,479.78	09/2009 -	03/2018

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
37	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	5,000.00	04/2009 -	09/2014
38	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	6,279.31	09/2010 -	12/2017
39	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) - [180100222	10/2003	768.92 -	1,628.00	1,467.53	03/2007 -	04/2013
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	5,139.00	2,330.55	05/2013 05/2013	03/2017
41	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	8,499.00	12/2009 -	02/2017
42	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,147.32	09/2009 -	11/2014
43	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	900.71	12/2007 -	-
44	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,819.66	10/2010 -	03/2014
45	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,750.74	11/2009 -	10/2013
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,869.99	09/2008 -	03/2013
47	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	747.88	08/2010 -	10/2013
48	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	731.93	02/2011 -	01/2013
49	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	489.19	07/2010 -	11/2016
50	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018	07/2006	557.24 -	775.25	641.00	01/2010 -	07/2013
51	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,606.19	01/2016 -	11/2016
52	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,422.44	353.24	07/2014 -	05/2016
53	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,117.92	605.07	08/2012 -	09/2014
54	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013
55	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065	08/2008	2,360.95 -	2,580.90	2,051.68	08/2012 -	03/2014
56	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	572.96	- -	05/2014
57	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	121.80	06/2012 -	09/2013
58	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150	08/2008	126.18 -	159.54	53.95	06/2012 -	09/2013
	Total		51,424.02 -	197,620.40	133,683.65		
	<u>Railways</u>						
59	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	569.78	03/1994 -	10/2013

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
60	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	602.18	03/1995 -	03/2015
61	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	589.43	198.99	- 03/2010	-
62	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	610.14	- -	03/2012
63	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	553.35	06/1999 -	03/2011
64	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,822.50	03/2001 -	12/2017
65	New BG Rly line from Eklakhi-Balurghat including Gazole- Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	250.22	- -	03/2015
66	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	222.78	03/2002 -	07/2013
67	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	130.98	12/2012 -	-
68	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	599.40	- -	02/2012
69	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	244.66	03/2004 -	03/2016
70	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	688.14	12/2011 12/2010	03/2013
71	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	120.53	- -	-
72	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR [220100183	02/1997	295.00 -	412.91	651.15	- -	01/2013
73	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	218.54	- -	03/2014
74	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
75	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	356.76	07/2012 -	-
76	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	294.32	03/2012 -	03/2013
77	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	775.36	760.65	- -	10/2012
78	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	658.93	02/2009 -	03/2012
79	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	101.17	- -	-
80	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	1,461.89	- -	03/2013
81	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.65	2,762.83	04/2008 12/2011	12/2015
82	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	190.51	- -	03/2012
83	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	177.01	03/2007 03/2007	03/2015
84	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	352.23	- -	12/2012

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
85	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.00	329.21	06/2004 -	12/2012
86	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.56	07/2008 -	07/2008
87	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,562.12	07/2005 -	-
88	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	384.00	05/2008 -	-
89	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	708.64	03/2012 -	-
90	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	954.23	12/2012 -	04/2013
91	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	383.48	12/2009 -	10/2013
92	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	754.13	12/2010 -	03/2015
93	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	117.90	- -	-
94	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	343.64	- 05/2009	05/2009
95	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	688.17	- -	03/2012
96	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	511.26	- -	03/2014
97	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	117.78	- -	-
98	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	836.10	06/2007 -	06/2007
99	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	714.05	546.88	- -	-
100	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,029.92	808.27	- -	03/2013
101	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
102	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,350.00	1,446.69	12/2008 -	03/2015
103	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,440.96	12/2006 -	08/2010
104	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	281.25	02/2011 -	03/2013
105	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	623.46	- 12/2009	02/2012
106	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	492.47	12/2012 12/2012	02/2013
107	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.35	- -	-
108	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	477.57	03/2005 12/2008	12/2016

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
109	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	693.39	442.99	03/2012 -	12/2012
110	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	255.10	- -	03/2014
111	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	217.64	- 09/2009	-
112	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	279.07	02/2009 02/2009	08/2014
113	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,453.50	1,503.51	03/2011 -	03/2017
114	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	186.95	- -	-
115	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	288.18	03/2012 -	03/2013
116	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	483.81	- -	03/2010
117	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	1,076.75	03/2009 -	12/2014
118	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,802.56	10/2007 -	12/2015
119	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	100.07	- -	-
120	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	227.75	- -	-
121	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,000.00	1,952.57	- -	03/2014
122	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	172.72	- -	02/2013
123	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	221.58	12/2008 -	09/2014
124	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	175.75	03/1998 08/2005	08/2005
125	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
126	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	103.44	02/2015 -	-
127	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	244.34	03/2009 03/2009	08/2014
128	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	126.92	- -	-
129	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	264.04	12/2007 03/2010	-
130	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	437.86	03/2012 -	03/2013
131	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	0.76	- -	-
132	GOELKERA-MANOHPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	280.00	116.78	02/2006 -	-
133	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049	07/2006	743.00 -	1,117.11	453.72	03/2008 06/2008	-

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
134	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU - [N22000052]	04/2003	98.74 -	337.30	222.07	- -	03/2012
135	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
136	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	234.30	03/2010 -	-
137	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	735.19	03/2010 -	12/2015
138	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,190.05	314.06	- -	-
139	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	642.65	- -	12/2012
140	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	435.87	396.76	03/2011 -	03/2011
141	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	406.40	338.72	- -	12/2013
142	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	57.70	- -	-
143	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	172.82	- -	-
144	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	385.20	136.92	- -	03/2015
145	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	40.88	- -	-
146	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	205.54	03/2010 -	03/2017
147	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	225.88	12/2010 -	03/2011
148	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	1,209.40	03/2014 -	12/2016
149	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	141.55	03/2012 -	03/2014
150	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	439.86	06/2005 -	06/2016
151	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	483.50	03/2014 -	12/2015
152	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	91.59	04/2014 -	03/2017
153	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
154	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017
155	Ramanagram-Mysore doubling with electrification of Kengesil-Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	478.76	03/2013 -	03/2014
156	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	302.71	03/2016 -	03/2016
157	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	246.75	03/2014 -	03/2014

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
158	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	96.22	12/2011 -	02/2012
159	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	126.50	12/2011 -	11/2013
160	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	139.99	12/2010 -	12/2010
161	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	1,215.30	17.21	03/2013 -	03/2013
162	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	468.62	1.72	03/2012 -	-
163	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,441.48	8.94	03/2015 -	03/2017
164	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95	191.35	03/2011 -	-
165	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	5,000.00	3,582.57	03/2009 -	03/2015
166	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	30.73	- -	-
	Total		46,392.56 -	338,714.86	195,405.79		
	<u>Road Transport & Highways</u>						
167	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013
168	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014
169	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	194.80	03/2008 -	02/2008
170	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	301.70	05/2008 -	09/2013
171	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014
172	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014
173	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014
174	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	141.70	07/2009 -	05/2014
175	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
176	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	233.00	09/2007 -	03/2014
177	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013
	Total		3,324.28 -	344,160.06	200,484.95		
	<u>Shipping & Ports</u>						
178	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]	10/2005	800.00 -	1,571.60	5.75	10/2008 -	08/2012

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
179	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	221.58	- 01/2009	12/2010
180	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	956.18	12/2010 -	03/2014
181	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	139.80	03/2006 -	06/2013
182	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
183	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
184	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	3,661.95	01/2012 -	07/2013
185	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
186	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	371.18	04/2009 -	02/2011
	Total		8,628.97 -	355,378.56	206,424.52		
	<u>Steel</u>						
187	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10,417.06	10/2009 -	07/2013
188	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	351.04	12/2011 06/2010	12/2013
189	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	145.98	10/2012 -	08/2013
190	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	14,671.22	12/2011 -	12/2013
191	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00 -	343.58	260.49	02/2011 -	06/2013
192	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00 -	350.00	253.47	08/2010 -	06/2013
	Total		24,028.89 -	385,594.99	232,523.78		
	<u>Telecommunications</u>						
193	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013
194	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013
195	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70 -	930.60	828.80	11/2010 -	09/2013
	Total		1,393.98 -	387,076.44	233,598.89		
	<u>Urban Development</u>						

(Jun,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
196	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013
197	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048	11/2006	114.18 173.08	173.08	-	04/2009 -	-
	Total		6,509.18 -	398,858.52	236,081.07		
	<u>Water Resources</u>						
198	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012
	Total		542.90 -	400,045.52	236,116.56		
	Grand Total		235,193.71	3,072,641.61	1,877,294.19		

List of Projects without Milestones w.r.t. Original Schedule

				(Jun,2013)		
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Civil Aviation</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	06/2013	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011 04/2013	12/2014	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	03/2015	03/2015	0/0
7	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60	03/2015	03/2015	0/0
	Total		5,691.18			0/0
	<u>Coal</u>					
8	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88	04/2014	04/2014	0/0
9	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27	04/2015	04/2015	0/0
10	AMRAPALI OC - [N06000103]CCL,Jharkhand	02/2012	858.11	03/2020	03/2020	0/0
	Total		2,428.26			0/0
	<u>Steel</u>					
11	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhatisgarh - [N12000078]SAIL,Chhatisgarh	07/2012	332.65	08/2014	08/2014	0/0
12	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90	12/2014	12/2014	0/0
	Total		587.55			0/0
	<u>Petroleum</u>					
13	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 973.79	03/2011 05/2011	05/2013	0/0
14	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012	06/2013	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
16	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	07/2013	0/0
17	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	07/2013	0/0
18	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
19	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	09/2012 -	09/2013	0/0
20	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
21	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
22	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
23	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
24	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0
25	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	12/2013	0/0
26	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
27	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	12/2013	0/0
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	10/2011 -	12/2013	0/0
29	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	10/2011 -	12/2013	0/0
30	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
31	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
32	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
33	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	02/2014	0/0
34	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	02/2014	0/0
35	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
36	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	03/2014	0/0
37	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2014	0/0
38	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
39	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	03/2014	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
41	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 03/2014	04/2014	0/0
42	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	04/2014	0/0
43	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	05/2014	0/0
44	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	06/2012 -	05/2014	0/0
45	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
46	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
47	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]ONGC,Gujarat	10/2011	200.69 -	07/2014 -	07/2014	0/0
48	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	08/2014 -	10/2014	0/0
49	Construction of three ETPs, Mehsana - [N16000135]ONGC,Gujarat	03/2012	260.74 -	11/2014 -	11/2014	0/0
50	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
51	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2014	0/0
52	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
53	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
54	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
55	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
56	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
57	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	03/2015 -	03/2015	0/0
58	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
59	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
60	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
61	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	08/2015	0/0
62	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
63	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
64	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	12/2015	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
65	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
66	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089])OCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
	Total		104,628.74 -			0/0
	<u>Power</u>					
67	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	10/2011 -	07/2013	0/0
68	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	06/2012 -	09/2013	0/0
69	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	06/2012 -	09/2013	0/0
70	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
71	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
72	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	11/2014	0/0
73	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	11/2014	0/0
74	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	03/2015 -	03/2015	0/0
75	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
76	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
	Total		7,160.03 -			0/0
	<u>Railways</u>					
77	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
78	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
79	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
80	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
81	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
82	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
83	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
84	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
85	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
86	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
87	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
88	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
89	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
90	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
91	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
92	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
93	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
94	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
95	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
96	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
97	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
98	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
99	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
100	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
101	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
102	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
103	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
104	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
105	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
106	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
107	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
108	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
109	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
110	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
111	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
112	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013	0/0
113	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	07/2013	0/0
114	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
115	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
116	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
117	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
118	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	12/2013	0/0
119	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
120	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2014	0/0
121	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
122	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
123	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
124	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
125	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
126	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
127	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
128	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
129	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
130	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
131	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
132	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
133	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	12/2014	0/0
134	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	03/1995 -	03/2015	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
135	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
136	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
137	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
138	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0
139	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2015	0/0
140	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
141	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
142	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
143	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2015	0/0
144	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
145	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
146	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2015	0/0
147	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
148	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2016	0/0
149	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2016	0/0
150	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
151	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 2,913.51	03/2016 -	03/2016	0/0
152	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
153	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
154	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
155	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2016	0/0
156	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
157	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
158	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2017	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
160	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
161	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
163	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
164	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
165	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
166	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
167	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
168	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	-	0/0
169	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
170	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-	0/0
171	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
172	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
173	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-	0/0
174	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-	0/0
175	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-	0/0
176	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-	0/0
177	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-	0/0
178	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-	0/0
179	VIRAMGAM-BHILD(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
180	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-	0/0
181	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
182	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
183	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
184	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
185	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
186	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
187	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
188	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
189	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
190	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
191	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
192	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
193	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
194	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
195	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
196	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
197	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
198	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
199	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
200	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
201	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		65,894.92 -			0/0
	<u>Road Transport & Highways</u>					
202	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008	0/0
203	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
204	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	06/2013	0/0
205	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2013	0/0
206	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	06/2013	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
207	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	10/2009	06/2013	0/0
208	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70	02/2004	06/2013	0/0
209	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	01/2013	06/2013	0/0
210	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	02/2012	06/2013	0/0
211	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	06/2009	07/2013	0/0
212	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	593.00	07/2013	07/2013	0/0
213	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00	07/2013	07/2013	0/0
214	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	08/2004 07/2010	08/2013	0/0
215	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	08/2004	08/2013	0/0
216	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	03/2008	08/2013	0/0
217	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	01/2011	08/2013	0/0
218	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	07/2012	08/2013	0/0
219	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	11/2011	08/2013	0/0
220	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	12/2012	08/2013	0/0
221	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	08/2013	08/2013	0/0
222	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
223	BHUBANESWAR TO PURI - [N24000195]NHAI, Odisha	03/2011	500.29	08/2013	08/2013	0/0
224	4-laning of Faraka-Raiganj - [N24000202]NHAI, Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
225	4-laning of Brahmapore-Faraka - [N24000203]NHAI, Multi State	02/2011	998.79	08/2013	08/2013	0/0
226	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43	08/2013	08/2013	0/0
227	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	05/2008	09/2013	0/0
228	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	10/2008	09/2013	0/0
229	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	06/2008	09/2013	0/0
230	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	06/2008	09/2013	0/0
231	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	05/2012	09/2013	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
232	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
233	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	09/2013	0/0
234	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	09/2013	0/0
235	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	09/2013	0/0
236	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
237	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	10/2013	0/0
238	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
239	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	10/2013	0/0
240	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
241	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0
242	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	11/2013	0/0
243	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
244	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
245	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
246	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
247	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	12/2013	0/0
248	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2013	0/0
249	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2013	0/0
250	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	12/2013	0/0
251	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	12/2013	0/0
252	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2013	0/0
253	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	12/2013	0/0
254	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2013	0/0
255	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	12/2013	0/0
256	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	12/2013	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
257	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2013	0/0
258	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	12/2013	0/0
259	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	12/2013	0/0
260	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	12/2013	0/0
261	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	12/2013	0/0
262	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
263	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
264	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	12/2013	0/0
265	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	12/2013	0/0
266	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	12/2013	0/0
267	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	12/2013 -	12/2013	0/0
268	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
269	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
270	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
271	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
272	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
273	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
274	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2014	0/0
275	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2014	0/0
276	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
277	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
278	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
279	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	03/2014	0/0
280	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
281	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
282	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
283	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2014	0/0
284	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
285	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
286	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	03/2014	0/0
287	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
288	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
289	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
290	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
291	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
292	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
293	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
294	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
295	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
296	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
297	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
298	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
299	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
300	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
301	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
302	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
303	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
304	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
305	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2014	0/0
306	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
307	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
308	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
309	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
310	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
311	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
312	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2014	0/0
313	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
314	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
315	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
316	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
317	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
318	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	08/2014	0/0
319	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
320	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
321	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
322	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
323	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0
324	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
325	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
326	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
327	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
328	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2014	0/0
329	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
330	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	12/2014	0/0
331	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	02/2015	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
332	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
333	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
334	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
335	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
336	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
337	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
338	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
339	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	11/2015	0/0
340	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
341	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
342	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		96,923.58 -			0/0
	<u>Shipping & Ports</u>					
343	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
344	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 09/2011	09/2011	0/0
345	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
346	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	08/2012	0/0
347	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
348	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
349	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
350	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
351	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013	0/0
352	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
353	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
354	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	07/2013	0/0
355	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 10/2013	10/2013	0/0
356	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
357	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
358	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	03/2014	0/0
359	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
360	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
	Total		15,462.28 -			0/0
	<u>Telecommunications</u>					
361	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
362	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
363	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
364	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
365	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	09/2013	0/0
366	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	12/2013	0/0
367	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2013	0/0
368	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	12/2013	0/0
369	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
370	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
371	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
372	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
373	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 02/2013	-	0/0
	Total		5,699.24 -			0/0
	<u>Urban Development</u>					

			(Jun,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
374	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
375	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
376	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
	<u>Water Resources</u>					
377	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		342,868.86			0/0

List of Projects on schedule w.r.t. Latest Schedule

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065]	9/2008	626.00 -	626.00	449.97	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	108.03	03/2015 -	03/2015
3	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		1,295.60 -	1,295.60	558.02		
	<u>Coal</u>						
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	159.80	03/2015 03/2015	03/2015
5	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	149.34	03/2017 -	03/2017
6	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	44.50	03/2016 -	03/2016
7	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
8	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	88.71	03/2016 -	03/2016
9	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	38.62	03/2014 -	03/2014
10	KALYANIKHANI OPENCASE PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.02	07/2016 -	07/2016
11	RAMAGUNDUM OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	52.18	03/2016 -	03/2016
13	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
14	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.02	03/2015 -	03/2015
16	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
17	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.88	03/2018 03/2018	03/2018

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
19	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	49.30	03/2020 -	03/2020
20	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	259.21	03/2016 -	03/2016
21	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	36.82	03/2015 -	03/2015
22	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
23	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	84.50	03/2015 -	03/2015
24	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	45.02	03/2014 03/2014	03/2014
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	445.14	03/2016 03/2016	03/2016
	Total		10,739.01 -	10,367.67	1,474.54		
	<u>Petrochemicals</u>						
26	Assam gas Cracker project - [N16000106]	4/2006	5,460.61 -	8,920.00	4,510.51	04/2012 12/2013	12/2013
	Total		5,460.61 -	8,920.00	4,510.51		
	<u>Petroleum</u>						
27	IOR GELEKI (ONGCL) - [160100216]	9/2001	390.09 -	1,674.11	1,727.13	03/2007 03/2017	03/2017
28	Wax Project - [N16000101]	6/2010	576.60 -	576.60	34.77	12/2013 -	12/2013
29	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	4,763.44	02/2014 -	02/2014
30	Development of WO-16 Cluster Fields - [N16000105]	6/2010	2,523.00 -	2,523.00	955.50	01/2014 -	01/2014
31	Ahmedabad Redevelopment - [N16000120]	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014
32	Ankleswar Redevelopment - [N16000122]	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014
33	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	145.57	03/2015 -	03/2015
34	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
35	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]	6/2009	486.00 -	486.00	52.43	09/2013 -	09/2013
36	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
37	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	63.36	11/2015 -	11/2015

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
38	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	4.89	12/2014 -	12/2014
39	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	54.18	03/2014 -	03/2014
40	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	409.63	05/2014 -	05/2014
41	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	61.34	12/2014 -	12/2014
42	Construction of three ETPs, Mehsana - [N16000135]	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
43	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]	10/2011	200.69 -	200.69	2.96	07/2014 -	07/2014
44	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
45	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]	4/2011	152.89 -	152.89	3.79	06/2013 -	06/2013
46	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	31.35	07/2015 -	07/2015
47	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	741.77	05/2015 -	05/2015
48	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]	6/2010	202.94 -	202.94	4.12	01/2014 -	01/2014
49	Mehesana Redevelopment - [N16000121]	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
	Total		38,946.95 -	39,741.73	11,597.98		
	<u>Power</u>						
50	Transm System for development of Pooling strn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	384.67	01/2015 -	01/2015
51	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103]	9/2011	1,940.13 -	1,940.13	903.15	09/2014 -	09/2014
52	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	2.26	03/2015 -	03/2015
53	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
54	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
55	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	298.14	10/2014 -	10/2014
56	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	24.22	08/2014 -	08/2014

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	347.09	02/2015 -	02/2015
58	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]	1/2012	259.28 -	259.28	92.22	01/2014 -	01/2014
59	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	305.71	01/2015 -	01/2015
60	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	93.67	08/2014 -	08/2014
61	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]	12/2011	297.33 -	297.33	105.63	08/2014 -	08/2014
62	SOLAPUR STPP - [N18000133]	3/2012	9,395.18 -	9,395.18	1,508.00	11/2016 -	11/2016
63	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	1,008.00	09/2016 -	09/2016
64	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	1,629.00	12/2016 -	12/2016
65	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	171.52	11/2014 -	11/2014
66	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	712.82	10/2014 -	10/2014
67	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	153.17	11/2014 -	11/2014
68	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	260.49	08/2014 -	08/2014
69	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	39.74	06/2014 -	06/2014
70	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	721.59	06/2015 -	06/2015
71	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	115.30	06/2015 -	06/2015
72	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
73	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
74	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017
75	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,083.00	05/2017 -	05/2017

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
76	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
77	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	78.99	03/2015 -	03/2015
79	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	318.00	08/2015 -	08/2015
80	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	281.72	02/2014 -	02/2014
81	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113	12/2011	2,422.66 -	2,422.66	349.64	08/2014 -	08/2014
82	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112	11/2011	2,127.51 -	2,127.51	759.70	07/2014 -	07/2014
83	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	757.21	08/2014 -	08/2014
84	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	161.99	06/2014 -	06/2014
85	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	970.31	12/2013 -	12/2013
86	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106	8/2011	425.51 -	425.51	297.45	10/2013 -	10/2013
87	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	669.25	12/2013 -	12/2013
88	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	982.34	05/2014 -	05/2014
89	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	1,142.61	08/2013 -	08/2013
90	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	1,639.56	03/2014 -	03/2014
	Total		102,561.85 -	102,561.85	18,437.68		
	<u>Railways</u>						
91	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	4/2006	325.00 -	1,116.53	205.54	03/2010 03/2017	03/2017
92	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	157.91	03/2016 -	03/2016
93	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112	4/2008	829.74 -	829.74	26.54	03/2015 -	03/2015

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
94	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	378.80	03/2014 -	03/2014
95	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	575.05	03/2014 -	03/2014
96	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
97	Ghutiasharif-Canning (ER) - [N22000117	4/2009	189.97 -	611.03	126.50	12/2011 11/2013	11/2013
98	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	4/2008	653.19 -	653.46	246.75	03/2014 -	03/2014
99	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111	4/2010	2,619.02 -	2,913.51	302.71	03/2016 -	03/2016
	Total		15,349.33 -	16,856.68	2,019.80		
	<u>Road Transport & Highways</u>						
100	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
101	DEOLI-KOTA - [N24000148	1/2011	593.00 -	593.00	538.10	07/2013 -	07/2013
102	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168	3/2011	785.50 -	785.50	812.30	08/2013 -	08/2013
103	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,320.00	08/2013 -	08/2013
104	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	13.50	09/2015 -	09/2015
105	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	119.60	08/2015 -	08/2015
106	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	184.10	06/2014 -	06/2014
107	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	188.90	06/2015 -	06/2015
108	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213	4/2012	624.00 -	624.00	211.60	04/2014 -	04/2014
109	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
110	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	281.30	10/2014 -	10/2014
111	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	450.80	07/2014 -	07/2014
112	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	74.37	01/2014 -	01/2014
113	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
114	SAMAIKHALI GANDHIDHAM - [N24000223	9/2010	805.39 -	805.39	543.70	12/2013 -	12/2013

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
115	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	30.19	12/2015 -	12/2015
116	2 LANING WITH PS KANPUR KABRAI - [N24000221	1/2013	373.47 -	373.47	38.90	07/2014 -	07/2014
117	2 LANING WITH PS AGRA ALIGARH - [N24000220	10/2012	250.50 -	250.50	127.10	10/2014 -	10/2014
118	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	943.90	09/2014 -	09/2014
119	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	201.90	06/2014 -	06/2014
120	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	256.50	08/2013 -	08/2013
121	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	1,126.00	08/2013 -	08/2013
122	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	1,162.00	08/2013 -	08/2013
123	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	325.70	09/2013 -	09/2013
124	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,208.00	06/2014 -	06/2014
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	621.40	03/2014 -	03/2014
126	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 [N24000183	11/2011	1,535.00 -	1,535.00	1,117.00	05/2014 -	05/2014
127	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	845.00	03/2014 -	03/2014
128	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	288.50	02/2014 -	02/2014
129	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	501.60	01/2014 -	01/2014
130	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
131	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
132	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
133	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
134	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	904.30	05/2014 -	05/2014
135	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	504.20	08/2013 -	08/2013
136	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	122.70	01/2014 -	01/2014
137	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	431.00	02/2014 -	02/2014

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
138	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	160.90	05/2014 -	05/2014
139	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
140	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	616.00	11/2013 -	11/2013
141	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	714.20	07/2013 -	07/2013
142	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
143	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,026.00	11/2013 -	11/2013
144	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,262.00	10/2014 -	10/2014
145	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	1,124.00	11/2013 -	11/2013
	Total		42,017.52 -	42,017.52	21,349.89		
	<u>Shipping & Ports</u>						
146	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	139.80	03/2006 06/2013	06/2013
147	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051	8/2010	612.72 -	532.83	418.64	12/2012 10/2013	10/2013
148	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
149	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
150	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061	7/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013
151	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 -	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		3,489.64 -	3,872.24	1,681.27		
	<u>Steel</u>						
152	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072	4/2011	572.00 -	572.00	304.07	04/2013 12/2013	12/2013
153	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073	2/2011	898.55 -	898.55	200.10	05/2013 11/2013	11/2013
154	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	57.57	08/2014 -	08/2014
155	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	3.10	12/2014 -	12/2014
	Total		2,058.10 -	2,058.10	564.84		

(Jun,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Urban Development</u>						
156	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	3,548.47	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	3,548.47		
	Grand Total		257,160.61	262,933.39	65,743.00		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(Jun,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Petroleum</u>						
1	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	9/2001	345.10 663.69	663.69	711.61	03/2007 03/2014	12/2013
	Total		345.10 -	663.69	711.61		
	<u>Power</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	50.32	06/2016 -	04/2015
3	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	190.02	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	240.34		
	Grand Total		3,789.19	4,107.78	951.95		

List of Delayed Projects w.r.t. Latest Schedule

(Jun,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,262.00	12/2008 -	03/2014	63	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,140.48	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL, Gujarat	10/2009	11,459.00 -	11,459.00	2,940.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL, Rajasthan	10/2009	12,320.00 -	12,320.00	2,027.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	25,369.48				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building - [N04000069]AAI, Goa	05/2010	335.61 -	335.61	242.98	05/2012 -	06/2013	13	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI, Sikkim	01/2009	309.46 -	309.46	231.80	01/2011 04/2013	12/2014	47	20
	Total		645.07 -	645.07	474.78				
	<u>Coal</u>								
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,726.15	06/2009 -	01/2014	55	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL, Odisha	01/2005	302.96 -	302.96	114.77	03/2010 -	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL, Jharkhand	12/2007	471.66 341.63	341.63	108.36	03/2011 -	03/2014	36	-
10	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, Uttar Pradesh	06/2011	789.88 741.62	741.62	366.81	03/2013 -	03/2014	12	-
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,409.33	03/2012 -	03/2014	24	-
12	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL, Odisha	08/2008	207.28 -	207.28	112.08	03/2012 -	03/2014	24	-
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, Andhra Pradesh	12/2009	212.34 779.26	977.53	701.71	03/2013 09/2012	10/2014	19	25
14	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, Madhya Pradesh	10/2007	259.40 -	259.40	6.66	03/2012 -	03/2015	36	-
15	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL, Odisha	12/2007	457.77 -	457.77	112.74	03/2013 -	03/2015	24	-
16	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL, Odisha	12/2007	172.08 -	172.08	124.28	03/2010 -	03/2015	60	-
17	KAKATIYA LONGWALL - [N06000048]SCCL, Andhra Pradesh	12/2008	453.63 -	453.63	87.20	12/2012 -	03/2015	27	-
18	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL, Odisha	11/2008	479.63 -	479.63	113.75	03/2013 -	03/2015	24	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.29	03/2012 -	03/2015	36	-
20	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.20	03/2013 -	03/2015	24	-
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,408.71	03/2014 -	03/2016	24	-
22	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,246.22	03/2014 -	03/2016	24	-
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	24.32	07/2012 -	03/2016	44	-
24	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.36	03/2014 -	03/2016	24	-
25	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.91	03/2014 -	03/2016	24	-
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24	-
29	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
30	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	127.50	03/2012 -	03/2016	48	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72	-
32	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
33	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	30.75	12/2015 -	02/2018	26	-
	Total		24,633.81 -	28,090.60	12,537.44				
	<u>Steel</u>								
35	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	260.49	02/2011 -	06/2013	28	-
36	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	253.47	08/2010 -	06/2013	34	-
37	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 -	12,291.00	10,417.06	10/2009 -	07/2013	45	-
38	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	145.98	10/2012 -	08/2013	10	-
39	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	248.98	05/2012 -	08/2013	15	-
40	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	351.04	12/2011 03/2012	12/2013	24	21
41	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	14,671.22	12/2011 -	12/2013	24	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,628.95	12/2011 -	12/2013	24	-
43	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,413.47	03/2013 -	12/2013	9	-
44	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,642.51	12/2012 -	03/2014	15	-
45	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	74.71	10/2013 -	05/2014	7	-
46	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	63.20	11/2013 -	06/2014	7	-
47	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	9,540.32	03/2013 -	09/2014	18	-
	Total		63,227.77 -	69,385.31	50,711.40				
	<u>Petroleum</u>								
48	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013	2	-
49	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	176.83	04/2012 -	06/2013	14	-
50	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	726.73	12/2011 -	07/2013	19	-
51	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	187.51	02/2013 -	07/2013	5	-
52	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,371.54	01/2012 -	07/2013	18	-
53	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	682.23	04/2012 -	07/2013	15	-
54	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	23	17
55	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,124.72	09/2012 -	09/2013	12	-
56	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24	16
57	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12	-
58	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	594.83	01/2013 -	09/2013	8	-
59	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	96.88	09/2012 -	09/2013	12	-
60	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	719.20	07/2012 -	10/2013	15	-
61	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	217.08	11/2012 -	10/2013	11	-
62	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
63	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	275.07	05/2013 -	11/2013	6	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
64	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	399.30	03/2006 03/2013	12/2013	93	9
65	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	728.30	03/2010 03/2012	12/2013	45	21
66	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	247.86	03/2012 -	12/2013	21	-
67	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	372.11	221.02	03/2013 -	12/2013	9	-
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL, Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26	-
69	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL, Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26	-
70	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	331.20	57.39	08/2013 -	01/2014	5	-
71	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
72	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	920.79	07/2010 05/2012	02/2014	43	21
73	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
74	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
75	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	1,494.50	03/2013 -	03/2014	12	-
76	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	184.41	08/2012 -	03/2014	19	-
77	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	1,106.00	28.10	06/2012 -	03/2014	21	-
78	PARADIP REFINERY PROJECT - [N16000058]IOCL, Odisha	02/2009	29,777.00 -	32,710.00	22,254.00	11/2012 -	04/2014	17	-
79	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,347.71	03/2013 03/2014	04/2014	13	1
80	IOR of B-173A Field - [N16000140]ONGC, Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1	-
81	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,478.23	08/2010 03/2012	05/2014	45	26
82	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
83	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, Multi State	11/2012	309.81 -	309.82	48.71	08/2014 -	10/2014	2	-
84	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
85	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	344.95	09/2011 -	12/2014	39	-
86	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00 -	586.00	5.55	07/2015 -	08/2015	1	-
87	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,881.73	09/2010 03/2012	12/2015	63	45
88	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
89	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	20.90	12/2015 -	05/2016	5	-
	Total		118,916.32 -	132,904.03	71,087.35				
	<u>Power</u>								
90	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATH-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	775.25	641.00	01/2010 -	07/2013	42	-
91	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	149.64	06/2012 -	07/2013	13	-
92	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	81.80	10/2012 -	07/2013	9	-
93	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	149.92	10/2011 -	07/2013	21	-
94	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.88	11/2011 -	09/2013	22	-
95	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	824.07	05/2012 -	09/2013	16	-
96	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	130.78	01/2013 -	09/2013	8	-
97	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	85.91	04/2013 -	09/2013	5	-
98	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	121.80	06/2012 -	09/2013	15	-
99	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	53.95	06/2012 -	09/2013	15	-
100	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,750.74	11/2009 02/2013	10/2013	47	8
101	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	747.88	08/2010 01/2013	10/2013	38	9
102	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,342.00	10/2012 -	11/2013	13	-
103	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	884.11	10/2009 -	12/2013	50	-
104	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,493.74	12/2012 -	12/2013	12	-
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	363.76	11/2011 -	12/2013	25	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	267.02	02/2012 -	12/2013	22	-
107	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	123.44	07/2013 -	12/2013	5	-
108	PARBATHI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,819.66	10/2010 01/2013	03/2014	41	14

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
109	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,534.87	01/2012 -	03/2014	26	-
110	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,423.42	10/2012 -	03/2014	17	-
111	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,580.90	2,051.68	08/2012 -	03/2014	19	-
112	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,820.52	08/2012 -	03/2014	19	-
113	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,304.52	12/2012 -	03/2014	15	-
114	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	572.28	11/2012 -	03/2014	16	-
115	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,058.95	03/2013 -	03/2014	12	-
116	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,562.41	12/2013 -	03/2014	3	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	277.02	07/2013 -	03/2014	8	-
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	826.24	04/2013 -	03/2014	11	-
119	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	887.88	08/2012 -	06/2014	22	-
120	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	355.02	11/2011 -	07/2014	32	-
121	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	5,000.00	04/2009 -	09/2014	65	-
122	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NNEEPCO,Arunachal Pradesh	12/2008	573.99 -	1,117.92	605.07	08/2012 08/2013	09/2014	25	13
123	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,069.00	08/2013 -	09/2014	13	-
124	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	667.95	11/2012 -	09/2014	22	-
125	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	149.57	11/2013 -	09/2014	10	-
126	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,147.32	09/2009 06/2013	11/2014	62	17
127	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.74	01/2013 -	12/2014	23	-
128	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	910.47	11/2013 -	12/2014	13	-
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NNEEPCO,Mizoram	01/2011	913.63 -	913.63	425.99	07/2014 -	02/2015	7	-
130	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,511.10	11/2012 -	03/2015	28	-
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	23.88	04/2015 -	05/2015	1	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
132	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,045.64	08/2013 -	06/2015	22	-
133	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,886.00	07/2011 -	10/2015	51	-
134	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,841.00	03/2013 -	03/2016	36	-
135	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	353.24	07/2014 -	05/2016	22	-
136	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 -	2,978.86	489.19	07/2010 -	11/2016	76	-
137	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,606.19	01/2016 01/2016	11/2016	10	10
138	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,499.00	12/2009 -	02/2017	86	-
139	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,330.55	05/2013 05/2013	03/2017	46	46
140	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,279.31	09/2010 08/2014	12/2017	87	40
141	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,479.78	09/2009 07/2014	03/2018	102	44
	Total		120,984.15 -	137,546.20	90,245.90				
	<u>Railways</u>								
142	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	222.78	03/2002 -	07/2013	136	-
143	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	569.78	03/1994 -	10/2013	235	-
144	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	383.48	12/2009 03/2011	10/2013	46	31
145	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	169.89	12/2012 -	12/2013	12	-
146	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
147	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	478.76	03/2013 -	03/2014	12	-
148	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	279.07	02/2009 02/2009	08/2014	66	66
149	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	244.34	03/2009 03/2009	08/2014	65	65
150	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	221.58	12/2008 -	09/2014	69	-
151	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,076.75	03/2009 12/2012	12/2014	69	24
152	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	248.49	06/2013 06/2013	12/2014	18	18
153	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
154	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.01	03/2007 03/2007	03/2015	96	96

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
155	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	754.13	12/2010 12/2010	03/2015	51	51
156	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,446.69	12/2008 -	03/2015	75	-
157	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.26	12/2012 -	03/2015	27	-
158	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,582.57	03/2009 -	03/2015	72	-
159	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,762.83	04/2008 03/2014	12/2015	92	21
160	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,802.56	10/2007 12/2012	12/2015	98	36
161	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	735.19	03/2010 -	12/2015	69	-
162	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	483.50	03/2014 -	12/2015	21	-
163	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRT, Maharashtra	03/1996	401.81 495.44	1,814.48	244.66	03/2004 12/2010	03/2016	144	63
164	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	56.57	03/2014 -	03/2016	24	-
165	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	439.86	06/2005 07/2011	06/2016	132	59
166	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	47.45	03/2016 -	06/2016	3	-
167	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	477.57	03/2005 12/2008	12/2016	141	96
168	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRT, Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,209.40	03/2014 03/2016	12/2016	33	9
169	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,503.51	03/2011 03/2014	03/2017	72	36
170	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.48	91.59	04/2014 -	03/2017	35	-
171	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15	-
172	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24	-
173	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201	-
	Total		26,098.42 -	73,959.61	29,468.23				
	<u>Road Transport & Highways</u>								
174	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013	110	-
175	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54	-
176	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	06/2013	112	-
177	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	06/2013	44	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
178	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	06/2013	112	-
179	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	946.20	01/2013 -	06/2013	5	-
180	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	16	-
181	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	07/2013	49	-
182	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.52	08/2004 07/2010	08/2013	108	37
183	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.15	08/2004 -	08/2013	108	-
184	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	268.60	06/2011 06/2011	08/2013	26	26
185	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	08/2013	65	-
186	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31	-
187	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,293.00	07/2012 -	08/2013	13	-
188	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013	21	-
189	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,967.00	12/2012 -	08/2013	8	-
190	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	301.70	05/2008 -	09/2013	64	-
191	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	276.90	10/2008 -	09/2013	59	-
192	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	283.80	06/2008 -	09/2013	63	-
193	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	262.60	06/2008 -	09/2013	63	-
194	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	09/2013	16	-
195	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	09/2013	4	-
196	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,325.00	06/2013 -	09/2013	3	-
197	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	640.10	02/2013 -	09/2013	7	-
198	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	646.60	05/2010 -	10/2013	41	-
199	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
200	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.20	02/2013 -	10/2013	8	-
201	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	13.80	01/2013 -	10/2013	9	-
202	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
203	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.90	10/2008 -	12/2013	62	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
204	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.30	01/2009 -	12/2013	59	-
205	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	461.60	09/2008 -	12/2013	63	-
206	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	299.20	06/2008 -	12/2013	66	-
207	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	204.80	05/2008 -	12/2013	67	-
208	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	246.20	06/2008 -	12/2013	66	-
209	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42	-
210	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	506.20	09/2009 -	12/2013	51	-
211	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
212	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	12/2013	15	-
213	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26	-
214	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,688.00	08/2011 -	12/2013	28	-
215	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
216	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	803.40	03/2013 -	12/2013	9	-
217	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,063.00	11/2012 -	12/2013	13	-
218	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
219	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.70	05/2013 -	12/2013	7	-
220	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	563.30	03/2013 -	12/2013	9	-
221	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	447.50	05/2013 -	02/2014	9	-
222	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	238.00	09/2007 -	03/2014	78	-
223	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014	66	-
224	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	237.30	06/2005 -	03/2014	105	-
225	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	242.60	06/2008 -	03/2014	69	-
226	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	281.40	06/2008 -	03/2014	69	-
227	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	333.30	10/2008 -	03/2014	65	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
228	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	199.40	04/2008 -	03/2014	71	-
229	GUWHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	259.90	04/2008 -	03/2014	71	-
230	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	233.00	09/2007 -	03/2014	78	-
231	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	856.30	07/2010 -	03/2014	44	-
232	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	410.00	10/2011 -	03/2014	29	-
233	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	53.80	11/2012 -	03/2014	16	-
234	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,431.00	06/2013 -	03/2014	9	-
235	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	393.00	05/2013 -	03/2014	10	-
236	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	512.70	03/2013 -	03/2014	12	-
237	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	259.70	10/2013 -	03/2014	5	-
238	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79	-
239	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	04/2014	13	-
240	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	464.10	02/2014 -	04/2014	2	-
241	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	314.80	02/2009 03/2014	05/2014	63	2
242	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	300.90	04/2008 -	05/2014	73	-
243	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	141.70	07/2009 -	05/2014	58	-
244	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68	-
245	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014	67	-
246	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	795.20	10/2011 -	06/2014	32	-
247	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
248	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	649.90	07/2013 -	06/2014	11	-
249	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-
250	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.02	09/2013 -	07/2014	10	-
251	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	101.10	07/2012 -	07/2014	24	-
252	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	295.40	09/2010 -	08/2014	47	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
253	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.80	09/2009 -	09/2014	60	-
254	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	280.50	04/2010 -	11/2014	55	-
255	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68	-
256	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73	-
257	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	146.30	04/2009 -	12/2014	68	-
258	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.37	12/2009 -	12/2014	60	-
259	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,127.00	02/2010 -	12/2014	58	-
260	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
261	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	313.50	08/2013 -	02/2015	18	-
262	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
263	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,725.00	08/2014 -	07/2015	11	-
264	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13	-
265	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	42.90	10/2013 -	11/2015	25	-
266	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
267	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	881.20	07/2015 -	06/2016	11	-
	Total		54,711.29 -	56,623.08	52,658.15				
	<u>Shipping & Ports</u>								
268	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	07/2013	18	10
269	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	956.18	12/2010 09/2012	03/2014	39	18
	Total		4,728.00 -	5,610.00	4,618.13				
	<u>Telecommunications</u>								
270	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9
271	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28	-
272	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	81.73	06/2009 -	12/2013	54	-

(Jun,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
273	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
274	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
	Total		2,934.85 -	2,774.50	1,282.27				
	<u>Urban Development</u>								
275	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	300.76	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	300.76				
	Grand Total		459,815.68	556,758.40	338,753.89				
