


**293rd FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crores and above)
March, 2010**



Reactor Vault

Atomic Reactor

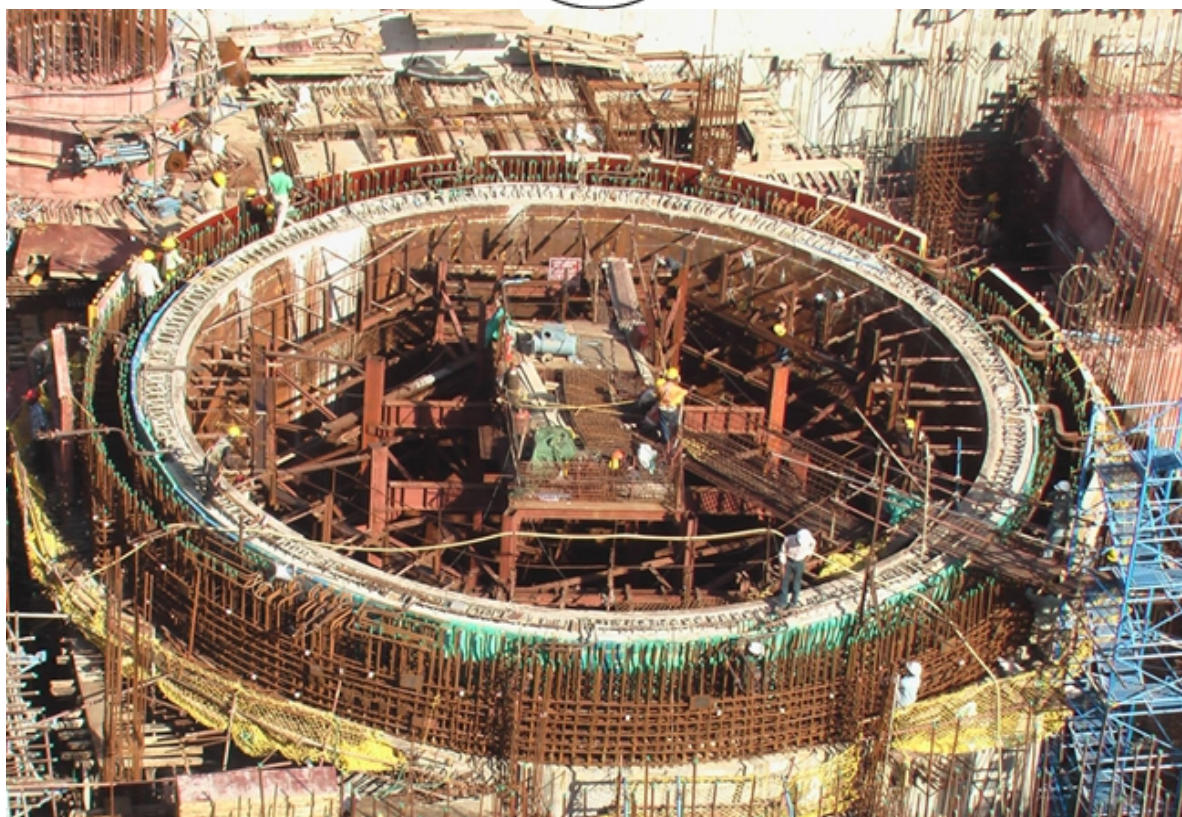

**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary	1 -6
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2008-09	7-13
Summary of Projects	14-25
Sector wise analysis of projects	26-64

EXECUTIVE SUMMARY

The 293rd Flash Report for March' 2010, that contains information on the status of 631 projects in the Central Sector, each costing Rs. 100 Crores and above. During March' 2010, twelve projects reported completion and have been dropped from the monitor of this Ministry. 27 new projects have been added during the month under reference. During March' 2010, three projects of Coal (1), Steel (1) and Shipping & Port (1) Sectors have shown considerable improvement over the completion schedule reported earlier. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	151
2.	RAILWAYS	155
3.	POWER	77
4.	PETROLEUM	78
5.	COAL	44
6.	TELECOMMUNICATION	40
7.	STEEL	29
8.	SHIPPING & PORTS	23
9.	CIVIL AVIATION	18
10.	ATOMIC ENERGY	4
11.	URBAN DEVELOPMENT	9
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		631

2. One hundred twelve (112) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1 to 60 months in respect of projects relating to Atomic Energy, Civil Aviation, Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports and Urban Development sectors.

3. In the **Atomic Energy sector**, Kaiga 3 and 4 Units Project (NPCIL) has shown additional delay of 3 months due to the continued problem of non availability of fuel.
4. In the **Civil Aviation Sector**, 2 projects have shown additional delays of 3-4 months. Construction of Integrated Passenger Terminal Building, NSCBI Airport, Kolkata has reported additional delays of 3 months due to delay in shifting of effluent treatment plant (ETP) falling in the layout of Flyover and approach road. Construction of New Expandable Modular Integrated Terminal Building at Raipur Airport has reported additional delays of 4 months due to change in location of service block.
5. In the **Coal sector**, 10 projects have reported additional delays in the range of 1-48 months whereas Tuticorin Thermal Power Project, has reported considerable improvement over the completion schedule by 1 month. Kakatiya Laongwall has reported additional delay of 3 months due to the revised proposal of SCCL to take up this project on technology provider cum operator (TPO) Concept on cost per tonne basis. Block-B-OCP NCL (3.5 MTY) has reported additional delays of 12 months due to delay in supply of Hydrolic Shovel 9.5 m³-face, Hydrolic Shovel 9.5 m³ Backhoe and 160 mm Drill. Jhanjra Continuous Miner for Jhanjra UG-II has reported additional delays of 21 months, however, no specific reasons have been given by the project authority. Amlohri EPR (NCL) (6 MTY) has reported additional delays of 24 months due to delay in award of construction of combined Coal Handling Plant (CHP). Narayankui UG has reported additional delay of 24 months due to delay in acquisition of land and delay in mechanized fast shaft sinking. Krishnashilla (NCL) (4MTY) has reported additional delay of 36 months due to delay in supply of 40 to 50 tonne cranes hydraulic. Shovel 9.5 m³-Backhoe and 160 mm Drill. Chitra East OCP has reported additional delays of 36 months due to delay in acquisition of land and diversion of forest land. Jhanjra Longwall UG Phase II has reported additional delay of 38 months due to delay in tender process. Dipka Expansion OCP has reported additional delays of 48 months due to delay in finalization of tender and work award for construction of Workshop.
6. In the **Steel Sector**, 9 projects have reported additional delay in the range of 1-12 months while Power Plant-1 (Boiler-6) in Vishakhapatnam Steel Plant of RINL has

reported additional delays of 5 months due to delay in supply of turbine motor by M/s BHEL. Rebuilding of Blast Furnace No. 2 has reported additional delay of 1 month due to delay in supply of equipments. Coal Dust Injection in Blast Furnace-2 and 3 have reported additional delay of 2 months each due to delay in design & erection of equipments. Expansion of Bokaro Steel Plant has reported additional delays of 2 months and no specific reason has been provided by the project authorities. Rebuilding of Coke Oven Battery-10 has reported additional delay of 3 months due to change in scope of work. Pulverised Coal Injection System for Blast Furnace-1 & 2 has reported additional delay of 5 months due to delay in design and inadequate mobilization of resources. Rebuilding of Coke Oven Battery No. 1 & 2, Expansion of Bhilai Steel Plant and Expansion of Rourkela Steel Plant have reported additional delay of 6 months, 6 months and 12 months respectively due to inadequate mobilization of resources by the contractor.

7. In the **Petroleum Sector**, 11 projects have reported additional delays in the range of 1-9 months. Development of B-193 Cluster Fields has reported additional delay of 1 month due to change in scope of work. Motor Spirit Quality (MSQ) Upgradation Project at Guwahati Refinery has reported additional delay of 1 month due to local constraints. MSQ Improvement Project has reported additional delays of 1 month due to slow progress by the contractor. Hira Reconstruction, Construction of New Terminal at Ennore, Chennai, Branch Pipeline from KSPL Viramgaon to Kandla and Development of C-Series Fields have reported additional delay of 1 months 2 months, 4 months and 5 months respectively, however, no specific reasons have been given by the concerned project authorities. Additional Gas processing units at (ONGC) Uran, Mumbai has reported additional delays of 9 months due to delay in tender process. MNW – NF Bridge Project at Hazira (ONGC) has reported additional delays of 7 months delayed due to adverse weather conditions.
8. In the **Power Sector**, 16 projects have reported additional delay in the range of 3-21 months. Kaiga 3 & 4 Transmission System (PGCIL) has reported additional delays of 3 months due to severe Right of Way (ROW) constraints in 50 km Karnataka portion. Farakka STPP Stage-III (NTPC) has reported additional delay of 3 months due to delay in erection schedule by M/s BHEL. Bongaigaon Thermal Power Project (NTPC) has reported additional delay of 3 months due to delay in slow progress by civil agency. Chamara, Hydro Electric Project Stage III (NHPC)

has reported additional delay of 4 months due to violence among contractor's laborers and court stay on crushing Plant leading to huge shortage of aggregate for concrete work. Nimoo Bazo Hydro Electric Project has reported additional delay of 4 months due to highly inclement weather condition, delay in award of E&M works due to poor participation, delay in HM works due to abnormal high price bid and retendering thereof. Koteswar Transmission System (PGCIL) and Western Region Strengthening Scheme have reported additional delay of 5 months each to match with the linked generation project. Transmission System for Startup Power to DVC & Maithon RB Generation project (PGCIL) has report additional delay of 2 months due to delay in forest clearance. Parbati Hydro Electric Project Stage-III 4x130 MW (NHPC) has reported additional delay of 7 months due to delay in land acquisition for Sainj bypass and delay in award of E&M contract. Transmission System Associated with Barh Generation Project (PGCIL) has reported additional delay of 9 months to match with the completion schedule of linked projects. Eastern Region Strengthening scheme –I (1142 CKM) has reported additional delay of 9 months due to delay in forest clearance. Koteswar HEP (THDC) has reported additional delay of 10 months, however, no specific reasons have been given by the concerned project authorities. Tehri Pumped Storage Plant has reported additional delay of 20 months due to delay in award of contract. Vishnugad-Pipalkoti Hydro Electric Project (THDCL) has reported additional delays of 21 months due to delay in acquisition of forest land.

9. In the **Road Transport and Highways Sector**, 50 projects have reported additional delay in the range of 1-24 months. No specific reasons have been reported by the project authorities for such additional delays.

10. In the **Railway Sector**, 9 projects have shown additional delays in the range of 3-60 months while Hajipur- Sugauli Via Vaishali New Line Project of ECR has reported considerable improvement of three months over the completion schedule reported earlier. Udampur-Srinagar-Baramulla (NL), NR has reported additional delay of 45 months due to delay in land acquisition of Army Land., Deograh-Dumka New BG Line (LD) ER of RVNL has reported additional delay of 8 months due to Maoists movement. New Guwahati- Digaru Patch (LD) Phase-I has reported additional delay of 12 months due to ban on cutting hills. Tollyganj-Garia (MTP) project, Sitamarhi- Raxaul- Narkataiganj (GC), Sriganganagar – Sarupasar,

Baramati - Lonand (NL), CR and Jayanagar-Darbahanga-Narkatiaganj have reported additional delay of 3 months, 9 months, 12 months, 9 months and 24 months respectively, however, no specific reasons have been given by the project authorities.

11. In the **Shipping & Ports Sector**, Deepening of Channel at Paradip Port has reported additional delay of 1 month but no specific reason is given while rail connectivity to ICTT at Vallarpadam has shown considerable improvement over the completion schedule reported earlier.
12. In the **Urban Development Sector**, 2 Projects have reported additional delay of 1 – 6 months. Delhi MRTS Phase-II Project has reported additional delay of 1 month due to slow process of land acquisition. Bangalore Metro Rail Project has reported additional delays of 6 months but no specific reason has been reported by the concerned project authority.
13. Status as on 01.04.2010 in respect of completion of projects costing Rs.100 Crores and above in different sectors during 2010-11 is indicated in the following tables.



(Pankaj Jain)

Additional Secretary to the Government of India
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	155	9
2	Road Transport & Highways	151	50
3	Petroleum	78	11
4	Power	77	16
5	Coal	44	10
6	Telecommunications	40	0
7	Steel	29	9
8	Shipping & Ports	23	2
9	Civil Aviation	18	2
10	Urban Development	9	2
11	Atomic Energy	4	1
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	631	112

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 100 Crore and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NATIONAL HIGHWAYS DEVELOPMENT PROJECT) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAVA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN RAPID TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
14	PARADIP PORT, NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ, NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
July, 2009				
<u>Power</u>				
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
<u>Road Transport & Highways</u>				
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET, KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
<u>Telecommunications</u>				
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
August, 2009				
<u>Power</u>				
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
<u>Railways</u>				
26	MADURAI-DINDIGUL,(LD)(SR)(SOUTHERN RAILWAY) - [N22000047]	73.19	-	181.81
<u>Road Transport & Highways</u>				
27	TIRUNELVEI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September,2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR,NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
Shipping & Ports				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24
October,2009				
Petroleum				
40	DEVELOPMENT OF BASSEIN EAST (ONGCL)() - [160100232]	985.17	03/2006	1,568.46
Railways				
41	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)(RAIL VIKAS NIGAM LTD.) - [220100221]	93.10	-	126.11
Telecommunications				
42	GSM EQUIPMENT OF 1015K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000044]	350.84	11/2008	182.06
43	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM(BHARAT SANCHAR NIGAM LIMITED) - [N26000059]	567.40	06/2009	241.85
November,2009				
Road Transport & Highways				

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
44	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106272]	327.20	01/2009	457.60
45	HYDERABAD BANGALORE SECTION(NH-7)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106284]	611.44	03/2009	834.20
46	KADAL TO ARMUR, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000092]	271.73	11/2009	303.80
<u>Telecommunications</u>				
47	GSM BASED NETWORK PH-4(BHARAT SANCHAR NIGAM LIMITED) - [N26000033]	174.36	11/2007	71.50
December,2009				
<u>Steel</u>				
48	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000024]	123.22	06/2009	77.00
<u>Telecommunications</u>				
49	GSM EQUIPMENT OF 1162K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000045]	325.00	12/2008	237.85
January,2010				
<u>Road Transport & Highways</u>				
50	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106231]	266.00	08/2007	.00
51	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106232]	133.03	08/2005	.00
February,2010				
<u>Civil Aviation</u>				
52	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000016]	245.58	12/2008	260.35
<u>Power</u>				
53	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL)() - [180100257]	813.67	06/2008	784.58
March,2010				
<u>Atomic Energy</u>				
54	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL)(NUCLEAR POWER CORPORATION OF INDIA LIMITED) - [020100042]	3,072.00	02/2008	2,151.00

**Month wise List of Completed Project Costing Rs. 100 Crore and above during
2009-2010**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Coal</u>				
55	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC)(NEYVELI LIGNITE CORPORATION) - [060100088]	2,161.28	06/2009	1,808.34
<u>Petroleum</u>				
56	CHENNAI-BANGALORE PIPELINE(INDIAN OIL CORPORATION LIMITED) - [N16000029]	232.11	07/2009	243.76
<u>Power</u>				
57	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL)() - [180100247]	691.83	12/2007	729.86
58	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL)() - [180100253]	279.30	07/2009	288.54
59	KOLDAM HEP TRANSMISSION LINE (PGCIL)() - [180100263]	464.91	09/2008	163.16
60	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- V(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000017]	721.25	06/2009	560.87
61	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000020]	150.26	10/2009	109.54
62	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- VI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000021]	186.95	07/2009	149.82
63	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST- WEST(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000026]	103.80	06/2009	72.52
<u>Railways</u>				
64	LUMDING-SILCHAR(GC),NEFR(NORTH EAST FRONTIER RAILWAY) - [220100170]	648.00	03/2009	2,160.89
65	REWARI-SADULPUR-HISSAR (GC),NWR(NORTH WESTERN RAILWAY) - [220100290]	198.96	-	70.43

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2010				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95


Summary of projects on the Flash Report for the month of March, 2010

I. Project Implementation – Current Status:

Number of Projects Previous Month	618
Number of Projects Completed/Dropped/Frozen in Previous Month	2
Number of Projects Completed/Dropped/Frozen in Current month	12
Number of Projects Added in Current month	27
Number of Projects in Current Month	631

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 631 projects, 14 projects are ahead of schedule, 118 projects are on schedule and 327 projects are delayed. Of the balance, 119 projects do not have fixed dates of commissioning while 53 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

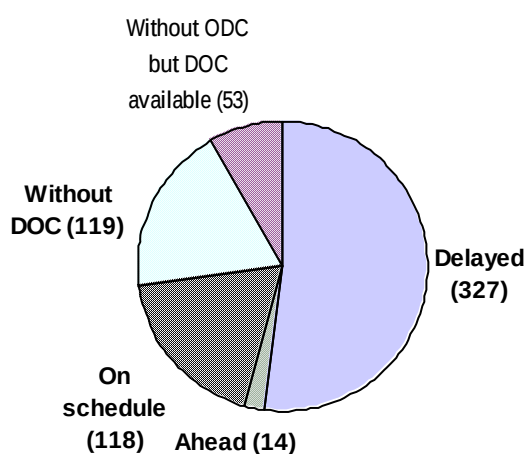

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 631 projects when sanctioned, was of the order of Rs. 590318.36 crore but this was subsequently revised to Rs. 651207.44 crore implying a cost overrun of 10.31%. The expenditure incurred on these projects till March, 2010 is Rs. 273582.18 crore, which is 42.01% of the revised cost of the projects.

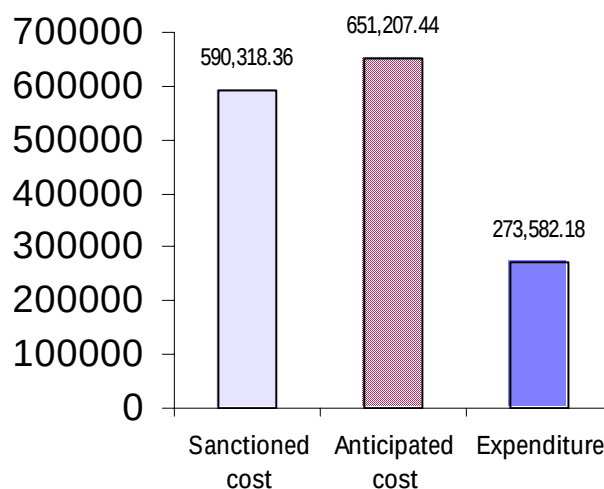

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	618
No of Projects Completed/Dropped/Frozen in Previous Month	2
No of Projects Completed/Dropped/Frozen in Current Month	12
No of Projects added in Current Month	27
No of Projects in Current Month	631

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original	327	14	118	53	119	631	51.82
Latest Approved	366	19	128	41	77	631	58.00

III. (A) Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	533	515,117.34	560,031.47	219,280.78	39.20	44,914.13	8.70
Latest Approved	98	75,201.02	91,175.97	54,301.40	59.60	15,974.95	21.20
Total	631	590,318.36	651,207.44	273,582.18	42.01	60889.08	10.31

III. (B) Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	327	329,972.48	382,184.94	195,567.78	51.20	52,212.46	15.80
Latest Approved	366	50,668.20	400,603.60	210,847.58	52.60	349,935.40	690.60

IV. Additional Delayed Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Latest Approved	112	108,755.63	123,927.54	67,126.87	54.20	15,171.91	14.00
Total	112	108,755.63	123,927.54	67,126.87	54.17	15171.91	13.95

V. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Atomic Energy</u>						
RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL)	04/2002	3,072.00	02/2008	3,072.00	03/2010	2,151.00
<u>Coal</u>						
EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC)	10/2004	2,161.28	06/2009	2,295.93	03/2010	1,808.34
<u>Power</u>						
SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL)	05/2005	279.30	07/2009	340.14	03/2010	288.54
KOLDAM HEP TRANSMISSION LINE (PGCIL)	09/2005	464.91	09/2008	464.91	03/2010	163.16
<u>Railways</u>						
LUMDING-SILCHAR(GC),NEFR	04/1996	648.00	03/2009	4,074.10	03/2012	2,160.89
REWARI-SADULPUR-HISSAR (GC),NWR	04/1997	198.96	N.A.	410.00	N.A.	70.43
<u>Petroleum</u>						
CHENNAI-BANGALORE PIPELINE	07/2007	232.11	07/2009	273.00	03/2010	243.76
<u>Power</u>						
NORTHERN REGION SYSTEM STRENGHTENING SCHEME-V	06/2006	721.25	06/2009	721.25	03/2010	560.87
NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL)	01/2005	691.83	12/2007	913.33	03/2010	729.86
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI	01/2007	186.95	07/2009	186.95	03/2010	149.82
SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN	10/2006	150.26	10/2009	153.24	03/2010	109.54
ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST	10/2006	103.80	06/2009	103.80	03/2010	72.52

VI. List of projects added (Cost in Rs. crore)					
		<u>Original</u>		<u>Anticipated</u>	
Project	DOA	Cost	DOC	Cost	DOC
Telecommunications					
Implementation of FTTH, the state of the art Acces	12/2007	152.65	3/2010	152.65	10/2010
Procurement of 10G (40 chl) DWDM equipment	8/2006	590.10	3/2009	590.10	12/2010
Coal					
MANUGURU OC-II EXTENSION PHASE-II	3/2010	181.91	3/2012	181.91	3/2012
Urban Development					
C/O of Jawahar Lal Nehru Bhawan at Janpath, New Del	9/2005	143.95	/	143.95	1/2010
Telecommunications					
Procurement of STM-16 ADM equipment	2/2007	477.00	3/2010	477.00	12/2010
Urban Development					
C/o Institute of traumatology for GMC srinagar und	6/2007	100.00	10/2009	101.00	6/2010
Shipping & Ports					
SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT	3/2008	375.00	1/2009	375.00	-
Telecommunications					
Procurement of 24 F OF cable.	2/2008	199.00	3/2010	136.00	11/2010
Procurement of STM-16 MADM equipment	3/2008	355.92	3/2010	355.92	12/2010
Execution of telecom network requirement of defence	5/2006	1,077.00	3/2009	1,077.00	9/2010
Shipping & Ports					
DEV. & OPERATION OF AN INTERNATIONAL CONTAINER TRA	11/2004	2,118.00	11/2004	2,118.00	8/2010
SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU	3/2009	3,500.00	1/2012	3,500.00	1/2012
Telecommunications					
Procurement of 2.5G DWDM equipment	8/2006	424.00	3/2009	424.00	12/2010
Procurement of STM-1 SDH equipment	2/2007	154.03	3/2010	154.03	12/2010
Urban Development					

C/o office building for IDBI at bandra Kurla Compl	11/2006	114.18	4/2009	114.18	2/2010
Telecommunications					
Procurement of DXC equipment	2/2008	229.00	3/2010	229.00	11/2010
Implementation of FTTH, the state of the art access ,gpon eq	12/2007	952.88	3/2010	952.88	10/2010
Steel					
BILADILLA IRON ORE DEPOSITE-11B	1/2009	295.89	10/2009	295.89	6/2010
Urban Development					
Upgradation of govt medical colg jammu &C/O supers	5/2007	100.00	4/2009	101.00	1/2010
Civil Aviation					
CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3	6/2009	213.35	9/2010	213.35	11/2010
Petroleum					
VKPL SPURLINE	12/2009	463.32	6/2011	463.32	5/2011
Urban Development					
C/O Bldg for Cabinet Sectt at pocket-5A,Lodhi Road	2/2004	146.18	/	146.18	11/2009
Telecommunications					
Procurement of 10G 40 CHL (12 chi equipped) DWDM	12/2007	545.50	3/2010	545.50	12/2010
Coal					
RKP OCP PHASE-I	3/2010	201.58	3/2015	201.58	3/2015
RAMAGUNDAM OC-II EXTENSION	12/2009	418.57	3/2012	418.57	3/2012
Petroleum					
BNPL SPURLINE	12/2009	540.92	6/2011	540.92	5/2011
Urban Development					
Development of Minto Road Area,New Delhi,C/O 140 t	8/2008	135.53	12/2010	135.53	4/2011

VII. Milestones (Cumulative due & achieved)

Total	1754
Achieved up to month	625

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	03/2010	06/2010	3
<u>Civil Aviation</u>						
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	1,942.51	1,942.51	05/2011	05/2011	08/2011	3
Construction of New Expandable Modular Integrated	135.72	135.72	09/2009	03/2010	07/2010	4
<u>Coal</u>						
TUTICORIN THERMAL POWER PROJECT	4,904.54	4,904.54	08/2012	09/2012	08/2012	-1
KAKATIYA LAONGWALL	453.63	453.63	12/2012	12/2012	03/2013	3
BLOCK-B OCP NCL (3.5 MTY)	746.04	437.34	03/2012	03/2012	03/2013	12
JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II	122.35	122.35	03/2010	03/2013	12/2014	21
AMLOHRI EPR (NCL) (6 MTY)	1,352.04	1,143.54	03/2014	03/2014	03/2016	24
NARAYANKURI UG	149.06	149.06	03/2013	03/2013	03/2015	24
KRISHNASHILA (NCL) (4MTY)	789.88	741.56	03/2010	03/2010	03/2013	36
CHITRA EAST OCP	112.69	112.69	11/2010	03/2013	03/2016	36
JHANJRA LONGWAL UG PHASE II	287.18	287.17	11/2009	01/2012	03/2015	38
DIPKA EXPANSION OCP (SECL) (20 MTY)	1,268.53	1,943.66	03/2010	03/2010	03/2014	48
<u>Steel</u>						
POWER PLANT-I	462.00	350.00	12/2009	01/2011	08/2010	-5
REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL	892.32	892.32	08/2009	03/2010	04/2010	1
COAL DUST INJECTION IN BF-2 and 3	132.73	133.92	05/2008	03/2010	05/2010	2
EXPANSION OF BOKARO STEEL PLANT	3,316.00	3,534.00	N.A.	10/2011	12/2011	2
REBUILDING OF COKE OVEN BATTERY-10	416.50	416.50	09/2009	03/2010	06/2010	3
Pulverised coal injection system for bf-1&2	125.00	133.00	09/2009	03/2010	08/2010	5
Rebuilding of coke oven battery No.1 & 2 (Bokaro S	500.90	500.90	04/2010	10/2010	04/2011	6
EXPANSION OF BHILAI STEEL PLANT	5,185.00	6,146.00	05/2011	09/2012	03/2013	6

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
EXPENSION OF ROURKELA STEEL PLANT	6,133.00	8,128.00	02/2011	03/2012	03/2013	12
<u>Petroleum</u>						
DEVELOPMENT OF B-193 CLUSTER FIELDS	3,248.78	5,633.44	03/2010	03/2012	04/2012	1
MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY	372.00	372.00	02/2010	06/2010	07/2010	1
MSQ UPGRADATION PROJECT AT DIGBOI REFINERY	356.00	356.00	02/2010	06/2010	07/2010	1
MSQ IMPROVMENT PROJECT	293.60	293.60	12/2009	06/2010	07/2010	1
HEERA RECONSTRUCTION	706.70	706.70	04/2010	04/2010	05/2010	1
CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	224.00	224.00	12/2010	12/2010	02/2011	2
BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA	349.00	349.00	08/2011	08/2011	12/2011	4
DEVELOPMENT OF C-SERIES FIELDS	3,195.16	2,800.00	12/2008	05/2010	10/2010	5
ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA	370.11	370.11	04/2011	12/2011	06/2012	6
MNW-NF BRIDGE PROJECT	175.21	162.12	03/2009	05/2010	12/2010	7
ADDITIONAL GAS PROCESSING UNITS AT URAN	1,797.35	1,797.35	12/2011	12/2011	09/2012	9
<u>Power</u>						
KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL)	596.45	1,007.16	12/2007	03/2010	06/2010	3
Farakka STPP Stage-III	2,570.44	2,570.44	08/2010	08/2010	11/2010	3
BONGAIGAON THERMAL POWER PROJECT	4,375.35	4,375.35	07/2011	11/2011	02/2012	3
CHAMERA,STAGE-III (NHPC)	1,405.63	1,405.63	08/2010	08/2010	12/2010	4
NIMOO BAZGO HYDROELECTRIC PROJECT	611.01	611.02	08/2010	08/2010	12/2010	4
KOTESWAR TRANSMISSION SYSTEM (PGCIL)	260.34	241.27	06/2008	03/2010	08/2010	5
WESTERN REGION STRENGTHENING SCHEME-II	5,221.23	5,221.23	07/2010	07/2010	12/2010	5
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G	290.49	290.49	04/2010	04/2010	09/2010	5

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME	803.70	803.76	06/2009	03/2010	09/2010	6
PARBATI H.E.P. STAGE -III (NHPC)	2,304.56	2,304.52	10/2010	11/2010	06/2011	7
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE	557.24	557.25	01/2010	11/2010	06/2011	7
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)	3,779.46	3,779.46	09/2009	03/2010	12/2010	9
EASTERN REGION STRENGTHENING SCHEME-I	975.96	975.96	10/2009	03/2010	12/2010	9
KOTESHWAR HEP(THDC)	1,301.56	1,301.56	04/2005	12/2010	10/2011	10
TEHRI PUMPED STORAGE PLANT(1000MW)	1,657.00	1,657.60	07/2010	04/2013	12/2014	20
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	2,491.58	2,491.58	06/2013	06/2013	03/2015	21
<u>Railways</u>						
TOLLYGANJ-GARIA(MTP)	907.69	1,032.76	12/2006	03/2010	06/2010	3
DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	180.73	335.00	12/2006	03/2010	11/2010	8
BARAMATI - LONAND (NL), CR	75.00	138.48	N.A.	06/2010	03/2011	9
SITAMARHI-RAXAUL-NARKATIAGANJ (GC)	501.69	501.69	03/2010	06/2011	03/2012	9
SRIGANGANAGAR-SARUPSAR (GC), NWR	143.92	168.80	N.A.	03/2010	03/2011	12
NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I	99.84	110.94	03/2010	03/2010	03/2011	12
JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	233.00	727.52	N.A.	03/2010	03/2012	24
HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	324.66	528.65	N.A.	06/2011	03/2015	45
UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	2,500.00	11,270.00	03/2001	12/2012	12/2017	60
<u>Road Transport & Highways</u>						
FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2)	372.40	372.40	07/2004	03/2010	04/2010	1
PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57	276.00	276.00	04/2008	03/2010	04/2010	1
PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57	310.00	310.00	04/2008	03/2010	04/2010	1
MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160	507.49	507.49	03/2008	03/2010	04/2010	1

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	263.00	263.00	02/2009	03/2010	04/2010	1
SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47	469.80	469.80	12/2008	03/2010	04/2010	1
BANGALORE- NEELAMANGLALA NH-4	445.00	445.00	07/2010	03/2010	04/2010	1
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00	193.09	193.09	03/2008	05/2010	07/2010	2
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80	166.27	166.27	03/2008	05/2010	07/2010	2
PADALUR-TRICHY, NH-45	320.00	320.00	05/2009	02/2010	04/2010	2
SIX LANING OF BANGLORE- HOSUR SECTION OF NH-7, PHAS	110.00	110.00	07/2008	01/2010	03/2010	2
BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5)	140.85	140.85	01/2004	12/2009	03/2010	3
GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH- 2)	399.75	399.75	03/2005	03/2010	06/2010	3
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31	205.73	205.73	07/2004	03/2010	06/2010	3
CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5	480.00	480.00	11/2007	03/2010	06/2010	3
DEVDHARI-KELAPUR	144.00	144.00	07/2005	03/2010	06/2010	3
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	359.00	359.00	03/2009	03/2010	06/2010	3
SAGAR - RAJMARG CHORAH, KM 255-297, NH- 26 (NHAI)	206.96	206.96	10/2008	01/2010	04/2010	3
NAGPUR-KONDHALI, NH- 6(NHAI)	168.00	168.00	12/2008	01/2010	04/2010	3
BARA TO ORAI, NH-2, 25	465.00	465.00	04/2009	03/2010	06/2010	3
GORAKHPUR BYPASS, NH- 28, PHASE-II EAST-WEST CORRID	600.24	600.24	10/2009	12/2010	03/2011	3
JHANSI TO LALITPUR, NH- 25,26	355.06	355.06	09/2009	06/2010	09/2010	3
AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2	193.00	193.00	10/2008	06/2010	10/2010	4
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	217.00	217.00	10/2008	06/2010	10/2010	4

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00	239.00	239.00	10/2008	06/2010	10/2010	4
GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00	205.00	205.00	10/2008	06/2010	10/2010	4
AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075	212.00	212.00	10/2008	06/2010	10/2010	4
ORAI TO JHANSI (UP-4),NH- 25, KM.170.0 TO KM.104.0	451.97	451.97	04/2008	06/2010	10/2010	4
VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)	467.93	467.93	03/2005	01/2010	06/2010	5
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	629.00	629.00	11/2010	01/2010	06/2010	5
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	225.00	225.00	10/2008	05/2010	10/2010	5
NEW MANGALORE PORT NH-17 AND 48	196.50	196.50	06/2008	01/2010	06/2010	5
TRICHY - KORUR NH-67	516.00	516.00	07/2010	07/2010	12/2010	5
KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203- 233.60), NH-7	120.00	120.00	09/2006	04/2010	10/2010	6
HAPUR-GARH Mukteswar (OTHERS) KM.58-93, NH-24	220.00	220.00	09/2007	12/2010	06/2011	6
MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH- 7,KM.80 TO KM.120	323.36	323.36	03/2008	03/2010	09/2010	6
LALITPUR TO SAGAR, NH-26 (NHAI)	198.00	198.00	11/2008	09/2010	03/2011	6
RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	251.03	251.03	10/2008	12/2010	06/2011	6
RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA)	229.91	229.91	10/2008	12/2010	06/2011	6
SITAPUR-LUCKNOW	322.00	322.00	06/2009	06/2010	12/2010	6
SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	157.47	154.57	09/2007	06/2010	03/2011	9
AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	367.49	367.49	03/2005	03/2010	12/2010	9
JHAJHARPUR TO DARBANGA (BR-7)	340.00	340.00	09/2008	03/2011	12/2011	9
NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	557.00	557.00	02/2010	02/2010	12/2010	10
BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	230.00	230.00	06/2005	12/2010	12/2011	12

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A	284.00	284.00	05/2008	12/2009	12/2010	12
BIJNI TO ASSAM /WB.BORDER (NH- 31.C)(2)(NHAI)	237.80	237.80	06/2008	12/2010	12/2011	12
SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)	225.00	225.00	04/2004	08/2010	10/2011	14
GUWHATI TO NALBARI (AS- 4)	175.96	175.96	04/2008	12/2010	03/2012	15
HARANGAJO TO MAIBANG, NH-54	196.00	196.00	07/2009	12/2010	12/2012	24
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	11/2010	03/2010	-8
DEEPENING OF CHEENEL AT PARADIP PORT	154.84	253.36	06/2007	03/2010	06/2010	3
<u>Urban Development</u>						
DELHI MRTS PHASE-II PROJECT	8,118.00	8,676.00	06/2010	10/2010	11/2010	1
BANGALORE METRO RAIL PROJECT	6,395.00	6,395.00	12/2011	12/2011	06/2012	6
Number of projects reporting additional delay = 112						

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	21,982.29	21,982.29	23,236.29
Civil Aviation	18	6,474.82	6,419.89	6,452.24
Coal	44	24,603.32	25,646.54	26,651.29
Mines	1	4,091.51	4,091.51	4,091.51
Steel	29	45,769.25	45,769.25	53,073.27
Petroleum	78	150,894.93	153,687.11	171,788.29
Power	77	162,568.99	164,383.07	166,946.23
Health & Family Welfare	1	71.18	422.60	443.15
Railways	155	52,917.97	65,046.53	95,910.99
Road Transport & Highways	151	43,916.82	43,916.82	44,119.51
Shipping & Ports	23	24,147.63	24,147.63	24,730.99
Telecommunications	40	16,794.98	16,616.45	16,628.81
Urban Development	9	15,336.51	17,645.77	15,947.87
Water Resources	1	542.90	542.90	1,187.00
Grand total	631	570,113.10	590,318.36	651,207.44


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	4
Number of Projects Wo_Odc_Original	1
Number of Projects Delayed	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 projects are Wo_Odc_Original and 3 projects are delayed.



Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 4 projects when sanctioned, was of the order of Rs. 21982.29 Crores but this was subsequently revised to Rs. 23236.29 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 18050.75 Crores.

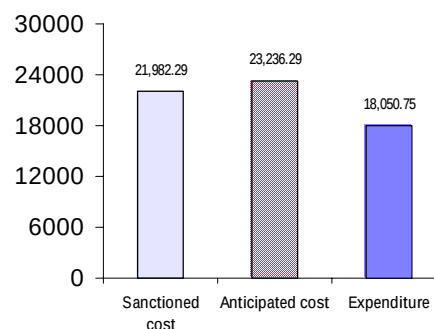


2. Sector: - Civil Aviation

Number of Projects	18
Number of Projects on schedule	3
Number of Projects Delayed	8
Number of Projects Wo_Doc_Original	3
Number of Projects Wo_Odc_Original	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are on schedule, 8 projects are delayed and 4 projects are original date of commissioning and 3 projects are Wo_Odc_original.



Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs. 6474.82 Crores but this was subsequently revised to Rs. 6452.64 Crores. The expenditure incurred on these projects till March, 2010 is Rs 1959.85 Crores.

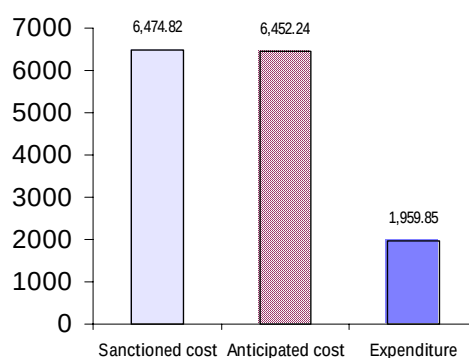


3. Sector: - Coal

Number of Projects	44
Number of Projects on schedule	15
Number of Projects Delayed	25
Number of Projects Ahead	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 44 projects, 15 projects are on schedule, 25 projects are delayed and 4 projects are ahead .



Investment Scenario

The total cost of implementation of 44 projects when sanctioned, was of the order of Rs. 24603.32 Crores but this was subsequently revised to Rs. 26651.29 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 9512.18 Crores

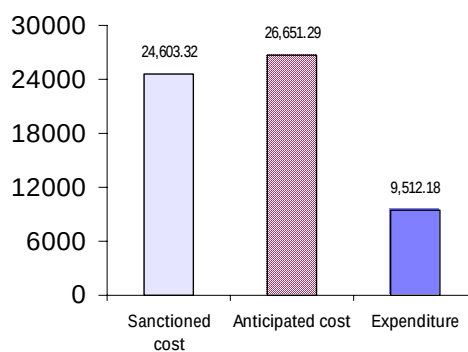


4. Sector: - Petroleum

Number of Projects	78
Number of Projects on schedule	41
Number of Projects Delayed	27
Number of Projects Ahead	5
Number of Projects Wo_Doc_Original	2
Number of Projects Without original date of commissioning	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 78 projects, 27 projects are on schedule, 41 projects are delayed and 5 projects are ahead and 2 projects are without date of commissioning and 3 Project is Without original date of commissioning.

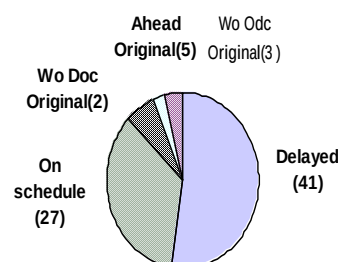

Investment Scenario

The total cost of implementation of 78 projects when sanctioned, was of the order of Rs. 150894.93 Crores but this was subsequently revised to Rs. 171788.29 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 53123.53 Crores.

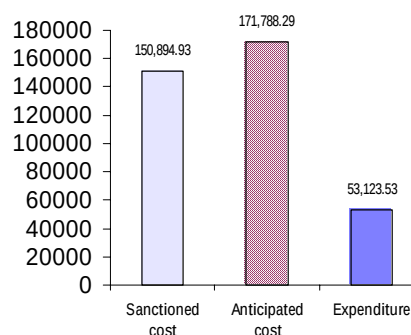


5. Sector: - Power

Number of Projects	77
Number of Projects on schedule	42
Number of Projects Delayed	33
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 77 projects, 42 projects are on schedule, 33 projects are delayed, 1 projects is without date of commissioning and 1 projects is with out original date of commissioning



Investment Scenario

The total cost of implementation of 77 projects when sanctioned, was of the order of Rs. 162568.99 Crores but this was subsequently revised to Rs. 166946.23 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 63339.08 Crores.

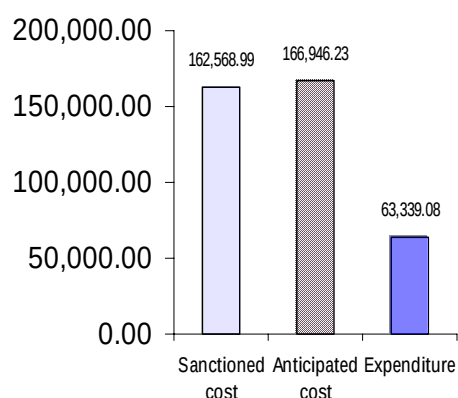


6. Sector: - Railways

Number of Projects	155
Number of Projects on schedule	9
Number of Projects Delayed	41
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	63
Number of Projects Wo_Odc_Original	41


Brief Analysis

Project Status with out respect Original Schedule: Out of 155 projects, 9 projects are on schedule, 41 projects are delayed, 1 projects is ahead. 63 projects are Without date of commissioning and 41 projects are without original date of commissioning.

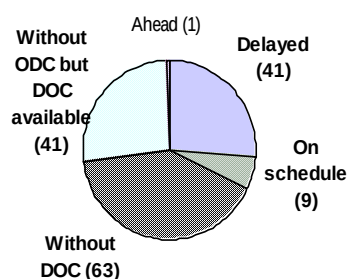

Investment Scenario

The total cost of implementation of 155 projects when sanctioned, was of the order of Rs. 52917.97 Crores but this was subsequently revised to Rs. 95910.99 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 41209.96 Crores.

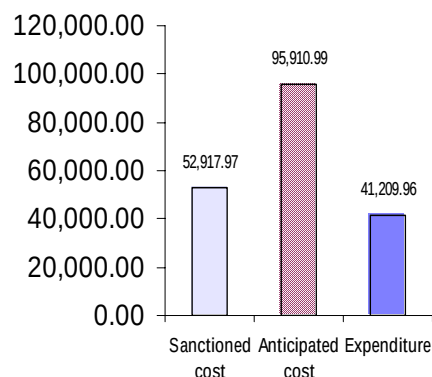


7. Sector: - Road Transport and Highways

Number of Projects	151
Number of Projects on schedule	12
Number of Projects Delayed	130
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	7


Brief Analysis

Project Status with respect to Original Schedule: Out of 151 projects, 12 projects are on schedule, 130 projects are delayed, 2 projects are ahead and 7 projects is with out date of commissioning .

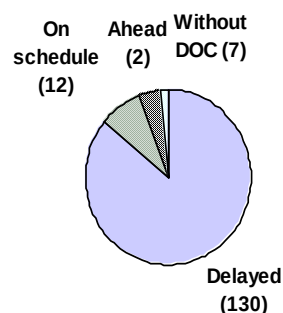

Investment Scenario

The total cost of implementation of 151 projects when sanctioned, was of the order of Rs 43916.82 Crores but this was subsequently revised to Rs. 44119.51 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 37904.15 Crores.

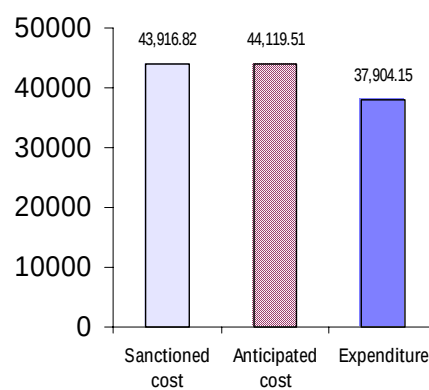


8. Sector: - Shipping and Ports

Number of Projects	23
Number of Projects on schedule	10
Number of Projects Delayed	8
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status with respect to Original Schedule: Out of 23 projects, 10 projects are on schedule, 8 projects are delayed, 2 projects are ahead and 3 projects are without date of commissioning.

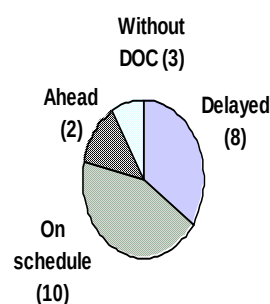

Investment Scenario

The total cost of implementation of 23 projects when sanctioned, was of the order of Rs.24147.63 Crores but this was subsequently revised to Rs. 24730.99 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 4002.18 Crores.

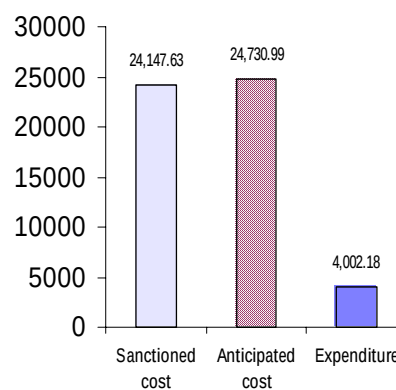


9. Sector: - Steel

Number of Projects	29
Number of Projects on schedule	2
Number of Projects Delayed	20
Number of Projects Wo_Doc_Original	3
Number of Projects Wo_Odc_Original	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 28 projects, 3 projects are on schedule, 22 projects are delayed and 3 projects are without date of commissioning and 4 projects are Wo_Odc_Original.

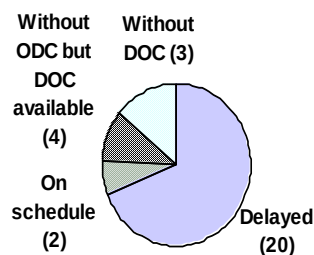

Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs.45769.25 Crores but this was subsequently revised to Rs. 53073.27 Crores. The expenditure incurred on these projects till March, 2010 is Rs. 19832.27 Crores.

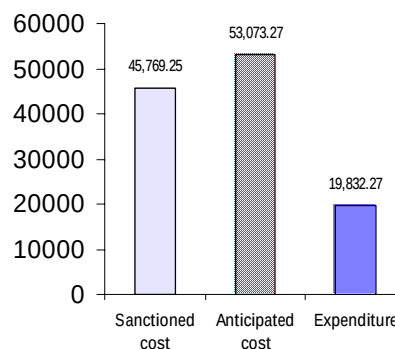


10. Sector: - Telecommunications

Number of Projects	40
Number of Projects Delayed	26
Number of Projects Wo_Doc_Original	14


Brief Analysis

Project Status with respect to Original Schedule: Out of 40 projects, 26 projects are delayed and 14 projects are with our date of commissioning.



Investment Scenario

The total cost of implementation of 40 projects when sanctioned, was of the order of Rs 16794.98 Crores but this was subsequently revised to Rs. 16628.81 Crores. The expenditure incurred on these projects till March, 2010 is Rs 4546.76 Crores.

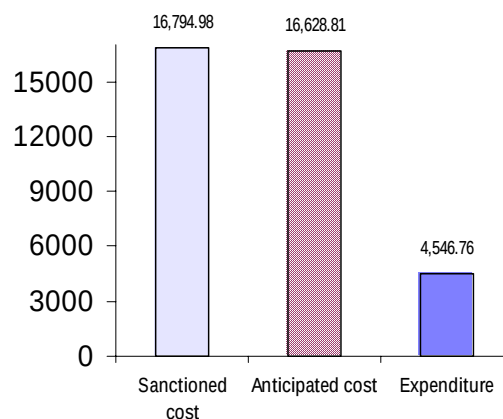

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,532.00	10/2009 09/2007	06/2010	33(R1)	71/75
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,657.00	12/2008	03/2011	27(O)	61/119
3	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	486.37	-	04/2011	-	0/1
4	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,375.38	09/2010	09/2011	12(O)	8/80
Total			21,982.29	23,236.29	18,050.75				140/275
<u>Civil Aviation</u>									
5	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65 135.72	129.65	35.92	09/2009 03/2010	03/2010	0(R3)	0/0
6	Construction of New Integrated Passenger Terminal - [N04000042]	03/2006	129.38	129.38	13.49	04/2009 10/2009	03/2010	5(R2)	0/0
7	Construction of New Integrated terminal building - [N04000051]	04/2007	128.96	128.96	20.90	02/2009 06/2009	03/2010	9(R2)	0/0
8	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60	113.02	44.76	-	05/2010	-	0/1
9	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	239.59	-	06/2010	-	1/24
10	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04	135.04	69.43	09/2009	06/2010	9(O)	0/0
11	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	143.97	06/2010	06/2010	0(O)	0/0
12	C/o new Integrated terminal Bldg. at Birsa Munda - [N04000049]	01/2009	137.79	137.79	7.50	01/2010 02/2010	06/2010	4(R2)	0/0
13	Construction of New Expandable Modular Integrated - [N04000047]	03/2008	135.72	135.72	41.96	09/2009 12/2009	07/2010	7(R2)	0/0
14	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3 - [N04000068]	06/2009	213.35	213.35	56.00	09/2010	11/2010	2(O)	0/0
15	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94	144.94	27.83	-	12/2010	-	0/2
16	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]	08/2008	1,273.00 1,212.00	1,273.00	255.24	01/2011	01/2011	0(O)	0/0
17	Extension of Secondary Runway(K2) - [N04000056]	08/2008	230.00	230.00	188.12	01/2011	01/2011	0(O)	0/0
18	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	579.26	05/2011	08/2011	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
19	C/o new Airport-SH: E/W in cutting and filling geogrid - [N04000050]	01/2009	264.29	264.29	10.02	01/2011	-	-	0/0
20	Construction of New Integrated Terminal Building - [N04000052]	10/2006	147.00	147.00	46.43	09/2008 02/2009	-	-	0/0
21	C/O PASSENGER LOUNGE BIRSI AIRPORT - [N04000057]	03/2006	108.07	108.07	19.14	08/2008	-	-	0/0
22	GAGAN PROJECT - [N04000065]	09/2008	393.60	393.60	160.29	06/2013	-	-	0/0
	Total		6,474.82	6,452.24	1,959.85				1/27
Coal									
23	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	989.35	03/2010	03/2010	0(O)	3/7
24	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39	131.39	382.90	03/2010	03/2010	0(O)	0/0
25	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	473.97	03/2009	03/2010	12(O)	0/0
26	KTK OC Sector-I - [N06000077]	01/2008	91.50	115.33	121.01	09/2010	03/2010	-6(O)	0/0
27	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07 254.60	254.60	214.51	06/2009	05/2010	11(O)	18/21
28	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18 1,626.09	1,626.09	1,407.82	06/2009	09/2010	15(O)	32/26
29	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74	116.54	247.82	03/2007	03/2011	48(O)	0/0
30	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 2,453.57	2,453.57	1,948.27	06/2009	06/2011	24(O)	23/24
31	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	57.90	03/2010	03/2012	24(O)	0/4
32	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66 341.63	341.63	101.35	03/2011	03/2012	12(O)	0/0
33	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	37.04	03/2012	03/2012	0(O)	0/0
34	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	-	03/2012	03/2012	0(O)	0/0
35	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	249.85	03/2012	03/2012	0(O)	0/0
36	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.57	418.57	36.78	03/2012	03/2012	0(O)	0/0
37	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]	03/2010	181.91	181.91	-	03/2012	03/2012	0(O)	0/0
38	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	725.00	08/2012	08/2012	0(O)	0/0
39	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34 779.26	779.26	41.48	03/2013	09/2012	-6(O)	2/11
40	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88 741.56	741.56	134.82	03/2010	03/2013	36(O)	0/1
41	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	583.32	03/2011 03/2013	03/2013	0(R3)	0/4

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
42	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04 437.34	437.34	135.44	03/2012 -	03/2013	12(O)	0/1
43	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	706.40	12.12	07/2012 -	03/2013	8(O)	0/1
44	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78 -	467.78	11.29	03/2013 -	03/2013	0(O)	0/7
45	KANIHA OCP - [N06000035]	12/2007	457.77 -	457.77	48.96	03/2012 -	03/2013	12(O)	0/0
46	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63 -	453.63	46.73	12/2012 -	03/2013	3(O)	0/0
47	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93 -	479.53	175.35	03/2013 -	03/2013	0(O)	0/0
48	BINA EXTN. PROJ - [N06000019]	11/2006	168.97 -	168.97	139.77	03/2014 -	11/2013	-4(O)	1/1
49	DIPKA EXPANSION OCP (SECL) (20 MTY) - [N06000094]	07/2005	1,268.53 -	1,943.66	777.67	03/2010 -	03/2014	48(O)	2/6
50	CHURCHA UG - [N06000046]	06/2008	462.35 -	462.35	270.87	06/2014 -	03/2014	-3(O)	0/0
51	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08 -	153.82	3.14	03/2010 -	03/2014	48(O)	0/0
52	PENGANGA OC - [N06000066]	10/2008	339.77 -	339.77	-	03/2014 -	03/2014	0(O)	0/0
53	KARTALI (EAST) OC - [N06000076]	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/0
54	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35 -	122.35	-	03/2010 12/2011	12/2014	36(R3)	0/0
55	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18 -	287.17	-	11/2009 01/2012	03/2015	38(R3)	0/0
56	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87 -	395.87	22.73	03/2013 -	03/2015	24(O)	0/0
57	PELMA OC - [N06000045]	07/2008	448.32 -	448.32	-	03/2012 -	03/2015	36(O)	0/0
58	Batura OC - [N06000049]	09/2008	203.82 -	203.82	-	03/2013 -	03/2015	24(O)	0/0
59	NARAYANKURI UG - [N06000059]	02/2009	149.06 -	149.06	-	03/2013 -	03/2015	24(O)	0/0
60	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58 -	135.58	25.88	03/2015 -	03/2015	0(O)	0/0
61	JAGANNATHPOR OC - [N06000075]	09/2008	152.43 -	152.43	-	03/2015 -	03/2015	0(O)	0/0
62	RKP OCP PHASE-I - [N06000079]	03/2010	201.58 -	201.58	0.19	03/2015 -	03/2015	0(O)	0/0
63	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04 1,143.54	1,143.54	27.01	03/2014 -	03/2016	24(O)	1/1
64	BHUBANESWARI OCP - [N06000034]	12/2007	490.10 -	490.10	56.52	03/2014 -	03/2016	24(O)	0/0
65	TALABIRA OCP - [N06000043]	03/2008	447.72 -	447.72	5.32	03/2015 -	03/2016	12(O)	0/0
66	CHITRA EAST OCP - [N06000060]	08/2007	112.69 -	112.69	-	11/2010 -	03/2016	64(O)	0/0
Total			24,603.32 -	26,651.29	9,512.18				82/115

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Mines</u>									
67	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51 -	4,091.51	3,316.00	12/2008 -	11/2009	11(O)	18/111
	Total		4,091.51 -	4,091.51	3,316.00				18/111
<u>Steel</u>									
68	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDC) - [N12000018]	01/2003	295.89 -	607.17	206.09	10/2009 -	10/2009	0(O)	2/21
69	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94 -	248.94	164.48	08/2009 -	02/2010	6(O)	0/0
70	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66 -	197.66	103.09	- -	03/2010	-	0/1
71	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32 -	892.32	527.00	08/2009 -	04/2010	8(O)	0/0
72	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73 -	133.92	87.24	05/2008 -	05/2010	24(O)	0/2
73	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50 -	416.50	244.28	09/2009 -	06/2010	9(O)	0/0
74	BILADILLA IRON ORE DEPOSIT-11B - [N12000017]	01/2009	295.89 -	295.89	213.74	10/2009 -	06/2010	8(O)	0/0
75	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88 -	119.88	47.03	- -	06/2010	-	0/1
76	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00 -	1,902.00	1,031.35	- -	06/2010	-	0/3
77	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78 -	191.00	74.27	01/2010 -	06/2010	5(O)	0/0
78	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00 -	170.00	42.02	06/2010 -	06/2010	0(O)	0/0
79	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70 -	302.70	227.50	06/2009 -	07/2010	13(O)	0/0
80	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00 -	133.00	36.47	09/2009 -	08/2010	11(O)	0/0
81	POWER PLANT-I - [N12000039]	09/2007	462.00 -	350.00	84.40	12/2009 -	08/2010	8(O)	0/0
82	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	353.00	80.00	02/2010 -	08/2010	6(O)	0/0
83	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50 -	145.00	6.64	12/2010 -	12/2010	0(O)	0/0
84	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00 -	358.00	114.32	02/2010 -	01/2011	11(O)	0/0
85	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90 -	500.90	165.99	04/2010 -	04/2011	12(O)	0/0
86	700TPD AIR SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30 -	232.93	50.18	07/2009 -	05/2011	22(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
87	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.33	12.97	08/2009	05/2011	21(O)	0/0
88	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	5,883.00	10/2009	06/2011	20(O)	0/126
89	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	12.00	10/2009	06/2011	20(O)	0/0
90	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	6,545.80	07/2010	06/2011	11(O)	0/0
91	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	4.04	09/2010	12/2011	15(O)	0/0
92	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,534.00	932.87	-	12/2011	-	0/2
93	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	8,128.00	1,253.17	02/2011	03/2013	25(O)	0/0
94	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	6,146.00	1,474.84	05/2011	03/2013	22(O)	0/0
95	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91	134.32	103.00	03/2008	-	-	0/3
96	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02	143.02	104.49	11/2008	-	-	0/0
Total			45,769.25	53,073.27	19,832.27				2/159
<u>Petroleum</u>									
97	CLEAN FUELS PROJECT AT VISAKH REFINERY (HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	43(O)	29/45
98	CRUDE OIL RECEIPT FACILITIES, KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.00	09/2009	12/2009	3(O)	0/0
99	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	750.71	12/2009	01/2010	1(O)	0/0
100	SHORT TERM LOW COST MUMBAI REFINERY - [N16000082]	12/2006	390.00	230.00	164.51	01/2010	01/2010	0(O)	0/0
101	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00	2,869.00	2,550.34	04/2009	02/2010	2(R1)	31/36
102	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	186.58	12/2009	02/2010	2(O)	0/0
103	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]	09/2009	2,591.80	3,941.41	2,176.19	12/2009	02/2010	2(O)	0/0
104	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	12,138.00	14,439.00	11,284.00	09/2009	03/2010	4(R1)	61/101
105	CHAINSARAJHAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77	565.00	382.13	09/2009	03/2010	6(O)	0/0
106	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13	396.13	52.34	10/2009	03/2010	5(O)	0/0
107	BINA DESPATCH TERMINAL - [N16000078]	05/2007	490.71	639.11	520.92	12/2009	03/2010	3(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	BINA KOTA PIPE LINE PROJECT - [N16000079]	07/2007	405.82	405.82	277.56	12/2009	03/2010	3(O)	0/0
109	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66 350.00	389.00	347.92	06/2008	04/2010	22(O)	0/0
110	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00	139.07	57.04	10/2009	04/2010	6(O)	0/0
111	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	3,114.04	11/2009 04/2010	04/2010	0(R3)	0/0
112	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	416.51	04/2009	05/2010	13(O)	0/0
113	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	198.16	05/2010	05/2010	0(O)	0/0
114	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	218.16	04/2010	05/2010	1(O)	0/0
115	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	418.76	-	05/2010	-	0/2
116	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,675.72	1,218.02	09/2009	06/2010	9(O)	0/0
117	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00	6,898.00	5,086.94	01/2010	06/2010	5(O)	0/0
118	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	2,305.30	1,966.04	06/2010 06/2010	06/2010	0(R1)	0/0
119	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	795.50	04/2010	06/2010	2(O)	0/0
120	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18	143.84	99.12	06/2010	06/2010	0(O)	0/0
121	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	258.82	09/2009	06/2010	9(O)	0/0
122	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	651.43	06/2006 05/2008	07/2010	26(R1)	0/2
123	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	184.43	02/2010	07/2010	5(O)	0/0
124	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	170.70	02/2010	07/2010	5(O)	0/0
125	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60	293.60	158.44	12/2009	07/2010	7(O)	0/0
126	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]	06/2005	806.00 1,007.83	1,007.83	593.33	03/2008 12/2009	08/2010	8(R1)	18/48
127	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	2,800.00	2,448.39	12/2008	10/2010	22(O)	0/0
128	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	8.66	10/2010	10/2010	0(O)	0/0
129	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	1.13	10/2010	10/2010	0(O)	0/0
130	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38	3,000.00	176.96	10/2010	10/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00	1,212.85	18.46	10/2011	10/2010	-12(O)	0/0
132	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009	12/2010	21(O)	0/0
133	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40 605.40	605.40	169.75	12/2010 12/2010	12/2010	0(R3)	0/18
134	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]	06/2008	304.40	304.40	32.06	12/2010	12/2010	0(O)	0/0
135	CAPACITY AUGMENTATION OF AGRA& FERROZABAD REGION - [N16000074]	07/2009	199.57	199.57	-	01/2011	01/2011	0(O)	0/0
136	CONSTRUCTION OF NEW TERMINAL AT ENnore CHENNAI - [N16000066]	01/2008	224.00	224.00	38.99	12/2010	02/2011	2(O)	0/0
137	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	600.00	523.08	03/2007	03/2011	48(O)	3/3
138	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	1,200.00	988.06	03/2007	03/2011	48(O)	6/6
139	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90	219.22	145.95	03/2006	03/2011	60(O)	6/6
140	NORTH TAPTI GAS FIELD DEV. - [N16000085]	07/2008	589.70	589.70	-	03/2011	03/2011	0(O)	0/0
141	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75	8,061.42	3,898.92	06/2009	04/2011	22(O)	0/0
142	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93	1,061.78	9.91	11/2011	04/2011	-7(O)	0/0
143	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	41.56	04/2011	04/2011	0(O)	0/0
144	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,234.69	03/2005	05/2011	74(O)	0/0
145	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	330.40	0.35	05/2010	05/2011	12(O)	0/0
146	BNPL superlines(Uttanchal & Punjab) - [N16000091]	12/2009	540.92	540.92	-	05/2011	05/2011	0(O)	0/0
147	VKPL Upgradation and Laying of Superlines - [N16000092]	12/2009	463.32	463.32	-	05/2011	05/2011	0(O)	0/0
148	VKPL SPURLINE - [N16000093]	12/2009	463.32	463.32	-	06/2011	05/2011	-1(O)	0/0
149	BNPL SPURLINE - [N16000094]	12/2009	540.92	540.92	-	06/2011	05/2011	-1(O)	0/0
150	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	267.00	63.58	-	08/2011	-	0/1
151	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	53.67	09/2011	09/2011	0(O)	0/0
152	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	47.31	09/2011	09/2011	0(O)	0/0
153	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	756.00	170.08	12/2011	12/2011	0(O)	0/0
154	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00	349.00	8.09	08/2011	12/2011	4(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
155	HYDROCRACKER REVAMP & SETTING - [N16000081]	02/2008	825.00	825.00	48.11	12/2011	12/2011	0(O)	0/0
156	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]	06/2007	736.65	736.65	-	12/2011	12/2011	0(O)	0/0
157	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]	01/2010	2,163.64	2,163.64	-	12/2011	12/2011	0(O)	0/0
158	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT. - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0(O)	0/0
159	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	298.68	03/2010 03/2012	03/2012	0(R1)	0/0
160	Integrated offshore crude Oil handling facilities at Paradip - [N16000090]	12/2009	1,492.33	1,492.33	18.75	06/2012	03/2012	-3(O)	0/0
161	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	2,920.82	5.24	02/2009 09/2010	04/2012	19(R1)	0/0
162	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78	5,633.44	0.61	03/2010 08/2010	04/2012	20(R1)	0/0
163	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29	6,326.40	599.85	05/2010	05/2012	24(O)	0/0
164	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2012	22(O)	0/0
165	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]	02/2008	370.11	370.11	8.53	04/2011	06/2012	14(O)	0/0
166	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	478.71	09/2012	09/2012	0(O)	0/0
167	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	9.77	12/2011	09/2012	9(O)	0/0
168	Paradip-Raipur-Sambalpur Ranchi Pipeline - [N16000088]	08/2009	1,793.00	1,793.00	7.12	09/2012	09/2012	0(O)	0/0
169	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	3,212.29	03/2012	11/2012	8(O)	0/0
170	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0(O)	0/0
171	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0(O)	0/0
172	De-bottlenecking of SMPL - [N16000089]	12/2009	1,584.00	1,584.00	1.51	-	12/2012	-	0/0
173	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	-	01/2013	01/2013	0(O)	0/0
174	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	109.52	03/2013	03/2013	0(O)	0/0
Total			150,894.93	171,788.29	53,123.53				154/268
Power									
175	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72	836.14	230.12	07/2006	03/2010	44(O)	2/5
176	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29	1,896.65	1,517.26	11/2008	03/2010	16(O)	25/38

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
177	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,016.74	961.39	09/2007	04/2010	31(O)	8/36
178	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	732.26	12/2007	06/2010	30(O)	7/18
179	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52	227.52	99.87	06/2010	06/2010	0(O)	0/0
180	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57	353.57	58.71	07/2010	07/2010	0(O)	0/0
181	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34	241.27	131.91	06/2008	08/2010	26(O)	8/20
182	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50	2,448.49	1,836.10	02/2010	08/2010	6(O)	5/24
183	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]	06/2006	803.70	803.76	565.34	06/2009	09/2010	15(O)	1/20
184	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69	477.69	272.65	09/2010	09/2010	0(O)	0/0
185	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49	290.49	226.45	04/2010	09/2010	5(O)	0/0
186	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10	262.10	131.66	09/2010	09/2010	0(O)	0/0
187	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33	5,135.33	3,788.60	10/2010	10/2010	0(O)	11/40
188	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44	2,570.44	1,556.10	08/2010	11/2010	3(O)	13/26
189	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72	340.72	113.44	11/2010	11/2010	0(O)	0/0
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55	261.55	98.09	11/2010	11/2010	0(O)	0/0
191	SYSTEM STRENGTHENING SCHEME-VIII OF SOUTHERN REGION - [N18000070]	02/2008	105.84	105.84	54.30	11/2010	11/2010	0(O)	0/0
192	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63	1,405.63	1,154.00	08/2010	12/2010	4(O)	0/0
193	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT (P.G.R.) - [180100260]	12/2005	3,779.46	3,779.46	3,277.46	09/2009	12/2010	15(O)	15/30
194	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96	975.96	552.96	10/2009	12/2010	14(O)	2/20
195	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01	611.02	442.64	08/2010	12/2010	4(O)	0/0
196	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23	5,221.23	2,134.33	07/2010	12/2010	5(O)	3/20
197	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76	417.76	221.24	12/2010	12/2010	0(O)	0/0
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36	408.36	266.49	12/2010	12/2010	0(O)	0/0
199	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89	230.89	13.77	01/2011	01/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
200	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	1,279.40	1,098.09	03/2007	02/2011	47(O)	1/25
201	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	1,084.56	11/2009	02/2011	15(O)	0/0
202	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	621.28	413.22	02/2011	02/2011	0(O)	0/1
203	URI-II - [N18000023]	10/2006	238.25	238.25	172.98	-	05/2011	-	0/0
204	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	2,630.80	05/2011	05/2011	0(O)	0/0
205	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,304.52	991.55	10/2010	06/2011	8(O)	0/0
206	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.25	308.56	01/2010	06/2011	17(O)	0/22
207	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	65.52	06/2011	06/2011	0(O)	0/0
208	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	92.04	06/2011	06/2011	0(O)	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	308.00	07/2011	07/2011	0(O)	0/0
210	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	151.82	07/2011	07/2011	0(O)	0/0
211	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	11.61	07/2011	07/2011	0(O)	0/0
212	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,307.03	707.60	09/2009	08/2011	23(O)	0/0
213	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19	132.19	9.30	08/2011	08/2011	0(O)	0/0
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	43.26	08/2011	08/2011	0(O)	0/0
215	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97	328.97	81.61	09/2011	09/2011	0(O)	0/0
216	KOTESHWAR HEP(THDC) - [180100184]	04/2000	1,301.56	1,301.56	1,771.49	04/2005	10/2011	78(O)	0/0
217	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39	8,323.39	6,617.70	12/2009	10/2011	22(O)	33/56
218	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48	520.48	122.49	11/2011	11/2011	0(O)	0/0
219	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66	509.66	16.10	11/2011	11/2011	0(O)	0/0
220	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69	317.69	2.51	11/2011	11/2011	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19	184.19	21.18	11/2011	11/2011	0(O)	0/0
222	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15	4,527.15	3,041.00	04/2009	12/2011	32(O)	19/41
223	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01	623.44	16.72	01/2012	01/2012	0(O)	0/0
224	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35	4,375.35	898.50	07/2011	02/2012	7(O)	0/0
225	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96	664.96	18.54	02/2012	02/2012	0(O)	0/0
226	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50	409.50	-	02/2012	02/2012	0(O)	0/0
227	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29	410.29	38.92	02/2012	02/2012	0(O)	0/0
228	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGION - [N18000060]	02/2009	120.62	120.62	17.22	02/2012	02/2012	0(O)	0/0
229	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32	1,347.32	184.05	02/2012	02/2012	0(O)	0/0
230	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03	2,047.03	787.30	01/2012	03/2012	2(O)	2/10
231	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]	12/2008	573.99	573.99	97.50	08/2012	08/2012	0(O)	0/0
232	MOUDA STPP - [N18000048]	11/2007	5,459.28	5,459.28	836.60	02/2012	08/2012	6(O)	0/0
233	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95	2,360.95	839.43	08/2012	08/2012	0(O)	0/0
234	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33	7,075.33	1,658.95	08/2012	08/2012	0(O)	0/0
235	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12	4,824.12	380.23	10/2012	10/2012	0(O)	0/0
236	VINDHYACHAL STTP STAGE-IV - [N18000072]	01/2009	5,915.00	5,915.00	551.00	11/2012	11/2012	0(O)	0/0
237	RIHAND STTP STAGE-III (2X500MW) - [N18000073]	01/2009	6,230.81	6,230.81	480.10	11/2012	11/2012	0(O)	0/0
238	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33	6,285.33	3,973.26	09/2010	12/2012	27(O)	2/11
239	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	6.09	12/2008 09/2010	12/2012	27(R1)	0/15
240	LOHARINAG-PAL HEP(4X150MW) - [N18000005]	06/2006	2,895.10	2,895.10	552.33	11/2011	12/2012	13(O)	6/34
241	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	540.91	12/2012	12/2012	0(O)	0/0
242	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,919.59	2,743.37	09/2009	03/2013	42(O)	1/20

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
243	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	750.60	03/2013	03/2013	0(O)	5/31
244	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	1,105.86	05/2013	05/2013	0(O)	37/161
245	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	660.60	08/2013	08/2013	0(O)	0/0
246	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	649.65	08/2013	08/2013	0(O)	0/0
247	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,684.40	11/2010	10/2013	35(O)	15/51
248	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	244.34	07/2010	12/2014	53(O)	0/0
249	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	102.49	06/2013	03/2015	21(O)	0/0
250	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	291.66	07/2014	01/2016	18(O)	0/0
251	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			162,568.99	166,946.23	63,339.08				221/775
<u>Health & Family Welfare</u>									
252	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	477.33	03/1999 03/2005	-	-	7/16
Total			71.18	443.15	477.33				7/16
<u>Railways</u>									
253	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38	700.00	97.09	- 03/2011	02/2011	-1(R3)	0/0
254	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 142.98	170.00	111.69	03/2002 03/2011	03/2010	-12(R3)	0/0
255	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00 107.29	103.57	108.76	03/2005 09/2008	05/2009	8(R3)	0/0
256	VALLAPARPADM-IDAPALLY,(NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	298.52	03/2009 03/2009	11/2009	8(R3)	0/0
257	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70 129.70	142.48	110.50	12/2008	12/2009	12(O)	0/0
258	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74	224.51	41.39	-	12/2009	-	0/0
259	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44	209.57	174.22	03/2009	02/2010	11(O)	0/0
260	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	556.48	03/1995	03/2010	180(O)	0/0
261	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998	03/2010	144(O)	0/0
262	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 459.55	571.55	570.37	-	03/2010	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
263	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	758.38	03/2001 -	03/2010	108(O)	0/0
264	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	393.37	03/2004 03/2005	03/2010	60(R1)	0/0
265	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 124.13	281.20	195.39	- -	03/2010	-	0/0
266	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 -	960.48	994.51	03/2003 -	03/2010	84(O)	0/0
267	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 356.90	425.90	122.32	- 11/2008	03/2010	16(R3)	0/0
268	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	502.14	475.41	- -	03/2010	-	0/0
269	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	746.02	06/2007 -	03/2010	33(O)	0/0
270	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	228.09	147.18	- -	03/2010	-	0/0
271	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 546.49	610.07	563.62	- 02/2009	03/2010	13(R1)	0/0
272	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	463.52	- 03/2009	03/2010	12(R1)	0/0
273	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84 -	136.45	131.28	03/2002 -	03/2010	96(O)	0/0
274	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 -	227.52	230.48	03/2008 03/2009	03/2010	12(R1)	0/0
275	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	134.52	03/1998 08/2005	03/2010	55(R3)	0/0
276	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	211.90	142.88	- 03/2009	03/2010	12(R1)	0/0
277	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	126.50	03/2006 -	03/2010	48(O)	0/0
278	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	210.09	03/2008 06/2008	03/2010	21(R3)	0/0
279	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	405.60	130.23	- -	03/2010	-	0/0
280	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 654.51	1,160.52	541.51	- -	06/2010	-	0/0
281	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	296.20	252.59	04/2003 03/2010	06/2010	3(R1)	0/0
282	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	798.33	12/2006 -	06/2010	42(O)	0/0
283	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	194.56	- 02/2009	06/2010	16(R1)	0/0
284	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	221.90	107.41	12/2007 03/2010	07/2010	4(R1)	0/0
285	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	-	0/0
286	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	135.11	- -	09/2010	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
287	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	335.00	303.65	12/2006 12/2008	11/2010	23(R3)	0/0
288	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 -	273.00	256.42	- 03/2009	11/2010	20(R1)	0/0
289	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	24.68	02/2015 -	11/2010	-51(O)	0/0
290	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	263.64	03/2004 -	12/2010	81(O)	0/0
291	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	672.38	674.83	- -	12/2010	-	0/0
292	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 479.20	567.00	219.65	- 12/2009	12/2010	12(R1)	0/0
293	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 -	135.10	-	- -	12/2010	-	0/0
294	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 716.64	718.30	610.35	03/2008 08/2008	12/2010	28(R1)	0/0
295	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
296	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	450.00	26.80	12/2010 -	12/2010	0(O)	0/0
297	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,103.20	3,338.94	12/2010 -	12/2010	0(O)	0/0
298	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	338.18	02/2010 -	02/2011	12(O)	0/0
299	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 -	810.78	39.55	- 03/2011	02/2011	-1(R3)	0/0
300	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	375.21	191.13	- 03/2010	03/2011	12(R1)	0/0
301	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 284.27	475.00	272.66	06/1999 -	03/2011	141(O)	0/0
302	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	80.21	- -	03/2011	-	0/0
303	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	456.45	240.05	06/2004 -	03/2011	81(O)	0/0
304	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	432.50	05/2008 -	03/2011	34(O)	0/0
305	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00 214.09	214.09	132.30	12/2009 -	03/2011	15(O)	0/0
306	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	341.81	- 06/2009	03/2011	21(R3)	0/0
307	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 138.48	138.48	41.06	- -	03/2011	-	0/0
308	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	371.36	234.34	- -	03/2011	-	0/0
309	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	70.43	- -	03/2011	-	0/0
310	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	348.78	53.31	- -	03/2011	-	0/0
311	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	329.70	253.39	03/2009 12/2009	03/2011	15(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
312	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	77.17	03/2010 -	03/2011	12(O)	0/0
313	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0(O)	0/0
314	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.38	03/2011 -	03/2011	0(O)	0/0
315	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	72.27	03/2011 -	03/2011	0(O)	0/0
316	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	60.91	02/2010 -	11/2011	21(O)	0/0
317	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	587.08	645.88	- -	12/2011	-	0/0
318	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
319	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	496.03	27.08	03/2010 -	12/2011	21(O)	0/0
320	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54 -	141.40	103.18	03/2003 -	03/2012	108(O)	0/0
321	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	727.52	75.94	- -	03/2012	-	0/0
322	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	234.45	135.75	- -	03/2012	-	0/0
323	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	341.41	91.23	- -	03/2012	-	0/0
324	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59 -	495.74	58.70	- -	03/2012	-	0/0
325	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	324.90	95.53	03/2010 -	03/2012	24(O)	0/0
326	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69 -	501.69	45.90	03/2010 -	03/2012	24(O)	0/0
327	TAMLUK DIGHA - [N22000097]	03/1984	293.97 -	293.97	1.91	06/2005 -	04/2012	82(O)	0/0
328	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77 274.56	432.46	464.80	03/1994 -	12/2012	225(O)	0/0
329	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	921.00	236.87	03/2009 -	12/2012	45(O)	0/0
330	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	1,480.71	445.84	10/2007 -	12/2012	62(O)	0/0
331	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	687.20	115.25	03/2010 -	12/2012	33(O)	0/0
332	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84 -	410.08	101.53	- -	03/2013	-	0/0
333	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 280.00	899.42	549.08	- -	03/2013	-	0/0
334	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70 915.70	1,556.23	209.47	- -	03/2013	-	0/0
335	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	04/1996	1,000.00 1,500.00	3,087.44	1,843.04	04/2008 12/2011	03/2014	27(R1)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL),NEFR - [220100266]	02/2000	733.00 733.00	1,502.29	483.71	12/2008 -	03/2014	63(O)	0/0
337	CONSTRUCTION OF NEW LINE FROM HARMATHI-TANAGAR/NAR - [N22000083]	09/1996	156.00 156.00	160.48	72.47	- -	03/2014	-	0/0
338	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00 200.00	546.47	0.54	- -	03/2014	-	0/0
339	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	5,300.00	106.13	03/2014 -	03/2014	0(O)	0/0
340	AGARTALA SABROOM - [N22000099]	04/2008	813.34 -	813.34	13.89	03/2014 -	03/2014	0(O)	0/0
341	BHAIRABI SAIRONG - [N22000100]	04/2008	619.34 -	619.34	0.01	04/2014 -	04/2014	0(O)	0/0
342	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	35.74	- -	03/2015	-	0/0
343	SEVOK RANGPO - [N22000102]	04/2008	1,339.48 -	1,339.48	1.42	12/2015 -	12/2015	0(O)	0/0
344	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	2,492.53	186.52	03/2011 -	03/2016	60(O)	0/0
345	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 8,000.00	11,270.00	6,220.19	03/2001 -	12/2017	201(O)	0/0
346	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 407.78	617.63	341.48	- -	-	-	0/0
347	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53 320.66	464.50	487.70	03/1996 06/2009	-	-	0/0
348	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
349	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	232.01	- -	-	-	0/0
350	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
351	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	312.72	- -	-	-	0/0
352	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
353	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
354	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 450.00	730.00	268.96	- -	-	-	0/0
355	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	71.76	- -	-	-	0/0
356	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	341.30	- -	-	-	0/0
357	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	283.44	02/2009 -	-	-	0/0
358	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	103.72	44.83	- -	-	-	0/0
359	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 -	268.00	283.49	12/1999 03/2008	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
360	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0
361	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	63.03	- -	-	-	0/0
362	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	89.61	03/2007 03/2007	-	-	0/0
363	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
364	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	540.09	07/2005 -	-	-	0/0
365	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	- -	-	-	0/0
366	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	62.14	- -	-	-	0/0
367	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
368	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	130.40	- 05/2009	-	-	0/0
369	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
370	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
371	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	5.76	- -	-	-	0/0
372	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	389.28	- -	-	-	0/0
373	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	695.00	9.41	- -	-	-	0/0
374	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	0.28	- -	-	-	0/0
375	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	325.17	278.36	03/2005 12/2008	-	-	0/0
376	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00 -	133.00	-	- -	-	-	0/0
377	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00 -	137.71	9.71	- -	-	-	0/0
378	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	459.91	36.40	- -	-	-	0/0
379	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23 -	120.23	220.17	- -	-	-	0/0
380	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86 -	103.86	28.93	- -	-	-	0/0
381	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	104.79	34.13	- -	-	-	0/0
382	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006 -	-	-	0/0
383	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	1,225.00	120.45	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
384	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10	113.75	40.35	-	-	-	0/0
385	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67	165.67	0.15	-	-	-	0/0
386	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73	230.03	45.76	-	-	-	0/0
387	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79	585.93	102.78	-	-	-	0/0
388	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45	573.12	555.49	-	-	-	0/0
389	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27	100.27	0.01	-	-	-	0/0
390	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10	102.10	22.75	-	-	-	0/0
391	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56	671.82	0.74	-	-	-	0/0
392	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92	261.70	0.08	02/2006	-	-	0/0
393	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67	129.78	90.84	-	-	-	0/0
394	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94	124.00	151.76	03/2004	-	-	0/0
395	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]	09/2007	404.19	711.15	43.36	07/2008	-	-	0/0
396	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17	639.00	190.86	-	-	-	0/0
397	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00	255.96	75.34	-	-	-	0/0
398	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00	227.40	12.67	-	-	-	0/0
399	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00	582.83	28.22	-	-	-	0/0
400	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00	529.88	24.22	-	-	-	0/0
401	BHAKURA DAMODAR - [N22000098]	03/1998	282.70	325.17	24.32	07/2008	-	-	0/0
402	KISHANGANJ JALALGARH - [N22000101]	04/2008	282.92	359.86	0.71	-	-	-	0/0
403	RESTORATION WITH GAUGE CONVERSION OF SILIGHAT TOWN - [N22000103]	04/1993	100.41	949.22	15.65	12/2009	-	-	0/0
404	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00	676.00	300.65	-	06/2011	-6(R3)	0/0
405	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08	1,010.00	45.59	-	12/2012	0(R3)	0/0
406	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00	607.09	189.55	-	12/2012	0(R1)	0/0
407	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64	106.64	141.98	03/2007	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			52,917.97	95,910.99	41,209.96				0/0
<u>Road Transport & Highways</u>									
408	JAWAHARLAL NEHRU PORT PHASE-II, SH-54 - [N24000039]	04/2000	143.00	143.00	120.30	05/2007	10/2009	29(O)	0/0
409	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93	440.93	641.40	12/2006	12/2009	36(O)	0/0
410	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39	534.39	716.15	05/2007	12/2009	31(O)	0/0
411	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]	04/2000	263.00	263.00	317.74	08/2008	12/2009	16(O)	0/0
412	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80	402.80	453.70	03/2009	12/2009	9(O)	0/0
413	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00	450.00	876.61	07/2008	01/2010	18(O)	0/0
414	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85	140.85	149.17	01/2004	03/2010	74(O)	0/0
415	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00	110.00	106.18	06/2005	03/2010	57(O)	0/0
416	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	568.50	03/2009	03/2010	12(O)	0/0
417	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	286.30	08/2008	03/2010	19(O)	0/0
418	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	164.23	06/2008	03/2010	21(O)	0/0
419	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	170.85	04/2008	03/2010	23(O)	0/0
420	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00	110.00	113.84	07/2008	03/2010	20(O)	0/0
421	MAHARASHTRA/AP BORDER TO ISLAM NAGAR, (NS-2/BOT/AP-6), NH-7 - [N24000093]	12/2003	360.42	360.42	457.70	11/2009	03/2010	4(O)	0/0
422	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	127.92	08/2006	04/2010	44(O)	0/0
423	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40	372.40	399.29	07/2004	04/2010	69(O)	0/0
424	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	360.00	04/2008	04/2010	24(O)	0/0
425	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00	310.00	392.26	04/2008	04/2010	24(O)	0/0
426	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	331.03	03/2008	04/2010	25(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
427	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	379.50	02/2009	04/2010	14(O)	0/0
428	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	665.80	12/2008	04/2010	16(O)	0/0
429	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	04/2010	18(O)	0/0
430	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]	03/2005	168.00	168.00	305.42	12/2008	04/2010	16(O)	0/0
431	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	169.40	08/2009	04/2010	8(O)	0/0
432	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	177.40	08/2009	04/2010	8(O)	0/0
433	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	232.50	08/2009	04/2010	8(O)	0/0
434	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	149.80	08/2009	04/2010	8(O)	0/0
435	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	636.10	05/2009	04/2010	11(O)	0/0
436	BANGALORE-NEELAMANGALALA NH-4 - [N24000104]	03/2005	445.00	445.00	772.29	07/2010	04/2010	-3(O)	0/0
437	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	154.37	08/2004	05/2010	69(O)	0/0
438	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	204.68	01/2009	05/2010	16(O)	0/0
439	GONDE-VADAPPE (THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	677.94	04/2009	05/2010	13(O)	0/0
440	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	222.58	05/2010	05/2010	0(O)	0/0
441	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	71.35	08/2004	06/2010	70(O)	0/0
442	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	450.31	03/2005	06/2010	63(O)	0/0
443	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	405.24	03/2005	06/2010	63(O)	0/0
444	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	241.10	07/2004	06/2010	71(O)	0/0
445	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	782.86	11/2007	06/2010	31(O)	0/0
446	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00	144.00	125.73	07/2005	06/2010	59(O)	0/0
447	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	423.50	11/2007	06/2010	31(O)	0/0
448	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	148.72	08/2005	06/2010	58(O)	0/0
449	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	560.71	03/2009	06/2010	15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
450	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	838.94	11/2010	06/2010	-5(O)	0/0
451	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	356.54	06/2008	06/2010	24(O)	0/0
452	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	386.96	06/2008	06/2010	24(O)	0/0
453	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	207.07	10/2008	06/2010	20(O)	0/0
454	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	55.20	07/2008	06/2010	23(O)	0/0
455	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	413.08	06/2008	06/2010	24(O)	0/0
456	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	06/2010	15(O)	0/0
457	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.44	06/2008	06/2010	24(O)	0/0
458	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	167.23	11/2008	06/2010	19(O)	0/0
459	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]	03/2005	280.00	280.00	550.82	06/2009	06/2010	12(O)	0/0
460	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	201.38	02/2004	06/2010	76(O)	0/0
461	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	30.89	04/2009	06/2010	14(O)	0/0
462	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	200.00	09/2009	06/2010	9(O)	0/0
463	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	214.80	09/2008	06/2010	21(O)	0/0
464	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	403.39	06/2010	06/2010	0(O)	0/0
465	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]	12/2003	407.60	407.60	181.76	06/2010	06/2010	0(O)	0/0
466	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	164.02	06/2010	06/2010	0(O)	0/0
467	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	67.03	08/2004	07/2010	71(O)	0/0
468	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	111.60	03/2008	07/2010	28(O)	0/0
469	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	83.56	03/2008	07/2010	28(O)	0/0
470	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	168.08	06/2008	07/2010	25(O)	0/0
471	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.55	07/2010	07/2010	0(O)	0/0
472	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	415.64	07/2010	07/2010	0(O)	0/0
473	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	831.21	07/2010	07/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
474	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	666.80	03/2010	07/2010	4(O)	0/0
475	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	177.44	06/2008	08/2010	26(O)	0/0
476	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	393.08	08/2010	08/2010	0(O)	0/0
477	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52	111.78	0.52	06/2004	09/2010	75(O)	0/0
478	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00	522.00	265.59	03/2005	09/2010	66(O)	0/0
479	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.90	03/2008	09/2010	30(O)	0/0
480	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17	263.17	232.35	09/2009	09/2010	12(O)	0/0
481	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	242.30	09/2009	09/2010	12(O)	0/0
482	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09	276.09	184.60	09/2009	09/2010	12(O)	0/0
483	LUMDING TO DABOKA - [N24000110]	12/2003	130.00	130.00	65.76	08/2010	09/2010	1(O)	0/0
484	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00	424.00	275.60	09/2010	09/2010	0(O)	0/0
485	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	153.92	09/2006	10/2010	49(O)	0/0
486	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	262.59	10/2008	10/2010	24(O)	0/0
487	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	287.70	10/2008	10/2010	24(O)	0/0
488	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	339.95	10/2008	10/2010	24(O)	0/0
489	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	264.37	10/2008	10/2010	24(O)	0/0
490	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	292.12	10/2008	10/2010	24(O)	0/0
491	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	436.32	04/2008	10/2010	30(O)	0/0
492	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	180.02	10/2008	10/2010	24(O)	0/0
493	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93	300.93	231.89	10/2009	10/2010	12(O)	0/0
494	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	418.65	03/2005	12/2010	69(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
495	KUNJWANI-VIJAYPUR(NS-15) (NS & EW-PH-I) KM.80-KM.97.20,NH-1A - [240102193]	04/2000	110.00 -	110.00	142.24	12/2004 -	12/2010	72(O)	0/0
496	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00 -	210.00	617.30	04/2007 -	12/2010	44(O)	0/0
497	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00 -	275.00	277.35	09/2007 -	12/2010	39(O)	0/0
498	JAM-WADNER - [240106209]	12/2003	145.00 -	145.00	77.62	07/2005 -	12/2010	65(O)	0/0
499	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00 -	284.00	290.99	05/2008 -	12/2010	31(O)	0/0
500	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00 -	227.00	218.04	10/2008 -	12/2010	26(O)	0/0
501	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68 -	340.68	236.56	03/2008 -	12/2010	33(O)	0/0
502	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	280.00	122.68	02/2009 -	12/2010	22(O)	0/0
503	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	199.81	28.10	04/2009 -	12/2010	20(O)	0/0
504	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	167.64	39.49	11/2008 -	12/2010	25(O)	0/0
505	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	155.04	28.05	11/2008 -	12/2010	25(O)	0/0
506	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	200.00	61.40	04/2009 -	12/2010	20(O)	0/0
507	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00 -	225.00	165.70	06/2008 -	12/2010	30(O)	0/0
508	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00 -	195.00	88.52	06/2008 -	12/2010	30(O)	0/0
509	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00 -	242.00	297.40	12/2008 -	12/2010	24(O)	0/0
510	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00 -	227.00	269.08	12/2008 -	12/2010	24(O)	0/0
511	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30 -	151.30	109.95	10/2008 -	12/2010	26(O)	0/0
512	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43 -	203.43	108.10	10/2008 -	12/2010	26(O)	0/0
513	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00 -	322.00	254.27	06/2009 -	12/2010	18(O)	0/0
514	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72 -	264.72	166.99	06/2008 -	12/2010	30(O)	0/0
515	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00 -	245.00	227.20	03/2008 -	12/2010	33(O)	0/0
516	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16 -	198.16	86.08	04/2008 -	12/2010	32(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	117.50	06/2008	12/2010	30(O)	0/0
518	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	116.30	04/2008	12/2010	32(O)	0/0
519	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	54.05	05/2008	12/2010	31(O)	0/0
520	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	124.79	06/2008	12/2010	30(O)	0/0
521	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	131.07	06/2008	12/2010	30(O)	0/0
522	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	34.11	09/2007	12/2010	39(O)	0/0
523	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	63.87	04/2010	12/2010	8(O)	0/0
524	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	142.40	10/2008	12/2010	26(O)	0/0
525	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	177.32	02/2010	12/2010	10(O)	0/0
526	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	252.52	12/2009	12/2010	12(O)	0/0
527	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	12/2010	5(O)	0/0
528	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]	03/2005	557.00	557.00	808.79	02/2010	12/2010	10(O)	0/0
529	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	0.41	02/2004	12/2010	82(O)	0/0
530	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	254.40	07/2010	01/2011	6(O)	0/0
531	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	526.99	01/2011	01/2011	0(O)	0/0
532	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00	464.00	207.70	01/2011	01/2011	0(O)	0/0
533	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]	12/2003	348.16	348.16	107.80	09/2007	02/2011	41(O)	0/0
534	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	130.80	09/2007	03/2011	42(O)	0/0
535	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00	239.00	195.53	07/2005	03/2011	68(O)	0/0
536	MUZZAFFARPUR TO MEHSI (LMNHP-12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00	275.00	229.19	07/2005	03/2011	68(O)	0/0
537	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00	240.00	166.62	10/2008	03/2011	29(O)	0/0
538	FORBESGANJ TO SIMRAHI (NH-57)(NHA) - [240106294]	12/2003	332.94	332.94	147.14	09/2008	03/2011	30(O)	0/0
539	LALITPUR TO SAGAR, NH-26 (NHA) - [240106299]	12/2003	198.00	198.00	110.72	11/2008	03/2011	28(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
540	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	437.37	10/2009	03/2011	17(O)	0/0
541	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45	232.45	84.04	09/2010	03/2011	6(O)	0/0
542	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00	549.00	453.26	05/2010	05/2011	12(O)	0/0
543	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00	220.00	133.59	09/2007	06/2011	45(O)	0/0
544	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00	201.66	53.32	09/2008	06/2011	33(O)	0/0
545	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40	117.40	36.41	11/2008	06/2011	31(O)	0/0
546	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHA) - [240106304]	12/2003	251.03	251.03	205.56	10/2008	06/2011	32(O)	0/0
547	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	150.26	10/2008	06/2011	32(O)	0/0
548	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	228.00	03/2010	06/2011	15(O)	0/0
549	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	145.54	04/2004	10/2011	90(O)	0/0
550	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00	230.00	98.69	06/2005	12/2011	78(O)	0/0
551	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHA) - [240106293]	12/2003	237.80	237.80	98.64	06/2008	12/2011	42(O)	0/0
552	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00	340.00	254.36	09/2008	12/2011	39(O)	0/0
553	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	54.47	04/2008	03/2012	47(O)	0/0
554	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00	940.00	0.33	07/2012	07/2012	0(O)	0/0
555	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	8.72	05/2010	08/2012	27(O)	0/0
556	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.53	07/2009	12/2012	41(O)	0/0
557	DEVDHARI-WADNER - [240106208]	12/2003	145.00	145.00	24.71	07/2005	-	-	0/0
558	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]	12/2003	300.00	300.00	-	10/2008	-	-	0/0
Total			43,916.82	44,119.51	37,904.15				0/0
Shipping & Ports									
559	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00	100.00	0.50	01/2010	01/2010	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
560	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [N250100112]	01/2002	165.00	165.00	78.35	12/2005	03/2010	51(O)	0/0
561	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N250000013]	12/2006	411.32	411.32	406.28	03/2010	03/2010	0(O)	0/0
562	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N250000015]	03/2007	245.67	298.17	290.07	04/2009	03/2010	11(O)	0/0
563	DEEPENING OF CHEENEL AT PARADIP PORT - [N250000004]	12/2005	154.84	253.36	181.71	06/2007 01/2009	06/2010	17(R1)	0/0
564	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N250000029]	10/2006	1,658.59	1,658.59	318.24	07/2010	07/2010	0(O)	0/0
565	DEV. & ORPATION OF AN INTERNATIONAL CONTAINER TRA - [N250000046]	11/2004	2,118.00	2,118.00	-	11/2004	08/2010	69(O)	0/0
566	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40	2,427.40	814.48	10/2008	11/2010	25(O)	0/0
567	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N250000030]	08/2007	586.58	586.58	241.64	11/2010	11/2010	0(O)	0/0
568	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N250000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0(O)	0/0
569	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N250000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0(O)	0/0
570	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N250000037]	04/2005	882.00	1,140.00	0.16	02/2011	02/2011	0(O)	0/0
571	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N250000039]	12/2005	702.00	755.50	0.73	03/2011	03/2011	0(O)	0/0
572	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N250000014]	10/2007	359.44	359.44	211.21	04/2011	04/2011	0(O)	0/0
573	Acquisition of two nos. of 120 B.P - [N250000042]	04/2009	2,908.48	2,908.48	58.18	03/2011	06/2011	3(O)	0/0
574	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N250000032]	08/2008	1,108.12	1,168.42	374.36	04/2011	12/2011	8(O)	0/0
575	Acquisition of Two nos. of 3060 DWT - [N250000043]	04/2009	2,770.32	2,770.42	554.06	09/2011	12/2011	3(O)	0/0
576	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N250000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	-2(O)	0/0
577	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N250000048]	03/2009	3,500.00	3,500.00	-	01/2012	01/2012	0(O)	0/0
578	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N250000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	-1(O)	0/0
579	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N250000003]	10/2005	800.00	800.00	4.63	10/2008	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
580	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00 -	309.00	23.26	09/2005 -	-	-	0/0
581	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]	03/2008	375.00 -	375.00	-	01/2009 -	-	-	0/0
	Total		24,147.63 -	24,730.99	4,002.18				0/0
Telecommunications									
582	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00 -	425.51	68.50	12/2005 -	10/2009	46(O)	0/0
583	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52 -	364.52	51.44	12/2006 -	10/2009	34(O)	0/0
584	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19 -	239.19	104.48	04/2008 -	12/2009	20(O)	0/0
585	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50 -	208.50	146.38	09/2008 -	12/2009	15(O)	0/0
586	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49 -	601.49	422.85	12/2008 -	12/2009	12(O)	0/0
587	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48 -	192.48	113.34	03/2009 -	12/2009	9(O)	0/0
588	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21 -	483.54	470.24	12/2008 -	12/2009	12(O)	0/0
589	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34 -	277.34	180.93	03/2009 -	12/2009	9(O)	0/0
590	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00 -	366.00	-	09/2009 -	12/2009	3(O)	0/0
591	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94 -	373.94	169.33	12/2008 -	01/2010	13(O)	0/0
592	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	0.00 -	278.16	175.77	12/2008 12/2009	01/2010	1(R3)	0/0
593	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91 -	335.91	110.83	03/2009 -	01/2010	10(O)	0/0
594	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15 -	149.15	40.87	06/2009 -	01/2010	7(O)	0/0
595	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81 -	336.81	64.50	01/2009 -	01/2010	12(O)	0/0
596	NATIONAL RADIO SPECTRUM MANAGEMENTand MONIT. SY. I - [260100051]	08/2000	279.97 -	172.04	136.24	12/2004 -	02/2010	62(O)	0/0
597	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00 -	247.00	119.50	02/2007 12/2009	03/2010	3(R3)	0/0
598	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38 -	168.30	94.13	10/2007 12/2009	03/2010	3(R3)	0/0
599	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25 -	133.75	34.05	06/2008 02/2010	03/2010	1(R3)	0/0
600	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61 -	463.61	104.60	12/2009 12/2009	03/2010	3(R3)	0/0
601	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86 -	353.00	161.35	02/2008 -	05/2010	27(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
602	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	73.54	09/2009	06/2010	9(O)	0/0
603	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	10(O)	0/0
604	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	25.97	12/2009	06/2010	6(O)	0/0
605	Execution of telecom network requirement of defence - [N26000065]	05/2006	1,077.00	1,077.00	841.00	03/2009	09/2010	18(O)	0/0
606	Implementation of FTTH, the state of the art access .gpon eq - [N26000072]	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
607	Implementation of FTTH, the state of the art Acces - [N26000073]	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
608	Procurement of DXC equipment - [N26000074]	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
609	Procurement of 24 F OF cable. - [N26000075]	02/2008	199.00	136.00	-	03/2010	11/2010	8(O)	0/0
610	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007	12/2010	13(R3)	0/0
611	Procurement of 2.5G DWDM equipment - [N26000066]	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
612	Procurement of 10G (40 chl) DWDM equipment - [N26000067]	08/2006	590.10	590.10	-	03/2009	12/2010	21(O)	0/0
613	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
614	Procurement of STM-1 SDH equipment - [N26000069]	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
615	Procurement of STM-16 ADM equipment - [N26000070]	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
616	Procurement of STM-16 ADM equipment - [N26000071]	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
617	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
618	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
619	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
620	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]	11/2008	350.00	350.00	-	-	-	-	0/0
621	CENTRALISED TRANSMISSION NMS - [N26000064]	08/2009	300.00	300.00	-	-	-	-	0/0
	Total		16,794.98	16,628.81	4,546.76				0/0
Urban Development									
622	C/O of Jawahar Lal Nehru Bhawan at Janpath, New Del - [N28000029]	09/2005	143.95	143.95	96.76	-	01/2010	-	0/0
623	Upgradation of govt medical colg jammu & C/O supers - [N28000042]	05/2007	100.00	101.00	28.76	04/2009	01/2010	9(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
624	C/o office building for IDBI at bandra Kurla Compl - [N28000048]	11/2006	114.18 173.08	114.18	60.09	04/2009 -	02/2010	10(O)	0/0
625	C/O Bldg for Cabinet Sectt at pocket-5A,Lodhi Road - [N28000030]	02/2004	146.18 -	146.18	79.12	- -	11/2009	-	0/0
626	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67 -	135.03	-	02/2010 -	02/2010	0(O)	0/0
627	C/o Institute of traumatology for GMC Srinagar und - [N28000043]	06/2007	100.00 -	101.00	8.47	10/2009 -	06/2010	8(O)	0/0
628	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00 8,605.36	8,676.00	13,719.69	06/2010 -	11/2010	5(O)	0/7
629	Development of Minto Road Area, New Delhi, C/O 140 t - [N28000027]	08/2008	135.53 -	135.53	12.19	12/2010 -	04/2011	4(O)	0/0
630	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 8,158.00	6,395.00	2,267.57	12/2011 09/2012	06/2012	-3(R3)	0/1
Total			15,336.51 -	15,947.87	16,272.65				0/8
<u>Water Resources</u>									
631	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
Total			542.90 -	1,187.00	35.49				0/0
Grand Total			570,113.10	651,207.44	273,582.18				625/1754
