

**317th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
March, 2012**



UCIL



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -7
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	8-14
List of Delete Projects	15
Summary of Projects	16-31
Sector wise Trend and Graphicalf Analysis	32-45
Sector wise analysis of projects	46-76
Graph	77-89
Statewise Summary of All Ongoing Projects	91
List of Abbreviations	154-155

EXECUTIVE SUMMARY

The Flash Report for March, 2012 contains information on the status of the 554 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During, March, 2012, 13 projects (1 project each of Shipping & Ports, Telecommunication and Road Transport & Highways, 2 projects of Power and 8 projects of Petroleum Sectors) have reported completion.

During the reference month, 75 projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 60 months, in respect of projects relating to Road Transport and Highways, Fertilizer, Power, Petroleum, Coal, Shipping & Ports, Steel, Civil Aviation and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	131	0
2.	ROAD TRANSPORT & HIGHWAYS	133	24
3.	POWER	101	17
4.	PETROLEUM	61	14
5.	COAL	50	3
6.	TELECOMMUNICATION	16	6
7.	SHIPPING & PORTS	24	1
8.	STEEL	16	7
9.	FERTILISERS	6	2
10.	CIVIL AVIATION	5	1
11.	ATOMIC ENERGY	5	0
12.	URBAN DEVELOPMENT	4	0
13.	WATER RESOURCES	1	0
14.	PETROCHEMICALS	1	0
Total		554	75

3. The total original cost of implementation of the 554 projects was about ₹ 7, 24,460.43 Crores and their anticipated completion cost is likely to be ₹ 8, 44,195.74 Crores, which reflects an overall cost overrun of ₹1, 19,735.31 Crores (16.5 % of original cost). The expenditure incurred on these projects till March, 2012 is ₹ 3, 77,551.83 Crores, which is 44.7 % of the anticipated cost of the projects.

4. Out of the 554 projects, 4 projects are ahead of schedule, 184 are on schedule, 264 projects are delayed, and 78 projects have been sanctioned without any commissioning schedule/date. Further, in case of 24 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. Out of 264 delayed projects, 76 projects had overall delay in the range of 1 to 12 months, 47 projects had a delay in the range of 13 to 24 months, 106 projects had a delay in the range of 25 to 60 months and 35 projects had a delay of 61 months and above.

5. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

6. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, delay in land acquisitions, law and order problems, revision of scope of work, delay in supply of equipment, ROW problem, inadequate deployment of man power, delay in testing and stabilization of electrical and automation system, delay in handing over the sites, delay in equipment erection and civil works and forest and environment clearances, etc

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

8. The Sector-wise details of additional delays are as under:-

i) In the **Shipping and Ports sector**, the project 'Acquisition of 2 Nos. of 120 BP by 077 & 078, SCI' has reported additional delay of 4 months, for which no reason has been reported by the project authority.

ii) In the **Telecommunications sector**, 6 projects have reported additional delay in the range of 1-6 months. The project 'Project-III of NIB-II of Messaging Storage, BSNL' has reported an additional delay of 1 month due to delay in supply of equipment, "GSM Equipment of 390K lines (2G) and 130K Lines (3G), BSNL' has reported additional delay of 3 months due to delay in permission by the Municipality, 'Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL', 'GSM Equipment of 799K lines (2G) and 101k Lines (3G),BSNL' Jharkhand and 'GSM Equipment of 1867K lines (2G) and 383K Lines (3G), BSNL' Gujarat have reported additional delay of 3 months each due to delay in permission to lay optical fiber cable from local bodies. 'Uttaranchal Telecom Circle Phase-VI (2G & 3G), BSNL' has reported additional delay of 6 months due to Municipal permission issue.

iii) In the **Petroleum Sector**, 14 projects have reported additional delays in the range of 1-12 months. 4 projects have reported additional delay of one month each. The project 'Construction of New Process Complex MHN, ONGC' has reported additional delay of 2 months due to delay in award of works, 'Offshore Grid Interconnectivity project in Mumbai High, ONGC' has reported additional delay of 2 months due to serious financial constraint, 'VKPL Upgradation and Laying of Spurline, GAIL' has reported additional delays of 3 months due to delay in opening of ROU in some positions, 'Construction of Tanks and Blending Facility at Vad, IOCL' has reported additional delay of 3 months due to poor performance of earlier contractors, 'CDU/VDU-II, CPCL' has reported additional delay of 4 months due to delay in delivery of critical equipment, 'MRPL Phase-III Expansion, Mangalore Refinery' has reported additional delay of 4 months due to delay in land acquisition, 'Construction of 23 immediate Supply vessels(ISV), ONGC' has reported additional delay of 5 months due to delay in contractual completion date, 'Additional Development of D-1 Field, ONGC' has reported additional delay of 6 months due to slow fabrication and installation work by contractors, 'Construction of one Multi-Purpose Support Vessel, ONGC' has reported additional delay of 8 months due to

revision of scope of work and 'Assam Renewal Project for Group-A, ONGC' has reported additional delay of 12 months due to delay in laying of pipelines, Court cases and ROU issues, etc.

iv) In the **Power Sector**, 17 projects have reported additional delays in the range of 1-13 months. One project has reported additional delay of one month, two projects have reported additional delay of two months each and three projects have reported additional delay of three months each. 'Interconnection Between Electrical Grids Of India and B, PGCIL' has reported additional delay 5 months as land for Baharampur Sights yet to be acquired, 'Uri HEP, Stage-II, NHPC' has reported additional delay of 6 months due to local unrest, 'Western Region System Strengthening Scheme-II, PGCIL' and 'Transmission System Associated with Chamara III HEP, PGCIL' have reported additional delay of 6 months each due to delay in forest clearance, 'Transmission System Associated with Rampur HEP, PGCIL' has reported additional delay 6 months due to delay in generation project, 'Bongaigaon Thermal Power Project, NTPC' has reported additional delay of 7 months due to delay in TG erection start, 'Supplementary Transmission Associated with DVC, PGCIL' and '765 KV Pooling Station and Network with DVC and MA, PGCIL' have reported additional delay of 7 months each due to delay in forest clearance, 'Transmission System of Vindhyachal-IV and Rihand-I, PGCIL' has reported additional delay of 7 months due to delay in land acquisition, 'Transmission System Associated with Mundra Ultra Mega Power Project, PGCIL' and 'Eastern Region Transmission System-III, PGCIL' have reported additional of 13 months each due to ROW problem and delay in land acquisition respectively.

v) In **Steel sector**, 7 projects have reported additional delays in the range of 2-9 months. '67.5 MW TG-5 System Emergency Power Requirement, RINL' and '330 TPH Boiler-6, and Auxiliary System, RINL' have reported additional delay of two months each and Bailadila Iron Ore Deposit –IIB, NDMC ' has reported additional delay of 7 months. However, no specific reasons have been reported by the project authorities for delay in these projects. 'Expansion Bhilai Steel Plant, SAIL' and 'Expansion of Durgapur Steel Plant, SAIL' have reported additional delays of 3 months each due to inadequate deployment of man power and increase in scope of work respectively. 'Expansion of Bokaro Steel Plant, SAIL' has reported an additional delay of 7 months due to delay in testing and stabilization

of electrical and automation system and 'Expansion of IISCO Steel Plant' has reported an additional delay of 9 months due to difficult and unforeseen soil conditions.

vi) In the **Road Transport and Highways Sector**, 24 projects of NHAI have reported additional delays in the range of 1-9 months. Four projects have reported additional delays of one month each, three projects have reported additional delay of two months each and eleven projects have reported additional delay of three months each. The project Chambal Bridge, NH-76 (RJ-5), NHAI' has reported additional delay of 5 months, 'Deewapur To UP/Bihar Border (LMNHP-9)-NH-28, KM.402-360.915, NHAI', 'Gwalior Bypass, NH-75.3 , NHAI' have reported additional delay of 6 months each, 'Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1), NHAI' has reported additional delay of 8 months, 'Forbesganj To Simrahi (NH-57), NHAI' and 'Indore-Dewas (NH-3), NHAI' have reported an additional delay of 9 months each. The project agency has not mentioned any specific reason for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

vii) In the **Fertilizer Sector**, 02 projects of NFL have reported additional delay in the range of 1-3 months. 'Capacity Enhancement of Vijaipur-I Plants, NFL' and 'Capacity Enhancement of Ammonia and Urea Plant VIJ, NFL' have reported additional delay of 1 and 3 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

viii) In the **Civil Aviation Sector**, the project 'C/O New Airport at Pakyong (Sikkim) Airport, AAI' has reported additional delay of 4 months due to handing over the site and hindrance due to tree, power lines and water pipelines.

ix) In the **Coal Sector**, 3 projects have been reported additional delays in the range of 8-60 months. The project 'TPS-II Expansion (1470 MW to 1970 MW), NLC' has reported additional delay of 8 months due to inadequate mobilization by the contractor and delay in equipment erection, 'Tuticorin Thermal Power Project, NLC' has reported additional delay

of 13 months due to delay in equipment erection and civil works and 'Balram OCP Extension, MCL (8.00 MTY), MLC' has reported additional delay of 60 months due to delay in handing over the R&R site by State Govt. and law and order problem .

9. The status as on 01.04.2012 in respect of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.



(Pankaj Jain)
Special Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	133	24
2	Railways	131	0
3	Power	101	17
4	Petroleum	61	14
5	Coal	50	3
6	Shipping & Ports	24	1
7	Steel	16	7
8	Telecommunications	16	6
9	Fertilisers	6	2
10	Atomic Energy	5	0
11	Civil Aviation	5	1
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	554	75

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	253.60
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	510.00
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	2,445.11
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	573.12
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING crp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC AND MAITHON RB(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00

July,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
August,2011				
<u>Power</u>				
30	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
31	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
32	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
33	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
34	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
35	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

September,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Petroleum</u>				
36	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
37	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
38	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
39	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26
October,2011				
<u>Power</u>				
40	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000043]	204.07	06/2011	129.60
November,2011				
41	WESTERN REGION STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000050]	230.89	01/2011	98.20
<u>Road Transport & Highways</u>				
42	RINGBUNDS TO JHAJHANPUR (BR-6)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000030]	340.00	06/2008	570.00
43	THRISSUR TO ANGAMALI (NH-47)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000037]	312.50	03/2009	604.40
December,2011				
<u>Mines</u>				
44	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE(NATIONAL ALUMINUM COMPANY LIMITED (NALCO)) - [100100054]	4,091.51	12/2008	4,183.00
<u>Petroleum</u>				
45	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000024]	2,305.30	06/2010	1,266.47
46	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II)(GAS AUTHORITY OF INDIA LIMITED) - [N16000052]	4,429.38	10/2010	2,325.60
<u>Power</u>				
47	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000023]	238.25	05/2011	220.82

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
48	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106246]	227.00	10/2008	403.60
49	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106276]	629.00	11/2010	910.00
50	LALITPUR TO SAGAR, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106299]	198.00	11/2008	187.30
51	JHANSI TO LALITPUR, NH-26(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000097]	276.09	09/2009	295.40
52	PONDICHERY - TINDIVANAU NH-66(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000100]	285.00	07/2010	359.40
<u>Shipping & Ports</u>				
53	Construction of captive jetty for handling coal, N(PORT TRUST) - [N25000038]	230.00	12/2010	219.00
<u>Telecommunications</u>				
54	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000039]	601.49	12/2008	496.20
55	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1(BHARAT SANCHAR NIGAM LIMITED) - [N26000040]	192.48	03/2009	119.45
56	Procurement of 2.5G DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000066]	424.00	03/2009	.00
57	Procurement of 10G (40 chl) DWDM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000067]	590.10	03/2009	.00
58	Procurement of 10G 40 CHL (12 chl equipped) DWDM(BHARAT SANCHAR NIGAM LIMITED) - [N26000068]	545.50	03/2010	.00
59	Procurement of STM-1 SDH equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000069]	154.03	03/2010	.00
60	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000070]	355.92	03/2010	.00
61	Procurement of STM-16 ADM equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000071]	477.00	03/2010	.00
62	Procurement of DXC equipment(BHARAT SANCHAR NIGAM LIMITED) - [N26000074]	229.00	03/2010	.00
63	GSM equipment of 900000Lines (2G) PunjabPhase V.2(BHARAT SANCHAR NIGAM LIMITED) - [N26000081]	241.49	09/2009	123.76
64	GSM equipment of 975000Lines (2G) 325000 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000083]	625.53	02/2010	.00
65	GSM equipment of 1100000Lines (2G) UP East Phase(BHARAT SANCHAR NIGAM LIMITED) - [N26000084]	624.75	09/2010	.00
66	GSM equipment of 375000Lines (2G) 75000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000085]	170.23	06/2009	.00
67	GSM equipment of 849862Lines (2G) 150138 lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000087]	584.33	02/2009	403.71
68	GSM equipment of 1900000Lines (2G) 401700 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000091]	760.20	-	819.57
69	GSM equipment of 1700000Lines (2G) 234100 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000092]	677.75	10/2009	461.56

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
January,2012				
<u>Railways</u>				
70	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)(WESTERN RAILWAY) - [220100322]	148.61	03/2008	260.07
<u>Road Transport & Highways</u>				
71	KASIA TO GORAKHPUR (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106291]	242.00	12/2008	434.10
72	SITAPUR-LUCKNOW(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000036]	322.00	06/2009	553.70
73	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000090]	418.04	03/2010	343.30
74	TRICHY - DINDIGUL NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000099]	576.00	07/2010	661.40
<u>Telecommunications</u>				
75	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3(BHARAT SANCHAR NIGAM LIMITED) - [N26000043]	1,799.94	09/2009	309.79
76	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN(BHARAT SANCHAR NIGAM LIMITED) - [N26000050]	335.91	03/2009	182.45
77	GSM equipment of 945000Lines (2G) 225000lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000086]	366.00	10/2008	227.39
78	GSM equipment of 1900000Lines (2G) 335500lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000094]	848.70	01/2010	712.86
February,2012				
<u>Coal</u>				
79	BARSINGSAR TPS (2 125MW) (NLC)(NEYVELI LIGNITE CORPORATION) - [060100089]	1,114.18	06/2009	1,714.72
<u>Power</u>				
80	EASTERN REGION STRENGTHENING SCHEME-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000033]	227.52	06/2010	140.70
81	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000062]	353.57	07/2010	221.20
<u>Road Transport & Highways</u>				
82	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106216]	412.78	11/2007	437.80
March,2012				
<u>Petroleum</u>				
83	MNW-NF BRIDGE PROJECT(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000045]	175.21	03/2009	172.42

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
84	BAWANA NANGAL PIPE LINE PROJECT(GAS AUTHORITY OF INDIA LIMITED) - [N16000050]	1,816.07	12/2011	1,209.40
85	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA(INDIAN OIL CORPORATION LIMITED) - [N16000059]	250.00	03/2013	233.51
86	HEERA RECONSTRUCTION(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000062]	706.70	04/2010	700.75
87	NEELAM RECONSTRUCTION(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000063]	305.08	04/2011	298.66
88	REFRIGERATED LPG STORAGE AT JNPT(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000083]	304.40	09/2010	271.00
89	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000102]	613.54	12/2010	736.18
90	WIND ENERGY(GAS AUTHORITY OF INDIA LIMITED) - [N16000126]	616.00	-	344.74
<u>Power</u>				
91	SIMHADRI STPP STAGE -II(NATIONAL THERMAL POWER CORPORATION) - [N18000032]	5,103.39	05/2011	4,405.00
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000058]	210.79	08/2011	169.60
<u>Road Transport & Highways</u>				
93	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000117]	295.00	08/2010	763.80
<u>Shipping & Ports</u>				
94	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH(SHIPPING corp. of india) - [250100112]	165.00	12/2005	135.85
<u>Telecommunications</u>				
95	GSM equipment of 1500000Lines (2G) 264700lines 3(G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000093]	922.91	01/2010	434.75

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2011				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97
January,2012				
<u>Power</u>				
2	TUIRIAL HE PROJECT(NEEPCO)(NORTH EAST ELECTRIC POWER CORPORATION) - [N16000049]	368.72	07/2006	295.47
March,2012				
<u>Shipping & Ports</u>				
3	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT(PORT TRUST) - [N16000076]	375.00	01/2009	.00
<u>Telecommunications</u>				
4	FTTH BO-3474 /08-09 in Mumbai(MAHANAGAR TELEPHONE NIGAM LIMITED) - [N18000016]	389.86	09/2011	3.06


Summary of projects in the Flash Report for the month of March, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	570
Number of Projects completed/dropped/frozen in Previous Month	4
Number of Projects completed/dropped/frozen in Current Month	15
Number of Projects Removed From the System	1
Number of Projects Added in Current Month	4
Number of Projects in Current Month	554

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 554 projects, 4 projects are ahead of schedule, 184 projects are on schedule and 264 projects are delayed. Of the balance, 78 projects do not have fixed dates of commissioning while 24 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

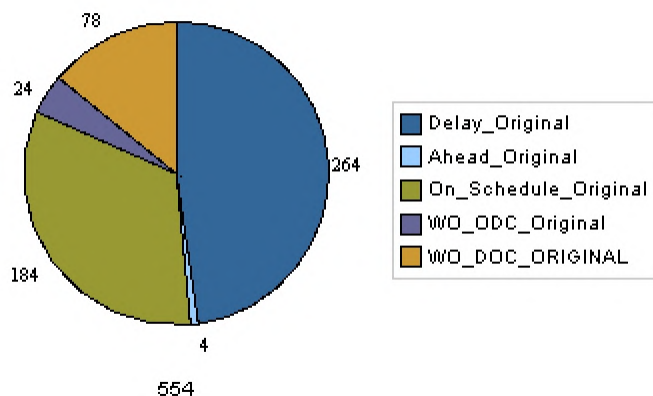

III. Investment Scenario

The Total Original cost of implementation of 554 projects when sanctioned, was of the order of Rs. 724460.43 crore but this was subsequently revised to Rs. 844195.74 crore implying a cost overrun of 16.5%. The expenditure incurred on these projects till March, 2012 is Rs. 377551.83 crore, which is 44.7% of the revised cost of the projects.

Figures are in Rs. Crore

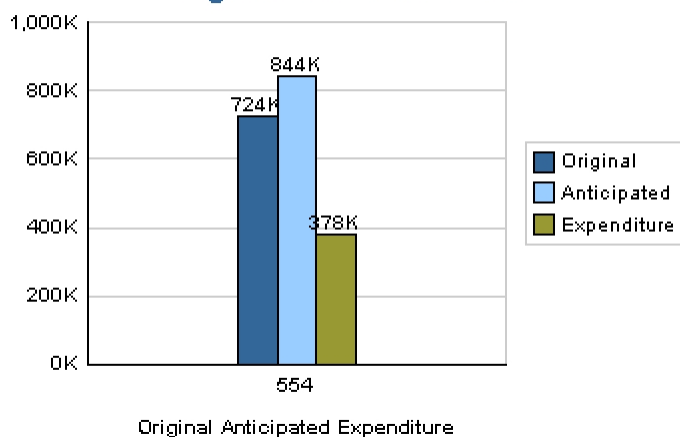

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	570
No of Projects Completed/Dropped/Frozen in Previous Month	4
No of Projects Completed/Dropped/Frozen in Current Month	15
No. of Projects Removed from the System	1
No of Projects added in Current Month	4
No of Projects in Current Month	554

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original (Date)	264	4	184	24	78	554	47.65
Latest Approved (Date)	250	3	240	29	32	554	45.13

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	435	587,712.52	631,307.03	249,786.88	39.60	43,594.51	7.40
Latest Approved (RCE)	119	189,481.63	212,888.71	127,764.95	60.00	23,407.08	12.40
Total (RCE)	554	777,194.15	844,195.74	377,551.83	44.72	67001.59	8.62
Original Cost of All Projects							
Original Cost	554	724,460.43	844,195.74	377,551.83	44.70	119,735.31	16.50

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	264	425,998.01	500,467.69	271,057.14	54.20	74,469.68	17.50
Latest Approved (RCE)	250	373,947.99	418,010.73	225,879.61	54.00	44,062.74	11.80

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	75	131,222.03	139,695.31	85,221.93	61.00	8,473.28	6.50

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	50	33,604.6	37,053.1	10.3	11	12,628.6	16,674.9	32.0
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	65,244.8	71,412.4	9.5	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	61	145,017.8	152,886.9	5.4	15	49,354.4	65,241.1	32.2
8	Power	101	208,284.4	223,398.2	7.3	19	42,231.6	57,345.4	35.8
9	Railways	131	65,286.3	134,791.5	106.5	102	38,348.2	107,900.0	181.4
10	Road Transport & Highways	133	79,244.5	81,045.3	2.3	12	3,597.3	5,967.2	65.9
11	Shipping & Ports	24	18,511.4	19,421.4	4.9	10	6,294.5	7,511.6	19.3
12	Telecommunications	16	7,130.8	7,247.1	1.6	3	1,315.9	1,514.8	15.1
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		554	724,460.4	844,195.7	16.5	186	210,725.5	340,101.6	61.4

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	36	31,031.6	37,863.8	22.0	14	12,420.0	20,119.2	62.0
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	2	6,441.3	11,082.7	72.1
3	Assam	37	23,895.8	35,508.9	48.6	13	11,923.7	23,630.9	98.2
4	Bihar	30	29,665.0	34,323.9	15.7	13	12,338.8	16,997.7	37.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	25	32,377.3	32,630.3	0.8	5	2,413.7	2,875.2	19.1
7	Haryana	10	5,795.4	7,611.8	31.3	3	1,448.2	3,264.7	125.4
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	3	7,629.8	10,324.0	35.3
9	J and K	10	14,019.4	33,312.4	137.6	6	7,866.5	27,186.4	245.6
10	Karnataka	25	30,657.6	38,936.0	27.0	9	8,598.8	17,283.7	101.0
11	Kerala	6	5,711.2	6,502.7	13.9	2	795.7	1,587.2	99.5
12	Madhya pradesh	24	16,759.5	17,053.9	1.8	3	2,027.6	2,741.5	35.2
13	Maharashtra	47	68,515.1	81,772.1	19.3	18	29,685.2	45,706.8	54.0
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	320.2
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	3	1,901.7	4,220.8	121.9	2	988.1	3,307.1	234.7
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	27	54,277.4	57,448.4	5.8	13	33,147.5	36,510.8	10.1
19	Punjab	6	4,384.2	5,314.2	21.2	2	532.4	1,462.5	174.7
20	Rajasthan	13	24,032.2	24,026.8	-0.0	3	570.8	950.0	66.4
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	35	52,241.3	61,099.8	17.0	13	27,364.2	36,222.7	32.4
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	25	18,333.9	22,339.5	21.8	9	3,729.2	7,783.0	108.7
25	West Bengal	26	40,460.8	49,844.4	23.2	12	20,281.1	29,664.7	46.3
26	Delhi	3	37,985.0	37,965.4	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	25	52,927.0	56,158.4	6.1	7	4,746.6	7,977.9	68.1
28	Jharkhandd	22	14,396.5	15,999.9	11.1	6	1,897.3	3,672.5	93.6
29	Uttaranchal	5	9,815.9	11,738.4	19.6	3	3,942.3	5,864.8	48.8
30	Multi State	94	125,156.8	130,167.1	4.0	21	6,635.4	15,682.9	136.4
Total		554	724,460.4	844,195.7	16.5	186	210,725.5	340,101.6	61.4

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	4	38,056.3	40,709.3	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	3	2,587.6	2,970.1	3 - 27
3	Coal	50	33,604.6	37,053.1	10.3	19	13,791.0	15,101.7	12 - 60
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	9 - 12
5	Steel	16	65,244.8	71,412.4	9.5	10	51,098.8	57,157.7	3 - 36
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	61	145,017.8	152,886.9	5.4	38	107,198.2	115,427.4	1 - 120
8	Power	101	208,284.4	223,398.2	7.3	50	137,766.1	152,266.8	1 - 90
9	Railways	131	65,286.3	134,791.5	106.5	34	23,670.8	56,067.8	3 - 204
10	Road Transport & Highways	133	79,244.5	81,045.3	2.3	81	30,305.8	32,466.6	2 - 101
11	Shipping & Ports	24	18,511.4	19,421.4	4.9	12	9,966.9	10,706.2	1 - 93
12	Telecommunications	16	7,130.8	7,247.1	1.6	9	3,855.7	4,035.1	16 - 76
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		554	724,460.4	844,195.7	16.5	264	425,998.0	500,467.7	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	36	31,031.6	37,863.8	22.0	13	17,016.5	21,345.6	2 - 37
2	Arunachal Pr.	4	9,512.2	14,153.6	48.8	3	9,356.2	13,737.9	12 - 63
3	Assam	37	23,895.8	35,508.9	48.6	32	16,023.7	23,735.2	12 - 120
4	Bihar	30	29,665.0	34,323.9	15.7	13	24,010.8	25,796.2	2 - 62
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	3 - 3
6	Gujarat	25	32,377.3	32,630.3	0.8	7	15,308.1	15,331.1	11 - 34
7	Haryana	10	5,795.4	7,611.8	31.3	4	2,065.9	3,555.1	7 - 50
8	Himachal Pr.	6	14,761.2	17,455.4	18.3	6	14,761.2	17,455.4	20 - 58
9	J and K	10	14,019.4	33,312.4	137.6	8	9,873.4	29,166.4	10 - 201
10	Karnataka	25	30,657.6	38,936.0	27.0	6	19,921.5	24,729.0	9 - 94
11	Kerala	6	5,711.2	6,502.7	13.9	4	4,915.5	4,915.5	2 - 27
12	Madhya pradesh	24	16,759.5	17,053.9	1.8	16	13,189.1	12,783.6	5 - 50
13	Maharashtra	47	68,515.1	81,772.1	19.3	21	44,906.6	54,110.1	1 - 52
14	Manipur	1	727.6	3,056.9	320.2	1	727.6	3,056.9	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	3	1,901.7	4,220.8	121.9	1	368.7	913.6	90 - 90
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	27	54,277.4	57,448.4	5.8	9	31,368.6	32,330.9	7 - 120
19	Punjab	6	4,384.2	5,314.2	21.2	3	1,362.9	1,437.9	7 - 51
20	Rajasthan	13	24,032.2	24,026.8	-0.0	5	19,197.2	19,178.9	3 - 47
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	35	52,241.3	61,099.8	17.0	9	24,126.0	28,230.2	16 - 93
23	Tripura	3	1,522.4	2,053.2	34.9	0	0.0	0.0	-
24	Uttar Pradesh	25	18,333.9	22,339.5	21.8	15	12,171.8	14,224.6	5 - 87
25	West Bengal	26	40,460.8	49,844.4	23.2	16	27,444.9	33,577.3	3 - 132
26	Delhi	3	37,985.0	37,965.4	-0.1	1	249.0	229.4	61 - 61
27	Chhatisgarh	25	52,927.0	56,158.4	6.1	7	27,096.1	27,407.4	6 - 41
28	Jharkhandd	22	14,396.5	15,999.9	11.1	10	8,767.6	9,723.8	3 - 102
29	Uttaranchal	5	9,815.9	11,738.4	19.6	5	9,815.9	11,738.4	13 - 83
30	Multi State	94	125,156.8	130,167.1	4.0	47	71,308.2	71,112.3	1 - 204
Total		554	724,460.4	844,195.7	16.5	264	425,998.0	500,467.7	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	46,386.3	11.6	5	41,548.3	46,386.3	3 - 51
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	2,278.1	2,660.6	3 - 17
3	Coal	50	33,604.6	37,053.1	10.3	17	11,692.9	13,423.1	12 - 60
4	Fertilisers	6	5,317.4	5,317.4	0.0	2	763.0	763.0	9 - 12
5	Steel	16	65,244.8	71,412.4	9.5	9	42,406.8	44,866.7	3 - 21
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	61	145,017.8	152,886.9	5.4	30	63,046.6	68,912.5	1 - 74
8	Power	101	208,284.4	223,398.2	7.3	44	120,057.0	131,086.5	1 - 83
9	Railways	131	65,286.3	134,791.5	106.5	35	15,618.0	48,580.4	0 - 213
10	Road Transport & Highways	133	79,244.5	81,045.3	2.3	81	30,305.8	32,466.6	2 - 101
11	Shipping & Ports	24	18,511.4	19,421.4	4.9	11	9,644.7	10,497.4	1 - 93
12	Telecommunications	16	7,130.8	7,247.1	1.6	12	5,392.5	5,571.8	7 - 76
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		554	724,460.4	844,195.7	16.5	250	349,691.4	418,010.7	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	46,386.3	11.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	50	34,238.2	37,053.1	8.2	8	7,464.7	10,279.7	37.7
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Steel	16	71,120.1	71,412.4	0.4	3	598.0	910.3	52.2
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	61	158,163.4	152,886.9	-3.3	2	31,423.4	32,116.1	2.2
8	Power	101	212,168.2	223,398.2	5.3	13	36,652.4	47,882.4	30.6
9	Railways	131	89,833.8	134,791.5	50.0	81	46,674.4	91,913.5	96.9
10	Road Transport & Highways	133	79,411.0	81,045.3	2.1	12	3,597.3	5,967.2	65.9
11	Shipping & Ports	24	19,263.5	19,421.4	0.8	8	5,384.2	5,852.1	8.7
12	Telecommunications	16	7,134.7	7,247.1	1.6	1	250.0	425.5	70.2
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		554	777,194.2	844,195.7	8.6	133	157,587.7	231,968.8	47.2

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,808.00	2,015.00	13- 13
3	Coal	50	33,604.55	37,053.10	10.26	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	2	8,987.89	12,898.17	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	61	145,017.77	152,886.87	5.43	13	18,756.72	32,734.21	6- 120
8	Power	101	208,284.36	223,398.21	7.26	3	2,622.17	4,899.65	24- 90
9	Railways	131	65,286.30	134,791.49	106.46	10	3,776.06	13,099.47	12- 141
10	Road Transport & Highways	133	79,244.48	81,045.31	2.27	0	0.00	0.00	0- 0
11	Shipping & Ports	24	18,511.36	19,421.43	4.92	2	522.70	650.25	8- 22
12	Telecommunications	16	7,130.82	7,247.12	1.63	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		554	724460.43	844195.74	16.53	32	36943.32	67003.15	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	46,386.29	11.64	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	1	1,942.51	2,325.00	17- 17
3	Coal	50	33,604.55	37,053.10	10.26	5	7,667.52	9,576.02	19- 45
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Steel	16	65,244.82	71,412.36	9.45	5	23,920.89	29,999.75	10- 36
6	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
7	Petroleum	61	145,017.77	152,886.87	5.43	12	46,873.51	61,425.00	6- 120
8	Power	101	208,284.36	223,398.21	7.26	16	40,592.86	55,093.55	7- 90
9	Railways	131	65,286.30	134,791.49	106.46	25	11,673.45	44,075.40	3- 204
10	Road Transport & Highways	133	79,244.48	81,045.31	2.27	12	3,597.28	5,967.20	7- 99
11	Shipping & Ports	24	18,511.36	19,421.43	4.92	6	4,314.81	5,262.56	1- 93
12	Telecommunications	16	7,130.82	7,247.12	1.63	3	1,315.85	1,514.83	16- 76
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		554	724460.43	844195.74	16.53	87	148836.58	228035.31	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>							
1	NEELAM RECONSTRUCTION	05/2008	305.08	04/2011	305.08	03/2012	298.66
2	BAWANA NANGAL PIPE LINE PROJECT	11/2007	1,816.07	12/2011	1,385.00	03/2012	1,209.40
3	MNW-NF BRIDGE PROJECT	05/2008	175.21	03/2009	175.21	02/2012	172.42
4	HEERA RECONSTRUCTION	05/2008	706.70	04/2010	706.70	03/2012	700.75
5	WIND ENERGY	05/2011	616.00	N.A.	616.00	03/2012	344.74
6	REFRIGERATED LPG STORAGE AT JNPT	06/2008	304.40	09/2010	304.40	01/2012	271.00
7	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA	02/2009	250.00	03/2013	250.00	03/2012	233.51
8	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli	06/2009	613.54	12/2010	727.88	06/2011	736.18
<u>Power</u>							
9	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII	02/2009	210.79	08/2011	210.79	01/2012	169.60
10	SIMHADRI STPP STAGE -II	08/2007	5,103.39	05/2011	5,038.83	03/2012	4,405.00
<u>Road Transport & Highways</u>							
11	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH)	02/2008	295.00	08/2010	295.00	03/2012	763.80
<u>Shipping & Ports</u>							
12	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH	01/2002	165.00	12/2005	165.00	10/2011	135.85
13	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT	03/2008	375.00	01/2009	272.50	05/2013	.00
<u>Telecommunications</u>							
14	FTTH BO-3474 /08-09 in Mumbai	04/2010	389.86	09/2011	389.86	09/2011	3.06
15	GSM equipment of 1500000Lines (2G) 264700lines 3(G	01/2009	922.91	01/2010	922.91	03/2012	434.75

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	<u>Power</u>					
1	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER	3/2012	198.63	9/2014	198.63	9/2014
2	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS	3/2012	213.78	3/2014	213.78	3/2014
3	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	3/2012	9,569.76	6/2015	9,569.76	6/2015
4	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA	3/2012	206.44	6/2014	206.44	6/2014

VII. Milestones (Cumulative due & achieved)

Total	2457
Achieved up to month	1109

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Civil Aviation</u>						
1	C/o new Airport at Pakyong(Sikkim) Airport AAI	309.46	309.46	01/2011	12/2012	04/2013	4
	<u>Coal</u>						
2	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,027.00	06/2009	07/2012	03/2013	8
3	TUTICORIN THERMAL POWER PROJECT NLC	4,904.54	4,909.54	03/2012	02/2013	03/2014	13
4	BALRAM OCP EXTENSION,MCL (8.00 Mty) MCL	172.08	172.08	03/2010	03/2010	03/2015	60
	<u>Fertilisers</u>						
5	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS NFL	325.00	325.00	07/2011	03/2012	04/2012	1
6	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ NFL	438.00	438.00	07/2011	04/2012	07/2012	3
	<u>Steel</u>						
7	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	04/2012	06/2012	2
8	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	03/2012	05/2012	2
9	EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	06/2013	09/2013	3
10	EXPANSION OF DURGAPUR STEEL PLANT SAIL	2,875.00	2,875.00	12/2012	12/2012	03/2013	3
11	Bailadila Iron Ore Deposit- IIB(NMDC) NMDC	295.89	607.17	12/2011	03/2012	10/2012	7
12	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	03/2012	10/2012	7
13	EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	03/2012	12/2012	9
	<u>Petroleum</u>						
14	INTEGRATED DEV OF G1 and GS-15 (ONGCL) ONGC	429.82	2,218.01	04/2006	05/2012	06/2012	1
15	KOCHI-KOOTANAD BANGALORE- MANGALORE PIPELINE PROJEC GAIL	348.00	261.00	03/2012	04/2012	05/2012	1
16	Development of Cluster-7 Fields ONGC	3,241.03	3,241.03	03/2013	03/2013	04/2013	1
17	Development of BHE and BH-35 Area. ONGC	372.11	372.11	03/2013	03/2013	04/2013	1
18	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	05/2012	07/2012	2
19	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	03/2013	05/2013	2
20	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	330.47	03/2012	03/2012	06/2012	3

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
21	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD IOCL	267.00	267.00	09/2012	06/2012	09/2012	3
22	CDU/VDU-II CPCL	333.99	333.99	N.A.	05/2012	09/2012	4
23	MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	06/2012	10/2012	4
24	Construction of 23 Immediate Supply Vessels (ISV) ONGC	331.20	269.10	08/2013	08/2013	01/2014	5
25	ADDITIONAL DEV. OF D-1 FIELD ONGC	2,163.64	2,163.64	06/2012	06/2012	12/2012	6
26	Construction of one Multipurpose Support Vessel ONGC	723.64	723.64	03/2013	03/2013	11/2013	8
27	ASSAM RENEWAL PROJECT FOR GROUP A ONGC	2,465.15	2,378.86	03/2013	03/2013	03/2014	12
Power							
28	SIPAT STPP STAGE - I (NTPC) NTPC	8,323.39	8,323.39	12/2009	03/2012	04/2012	1
29	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	03/2012	05/2012	2
30	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION PGCIL	196.10	196.10	07/2011	03/2012	05/2012	2
31	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	557.24	01/2010	09/2012	12/2012	3
32	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI PGCIL	409.50	409.50	02/2012	03/2012	06/2012	3
33	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS PGCIL	215.86	215.86	06/2012	03/2012	06/2012	3
34	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B PGCIL	160.32	160.32	10/2012	10/2012	03/2013	5
35	URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	1,794.00	11/2009	08/2012	02/2013	6
36	WESTERN REGION STRENGTHENING SCHEME-II PGCIL	5,221.23	5,221.23	07/2010	06/2012	12/2012	6
37	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP PGCIL	184.19	184.19	11/2011	03/2013	09/2013	6
38	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.91	07/2011	06/2012	12/2012	6
39	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	06/2011	04/2014	11/2014	7
40	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND PGCIL	2,360.95	2,360.95	08/2012	08/2012	03/2013	7
41	765 KV POOLING STATION AND NETWORK WITH DVC AND MA PGCIL	7,075.33	7,075.33	08/2012	08/2012	03/2013	7
42	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I PGCIL	4,672.99	4,672.99	11/2012	11/2012	06/2013	7
43	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	10/2012	11/2013	13
44	EASTERN REGION TRANSMISSION SYSTEM-III PGCIL	1,272.80	1,272.80	11/2012	11/2012	12/2013	13
Road Transport & Highways							
45	HALDIA PORT (PORT CONNECTIVITY) (NH-41) NHAI	273.00	522.00	03/2005	03/2012	04/2012	1


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
46	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) NHAI	227.00	227.00	12/2008	03/2012	04/2012	1
47	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	05/2012	06/2012	1
48	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI NHAI	441.00	441.00	N.A.	03/2012	04/2012	1
49	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 NHAI	193.09	166.30	03/2008	03/2012	05/2012	2
50	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	03/2012	05/2012	2
51	2-LANNING WITH PS KHAGARIA-PURNEA NHAI	664.00	664.00	02/2014	02/2014	04/2014	2
52	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	03/2012	06/2012	3
53	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	03/2012	06/2012	3
54	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 NHAI	240.00	240.00	10/2008	03/2012	06/2012	3
55	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	03/2012	06/2012	3
56	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	03/2012	06/2012	3
57	DAKOPA TO NAGAON (NH-36)(NHAI) NHAI	225.00	225.00	06/2008	03/2012	06/2012	3
58	JHAJHARPUR TO DARBANGA (BR-7) NHAI	340.00	340.00	09/2008	03/2012	06/2012	3
59	NEW MANGALORE PORT NH-17 AND 48 NHAI	196.50	196.50	06/2011	03/2012	06/2012	3
60	ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	03/2012	06/2012	3
61	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER NHAI	464.00	464.00	01/2011	03/2012	06/2012	3
62	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	03/2012	06/2012	3
63	CHAMBAL BRIDGE, NH-76 (RJ-5) NHAI	275.00	281.31	02/2010	07/2013	12/2013	5
64	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 NHAI	300.00	300.00	10/2008	06/2012	12/2012	6
65	GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	06/2012	12/2012	6
66	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) NHAI	572.30	572.30	10/2011	10/2012	06/2013	8
67	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	03/2012	12/2012	9
68	INDORE-DEWAS(NH-3) NHAI	325.00	325.00	05/2013	05/2013	02/2014	9
Shipping & Ports							
69	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH SHIPP.	241.50	241.50	09/2011	12/2011	04/2012	4
Telecommunications							
70	PROJ.III OF NIB-II OF MESSAGING STORAGE BSNL	250.00	425.51	12/2005	03/2012	04/2012	1


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
71	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) BSNL	373.94	373.94	12/2008	03/2012	06/2012	3
72	Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	03/2012	06/2012	3
73	GSM equipment of 799000Lines (2G) 101000 lines 3(G BSNL	328.13	328.12	03/2009	03/2012	06/2012	3
74	GSM equipment of 1867000Lines (2G) 383000 lines 3(BSNL	868.00	868.00	08/2009	03/2012	06/2012	3
75	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) BSNL	149.15	158.72	06/2009	12/2011	06/2012	6

Trend and Graphical Analysis of All Projects

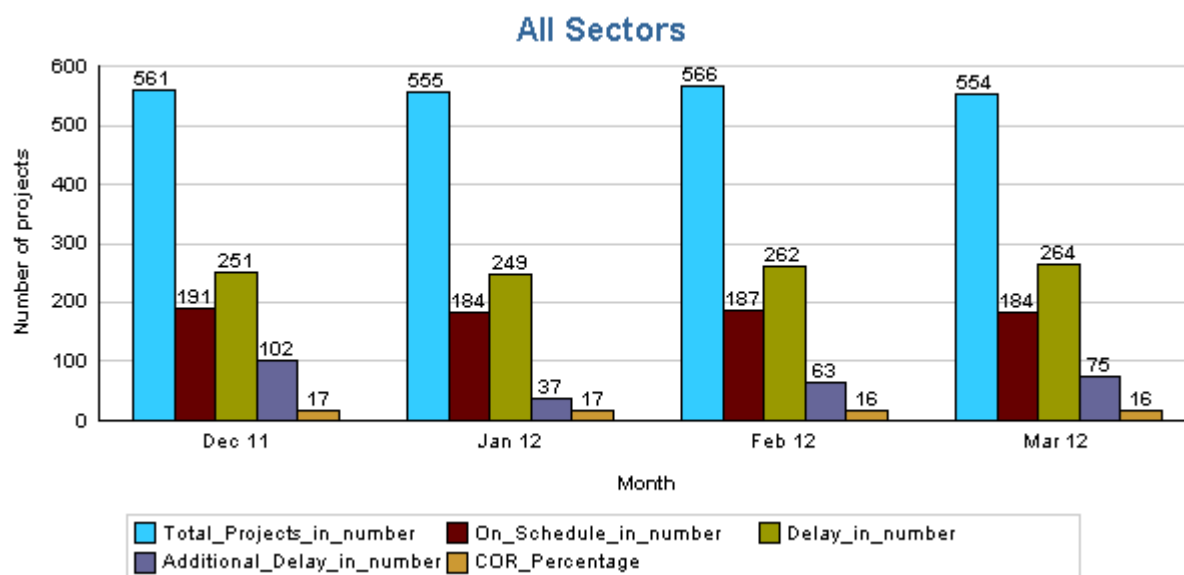


All Sectors Break-up of 264 Delayed projects in March 2012

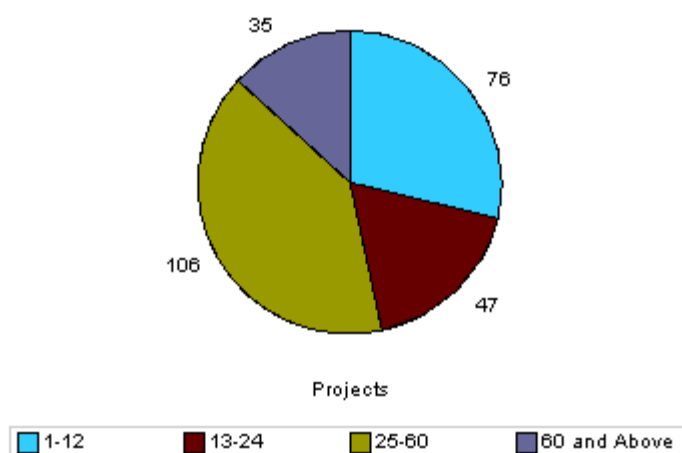


Trend and Graphical Analysis

Water Resources Sector

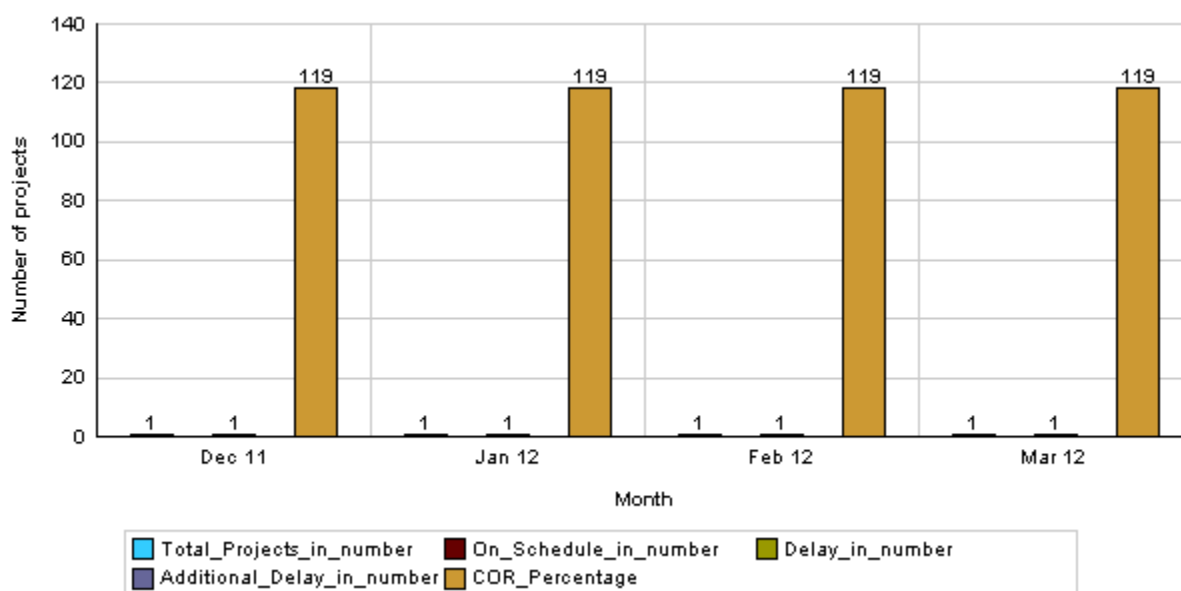


Water Resources Sector Sector Break-up of 1 Delayed projects in March 2012

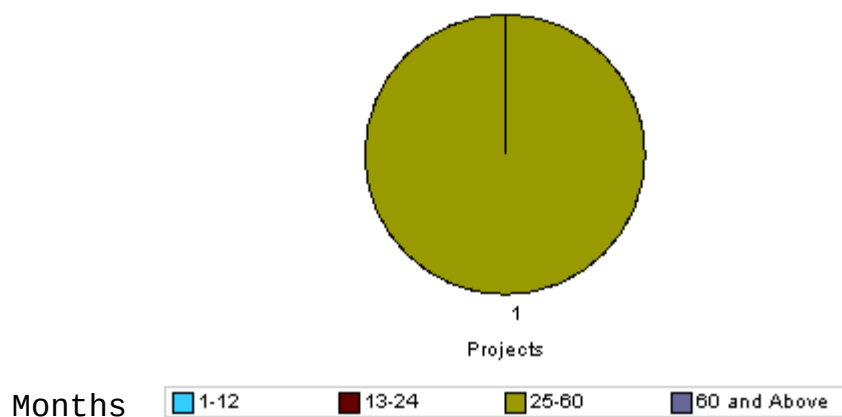


Trend and Graphical Analysis

Urban Development Sector

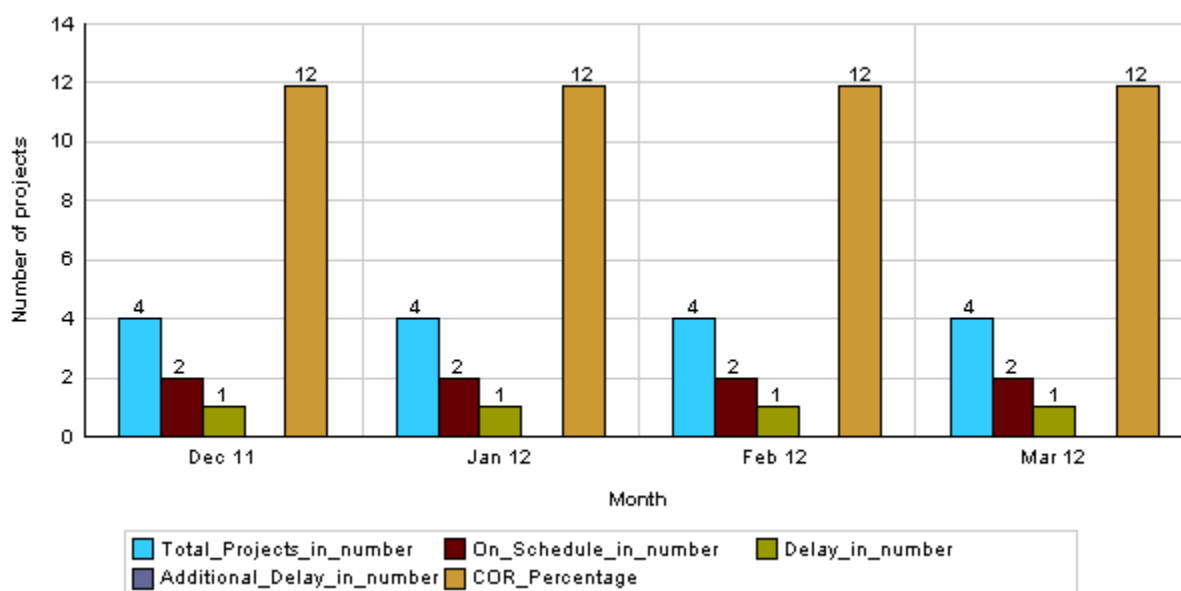


Urban Development Sector Break-up of 1 Delayed projects in March 2012

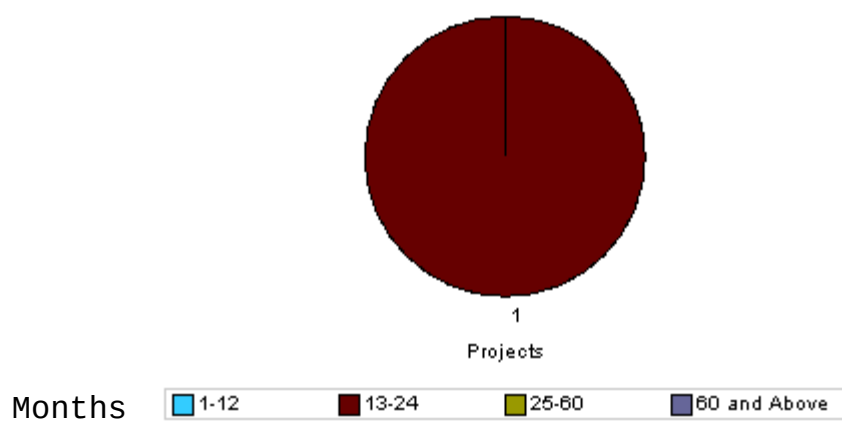


Trend and Graphical Analysis


Telecommunications Sector

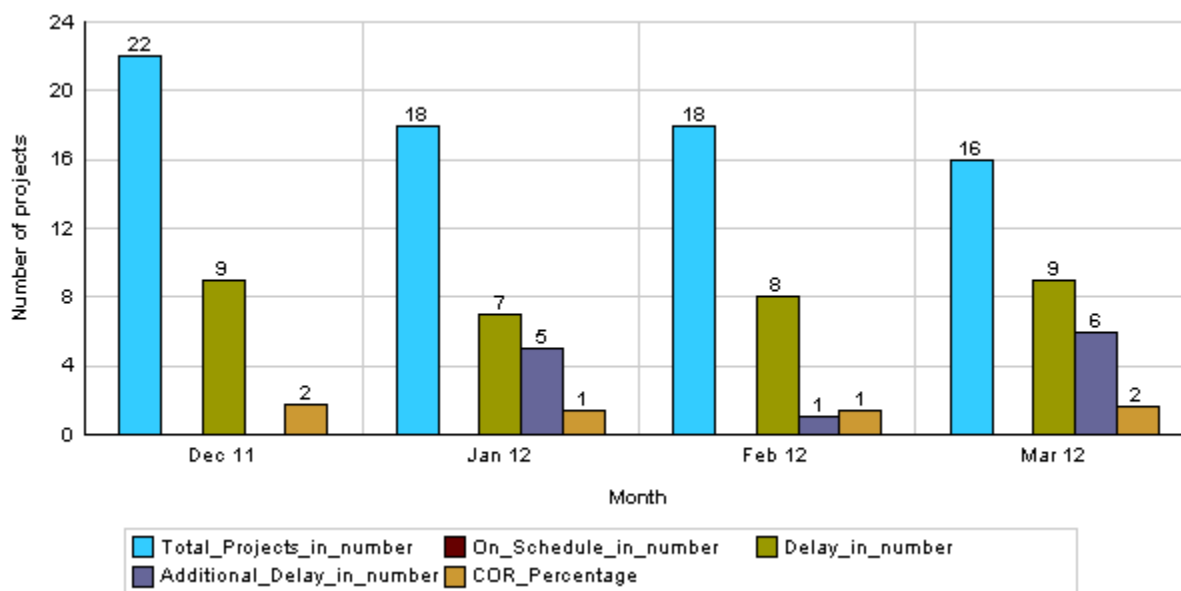


Telecommunications Sector Sector Break-up of 9 Delayed projects in March 2012

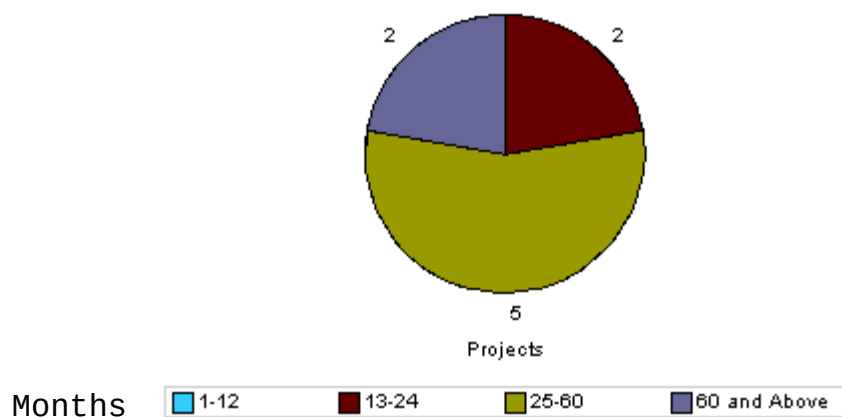


Trend and Graphical Analysis Shipping and Ports Sector

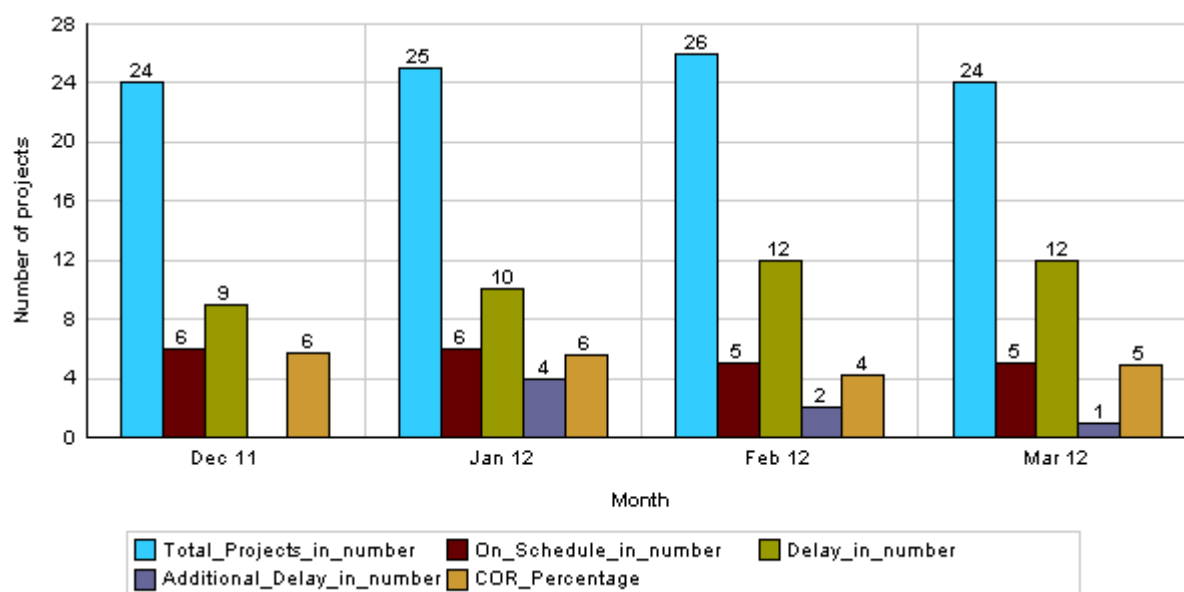


Sector Break-up of 12 Delayed projects in March 2012

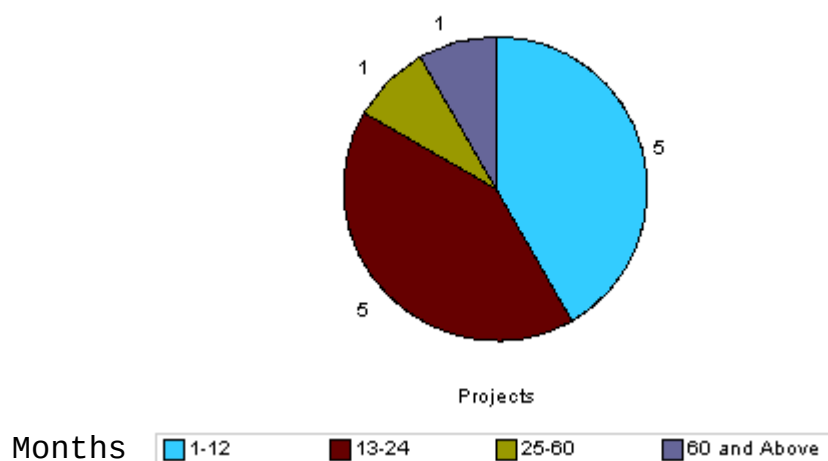

Trend and Graphical Analysis Road Transport and Highways Sector

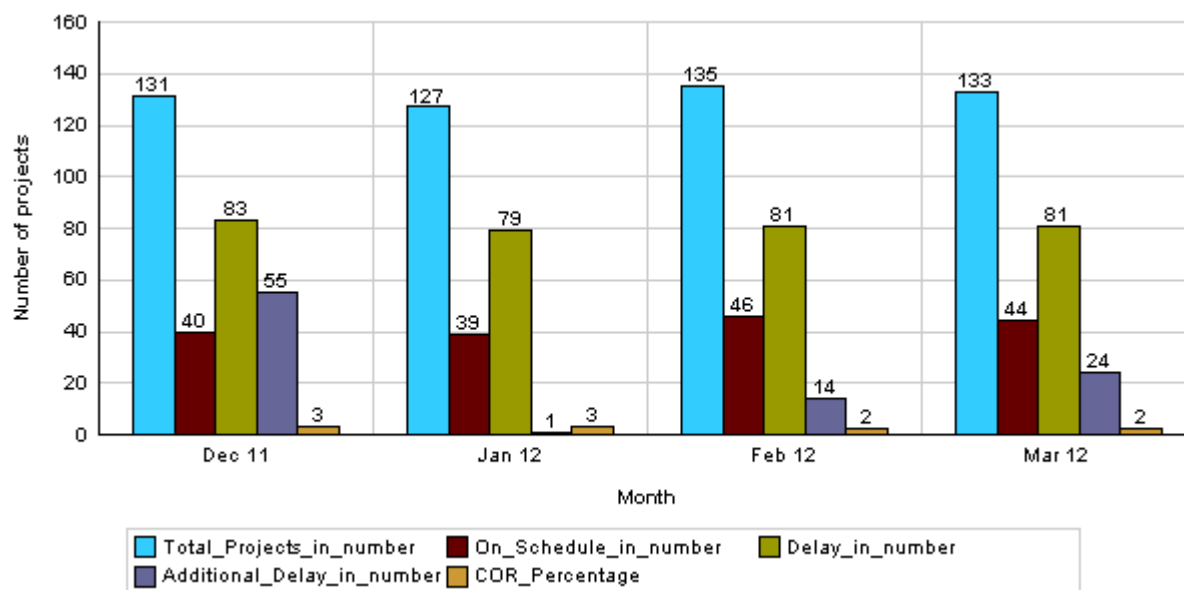


Sector Break-up of 81 Delayed projects in March 2012

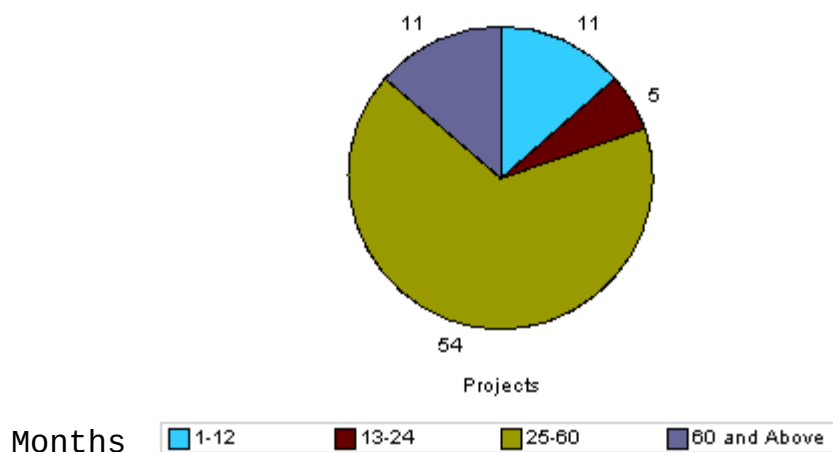


Trend and Graphical Analysis

Railways Sector

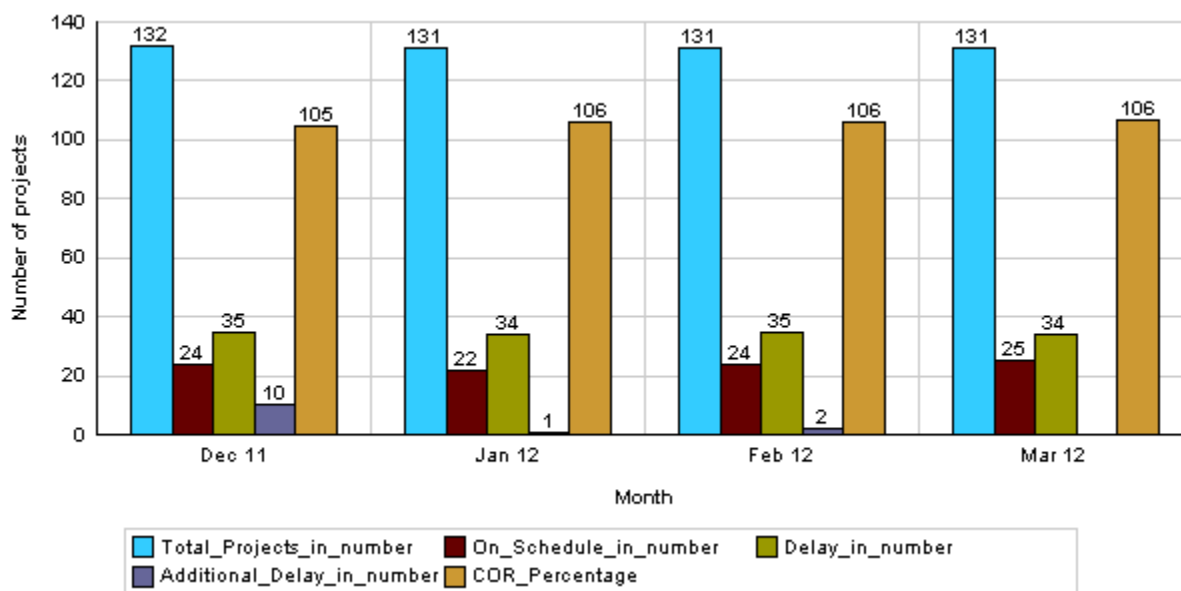


Railways Sector Break-up of 34 Delayed projects in March 2012

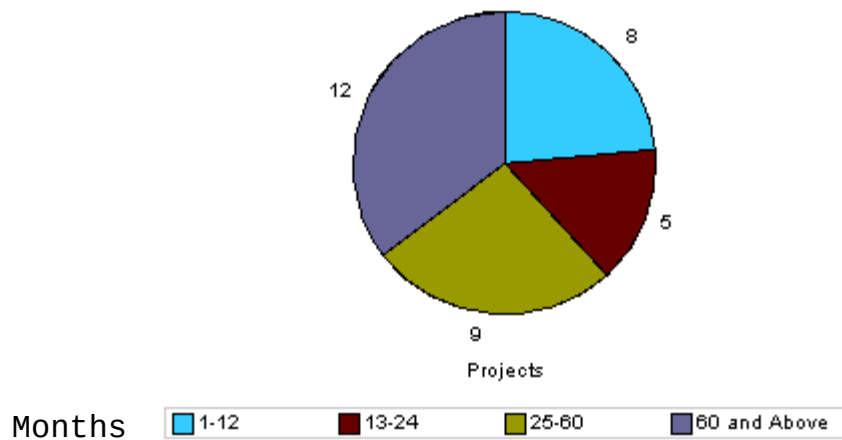


Trend and Graphical Analysis

Power Sector

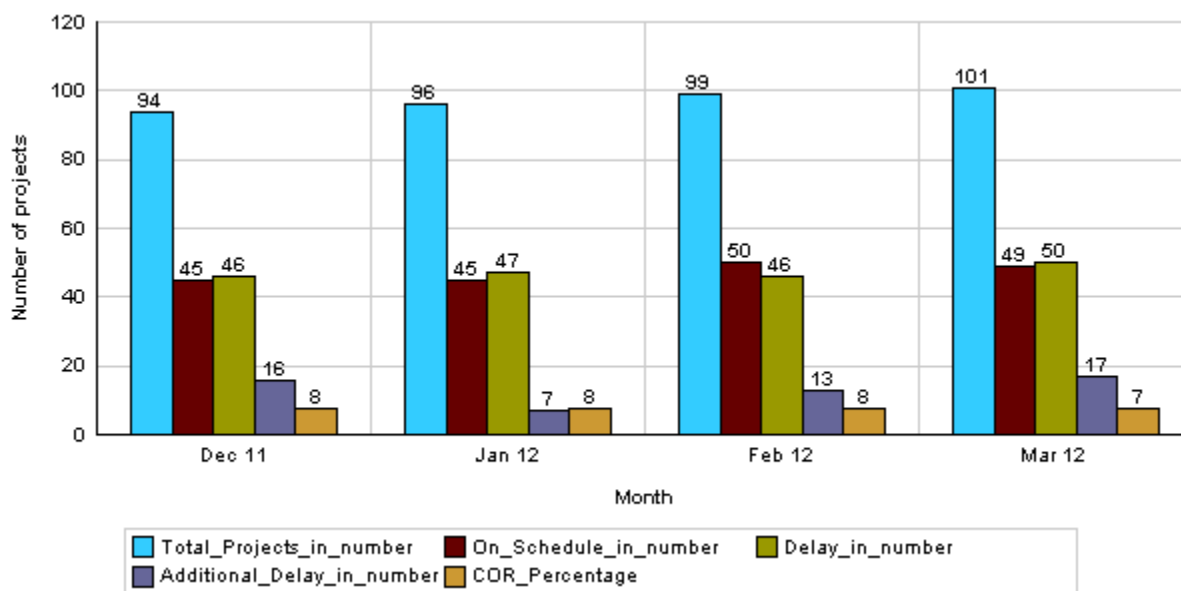

Power Sector Sector Break-up of 50 Delayed projects in March 2012

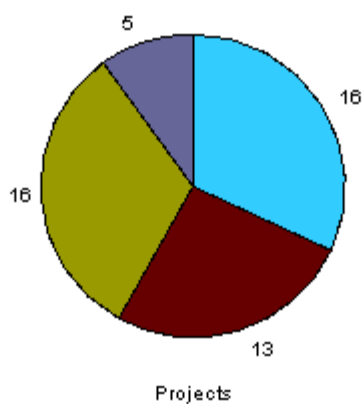


Months




Trend and Graphical Analysis

Petroleum Sector

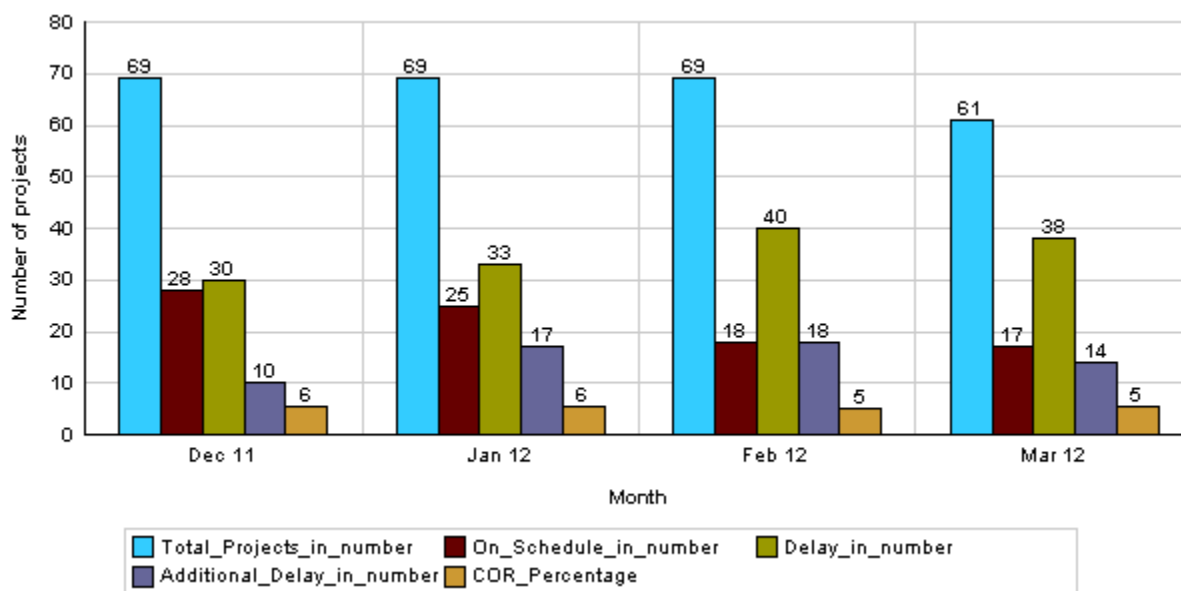


Petroleum Sector Sector Break-up of 38 Delayed projects in March 2012

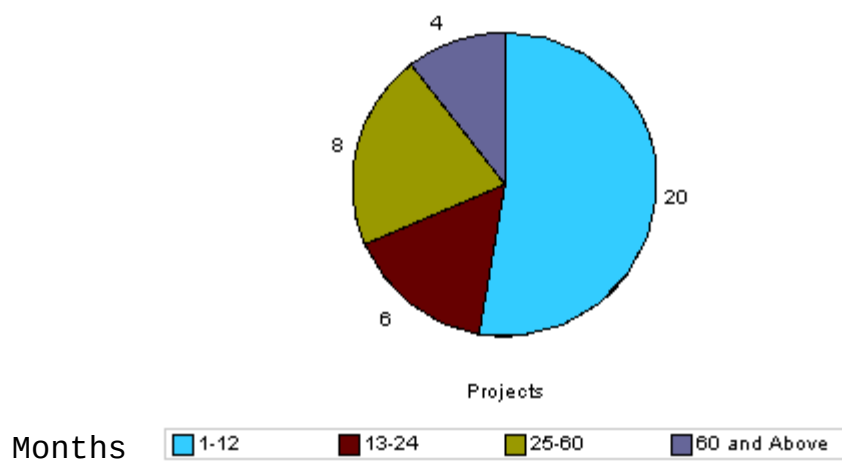


Trend and Graphical Analysis

Steel Sector

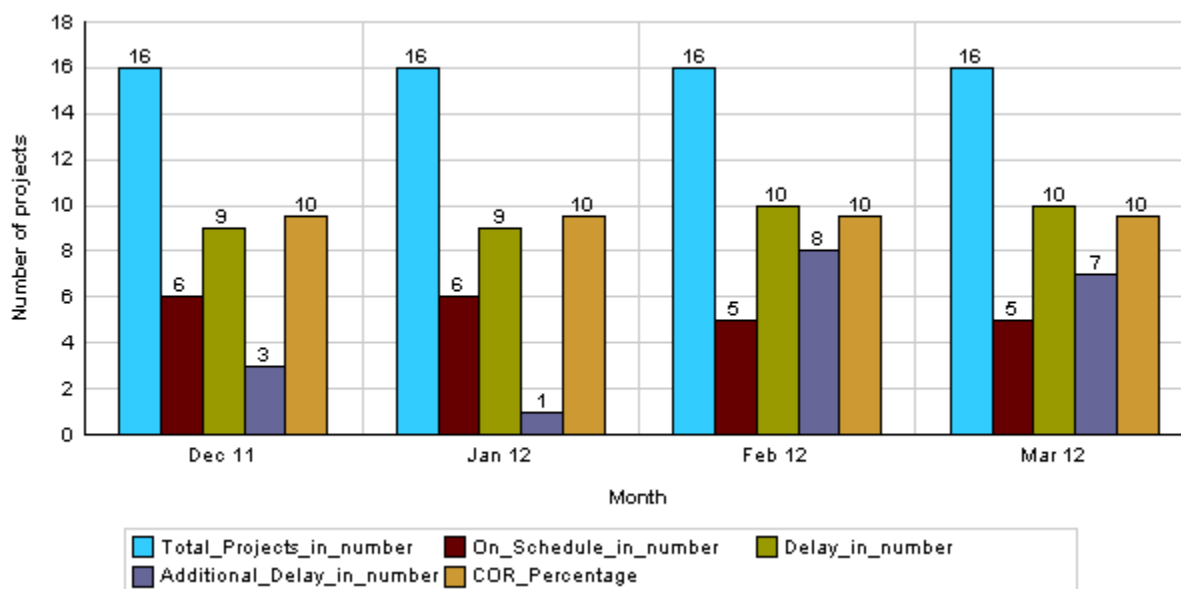


Steel Sector Sector Break-up of 10 Delayed projects in March 2012

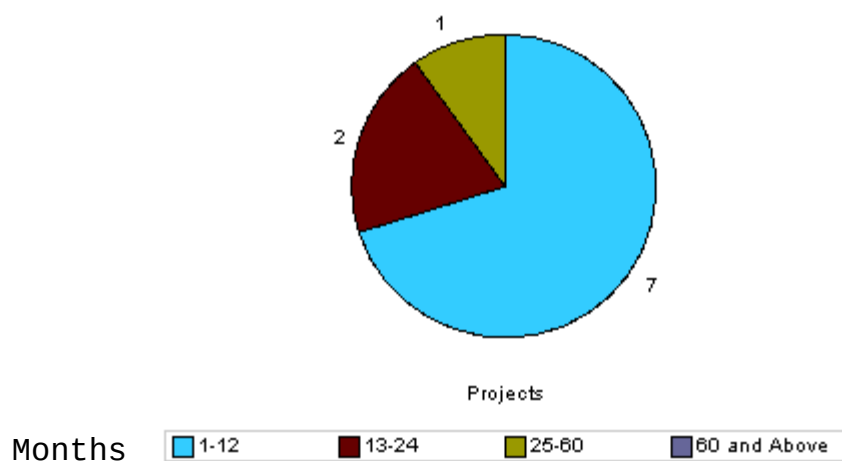


Trend and Graphical Analysis

Fertilisers Sector

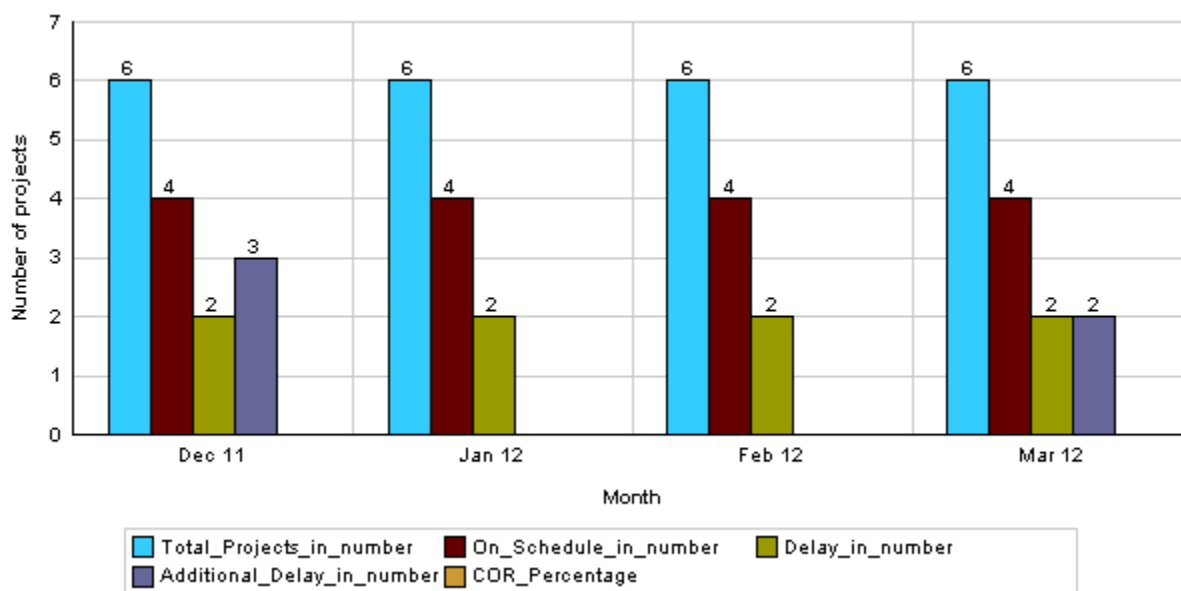


Fertilisers Sector Sector Break-up of 2 Delayed projects in March 2012

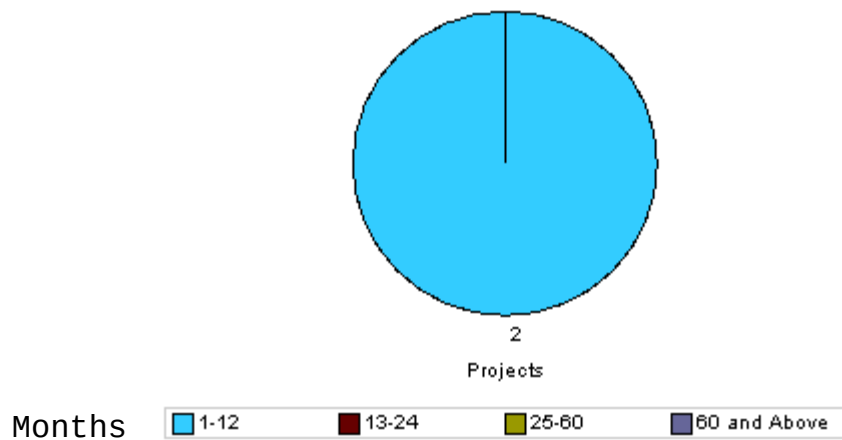


Trend and Graphical Analysis

Coal Sector

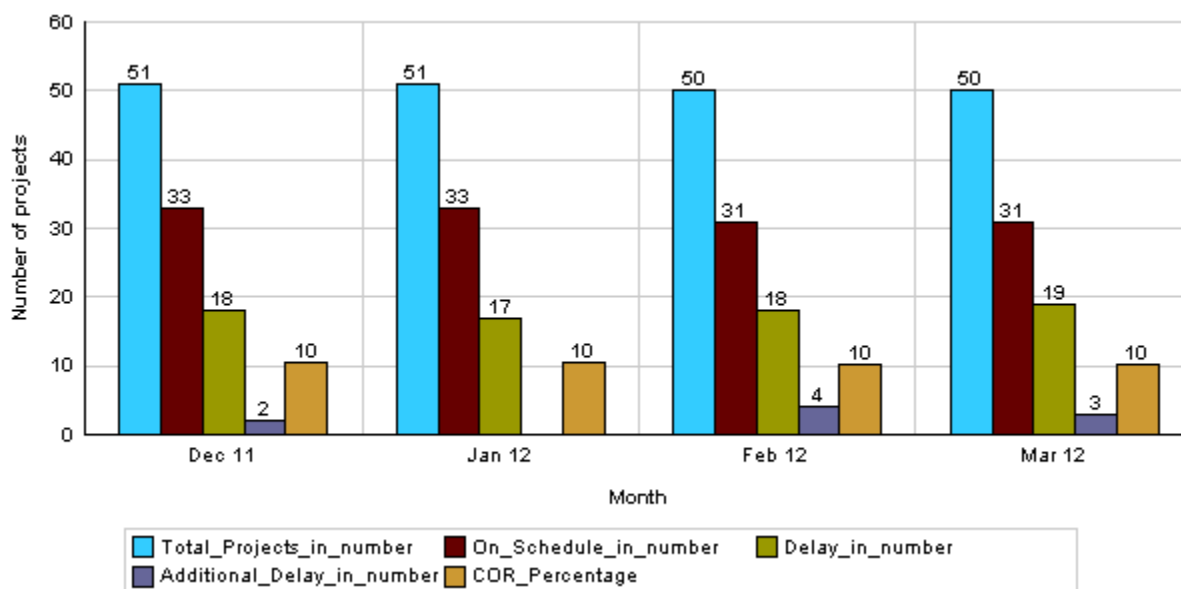


Coal Sector Sector Break-up of 19 Delayed projects in March 2012

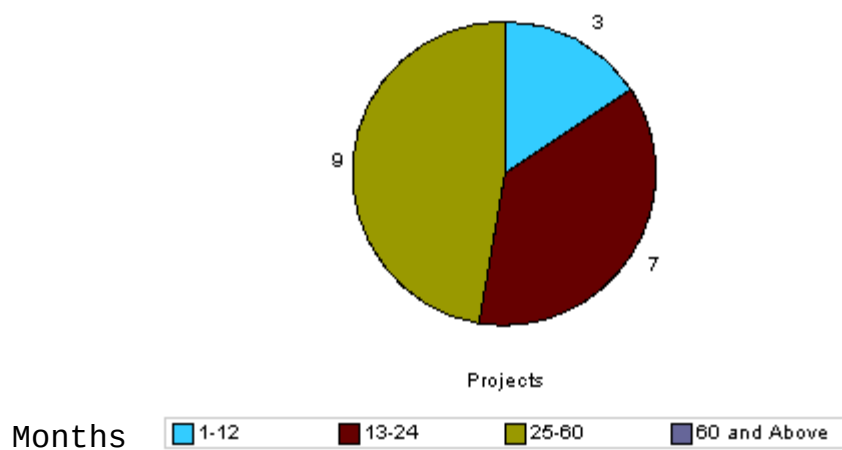


Trend and Graphical Analysis

Civil Aviation Sector

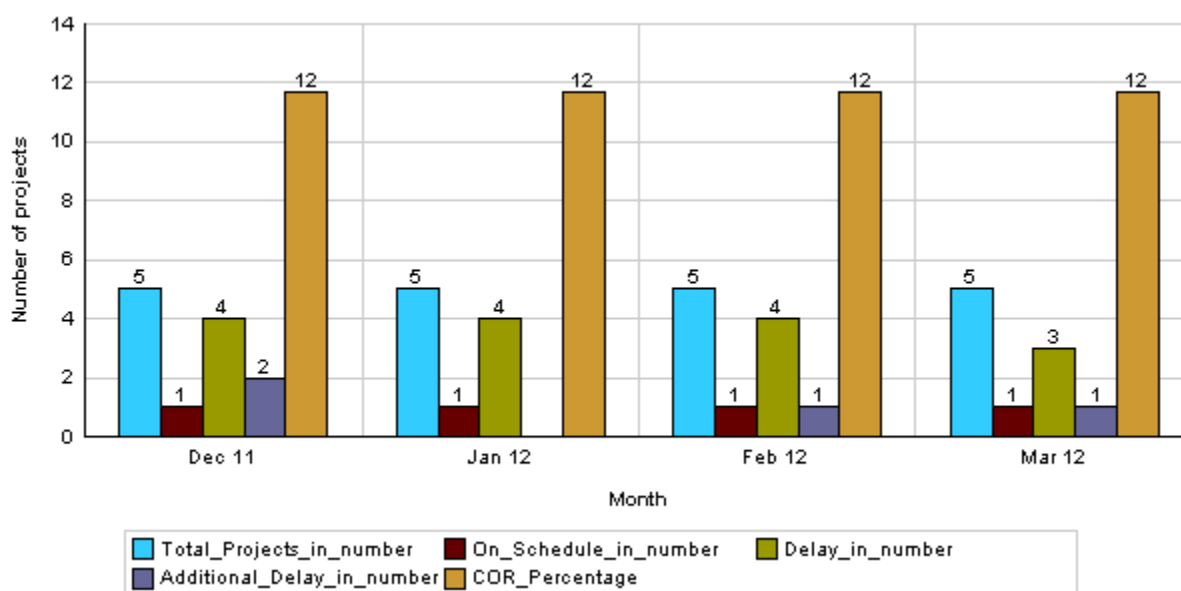


Civil Aviation Sector Break-up of 3 Delayed projects in March 2012

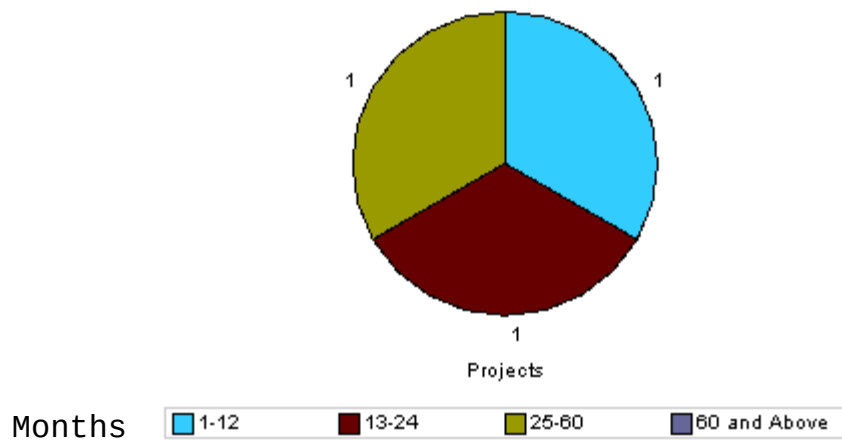


Trend and Graphical Analysis

Atomic Energy Sector

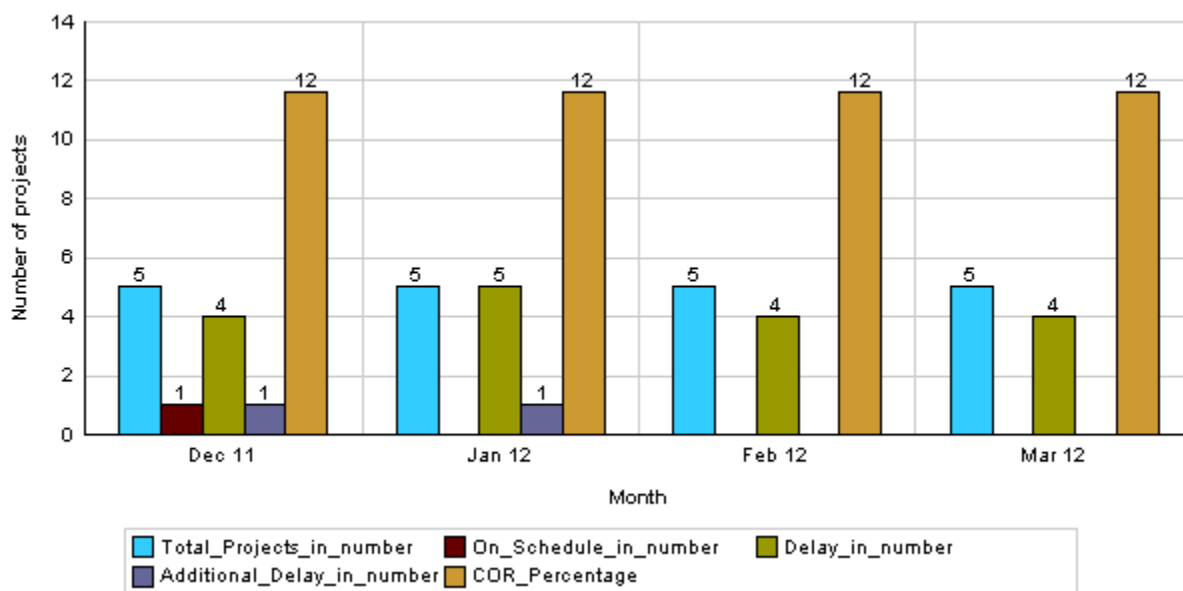

Atomic Energy Sector Sector Break-up of 4 Delayed projects in March 2012

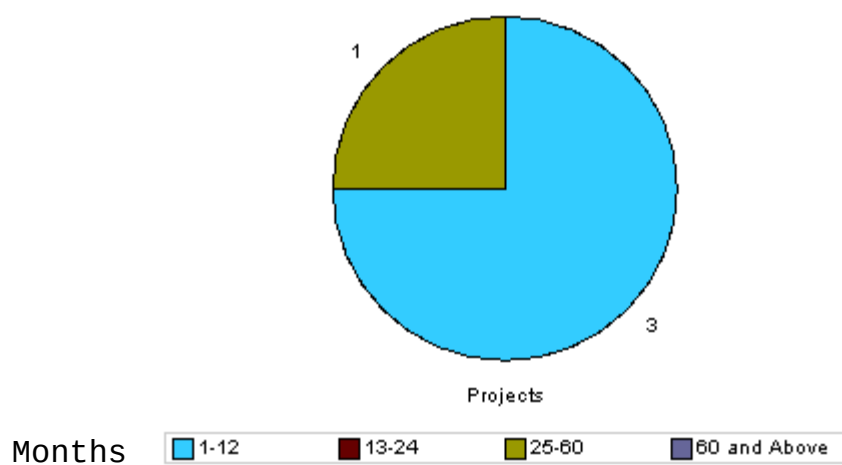

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			Cumm Expenditure
		Original	Latest	Anticipated	
Atomic Energy	5	41,548.29	41,548.29	46,386.29	21,460.84
Civil Aviation	5	5,021.58	5,228.58	5,611.07	4,128.55
Coal	50	33,604.55	34,238.15	37,053.10	11,667.00
Fertilisers	6	5,317.41	5,317.41	5,317.41	2,197.80
Steel	16	65,244.82	71,120.10	71,412.36	39,595.77
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	61	145,017.77	158,163.42	152,886.87	67,696.95
Power	101	208,284.36	212,168.18	223,398.21	100,309.31
Railways	131	65,286.30	89,833.84	134,791.49	59,357.04
Road Transport & Highways	133	79,244.48	79,410.98	81,045.31	57,020.34
Shipping & Ports	24	18,511.36	19,263.52	19,421.43	5,128.63
Telecommunications	16	7,130.82	7,134.70	7,247.12	2,031.42
Urban Development	4	44,245.18	44,304.08	49,518.08	2,412.18
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	554	724,460.43	777,194.15	844,195.74	377,551.83

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,498.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,380.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,577.60	09/2010	01/2012	16(O)	6/80
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	921.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011	04/2012	12(O) 12(R)	0/0
Total			41,548.29	46,386.29	21,460.84				45/325
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,839.13	05/2011 03/2012	10/2012	17(O) 7(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	182.84	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	108.57	05/2012	08/2012	3(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,651.68	01/2011 02/2012	02/2012	13(O) 0(R)	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	346.33	06/2013	06/2013	0(O)	0/0
Total			5,021.58	5,611.07	4,128.55				0/0
<u>Coal</u>									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	264.20	03/2013 09/2012	10/2014	19(O) 25(R)	6/22
12	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	92.74	03/2016	03/2016	0(O)	0/1
13	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	317.40	03/2014 03/2016	03/2016	24(O) 0(R)	2/2

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	75.41	03/2012 03/2012	03/2012	0(O) 0(R)	5/7
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	108.35	03/2011 03/2012	03/2013	24(O) 12(R)	0/2
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	100.57	03/2010 -	03/2015	60(O) -	4/4
17	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	106.63	03/2017 03/2017	03/2017	0(O) 0(R)	6/12
18	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	161.76	03/2012 03/2015	03/2015	36(O) 0(R)	0/0
20	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015 -	03/2015	0(O) -	0/1
21	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	263.89	03/2014 03/2014	03/2014	0(O) 0(R)	0/4
22	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	34.01	03/2011 03/2012	03/2014	36(O) 24(R)	1/2
23	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,194.78	03/2014 -	03/2014	0(O) -	0/13
24	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,325.28	03/2014 -	03/2014	0(O) -	0/15
25	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	59.64	03/2015 03/2015	03/2015	0(O) 0(R)	2/12
26	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	91.35	03/2013 03/2013	03/2013	0(O) 0(R)	5/7
27	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2015	0(O) -	1/1
28	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	0/31
29	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	3/83
30	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48(O) -	0/1
31	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	71.92	12/2012 -	03/2015	27(O) -	7/44
32	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	117.33	03/2013 03/2013	03/2013	0(O) 0(R)	6/11
33	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	33.85	03/2014 -	03/2014	0(O) -	0/0
34	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O) -	0/1
35	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
36	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	330.76	03/2010 -	03/2013	36(O) -	2/2

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	87.96	03/2010	03/2012	24(O)	9/11
38	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	634.55	03/2013 03/2013	03/2013	0(O) 0(R)	0/8
39	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
40	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	44(O) 24(R)	1/2
41	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	209.33	03/2014 03/2014	03/2014	0(O) 0(R)	0/5
42	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	36.96	03/2012	03/2013	12(O)	8/34
43	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	1,230.27	-	04/2015	04/2015	0(O)	0/0
44	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	339.88	-	04/2014	04/2014	0(O)	0/0
45	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	14.47	12/2015	12/2015	0(O)	0/33
46	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40	259.40	1.20	03/2012	03/2012	0(O)	0/1
47	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	62.45	03/2012 03/2012	03/2014	24(O) 24(R)	0/2
48	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
49	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.82	03/2014	03/2015	12(O)	0/1
50	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98	210.98	33.74	03/2013	03/2013	0(O)	0/2
51	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08	153.82	22.64	03/2011	03/2014	36(O)	0/1
52	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	82.58	03/2012	03/2013	12(O)	21/27
53	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.24	03/2015	03/2015	0(O)	0/29
54	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78	209.78	21.83	03/2015	03/2015	0(O)	4/31
55	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	284.57	03/2016	03/2016	0(O)	1/2
56	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	45.80	03/2012	03/2012	0(O)	11/41
57	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	46.63	03/2016 03/2016	03/2016	0(O) 0(R)	1/12
58	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	3,027.00	2,394.54	06/2009	03/2013	45(O)	19/24

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,768.27	03/2012 -	03/2014	24(O) -	0/39
60	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	96.73	03/2012 03/2013	03/2014	24(O) 12(R)	0/2
	Total		33,604.55 -	37,053.10	11,667.00				126/616
Fertilisers									
61	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	490.31	01/2013 -	01/2013	0(O) -	0/5
62	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	203.75	07/2011 -	07/2012	12(O) -	0/0
63	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	161.95	07/2011 -	04/2012	9(O) -	0/0
64	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	522.16	01/2013 01/2013	01/2013	0(O) 0(R)	8/8
65	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	530.91	01/2013 -	01/2013	0(O) -	0/5
66	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	288.72	04/2012 04/2012	04/2012	0(O) 0(R)	12/22
	Total		5,317.41 -	5,317.41	2,197.80				20/40
Steel									
67	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O) -	0/0
68	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	241.50	08/2010 08/2010	05/2012	21(O) 21(R)	0/1
69	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	246.84	02/2011 02/2011	06/2012	16(O) 16(R)	2/3
70	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O) -	0/0
71	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 -	232.93	191.33	05/2011 -	05/2012	12(O) -	1/1
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	460.00	190.54	05/2012 05/2012	12/2012	7(O) 7(R)	1/2
73	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	323.39	12/2011 03/2012	10/2012	10(O) 7(R)	15/21
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	77.01	10/2012 10/2012	10/2012	0(O) 0(R)	3/4

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55	254.55	3.47	11/2013	11/2013	0(O)	0/0
76	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00	17,265.00	5,179.68	03/2013	09/2013	6(O)	18/20
77	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00	6,325.00	2,624.65	12/2011	10/2012	10(O)	10/11
78	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00	2,875.00	750.85	12/2012	03/2013	3(O)	5/6
79	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00	16,408.00	13,087.79	12/2011	12/2012	12(O)	13/14
80	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00	12,291.00	9,481.85	10/2009	10/2012	36(O) 0(R)	59/64
81	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	11,812.00	11,812.00	6,841.66	03/2013	03/2013	0(O)	5/8
82	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL, Jharkhand)	10/2007	500.90	500.90	355.21	-	02/2012	-	3/3
Total			65,244.82	71,412.36	39,595.77				135/158
Petrochemicals									
83	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61	8,920.00	4,510.51	12/2013	12/2013	0(O) 0(R)	10/30
Total			5,460.61	8,920.00	4,510.51				10/30
Petroleum									
84	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00	1,106.00	-	06/2012	04/2013	10(O)	0/0
85	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64	2,163.64	798.79	06/2012	12/2012	6(O)	0/0
86	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11	370.11	194.89	04/2011	07/2012	15(O)	0/0
87	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35	977.00	261.99	12/2011	01/2013	13(O)	0/0
88	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	589.71	03/2013	03/2014	12(O)	0/0
89	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	5.57	12/2014	12/2014	0(O)	0/0
90	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014	12/2014	0(O)	0/0
91	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	460.70	195.06	07/2012	03/2013	8(O) 8(R)	0/16
92	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50	341.50	54.57	02/2013	02/2013	0(O) 0(R)	30/42

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	114.65	-	09/2012	-	23/36
94	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	706.29	04/2011 12/2011	04/2012	12(O) 4(R)	2/2
95	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65	736.65	257.92	09/2011	12/2012	15(O)	0/0
96	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,861.93	05/2010 05/2012	07/2012	26(O) 2(R)	0/0
97	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	312.61	02/2011 08/2011	08/2011	6(O) 0(R)	0/0
98	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94	202.94	-	01/2014	01/2014	0(O)	0/0
99	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	195.09	09/2012 09/2012	09/2012	0(O) 0(R)	0/0
100	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	861.79	-	05/2013	05/2013	0(O)	0/0
101	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	269.10	-	08/2013	01/2014	5(O)	0/0
102	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	302.26	29.49	09/2012	09/2012	0(O)	0/0
103	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
104	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,658.05	03/2012 08/2012	08/2012	5(O) 0(R)	0/17
105	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	12.70	-	-	-	0/0
106	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,584.43	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
107	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,204.08	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
108	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	697.35	07/2010 05/2012	07/2012	24(O) 2(R)	0/0
109	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	12/2008 12/2008	04/2013	52(O) 52(R)	0/0
110	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009	08/2011	23(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
111	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	834.60	09/2012 05/2012	05/2012	-4(O) 0(R)	0/76
112	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,155.00	09/2011 03/2012	03/2012	6(O) 0(R)	0/0
113	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	29.47	03/2013 -	04/2013	1(O) -	0/0
114	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	158.92	03/2013 -	04/2013	1(O) -	0/0
115	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	05/2013	6(O) -	0/0
116	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O) -	0/0
117	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,890.36	- -	12/2011	- -	114/116
118	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	81.36	01/2013 -	01/2013	0(O) -	15/18
119	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	462.74	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
120	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,918.57	04/2006 05/2011	06/2012	74(O) 13(R)	0/0
121	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,300.00	1,068.89	06/2012 06/2012	06/2012	0(O) 0(R)	6/8
122	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,447.85	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
123	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	597.20	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
124	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	274.39	03/2006 03/2013	03/2013	84(O) 0(R)	6/6
125	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.20	01/2013 -	07/2015	30(O) -	0/0
126	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50(O) -	0/0
127	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 252.37	204.00	168.94	01/2012 -	05/2012	4(O) -	3/8
128	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	711.38	12/2012 12/2012	04/2013	4(O) 4(R)	0/21
129	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	193.21	03/2012 08/2012	05/2012	2(O) -3(R)	2/4
130	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,412.96	01/2012 -	10/2012	9(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	3,249.02	09/2012	09/2013	12(O) -	0/0
132	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,863.48	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
133	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	5.67	04/2015	04/2015	0(O) -	0/0
134	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	534.30	03/2011 05/2011	10/2012	19(O) 17(R)	0/0
135	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	417.93	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
136	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	14,627.00	11/2012 06/2013	06/2013	7(O) 0(R)	57/100
137	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,400.00	596.26	09/2012 09/2012	09/2012	0(O) 0(R)	0/11
138	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	894.36	02/2014	02/2014	0(O) -	0/0
139	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	546.61	07/2012	07/2012	0(O) -	0/0
140	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	842.61	09/2011 03/2012	03/2012	6(O) 0(R)	0/0
141	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	463.51	05/2010 04/2012	05/2012	24(O) 1(R)	0/0
142	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	153.24	08/2012	08/2012	0(O) -	0/0
143	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32	330.47	199.02	03/2012 03/2012	06/2012	3(O) 3(R)	0/20
144	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	576.60	34.77	12/2013 12/2013	12/2013	0(O) 0(R)	0/0
Total			145,017.77	152,886.87	67,696.95				267/677
Power									
145	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	4,740.40	08/2012	03/2013	7(O) -	0/0
146	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	994.10	02/2012	06/2012	4(O) -	0/0
147	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	454.10	05/2012	05/2012	0(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	715.30	06/2012	06/2012	0(O)	0/0
149	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	3,595.00	08/2013	01/2014	5(O)	5/18
150	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97	8,693.00	6,543.00	12/2009 12/2014	12/2014	60(O) 0(R)	26/47
151	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	2,861.00	06/2011	11/2014	41(O)	2/29
152	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	2,084.00	1,794.22	08/2010 08/2011	04/2012	20(O) 8(R)	0/2
153	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	621.28	-	02/2011	12/2012	22(O)	2/4
154	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	24.10	08/2014	08/2014	0(O)	0/0
155	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44	206.44	-	06/2014	06/2014	0(O)	0/0
156	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	150.70	09/2014	09/2014	0(O)	0/0
157	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	768.10	10/2009	05/2012	31(O)	20/20
158	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	181.20	11/2012	12/2013	13(O)	0/0
159	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	198.63	-	09/2014	09/2014	0(O)	0/0
160	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	135.60	05/2014	05/2014	0(O)	0/0
161	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	328.20	08/2013	08/2013	0(O)	0/0
162	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	166.20	06/2012	06/2012	0(O)	0/0
163	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	77.60	12/2013	12/2013	0(O)	0/0
164	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	-	12/2013	12/2013	0(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
165	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	25.60	10/2012 -	03/2013	5(O) -	0/0
166	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	825.50	12/2007 12/2009	12/2009	24(O) 0(R)	0/18
167	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,788.85	05/2013 06/2016	06/2016	37(O) 0(R)	2/22
168	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,390.53	01/2016 01/2016	11/2016	10(O) 10(R)	0/2
169	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,149.00	04/2009 04/2011	03/2013	47(O) 23(R)	0/9
170	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,283.68	2,618.18	04/2005 -	03/2012	83(O) -	8/8
171	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,791.78	09/2008 -	03/2013	54(O) -	3/37
172	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/0
173	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	686.00	11/2011 -	12/2012	13(O) -	6/34
174	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	469.38	213.10	10/2012 -	04/2012	-6(O) -	0/0
175	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	3,635.00	08/2012 -	03/2013	7(O) -	9/16
176	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	723.13	08/2010 09/2011	01/2013	29(O) 16(R)	0/3
177	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	3,668.20	08/2013 -	09/2014	13(O) -	0/0
178	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	164.60	11/2011 11/2011	06/2012	7(O) 7(R)	0/0
179	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	151.60	02/2012 -	12/2012	10(O) -	0/0
180	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	276.60	11/2011 -	12/2012	13(O) -	0/0
181	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	314.90	11/2011 -	12/2012	13(O) -	0/0
182	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	27.30	01/2013 -	01/2013	0(O) -	0/0
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	118.40	07/2013 -	07/2013	0(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	290.00	04/2013	04/2013	0(O)	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	39.60	08/2013	08/2013	0(O)	0/0
186	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	337.20	11/2012	11/2012	0(O)	0/0
187	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	2,716.00	1,756.57	10/2010	01/2013	27(O) 13(R)	0/1
188	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59	5,524.00	3,535.89	09/2009	07/2014	58(O) 0(R)	1/20
189	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	305.83	08/2012	08/2013	12(O) 0(R)	9/19
190	RAMPUR HEP(412 MW) - [N18000024]SJVN,Himachal Pr.	01/2007	2,047.03	2,047.03	1,599.91	01/2012	09/2013	20(O)	0/0
191	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	2,760.00	10/2012	03/2013	5(O)	8/16
192	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,745.00	12/2009	04/2012	28(O) 4(R)	59/60
193	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33	10,667.00	5,603.13	09/2010	12/2015	63(O) 16(R)	11/11
194	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	19.30	04/2013	04/2013	0(O)	0/0
195	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,844.90	08/2012	03/2013	7(O)	0/0
196	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	124.00	07/2011	05/2012	10(O)	0/0
197	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	-	08/2014	08/2014	0(O)	0/0
198	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	-	02/2015	02/2015	0(O)	0/0
199	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	-	01/2015	01/2015	0(O)	0/0
200	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	-	08/2014	08/2014	0(O)	0/0
201	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	3.70	06/2014	06/2014	0(O)	0/0
202	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	134.40	04/2012	04/2012	0(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
203	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	66.58	06/2012	06/2012	0(O)	0/0
204	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	639.90	08/2012	08/2012	0(O)	0/0
205	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,377.00	03/2013	06/2014	15(O)	2/13
206	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,102.86	09/2009	06/2013	45(O)	0/0
207	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.39	1,454.67	03/2007	09/2012	66(O)	25/25
208	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00	2,978.86	320.70	07/2010	02/2016	67(O) 0(R)	1/10
209	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	-	01/2013	01/2013	0(O)	0/0
210	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93	181.93	0.02	07/2013	07/2013	0(O)	0/0
211	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	-	08/2014	08/2014	0(O)	0/0
212	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.91	310.93	07/2011	12/2012	17(O)	0/0
213	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,538.90	10/2012	11/2013	13(O)	0/0
214	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
215	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	306.30	03/2014	03/2014	0(O)	0/0
216	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,779.46	3,652.60	09/2009	06/2012	33(O)	11/30
217	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	268.80	08/2013	08/2013	0(O)	0/0
218	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33	324.33	-	08/2014	08/2014	0(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
219	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	-	10/2014 -	10/2014	0(O) -	0/0
220	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	523.00	01/2010 -	12/2012	35(O) -	0/22
221	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	142.40	11/2011 -	09/2013	22(O) -	0/0
222	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	3,157.10	12/2012 -	12/2012	0(O) -	0/0
223	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	-	02/2014 -	02/2014	0(O) -	0/0
224	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	33.90	10/2013 -	10/2013	0(O) -	0/0
225	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O) -	0/0
226	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	85.20	12/2013 -	12/2013	0(O) -	0/0
227	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	558.26	-	11/2013 -	11/2013	0(O) -	0/0
228	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	383.10	03/2013 -	03/2013	0(O) -	0/0
229	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	401.00	12/2013 -	12/2013	0(O) -	0/0
230	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	820.40	11/2012 -	06/2013	7(O) -	0/0
231	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	-	07/2014 -	07/2014	0(O) -	0/0
232	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	157.87	07/2013 07/2013	07/2013	0(O) 0(R)	0/30
233	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	303.47	07/2006 01/2014	01/2014	90(O) 0(R)	7/24
234	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	303.47	01/2014 -	01/2014	0(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
235	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	647.90	12/2012	12/2012	0(O)	0/0
236	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	194.50	11/2013	11/2013	0(O)	0/0
237	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	39.60	01/2013	01/2013	0(O)	0/0
238	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29	1,794.00	1,691.47	11/2009	02/2013	39(O) 15(R)	0/4
239	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	2,965.00	10/2012	03/2013	5(O)	7/15
240	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58	3,422.44	296.15	07/2014	05/2016	22(O)	1/2
241	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	362.10	02/2012	03/2012	1(O)	0/0
242	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,071.70	07/2010	12/2012	29(O)	20/20
243	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	390.90	09/2010	03/2013	30(O)	0/0
244	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	103.30	02/2012	06/2012	4(O) 4(R)	0/0
245	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76	9,569.76	-	06/2015	06/2015	0(O)	0/0
Total			208,284.36	223,398.21	100,309.31				245/591
Railways									
246	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.75	319.74	03/2014	03/2014	0(O)	0/0
247	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00	227.42	250.82	12/2009	03/2011	15(O) 0(R)	0/0
248	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08	1,010.00	135.21	-	-	-	0/0
249	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73	399.50	322.76	03/2009	12/2010	21(O) 24(R)	0/0
250	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00	435.87	390.92	03/2011	03/2011	0(O) 0(R)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
251	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	508.15	06/1999 03/2011	03/2011	141(O) 0(R)	0/0
252	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
253	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O) -	0/0
254	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
255	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,173.79	424.73	03/2005 12/2008	03/2016	132(O) 87(R)	0/0
256	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	189.98	12/2010 03/2011	03/2011	3(O) 0(R)	0/0
257	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	174.27	03/2004 12/2010	12/2010	81(O) 0(R)	0/0
258	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	4.41	04/2014 -	03/2014	-1(O) -	0/0
259	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	269.02	- -	-	-	0/0
260	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	486.33	03/2010 -	12/2012	33(O) -	0/0
261	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	309.21	- 03/2009	03/2011	- 24(R)	0/0
262	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	121.09	12/2012 -	12/2012	0(O) -	0/0
263	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	177.89	03/2011 -	03/2011	0(O) -	0/0
264	Bhuj-Naliya(GC) with extension from naliya to vador - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	0.99	03/2012 -	03/2012	0(O) -	0/0
265	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
266	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,103.47	856.18	12/2012 -	12/2012	0(O) -	0/0
267	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
268	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
269	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	415.73	231.82	- -	03/2012	-	0/0
270	CONV.OF 1500V DC TRACTION TO 25 KV AC,CR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2012	06/2012	-12(O) 0(R)	0/0
271	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	103.49	12/2012 -	12/2012	0(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
272	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	180.95	- -	03/2013	- -	0/0
273	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	375.04	12/2012 12/2012	12/2012	0(O) 0(R)	0/0
274	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	502.08	- -	-	- -	0/0
275	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	80.01	12/2011 02/2012	02/2012	2(O) 0(R)	0/0
276	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	0(O) -	0/0
277	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12(O) -	0/0
278	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	151.38	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
279	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	548.61	03/1995 -	03/2012	204(O) -	0/0
280	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	257.85	02/2011 02/2011	03/2012	13(O) 13(R)	0/0
281	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	283.10	39.12	02/2006 -	12/2012	82(O) -	0/0
282	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	863.23	498.94	- -	-	- -	0/0
283	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	03/1998	0(O) -	0/0
284	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	307.52	- 05/2009	05/2009	- 0(R)	0/0
285	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213(O) -	0/0
286	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	65.91	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
287	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	176.77	- -	03/2015	- -	0/0
288	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	210.32	- 09/2009	12/2011	- 27(R)	0/0
289	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	- -	0/0
290	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	483.14	- -	-	- -	0/0
291	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	137.53	- -	-	- -	0/0
292	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	159.83	03/2007 03/2007	03/2014	84(O) 84(R)	0/0
293	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	69.17	- -	-	- -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
294	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	3.08	03/2015 -	03/2015	0(O) -	0/0
295	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	829.07	06/2007 -	06/2007	0(O) -	0/0
296	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	903.56	603.60	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
297	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	390.91	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
298	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	679.56	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
299	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	95.65	03/2014 -	03/2014	0(O) -	0/0
300	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	212.77	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
301	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,252.53	- -	02/2012	- -	0/0
302	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	471.31	- -	-	- -	1/1
303	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	712.00	703.73	- -	-	- -	0/0
304	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	725.17	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
305	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	88.62	- -	-	- -	0/0
306	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	-	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
307	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	206.01	- -	03/2012	- -	0/0
308	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	1.22	- -	03/2015	- -	0/0
309	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	397.67	- -	-	- -	0/0
310	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,212.31	07/2005 -	07/2005	0(O) -	0/0
311	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	88.97	- -	-	- -	0/0
312	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	260.24	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
313	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.41	- -	-	- -	0/0
314	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	331.25	- -	03/2011	- -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
315	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	103.18	12/2012 -	03/2014	15(O) -	0/0
316	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	03/2011	34(O) 0(R)	0/0
317	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	200.08	03/2002 -	03/2012	120(O) -	0/0
318	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,027.93	3,028.24	03/2009 -	12/2013	57(O) -	0/0
319	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	458.26	0.35	07/2008 -	07/2008	0(O) -	0/0
320	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	150.66	- -	-	- -	0/0
321	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	516.84	12/2011 12/2011	03/2012	3(O) 3(R)	0/0
322	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	- -	0/0
323	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	427.89	375.30	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
324	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]JR,Tamil Nadu	09/2007	404.19 -	900.00	238.01	- -	-	- -	0/0
325	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,228.31	06/2011 06/2011	06/2011	0(O) 0(R)	0/0
326	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	12(O) 0(R)	0/0
327	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	118.87	- -	03/2012	- -	0/0
328	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	411.22	447.44	03/2012 03/2012	03/2012	0(O) 0(R)	0/0
329	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	840.32	571.01	02/2009 -	03/2012	37(O) -	0/0
330	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	340.08	07/2012 07/2012	07/2012	0(O) 0(R)	0/0
331	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	529.88	37.89	- -	-	- -	0/0
332	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	93.06	- -	03/2014	- -	0/0
333	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,078.41	12/2008 -	03/2014	63(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
334	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	239.06	- -	03/2015	- -	0/0
335	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.45	03/2015 -	03/2015	0(O) -	0/0
336	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	94.28	03/2016 -	03/2016	0(O) -	0/0
337	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	5.24	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
338	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	16.65	03/2016 -	03/2016	0(O) -	0/0
339	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	13.85	03/2016 -	06/2016	3(O) -	0/0
340	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	404.40	03/2008 06/2008	06/2008	3(O) 0(R)	0/0
341	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	324.21	03/2009 12/2009	03/2011	24(O) 15(R)	0/0
342	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	227.13	02/2010 -	12/2015	70(O) -	0/0
343	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,178.15	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
344	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	820.32	551.10	- -	03/2012	- -	0/0
345	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	135.87	12/2010 12/2010	12/2010	0(O) 0(R)	0/0
346	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	731.78	- -	03/2013	- -	0/0
347	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	211.08	12/2007 03/2010	12/2010	36(O) 9(R)	0/0
348	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	689.00	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
349	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,382.73	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
350	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	247.14	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
351	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	209.64	03/2011 -	03/2012	12(O) -	0/0
352	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	223.17	- -	-	- -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
353	RANCHI-LOHARDAGA(GC).SER - [220100214]SER,Jharkhandd	04/1997	194.07	456.45	278.64	06/2004	12/2012	102(O)	0/0
354	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70	1,717.29	1,073.81	-	03/2013	-	0/0
355	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	329.74	04/2003	03/2010	83(O)	0/0
356	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38	476.68	512.37	02/2010	02/2011	12(O)	0/0
357	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	639.97	176.98	03/1998	08/2005	89(O)	0/0
358	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00	482.70	254.35	03/2013	03/2013	0(O)	0/0
359	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	603.04	59.09	03/2012	03/2013	12(O)	0/0
360	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	216.05	03/2010	03/2012	24(O)	0/0
361	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	3,380.57	52.63	12/2015	12/2015	0(O)	0/0
362	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92	258.60	229.37	03/2011	03/2011	0(O)	0/0
363	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	62.47	02/2015	02/2015	0(O)	0/0
364	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23	516.23	172.89	03/2014	03/2014	0(O)	0/0
365	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96	810.78	108.35	-	03/2013	-	0/0
366	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97	723.71	400.52	06/2005	06/2015	120(O)	0/0
367	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96	762.33	482.90	-	02/2012	-	0/0
368	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	110.72	-	-	-	0/0
369	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	34.14	-	-	-	0/0
370	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	495.55	-	-	-	0/0
371	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69	3,176.10	3,021.15	12/2006	08/2010	44(O)	0/0
372	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73	167.73	41.50	03/2012	03/2012	0(O)	0/0
373	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00	20,000.00	8,035.01	03/2001	12/2017	201(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
374	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	819.40	114.31	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
375	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	276.81	03/2014 -	03/2014	0(O) -	0/0
376	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	158.16	- 03/2010	-	- -	0/0
	Total		65,286.30 -	134,791.49	59,357.04				1/1
Road Transport & Highways									
377	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	163.90	05/2013 -	03/2014	10(O) -	0/0
378	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
379	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	129.80	02/2014 -	02/2014	0(O) -	0/0
380	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	15.15	02/2014 -	04/2014	2(O) -	0/0
381	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	20.75	04/2014 -	04/2014	0(O) -	0/0
382	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	71.58	08/2014 -	08/2014	0(O) -	0/0
383	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,079.00	06/2013 -	06/2013	0(O) -	0/0
384	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	32.08	09/2013 -	07/2014	10(O) -	0/0
385	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	425.70	08/2013 -	08/2013	0(O) -	0/0
386	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	293.00	07/2013 -	07/2013	0(O) -	0/0
387	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	143.90	09/2007 -	06/2013	69(O) -	0/0
388	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	06/2012	87(O) -	0/0
389	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	902.20	11/2012 -	06/2013	7(O) -	0/0
390	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	275.80	11/2008 -	06/2012	43(O) -	0/0
391	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	251.60	01/2009 -	06/2012	41(O) -	0/0
392	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.70	02/2012 -	04/2012	2(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
393	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	182.07	02/2004	07/2012	101(O)	0/0
394	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	303.50	-	10/2013	-	0/1
395	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	237.20	06/2008	12/2012	54(O)	0/0
396	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	195.00	06/2008	06/2012	48(O)	0/0
397	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	224.10	06/2005	09/2012	87(O)	0/0
398	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	165.80	04/2010	12/2012	32(O)	0/0
399	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	1,438.00	-	03/2013	-	0/3
400	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	12/2013	46(O)	0/0
401	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	523.60	03/2013	03/2013	0(O)	0/0
402	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	-	-	12/2013	-	0/1
403	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	845.80	05/2013	05/2013	0(O)	0/0
404	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	231.90	10/2011	03/2014	29(O)	0/0
405	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	628.10	10/2011	06/2013	20(O)	0/0
406	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	267.40	06/2008	06/2012	48(O)	0/0
407	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.20	10/2008	12/2012	50(O)	0/0
408	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	577.70	05/2010	12/2012	31(O)	0/0
409	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	293.20	07/2013	07/2013	0(O)	0/0
410	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
411	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	207.90	-	06/2013	-	1/1
412	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	209.80	06/2008	06/2012	48(O)	0/0
413	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	132.10	05/2008	06/2012	49(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
414	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	251.80	09/2010	12/2012	27(O)	0/0
415	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00	485.00	40.61	08/2013	08/2013	0(O)	0/0
416	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	533.80	01/2011	06/2012	17(O)	0/0
417	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	357.40	09/2008	12/2012	51(O)	0/0
418	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
419	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	201.66	112.00	09/2008	06/2012	45(O)	0/0
420	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	263.96	02/2004	06/2012	100(O)	0/0
421	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	303.60	09/2007	06/2012	57(O)	0/0
422	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	1,141.00	483.10	08/2013	08/2013	0(O)	0/0
423	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	805.10	10/2009	06/2012	32(O)	0/0
424	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	192.90	04/2008	12/2012	56(O)	0/0
425	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	129.50	04/2008	12/2012	56(O)	0/0
426	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	302.70	10/2009	12/2012	38(O)	0/0
427	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	494.30	12/2009	12/2012	36(O)	0/0
428	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	1,238.00	09/2012	09/2012	0(O)	0/0
429	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	2,406.00	10/2011	06/2012	8(O)	0/0
430	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	475.60	03/2005	04/2012	85(O)	0/0
431	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	269.90	09/2007	06/2012	57(O)	0/0
432	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	258.60	02/2009	03/2013	49(O)	0/0
433	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	32.51	07/2009	04/2014	57(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
434	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	21.56	09/2007	04/2014	79(O)	0/0
435	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	180.59	08/2004	06/2012	94(O)	0/0
436	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	171.00	08/2004 07/2010	06/2012	94(O) 23(R)	0/0
437	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	758.60	01/2013	01/2013	0(O)	0/0
438	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	1,065.00	-	03/2013	-	2/2
439	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,416.00	10/2012	10/2012	0(O)	0/0
440	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	506.40	05/2012	05/2012	0(O)	0/0
441	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00	325.00	296.70	05/2013	02/2014	9(O)	0/0
442	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
443	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
444	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	486.50	09/2008	06/2012	45(O)	0/0
445	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	436.70	09/2009	12/2012	39(O)	0/0
446	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	536.00	333.90	01/2014	01/2014	0(O)	0/0
447	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	838.20	12/2012	12/2012	0(O)	0/0
448	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	279.30	10/2008	09/2012	47(O)	0/0
449	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	285.60	10/2008	06/2012	44(O)	0/0
450	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	644.80	-	03/2013	-	0/1
451	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	917.50	05/2012	05/2012	0(O)	0/0
452	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	185.50	06/2010	10/2012	28(O)	0/0
453	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.80	09/2009	10/2012	37(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
454	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	261.90	10/2008 -	04/2012	42(O) -	0/0
455	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	85.39	11/2008 -	07/2013	56(O) -	0/0
456	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	48.94	04/2009 -	07/2013	51(O) -	0/0
457	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	6.00	11/2008 -	01/2014	62(O) -	0/0
458	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	96.26	04/2009 -	03/2013	47(O) -	0/0
459	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	835.00	1,069.00	06/2012 -	06/2012	0(O) -	0/0
460	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,255.00	06/2013 -	06/2013	0(O) -	0/0
461	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
462	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	272.50	06/2008 -	06/2012	48(O) -	0/0
463	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2012	42(O) -	0/0
464	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	235.50	04/2008 -	12/2012	56(O) -	0/0
465	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	188.90	06/2008 -	06/2012	48(O) -	0/0
466	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	273.10	06/2008 -	06/2012	48(O) -	0/0
467	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	06/2015	0(O) -	0/0
468	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00 -	441.00	947.20	- -	04/2012	- -	0/0
469	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	246.00	06/2011 06/2011	06/2012	12(O) 12(R)	0/2
470	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27(O) -	0/0
471	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013	0(O) -	0/0
472	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	367.00	03/2008 -	06/2012	51(O) -	0/0
473	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	700.90	10/2014 -	10/2014	0(O) -	0/0
474	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	179.00	05/2008 -	08/2012	51(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
475	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00	574.00	58.67	03/2014	03/2014	0(O)	0/0
476	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	671.30	496.20	02/2013	02/2013	0(O)	0/0
477	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	1,141.00	07/2012	07/2012	0(O)	0/0
478	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	747.80	03/2013	03/2013	0(O)	0/0
479	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	3,337.00	11/2011	06/2012	7(O)	0/0
480	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0
481	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
482	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	297.80	10/2008	12/2012	50(O)	0/0
483	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	229.91	248.00	10/2008	09/2012	47(O)	0/0
484	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	581.30	11/2013	11/2013	0(O)	0/0
485	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya pradesh	12/2003	203.43	203.43	223.90	10/2008	12/2012	50(O)	0/0
486	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30	151.30	180.20	10/2008	05/2012	43(O)	0/0
487	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2012	16(O)	0/0
488	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	209.80	03/2013	03/2013	0(O)	0/0
489	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	195.20	09/2007	06/2012	57(O)	0/0
490	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	177.70	07/2008	12/2012	53(O)	0/0
491	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
492	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	4.93	12/2013	12/2013	0(O)	0/0
493	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	1,535.00	563.40	05/2014	05/2014	0(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
494	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
495	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	491.20	03/2008	05/2012	50(O)	0/0
496	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	109.99	04/2004	07/2012	99(O)	0/0
497	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,639.00	08/2011	06/2012	10(O)	0/0
498	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	581.50	06/2009	11/2012	41(O)	0/0
499	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	691.90	07/2010	03/2013	32(O)	0/0
500	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	361.30	11/2013	11/2013	0(O)	0/0
501	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
502	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	55.89	05/2013	05/2013	0(O)	0/0
503	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	-	04/2013	-	2/2
504	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	383.20	12/2008	04/2012	40(O)	0/0
505	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00	2,848.00	485.80	03/2014	03/2014	0(O)	0/0
506	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J and K	12/2003	193.09	166.30	184.90	03/2008	05/2012	50(O)	0/0
507	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27	193.10	161.40	03/2008	05/2012	50(O)	0/0
508	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.71	11/2012	11/2012	0(O)	0/0
509	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	247.70	07/2013	07/2013	0(O)	0/0
Total			79,244.48	81,045.31	57,020.34				5/13
Shipping & Ports									
510	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 06/2011	06/2012	14(O) 12(R)	0/0
511	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	344.33	09/2012	09/2012	0(O)	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
512	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	1,143.89	03/2012 -	04/2012	1(O) -	0/0
513	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	241.50	262.80	09/2011 -	04/2012	7(O) -	0/0
514	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	106.93	12/2012 -	12/2012	0(O) -	0/0
515	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8(O) 0(R)	0/0
516	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 06/2012	06/2012	12(O) 0(R)	0/0
517	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O) -	0/0
518	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O) -	0/0
519	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	724.00	12/2010 -	12/2012	24(O) -	0/0
520	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
521	CONSTRUCTION OF Berthing and Allied Facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
522	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	10/2008	0(O) -	0/0
523	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	01/2009	13(O) 0(R)	0/0
524	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	399.13	-	08/2010 -	-	- -	0/0
525	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	- -	0/0
526	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O) -	0/0
527	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	196.25	-	06/2006 09/2011	09/2011	63(O) 0(R)	0/0
528	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
529	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	0(O) -	0/0
530	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 298.17	373.22	336.26	04/2009 11/2009	02/2011	22(O) 15(R)	0/0
531	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40 -	2,427.40	829.01	10/2008 -	10/2008	0(O) -	0/0
532	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O) -	0/0
533	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST, Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	07/2014	14(O) -	0/0
Total			18,511.36 -	19,421.43	5,128.63				0/0
<u>Telecommunications</u>									
534	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2012	41(O) -	0/0
535	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	08/2011	54(O) 8(R)	0/0
536	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2011	03/2012	61(O) 12(R)	0/0
537	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	21.80	10/2010 03/2012	07/2012	21(O) 4(R)	0/0
538	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	- -	0/0
539	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	- -	0/0
540	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL, Punjab	02/2008	373.94 -	373.94	227.28	12/2008 -	06/2012	42(O) -	0/0
541	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL, Orissa	11/2007	277.34 -	277.34	-	03/2009 -	-	- -	0/0
542	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL, Madhya pradesh	11/2009	916.70 930.60	930.60	757.02	11/2010 -	03/2012	16(O) -	0/0
543	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL, Gujarat	08/2008	868.00 -	868.00	366.90	08/2009 -	06/2012	34(O) -	0/0

Sector Wise Details

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
544	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0
545	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	06/2012	39(O)	0/0
546	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
547	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
548	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	80.47	12/2005 03/2008	04/2012	76(O) 49(R)	0/0
549	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009	06/2012	36(O)	0/0
	Total		7,130.82	7,247.12	2,031.42				0/0
	Urban Development								
550	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	12/2013	24(O)	6/6
551	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
552	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	144.61	03/2016	03/2016	0(O)	0/0
553	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	2,412.18				6/6
	Water Resources								
554	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			724,460.43	844,195.74	377,551.83				860/2457

Sector wise current status of projects on theFlash Report


Water Resources

I. Current Status:

Number of Projects	1
Number of Projects Delayed	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 1 project, 1 project are delayed .



III. Investment Scenario

The Total Original cost of implementation of 1 projects when sanctioned, was of the order of Rs. 542.9 crore but this was subsequently revised to Rs. 1187 crore implying a cost overrun of 118.6%. The expenditure incurred on these projects till March, 2012 is Rs. 35.49 crore, which is 3% of the revised cost of the projects.

Figures are in Rs. Crore

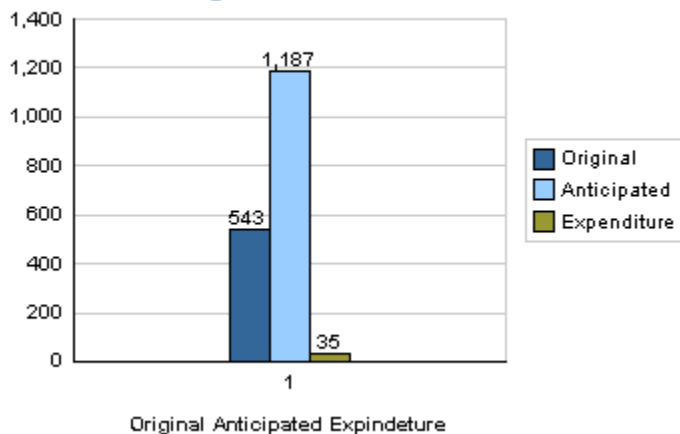

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

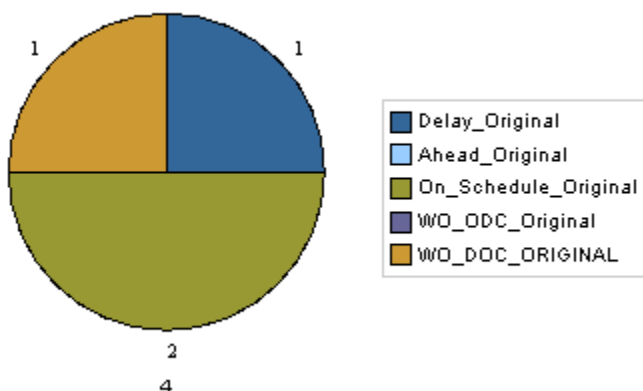

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till March, 2012 is Rs. 2412.18 crore, which is 4.9% of the revised cost of the projects.

Figures are in Rs. Crore

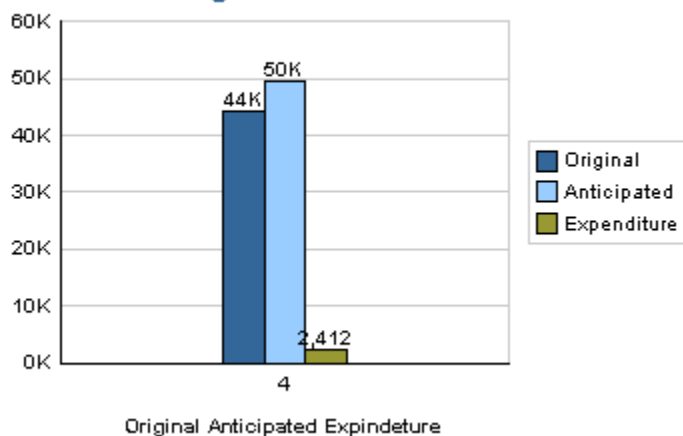

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects 16

Number of Projects Delayed 9

Number of Projects Without Date Of Commissioning 7

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 9 projects are delayed .7 projects do not have fixed dates of commissioning.

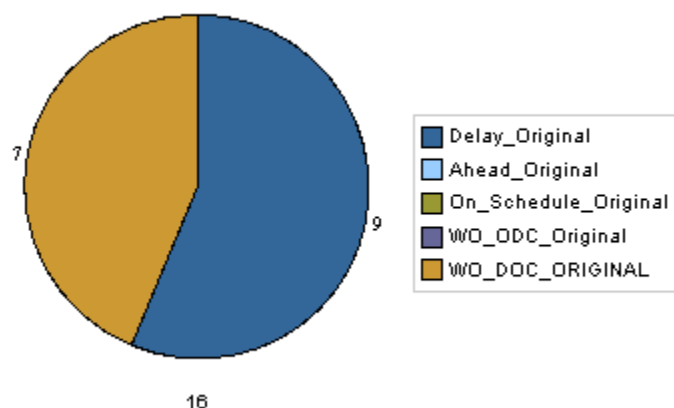

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 7130.82 crore but this was subsequently revised to Rs. 7247.12 crore implying a cost overrun of 1.6%. The expenditure incurred on these projects till March, 2012 is Rs. 2031.42 crore, which is 28% of the revised cost of the projects.

Figures are in Rs. Crore

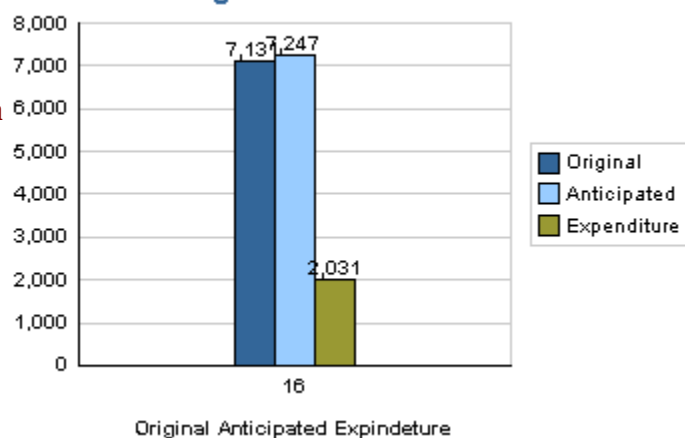

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	24
Number of Projects On Schedule	5
Number of Projects Delayed	12

Number of Projects Without Date Of Commissioning	7
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 24 projects, 5 projects are on schedule and 12 projects are delayed .7 projects do not have fixed dates of commissioning.

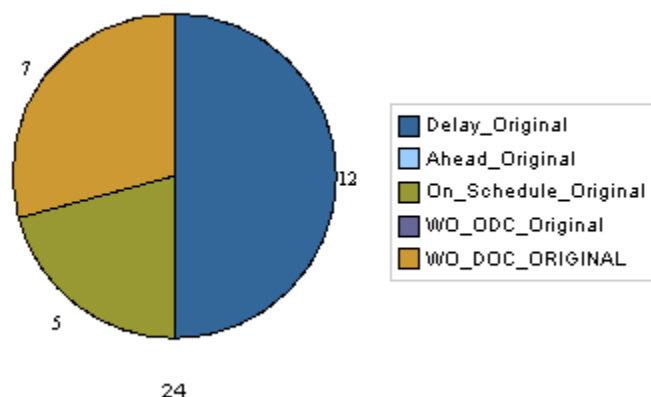

III. Investment Scenario

The Total Original cost of implementation of 24 projects when sanctioned, was of the order of Rs. 18511.36 crore but this was subsequently revised to Rs. 19421.43 crore implying a cost overrun of 4.9%. The expenditure incurred on these projects till March, 2012 is Rs. 5128.63 crore, which is 26.4% of the revised cost of the projects.

Figures are in Rs. Crore

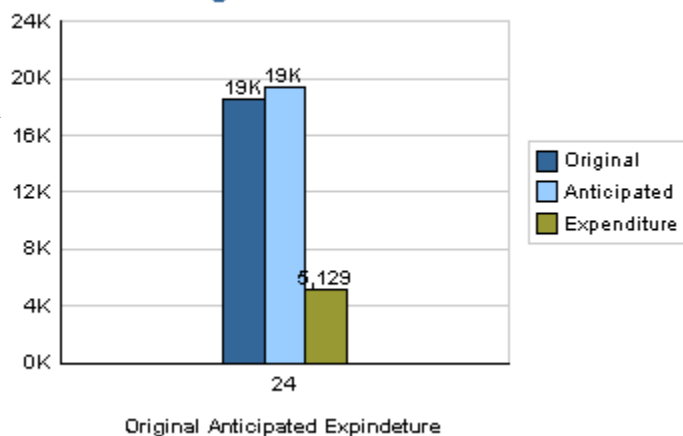

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	134
Number of Projects On Schedule	44
Number of Projects Delayed	81

Number of Projects Without Original Date of Commissioning	8
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 133 projects, 44 projects are on schedule and 81 projects are delayed .8 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

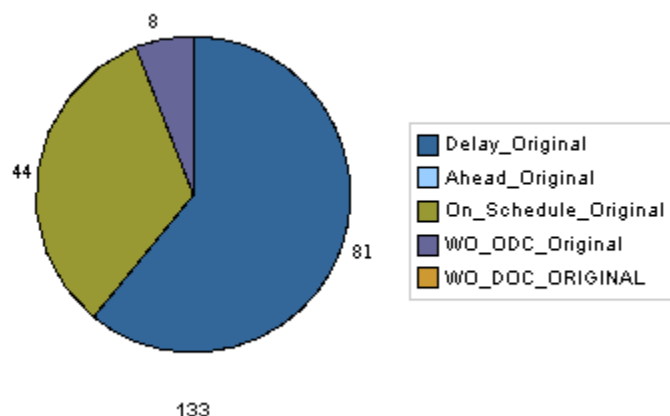

III. Investment Scenario

The Total Original cost of implementation of 133 projects when sanctioned, was of the order of Rs. 79244.48 crore but this was subsequently revised to Rs. 81045.31 crore implying a cost overrun of 2.3%. The expenditure incurred on these projects till March, 2012 is Rs. 57020.34 crore, which is 70.4% of the revised cost of the projects.

Figures are in Rs. Crore

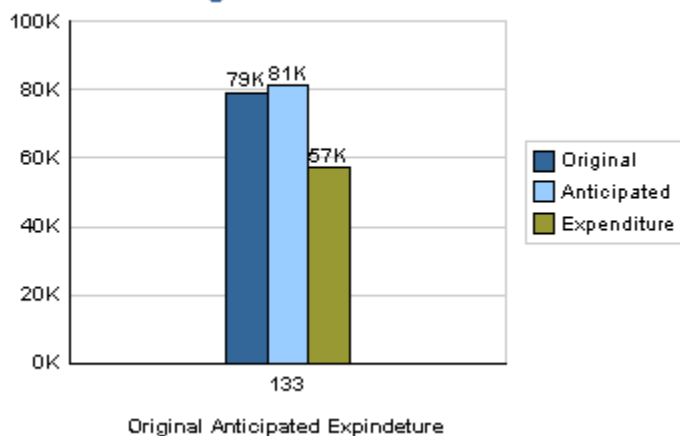

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	131
Number of Projects On Schedule	25
Number of Projects Delayed	34
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	15
Number of Projects Without Date Of Commissioning	55

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 131 projects, 2 projects are ahead of schedule, 25 projects are on schedule and 34 projects are delayed. 55 projects do not have fixed dates of commissioning. 15 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

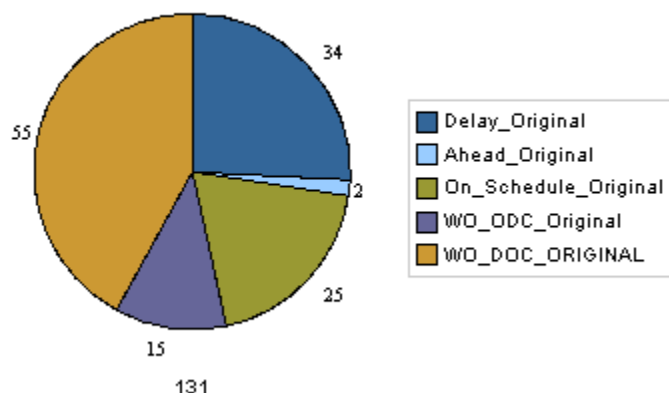

III. Investment Scenario

The Total Original cost of implementation of 131 projects when sanctioned, was of the order of Rs. 65286.3 crore but this was subsequently revised to Rs. 134791.49 crore implying a cost overrun of 106.5%. The expenditure incurred on these projects till March, 2012 is Rs. 59357.04 crore, which is 44% of the revised cost of the projects.

Figures are in Rs. Crore

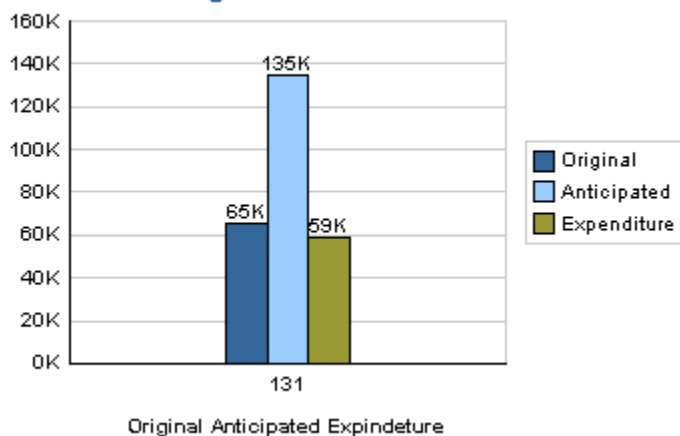

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	101
Number of Projects On Schedule	49
Number of Projects Delayed	50
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 101 projects, 1 project are ahead of schedule, 49 projects are on schedule and 50 projects are delayed .1 project do not have fixed dates of commissioning.

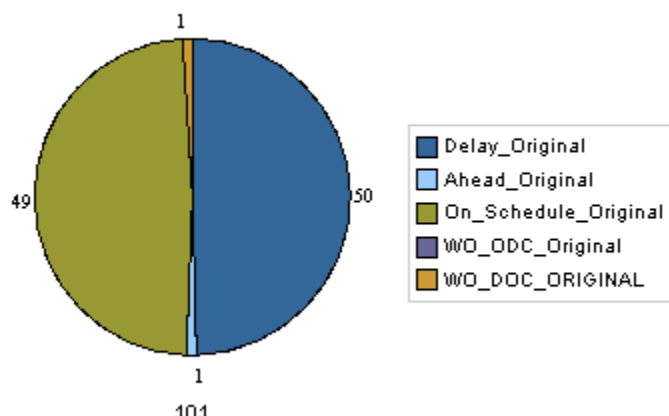

III. Investment Scenario

The Total Original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 208284.36 crore but this was subsequently revised to Rs. 223398.21 crore implying a cost overrun of 7.3%. The expenditure incurred on these projects till March, 2012 is Rs. 100309.31 crore, which is 44.9% of the revised cost of the projects.

Figures are in Rs. Crore

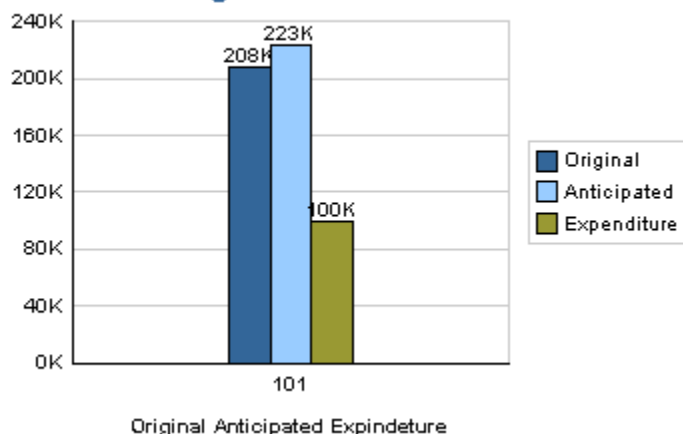

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	61
Number of Projects On Schedule	17
Number of Projects Delayed	38
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 61 projects, 1 project are ahead of schedule, 17 projects are on schedule and 38 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

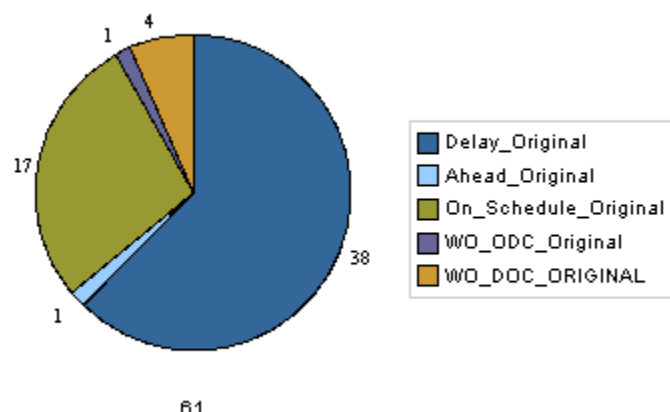

III. Investment Scenario

The Total Original cost of implementation of 61 projects when sanctioned, was of the order of Rs. 145017.77 crore but this was subsequently revised to Rs. 152886.87 crore implying a cost overrun of 5.4%. The expenditure incurred on these projects till March, 2012 is Rs. 67696.95 crore, which is 44.3% of the revised cost of the projects.

Figures are in Rs. Crore

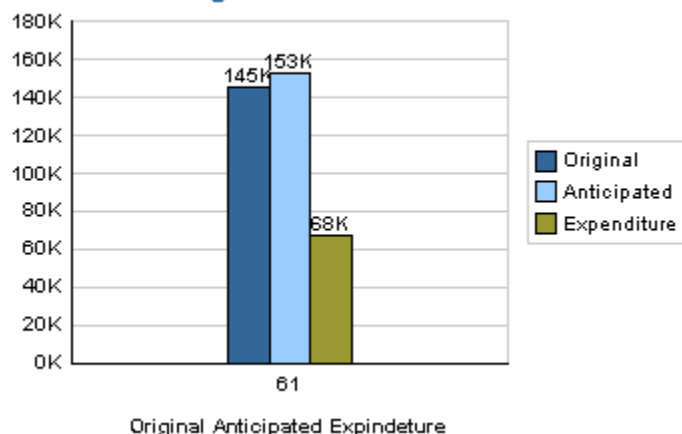

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	16
Number of Projects On Schedule	5
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 5 projects are on schedule and 10 projects are delayed .1 project do not have fixed dates of commissioning.

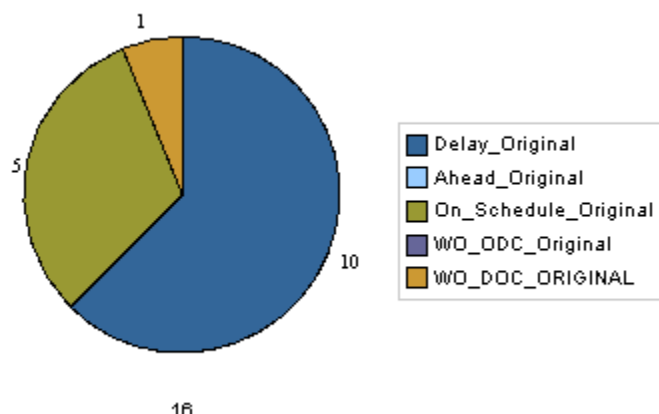

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 65244.82 crore but this was subsequently revised to Rs. 71412.36 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till March, 2012 is Rs. 39595.77 crore, which is 55.4% of the revised cost of the projects.

Figures are in Rs. Crore

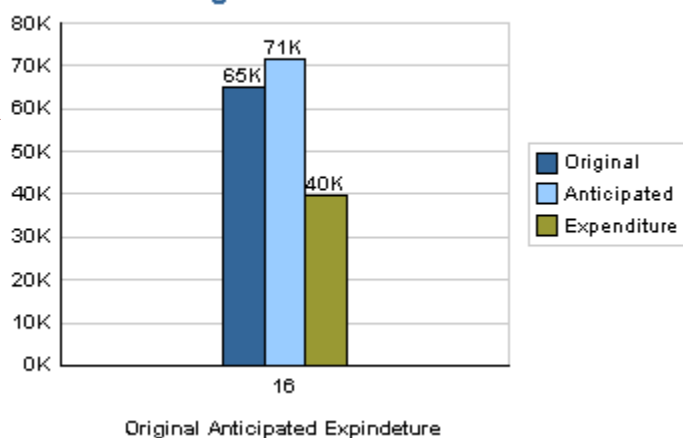

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule and 2 projects are delayed.

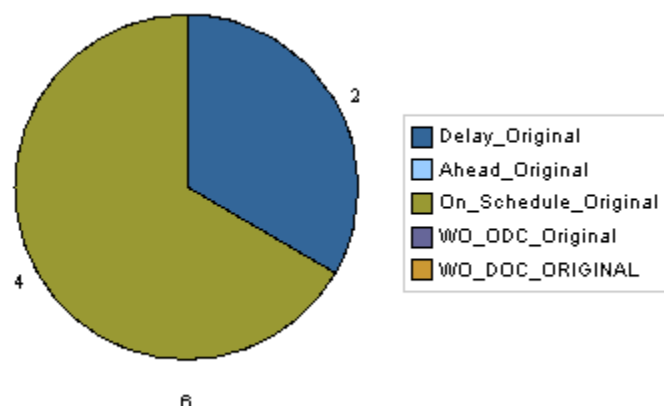

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till March, 2012 is Rs. 2197.8 crore, which is 41.3% of the revised cost of the projects.

Figures are in Rs. Crore

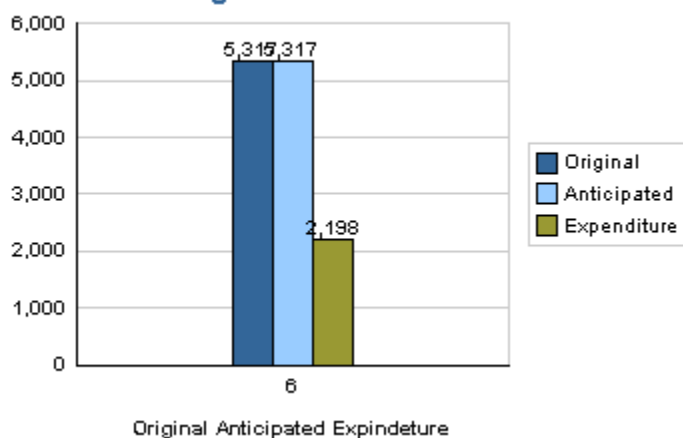

Sector wise current status of projects on theFlash Report


Coal

I. Current Status:

Number of Projects	50
Number of Projects On Schedule	31
Number of Projects Delayed	19

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 50 projects, 31 projects are on schedule and 19 projects are delayed .

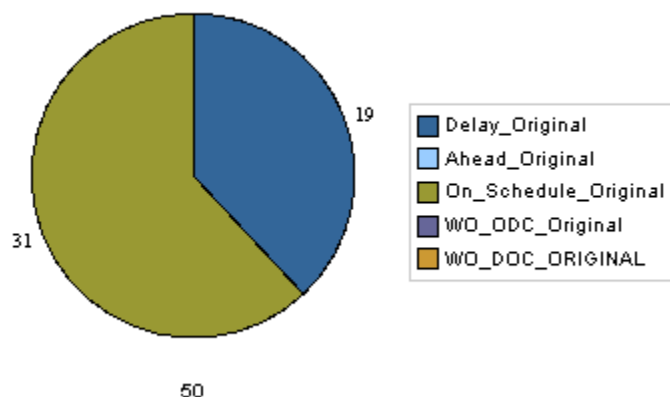

III. Investment Scenario

The Total Original cost of implementation of 50 projects when sanctioned, was of the order of Rs. 33604.55 crore but this was subsequently revised to Rs. 37053.1 crore implying a cost overrun of 10.3%. The expenditure incurred on these projects till March, 2012 is Rs. 11667 crore, which is 31.5% of the revised cost of the projects.

Figures are in Rs. Crore

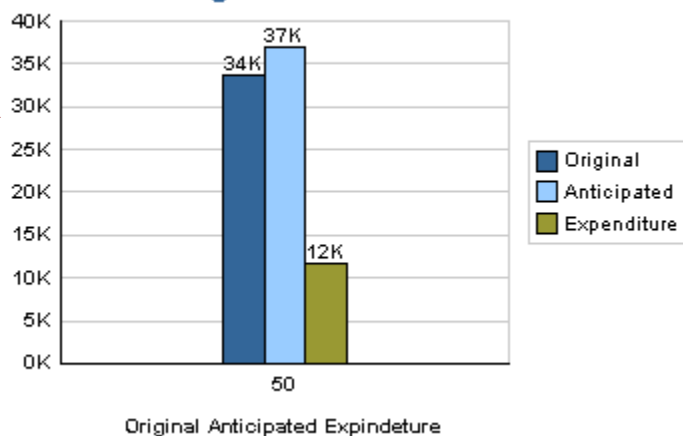

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

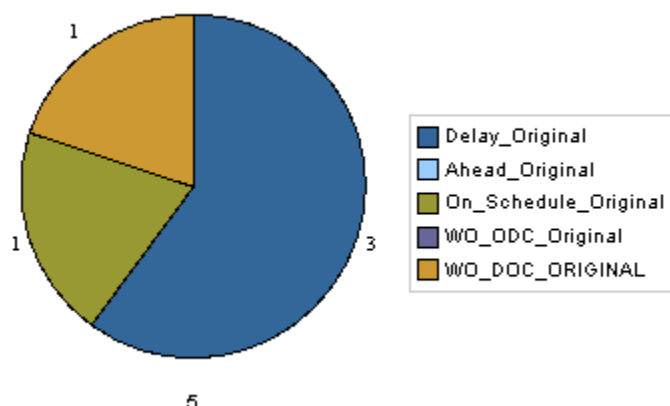

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till March, 2012 is Rs. 4128.55 crore, which is 73.6% of the revised cost of the projects.

Figures are in Rs. Crore

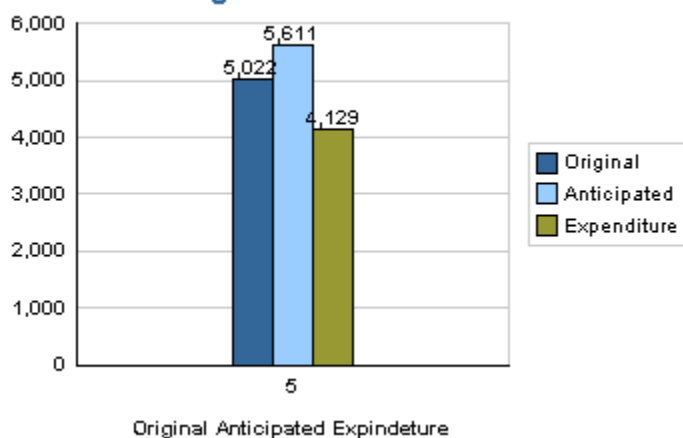

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 4

Number of Projects Without Date Of Commissioning 1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 4 projects are delayed .1 project do not have fixed dates of commissioning.

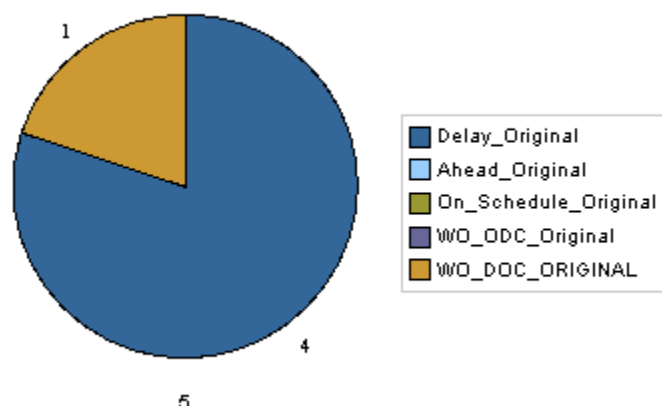

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 46386.29 crore implying a cost overrun of 11.6%. The expenditure incurred on these projects till March, 2012 is Rs. 21460.84 crore, which is 46.3% of the revised cost of the projects.

Figures are in Rs. Crore

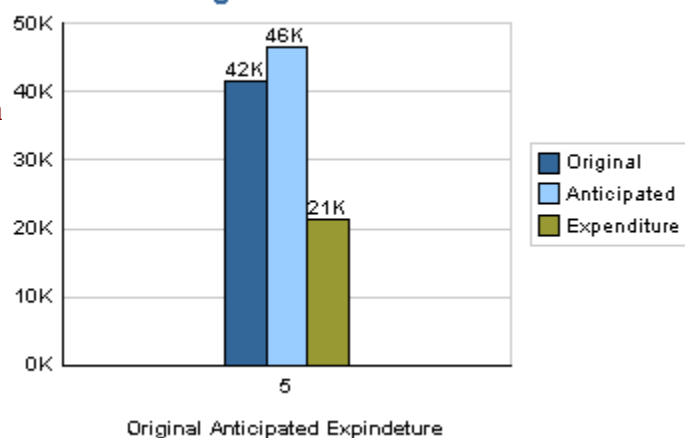

ANNEXURES

CENTRAL SECTOR PROJECTS as on 31-03-2012

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	36	31031.62	37863.82	20556.12
2	Arunachal Pr.	4	9512.22	14153.62	7929.63
3	Assam	37	23895.78	35508.89	21672.37
4	Bihar	30	29665.00	34323.89	22402.95
5	Chhatisgarh	25	52927.04	56158.39	19037.92
6	Delhi	3	37985.00	37965.41	211.81
7	Goa	1	335.61	335.61	108.57
8	Gujarat	25	32377.31	32630.32	6655.63
9	Haryana	10	5795.35	7611.84	6977.79
10	Himachal Pr.	6	14761.20	17455.42	13358.59
11	J and K	10	14019.35	33312.44	12186.44
12	Jharkhandd	22	14396.48	15999.88	7149.95
13	Karnataka	25	30657.64	38935.96	18947.20
14	Kerala	6	5711.17	6502.72	1781.42
15	Madhya pradesh	24	16759.45	17053.92	7754.50
16	Maharashtra	47	68515.10	81772.11	43828.76
17	Manipur	1	727.56	3056.85	679.56
18	Meghalaya	2	762.00	762.00	463.70
19	Mizoram	3	1901.69	4220.75	611.35
20	Multi State	94	125156.83	130167.08	50119.64
21	Nagaland	1	850.00	850.00	8.45
22	Orissa	27	54277.41	57448.40	25778.01
23	Punjab	6	4384.20	5314.23	3177.13
24	Rajasthan	13	24032.21	24026.83	7182.04
25	Sikkim	2	1648.94	3690.03	235.47
26	Tamil Nadu	35	52241.33	61099.83	36679.16
27	Tripura	3	1522.39	2053.23	630.85
28	Uttar Pradesh	25	18333.91	22339.45	11530.34
29	Uttaranchal	5	9815.87	11738.42	5053.88
30	West Bengal	26	40460.77	49844.40	24842.60
TOTAL		554	724460.43	844195.74	377551.83

LIST OF PROJECTS HAVING EXPENDITURE MORE THAN COST as on 31-03-2012

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	BHAVNI	3492.00	0.00	3577.60
2	KUDANKULAM APP (NPCIL)	Atomic Energy	NPCIL	13171.00	0.00	14380.00
3	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	Petroleum	HPCL	224.00	299.00	312.61
4	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	NHPC	768.92	0.00	1454.67
5	KOTESHWAR HEP (THDC)	Power	THDCL	1301.56	0.00	2618.18
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	NHPC	1061.38	0.00	1102.86
7	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	PGCIL	297.37	297.91	310.93
8	CHAMERA, STAGE-III (NHPC)	Power	NHPC	1405.63	0.00	1794.22
9	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL)	Power	PGCIL	1779.29	0.00	1791.78
10	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	NHPC	611.01	0.00	723.13
11	GUNA-ETAWAH (NCR), NL	Railways	NCR	158.77	432.46	558.07
12	CALICUT-MANGALORE (DL) (SR)	Railways	SR	240.00	0.00	599.40
13	KARUR-SALEM (NL), SR	Railways	SR	155.55	229.88	703.73
14	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	Railways	ECR	491.19	1099.20	1212.31
15	CHANDIGARH-LUDHIANA (NEW BG LINE), NR	Railways	(NR)	248.44	576.27	856.18
16	BILASPUR-URKURA (DL)	Railways	RVNL	151.52	0.00	309.21
17	RAICHUR-GUNTAKAL (DL) (SCR)	Railways	RVNL	136.62	0.00	211.08
18	JAYNAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	Railways	ECR	233.00	501.69	603.60
19	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES, NEFR	Railways	NEFR	1000.00	1500.00	2382.73
20	MANDARHILL-DUMKA-RAMPURHAT (NL), ER	Railways	ER	184.00	254.07	516.84
21	KODERMA GIRIDH (NL), ECR	Railways	ECR	371.36	0.00	397.67
22	LANJHIGARH-JUNAGARH NL (ECOR)	Railways	ECOR	100.00	142.98	200.08
23	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	Railways	M RTP	3125.20	4174.40	4228.31
24	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	114.01	332.92	375.30
25	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	SR	343.17	0.00	502.08
26	PALWAL-BHUTESWAR 3RD LINE DOUBLING (NCR) (RVNL)	Railways	RVNL	240.00	0.00	324.21
27	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR	Railways	(NR)	409.00	625.30	829.07
28	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	Railways	(NR)	2500.00	8000.00	8035.01
29	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	NER	323.40	0.00	471.31
30	KANPUR-KASGANJ-MATHURA (GC), NER	Railways	NER	395.00	1062.36	1252.53
31	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	NEFR	1676.31	0.00	3028.24
32	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	NEFR	156.00	0.00	231.82
33	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	NEFR	170.00	0.00	390.92
34	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	Railways	NEFR	733.00	0.00	1078.41
35	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	NCR	108.00	214.09	250.82
36	RAJPIPLA-ANKELASHWAR, WR (GC)	Railways	WR	196.97	0.00	209.64

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
37	AMRAVATI-NARKHER NL(CR)	Railways	CR	120.90	284.27	508.15
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	124.43	407.78	551.10
39	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	SR	100.00	0.00	495.55
40	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	SWR	295.00	412.91	483.14
41	KOTTUR-HARIHAR(NL),(SWR)	Railways	SWR	65.94	302.23	331.25
42	RANCHI-LOHARDAGA(GC),SER	Railways	SER	194.07	0.00	278.64
43	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	SCR	155.74	164.36	571.01
44	ELECTRIFICATION OF MORADABAD-ROZA	Railways	RE	129.17	0.00	227.48
45	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	RVNL	200.80	0.00	269.02
46	RENIGUNTA-GUNTAKAL(RE)	Railways	RVNL	168.34	0.00	329.74
47	RAJATGARH-BARANG(LD),ECOR	Railways	RVNL	166.16	0.00	247.14
48	REWARI-ROHTAK (NL),NR	Railways	(NR)	149.38	330.23	512.37
49	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	NEFR	915.70	0.00	1073.81
50	KATIHAR - JOGBANI (GC)(NEFR)	Railways	NEFR	100.00	492.98	725.17
51	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	NER	381.17	0.00	498.94
52	GADWAL - RAICHUR (NL), SCR	Railways	SCR	92.63	228.09	257.85
53	JIND-SONEPAT (NL),NR	Railways	(NR)	190.81	238.56	390.91
54	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	NHAI	240.00	0.00	285.60
55	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	NHAI	157.47	0.00	195.20
56	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	NHAI	367.49	0.00	453.68
57	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	NHAI	280.00	0.00	581.50
58	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	NHAI	941.00	0.00	1901.00
59	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	792.06	0.00	838.20
60	AMRITSAR-PATHANKOT	Road Transport & Highways	NHAI	705.00	0.00	902.20
61	Pune-sholapur,pkg1	Road Transport & Highways	NHAI	1110.00	0.00	1802.00

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
62	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	940.00	0.00	1141.00
63	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	835.00	0.00	1069.00
64	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	625.07	0.00	758.60
65	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	NHAI	190.00	0.00	251.60
66	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	NHAI	441.00	0.00	947.20
67	Bijapur-Hungund Section	Road Transport & Highways	NHAI	748.00	0.00	1438.00
68	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	1008.50	0.00	1079.00
69	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	NHAI	946.00	0.00	1065.00
70	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	NHAI	557.00	0.00	930.90
71	Chilkaluri pet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	NHAI	572.30	0.00	628.10
72	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	NHAI	1693.75	0.00	2639.00
73	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	NHAI	1673.70	0.00	2406.00
74	TRICHY - KORUR NH-67	Road Transport & Highways	NHAI	516.00	0.00	691.90

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
75	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER	Road Transport & Highways	NHAI	464.00	0.00	533.80
76	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	NHAI	263.27	0.00	263.96
77	Armur to kadloor yellareddy	Road Transport & Highways	NHAI	390.56	0.00	631.70
78	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	Road Transport & Highways	NHAI	229.91	0.00	248.00
79	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	NHAI	203.43	0.00	223.90
80	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	NHAI	151.30	0.00	180.20
81	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	NHAI	225.00	0.00	261.90
82	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	NHAI	264.72	0.00	272.50
83	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	NHAI	1108.00	0.00	3337.00
84	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	795.00	0.00	917.50
85	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	388.00	0.00	506.40
86	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	NHAI	168.00	0.00	457.30
87	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	NHAI	232.45	0.00	251.80

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
88	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	NHAI	300.93	0.00	302.70
89	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	NHAI	600.24	0.00	805.10
90	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	NHAI	332.94	0.00	357.40
91	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	NHAI	355.06	0.00	436.70
92	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	NHAI	275.00	0.00	279.30
93	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	NHAI	340.68	0.00	367.00
94	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	NHAI	340.00	0.00	486.50
95	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	NHAI	221.82	0.00	275.80
96	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	NHAI	200.00	0.00	273.10
97	NALBARI T BIJNI (AS-7)	Road Transport & Highways	NHAI	208.00	0.00	235.50
98	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	NHAI	245.00	0.00	491.20
99	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	NHAI	200.00	0.00	209.80
100	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	NHAI	251.03	0.00	297.80

SN	PROJECT	SECTOR	AGENCY	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
101	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	NHAI	227.00	0.00	383.20
102	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	NHAI	225.00	0.00	267.40
103	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	NHAI	486.00	0.00	577.70
104	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	NHAI	273.00	0.00	475.60
105	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	NHAI	275.00	0.00	303.60
106	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	NHAI	220.00	0.00	269.90
107	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	RVNL	245.67	298.17	336.26
108	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK CARRIERS	Shipping & Ports	SHIPP.	1061.96	1077.60	1143.89
109	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH03TYPE) AHTS VESSELS	Shipping & Ports	SHIPP.	241.50	0.00	262.80
110	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	RINL	230.00	0.00	246.84

Ahead of Schedule

S.No	Project	DOA	DOC Original	DOC Revised	DOC Anticipated	COST Original	Cost Anticipated
1	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY	3/2009	09/2012	05/2012	05/2012	3284	2174
2	BHAIRABI SAIRONG, NL, NEFR	4/2008	04/2014	N.A.	03/2014	619.34	2393.49
3	MAUDA TRANSMISSION SYSTEM	2/2010	10/2012	N.A.	04/2012	469.38	469.38
4	CONV.OF 1500V DC TRACTION TO 25 KV AC,CR	7/1996	06/2013	06/2012	06/2012	653.84	1302.12

LIST OF ON SCHEDULED PROJECTS as on 31-03-2012

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
1	GAGAN PROJECT	Civil Aviation	AAI	09/2008	06/2013	N.A.	06/2013	626.00	626.00
2	Muraidih UG Turn-key Project	Coal	BCCL	02/2011	04/2014	N.A.	04/2014	339.88	339.88
3	Moonidih XV Seam UG	Coal	BCCL	08/2011	04/2015	N.A.	04/2015	1230.27	1230.27
4	Purnadih OCP	Coal	CCL	07/2008	03/2013	N.A.	03/2013	210.98	210.98
5	KARMA OCP	Coal	CCL	06/2009	03/2014	N.A.	03/2014	162.46	162.46
6	Rajrappa RCE OCP	Coal	CCL	12/2009	03/2016	N.A.	03/2016	510.85	510.85
7	KANIHA OCP, MCL, (10.0 Mty)	Coal	MCL	12/2007	03/2013	03/2013	03/2013	457.77	457.77
8	ANANTA OC EXPANSION PH-III (15.0 Mty)	Coal	MCL	08/2008	03/2012	03/2012	03/2012	207.28	207.28
9	TALABIRA OCP	Coal	MCL	03/2008	03/2016	03/2016	03/2016	447.72	447.72
10	GOPAL PRASAD OCP	Coal	MCL	02/2008	03/2015	03/2015	03/2015	395.87	395.87
11	BHUBANESWARI OCP, MCL (20.0 Mty)	Coal	MCL	12/2007	03/2017	03/2017	03/2017	490.00	490.10
12	HINGULA OC-II EXP. PH-III (15 MTY)	Coal	MCL	11/2008	03/2013	03/2013	03/2013	475.93	479.63
13	NIGAH I OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI	Coal	NCL	10/2007	03/2012	N.A.	03/2012	259.40	259.40
14	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL)	Coal	NCL	06/2011	03/2018	03/2018	03/2018	1131.28	1131.28
15	BINA EXTN. PROJ(6.0 Mtpa)	Coal	NCL	11/2006	03/2014	03/2014	03/2014	168.97	168.97
16	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW)	Coal	NLC	06/2011	12/2015	N.A.	12/2015	5907.11	5907.11
17	SHANTIKHANI LONGWALL PROJ-SCCL	Coal	SCCL	10/2006	03/2012	N.A.	03/2012	249.03	249.03
18	JALAGAM VENGALA RAO OCP	Coal	SCCL	07/2011	03/2015	N.A.	03/2015	447.06	447.06
19	RCE OF INDARAM OCP(1.20 MTPA)	Coal	SCCL	07/2011	03/2015	N.A.	03/2015	162.76	162.76
20	RKP OCP PHASE-I	Coal	SCCL	03/2010	03/2015	N.A.	03/2015	209.78	209.78
21	JALLARAM SHAFT PROJECT	Coal	SCCL	03/2013	03/2013	N.A.	03/2013	467.78	467.78
22	Kistaram OCP	Coal	SCCL	11/2010	03/2015	N.A.	03/2015	242.29	242.29
23	JAGANNATHPUR OCP(3.00 MTY)	Coal	SECL	09/2008	03/2015	N.A.	03/2015	152.43	152.43
24	KARTALI (EAST) OCP(2.50 MTY)	Coal	SECL	07/2008	03/2014	N.A.	03/2014	178.44	178.44
25	AMLAI OC EXPANSION SECTOR 1.50 MTY	Coal	SECL	11/2009	03/2016	N.A.	03/2016	198.59	198.59
26	DIPKA EXPANSION OCP (SECL) (20-25 MTY)	Coal	SECL	07/2005	03/2014	N.A.	03/2014	1268.53	1943.66
27	GEVRA EXPANSION OCP (SECL) (25-35) MTY	Coal	SECL	07/2005	03/2014	N.A.	03/2014	1667.55	2675.67
28	MANIKPUR OC EXPANTION (3.50 MTY)	Coal	SECL	11/2009	03/2014	03/2014	03/2014	321.42	321.50
29	CHURCHA RO UG (1.35MTY)	Coal	SECL	06/2008	03/2014	03/2014	03/2014	462.35	462.35
30	KUSMUNDA EXPN.OCP(SECL)(10-15MTY)	Coal	SECL	06/2006	03/2013	03/2013	03/2013	737.65	1188.31
31	PELMA OCP(10.00MTY)	Coal	SECL	07/2008	03/2015	N.A.	03/2015	448.32	448.32
32	Batura OCP (2.0 MTY)	Coal	SECL	09/2008	03/2015	N.A.	03/2015	203.82	203.82
33	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	Fertilisers	NFL	01/2010	01/2013	N.A.	01/2013	1294.19	1294.19

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
34	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	Fertilisers	NFL	01/2010	01/2013	01/2013	01/2013	1478.63	1478.63
35	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT	Fertilisers	NFL	01/2010	01/2013	N.A.	01/2013	1292.84	1292.84
36	THAL AMMONIA REVAMP PROJECT	Fertilisers	RCF	01/2009	04/2012	04/2012	04/2012	488.75	488.75
37	Assam gas Cracker project	Petrochemicals	BCPL	04/2006	12/2013	12/2013	12/2013	5460.61	8920.00
38	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	BPCL	04/2008	04/2013	04/2013	04/2013	825.00	1827.00
39	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA	Petroleum	GAIL	08/2010	02/2014	N.A.	02/2014	8140.00	8140.00
40	Butadiene Extraction Unit(BDEU) at Panipat	Petroleum	IOCL	11/2009	02/2013	02/2013	02/2013	341.50	341.50
41	Integrated crude Oil handling facilities at Paradip(2nd SPM)	Petroleum	IOCL	12/2009	06/2012	06/2012	06/2012	1492.33	1300.00
42	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	Petroleum	IOCL	07/2010	01/2013	N.A.	01/2013	1000.00	1000.00
43	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE	Petroleum	IOCL	08/2009	09/2012	09/2012	09/2012	1793.00	1400.00
44	Construction of tanks and blending facility at vadinar	Petroleum	IOCL	02/2009	09/2012	09/2012	09/2012	267.00	267.00
45	Polypropylene unit	Petroleum	Mangalore Refin	05/2009	07/2012	N.A.	07/2012	1803.78	1803.78
46	Wax Project	Petroleum	NRL	06/2010	12/2013	12/2013	12/2013	576.60	576.60
47	Ahmedabad Redevelopment	Petroleum	ONGC	11/2010	12/2014	N.A.	12/2014	1916.10	1916.10
48	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura	Petroleum	ONGC	07/2008	08/2012	N.A.	08/2012	288.04	288.04
49	Development of WO-16 Cluster Fields	Petroleum	ONGC	06/2010	01/2014	N.A.	01/2014	2523.00	2523.00
50	Construction of 6 ETPs	Petroleum	ONGC	03/2009	09/2012	N.A.	09/2012	302.26	302.26
51	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	Petroleum	ONGC	03/2011	05/2013	N.A.	05/2013	861.79	861.79
52	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP)	Petroleum	ONGC	06/2010	01/2014	N.A.	01/2014	202.94	202.94
53	Mehesana Redevelopment	Petroleum	ONGC	11/2010	04/2015	N.A.	04/2015	3823.00	3823.00
54	Ankleswar Redevelopment	Petroleum	ONGC	11/2010	12/2014	N.A.	12/2014	2189.63	2189.63
55	TUIRIAL HYDRO ELECTRIC PROJECT (60MW)	Power	NEEPCO	01/2011	01/2014	N.A.	01/2014	913.63	913.63
56	TRIPURA GAS BASED POWER PROJECT	Power	NEEPCO	07/2009	07/2013	07/2013	07/2013	421.01	623.44

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
57	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA MEGA POWER PROJECT	Power	PGCIL	12/2008	12/2012	N.A.	12/2012	7031.88	7031.88
58	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B	Power	PGCIL	03/2011	11/2013	N.A.	11/2013	1585.12	1585.12
59	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	2422.66	2422.66
60	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR TPS	Power	PGCIL	08/2010	04/2013	N.A.	04/2013	170.36	170.36
61	System Strengthening -XII of SR	Power	PGCIL	02/2010	06/2012	N.A.	06/2012	232.34	232.34
62	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A	Power	PGCIL	05/2010	01/2013	N.A.	01/2013	250.03	250.03
63	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI	Power	PGCIL	07/2010	07/2013	N.A.	07/2013	752.64	752.64
64	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH	Power	PGCIL	05/2011	05/2014	N.A.	05/2014	1961.87	1961.87
65	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN ORISSA-B	Power	PGCIL	12/2010	12/2013	N.A.	12/2013	2743.19	2743.19
66	Trans. System associated with PALLATANA GBPP & BPTS.	Power	PGCIL	02/2010	12/2012	N.A.	12/2012	2144.00	2144.00
67	System Strengthening in NR for SASAN & MUNDRA (UMPP)	Power	PGCIL	12/2009	08/2012	N.A.	08/2012	1216.83	1216.83
68	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-III	Power	PGCIL	11/2009	05/2012	N.A.	05/2012	1075.12	1075.12
69	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-PART A	Power	PGCIL	09/2010	03/2013	N.A.	03/2013	2074.86	2074.86
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX	Power	PGCIL	10/2010	01/2013	N.A.	01/2013	182.68	182.68
71	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	1719.52	1719.52
72	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM BHU	Power	PGCIL	04/2010	01/2015	N.A.	01/2015	4404.57	4404.57
73	System Strengthening -X of SR	Power	PGCIL	12/2009	04/2012	N.A.	04/2012	276.61	276.61
74	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT KALA IN UT DNH	Power	PGCIL	07/2011	07/2013	N.A.	07/2013	181.93	181.93

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
75	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	Power	PGCIL	08/2011	12/2013	N.A.	12/2013	1391.97	1391.97
76	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	Power	PGCIL	08/2011	10/2013	N.A.	10/2013	425.51	425.51
77	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH	Power	PGCIL	09/2011	12/2013	N.A.	12/2013	1366.34	1366.34
78	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power Madras Limited LT	Power	PGCIL	09/2011	09/2014	N.A.	09/2014	1940.13	1940.13
79	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A	Power	PGCIL	10/2011	11/2013	N.A.	11/2013	558.26	558.26
80	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH	Power	PGCIL	07/2011	07/2013	N.A.	07/2013	181.93	181.93
81	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM PART A	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	779.21	779.21
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII	Power	PGCIL	12/2010	08/2013	N.A.	08/2013	209.78	209.78
83	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD	Power	PGCIL	01/2012	01/2013	N.A.	01/2013	259.28	259.28
84	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH	Power	PGCIL	01/2012	01/2015	N.A.	01/2015	1422.85	1422.85
85	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH-PART-E	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	1746.65	1746.65
86	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV	Power	PGCIL	12/2011	08/2014	N.A.	08/2014	297.33	297.33
87	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED	Power	PGCIL	12/2011	02/2014	N.A.	02/2014	552.44	552.44
88	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH	Power	PGCIL	11/2011	07/2014	N.A.	07/2014	2127.51	2127.51
89	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL)	Power	PGCIL	08/2011	08/2014	N.A.	08/2014	1637.34	1637.34

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
90	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	Power	PGCIL	08/2011	12/2013	N.A.	12/2013	1391.97	1391.97
91	SYSTEM STRENGTHENING XIII OF SR GRID	Power	PGCIL	10/2011	06/2014	N.A.	06/2014	487.49	487.49
92	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1	Power	PGCIL	03/2012	06/2014	N.A.	06/2014	206.44	206.44
93	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH	Power	PGCIL	03/2012	06/2015	N.A.	06/2015	9569.76	9569.76
94	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS ASSOCIATED WITH SYSTEM STRENGTHENING COMMO	Power	PGCIL	03/2012	03/2014	N.A.	03/2014	213.78	213.78
95	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION	Power	PGCIL	03/2012	09/2014	N.A.	09/2014	198.63	198.63
96	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B	Power	PGCIL	02/2012	10/2014	N.A.	10/2014	1927.16	1927.16
97	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1	Power	PGCIL	02/2012	08/2014	N.A.	08/2014	324.33	324.33
98	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH	Power	PGCIL	02/2012	02/2015	N.A.	02/2015	1310.85	1310.85
99	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS	Power	PGCIL	02/2010	06/2012	N.A.	06/2012	215.86	215.86
100	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME	Power	PGCIL	03/2010	11/2012	N.A.	11/2012	965.58	965.58
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI	Power	PGCIL	08/2010	04/2013	N.A.	04/2013	1677.57	1677.57
102	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C	Power	PGCIL	03/2011	03/2014	N.A.	03/2014	2569.25	2569.25
103	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION GRID PART-II	Power	PGCIL	07/2009	06/2012	N.A.	06/2012	1736.36	1736.36
104	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	(NR)	07/1998	12/2012	N.A.	12/2012	248.44	1103.47
105	NANGALDAM-TALWARA(NL),NR	Railways	(NR)	03/1981	07/2012	07/2012	07/2012	37.68	730.00

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
106	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	ECR	04/1997	03/2012	03/2012	03/2012	100.00	411.22
107	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	ECR	04/1997	03/2012	03/2012	03/2012	233.00	903.56
108	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	ECR	04/1996	03/2012	03/2012	03/2012	114.01	427.89
109	DEOGHAR - SULTANGANJ (INL), ER	Railways	ER	04/2000	12/2012	12/2012	12/2012	138.00	607.09
110	Tinpahar - Sahibganj (ER)	Railways	ER	04/2008	03/2012	N.A.	03/2012	167.73	167.73
111	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER)	Railways	ER	04/1999	12/2012	N.A.	12/2012	207.52	207.52
112	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	Railways	M RTP	04/2006	06/2013	06/2013	06/2013	495.74	495.74
113	New Line from Dimapur to Zubza(Kohima) national project (NEFR)	Railways	NEFR	04/2006	03/2015	N.A.	03/2015	850.00	850.00
114	AGARTALA SABROOM, NL, NEFR	Railways	NEFR	04/2008	03/2014	N.A.	03/2014	813.34	1141.75
115	SEVOK RANGPO, NEFR	Railways	NEFR	04/2008	12/2015	N.A.	12/2015	1339.48	3380.57
116	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR)	Railways	NWR	04/2008	03/2014	N.A.	03/2014	653.19	653.19
117	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR)	Railways	NWR	04/2008	03/2014	N.A.	03/2014	516.23	516.23
118	Himmatnagar - Udaipur Gauge Canvession (NWR)	Railways	NWR	04/2008	03/2015	N.A.	03/2015	829.74	829.74
119	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT	Railways	RE	02/2008	03/2012	N.A.	03/2012	171.10	171.10
120	SUKINDA ROAD - ANGUL (NL)(ECOR)	Railways	RVNL	04/1998	02/2015	N.A.	N.A.	183.23	638.00
121	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh.	Railways	RVNL	04/2010	03/2016	N.A.	03/2016	2619.02	2619.02
122	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP)	Railways	RVNL	04/2010	03/2016	N.A.	03/2016	3951.98	3951.98
123	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	Railways	RVNL	04/1995	12/2012	N.A.	N.A.	304.00	968.60
124	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	SWR	04/1996	03/2012	03/2012	03/2012	157.00	262.82
125	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	Railways	SWR	04/2007	03/2013	N.A.	03/2013	482.00	482.70
126	Udhna-Jalgaon with electrification(doubling) (WR)	Railways	WR	04/2008	03/2014	N.A.	03/2014	1389.62	1389.62
127	Bhuj-Naliya(GC) with extension from naliyate vayor (WR)	Railways	WR	04/2008	03/2012	N.A.	03/2012	318.24	468.62

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
128	Ahmedabad-Himmatnagar-Udaipur (WR)	Railways	WR	04/2008	03/2013	N.A.	03/2013	394.13	394.14
129	Talegaon-amravati	Road Transport & Highways	NHAI	11/2009	11/2013	N.A.	11/2013	567.00	567.00
130	SAMAIKHALI - GANDHIDHAM	Road Transport & Highways	NHAI	09/2010	03/2013	N.A.	03/2013	805.39	805.39
131	Tirupati - Tiruthani - Chennai	Road Transport & Highways	NHAI	04/2011	10/2013	N.A.	10/2013	571.00	571.00
132	2 laning of Dindigul - Perigulam Theni- kumili	Road Transport & Highways	NHAI	09/2011	08/2013	N.A.	08/2013	485.00	485.00
133	Two laning of Trichy - Karaikudi and Trychi Bypass	Road Transport & Highways	NHAI	05/2010	05/2013	N.A.	05/2013	374.00	374.00
134	Kandla - Mundra port	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	953.88	953.88
135	2 Laning of Muzaffarpur - Sonbarsa	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	511.54	511.54
136	NASHRI CHANANI	Road Transport & Highways	NHAI	06/2010	06/2015	N.A.	06/2015	2159.00	2159.00
137	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	Road Transport & Highways	NHAI	07/2010	07/2015	N.A.	07/2015	1987.00	1987.00
138	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4	Road Transport & Highways	NHAI	09/2010	09/2013	N.A.	09/2013	1655.00	1655.00
139	Jaipur-Tonk-Deoli	Road Transport & Highways	NHAI	06/2010	12/2012	N.A.	12/2012	792.06	792.06
140	Pune-sholapur, pkg1	Road Transport & Highways	NHAI	11/2009	05/2012	N.A.	05/2012	1110.00	1110.00
141	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	NHAI	03/2005	07/2012	N.A.	07/2012	940.00	940.00

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
142	MP/Maharashtra Border-Dhula	Road Transport & Highways	NHAI	12/2009	06/2012	N.A.	06/2012	835.00	835.00
143	Indore-Jhabua-Gujrat/MP	Road Transport & Highways	NHAI	10/2010	04/2013	N.A.	04/2013	1175.00	1175.00
144	Hazaribagh-Ranchi	Road Transport & Highways	NHAI	08/2010	01/2013	N.A.	01/2013	625.07	625.07
145	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	511.54	511.54
146	4-LANNING OF CHAPRA-HAJIPUR	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	575.00	575.00
147	2-LANNING WITH PS MOTIHARI-RAXAUL	Road Transport & Highways	NHAI	10/2011	04/2014	N.A.	04/2014	375.09	375.09
148	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	Road Transport & Highways	NHAI	09/2011	03/2014	N.A.	03/2014	574.00	574.00
149	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	Road Transport & Highways	NHAI	11/2011	05/2014	N.A.	05/2014	1535.00	1535.00
150	VARANASI-AURANGABAD KM.786 TO KM.978.40	Road Transport & Highways	NHAI	09/2011	03/2014	N.A.	03/2014	2848.00	2848.00
151	2-LANNING OF SHILONG BYPASS	Road Transport & Highways	NHAI	02/2011	02/2014	N.A.	02/2014	226.00	226.00
152	JORBAT - BARAPANI	Road Transport & Highways	NHAI	01/2011	01/2014	N.A.	01/2014	536.00	536.00
153	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	Road Transport & Highways	NHAI	06/2011	06/2013	N.A.	06/2013	600.00	600.00
154	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	Road Transport & Highways	NHAI	09/2011	12/2013	N.A.	12/2013	1250.00	1250.00

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
155	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO KM.93.00	Road Transport & Highways	NHAI	06/2011	12/2013	N.A.	12/2013	535.00	535.00
156	GHAZIABAD-ALIGARH NH-91	Road Transport & Highways	NHAI	02/2011	08/2013	N.A.	08/2013	1141.00	1141.00
157	ROHTAK-BAWAL	Road Transport & Highways	NHAI	05/2011	11/2013	N.A.	11/2013	650.00	650.00
158	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport & Highways	NHAI	03/2011	08/2013	N.A.	08/2013	785.50	785.50
159	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	NHAI	12/2010	06/2013	N.A.	06/2013	1008.50	1008.50
160	PATNA-MUZZAFFARPUR	Road Transport & Highways	NHAI	08/2010	02/2013	N.A.	02/2013	671.30	671.30
161	Gujarat/Maharashtra BorderSurat-Hazira Port Section	Road Transport & Highways	NHAI	03/2010	09/2012	N.A.	09/2012	1509.10	1509.10
162	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM	Road Transport & Highways	NHAI	11/2010	05/2013	N.A.	05/2013	1585.00	1585.00
163	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	Road Transport & Highways	NHAI	09/2010	03/2013	N.A.	03/2013	852.00	852.00
164	PUNE-SATARA(NH-4)	Road Transport & Highways	NHAI	10/2010	03/2013	N.A.	03/2013	1724.55	1724.55
165	4 LANING OF NAGPUR-BETUL	Road Transport & Highways	NHAI	02/2011	08/2014	N.A.	08/2014	2498.76	2498.76
166	MURADABAD-BAREILY	Road Transport & Highways	NHAI	04/2010	06/2013	N.A.	06/2013	1267.00	1267.00
167	PANIPAT-ROHTAK	Road Transport & Highways	NHAI	04/2011	10/2014	N.A.	10/2014	807.00	807.00

SN	PROJECT	SECTOR	AGENCY	DOA	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED
168	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	Road Transport & Highways	NHAI	02/2011	11/2012	N.A.	11/2012	193.45	193.45
169	Hyderabad-yadgiri N.H no-202	Road Transport & Highways	NHAI	08/2010	05/2012	N.A.	05/2012	388.00	388.00
170	Kishangarh-Ajmer-Beawer	Road Transport & Highways	NHAI	11/2009	05/2012	N.A.	05/2012	795.00	795.00
171	DEOLI-KOTA	Road Transport & Highways	NHAI	01/2011	07/2013	N.A.	07/2013	953.00	593.00
172	Hyderabad-Vijaywada Km. 40 to 221.50 Km	Road Transport & Highways	NHAI	04/2010	10/2012	N.A.	10/2012	1740.00	1740.00
173	Modification & Strengthening of Existing Berth No. 1 to 6	Shipping & Ports	PORT TRUST	06/2010	03/2012	N.A.	03/2012	277.00	277.00
174	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CARRIERS	Shipping & Ports	SHIPP.	08/2008	09/2012	N.A.	09/2012	1066.91	968.35
175	Acquistion of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd.	Shipping & Ports	SHIPP.	10/2010	12/2013	N.A.	12/2013	1028.10	1028.10
176	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries	Shipping & Ports	SHIPP.	08/2010	12/2012	N.A.	12/2012	612.72	627.64
177	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy	Shipping & Ports	SHIPP.	10/2010	02/2014	N.A.	02/2014	966.46	994.82
178	1.2 MTPA PELLET PLANT DONIMALAI	Steel	NMDC	04/2011	04/2013	N.A.	04/2013	572.00	572.00
179	7.0 MTPA KUMARASWAMY IRON ORE MINE	Steel	NMDC	02/2011	05/2013	N.A.	05/2013	898.55	898.55
180	COKE OVEN BATTERY NO. 4 PHASE-II	Steel	RINL	08/2007	10/2012	10/2012	10/2012	108.00	216.68
181	EXPENSION OF ROURKELA STEEL PLANT	Steel	SAIL	09/2008	03/2013	N.A.	03/2013	11812.00	11812.00
182	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES	Steel	SAIL	11/2011	11/2013	N.A.	11/2013	254.55	254.55
183	DELHI MRTS PHASE-III	Urban Development	DMRC	09/2011	03/2016	N.A.	03/2016	35242.00	35242.00
184	FARIDABAD EXTENSION	Urban Development	DMRC	09/2011	09/2014	N.A.	09/2014	2494.00	2494.00

List of project Without Original Date of Commissioning

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						DOC Original / Revised	DOC Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Petroleum</u>									
1	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99	333.99	114.65	-	09/2012	-	23/36
			-			-			
	Total		333.99	333.99	114.65				23/36
			-						
<u>Railways</u>									
2	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	820.32	551.10	-	03/2012	-	0/0
						-			
3	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	118.87	-	03/2012	-	0/0
						-			
4	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	206.01	-	03/2012	-	0/0
						-			
5	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	-	03/2012	-	0/0
						-			
6	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	-	03/2012	-	0/0
						-			
7	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00	415.73	231.82	-	03/2012	-	0/0
			-			-			
8	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	180.95	-	03/2013	-	0/0
						-			
9	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	731.78	-	03/2013	-	0/0
						-			
10	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70	1,717.29	1,073.81	-	03/2013	-	0/0
			-			-			
11	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	108.35	-	03/2013	-	0/0
						-			
12	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	585.93	194.91	-	12/2013	-	0/0
			-			-			
13	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00	384.04	93.06	-	03/2014	-	0/0
			-			-			
14	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	239.06	-	03/2015	-	0/0
						-			
15	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	176.77	-	03/2015	-	0/0
						-			
16	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	1.22	-	03/2015	-	0/0
			-			-			
	Total		4,725.55	10,665.66	5,140.87				0/0
			-						

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						DOC Original / Revised	DOC Anticipated		
1	2	3	4	5	6	7	8	9	10
Road Transport & Highways									
17	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00 -	441.00	947.20	- -	04/2012	-	0/0
18	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00 -	748.00	1,438.00	- -	03/2013	-	0/3
19	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	946.00	1,065.00	- -	03/2013	-	2/2
20	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00 -	671.00	644.80	- -	03/2013	-	0/1
21	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
22	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00 -	453.00	207.90	- -	06/2013	-	1/1
23	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00 -	480.00	303.50	- -	10/2013	-	0/1
24	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00 -	839.00	-	- -	12/2013	-	0/1
Total			5,258.00 -	5,258.00	4,606.40				5/11
Grand Total				10,317.54	16,257.65	9,861.92			28/47

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated
1	2	3	4	5	6
	<u>Atomic Energy</u>				
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	09/2010	01/2012
	Total		3,492.00		
	<u>Civil Aviation</u>				
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
	Total		1,808.00	02/2012	
	<u>Steel</u>				
3	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90	-	02/2012
	Total		500.90		
	<u>Petroleum</u>				
4	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	-	12/2011
5	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00	02/2011	08/2011
6	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-
7	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91	09/2009	08/2011
	Total		5,855.60		
	<u>Power</u>				
8	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45	12/2007	12/2009
	Total		596.45	12/2009	
	<u>Railways</u>				
9	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30	03/1998	03/1998
10	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	1,038.00	-	07/2005
11	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	491.19	07/2005	08/2005
12	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	1,099.20	-	06/2007
13	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	57.94	03/1998	06/2008
			604.04	08/2005	
			409.00	06/2007	
			625.30	-	
			743.00	03/2008	
			-	06/2008	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated
1	2	3	4	5	6
14	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
15	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
16	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	03/2010
17	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTD,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010
18	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTD,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2010
19	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
20	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010
21	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	12/2010 12/2010	12/2010
22	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
23	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
24	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011
25	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
26	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
27	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	03/2011 03/2011	03/2011
28	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
29	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
30	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011
31	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	12/2010 03/2011	03/2011
32	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011
33	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTD,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 06/2011	06/2011
34	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
35	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	12/2011
36	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
37	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012
38	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	- 12/2009	02/2012
39	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	12/2011 02/2012	02/2012
40	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated
1	2	3	4	5	6
41	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-
42	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	-
43	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-
44	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
45	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
46	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
47	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-
48	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	- -	-
49	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-
50	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
51	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
52	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
53	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
54	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-
55	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	-
56	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-
57	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-
58	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-
59	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-
60	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	- -	-
61	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	- -	-
62	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-
63	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-
Total			18,902.40 -		
<u>Shipping & Ports</u>					
64	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	10/2008
65	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated
1	2	3	4	5	6
66	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 -	12/2007 01/2009	01/2009
67	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
68	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK, Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011
69	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD, Tamil Nadu	09/2006	399.13 -	08/2010 -	-
70	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD, Tamil Nadu	09/2006	370.00 -	08/2010 -	-
	Total		4,593.29 -		
Telecommunications					
71	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL, Multi State	12/2007	952.88 -	03/2010 -	10/2010
72	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL, Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
73	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00 -	02/2007 12/2010	08/2011
74	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	10/2007 -	-
75	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL, Orissa	11/2007	277.34 -	03/2009 -	-
76	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	03/2009 -	-
77	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL, Multi State	12/2007	152.65 -	03/2010 -	-
	Total		3,275.09 -		
Urban Development					
78	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD, Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			39,137.91		

List of Delay Project w.r.t Original and Revised

(Mar,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,084.24	04/2011 04/2011	04/2012	12	12
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,498.00	12/2015 -	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	921.00	12/2016 -	03/2017	3	-
4	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,380.00	12/2008 -	03/2013	51	-
Total			38,056.29 -	40,709.29	17,883.24				
<u>Civil Aviation</u>									
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	108.57	05/2012 -	08/2012	3	-
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,839.13	05/2011 03/2012	10/2012	17	7
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	182.84	01/2011 04/2013	04/2013	27	0
Total			2,587.58 -	2,970.07	2,130.54				
<u>Coal</u>									
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	87.96	03/2010 -	03/2012	24	-
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	3,027.00	2,394.54	06/2009 -	03/2013	45	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	04/2006	471.66 341.63	341.63	108.35	03/2011 03/2012	03/2013	24	12

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	05/2006	789.88 741.62	741.62	330.76	03/2010 -	03/2013	36	-
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	82.58	03/2012 -	03/2013	12	-
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	36.96	03/2012 -	03/2013	12	-
14	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,768.27	03/2012 -	03/2014	24	-
15	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 -	153.82	22.64	03/2011 -	03/2014	36	-
16	Churi Benti UG - [N06000083]CCL,Jharkhand	06/2007	163.51 -	163.51	34.01	03/2011 03/2012	03/2014	36	24
17	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	62.45	03/2012 03/2012	03/2014	24	24
18	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	96.73	03/2012 03/2013	03/2014	24	12
19	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	264.20	03/2013 09/2012	10/2014	19	25
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	535.10	161.76	03/2012 03/2015	03/2015	36	0
21	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48	-
22	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	100.57	03/2010 -	03/2015	60	-
23	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	71.92	12/2012 -	03/2015	27	-
24	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.82	03/2014 -	03/2015	12	-
25	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 1,143.54	1,143.54	317.40	03/2014 03/2016	03/2016	24	0
26	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	07/2006	469.78 706.40	706.40	18.16	07/2012 03/2014	03/2016	44	24

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Total			13,790.98	15,101.74	6,960.08				
			-						
<u>Fertilisers</u>									
27	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya Pradesh	09/2008	325.00	325.00	161.95	07/2011	04/2012	9	-
			-			-			
28	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya Pradesh	09/2008	438.00	438.00	203.75	07/2011	07/2012	12	-
			-			-			
Total			763.00	763.00	365.70				
			-						
<u>Steel</u>									
29	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93	232.93	191.33	05/2011	05/2012	12	-
			-			-			
30	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	241.50	08/2010	05/2012	21	21
			-			08/2010			
31	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	246.84	02/2011	06/2012	16	16
			-			02/2011			
32	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	9,481.85	10/2009	10/2012	36	0
			12,291.00			10/2012			
33	Bailadila Iron Ore Deposit-IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89	607.17	323.39	12/2011	10/2012	10	7
			607.17			03/2012			
34	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00	6,325.00	2,624.65	12/2011	10/2012	10	-
			-			-			
35	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00	16,408.00	13,087.79	12/2011	12/2012	12	-
			16,408.00			-			
36	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	460.00	190.54	05/2012	12/2012	7	7
			-			05/2012			

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
37	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	750.85	12/2012 -	03/2013	3	-
38	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhattisgarh	09/2008	17,265.00 -	17,265.00	5,179.68	03/2013 -	09/2013	6	-
Total			51,098.82 -	57,157.68	32,318.42				
<u>Petroleum</u>									
39	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 898.00	898.00	842.61	09/2011 03/2012	03/2012	6	0
40	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,155.00	09/2011 03/2012	03/2012	6	0
41	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	706.29	04/2011 12/2011	04/2012	12	4
42	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	463.51	05/2010 04/2012	05/2012	24	1
43	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 252.37	204.00	168.94	01/2012 -	05/2012	4	-
44	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL, Multi State	06/2009	348.00 -	261.00	193.21	03/2012 08/2012	05/2012	2	-3
45	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,918.57	04/2006 05/2011	06/2012	74	13
46	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	199.02	03/2012 03/2012	06/2012	3	3
47	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	4,861.93	05/2010 05/2012	07/2012	26	2

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
48	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	697.35	07/2010 05/2012	07/2012	24	2
49	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	194.89	04/2011 -	07/2012	15	-
50	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,658.05	03/2012 08/2012	08/2012	5	0
51	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	534.30	03/2011 05/2011	10/2012	19	17
52	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	8,412.96	01/2012 -	10/2012	9	-
53	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	257.92	09/2011 -	12/2012	15	-
54	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	798.79	06/2012 -	12/2012	6	-
55	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	261.99	12/2011 -	01/2013	13	-
56	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	274.39	03/2006 03/2013	03/2013	84	0
57	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,863.48	05/2010 03/2013	03/2013	34	0
58	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	195.06	07/2012 07/2012	03/2013	8	8
59	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	04/2013	52	52
60	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,204.08	09/2010 03/2012	04/2013	31	13

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
61	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	158.92	03/2013 -	04/2013	1	-
62	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	29.47	03/2013 -	04/2013	1	-
63	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	04/2013	10	-
64	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	711.38	12/2012 12/2012	04/2013	4	4
65	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	417.93	03/2010 03/2012	05/2013	38	14
66	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	05/2013	6	-
67	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	14,627.00	11/2012 06/2013	06/2013	7	0
68	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	3,249.02	09/2012 -	09/2013	12	-
69	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
70	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	2,584.43	08/2010 03/2012	12/2013	40	21
71	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
72	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	597.20	03/2007 03/2014	03/2014	84	0
73	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	589.71	03/2013 -	03/2014	12	-
74	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
75	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.20	01/2013	07/2015	30	-
76	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,447.85	03/2007 03/2017	03/2017	120	0
	Total		107,198.21	115,427.42	58,801.77				
			-	-					
	Power								
77	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26	621.28	-	02/2011	12/2012	22	-
78	KOTESHWAR HEP (THDC) - [180100184]THDC, Uttarakhal	04/2000	1,301.56	2,283.68	2,618.18	04/2005	03/2012	83	-
79	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	362.10	02/2012	03/2012	1	-
80	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,745.00	12/2009 12/2011	04/2012	28	4
81	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63	2,084.00	1,794.22	08/2010 08/2011	04/2012	20	8
82	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	975.96	768.10	10/2009	05/2012	31	-
83	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	124.00	07/2011	05/2012	10	-
84	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT (P.G.R.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,779.46	3,652.60	09/2009	06/2012	33	-
85	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	103.30	02/2012 02/2012	06/2012	4	4

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
86	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	164.60	11/2011 11/2011	06/2012	7	7
87	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	994.10	02/2012 -	06/2012	4	-
88	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.39	1,454.67	03/2007 -	09/2012	66	-
89	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	686.00	11/2011 -	12/2012	13	-
90	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	523.00	01/2010 -	12/2012	35	-
91	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,071.70	07/2010 -	12/2012	29	-
92	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	276.60	11/2011 -	12/2012	13	-
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	314.90	11/2011 -	12/2012	13	-
94	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	151.60	02/2012 -	12/2012	10	-
95	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	310.93	07/2011 -	12/2012	17	-
96	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,756.57	10/2010 12/2011	01/2013	27	13

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
97	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	723.13	08/2010 09/2011	01/2013	29	16
98	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	1,794.00	1,691.47	11/2009 11/2011	02/2013	39	15
99	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,149.00	04/2009 04/2011	03/2013	47	23
100	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	3,635.00	08/2012 -	03/2013	7	-
101	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,844.90	08/2012 -	03/2013	7	-
102	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	4,740.40	08/2012 -	03/2013	7	-
103	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,965.00	10/2012 -	03/2013	5	-
104	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,760.00	10/2012 -	03/2013	5	-
105	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	25.60	10/2012 -	03/2013	5	-
106	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,102.86	09/2009 -	06/2013	45	-
107	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	820.40	11/2012 -	06/2013	7	-
108	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	305.83	08/2012 08/2013	08/2013	12	0
109	RAMPUR HEP(412 MW) - [N18000024]SJVN,Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,599.91	01/2012 -	09/2013	20	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
110	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	142.40	11/2011 -	09/2013	22	-
111	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,538.90	10/2012 -	11/2013	13	-
112	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	181.20	11/2012 -	12/2013	13	-
113	TUIRIAL HE PROJECT(NEPCO) - [180100165]NEPCO,Mizoram	07/1998	368.72 913.63	913.63	303.47	07/2006 01/2014	01/2014	90	0
114	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,595.00	08/2013 -	01/2014	5	-
115	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,377.00	03/2013 -	06/2014	15	-
116	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,524.00	3,535.89	09/2009 07/2014	07/2014	58	0
117	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	3,668.20	08/2013 -	09/2014	13	-
118	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,861.00	06/2011 -	11/2014	41	-
119	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,543.00	12/2009 12/2014	12/2014	60	0
120	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,603.13	09/2010 08/2014	12/2015	63	16
121	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	320.70	07/2010 02/2016	02/2016	67	0
122	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	296.15	07/2014 -	05/2016	22	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
123	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,788.85	05/2013 06/2016	06/2016	37	0
124	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,390.53	01/2016 01/2016	11/2016	10	10
125	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,791.78	09/2008 -	03/2013	54	-
126	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	390.90	09/2010 -	03/2013	30	-
Total			137,766.12	152,266.83	89,563.77				
<u>Railways</u>									
127	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	548.61	03/1995 -	03/2012	204	-
128	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	200.08	03/2002 -	03/2012	120	-
129	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	516.84	12/2011 12/2011	03/2012	3	3
130	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	840.32	571.01	02/2009 -	03/2012	37	-
131	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	257.85	02/2011 02/2011	03/2012	13	13
132	SALKA ROAD - ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	216.05	03/2010 -	03/2012	24	-
133	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	12	-
134	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	209.64	03/2011 -	03/2012	12	-
135	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 -	456.45	278.64	06/2004 -	12/2012	102	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
136	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	390.91	03/2012 03/2012	12/2012	9	9
137	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	260.24	03/2012 03/2012	12/2012	9	9
138	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	689.00	03/2009 12/2012	12/2012	45	0
139	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	1,389.98	1,178.15	10/2007 12/2012	12/2012	62	0
140	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	283.10	39.12	02/2006 -	12/2012	82	-
141	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	486.33	03/2010 -	12/2012	33	-
142	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	59.09	03/2012 -	03/2013	12	-
143	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	247.14	02/2009 02/2009	04/2013	50	50
144	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	-	03/2009 03/2009	04/2013	49	49
145	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	65.91	12/2011 11/2013	11/2013	23	0
146	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,027.93	3,028.24	03/2009 -	12/2013	57	-
147	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	159.83	03/2007 03/2007	03/2014	84	84
148	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	1,078.41	12/2008 -	03/2014	63	-
149	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	103.18	12/2012 -	03/2014	15	-
150	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	819.40	114.31	03/2010 06/2014	06/2014	51	0
151	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	725.17	12/2010 12/2010	03/2015	51	51

List of Delay Project w.r.t Original and Revised

(Mar,2012)

						Date of Commissioning			
S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	
152	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	397.53	03/2014 03/2015	03/2015	12	0
153	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	723.71	400.52	06/2005 07/2011	06/2015	120	47
154	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,382.73	04/2008 03/2014	12/2015	92	21
155	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	227.13	02/2010 -	12/2015	70	-
156	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	1,173.79	424.73	03/2005 12/2008	03/2016	132	87
157	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	3,056.85	679.56	03/2011 03/2014	03/2016	60	24
158	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	5.24	03/2014 03/2016	03/2016	24	0
159	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	13.85	03/2016 -	06/2016	3	-
160	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	20,000.00	8,035.01	03/2001 -	12/2017	201	-
Total			23,670.75 -	56,067.81	24,217.53				
<u>Road Transport & Highways</u>									
161	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	04/2012	85	-
162	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	383.20	12/2008 -	04/2012	40	-
163	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	261.90	10/2008 -	04/2012	42	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
164	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	631.70	02/2012 -	04/2012	2	-
165	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09 -	166.30	184.90	03/2008 -	05/2012	50	-
166	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27 -	193.10	161.40	03/2008 -	05/2012	50	-
167	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	180.20	10/2008 -	05/2012	43	-
168	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	05/2012	50	-
169	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	05/2012	16	-
170	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27	-
171	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	195.20	09/2007 -	06/2012	57	-
172	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	171.00	08/2004 07/2010	06/2012	94	23
173	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	180.59	08/2004 -	06/2012	94	-
174	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	06/2012	87	-
175	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	275.00	303.60	09/2007 -	06/2012	57	-
176	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	269.90	09/2007 -	06/2012	57	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
177	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	112.00	09/2008 -	06/2012	45	-
178	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	285.60	10/2008 -	06/2012	44	-
179	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	367.00	03/2008 -	06/2012	51	-
180	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	251.60	01/2009 -	06/2012	41	-
181	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	267.40	06/2008 -	06/2012	48	-
182	BIJUNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	195.00	06/2008 -	06/2012	48	-
183	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	486.50	09/2008 -	06/2012	45	-
184	NALBARI TO BIJUNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	273.10	06/2008 -	06/2012	48	-
185	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	246.00	06/2011 06/2011	06/2012	12	12
186	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	272.50	06/2008 -	06/2012	48	-
187	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	221.82	275.80	11/2008 -	06/2012	43	-
188	NALBARI TO BIJUNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	188.90	06/2008 -	06/2012	48	-
189	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	132.10	05/2008 -	06/2012	49	-
190	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	209.80	06/2008 -	06/2012	48	-
191	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2012	42	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
192	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	263.96	02/2004 -	06/2012	100	-
193	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	805.10	10/2009 -	06/2012	32	-
194	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	464.00	533.80	01/2011 -	06/2012	17	-
195	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,406.00	10/2011 -	06/2012	8	-
196	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,639.00	08/2011 -	06/2012	10	-
197	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,337.00	11/2011 -	06/2012	7	-
198	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	109.99	04/2004 -	07/2012	99	-
199	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	182.07	02/2004 -	07/2012	101	-
200	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	179.00	05/2008 -	08/2012	51	-
201	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	224.10	06/2005 -	09/2012	87	-
202	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.30	10/2008 -	09/2012	47	-
203	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	248.00	10/2008 -	09/2012	47	-
204	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	185.50	06/2010 -	10/2012	28	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
205	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17 -	263.17	233.80	09/2009 -	10/2012	37	-
206	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	-
207	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	11/2012	41	-
208	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	170.20	10/2008 -	12/2012	50	-
209	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	237.20	06/2008 -	12/2012	54	-
210	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	357.40	09/2008 -	12/2012	51	-
211	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	223.90	10/2008 -	12/2012	50	-
212	RAJMARG CHORAH TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	297.80	10/2008 -	12/2012	50	-
213	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	177.70	07/2008 -	12/2012	53	-
214	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	129.50	04/2008 -	12/2012	56	-
215	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	192.90	04/2008 -	12/2012	56	-
216	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	235.50	04/2008 -	12/2012	56	-
217	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	165.80	04/2010 -	12/2012	32	-
218	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93 -	300.93	302.70	10/2009 -	12/2012	38	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
219	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.30	12/2009 -	12/2012	36	-
220	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	436.70	09/2009 -	12/2012	39	-
221	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	251.80	09/2010 -	12/2012	27	-
222	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	577.70	05/2010 -	12/2012	31	-
223	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	258.60	02/2009 -	03/2013	49	-
224	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	96.26	04/2009 -	03/2013	47	-
225	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	691.90	07/2010 -	03/2013	32	-
226	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	143.90	09/2007 -	06/2013	69	-
227	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	628.10	10/2011 -	06/2013	20	-
228	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	902.20	11/2012 -	06/2013	7	-
229	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	48.94	04/2009 -	07/2013	51	-
230	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	85.39	11/2008 -	07/2013	56	-
231	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	10/2013	14	-
232	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.20	02/2010 -	12/2013	46	-

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
233	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	6.00	11/2008 -	01/2014	62	-
234	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	296.70	05/2013 -	02/2014	9	-
235	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	231.90	10/2011 -	03/2014	29	-
236	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	163.90	05/2013 -	03/2014	10	-
237	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	21.56	09/2007 -	04/2014	79	-
238	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	32.51	07/2009 -	04/2014	57	-
239	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	15.15	02/2014 -	04/2014	2	-
240	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
241	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00 -	359.00	32.08	09/2013 -	07/2014	10	-
Total			30,305.75 -	32,466.58	31,648.99				
<u>Shipping & Ports</u>									
242	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2	-
243	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Mahara shtra	11/2007	1,061.96 1,077.60	1,082.06	1,143.89	03/2012 -	04/2012	1	-
244	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	241.50	262.80	09/2011 -	04/2012	7	-
245	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Mahara shtra	10/2007	359.44 -	359.44	358.78	04/2011 06/2011	06/2012	14	12

List of Delay Project w.r.t Original and Revised

(Mar,2012)

						Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
246	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	86.46	06/2011 06/2012	06/2012	12	0
247	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 08/2012	08/2012	8	0
248	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	-
249	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	724.00	12/2010 -	12/2012	24	-
250	CONSTRUCTION OF Berthing and Allied Facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22	-
251	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
252	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93	-
253	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	07/2014	14	-
Total			9,966.88 -	10,706.16	2,944.26				
<u>Telecommunications</u>									
254	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2011	03/2012	61	12
255	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	757.02	11/2010 -	03/2012	16	-
256	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	80.47	12/2005 03/2008	04/2012	76	49

List of Delay Project w.r.t Original and Revised

(Mar,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
257	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	227.28	12/2008 -	06/2012	42	-
258	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	06/2012	36	-
259	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2012	41	-
260	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	06/2012	39	-
261	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	366.90	08/2009 -	06/2012	34	-
262	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.80	10/2010 03/2012	07/2012	21	4
Total			3,855.73 -	4,035.11	1,919.78				
Urban Development									
263	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24	-
Total			6,395.00 -	11,609.00	2,267.57				
Water Resources									
264	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
Total			542.90 -	1,187.00	35.49				
Grand Total			425,998.01	500,467.69	271,057.14				

List of Projects Without Milestones

(Mar,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	04/2011 04/2011	04/2012	0/0
	Total		1,106.29 -			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	08/2012	0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 03/2012	10/2012	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
	Total		5,021.58 -			0/0
<u>Coal</u>						
7	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014	0/0
8	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014	0/0
9	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 535.10	03/2012 03/2015	03/2015	0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
11	KHADIA EXPANSION OPENCASE PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		3,609.93 -			0/0
<u>Fertilisers</u>						
12	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012	0/0
13	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012	0/0
	Total		763.00 -			0/0
<u>Steel</u>						
14	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	04/2013 -	04/2013	0/0
15	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	05/2013 -	05/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
16	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55 -	11/2013 -	11/2013	0/0
	Total		1,725.10 -			0/0
<u>Petroleum</u>						
17	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	02/2011 08/2011	08/2011	0/0
18	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 898.00	09/2011 03/2012	03/2012	0/0
19	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	03/2012	0/0
20	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	05/2010 04/2012	05/2012	0/0
21	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	04/2006 05/2011	06/2012	0/0
22	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	07/2012	0/0
23	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	07/2012	0/0
24	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	04/2011 -	07/2012	0/0
25	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	07/2012 -	07/2012	0/0
26	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	08/2012 -	08/2012	0/0
27	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL, Gujarat	02/2009	267.00 -	09/2012 09/2012	09/2012	0/0
28	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	09/2012 -	09/2012	0/0
29	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	03/2011 05/2011	10/2012	0/0
30	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 12,160.26	01/2012 -	10/2012	0/0
31	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	09/2011 -	12/2012	0/0
32	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	06/2012 -	12/2012	0/0
33	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
34	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
35	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 -	12/2008 12/2008	04/2013	0/0
36	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
37	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 -	03/2013 -	04/2013	0/0
38	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
39	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	06/2012 -	04/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
41	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	05/2013	0/0
42	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
43	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
44	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
45	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
46	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
47	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
48	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
49	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	01/2014 -	01/2014	0/0
50	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
51	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
52	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
53	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
54	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
55	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
56	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	07/2015	0/0
57	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
58	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	09/2009 -	08/2011	0/0
	Total		92,489.82 -			0/0
Power						
59	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96 -	02/2012 -	03/2012	0/0
60	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	10/2012 -	04/2012	0/0
61	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	04/2012	0/0
62	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	07/2011 -	05/2012	0/0
63	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	05/2012 -	05/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
64	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	02/2012 02/2012	06/2012	0/0
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	11/2011 11/2011	06/2012	0/0
66	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	02/2012 -	06/2012	0/0
67	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	06/2012 -	06/2012	0/0
68	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	06/2012 -	06/2012	0/0
69	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	06/2012 -	06/2012	0/0
70	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	08/2012 -	08/2012	0/0
71	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	11/2012 -	11/2012	0/0
72	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	12/2012 -	12/2012	0/0
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	11/2011 -	12/2012	0/0
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	11/2011 -	12/2012	0/0
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	02/2012 -	12/2012	0/0
76	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	07/2011 -	12/2012	0/0
77	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	12/2012 -	12/2012	0/0
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	01/2013 -	01/2013	0/0
79	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	01/2013 -	01/2013	0/0
80	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	01/2013 -	01/2013	0/0
81	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	08/2012 -	03/2013	0/0
82	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	08/2012 -	03/2013	0/0
83	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	03/2013 -	03/2013	0/0
84	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	10/2012 -	03/2013	0/0
85	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	04/2013 -	04/2013	0/0
86	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	04/2013 -	04/2013	0/0
87	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 -	06/2013	0/0
88	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	11/2012 -	06/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
89	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	07/2013 -	07/2013	0/0
90	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
91	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	07/2013 -	07/2013	0/0
92	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	08/2013 -	08/2013	0/0
93	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	08/2013 -	08/2013	0/0
94	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	08/2013 -	08/2013	0/0
95	RAMPUR HEP (412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	01/2012 -	09/2013	0/0
96	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	11/2011 -	09/2013	0/0
97	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	10/2013 -	10/2013	0/0
98	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	10/2012 -	11/2013	0/0
99	Transmission system for transfer of power from Gen- PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	11/2013 -	11/2013	0/0
100	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	11/2013 -	11/2013	0/0
101	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	12/2013 -	12/2013	0/0
102	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	11/2012 -	12/2013	0/0
103	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	12/2013 -	12/2013	0/0
104	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	12/2013 -	12/2013	0/0
105	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	12/2013	0/0
106	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	01/2014 -	01/2014	0/0
107	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	02/2014 -	02/2014	0/0
108	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	03/2014 -	03/2014	0/0
109	LINE BAYS AND REACTOR PROVISIONS AT POWERGRID SUBSTATIONS AS - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
110	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	05/2014 -	05/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
111	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	06/2014 -	06/2014	0/0
112	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	06/2014 -	06/2014	0/0
113	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	07/2014 -	07/2014	0/0
114	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	08/2014 -	08/2014	0/0
115	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND W - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
116	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	08/2014 -	08/2014	0/0
117	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	08/2014 -	08/2014	0/0
118	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	08/2014 -	08/2014	0/0
119	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	08/2013 -	09/2014	0/0
120	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	09/2014 -	09/2014	0/0
121	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
122	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	10/2014 -	10/2014	0/0
123	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	01/2015 -	01/2015	0/0
124	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	01/2015 -	01/2015	0/0
125	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
126	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	06/2015 -	06/2015	0/0
127	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	03/2013	0/0
	Total		109,441.14 -			0/0
Railways						
128	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	02/2015	0/0
129	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	12/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
130	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	03/1998	0/0
131	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	07/2005 -	07/2005	0/0
132	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
133	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
134	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	06/2008	0/0
135	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
136	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
137	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	03/2010	0/0
138	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,176.10	12/2006 08/2010	08/2010	0/0
139	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2010	0/0
140	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
141	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010	0/0
142	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	12/2010 12/2010	12/2010	0/0
143	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
144	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
145	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	03/2011	0/0
146	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
147	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
148	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	03/2011 03/2011	03/2011	0/0
149	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
150	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
151	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 -	03/2011 03/2011	03/2011	0/0
152	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	12/2010 03/2011	03/2011	0/0
153	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	03/2011	0/0
154	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 06/2011	06/2011	0/0
155	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
156	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	12/2011	0/0
157	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
158	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	02/2012	0/0
159	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	- 12/2009	02/2012	0/0
160	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	12/2011 02/2012	02/2012	0/0
161	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2012	0/0
162	PEDAPALLI-KARIMNAGAR-NIZAMABAD (SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	- -	03/2012	0/0
163	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	03/2012	0/0
164	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	12/2011 12/2011	03/2012	0/0
165	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2012	0/0
166	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	02/2009 -	03/2012	0/0
167	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 483.62	03/2012 03/2012	03/2012	0/0
168	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
169	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 03/2012	03/2012	0/0
170	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2012	0/0
171	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2012	0/0
172	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2012	03/2012	0/0
173	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
174	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
175	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
176	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012	0/0
177	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
178	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0
179	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	03/2012	0/0
180	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	03/2012 -	03/2012	0/0
181	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
182	CONV.OF 1500V DC TRACTION TO 25 KV AC,CR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2012	06/2012	0/0
183	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 07/2012	07/2012	0/0
184	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	06/2004 -	12/2012	0/0
185	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 -	12/2012	0/0
186	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	12/2012 12/2012	12/2012	0/0
187	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
188	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	03/2012 03/2012	12/2012	0/0
189	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 12/2012	12/2012	0/0
190	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 1,389.98	10/2007 12/2012	12/2012	0/0
191	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 261.70	02/2006 -	12/2012	0/0
192	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
193	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	12/2012	0/0
194	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
195	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013	0/0
196	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2013	0/0
197	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
198	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2013	0/0
199	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2013	0/0
200	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	03/2013 -	03/2013	0/0
201	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
202	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
203	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	06/2013	0/0
204	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	12/2011 11/2013	11/2013	0/0
205	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
206	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013	0/0
207	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
208	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014	0/0
209	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	03/2014	0/0
210	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014	0/0
211	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2014	0/0
212	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014	0/0
213	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014	0/0
214	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
215	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	03/2014	0/0
216	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014	0/0
217	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
218	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
219	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	03/2015	0/0
220	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2015	03/2015	0/0
221	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	03/2015	0/0
222	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	03/2015 -	03/2015	0/0
223	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	03/2015 -	03/2015	0/0
224	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 662.69	06/2005 07/2011	06/2015	0/0
225	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
226	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 -	12/2015	0/0
227	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
228	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 789.10	03/2005 12/2008	03/2016	0/0
229	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 -	03/2011 03/2014	03/2016	0/0
230	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
231	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
232	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
233	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
234	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 8,000.00	03/2001 -	12/2017	0/0
235	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
236	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-	0/0
237	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	-	0/0
238	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 229.88	- -	-	0/0
239	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-	0/0
240	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
241	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
242	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-	0/0
243	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	- -	-	0/0
244	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-	0/0
245	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
246	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
247	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
248	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-	0/0
249	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-	0/0
250	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	-	0/0
251	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-	0/0
252	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 582.83	- -	-	0/0
253	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 -	- -	-	0/0
254	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 -	- -	-	0/0
255	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	- -	-	0/0
256	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-	0/0
257	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-	0/0
Total			64,962.90 -			0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
258	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	03/2005 -	04/2012	0/0
259	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	12/2008 -	04/2012	0/0
260	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00 -	10/2008 -	04/2012	0/0
261	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00 -	- -	04/2012	0/0
262	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	02/2012 -	04/2012	0/0
263	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J and K	12/2003	193.09 -	03/2008 -	05/2012	0/0
264	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J and K	12/2003	166.27 -	03/2008 -	05/2012	0/0
265	SAGAR BY PASS, KM 187 TO KM 211, NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	10/2008 -	05/2012	0/0
266	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	05/2012	0/0
267	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00 -	01/2011 -	05/2012	0/0
268	NH CONNECTIVITY TO ICTT VALLARPADA EU NH -SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	02/2010 -	05/2012	0/0
269	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	05/2012 -	05/2012	0/0
270	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	05/2012 -	05/2012	0/0
271	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00 -	05/2012 -	05/2012	0/0
272	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	09/2007 -	06/2012	0/0
273	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	08/2004 07/2010	06/2012	0/0
274	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	08/2004 -	06/2012	0/0
275	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	03/2005 -	06/2012	0/0
276	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	09/2007 -	06/2012	0/0
277	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	09/2007 -	06/2012	0/0
278	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	09/2008 -	06/2012	0/0
279	KOTWA TO DEWAPUR (10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	10/2008 -	06/2012	0/0
280	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	03/2008 -	06/2012	0/0
281	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	01/2009 -	06/2012	0/0
282	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	06/2008 -	06/2012	0/0
283	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	06/2008 -	06/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
284	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	06/2012	0/0
285	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	06/2012	0/0
286	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	06/2012	0/0
287	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	06/2012	0/0
288	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	06/2012	0/0
289	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	06/2012	0/0
290	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	06/2012	0/0
291	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2012	0/0
292	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	06/2012	0/0
293	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	10/2009 -	06/2012	0/0
294	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	06/2012	0/0
295	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	06/2012	0/0
296	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	06/2012	0/0
297	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	06/2012	0/0
298	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	06/2012	0/0
299	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	07/2012	0/0
300	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	07/2012	0/0
301	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	07/2012	0/0
302	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	08/2012	0/0
303	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	09/2012	0/0
304	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2012	0/0
305	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	09/2012	0/0
306	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	09/2012	0/0
307	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012	0/0
308	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	10/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
309	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012	0/0
310	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012	0/0
311	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
312	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
313	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	12/2012	0/0
314	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
315	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
316	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
317	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
318	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
319	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
320	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
321	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
322	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
323	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
324	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2012	0/0
325	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	12/2012	0/0
326	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
327	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
328	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
329	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	01/2013	0/0
330	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
331	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 -	03/2013	0/0
332	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
333	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
334	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
335	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	03/2013	03/2013	0/0
			-	-		
336	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	03/2013	03/2013	0/0
			-	-		
337	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya Pradesh	10/2010	1,175.00	04/2013	04/2013	0/0
			-	-		
338	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	05/2013	05/2013	0/0
			-	-		
339	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	05/2013	05/2013	0/0
			-	-		
340	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	09/2007	06/2013	0/0
			-	-		
341	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	10/2011	06/2013	0/0
			-	-		
342	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	11/2012	06/2013	0/0
			-	-		
343	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	06/2013	06/2013	0/0
			-	-		
344	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	06/2013	06/2013	0/0
			-	-		
345	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	06/2013	06/2013	0/0
			-	-		
346	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	04/2009	07/2013	0/0
			-	-		
347	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	11/2008	07/2013	0/0
			-	-		
348	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	07/2013	07/2013	0/0
			-	-		
349	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	07/2013	07/2013	0/0
			-	-		
350	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	07/2013	07/2013	0/0
			-	-		
351	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0
			-	-		
352	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
			-	-		
353	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
			-	-		
354	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
			-	-		
355	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	08/2012	10/2013	0/0
			-	-		
356	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
			-	-		
357	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
			-	-		
358	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
			-	-		
359	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
			-	-		
360	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
			-	-		

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
361	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	12/2013	0/0
362	SIX LANNING OF HOSUR- KRISHNAGIRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
363	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
364	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	01/2014	0/0
365	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
366	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
367	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
368	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
369	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
370	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
371	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
372	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
373	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
374	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
375	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
376	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
377	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
378	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
379	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
380	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
381	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	06/2015	0/0
382	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	07/2015	0/0
	Total		74,230.98 -			0/0
Shipping & Ports						
383	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	10/2008	0/0
384	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	10/2008	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
385	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	12/2007 01/2009	01/2009	0/0
386	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
387	MARINE LIQUID TERMINALS - [N25000054]JENNORE TANK,Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011	0/0
388	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	01/2012 -	03/2012	0/0
389	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
390	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	03/2012 -	04/2012	0/0
391	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	09/2011 -	04/2012	0/0
392	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 06/2011	06/2012	0/0
393	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 06/2012	06/2012	0/0
394	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	12/2011 08/2012	08/2012	0/0
395	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012	0/0
396	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
397	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 -	12/2012	0/0
398	CONSTRUCTION OF Berthing and Allied Facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
399	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 -	12/2012	0/0
400	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
401	JENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEH - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	03/2006 -	12/2013	0/0
402	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013	0/0
403	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
404	SETTING UP OF SINGLE POINT MOORING (SPM) - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	07/2014	0/0
405	DEVELOPMENT OF COAL TERMINAL - [N25000055]JENNORE PORT LTD,Tamil Nadu	09/2006	399.13 -	08/2010 -	-	0/0
406	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]JENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-	0/0
Total			18,511.36 -			0/0
Telecommunications						
407	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010	0/0
408	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
409	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	08/2011	0/0
410	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2011	03/2012	0/0
411	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	03/2012	0/0
412	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 03/2008	04/2012	0/0
413	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	06/2012	0/0
414	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	06/2012	0/0
415	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2012	0/0
416	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	06/2012	0/0
417	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	08/2009 -	06/2012	0/0
418	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	07/2012	0/0
419	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
420	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	03/2009 -	-	0/0
421	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
422	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
	Total		7,130.82 -			0/0
Urban Development						
423	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
424	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
425	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
426	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			417,386.00			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
