

**329th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
March 2013**



ONGC - Ahmedabad Redevelopment



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

मार्च, 2013 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 558 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। मार्च, 2013 के दौरान 12 परियोजनाओं (सड़क परिवहन तथा राजमार्ग की 05 परियोजनाओं, पेट्रोलियम की 04 परियोजनाओं तथा विद्युत क्षेत्र की 03 परियोजनाओं) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 558 परियोजनाओं में से 272 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 59 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 59 परियोजनाओं में से, 25 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। ऊर्वरक, पोत परिवहन तथा पत्तन, कोयला, इस्पात, रेलवे, पेट्रोलियम, विद्युत, तथा सड़क परिवहन एवं राजमार्ग क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 36 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	सड़क परिवहन एवं राजमार्ग	149	89	17	2
2.	रेलवे	124	36	8	4
3.	विद्युत	101	53	14	9
4.	पेट्रोलियम	67	36	10	4
5.	कोयला	51	28	3	1
6.	पोत परिवहन एवं पत्तन	19	4	2	2
7.	इस्पात	17	13	4	2
8.	दूरसंचार	13	5	0	0
9.	नागर विमानन	6	3	0	0
10.	परमाणु ऊर्जा	4	3	0	0
11.	शहरी विकास	4	1	0	0
12.	ऊर्वरक	1	1	1	1
13.	पेट्रोरसायन	1	0	0	0
14.	जल संसाधन	1	0	0	0
कुल		558	272	59	25

3. 558 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,89,713.63 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,29,738.10 करोड़ रुपए होने की संभावना है जो 1,40,024.47 करोड़ रुपए (मूल लागत का 17.70%) की समग्र लागत वृद्धि को दर्शाता है। मार्च, 2013

तक इन परियोजनाओं पर किया गया व्यय 4,47,761.07 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 48.20% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.03.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
				मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	450.00	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	04/1974	31.42	393.46	535.40	1604.01
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1028.05	1423.98	1172.55
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. 558 परियोजनाओं में से, 2 परियोजनाएं समय से पहले चल रही हैं, 170 समय पर तथा 272 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या 285 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है। इसके अलावा, 20 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 94 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया गया है। 272 विलंबित परियोजनाओं में से, 68 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 68 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 79 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 57 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ। अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.03.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावा बरास्ता शिवपुरी-ग्वालियर-भिंड एनएलए(एनसीआर)	रेलवे	04/1986	03/1994	10/2013	235
2	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2013	216
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	03/2001	12/2017	201
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	03/2005	06/2016	135
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	03/2002	03/2013	132

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

5. विभिन्न परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, वन संबंधी स्वीकृति में विलंब, उपस्करों के संस्थापन में विलम्ब, सामग्री की आपूर्ति में विलंब, भू वैज्ञानिक गतिविधियां, कार्यक्षेत्र में परिवर्तन, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था आदि शामिल हैं ।

6. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है । परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें । तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं । पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.03.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रेट आप्रेशनस इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

7. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.03.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
				मूल	अनुमानित	
1	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	04/1993	100.00	142.98	211.19
2	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	120.90	284.27	541.95
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	597.99
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8549.43
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	65.94	302.23	344.29

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.03.2013 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगाम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012

5	कोटर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012
---	-------------------------------------	-------	---------	--------	--------	---------

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

एन.आर.: सूचित नहीं ।

8. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) **उर्वरक क्षेत्र** में, माह के दौरान 'नांगल-अमोनिया संयंत्र फीडस्टॉक एनएफएल' नामक परियोजना के संबंध में 2 माह के अतिरिक्त विलम्ब की सूचना दी गई है । तथापि, इस परियोजना में विलम्ब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है ।

(ii) **पोत परिवहन तथा पत्तन क्षेत्र** में, 19 परियोजनाओं में से 4 परियोजनाएं विलंबित हैं । माह के दौरान, 2 परियोजनाओं के संबंध में अतिरिक्त विलंब की सूचना प्राप्त हुई है । ये दोनों परियोजनाएं मेगा परियोजनाएं हैं । 'पुथु पोर्ट ट्रस्ट में एलएनजी रीगैसीफिकेशन टर्मिनल की स्थापना' और 'मुम्बई पोर्ट ट्रस्ट में 2 ऑफशोर कंटेनर बर्थ और टर्मिनल का निर्माण एवं विकास' परियोजनाओं के संबंध में क्रमशः 1 तथा 4 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है । तथापि, इन परियोजनाओं में विलम्ब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है ।

(iii) **कोयला क्षेत्र** में, 51 परियोजनाओं में से 28 परियोजनाएं विलंबित हैं । माह के दौरान 03 परियोजनाओं के संबंध में 4-24 माह के अतिरिक्त विलंब की सूचना दी है जिनमें से 1 मेगा परियोजना है । 'टीपीएस-II विस्तार (1470 मे.वा. से 1970 मे.वा.), एनएलसी' परियोजना के संबंध में उपस्करों के संस्थापन में विलम्ब के कारण 4 माह के अतिरिक्त विलंब की सूचना दी गई है । वन संबंधी स्वीकृति में विलंब के कारण 'कानिहा (ओसीपी) एमसीएल, (10.0 एमटीवाई), एमसीएल' तथा 'हिंगुला ओसी-II विस्तार फेज-III (15 एमटीवाई)' परियोजनाओं के संबंध में 24 माह के अतिरिक्त विलंब की सूचना दी गई है ।

(iv) **इस्पात क्षेत्र** में, 17 परियोजनाओं में से 13 परियोजनाएं विलंबित हैं । माह के दौरान 4 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 2 मेगा परियोजनाएं हैं । '330 टीपीएच बॉयलर-6 तथा सहायक प्रणाली, आरआईएनएल' तथा '1X45 एमवीए सबमर्ज्ड आर्क फर्नेस का संस्थापन, सेल' तथा 'बोकारो इस्पात संयंत्र का विस्तार, सेल' परियोजनाओं के संबंध में प्रत्येक में 6 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है । तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है ।

(V) **रेलवे क्षेत्र** में, 124 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं। माह के दौरान, 8 परियोजनाओं के संबंध में 1-36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है जिनमें से 4 बड़ी परियोजनाएं हैं। 8 परियोजनाओं में से, 2 परियोजनाओं के संबंध में क्रमशः 1 माह तथा 2 माह के अतिरिक्त विलंब की सूचना दी गई है तथा 2 परियोजनाओं के संबंध में क्रमशः 6 माह तथा 12 माह के अतिरिक्त विलंब की सूचना दी गई है तथा 2 परियोजनाओं के संबंध में प्रत्येक में 16 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'भैरवी सेरांग, एनएल, एनईएफआर' के संबंध में वन स्वीकृति के कारण 36 माह के अतिरिक्त विलंब की सूचना दी गई है। 'बारानगर से बैरकपुर तक मेट्रो के निर्माण हेतु नवीन कार्य, आरवीएनएल' परियोजना के संबंध में 24 माह के अतिरिक्त विलम्ब की सूचना दी गई है। तथापि, परियोजना प्राधिकारियों द्वारा इन परियोजनाओं में विलंब के लिए कोई विशेष कारण नहीं बताया गया है।

(Vi) **पेट्रोलियम क्षेत्र** में, 76 परियोजनाओं में से 36 परियोजनाएं विलंबित हैं। माह के दौरान, 10 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 3 बड़ी परियोजनाएं हैं। इन 10 परियोजनाओं में से, 3 परियोजनाओं के संबंध में 1 माह तथा 3 परियोजनाओं में 2 माह के अतिरिक्त विलम्ब की सूचना दी गई है। 'आईओआर रुद्रसागर, ओएनजीसी' के संबंध में कार्यक्षेत्र में परिवर्तन के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'पारादीप रिफाइनरी परियोजना, आईओसीएल' के संबंध में कानून और व्यवस्था के कारण 6 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'विशाख रिफाइनरी में डीजल हाइड्रोट्रीटर परियोजना, एचपीसीएल' तथा 'पॉलीप्रॉपिलीन यूनिट मंगलौर रिफाइनरी' में वन संबंधी स्वीकृति में विलम्ब के कारण 3 और 4 माह के अतिरिक्त विलम्ब की जसूचना प्राप्त हुई है।

(Vii) **विद्युत क्षेत्र** में, 101 परियोजनाओं में से 53 परियोजनाएं विलंबित हैं। माह के दौरान 14 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 9 मेगा परियोजनाएं हैं। इन 14 परियोजनाओं में से 3 परियोजना के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 1 परियोजना के संबंध में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 6 परियोजनाओं के संबंध में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'तपोवन-विष्णुगाड़ एचईपी (4X130 मे.वा.), एनटीपीसी' तथा 'सासन अल्ट्रा से संबद्ध पारेषण प्रणाली, पीजीसीआईएल' परियोजनाओं के संबंध में क्रमशः भू-वैज्ञानिक गतिविधियों तथा चीन से ट्रांसफार्मर की आपूर्ति में विलम्ब के कारण 6 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'उत्तर-पूर्व तथा उत्तर-पश्चिम इंटर कनेक्टर I परियोजना, पीजीसीआईएल' तथा 'ओआरआई में फेज-I जनरेशन परियोजना के लिए पारेषण प्रणाली, पीजीसीआईएल' के संबंध में क्रमशः कानून और व्यवस्था एवं वन संबंधी स्वीकृति के कारण प्रत्येक में 6 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है।

(iii) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 149 परियोजनाओं में से 89 परियोजनाएं विलंबित हैं। माह के दौरान 17 परियोजनाओं के संबंध में 1-15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 मेगा परियोजनाएं हैं। इन 17 परियोजनाओं में से 6 परियोजनाओं के संबंध में प्रत्येक में 1 माह, 4 परियोजनाओं के संबंध में प्रत्येक में 3 माह, 1 परियोजना के संबंध में 4 माह, तथा 2 परियोजनाओं के संबंध में क्रमशः 6 तथा 8 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'सिलचर-उदरबंद (पीएच-II) एनएच-54, 309 कि.मी. से 275 कि.मी., एनएचएआई' कोटला से देवपुर (10 एलएमएनएचपी), एनएच-28 फेज़-II 440 कि.मी. से 402 कि.मी., एनएचएआई एवं 'गुजरात/महाराष्ट्र सीमा सूरत-हजीरा पोर्ट स्टेशन, एनएचएआई' परियोजनाओं के संबंध में प्रत्येक में 9 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। 'कुंझपुर-सुरतकल और मंगलौर, एनएचएआई,' परियोजना के संबंध में 15 माह के अतिरिक्त विलम्ब की सूचना प्राप्त हुई है। परियोजना कार्यान्वयन एजेंसी ने इन परियोजनाओं में विलम्ब के लिए किसी विशेष कारण का उल्लेख नहीं किया है। तथापि, इन परियोजनाओं में विलम्ब के कारण भूमि अधिग्रहण में विलम्ब, वन तथा पर्यावरण संबंधी स्वीकृति में विलम्ब, जनोपयोगी सुविधाओं के प्रतिस्थापन की समस्या, ठेकेदारों का घटिया कार्य निष्पादन आदि हैं।

9. दिनांक 31.03.2013 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपए तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में दर्शाई गई है।

10. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for March 2013 contains information on the status of the 558 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During March 2013, 12 projects (5 projects in Road transport & Highways, 4 projects in Petroleum and 3 projects in Power Sector) have reported completion.

2. During the reference month, out of 558 projects, 272 projects are delayed with respect to latest schedule and 59 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 59 projects, 25 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 36 months in respect of projects relating to Fertilizers, Shipping & Ports, Coal, Steel, Railways, Petroleum, Power and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Road Transport & Highways	149	89	17	2
2.	Railways	124	36	8	4
3.	Power	101	53	14	9
4.	Petroleum	67	36	10	4
5.	Coal	51	28	3	1
6.	Shipping & Ports	19	4	2	2
7.	Steel	17	13	4	2
8.	Telecommunications	13	5	0	0
9.	Civil Aviation	6	3	0	0
10.	Atomic Energy	4	3	0	0
11.	Urban Development	4	1	0	0
12.	Fertilizers	1	1	1	1
13.	Petrochemicals	1	0	0	0
14.	Water Resources	1	0	0	0
Total		558	272	59	25

3. Total original cost of implementation of the 558 projects was about ₹ 7,89,713.63 crore and their anticipated completion cost is likely to be ₹ 9,29,738.10 crore, which reflects an overall cost overruns of ₹ 1,40,024.47 crore (17.70 % of original cost). The expenditure incurred on these projects till March 2013 is ₹ 4,47,761.07 crore, which is 48.20 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-03-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Out of the 558 projects, 2 projects are ahead of schedule, 170 are on schedule and 272 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 285 if delay is calculated on the basis of original schedule of completion. Further, 20 projects have been sanctioned without any commissioning schedule/date and for 94 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 272 delayed projects, 68 projects have overall delay in the range of 1 to 12 months, 68 projects have a delay in the range of 13 to 24 months, 79 projects have a delay in the range of 25 to 60 months and 57 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-03-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI- GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
3	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
5	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

5. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in equipment erection, supply of material, geological surprises, change in scope of work, ROU/ROW problems, law and order, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-03-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		EXPENDITURE CUMULATIVE (₹ ; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADAN GA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

7. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-03-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.03.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

8. **The Sector-wise details of delays/additional delays are as under:-**

i) In the **Fertilizers Sector**, during the month 'Nangal - Ammonia Plant Feedstock Project, NFL' has reported additional delays of 2 months. However, no specific reasons have been reported by the project authorities for delay in this project.

ii) In the **Shipping & Ports Sector**, out of 19 projects, 4 projects are delayed and 2 projects have reported additional delays. The projects 'Setting up of LNG Regasification Terminal at Puthu, Port Trust' and 'Construction. & Development of 2 Offshore Container Berths & Terminal, Mumbai Port Trust' have reported additional delay of 1 and 4 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

iii) In the **Coal Sector**, out of 51 projects, 28 projects are delayed. During the month 3 projects have reported additional delays in the range of 4-24 months, out of which 1 is a Mega project. The project 'TPS-II Expansion (1470MW TO 1970MW), NLC' has reported additional delay of 4 months due to delay in equipment erection. The projects 'Kaniha OCP, MCL, (10.0 MTY)' and 'Hingula OC-II EXP PH-III (15 MTY), MCL' have reported additional delay of 24 months each due to delay in forest clearance.

iv) In the **Steel Sector**, out of 17 projects, 13 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-6 months, out of which 2 are Mega project. The projects '330 TPH Boiler-6 and Auxiliary System, RINL' and 'Installation of 1x45 MVA Submerged Arc Furnace, SAIL' have reported additional delay of 1 and 3 months respectively. The Projects 'Expansion of IISCO Steel Plant, SAIL' and 'Expansion of Bokaro Steel Plant, SAIL' have reported additional delay of 6 months each. However, no specific reasons have been reported by the project authorities for delay in these projects

v) In the **Railways Sector**, out of 124 projects, 36 projects are delayed. During the month 8 projects have reported additional delays in the range of 1-36 months, out of which 4 are Mega projects. Of these 8 projects, 2 projects have reported additional delay of 1 and 3 month respectively, 2 projects have reported additional delay of 6 and 12 months respectively and 2 projects have reported additional delay of 16 months each; the project 'Bhairabi Sairong, NL, NEFR' has reported additional delay of 36 months due to forest

clearance. The project 'New Work for Construction of Metro railway from Baranagar to Barraackpore, RVNL' has reported additional delay of 24 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vi) In the **Petroleum Sector**, out of 67 projects, 36 projects are delayed. During the month 10 projects have reported additional delays in the range of 1-6 months, out of which 3 are Mega projects. Of these 10 projects, 3 projects have reported additional delay of 1 month and 3 projects have reported additional delay of 2 months. The projects 'IOR, Rudrasagar, ONGC' has reported additional delay of 3 month due to change in scope of work and 'Paradip Refinery Project, IOCL' has reported additional delay of 6 months due to law & order. The projects 'Diesel Hydrotreator Project at Visakh Refinery, HPCL' and 'Polypropylene unit Mangalore Refinery' have reported additional delay of 3 and 4 months respectively due to delay in forest clearance.

vii) In the **Power Sector**, out of 101 projects, 53 projects are delayed. During the month 14 projects have reported additional delays in the range of 1-6 months, out of which 9 are Mega projects. Of these 14 projects, 3 projects have reported additional delay of 1 month each, 1 project has reported additional delay of 2 months and 6 projects have reported additional delay of 3 months each; the projects 'Tapovan-Vishnugad HEP (4x130MW), NTPC' and 'Transmission System Associated with Sasan Ultra, PGCIL' have reported additional delay of 6 months each due to geological surprises and delay in supply of transformer from China respectively. The projects 'North- East North Western Interconnector I Project, PGCIL' and 'Transmission System for Phase-I Gen. Project in ORI, PGCIL' have reported additional delay of 6 months each due to law & order and forest clearance respectively.

viii) In the **Road Transport & Highways Sector**, out of 149 projects, 89 are delayed. During the month 17 projects have reported additional delays in the range of 1-15 months, out of which 2 are Mega Projects. Of these 17 projects, 6 projects have reported additional delay of 1 month each, 4 projects have reported additional delay of 3 months each, 1 project has reported additional delay of 4 months and 2 projects have reported additional delay of 6 and 8 months respectively; the projects 'Silchar-Udarband (PH.II) HN-54, KM.309 TO KM.275, NHAI', 'Kotwa to Dewapur (10 LMNHP), NH-28 Phase-II, KM.440 TO KM.402, NHAI' and 'Gujarat/Maharashtra Border Surat-Hazira Port Section, NHAI' have reported additional delay of 9 months each. The project 'Kundupur-Surathkal & Manglor, NHAI' has reported additional delay of 15 months. The project implementing agency has not mentioned any specific reasons for delay in these projects. However,

general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

9. The status as on 31.03.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

10. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Road Transport & Highways	149	17
2	Railways	124	8
3	Power	101	14
4	Petroleum	67	10
5	Coal	51	3
6	Shipping & Ports	19	2
7	Steel	17	4
8	Telecommunications	13	0
9	Civil Aviation	6	0
10	Atomic Energy	4	0
11	Urban Development	4	0
12	Fertilisers	1	1
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	558	59

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2012				
<u>Power</u>				
1	KOTESHWAR HEP(THDC)(TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	1438
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C(SHIPPING crp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH(SHIPPING crp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G)(BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000Lines (2G) 383000 lines 3((BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May,2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT(RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON(BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
<u>Railways</u>				
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
<u>Road Transport & Highways</u>				
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
<u>Shipping & Ports</u>				
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
June,2012				
<u>Steel</u>				
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
<u>Power</u>				
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	3779.46
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
<u>Railways</u>				
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
<u>Road Transport & Highways</u>				
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300]	225.00	10/2008	261.9
July,2012				
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096]	196.97	03/2011	218.66
	August,2012			
	<u>Steel</u>			
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
	<u>Power</u>			
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
	<u>Road Transport & Highways</u>			
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235]	193.09	03/2008	189.15
	September,2012			
	<u>Petroleum</u>			
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
	<u>Telecommunications</u>			
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84
	October,2012			
	<u>Road Transport & Highways</u>			
37	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93- 149.25, NH-24(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106204]	275.00	09/2007	306.65
38	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106301]	151.30	10/2008	190.61

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
November,2012				
<u>Petroleum</u>				
39	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC(GAS AUTHORITY OF INDIA LIMITED) - [N16000071]	348.00	03/2012	203.31
December,2012				
<u>Fertilisers</u>				
40	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS(NATIONAL FERTILISER LIMITED) - [N08000007]	325.00	07/2011	185.1
41	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ(NATIONAL FERTILISER LIMITED) - [N08000008]	438.00	07/2011	239.93
<u>Power</u>				
42	WESTERN REGION STRENGTHENING SCHEME-II(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000022]	5,221.23	07/2010	3175.3
<u>Railways</u>				
43	MUMBAI URBAN TRANSPORT PROJECT PHASE- I(METROPOLITAN RAPID TRANSPORT PROJECTS) - [N22000093]	3,125.20	06/2011	4334
<u>Road Transport & Highways</u>				
44	DAKOPA TO NAGAON (NH-36)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106288]	225.00	06/2008	285.2
45	JHAJHARPUR TO DARBANGA (BR-7)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000031]	340.00	09/2008	575.32
46	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000118]	464.00	01/2011	535.62
47	Hyderabad-yadgiri N.H no-202(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000142]	388.00	05/2012	537.91
<u>Shipping & Ports</u>				
48	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA(SHIPPING crp. of india) - [N25000031]	1,066.91	09/2012	1027.12
January,2013				
<u>Fertilisers</u>				
49	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJE(NATIONAL FERTILISER LIMITED) - [N08000004]	1,292.84	01/2013	987.72
50	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEVER PROJ(NATIONAL FERTILISER LIMITED) - [N08000005]	1,294.19	01/2013	972.95
<u>Railways</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
51	REWARI-ROHTAK (NL),NR(NORTHERN RAILWAY) - [220100279]	149.38	02/2010	508.76
52	PODAPAHAR-BANSPANI,(LD)(SER)(SOUTH EASTERN RAILWAY) - [N22000046]	129.74	03/2006	162.27
February,2013				
<u>Atomic Energy</u>				
53	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP(URANIUM CORPORATION OF INDIA LIMITED) - [N02000007]	1,106.29	04/2011	1084.24
<u>Petroleum</u>				
54	COMPRESSOR STATIONS (KAILARAS AND CHAINSA)(GAS AUTHORITY OF INDIA LIMITED) - [N16000054]	1,167.00	04/2011	715.73
55	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000073]	4,543.43	03/2012	1709.62
56	EURO-IV DHDT(CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000109]	2,615.69	05/2010	1981.03
57	CDU/VDU-II(CHENNAI PETROLEUM CORPORATION LIMITED) - [N16000110]	333.99	10/2012	228.26
<u>Railways</u>				
58	ELECTRIFICATION OF MORADABAD-ROZA(RAILWAY ELECTRIFICATION) - [N22000095]	129.17	03/2011	227.48
<u>Road Transport & Highways</u>				
59	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240101173]	367.49	03/2005	453.68
60	TUTICORIN-PORT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000217]	182.25	02/2013	N.A.
<u>Shipping & Ports</u>				
61	Acquisition of two nos. of 120 B.P BY 079& 080(SHIPPING crp. of india) - [N25000042]	290.85	06/2011	294.52
March,2013				
<u>Petroleum</u>				
62	CONSTRUCTION OF NEW PROCESS COMPLEX MHN(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000030]	2,853.29	05/2010	5659.05
63	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000065]	370.11	04/2011	279.73
64	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES(INDIAN OIL CORPORATION LIMITED) - [N16000090]	1,492.33	06/2012	1219.5
65	Construction of tanks and blending facility at Vad(INDIAN OIL CORPORATION LIMITED) - [N16000115]	267.00	09/2012	224.41
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
66	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000064]	297.37	07/2011	338.93
67	System Strengthening -X of SR(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000086]	276.61	04/2012	170.6
68	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000090]	779.21	08/2013	756.5
<u>Road Transport & Highways</u>				
69	SAGAR - RAJMARG CHORAH,KM 211 TO KM 255, NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106303]	203.43	10/2008	256.53
70	RAJMARG CHORAH TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106305]	229.91	10/2008	289.95
71	ASSAM/WB BORDER TO GAIRKATTA (WB-1)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000045]	221.82	11/2008	299.96
72	MP/Maharashtra Border-Dhula(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000126]	835.00	06/2012	1068.7
73	Hyderabad-Vijaywada Km. 40 to 221.50 Km(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000134]	1,740.00	10/2012	1944.2

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
March,2013				
<u>Telecommunications</u>				
1	Execution of telecom network requirement of defence(BHARAT SANCHAR NIGAM LIMITED) - [180100184]	1,077.00	03/2009	.00
2	GSM equipment of 200000Lines (2G) UP(West)Phase V.(BHARAT SANCHAR NIGAM LIMITED) - [N18000049]	336.84	10/2009	35.75


Summary of projects in the Flash Report for the month of March, 2013

I. Project Implementation - Current Status:

Number of Projects in Previous Month	564
Number of Projects completed/dropped/frozen in Current Month	14
Number of Projects not Reported in Current Month	1
Number of Projects Added in Current Month	9
Number of Projects in Current Month	558


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 558 projects, 3 projects are ahead of schedule, 156 projects are on schedule and 285 projects are delayed. Of the balance, 94 projects do not have fixed dates of commissioning while 20 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

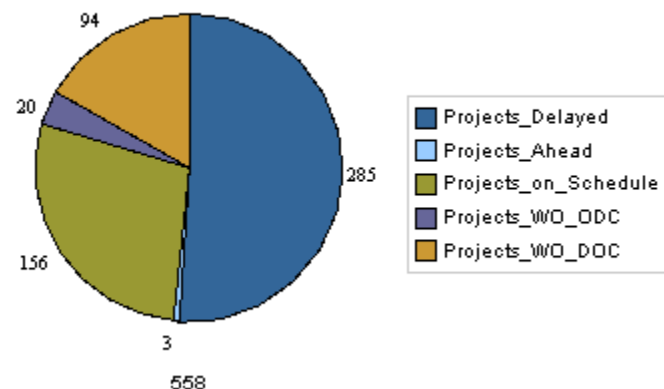

III. Investment Scenario

The Total Original cost of implementation of 558 projects when sanctioned, was of the order of Rs. 789713.63 crore but this was subsequently revised to Rs. 929738.1 crore implying a cost overrun of 17.7%. The expenditure incurred on these projects till March, 2013 is Rs. 447761.07 crore, which is 48.2% of the revised cost of the projects.

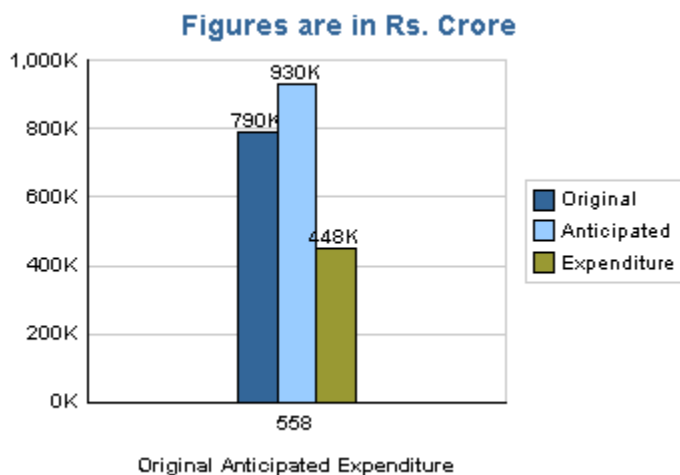

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	564
No of Projects Completed/Dropped/Frozen in Current Month	14
No of Projects not reported in Current Month	1
No of Projects added in Current Month	9
No of Projects in Current Month	558

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	285	3	156	20	94	558	51.08
Latest Approved (Date)	272	2	170	20	94	558	48.75

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	416	670,612.52	708,374.55	315,506.78	44.50	37,762.03	5.60
Latest Approved (RCE)	142	172,658.59	221,363.55	132,254.29	59.70	48,704.96	28.20
Total (RCE)	558	843,271.11	929,738.10	447,761.07	48.16	86466.99	10.25
Original Cost of All Projects							
Original Cost	558	789,713.63	929,738.10	447,761.07	48.20	140,024.47	17.70

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	285	475,041.19	569,841.52	347,325.53	61.00	94,800.33	20.00
Latest Approved (RCE)	272	483,767.70	544,740.25	333,391.32	61.20	60,972.55	12.60

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	59	129,437.28	142,512.13	98,202.14	68.90	13,074.85	10.10

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,510.5	4.0	7	8,579.5	10,631.3	23.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	67	164,236.7	173,456.8	5.6	15	51,418.8	67,064.6	30.4
8	Power	101	243,054.8	258,796.1	6.5	18	45,722.0	61,463.3	34.4
9	Railways	124	60,590.8	147,761.5	143.9	107	39,439.2	126,656.5	221.1
10	Road Transport & Highways	149	101,529.8	103,468.4	1.9	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	9	8,629.0	11,218.5	30.0
12	Telecommunications	13	5,699.2	5,506.3	-3.4	2	477.3	550.9	15.4
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		558	789,713.6	929,738.1	17.7	183	214,545.1	362,422.7	68.9

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	33	27,471.8	35,095.6	27.8	14	12,420.0	20,910.9	68.4
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	2	6,441.3	11,073.4	71.9
3	Assam	34	22,035.9	35,386.1	60.6	12	10,491.8	23,936.0	128.1
4	Bihar	30	26,917.6	34,877.4	29.6	14	12,668.3	20,628.1	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	33,405.1	33,607.0	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	8	4,054.4	5,741.0	41.6	2	1,298.8	2,985.5	129.9
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	26	46,344.4	55,830.8	20.5	9	8,598.8	18,491.8	115.1
11	Kerala	7	20,376.7	21,818.2	7.1	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	20	18,545.6	18,826.2	1.5	2	1,110.9	1,810.9	63.0
13	Maharashtra	48	88,574.5	99,360.8	12.2	14	24,995.9	38,254.1	53.0
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Odisha	30	56,171.6	61,152.9	8.9	12	32,671.6	37,652.9	15.2
19	Punjab	6	3,542.0	4,483.8	26.6	2	532.4	1,474.2	176.9
20	Rajasthan	14	21,115.8	20,928.0	-0.9	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	48,788.1	59,567.9	22.1	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	24	20,316.1	24,537.7	20.8	9	3,670.1	7,940.1	116.3
25	West Bengal	26	42,064.3	54,403.5	29.3	16	22,998.0	35,337.2	53.7
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	25	58,429.8	59,712.9	2.2	6	1,548.3	2,831.4	82.9
28	Jharkhand	23	14,447.4	18,632.5	29.0	7	2,225.5	6,582.4	195.8
29	Uttarakhand	5	7,624.2	8,564.6	12.3	2	2,640.7	3,581.2	35.6
30	Multi State	110	146,099.9	157,392.0	7.7	20	10,203.9	24,093.9	136.1
Total		558	789,713.6	929,738.1	17.7	183	214,545.1	362,422.7	68.9

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	13 - 35
3	Coal	51	36,056.5	37,510.5	4.0	28	24,262.9	26,136.6	16 - 72
4	Fertilisers	1	1,478.6	1,478.6	0.0	1	1,478.6	1,478.6	2 - 2
5	Steel	17	65,285.9	71,443.4	9.4	15	64,698.3	70,855.9	4 - 44
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	67	164,236.7	173,456.8	5.6	39	111,742.9	121,838.0	1 - 120
8	Power	101	243,054.8	258,796.1	6.5	53	135,655.6	150,492.0	1 - 102
9	Railways	124	60,590.8	147,761.5	143.9	41	27,923.9	73,536.6	3 - 235
10	Road Transport & Highways	149	101,529.8	103,468.4	1.9	89	48,537.7	50,476.4	2 - 110
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	6	6,413.2	7,718.8	5 - 87
12	Telecommunications	13	5,699.2	5,506.3	-3.4	5	2,934.9	2,760.6	25 - 53
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		558	789,713.6	929,738.1	17.7	285	475,041.2	569,841.5	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	33	27,471.8	35,095.6	27.8	12	16,701.0	20,510.4	4 - 44
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	3	9,356.2	13,737.9	25 - 87
3	Assam	34	22,035.9	35,386.1	60.6	31	20,716.4	33,237.3	12 - 120
4	Bihar	30	26,917.6	34,877.4	29.6	13	20,676.7	25,738.9	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	13 - 13
6	Gujarat	22	33,405.1	33,607.0	0.6	6	15,731.6	15,723.8	9 - 24
7	Haryana	8	4,054.4	5,741.0	41.6	4	2,216.6	3,396.6	3 - 50
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	25 - 102
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	8	13,205.0	32,811.9	10 - 201
10	Karnataka	26	46,344.4	55,830.8	20.5	11	23,834.8	28,819.5	6 - 106
11	Kerala	7	20,376.7	21,818.2	7.1	5	19,581.0	20,231.0	5 - 58
12	Madhya pradesh	20	18,545.6	18,826.2	1.5	10	9,535.0	9,535.0	5 - 69
13	Maharashtra	48	88,574.5	99,360.8	12.2	25	49,293.1	55,402.6	5 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	72 - 72
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 35
17	Nagaland	1	850.0	850.0	0.0	1	850.0	850.0	24 - 24
18	Odisha	30	56,171.6	61,152.9	8.9	16	49,397.9	50,455.8	3 - 135
19	Punjab	6	3,542.0	4,483.8	26.6	3	2,467.6	2,542.6	2 - 64
20	Rajasthan	14	21,115.8	20,928.0	-0.9	7	15,830.9	15,384.6	3 - 59
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 35
22	Tamil Nadu	32	48,788.1	59,567.9	22.1	12	31,380.8	37,311.4	4 - 87
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,101.4	1,395.4	10 - 21
24	Uttar Pradesh	24	20,316.1	24,537.7	20.8	13	11,676.4	14,150.9	7 - 84
25	West Bengal	26	42,064.3	54,403.5	29.3	15	27,157.6	34,327.7	3 - 141
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	-
27	Chhatisgarh	25	58,429.8	59,712.9	2.2	9	23,484.9	23,796.2	12 - 59
28	Jharkhand	23	14,447.4	18,632.5	29.0	11	9,235.3	10,132.7	5 - 100
29	Uttarakhand	5	7,624.2	8,564.6	12.3	4	6,097.2	7,037.6	5 - 48
30	Multi State	110	146,099.9	157,392.0	7.7	53	77,913.2	84,288.3	1 - 235
Total		558	789,713.6	929,738.1	17.7	285	475,041.2	569,841.5	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	13 - 35
3	Coal	51	36,056.5	37,510.5	4.0	28	24,262.9	26,136.6	16 - 72
4	Fertilisers	1	1,478.6	1,478.6	0.0	1	1,478.6	1,478.6	2 - 2
5	Steel	17	65,285.9	71,443.4	9.4	13	63,227.8	69,385.3	4 - 44
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	67	164,236.7	173,456.8	5.6	36	107,812.5	115,809.9	1 - 87
8	Power	101	243,054.8	258,796.1	6.5	53	135,655.6	150,492.0	1 - 102
9	Railways	124	60,590.8	147,761.5	143.9	36	21,671.5	65,986.8	3 - 235
10	Road Transport & Highways	149	101,529.8	103,468.4	1.9	89	48,537.7	50,476.4	2 - 110
11	Shipping & Ports	19	15,617.1	17,902.4	14.6	4	5,650.5	6,586.0	5 - 40
12	Telecommunications	13	5,699.2	5,506.3	-3.4	5	2,934.9	2,760.6	25 - 53
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		558	789,713.6	929,738.1	17.7	272	457,164.6	544,740.3	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,510.5	1.3	6	7,115.6	7,603.7	6.9
4	Fertilisers	1	1,478.6	1,478.6	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	67	176,275.2	173,456.8	-1.6	2	30,602.0	32,253.0	5.4
8	Power	101	246,570.5	258,796.1	5.0	14	39,450.6	51,676.2	31.0
9	Railways	124	89,687.6	147,761.5	64.8	78	44,076.7	102,182.2	131.8
10	Road Transport & Highways	149	101,696.3	103,468.4	1.7	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	17,389.4	17,902.4	3.0	6	3,312.5	4,036.9	21.9
12	Telecommunications	13	5,699.2	5,506.3	-3.4	2	477.3	550.9	15.4
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		558	843,271.1	929,738.1	10.3	128	163,192.3	255,017.3	56.3

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	51	36,056.46	37,510.52	4.03	0	0.00	0.00	0- 0
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	18- 18
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	67	164,236.71	173,456.75	5.61	11	21,026.22	34,678.96	13- 120
8	Power	101	243,054.78	258,796.07	6.48	2	2,253.45	3,986.02	0- 76
9	Railways	124	60,590.79	147,761.45	143.87	18	6,330.26	24,861.61	0- 141
10	Road Transport & Highways	149	101,529.76	103,468.38	1.91	0	0.00	0.00	0- 0
11	Shipping & Ports	19	15,617.12	17,902.42	14.63	5	5,400.70	6,860.25	10- 87
12	Telecommunications	13	5,699.24	5,506.32	-3.39	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		558	789713.63	929738.1	17.73	39	42575.13	81929.01	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	22- 22
3	Coal	51	36,056.46	37,510.52	4.03	5	7,938.86	9,942.56	16- 55
4	Fertilisers	1	1,478.63	1,478.63	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	8- 44
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	67	164,236.71	173,456.75	5.61	12	49,613.82	63,945.58	13- 120
8	Power	101	243,054.78	258,796.07	6.48	15	44,083.26	58,919.67	7- 102
9	Railways	124	60,590.79	147,761.45	143.87	34	17,757.78	63,375.37	12- 235
10	Road Transport & Highways	149	101,529.76	103,468.38	1.91	11	3,324.28	5,445.20	21- 108
11	Shipping & Ports	19	15,617.12	17,902.42	14.63	4	5,580.00	6,965.50	15- 87
12	Telecommunications	13	5,699.24	5,506.32	-3.39	1	149.15	158.72	48- 48
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		558	789713.63	929738.1	17.73	92	179445.16	279093.03	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

S.no	Project	DOA	Original		Now anticipated		Final
			Cost	DOC	Cost	DOC	Expenditure
<u>Petroleum</u>							
1	CONSTRUCTION OF NEW PROCESS COMPLEX MHN	01/2007	2,853.29	05/2010	6,326.40	03/2013	5,659.05
2	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA	02/2008	370.11	04/2011	370.11	03/2013	279.73
3	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES	12/2009	1,492.33	06/2012	1,492.33	03/2013	1,219.50
4	Construction of tanks and blending facility at Vad	02/2009	267.00	09/2012	267.00	03/2013	224.41
<u>Power</u>							
5	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	04/2008	297.37	07/2011	386.32	03/2013	338.93
6	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM	12/2010	779.21	08/2013	779.21	03/2013	756.50
7	System Strengthening -X of SR	12/2009	276.61	04/2012	276.61	03/2013	170.60
<u>Road Transport & Highways</u>							
8	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	12/2003	203.43	10/2008	203.43	03/2013	256.53
9	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	12/2003	221.82	11/2008	221.82	03/2013	299.96
10	Hyderabad-Vijaywada Km. 40 to 221.50 Km	04/2010	1,740.00	10/2012	1,740.00	03/2013	1,944.20
11	MP/Maharashtra Border-Dhula	12/2009	835.00	06/2012	835.00	03/2013	1,068.70
12	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	12/2003	229.91	10/2008	229.91	03/2013	289.95
<u>Telecommunications</u>							
13	Execution of telecom network requirement of defence	05/2006	1,077.00	03/2009	1,077.00	N.A.	.00
14	GSM equipment of 200000Lines (2G) UP(West)Phase V.	10/2008	336.84	10/2009	336.84	N.A.	35.75

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC
	<u>Power</u>					
1	COMMON TR. SYS. ASSOCIATED WITH EAST A.P	3/2013	514.20	6/2015	514.20	6/2015
2	COMMON SYS. ASSOCIATED PART- B	3/2013	2,514.88	12/2015	2,514.88	12/2015
	<u>Road Transport & Highways</u>					
3	FOUR LANING OF ORISSA CHATTISHGARH BORDER	2/2013	1,232.00	8/2015	1,232.00	8/2015
4	ETAWAH CHAKERI	3/2013	1,573.00	9/2015	1,573.00	9/2015
5	2 LANING WITH PS AGRA ALIGARH	10/2012	250.50	10/2014	250.50	10/2014
6	2 LANING WITH PS KANPUR KABRAI	1/2013	373.47	7/2014	373.47	7/2014
7	AHMEDABAD TO VADODARA SECTION	1/2013	2,125.24	12/2015	2,125.24	12/2015
8	SAMAIKHALI GANDHIDHAM	9/2010	805.39	12/2013	805.39	12/2013
9	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	1,928.22	4/2015	1,928.22	4/2015

VII. Milestones (Cumulative due & achieved)

Total	3359
Achieved up to month	1235

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay
		Original	Anticipated	Original	Last month	This month	(in months)
<u>Coal</u>							
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	3,027.59	06/2009	09/2013	01/2014	4
2	KANIHA OCP, MCL, (10.0 Mty) MCL	457.77	457.77	03/2013	03/2013	03/2015	24
3	HINGULA OC-II EXP PH-III (15 MTY) MCL	479.63	479.63	03/2013	03/2013	03/2015	24
<u>Fertilisers</u>							
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT NFL	1,478.63	1,478.63	01/2013	01/2013	03/2013	2
<u>Steel</u>							
5	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	03/2013	04/2013	1
6	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT SAIL	187.33	187.33	10/2013	12/2013	03/2014	3
7	EXPANSION OF IISCO STEEL PLANT SAIL	14,443.00	16,408.00	12/2011	06/2013	12/2013	6
8	EXPANSION OF BOKARO STEEL PLANT SAIL	6,325.00	6,325.00	12/2011	06/2013	12/2013	6
<u>Petroleum</u>							
9	Up-gradation of Konaban GGS and Pipeline Grid Project ONGC	288.04	253.66	08/2012	05/2013	06/2013	1
10	IOR of B-173A Field ONGC	352.49	352.49	03/2014	03/2014	04/2014	1
11	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE IOCL	586.00	586.00	07/2015	07/2015	08/2015	1
12	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 ONGC	5,713.03	8,813.41	05/2010	03/2013	05/2013	2
13	North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	03/2013	05/2013	2
14	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL	341.50	341.50	02/2013	03/2013	05/2013	2
15	IOR, RUDRASAGAR (ONGCL) ONGC	113.90	438.85	03/2006	03/2013	06/2013	3
16	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	03/2013	06/2013	3
17	Polypropylene unit Mangalore Refin	1,803.78	1,803.78	07/2012	06/2013	10/2013	4
18	PARADIP REFINERY PROJECT IOCL	29,777.00	30,426.00	11/2012	09/2013	03/2014	6
<u>Power</u>							
19	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE NHPC	768.92	1,628.00	03/2007	03/2013	04/2013	1
20	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATHI-III HEP PGCIL	557.24	758.75	01/2010	03/2013	04/2013	1
21	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B PGCIL	160.32	160.32	10/2012	03/2013	04/2013	1
22	765 KV POOLING STATION AND NETWORK WITH DVC AND MA PGCIL	7,075.33	7,075.33	08/2012	01/2014	03/2014	2


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
23	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	06/2013	09/2013	3
24	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	12/2013	03/2014	3
25	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	12/2013	03/2014	3
26	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND PGCIL	2,360.95	2,360.95	08/2012	12/2013	03/2014	3
27	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR PGCIL	2,743.19	2,743.19	12/2013	12/2013	03/2014	3
28	Transmission system for transfer of power from Gen. PGCIL	250.03	250.03	01/2013	03/2014	06/2014	3
29	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	09/2015	03/2016	6
30	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME PGCIL	7,031.88	7,031.88	12/2012	06/2013	12/2013	6
31	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	11,130.19	08/2013	09/2014	03/2015	6
32	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI PGCIL	2,074.86	2,074.86	03/2013	06/2013	12/2013	6
<u>Railways</u>							
33	GADWAL - RAICHUR (NL), SCR SCR	92.63	270.00	02/2011	02/2013	03/2013	1
34	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	03/2013	06/2013	3
35	BANKURA - DAMODAR (GC) (SER) SER	111.90	1,423.98	03/2005	06/2016	12/2016	6
36	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	733.00	1,655.81	12/2008	03/2014	03/2015	12
37	RAJATGARH-BARANG(LD),ECOR RVNL	166.16	288.00	02/2009	04/2013	08/2014	16
38	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) RVNL	133.41	276.00	03/2009	04/2013	08/2014	16
39	New Work for Construction of Metro railway from Ba RVNL	2,069.60	2,298.42	03/2014	03/2014	03/2016	24
40	BHAIRABI SAIRONG, NL, NEFR NEFR	619.34	2,393.49	04/2014	03/2014	03/2017	36
<u>Road Transport & Highways</u>							
41	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	03/2013	04/2013	1
42	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 NHAI	340.68	340.68	03/2008	03/2013	04/2013	1
43	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	03/2013	04/2013	1
44	GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	03/2013	04/2013	1
45	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	03/2013	04/2013	1
46	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	03/2013	04/2013	1
47	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	03/2013	06/2013	3
48	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	03/2013	06/2013	3

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
49	DELHI/ HARYANA BORDER TO ROHTAK NHAI	486.00	486.00	05/2010	03/2013	06/2013	3
50	Hungund-Surathkal and Mangalore-Knt/Kerala Border NHAI	946.00	946.00	N.A.	03/2013	06/2013	3
51	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM NHAI	1,585.00	1,585.00	05/2013	05/2013	09/2013	4
52	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A NHAI	284.00	359.00	05/2008	03/2013	09/2013	6
53	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	03/2013	11/2013	8
54	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 NHAI	157.47	154.57	09/2007	03/2013	12/2013	9
55	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 NHAI	240.00	240.00	10/2008	03/2013	12/2013	9
56	Gujarat/Maharashtra BorderSurat-Hazira Port Section NHAI	1,509.10	1,509.10	09/2012	03/2013	12/2013	9
57	KUNDUPUR-SURATHKAL & MANGLORE NHAI	671.00	671.00	N.A.	03/2013	06/2014	15
<u>Shipping & Ports</u>							
58	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU PORT TRUST	3,500.00	4,150.00	01/2012	03/2013	04/2013	1
59	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER MUMBAI PORT TRU	1,228.00	1,460.00	12/2010	12/2013	04/2014	4

Graphical Analysis of Telecommunications Sector

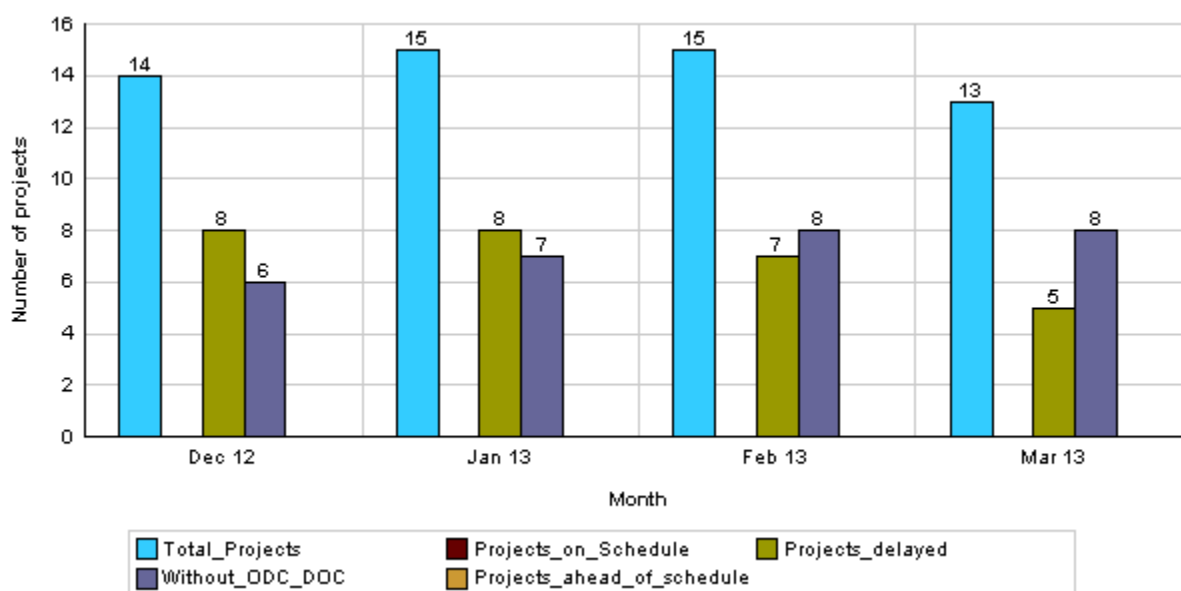


Break-up of 5 Delayed projects in March 2013




Delay in Months



Graphical Analysis of Shipping & Ports Sector

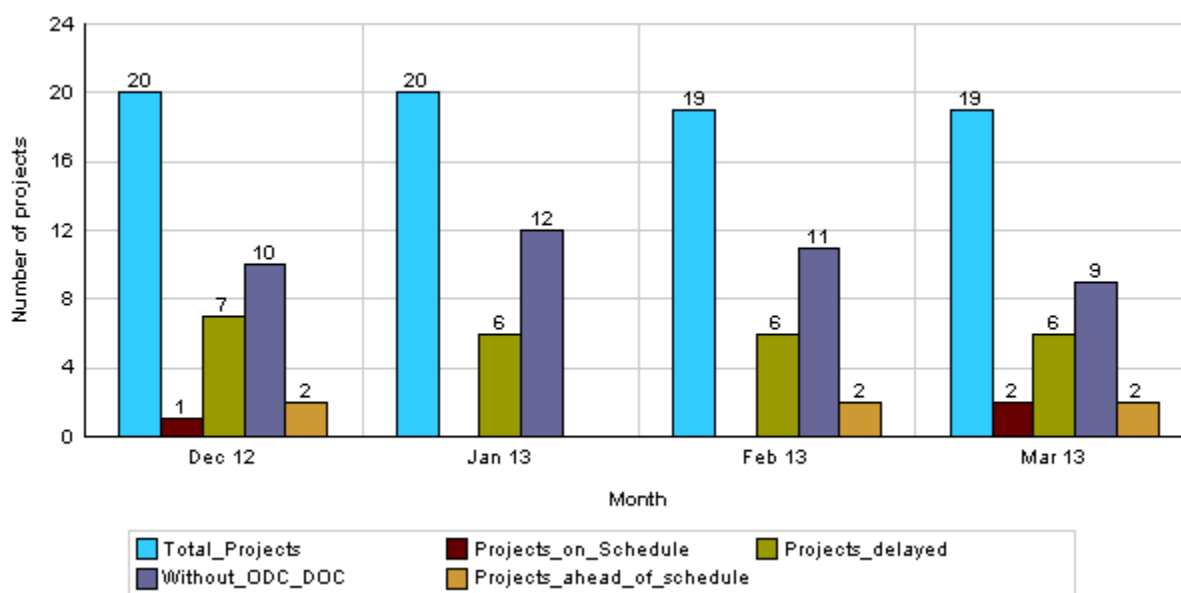


Break-up of 6 Delayed projects in March 2013

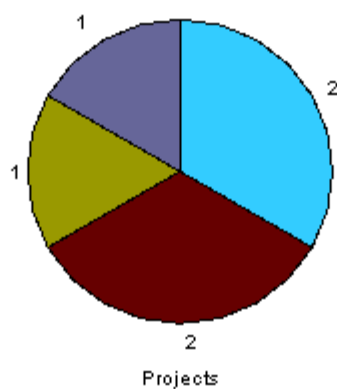


Delay in Months



Graphical Analysis of Road Transport & Highways Sector

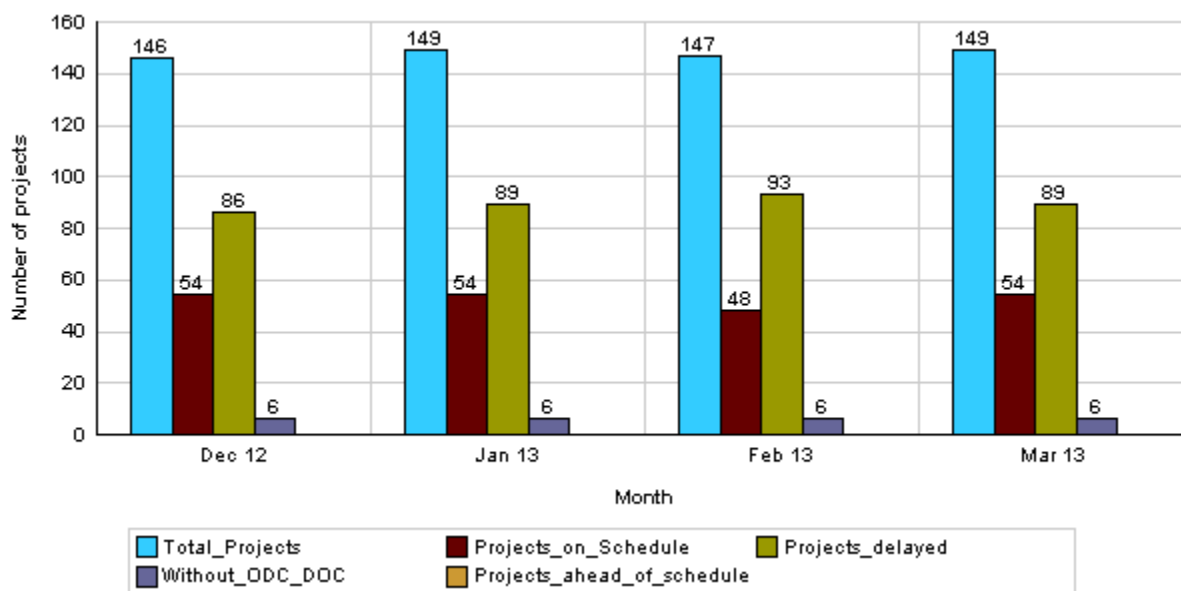


Break-up of 89 Delayed projects in March 2013

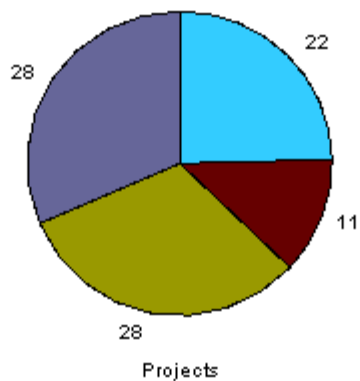


Delay in Months



Graphical Analysis of Railways Sector

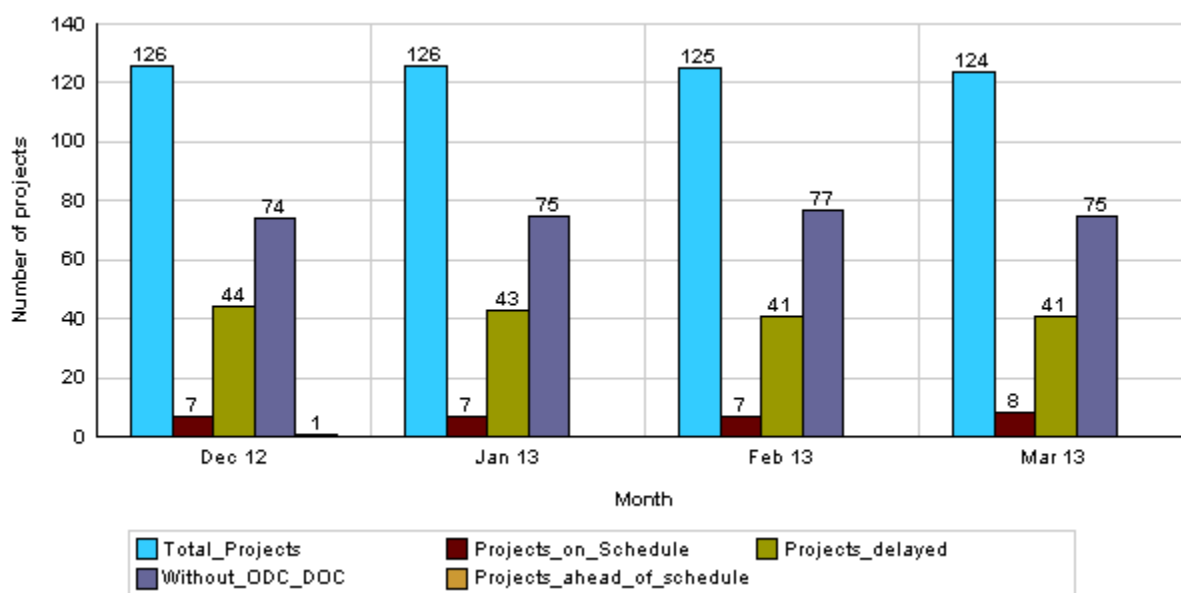


Break-up of 41 Delayed projects in March 2013

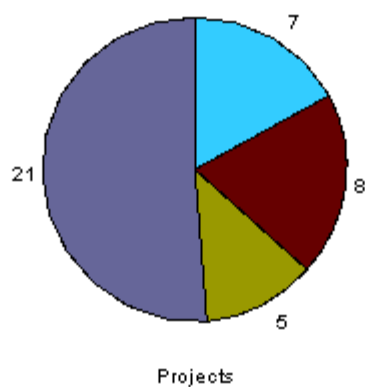


Delay in Months



Graphical Analysis of Power Sector

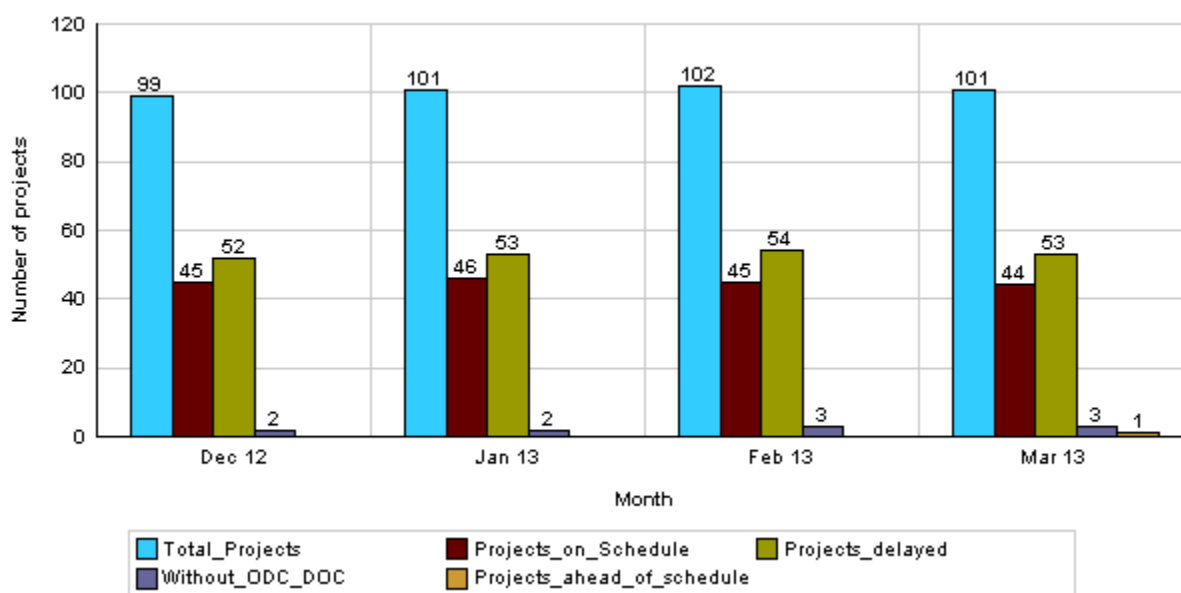


Break-up of 53 Delayed projects in March 2013

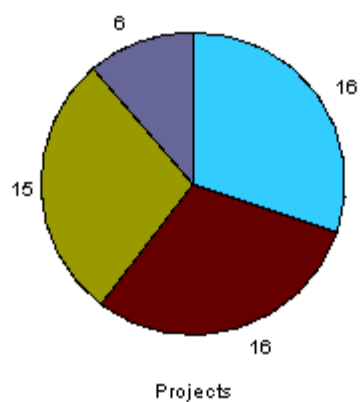


Delay in Months



Graphical Analysis of Petroleum Sector

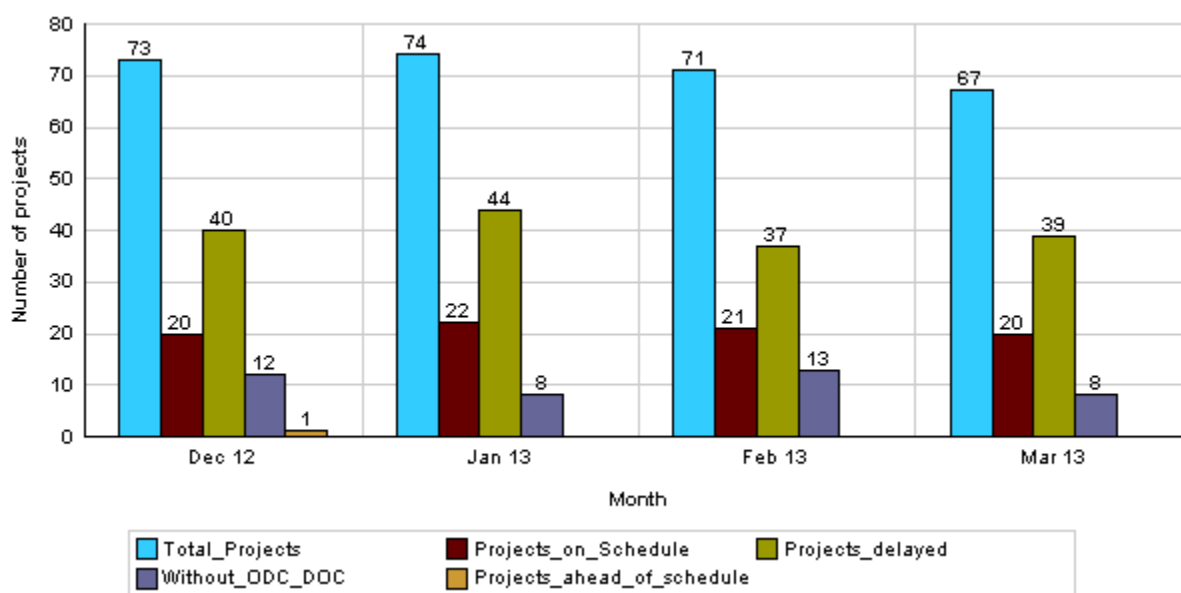


Break-up of 39 Delayed projects in March 2013

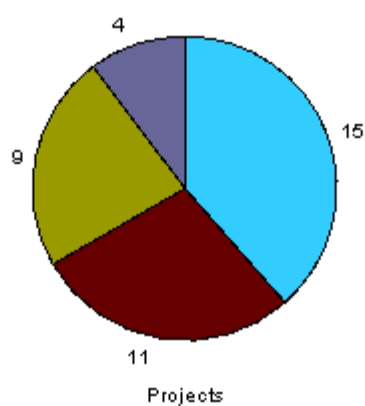


Delay in Months



Graphical Analysis of Steel Sector

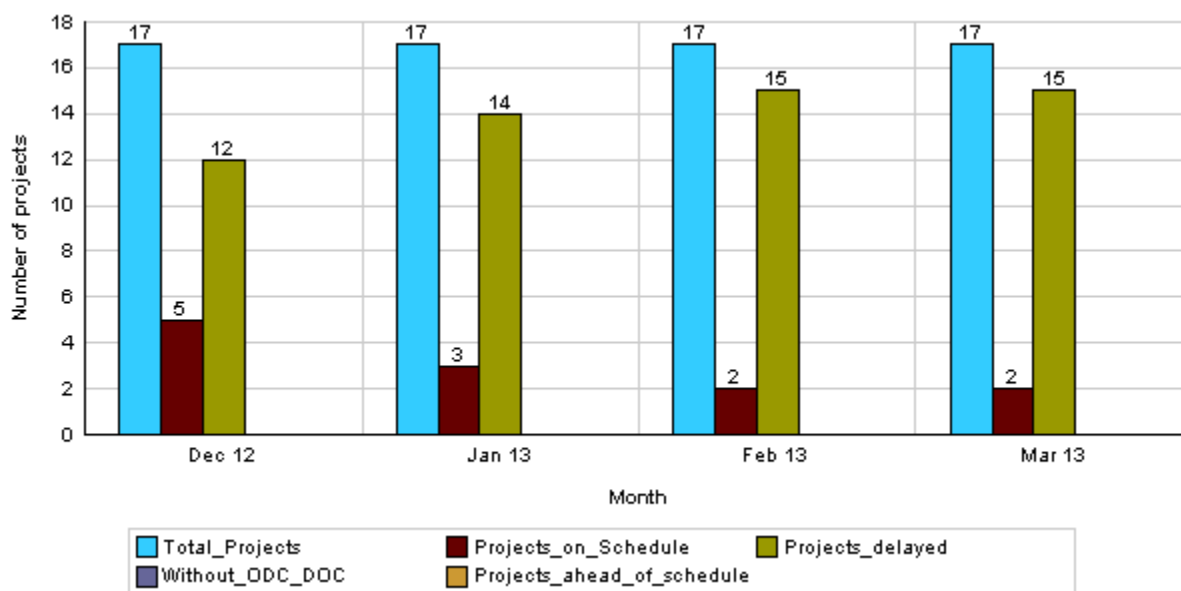


Break-up of 15 Delayed projects in March 2013

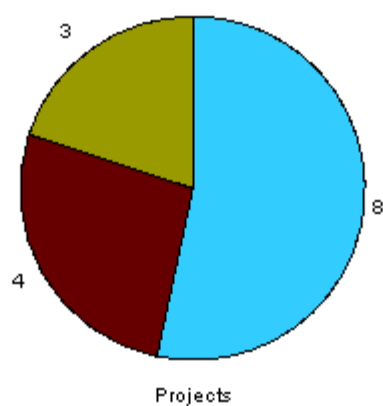


Delay in Months



Graphical Analysis of Coal Sector

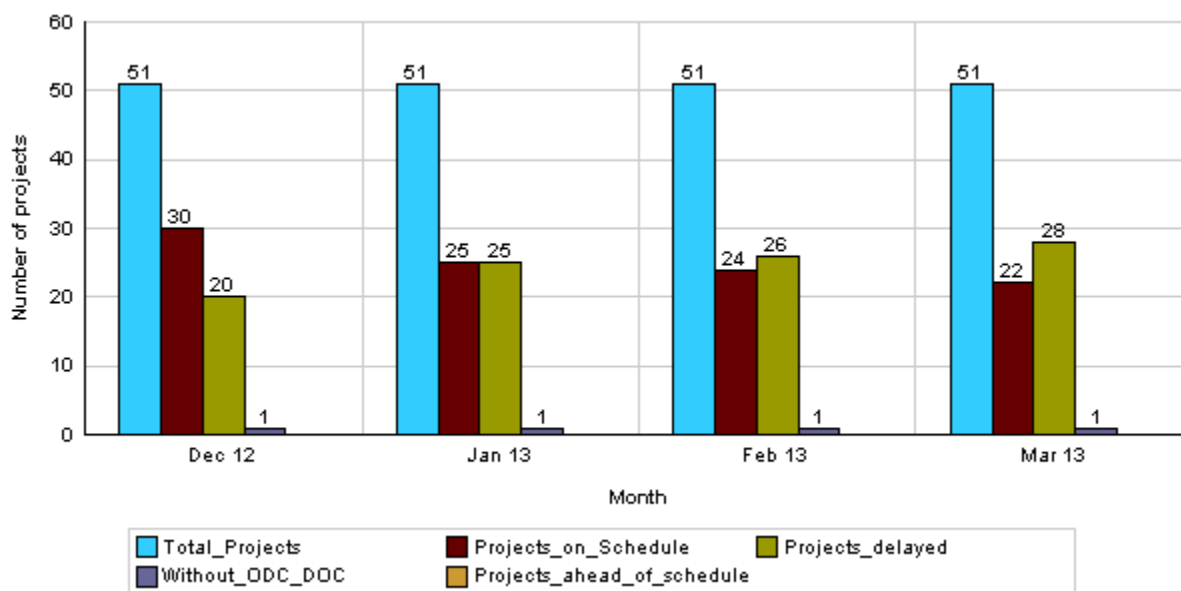


Break-up of 28 Delayed projects in March 2013

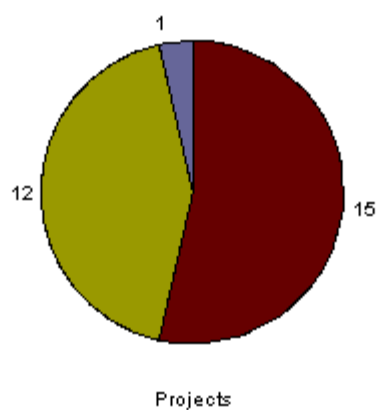


Delay in Months



Graphical Analysis of Civil Aviation Sector

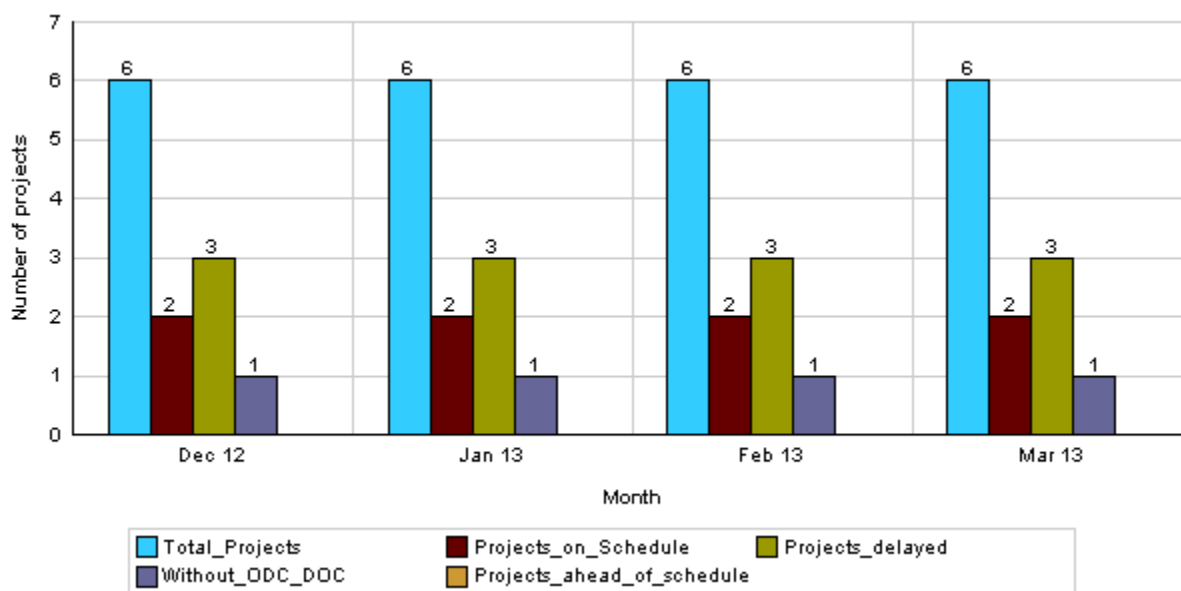


Break-up of 3 Delayed projects in March 2013

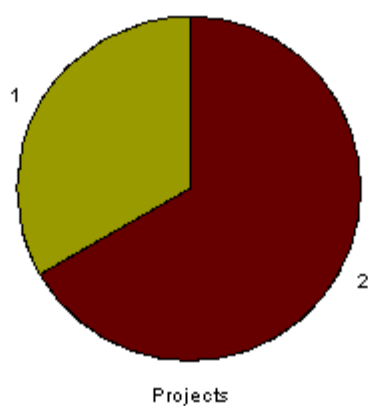


Delay in Months



Graphical Analysis of Atomic Energy Sector

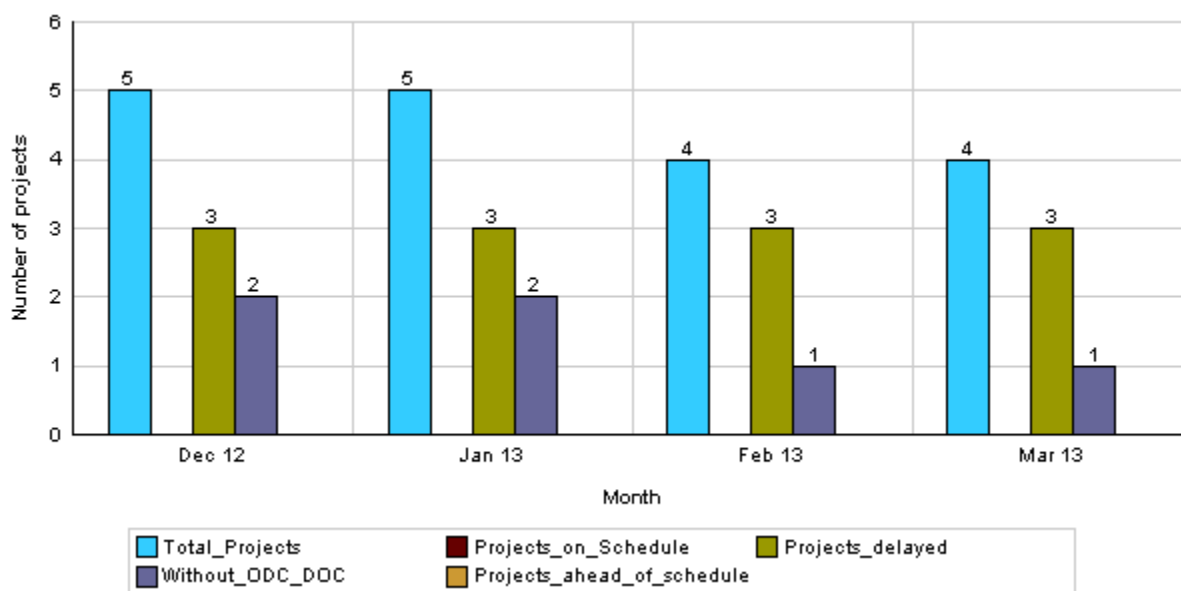


Break-up of 3 Delayed projects in March 2013

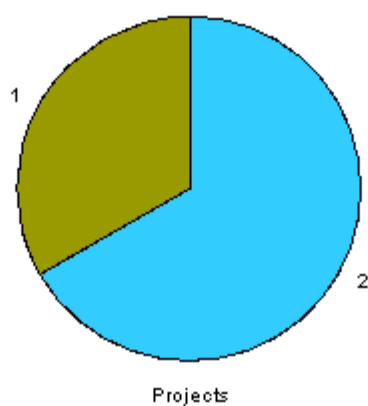


Delay in Months



Graphical Analysis of All Projects w.r.t. Revised Schedule

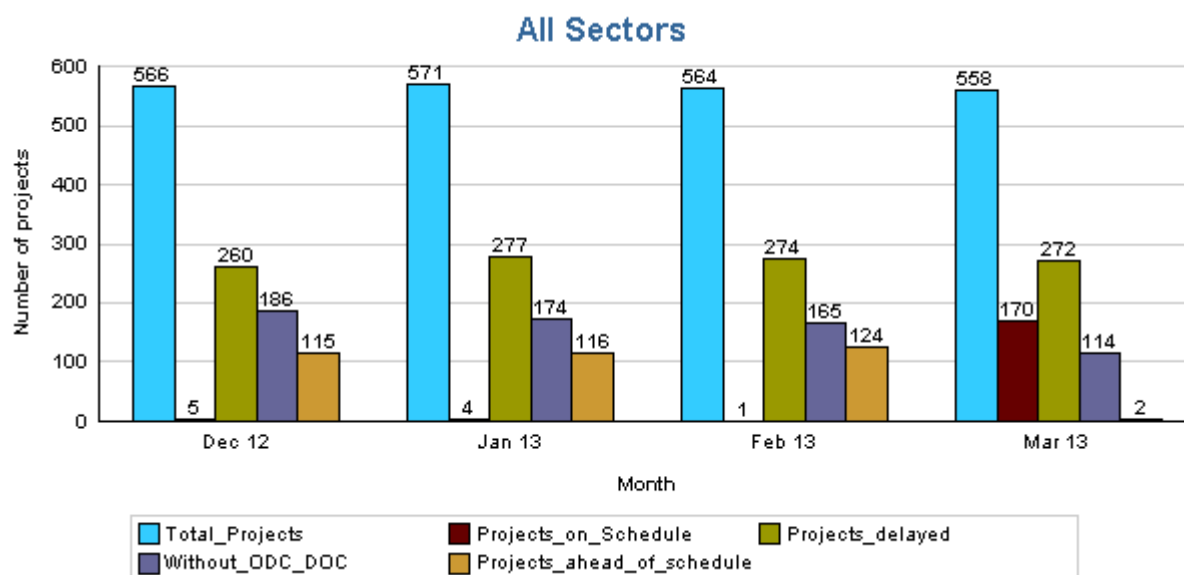


Break-up of 272 Delayed projects in March 2013

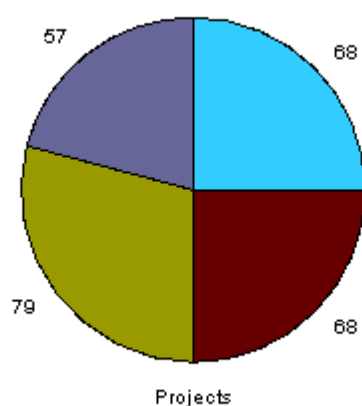


Delay in Months



Graphical Analysis of All Projects w.r.t. Original Schedule

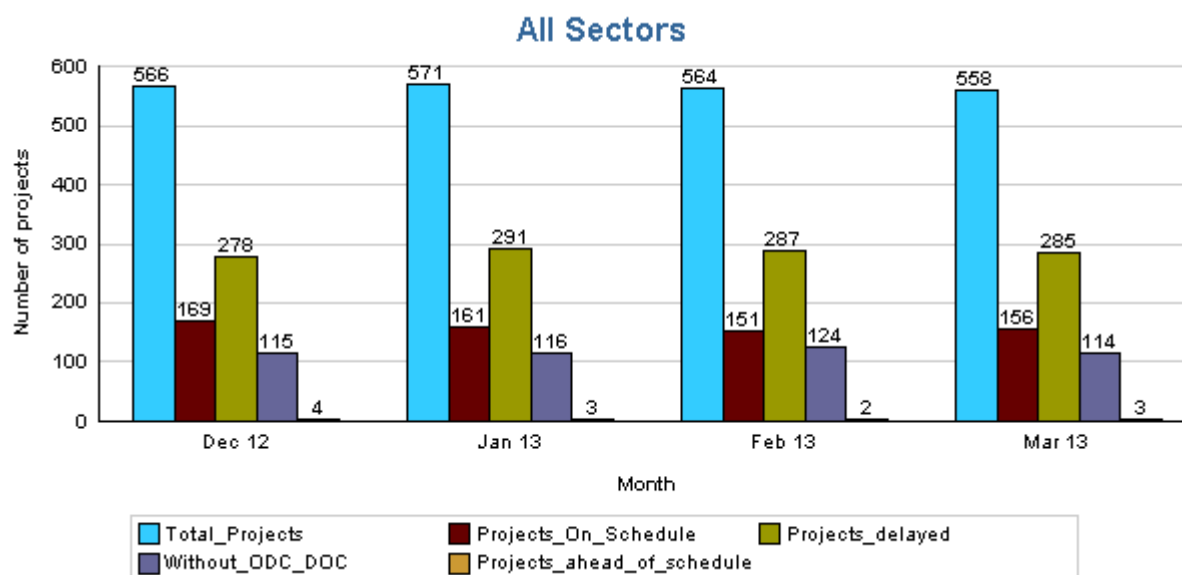

Break-up of 285 Delayed projects in March 2013

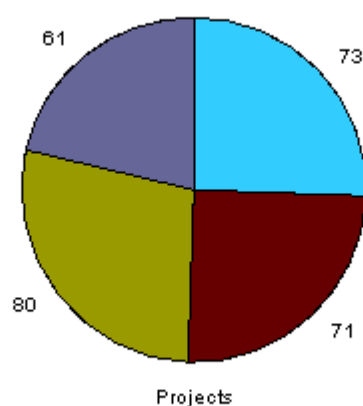

Delay in Months



Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	4	40,442.00	40,442.00	46,726.00	23,769.48
Civil Aviation	6	5,473.58	5,680.58	6,063.07	5,205.34
Coal	51	36,056.46	37,022.46	37,510.52	14,345.29
Fertilisers	1	1,478.63	1,478.63	1,478.63	1,087.00
Steel	17	65,285.87	67,562.15	71,443.41	49,110.80
Petrochemicals	1	5,460.61	8,920.00	8,920.00	6,229.56
Petroleum	67	164,236.71	176,275.22	173,456.75	79,188.84
Power	101	243,054.78	246,570.52	258,796.07	118,189.09
Railways	124	60,590.79	89,687.64	147,761.45	62,924.93
Road Transport & Highways	149	101,529.76	101,696.26	103,468.38	72,105.04
Shipping & Ports	19	15,617.12	17,389.43	17,902.42	8,251.99
Telecommunications	13	5,699.24	5,699.24	5,506.32	1,800.89
Urban Development	4	44,245.18	44,304.08	49,518.08	5,517.33
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	558	789,713.63	843,271.11	929,738.10	447,761.07

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Atomic Energy									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,469.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	15,550.00	12/2008 -	03/2013	51(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,058.48	09/2010 -	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,692.00	12/2016 -	03/2017	3(O) -	0/69
Total			40,442.00 -	46,726.00	23,769.48				47/327
Civil Aviation									
5	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,463.38	05/2011 -	03/2013	22(O) -	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	226.70	01/2011 04/2013	12/2013	35(O) 8(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	206.39	05/2012 -	06/2013	13(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,846.60	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	452.00	85.30	03/2015 -	03/2015	0(O) -	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	376.97	06/2013 -	06/2013	0(O) -	0/0
Total			5,473.58 -	6,063.07	5,205.34				0/0
Coal									
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	431.80	03/2013 09/2012	07/2014	16(O) 22(R)	7/22
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	95.10	03/2016 -	03/2016	0(O) -	2/6
13	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	437.14	03/2016 03/2016	03/2016	0(O) 0(R)	2/4

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL, Odisha	08/2008	207.28	207.28	102.56	03/2012	03/2014	24(O)	5/9
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66	341.63	236.09	03/2011	03/2014	36(O)	0/4
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08	172.08	119.73	03/2010	03/2015	60(O)	4/5
17	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	258.56	40.47	03/2016	03/2016	0(O)	0/1
18	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00	490.10	123.40	03/2017	03/2017	0(O)	6/12
19	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97	168.97	40.86	03/2014	03/2014	0(O)	1/4
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04	535.10	169.96	03/2015	03/2015	0(O)	0/3
21	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	1/2
22	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	265.64	03/2014	03/2016	24(O)	2/7
23	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.91	03/2011	03/2016	60(O)	0/2
24	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66	1,943.66	1,268.44	03/2014	03/2016	24(O)	6/12
25	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67	2,675.67	1,409.32	03/2014	03/2016	24(O)	10/15
26	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87	395.87	71.92	03/2015	03/2015	0(O)	2/12
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63	479.63	126.19	03/2013	03/2015	24(O)	5/10
28	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24(O)	1/7
29	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	3.02	03/2015	03/2015	0(O)	4/31
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78	467.78	12.31	03/2013	03/2013	0(O)	4/83
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.92	03/2011	03/2017	72(O)	0/2
32	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63	453.63	83.46	12/2012	03/2016	39(O)	8/44
33	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77	457.77	113.13	03/2013	03/2015	24(O)	6/11
34	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46	162.46	35.83	03/2014	03/2014	0(O)	0/3
35	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24(O)	1/7
36	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28	1,131.28	3.87	03/2018	03/2018	0(O)	0/3

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.32	03/2013 -	03/2013	0(O) -	2/5
38	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	109.05	03/2010 -	03/2014	48(O) -	7/10
39	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	716.99	03/2013 -	03/2013	0(O) -	0/9
40	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
41	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44(O) -	1/5
42	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	205.78	03/2014 -	03/2016	24(O) -	1/6
43	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.77	03/2012 -	03/2015	36(O) -	7/20
44	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
45	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
46	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	28.00	12/2015 -	08/2017	20(O) -	0/33
47	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	4.42	03/2012 -	03/2015	36(O) -	0/2
48	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	60.75	03/2012 -	03/2017	60(O) -	0/4
49	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
50	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.91	03/2014 -	03/2016	24(O) -	0/1
51	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	91.56	03/2013 -	03/2015	24(O) -	2/4
52	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2016	24(O) -	0/2
53	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	142.90	03/2012 -	03/2015	36(O) -	24/27
54	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
55	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	31.29	03/2015 -	03/2015	0(O) -	4/31
56	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85 -	510.85	269.10	03/2016 -	03/2016	0(O) -	1/4
57	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	49.64	03/2012 -	-	-	11/42
58	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72 -	447.72	43.33	03/2016 -	03/2016	0(O) -	0/10

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,654.23	06/2009 -	01/2014	55(O) -	19/24
60	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 -	4,909.54	4,128.29	03/2012 -	03/2014	24(O) -	0/39
61	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	130.79	03/2012 -	03/2016	48(O) -	0/4
Total			36,056.46 -	37,510.52	14,345.29				161/661
<u>Fertilisers</u>									
62	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	1,087.00	01/2013 -	03/2013	2(O) -	0/8
Total			1,478.63 -	1,478.63	1,087.00				0/8
<u>Steel</u>									
63	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	268.27	04/2013 12/2013	12/2013	8(O) 0(R)	16/19
64	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	252.34	08/2010 -	04/2013	32(O) -	0/1
65	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	254.92	02/2011 -	04/2013	26(O) -	2/3
66	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	191.31	05/2013 11/2013	11/2013	6(O) 0(R)	11/21
67	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	235.36	05/2012 -	06/2013	13(O) -	1/2
68	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	349.17	12/2011 03/2012	06/2013	18(O) 15(R)	16/21
69	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	137.65	10/2012 -	06/2013	8(O) -	3/4
70	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	332.65	42.40	08/2014 -	08/2014	0(O) -	0/0
71	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	32.28	11/2013 -	03/2014	4(O) -	1/1
72	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	8,533.85	03/2013 -	03/2014	12(O) -	22/27
73	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,469.92	12/2011 -	12/2013	24(O) -	16/16
74	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,521.60	12/2012 -	12/2013	12(O) -	10/12

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
75	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,480.55	12/2011 -	12/2013	24(O) -	19/19
76	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	10,235.67	10/2009 -	06/2013	44(O) -	62/64
77	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Odisha	09/2008	11,812.00 11,812.00	11,812.00	9,032.45	03/2013 -	12/2013	9(O) -	11/14
78	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	70.18	10/2013 -	03/2014	5(O) -	0/1
79	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL, Odisha	01/2012	254.90 -	254.90	2.88	12/2014 -	12/2014	0(O) -	0/0
Total			65,285.87 -	71,443.41	49,110.80				190/225
<u>Petrochemicals</u>									
80	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	6,229.56	04/2012 12/2013	12/2013	20(O) 0(R)	19/29
Total			5,460.61 -	8,920.00	6,229.56				19/29
<u>Petroleum</u>									
81	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	678.02	-	06/2012 -	03/2014	21(O) -	0/0
82	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	1,483.80	06/2012 -	06/2013	12(O) -	0/0
83	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	07/2013	19(O) -	0/0
84	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	1,410.63	03/2013 -	03/2014	12(O) -	0/0
85	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00 -	586.00	4.28	07/2015 -	08/2015	1(O) -	0/0
86	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014	0(O) -	0/0
87	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014	0(O) -	0/0
88	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	460.70	-	07/2012 07/2012	-	-	0/17
89	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50 -	341.50	165.28	02/2013 -	05/2013	3(O) -	38/42
90	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00 -	190.00	34.37	03/2014 -	03/2014	0(O) -	0/24
91	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	344.88	09/2011 -	12/2013	27(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
92	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	381.67	- -	03/2013	- -	18/19
93	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	97.69	05/2013 -	11/2013	6(O) -	0/0
94	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	152.89	105.27	06/2013 -	06/2013	0(O) -	0/0
95	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	35.90	08/2013 -	01/2014	5(O) -	0/0
96	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	73.90	09/2012 -	09/2013	12(O) -	0/0
97	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
98	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	486.00	44.40	09/2013 -	09/2013	0(O) -	0/0
99	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	215.51	- -	-	-	0/0
100	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86(O) 12(R)	0/0
101	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,204.63	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
102	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
103	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
104	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
105	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,448.09	09/2011 05/2012	06/2013	21(O) 13(R)	5/76
106	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,663.16	09/2011 03/2012	06/2013	21(O) 15(R)	53/59
107	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	195.28	03/2013 -	04/2013	1(O) -	0/0
108	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
109	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,158.35	03/2013 03/2014	04/2014	13(O) 1(R)	0/0
110	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	111.54	11/2012 -	10/2013	11(O) -	0/0
111	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	577.61	01/2014 -	01/2014	0(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
112	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
113	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	422.00	01/2013 -	08/2013	7(O) -	18/18
114	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,379.28	04/2013 -	04/2013	0(O) -	0/167
115	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	678.24	05/2015 -	05/2015	0(O) -	0/0
116	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
117	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
118	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1(O) -	0/0
119	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	06/2013	87(O) 3(R)	6/6
120	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	311.69	12/2015 -	05/2016	5(O) -	0/0
121	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	2,059.63	69.89	03/2015 -	03/2015	0(O) -	0/0
122	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	2.20	01/2013 -	-	-	0/0
123	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50(O) -	0/0
124	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL,Multi State	07/2009	238.68 -	204.00	-	01/2012 -	-	-	0/1
125	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	765.59	12/2012 -	12/2014	24(O) -	0/21
126	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	666.00	-	11/2015 -	11/2015	0(O) -	0/0
127	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	8,727.48	01/2012 -	05/2013	16(O) -	0/108
128	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,067.86	09/2012 -	09/2013	12(O) -	0/0
129	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,185.52	05/2010 03/2013	05/2013	36(O) 2(R)	0/0
130	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015	0(O) -	0/0
131	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	279.00	-	12/2014 -	12/2014	0(O) -	0/0
132	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	05/2013	26(O) 24(R)	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
133	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	660.26	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
134	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]OCL,Multi State	02/2011	913.00 -	913.00	21.84	07/2015 -	07/2015	0(O) -	0/0
135	PARADIP REFINERY PROJECT - [N16000058]OCL,Odisha	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	03/2014	16(O) -	60/100
136	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]OCL,Multi State	08/2009	1,793.00 -	1,793.00	726.16	09/2012 -	-	-	0/11
137	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	1,701.79	02/2014 -	02/2014	0(O) -	0/0
138	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	211.00	04/2012 -	06/2013	14(O) -	0/0
139	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	192.77	05/2014 -	05/2014	0(O) -	0/0
140	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	566.69	07/2012 -	10/2013	15(O) -	0/31
141	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	915.58	- -	-	-	51/53
142	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64 -	1,210.64	60.89	11/2015 -	11/2015	0(O) -	3/25
143	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	36.13	12/2014 -	12/2014	0(O) -	0/0
144	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	1,043.57	1,024.65	04/2012 -	01/2013	-	0/0
145	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	170.77	08/2012 -	06/2013	10(O) -	0/0
146	VKPL UPGRADEATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	201.83	03/2012 -	12/2013	21(O) -	13/20
147	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	47.04	12/2013 -	12/2013	0(O) -	0/0
Total			164,236.71 -	173,456.75	79,188.84				274/807
Power									
148	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,640.10	08/2012 -	03/2014	19(O) -	0/11
149	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,187.00	02/2012 -	05/2013	15(O) -	0/7

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
150	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	737.90	05/2012 -	09/2013	16(O) -	0/11
151	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,122.60	06/2012 -	05/2013	11(O) -	0/4
152	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/0
153	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	5,341.00	08/2013 -	09/2014	13(O) -	8/19
154	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,052.00	12/2009 -	02/2017	86(O) -	27/47
155	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,628.00	07/2011 -	10/2015	51(O) -	5/28
156	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	913.00	775.32	02/2011 10/2012	01/2013	-	2/4
157	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015	0(O) -	0/0
158	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	535.50	08/2014 -	08/2014	0(O) -	0/20
159	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	33.90	06/2014 -	06/2014	0(O) -	0/20
160	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
161	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	-	10/2014 -	10/2014	0(O) -	0/0
162	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	682.60	09/2014 -	09/2014	0(O) -	8/19
163	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	873.40	10/2009 -	09/2013	47(O) -	20/20
164	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	570.80	11/2012 -	03/2014	16(O) -	3/11
165	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
166	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	705.60	05/2014 -	05/2014	0(O) -	0/16

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	920.30	08/2013 -	08/2013	0(O) -	0/14
168	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	157.00	08/2014 -	08/2014	0(O) -	0/21
169	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	838.60	12/2013 -	12/2013	0(O) -	0/13
170	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	67.30	10/2012 -	04/2013	6(O) -	5/14
171	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	871.93	12/2007 12/2009	-	-	0/10
172	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	2,496.90	2,208.33	05/2013 06/2016	03/2017	46(O) 9(R)	6/22
173	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,095.31	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
174	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	4,842.00	04/2009 -	09/2014	65(O) -	0/9
175	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,295.00	12/2016 -	12/2016	0(O) -	4/9
176	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,846.81	09/2008 -	03/2013	54(O) -	17/37
177	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	952.00	05/2017 -	05/2017	0(O) -	2/4
178	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	1,527.00	36.00	08/2017 -	08/2017	0(O) -	0/0
179	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,900.00	08/2012 -	03/2013	7(O) -	16/16
180	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	774.00	09/2016 -	09/2016	0(O) -	13/14
181	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	841.10	08/2010 01/2013	06/2013	34(O) 5(R)	0/3
182	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,609.30	08/2013 -	03/2015	19(O) -	0/17
183	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	253.50	02/2012 -	12/2013	22(O) -	0/14
184	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	341.70	11/2011 -	03/2014	28(O) -	0/11
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	353.20	11/2011 -	12/2013	25(O) -	0/14

Sector Wise Details

(Mar,2013)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	116.20	01/2013 -	09/2013	8(O) -	0/7
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	245.40	07/2013 -	03/2014	8(O) -	0/12
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	747.10	04/2013 -	03/2014	11(O) -	0/12
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	119.20	08/2013 -	03/2013	-5(O) -	0/16
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	95.50	11/2014 -	11/2014	0(O) -	0/0
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	0/0
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	14.90	04/2015 -	05/2015	1(O) -	0/0
193	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	524.70	11/2012 -	12/2013	13(O) -	0/10
194	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,078.38	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
195	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,877.58	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
196	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	573.99	505.68	08/2012 08/2013	09/2014	25(O) 13(R)	16/22
197	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,325.70	01/2012 -	02/2014	25(O) -	0/27
198	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,058.00	10/2012 -	11/2013	13(O) -	12/16
199	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,286.00	11/2016 -	11/2016	0(O) -	13/13
200	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,201.82	09/2010 08/2014	12/2017	87(O) 40(R)	11/11
201	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	75.60	04/2013 -	09/2013	5(O) -	0/15
202	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	2,015.00	08/2012 -	03/2014	19(O) -	0/7
203	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016	0(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
204	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014	0(O) -	0/0
205	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/0
206	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	77.30	08/2014 -	08/2014	0(O) -	0/20
207	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	224.20	02/2015 -	02/2015	0(O) -	0/0
208	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	183.60	11/2014 -	11/2014	0(O) -	0/0
209	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	206.30	01/2015 -	01/2015	0(O) -	0/19
210	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	74.00	08/2014 -	08/2014	0(O) -	0/20
211	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	107.00	06/2014 -	06/2014	0(O) -	0/19
212	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	135.88	06/2012 -	06/2013	12(O) -	0/9
213	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	838.50	08/2012 -	03/2014	19(O) -	0/11
214	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,730.00	03/2013 -	03/2016	36(O) -	2/15
215	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,310.02	09/2009 06/2013	03/2014	54(O) 9(R)	0/0
216	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,686.98	03/2007 09/2012	04/2013	73(O) 7(R)	25/25
217	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.88	2,978.86	464.30	07/2010 02/2016	11/2016	76(O) 9(R)	1/10
218	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	76.30	01/2014 -	01/2014	0(O) -	0/17
219	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	229.80	08/2014 -	08/2014	0(O) -	0/0
220	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	426.40	10/2014 -	10/2014	0(O) -	0/21

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,288.60	10/2012 -	03/2014	17(O) -	0/12
222	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	370.00	01/2015 -	01/2015	0(O) -	0/20
223	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,290.90	03/2014 -	03/2014	0(O) -	0/15
224	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	10.70	08/2014 -	08/2014	0(O) -	0/20
225	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	90.50	10/2014 -	10/2014	0(O) -	0/20
226	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATH-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	758.75	598.40	01/2010 -	04/2013	39(O) -	0/22
227	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	157.50	11/2011 -	09/2013	22(O) -	0/7
228	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,330.80	12/2012 -	12/2013	12(O) -	0/11
229	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	197.90	02/2014 -	02/2014	0(O) -	0/20
230	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	251.70	10/2013 -	10/2013	0(O) -	0/18
231	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	65.40	07/2013 -	07/2013	0(O) -	0/0
232	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	491.90	12/2013 -	12/2013	0(O) -	0/18
233	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	124.50	11/2013 -	11/2013	0(O) -	0/20
234	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	895.20	03/2013 -	12/2013	9(O) -	0/14
235	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,337.70	12/2013 -	03/2014	3(O) -	0/13
236	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,241.40	11/2012 -	03/2014	16(O) -	0/15

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
237	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	565.90	07/2014 -	07/2014	0(O) -	0/19
238	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	514.21	- -	07/2013	- -	7/29
239	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	394.95	07/2014 -	02/2015	7(O) -	1/16
240	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,204.40	12/2012 -	12/2013	12(O) -	0/11
241	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	775.00	11/2013 -	11/2013	0(O) -	0/15
242	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	61.40	01/2013 -	06/2014	17(O) -	0/16
243	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,927.67	11/2009 02/2013	05/2013	42(O) 3(R)	0/4
244	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	197.00	08/2015 -	08/2015	0(O) -	5/10
245	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	4,300.00	10/2012 -	03/2013	5(O) -	15/15
246	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	342.92	07/2014 -	05/2016	22(O) -	1/1
247	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	429.40	09/2010 -	03/2013	30(O) -	0/9
248	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	586.70	06/2015 -	06/2015	0(O) -	0/24
Total			243,054.78 -	258,796.07	118,189.09				246/1277
Railways									
249	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	456.83	03/2014 -	12/2015	21(O) -	0/0
250	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	369.21	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
251	AHMEDNAGAR-PARLI VAJUNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	226.28	- -	-	-	0/0
252	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	396.76	03/2011 03/2011	03/2011	-	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
253	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	550.45	06/1999 03/2011	03/2011	-	0/0
254	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
255	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	404.39	15.76	03/2013 -	03/2013	0(O) -	0/0
256	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.35	- -	-	-	0/0
257	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	472.01	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
258	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	224.41	12/2010 03/2011	03/2011	-	0/0
259	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTTP,Maharashtra	03/1996	401.81 495.44	1,512.86	246.40	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
260	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	42.44	04/2014 -	03/2017	35(O) -	0/0
261	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	702.45	03/2010 -	12/2015	69(O) -	0/0
262	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	350.00	334.15	- 03/2009	-	-	0/0
263	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,701.00	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
264	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	158.71	12/2012 -	12/2013	12(O) -	0/0
265	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	195.19	03/2011 -	-	-	0/0
266	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.57	03/2012 -	-	-	0/0
267	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
268	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	946.07	12/2012 01/2013	02/2013	-	0/0
269	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
270	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
271	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	318.86	- -	06/2013	-	0/0
272	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD) - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	121.47	12/2012 -	-	-	0/0
273	DANIYAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	94.20	- -	-	-	0/0
274	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	211.53	- -	03/2013	-	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	484.04	12/2012 12/2012	02/2013	-	0/0
276	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	592.35	- -	12/2012	-	0/0
277	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	95.48	12/2011 02/2012	02/2012	-	0/0
278	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	224.89	141.55	03/2012 -	12/2013	21(O) -	0/0
279	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	208.66	12/2008 -	09/2014	69(O) -	0/0
280	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	220.91	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
281	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
282	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	278.33	02/2011 02/2011	03/2013	25(O) 25(R)	0/0
283	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	116.77	02/2006 -	06/2014	100(O) -	0/0
284	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	626.57	- -	03/2012	-	0/0
285	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
286	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	345.44	- 05/2009	05/2009	-	0/0
287	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	557.35	03/1994 -	10/2013	235(O) -	0/0
288	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	124.23	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
289	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	185.78	- -	-	-	0/0
290	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	224.33	- 09/2009	-	-	0/0
291	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
292	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	603.29	- -	01/2013	-	0/0
293	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.22	- -	03/2014	-	0/0
294	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.33	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
295	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	71.68	- -	-	-	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
296	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	16.64	03/2015 -	03/2015	0(O) -	0/0
297	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	835.94	06/2007 -	06/2007	-	0/0
298	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	691.31	03/2012 08/2012	-	-	0/0
299	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	697.45	434.76	03/2012 03/2012	12/2012	-	0/0
300	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,295.18	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
301	Jaipur - Ringus - Churu and Sikar - Loharu Gauge C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	230.27	03/2014 -	03/2014	0(O) -	0/0
302	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	288.23	03/2012 03/2012	03/2013	12(O) 12(R)	0/0
303	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,408.47	- -	03/2013	- -	0/0
304	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	504.57	- -	03/2014	- -	1/1
305	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	762.61	- -	10/2012	-	0/0
306	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.20	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
307	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	107.58	- -	-	-	0/0
308	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	222.32	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
309	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	239.15	- -	03/2014	- -	0/0
310	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
311	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	460.04	- 03/2010	03/2010	-	0/0
312	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,433.38	07/2005 -	-	-	0/0
313	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	139.03	- -	-	-	0/0
314	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	285.99	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
315	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
316	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	349.90	- -	12/2012	-	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90 227.90	223.01	118.88	12/2012 -	03/2015	27(O) -	0/0
318	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	1,630.97	369.27	05/2008 03/2011	-	-	0/0
319	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148]ECOR, Odisha	04/1993	100.00 142.98	227.94	215.16	03/2002 -	06/2013	135(O) -	0/0
320	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31 1,676.31	4,255.37	3,425.69	03/2009 -	03/2015	72(O) -	0/0
321	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	480.00	0.37	07/2008 -	07/2008	-	0/0
322	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, Bihar	04/2003	218.19 218.19	218.19	167.25	- -	02/2013	-	0/0
323	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00 900.05	900.05	677.11	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
324	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
325	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N220000002]ECR, Bihar	04/1996	114.01 332.92	477.88	419.20	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
326	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR, Tamil Nadu	09/2007	404.19 404.19	900.00	295.40	- -	-	-	0/0
327	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	5,300.00	1,008.73	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
328	MUNEERABAD-MAHABOONNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	645.00	181.84	- -	03/2012	-	0/0
329	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 429.49	883.00	641.37	02/2009 -	03/2012	-	0/0
330	NANGALDAM-TALWARA(NL), NR - [220100188]NR, Multi State	03/1981	37.68 450.00	1,036.78	355.90	07/2012 -	-	-	0/0
331	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR, Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
332	NEW B.G. LINE FROM TETELIA TO BYRNHAT (NATIONAL P - [N22000086]NEFR, Assam	09/2006	200.00 200.00	385.20	130.40	- -	03/2015	- -	0/0
333	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00 733.00	1,655.81	1,344.95	12/2008 -	03/2015	75(O) -	0/0
334	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR, West Bengal	04/1983	36.80 274.41	703.17	248.71	- -	03/2015	- -	0/0
335	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	2,619.02	275.37	03/2016 -	03/2016	0(O) -	0/0
337	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,298.42	49.50	03/2014 -	03/2016	24(O) -	0/0
338	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98 -	3,951.98	93.92	03/2016 -	03/2016	0(O) -	0/0
339	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	33.44	03/2016 -	06/2016	3(O) -	0/0
340	OBULAVARIPALLE- KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	1,117.11	445.88	03/2008 06/2008	-	-	0/0
341	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 380.00	355.00	378.12	03/2009 11/2012	-	-	0/0
342	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 529.23	529.23	249.38	02/2010 11/2012	12/2015	70(O) 37(R)	0/0
343	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 2,921.00	2,921.00	1,696.36	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
344	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	599.81	- -	03/2012	-	0/0
345	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	138.09	12/2010 12/2010	12/2010	-	0/0
346	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.00	792.25	- -	03/2013	- -	0/6
347	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	221.90	243.81	12/2007 03/2010	-	-	0/0
348	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00 2,363.00	2,363.00	960.22	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
349	RAJATGARH-BARANG(LD), ECR - [220100286]RVNL, Odisha	04/1999	166.16 -	288.00	259.32	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
350	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	227.53	- -	-	-	0/0
351	RANCHI-LOHARDAGA(GC), SER - [220100214]SER, Jharkhand	04/1997	194.07 194.07	596.00	325.62	06/2004 -	12/2012	-	0/0
352	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70 915.70	2,232.50	1,703.60	- -	03/2014	- -	0/0
353	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	370.00	344.44	04/2003 03/2010	-	-	0/0
354	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Odisha	02/1996	57.94 604.04	639.97	175.76	03/1998 08/2005	08/2005	-	0/0
355	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00 482.70	482.70	440.63	03/2013 -	03/2014	12(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04 603.04	603.04	192.05	03/2012 -	-	-	0/0
357	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	385.54	230.30	03/2010 -	-	-	0/0
358	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017	15(O) -	0/0
359	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Odisha	04/1998	183.23 -	818.29	78.15	02/2015 -	02/2015	0(O) -	0/0
360	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR, Rajasthan	04/2008	516.23 516.23	516.23	344.53	03/2014 -	03/2014	0(O) -	0/0
361	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR, Odisha	04/2005	726.96 810.78	810.78	121.87	- -	-	-	0/0
362	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,074.47	439.39	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
363	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	1,188.91	602.44	- 12/2009	02/2012	-	0/0
364	TIDIVANAM-NAGARI (NL) - [N22000085]SR, Tamil Nadu	09/2006	456.00 456.00	582.83	145.76	- -	-	-	0/0
365	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, Tamil Nadu	09/2006	125.00 125.00	227.40	40.72	- -	-	-	0/0
366	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 100.00	548.96	536.30	- -	-	-	0/0
367	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	3,176.10	3,374.48	12/2006 08/2010	08/2010	-	0/0
368	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73 167.73	167.73	65.64	03/2012 -	02/2013	-	0/0
369	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	9,001.45	03/2001 -	12/2017	201(O) -	0/0
370	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, Uttar Pradesh	04/2006	325.00 325.00	819.40	188.04	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
371	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62 -	1,389.62	527.10	03/2014 -	03/2014	0(O) -	0/0
372	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	356.87	180.02	- 03/2010	-	-	0/0
Total			60,590.79 -	147,761.45	62,924.93				1/7
Road Transport & Highways									
373	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI, Uttar Pradesh	10/2012	250.50 -	250.50	65.26	10/2014 -	10/2014	0(O) -	0/0
374	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, Uttar Pradesh	01/2013	373.47 -	373.47	28.51	07/2014 -	07/2014	0(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
375	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	392.02	05/2013	03/2014	10(O)	0/0
376	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	511.54	579.51	11/2013	11/2013	0(O)	0/0
377	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00	624.00	137.99	04/2014	04/2014	0(O)	0/0
378	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40	356.40	-	07/2014	07/2014	0(O)	0/0
379	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36	291.36	52.86	01/2014	01/2014	0(O)	0/0
380	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00	226.00	282.33	02/2014	02/2014	0(O)	0/0
381	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00	664.00	400.45	02/2014	04/2014	2(O)	0/0
382	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09	375.09	124.43	04/2014	04/2014	0(O)	0/0
383	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00	325.00	160.24	05/2014	05/2014	0(O)	0/0
384	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	1,718.30	08/2014	07/2015	11(O)	0/0
385	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	1,151.40	06/2013	06/2013	0(O)	0/0
386	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	38.30	09/2013	07/2014	10(O)	0/0
387	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	745.79	08/2013	08/2013	0(O)	0/0
388	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00	575.00	712.68	07/2013	07/2013	0(O)	0/0
389	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00	398.00	344.43	02/2014	02/2014	0(O)	0/0
390	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	998.79	805.45	08/2013	08/2013	0(O)	0/0
391	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	1,078.84	967.11	08/2013	08/2013	0(O)	0/0
392	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
393	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18	1,396.18	636.24	09/2014	09/2014	0(O)	0/0
394	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	465.50	214.69	09/2007	03/2014	78(O)	0/0
395	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24	2,125.24	30.08	12/2015	12/2015	0(O)	0/0
396	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	1,252.70	11/2012	06/2013	7(O)	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [N240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	264.27	01/2009	12/2013	59(O)	0/0
398	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	04/2013	14(O)	0/0
399	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70	228.70	194.51	02/2004	04/2013	110(O)	0/0
400	BAREILLY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00	1,046.00	291.01	09/2013	09/2013	0(O)	0/0
401	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan	12/2011	2,388.00	2,388.00	956.68	06/2014	06/2014	0(O)	0/0
402	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	437.95	-	10/2013	-	2/2
403	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00	209.00	11.28	01/2013	10/2013	9(O)	0/0
404	BHUBANESWAR TO PURI - [N24000195]NHAI, Odisha	03/2011	500.29	500.29	450.94	08/2013	08/2013	0(O)	0/0
405	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	237.80	275.04	06/2008	03/2014	69(O)	0/0
406	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00	195.00	231.15	06/2008	03/2014	69(O)	0/0
407	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	233.03	06/2005	03/2014	105(O)	0/0
408	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	258.43	04/2010	11/2014	55(O)	0/0
409	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	179.23	02/2010	07/2014	53(O)	0/0
410	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	790.93	03/2013	07/2013	4(O)	0/0
411	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	570.06	-	12/2013	-	0/1
412	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	09/2013	4(O)	0/0
413	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	395.08	10/2011	03/2014	29(O)	0/0
414	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	761.43	10/2011	06/2013	20(O)	0/0
415	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	176.84	10/2008	06/2014	68(O)	0/0
416	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI, Multi State	10/2012	1,928.22	1,928.22	255.27	04/2015	04/2015	0(O)	0/0
417	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	637.97	05/2010	06/2013	37(O)	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
418	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00	593.00	485.67	07/2013	07/2013	0(O)	0/0
419	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.82	06/2013	06/2013	0(O)	0/0
420	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	487.86	-	06/2013	-	1/1
421	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	246.20	06/2008	05/2013	59(O)	0/0
422	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	197.55	05/2008	12/2013	67(O)	0/0
423	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	295.39	09/2010	01/2014	40(O)	0/0
424	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	303.41	08/2013	08/2013	0(O)	0/0
425	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00	1,573.00	13.39	09/2015	09/2015	0(O)	0/0
426	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	441.45	09/2008	05/2013	56(O)	0/0
427	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00	1,232.00	87.61	08/2015	08/2015	0(O)	0/0
428	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00	682.00	-	10/2013	03/2014	5(O)	0/0
429	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	12/2013	30(O)	0/0
430	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	142.58	09/2008	03/2013	54(O)	0/0
431	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27	263.27	276.26	02/2004	04/2013	110(O)	0/0
432	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	1,200.30	08/2013	08/2013	0(O)	0/0
433	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	242.38	04/2008	03/2014	71(O)	0/0
434	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	182.53	04/2008	03/2014	71(O)	0/0
435	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	303.02	10/2009	04/2013	42(O)	0/0
436	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	495.37	12/2009	07/2013	43(O)	0/0
437	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	1,675.00	09/2012	12/2013	15(O)	0/0
438	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	2,777.00	10/2011	12/2013	26(O)	0/0
439	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	282.68	09/2007	11/2013	74(O)	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
440	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	301.81	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
441	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	363.74	131.26	07/2009 -	05/2014	58(O) -	0/0
442	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79(O) -	0/0
443	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, Uttarakhand	11/2011	478.00 -	478.00	245.23	10/2013 -	03/2014	5(O) -	0/0
444	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	192.39	08/2004 -	06/2013	106(O) -	0/0
445	HVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	192.06	08/2004 07/2010	06/2013	106(O) 35(R)	0/0
446	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	625.07	928.03	01/2013 -	06/2013	5(O) -	0/0
447	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	06/2013	- -	3/3
448	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	447.45	05/2013 -	02/2014	9(O) -	0/0
449	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013	0(O) -	0/0
450	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81 -	267.81	564.50	02/2013 -	07/2013	5(O) -	0/0
451	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
452	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	501.86	09/2009 -	06/2013	45(O) -	0/0
453	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00 -	536.00	450.46	01/2014 -	01/2014	0(O) -	0/0
454	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	792.06	1,649.10	12/2012 -	04/2013	4(O) -	0/0
455	KOTA BYPASS, RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	279.76	10/2008 -	09/2013	59(O) -	0/0
456	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	294.65	10/2008 -	12/2013	62(O) -	0/0
457	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI, West Bengal	02/2012	702.16 -	702.16	398.24	07/2014 -	07/2014	0(O) -	0/0
458	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00 -	671.00	737.54	- -	06/2014	- -	2/3
459	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00 -	795.00	1,055.70	05/2012 -	06/2013	13(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
460	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	407.60	186.29	06/2010 -	12/2013	42(O) -	0/0
461	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60(O) -	0/0
462	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24(O) -	0/0
463	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014	67(O) -	0/0
464	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68(O) -	0/0
465	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73(O) -	0/0
466	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	141.82	04/2009 -	12/2014	68(O) -	0/0
467	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,313.30	06/2013 -	06/2013	0(O) -	0/0
468	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	510.99	03/2013 -	03/2014	12(O) -	0/0
469	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54 -	511.54	269.32	11/2013 -	11/2013	0(O) -	0/0
470	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	299.20	06/2008 -	05/2013	59(O) -	0/0
471	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54(O) -	0/0
472	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19 -	484.19	34.07	10/2014 -	10/2014	0(O) -	0/0
473	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	290.59	04/2008 -	05/2014	73(O) -	0/0
474	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	258.39	06/2008 -	09/2013	63(O) -	0/0
475	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	281.55	06/2008 -	09/2013	63(O) -	0/0
476	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
477	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	268.59	06/2011 06/2011	04/2013	22(O) 22(R)	0/2
478	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	932.27	02/2010 -	12/2014	58(O) -	0/0
479	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00 -	586.00	237.55	01/2014 -	01/2014	0(O) -	0/0
480	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	1,655.00	494.71	09/2013 -	09/2013	0(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
481	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	400.56	03/2008 -	04/2013	61(O) -	0/0
482	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014	0(O) -	0/0
483	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	1,152.40	10/2014 -	10/2014	0(O) -	0/0
484	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	942.69	128.49	06/2014 -	06/2014	0(O) -	0/0
485	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	272.75	05/2008 -	09/2013	64(O) -	0/0
486	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	574.00	536.03	03/2014 -	03/2014	0(O) -	0/0
487	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	602.63	02/2013 -	10/2013	8(O) -	0/0
488	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,293.20	07/2012 -	06/2013	11(O) -	0/0
489	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.30	03/2013 -	04/2014	13(O) -	0/0
490	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	835.00	122.65	01/2014 -	01/2014	0(O) -	0/0
491	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	08/2013	21(O) -	0/0
492	Pune-sholapur, pkg 1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17(O) -	0/0
493	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	764.56	07/2015 -	06/2016	11(O) -	0/0
494	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03 -	251.03	326.29	10/2008 -	06/2013	56(O) -	0/0
495	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	1,479.00	162.70	06/2015 -	06/2015	0(O) -	0/0
496	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	928.72	11/2013 -	11/2013	0(O) -	0/0
497	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	05/2013	28(O) -	0/0
498	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	451.09	03/2013 -	12/2013	9(O) -	0/0
499	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	805.39	-	12/2013 -	12/2013	0(O) -	0/0
500	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014	0(O) -	0/0
501	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	228.28	09/2007 -	12/2013	75(O) -	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
502	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	190.95	07/2008	03/2013	56(O)	0/0
503	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
504	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	14.58	12/2013	12/2013	0(O)	0/0
505	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
506	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2015	31(O)	0/0
507	SNG toBANL - [N24000189]NHAI, Jammu and Kashmir	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
508	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	491.21	03/2008	06/2013	63(O)	0/0
509	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Odisha	04/2000	225.00	241.53	161.44	04/2004	04/2013	108(O)	0/0
510	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,685.60	08/2011	06/2013	22(O)	0/0
511	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	04/2013	46(O)	0/0
512	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	09/2013	38(O)	0/0
513	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	891.08	11/2013	11/2013	0(O)	0/0
514	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
515	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	101.30	05/2013	05/2013	0(O)	0/0
516	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	188.39	-	04/2013	-	2/2
517	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, Multi State	09/2011	2,848.00	2,848.00	771.14	03/2014	03/2014	0(O)	0/0
518	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, Jammu and Kashmir	12/2003	166.27	193.10	165.13	03/2008	03/2013	60(O)	0/0
519	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	47.41	11/2012	03/2014	16(O)	0/0
520	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	953.88	560.12	07/2013	06/2014	11(O)	0/0
521	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI, Multi State	12/2011	1,047.00	1,047.00	201.61	06/2014	06/2014	0(O)	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			101,529.76	103,468.38	72,105.04				10/14
Shipping & Ports									
522	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011	11/2012	-	0/0
523	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49	220.49	98.31	01/2013	06/2013	5(O)	0/0
524	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87	511.87	107.56	03/2014	03/2014	0(O)	0/0
525	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	532.83	364.52	12/2012	10/2013	10(O)	0/0
526	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03	277.03	294.87	12/2011	10/2012	-	0/0
527	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	306.12	02/2014	02/2014	0(O)	0/0
528	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10	1,012.23	554.60	12/2013	10/2013	-2(O)	0/0
529	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00	1,460.00	937.28	12/2010	04/2014	40(O)	0/0
530	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24(O)	0/0
531	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.93	02/2011	12/2012	-	0/0
532	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	1,571.60	5.75	10/2008	10/2008	-	0/0
533	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84	253.36	-	-	01/2009	-	0/1
534	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00	600.00	139.80	03/2006	06/2013	87(O)	0/0
535	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	-	0/0
536	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.21	03/2012	03/2012	-	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
537	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
538	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	831.13	10/2008 11/2010	-	-	0/0
539	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	04/2013	15(O) 7(R)	0/0
540	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
Total			15,617.12 -	17,902.42	8,251.99				0/1
Telecommunications									
541	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53(O) -	0/0
542	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
543	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.21	02/2007 03/2012	02/2013	-	0/0
544	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	-	03/2012 -	02/2013	-	0/0
545	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 -	09/2013	35(O) -	0/0
546	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
547	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	06/2013	48(O) -	0/0
548	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	12/2012	-	0/0
549	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	823.48	11/2010 -	06/2013	31(O) -	0/0
550	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
551	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0

Sector Wise Details

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
552	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
553	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	170.25	05/2011 -	06/2013	25(O) -	0/0
Total			5,699.24 -	5,506.32	1,800.89				0/0
Urban Development									
554	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013	21(O) -	3/3
555	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
556	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	2,804.31	03/2016 -	03/2016	0(O) -	0/0
557	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	230.84	09/2014 -	09/2014	0(O) -	0/0
Total			44,245.18 -	49,518.08	5,517.33				3/3
Water Resources									
558	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
Total			542.90 -	1,187.00	35.49				0/0
Grand Total			789,713.63	929,738.10	447,761.07				951/3359

Sector wise current status of projects on the Flash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

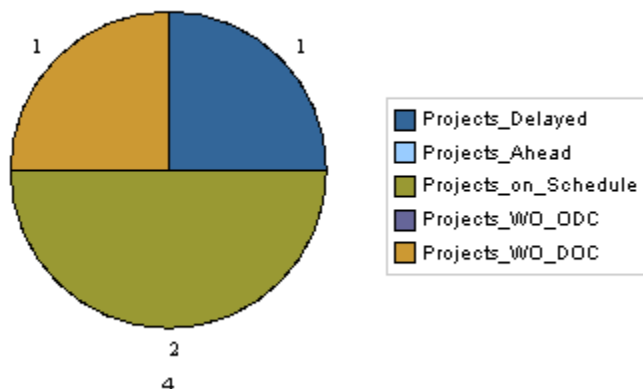

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till March, 2013 is Rs. 5517.33 crore, which is 11.1% of the revised cost of the projects.

Figures are in Rs. Crore

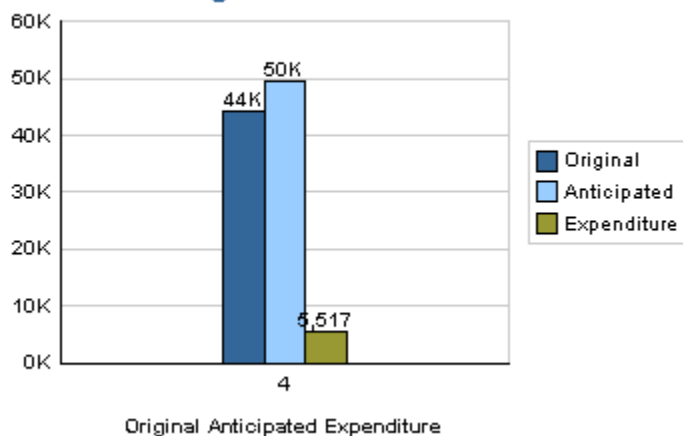

Sector wise current status of projects on the Flash Report

Telecommunications

I. Current Status:


Number of Projects **13**

Number of Projects Delayed **5**

Number of Projects Without Date Of Commissioning **8**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are delayed .8 projects do not have fixed dates of commissioning.

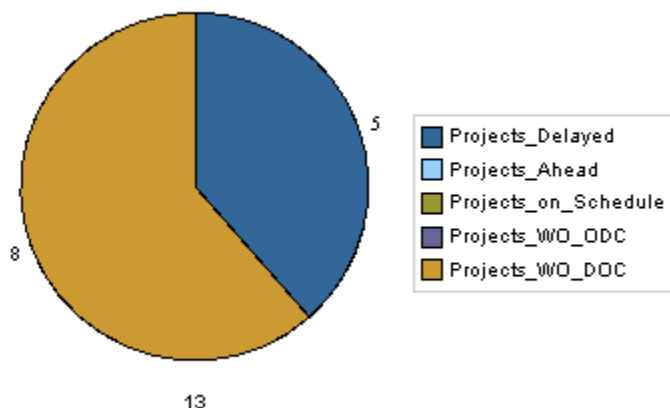

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5506.32 crore implying a cost overrun of -3.4%. The expenditure incurred on these projects till March, 2013 is Rs. 1800.89 crore, which is 32.7% of the revised cost of the projects.

Figures are in Rs. Crore

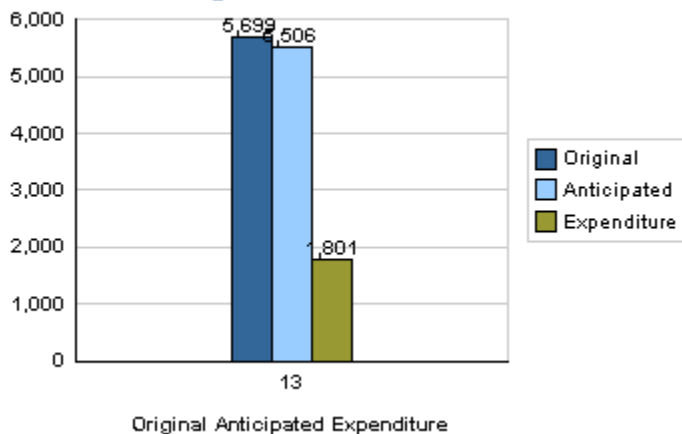

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	2
Number of Projects Delayed	6
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 2 projects are ahead of schedule, 2 projects are on schedule and 6 projects are delayed .9 projects do not have fixed dates of commissioning.

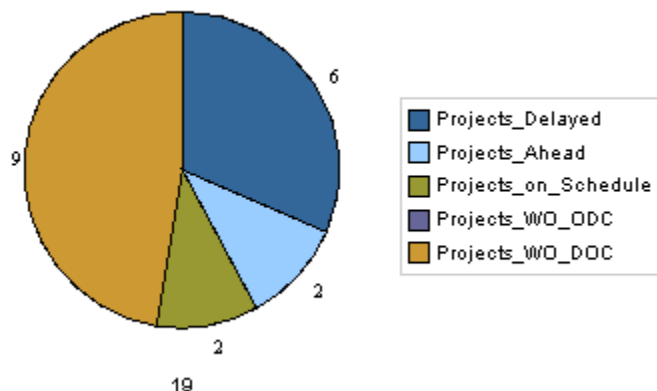

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till March, 2013 is Rs. 8251.99 crore, which is 46.1% of the revised cost of the projects.

Figures are in Rs. Crore

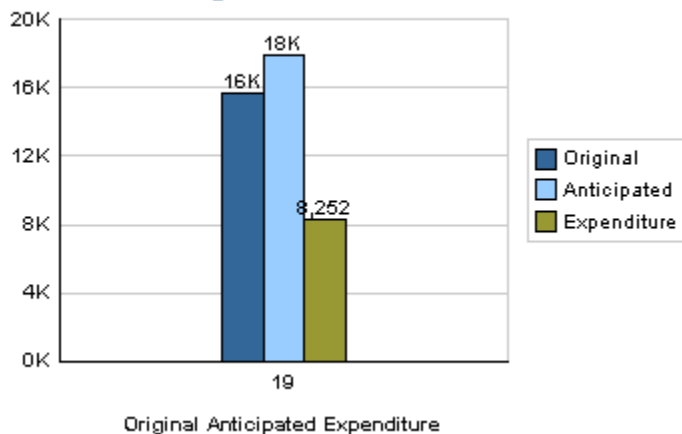

Sector wise current status of projects on the Flash Report

Road Transport & Highways


I. Current Status:

Number of Projects	149
Number of Projects On Schedule	54
Number of Projects Delayed	89

Number of Projects Without Original Date of Commissioning	6
---	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 149 projects, 54 projects are on schedule and 89 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

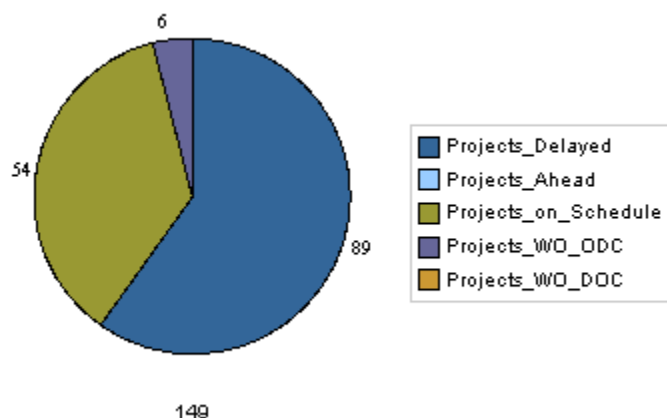

III. Investment Scenario

The Total Original cost of implementation of 149 projects when sanctioned, was of the order of Rs. 101529.76 crore but this was subsequently revised to Rs. 103468.38 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till March, 2013 is Rs. 72105.04 crore, which is 69.7% of the revised cost of the projects.

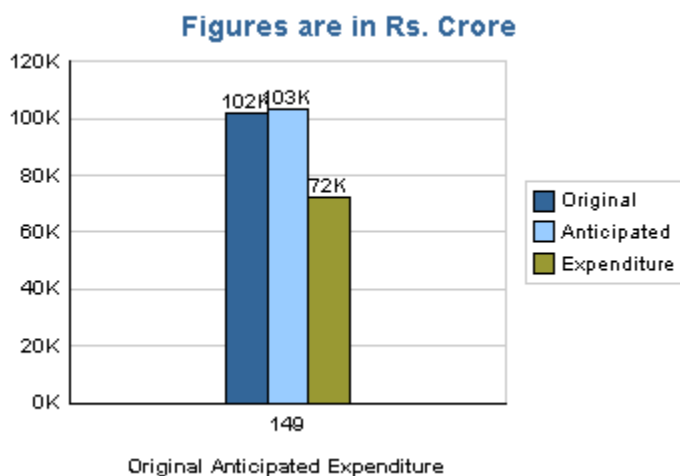

Sector wise current status of projects on the Flash Report

Railways


I. Current Status:

Number of Projects	124
Number of Projects On Schedule	8
Number of Projects Delayed	41

Number of Projects Without Original Date of Commissioning	12
Number of Projects Without Date Of Commissioning	63

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 124 projects, 8 projects are on schedule and 41 projects are delayed .63 projects do not have fixed dates of commissioning.12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

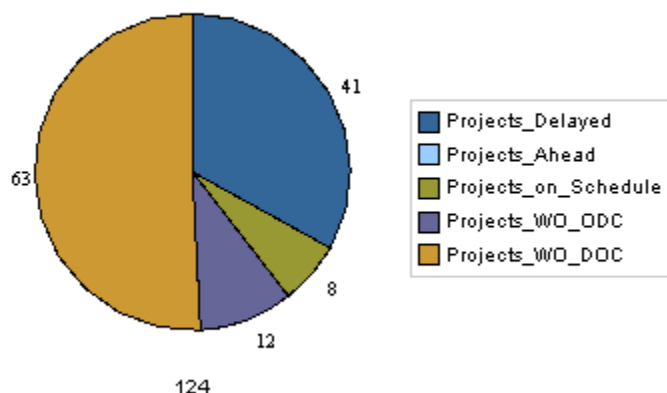

III. Investment Scenario

The Total Original cost of implementation of 124 projects when sanctioned, was of the order of Rs. 60590.79 crore but this was subsequently revised to Rs. 147761.45 crore implying a cost overrun of 143.9%. The expenditure incurred on these projects till March, 2013 is Rs. 62924.93 crore, which is 42.6% of the revised cost of the projects.

Figures are in Rs. Crore

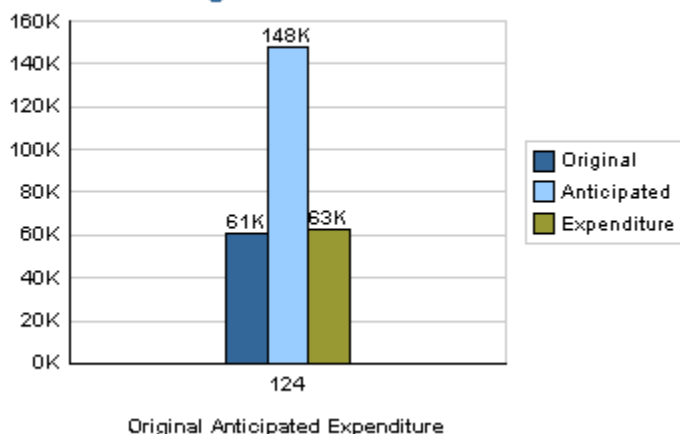

Sector wise current status of projects on the Flash Report


Power

I. Current Status:

Number of Projects	101
Number of Projects On Schedule	44
Number of Projects Delayed	53
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	2


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 101 projects, 1 project are ahead of schedule, 44 projects are on schedule and 53 projects are delayed .2 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

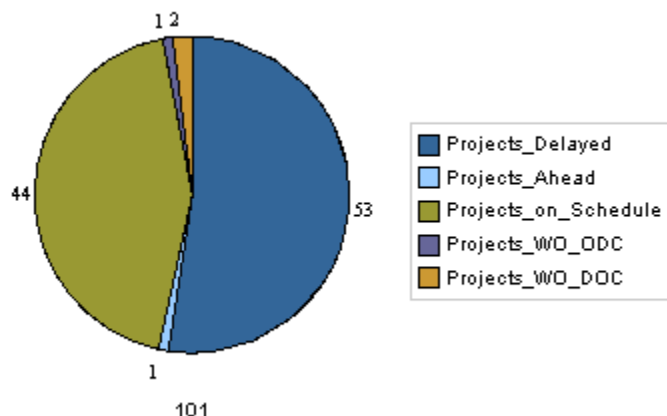

III. Investment Scenario

The Total Original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 243054.78 crore but this was subsequently revised to Rs. 258796.07 crore implying a cost overrun of 6.5%. The expenditure incurred on these projects till March, 2013 is Rs. 118189.09 crore, which is 45.7% of the revised cost of the projects.

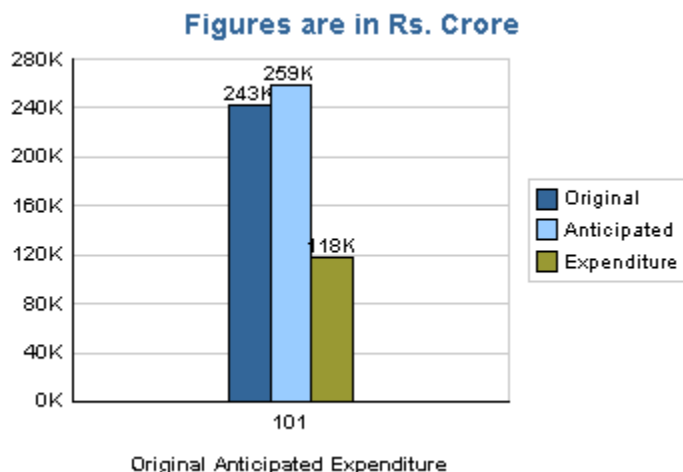

Sector wise current status of projects on the Flash Report

Petroleum


I. Current Status:

Number of Projects	67
Number of Projects On Schedule	20
Number of Projects Delayed	39

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 67 projects, 20 projects are on schedule and 39 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

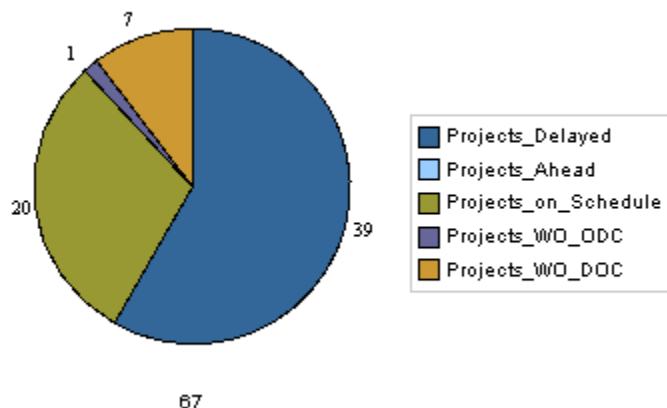

III. Investment Scenario

The Total Original cost of implementation of 67 projects when sanctioned, was of the order of Rs. 164236.71 crore but this was subsequently revised to Rs. 173456.75 crore implying a cost overrun of 5.6%. The expenditure incurred on these projects till March, 2013 is Rs. 79188.84 crore, which is 45.7% of the revised cost of the projects.

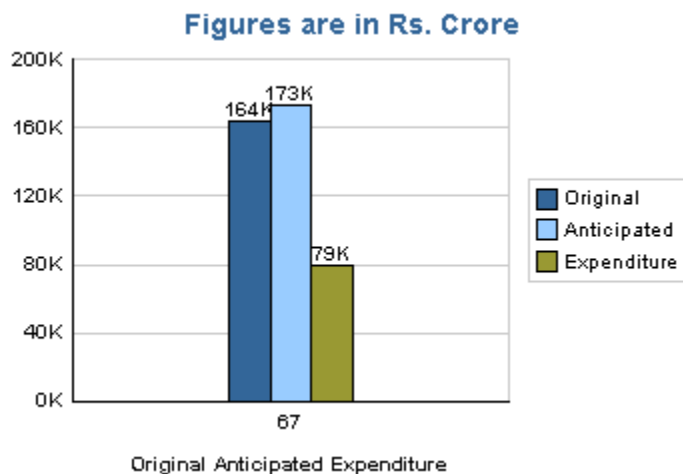

Sector wise current status of projects on the Flash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	2
Number of Projects Delayed	15

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 2 projects are on schedule and 15 projects are delayed.

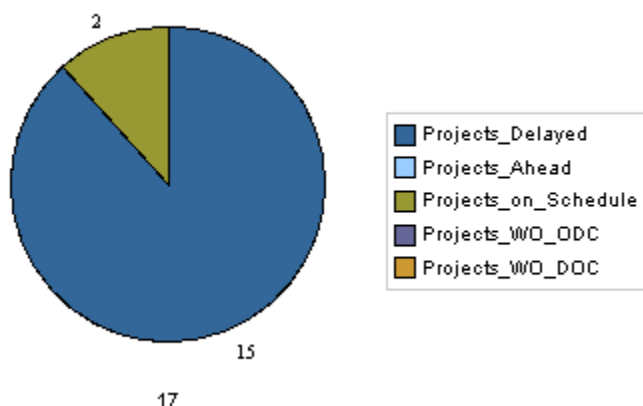

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till March, 2013 is Rs. 49111 crore, which is 68.7% of the revised cost of the projects.

Figures are in Rs. Crore

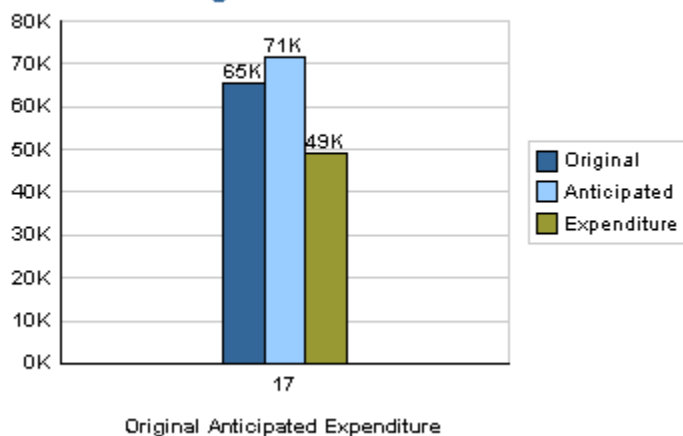

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	22
Number of Projects Delayed	28

Number of Projects Without Date Of Commissioning	1
--	---


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 51 projects, 22 projects are on schedule and 28 projects are delayed .1 project do not have fixed dates of commissioning.

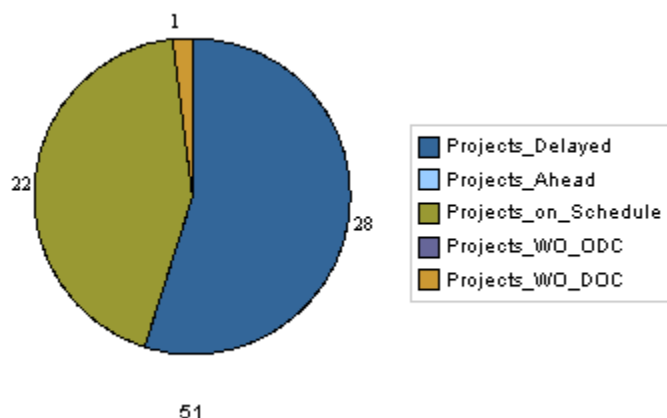

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37510.52 crore implying a cost overrun of 4%. The expenditure incurred on these projects till March, 2013 is Rs. 14345.29 crore, which is 38.2% of the revised cost of the projects.

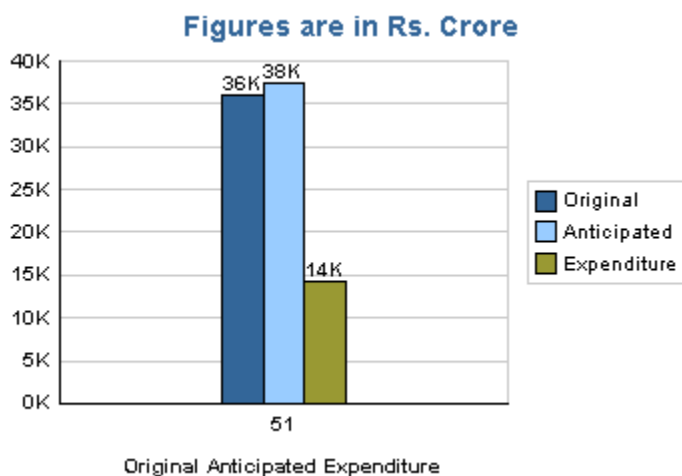

Sector wise current status of projects on the Flash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

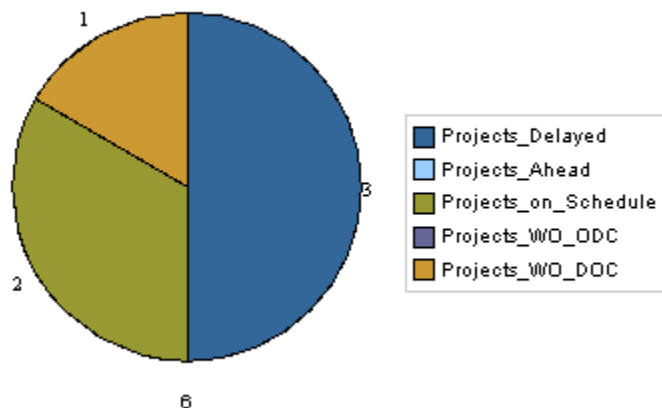

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till March, 2013 is Rs. 5205.34 crore, which is 85.9% of the revised cost of the projects.

Figures are in Rs. Crore

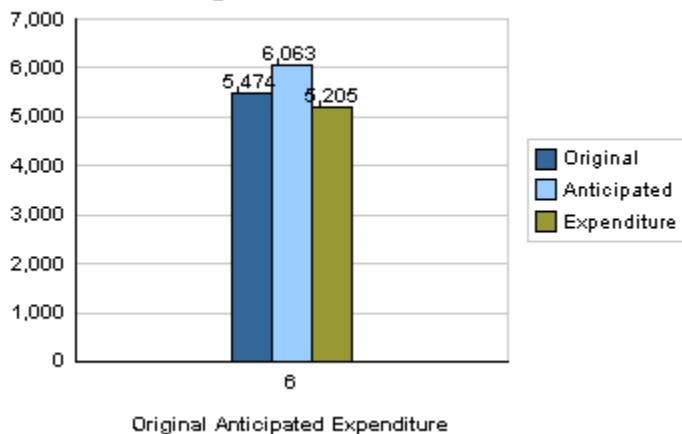

Sector wise current status of projects on the Flash Report

Atomic Energy

I. Current Status:


Number of Projects 4

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project do not have fixed dates of commissioning.

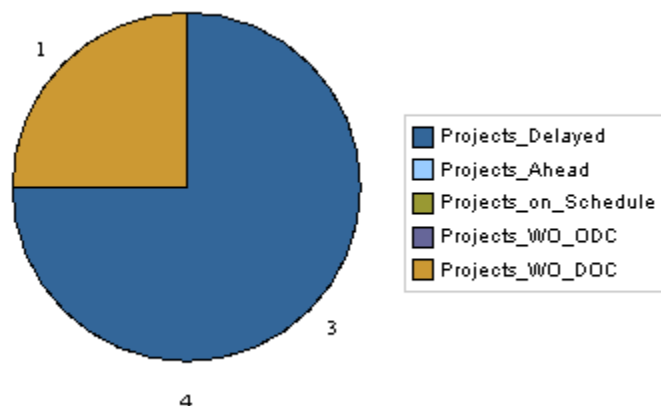

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till March, 2013 is Rs. 23769.48 crore, which is 50.9% of the revised cost of the projects.

Figures are in Rs. Crore

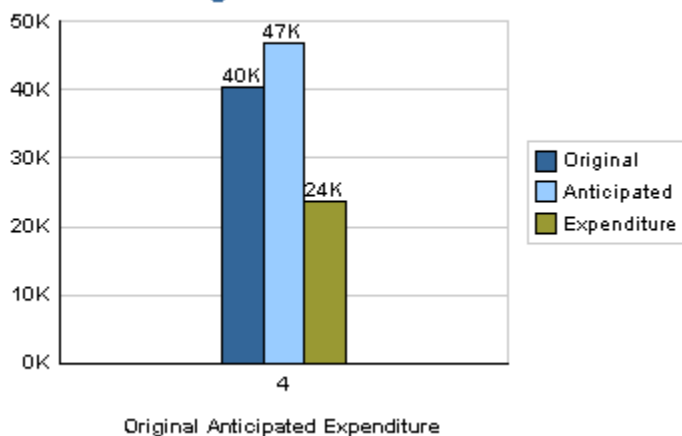

ANNEXURES

CENRAL SECTOR PROJECTS					
SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	33	27471.75	35095.62	20386.23
2	Arunachal Pradesh	4	9512.22	14144.29	9234.69
3	Assam	34	22035.93	35386.06	24969.70
4	Bihar	30	26917.64	34877.43	24864.60
5	Chhatisgarh	25	58429.84	59712.92	18730.05
6	Delhi	4	38214.41	38194.82	3102.36
7	Goa	1	335.61	335.61	206.39
8	Gujarat	22	33405.07	33607.01	10915.01
9	Haryana	8	4054.38	5741.02	6822.81
10	Himachal Pradesh	5	13355.57	17246.69	13722.06
11	Jammu and Kashmir	10	14926.96	34825.56	15570.54
12	Jharkhand	23	14447.40	18632.54	9151.70
13	Karnataka	26	46344.40	55830.82	22034.57
14	Kerala	7	20376.67	21818.22	5528.57
15	Madhya pradesh	20	18545.58	18826.15	9147.41
16	Maharashtra	48	88574.45	99360.84	45692.26
17	Manipur	1	727.56	4444.00	1295.18
18	Meghalaya	2	762.00	762.00	732.79
19	Mizoram	2	1532.97	3307.12	437.39
20	Multi State	110	146099.85	157391.95	70569.95
21	Nagaland	1	850.00	850.00	8.45
22	Odisha	30	56171.63	61152.93	36389.40
23	Punjab	6	3542.01	4483.78	3875.82
24	Rajasthan	14	21115.76	20927.99	7770.88
25	Sikkim	2	1648.94	3690.04	286.44
26	Tamil Nadu	32	48788.07	59567.94	40160.05
27	Tripura	3	1522.39	2018.85	1141.81
28	Uttar Pradesh	24	20316.07	24537.74	12763.99
29	Uttarakhand	5	7624.21	8564.64	2434.20
30	West Bengal	26	42064.29	54403.52	29815.77
TOTAL		558	789713.63	929738.10	447761.07

List of Projects in which Expenditure is more than cost

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	0.00	15550.00
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492.00	0.00	4058.48
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0.00	2463.38
4	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756.00	898.00	915.58
5	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2008	825.00	0.00	1379.28
6	KOLDAM HEP (NTPC)	Power	10/2002	4527.15	0.00	4842.00
7	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	10/2003	768.92	0.00	1686.98
8	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0.00	1310.02
9	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	0.00	1927.67
10	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	611.01	0.00	841.10
11	CHUTAK HYDRO-ELECTRIC PROJECT	Power	08/2006	621.26	0.00	775.32
12	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	Power	07/2006	557.24	0.00	598.40
13	RAMPUR HEP(412 MW)	Power	01/2007	2047.03	0.00	2325.70
14	TRIPURA GAS BASED POWER PROJECT	Power	07/2009	421.01	0.00	514.21
15	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	599.81
16	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	550.45
17	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	9001.45
18	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	215.16
19	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240.00	0.00	600.41
20	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	02/1997	295.00	412.91	603.29
21	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	04/1996	157.00	262.82	288.23
22	KARUR-SALEM(NL),SR	Railways	02/1997	155.55	155.00	762.61
23	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	03/1996	155.74	429.49	641.37
24	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	1500.00	2701.00
25	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	349.90
26	RANCHI-LOHARDAGA(GC),SER	Railways	04/1997	194.07	194.07	325.62
27	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	04/1997	233.00	501.69	691.31
28	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	07/1998	248.44	576.27	946.07

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
29	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100.00	492.98	741.20
30	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	03/2002	381.17	381.17	626.57
31	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.40	323.40	504.57
32	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	03/2002	409.00	625.30	835.94
33	RENIGUNTA-GUNTAKAL(RE)	Railways	06/2000	168.34	0.00	344.44
34	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100.00	100.00	536.30
35	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	733.00	733.00	1344.95
36	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	03/2000	907.69	3156.32	3374.48
37	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	278.33
38	JIND-SONEPAT (NL),NR	Railways	01/2004	190.81	238.56	434.76
39	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	166.16	0.00	259.32
40	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	727.53	1295.18
41	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.70	915.70	1703.60
42	BILASPUR-URKURA (DL)	Railways	04/1997	151.52	0.00	334.15
43	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	04/2000	133.41	207.00	222.32
44	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	04/2003	136.62	0.00	243.81
45	MANSI-PURNIA (EXTENSION OF MANSI SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	419.20
46	BHOPAL BINA 3D LINE DOUBLING	Railways	09/2007	687.20	0.00	702.45
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	592.35
48	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170.00	170.00	396.76
49	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156.00	156.00	318.86
50	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3425.69
51	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	12/2003	157.47	0.00	228.28
52	HAPUR-GARHMAKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	03/2005	220.00	0.00	282.68
53	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport & Highways	12/2003	230.00	0.00	233.03

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
54	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	12/2003	240.00	0.00	294.65
55	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	12/2003	340.68	0.00	400.56
56	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	03/2005	190.00	0.00	264.27
57	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport & Highways	12/2003	280.00	0.00	301.81
58	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport & Highways	12/2003	195.00	0.00	231.15
59	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport & Highways	12/2003	237.80	0.00	275.04
60	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport & Highways	12/2003	332.94	0.00	441.45
61	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	12/2003	275.00	0.00	279.76
62	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	12/2003	251.03	0.00	326.29
63	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	12/2003	200.00	0.00	281.55
64	GUWHATI TO NALBARI (AS-4)	Road Transport & Highways	12/2003	175.96	0.00	182.53
65	NAGAON TO DHARAMTUL (AS-2)	Road Transport & Highways	12/2003	264.72	0.00	299.20
66	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	12/2003	245.00	0.00	491.21
67	GUWAHATI TO NALBARI (AS-5)	Road Transport & Highways	12/2003	198.16	0.00	242.38
68	NALBARI TO BIJNI (AS-6)	Road Transport & Highways	12/2003	225.00	0.00	258.39
69	NALBARI T BIJNI (AS-7)	Road Transport & Highways	12/2003	208.00	0.00	290.59

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
70	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport & Highways	12/2003	160.00	0.00	197.55
71	DHARAMTUL TO SONAPUR (AS-19)	Road Transport & Highways	12/2003	200.00	0.00	246.20
72	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	03/2005	168.00	0.00	457.30
73	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	03/2005	280.00	0.00	581.49
74	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport & Highways	04/2000	263.27	0.00	276.26
75	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport & Highways	12/2003	217.61	0.00	258.43
76	GWALIOR BYPASS, NH-75,3	Road Transport & Highways	12/2003	300.93	0.00	303.02
77	JHANSI TO LALITPUR, NH-25,26	Road Transport & Highways	12/2003	355.06	0.00	501.86
78	TRICHY - KORUR NH-67	Road Transport & Highways	03/2005	516.00	0.00	760.07
79	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	03/2005	941.00	0.00	1901.00
80	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH	Road Transport & Highways	03/2005	557.00	0.00	932.27
81	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport & Highways	12/2003	232.45	0.00	295.39
82	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	04/2007	486.00	0.00	637.97
83	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport & Highways	03/2005	940.00	0.00	1293.20
84	Gujarat/Maharashtra BorderSurat-Hazira Port Section	Road Transport & Highways	03/2010	1509.10	0.00	1675.00
85	Pune-sholapur,pkg1	Road Transport & Highways	11/2009	1110.00	0.00	1802.10

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
86	Kishangarh-Ajmer-Beawer	Road Transport & Highways	11/2009	795.00	0.00	1055.70
87	Chennai-Tada(Six lane)	Road Transport & Highways	04/2009	353.37	0.00	395.08
88	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport & Highways	04/2009	1673.70	0.00	2777.00
89	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	02/2009	1693.75	0.00	2685.60
90	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport & Highways	05/2009	572.30	0.00	761.43
91	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	05/2009	1108.00	0.00	3465.90
92	Jaipur-Tonk-Deoli	Road Transport & Highways	06/2010	792.06	0.00	1649.10
93	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport & Highways	09/2010	946.00	0.00	1394.40
94	Talegaon-amravati	Road Transport & Highways	11/2009	567.00	0.00	891.08
95	Hazaribagh-Ranchi	Road Transport & Highways	08/2010	625.07	0.00	928.03
96	Armur to kadloor yellareddy	Road Transport & Highways	02/2010	390.56	0.00	631.65
97	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport & Highways	09/2010	671.00	0.00	737.54
98	AMRITSAR-PATHANKOT	Road Transport & Highways	05/2010	705.00	0.00	1252.70
99	PANIPAT-ROHTAK	Road Transport & Highways	04/2011	807.00	0.00	1152.40
100	DEVIHALLI-HASSAN	Road Transport & Highways	12/2010	453.00	0.00	487.86
101	MURADABAD-BAREILY	Road Transport & Highways	04/2010	1267.00	0.00	1313.30

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	CUMULATIVE EXPENDITURE
102	INDORE-DEWAS(NH-3)	Road Transport & Highways	11/2010	325.00	0.00	447.45
103	2 LANNING OF MOKAMA-MUNGER	Road Transport & Highways	05/2011	351.54	0.00	392.02
104	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport & Highways	12/2010	1008.50	0.00	1151.40
105	ROHTAK-BAWAL	Road Transport & Highways	05/2011	650.00	0.00	928.72
106	GHAZIABAD-ALIGARH NH-91	Road Transport & Highways	02/2011	1141.00	0.00	1200.30
107	2-LANNING OF SHILONG BYPASS	Road Transport & Highways	02/2011	226.00	0.00	282.33
108	4-LANNING OF CHAPRA-HAJIPUR	Road Transport & Highways	01/2011	575.00	0.00	712.68
109	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport & Highways	05/2011	511.54	0.00	579.51
110	JAIPUR-REENGUS	Road Transport & Highways	08/2010	267.81	0.00	564.50
111	Acquisition of Two nos. of 3060 DWT	Shipping & Ports	04/2009	277.03	280.00	294.87
112	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	03/2007	245.67	298.17	371.18
113	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	Steel	10/2005	8692.00	0.00	10235.67
114	COKE OVEN BATTERY NO. 4 PHASE-II	Steel	08/2007	108.00	0.00	137.65
115	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	07/2007	230.00	0.00	254.92

List of Projects Ahead of Schedule

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	Northern Region system strengthening scheme-XXII - [N18000091	12/2010	209.78 -	209.78	119.20	08/2013 -	03/2013
	Total		209.78 -	209.78	119.20		
	<u>Shipping & Ports</u>						
2	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 10/2013	10/2013
3	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,633.76	554.60		
	Grand Total		2,067.88	1,843.54	673.80		

List of project Without Original Date of Commissioning

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Petroleum</u>									
1	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 394.00	394.00	381.67	- -	03/2013	-	21/19
	Total		224.00 -	394.00	381.67				21/19
<u>Power</u>									
2	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01 -	623.44	514.21	- -	07/2013	-	7/29
	Total		421.01 -	623.44	514.21				7/29
<u>Railways</u>									
3	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	211.53	- -	03/2013	-	0/0
4	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,408.47	- -	03/2013	-	0/0
5	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	792.25	- -	03/2013	-	0/6
6	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	318.86	- -	06/2013	-	0/0
7	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
8	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	504.57	- -	03/2014	-	0/1
9	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	239.15	- -	03/2014	-	0/0
10	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	2,232.50	1,703.60	- -	03/2014	-	0/0
11	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	145.22	- -	03/2014	-	0/0
12	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	248.71	- -	03/2015	-	0/0
13	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	130.40	- -	03/2015	-	0/0
14	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
	Total		3,710.86 -	10,796.72	5,898.89				0/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Road Transport & Highways									
15	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	188.39	-	04/2013	-	2/2
16	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	1,394.40	-	06/2013	-	3/3
17	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	487.86	-	06/2013	-	1/1
18	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	437.95	-	10/2013	-	2/2
19	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	570.06	-	12/2013	-	0/1
20	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	737.54	-	06/2014	-	2/3
Total			4,069.00	4,069.00	3,816.20				10/12
Grand Total			8,424.87	15,883.16	10,610.97				38/67

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
Atomic Energy					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI, Tamil Nadu	09/2003	3,492.00	09/2010	-
			-	-	
	Total		3,492.00		
			-		
Civil Aviation					
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI, Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
			2,015.00	02/2012	
	Total		1,808.00		
			-		
Coal					
3	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL, Andhra Pradesh	10/2006	249.03	03/2012	-
			-	-	
	Total		249.03		
			-		
Petroleum					
4	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin, Karnataka	07/2010	1,043.57	04/2012	01/2013
			-	-	
5	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	-	-
			898.00	-	
6	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - [N16000070]GAIL, Multi State	07/2009	238.68	01/2012	-
			-	-	
7	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18	01/2013	-
			-	-	
8	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL, Multi State	08/2009	1,793.00	09/2012	-
			-	-	
9	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00	-	-
			-	-	
10	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	07/2012	-
			-	07/2012	
	Total		13,552.35		
			-		
Power					
11	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC, Jammu and Kashmir	08/2006	621.26	02/2011	01/2013
			-	10/2012	
12	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45	12/2007	-
			1,007.16	12/2009	
	Total		1,217.71		
			-		
Railways					
13	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Odisha	02/1996	57.94	03/1998	08/2005
			604.04	08/2005	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
14	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
15	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
16	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
17	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
18	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
19	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
20	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
21	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
22	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
23	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012
24	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
25	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
26	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
27	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
28	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24 377.32	- -	03/2012
29	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER, Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
30	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	- -	03/2012
31	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	- -	03/2012
32	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
33	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR, Karnataka	04/1995	65.94 302.23	- -	12/2012
34	RANCHI-LOHARDAGA(GC),SER - [220100214]SER, Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
35	JIND-SONEPAT (NL), NR - [220100280]NR, Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
36	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR, Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
37	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 412.91	- -	01/2013
38	CHANDIGARH-LUDHIANA(NEW BG LINE), NR - [220100241]NR, Punjab	07/1998	248.44 576.27	12/2012 01/2013	02/2013
39	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
40	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER, Bihar	04/2003	218.19 218.19	- -	02/2013

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
41	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
42	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
43	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
44	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
45	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
46	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
47	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
48	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	-
49	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
50	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-
51	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
52	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
53	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
54	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	-
55	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
56	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
57	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
58	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
59	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
60	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
61	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
62	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
63	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
64	HAPIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
65	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
66	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya Pradesh	04/2001	727.13 727.13	- -	-
67	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
68	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
69	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
70	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
71	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
72	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
73	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-
74	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
75	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
Total			18,418.92 -		
Shipping & Ports					
76	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
77	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 -	- 01/2009	01/2009
78	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
79	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
80	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
81	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012
82	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
83	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
84	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
Total			5,867.48 -		
Telecommunications					
85	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
86	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
87	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013
88	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	02/2013
89	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
90	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
91	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
92	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
	Total		2,764.39 -		
	Urban Development				
93	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
	Water Resources				
94	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		48,026.96		

List of Delay Project w.r.t. original and revised

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,550.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	2,469.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,692.00	12/2016	03/2017	3	-
Total			36,950.00	41,049.00	19,711.00				
<u>Civil Aviation</u>									
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,463.38	05/2011	03/2013	22	-
5	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	206.39	05/2012	06/2013	13	-
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	226.70	01/2011 04/2013	12/2013	35	8
Total			2,587.58	2,970.07	2,896.47				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,654.23	06/2009	01/2014	55	-
8	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96	302.96	109.05	03/2010	03/2014	48	-
9	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	236.09	03/2011	03/2014	36	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	4,128.29	03/2012	03/2014	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
11	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	102.56	03/2012 -	03/2014	24	-
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	431.80	03/2013 09/2012	07/2014	16	22
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	4.42	03/2012 -	03/2015	36	-
14	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	113.13	03/2013 -	03/2015	24	-
15	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	119.73	03/2010 -	03/2015	60	-
16	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	126.19	03/2013 -	03/2015	24	-
17	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	142.90	03/2012 -	03/2015	36	-
18	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.77	03/2012 -	03/2015	36	-
19	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	91.56	03/2013 -	03/2015	24	-
20	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,409.32	03/2014 -	03/2016	24	-
21	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,268.44	03/2014 -	03/2016	24	-
22	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44	-
23	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	265.64	03/2014 -	03/2016	24	-
24	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	83.46	12/2012 -	03/2016	39	-
25	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2016	24	-
26	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.91	03/2014 -	03/2016	24	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24	-
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42	321.50	205.78	03/2014	03/2016	24	-
29	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.91	03/2011	03/2016	60	-
30	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	130.79	03/2012	03/2016	48	-
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.92	03/2011	03/2017	72	-
32	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-
33	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87	179.87	60.75	03/2012	03/2017	60	-
34	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	28.00	12/2015	08/2017	20	-
Total			24,262.90	26,136.56	11,832.26				
Fertilisers									
35	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	1,087.00	01/2013	03/2013	2	-
Total			1,478.63	1,478.63	1,087.00				
Steel									
36	67.5 MW TG-5 AUX. SYSTEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	254.92	02/2011	04/2013	26	-
37	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	252.34	08/2010	04/2013	32	-
38	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	10,235.67	10/2009	06/2013	44	-

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
39	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	349.17	12/2011 03/2012	06/2013	18	15
40	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	137.65	10/2012 -	06/2013	8	-
41	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	235.36	05/2012 -	06/2013	13	-
42	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	191.31	05/2013 11/2013	11/2013	6	0
43	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	14,480.55	12/2011 -	12/2013	24	-
44	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,469.92	12/2011 -	12/2013	24	-
45	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 11,812.00	11,812.00	9,032.45	03/2013 -	12/2013	9	-
46	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	268.27	04/2013 12/2013	12/2013	8	0
47	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,521.60	12/2012 -	12/2013	12	-
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	8,533.85	03/2013 -	03/2014	12	-
49	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	32.28	11/2013 -	03/2014	4	-
50	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	70.18	10/2013 -	03/2014	5	-
Total			64,698.32	70,855.86	49,065.52				
Petrochemicals									
51	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	6,229.56	04/2012 12/2013	12/2013	20	0

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
Total			5,460.61	8,920.00	6,229.56				
Petroleum									
52	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	765.59	12/2012	12/2014	24	-
53	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
54	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
55	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	195.28	03/2013	04/2013	1	-
56	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	660.26	03/2010 03/2012	05/2013	38	14
57	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,185.52	05/2010 03/2013	05/2013	36	2
58	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12
59	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	677.99	03/2011 05/2011	05/2013	26	24
60	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	165.28	02/2013	05/2013	3	-
61	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00	12,160.26	8,727.48	01/2012	05/2013	16	-
62	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	06/2013	87	3
63	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
64	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,663.16	09/2011 03/2012	06/2013	21	15
65	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,448.09	09/2011 05/2012	06/2013	21	13
66	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,483.80	06/2012 -	06/2013	12	-
67	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	170.77	08/2012 -	06/2013	10	-
68	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	211.00	04/2012 -	06/2013	14	-
69	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	07/2013	19	-
70	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	422.00	01/2013 -	08/2013	7	-
71	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,067.86	09/2012 -	09/2013	12	-
72	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	73.90	09/2012 -	09/2013	12	-
73	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	566.69	07/2012 -	10/2013	15	-
74	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	111.54	11/2012 -	10/2013	11	-
75	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
76	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	756.65	97.69	05/2013 -	11/2013	6	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
77	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,204.63	08/2010 03/2012	12/2013	40	21
78	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.88	09/2011 -	12/2013	27	-
79	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	201.83	03/2012 -	12/2013	21	-
80	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	35.90	08/2013 -	01/2014	5	-
81	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84	0
82	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	03/2014	16	-
83	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,410.63	03/2013 -	03/2014	12	-
84	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	-	06/2012 -	03/2014	21	-
85	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,158.35	03/2013 03/2014	04/2014	13	1
86	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1	-
87	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.41	10/2010 -	12/2014	50	-
88	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	586.00	4.28	07/2015 -	08/2015	1	-
89	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	311.69	12/2015 -	05/2016	5	-
90	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120	0
Total			111,742.87	121,838.03	68,448.88				

Power

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
91	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,846.81	09/2008 -	03/2013	54	-
92	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	429.40	09/2010 -	03/2013	30	-
93	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,900.00	08/2012 -	03/2013	7	-
94	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00 -	5,915.00	4,300.00	10/2012 -	03/2013	5	-
95	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,686.98	03/2007 09/2012	04/2013	73	7
96	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	758.75	598.40	01/2010 -	04/2013	39	-
97	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	67.30	10/2012 -	04/2013	6	-
98	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,927.67	11/2009 02/2013	05/2013	42	3
99	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,187.00	02/2012 -	05/2013	15	-
100	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,122.60	06/2012 -	05/2013	11	-
101	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	841.10	08/2010 01/2013	06/2013	34	5
102	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	135.88	06/2012 -	06/2013	12	-

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
103	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	873.40	10/2009 -	09/2013	47	-
104	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	157.50	11/2011 -	09/2013	22	-
105	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	737.90	05/2012 -	09/2013	16	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	116.20	01/2013 -	09/2013	8	-
107	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	75.60	04/2013 -	09/2013	5	-
108	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,058.00	10/2012 -	11/2013	13	-
109	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,330.80	12/2012 -	12/2013	12	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	353.20	11/2011 -	12/2013	25	-
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	253.50	02/2012 -	12/2013	22	-
112	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,204.40	12/2012 -	12/2013	12	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
113	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	524.70	11/2012 -	12/2013	13	-
114	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	895.20	03/2013 -	12/2013	9	-
115	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,325.70	01/2012 -	02/2014	25	-
116	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,310.02	09/2009 06/2013	03/2014	54	9
117	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,078.38	10/2010 01/2013	03/2014	41	14
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	341.70	11/2011 -	03/2014	28	-
119	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,288.60	10/2012 -	03/2014	17	-
120	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	2,015.00	08/2012 -	03/2014	19	-
121	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,640.10	08/2012 -	03/2014	19	-
122	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,241.40	11/2012 -	03/2014	16	-
123	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	838.50	08/2012 -	03/2014	19	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
124	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19	2,743.19	1,337.70	12/2013	03/2014	3	-
125	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	245.40	07/2013	03/2014	8	-
126	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	747.10	04/2013	03/2014	11	-
127	EASTERN REGION TRANSMISSION SYSTEM- III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	570.80	11/2012	03/2014	16	-
128	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	61.40	01/2013	06/2014	17	-
129	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15	6,358.91	4,842.00	04/2009	09/2014	65	-
130	PARE HYDRO ELECTRIC PROJECT (110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99	573.99	505.68	08/2012 08/2013	09/2014	25	13
131	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	5,341.00	08/2013	09/2014	13	-
132	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63	913.63	394.95	07/2014	02/2015	7	-
133	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	5,609.30	08/2013	03/2015	19	-
134	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40	524.40	14.90	04/2015	05/2015	1	-
135	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	3,628.00	07/2011	10/2015	51	-
136	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48	2,978.48	1,730.00	03/2013	03/2016	36	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
137	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	342.92	07/2014 -	05/2016	22	-
138	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.88	2,978.86	464.30	07/2010 02/2016	11/2016	76	9
139	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,095.31	01/2016 01/2016	11/2016	10	10
140	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,052.00	12/2009 -	02/2017	86	-
141	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	2,496.90	2,208.33	05/2013 06/2016	03/2017	46	9
142	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,201.82	09/2010 08/2014	12/2017	87	40
143	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,877.58	09/2009 07/2014	03/2018	102	44
Total			135,655.62	150,492.03	100,973.43				
Railways									
144	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-
145	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	677.11	12/2011 12/2011	03/2013	15	15
146	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	288.23	03/2012 03/2012	03/2013	12	12
147	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	278.33	02/2011 02/2011	03/2013	25	25
148	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	285.99	03/2012 03/2013	03/2013	12	0
149	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	419.20	03/2012 03/2013	03/2013	12	0
150	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	215.16	03/2002 -	06/2013	135	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
151	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Mult State	04/1986	158.77 580.83	580.83	557.35	03/1994 -	10/2013	235	-
152	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	369.21	12/2009 03/2011	10/2013	46	31
153	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	124.23	12/2011 11/2013	11/2013	23	0
154	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	224.89	141.55	03/2012 -	12/2013	21	-
155	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	158.71	12/2012 -	12/2013	12	-
156	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	246.40	03/2004 12/2010	03/2014	120	39
157	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	220.91	06/2013 06/2013	03/2014	9	9
158	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	440.63	03/2013 -	03/2014	12	-
159	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	116.77	02/2006 -	06/2014	100	-
160	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	259.32	02/2009 02/2009	08/2014	66	66
161	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	222.32	03/2009 03/2009	08/2014	65	65
162	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	208.66	12/2008 -	09/2014	69	-
163	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	960.22	03/2009 12/2012	12/2014	69	24
164	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	177.33	03/2007 03/2007	03/2015	96	96

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
165	KATIHAR - JOGBANI (GC)(NEFR) - [N20100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.20	12/2010 12/2010	03/2015	51	51
166	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [N20100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,344.95	12/2008 -	03/2015	75	-
167	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	118.88	12/2012 -	03/2015	27	-
168	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,425.69	03/2009 -	03/2015	72	-
169	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [N20100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,701.00	04/2008 03/2014	12/2015	92	21
170	PATNA GANGA BRIDGE (NL), ECR - [N20100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,696.36	10/2007 12/2012	12/2015	98	36
171	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	249.38	02/2010 11/2012	12/2015	70	37
172	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	702.45	03/2010 -	12/2015	69	-
173	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	456.83	03/2014 -	12/2015	21	-
174	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	1,008.73	03/2014 03/2016	03/2016	24	0
175	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	49.50	03/2014 -	03/2016	24	-
176	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	439.39	06/2005 07/2011	06/2016	132	59
177	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	33.44	03/2016 -	06/2016	3	-
178	BANKURA - DAMODAR (GC) (SER) - [N20100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	472.01	03/2005 12/2008	12/2016	141	96
179	JIRIBAM TO IMPHAL (TUPU)(NL)(NEFR) - [N20100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	1,295.18	03/2011 03/2014	03/2017	72	36

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
180	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	819.40	188.04	03/2010 03/2017	03/2017	84	0
181	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	42.44	04/2014 -	03/2017	35	-
182	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017	15	-
183	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2017	24	-
184	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	9,001.45	03/2001 -	12/2017	201	-
Total			27,923.86	73,536.56	30,958.01				
Road Transport & Highways									
185	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2013	54	-
186	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	165.13	03/2008 -	03/2013	60	-
187	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	190.95	07/2008 -	03/2013	56	-
188	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.44	04/2004 -	04/2013	108	-
189	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	400.56	03/2008 -	04/2013	61	-
190	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	268.59	06/2011 06/2011	04/2013	22	22
191	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	04/2013	46	-
192	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	04/2013	110	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
193	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	303.02	10/2009	04/2013	42	-
194	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70	228.70	194.51	02/2004	04/2013	110	-
195	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	1,649.10	12/2012	04/2013	4	-
196	Amur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	04/2013	14	-
197	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	441.45	09/2008	05/2013	56	-
198	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	299.20	06/2008	05/2013	59	-
199	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	246.20	06/2008	05/2013	59	-
200	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	05/2013	28	-
201	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	192.06	08/2004 07/2010	06/2013	106	35
202	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	192.39	08/2004	06/2013	106	-
203	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03	251.03	326.29	10/2008	06/2013	56	-
204	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	491.21	03/2008	06/2013	63	-
205	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	457.30	12/2008	06/2013	54	-
206	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	501.86	09/2009	06/2013	45	-
207	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	637.97	05/2010	06/2013	37	-

S.No Project		Date of Approval	Date of Commissioning		Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10	11	12
208	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,293.20	07/2012	06/2013	11	-		
209	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	1,055.70	05/2012	06/2013	13	-		
210	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,685.60	08/2011	06/2013	22	-		
211	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	572.30	761.43	10/2011	06/2013	20	-		
212	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	928.03	01/2013	06/2013	5	-		
213	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	1,252.70	11/2012	06/2013	7	-		
214	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	495.37	12/2009	07/2013	43	-		
215	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	790.93	03/2013	07/2013	4	-		
216	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81	267.81	564.50	02/2013	07/2013	5	-		
217	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	3,465.90	11/2011	08/2013	21	-		
218	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	272.75	05/2008	09/2013	64	-		
219	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00	250.39	279.76	10/2008	09/2013	59	-		
220	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	281.55	06/2008	09/2013	63	-		
221	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	258.39	06/2008	09/2013	63	-		
222	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	09/2013	38	-		
223	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	957.76	05/2013	09/2013	4	-		
224	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17	-		

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
225	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	602.63	02/2013 -	10/2013	8	-
226	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	11.28	01/2013 -	10/2013	9	-
227	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	282.68	09/2007 -	11/2013	74	-
228	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	228.28	09/2007 -	12/2013	75	-
229	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.65	10/2008 -	12/2013	62	-
230	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.27	01/2009 -	12/2013	59	-
231	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	197.55	05/2008 -	12/2013	67	-
232	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.29	06/2010 -	12/2013	42	-
233	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
234	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	12/2013	15	-
235	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,777.00	10/2011 -	12/2013	26	-
236	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	451.09	03/2013 -	12/2013	9	-
237	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	295.39	09/2010 -	01/2014	40	-
238	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	447.45	05/2013 -	02/2014	9	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
239	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	233.03	06/2005 -	03/2014	105	-
240	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	231.15	06/2008 -	03/2014	69	-
241	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	275.04	06/2008 -	03/2014	69	-
242	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	182.53	04/2008 -	03/2014	71	-
243	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	242.38	04/2008 -	03/2014	71	-
244	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	214.69	09/2007 -	03/2014	78	-
245	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	395.08	10/2011 -	03/2014	29	-
246	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	47.41	11/2012 -	03/2014	16	-
247	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	392.02	05/2013 -	03/2014	10	-
248	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	510.99	03/2013 -	03/2014	12	-
249	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI, Uttarakhand	11/2011	478.00 -	478.00	245.23	10/2013 -	03/2014	5	-
250	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI, Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5	-
251	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79	-
252	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.30	03/2013 -	04/2014	13	-
253	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	664.00	400.45	02/2014 -	04/2014	2	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
254	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	301.81	02/2009 03/2014	05/2014	63	2
255	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	290.59	04/2008 -	05/2014	73	-
256	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	131.26	07/2009 -	05/2014	58	-
257	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68	-
258	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014	67	-
259	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
260	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	560.12	07/2013 -	06/2014	11	-
261	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-
262	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	38.30	09/2013 -	07/2014	10	-
263	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24	-
264	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
265	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	258.43	04/2010 -	11/2014	55	-
266	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68	-
267	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73	-
268	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	141.82	04/2009 -	12/2014	68	-

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
269	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	932.27	02/2010 -	12/2014	58	-
270	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2015	31	-
271	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76 -	2,498.76	1,718.30	08/2014 -	07/2015	11	-
272	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
273	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	764.56	07/2015 -	06/2016	11	-
Total			48,537.74 -	50,476.36	46,959.15				
Shipping & Ports									
274	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST, Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	-
275	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	04/2013	15	7
276	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2013	06/2013	87	0
277	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP., Multi State	07/2011	220.49 -	220.49	98.31	01/2013 -	06/2013	5	-
278	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP., Mahara shtra	08/2010	612.72 532.83	532.83	364.52	12/2012 10/2013	10/2013	10	0
279	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	937.28	12/2010 09/2012	04/2014	40	19
Total			6,413.21 -	7,718.82	5,420.86				

(Mar,2013)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Telecommunications</u>									
280	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	06/2013	48	-
281	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53	-
282	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	823.48	11/2010 -	06/2013	31	-
283	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	170.25	05/2011 -	06/2013	25	-
284	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 -	09/2013	35	-
Total			2,934.85 -	2,760.60	1,261.21				
<u>Urban Development</u>									
285	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013	21	-
Total			6,395.00 -	11,609.00	2,482.18				
Grand Total			475,041.19	569,841.52	347,325.53				

List of On schedule Projects

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Civil Aviation						
1	GAGAN PROJECT - [N04000065]	9/2008	626.00 -	626.00	376.97	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	85.30	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	462.27		
	Coal						
3	KRISHNASHILA (NCL) (4MTY) - [N06000007]	6/2011	789.88 -	741.62	366.32	03/2013 -	03/2013
4	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	169.96	03/2015 03/2015	03/2015
5	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	40.86	03/2014 03/2014	03/2014
6	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	123.40	03/2017 -	03/2017
7	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	43.33	03/2016 -	03/2016
8	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
9	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	95.10	03/2016 -	03/2016
10	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	40.47	03/2016 -	03/2016
11	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
12	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
13	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	3.02	03/2015 -	03/2015
14	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
15	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	3.87	03/2018 03/2018	03/2018
16	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
17	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	35.83	03/2014 -	03/2014
18	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	269.10	03/2016 -	03/2016
19	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	31.29	03/2015 -	03/2015

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
20	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
21	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	71.92	03/2015 -	03/2015
22	JALLARAM SHAFT PROJECT - [N06000025	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
23	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	437.14	03/2016 03/2016	03/2016
24	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008	6/2008	1,188.31 -	1,188.31	716.99	03/2013 -	03/2013
Total			11,544.53 -	11,124.93	2,463.39		
<u>Petroleum</u>							
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	4/2008	825.00 -	1,827.00	1,379.28	04/2013 -	04/2013
26	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
27	Mounded Bullet Project at CPCL - [N16000154	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
28	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline [N16000153	4/2011	152.89 -	152.89	105.27	06/2013 -	06/2013
29	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	21.84	07/2015 -	07/2015
30	DABHOL BANGALORE PIPELINE PROJECT PHASE-II [N16000147	6/2009	486.00 -	486.00	44.40	09/2013 -	09/2013
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	666.00	-	11/2015 -	11/2015
32	REWARI KANPUR PIPELINE PROJECT - [N16000145	2/2012	1,210.64 -	1,210.64	60.89	11/2015 -	11/2015
33	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	36.13	12/2014 -	12/2014
34	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	34.37	03/2014 -	03/2014
35	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	192.77	05/2014 -	05/2014
36	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
37	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
38	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	678.24	05/2015 -	05/2015
39	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,059.63	69.89	03/2015 -	03/2015
40	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014
41	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
42	Wax Project - [N16000101	6/2010	576.60 -	576.60	47.04	12/2013 -	12/2013
43	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112	8/2010	8,140.00 -	8,140.00	1,701.79	02/2014 -	02/2014
44	Development of WO-16 Cluster Fields - [N16000105	6/2010	2,523.00 -	2,523.00	577.61	01/2014 -	01/2014
	Total		38,717.49 -	38,589.23	7,474.19		
Power							
45	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
46	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	1,290.90	03/2014 -	03/2014
47	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	705.60	05/2014 -	05/2014
48	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103	9/2011	1,940.13 -	1,940.13	682.60	09/2014 -	09/2014
49	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
50	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
51	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142	7/2012	1,527.00 -	1,527.00	36.00	08/2017 -	08/2017
52	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) [N18000140	11/2012	11,846.00 -	11,846.00	952.00	05/2017 -	05/2017
53	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139	1/2013	182.80 -	182.80	-	10/2014 -	10/2014
54	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A [N18000138	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
55	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID [N18000137	9/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI [N18000136	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
57	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	197.00	08/2015 -	08/2015
58	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	1,286.00	11/2016 -	11/2016
59	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	197.90	02/2014 -	02/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	229.80	08/2014 -	08/2014
61	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	565.90	07/2014 -	07/2014
62	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	535.50	08/2014 -	08/2014
63	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	107.00	06/2014 -	06/2014
64	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	838.60	12/2013 -	12/2013
65	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	251.70	10/2013 -	10/2013
66	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]	9/2011	1,366.34 -	1,366.34	491.90	12/2013 -	12/2013
67	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]	10/2011	558.26 -	558.26	124.50	11/2013 -	11/2013
68	MOUDA STPP STAGE 2 - [N18000132]	3/2012	7,921.47 -	7,921.47	774.00	09/2016 -	09/2016
69	KUDGI STPP STAGE 1 - [N18000131]	12/2011	15,166.19 -	15,166.19	1,295.00	12/2016 -	12/2016
70	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]	6/2012	1,263.26 -	1,263.26	183.60	11/2014 -	11/2014
71	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]	2/2012	3,201.44 -	3,201.44	426.40	10/2014 -	10/2014
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	95.50	11/2014 -	11/2014
73	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	157.00	08/2014 -	08/2014
74	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	33.90	06/2014 -	06/2014
75	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	586.70	06/2015 -	06/2015
76	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
77	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
78	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	90.50	10/2014 -	10/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	10.70	08/2014 -	08/2014
80	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	224.20	02/2015 -	02/2015
81	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	76.30	01/2014 -	01/2014
82	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117	1/2012	1,422.85 -	1,422.85	206.30	01/2015 -	01/2015
83	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	1,746.65	77.30	08/2014 -	08/2014
84	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	74.00	08/2014 -	08/2014
85	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102	7/2011	181.93 -	181.93	65.40	07/2013 -	07/2013
86	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099	3/2011	1,585.12 -	1,585.12	775.00	11/2013 -	11/2013
87	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	920.30	08/2013 -	08/2013
88	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077	4/2010	4,404.57 -	4,404.57	370.00	01/2015 -	01/2015
Total			105,550.66 -	105,550.66	14,935.00		
<u>Railways</u>							
89	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	78.15	02/2015 -	02/2015
90	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113	4/2008	653.19 -	653.46	230.27	03/2014 -	03/2014
91	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	4/2008	394.14 -	404.39	15.76	03/2013 -	03/2013
92	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	527.10	03/2014 -	03/2014
93	Suratpura - Hanumangarh - Sriganganagar Gauge Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	344.53	03/2014 -	03/2014
94	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112	4/2008	829.74 -	829.74	16.64	03/2015 -	03/2015
95	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	93.92	03/2016 -	03/2016

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
96	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. [N22000111]	4/2010	2,619.02 -	2,619.02	275.37	03/2016 -	03/2016
	Total		10,537.15 -	11,182.73	1,581.74		
<u>Road Transport & Highways</u>							
97	Indore-Jhabua-Gujrat/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013
98	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,152.40	10/2014 -	10/2014
99	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]	12/2010	1,008.50 -	1,008.50	1,151.40	06/2013 -	06/2013
100	ROHTAK-BAWAL - [N24000169]	5/2011	650.00 -	650.00	928.72	11/2013 -	11/2013
101	BAREILY-SITAPUR - [N24000200]	3/2011	1,046.00 -	1,046.00	291.01	09/2013 -	09/2013
102	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	956.68	06/2014 -	06/2014
103	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014
104	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196]	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
105	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	450.94	08/2013 -	08/2013
106	NIROLI-ROXY-RAJAMUNDA - [N24000194]	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
107	PUNE-SHOLAPUR,Pkg-II - [N24000193]	9/2011	835.00 -	835.00	122.65	01/2014 -	01/2014
108	4-laning of Barhi-Hazaribagh - [N24000191]	2/2012	398.00 -	398.00	344.43	02/2014 -	02/2014
109	JORBAT - BARAPANI - [N24000180]	1/2011	536.00 -	536.00	450.46	01/2014 -	01/2014
110	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	30.08	12/2015 -	12/2015
111	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	28.51	07/2014 -	07/2014
112	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	65.26	10/2014 -	10/2014
113	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	13.39	09/2015 -	09/2015
114	FOUR LANING OF ORISSA CHATTISHGARH BORDER [N24000218]	2/2013	1,232.00 -	1,232.00	87.61	08/2015 -	08/2015
115	PANVEL-INDAPUR - [N24000216]	12/2011	942.69 -	942.69	128.49	06/2014 -	06/2014
116	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	162.70	06/2015 -	06/2015
117	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	137.99	04/2014 -	04/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
118	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
119	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	255.27	04/2015 -	04/2015
120	SAMAIKHIALI GANDHIDHAM - [N24000223	9/2010	805.39 -	805.39	-	12/2013 -	12/2013
121	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	34.07	10/2014 -	10/2014
122	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	398.24	07/2014 -	07/2014
123	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	52.86	01/2014 -	01/2014
124	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	636.24	09/2014 -	09/2014
125	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	201.61	06/2014 -	06/2014
126	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43	218.49	08/2013 -	08/2013
127	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79	805.45	08/2013 -	08/2013
128	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	967.11	08/2013 -	08/2013
129	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
130	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	303.41	08/2013 -	08/2013
131	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	101.30	05/2013 -	05/2013
132	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
133	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.82	06/2013 -	06/2013
134	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	14.58	12/2013 -	12/2013
135	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
136	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,200.30	08/2013 -	08/2013
137	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	160.24	05/2014 -	05/2014
138	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
139	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	579.51	11/2013 -	11/2013
140	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	712.68	07/2013 -	07/2013
141	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	124.43	04/2014 -	04/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
142	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	536.03	03/2014 -	03/2014
143	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
144	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	771.14	03/2014 -	03/2014
145	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	282.33	02/2014 -	02/2014
146	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	745.79	08/2013 -	08/2013
147	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,313.30	06/2013 -	06/2013
148	DEOLI-KOTA - [N24000148	1/2011	593.00 -	593.00	485.67	07/2013 -	07/2013
149	New 4 Lane elevated road from chennai airport- maduravoyal NH no.4 [N24000139	9/2010	1,655.00 -	1,655.00	494.71	09/2013 -	09/2013
150	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	891.08	11/2013 -	11/2013
	Total		48,923.02 -	48,923.02	21,329.69		
Shipping & Ports							
151	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	306.12	02/2014 -	02/2014
152	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062	1/2012	511.87 -	511.87	107.56	03/2014 -	03/2014
	Total		1,478.33 -	1,506.69	413.68		
Steel							
153	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078	7/2012	332.65 -	332.65	42.40	08/2014 -	08/2014
154	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	2.88	12/2014 -	12/2014
	Total		587.55 -	587.55	45.28		
Urban Development							
155	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	2,804.31	03/2016 -	03/2016
156	FARIDABAD EXTENSION - [N28000057	9/2011	2,494.00 -	2,494.00	230.84	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	3,035.15		
	Grand Total		256,152.73	256,278.81	51,740.39		

List of Projects Without Milestones

(Mar,2013)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Civil Aviation</u>						
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	06/2013	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	12/2013	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	03/2015 -	03/2015	0/0
Total			5,473.58 -			0/0
<u>Coal</u>						
7	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	04/2014 -	04/2014	0/0
8	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
Total			1,570.15 -			0/0
<u>Steel</u>						
9	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	08/2014 -	08/2014	0/0
10	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	12/2014 -	12/2014	0/0
Total			587.55 -			0/0
<u>Petroleum</u>						
11	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	01/2013	0/0
12	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
15	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
16	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0
17	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	05/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
18	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
19	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	05/2013	0/0
20	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
21	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
22	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	06/2013	0/0
23	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012 -	06/2013	0/0
24	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
25	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	07/2013	0/0
26	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
27	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
28	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
29	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
30	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
31	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0
32	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
33	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2013	0/0
34	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
35	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
36	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
37	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
38	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
39	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
40	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 03/2014	04/2014	0/0
41	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	04/2014	0/0
42	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
43	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
44	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
45	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
46	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
47	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
48	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
49	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
50	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 -	03/2015 -	03/2015	0/0
51	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
52	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
53	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	08/2015	0/0
54	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
55	I REP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
56	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	-	0/0
57	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
Total			102,015.78 -			0/0
Power						
58	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013	0/0
59	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	03/2014	0/0
60	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	03/2014 -	03/2014	0/0
61	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	08/2014 -	08/2014	0/0
62	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
63	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	10/2014 -	10/2014	0/0
64	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
65	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
66	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0
67	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	12/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
68	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
69	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	03/2015 -	03/2015	0/0
70	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	04/2015 -	05/2015	0/0
71	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
72	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	12/2015 -	12/2015	0/0
73	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	06/2016 -	06/2016	0/0
74	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	08/2017 -	08/2017	0/0
Total			17,042.87 -			0/0
Railways						
75	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
76	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
77	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
78	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
79	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
80	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
81	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
82	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0
83	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
84	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
85	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
86	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
87	Dakshin-barasal-Iakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
88	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
89	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
90	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
91	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
92	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
93	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
94	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
95	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
96	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
97	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
98	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
99	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
100	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	02/2013	0/0
101	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
102	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
103	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
104	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
105	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
106	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
107	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
108	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
109	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
110	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
111	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
112	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
113	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	06/2013	0/0
114	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	06/2013	0/0
115	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
116	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
117	Ghutiasarif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
118	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
119	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 -	12/2013	0/0
120	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
121	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
122	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
123	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
124	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
125	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0
126	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
127	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
128	Suratpura - Hanumangarh - Sriganaganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
129	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
130	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	06/2014	0/0
131	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
132	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
133	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
134	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
135	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	02/2015	0/0
136	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
137	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
138	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
139	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0
140	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2015	0/0
141	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
142	Himmatnagar - Udaipur Gauge Convession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
143	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
144	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2015	0/0
145	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
146	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
147	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 11/2012	12/2015	0/0
148	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2015	0/0
149	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
150	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
151	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2016	0/0
152	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
153	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
154	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
155	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
156	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2016	0/0
157	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
158	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2017	0/0
160	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
161	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
163	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
164	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
165	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
166	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
167	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
168	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
169	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
170	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
171	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-	0/0
172	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
173	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
174	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
175	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	-	0/0
176	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
177	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
178	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
179	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
180	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
182	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
183	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
184	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
185	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
186	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
187	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
188	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
189	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
190	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
191	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
192	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
193	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
194	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
195	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
196	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
Total			59,987.39			0/0
Road Transport & Highways						
197	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
198	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	03/2013	0/0
199	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
200	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	04/2013	0/0
201	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	04/2013	0/0
202	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	04/2013	0/0
203	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	04/2013	0/0
204	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	04/2013	0/0
205	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	04/2013	0/0
206	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	04/2013	0/0
207	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
208	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	04/2013	0/0
209	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	05/2013	0/0
210	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	05/2013	0/0
211	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	05/2013	0/0
212	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	05/2013	0/0
213	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
214	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	06/2013	0/0
215	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	06/2013	0/0
216	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	06/2013	0/0
217	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	06/2013	0/0
218	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2013	0/0
219	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	06/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
220	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	06/2013	0/0
221	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	06/2013	0/0
222	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	06/2013	0/0
223	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	06/2013	0/0
224	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
225	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	06/2013	0/0
226	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
227	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
228	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
229	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
230	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	07/2013	0/0
231	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	07/2013	0/0
232	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	07/2013	0/0
233	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
234	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	07/2013	0/0
235	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
236	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
237	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
238	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	08/2013	0/0
239	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	08/2013 -	08/2013	0/0
240	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
241	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
242	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
243	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	09/2013	0/0
244	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2013	0/0
245	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	09/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
246	NALBARI TO BIJINI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	06/2008	09/2013	0/0
247	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	07/2010	09/2013	0/0
248	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
249	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	05/2013	09/2013	0/0
250	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
251	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
252	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	02/2013	10/2013	0/0
253	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
254	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0
255	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	09/2007	11/2013	0/0
256	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
257	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
258	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
259	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
260	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	09/2007	12/2013	0/0
261	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	10/2008	12/2013	0/0
262	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	01/2009	12/2013	0/0
263	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	05/2008	12/2013	0/0
264	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	06/2010	12/2013	0/0
265	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
266	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	09/2012	12/2013	0/0
267	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	12/2013	0/0
268	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
269	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
270	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	03/2013	12/2013	0/0
271	SAMAIKHIALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39	12/2013	12/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
272	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	01/2014	0/0
273	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
274	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
275	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	01/2014	0/0
276	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
277	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
278	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
279	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
280	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
281	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
282	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
283	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
284	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
285	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
286	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
287	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
288	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
289	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
290	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
291	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
292	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
293	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	03/2014	0/0
294	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
295	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
296	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
297	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
298	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHHTH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
299	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
300	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
301	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
302	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
303	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
304	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
305	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
306	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
307	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
308	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
309	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
310	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
311	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
312	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
313	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2014	0/0
314	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
315	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
316	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
317	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
318	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
319	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
320	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
321	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
322	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
323	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
324	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0
325	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
326	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
327	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
328	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
329	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
330	SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
331	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
332	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
333	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
334	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
335	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
336	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
337	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
338	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
Total			97,264.26 -			0/0
Shipping & Ports						
339	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
340	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
341	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
342	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
343	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 -	11/2012	0/0
344	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
345	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
346	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
347	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
348	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	04/2013	0/0
349	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
350	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 -	06/2013	0/0
351	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 10/2013	10/2013	0/0
352	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 10/2013	10/2013	0/0
353	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
354	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 -	03/2014	0/0
355	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	04/2014	0/0
356	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
Total			15,462.28 -			0/0
Telecommunications						
357	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
358	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
359	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
360	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	02/2013	0/0
361	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	06/2013	0/0
362	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2013	0/0
363	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 -	06/2013	0/0
364	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	06/2013	0/0
365	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 -	09/2013	0/0
366	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
367	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
368	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
369	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
Total			5,699.24 -			0/0

Urban Development

Date of Commissioning

S.No Project		Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
370	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	09/2014	09/2014	0/0
			-	-		
371	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	03/2016	03/2016	0/0
			-	-		
372	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-	0/0
			173.08	-		
Total			37,850.18			0/0
			-			
Water Resources						
373	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	12/2007	12/2012	0/0
			-	-		
Total			542.90			0/0
			-			
Grand Total			343,496.18			0/0

List of ongoing projects having cost overrun w.r.to original

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	15,550.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	4,058.48	09/2010 -	-
	Total		16,663.00 -	22,947.00	19,608.48		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,463.38	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038]	08/2008	1,808.00 -	2,015.00	1,846.60	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	23,918.46		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,654.23	06/2009 -	01/2014
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	431.80	03/2013 -	07/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	123.40	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	4,909.54	4,128.29	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	205.78	03/2014 -	03/2016
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	95.10	03/2016 -	03/2016
	Total		8,579.45 -	37,918.25	31,576.29		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	6,229.56	04/2012 -	12/2013
	Total		5,460.61 -	46,838.25	37,805.85		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	637.21	03/2007 -	03/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.44	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	296.85	03/2006 -	06/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,204.63	08/2010 03/2012	12/2013
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,185.52	05/2010 -	05/2013
21	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	915.58	- -	-
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	03/2014
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	381.67	- -	03/2013
24	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	1,379.28	04/2013 -	04/2013
25	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	05/2013
26	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	1,158.35	03/2013 -	04/2014
27	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	211.00	04/2012 -	06/2013
Total			51,418.82 -	113,902.83	83,399.70		
Power							
28	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,877.58	09/2009 -	03/2018
29	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,842.00	04/2009 -	09/2014
30	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	6,201.82	09/2010 -	12/2017
31	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,686.98	03/2007 -	04/2013
32	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	8,052.00	12/2009 -	02/2017
33	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,310.02	09/2009 -	03/2014
34	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	871.93	12/2007 -	-

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	2,078.38	10/2010 -	03/2014
36	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,927.67	11/2009 -	05/2013
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,846.81	09/2008 -	03/2013
38	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	841.10	08/2010 -	06/2013
39	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	775.32	02/2011 -	01/2013
40	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	464.30	07/2010 -	11/2016
41	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	598.40	01/2010 -	04/2013
42	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	2,095.31	01/2016 -	11/2016
43	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	342.92	07/2014 -	05/2016
44	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,900.00	08/2012 -	03/2013
45	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	514.21	- -	07/2013
	Total		45,721.98 -	175,366.10	126,626.45		
Railways							
46	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	557.35	03/1994 -	10/2013
47	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
48	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	180.02	- 03/2010	-
49	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	599.81	- -	03/2012
50	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	550.45	06/1999 -	03/2011
51	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	9,001.45	03/2001 -	12/2017
52	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	248.71	- -	03/2015
53	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	215.16	03/2002 -	06/2013
54	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	121.47	12/2012 -	-
55	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012
56	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	246.40	03/2004 -	03/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	677.11	12/2011 12/2010	03/2013
58	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	226.28	- -	-
59	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	603.29	- -	01/2013
60	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	211.53	- -	03/2013
61	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
62	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	355.90	07/2012 -	-
63	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	288.23	03/2012 -	03/2013
64	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	762.61	- -	10/2012
65	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	641.37	02/2009 -	03/2012
66	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	71.68	- -	-
67	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	1,408.47	- -	03/2013
68	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.65	2,701.00	04/2008 12/2011	12/2015
69	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	181.84	- -	03/2012
70	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	177.33	03/2007 03/2007	03/2015
71	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	349.90	- -	12/2012
72	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.00	325.62	06/2004 -	12/2012
73	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.37	07/2008 -	07/2008
74	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,433.38	07/2005 -	-
75	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	369.27	05/2008 -	-
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	691.31	03/2012 -	-
77	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	946.07	12/2012 -	02/2013
78	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	369.21	12/2009 -	10/2013
79	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	741.20	12/2010 -	03/2015
80	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-
81	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	345.44	- 05/2009	05/2009

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
82	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	381.17 -	863.23	626.57	- -	03/2012
83	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]	04/1999	323.40 -	750.89	504.57	- -	03/2014
84	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	04/1997	78.23 -	162.87	107.58	- -	-
85	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 408.76	847.75	835.94	06/2007 -	06/2007
86	RENIGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 -	370.00	344.44	04/2003 03/2010	-
87	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	536.30	- -	-
88	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 -	1,029.00	792.25	- -	03/2013
89	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,045.20	9.41	- -	-
90	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	1,655.81	1,344.95	12/2008 -	03/2015
91	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268]	03/2000	907.69 -	3,176.10	3,374.48	12/2006 -	08/2010
92	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	278.33	02/2011 -	03/2013
93	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 -	1,188.91	602.44	- 12/2009	02/2012
94	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 240.59	607.09	484.04	12/2012 12/2012	02/2013
95	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	0.35	- -	-
96	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,423.98	472.01	03/2005 12/2008	12/2016
97	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 -	697.45	434.76	03/2012 -	12/2012
98	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38 -	1,995.25	239.15	- -	03/2014
99	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 -	1,185.64	224.33	- 09/2009	-
100	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	259.32	02/2009 02/2009	08/2014
101	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	4,444.00	1,295.18	03/2011 -	03/2017
102	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	185.78	- -	-
103	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	341.41	285.99	03/2012 -	03/2013
104	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	768.87	460.04	- -	03/2010
105	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	960.22	03/2009 -	12/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
106	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,696.36	10/2007 -	12/2015
107	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	94.20	- -	-
108	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	227.53	- -	-
109	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	2,232.50	1,703.60	- -	03/2014
110	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	208.66	12/2008 -	09/2014
111	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	334.15	- 03/2009	-
112	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	175.76	03/1998 08/2005	08/2005
113	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
114	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	78.15	02/2015 -	02/2015
115	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	222.32	03/2009 03/2009	08/2014
116	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	121.87	- -	-
117	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	243.81	12/2007 03/2010	-
118	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	419.20	03/2012 -	03/2013
119	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N220000027	04/2005	240.00 -	355.00	378.12	03/2009 12/2009	-
120	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.60	0.76	- -	-
121	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	116.77	02/2006 -	06/2014
122	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	445.88	03/2008 06/2008	-
123	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N220000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
124	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N220000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
125	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	230.30	03/2010 -	-
126	PANSPURA-KHARAGPUR 3D LINE - [N220000076	09/2007	252.50 -	529.23	249.38	02/2010 -	12/2015
127	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N220000079	09/2007	404.19 -	900.00	295.40	- -	-
128	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N220000080	09/2006	343.17 -	900.00	592.35	- -	12/2012

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
129	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	435.87	396.76	03/2011 -	03/2011
130	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	406.40	318.86	- -	06/2013
131	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	40.72	- -	-
132	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	145.76	- -	-
133	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	200.00 -	385.20	130.40	- -	03/2015
134	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	40.88	- -	-
135	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	819.40	188.04	03/2010 -	03/2017
136	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	224.41	12/2010 -	03/2011
137	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	224.89	141.55	03/2012 -	12/2013
138	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	439.39	06/2005 -	06/2016
139	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	456.83	03/2014 -	12/2015
140	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.49	42.44	04/2014 -	03/2017
141	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
142	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017
143	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	440.63	03/2013 -	03/2014
144	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]	04/2010	2,069.60 -	2,298.42	49.50	03/2014 -	03/2016
145	Jaipur - Ringus - Churu and Sikar - Loharu Gauge Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	230.27	03/2014 -	03/2014
146	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	95.48	12/2011 -	02/2012
147	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	124.23	12/2011 -	11/2013
148	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	138.09	12/2010 -	12/2010
149	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	404.39	15.76	03/2013 -	03/2013
150	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	468.62	1.57	03/2012 -	-
151	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95	195.19	03/2011 -	-

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127]	04/1996	1,676.31 -	4,255.37	3,425.69	03/2009 -	03/2015
	Total		39,439.22 -	302,022.61	185,333.06		
Road Transport & Highways							
153	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	161.44	04/2004 -	04/2013
154	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 [240106221]	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2013
155	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	165.13	03/2008 -	03/2013
156	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	272.75	05/2008 -	09/2013
157	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014
158	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014
159	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014
160	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	131.26	07/2009 -	05/2014
161	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
162	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	214.69	09/2007 -	03/2014
163	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	08/2013
	Total		3,324.28 -	307,467.81	190,324.72		
Shipping & Ports							
164	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003]	10/2005	800.00 -	1,571.60	5.75	10/2008 -	10/2008
165	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
166	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	1,460.00	937.28	12/2010 -	04/2014
167	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 -	06/2013
168	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
169	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
170	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00	4,150.00	3,661.95	01/2012	04/2013
171	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46	994.82	306.12	02/2014	02/2014
172	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67	373.22	371.18	04/2009	02/2011
Total			8,628.97	318,686.31	195,966.73		
Steel							
173	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00	12,291.00	10,235.67	10/2009	06/2013
174	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89	607.17	349.17	12/2011 06/2010	06/2013
175	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	216.68	137.65	10/2012	06/2013
176	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	16,408.00	14,480.55	12/2011	12/2013
177	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	230.00	343.58	254.92	02/2011	04/2013
178	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	350.00	252.34	08/2010	04/2013
Total			24,028.89	348,902.74	221,677.03		
Telecommunications							
179	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15	158.72	80.05	06/2009	06/2013
180	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]	03/2008	328.13	392.13	164.58	03/2009	01/2013
Total			477.28	349,453.59	221,921.66		
Urban Development							
181	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	11,609.00	2,482.18	06/2011	03/2013
182	C/o office building for IDBI at bandra Kurla Complex, Mumbai - [N28000048]	11/2006	114.18 173.08	173.08	-	04/2009	-
Total			6,509.18	361,235.67	224,403.84		
Water Resources							
183	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		542.90	362,422.67	224,439.33		
			-				
	Grand Total		214,545.09	2,774,450.83	1,787,001.60		

List of ongoing projects having time and cost overrun w.r.to original

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	17,270.00	15,550.00	12/2008 -	03/2013
	Total		13,171.00 -	17,270.00	15,550.00		
	<u>Civil Aviation</u>						
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037	08/2008	1,942.51 -	2,325.00	2,463.38	05/2011 -	03/2013
	Total		1,942.51 -	19,595.00	18,013.38		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,654.23	06/2009 -	01/2014
4	MAGADH OC 20 MTY (CCL) - [N06000015	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	977.53	431.80	03/2013 -	07/2014
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047	05/2008	4,904.54 -	4,909.54	4,128.29	03/2012 -	03/2014
7	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	205.78	03/2014 -	03/2016
	Total		7,938.86 -	29,537.56	25,452.71		
	<u>Petrochemicals</u>						
8	Assam gas Cracker project - [N16000106	04/2006	5,460.61 -	8,920.00	6,229.56	04/2012 -	12/2013
	Total		5,460.61 -	38,457.56	31,682.27		
	<u>Petroleum</u>						
9	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	637.21	03/2007 -	03/2014
10	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.44	03/2007 -	03/2017
11	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	296.85	03/2006 -	06/2013
12	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
13	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,204.63	08/2010 03/2012	12/2013
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,185.52	05/2010 -	05/2013
17	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	20,426.00	11/2012 -	03/2014
18	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	677.99	03/2011 -	05/2013
19	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	1,158.35	03/2013 -	04/2014
20	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	211.00	04/2012 -	06/2013
	Total		49,613.82 -	102,403.14	74,599.59		
Power							
21	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,877.58	09/2009 -	03/2018
22	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,358.91	4,842.00	04/2009 -	09/2014
23	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	6,201.82	09/2010 -	12/2017
24	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,686.98	03/2007 -	04/2013
25	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	8,052.00	12/2009 -	02/2017
26	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,310.02	09/2009 -	03/2014
27	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	2,078.38	10/2010 -	03/2014
28	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,927.67	11/2009 -	05/2013
29	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,846.81	09/2008 -	03/2013
30	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	841.10	08/2010 -	06/2013
31	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	464.30	07/2010 -	11/2016
32	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	598.40	01/2010 -	04/2013
33	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	2,095.31	01/2016 -	11/2016
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	342.92	07/2014 -	05/2016
35	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,900.00	08/2012 -	03/2013

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		44,083.26	161,322.81	115,664.88		
	Railways						
36	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	557.35	03/1994	10/2013
37	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995	03/2013
38	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	9,001.45	03/2001	12/2017
39	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	215.16	03/2002	06/2013
40	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	246.40	03/2004	03/2014
41	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	677.11	12/2011 12/2010	03/2013
42	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	288.23	03/2012	03/2013
43	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.65	2,701.00	04/2008 12/2011	12/2015
44	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	177.33	03/2007 03/2007	03/2015
45	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	369.21	12/2009	10/2013
46	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	741.20	12/2010	03/2015
47	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,344.95	12/2008	03/2015
48	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	278.33	02/2011	03/2013
49	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	472.01	03/2005 12/2008	12/2016
50	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	259.32	02/2009 02/2009	08/2014
51	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	1,295.18	03/2011	03/2017
52	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	285.99	03/2012	03/2013
53	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	960.22	03/2009	12/2014
54	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,696.36	10/2007	12/2015
55	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	208.66	12/2008	09/2014
56	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	222.32	03/2009 03/2009	08/2014
57	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	419.20	03/2012	03/2013
58	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	116.77	02/2006	06/2014

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
59	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 -	529.23	249.38	02/2010 -	12/2015
60	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	819.40	188.04	03/2010 -	03/2017
61	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR & G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	224.89	141.55	03/2012 -	12/2013
62	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	439.39	06/2005 -	06/2016
63	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	456.83	03/2014 -	12/2015
64	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.49	42.44	04/2014 -	03/2017
65	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	59.74	12/2015 -	03/2017
66	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	440.63	03/2013 -	03/2014
67	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]	04/2010	2,069.60 -	2,298.42	49.50	03/2014 -	03/2016
68	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	124.23	12/2011 -	11/2013
69	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	4,255.37	3,425.69	03/2009 -	03/2015
Total			17,757.78 -	224,698.18	144,371.32		
Road Transport & Highways							
70	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	161.44	04/2004 -	04/2013
71	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	142.58	09/2008 -	03/2013
72	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27 -	193.10	165.13	03/2008 -	03/2013
73	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	272.75	05/2008 -	09/2013
74	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014
75	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	114.81	11/2008 -	06/2014
76	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014
77	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	131.26	07/2009 -	05/2014
78	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
79	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	214.69	09/2007 -	03/2014
80	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,465.90	11/2011 -	08/2013

(Mar,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		3,324.28	230,143.38	149,362.98		
			-				
	Shipping & Ports						
81	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00	1,460.00	937.28	12/2010	04/2014
			-			-	
82	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00	600.00	139.80	03/2006	06/2013
			-			-	
83	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00	755.50	219.00	03/2011	03/2013
			-			-	
84	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00	4,150.00	3,661.95	01/2012	04/2013
			-			-	
	Total		5,580.00	237,108.88	154,321.01		
			-				
	Steel						
85	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00	12,291.00	10,235.67	10/2009	06/2013
			-			-	
86	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89	607.17	349.17	12/2011 06/2010	06/2013
			-				
87	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	216.68	137.65	10/2012	06/2013
			-			-	
88	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	16,408.00	14,480.55	12/2011	12/2013
			-			-	
89	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	230.00	343.58	254.92	02/2011	04/2013
			-			-	
90	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	350.00	252.34	08/2010	04/2013
			-			-	
	Total		24,028.89	267,325.31	180,031.31		
			-				
	Telecommunications						
91	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15	158.72	80.05	06/2009	06/2013
			-			-	
	Total		149.15	267,484.03	180,111.36		
			-				
	Urban Development						
92	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	11,609.00	2,482.18	06/2011	03/2013
			-			-	
	Total		6,395.00	279,093.03	182,593.54		
			-				
	Grand Total		179,445.16	1,874,438.88	1,271,754.35		
