

**307th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
May, 2011**



Construction activity (Shipping Corporation of India)



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for May 2011 (the 307th Flash Report) contains information on the status of the 567 projects in the Central Sector costing ` ₹ . 150 Crores and above. During May 2011, fifteen projects have reported completion (which has now been dropped from the monitor of this Ministry).

The online submission of the implementation Status Report of the ongoing projects from the project authorities has improved considerably with majority of project authorities (except NHAI) are reporting online during the current month due to the continuous effort/persuasion by this Ministry. During May 2011, fifty two (52) projects have reported additional delays compared to the completion dates in the previous month. The additional delays are in the range of 1 to 24 months, in respect of projects relating to Coal, Steel, Petroleum, Power, Railways, Road Transport and Highways, Shipping & Ports and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	136	4
2.	ROAD TRANSPORT & HIGHWAYS	128	13
3.	POWER	85	19
4.	PETROLEUM	74	8
5.	COAL	45	2
6.	TELECOMMUNICATION	41	0
7.	SHIPPING & PORTS	23	1
8.	STEEL	15	4
9.	FERTILISERS	6	0
10.	CIVIL AVIATION	5	0
11.	ATOMIC ENERGY	4	1
12.	URBAN DEVELOPMENT	3	0
13.	MINES	1	0
14.	WATER RESOURCES	1	0
Total		567	52

3. The total original cost of implementation of the 567 projects was about ₹ 6,32,243.96 Crores and their anticipated completion cost is likely to be ₹ 7,58,171.90 Crores, which reflects an overall cost overrun of 19.90%. The expenditure incurred on these projects till May, 2011 is ₹ 3,32,247.24 Crores.

4. Out of the 567 projects, 7 projects are ahead of schedule, 145 are on schedule, 244 projects are delayed and 113 projects have been sanctioned without any commissioning schedule/date. Further, in case of 58 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently the date of completion have been finalized. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month, the projects reporting delays have marginally decreased to 244 from 251 in April'2011. The overall cost overrun has also decreased to 19.90% from 20.60% in April 2011. Out of 244 delayed projects, at the end of May, 2011, 49 projects had overall delay in the range of 1 to 12 months, 59 projects had delay in the range of 13 to 24 months, 103 projects had delay in the range of 25 to 60 months and 33 projects had delay of 61 months and above.

The Sector-wise details of delays are as under:-

i) In the **Coal sector**, 2 projects have reported additional delays of 2 months each. Barsingsar TPS, NLC has reported additional delay of two months due to delay in commissioning. Tuticorin Thermal Power Project, NLC has reported additional delay of two months (overall delay of 2 months) due to inadequate mobilization by the contractor.

ii) In the **Steel sector**, 4 projects have reported additional delays in the range of 2-5 months. 700TPD ARI Separation Unit-4 at Oxygen Plant-II Bhilai, SAIL, 67.5 MW TG-5 Auxiliary System Emergency Power Requirement project, RINL and 330 TPH Boiler-6 and Auxiliary System RINL have reported an additional delay of Two months each due to termination of contract, as the contractor demanded changes in terms and conditions, delay in supply of fireclay & silica brick by the contractor and increased cost of labour charges respectively. Bailadila Iron Ore Deposit- IIB, NMDC has reported an additional delay of 5 months due to Maoist problem.

iii) In the **Petroleum Sector**, 8 projects have reported additional delays in the range of 1-15 months. Diesel Hydrotreater Project at Visakh Refinery, HPCL has reported additional delay of 6 months due to delay in environment & forest clearance, which is still awaited. Hydrocracker Revamp Setting up a New CCR at Mumbai BPCL has reported additional delay

of 15 months as the project has been reformulated with enhanced capacity of CCR i.e. from 0.9 MMTPA to 1.2 MMTPA with matching new NHI and New Psa Unit. North Tapti Gas Field Development ONGC, Heera Reconstruction ONGC, Neelam Reconstruction ONGC, Construction of 23 Immediate Supply Vessels (ISV) ONGC, MNW-NF Bridge Project ONGC and Integrated Development of G1 and GS-15, ONGCL have reported an additional delay of one month, 2 months, 2 months, 5 months, 9 months and 12 months respectively, However no specific reason has been reported by the Project authorities.

iv) In the **Power Sector**, 19 projects have reported additional delays in the range of 1-22 months. URI H.E.P. Stage –II, NHPC has reported an additional delay of one month due to delay in overtopping of coffer dam affected entire HM work. Transmission System Associated with Barh. Gener Project PGCIL, North-East North Western Interconnector I Project PGCIL and Transmission System Associated with Rampur HEP PGCIL have reported an additional delay of 2 months, 13 months and 22 months respectively due to delay in associated generation projects. Transmission System Associated with URI-II PGCIL has reported an additional delay of 2 months due to law & order problem. Eastern Region Strengthening Scheme-II PGCIL and Eastern Region Strengthening Scheme-I PGCIL have reported an additional delay of 3 months and 9 months respectively due to severe ROW problems in West Bengal and Jharkhand. Tapovan Vishnugad Hydro Electric Project (HEP), NTPC has reported an additional delay of 4 months due to termination of contract in barrage & desilting chamber package, fait stopped due to rock fall. Subansiri Lower Hydro Electric Project NHPC has reported an additional delay of 8 months due to non-signing of MOA by Assam GAIL and stoppage of dam works by anti-dam activities. 765 KV System for Central Part of Northern Grid PAR PGCIL, Northern Region System Strengthening Scheme-XV PGCIL, Northern Region System Strengthening Scheme-XIX PGCIL, 765 KV System for Central Part of Northern Grid PA PGCIL and Northern Region System Strengthening Scheme-XVIII PGCIL have reported an additional delay of 10 months, 13 months, 13 months, 13 months and 16 months respectively due to delay in land acquisition. System Strengthening-X of SR PGCIL, Transmission System Associated with Krishnapatnam PGCIL, Western Region Strengthening Scheme-IX PGCIL, Transmission System Associated with Chamera-III HEP PGCIL and Tehri Pumped Storage Plant THDCL have reported an additional delay of one month, 3 months, 4 months, 5 months and 10 months respectively, However no specific reason has been reported by the project authorities.

v) In the **Road Transport and Highways Sector**, 13 projects have reported additional delay in the range of 1-8 months. 7 projects have reported additional delay of one month each due to slow progress of work by the contractor. Madurai-Arupkottai-Tuticorin, KM 138.8 to

KM 264.5, NH-45 B NHAI has reported additional delay of 3 months due to delay in land acquisition. Kota Bypass, RJ-4, NH-76, NHAI has reported additional delay of 6 months due to delay in land acquisition and removal of encroachment. Delhi/Haryana Border to Rohtak NHAI has reported additional delay of 6 months due to poor mobilization & slow progress by the contractor. Kasia to Gorakhpur NHAI has reported additional delay of 7 months due to delay in cutting of trees by forest department and delay in construction of underpass in urban areas. Zirakpur (Haryana) – Parwanoo (Himachal Pradesh) NHAI has reported an additional delay of 7 months due to change in alignment in the hilly portion. Mehsi to Kotwa (LMNHP-II), PH.II KM 480 to KM 440 NH-28 NHAI has reported an additional delay of 8 months due to slow mobilization of contractor & delay in land acquisition, shifting of utilities etc.

vi) In the **Railway Sector**, 4 projects have reported additional delay in the range of 3-24 months. Ghutiarisharif- Canning ER has reported an additional delay of 21 months due to encroachment. Tamluk Digha, Line Doubling, SER has reported an additional delay of 8 months as the land acquisition process is very slow and land owners are accepting the award at very slow pace. New Work for Construction of Metro railway from No RVNL and New Work for Construction of Metro railway from Ba RVNL have reported an additional delay of 3 months and 24 month respectively, however no specific reason has been reported by the project authority.

vii) In the **Atomic Energy Sector**, Kudankulam APP, NPCIL has an additional delay of 2 months due to slippage of commitments by Atom Slttoy Export (ASE), Russia.

viii) In the **Shipping & Ports Sector**, Acquisition of 4 No. of Anchor Handling Cum Supply Shipp. has reported an additional delay of 5 months due to revised production schedule by yard..

The status as on 01.05.2011 in respect of completion of projects costing ` 150 Crores and above in different sectors during 2011-12 is indicated in the Report.

(Pankaj Jain)

Additional Secretary

Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Railways	136	4
2	Road Transport & Highways	128	13
3	Power	85	19
4	Petroleum	74	8
5	Coal	45	2
6	Telecommunications	41	0
7	Shipping & Ports	23	1
8	Steel	15	4
9	Fertilisers	6	0
10	Civil Aviation	5	0
11	Atomic Energy	4	1
12	Urban Development	3	0
13	Mines	1	0
14	Water Resources	1	0
	Total	567	52

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
Road Transport & Highways				
13	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during

2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
	May,2011			
	<u>Civil Aviation</u>			
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97


Summary of projects in the Flash Report for the month of May, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	569
Number of Projects completed/dropped/frozen in Previous Month	9
Number of Projects completed/dropped/frozen in Current Month	11
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	3
Number of Projects Added in Current Month	15
Number of Projects in Current Month	567

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 567 projects, 7 projects are ahead of schedule, 145 projects are on schedule and 244 projects are delayed. Of the balance, 113 projects do not have fixed dates of commissioning while 58 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

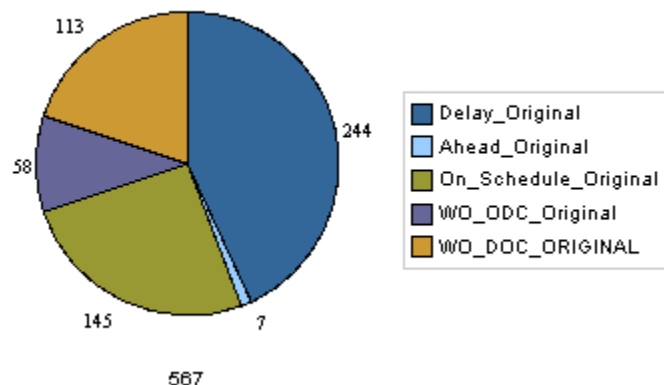

III. Investment Scenario

The Total Original cost of implementation of 567 projects when sanctioned, was of the order of Rs. 632243.96 crore but this was subsequently revised to Rs. 758171.9 crore implying a cost overrun of 19.9%. The expenditure incurred on these projects till May, 2011 is Rs. 332247.24 crore, which is 43.8% of the revised cost of the projects.

Figures are in Rs. Crore

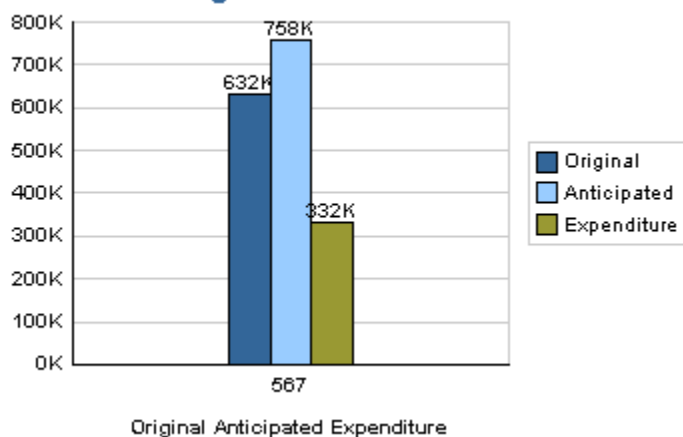

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	569
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	11
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	3
No of Projects added in Current Month	15
No of Projects in Current Month	567

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	244	7	145	58	113	567	43.03
Latest Approved (Date)	270	9	184	37	67	567	47.62

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	455	489,308.60	538,219.86	212,761.82	39.50	48,911.26	10.00
Latest Approved (RCE)	112	195,488.37	219,952.04	119,485.42	54.30	24,463.67	12.50
Total (RCE)	567	684,796.97	758,171.90	332,247.24	43.82	73374.93	10.71
Original Cost of All Projects							
Original Cost	567	632,243.96	758,171.90	332,247.24	43.80	125,927.94	19.90

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	244	269,534.24	339,961.73	197,078.41	58.00	70,427.49	26.10
Latest Approved (RCE)	270	284,389.05	336,761.57	193,393.45	57.40	52,372.52	18.40

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	52	71,063.60	78,525.52	44,381.86	56.50	7,461.92	10.50

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	4,123.2	4,078.1	-1.1	0	0.0	0.0	0.0
3	Coal	45	25,504.2	28,789.6	12.9	10	12,935.0	16,916.0	30.8
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	15	41,398.4	68,476.4	65.4	11	39,254.2	66,332.2	69.0
7	Petroleum	74	165,845.8	174,838.2	5.4	18	27,786.3	46,364.0	66.9
8	Power	85	178,267.7	183,786.7	3.1	11	17,404.2	23,396.8	34.4
9	Railways	136	66,442.6	122,507.3	84.4	101	36,325.6	92,490.5	154.6
10	Road Transport & Highways	128	61,806.6	63,270.0	2.4	11	3,482.9	5,515.4	58.4
11	Shipping & Ports	23	14,464.2	15,317.7	5.9	6	3,346.8	4,401.4	31.5
12	Telecommunications	41	20,026.0	21,450.8	7.1	9	3,362.9	4,870.4	44.8
13	Urban Development	3	15,185.2	30,684.7	102.1	3	15,185.2	30,684.7	102.1
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		567	632,244.0	758,171.9	19.9	184	180,380.5	318,061.0	76.3

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	3	28,122.0	32,960.0	11 - 41
2	Civil Aviation	5	4,123.2	4,078.1	-1.1	3	3,524.9	3,479.8	3 - 17
3	Coal	45	25,504.2	28,789.6	12.9	20	12,840.4	15,670.0	3 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	1	1,478.6	1,478.6	1 - 1
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	29 - 29
6	Steel	15	41,398.4	68,476.4	65.4	4	15,498.7	24,776.7	17 - 29
7	Petroleum	74	165,845.8	174,838.2	5.4	32	45,415.1	55,853.2	2 - 120
8	Power	85	178,267.7	183,786.7	3.1	43	84,047.0	88,727.4	4 - 90
9	Railways	136	66,442.6	122,507.3	84.4	25	21,841.0	42,286.8	2 - 213
10	Road Transport & Highways	128	61,806.6	63,270.0	2.4	94	31,110.7	31,754.1	1 - 90
11	Shipping & Ports	23	14,464.2	15,317.7	5.9	13	5,454.5	6,406.5	5 - 72
12	Telecommunications	41	20,026.0	21,450.8	7.1	2	496.0	476.4	54 - 54
13	Urban Development	3	15,185.2	30,684.7	102.1	2	15,071.0	30,503.4	12 - 15
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		567	632,244.0	758,171.9	19.9	244	269,534.2	339,961.7	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	2	16,663.00	21,501.00	16- 41
2	Civil Aviation	5	4,123.24	4,078.13	-1.09	0	0.00	0.00	0- 0
3	Coal	45	25,504.15	28,789.58	12.88	7	6,813.24	10,338.47	3- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	29- 29
6	Steel	15	41,398.40	68,476.43	65.41	2	14,825.00	24,103.00	25- 29
7	Petroleum	74	165,845.81	174,838.18	5.42	16	24,407.98	40,740.80	3- 120
8	Power	85	178,267.70	183,786.71	3.10	9	11,348.50	16,437.94	18- 90
9	Railways	136	66,442.61	122,507.27	84.38	18	9,818.02	30,612.46	12- 213
10	Road Transport & Highways	128	61,806.58	63,269.99	2.37	10	2,374.90	3,227.40	19- 90
11	Shipping & Ports	23	14,464.19	15,317.65	5.90	6	3,346.84	4,401.36	6- 72
12	Telecommunications	41	20,025.99	21,450.84	7.12	7	2,274.59	3,165.48	17- 58
13	Urban Development	3	15,185.18	30,684.66	102.07	3	15,185.18	30,684.66	12- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		567	632243.96	758171.9	19.92	82	111691.66	190801.33	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP	12/2005	358.42	12/2008	358.42	12/2012	5.49
<u>Railways</u>						
DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)	02/1999	180.73	12/2006	358.00	N.A.	352.32
HAPUR-KANKATHER (LD),NR	04/2003	106.64	03/2007	166.61	N.A.	147.32
<u>Road Transport & Highways</u>						
GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500	03/2005	579.00	04/2009	579.00	05/2011	765.90
NAGAON BYPASS (NH-37)(NHAI)	12/2003	230.00	06/2008	230.00	05/2011	312.00
<u>Power</u>						
LOHARINAG-PAL HEP(4X150MW)	06/2006	2,895.10	11/2011	2,895.10	12/2012	693.00
TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.	04/2008	290.49	04/2010	299.08	05/2011	346.80
<u>Railways</u>						
SHIMOGA-TALAGUPPA (SWR), GC	12/1992	46.00	N.A.	218.00	N.A.	244.16
<u>Road Transport & Highways</u>						
KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70	11/2008	549.00	05/2010	549.00	05/2011	815.00
<u>Civil Aviation</u>						
D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA	01/2008	535.00	06/2010	535.00	N.A.	143.97
CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3	06/2009	213.35	09/2010	213.35	N.A.	60.89

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Road Transport & Highways</u>					
SIX LANNING OF VADAKKANCHERRY THRISSURESECTION	2/2010	617.00	8/2012	617.00	8/2012
4 LANING OF NAGPUR-BETUL	2/2011	2,498.76	8/2014	2,498.76	8/2014
4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING	3/2011	359.00	9/2013	359.00	9/2013
MURADABAD-BAREILY	4/2010	1,267.00	6/2013	1,267.00	6/2013
CHITRADURGA-TUMKUR(NH-4)	3/2011	839.00	8/2013	839.00	8/2013
<u>Petroleum</u>					
SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION	5/2011	616.00	3/2012	616.00	3/2012
<u>Road Transport & Highways</u>					
DEVIHALLI-HASSAN	12/2010	453.00	5/2013	453.00	5/2013
PANIPAT-ROHTAK	4/2011	807.00	10/2014	807.00	10/2014
UGRADATION OF HYDERABAD-BANGALORE SECTION	11/2010	680.00	11/2012	680.00	11/2012
<u>Steel</u>					
7.0 MTPA KUMARASWAMY IRON ORE MINE	2/2011	898.55	5/2013	898.55	5/2013
<u>Road Transport & Highways</u>					
BELGAUM-DHARWAD(NH-4)	12/2010	480.00	6/2013	480.00	6/2013
WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM)	2/2011	193.45	11/2012	193.45	11/2012
INDORE-DEWAS(NH-3)	11/2010	325.00	5/2013	325.00	5/2013
PUNE-SATARA(NH-4)	10/2010	1,724.55	3/2013	1,724.55	3/2013
<u>Steel</u>					
1.2 MTPA PELLET PLANT DONIMALAI	4/2011	572.00	4/2013	572.00	4/2013

VII. Milestones (Cumulative due & achieved)

Total	2190
Achieved up to month	864


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	03/2012	05/2012	2
<u>Coal</u>						
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	06/2011	08/2011	2
TUTICORIN THERMAL POWER PROJECT NLC	4,904.54	4,909.54	N.A.	08/2012	10/2012	2
<u>Steel</u>						
700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT- II, BHILLAI SAIL	111.28	232.93	N.A.	05/2011	07/2011	2
67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	08/2011	10/2011	2
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	07/2011	09/2011	2
Bailadila Iron Ore Deposit- IIB(NMDC) NMDC	295.89	607.17	N.A.	10/2011	03/2012	5
<u>Petroleum</u>						
North Tapti Gas Field Development ONGC	589.70	755.76	03/2011	05/2011	06/2011	1
HEERA RECONSTRUCTION ONGC	706.70	706.70	04/2010	04/2011	06/2011	2
NEELAM RECONSTRUCTION ONGC	305.08	305.08	04/2011	04/2011	06/2011	2
Construction of 23 Immediate Supply Vessels (ISV) ONGC	331.20	331.20	08/2013	03/2013	08/2013	5
DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY HPCL	3,597.00	2,730.00	09/2011	09/2011	03/2012	6
MNW-NF BRIDGE PROJECT ONGC	175.21	162.12	03/2009	05/2011	02/2012	9
INTEGRATED DEV OF G1 and GS-15 (ONGCL) ONGC	429.82	2,218.01	04/2006	05/2011	05/2012	12
HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB BPCL	825.00	1,827.00	N.A.	01/2012	04/2013	15
<u>Power</u>						
URI H.E.P STAGE -II (NHPC) NHPC	1,724.79	1,724.79	11/2009	11/2011	12/2011	1


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
System Strengthening -X of SR PGCIL	276.61	276.61	04/2012	03/2012	04/2012	1
TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) PGCIL	3,779.46	3,725.13	09/2009	10/2011	12/2011	2
TRANSMISSION SYSTEM ASSOCIATED WITH URI-II PGCIL	238.25	227.03	05/2011	07/2011	09/2011	2
EASTERN REGION STRENGTHENING SCHEME-II PGCIL	227.52	227.52	06/2010	06/2011	09/2011	3
TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM PGCIL	779.21	779.21	08/2013	05/2013	08/2013	3
TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	N.A.	02/2014	06/2014	4
WESTERN REGION STRENGTHENING SCHEME-IX PGCIL	230.89	230.89	01/2011	06/2011	10/2011	4
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.37	07/2011	07/2011	12/2011	5
SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	6,285.33	09/2010	12/2013	08/2014	8
EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	894.26	10/2009	06/2011	03/2012	9
TEHRI PUMPED STORAGE PLANT(1000MW) THDCL	1,657.00	2,978.86	07/2010	03/2015	01/2016	10
765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR PGCIL	1,075.12	1,075.12	05/2012	05/2012	03/2013	10
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV PGCIL	520.48	520.48	11/2011	02/2012	03/2013	13
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX PGCIL	410.29	410.29	02/2012	02/2012	03/2013	13
NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT PGCIL	11,130.19	11,130.19	08/2013	08/2013	09/2014	13
765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	02/2012	03/2013	13
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII PGCIL	509.66	509.66	11/2011	11/2011	03/2013	16


Trend and Graphical Analysis of All Projects

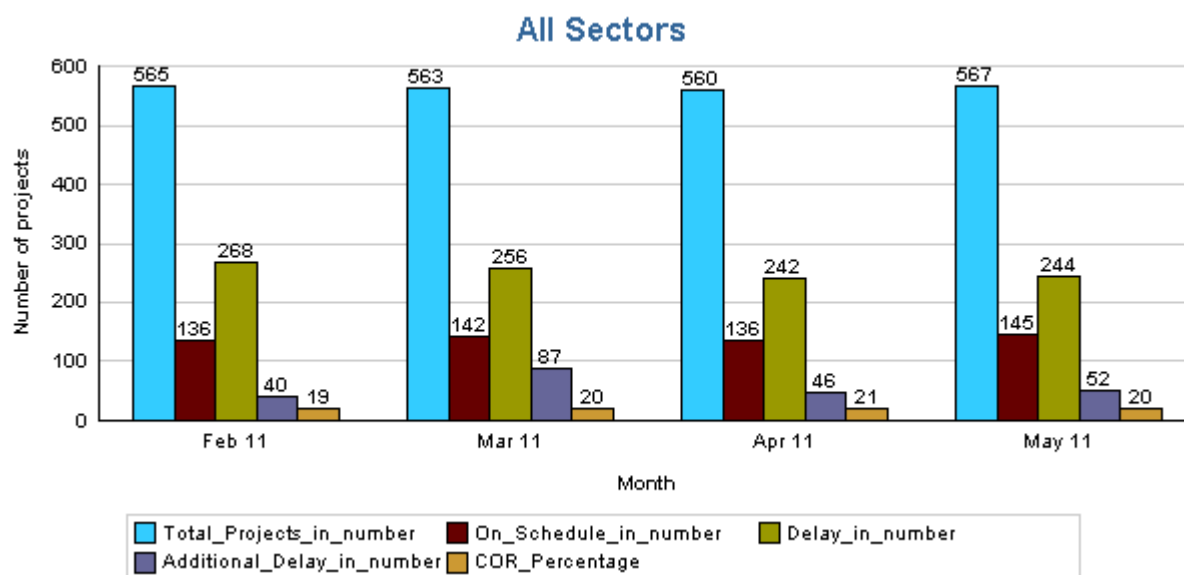


All Sectors Break-up of 244 Delayed projects in May 2011

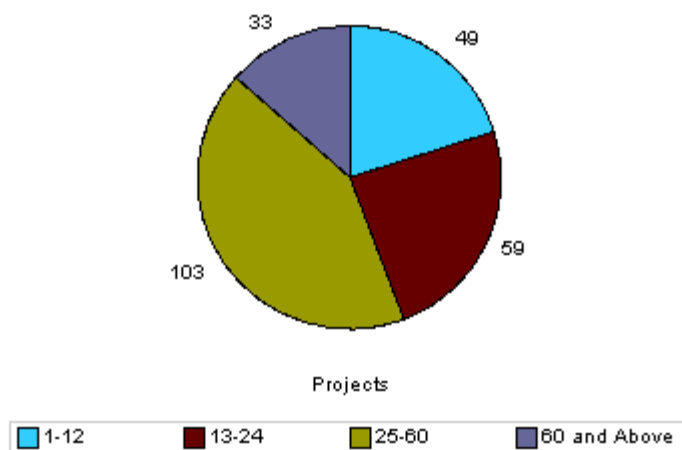


Trend and Graphical Analysis Telecommunications Sector

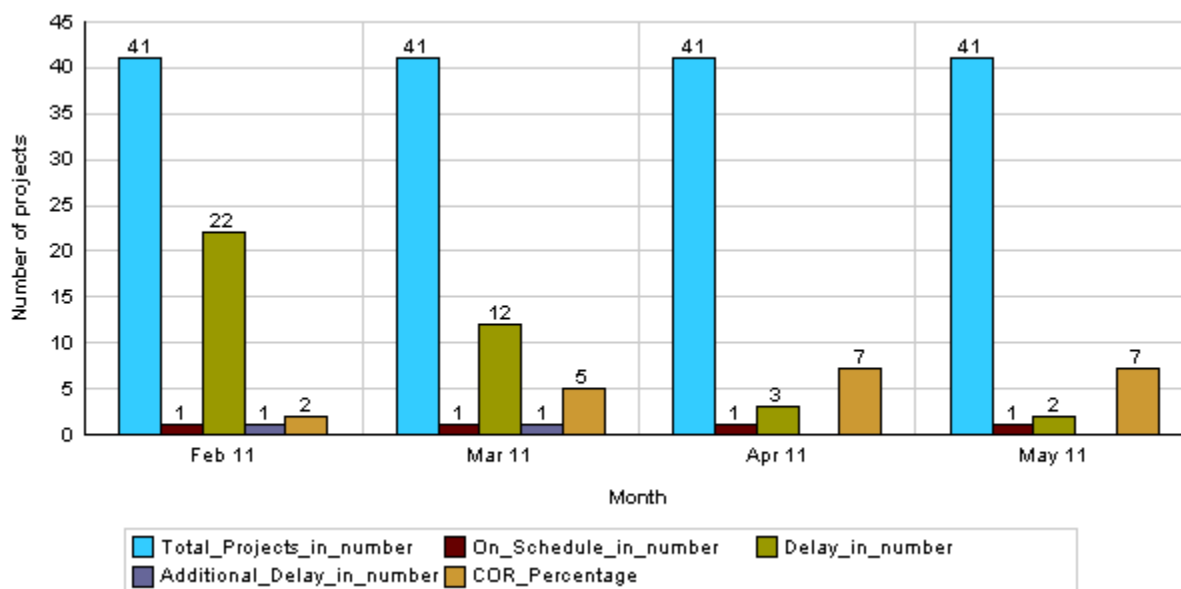


Telecommunications Sector Sector Break-up of 2 Delayed projects in May 2011

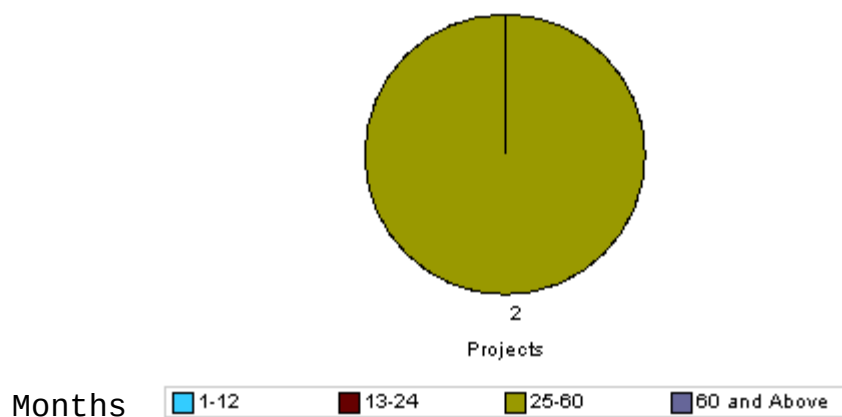


Trend and Graphical Analysis Shipping and Ports Sector

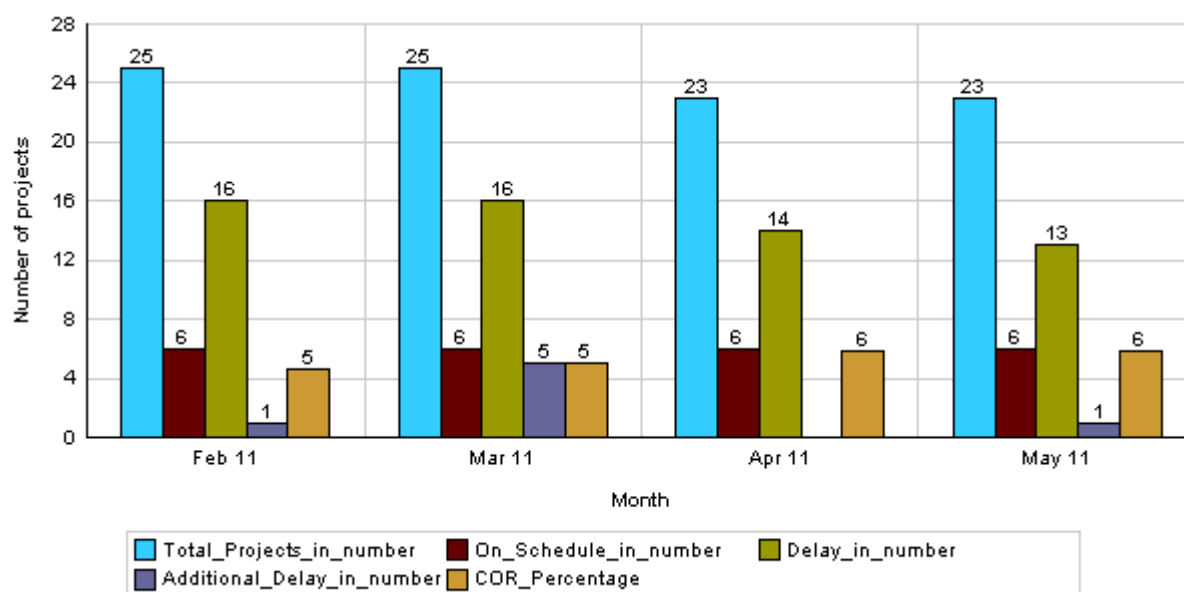


Sector Break-up of 13 Delayed projects in May 2011

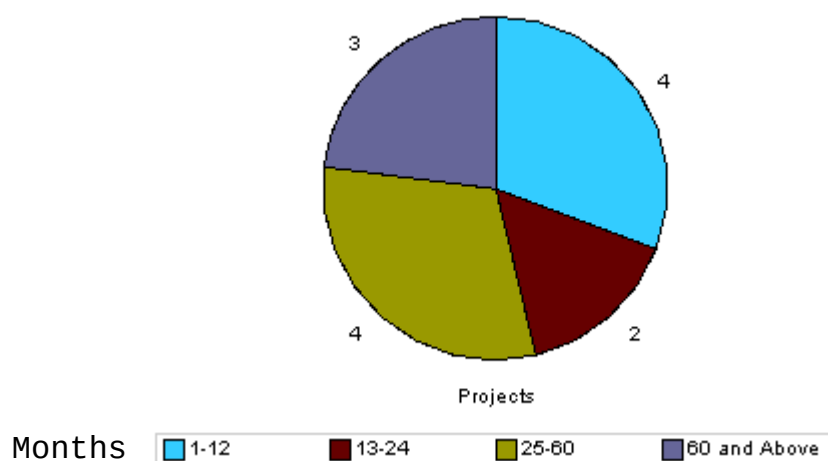

Trend and Graphical Analysis Road Transport and Highways Sector

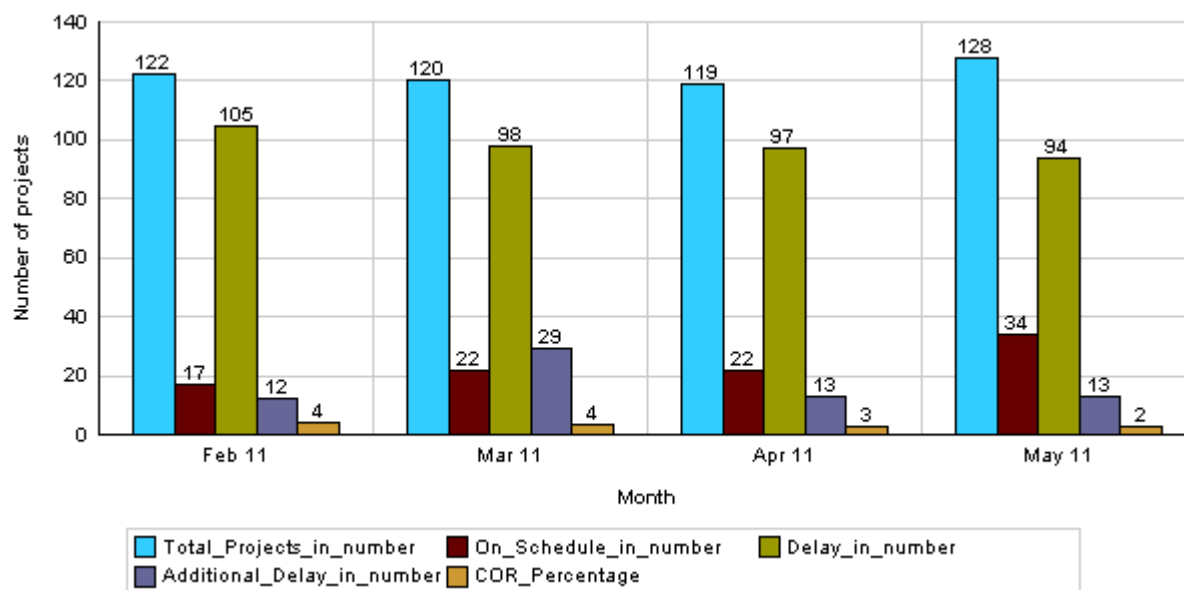


Sector Break-up of 94 Delayed projects in May 2011

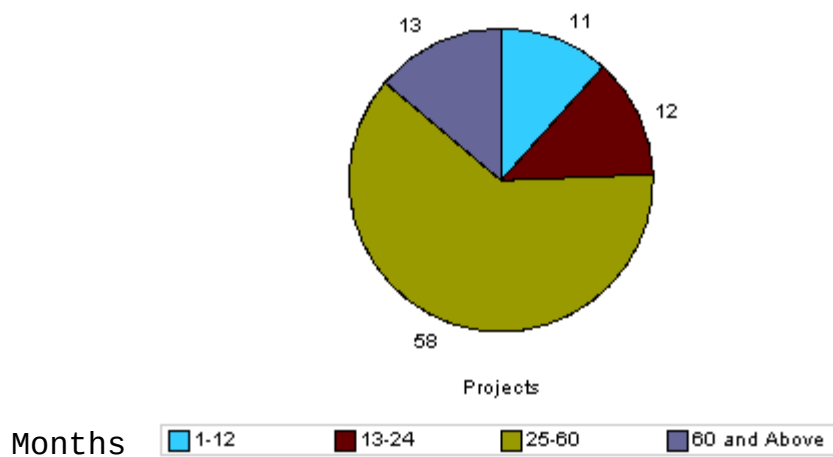


Trend and Graphical Analysis

Railways Sector

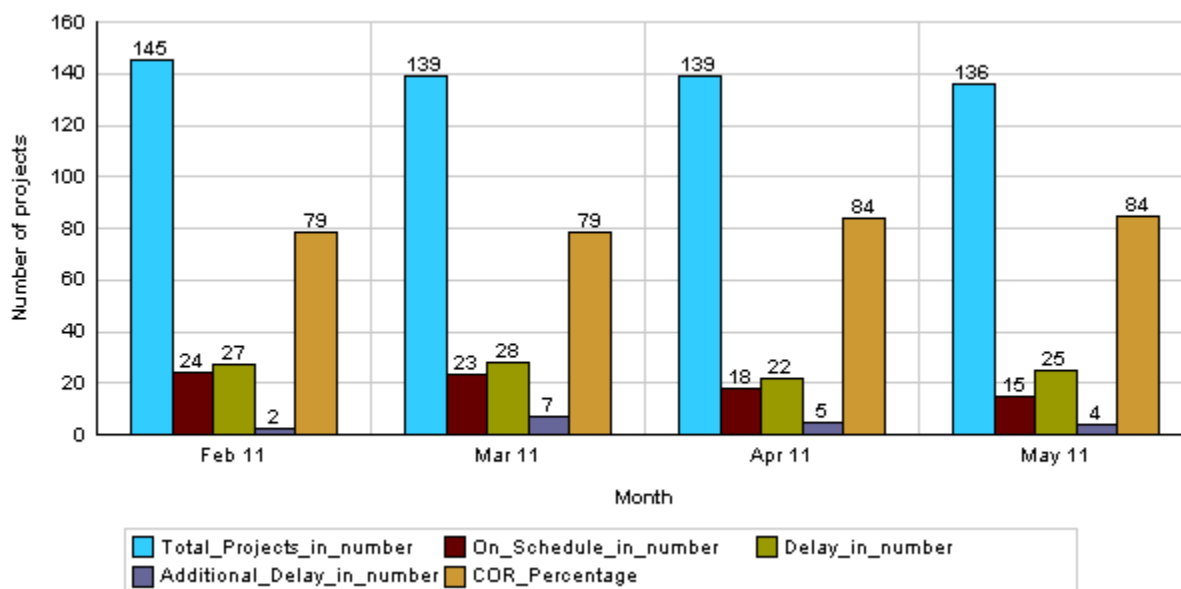


Railways Sector Sector Break-up of 25 Delayed projects in May 2011

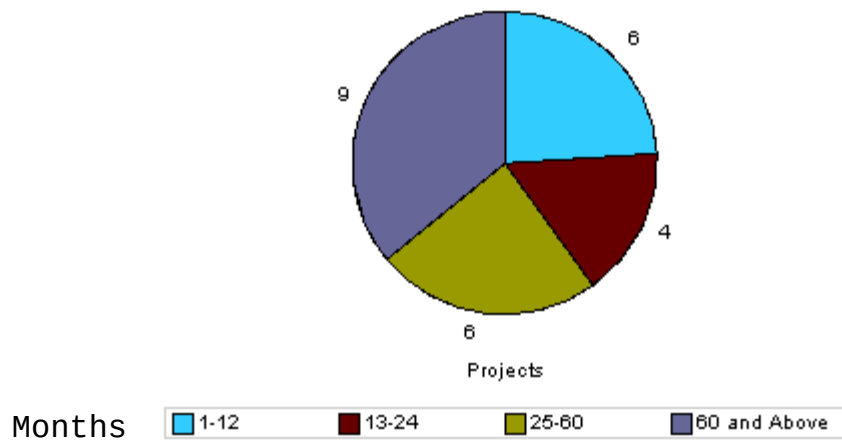


Trend and Graphical Analysis

Power Sector

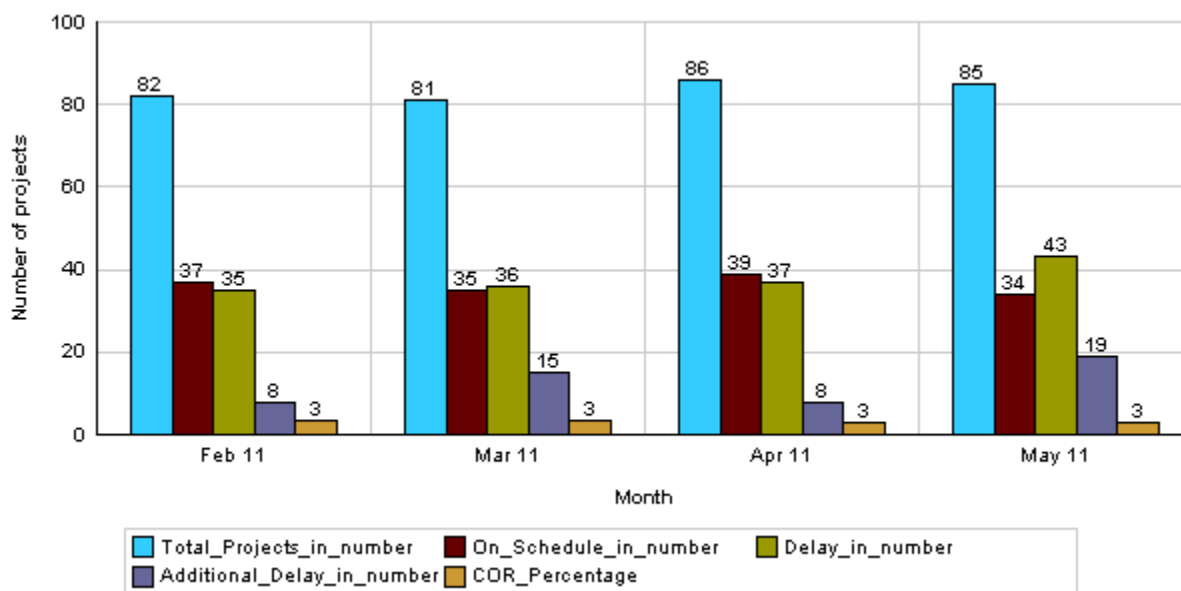


Power Sector Sector Break-up of 43 Delayed projects in May 2011

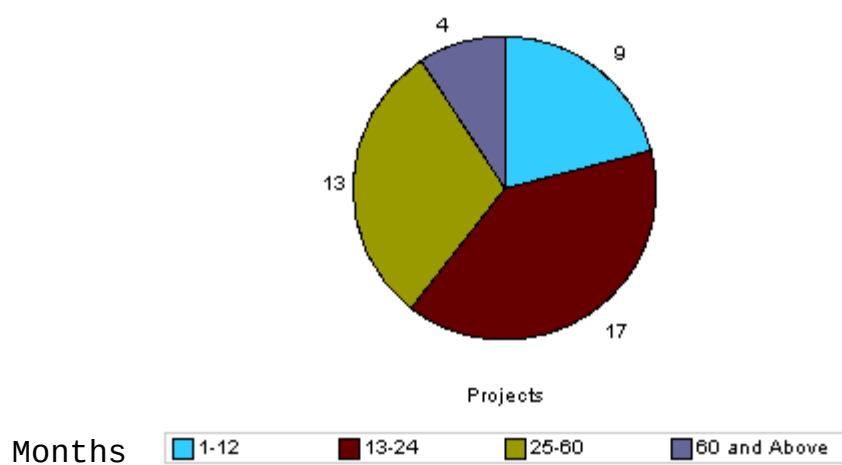


Trend and Graphical Analysis

Petroleum Sector

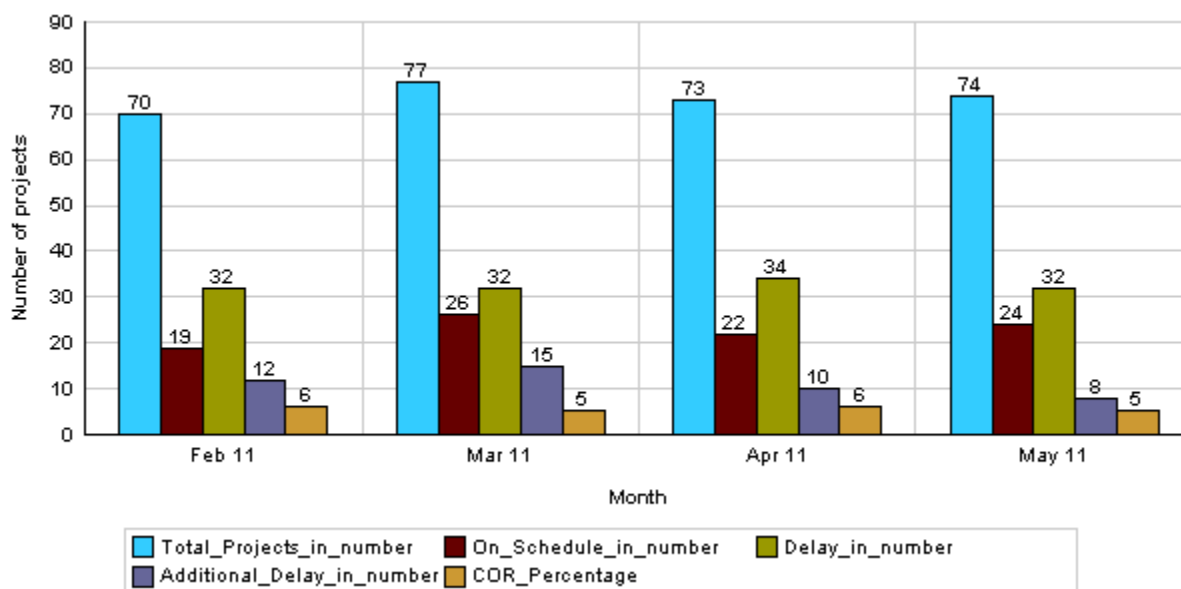


Petroleum Sector Sector Break-up of 32 Delayed projects in May 2011

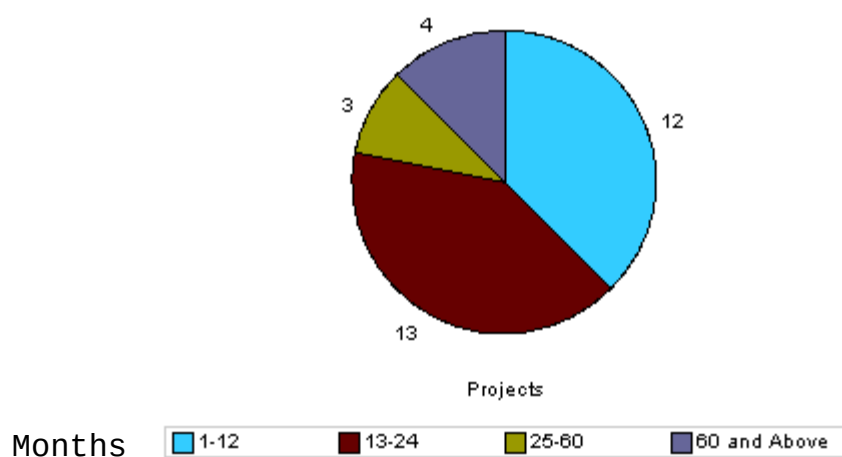


Trend and Graphical Analysis

Steel Sector

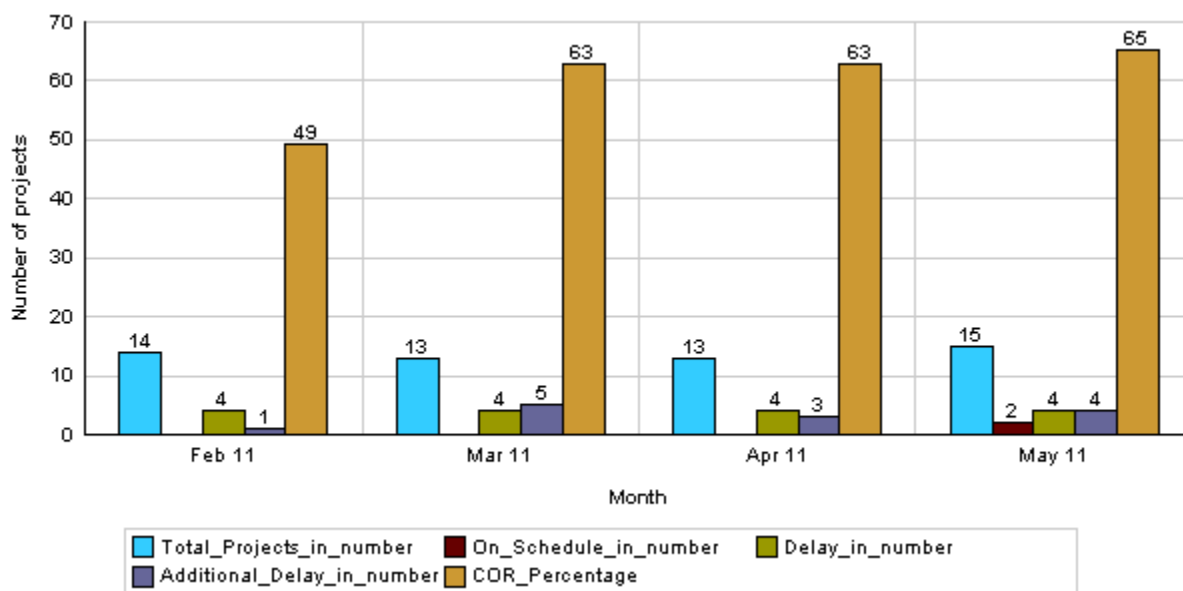


Steel Sector Sector Break-up of 4 Delayed projects in May 2011

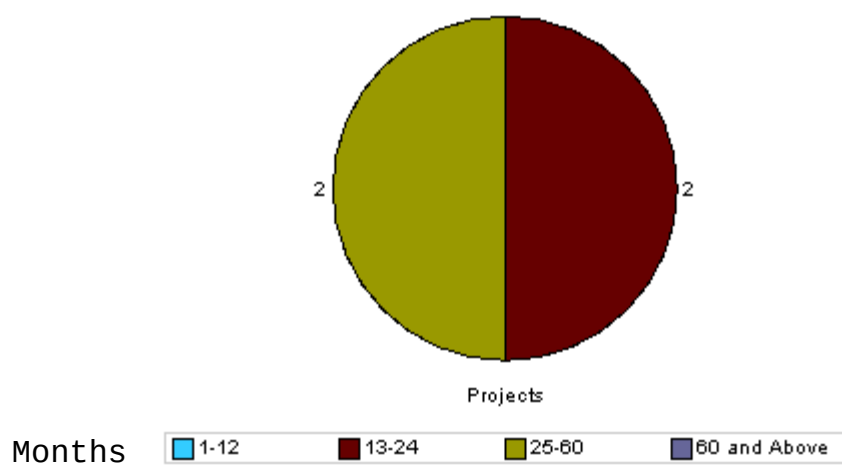


Trend and Graphical Analysis

Fertilisers Sector

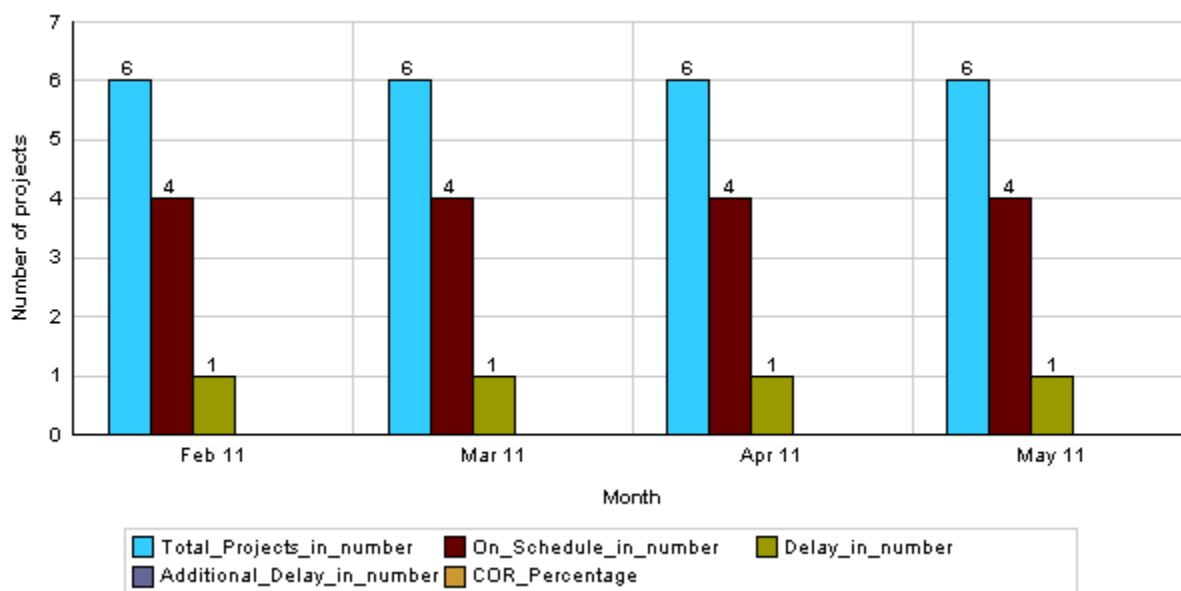


Fertilisers Sector Sector Break-up of 1 Delayed projects in May 2011

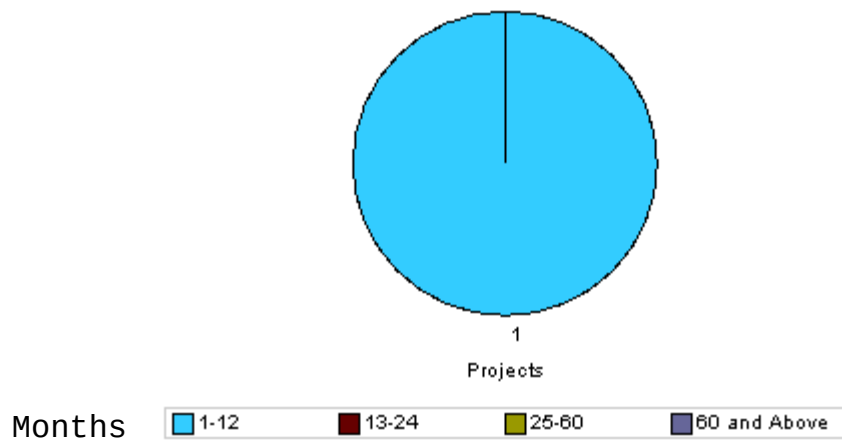


Trend and Graphical Analysis

Coal Sector

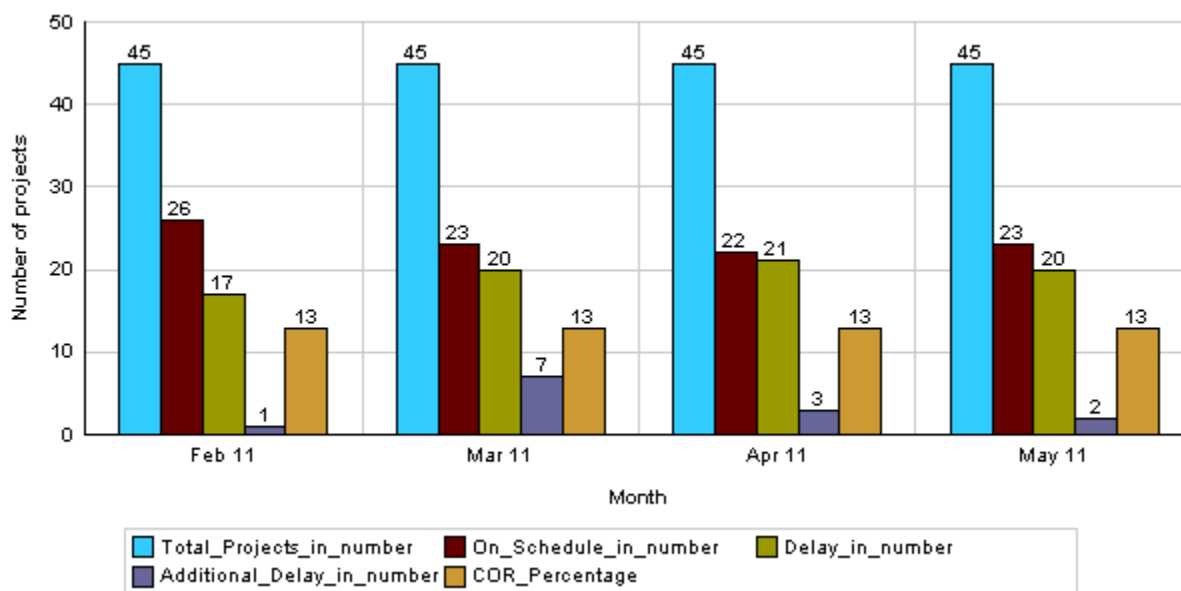


Coal Sector Sector Break-up of 20 Delayed projects in May 2011

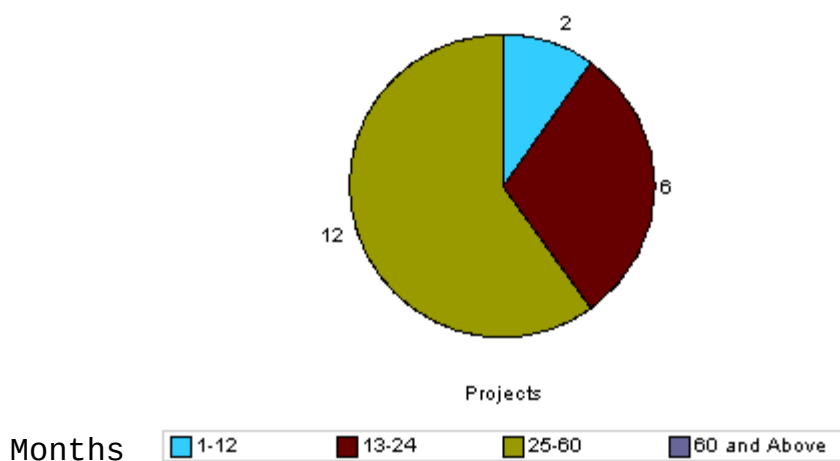


Trend and Graphical Analysis

Civil Aviation Sector

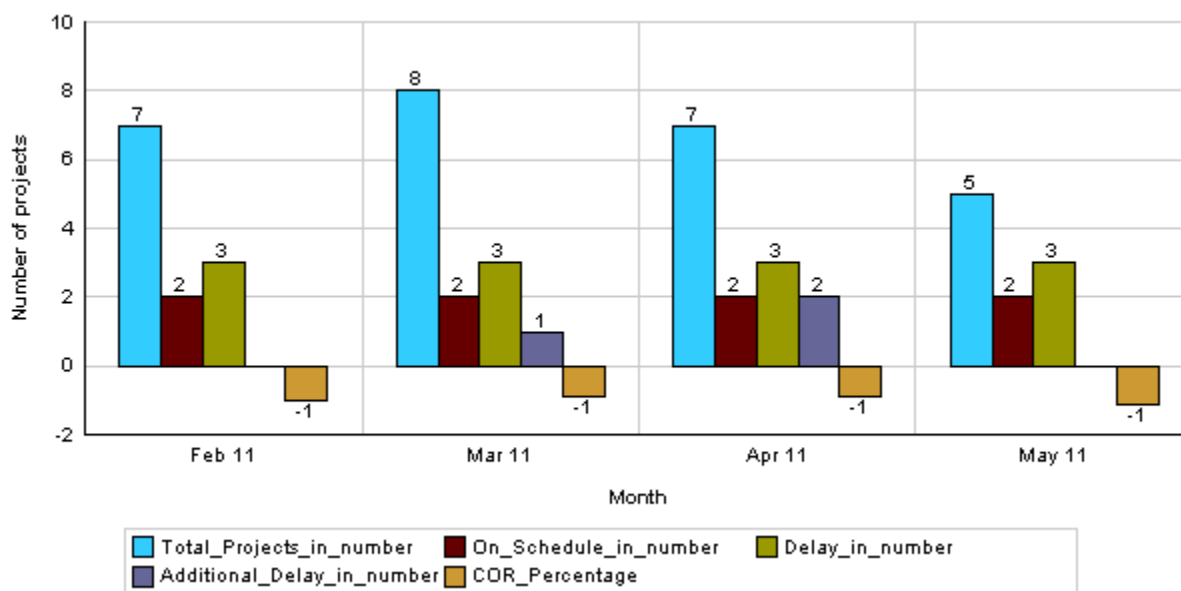


Civil Aviation Sector Break-up of 3 Delayed projects in May 2011

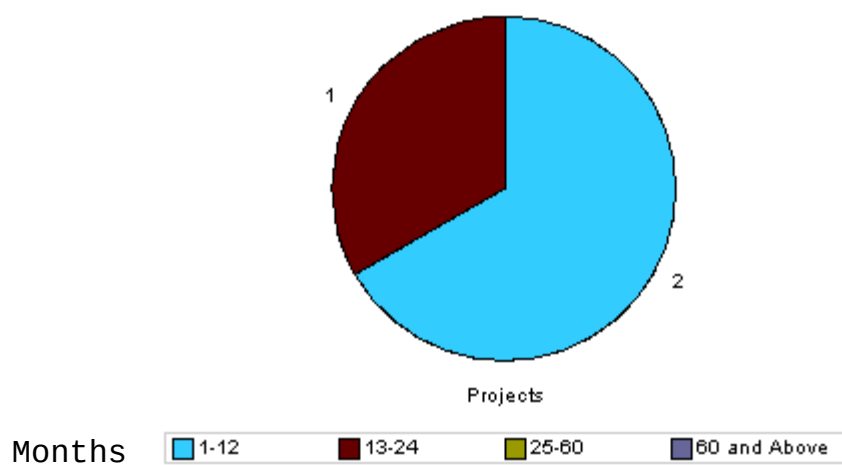


Trend and Graphical Analysis

Atomic Energy Sector

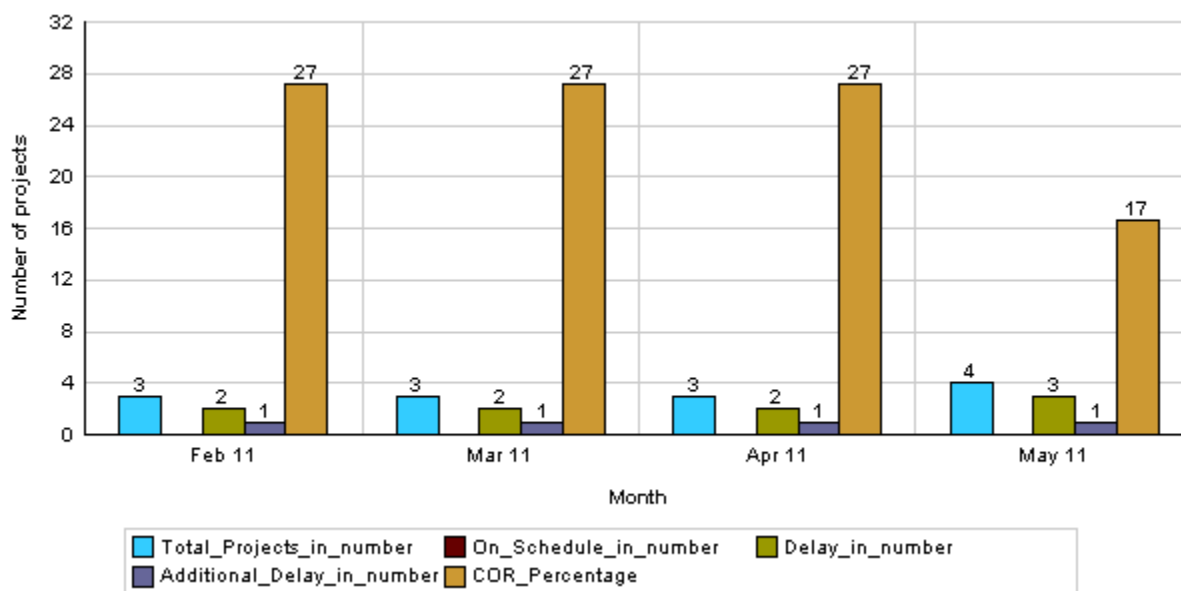

Atomic Energy Sector Sector Break-up of 3 Delayed projects in May 2011

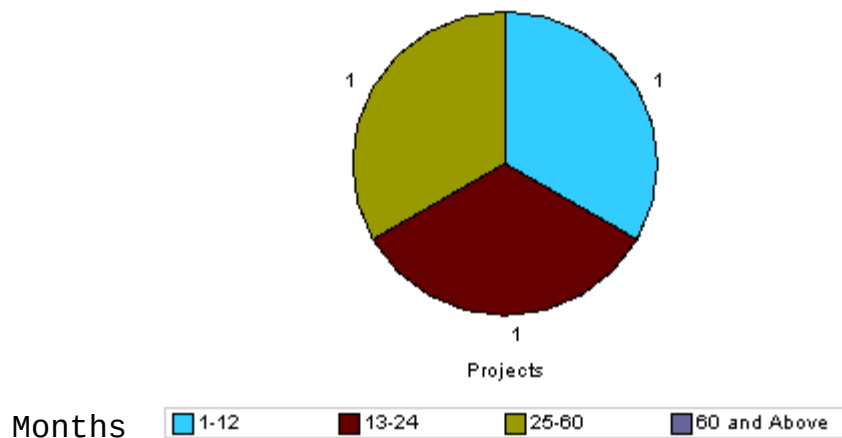

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	29,228.29	29,228.29	34,066.29
Civil Aviation	5	4,123.24	4,123.24	4,078.13
Coal	45	25,504.15	27,012.60	28,789.58
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	15	41,398.40	58,574.05	68,476.43
Petroleum	74	165,845.81	179,429.44	174,838.18
Power	85	178,267.70	179,493.46	183,786.71
Railways	136	66,442.61	84,572.09	122,507.27
Road Transport & Highways	128	61,806.58	61,806.58	63,269.99
Shipping & Ports	23	14,464.19	15,142.21	15,317.65
Telecommunications	41	20,025.99	19,979.50	21,450.84
Urban Development	3	15,185.18	15,173.44	30,684.66
Water Resources	1	542.90	542.90	1,187.00
Grand total	567	632,243.96	684,796.97	758,171.90

(May,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,001.38	09/2010 -	01/2012	16(O)	8/80
2	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	966.78	- 04/2011	04/2012	12(R3)	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	13,811.00	12/2008 -	05/2012	41(O)	61/119
4	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,	10/2009	11,459.00 -	11,459.00	626.00	12/2015 05/2016	11/2016	6(R1)	0/70
	Total		29,228.29 -	34,066.29	18,405.16				69/270
<u>Civil Aviation</u>									
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	1,942.51	1,158.51	05/2011 -	08/2011	3(O)	0/0
6	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI,Tamil Nadu	08/2008	1,273.00 -	1,273.00	835.91	01/2011 -	10/2011	9(O)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	204.73 -	204.73	32.50	05/2012 -	05/2012	0(O)	0/0
8	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.40 -	264.29	136.56	01/2011 -	06/2012	17(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	393.60 -	393.60	275.83	06/2013 -	06/2013	0(O)	0/0
	Total		4,123.24 -	4,078.13	2,439.31				0/0
<u>Coal</u>									
10	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,599.60	06/2009 -	08/2011	26(O)	59/26
11	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,199.49	06/2009 -	03/2012	33(O)	60/24
12	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	76.52	03/2010 -	03/2012	24(O)	0/4
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.49	03/2012 -	03/2012	0(O)	0/1
14	BALRAM OCP EXTENSION - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	111.23	03/2009 -	03/2012	36(O)	0/2
15	ANANTA OC EXPANSION PH-III - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	38.29	03/2012 -	03/2012	0(O)	0/0
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	73.65	03/2012 -	03/2012	0(O)	28/27

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	0.93	03/2012 -	03/2012	0(O)	7/34
18	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	1,724.26	- -	10/2012	-	0/6
19	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.65	03/2011 03/2013	03/2013	0(R3)	0/2
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.56	-	03/2010 -	03/2013	36(O)	0/2
21	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	609.15	03/2013 -	03/2013	0(O)	0/3
22	KANIHA OCP - [N06000035]MCL,Multi State	12/2007	457.77 -	457.77	97.00	03/2013 -	03/2013	0(O)	0/2
23	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.53 -	479.63	31.51	03/2013 -	03/2013	0(O)	0/2
24	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	23.08	03/2013 -	03/2013	0(O)	0/2
25	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	158.25	03/2013 09/2012	06/2013	9(R3)	2/22
26	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,064.86	03/2010 -	03/2014	48(O)	3/2
27	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,069.30	03/2010 -	03/2014	48(O)	2/3
28	BINA EXTN. PROJ - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	145.92	03/2014 -	03/2014	0(O)	1/2
29	CHURCHA UG - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	256.40	03/2014 -	03/2014	0(O)	0/2
30	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	17.63	03/2011 -	03/2014	36(O)	0/3
31	PENGANGA OC - [N06000066]WCL,	10/2008	339.77 -	339.77	0.10	- -	03/2014	-	0/0
32	KARTALI (EAST) OC - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
33	MANIKPUR OC EXPANTION - [N06000081]SECL,Chhatisgarh	11/2009	321.50 -	321.50	223.01	03/2014 -	03/2014	0(O)	0/1
34	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.60	03/2011 03/2012	03/2014	24(R3)	0/2
35	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.47	03/2012 -	03/2014	24(O)	0/2
36	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	76.04	03/2012 03/2013	03/2014	12(R3)	0/2
37	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	25.21	03/2014 -	03/2014	0(O)	0/0
38	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 -	437.34	138.07	03/2012 -	03/2015	36(O)	0/2
39	JHANJRA LONGWAL UG PHASE II - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48(O)	1/5
40	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	23.97	03/2013 03/2015	03/2015	0(R3)	0/3

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
41	PELMA OC - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
42	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	64.40	12/2012	03/2015	27(O)	11/44
43	Batura OC - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
44	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	0/1
45	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	16.26	03/2015	03/2015	0(O)	4/31
46	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
47	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	67.11	03/2014	03/2016	24(O)	1/2
48	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78	706.40	16.23	07/2012 03/2014	03/2016	24(R3)	0/2
49	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.20	03/2015	03/2016	12(O)	0/2
50	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	109.84	03/2016	03/2016	0(O)	0/1
51	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	289.69	03/2016	03/2016	0(O)	0/2
52	BHUBANESWARI OCP - [N06000034]MCL,Orissa	12/2007	490.10	490.10	80.33	03/2017	03/2017	0(O)	0/1
53	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	38.43	03/2012	03/2012	0(O)	13/42
54	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013	03/2013	0(O)	0/83
Total			25,504.15	28,789.58	10,716.48				192/430
Fertilisers									
55	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
56	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
57	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	85.96	- 11/2011	11/2011	0(R3)	2/22
58	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	132.25	01/2013	01/2013	0(O)	0/5
59	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	115.95	01/2013	01/2013	0(O)	0/5
60	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	119.71	12/2012	01/2013	1(O)	0/8

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		5,317.41	5,317.41	453.87				2/40
	<u>Mines</u>								
61	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa	10/2004	4,091.51 4,401.76	4,401.76	3,983.00	12/2008 01/2011	05/2011	4(R3)	117/110
	Total		4,091.51	4,401.76	3,983.00				117/110
	<u>Steel</u>								
62	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]SAIL, Jharkhand	07/2008	172.78 -	172.78	129.87	01/2010 -	06/2011	17(O)	0/1
63	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Chhatisgarh	07/2007	111.28 232.93	232.93	148.35	- -	07/2011	-	0/1
64	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]SAIL, Jharkhand	10/2007	500.90 -	500.90	174.51	04/2010 -	09/2011	17(O)	0/2
65	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	216.05	- -	09/2011	-	1/2
66	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	220.64	- -	10/2011	-	2/3
67	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,	02/2008	14,443.00 16,408.00	16,408.00	10,895.83	- 12/2011	12/2011	0(R3)	1/14
68	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	3,316.00 6,325.00	6,325.00	1,968.86	- 12/2011	12/2011	0(R3)	0/11
69	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	8,370.23	10/2009 -	03/2012	29(O)	45/59
70	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 -	607.17	282.27	- -	03/2012	-	3/7
71	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	480.84	90.90	- 05/2012	05/2012	0(R3)	1/2
72	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	41.11	- 10/2012	10/2012	0(R3)	3/4
73	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00 -	11,812.00	1,253.17	02/2011 -	03/2013	25(O)	0/0
74	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	5,185.00 17,265.00	17,265.00	2,594.45	- 03/2013	03/2013	0(R3)	0/20
75	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
76	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		41,398.40	68,476.43	26,386.24				56/126
	<u>Petroleum</u>								

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
77	CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL,Kerala	09/2009	2,591.80 3,941.41	3,941.41	3,252.92	12/2009 -	12/2010	12(O)	0/0
78	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]ONGC,Gujarat	12/2003	900.92 1,493.49	976.08	774.32	05/2008 07/2010	04/2011	9(R3)	0/2
79	Pipeline Replacement project-2 - [N16000111]ONGC,Multi State	12/2007	2,553.28 3,796.21	3,796.21	3,614.84	05/2011 -	05/2011	0(O)	0/0
80	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,577.70	09/2009 -	06/2011	21(O)	0/0
81	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	578.60	04/2010 -	06/2011	14(O)	0/0
82	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	229.89	04/2011 -	06/2011	2(O)	0/0
83	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 196.25	200.00	85.74	- 06/2011	06/2011	0(R3)	1/8
84	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	227.20	12/2010 -	06/2011	6(O)	0/0
85	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	411.26	03/2011 05/2011	06/2011	1(R3)	0/0
86	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	620.66	12/2010 -	06/2011	6(O)	0/0
87	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL,Assam	04/2008	293.60 -	293.60	219.75	12/2009 -	07/2011	19(O)	0/0
88	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	198.79	12/2010 08/2011	08/2011	0(R3)	0/0
89	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,403.26 4,403.26	2,500.00	2,135.08	10/2011 09/2011	09/2011	0(R3)	0/2
90	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 -	756.00	637.09	12/2011 -	09/2011	-3(O)	0/0
91	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
92	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	267.00	160.00	09/2012 -	10/2011	-11(O)	0/0
93	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
94	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 1,816.07	1,400.00	807.12	- 12/2011	12/2011	0(R3)	0/1
95	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]GAIL,Madhya pradesh	11/2007	1,512.00 1,434.00	982.00	837.10	04/2011 12/2011	12/2011	0(R3)	0/3
96	COMPRESSOR STATIONS (KAILARAS &CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 1,167.00	810.00	448.39	04/2011 12/2011	12/2011	0(R3)	0/2

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
97	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	169.28	03/2013 -	12/2011	-15(O)	0/0
98	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.29	09/2011 -	12/2011	3(O)	0/0
99	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,528.91	05/2011 -	12/2011	7(O)	0/116
100	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	5,898.46	01/2012 -	01/2012	0(O)	0/0
101	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	02/2012	35(O)	0/0
102	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
103	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	447.73	09/2011 03/2012	03/2012	0(R3)	0/0
104	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJECT PHASE-I - [N16000071]GAIL,Multi State	06/2009	348.00 348.00	260.00	114.08	03/2012 12/2012	03/2012	-9(R3)	6/12
105	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	340.00	95.29	06/2011 03/2012	03/2012	0(R3)	3/9
106	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
107	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 -	5,460.61	2,285.02	- -	04/2012	-	0/30
108	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
109	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,113.55	05/2010 05/2012	05/2012	0(R3)	0/0
110	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,093.65	09/2010 03/2012	05/2012	2(R3)	0/0
111	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	12.28	05/2010 04/2012	05/2012	1(R3)	0/0
112	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	52.56	07/2010 05/2012	05/2012	0(R3)	0/0
113	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	36.86	05/2012 -	05/2012	0(O)	5/36
114	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,113.85	08/2010 03/2012	06/2012	3(R3)	0/0
115	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	466.18	06/2012 -	06/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
116	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33	1,492.33	663.21	-	06/2012	-	6/9
117	Wind Power Project - [N16000119]ONGC,Gujarat	07/2010	1,106.00	1,106.00	-	06/2012	06/2012	0(O)	0/0
118	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11	370.11	50.26	04/2011	07/2012	15(O)	0/0
119	BNPL SPURLINE (UTTRANCHAL & PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92	400.00	56.20	06/2011 07/2012	07/2012	0(R3)	7/9
120	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	289.60	07/2012	07/2012	0(O)	0/0
121	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,500.00	605.45	03/2012 08/2012	08/2012	0(R3)	11/10
122	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	45.06	08/2012	08/2012	0(O)	0/0
123	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	2,003.05	09/2012	09/2012	0(O)	0/0
124	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	315.60	- 09/2012	09/2012	0(R3)	0/15
125	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26	302.26	15.78	09/2012	09/2012	0(O)	0/0
126	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	29,777.00	7,148.66	-	11/2012	-	107/103
127	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	1,797.35	49.86	12/2011	01/2013	13(O)	0/0
128	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	9.77	-	01/2013	-	11/18
129	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	-	01/2013	01/2013	0(O)	0/0
130	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	5.49	-	02/2013	-	12/42
131	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	218.08	03/2006 03/2013	03/2013	0(R3)	6/6
132	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,653.89	05/2010 03/2013	03/2013	0(R3)	0/0
133	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	281.62	03/2013	03/2013	0(O)	0/0
134	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
135	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	-	03/2013	03/2013	0(O)	0/0
136	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	-	03/2013	03/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
137	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	02/2008	825.00 1,827.00	1,827.00	128.33	- 04/2013	04/2013	0(R3)	0/203
138	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	1.69	- -	08/2013	-	0/0
139	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
140	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
141	Wax Project - [N16000101]NRL,Assam	08/2010	576.60 -	576.60	1.74	02/2014 -	02/2014	0(O)	0/0
142	Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	85.38	02/2014 -	02/2014	0(O)	0/0
143	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	559.61	03/2007 03/2014	03/2014	0(R3)	3/3
144	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	-	12/2014 -	12/2014	0(O)	0/0
145	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O)	0/0
146	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	-	04/2015 -	04/2015	0(O)	0/0
147	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,209.98	03/2007 03/2017	03/2017	0(R3)	6/6
148	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.29	10/2010 -	-	-	0/0
149	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	384.00	09/2011 03/2012	09/2011	-6(R3)	0/0
150	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 6,652.22	6,652.22	0.80	03/2012 -	-	-	0/0
Total			165,845.81 -	174,838.18	60,887.36				184/645
Power									
151	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]PGCIL,Uttaranchal	06/2006	260.34 -	241.27	184.12	06/2008 -	06/2011	36(O)	9/20
152	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME - [260100100]PGCIL,Multi State	06/2006	803.70 -	803.76	665.56	06/2009 -	06/2011	24(O)	1/20
153	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07 -	204.07	110.58	06/2011 -	06/2011	0(O)	0/0
154	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE - [N18000059]PGCIL,Madhya Pradesh	02/2009	276.61 -	276.61	197.24	06/2011 -	06/2011	0(O)	0/0
155	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,609.35	08/2010 -	08/2011	12(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	642.99	02/2011	08/2011	6(O)	0/1
157	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.60	09/2010	08/2011	11(O)	0/0
158	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	210.01	05/2011	09/2011	4(R3)	0/0
159	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.47	06/2010	09/2011	15(O)	0/0
160	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL,Multi State	04/2008	230.89	230.89	77.04	01/2011	10/2011	9(O)	0/1
161	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	459.86	01/2010	11/2011	22(O)	0/22
162	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	49.80	11/2011	11/2011	0(O)	0/0
163	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,461.01	10/2010	12/2011	14(O)	0/0
164	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,451.77	11/2009	12/2011	25(O)	0/0
165	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,477.70	09/2009	12/2011	27(O)	15/30
166	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	4,978.56	2,894.24	07/2010	12/2011	17(O)	3/20
167	SIMHADRI STPP STAGE -II - [N18000032]NTPC,	08/2007	5,103.39	5,038.83	3,910.00	-	12/2011	-	0/6
168	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	289.14	07/2011	12/2011	5(O)	0/0
169	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	229.52	02/2012	02/2012	0(O)	0/0
170	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	31.50	02/2012	02/2012	0(O)	0/0
171	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	143.12	08/2011	02/2012	6(O)	0/0
172	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	204.48	07/2010	02/2012	0(R3)	0/0
173	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	60.47	07/2011	02/2012	7(O)	0/0
174	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,398.39	2,381.37	04/2005	03/2012	83(O)	2/12

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
175	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC, Chhatisgarh	12/2003	8,323.39	8,323.39	7,128.00	12/2009	03/2012	27(O)	33/56
176	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu	05/2005	1,779.29	1,946.85	1,708.94	11/2008	03/2012	40(O)	25/38
177	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Multi State	10/2006	975.96	894.26	682.82	10/2009	03/2012	29(O)	2/20
178	System Strengthening -X of SR - [N18000086]PGCIL, Multi State	12/2009	276.61	276.61	64.84	04/2012	04/2012	0(O)	0/0
179	TESSTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC, West Bengal	10/2003	768.92	768.92	1,319.23	03/2007	05/2012	62(O)	1/25
180	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, J & K	08/2006	611.02	611.02	634.88	08/2010	06/2012	22(O)	0/0
181	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL, Multi State	07/2009	1,736.36	1,736.36	274.00	06/2012	06/2012	0(O)	0/0
182	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL, Bihar	02/2010	215.86	215.86	101.79	06/2012	06/2012	0(O)	0/0
183	System Strengthening -XII of SR - [N18000085]PGCIL, Multi State	02/2010	232.34	232.34	6.89	06/2012	06/2012	0(O)	0/0
184	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL, Multi State	08/2008	2,360.95	2,360.95	1,631.54	08/2012	08/2012	0(O)	0/0
185	765 KV POOLING STATION & NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL, Multi State	08/2008	7,075.33	7,075.33	3,758.75	08/2012	08/2012	0(O)	0/0
186	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL, Multi State	12/2009	1,216.83	1,216.83	275.04	08/2012	08/2012	0(O)	0/0
187	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, Multi State	10/2008	4,824.12	4,824.12	1,722.37	10/2012	10/2012	0(O)	0/0
188	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL, Maharashtra	02/2010	469.38	469.38	111.94	10/2012	10/2012	0(O)	0/0
189	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL, Multi State	10/2010	160.32	160.32	11.23	10/2012	10/2012	0(O)	0/0
190	MOUDA STPP (NTPC) - [N18000048]NTPC, Maharashtra	11/2007	5,459.28	6,010.89	2,449.00	-	11/2012	-	0/16
191	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL, Multi State	03/2010	4,672.99	4,672.99	264.04	11/2012	11/2012	0(O)	0/0
192	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL, Multi State	03/2010	965.58	965.58	202.20	11/2012	11/2012	0(O)	0/0
193	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL, Multi State	07/2010	1,272.80	1,272.80	85.21	11/2012	11/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
194	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38	1,061.38	953.10	09/2009	12/2012	39(O)	0/0
195	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88	7,031.88	2,248.33	12/2012	12/2012	0(O)	0/0
196	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,	01/2009	5,915.00	5,915.00	1,910.00	-	12/2012	-	0/15
197	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,	01/2009	6,230.81	6,230.81	1,796.00	-	12/2012	-	0/16
198	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL, Multi State	02/2010	2,144.00	2,144.00	197.77	12/2012	12/2012	0(O)	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL, Multi State	10/2010	182.68	182.68	25.54	01/2013	01/2013	0(O)	0/0
200	Transmission system for transfer of power from Gen. - [N18000098]PGCIL, Multi State	05/2010	250.03	250.03	17.35	01/2013	01/2013	0(O)	0/0
201	KOLDAM HEP (NTPC) - [180100211]NTPC, Himachal Pr.	10/2002	4,527.15	4,527.15	3,657.00	04/2009	03/2013	47(O)	19/9
202	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra	12/2007	477.69	477.69	337.28	09/2010	03/2013	30(O)	0/0
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL, Multi State	02/2009	520.48	520.48	249.06	11/2011	03/2013	16(O)	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66	509.66	233.23	11/2011	03/2013	16(O)	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, Multi State	02/2009	410.29	410.29	115.67	02/2012	03/2013	13(O)	0/0
206	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL, Multi State	02/2009	1,347.32	1,347.32	787.90	02/2012	03/2013	13(O)	0/0
207	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL, Multi State	11/2009	1,075.12	1,075.12	216.15	05/2012	03/2013	10(O)	0/0
208	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL, Orissa	09/2010	2,074.86	2,074.86	99.43	03/2013	03/2013	0(O)	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL, Multi State	08/2010	1,677.57	1,677.57	62.92	04/2013	04/2013	0(O)	0/0
210	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR - [N18000097]PGCIL, Multi State	08/2010	170.36	170.36	8.70	04/2013	04/2013	0(O)	0/0
211	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO, Tripura	07/2009	421.01	623.44	66.06	01/2012	07/2013	18(O)	0/0
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, Multi State	07/2010	752.64	752.64	33.37	07/2013	07/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
213	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	186.98	08/2013 08/2013	08/2013	0(R3)	8/17
214	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	54.88	08/2013 -	08/2013	0(O)	0/0
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	15.15	08/2013 -	08/2013	0(O)	0/0
216	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	122.97	08/2013 -	08/2013	0(O)	0/0
217	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,181.28	01/2012 -	09/2013	20(O)	2/10
218	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	123.79	11/2011 -	09/2013	22(O)	0/0
219	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,	01/2008	4,375.35 -	4,375.35	2,122.00	- -	10/2013	-	0/29
220	BARH STPP STAGE -II - [N18000047]NTPC,	02/2008	7,341.04 -	7,341.04	2,205.00	- -	10/2013	-	0/18
221	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	55.83	11/2013 -	11/2013	0(O)	0/0
222	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	210.01	12/2013 -	12/2013	0(O)	0/0
223	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	228.32	07/2006 01/2014	01/2014	0(R3)	2/5
224	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014	0(O)	0/0
225	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,	11/2006	2,978.48 -	2,978.48	1,116.00	- -	06/2014	-	5/13
226	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,179.39	09/2009 -	07/2014	58(O)	1/20
227	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	6,285.33	4,932.69	09/2010 -	08/2014	47(O)	2/11
228	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,693.00 -	8,693.00	5,729.00	11/2010 -	09/2014	46(O)	15/51
229	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	2,477.88	08/2013 -	09/2014	13(O)	0/0
230	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	-	01/2015 -	01/2015	0(O)	0/0
231	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttaranchal	07/2006	1,657.00 -	2,978.86	260.63	07/2010 -	01/2016	66(O)	1/1
232	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67 -	3,642.04	731.24	07/2014 -	01/2016	18(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
233	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,221.31 2,491.45	2,491.45	154.91	07/2014 -	03/2016	20(O)	0/8
234	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,465.35	05/2013 06/2016	06/2016	0(R3)	78/22
235	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	820.09	12/2007 12/2009	-	-	14/18
Total			178,267.70 -	183,786.71	83,857.90				238/550
<u>Railways</u>									
236	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	228.80	- 02/2009	12/2010	22(R1)	0/0
237	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	144.65	- 03/2009	12/2010	21(R1)	0/0
238	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	-	12/2007 03/2010	12/2010	9(R1)	0/0
239	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
240	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	237.62	- -	12/2010	-	0/0
241	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	294.96	- 03/2009	03/2011	24(R1)	0/0
242	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
243	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]JMRT,Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,157.68	- 12/2010	06/2011	6(R3)	0/1
244	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	592.12	- -	07/2011	-	0/0
245	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	149.34	- -	08/2011	-	0/0
246	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.39	03/2002 -	09/2011	114(O)	0/0
247	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	154.69	02/2010 -	11/2011	21(O)	0/0
248	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	549.11	03/1994 -	12/2011	213(O)	0/0
249	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	445.50	02/2009 -	12/2011	34(O)	0/0
250	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	194.26	- 09/2009	12/2011	27(R1)	0/0
251	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	73.22	- -	12/2011	-	0/0
252	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	203.03	03/2013 -	12/2011	-15(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
253	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,058.17	- -	02/2012	-	0/0
254	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	383.65	- 12/2009	02/2012	26(R1)	0/0
255	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	56.75	12/2011 -	02/2012	2(O)	0/0
256	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	617.62	465.90	- -	03/2012	-	0/0
257	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	421.09	- 12/2011	03/2012	3(R3)	0/0
258	KADUR-CHIKMAGALUR-SAKLESHUPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	194.04	- 03/2012	03/2012	0(R3)	0/0
259	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	414.15	- -	03/2012	-	0/0
260	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.52	- -	03/2012	-	0/0
261	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	69.02	- -	03/2012	-	0/0
262	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	332.36	- 03/2011	03/2012	12(R3)	0/0
263	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	180.10	- -	03/2012	-	0/0
264	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	868.14	- -	03/2012	-	0/0
265	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	185.70	03/2010 -	03/2012	24(O)	0/0
266	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	164.50	- -	03/2012	-	0/0
267	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	74.98	03/2012 -	03/2012	0(O)	0/0
268	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	165.75	03/2011 -	03/2012	12(O)	0/0
269	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	372.55	06/2005 07/2011	03/2012	8(R3)	0/0
270	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36 -	803.39	774.66	03/2011 -	03/2012	12(O)	0/0
271	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	41.89	03/2012 -	03/2012	0(O)	0/0
272	Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	28.78	03/2012 -	03/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
273	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	318.24	0.53	03/2012 -	03/2012	0(O)	0/0
274	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	131.08	03/2007 03/2007	06/2012	63(R1)	0/0
275	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	319.27	- 07/2012	07/2012	0(R3)	0/0
276	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,404.00	563.89	- -	12/2012	-	0/0
277	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	739.28	12/2012 -	12/2012	0(O)	0/0
278	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	379.62	03/2005 12/2008	12/2012	48(R1)	0/0
279	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	235.42	- 03/2012	12/2012	9(R3)	0/0
280	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	229.70	- -	12/2012	-	0/0
281	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	921.00	462.04	03/2009 -	12/2012	45(O)	0/0
282	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	908.13	10/2007 -	12/2012	62(O)	0/0
283	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	306.18	03/2010 -	12/2012	33(O)	0/0
284	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	97.88	12/2012 -	12/2012	0(O)	0/0
285	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	141.42	- 03/2013	03/2013	0(R3)	0/0
286	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	142.04	- -	03/2013	-	0/0
287	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 912.70	1,556.23	589.56	- -	03/2013	-	0/0
288	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	350.81	-	03/2013 -	03/2013	0(O)	0/0
289	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	113.48	- 06/2013	06/2013	0(R3)	0/0
290	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	48.77	12/2011 -	11/2013	23(O)	0/0
291	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	159.94	- -	12/2013	-	0/0
292	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	81.30	12/2012 -	12/2013	12(O)	0/0
293	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	4,091.33	2,682.87	03/2009 -	12/2013	57(O)	0/0
294	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,186.05	04/2008 03/2014	03/2014	0(R3)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
295	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	725.92	12/2008 -	03/2014	63(O)	0/0
296	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	190.07	03/2014 -	03/2014	0(O)	0/0
297	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	2.90	04/2014 -	03/2014	-1(O)	0/0
298	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	3.51	03/2014 -	03/2014	0(O)	0/0
299	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	18.22	03/2014 -	03/2014	0(O)	0/0
300	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	151.97	03/2014 -	03/2014	0(O)	0/0
301	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	93.63	03/2010 06/2014	06/2014	0(R3)	0/0
302	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	159.96	- -	03/2015	-	0/0
303	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTTP,Maharashtra	04/2008	5,300.00 -	5,300.00	239.18	03/2014 -	03/2015	12(O)	0/0
304	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.69	12/2015 -	03/2015	-9(O)	0/0
305	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
306	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	7.98	03/2015 -	03/2015	0(O)	0/0
307	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	419.75	03/2011 03/2014	03/2016	24(R3)	0/0
308	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.21	03/2014 -	03/2016	24(O)	0/0
309	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	1.42	03/2016 -	03/2016	0(O)	0/0
310	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	19.73	03/2016 -	03/2016	0(O)	0/0
311	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	-	03/2016 -	06/2016	3(O)	0/0
312	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
313	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	480.19	03/1995 -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
314	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	507.39	03/1996 08/2009	-	-	0/0
315	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	133.43	- -	-	-	0/0
316	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	83.06	12/2012 -	-	-	0/0
317	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	78.19	- -	-	-	0/0
318	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	452.09	- -	-	-	0/0
319	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
320	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	712.00	533.40	- -	-	-	0/0
321	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	64.07	- -	-	-	0/0
322	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	83.34	- -	-	-	0/0
323	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
324	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,014.10	07/2005 -	-	-	0/0
325	VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	538.29	- -	-	-	0/0
326	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	82.96	- -	-	-	0/0
327	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	809.39	06/2007 -	-	-	0/0
328	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	297.07	04/2003 03/2010	-	-	0/0
329	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	458.15	- -	-	-	0/0
330	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
331	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	297.46	- 12/2012	-	-	0/0
332	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
333	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	70.29	- -	-	-	0/0
334	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	205.74	- -	-	-	0/0
335	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	170.73	03/1998 08/2005	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	24.93	02/2015	-	-	0/0
337	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0
338	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92	261.70	14.68	02/2006	-	-	0/0
339	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	281.83	03/2008 06/2008	-	-	0/0
340	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	160.00	-	-	-	0/0
341	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	373.46	-	-	-	0/0
342	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	20.45	-	-	-	0/0
343	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	75.90	-	-	-	0/0
344	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	34.57	-	-	-	0/0
345	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
346	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	430.95	06/1999 03/2011	-	-	0/0
347	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	164.54	03/2004	-	-	0/0
348	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	546.68	- 11/2010	-	-	0/0
349	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 589.86	563.25	544.24	03/2004 03/2010	-	-	0/0
350	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	321.23	- 03/2011	-	-	0/0
351	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07	456.45	263.34	06/2004 04/2005	-	-	0/0
352	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00	925.00	495.62	05/2008 03/2011	-	-	0/0
353	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	217.89	12/2009 03/2011	-	-	0/0
354	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	744.69	716.20	- 12/2010	-	-	0/0
355	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	287.38	-	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
356	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	239.95	- -	-	-	0/1
357	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	662.50	- -	-	-	0/0
358	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	2,945.43	12/2006 08/2010	-	-	0/0
359	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	221.51	- 02/2011	-	-	0/0
360	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	421.89	02/2010 02/2011	-	-	0/0
361	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	346.13	- -	-	-	0/0
362	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	228.79	- 03/2011	-	-	0/0
363	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	63.42	- -	-	-	0/0
364	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	126.80	- -	-	-	0/0
365	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	256.44	03/2008 10/2010	-	-	0/0
366	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	415.50	355.38	- 03/2011	03/2011	0(R3)	0/0
367	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	46.05	- -	-	-	0/0
368	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	134.79	12/2010 03/2011	-	-	0/0
369	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	145.48	03/2011 -	-	-	0/0
370	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	125.98	- 12/2010	-	-	0/0
371	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	167.30	03/2011 03/2011	-	-	0/0
Total			66,442.61 -	122,507.27	52,515.94				0/2
Road Transport & Highways									
372	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	598.90	03/2009 -	05/2011	26(O)	0/0
373	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	138.59	08/2004 -	06/2011	82(O)	0/0
374	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	148.38	08/2004 -	06/2011	82(O)	0/0
375	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	247.70	07/2004 -	06/2011	83(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
376	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	522.00	476.60	03/2005	06/2011	75(O)	0/0
377	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI, Tamil Nadu	12/2003	210.00	210.00	672.30	04/2007	06/2011	50(O)	0/0
378	GARMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	275.00	288.10	09/2007	06/2011	45(O)	0/0
379	HAPUR-GARMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	213.80	09/2007	06/2011	45(O)	0/0
380	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	479.54	435.90	11/2007	06/2011	43(O)	0/0
381	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI, Uttar Pradesh	12/2003	193.00	193.00	324.40	10/2008	06/2011	32(O)	0/0
382	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI, Uttar Pradesh	12/2003	217.00	217.00	345.60	10/2008	06/2011	32(O)	0/0
383	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	242.60	10/2008	06/2011	32(O)	0/0
384	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	227.00	381.70	10/2008	06/2011	32(O)	0/0
385	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	337.10	03/2008	06/2011	39(O)	0/0
386	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI, Uttar Pradesh	03/2005	359.00	359.00	772.80	03/2009	06/2011	27(O)	0/0
387	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	06/2011	29(O)	0/0
388	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00	227.00	357.50	12/2008	06/2011	30(O)	0/0
389	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	255.20	09/2008	06/2011	33(O)	0/0
390	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya pradesh	12/2003	198.00	198.00	183.40	11/2008	06/2011	31(O)	0/0
391	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	247.20	10/2008	06/2011	32(O)	0/0
392	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	229.91	197.60	10/2008	06/2011	32(O)	0/0
393	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00	340.00	548.10	06/2008	06/2011	36(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
394	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	06/2011	24(O)	0/0
395	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	243.75	02/2004	06/2011	88(O)	0/0
396	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	665.50	10/2009	06/2011	20(O)	0/0
397	KURALI-KIRATPUR, NH-21 - [N24000087]NHAI, Punjab	03/2005	309.00	309.00	553.60	06/2010	06/2011	12(O)	0/0
398	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	412.10	12/2009	06/2011	18(O)	0/0
399	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.40	09/2009	06/2011	21(O)	0/0
400	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	276.09	294.90	09/2009	06/2011	21(O)	0/0
401	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	576.00	653.50	07/2010	06/2011	11(O)	0/0
402	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	285.00	355.80	07/2010	06/2011	11(O)	0/0
403	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	548.70	07/2010	06/2011	11(O)	0/0
404	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,803.00	01/2011	06/2011	5(O)	0/0
405	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	825.30	07/2010	06/2011	11(O)	0/0
406	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI, Karnataka	03/2005	565.00	565.00	1,080.00	07/2010	06/2011	11(O)	0/0
407	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	141.87	02/2004	06/2011	88(O)	0/0
408	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	06/2011	5(O)	0/0
409	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K	12/2003	193.09	166.30	174.10	03/2008	07/2011	40(O)	0/0
410	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27	193.10	142.20	03/2008	07/2011	40(O)	0/0
411	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya pradesh	12/2003	225.00	225.00	248.40	10/2008	07/2011	33(O)	0/0
412	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	228.80	06/2008	07/2011	37(O)	0/0
413	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI, Tamil Nadu	03/2005	629.00	629.00	910.00	11/2010	08/2011	9(O)	0/0
414	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	385.30	12/2008	08/2011	32(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
415	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,339.00	08/2011	08/2011	0(O)	0/0
416	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	218.90	11/2008	09/2011	34(O)	0/0
417	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	62.44	04/2004	10/2011	90(O)	0/0
418	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	246.00	06/2008	10/2011	40(O)	0/0
419	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	171.50	10/2011	10/2011	0(O)	0/0
420	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	498.30	10/2011	10/2011	0(O)	0/0
421	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	275.30	10/2008	11/2011	37(O)	0/0
422	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	166.90	10/2008	11/2011	37(O)	0/0
423	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	520.70	05/2010	11/2011	18(O)	0/0
424	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,372.00	11/2011	11/2011	0(O)	0/0
425	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
426	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	80.78	09/2008	12/2011	39(O)	0/0
427	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00	239.00	317.60	07/2005	12/2011	77(O)	0/0
428	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	200.30	06/2005	12/2011	78(O)	0/0
429	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	216.00	02/2009	12/2011	34(O)	0/0
430	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	74.70	04/2009	12/2011	32(O)	0/0
431	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	163.10	06/2008	12/2011	42(O)	0/0
432	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	371.00	12/2008	12/2011	36(O)	0/0
433	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	188.70	06/2008	12/2011	42(O)	0/0
434	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	199.80	10/2008	12/2011	38(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	411.00	09/2008	12/2011	39(O)	0/0
436	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	249.80	06/2008	12/2011	42(O)	0/0
437	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72	264.72	235.00	06/2008	12/2011	42(O)	0/0
438	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	462.20	03/2008	12/2011	45(O)	0/0
439	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00	225.00	160.90	06/2008	12/2011	42(O)	0/0
440	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00	208.00	197.20	04/2008	12/2011	44(O)	0/0
441	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00	160.00	111.60	05/2008	12/2011	43(O)	0/0
442	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	180.10	06/2008	12/2011	42(O)	0/0
443	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.00	06/2009	12/2011	30(O)	0/0
444	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	301.30	03/2010	12/2011	21(O)	0/0
445	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	324.70	05/2010	12/2011	19(O)	0/0
446	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	622.90	08/2010	12/2011	16(O)	0/0
447	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	344.20	02/2012	02/2012	0(O)	0/0
448	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	171.00	09/2007	03/2012	54(O)	0/0
449	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	109.30	04/2008	03/2012	47(O)	0/0
450	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	169.60	04/2008	03/2012	47(O)	0/0
451	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	125.50	04/2010	03/2012	23(O)	0/0
452	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	178.50	02/2010	03/2012	25(O)	0/0
453	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
454	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	611.40	05/2012	05/2012	0(O)	0/0
455	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	795.00	776.40	05/2012	05/2012	0(O)	0/0
456	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	268.00	05/2012	05/2012	0(O)	0/0
457	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	300.00	156.10	10/2008	06/2012	44(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	293.90	10/2009	06/2012	32(O)	0/0
459	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	232.45	157.00	09/2010	06/2012	21(O)	0/0
460	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	835.00	374.00	06/2012	06/2012	0(O)	0/0
461	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	1,478.00	10/2011	06/2012	8(O)	0/0
462	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	300.70	07/2012	07/2012	0(O)	0/0
463	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	109.30	05/2008	08/2012	51(O)	0/0
464	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.50	08/2012	08/2012	0(O)	0/0
465	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60	407.60	183.50	06/2010	10/2012	28(O)	0/0
466	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17	263.17	232.70	09/2009	10/2012	37(O)	0/0
467	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
468	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	726.70	09/2012	10/2012	1(O)	0/0
469	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	804.60	10/2012	10/2012	0(O)	0/0
470	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	588.40	11/2012	11/2012	0(O)	0/0
471	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
472	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
473	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	173.60	07/2008	12/2012	53(O)	0/0
474	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	355.10	12/2012	12/2012	0(O)	0/0
475	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	542.90	01/2013	01/2013	0(O)	0/0
476	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	695.00	09/2010	03/2013	30(O)	0/0
477	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
478	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	197.70	03/2013 -	03/2013	0(O)	0/0
479	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	173.20	03/2013 -	03/2013	0(O)	0/0
480	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	96.94	03/2013 -	03/2013	0(O)	0/0
481	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	04/2013	0(O)	0/0
482	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	125.00	05/2013 -	05/2013	0(O)	0/0
483	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	97.36	05/2013 -	05/2013	0(O)	0/0
484	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	138.70	05/2013 -	05/2013	0(O)	0/0
485	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	348.16	110.90	09/2007 -	06/2013	69(O)	0/0
486	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	-	06/2013 -	06/2013	0(O)	0/0
487	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	-	06/2013 -	06/2013	0(O)	0/0
488	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	29.60	04/2009 -	07/2013	51(O)	0/0
489	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	39.25	11/2008 -	07/2013	56(O)	0/0
490	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00 -	593.00	50.83	07/2013 -	07/2013	0(O)	0/0
491	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	-	08/2013 -	08/2013	0(O)	0/0
492	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	1,655.00	0.18	09/2013 -	09/2013	0(O)	0/0
493	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	0.99	09/2013 -	09/2013	0(O)	0/0
494	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	10.04	11/2013 -	11/2013	0(O)	0/0
495	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	40.71	11/2008 -	12/2013	61(O)	0/0
496	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	212.00	38.61	09/2007 -	12/2013	75(O)	0/0
497	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	196.00	27.66	07/2009 -	12/2013	53(O)	0/0
498	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	-	08/2014 -	08/2014	0(O)	0/0
499	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	807.00	299.90	10/2014 -	10/2014	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Total			61,806.58	63,269.99	44,209.21				0/0
	<u>Shipping & Ports</u>								
500	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	820.91	10/2008	11/2010	25(O)	0/0
501	DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD,Tamil Nadu	09/2006	399.13	399.13	-	08/2010	03/2011	7(O)	0/0
502	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	04/2011	8(O)	0/0
503	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 253.36	253.36	223.60	12/2007 07/2009	06/2011	23(R3)	0/0
504	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
505	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
506	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00	165.00	90.10	12/2005 01/2008	10/2011	45(R3)	0/0
507	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
508	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85	290.85	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
509	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96	1,061.96	280.33	03/2012	03/2012	0(O)	0/0
510	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006	03/2012	72(O)	0/0
511	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2012	0(O)	0/0
512	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03	277.03	55.41	12/2011 05/2012	05/2012	0(R3)	0/0
513	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	269.69	12/2010 09/2012	09/2012	0(R3)	0/0
514	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	222.91	09/2012	09/2012	0(O)	0/0
515	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29(O)	0/0
516	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72	612.72	61.31	12/2012	12/2012	0(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
517	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
518	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	0.73	03/2011 -	03/2013	24(O)	0/0
519	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
520	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 -	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
521	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	966.46	189.92	02/2014 -	02/2014	0(O)	0/0
522	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
Total			14,464.19 -	15,317.65	3,150.17				0/0
Telecommunications									
523	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	50.11	09/2009 -	02/2010	5(O)	0/0
524	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	102.34	12/2005 -	10/2010	58(O)	0/0
525	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
526	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	10/2010	7(O)	0/0
527	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	11/2010	8(O)	0/0
528	NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86 234.24	353.00	210.69	02/2008 -	12/2010	34(O)	0/0
529	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	12/2010	21(O)	0/0
530	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	12/2010	9(O)	0/0
531	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	12/2010	9(O)	0/0
532	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	12/2010	9(O)	0/0
533	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	12/2010	9(O)	0/0
534	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	127.26	06/2009 -	01/2011	19(O)	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
535	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.82	03/2009	02/2011	23(O)	0/0
536	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	171.01	12/2008	02/2011	26(O)	0/0
537	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	128.29	03/2009	02/2011	23(O)	0/0
538	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	25.67	06/2009	02/2011	20(O)	0/0
539	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	02/2011	25(O)	0/0
540	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	19.52	02/2010	02/2011	12(O)	0/0
541	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	112.89	10/2008	02/2011	28(O)	0/0
542	GSM equipment of 1900000Lines (2G) 401700 lines 3(-) - [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,312.52	579.17	- 03/2011	02/2011	-1(R3)	0/1
543	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	161.71	01/2010	02/2011	13(O)	0/0
544	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	399.04	01/2010	02/2011	13(O)	0/0
545	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	68.99	01/2010	02/2011	13(O)	0/0
546	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	438.00	12/2008	03/2011	27(O)	0/0
547	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	140.73	03/2009	03/2011	24(O)	0/0
548	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	601.49	480.57	09/2009	03/2011	18(O)	0/0
549	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	22.06	10/2009	03/2011	17(O)	0/0
550	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	11.21	09/2010	03/2011	6(O)	0/0
551	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	171.99	02/2009	03/2011	25(O)	0/0
552	GSM equipment of 1867000Lines (2G) 383000 lines 3(-) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	191.48	08/2009	03/2011	19(O)	0/0

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	151.70	11/2010 -	03/2011	4(O)	0/0
554	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	238.44	10/2009 -	03/2011	17(O)	0/0
555	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	12.01	10/2010 -	04/2011	6(O)	0/0
556	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
557	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
558	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 389.86	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
559	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	94.13	10/2007 -	-	-	0/0
560	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
561	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	841.00	03/2009 -	-	-	0/0
562	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0
563	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	392.44	-	03/2009 -	-	-	0/0
Total			20,025.99 -	21,450.84	5,311.14				0/1
<u>Urban Development</u>									
564	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	79.96	04/2009 -	01/2011	21(O)	0/0
565	DELHI MRTS PHASE-II PROJECT - [280100002]DMRC,Delhi	08/2005	8,676.00 8,605.36	18,894.36	17,548.44	06/2010 -	06/2011	12(O)	0/10
566	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	03/2013	15(O)	6/6
Total			15,185.18 -	30,684.66	19,895.97				6/16
<u>Water Resources</u>									
567	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
Total			542.90 -	1,187.00	35.49				0/0
Grand Total			632,243.96	758,171.90	332,247.24				864/2190

Sector wise current status of projects on theFlash Report

Telecommunications


I. Current Status:

Number of Projects	41
Number of Projects On Schedule	1
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning 38

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 41 projects, 1 project are on schedule and 2 projects are delayed .38 projects do not have fixed dates of commissioning.

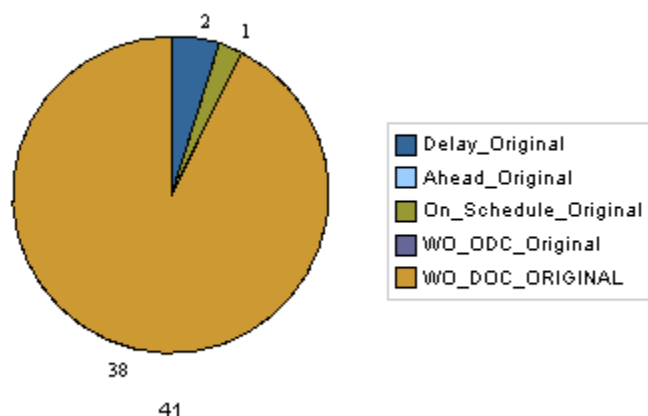

III. Investment Scenario

The Total Original cost of implementation of 41 projects when sanctioned, was of the order of Rs. 20025.99 crore but this was subsequently revised to Rs. 21450.84 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till May, 2011 is Rs. 5311.14 crore, which is 24.8% of the revised cost of the projects.

Figures are in Rs. Crore

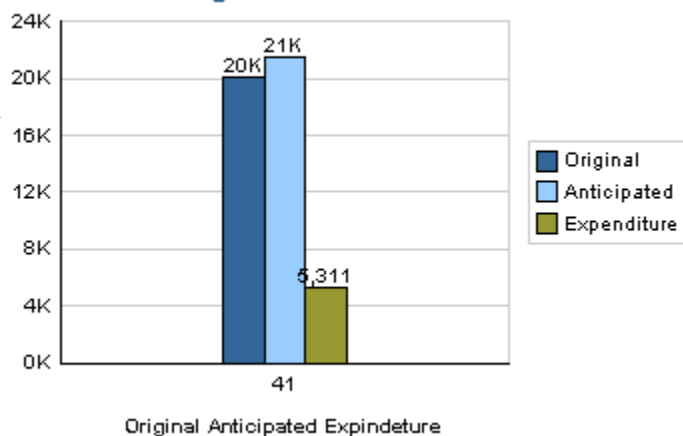

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	23
Number of Projects On Schedule	6
Number of Projects Delayed	13

Number of Projects Without Date Of Commissioning	4
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 23 projects, 6 projects are on schedule and 13 projects are delayed .4 projects do not have fixed dates of commissioning.

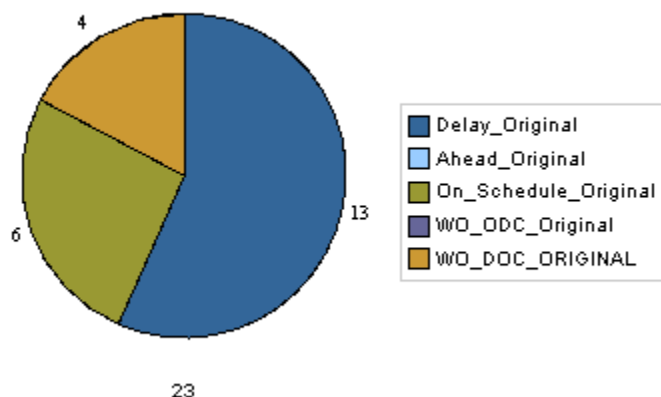

III. Investment Scenario

The Total Original cost of implementation of 23 projects when sanctioned, was of the order of Rs. 14464.19 crore but this was subsequently revised to Rs. 15317.65 crore implying a cost overrun of 5.9%. The expenditure incurred on these projects till May, 2011 is Rs. 3150.17 crore, which is 20.6% of the revised cost of the projects.

Figures are in Rs. Crore

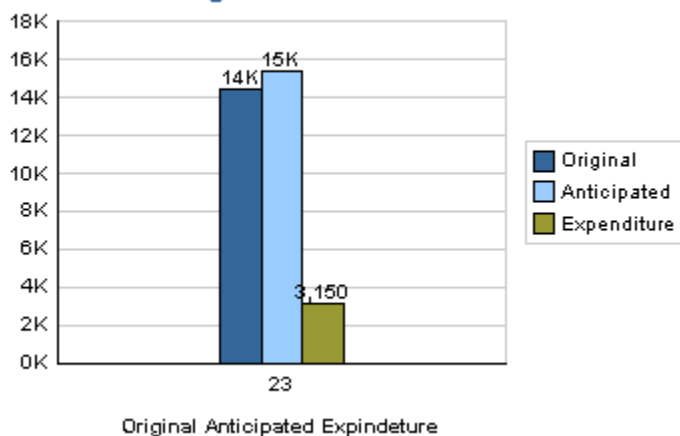

Sector wise current status of projects on theFlash Report


Road Transport & Highways

I. Current Status:

Number of Projects	128
Number of Projects On Schedule	34
Number of Projects Delayed	94

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 128 projects, 34 projects are on schedule and 94 projects are delayed .

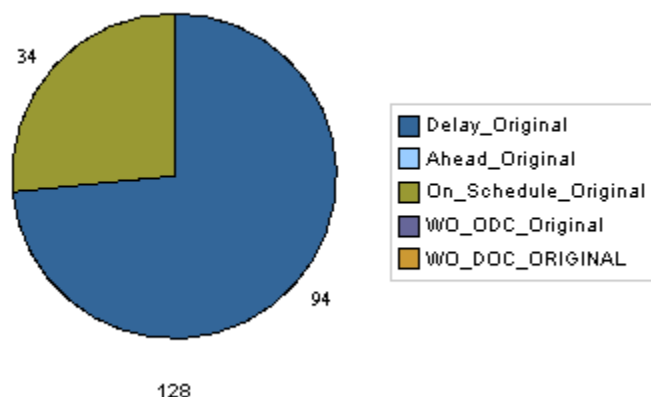

III. Investment Scenario

The Total Original cost of implementation of 128 projects when sanctioned, was of the order of Rs. 61806.58 crore but this was subsequently revised to Rs. 63269.99 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till May, 2011 is Rs. 44209.21 crore, which is 69.9% of the revised cost of the projects.

Figures are in Rs. Crore

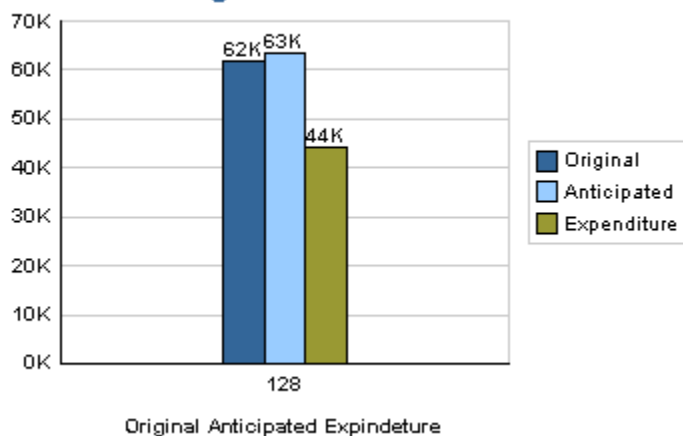

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	136
Number of Projects On Schedule	15
Number of Projects Delayed	25
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	28
Number of Projects Without Date Of Commissioning	65

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 136 projects, 3 projects are ahead of schedule, 15 projects are on schedule and 25 projects are delayed. 65 projects do not have fixed dates of commissioning. 28 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

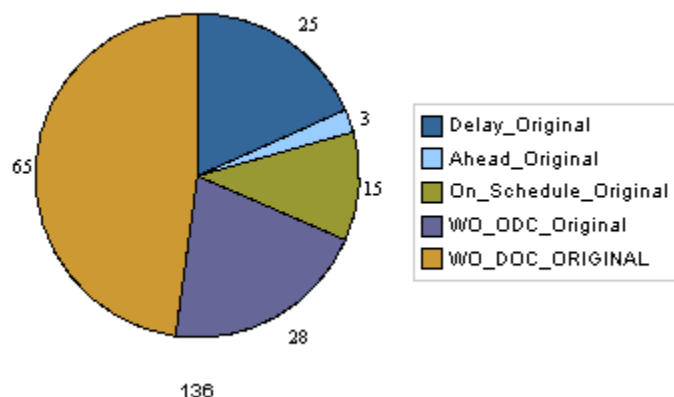

III. Investment Scenario

The Total Original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 66442.61 crore but this was subsequently revised to Rs. 122507.27 crore implying a cost overrun of 84.4%. The expenditure incurred on these projects till May, 2011 is Rs. 52515.94 crore, which is 42.9% of the revised cost of the projects.

Figures are in Rs. Crore

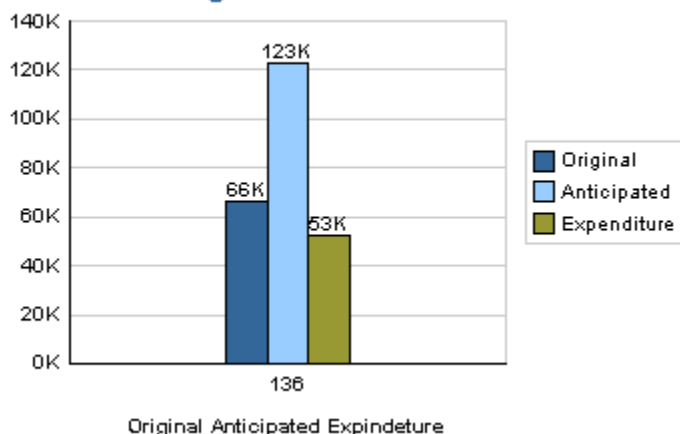

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	85
Number of Projects On Schedule	34
Number of Projects Delayed	43

Number of Projects Without Original Date of Commissioning	7
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 85 projects, 34 projects are on schedule and 43 projects are delayed .1 project do not have fixed dates of commissioning.7 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

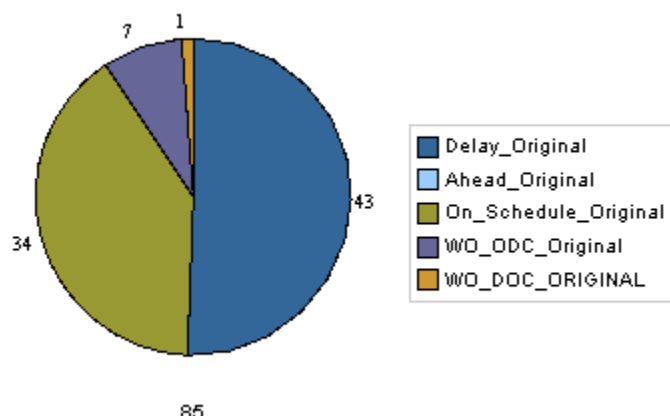

III. Investment Scenario

The Total Original cost of implementation of 85 projects when sanctioned, was of the order of Rs. 178267.7 crore but this was subsequently revised to Rs. 183786.71 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till May, 2011 is Rs. 83857.9 crore, which is 45.6% of the revised cost of the projects.

Figures are in Rs. Crore

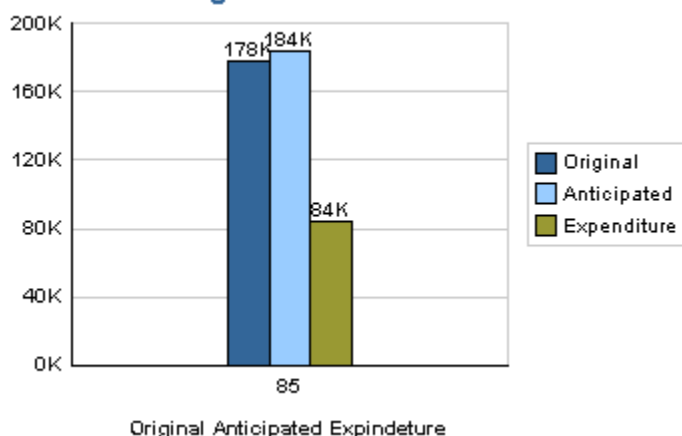

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	74
Number of Projects On Schedule	24
Number of Projects Delayed	32
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	10
Number of Projects Without Date Of Commissioning	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 74 projects, 4 projects are ahead of schedule, 24 projects are on schedule and 32 projects are delayed. 4 projects do not have fixed dates of commissioning. 10 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

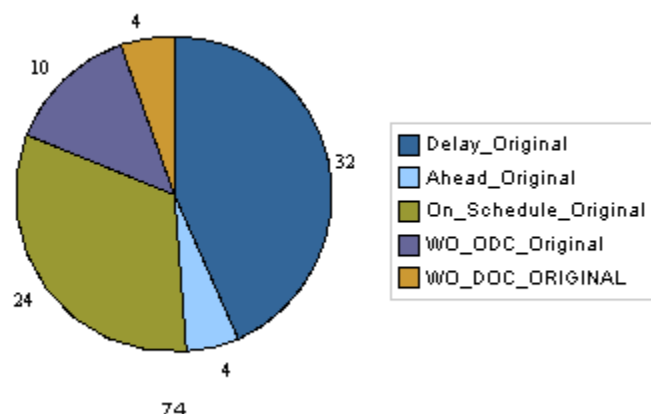

III. Investment Scenario

The Total Original cost of implementation of 74 projects when sanctioned, was of the order of Rs. 165845.81 crore but this was subsequently revised to Rs. 174838.18 crore implying a cost overrun of 5.4%. The expenditure incurred on these projects till May, 2011 is Rs. 60887.36 crore, which is 34.8% of the revised cost of the projects.

Figures are in Rs. Crore

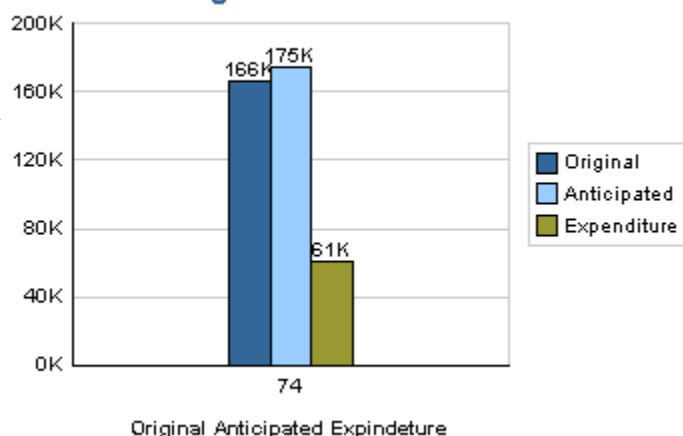

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	15
Number of Projects On Schedule	2
Number of Projects Delayed	4

Number of Projects Without Original Date of Commissioning	9
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 2 projects are on schedule and 4 projects are delayed .9 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

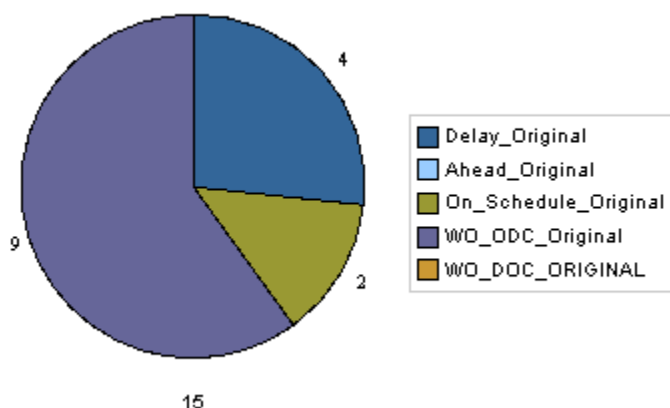

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 41398.4 crore but this was subsequently revised to Rs. 68476.43 crore implying a cost overrun of 65.4%. The expenditure incurred on these projects till May, 2011 is Rs. 26386.24 crore, which is 38.5% of the revised cost of the projects.

Figures are in Rs. Crore

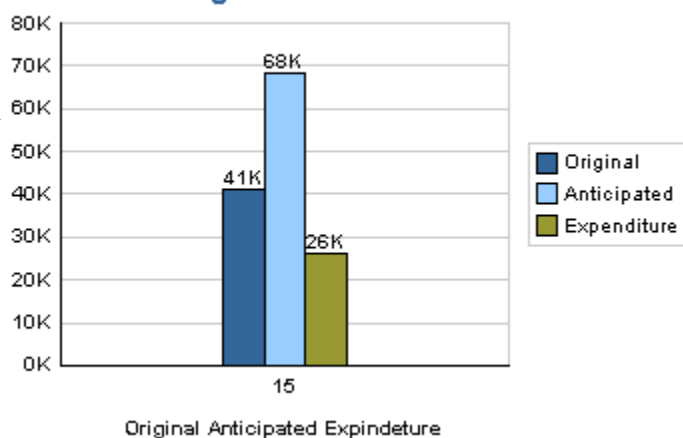

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	4
Number of Projects Delayed	1

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 4 projects are on schedule and 1 project are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

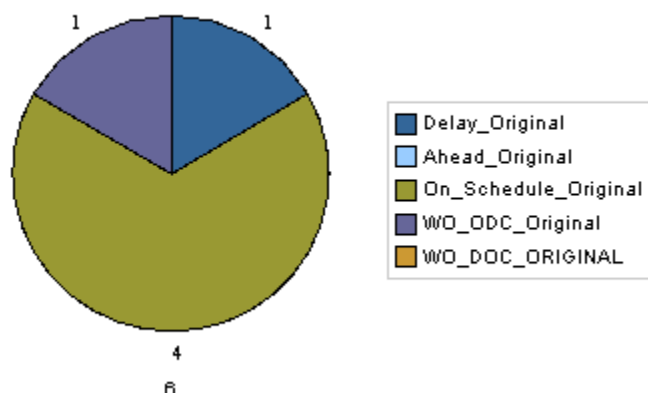

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till May, 2011 is Rs. 453.87 crore, which is 8.5% of the revised cost of the projects.

Figures are in Rs. Crore

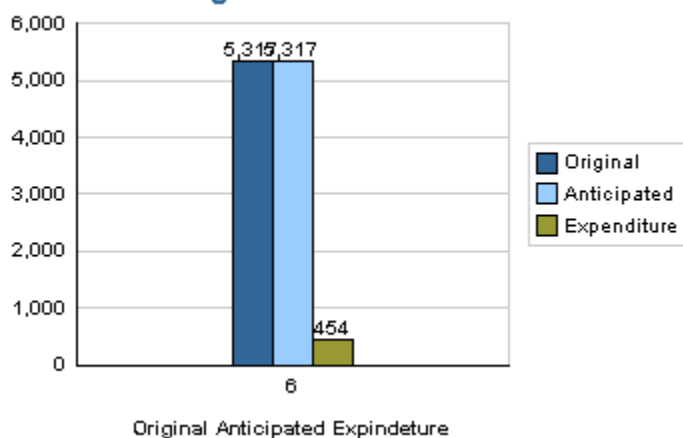

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	45
Number of Projects On Schedule	23
Number of Projects Delayed	20

Number of Projects Without Original Date of Commissioning	2
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 45 projects, 23 projects are on schedule and 20 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

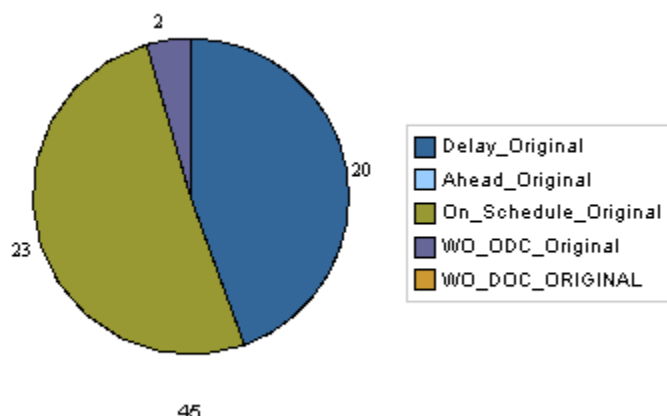

III. Investment Scenario

The Total Original cost of implementation of 45 projects when sanctioned, was of the order of Rs. 25504.15 crore but this was subsequently revised to Rs. 28789.58 crore implying a cost overrun of 12.9%. The expenditure incurred on these projects till May, 2011 is Rs. 10716.48 crore, which is 37.2% of the revised cost of the projects.

Figures are in Rs. Crore

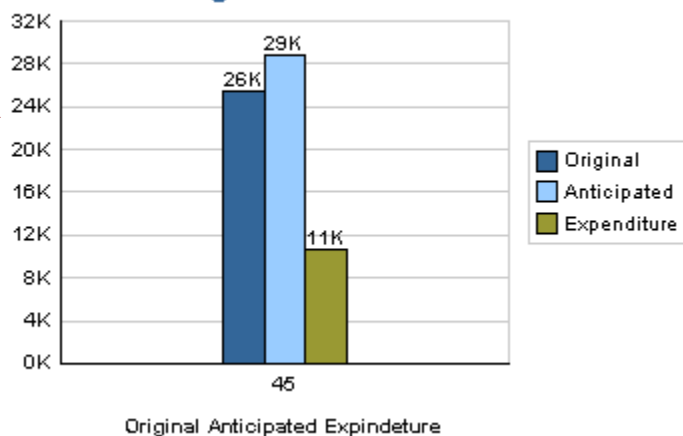

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 3 projects are delayed .

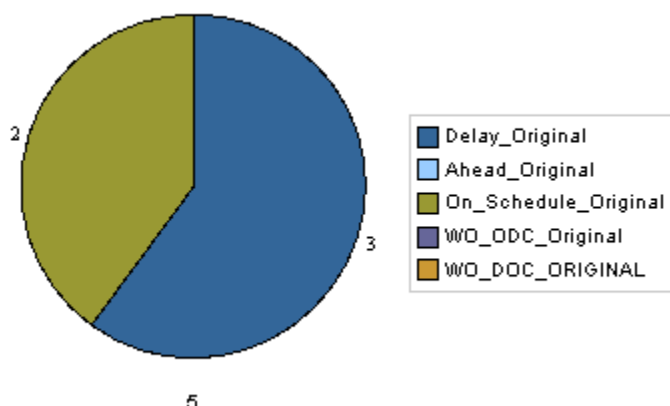

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 4123.24 crore but this was subsequently revised to Rs. 4078.13 crore implying a cost overrun of -1.1%. The expenditure incurred on these projects till May, 2011 is Rs. 2439.31 crore, which is 59.8% of the revised cost of the projects.

Figures are in Rs. Crore

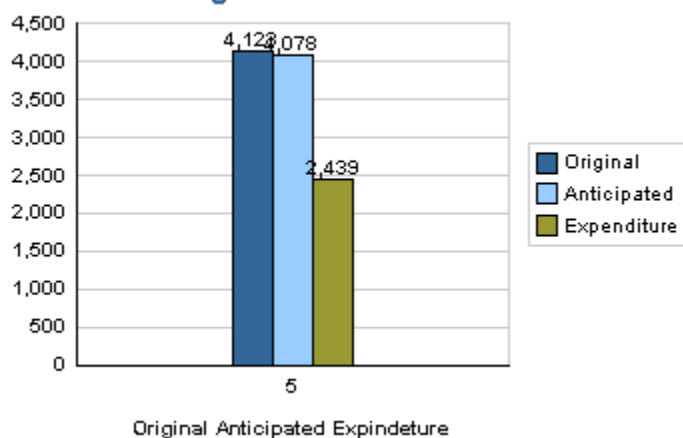

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

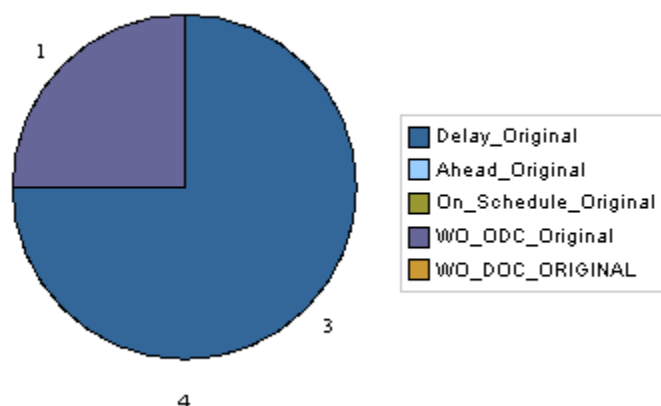

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till May, 2011 is Rs. 18405.16 crore, which is 54% of the revised cost of the projects.

Figures are in Rs. Crore

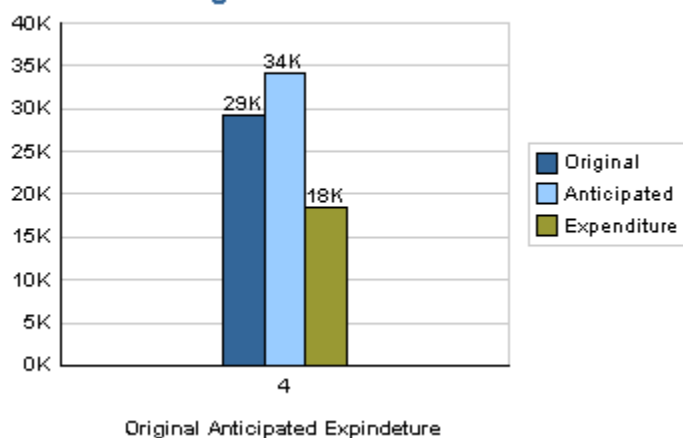

ANNEXURES

STATE WISE SUMMARY OF ONGOING PROJECTS AS ON				31.05.2011	
S.No.	State	No. Of Projects	Original Cost (In Crores)	Anticipated Cost (In Crores)	Cummulative Expenditure (In Crores)
1	Andhra Pradesh	29	25,504.66	31,102.02	14,940.64
2	Arunachal Pr.	4	9,512.22	9,610.51	6,749.52
3	Assam	35	17,934.78	23,395.04	12,244.38
4	Bihar	26	20,172.29	24,052.69	16,784.40
5	Chhatisgarh	19	22,504.86	37,937.78	14,819.22
6	Delhi	2	8,925.00	19,123.77	17,614.64
7	Goa	1	204.73	204.73	32.50
8	Gujarat	25	19,256.56	20,222.98	4,625.72
9	Haryana	10	5,337.83	7,054.75	4,187.72
10	Himachal Pr.	7	15,023.26	15,105.54	11,711.49
11	J & K	8	8,293.37	18,455.56	11,155.72
12	Jharkhandd	20	9,431.85	14,087.17	5,619.63
13	Karnataka	27	31,887.97	39,126.52	14,355.53
14	Kerala	7	5,852.00	7,099.11	5,405.28
15	Madhya pradesh	24	12,799.72	12,404.21	4,157.25
16	Maharashtra	50	71,427.08	85,526.48	33,427.57
17	Mizoram	2	988.06	3,343.04	231.22
18	Multi State	109	130,900.42	140,220.70	46,286.75
19	Nagaland	1	850.00	850.00	7.98
20	Orissa	26	51,981.30	59,843.85	15,721.80
21	Punjab	9	5,163.69	6,509.65	3,202.52
22	Rajasthan	16	13,438.03	14,167.15	8,424.99
23	Sikkim	2	1,648.88	3,644.86	189.25
24	Tamil Nadu	34	42,994.48	52,130.59	34,747.42
25	Tripura	3	1,522.39	2,053.24	301.19
26	Uttar Pradesh	30	10,806.22	12,941.32	8,113.85
27	Uttaranchal	6	5,799.14	8,478.47	3,022.96
28	West Bengal	26	23,897.33	29,393.89	9,585.17
29		9	58,185.84	60,086.28	24,580.93
Total	All States	567	632,243.96	758,171.90	332,247.24

**LIST OF PROJECTS WITHOUT ORIGINAL DATE OF
COMMISSIONING AS ON 01.06.2011**

SN	PROJECTS NAME	SECTOR	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
1	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALLE	Atomic Energy	N.A.	04/2011	04/2012
2	PENGANGA OC	Coal	N.A.	N.A.	03/2014
3	TUTICORIN THERMAL POWER PROJECT	Coal	N.A.	N.A.	10/2012
4	THAL AMMONIA REVAMP PROJECT	Fertilisers	N.A.	11/2011	11/2011
5	ASSAM GAS CRACKER PROJECT	Petroleum	N.A.	N.A.	04/2012
6	BAWANA NANGAL PIPE LINE PROJECT	Petroleum	N.A.	12/2011	12/2011
7	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT	Petroleum	N.A.	N.A.	02/2013
8	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pipeline)	Petroleum	N.A.	N.A.	08/2013
9	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery	Petroleum	N.A.	N.A.	01/2013
10	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	N.A.	04/2013	04/2013
11	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES AT PARADIP	Petroleum	N.A.	N.A.	06/2012
12	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	Petroleum	N.A.	06/2011	06/2011
13	PARADIP REFINERY PROJECT	Petroleum	N.A.	N.A.	11/2012
14	PARADIP-RAIPUR-SAMBALPUR- RANCHI PIPELINE	Petroleum	N.A.	09/2012	09/2012
15	BARH STPP STAGE -II	Power	N.A.	N.A.	10/2013
16	BONGAIGAON THERMAL POWER PROJECT	Power	N.A.	N.A.	10/2013
17	MOUDA STPP	Power	N.A.	N.A.	11/2012
18	RIHAND STTP STAGE-III (2X500MW)	Power	N.A.	N.A.	12/2012
19	SIMHADRI STPP STAGE -II	Power	N.A.	N.A.	12/2011
20	Tapovan-Vishnugad HEP (4x130MW)	Power	N.A.	N.A.	06/2014
21	VINDHYACHAL STTP STAGE-IV	Power	N.A.	N.A.	12/2012
22	ANGAMALI-SABARIMALA (N.L.)(SR)	Railways	N.A.	N.A.	03/2012
23	CALICUT-MANGALORE (DL) (SR)	Railways	N.A.	N.A.	07/2011
24	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT	Railways	N.A.	N.A.	03/2012
25	CHHINDWARA - NAGPUR (GC)(SECR)	Railways	N.A.	N.A.	12/2013
26	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	N.A.	N.A.	03/2012
27	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR	Railways	N.A.	N.A.	12/2012
28	DAUSA-GANGAPUR CITY(NL),NWR	Railways	N.A.	N.A.	03/2013
29	DEOGHAR - SULTANGANJ (INL), ER	Railways	N.A.	12/2012	N.A.
30	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	Railways	N.A.	06/2013	06/2013
31	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	Railways	N.A.	N.A.	03/2015
32	HARIDASPUR-PARADEEP(NL)	Railways	N.A.	09/2009	12/2011
33	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU	Railways	N.A.	N.A.	03/2012

34	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	N.A.	N.A.	03/2012
35	JIND-SONEPAT (NL),NR	Railways	N.A.	03/2012	12/2012
36	KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR)	Railways	N.A.	03/2012	03/2012
37	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	N.A.	N.A.	02/2012
38	KHURDA ROAD-BOLANGIR(NL)ECOR	Railways	N.A.	N.A.	08/2011
39	KOSI BRIDGE (NL), ECR	Railways	N.A.	N.A.	12/2012
40	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	N.A.	12/2011	03/2012
41	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	N.A.	03/2011	03/2012
42	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP	Railways	N.A.	12/2010	06/2011
43	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	N.A.	N.A.	03/2012
44	NANGALDAM-TALWARA(NL),NR	Railways	N.A.	07/2012	07/2012
45	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	N.A.	N.A.	03/2012
46	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	N.A.	N.A.	03/2013
47	TALCHER-BIMALAGARH(NL)(ECOR)	Railways	N.A.	N.A.	12/2011
48	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	Railways	N.A.	12/2009	02/2012
49	VIRAMGAM-BHILDI(WR),GC	Railways	N.A.	03/2013	03/2013
50	330 TPH BOILER-6 AND AUXILIARY SYSTEM	Steel	N.A.	N.A.	09/2011
51	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	N.A.	N.A.	10/2011
52	Augmentation of Iron Ore Storage in RMHP	Steel	N.A.	05/2012	05/2012
53	Bailadila Iron Ore Deposit- 11B(NMDC)	Steel	N.A.	N.A.	03/2012
54	COKE OVEN BATTERY NO. 4 PHASE-II	Steel	N.A.	10/2012	10/2012
55	EXPANSION OF BHILAI STEEL PLANT	Steel	N.A.	03/2013	03/2013
56	EXPANSION OF BOKARO STEEL PLANT	Steel	N.A.	12/2011	12/2011
57	EXPANSION OF IISCO STEEL PLANT	Steel	N.A.	12/2011	12/2011
58	INSTALLATION OF 700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI	Steel	N.A.	N.A.	07/2011

LIST OF PROJECTS WITHOUT DATE OF COMMISSIONING AS ON 01.06.2011

SN	PROJECT NAME	SECTOR	DOC ORIGINAL	DOC REVISED	DOC ANTICIPATED
4	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)	Petroleum	05/2008	07/2010	04/2011
1	CAPACITY EXP. CUM MODERNISATION PH-II	Petroleum	12/2009	N.A.	12/2010
2	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE I	Petroleum	03/2012	N.A.	N.A.
3	JHAJJAR HISSAR PIPE LINE PROJECT	Petroleum	10/2010	N.A.	N.A.
5	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	Power	12/2007	12/2009	N.A.
19	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	12/2009	03/2011	N.A.
8	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	Railways	N.A.	N.A.	N.A.
32	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	Railways	N.A.	11/2010	N.A.
35	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)	Railways	03/2009	12/2008	12/2010
26	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	N.A.	03/2011	03/2011
9	AMRAVATI-NARKHER NL(CR)	Railways	06/1999	03/2011	N.A.
61	BANGLORE - SATYAMANGALAM (NL)(SWR)	Railways	N.A.	N.A.	N.A.
15	BARDHAMAN-KATWA, ER (GC)	Railways	12/2010	03/2011	N.A.
18	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	Railways	03/2004	N.A.	N.A.
33	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION	Railways	N.A.	N.A.	12/2010
70	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR)	Railways	03/2011	03/2011	N.A.
40	BILASPUR-URKURA (DL)	Railways	N.A.	03/2009	03/2011
38	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	Railways	12/2012	N.A.	N.A.
55	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	N.A.	N.A.	N.A.
16	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1995	N.A.	N.A.
48	GADWAL - RAICHUR (NL), SCR	Railways	N.A.	02/2011	N.A.
50	GOELKERA-MANOHARPUR,(LD)(SER)	Railways	02/2006	N.A.	N.A.
28	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	Railways	N.A.	N.A.	N.A.
49	GONDIA-JABALPUR(GC),(SECR)	Railways	03/1998	N.A.	N.A.
64	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	N.A.	N.A.	N.A.
30	HATHUA-BHATNI (N L) (NER)	Railways	N.A.	N.A.	N.A.
62	HUBLI-ANKOLA(NL),SWR	Railways	N.A.	N.A.	N.A.
7	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	06/2007	N.A.	N.A.
27	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	N.A.	N.A.	N.A.
59	KARUR-SALEM(NL),SR	Railways	N.A.	N.A.	N.A.

22	KATIHAR - JOGBANI (GC)(NEFR)	Railways	N.A.	12/2010	N.A.
11	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	Railways	N.A.	N.A.	N.A.
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	N.A.	03/2009	12/2010
21	KISHANGANJ JALALGARH, NL, NEFR	Railways	N.A.	N.A.	N.A.
10	KODERMA GIRIDH (NL), ECR	Railways	N.A.	N.A.	N.A.
12	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	07/2005	N.A.	N.A.
13	KODERMA-TILAIYA (NL), ECR	Railways	N.A.	N.A.	N.A.
45	KOTLPALLI-NARASAPUR (NL) (SCR)	Railways	N.A.	N.A.	N.A.
63	KOTTUR-HARIHAR(NL),(SWR)	Railways	N.A.	03/2011	N.A.
20	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	05/2008	03/2011	N.A.
46	MACHERLA-NALGONDA(NL)(SCR)	Railways	07/2008	N.A.	N.A.
29	MAHARAJGANJ-MASRAKH (NL) - NER	Railways	N.A.	N.A.	N.A.
44	MANOHARABAD-KOTHPALL NEW LINE(SCR)	Railways	N.A.	N.A.	N.A.
56	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTHAMPALLI	Railways	N.A.	N.A.	N.A.
47	MUNEERABAD-MAHABOBNAGAR(NL),SCR	Railways	N.A.	N.A.	N.A.
23	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	Railways	N.A.	N.A.	N.A.
25	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	Railways	N.A.	N.A.	N.A.
24	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR	Railways	N.A.	N.A.	N.A.
34	OBULAVARIPALLE-KRISHNAPATNAM(RVNL)	Railways	03/2008	06/2008	N.A.
43	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	03/2009	12/2009	03/2011
14	Pandabeswar-Chinpai doubling (ER)	Railways	N.A.	12/2010	N.A.
66	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	Railways	03/2008	10/2010	N.A.
57	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	Railways	N.A.	N.A.	N.A.
42	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	12/2007	03/2010	12/2010
36	RAJATGARH-BARANG(LD),ECOR	Railways	N.A.	02/2009	12/2010
68	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	Railways	03/1996	08/2009	N.A.
67	RAJPIPLA-ANKELASHWAR, WR (GC)	Railways	03/2011	N.A.	N.A.
65	RAMGANJMUUNDI-BHOPAL (NL),WCR	Railways	N.A.	N.A.	N.A.
51	RANCHI-LOHARDAGA(GC),SER	Railways	06/2004	04/2005	N.A.
39	RENIGUNTA-GUNTAKAL(RE)	Railways	04/2003	03/2010	N.A.
6	REWARI-ROHTAK (NL),NR	Railways	02/2010	02/2011	N.A.
52	RUPSA-BANGRIPOSI (GC)(SER)	Railways	03/1998	08/2005	N.A.
31	SRIGANGANAGAR-SARUPSAR (GC), NWR	Railways	N.A.	03/2011	N.A.
41	SUKINDA ROAD - ANGUL (NL)(ECOR)	Railways	02/2015	N.A.	N.A.
69	SURENDRANAGAR-BHAVNAGAR(GC),WR	Railways	03/2004	03/2010	N.A.
53	TIDIVANAM-NAGARI (NL)	Railways	N.A.	N.A.	N.A.
54	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	Railways	N.A.	N.A.	N.A.
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	N.A.	N.A.	N.A.
17	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	12/2006	08/2010	N.A.
58	VILLUPURAM-KATPADI (GC)(SR)	Railways	N.A.	N.A.	N.A.

74	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL	Shipping & Ports	10/2008	N.A.	N.A.
72	DEVELOPMENT OF COAL TERMINAL	Shipping & Ports	08/2010	N.A.	03/2011
71	DEVELOPMENT OF IRON ORE TERMINAL	Shipping & Ports	08/2010	N.A.	04/2011
73	SETHUSAMUDRAM SHIP CHANNEL PROJECT	Shipping & Ports	10/2008	N.A.	11/2010
95	Assam Telecom Circle, Phase-V.I, 2G & 3G	Telecommunication s	01/2009	N.A.	02/2011
104	ERP implementation in BSNL on Turnkey basis	Telecommunication s	10/2010	N.A.	04/2011
88	Execution of telecom network requirement of defence forces	Telecommunication s	03/2009	N.A.	N.A.
98	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06	Telecommunication s	10/2007	N.A.	N.A.
83	GSM equipment of 1100000Lines (2G) UP East Phase V.2 Telecom Circle	Telecommunication s	09/2010	N.A.	03/2011
112	GSM equipment of 1500000Lines (2G) 264700lines 3(G)Andhra Pradesh Phase V.1 Telecom Circle	Telecommunication s	01/2010	N.A.	02/2011
109	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle	Telecommunication s	11/2010	N.A.	03/2011
99	GSM equipment of 1700000Lines (2G) 234100 lines 3(G)Karnataka Phase V.1 Telecom Circle	Telecommunication s	10/2009	N.A.	03/2011
82	GSM equipment of 1867000Lines (2G) 383000 lines 3(G) GujaratPhase V.1 Telecom Circle	Telecommunication s	08/2009	N.A.	03/2011
77	GSM equipment of 1900000Lines (2G) 335500lines 3(G)kerala Phase V.1 Telecom Circle	Telecommunication s	01/2010	N.A.	02/2011
75	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	Telecommunication s	N.A.	03/2011	02/2011
80	GSM equipment of 200000Lines (2G) UP(West)Phase V.2 Telecom Circle	Telecommunication s	10/2009	N.A.	03/2011
90	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1	Telecommunication s	03/2009	N.A.	02/2011
101	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3G) PH-5.1	Telecommunication s	09/2009	N.A.	02/2010
111	GSM equipment of 375000Lines (2G) 75000lines 3(G) Kolkatta Phase V.1 Telecom Circle	Telecommunication s	06/2009	N.A.	01/2011
91	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1	Telecommunication s	12/2008	N.A.	02/2011
107	GSM equipment of 614000Lines (2G) 150000lines 3(G) Chennai TD Phase V.1 Telecom Circle	Telecommunication s	01/2010	N.A.	02/2011
92	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	Telecommunication s	03/2009	N.A.	02/2011
79	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle	Telecommunication s	03/2009	N.A.	N.A.
100	GSM equipment of 849862Lines (2G) 150138 lines 3(G) West Bengal Phase V.1 Telecom Circle	Telecommunication s	02/2009	N.A.	03/2011
87	GSM equipment of 900000Lines (2G) PunjabPhase V.2 Telecom Circle	Telecommunication s	09/2009	N.A.	03/2011
89	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G)PH-5	Telecommunication s	12/2008	N.A.	03/2011

76	GSM equipment of 945000Lines (2G) 225000lines 3(G) Bihar Phase V.1 Telecom Circle	Telecommunication s	10/2008	N.A.	02/2011
84	GSM equipment of 975000Lines (2G) 325000 lines 3(G) UP East Phase V.1 Telecom Circle	Telecommunication s	02/2010	N.A.	02/2011
93	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN UP(W)-PH-V.I	Telecommunication s	03/2009	N.A.	03/2011
102	Implementation of FTTH, the state of the art Access Network,procurement of gepon equipment	Telecommunication s	03/2010	N.A.	10/2010
78	Implementation of FTTH, the state of the art access network.Procurement of gpon equipmant	Telecommunication s	03/2010	N.A.	10/2010
97	MANAGED LEASED LINE NETWORK PH-VI	Telecommunication s	N.A.	N.A.	N.A.
103	NIB-II PROJECT RURAL BROADBAND	Telecommunication s	02/2008	N.A.	12/2010
105	Procurement of 10G (40 chl) DWDM equipment	Telecommunication s	03/2009	N.A.	N.A.
108	Procurement of 10G 40 CHL (12 chi equipped) DWDM equipment (SDCA level)	Telecommunication s	03/2010	N.A.	12/2010
110	Procurement of 2.5G DWDM equipment	Telecommunication s	03/2009	N.A.	12/2010
85	Procurement of DXC equipment	Telecommunication s	03/2010	N.A.	11/2010
96	Procurement of STM-1 SDH equipment	Telecommunication s	03/2010	N.A.	12/2010
81	Procurement of STM-16 ADM equipment	Telecommunication s	03/2010	N.A.	12/2010
86	Procurement of STM-16 MADM equipment	Telecommunication s	03/2010	N.A.	12/2010
106	PROJ.III OF NIB-II OF MESSAGING STORAGE	Telecommunication s	12/2005	N.A.	10/2010
94	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G)	Telecommunication s	06/2009	N.A.	02/2011
113	C/o office building for IDBI at bandra Kurla Complex,Mumbai	Urban Development	04/2009	N.A.	01/2011

List of Projects Where in Revised cost Estimates'(s) is Required as on 01.06.2011

SN	PROJECT NAME	SECTOR	COST ORIGINAL	COST REVISED	CUMMLU TIVE EXPENDI TURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	13171.00	0.00	13811.00
2	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	Petroleum	2305.30	700.00	2416.96
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	613.54	0.00	620.66
4	CHAMERA,STAGE-III (NHPC)	Power	1405.63	0.00	1609.35
5	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	Power	621.28	0.00	642.99
6	KOTESHWAR HEP(THDC)	Power	1301.56	0.00	2381.37
7	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	611.02	0.00	634.88
8	TESSTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	768.92	0.00	1319.23
9	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	108.00	214.09	217.89
10	AJMER-CHITTAURGARH -UDAIPUR-UMRA (GC),NWR	Railways	262.00	456.00	546.68
11	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	170.00	170.00	355.38
12	AMRAVATI-NARKHER NL(CR)	Railways	120.90	284.27	430.95
13	BANKURA - DAMODAR (GC) (SER)	Railways	111.90	0.00	379.62
14	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	200.80	0.00	237.62
15	BILASPUR-URKURA (DL)	Railways	151.52	0.00	294.96
16	CALICUT-MANGALORE (DL) (SR)	Railways	240.00	0.00	592.12
17	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	248.44	576.27	739.28
18	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR	Railways	156.00	0.00	164.50
19	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	343.17	0.00	373.46
20	ELECTRIFICATION OF MORADABAD-ROZA	Railways	129.17	0.00	165.75
21	GADWAL - RAICHUR (NL), SCR	Railways	92.63	108.91	221.51
22	GONDIA-JABALPUR(GC),(SECR)	Railways	386.30	0.00	524.23
23	GUNA-ETAWAH(NCR), NL	Railways	158.77	432.46	549.11
24	HASSAN-BANGALORE VIA SHRAVANA- BELGOLA(NL),SWR	Railways	295.00	0.00	452.09
25	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	409.00	625.30	809.39
26	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	233.00	335.77	526.52
27	KARUR-SALEM(NL),SR	Railways	155.55	0.00	533.40
28	KATIHAR - JOGBANI (GC)(NEFR)	Railways	100.00	492.98	716.20
29	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	Railways	78.23	0.00	82.96
30	KOTTUR-HARIHAR(NL),(SWR)	Railways	65.94	281.20	321.23
31	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	100.00	142.90	181.39
32	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	1676.31	0.00	2682.87
33	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	184.00	254.07	421.09
34	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	114.01	283.95	332.36
35	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	100.00	322.29	414.15
36	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	155.74	164.36	445.50

SN	PROJECT NAME	SECTOR	COST ORIGINAL	COST REVISED	CUMMLU TIVE EXPENDI TURE
37	PATNA GANGA BRIDGE (NL), ECR	Railways	624.47	0.00	908.13
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	124.43	407.78	465.90
39	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	Railways	148.61	0.00	256.44
40	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC)	Railways	280.00	0.00	662.50
41	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	1000.00	1500.00	2186.05
42	RAJATGARH-BARANG(LD),ECOR	Railways	166.16	0.00	228.80
43	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AND VERAVAL SOMNATH NL(WR)	Railways	112.53	320.66	507.39
44	RANCHI-LOHARDAGA(GC),SER	Railways	194.07	0.00	263.34
45	RENIGUNTA-GUNTAKAL(RE)	Railways	168.34	0.00	297.07
46	REWARI-ROHTAK (NL),NR	Railways	149.38	330.23	421.89
47	RUPSA-BANGRIPOSI (GC)(SER)	Railways	57.94	0.00	170.73
48	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canvession (NWR)	Railways	643.36	0.00	774.66
49	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	293.97	0.00	372.55
50	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	100.00	0.00	458.15
51	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	907.69	1032.76	2945.43
52	VILLUPURAM-KATPADI (GC)(SR)	Railways	175.00	0.00	538.29
53	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	367.49	0.00	453.68
54	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	190.00	0.00	227.00
55	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	Road Transport & Highways	193.00	0.00	324.40
56	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	Road Transport & Highways	217.00	0.00	345.60
57	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	Road Transport & Highways	565.00	0.00	1080.00
58	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	225.00	0.00	246.00
59	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	486.00	0.00	520.70
60	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	412.78	0.00	435.90

SN	PROJECT NAME	SECTOR	COST ORIGINAL	COST REVISED	CUMMLU TIVE EXPENDI TURE
61	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	275.00	0.00	288.10
62	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	600.24	0.00	665.50
63	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	Road Transport & Highways	227.00	0.00	381.70
64	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	273.00	0.00	476.60
65	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	Road Transport & Highways	210.00	0.00	672.30
66	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	340.00	0.00	411.00
67	JHANSI TO LALITPUR, NH-26	Road Transport & Highways	276.09	0.00	294.90
68	KASIA TO GORAKHPUR (NH-28)(NHAI)	Road Transport & Highways	242.00	0.00	371.00
69	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	275.00	0.00	275.30
70	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	240.00	0.00	242.60
71	KURALI-KIRATPUR, NH-21	Road Transport & Highways	309.00	0.00	553.60
72	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	225.00	0.00	248.40
73	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	Road Transport & Highways	629.00	0.00	910.00
74	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	Road Transport & Highways	359.00	0.00	772.80
75	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28	Road Transport & Highways	239.00	0.00	317.60
76	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	168.00	0.00	385.30

SN	PROJECT NAME	SECTOR	COST ORIGINAL	COST REVISED	CUMMLU TIVE EXPENDI TURE
77	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	200.00	0.00	249.80
78	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	441.00	0.00	825.30
79	NEW MANGALORE PORT NH-17 AND 48	Road Transport & Highways	196.50	0.00	228.80
80	NH CONNECTIVITY TO ICTT VALLARPADAEU NH - SH	Road Transport & Highways	557.00	0.00	930.90
81	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	1108.00	0.00	2372.00
82	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	229.00	0.00	324.70
83	PONDICHERY - TINDIVANAU NH-66	Road Transport & Highways	285.00	0.00	355.80
84	PURNEA-GOYAKOTA SEC.(EW) (NS AND EW-PH-I) KM.419-KM.447, NH-31	Road Transport & Highways	205.73	0.00	247.70
85	RINGBUNDS TO JHAJHANPUR (BR-6)	Road Transport & Highways	340.00	0.00	548.10
86	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	151.30	0.00	166.90
87	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	941.00	0.00	1803.00
88	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	157.47	0.00	171.00
89	SITAPUR-LUCKNOW	Road Transport & Highways	322.00	0.00	553.70
90	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	245.00	0.00	462.20
91	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	1693.75	0.00	2339.00
92	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	280.00	0.00	580.00

SN	PROJECT NAME	SECTOR	COST ORIGINAL	COST REVISED	CUMMLU TIVE EXPENDI TURE
93	THRISSUR TO ANGAMALI (NH-47)	Road Transport & Highways	312.50	0.00	598.90
94	TRICHY - DINDIGUAL NH-45	Road Transport & Highways	576.00	0.00	653.50
95	TRICHY - KORUR NH-67	Road Transport & Highways	516.00	0.00	548.70
96	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	227.00	0.00	357.50
97	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	295.00	0.00	622.90
98	GSM equipment of 900000Lines (2G) PunjabPhase V.2 Telecom Circle	Telecommuni cations	241.49	0.00	480.57
99	DELHI MRTS PHASE-II PROJECT	Urban Development	8676.00	8605.36	17548.44

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
<u>Civil Aviation</u>								
C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI, West Bengal	08/2008	1,942.51	1,942.51	1,158.51	05/2011	08/2011	3(O)	0/0
D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE(K1) - [N04000038]AAI, Tamil Nadu	08/2008	1,273.00	1,273.00	835.91	01/2011	10/2011	9(O)	0/0
Construction of New International Terminal Building - [N04000069]AAI, Goa	05/2010	204.73	204.73	32.50	05/2012	05/2012	0(O)	0/0
C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI, Sikkim	01/2009	309.40	264.29	136.56	01/2011	06/2012	17(O)	0/0
GAGAN PROJECT - [N04000065]AAI, Multi State	09/2008	393.60	393.60	275.83	06/2013	06/2013	0(O)	0/0
<u>Coal</u>								
ANANTA OC EXPANSION PH-III - [N06000067]MCL, Orissa	08/2008	207.28	207.28	38.29	03/2012	03/2012	0(O)	0/0
PENGANGA OC - [N06000066]WCL,	10/2008	339.77	339.77	0.10	-	03/2014	-	0/0
KARMA OCP - [N06000088]CCL, Jharkhand	06/2009	162.46	162.46	25.21	03/2014	03/2014	0(O)	0/0
<u>Fertilisers</u>								
CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL, Madhya pradesh	09/2008	325.00	325.00	-	07/2011	07/2011	0(O)	0/0
CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL, Madhya pradesh	09/2008	438.00	438.00	-	07/2011	07/2011	0(O)	0/0
<u>Steel</u>								
EXPENSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Orissa	09/2008	6,133.00	11,812.00	1,253.17	02/2011	03/2013	25(O)	0/0
1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00	572.00	-	04/2013	04/2013	0(O)	0/0
7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55	898.55	-	05/2013	05/2013	0(O)	0/0
<u>Petroleum</u>								
CAPACITY EXP. CUM MODERNISATION PH-II - [N16000080]BPCL, Kerala	09/2009	2,591.80	3,941.41	3,252.92	12/2009	12/2010	12(O)	0/0
Pipeline Replacement project-2 - [N16000111]ONGC, Multi State	12/2007	2,553.28	3,796.21	3,614.84	05/2011	05/2011	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91 1,646.39	1,690.13	1,577.70	09/2009 -	06/2011	21(O)	0/0
HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70 -	706.70	578.60	04/2010 -	06/2011	14(O)	0/0
NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08 -	305.08	229.89	04/2011 -	06/2011	2(O)	0/0
REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40 -	304.40	227.20	12/2010 -	06/2011	6(O)	0/0
North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	411.26	03/2011 05/2011	06/2011	1(R3)	0/0
Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54 -	727.88	620.66	12/2010 -	06/2011	6(O)	0/0
MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF - [N16000040]IOCL, Assam	04/2008	293.60 -	293.60	219.75	12/2009 -	07/2011	19(O)	0/0
CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	299.00	198.79	12/2010 08/2011	08/2011	0(R3)	0/0
RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 -	756.00	637.09	12/2011 -	09/2011	-3(O)	0/0
HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC, Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL, Gujarat	02/2009	267.00 -	267.00	160.00	09/2012 -	10/2011	-11(O)	0/0
DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL, Gujarat	02/2009	250.00 349.00	250.00	169.28	03/2013 -	12/2011	-15(O)	0/0
CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.29	09/2011 -	12/2011	3(O)	0/0
MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00 12,160.26	12,160.26	5,898.46	01/2012 -	01/2012	0(O)	0/0
MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21 -	162.12	58.26	03/2009 -	02/2012	35(O)	0/0
OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	447.73	09/2011 03/2012	03/2012	0(R3)	0/0
SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL, Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,113.55	05/2010 05/2012	05/2012	0(R3)	0/0
DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,093.65	09/2010 03/2012	05/2012	2(R3)	0/0
REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	12.28	05/2010 04/2012	05/2012	1(R3)	0/0
DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 -	1,436.21	52.56	07/2010 05/2012	05/2012	0(R3)	0/0
DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,113.85	08/2010 03/2012	06/2012	3(R3)	0/0
ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	466.18	06/2012 -	06/2012	0(O)	0/0
INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	663.21	- -	06/2012	-	6/9
Wind Power Project - [N16000119]ONGC,Gujarat	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	50.26	04/2011 -	07/2012	15(O)	0/0
Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	289.60	07/2012 -	07/2012	0(O)	0/0
Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	45.06	08/2012 -	08/2012	0(O)	0/0
MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,003.05	09/2012 -	09/2012	0(O)	0/0
Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	15.78	09/2012 -	09/2012	0(O)	0/0
ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	1,797.35	49.86	12/2011 -	01/2013	13(O)	0/0
Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	01/2013 -	01/2013	0(O)	0/0
IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	218.08	03/2006 03/2013	03/2013	0(R3)	6/6
MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,653.89	05/2010 03/2013	03/2013	0(R3)	0/0
ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	281.62	03/2013 -	03/2013	0(O)	0/0
Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	-	03/2013 -	03/2013	0(O)	0/0
Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	1.69	- -	08/2013	-	0/0
Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
Wax Project - [N16000101]NRL,Assam	08/2010	576.60	576.60	1.74	02/2014	02/2014	0(O)	0/0
Petrochemical Complex-II - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	85.38	02/2014	02/2014	0(O)	0/0
Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	384.00	09/2011 03/2012	09/2011	-6(R3)	0/0
JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 6,652.22	6,652.22	0.80	03/2012	-	-	0/0
Power								
TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]PGCIL,Multi State	12/2008	204.07	204.07	110.58	06/2011	06/2011	0(O)	0/0
TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE - [N18000059]PGCIL,Madhya pradesh	02/2009	276.61	276.61	197.24	06/2011	06/2011	0(O)	0/0
CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,609.35	08/2010	08/2011	12(O)	0/0
EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]PGCIL,Himachal Pr.	09/2007	262.10	262.10	163.60	09/2010	08/2011	11(O)	0/0
TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	227.03	210.01	05/2011 05/2011	09/2011	4(R3)	0/0
EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	132.47	06/2010	09/2011	15(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	49.80	11/2011	11/2011	0(O)	0/0
PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,461.01	10/2010	12/2011	14(O)	0/0
URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,451.77	11/2009	12/2011	25(O)	0/0
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37	297.37	289.14	07/2011	12/2011	5(O)	0/0
WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	229.52	02/2012	02/2012	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	31.50	02/2012	02/2012	0(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	143.12	08/2011	02/2012	6(O)	0/0
TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	204.48	07/2010 02/2012	02/2012	0(R3)	0/0
SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	60.47	07/2011	02/2012	7(O)	0/0
System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	64.84	04/2012	04/2012	0(O)	0/0
NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	634.88	08/2010	06/2012	22(O)	0/0
765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	274.00	06/2012	06/2012	0(O)	0/0
IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	101.79	06/2012	06/2012	0(O)	0/0
System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	6.89	06/2012	06/2012	0(O)	0/0
SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,631.54	08/2012	08/2012	0(O)	0/0
765 KV POOLING STATION & NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	3,758.75	08/2012	08/2012	0(O)	0/0
System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	275.04	08/2012	08/2012	0(O)	0/0
TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	1,722.37	10/2012	10/2012	0(O)	0/0
MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	111.94	10/2012	10/2012	0(O)	0/0
INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	11.23	10/2012	10/2012	0(O)	0/0
TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	264.04	11/2012	11/2012	0(O)	0/0
NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	202.20	11/2012	11/2012	0(O)	0/0
EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	85.21	11/2012	11/2012	0(O)	0/0
TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	953.10	09/2009	12/2012	39(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,248.33	12/2012	12/2012	0(O)	0/0
Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	197.77	12/2012	12/2012	0(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	25.54	01/2013	01/2013	0(O)	0/0
Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	17.35	01/2013	01/2013	0(O)	0/0
WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	337.28	09/2010	03/2013	30(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	249.06	11/2011	03/2013	16(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	233.23	11/2011	03/2013	16(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	115.67	02/2012	03/2013	13(O)	0/0
765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	787.90	02/2012	03/2013	13(O)	0/0
765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	216.15	05/2012	03/2013	10(O)	0/0
TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	99.43	03/2013	03/2013	0(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	62.92	04/2013	04/2013	0(O)	0/0
SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VELLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	8.70	04/2013	04/2013	0(O)	0/0
TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	66.06	01/2012	07/2013	18(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	33.37	07/2013	07/2013	0(O)	0/0
TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	54.88	08/2013	08/2013	0(O)	0/0
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	15.15	08/2013	08/2013	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	122.97	08/2013 -	08/2013	0(O)	0/0
TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	123.79	11/2011 -	09/2013	22(O)	0/0
Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	55.83	11/2013 -	11/2013	0(O)	0/0
TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	2,743.19	210.01	12/2013 -	12/2013	0(O)	0/0
TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	-	03/2014 -	03/2014	0(O)	0/0
NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	2,477.88	08/2013 -	09/2014	13(O)	0/0
TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	-	01/2015 -	01/2015	0(O)	0/0
KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67 -	3,642.04	731.24	07/2014 -	01/2016	18(O)	0/0
Railways								
RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	228.80	- 02/2009	12/2010	22(R1)	0/0
KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	211.90	144.65	- 03/2009	12/2010	21(R1)	0/0
RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	221.90	-	12/2007 03/2010	12/2010	9(R1)	0/0
ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73 399.73	399.50	-	03/2009 12/2008	12/2010	24(R1)	0/0
BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	200.80	237.62	- -	12/2010	-	0/0
BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	273.00	294.96	- 03/2009	03/2011	24(R1)	0/0
PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	329.70	-	03/2009 12/2009	03/2011	15(R1)	0/0
CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	592.12	- -	07/2011	-	0/0
KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	700.00	149.34	- -	08/2011	-	0/0
LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	170.00	181.39	03/2002 -	09/2011	114(O)	0/0
PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	154.69	02/2010 -	11/2011	21(O)	0/0
GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	549.11	03/1994 -	12/2011	213(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	429.49	445.50	02/2009 -	12/2011	34(O)	0/0
HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	194.26	- 09/2009	12/2011	27(R1)	0/0
TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	73.22	- -	12/2011	-	0/0
Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	203.03	03/2013 -	12/2011	-15(O)	0/0
KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,058.17	- -	02/2012	-	0/0
TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	383.65	- 12/2009	02/2012	26(R1)	0/0
Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	56.75	12/2011 -	02/2012	2(O)	0/0
PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	617.62	465.90	- -	03/2012	-	0/0
MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	421.09	- 12/2011	03/2012	3(R3)	0/0
KADUR-CHIKMAGALUR-SAKLSEHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	194.04	- 03/2012	03/2012	0(R3)	0/0
MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	414.15	- -	03/2012	-	0/0
JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	526.52	- -	03/2012	-	0/0
ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	550.00	69.02	- -	03/2012	-	0/0
MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	332.36	- 03/2011	03/2012	12(R3)	0/0
HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	180.10	- -	03/2012	-	0/0
CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	868.14	- -	03/2012	-	0/0
SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	185.70	03/2010 -	03/2012	24(O)	0/0
CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	164.50	- -	03/2012	-	0/0
ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	74.98	03/2012 -	03/2012	0(O)	0/0
ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	165.75	03/2011 -	03/2012	12(O)	0/0
TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	372.55	06/2005 07/2011	03/2012	8(R3)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves - [N22000106]NWR,Rajasthan	04/2007	643.36	803.39	774.66	03/2011	03/2012	12(O)	0/0
Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73	167.73	41.89	03/2012	03/2012	0(O)	0/0
Rattam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	603.04	28.78	03/2012	03/2012	0(O)	0/0
Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24	318.24	0.53	03/2012	03/2012	0(O)	0/0
HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	131.08	03/2007 03/2007	06/2012	63(R1)	0/0
NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	319.27	- 07/2012	07/2012	0(R3)	0/0
CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,404.00	563.89	- -	12/2012	-	0/0
CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	739.28	12/2012	12/2012	0(O)	0/0
BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	1,211.22	379.62	03/2005 12/2008	12/2012	48(R1)	0/0
JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	235.42	- 03/2012	12/2012	9(R3)	0/0
KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41	341.41	229.70	-	12/2012	-	0/0
RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	921.00	462.04	03/2009	12/2012	45(O)	0/0
PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.98	908.13	10/2007	12/2012	62(O)	0/0
BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	306.18	03/2010	12/2012	33(O)	0/0
Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52	207.52	97.88	12/2012	12/2012	0(O)	0/0
VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	141.42	- 03/2013	03/2013	0(R3)	0/0
DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	142.04	-	03/2013	-	0/0
RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 912.70	1,556.23	589.56	-	03/2013	-	0/0
Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13	350.81	-	03/2013	03/2013	0(O)	0/0
EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	113.48	- 06/2013	06/2013	0(R3)	0/0
Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97	189.97	48.77	12/2011	11/2013	23(O)	0/0
CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79	585.93	159.94	-	12/2013	-	0/0
Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90	223.01	81.30	12/2012	12/2013	12(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Multi State	04/1996	1,676.31 -	4,091.33	2,682.87	03/2009 -	12/2013	57(O)	0/0
RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,186.05	04/2008 03/2014	03/2014	0(R3)	0/0
NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	725.92	12/2008 -	03/2014	63(O)	0/0
AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.76	190.07	03/2014 -	03/2014	0(O)	0/0
BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,429.41	2.90	04/2014 -	03/2014	-1(O)	0/0
Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	3.51	03/2014 -	03/2014	0(O)	0/0
Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	18.22	03/2014 -	03/2014	0(O)	0/0
Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	151.97	03/2014 -	03/2014	0(O)	0/0
UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	93.63	03/2010 06/2014	06/2014	0(R3)	0/0
HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	159.96	- -	03/2015	-	0/0
MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	239.18	03/2014 -	03/2015	12(O)	0/0
SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.69	12/2015 -	03/2015	-9(O)	0/0
Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	7.98	03/2015 -	03/2015	0(O)	0/0
JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Multi State	04/2003	727.56 727.53	3,056.85	419.75	03/2011 03/2014	03/2016	24(R3)	0/0
New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	0.21	03/2014 -	03/2016	24(O)	0/0
New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	1.42	03/2016 -	03/2016	0(O)	0/0
New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	19.73	03/2016 -	03/2016	0(O)	0/0
New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	-	03/2016 -	06/2016	3(O)	0/0
UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	11,270.00	7,168.53	03/2001 -	12/2017	201(O)	0/0
FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 422.79	634.13	480.19	03/1995 -	-	-	0/0
RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN - [220100116]WR,Gujarat	04/1992	112.53 320.66	464.50	507.39	03/1996 08/2009	-	-	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	133.43	- -	-	-	0/0
DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	83.06	12/2012 -	-	-	0/0
AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	78.19	- -	-	-	0/0
HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	412.91	452.09	- -	-	-	0/0
GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	524.23	03/1998 -	-	-	0/0
KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	712.00	533.40	- -	-	-	0/0
HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	64.07	- -	-	-	0/0
MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	497.47	83.34	- -	-	-	0/0
MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,014.10	07/2005 -	-	-	0/0
VILLUPURAM-KATPADI (GC)(SR) - [220100251]SR,Tamil Nadu	02/2000	175.00 -	513.16	538.29	- -	-	-	0/0
KHAGARIA-KUSHESHWAR ASTHAN (NL)(ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	82.96	- -	-	-	0/0
JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	809.39	06/2007 -	-	-	0/0
REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	297.07	04/2003 03/2010	-	-	0/0
TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	458.15	- -	-	-	0/0
KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	297.46	- 12/2012	-	-	0/0
BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	70.29	- -	-	-	0/0
RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	205.74	- -	-	-	0/0
RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	170.73	03/1998 08/2005	-	-	0/0
SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	24.93	02/2015 -	-	-	0/0
MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.74	- -	-	-	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92	261.70	14.68	02/2006	-	-	0/0
OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	281.83	03/2008 06/2008	-	-	0/0
MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	160.00	-	-	-	0/0
DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	373.46	-	-	-	0/0
TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	20.45	-	-	-	0/0
TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	75.90	-	-	-	0/0
NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	34.57	-	-	-	0/0
KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	488.76	430.95	06/1999 03/2011	-	-	0/0
BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	164.54	03/2004	-	-	0/0
AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]NWR,Rajasthan	09/1996	262.00 456.00	567.23	546.68	-	-	-	0/0
SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]WR,Gujarat	03/1997	437.40 589.86	563.25	544.24	03/2004 03/2010	-	-	0/0
KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	321.23	-	-	-	0/0
RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07	456.45	263.34	06/2004 04/2005	-	-	0/0
LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00	925.00	495.62	05/2008 03/2011	-	-	0/0
AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	217.89	12/2009 03/2011	-	-	0/0
KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Multi State	09/2001	100.00 492.98	744.69	716.20	-	-	-	0/0
GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	287.38	-	-	-	0/0
QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00	1,029.00	662.50	-	-	-	0/0
TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	2,945.43	12/2006 08/2010	-	-	0/0
GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	228.09	221.51	-	-	-	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	421.89	02/2010 02/2011	-	-	0/0
KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	452.35	346.13	- -	-	-	0/0
SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	228.79	- 03/2011	-	-	0/0
MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	63.42	- -	-	-	0/0
HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	126.80	- -	-	-	0/0
PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	256.44	03/2008 10/2010	-	-	0/0
ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	415.50	355.38	- 03/2011	03/2011	0(R3)	0/0
NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	46.05	- -	-	-	0/0
BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	134.79	12/2010 03/2011	-	-	0/0
RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	145.48	03/2011 -	-	-	0/0
Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	125.98	- 12/2010	-	-	0/0
Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	167.30	03/2011 03/2011	-	-	0/0

Road Transport & Highways

THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	598.90	03/2009 -	05/2011	26(O)	0/0
HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	138.59	08/2004 -	06/2011	82(O)	0/0
HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	148.38	08/2004 -	06/2011	82(O)	0/0
PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]NHAI,Bihar	04/2000	205.73 -	205.73	247.70	07/2004 -	06/2011	83(O)	0/0
HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	476.60	03/2005 -	06/2011	75(O)	0/0
IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]NHAI,Tamil Nadu	12/2003	210.00 -	210.00	672.30	04/2007 -	06/2011	50(O)	0/0
GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	288.10	09/2007 -	06/2011	45(O)	0/0
HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	213.80	09/2007 -	06/2011	45(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	435.90	11/2007 -	06/2011	43(O)	0/0
AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]NHAI,Uttar Pradesh	12/2003	193.00 -	193.00	324.40	10/2008 -	06/2011	32(O)	0/0
AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]NHAI,Uttar Pradesh	12/2003	217.00 -	217.00	345.60	10/2008 -	06/2011	32(O)	0/0
KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	242.60	10/2008 -	06/2011	32(O)	0/0
GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	381.70	10/2008 -	06/2011	32(O)	0/0
ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	337.10	03/2008 -	06/2011	39(O)	0/0
MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]NHAI,Uttar Pradesh	03/2005	359.00 -	359.00	772.80	03/2009 -	06/2011	27(O)	0/0
AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	06/2011	29(O)	0/0
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	357.50	12/2008 -	06/2011	30(O)	0/0
FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	255.20	09/2008 -	06/2011	33(O)	0/0
LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	198.00	183.40	11/2008 -	06/2011	31(O)	0/0
RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	247.20	10/2008 -	06/2011	32(O)	0/0
RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	229.91	197.60	10/2008 -	06/2011	32(O)	0/0
RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	548.10	06/2008 -	06/2011	36(O)	0/0
SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00 -	322.00	553.70	06/2009 -	06/2011	24(O)	0/0
GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	243.75	02/2004 -	06/2011	88(O)	0/0
GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	665.50	10/2009 -	06/2011	20(O)	0/0
KURALI-KIRATPUR, NH-21 - [N24000087]NHAI,Punjab	03/2005	309.00 -	309.00	553.60	06/2010 -	06/2011	12(O)	0/0
GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	412.10	12/2009 -	06/2011	18(O)	0/0
JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	294.40	09/2009 -	06/2011	21(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	294.90	09/2009	06/2011	21(O)	0/0
TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	653.50	07/2010	06/2011	11(O)	0/0
PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	355.80	07/2010	06/2011	11(O)	0/0
TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	548.70	07/2010	06/2011	11(O)	0/0
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,803.00	01/2011	06/2011	5(O)	0/0
NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	825.30	07/2010	06/2011	11(O)	0/0
BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]NHAI,Karnataka	03/2005	565.00	565.00	1,080.00	07/2010	06/2011	11(O)	0/0
BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	141.87	02/2004	06/2011	88(O)	0/0
END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	419.90	01/2011	06/2011	5(O)	0/0
VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	174.10	03/2008	07/2011	40(O)	0/0
VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	142.20	03/2008	07/2011	40(O)	0/0
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	248.40	10/2008	07/2011	33(O)	0/0
NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	228.80	06/2008	07/2011	37(O)	0/0
MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00	629.00	910.00	11/2010	08/2011	9(O)	0/0
NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	08/2011	32(O)	0/0
Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,339.00	08/2011	08/2011	0(O)	0/0
ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	218.90	11/2008	09/2011	34(O)	0/0
SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	62.44	04/2004	10/2011	90(O)	0/0
DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	246.00	06/2008	10/2011	40(O)	0/0
Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37	353.37	171.50	10/2011	10/2011	0(O)	0/0
Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	498.30	10/2011	10/2011	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	275.30	10/2008	11/2011	37(O)	0/0
SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	166.90	10/2008	11/2011	37(O)	0/0
DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	520.70	05/2010	11/2011	18(O)	0/0
Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,372.00	11/2011	11/2011	0(O)	0/0
AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	80.78	09/2008	12/2011	39(O)	0/0
MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]NHAI,Bihar	12/2003	239.00	239.00	317.60	07/2005	12/2011	77(O)	0/0
BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	200.30	06/2005	12/2011	78(O)	0/0
HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	216.00	02/2009	12/2011	34(O)	0/0
MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	74.70	04/2009	12/2011	32(O)	0/0
BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	163.10	06/2008	12/2011	42(O)	0/0
KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	371.00	12/2008	12/2011	36(O)	0/0
BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	188.70	06/2008	12/2011	42(O)	0/0
SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	199.80	10/2008	12/2011	38(O)	0/0
JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	411.00	09/2008	12/2011	39(O)	0/0
NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	249.80	06/2008	12/2011	42(O)	0/0
NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	235.00	06/2008	12/2011	42(O)	0/0
SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	462.20	03/2008	12/2011	45(O)	0/0
NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	160.90	06/2008	12/2011	42(O)	0/0
NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	197.20	04/2008	12/2011	44(O)	0/0
DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	111.60	05/2008	12/2011	43(O)	0/0
DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	180.10	06/2008	12/2011	42(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056] NHAI, Tamil Nadu	03/2005	280.00	280.00	580.00	06/2009	12/2011	30(O)	0/0
KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090] NHAI, Bihar	12/2003	418.04	418.04	301.30	03/2010	12/2011	21(O)	0/0
PATHANKOT BHOGPUR NH-1A - [N24000115] NHAI, Punjab	12/2003	229.00	284.00	324.70	05/2010	12/2011	19(O)	0/0
ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117] NHAI, Multi State	02/2008	295.00	295.00	622.90	08/2010	12/2011	16(O)	0/0
Armur to kadloor yellareddy - [N24000143] NHAI, Andhra Pradesh	02/2010	390.56	390.56	344.20	02/2012	02/2012	0(O)	0/0
SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207] NHAI, Assam	12/2003	157.47	154.57	171.00	09/2007	03/2012	54(O)	0/0
GUWHATI TO NALBARI (AS-4) - [N24000038] NHAI, Assam	12/2003	175.96	175.96	109.30	04/2008	03/2012	47(O)	0/0
GUWAHATI TO NALBARI (AS-5) - [N24000046] NHAI, Assam	12/2003	198.16	198.16	169.60	04/2008	03/2012	47(O)	0/0
BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063] NHAI, Assam	12/2003	217.61	217.61	125.50	04/2010	03/2012	23(O)	0/0
CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068] NHAI, Rajasthan	12/2003	275.00	281.31	178.50	02/2010	03/2012	25(O)	0/0
NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107] NHAI, Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
Pune-sholapur, pkg1 - [N24000127] NHAI, Maharashtra	11/2009	1,110.00	1,110.00	611.40	05/2012	05/2012	0(O)	0/0
Kishangarh-Ajmer-Beawer - [N24000128] NHAI, Rajasthan	11/2009	795.00	795.00	776.40	05/2012	05/2012	0(O)	0/0
Hyderabad-yadgiri N.H no-202 - [N24000142] NHAI, Andhra Pradesh	08/2010	388.00	388.00	268.00	05/2012	05/2012	0(O)	0/0
DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244] NHAI, Bihar	12/2003	300.00	300.00	156.10	10/2008	06/2012	44(O)	0/0
GWALIOR BYPASS, NH-75, 3 - [N24000088] NHAI, Madhya pradesh	12/2003	300.93	300.93	293.90	10/2009	06/2012	32(O)	0/0
DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108] NHAI, Multi State	12/2003	232.45	232.45	157.00	09/2010	06/2012	21(O)	0/0
MP/Maharashtra Border-Dhula - [N24000126] NHAI, Maharashtra	12/2009	835.00	835.00	374.00	06/2012	06/2012	0(O)	0/0
Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130] NHAI, Multi State	04/2009	1,673.70	1,673.70	1,478.00	10/2011	06/2012	8(O)	0/0
PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123] NHAI, Maharashtra	03/2005	940.00	940.00	300.70	07/2012	07/2012	0(O)	0/0
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237] NHAI, Punjab	12/2003	284.00	359.00	109.30	05/2008	08/2012	51(O)	0/0
SIX LANNING OF VADAKKANCHERRY THRISSURE SECTION - [N24000149] NHAI, Kerala	02/2010	617.00	617.00	154.50	08/2012	08/2012	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	183.50	06/2010	10/2012	28(O)	0/0
LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	232.70	09/2009	10/2012	37(O)	0/0
Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	726.70	09/2012	10/2012	1(O)	0/0
Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	804.60	10/2012	10/2012	0(O)	0/0
AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	588.40	11/2012	11/2012	0(O)	0/0
WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	173.60	07/2008	12/2012	53(O)	0/0
Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	355.10	12/2012	12/2012	0(O)	0/0
Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07	625.07	542.90	01/2013	01/2013	0(O)	0/0
Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	695.00	09/2010	03/2013	30(O)	0/0
Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	-	03/2013	03/2013	0(O)	0/0
CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	197.70	03/2013	03/2013	0(O)	0/0
KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	96.94	03/2013	03/2013	0(O)	0/0
Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	125.00	05/2013	05/2013	0(O)	0/0
DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	97.36	05/2013	05/2013	0(O)	0/0
INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	110.90	09/2007	06/2013	69(O)	0/0
MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0
MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	29.60	04/2009	07/2013	51(O)	0/0
MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	39.25	11/2008	07/2013	56(O)	0/0
DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	593.00	50.83	07/2013	07/2013	0(O)	0/0
CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	0.18	09/2013	09/2013	0(O)	0/0
4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	0.99	09/2013	09/2013	0(O)	0/0
Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	10.04	11/2013	11/2013	0(O)	0/0
MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	212.00	38.61	09/2007	12/2013	75(O)	0/0
HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	196.00	27.66	07/2009	12/2013	53(O)	0/0
4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	299.90	10/2014	10/2014	0(O)	0/0

Shipping & Ports

SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40	2,427.40	820.91	10/2008	11/2010	25(O)	0/0
DEVELOPMENT OF COAL TERMINAL - [N25000055]ENNORE PORT LTD, Tamil Nadu	09/2006	399.13	399.13	-	08/2010	03/2011	7(O)	0/0
DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD, Tamil Nadu	09/2006	370.00	370.00	-	08/2010	04/2011	8(O)	0/0
DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 253.36	253.36	223.60	12/2007 07/2009	06/2011	23(R3)	0/0
Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST, Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK, Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 -	165.00	90.10	12/2005 01/2008	10/2011	45(R3)	0/0
ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	354.81	04/2011 06/2011	11/2011	5(R3)	0/0
Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	290.85	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 -	1,061.96	280.33	03/2012 -	03/2012	0(O)	0/0
ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	03/2012	72(O)	0/0
Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 -	277.03	55.41	12/2011 05/2012	05/2012	0(R3)	0/0
CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	269.69	12/2010 09/2012	09/2012	0(R3)	0/0
ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 -	612.72	61.31	12/2012 -	12/2012	0(O)	0/0
C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	0.73	03/2011 -	03/2013	24(O)	0/0
SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 -	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	966.46	189.92	02/2014 -	02/2014	0(O)	0/0
DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0

Telecommunications

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	50.11	09/2009	02/2010	5(O)	0/0
PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	102.34	12/2005	10/2010	58(O)	0/0
Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	10/2010	7(O)	0/0
Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	11/2010	8(O)	0/0
NIB-II PROJECT RURAL BROADBAND - [N26000037]BSNL,Multi State	12/2007	312.86	353.00	210.69	02/2008	12/2010	34(O)	0/0
Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	12/2010	21(O)	0/0
Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	12/2010	9(O)	0/0
Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	12/2010	9(O)	0/0
Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	12/2010	9(O)	0/0
Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	12/2010	9(O)	0/0
GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	127.26	06/2009	01/2011	19(O)	0/0
GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	110.82	03/2009	02/2011	23(O)	0/0
GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	171.01	12/2008	02/2011	26(O)	0/0
GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	128.29	03/2009	02/2011	23(O)	0/0
UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	158.72	25.67	06/2009	02/2011	20(O)	0/0
Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	105.16	01/2009	02/2011	25(O)	0/0
GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	19.52	02/2010	02/2011	12(O)	0/0
GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	529.32	112.89	10/2008	02/2011	28(O)	0/0
GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,312.52	579.17	-	02/2011	-1(R3)	0/1
GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	161.71	01/2010	02/2011	13(O)	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10
GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	399.04	01/2010	02/2011	13(O)	0/0
GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	68.99	01/2010	02/2011	13(O)	0/0
GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	438.00	12/2008	03/2011	27(O)	0/0
GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	140.73	03/2009	03/2011	24(O)	0/0
GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	601.49	480.57	09/2009	03/2011	18(O)	0/0
GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	22.06	10/2009	03/2011	17(O)	0/0
GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	11.21	09/2010	03/2011	6(O)	0/0
GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	171.99	02/2009	03/2011	25(O)	0/0
GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	191.48	08/2009	03/2011	19(O)	0/0
GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	151.70	11/2010	03/2011	4(O)	0/0
GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	238.44	10/2009	03/2011	17(O)	0/0
ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	12.01	10/2010	04/2011	6(O)	0/0
CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007	08/2011	54(O)	0/0
CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	94.13	10/2007	-	-	0/0
MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	841.00	03/2009	-	-	0/0
Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	392.44	-	03/2009	-	-	0/0

LIST OF PROJECTS WITHOUT MILESTONE (May,2011)

Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
					Original / Revised	Anticipated		
2	3	4	5	6	7	8	9	10

Urban Development

C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	181.30	79.96	04/2009 -	01/2011	21(O)	0/0
--	---------	------------------	--------	-------	--------------	---------	-------	-----

Water Resources

PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
---	---------	-------------	----------	-------	--------------	---------	-------	-----

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
Atomic Energy							
1	KUDANKULAM APP (NPCIL)	12/2008	05/2012	13171.00	15824.00	20.14	41
2	KAKRAPAR ATOMIC POWER PROJECT - 3&4	12/2015	11/2016	11459.00	11459.00	0.00	11
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2010	01/2012	3492.00	5677.00	62.57	16
Civil Aviation							
1	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TER BLDG(K1)	01/2011	10/2011	1273.00	1273.00	0.00	9
2	C/o new Airport at Pakyong(Sikkim) Airport	01/2011	06/2012	309.40	264.29	-14.58	17
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	05/2011	08/2011	1942.51	1942.51	0.00	3
Coal							
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	06/2009	03/2012	2030.78	2453.57	20.82	33
2	BARSINGSAR TPS (2X125MW) (NLC)	06/2009	08/2011	1114.18	1626.09	45.94	26
3	KULDA OCP (MAHANADI COALFIELDS LTD.)	03/2010	03/2012	302.96	302.96	0.00	24
4	ASHOK EXPN.OCP -CCL (6.5 MTY)	03/2011	03/2013	471.66	341.63	-27.57	24
5	KRISHNASHILA (NCL) (4MTY)	03/2010	03/2013	789.88	741.56	-6.12	36
6	BLOCK-B OCP NCL (3.5 MTY)	03/2012	03/2015	746.04	437.34	-41.38	36
7	AMLOHRI EPR (NCL) (6 MTY)	03/2014	03/2016	1352.04	1143.54	-15.42	24
8	MAGADH OC (CCL)	07/2012	03/2016	469.78	706.40	50.37	44
9	ADRIYALA SHAFT PROJECT	03/2013	06/2013	212.34	779.26	266.99	3
10	GOPAL PRASAD OCP	03/2013	03/2015	395.87	395.87	0.00	24
11	TALABIRA OCP	03/2015	03/2016	447.72	447.72	0.00	12
12	BALRAM OCP EXTENSION	03/2009	03/2012	172.08	172.08	0.00	36
13	Tapin OCP	03/2012	03/2014	264.68	264.68	0.00	24
14	GEVRA EXPANSION OCP (SECL) (25 MTY)	03/2010	03/2014	1667.55	2675.67	60.46	48
15	RAJMAHAL OC EXP.	03/2011	03/2014	50.08	153.82	207.15	36
16	KAKATIYA LAONGWALL	12/2012	03/2015	453.63	453.63	0.00	27
17	JHANJRA LONGWAL UG PHASE II	03/2011	03/2015	287.18	287.17	0.00	48
18	Churi Benti UG	03/2011	03/2014	163.51	163.51	0.00	36
19	North Urimari OCP	03/2012	03/2014	179.87	179.87	0.00	24
20	DIPKA EXPANSION OCP (SECL) (20 MTY)	03/2010	03/2014	1268.53	1943.66	53.22	48
Fertilisers							
1	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	12/2012	01/2013	1478.63	1478.63	0.00	1

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
	Mines						
1	SECOND PHASE EXPANSION OF NALCO MINE, REFINERY, SMELTER AND CAPTIVE POWER PLANT	12/2008	05/2011	4091.51	4401.76	7.58	29
	Petroleum						
1	IOR LAKWA - LAKHMANI (ONGCL)	03/2007	03/2014	345.10	663.69	92.32	84
2	IOR GELEKI (ONGCL)	03/2007	03/2017	390.09	1674.11	329.16	120
3	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON	09/2009	06/2011	1431.91	1690.13	18.03	21
4	DEVELOPMENT OF C-SERIES FIELDS	12/2008	11/2011	3195.16	2800.00	-12.37	35
5	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	06/2010	10/2011	2305.30	3005.30	30.36	16
6	DEVELOPMENT OF B-22 CLUSTER FIELDS	09/2010	05/2012	2323.40	2920.82	25.71	20
7	DEVELOPMENT OF B-193 CLUSTER FIELDS	08/2010	06/2012	3248.78	5633.44	73.40	22
8	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2	05/2010	03/2013	5713.03	8813.41	54.27	34
9	DEVELOPMENT OF B-46 CLUSTER FIELD	07/2010	05/2012	1436.21	1436.21	0.00	22
10	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA	04/2011	07/2012	370.11	370.11	0.00	15
11	DHABOL-BANGALORE PIPELINE PROJECT PHASE-I	03/2012	08/2012	4543.43	2500.00	-44.98	5
12	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH)	06/2011	03/2012	463.32	340.00	-26.62	9
13	MNW-NF BRIDGE PROJECT	03/2009	02/2012	175.21	162.12	-7.47	35
14	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY	09/2011	03/2012	3597.00	2730.00	-24.10	6
15	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REFINERY	12/2009	07/2011	293.60	293.60	0.00	19
16	IOR, RUDRASAGAR (ONGCL)	03/2006	03/2013	113.90	438.85	285.29	84
17	North Tapti Gas Field Development	03/2011	06/2011	589.70	755.76	28.16	3
18	REFRIGERATED LPG STORAGE AT JNPT	12/2010	06/2011	304.40	304.40	0.00	6
19	ADDITIONAL GAS PROCESSING UNITS AT URAN	12/2011	01/2013	1797.35	1797.35	0.00	13
20	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I & II	04/2011	12/2011	1512.00	982.00	-35.05	8
21	EURO-IV DHDT	05/2011	12/2011	2615.69	2615.69	0.00	7
22	REVAMPING OF WIN PLATFORM AT MH ASSET	05/2010	05/2012	333.40	656.51	96.91	24
23	HEERA RECONSTRUCTION	04/2010	06/2011	706.70	706.70	0.00	14
24	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV)	09/2011	12/2011	736.65	736.65	0.00	3
25	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	12/2010	06/2011	613.54	727.88	18.64	6

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
26	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI	12/2010	08/2011	224.00	299.00	33.48	8
27	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH	03/2010	03/2012	740.02	740.02	0.00	24
28	NEELAM RECONSTRUCTION	04/2011	06/2011	305.08	305.08	0.00	2
29	COMPRESSOR STATIONS (KAILARAS & CHAINSA)	04/2011	12/2011	1167.00	810.00	-30.59	8
30	CONSTRUCTION OF NEW PROCESS COMPLEX MHN	05/2010	05/2012	2853.29	6326.40	121.72	24
31	INTEGRATED DEV OF G1 and GS-15 (ONGCL)	04/2006	05/2012	429.82	2218.01	416.03	73
32	BNPL SPURLINE (UTTRANCHAL & PUNJAB)	06/2011	07/2012	540.92	400.00	-26.05	13
Power							
1	TUIRIAL HE PROJECT(NEEPCO)	07/2006	01/2014	368.72	913.63	147.78	90
2	KOTESHWAR HEP(THDC)	04/2005	03/2012	1301.56	2398.39	84.27	83
3	PARBATI HEP (NHPC) II	09/2009	07/2014	3919.59	3919.59	0.00	58
4	SUBANSIRI LOWER H.E.P (NHPC)	09/2010	08/2014	6285.33	6285.33	0.00	47
5	TESSTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	03/2007	05/2012	768.92	768.92	0.00	62
6	SIPAT STPP STAGE - I (NTPC)	12/2009	03/2012	8323.39	8323.39	0.00	27
7	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	05/2013	06/2016	2496.90	2496.90	0.00	37
8	CHAMERA, STAGE-III (NHPC)	08/2010	08/2011	1405.63	1405.63	0.00	12
9	BARH STPP STAGE I (3X660MW) NTPC	11/2010	09/2014	8693.00	8693.00	0.00	46
10	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	09/2009	12/2012	1061.38	1061.38	0.00	39
11	PARBATI H.E.P. STAGE -III (NHPC)	10/2010	12/2011	2304.52	2304.52	0.00	14
12	URI H.E.P STAGE -II (NHPC)	11/2009	12/2011	1724.79	1724.79	0.00	25
13	KOTESWAR TRANSMISSION SYSTEM (PGCIL)	06/2008	06/2011	260.34	241.27	-7.33	36
14	KUDANKULAM-APP TRANS. SYSTEM (PGCIL)	11/2008	03/2012	1779.29	1946.85	9.42	40
15	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)	09/2009	12/2011	3779.46	3725.13	-1.44	27
16	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME	06/2009	06/2011	803.70	803.76	0.01	24
17	EASTERN REGION STRENGTHENING SCHEME-I	10/2009	03/2012	975.96	894.26	-8.37	29
18	NIMOO BAZGO HYDROELECTRIC PROJECT	08/2010	06/2012	611.02	611.02	0.00	22
19	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	02/2011	08/2011	621.28	621.28	0.00	6
20	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	01/2010	11/2011	557.24	639.52	14.77	22

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
21	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II	05/2011	09/2011	238.25	227.03	-4.71	4
22	RAMPUR HEP(412 MW)	01/2012	09/2013	2047.03	2047.03	0.00	20
23	KISHANGANGA HEP	07/2014	01/2016	2238.67	3642.04	62.69	18
24	EASTERN REGION STRENGTHENING SCHEME-II	06/2010	09/2011	227.52	227.52	0.00	15
25	WESTERN REGION STRENGTHENING SCHEME-V	09/2010	03/2013	477.69	477.69	0.00	30
26	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMERA-II HEP	09/2010	08/2011	262.10	262.10	0.00	11
27	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	07/2014	03/2016	2221.31	2491.45	12.16	20
28	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV	11/2011	03/2013	520.48	520.48	0.00	16
29	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII	11/2011	03/2013	509.66	509.66	0.00	16
30	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX	02/2012	03/2013	410.29	410.29	0.00	13
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII	08/2011	02/2012	210.79	210.79	0.00	6
32	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS	07/2010	02/2012	353.57	353.57	0.00	19
33	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP	11/2011	09/2013	184.19	184.19	0.00	22
34	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	07/2011	12/2011	297.37	297.37	0.00	5
35	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	08/2013	09/2014	11130.19	11130.19	0.00	13
36	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION	07/2011	02/2012	196.10	196.10	0.00	7
37	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-I	02/2012	03/2013	1347.32	1347.32	0.00	13
38	TRIPURA GAS BASED POWER PROJECT	01/2012	07/2013	421.01	623.44	48.08	18
39	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PART-III	05/2012	03/2013	1075.12	1075.12	0.00	10
40	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2010	01/2016	1657.00	2978.86	79.77	66
41	WESTERN REGION STRENGTHENING SCHEME-IX	01/2011	10/2011	230.89	230.89	0.00	9
42	KOLDAM HEP (NTPC)	04/2009	03/2013	4527.15	4527.15	0.00	47
43	WESTERN REGION STRENGTHENING SCHEME-II	07/2010	12/2011	5221.23	4978.56	-4.65	17
Railways							
1	GUNA-ETAWAH(NCR), NL	03/1994	12/2011	158.77	540.96	240.72	213
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/2001	12/2017	2500.00	11270.00	350.80	201
3	LANJHIGARH-JUNAGARH NL(ECOR)	03/2002	09/2011	100.00	170.00	70.00	114
4	NANDYAL-YERRAGUNTLA(NL),SCR	02/2009	12/2011	155.74	429.49	175.77	34

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
5	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	04/2008	03/2014	1000.00	3230.01	223.00	71
6	HOWRAH-AMTA-CHAMPADANGA NL (SER)	03/2007	06/2012	31.42	499.16	1488.67	63
7	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	12/2008	03/2014	733.00	1655.80	125.89	63
8	BANKURA - DAMODAR (GC) (SER)	03/2005	12/2012	111.90	1211.22	982.41	93
9	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	03/2011	03/2016	727.56	3056.85	320.15	60
10	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR	03/2009	12/2012	921.00	921.00	0.00	45
11	PATNA GANGA BRIDGE (NL), ECR	10/2007	12/2012	624.47	1389.98	122.59	62
12	SALKA ROAD -ANUPNAGAR LINE DOUBLING	03/2010	03/2012	324.90	324.90	0.00	24
13	PANSPURA-KHARAGPUR 3D LINE	02/2010	11/2011	252.50	252.50	0.00	21
14	BHOPAL BINA 3D LINE DOUBLING	03/2010	12/2012	687.20	687.20	0.00	33
15	UTRATIA-ZAFRABAD, NR (LINE DOUBLING)	03/2010	06/2014	325.00	369.90	13.82	51
16	Sadulpur-Bikaner and Ratangarh-Degana Gauge Conversion (NWR)	03/2011	03/2012	643.36	803.39	24.87	12
17	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbender (MTP)	03/2016	06/2016	2397.72	2397.72	0.00	3
18	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP)	03/2014	03/2016	2069.60	2069.60	0.00	24
19	Dakshin-barasat-lakshmikantapur (ER)	12/2011	02/2012	259.51	259.51	0.00	2
20	Ghutiasharif-Canning (ER)	12/2011	11/2013	189.97	189.97	0.00	23
21	Katakhal to Bhairabi	12/2012	12/2013	227.90	223.01	-2.15	12
22	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP	03/2014	03/2015	5300.00	5300.00	0.00	12
23	ELECTRIFICATION OF MORADABAD-ROZA	03/2011	03/2012	129.17	220.00	70.32	12
24	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	03/2009	12/2013	1676.31	4091.33	144.07	57
25	TAMLUK DIGHA,LINE DOUBLING (SER)	06/2005	03/2012	293.97	723.27	146.04	81
Road Transport & Highways							
1	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4)	08/2004	06/2011	241.00	196.65	-18.40	82
2	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4)	08/2004	06/2011	318.00	207.56	-34.73	82
3	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5)	04/2004	10/2011	225.00	241.53	7.35	90
4	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	03/2005	12/2011	367.49	367.49	0.00	81

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
5	PURNEA-GOYAKOTA SEC.(EW) (NS AND EW-PH-I) KM.419-KM.447, NH-31	07/2004	06/2011	205.73	205.73	0.00	83
6	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	03/2005	06/2011	273.00	522.00	91.21	75
7	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS	04/2007	06/2011	210.00	210.00	0.00	50
8	GARHMAKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	09/2007	06/2011	275.00	275.00	0.00	45
9	HAPUR-GARHMAKTESWAR (OTHERS) KM.58-93, NH-24	09/2007	06/2011	220.00	220.00	0.00	45
10	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	11/2007	06/2011	412.78	479.54	16.17	43
11	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	09/2008	12/2011	155.00	201.66	30.10	39
12	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.250, NH-28	10/2008	06/2011	193.00	193.00	0.00	32
13	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28	07/2005	12/2011	239.00	239.00	0.00	77
14	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28	10/2008	06/2011	217.00	217.00	0.00	32
15	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	06/2005	12/2011	230.00	230.00	0.00	78
16	VIJAYAPUR TO PATHANKOT (J AND K) NH-1A KM.16.35 TO KM.50.00	03/2008	07/2011	193.09	166.30	-13.87	40
17	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	03/2008	07/2011	166.27	193.10	16.14	40
18	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A	05/2008	08/2012	284.00	359.00	26.41	51
19	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	10/2008	06/2011	240.00	240.00	0.00	32
20	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	10/2008	06/2011	227.00	227.00	0.00	32
21	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	03/2008	06/2011	340.68	340.68	0.00	39
22	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00	03/2009	06/2011	359.00	359.00	0.00	27
23	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	01/2009	06/2011	190.00	190.00	0.00	29
24	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	11/2010	08/2011	629.00	629.00	0.00	9

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
25	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	02/2009	12/2011	280.00	280.00	0.00	34
26	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000	04/2009	07/2013	199.81	385.13	92.75	51
27	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54	11/2008	12/2013	167.64	167.64	0.00	61
28	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450	11/2008	07/2013	155.04	280.13	80.68	56
29	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500	04/2009	12/2011	200.00	200.00	0.00	32
30	DAKOPA TO NAGAON (NH-36)(NHAI)	06/2008	10/2011	225.00	225.00	0.00	40
31	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	06/2008	12/2011	195.00	195.00	0.00	42
32	KASIA TO GORAKHPUR (NH-28)(NHAI)	12/2008	12/2011	242.00	242.00	0.00	36
33	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	12/2008	06/2011	227.00	227.00	0.00	30
34	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI)	06/2008	12/2011	237.80	237.80	0.00	42
35	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	09/2008	06/2011	332.94	332.94	0.00	33
36	KOTA BYPASS,RJ-4, NH-76 (NHAI)	10/2008	11/2011	275.00	250.39	-8.95	37
37	LALITPUR TO SAGAR, NH-26 (NHAI)	11/2008	06/2011	198.00	198.00	0.00	31
38	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	10/2008	07/2011	225.00	225.00	0.00	33
39	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	10/2008	11/2011	151.30	151.30	0.00	37
40	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	10/2008	12/2011	203.43	203.43	0.00	38
41	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	10/2008	06/2011	251.03	251.03	0.00	32
42	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA	10/2008	06/2011	229.91	229.91	0.00	32
43	SILIGURI TO ISLAMPUR (WB-7)	07/2008	12/2012	225.00	225.00	0.00	53
44	RINGBUNDS TO JHAJHANPUR (BR-6)	06/2008	06/2011	340.00	340.00	0.00	36
45	JHAJHARPUR TO DARBANGA (BR-7)	09/2008	12/2011	340.00	340.00	0.00	39
46	NALBARI TO BIJNI (AS-8)	06/2008	12/2011	200.00	200.00	0.00	42
47	SITAPUR-LUCKNOW	06/2009	06/2011	322.00	322.00	0.00	24
48	THRISSUR TO ANGAMALI (NH-47)	03/2009	05/2011	312.50	312.50	0.00	26
49	GUWHATI TO NALBARI (AS-4)	04/2008	03/2012	175.96	175.96	0.00	47
50	NEW MANGALORE PORT NH-17 AND 48	06/2008	07/2011	196.50	196.50	0.00	37
51	NAGAON TO DHARAMTUL (AS-2)	06/2008	12/2011	264.72	264.72	0.00	42
52	SONAPUR TO GUWAHTI (AS-3)	03/2008	12/2011	245.00	245.00	0.00	45
53	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	11/2008	09/2011	221.82	221.82	0.00	34
54	GUWAHATI TO NALBARI (AS-5)	04/2008	03/2012	198.16	198.16	0.00	47

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
55	NALBARI TO BIJNI (AS-6)	06/2008	12/2011	225.00	225.00	0.00	42
56	NALBARI T BIJNI (AS-7)	04/2008	12/2011	208.00	208.00	0.00	44
57	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	05/2008	12/2011	160.00	160.00	0.00	43
58	DHARAMTUL TO SONAPUR (AS-19)	06/2008	12/2011	200.00	200.00	0.00	42
59	NAGPUR-KONDHALI,NH-6(NHAI)	12/2008	08/2011	168.00	168.00	0.00	32
60	THANJAUR-TRICHY,NH-67(NHAI)	06/2009	12/2011	280.00	280.00	0.00	30
61	GANJAM-ICCHAPURUM,NH-5(NHAI)	02/2004	06/2011	263.27	263.27	0.00	88
62	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54	09/2007	12/2013	212.00	212.00	0.00	75
63	HARANGAJO TO MAIBANG, NH-54	07/2009	12/2013	196.00	196.00	0.00	53
64	BRAHMPUTRA BRIDGE,NH NO-31	04/2010	03/2012	217.61	217.61	0.00	23
65	CHAMBAL BRIDGE, NH-76 (RJ-5)	02/2010	03/2012	275.00	281.31	2.29	25
66	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	10/2009	06/2011	600.24	600.24	0.00	20
67	KURALI-KIRATPUR, NH-21	06/2010	06/2011	309.00	309.00	0.00	12
68	GWALIOR BYPSS, NH-75,3	10/2009	06/2012	300.93	300.93	0.00	32
69	GWALIOR-JHANSI, NH-75	12/2009	06/2011	604.00	604.00	0.00	18
70	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AND AFFLUX-BOND (BR-5)	03/2010	12/2011	418.04	418.04	0.00	21
71	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7	06/2010	10/2012	407.60	407.60	0.00	28
72	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7	09/2009	10/2012	263.17	263.17	0.00	37
73	JHANSI TO LALITPUR, NH-25,26	09/2009	06/2011	355.06	355.06	0.00	21
74	JHANSI TO LALITPUR, NH-26	09/2009	06/2011	276.09	276.09	0.00	21
75	AGRA-BYPASS(NS-1/UP-1), NH-2,3	09/2007	06/2013	348.16	348.16	0.00	69
76	TRICHY - DINDIGUAL NH-45	07/2010	06/2011	576.00	576.00	0.00	11
77	PONDICHERY - TINDIVANAU NH-66	07/2010	06/2011	285.00	285.00	0.00	11
78	TRICHY - KORUR NH-67	07/2010	06/2011	516.00	516.00	0.00	11
79	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	01/2011	06/2011	941.00	941.00	0.00	5
80	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	07/2010	06/2011	441.00	441.00	0.00	11
81	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4	07/2010	06/2011	565.00	565.00	0.00	11
82	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	02/2010	05/2012	557.00	557.00	0.00	27

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
83	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	09/2010	06/2012	232.45	232.45	0.00	21
84	PATHANKOT BHOGPUR NH-1A	05/2010	12/2011	229.00	284.00	24.02	19
85	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5	02/2004	06/2011	228.70	228.70	0.00	88
86	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	08/2010	12/2011	295.00	295.00	0.00	16
87	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER	01/2011	06/2011	464.00	464.00	0.00	5
88	DELHI/ HARYANA BORDER TO ROHTAK	05/2010	11/2011	486.00	486.00	0.00	18
89	Bijapur-Hungund Section	09/2010	03/2013	748.00	748.00	0.00	30
90	Gurgaon-Kotputli Km 42.70 to 54.4 Km	10/2011	06/2012	1673.70	1673.70	0.00	8
91	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass	06/2011	10/2012	1170.52	1170.52	0.00	16
92	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	09/2007	03/2012	157.47	154.57	-1.84	54
93	Gujarat/Maharashtra BorderSurat-Hazira Port Section	09/2012	10/2012	1509.10	1509.10	0.00	1
94	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915	10/2008	06/2012	300.00	300.00	0.00	44
Shipping & Ports							
1	DEEPENING OF CHANNEL AT PARADIP PORT	12/2007	06/2011	154.84	253.36	63.63	42
2	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL	12/2010	09/2012	1228.00	1460.00	18.89	21
3	C/O Berthing and Allied Facilities off tekra near TUNA	02/2011	03/2013	882.00	1060.00	20.18	25
4	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH	12/2005	10/2011	165.00	165.00	0.00	70
5	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT COCHIN	01/2009	05/2013	375.00	272.50	-27.33	52
6	Acquisition of two nos. of 120 B.P	06/2011	01/2012	290.85	290.85	0.00	7
7	MARINE LIQUID TERMINALS	06/2006	09/2011	196.25	196.25	0.00	63
8	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA	03/2011	03/2013	702.00	755.50	7.62	24
9	Mechanization of coal handling facilities to 200000 DWT Vessels on DBFOT basis	06/2010	11/2012	444.10	444.10	0.00	29
10	Construction & License out the OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR COAL HANDELLING	12/2010	06/2011	230.00	272.50	18.48	6
11	Acquisition of Two nos. of 3060 DWT	12/2011	05/2012	277.03	277.03	0.00	5

LIST OF DELAYED PROJECTS AS ON 01.06.2011

SN	TITLE	DOC ORIGINAL	DOC ANTICIPATED	COST ORIGINAL	COST ANTICIPATED	COST OVERRUN (%)	TIME OVERRUN IN MONTHS
12	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS	04/2011	11/2011	359.44	359.44	0.00	7
13	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV)	03/2006	03/2012	150.00	600.00	300.00	72
Steel							
1	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	10/2009	03/2012	8692.00	12291.00	41.41	29
2	EXPENSION OF ROURKELA STEEL PLANT	02/2011	03/2013	6133.00	11812.00	92.60	25
3	Rebuilding of coke oven battery No.1 & 2 (Bokaro Steel Plant)	04/2010	09/2011	500.90	500.90	0.00	17
4	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)	01/2010	06/2011	172.78	172.78	0.00	17
Telecommunications							
1	CONVERGENT BILLING AND CRM-MTNL(DELHI)	02/2007	08/2011	249.00	229.41	-7.87	54
2	CONVERGENT BILLING AND CRM(MUMBAI)	02/2007	08/2011	247.00	247.00	0.00	54
Urban Development							
1	BANGALORE METRO RAIL PROJECT	12/2011	03/2013	6395.00	11609.00	81.53	15
2	DELHI MRTS PHASE-II PROJECT	06/2010	06/2011	8676.00	18894.36	117.78	12
Water Resources							
1	PAGLADIYA DAM PROJECT	12/2007	12/2012	542.90	1187.00	118.64	60

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
