

**331st FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
May 2013**



MUMBAI PORT - CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

EXECUTIVE SUMMARY

1. The Flash Report for May 2013 contains information on the status of the 569 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During May 2013, 4 projects (2 projects in Power and 1 project each in Road and Fertilizer Sector) have reported completion.

2. During the reference month, out of 569 projects, 266 projects are delayed with respect to latest schedule and 43 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 43 projects, 11 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 46 months in respect of projects relating to Coal, Civil Aviation, Shipping & Ports, Telecommunication, Steel, Railways, Petroleum, Power and Road Transport & Highways Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Road Transport & Highways	148	90	15	1
2.	Railways	129	33	3	2
3.	Power	103	51	5	1
4.	Petroleum	70	40	7	5
5.	Coal	54	28	1	0
6.	Shipping & Ports	19	2	2	1
7.	Steel	17	13	5	1
8.	Telecommunications	13	5	4	0
9.	Civil Aviation	6	2	1	0
10.	Atomic Energy	4	2	0	0
11.	Urban Development	4	0	0	0
12.	Petrochemicals	1	0	0	0
13.	Water Resources	1	0	0	0
Total		569	266	43	11

3. Total original cost of implementation of the 569 projects was about ₹ 7,97,194.85 crore and their anticipated completion cost is likely to be ₹ 9,46,877.84 crore, which reflects an overall cost overruns of ₹ 1,49,682.99 crore (18.80 % of original cost). The expenditure incurred on these projects till May 2013 is ₹ 4,47,272.38 crore, which is 47.20 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 31-05 -2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 31-05-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 569 projects, 2 projects are ahead of schedule, 161 are on schedule and 266 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 277 if delay is calculated on the basis of original schedule of completion. Further, 18 projects have been sanctioned without any commissioning schedule/date and for 122 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 266 delayed projects, 65 projects have overall delay in the range of 1 to 12 months, 69 projects have a delay in the range of 13 to 24 months, 74 projects have a delay in the range of 25 to 60 months and 58 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-05-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI- GWALIOR - BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2013	216
3	UDHAMPUR- SRINAGAR- BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	06/2016	135
5	LANJHIGARH- JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	03/2013	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, legal issue, delay in supply of equipment, municipal permission, geological surprises, no-response to Nit by bidder, delay in package by M/s BHEL, delay in erection activities by M/s BHEL, seepage in power house, delay in handing over the full site, ROU/ROW problems, law and order, etc.

7. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 31-05-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMMULATIVE (₹ crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADAN GANL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

8. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-05-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMMULATIVE (₹ crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 31.05.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012

5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012
---	--------------------------	----------	---------	------	------	---------

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

9. The Sector-wise details of delays/additional delays are as under:-

i) In the **Coal Sector**, out of 54 projects, 28 projects are delayed. During the month the projects 'Kakatiya Longwall, SCCL' has reported additional delay of 12 months due to delay in decision on Technology Provider cum Operator (TPO).

ii) In the **Civil Aviation Sector**, out of 6 projects, 2 projects are delayed. During the month the projects 'Construction of new Airport at Pakyong (Sikkim) Airport, AAI' has reported additional delay of 12 months due to delay in handing over the full site and geological surprises.

iii) In the **Shipping & Ports Sector**, out of 19 projects, 2 projects are delayed. During the month 2 projects have reported additional delays of 23 and 46 months respectively, out of which 1 project is Mega project. The projects 'Deepening of Channel at Paradip Port, Port Trust of India' and 'Deepening and Widening of Mumbai Harbour Channel, Port Trust of India' have reported additional delay of 23 and 46 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

iv) In the **Railways Sector**, out of 129 projects, 33 projects are delayed. During the month 3 projects have reported additional delays in the range of 2-24 months, out of which 2 are Mega projects. The project 'Chandigarh-Ludhiana (New BG Line), NR', 'Dausa-Gangapur City (NL), NWR' and 'New Work for Construction of Metro railway from Baranagar to Barrackpure, RVNL' have reported additional delay of 2, 12 and 24 months respectively. However, no specific reasons have been reported by the project authorities for delay in these projects.

v) In the **Telecommunication Sector**, out of 13 projects, 5 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-4 months. The projects 'Supply Installation Testing and Commissioning of Rural Wimax, BSNL' has reported additional delay of 1 month due to delay in supply of equipment; the projects

‘GSM Equipment of 1625000 Lines (2G) 325000 Lines 3, BSNL’ has reported additional delay of 3 months each due to delay in municipal permission. The Project ‘GSM Equipment of 283000 Lines (2G) and 75000 Lines, BSNL’ and ‘Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL’ have reported additional delay of 4 months each due to delay in municipal permission.

vi) In the **Steel Sector**, out of 17 projects, 13 projects are delayed. During the month 5 projects have reported additional delay in the range of 1-2 months, out of which 1 is Mega project. Of these 5 projects, 1 project has reported additional delay of 1 month; the project ‘Coke Oven Battery No. 4 Phase-II, RINL’, ‘67.5 MW TG-5 Auxiliary System Emergency Power Requirement, RINL’ and ‘330 TPH Boiler-6 and Auxiliary System, RINL’ have reported additional delays of 2 months each due to delay in no response to NIT by bidders, delay in package by M/s BHEL and delay in erection activities by M/s BHEL respectively. The project ‘Augmentation of Iron Ore Storage in RMHP, RINL’ has reported additional delay of 2 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vii) In the **Power Sector**, out of 103 projects, 51 projects are delayed. During the month 5 projects have reported additional delays in the range of 1-3 months, out of which 1 is Mega project. Of these 5 projects, 2 projects have reported additional delay of 1 month each; the projects ‘URI H.E.P Stage –II, NHPC’ and ‘Interconnection Between Electrical Grids of India, PGCIL’ have reported additional delay of 2 months each due to delay in seepage in power house and land acquisition & ROW problem. The projects ‘Eastern Region Strengthening Scheme-I, PGCIL’ has reported additional delay of 3 months. However, no specific reasons have been reported by the project authorities for delay in this project.

viii) In the **Petroleum Sector**, out of 70 projects, 40 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-8 months, out of which 5 are Mega projects. Of these 7 projects, 1 project has reported additional delay of 1 month and 4 projects have reported additional delay of 2 months each ; the projects ‘Development of G1 and GS-15, ONGC’ has reported additional delay of 8 month due to delay in supply of equipment and legal issue. The project ‘Butadiene Extraction Unit (BDEU) at Panipat, IOCL’ has reported additional delay of 3 months. However, no specific reasons have been reported by the project authorities for delay in this project.

ix) In the **Road Transport & Highways Sector**, out of 148 projects, 90 are delayed. During the month 15 projects have reported additional delays in the range of 1-17 months, out of which 1 is Mega project. Of these 15 projects, 4 projects have reported additional delay of 1 month each, 3 projects have reported additional delay of 2 months each, 2 projects have reported additional delay of 3 months each and 1 project has reported additional delay of 4 months; the projects 'Forbesganj to Simrahi (NH-57), NHAI' and 'Nagaon to Dharamtul (AS-2), NHAI' have reported additional delay of 7 months each. The project 'Indore-Jhabua-Gujrat/MP, NHAI' , 'Niroli-Roxy-Rajamunda, NHAI' and 'Gwalior-Jhansi, NH-75, NHAI' have reported additional delay of 8, 11 and 17 months respectively. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

10. The status as on 31.05.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

11. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Road Transport & Highways	148	15
2	Railways	129	3
3	Power	103	5
4	Petroleum	70	7
5	Coal	54	1
6	Shipping & Ports	19	2
7	Steel	17	5
8	Telecommunications	13	4
9	Civil Aviation	6	1
10	Atomic Energy	4	0
11	Urban Development	4	0
12	Petrochemicals	1	0
13	Water Resources	1	0
	Total	569	43

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No.	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>Power</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>Railways</u>			
2	REINGUNTA-GUNTAKAL(RE)(RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL)(RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>Fertilisers</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT(NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>Power</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>Road Transport & Highways</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56


Summary of projects in the Flash Report for the month of May, 2013

Project Implementation - Current Status:

Number of Projects in Previous Month	566
Number of Projects completed/dropped/frozen in Current Month	4
Number of Projects elevated to the status of Major project during the current month	2
Number of Projects Added in Current Month	5
Number of Projects in Current Month	569


Brief Analysis

Project Status with respect to Original Schedule: Out of 569 projects, 3 projects are ahead of schedule, 149 projects are on schedule and 277 projects are delayed. Of the balance, 122 projects do not have fixed dates of commissioning while 18 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

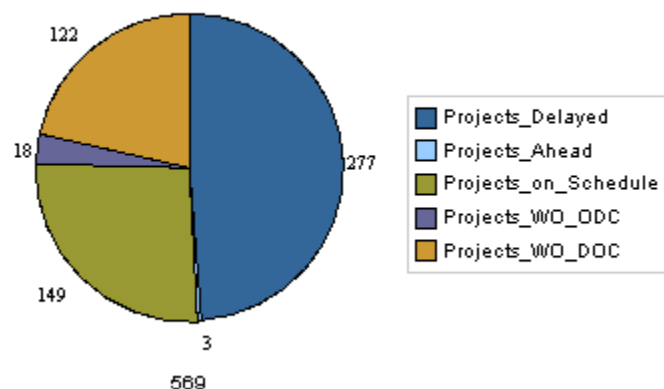

Investment Scenario

The Total Original cost of implementation of 569 projects when sanctioned, was of the order of Rs. 797194.85 crore but this was subsequently revised to Rs. 946877.84 crore implying a cost overrun of 18.8%. The expenditure incurred on these projects till May, 2013 is Rs. 447272.47 crore, which is 47.2% of the revised cost of the projects.

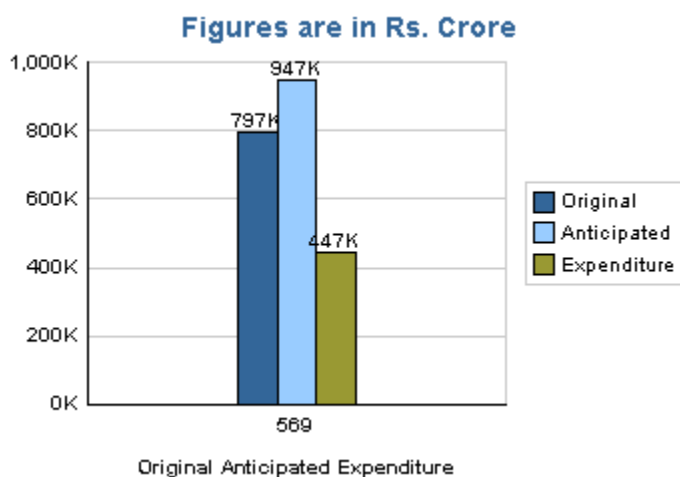

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	566
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects elevated to the status of Major Project during the Current Month	2
No of Projects added in Current Month	5
No of Projects in Current Month	569

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	277	3	149	18	122	569	48.68
Latest Approved (Date)	266	2	161	18	122	569	46.75

(A) Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	420	663,577.17	705,986.87	311,977.72	44.20	42,409.70	6.40
Latest Approved (RCE)	149	189,399.51	240,890.97	135,294.66	56.20	51,491.46	27.20
Total (RCE)	569	852,976.68	946,877.84	447,272.38	47.24	93901.16	11.01
Original Cost of All Projects							
Original Cost	569	797,194.85	946,877.84	447,272.38	47.20	149,682.99	18.80

(B) Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	277	444,788.61	535,854.17	306,815.52	57.30	91,065.56	20.50
Latest Approved (RCE)	266	462,347.35	519,533.07	298,526.26	57.50	57,185.72	12.40

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	43	43,615.08	52,627.88	38,181.92	72.60	9,012.80	20.70

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of Projects				Projects with cost overrun			
			Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	54	37,268.9	40,354.4	8.3	7	8,579.5	12,262.6	42.9
4	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	Petroleum	70	165,950.5	179,743.3	8.3	20	57,284.8	77,140.9	34.7
7	Power	103	243,029.0	259,083.9	6.6	21	48,353.1	64,408.0	33.2
8	Railways	129	66,990.8	157,490.0	135.1	111	48,954.7	139,500.4	185.0
9	Road Transport & Highways	148	101,189.1	103,127.7	1.9	11	3,324.3	5,445.2	63.8
10	Shipping & Ports	19	15,617.1	17,700.8	13.3	9	8,629.0	11,016.9	27.7
11	Telecommunications	13	5,699.2	5,520.2	-3.1	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		569	797,194.9	946,877.8	18.8	196	233,474.3	390,648.0	67.3

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

Sl.No	State	No. of Projects				Projects with cost overrun			
			Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Andhra Pradesh	37	31,097.1	38,550.4	24.0	14	12,923.7	21,243.9	64.4
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	2	6,441.3	11,073.4	71.9
3	Assam	38	23,394.4	36,838.1	57.5	14	10,762.0	24,299.8	125.8
4	Bihar	30	26,917.6	35,131.2	30.5	15	12,886.5	21,100.1	63.7
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	33,405.1	33,607.0	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	8	4,054.4	5,737.0	41.5	2	1,298.8	2,981.4	129.5
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	4	11,308.5	15,199.7	34.4
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	27	47,076.4	56,439.7	19.9	10	9,330.8	19,187.1	105.6
11	Kerala	7	20,376.7	22,170.2	8.8	3	4,295.7	6,089.2	41.8
12	Madhya pradesh	20	18,545.6	18,953.8	2.2	4	2,714.8	3,542.4	30.5
13	Maharashtra	48	88,574.5	100,866.5	13.9	16	32,355.5	47,114.3	45.6
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	512.1
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,298.0	115.1	1	619.3	2,384.3	285.0
17	Nagaland	1	850.0	2,446.8	187.9	1	850.0	2,446.8	187.9
18	Odisha	30	56,171.6	63,436.9	12.9	12	32,671.6	39,936.9	22.2
19	Punjab	5	2,063.4	3,005.2	45.6	2	532.4	1,474.2	176.9
20	Rajasthan	14	21,115.8	20,928.0	-0.9	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	48,788.1	61,732.8	26.5	14	29,143.5	42,088.3	44.4
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	27	21,281.9	25,861.1	21.5	10	3,831.0	8,458.5	120.8
25	West Bengal	27	46,938.9	59,572.6	26.9	17	25,617.0	38,250.7	49.3
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
28	Jharkhand	23	14,447.4	18,632.5	29.0	7	2,225.5	6,582.4	195.8
29	Uttarakhand	5	7,624.2	8,564.6	12.3	2	2,640.7	3,581.2	35.6
30	Multi State	110	143,655.0	156,071.1	8.6	23	14,967.2	29,537.4	97.3
Total		569	797,194.9	946,877.8	18.8	196	233,474.3	390,648.0	67.3

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No	Sector	No. of Projects				Projects with time overruns			
			Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	23,779.0	23,779.0	3 - 11
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	645.1	645.1	13 - 47
3	Coal	54	37,268.9	40,354.4	8.3	28	24,633.8	28,090.6	12 - 72
4	Steel	17	65,285.9	71,443.4	9.4	15	64,698.3	70,855.9	4 - 45
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
6	Petroleum	70	165,950.5	179,743.3	8.3	42	118,653.1	133,286.3	1 - 120
7	Power	103	243,029.0	259,083.9	6.6	51	120,802.2	134,161.7	1 - 102
8	Railways	129	66,990.8	157,490.0	135.1	35	26,532.8	73,528.4	3 - 235
9	Road Transport & Highways	148	101,189.1	103,127.7	1.9	90	50,425.8	52,337.6	2 - 112
10	Shipping & Ports	19	15,617.1	17,700.8	13.3	6	6,223.1	7,475.2	5 - 87
11	Telecommunications	13	5,699.2	5,520.2	-3.1	5	2,934.9	2,774.5	28 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	0	0.0	0.0	-
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total			569	797,194.9	946,877.8	18.8	277	444,788.6	535,854.2

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

Sl.No	State	No. of Projects				Projects with time overruns			
			Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Andhra Pradesh	37	31,097.1	38,550.4	24.0	12	16,954.0	21,129.5	4 - 45
2	Arunachal Pradesh	4	9,512.2	14,144.3	48.7	3	9,356.2	13,737.9	25 - 87
3	Assam	38	23,394.4	36,838.1	57.5	34	21,203.5	33,818.0	12 - 120
4	Bihar	30	26,917.6	35,131.2	30.5	11	20,239.3	24,919.6	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	13 - 13
6	Gujarat	22	33,405.1	33,607.0	0.6	5	15,029.6	14,968.3	9 - 15
7	Haryana	8	4,054.4	5,737.0	41.5	4	2,216.6	3,396.6	5 - 50
8	Himachal Pradesh	5	13,355.6	17,246.7	29.1	5	13,355.6	17,246.7	26 - 102
9	Jammu and Kashmir	10	14,927.0	34,825.6	133.3	7	13,038.7	32,618.8	10 - 201
10	Karnataka	27	47,076.4	56,439.7	19.9	10	18,014.8	18,104.0	6 - 108
11	Kerala	7	20,376.7	22,170.2	8.8	5	19,581.0	20,231.0	5 - 58
12	Madhya pradesh	20	18,545.6	18,953.8	2.2	10	4,795.0	4,921.7	8 - 69
13	Maharashtra	48	88,574.5	100,866.5	13.9	24	44,181.1	51,666.2	2 - 144
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	72 - 72
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,298.0	115.1	2	1,533.0	3,298.0	7 - 35
17	Nagaland	1	850.0	2,446.8	187.9	1	850.0	2,446.8	24 - 24
18	Odisha	30	56,171.6	63,436.9	12.9	17	49,983.9	53,325.8	3 - 136
19	Punjab	5	2,063.4	3,005.2	45.6	2	989.0	1,064.0	7 - 64
20	Rajasthan	14	21,115.8	20,928.0	-0.9	7	15,830.9	15,384.6	3 - 59
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 47
22	Tamil Nadu	32	48,788.1	61,732.8	26.5	12	17,289.5	20,372.7	3 - 87
23	Tripura	3	1,522.4	2,018.9	32.6	2	1,101.4	1,395.4	10 - 21
24	Uttar Pradesh	27	21,281.9	25,861.1	21.5	13	12,125.6	14,870.5	8 - 84
25	West Bengal	27	46,938.9	59,572.6	26.9	12	24,221.2	30,149.7	3 - 141
26	Delhi	4	38,214.4	38,194.8	-0.1	0	0.0	0.0	-
27	Chhatisgarh	24	58,278.3	59,362.9	1.9	9	23,484.9	23,796.2	12 - 59
28	Jharkhand	23	14,447.4	18,632.5	29.0	11	9,609.6	9,790.9	5 - 100
29	Uttarakhand	5	7,624.2	8,564.6	12.3	4	6,097.2	7,037.6	5 - 54
30	Multi State	110	143,655.0	156,071.1	8.6	51	80,995.0	87,684.6	1 - 235
	Total	569	797,194.9	946,877.8	18.8	277	444,788.6	535,854.2	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No	Sector	No. of Projects				Projects with time overruns			
			Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	23,779.0	23,779.0	3 - 11
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	645.1	645.1	13 - 47
3	Coal	54	37,268.9	40,354.4	8.3	28	24,633.8	28,090.6	12 - 72
4	Steel	17	65,285.9	71,443.4	9.4	13	63,227.8	69,385.3	4 - 45
5	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	Petroleum	70	165,950.5	179,743.3	8.3	40	117,917.9	130,948.5	1 - 94
7	Power	103	243,029.0	259,083.9	6.6	51	120,802.2	134,161.7	1 - 102
8	Railways	129	66,990.8	157,490.0	135.1	33	26,017.8	71,800.8	3 - 235
9	Road Transport & Highways	148	101,189.1	103,127.7	1.9	90	50,425.8	52,337.6	2 - 112
10	Shipping & Ports	19	15,617.1	17,700.8	13.3	2	4,728.0	5,610.0	18 - 40
11	Telecommunications	13	5,699.2	5,520.2	-3.1	5	2,934.9	2,774.5	28 - 59
12	Urban Development	4	44,245.2	49,518.1	11.9	0	0.0	0.0	-
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		569	797,194.9	946,877.8	18.8	266	435,112.2	519,533.1	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of projects				Projects with cost overruns			
			Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	54	39,871.3	40,354.4	1.2	5	2,211.1	2,694.1	21.8
4	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
5	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
6	Petroleum	70	179,842.1	179,743.3	-0.1	3	30,840.7	34,849.0	13.0
7	Power	103	245,222.9	259,083.9	5.7	18	43,738.7	57,599.8	31.7
8	Railways	129	96,046.0	157,490.0	64.0	81	53,100.7	114,576.4	115.8
9	Road Transport & Highways	148	101,355.6	103,127.7	1.7	11	3,324.3	5,445.2	63.8
10	Shipping & Ports	19	17,488.0	17,700.8	1.2	5	3,157.6	3,783.5	19.8
11	Telecommunications	13	5,699.2	5,520.2	-3.1	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		569	852,976.7	946,877.8	11.0	135	172,600.5	271,698.8	57.4

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of projects				Projects with time & cost overruns			
			Original Cost	Anticipated Cost	Cost overrun(%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	54	37,268.94	40,354.39	8.28	0	0.00	0.00	0- 0
4	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	24- 24
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	70	165,950.52	179,743.33	8.31	11	21,026.22	34,896.99	13- 120
7	Power	103	243,028.99	259,083.86	6.61	1	596.45	1,007.16	0- 0
8	Railways	129	66,990.82	157,489.96	135.09	17	6,331.52	23,220.15	0- 144
9	Road Transport & Highways	148	101,189.08	103,127.70	1.92	0	0.00	0.00	0- 0
10	Shipping & Ports	19	15,617.12	17,700.82	13.34	5	5,400.70	6,860.25	10- 87
11	Telecommunications	13	5,699.24	5,520.22	-3.14	0	0.00	0.00	0- 0
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		569	797194.85	946877.84	18.78	37	40919.39	77526.72	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

Sl.No.	Sector	No. of projects				Projects with time & cost overruns			
			Original Cost	Anticipated Cost	Cost overrun(%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	0	0.00	0.00	0- 0
3	Coal	54	37,268.94	40,354.39	8.28	5	7,938.86	11,573.95	19- 55
4	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	10- 45
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	70	165,950.52	179,743.33	8.31	16	54,006.46	72,871.23	2- 120
7	Power	103	243,028.99	259,083.86	6.61	15	38,706.92	52,066.44	10- 102
8	Railways	129	66,990.82	157,489.96	135.09	31	23,203.93	70,204.39	12- 235
9	Road Transport & Highways	148	101,189.08	103,127.70	1.92	10	3,158.01	5,252.10	21- 110
10	Shipping & Ports	19	15,617.12	17,700.82	13.34	3	4,878.00	6,210.00	18- 87
11	Telecommunications	13	5,699.24	5,520.22	-3.14	2	1,065.85	1,089.32	34- 54
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		569	797194.85	946877.84	18.78	89	162447.53	258403.86	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>Fertilisers</u>						
1	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT	01/2010	1,478.63	01/2013	1,478.63	04/2013	1,133.00
	<u>Power</u>						
2	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA	02/2009	1,347.32	02/2012	1,347.32	05/2013	1,206.10
3	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G	07/2009	1,736.36	06/2012	1,736.36	05/2013	1,240.75
	<u>Road Transport & Highways</u>						
4	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	12/2003	340.68	03/2008	340.68	05/2013	400.56

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl. No	Project	DOA	Cost	DOC	Cost	DOC
	<u>Power</u>					
1	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. &	6/2012	1,909.24	6/2015	1,909.24	6/2015
2	GAS TURBINE GENERATION SET	7/2009	216.88	10/2011	216.88	7/2013
3	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN	9/2012	871.35	3/2015	871.35	3/2015
4	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	8/2008	144.02	6/2012	204.29	9/2013
5	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN	8/2008	126.18	6/2012	159.54	9/2013

Milestones (Cumulative due & achieved)

Total	3434
Achieved up to month	1308


List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs. crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Civil Aviation</u>						
1	C/o new Airport at Pakyong(Sikkim) Airport AAI	309.46	309.46	01/2011	12/2013	12/2014	12
	<u>Coal</u>						
2	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
	<u>Steel</u>						
3	EXPANSION OF RINL/VSP FROM 3 MTPY- 6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	06/2013	07/2013	1
4	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	10/2012	06/2013	08/2013	2
5	Augmentation of Iron Ore Storage in RMHP RINL	480.00	450.00	05/2012	06/2013	08/2013	2
6	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	04/2013	06/2013	2
7	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	04/2013	06/2013	2
	<u>Petroleum</u>						
8	Fluidized catalytic cracking unit(FCCU) revamp IOCL	1,000.00	1,000.00	01/2013	08/2013	09/2013	1
9	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH ONGC	740.02	740.02	03/2010	05/2013	07/2013	2
10	DEVELOPMENT OF B-46 CLUSTER FIELD ONGC	1,436.21	1,436.21	07/2010	05/2013	07/2013	2
11	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU BPCL	825.00	1,827.00	04/2013	04/2013	06/2013	2
12	MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	05/2013	07/2013	2
13	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT IOCL	341.50	341.50	02/2013	04/2013	07/2013	3
14	DEV OF G1 AND GS-15 (ONGCL) ONGC	429.82	2,735.65	04/2006	06/2013	02/2014	8
	<u>Power</u>						
15	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	06/2013	07/2013	1
16	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII PGCIL	524.40	524.40	04/2015	04/2015	05/2015	1
17	URI H.E.P STAGE -II (NHPC) NHPC	1,729.29	2,081.00	11/2009	05/2013	07/2013	2
18	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B PGCIL	160.32	160.32	10/2012	05/2013	07/2013	2

List of projects reporting additional delays


Sl. No	Project name	Cost (Rs. crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
19	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	09/2013	12/2013	3
	<u>Railways</u>						
20	CHANDIGARH-LUDHIANA(NEW BG LINE),NR NR	248.44	1,115.21	12/2012	02/2013	04/2013	2
21	DAUSA-GANGAPUR CITY(NL),NWR NWR	151.84	410.08	N.A.	03/2013	03/2014	12
22	New Work for Construction of Metro railway from Ba RVNL	2,069.60	2,298.42	03/2014	03/2014	03/2016	24
	<u>Road Transport & Highways</u>						
23	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	05/2013	06/2013	1
24	GANJAM-ICCHAPURUM,NH-5(NHAI) NHAI	263.27	263.27	02/2004	05/2013	06/2013	1
25	GWALIOR BYPASS, NH-75,3 NHAI	300.93	300.93	10/2009	05/2013	06/2013	1
26	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	05/2013	06/2013	1
27	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	06/2013	08/2013	2
28	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	06/2013	08/2013	2
29	SONAPUR TO GUWAHTI (AS-3) NHAI	245.00	245.00	03/2008	06/2013	08/2013	2
30	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 NHAI	941.00	941.00	01/2011	05/2013	08/2013	3
31	Trichy Bypass NHAI	374.00	374.00	05/2013	05/2013	08/2013	3
32	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	05/2013	09/2013	4
33	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	05/2013	12/2013	7
34	NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	05/2013	12/2013	7
35	Indore-Jhabua-Gujrat/MP NHAI	1,175.00	1,175.00	04/2013	04/2013	12/2013	8
36	NIROLI-ROXY-RAJAMUNDA NHAI	586.00	586.00	01/2014	01/2014	12/2014	11
37	GWALIOR-JHANSI, NH-75 NHAI	604.00	604.00	12/2009	07/2013	12/2014	17
	<u>Shipping & Ports</u>						
38	DEEPENING OF CHANNEL AT PARADIP PORT TRUST	154.84	253.36	N.A.	01/2009	12/2010	23
39	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A PORT TRUST	800.00	1,370.00	10/2008	10/2008	08/2012	46
	<u>Telecommunications</u>						
40	Supply Installation testing and commissioning of Rural Wimax BSNL	1,148.19	964.37	05/2011	08/2013	09/2013	1
41	GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	930.60	11/2010	06/2013	09/2013	3

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs. crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
42	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES BSNL	149.15	158.72	06/2009	08/2013	12/2013	4
43	Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	08/2013	12/2013	4
	43						

Graphical Analysis of All Projects w.r.t. Original Schedule

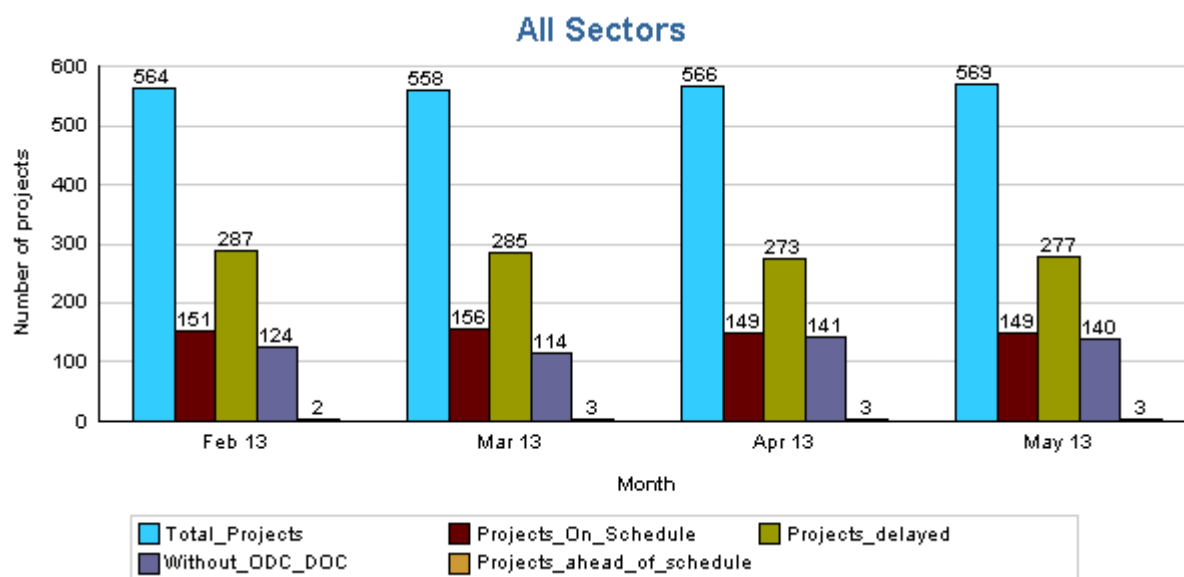


Break-up of 277 Delayed projects in May 2013

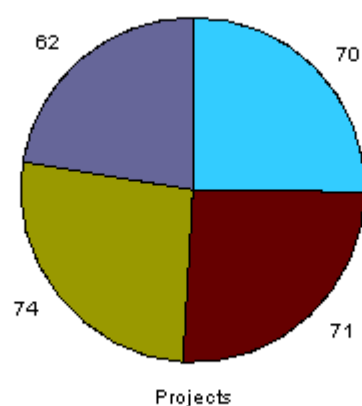


Delay in Months



Graphical Analysis of All Projects w.r.t. Revised Schedule

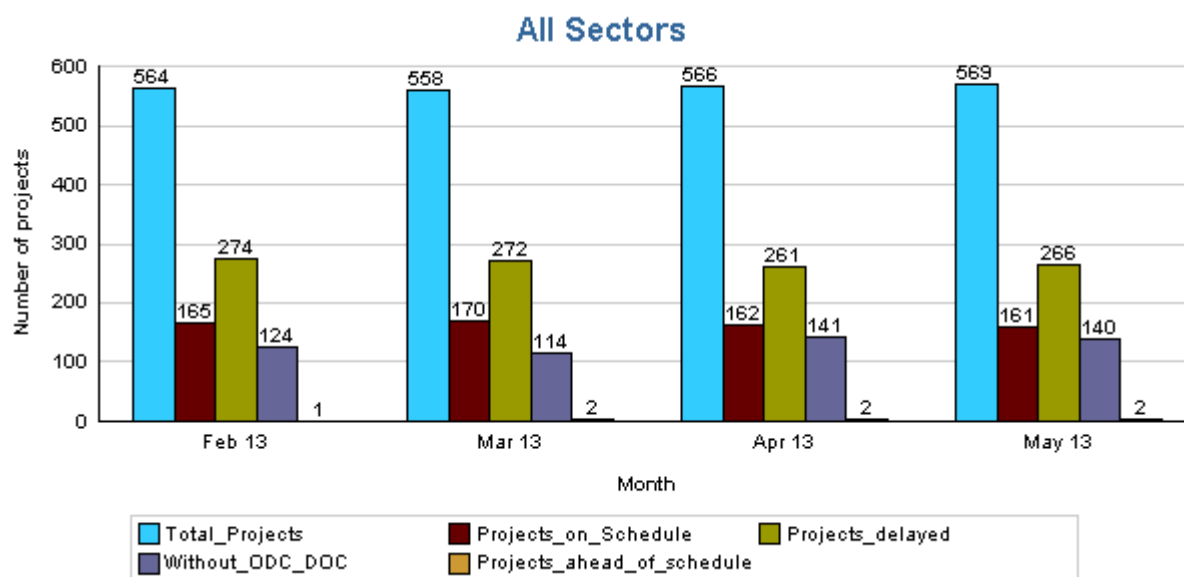


Break-up of 266 Delayed projects in May 2013

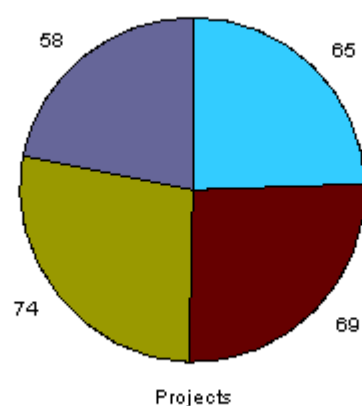

Delay in Months



Graphical Analysis of Urban Development Sector

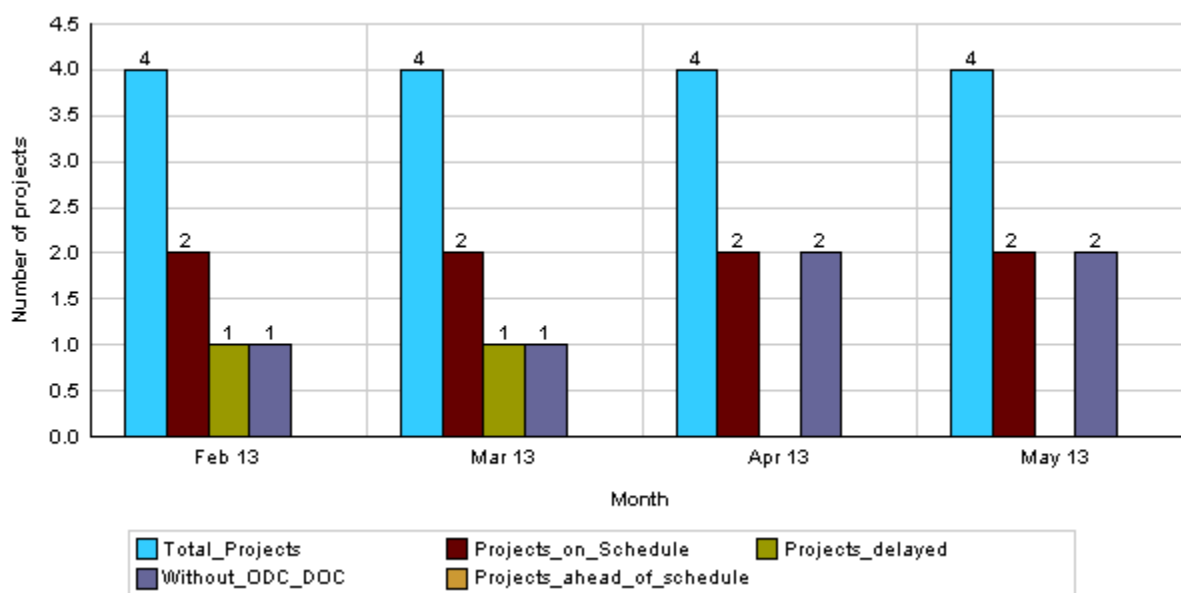


Break-up of 0 Delayed projects in May 2013

Delay in Months



Graphical Analysis of Telecommunications Sector

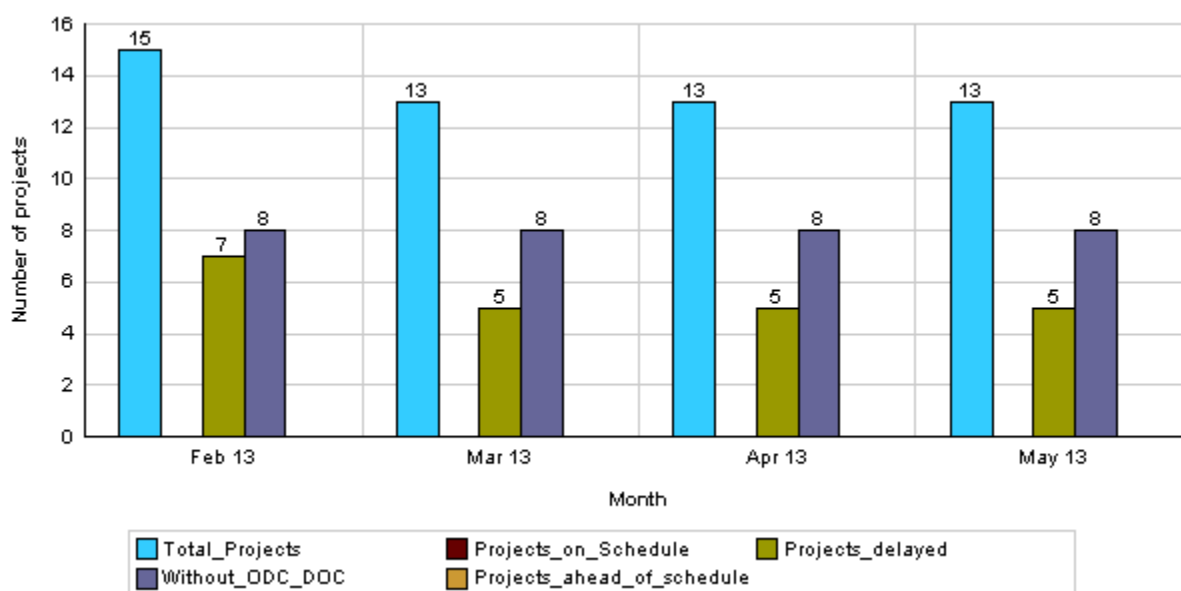


Break-up of 5 Delayed projects in May 2013




Delay in Months



Graphical Analysis of Shipping & Ports Sector

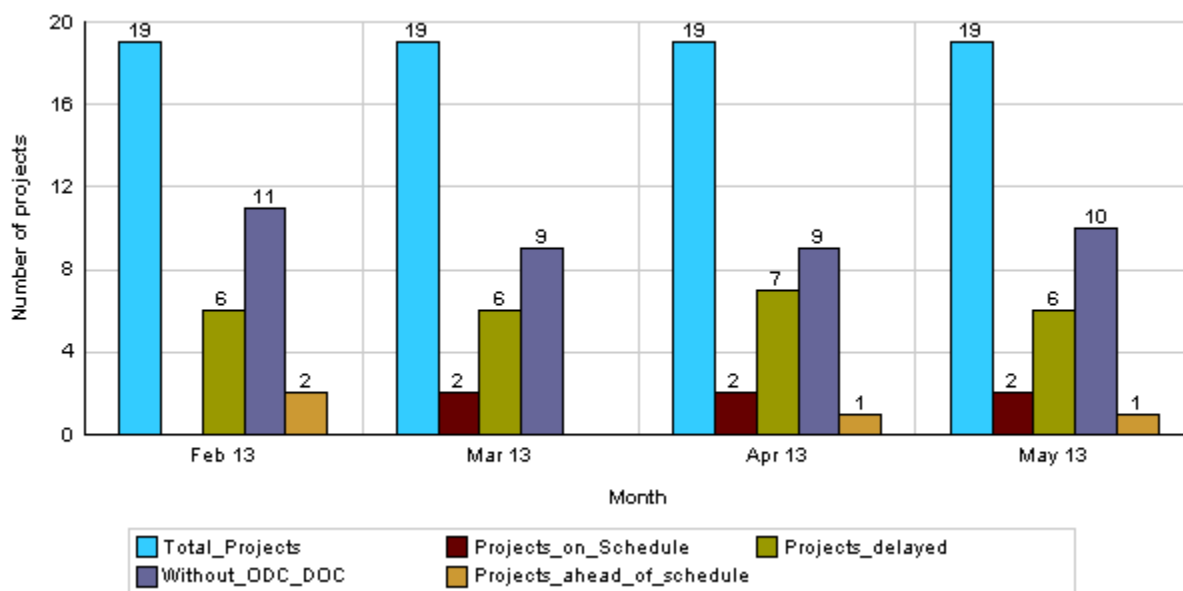


Break-up of 6 Delayed projects in May 2013

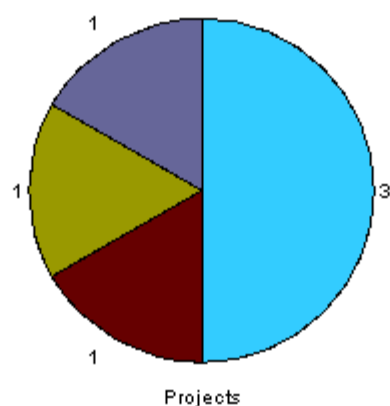


Delay in Months



Graphical Analysis of Road Transport & Highways Sector

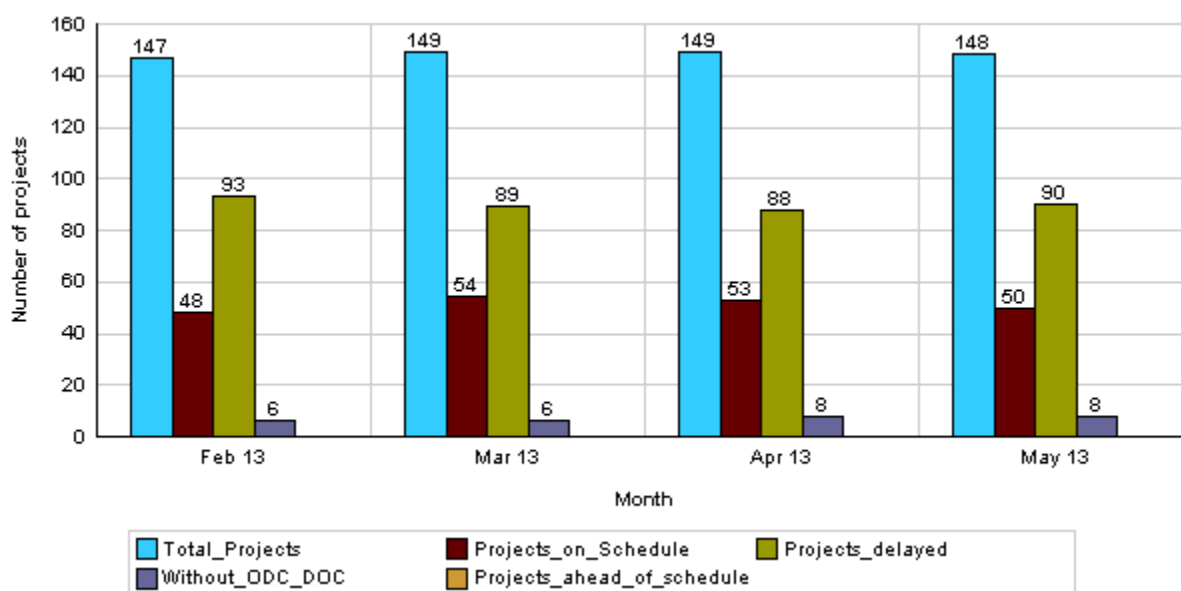


Break-up of 90 Delayed projects in May 2013

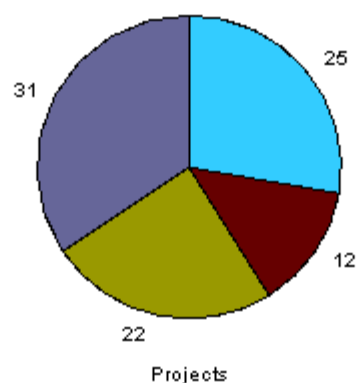


Delay in Months



Graphical Analysis of Railways Sector

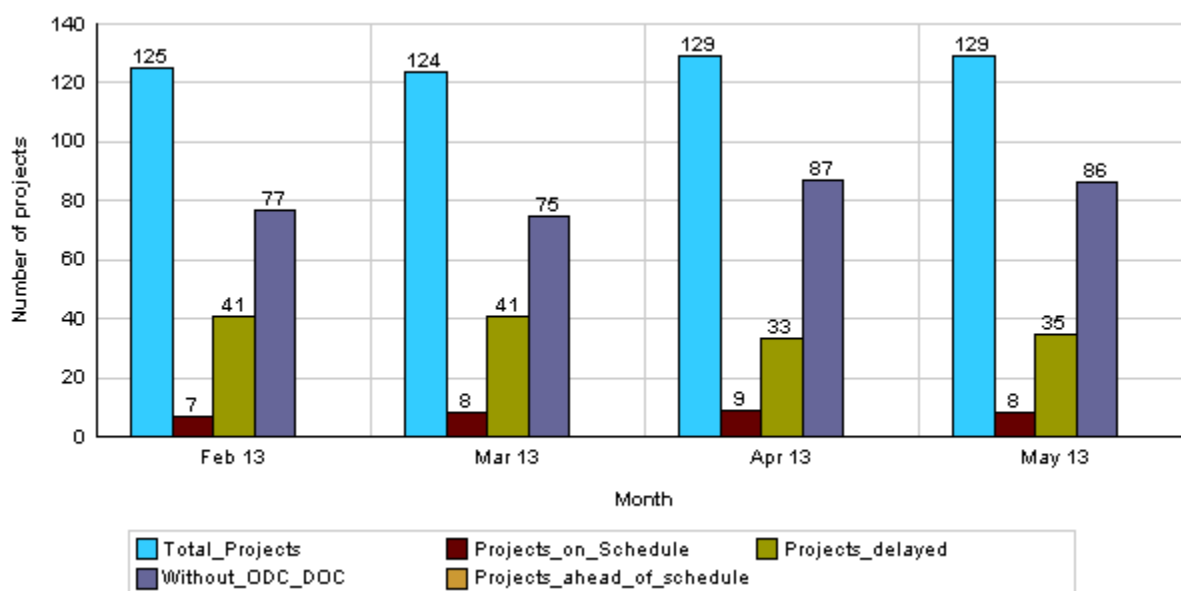


Break-up of 35 Delayed projects in May 2013

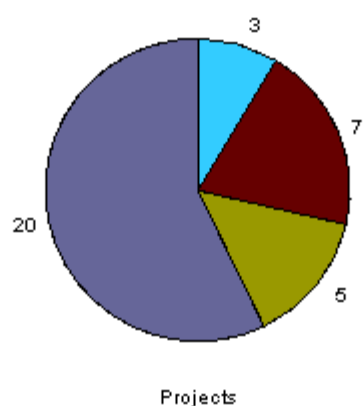


Delay in Months



Graphical Analysis of Power Sector

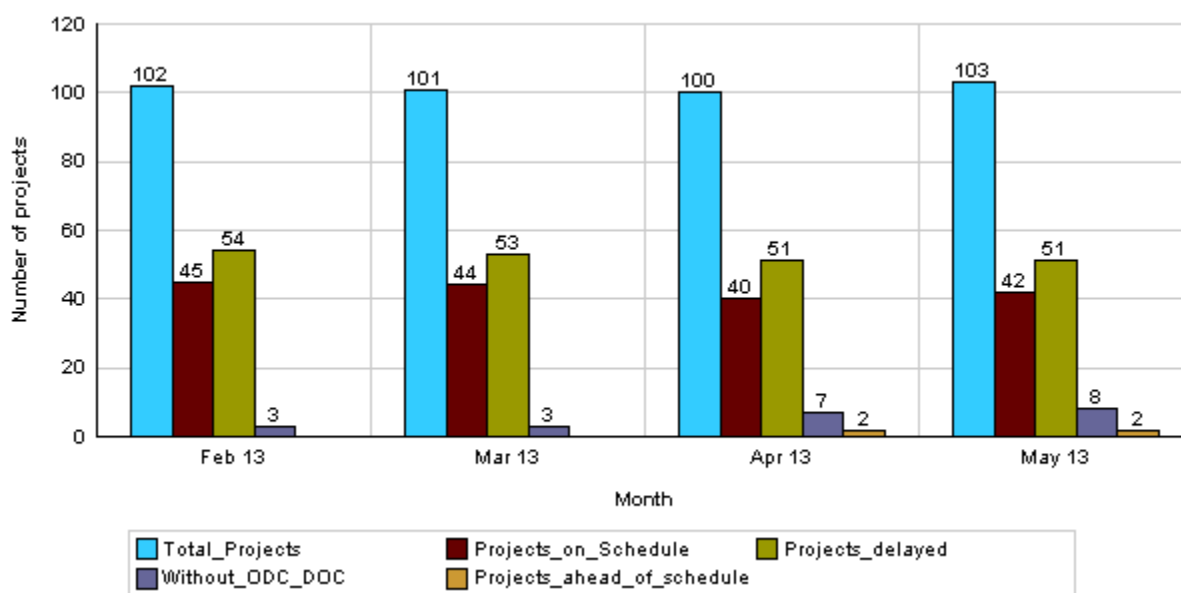


Break-up of 51 Delayed projects in May 2013

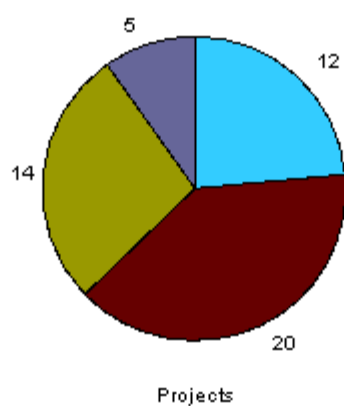


Delay in Months



Graphical Analysis of Petroleum Sector

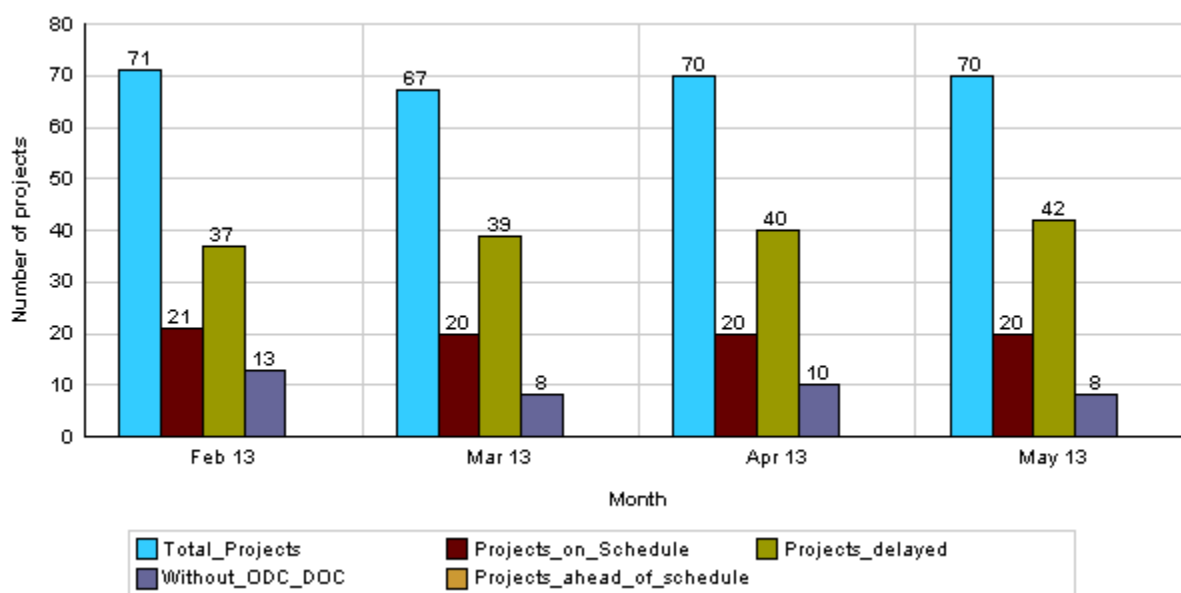


Break-up of 42 Delayed projects in May 2013

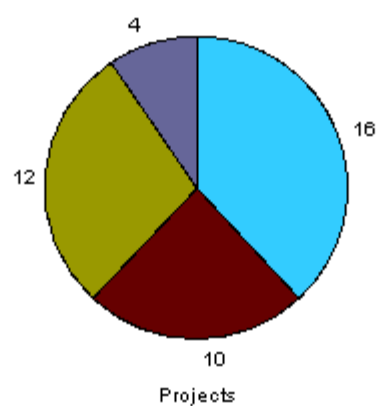


Delay in Months



Graphical Analysis of Steel Sector

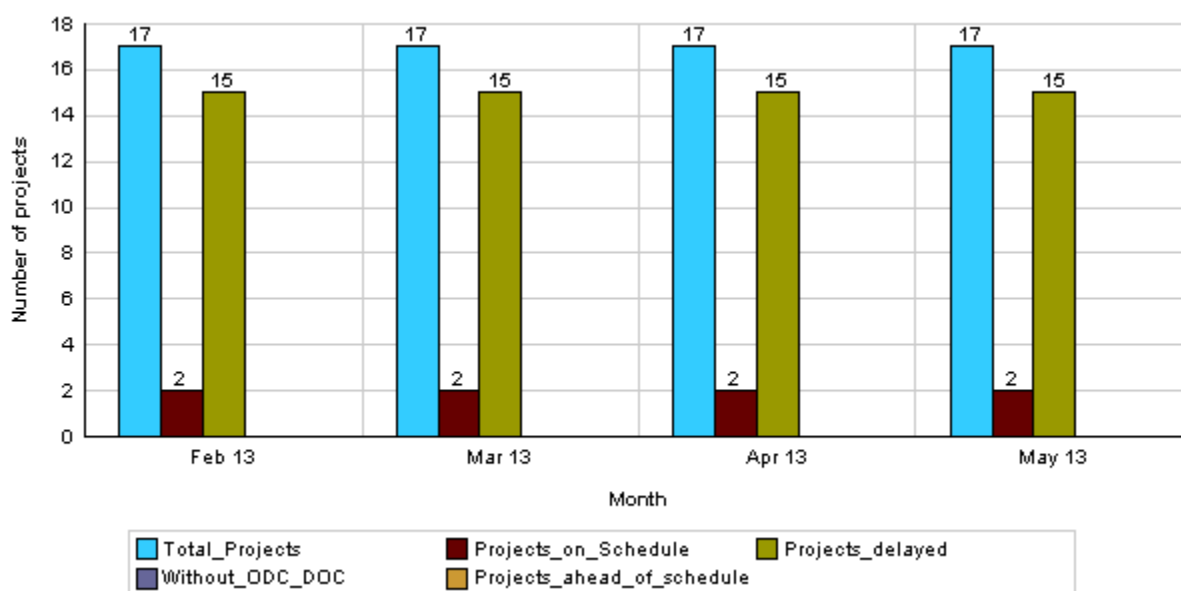


Break-up of 15 Delayed projects in May 2013

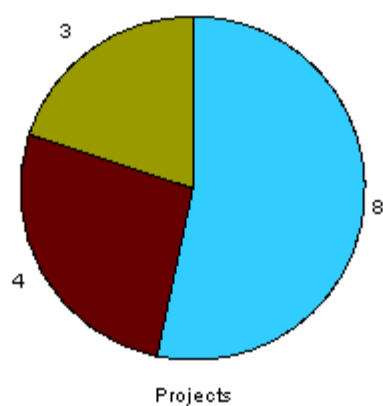


Delay in Months



Graphical Analysis of Coal Sector

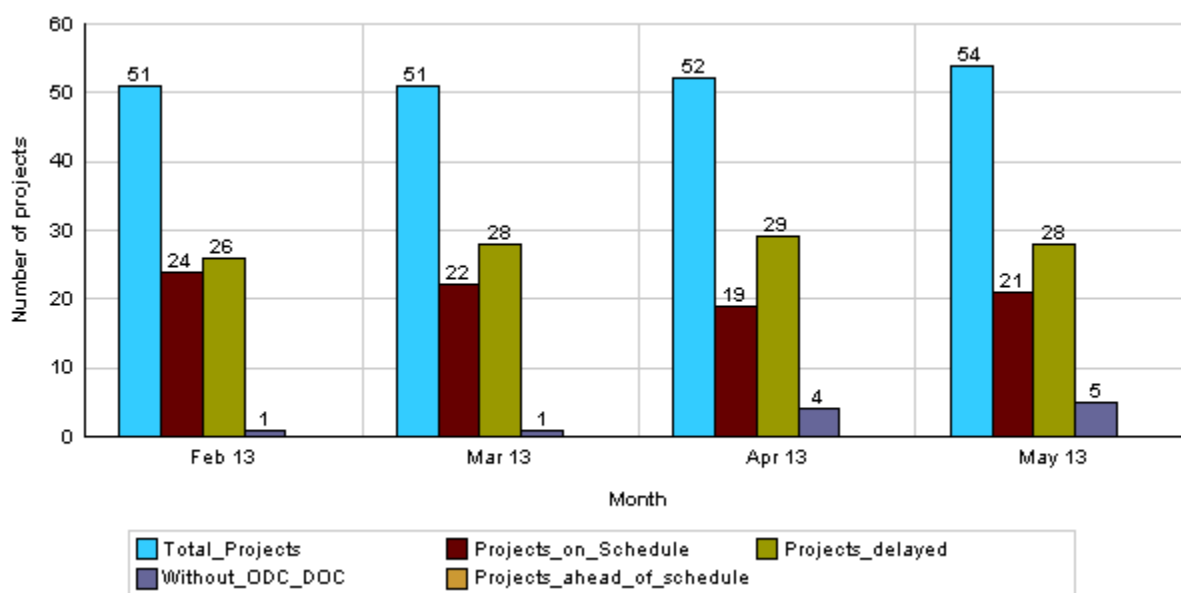


Break-up of 28 Delayed projects in May 2013

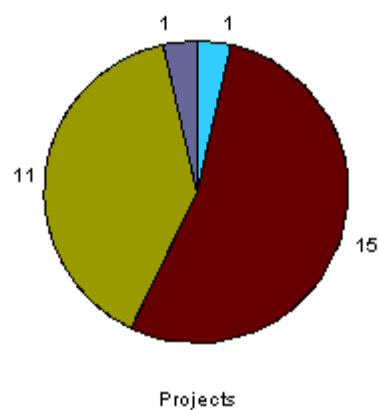


Delay in Months



Graphical Analysis of Civil Aviation Sector

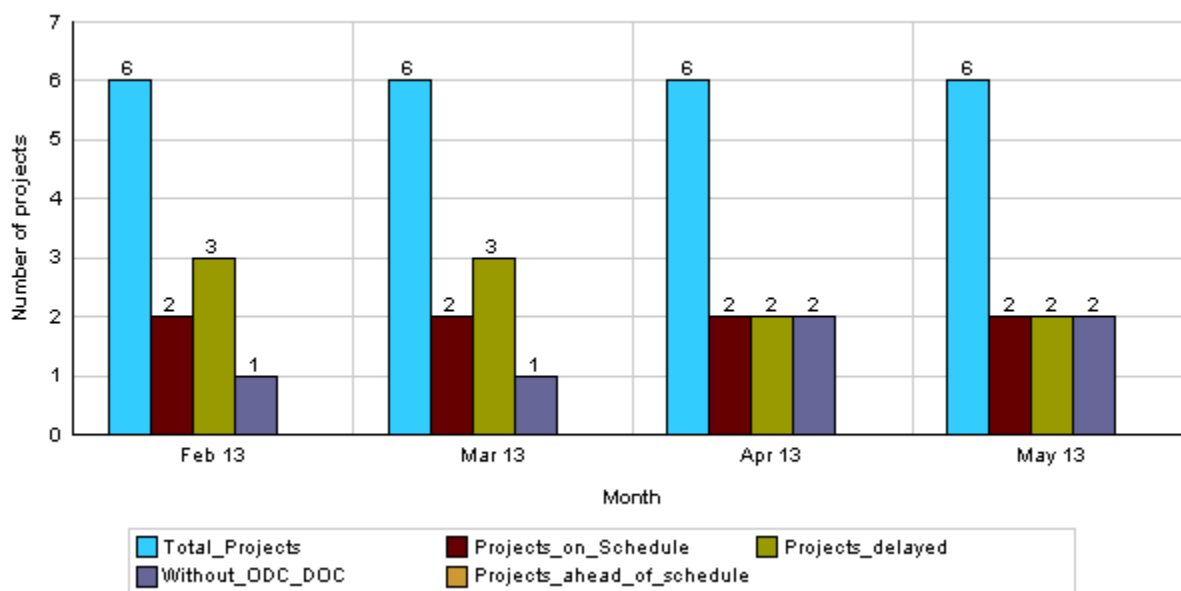


Break-up of 2 Delayed projects in May 2013

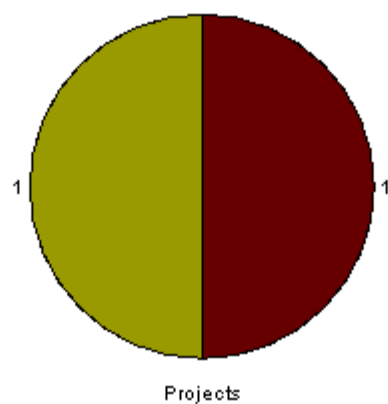

Delay in Months



Graphical Analysis of Atomic Energy Sector

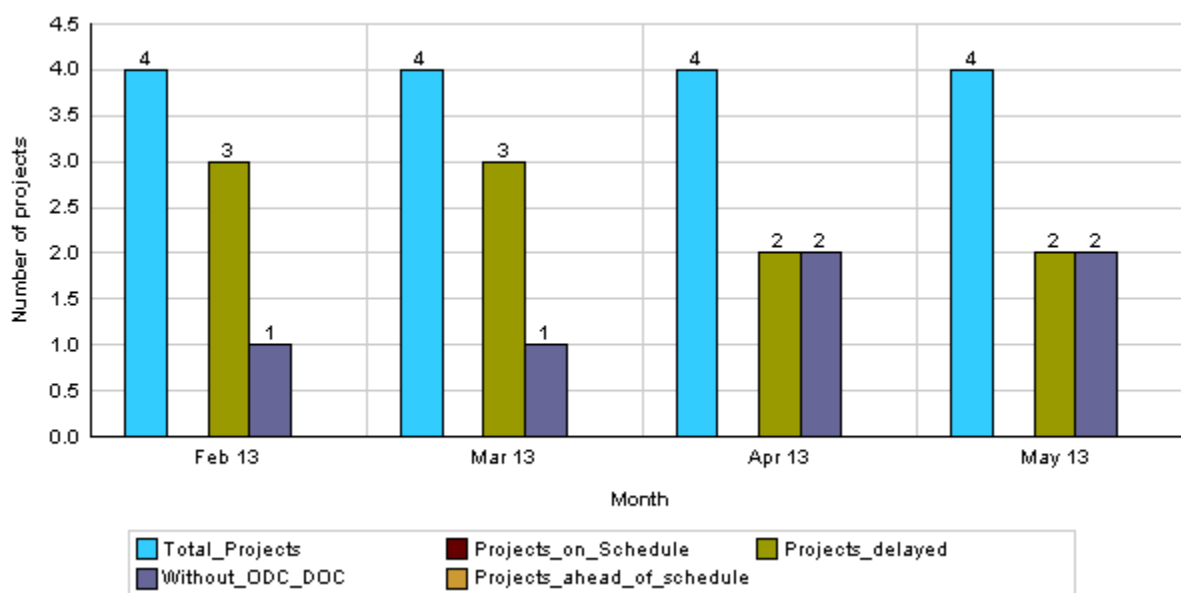

Break-up of 2 Delayed projects in May 2013



Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
Atomic Energy	4	40,442.00	40,442.00	46,726.00	24,795.48
Civil Aviation	6	5,473.58	5,680.58	6,063.07	5,287.95
Coal	54	37,268.94	39,871.33	40,354.39	14,787.57
Steel	17	65,285.87	67,562.15	71,443.41	40,721.93
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	70	165,950.52	179,842.06	179,743.33	82,724.37
Power	103	243,028.99	245,222.85	259,083.86	118,566.19
Railways	129	66,990.82	96,045.96	157,489.96	63,875.57
Road Transport & Highways	148	101,189.08	101,355.58	103,127.70	75,502.51
Shipping & Ports	19	15,617.12	17,487.95	17,700.82	8,592.87
Telecommunications	13	5,699.24	5,699.24	5,520.22	1,901.95
Urban Development	4	44,245.18	44,304.08	49,518.08	5,969.99
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	569	797,194.85	852,976.68	946,877.84	447,272.38

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(May,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,771.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	17,270.00	16,007.00	12/2008 -	03/2013	-	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,080.48	09/2010 -	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,937.00	12/2016 -	03/2017	3(O) -	0/69
	Total		40,442.00 -	46,726.00	24,795.48				47/327
	<u>Civil Aviation</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,462.87	05/2011 -	03/2013	-	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	226.70	01/2011 04/2013	12/2014	47(O) 20(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	215.29	05/2012 -	06/2013	13(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,903.36	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	452.00	102.76	03/2015 -	03/2015	0(O) -	0/0
10	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	376.97	06/2013 -	06/2013	0(O) -	0/0
	Total		5,473.58 -	6,063.07	5,287.95				0/0
	<u>Coal</u>								
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	704.25	03/2013 09/2012	10/2014	19(O) 25(R)	18/22
12	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	81.18	03/2016 -	03/2016	0(O) -	2/6
13	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	438.86	03/2016 03/2016	03/2016	0(O) 0(R)	2/4
14	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	102.56	03/2012 -	03/2014	24(O) -	5/9
15	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.49	03/2011 -	03/2014	36(O) -	0/2

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	119.73	03/2010 -	03/2015	60(O) -	4/5
17	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	50.53	03/2016 -	03/2016	0(O) -	0/6
18	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00 -	490.10	123.40	03/2017 -	03/2017	0(O) -	6/12
19	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	43.29	03/2014 03/2014	03/2014	0(O) 0(R)	1/4
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	159.13	03/2015 03/2015	03/2015	0(O) 0(R)	0/3
21	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/2
22	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	264.13	03/2014 -	03/2016	24(O) -	2/8
23	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60(O) -	0/2
24	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,240.49	03/2014 -	03/2016	24(O) -	6/12
25	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,406.74	03/2014 -	03/2016	24(O) -	10/15
26	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87 -	395.87	84.50	03/2015 -	03/2015	0(O) -	2/12
27	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	126.19	03/2013 -	03/2015	24(O) -	5/10
28	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
29	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	14.02	03/2015 -	03/2015	0(O) -	4/31
30	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
31	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72(O) -	0/2
32	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	85.21	12/2012 -	03/2016	39(O) -	9/44
33	KALYANIKHANI OPENCAS PROJECT - [N06000101]SCCL,Andhra Pradesh	07/2012	417.33 -	417.33	0.02	07/2016 -	07/2016	0(O) -	0/0
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	113.13	03/2013 -	03/2015	24(O) -	6/11
35	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46 -	162.46	34.71	03/2014 -	03/2014	0(O) -	0/3
36	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
37	KHADIA EXPANSION OPENCAS PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	4.68	03/2018 03/2018	03/2018	0(O) 0(R)	0/3
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.34	03/2013 -	03/2014	12(O) -	2/5

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	109.05	03/2010 -	03/2014	48(O) -	7/10
40	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	701.91	03/2013 -	03/2013	-	0/9
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	24.38	07/2012 -	03/2016	44(O) -	1/5
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24(O) -	1/6
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.29	03/2012 -	03/2015	36(O) -	10/20
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	29.84	12/2015 -	12/2017	24(O) -	1/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.26	03/2012 -	03/2015	36(O) -	0/2
49	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60(O) -	0/4
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.01	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.20	03/2013 -	03/2015	24(O) -	2/4
53	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24(O) -	0/2
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	215.46	03/2012 -	-	-	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
56	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.31	-	03/2016	-	0/0
57	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,Andhra Pradesh	06/2012	365.01 -	365.01	-	06/2015 -	06/2015	0(O) -	0/0
58	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	35.71	03/2015 -	03/2015	0(O) -	6/31
59	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85 -	510.85	259.21	03/2016 -	03/2016	0(O) -	1/4
60	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	49.73	03/2012 -	-	-	12/42
61	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72 -	447.72	44.50	03/2016 -	03/2016	0(O) -	0/10

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
62	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,714.27	06/2009 -	01/2014	55(O) -	20/24
63	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,284.55	03/2012 -	03/2014	24(O) -	20/39
64	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	117.18	03/2012 -	03/2016	48(O) -	0/4
	Total		37,268.94 -	40,354.39	14,787.57				203/665
	<u>Steel</u>								
65	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	291.02	04/2013 12/2013	12/2013	8(O) 0(R)	16/19
66	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	252.86	08/2010 -	06/2013	34(O) -	0/1
67	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	258.32	02/2011 -	06/2013	28(O) -	2/3
68	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	198.57	05/2013 11/2013	11/2013	6(O) 0(R)	12/21
69	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	246.54	05/2012 -	08/2013	15(O) -	0/1
70	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	350.85	12/2011 03/2012	12/2013	24(O) 21(R)	16/21
71	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	140.71	10/2012 -	08/2013	10(O) -	3/4
72	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	332.65	54.07	08/2014 -	08/2014	0(O) -	0/0
73	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	4.29	11/2013 -	03/2014	4(O) -	1/1
74	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	5,179.68	03/2013 -	03/2014	12(O) -	22/27
75	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	2,624.65	12/2011 -	12/2013	24(O) -	16/16
76	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	750.85	12/2012 -	12/2013	12(O) -	10/12
77	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,087.79	12/2011 -	12/2013	24(O) -	19/19
78	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 -	12,291.00	10,366.21	10/2009 -	07/2013	45(O) -	63/67

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
79	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 11,812.00	11,812.00	6,841.66	03/2013 -	12/2013	9(O) -	11/14
80	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	70.98	10/2013 -	03/2014	5(O) -	0/1
81	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	254.90	2.88	12/2014 -	12/2014	0(O) -	0/0
	Total		65,285.87 -	71,443.41	40,721.93				191/227
	<u>Petrochemicals</u>								
82	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20(O) 0(R)	19/29
	Total		5,460.61 -	8,920.00	4,510.51				19/29
	<u>Petroleum</u>								
83	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	-	06/2012 -	03/2014	21(O) -	0/0
84	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	06/2013	12(O) -	0/0
85	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	07/2013	19(O) -	0/0
86	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,410.63	03/2013 -	03/2014	12(O) -	0/0
87	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	586.00	5.55	07/2015 -	08/2015	1(O) -	0/0
88	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014	0(O) -	0/0
89	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014	0(O) -	0/0
90	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	540.92	283.34	07/2012 07/2012	-	-	0/17
91	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	180.06	02/2013 -	07/2013	5(O) -	38/42
92	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00 -	190.00	48.09	03/2014 -	03/2014	0(O) -	0/24
93	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.95	09/2011 -	12/2013	27(O) -	0/0
94	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	394.00	312.61	- -	03/2013	-	18/19
95	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	273.53	05/2013 -	11/2013	6(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
96	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	152.89	3.79	06/2013 -	06/2013	0(O) -	0/0
97	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	35.90	08/2013 -	01/2014	5(O) -	0/0
98	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	95.34	09/2012 -	09/2013	12(O) -	0/0
99	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8(O) -	0/0
100	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	486.00	52.05	09/2013 -	09/2013	0(O) -	0/0
101	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	329.06	- -	-	-	0/0
102	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94(O) 20(R)	0/0
103	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,464.10	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
104	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,881.73	09/2010 03/2012	06/2013	33(O) 15(R)	0/0
105	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	920.79	07/2010 05/2012	07/2013	36(O) 14(R)	0/0
106	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	06/2013	54(O) 2(R)	0/0
107	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,441.01	09/2011 05/2012	06/2013	21(O) 13(R)	5/76
108	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,663.16	09/2011 03/2012	06/2013	21(O) 15(R)	54/59
109	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	215.02	03/2013 -	06/2013	3(O) -	0/0
110	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
111	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,301.61	03/2013 03/2014	04/2014	13(O) 1(R)	0/0
112	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	215.26	11/2012 -	10/2013	11(O) -	0/0
113	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	883.68	01/2014 -	01/2014	0(O) -	0/0
114	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	51.17	12/2014 -	12/2014	0(O) -	0/0
115	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	541.27	01/2013 -	09/2013	8(O) -	18/18

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
116	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013	2(O) -	0/167
117	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	712.11	05/2015 -	05/2015	0(O) -	0/0
118	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
119	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
120	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1(O) -	0/0
121	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	06/2013	87(O) 3(R)	6/6
122	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	20.90	12/2015 -	05/2016	5(O) -	0/0
123	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	2,665.65	113.16	03/2015 -	03/2015	0(O) -	0/0
124	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.36	01/2013 -	12/2015	35(O) -	0/0
125	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.49	10/2010 -	12/2014	50(O) -	0/0
126	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	289.64	01/2012 -	-	-	0/1
127	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	1,211.00	12/2012 -	-	-	0/21
128	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	666.00	-	11/2015 -	11/2015	0(O) -	0/0
129	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,295.14	01/2012 -	07/2013	18(O) -	0/108
130	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,124.72	09/2012 -	09/2013	12(O) -	0/0
131	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	06/2013	37(O) 3(R)	0/0
132	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015	0(O) -	0/0
133	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	279.00	-	12/2014 -	12/2014	0(O) -	0/0
134	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 973.79	973.79	729.51	03/2011 05/2011	05/2013	26(O) 24(R)	0/0
135	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	704.59	03/2010 03/2012	07/2013	40(O) 16(R)	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
136	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	913.00	30.60	07/2015 -	07/2015	0(O) -	0/0
137	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	21,762.00	11/2012 -	03/2014	16(O) -	60/100
138	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	821.13	09/2012 -	-	-	5/11
139	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	894.36	02/2014 -	02/2014	0(O) -	0/0
140	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	176.83	04/2012 -	06/2013	14(O) -	0/0
141	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	336.94	05/2014 -	05/2014	0(O) -	0/0
142	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	701.47	07/2012 -	10/2013	15(O) -	0/31
143	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	- -	52/53
144	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64 -	1,210.64	61.81	11/2015 -	11/2015	0(O) -	4/25
145	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	4.89	12/2014 -	12/2014	0(O) -	0/0
146	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	671.01	04/2012 -	-	-	0/0
147	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26(O) -	0/0
148	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26(O) -	0/0
149	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.81	-	08/2014 -	08/2014	0(O) -	0/0
150	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	170.77	08/2012 -	06/2013	10(O) -	0/0
151	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	249.68	03/2012 -	12/2013	21(O) -	13/20
152	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	34.77	12/2013 -	12/2013	0(O) -	0/0
	Total		165,950.52 -	179,743.33	82,724.37				282/807
	Power								

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
153	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,797.73	08/2012 -	03/2014	19(O) -	0/11
154	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	817.81	05/2012 -	09/2013	16(O) -	0/8
155	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/7
156	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,000.00	08/2013 -	09/2014	13(O) -	10/19
157	BARH STPP STAGE I (3X660MW) NTPC - [N180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,457.00	12/2009 -	02/2017	86(O) -	27/47
158	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,837.00	07/2011 -	10/2015	51(O) -	5/28
159	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	-	06/2012 -	09/2013	15(O) -	0/0
160	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	913.00	731.93	02/2011 10/2012	01/2013	-	2/4
161	COMMON SYS. ASSOCIATED PART-B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015	0(O) -	0/20
162	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	1,909.24	98.76	06/2015 -	06/2015	0(O) -	0/0
163	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	699.90	08/2014 -	08/2014	0(O) -	7/20
164	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	39.21	06/2014 -	06/2014	0(O) -	0/20
165	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
166	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	3.60	10/2014 -	10/2014	0(O) -	0/0
167	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	-	06/2012 -	09/2013	15(O) -	0/0
168	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	845.25	09/2014 -	09/2014	0(O) -	7/20
169	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	881.79	10/2009 -	12/2013	50(O) -	5/15
170	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	639.72	11/2012 -	09/2014	22(O) -	2/13

Sector Wise Details									
(May,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
171	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
172	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	892.93	05/2014 -	05/2014	0(O) -	1/11
173	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,090.11	08/2013 -	08/2013	0(O) -	1/12
174	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	-	10/2011 -	07/2013	21(O) -	0/0
175	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	216.50	08/2014 -	08/2014	0(O) -	1/16
176	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	928.77	12/2013 -	12/2013	0(O) -	1/12
177	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	76.74	10/2012 -	07/2013	9(O) -	4/14
178	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	899.72	12/2007 12/2009	-	-	2/11
179	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	2,496.90	2,270.21	05/2013 06/2016	03/2017	46(O) 9(R)	7/22
180	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,497.94	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
181	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	4,968.00	04/2009 -	09/2014	65(O) -	0/9
182	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,573.00	12/2016 -	12/2016	0(O) -	10/14
183	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,868.68	09/2008 -	03/2013	-	15/23
184	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	1,056.00	05/2017 -	05/2017	0(O) -	4/4
185	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017	0(O) -	0/15
186	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
187	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	942.00	09/2016 -	09/2016	0(O) -	14/14
188	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	739.41	08/2010 01/2013	10/2013	38(O) 9(R)	0/3
189	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,911.99	08/2013 -	06/2015	22(O) -	0/17

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.41	02/2012 -	12/2013	22(O) -	1/13
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	352.26	11/2011 -	07/2014	32(O) -	0/11
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	362.90	11/2011 -	12/2013	25(O) -	1/14
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	130.43	01/2013 -	09/2013	8(O) -	1/6
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	264.68	07/2013 -	03/2014	8(O) -	1/11
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	812.28	04/2013 -	03/2014	11(O) -	0/11
196	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	136.63	11/2014 -	11/2014	0(O) -	1/12
197	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	70.26	03/2015 -	03/2015	0(O) -	0/15
198	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	23.70	04/2015 -	05/2015	1(O) -	0/16
199	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	550.64	11/2012 -	03/2014	16(O) -	0/11
200	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,805.96	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
201	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,455.29	09/2009 07/2014	03/2018	102(O) 44(R)	1/20
202	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	573.99	565.32	08/2012 08/2013	09/2014	25(O) 13(R)	16/22
203	RAMPUR HEP(412 MW) - [N18000024]SJVN,L Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,420.93	01/2012 -	03/2014	26(O) -	0/27
204	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,301.00	10/2012 -	11/2013	13(O) -	12/16
205	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,470.00	11/2016 -	11/2016	0(O) -	15/15
206	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	5,668.68	09/2010 08/2014	12/2017	87(O) 40(R)	11/11
207	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	84.64	04/2013 -	09/2013	5(O) -	4/15
208	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,580.90	2,050.21	08/2012 -	03/2014	19(O) -	0/5

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
209	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	50.32	06/2016 -	04/2015	-14(O) -	0/20
210	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	161.49	12/2014 -	11/2014	-1(O) -	0/0
211	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/7
212	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	87.59	08/2014 -	08/2014	0(O) -	2/19
213	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	289.64	02/2015 -	02/2015	0(O) -	0/14
214	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	143.37	11/2014 -	11/2014	0(O) -	0/16
215	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	270.30	01/2015 -	01/2015	0(O) -	3/19
216	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	99.60	08/2014 -	08/2014	0(O) -	7/20
217	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	145.70	06/2014 -	06/2014	0(O) -	7/20
218	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	149.17	06/2012 -	07/2013	13(O) -	0/3
219	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	866.87	08/2012 -	06/2014	22(O) -	0/11
220	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,827.00	03/2013 -	03/2016	36(O) -	2/15
221	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,130.75	09/2009 06/2013	05/2014	56(O) 11(R)	0/0
222	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,467.53	03/2007 09/2012	04/2013	-	25/25
223	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 -	2,978.86	483.98	07/2010 -	11/2016	76(O) -	1/10
224	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	85.88	01/2014 -	01/2014	0(O) -	3/18
225	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	281.68	08/2014 -	08/2014	0(O) -	2/19

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
226	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	541.70	10/2014 -	10/2014	0(O) -	2/18
227	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,388.27	10/2012 -	03/2014	17(O) -	0/11
228	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	373.68	01/2015 -	01/2015	0(O) -	0/20
229	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,505.63	03/2014 -	03/2014	0(O) -	4/15
230	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	19.50	08/2014 -	08/2014	0(O) -	7/20
231	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	252.96	10/2014 -	10/2014	0(O) -	3/16
232	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	758.75	639.43	01/2010 -	06/2013	41(O) -	2/11
233	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.80	11/2011 -	09/2013	22(O) -	0/4
234	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,456.16	12/2012 -	12/2013	12(O) -	0/9
235	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	-	02/2014 -	02/2014	0(O) -	3/17
236	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	290.84	10/2013 -	10/2013	0(O) -	2/13
237	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	107.52	07/2013 -	07/2013	0(O) -	0/13
238	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	578.32	12/2013 -	12/2013	0(O) -	2/13
239	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	237.25	11/2013 -	09/2014	10(O) -	7/20
240	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,027.69	03/2013 -	03/2014	12(O) -	4/15

Sector Wise Details									
(May,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
241	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,492.08	12/2013 -	03/2014	3(O) -	0/13
242	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,413.59	11/2012 -	03/2015	28(O) -	0/15
243	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	759.70	07/2014 -	07/2014	0(O) -	2/14
244	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	527.59	- -	07/2013	- -	10/29
245	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	418.04	07/2014 -	02/2015	7(O) -	1/16
246	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,278.57	12/2012 -	03/2014	15(O) -	0/11
247	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	887.65	11/2013 -	12/2014	13(O) -	5/16
248	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.70	01/2013 -	12/2014	23(O) -	5/18
249	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	-	03/2015 -	03/2015	0(O) -	0/0
250	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,738.26	11/2009 02/2013	07/2013	44(O) 5(R)	0/4
251	VINDHYACHAL STTP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	286.00	08/2015 -	08/2015	0(O) -	11/12
252	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
253	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	349.34	07/2014 -	05/2016	22(O) -	1/1
254	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	437.31	09/2010 -	03/2013	-	0/5
255	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	701.90	06/2015 -	06/2015	0(O) -	3/28
	Total		243,028.99 -	259,083.86	118,566.19				346/1354
	<u>Railways</u>								
256	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	475.23	03/2014 -	12/2015	21(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
257	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	250.82	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
258	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,820.00	113.86	- -	-	-	0/0
259	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	396.76	03/2011 03/2011	03/2011	-	0/0
260	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	725.00	551.15	06/1999 03/2011	03/2011	-	0/0
261	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	307.00	-	- -	-	-	0/0
262	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,566.00	116.70	- -	-	-	0/0
263	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	199.75	36.94	- -	-	-	0/0
264	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	404.39	17.21	03/2013 -	03/2013	-	0/0
265	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.35	- -	-	-	0/0
266	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	478.51	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
267	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	225.88	12/2010 03/2011	03/2011	-	0/0
268	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	223.23	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
269	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	89.40	04/2014 -	03/2017	35(O) -	0/0
270	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	195.64	63.83	- -	-	-	0/0
271	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015	69(O) -	0/0
272	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,735.50	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
273	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	165.13	12/2012 -	12/2013	12(O) -	0/0
274	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	191.35	03/2011 -	-	-	0/0
275	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.72	03/2012 -	-	-	0/0
276	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
277	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	954.23	12/2012 01/2013	04/2013	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
278	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	295.00	0.06	- -	-	-	0/0
279	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
280	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
281	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	243.78	25.59	- -	-	-	0/0
282	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	331.85	- -	06/2013	- -	0/0
283	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	126.84	12/2012 -	-	-	0/0
284	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	97.07	- -	-	-	0/0
285	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	216.92	- -	03/2014	- -	0/0
286	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	489.69	12/2012 12/2012	02/2013	-	0/0
287	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	914.98	634.48	- -	12/2012	-	0/0
288	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	96.15	12/2011 02/2012	02/2012	-	0/0
289	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
290	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
291	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	210.67	12/2008 -	09/2014	69(O) -	0/0
292	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	246.22	06/2013 06/2013	12/2014	18(O) 18(R)	0/0
293	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	550.42	03/1995 -	03/2013	-	0/0
294	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	280.09	02/2011 02/2011	03/2013	-	0/0
295	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	116.77	02/2006 -	06/2014	100(O) -	0/0
296	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	672.57	- -	03/2012	-	0/0
297	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
298	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	342.66	- 05/2009	05/2009	-	0/0
299	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	548.65	03/1994 -	10/2013	235(O) -	0/0
300	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	126.50	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
301	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	186.95	- -	-	-	0/0
302	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	195.65	- 09/2009	-	-	0/0
303	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
304	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	412.91	636.65	- -	01/2013	-	0/0
305	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	147.52	- -	03/2014	- -	0/0
306	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	176.41	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
307	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	100.89	- -	-	-	0/0
308	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	24.79	03/2015 -	03/2015	0(O) -	0/0
309	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	836.10	06/2007 -	06/2007	-	0/0
310	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	699.67	03/2012 08/2012	-	-	0/0
311	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	693.39	442.99	03/2012 03/2012	12/2012	-	0/0
312	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,438.50	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
313	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	246.74	03/2014 -	03/2014	0(O) -	0/0
314	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	300.79	03/2012 03/2012	03/2013	-	0/0
315	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,444.63	- -	03/2013	-	0/0
316	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	643.00	-	- -	-	-	0/0
317	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	508.81	- -	03/2014	- -	1/1

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
318	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	775.36	760.40	- -	10/2012	-	0/0
319	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.20	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
320	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	116.29	- -	-	-	0/0
321	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	206.41	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
322	KHURDA ROAD- BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	251.70	- -	03/2014	- -	0/0
323	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
324	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	479.24	- 03/2010	03/2010	-	0/0
325	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,523.57	07/2005 -	-	-	0/0
326	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	147.53	- -	-	-	0/0
327	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	288.14	03/2012 03/2013	03/2013	-	0/0
328	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
329	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	352.05	- -	12/2012	-	0/0
330	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.38	12/2012 -	03/2015	27(O) -	0/0
331	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	377.65	05/2008 03/2011	-	-	0/0
332	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	221.82	03/2002 -	07/2013	136(O) -	0/0
333	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,498.06	03/2009 -	03/2015	72(O) -	0/0
334	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.44	07/2008 -	07/2008	-	0/0
335	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	472.00	172.27	- -	02/2013	-	0/0
336	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	688.14	12/2011 12/2011	03/2013	-	0/0
337	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0
338	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	433.30	03/2012 03/2013	03/2013	-	0/0
339	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	1,190.05	309.37	- -	-	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
340	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,207.39	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
341	MUNEERABAD-MAHABOONAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	189.54	- -	03/2012	-	0/0
342	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	480.00	655.91	02/2009 -	03/2012	-	0/0
343	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	356.76	07/2012 -	-	-	0/0
344	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	40.88	- -	-	-	0/0
345	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	135.06	- -	03/2015	- -	0/0
346	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,443.16	12/2008 -	03/2015	75(O) -	0/0
347	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	249.90	- -	03/2015	- -	0/0
348	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,446.81	8.45	03/2015 -	03/2017	24(O) -	0/0
349	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,913.51	286.84	03/2016 -	03/2016	0(O) -	0/0
350	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	54.51	03/2014 -	03/2016	24(O) -	0/0
351	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	116.43	03/2016 -	03/2016	0(O) -	0/0
352	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	44.65	03/2016 -	06/2016	3(O) -	0/0
353	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	437.69	03/2008 06/2008	-	-	0/0
354	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	355.00	334.59	03/2009 11/2012	-	-	0/0
355	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	249.36	02/2010 11/2012	12/2015	70(O) 37(R)	0/0
356	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,801.39	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
357	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	606.94	- -	03/2012	-	0/0
358	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	139.01	12/2010 12/2010	12/2010	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
359	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.92	803.33	- -	03/2013	-	0/6
360	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	289.93	257.91	12/2007 03/2010	-	-	0/0
361	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,062.20	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
362	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
363	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.90	226.32	- -	-	-	0/0
364	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.00	329.21	06/2004 -	12/2012	-	0/0
365	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	2,232.50	1,954.09	- -	03/2014	- -	0/0
366	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	639.97	175.75	03/1998 08/2005	08/2005	-	0/0
367	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	469.03	03/2013 -	03/2014	12(O) -	0/0
368	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	222.76	03/2012 -	-	-	0/0
369	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	233.73	03/2010 -	-	-	0/0
370	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15(O) -	0/0
371	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	84.10	02/2015 -	02/2015	0(O) -	0/0
372	Suratpura - Hanumangarh - Sriganganagar Gauge Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	360.79	03/2014 -	03/2014	0(O) -	0/0
373	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	126.01	- -	-	-	0/0
374	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	443.71	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
375	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	620.77	- 12/2009	02/2012	-	0/0
376	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	170.05	- -	-	-	0/0
377	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	56.06	- -	-	-	0/0
378	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	714.05	544.88	- -	-	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
379	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,429.24	12/2006 08/2010	08/2010	-	0/0
380	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	44.70	03/2012 -	02/2013	-	0/0
381	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201(O) -	0/0
382	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	205.54	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
383	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	575.05	03/2014 -	03/2014	0(O) -	0/0
384	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	198.99	- 03/2010	-	-	0/0
	Total		66,990.82 -	157,489.96	63,875.57				1/7
	<u>Road Transport & Highways</u>								
385	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	250.50	108.20	10/2014 -	10/2014	0(O) -	0/0
386	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	373.47	38.08	07/2014 -	07/2014	0(O) -	0/0
387	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	392.70	05/2013 -	03/2014	10(O) -	0/0
388	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	616.00	11/2013 -	11/2013	0(O) -	0/0
389	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	167.10	04/2014 -	04/2014	0(O) -	0/0
390	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
391	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	62.81	01/2014 -	01/2014	0(O) -	0/0
392	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	129.80	02/2014 -	02/2014	0(O) -	0/0
393	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	464.10	02/2014 -	04/2014	2(O) -	0/0
394	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014	0(O) -	0/0
395	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	160.70	05/2014 -	05/2014	0(O) -	0/0
396	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,718.00	08/2014 -	07/2015	11(O) -	0/0
397	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,284.00	06/2013 -	06/2013	0(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
398	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	38.55	09/2013 -	07/2014	10(O) -	0/0
399	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	797.00	08/2013 -	08/2013	0(O) -	0/0
400	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	712.90	07/2013 -	07/2013	0(O) -	0/0
401	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	398.00	427.00	02/2014 -	02/2014	0(O) -	0/0
402	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,088.00	08/2013 -	08/2013	0(O) -	0/0
403	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,134.00	08/2013 -	08/2013	0(O) -	0/0
404	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	218.50	08/2013 -	08/2013	0(O) -	0/0
405	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	1,396.18	754.50	09/2014 -	09/2014	0(O) -	0/0
406	AGRA-BYPASS(NS-1UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	225.70	09/2007 -	03/2014	78(O) -	0/0
407	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	2,125.24	30.19	12/2015 -	12/2015	0(O) -	0/0
408	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	1,259.00	11/2012 -	06/2013	7(O) -	0/0
409	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.30	01/2009 -	12/2013	59(O) -	0/0
410	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	16(O) -	0/0
411	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	06/2013	112(O) -	0/0
412	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	325.70	09/2013 -	09/2013	0(O) -	0/0
413	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	2,388.00	1,118.00	06/2014 -	06/2014	0(O) -	0/0
414	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	488.70	-	10/2013	-	2/2
415	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	13.80	01/2013 -	10/2013	9(O) -	0/0
416	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	450.90	08/2013 -	08/2013	0(O) -	0/0
417	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	279.80	06/2008 -	03/2014	69(O) -	0/0
418	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	237.30	06/2008 -	03/2014	69(O) -	0/0
419	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	236.50	06/2005 -	03/2014	105(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
420	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	272.50	04/2010 -	11/2014	55(O) -	0/0
421	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53(O) -	0/0
422	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	797.20	03/2013 -	08/2013	5(O) -	0/0
423	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	632.60	- -	12/2013	- -	0/1
424	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	09/2013	4(O) -	0/0
425	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	403.50	10/2011 -	03/2014	29(O) -	0/0
426	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	772.60	10/2011 -	06/2013	20(O) -	0/0
427	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68(O) -	0/0
428	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015	0(O) -	0/0
429	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	646.60	05/2010 -	06/2013	37(O) -	0/0
430	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	524.00	07/2013 -	07/2013	0(O) -	0/0
431	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	06/2013	0(O) -	0/0
432	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	685.10	- -	06/2013	- -	1/1
433	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	246.20	06/2008 -	09/2013	63(O) -	0/0
434	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	202.90	05/2008 -	12/2013	67(O) -	0/0
435	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	295.40	09/2010 -	01/2014	40(O) -	0/0
436	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	307.90	08/2013 -	02/2015	18(O) -	0/0
437	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	1,573.00	13.39	09/2015 -	09/2015	0(O) -	0/0
438	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	441.45	09/2008 -	12/2013	63(O) -	0/0
439	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	1,232.00	119.60	08/2015 -	08/2015	0(O) -	0/0
440	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
441	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0
442	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014	66(O) -	0/0
443	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	06/2013	112(O) -	0/0
444	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,213.00	08/2013 -	08/2013	0(O) -	0/0
445	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	242.40	04/2008 -	03/2014	71(O) -	0/0
446	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	182.50	04/2008 -	03/2014	71(O) -	0/0
447	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	06/2013	44(O) -	0/0
448	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60(O) -	0/0
449	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	12/2013	15(O) -	0/0
450	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,836.00	10/2011 -	12/2013	26(O) -	0/0
451	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74(O) -	0/0
452	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	303.30	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
453	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	132.70	07/2009 -	05/2014	58(O) -	0/0
454	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79(O) -	0/0
455	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	245.40	10/2013 -	03/2014	5(O) -	0/0
456	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.90	08/2004 -	08/2013	108(O) -	0/0
457	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.57	08/2004 07/2010	08/2013	108(O) 37(R)	0/0
458	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	944.50	01/2013 -	06/2013	5(O) -	0/0
459	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,486.00	- -	06/2013	- -	3/3
460	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	447.50	05/2013 -	02/2014	9(O) -	0/0
461	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
462	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	630.40	02/2013 -	07/2013	5(O) -	0/0
463	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
464	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	501.90	09/2009 -	06/2013	45(O) -	0/0
465	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	536.00	333.90	01/2014 -	01/2014	0(O) -	0/0
466	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,959.00	12/2012 -	06/2013	6(O) -	0/0
467	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.83	10/2008 -	09/2013	59(O) -	0/0
468	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.90	10/2008 -	12/2013	62(O) -	0/0
469	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	702.16	430.90	07/2014 -	07/2014	0(O) -	0/0
470	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.50	- -	06/2014	- -	2/3
471	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,056.00	05/2012 -	06/2013	13(O) -	0/0
472	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.40	06/2010 -	12/2013	42(O) -	0/0
473	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.80	09/2009 -	09/2014	60(O) -	0/0
474	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	101.10	07/2012 -	07/2014	24(O) -	0/0
475	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	114.80	11/2008 -	06/2014	67(O) -	0/0
476	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68(O) -	0/0
477	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73(O) -	0/0
478	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	141.80	04/2009 -	12/2014	68(O) -	0/0
479	MURADABAD-BAREILI - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,431.00	06/2013 -	06/2013	0(O) -	0/0
480	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	512.10	03/2013 -	03/2014	12(O) -	0/0
481	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
482	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	299.20	06/2008 -	12/2013	66(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
483	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54(O) -	0/0
484	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19 -	484.19	34.70	10/2014 -	10/2014	0(O) -	0/0
485	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	296.80	04/2008 -	05/2014	73(O) -	0/0
486	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	258.40	06/2008 -	09/2013	63(O) -	0/0
487	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	283.10	06/2008 -	09/2013	63(O) -	0/0
488	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
489	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	286.60	06/2011 06/2011	06/2013	24(O) 24(R)	0/2
490	NH CONNECTIVITY TO ICTT VALLARPADA NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	932.30	02/2010 -	12/2014	58(O) -	0/0
491	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11(O) -	0/0
492	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013	0(O) -	0/0
493	PANIKHOLI-RIMOLI - [N24000197]NHAI, Odisha	03/2012	1,410.00 -	1,410.00	153.70	09/2014 -	09/2014	0(O) -	0/0
494	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00 -	807.00	1,262.00	10/2014 -	10/2014	0(O) -	0/0
495	PANVEL-INDAPUR - [N24000216]NHAI, Multi State	12/2011	942.69 -	942.69	177.50	06/2014 -	06/2014	0(O) -	0/0
496	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	294.30	05/2008 -	09/2013	64(O) -	0/0
497	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00 -	574.00	604.50	03/2014 -	03/2014	0(O) -	0/0
498	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	608.10	02/2013 -	10/2013	8(O) -	0/0
499	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00 -	940.00	1,293.00	07/2012 -	06/2013	11(O) -	0/0
500	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	04/2014	13(O) -	0/0
501	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00 -	835.00	122.70	01/2014 -	01/2014	0(O) -	0/0
502	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013	21(O) -	0/0
503	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17(O) -	0/0
504	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI, Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	843.40	07/2015 -	06/2016	11(O) -	0/0

Sector Wise Details									
(May,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
505	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	326.80	10/2008 -	06/2013	56(O) -	0/0
506	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	1,479.00	162.80	06/2015 -	06/2015	0(O) -	0/0
507	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	1,025.00	11/2013 -	11/2013	0(O) -	0/0
508	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31(O) -	0/0
509	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	563.30	03/2013 -	12/2013	9(O) -	0/0
510	SAMAIKHALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	805.39	543.70	12/2013 -	12/2013	0(O) -	0/0
511	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	909.00	867.50	05/2014 -	05/2014	0(O) -	0/0
512	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	231.80	09/2007 -	12/2013	75(O) -	0/0
513	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	191.00	07/2008 -	03/2013	-	0/0
514	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
515	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	1,250.00	14.58	12/2013 -	12/2013	0(O) -	0/0
516	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	1,535.00	1,085.00	05/2014 -	05/2014	0(O) -	0/0
517	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31(O) -	0/0
518	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
519	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	08/2013	65(O) -	0/0
520	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013	110(O) -	0/0
521	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,686.00	08/2011 -	06/2013	22(O) -	0/0
522	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	06/2013	48(O) -	0/0
523	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	855.90	07/2010 -	03/2014	44(O) -	0/0
524	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	1,110.00	11/2013 -	11/2013	0(O) -	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
525	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	0(O) -	0/0
526	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.70	05/2013 -	08/2013	3(O) -	0/0
527	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
528	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	788.00	03/2014 -	03/2014	0(O) -	0/0
529	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	194.20	03/2008 -	02/2008	-	0/0
530	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	47.41	11/2012 -	03/2014	16(O) -	0/0
531	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	588.50	07/2013 -	06/2014	11(O) -	0/0
532	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	201.60	06/2014 -	06/2014	0(O) -	0/0
	Total		101,189.08 -	103,127.70	75,502.51				10/14
	<u>Shipping & Ports</u>								
533	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.69	04/2011 09/2011	09/2011	-	0/0
534	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	5(O) 0(R)	0/0
535	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
536	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	418.64	12/2012 10/2013	10/2013	10(O) 0(R)	0/0
537	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
538	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014	0(O) -	0/0
539	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-1(O) 0(R)	0/0
540	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	946.21	12/2010 09/2012	04/2014	40(O) 19(R)	0/0
541	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
542	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
543	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,370.00	5.75	10/2008 -	08/2012	-	0/0
544	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
545	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
546	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
547	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
548	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
549	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
550	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	07/2013	18(O) 10(R)	0/0
551	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	0(O) -	0/0
	Total		15,617.12 -	17,700.82	8,592.87				0/1
	<u>Telecommunications</u>								
552	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59(O) -	0/0
553	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	-	-	0/0
554	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.20	02/2007 03/2012	02/2013	-	0/0
555	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	-	03/2012 -	-	-	0/0
556	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38(O) 21(R)	0/0
557	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	168.30	86.11	10/2007 -	-	-	0/0

Sector Wise Details

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original/ Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
558	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	12/2013	54(O) -	0/0
559	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
560	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34(O) 9(R)	0/0
561	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
562	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
563	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
564	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28(O) -	0/0
	Total		5,699.24 -	5,520.22	1,901.95				0/0
	<u>Urban Development</u>								
565	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013	-	3/3
566	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
567	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	3,222.85	03/2016 -	03/2016	0(O) -	0/0
568	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	264.96	09/2014 -	09/2014	0(O) -	0/0
	Total		44,245.18 -	49,518.08	5,969.99				3/3
	<u>Water Resources</u>								
569	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		797,194.85	946,877.84	447,272.38				1102/3434

Sector wise current status of projects on the Flash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 2 projects do not have fixed dates of commissioning.

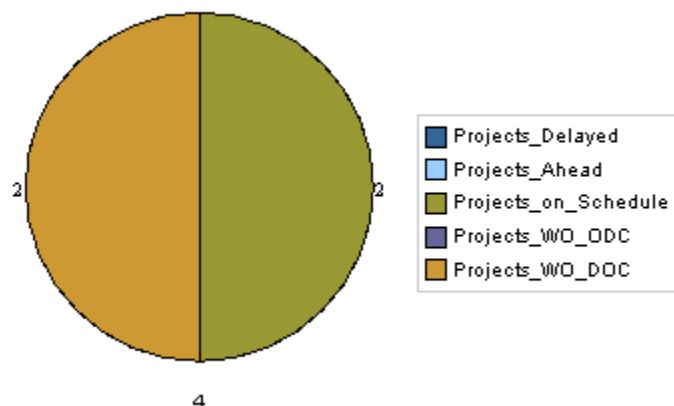

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till May, 2013 is Rs. 5969.99 crore, which is 12.1% of the revised cost of the projects.

Figures are in Rs. Crore

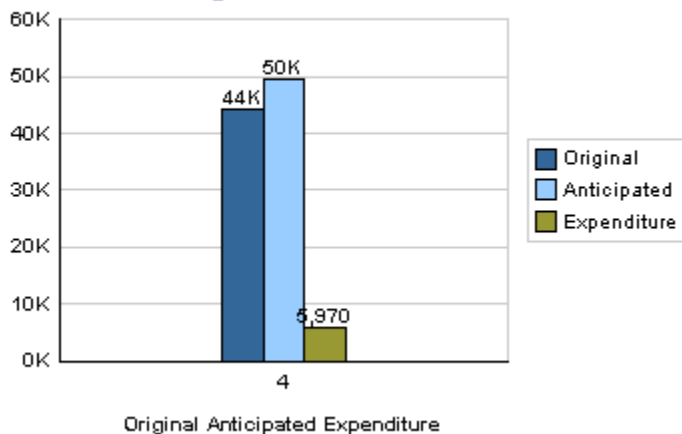

Sector wise current status of projects on the Flash Report

Telecommunications

I. Current Status:


Number of Projects **13**

Number of Projects Delayed **5**

Number of Projects Without Date Of Commissioning **8**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 5 projects are delayed .8 projects do not have fixed dates of commissioning.

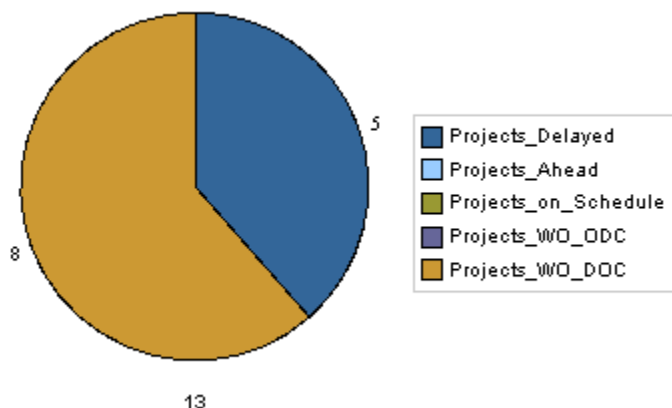

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5520.22 crore implying a cost overrun of -3.1%. The expenditure incurred on these projects till May, 2013 is Rs. 1901.95 crore, which is 34.5% of the revised cost of the projects.

Figures are in Rs. Crore

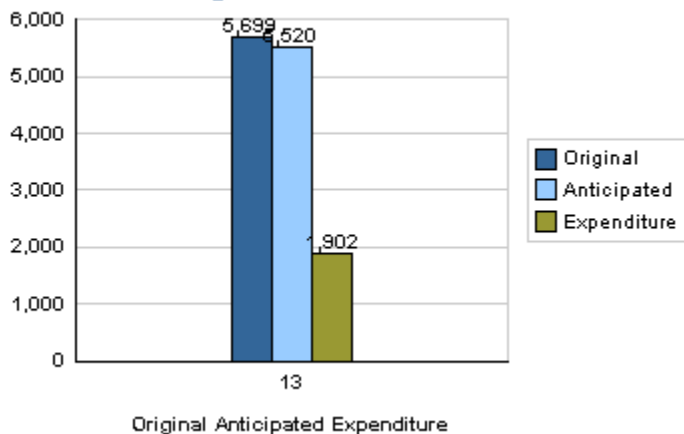

Sector wise current status of projects on the Flash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	2
Number of Projects Delayed	6
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	10

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 2 projects are on schedule and 6 projects are delayed .10 projects do not have fixed dates of commissioning.

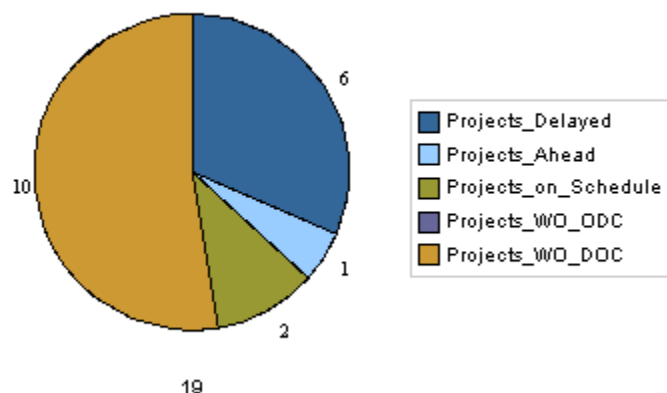

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17700.82 crore implying a cost overrun of 13.3%. The expenditure incurred on these projects till May, 2013 is Rs. 8592.96 crore, which is 48.5% of the revised cost of the projects.

Figures are in Rs. Crore

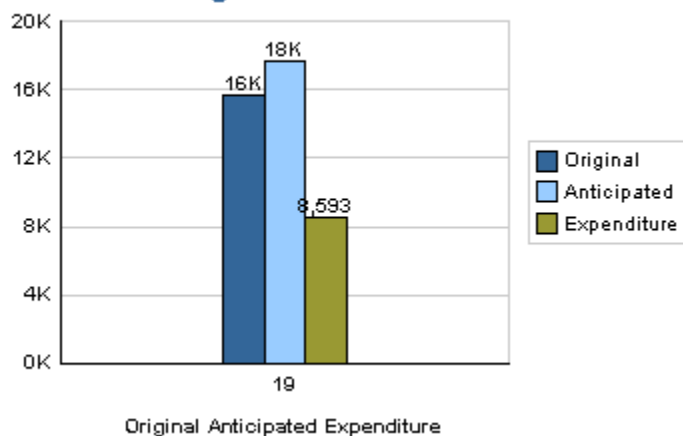

Sector wise current status of projects on the Flash Report

Road Transport & Highways


I. Current Status:

Number of Projects	148
Number of Projects On Schedule	50
Number of Projects Delayed	90

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	3


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 148 projects, 50 projects are on schedule and 90 projects are delayed .3 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

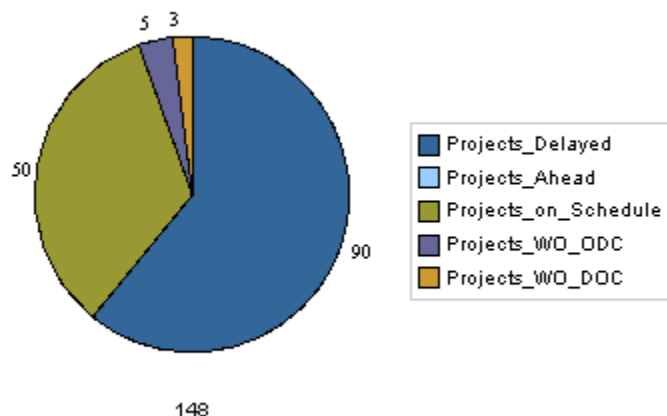

III. Investment Scenario

The Total Original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 101189.08 crore but this was subsequently revised to Rs. 103127.7 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till May, 2013 is Rs. 75502.51 crore, which is 73.2% of the revised cost of the projects.

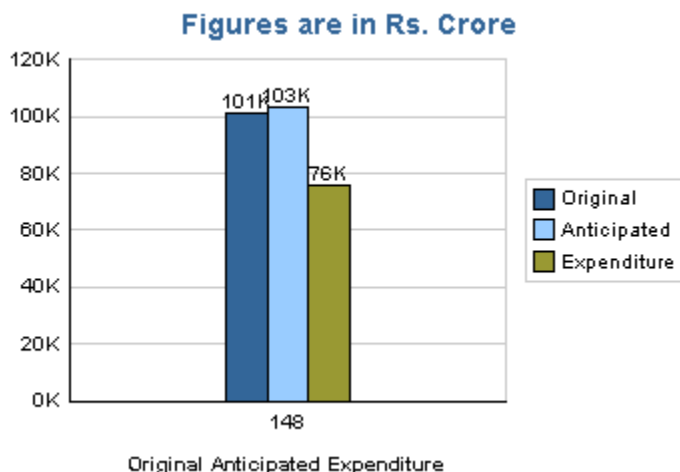

Sector wise current status of projects on the Flash Report

Railways


I. Current Status:

Number of Projects	129
Number of Projects On Schedule	8
Number of Projects Delayed	35

Number of Projects Without Original Date of Commissioning	10
Number of Projects Without Date Of Commissioning	76

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 129 projects, 8 projects are on schedule and 35 projects are delayed .76 projects do not have fixed dates of commissioning.10 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

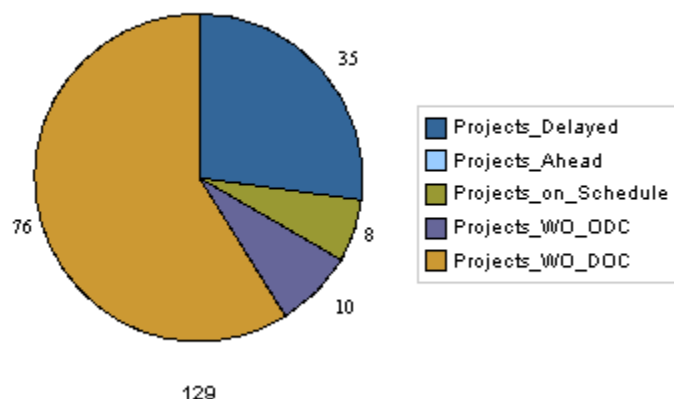

III. Investment Scenario

The Total Original cost of implementation of 129 projects when sanctioned, was of the order of Rs. 66990.82 crore but this was subsequently revised to Rs. 157489.96 crore implying a cost overrun of 135.1%. The expenditure incurred on these projects till May, 2013 is Rs. 63875.57 crore, which is 40.6% of the revised cost of the projects.

Figures are in Rs. Crore

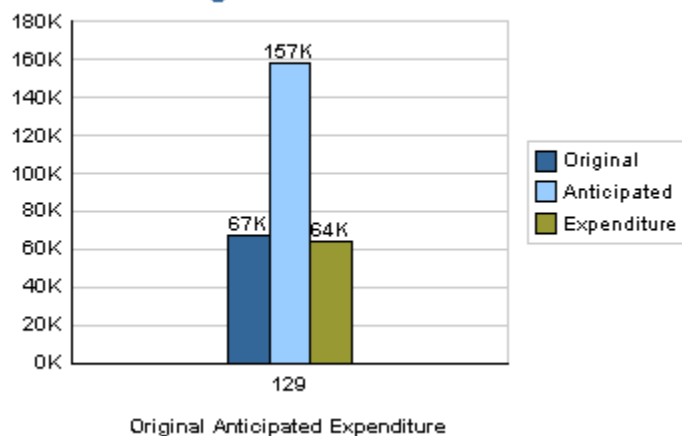

Sector wise current status of projects on the Flash Report


Power

I. Current Status:

Number of Projects	103
Number of Projects On Schedule	42
Number of Projects Delayed	51
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 103 projects, 2 projects are ahead of schedule, 42 projects are on schedule and 51 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

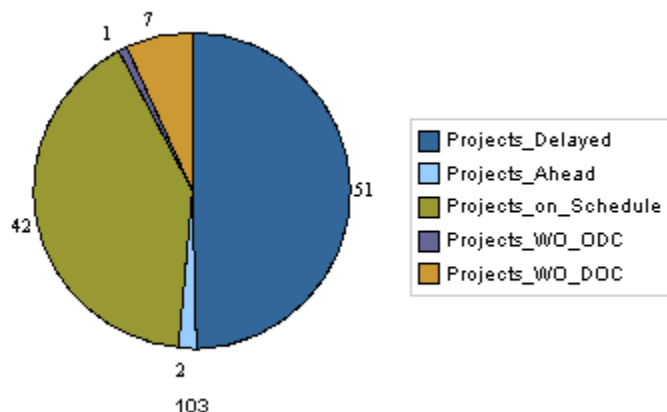

III. Investment Scenario

The Total Original cost of implementation of 103 projects when sanctioned, was of the order of Rs. 243028.99 crore but this was subsequently revised to Rs. 259083.86 crore implying a cost overrun of 6.6%. The expenditure incurred on these projects till May, 2013 is Rs. 118566.19 crore, which is 45.8% of the revised cost of the projects.

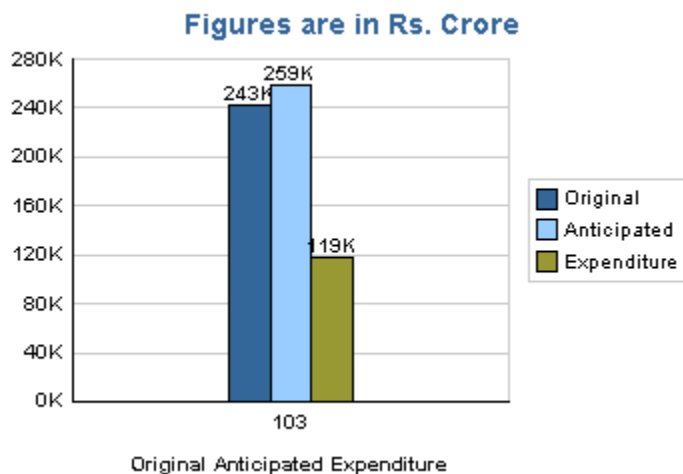

Sector wise current status of projects on the Flash Report

Petroleum


I. Current Status:

Number of Projects	70
Number of Projects On Schedule	20
Number of Projects Delayed	42

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	7


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 70 projects, 20 projects are on schedule and 42 projects are delayed .7 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

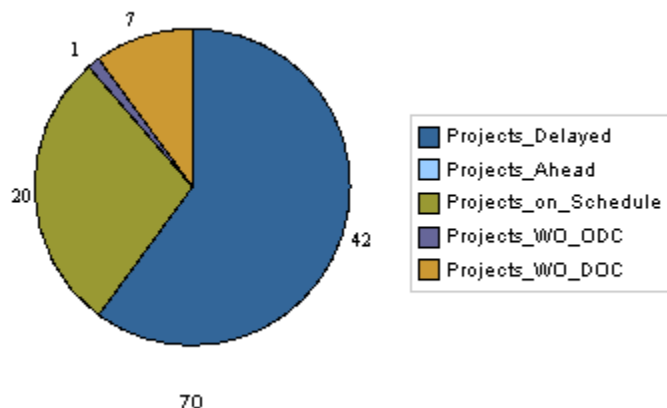

III. Investment Scenario

The Total Original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 165950.52 crore but this was subsequently revised to Rs. 179743.33 crore implying a cost overrun of 8.3%. The expenditure incurred on these projects till May, 2013 is Rs. 82724.37 crore, which is 46% of the revised cost of the projects.

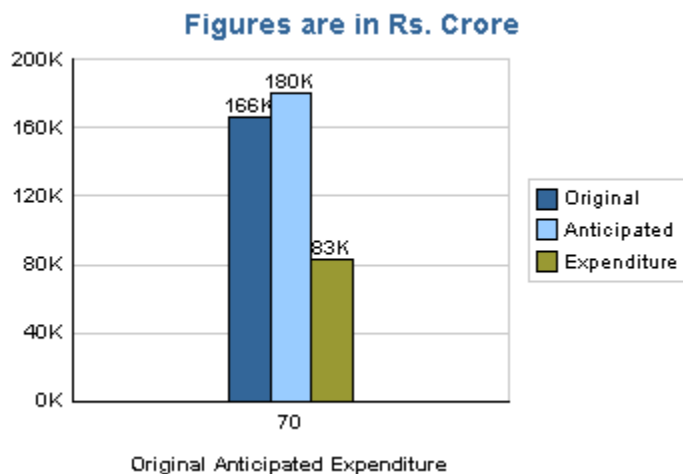

Sector wise current status of projects on the Flash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	2
Number of Projects Delayed	15

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 2 projects are on schedule and 15 projects are delayed.

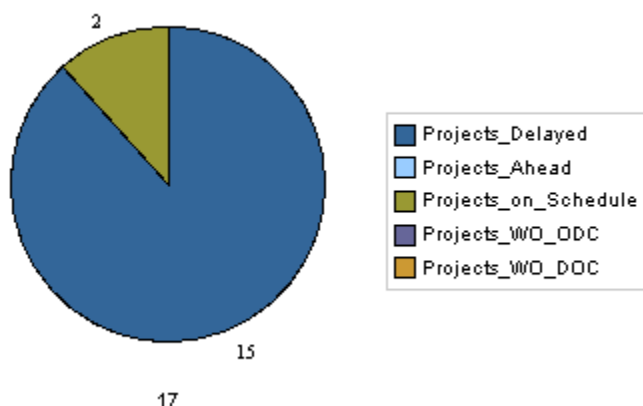

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till May, 2013 is Rs. 40721.93 crore, which is 57% of the revised cost of the projects.

Figures are in Rs. Crore

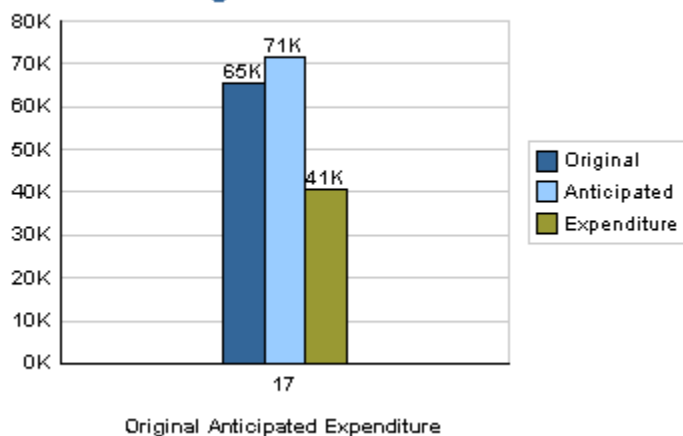

Sector wise current status of projects on the Flash Report

Coal


I. Current Status:

Number of Projects	54
Number of Projects On Schedule	21
Number of Projects Delayed	28

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	4


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 54 projects, 21 projects are on schedule and 28 projects are delayed .4 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

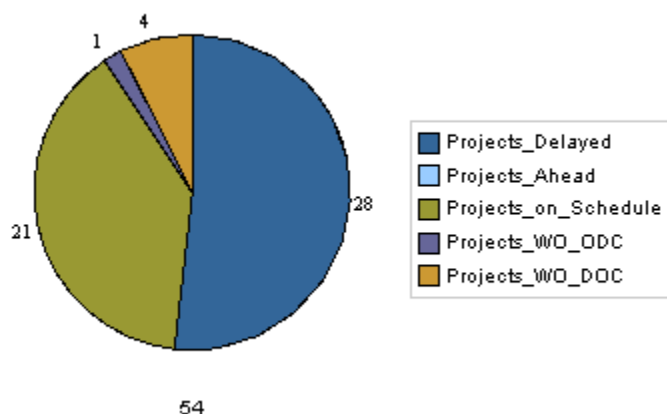

III. Investment Scenario

The Total Original cost of implementation of 54 projects when sanctioned, was of the order of Rs. 37268.94 crore but this was subsequently revised to Rs. 40354.39 crore implying a cost overrun of 8.3%. The expenditure incurred on these projects till May, 2013 is Rs. 14787.57 crore, which is 36.6% of the revised cost of the projects.

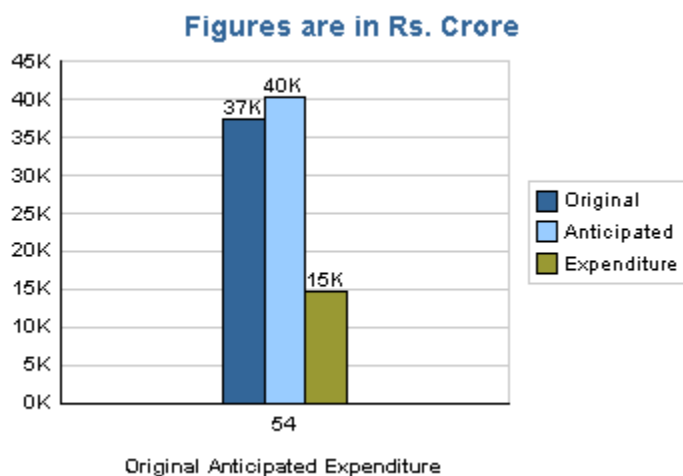

Sector wise current status of projects on the Flash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	2

Number of Projects Without Date Of Commissioning	2
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 2 projects are delayed .2 projects do not have fixed dates of commissioning.

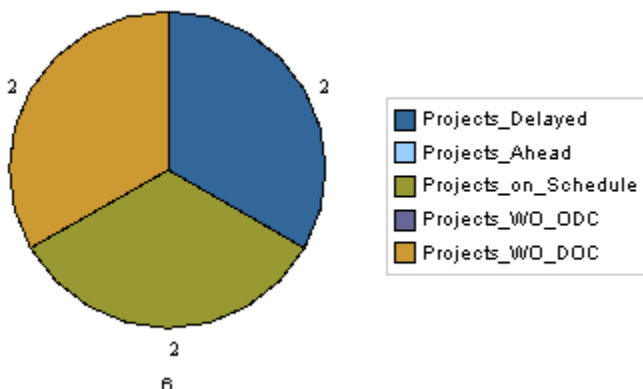

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till May, 2013 is Rs. 5287.95 crore, which is 87.2% of the revised cost of the projects.

Figures are in Rs. Crore

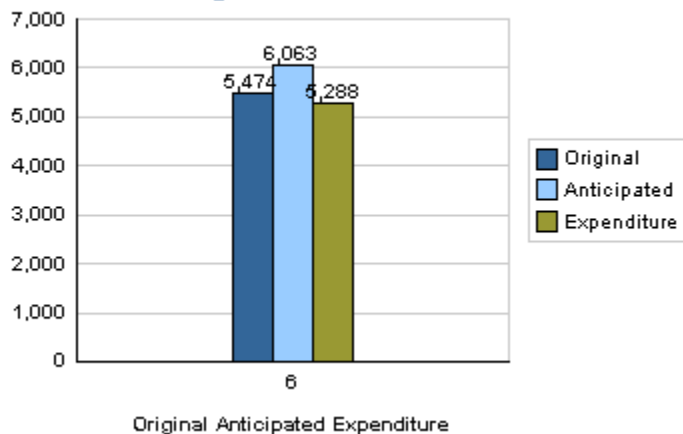

Sector wise current status of projects on the Flash Report

Atomic Energy

I. Current Status:


Number of Projects 4

Number of Projects Delayed 2

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed .2 projects do not have fixed dates of commissioning.

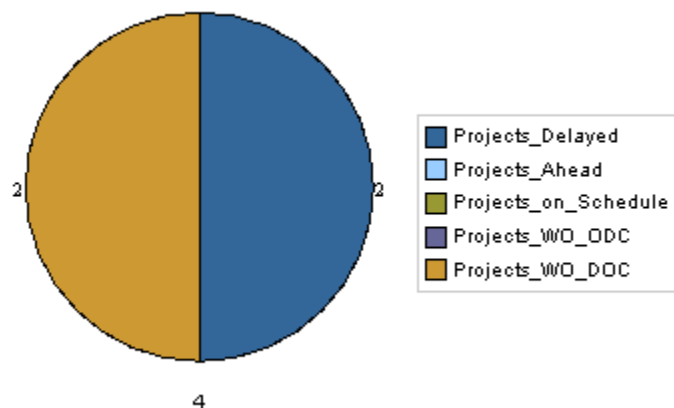

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till May, 2013 is Rs. 24795.48 crore, which is 53.1% of the revised cost of the projects.

Figures are in Rs. Crore

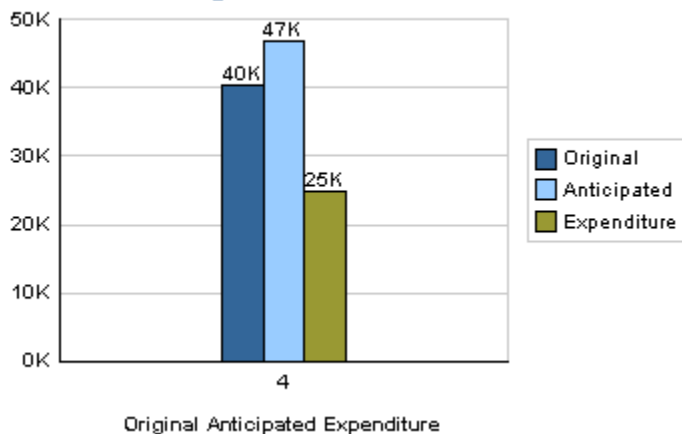

ANNEXURES

LIST OF CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	37	31097.13	38550.36	21473.96
2	Arunachal Pradesh	4	9512.22	14144.29	8836.06
3	Assam	38	23394.36	36838.12	23618.58
4	Bihar	30	26917.64	35131.24	26259.61
5	Chhatisgarh	24	58278.32	59362.92	15951.62
6	Delhi	4	38214.41	38194.82	3555.01
7	Goa	1	335.61	335.61	215.29
8	Gujarat	22	33405.07	33607.01	11964.05
9	Haryana	8	4054.38	5736.96	7075.23
10	Himachal Pradesh	5	13355.57	17246.69	13289.61
11	Jammu and Kashmir	10	14926.96	34825.56	14567.64
12	Jharkhand	23	14447.40	18632.54	8475.86
13	Karnataka	27	47076.40	56439.71	24061.05
14	Kerala	7	20376.67	22170.22	5257.53
15	Madhya pradesh	20	18545.58	18953.75	8423.79
16	Maharashtra	48	88574.45	100866.49	45685.00
17	Manipur	1	727.56	4453.50	1438.50
18	Meghalaya	2	762.00	762.00	463.70
19	Mizoram	2	1532.97	3297.97	507.44
20	Multi State	110	143654.98	156071.14	72779.50
21	Nagaland	1	850.00	2446.81	8.45
22	Odisha	30	56171.63	63436.93	36050.59
23	Punjab	5	2063.38	3005.15	2837.87
24	Rajasthan	14	21115.76	20927.99	8536.49
25	Sikkim	2	1648.94	3690.04	285.49
26	Tamil Nadu	32	48788.07	61732.81	41187.96
27	Tripura	3	1522.39	2018.85	1173.59
28	Uttar Pradesh	27	21281.92	25861.13	13171.50
29	Uttarakhand	5	7624.21	8564.64	2567.71
30	West Bengal	27	46938.87	59572.59	27553.79
TOTAL		569	797194.85	946877.84	447272.47

List of Projects Ahead of Schedule w.r.t. Original Schedule

(May,2013)

Sl.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised DOC	Anticipated DOC
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	50.32	06/2016 -	04/2015
2	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	161.49	12/2014 -	11/2014
	Total		3,444.09 -	3,444.09	211.81		
	<u>Shipping & Ports</u>						
3	Acquisition of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		1,028.10 -	1,012.23	554.60		
	Grand Total		4,472.19	4,456.32	766.41		

List of project Without Original Date of Commissioning w.r.t. Original Schedule

(May,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Coal</u>								
1	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.31	- -	03/2016	-	0/0
	Total		430.14 -	430.14	58.31				0/0
	<u>Petroleum</u>								
2	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	- -	08/2013	-	52/53
	Total		756.00 -	898.00	913.72				52/53
	<u>Power</u>								
3	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	527.59	- -	07/2013	-	10/29
	Total		421.01 -	623.44	527.59				10/29
	<u>Railways</u>								
4	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	331.85	- -	06/2013	-	0/0
5	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
6	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	216.92	- -	03/2014	-	0/0
7	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	508.81	- -	03/2014	-	0/1
8	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	251.70	- -	03/2014	-	0/0

(May,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
9	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	2,232.50	1,954.09	- -	03/2014	-	0/0
10	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	147.52	- -	03/2014	-	0/0
11	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	249.90	- -	03/2015	-	0/0
12	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	135.06	- -	03/2015	-	0/0
13	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
	Total		3,035.86 -	8,059.31	3,991.98				0/1
	<u>Road Transport & Highways</u>								
14	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,486.00	- -	06/2013	-	3/3
15	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	685.10	- -	06/2013	-	1/1
16	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	488.70	- -	10/2013	-	2/2
17	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	632.60	- -	12/2013	-	0/1
18	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.50	- -	06/2014	-	2/3
	Total		3,389.00 -	3,389.00	4,029.90				8/10
	Grand Total		8,032.01	13,399.89	9,521.50				70/93

List of project Without Date of Commissioning w.r.t. Original Schedule

Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised DOC	Anticipated DOC
1	2	3	4	5	6
	<u>Atomic Energy</u>				
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	09/2010 -	-
	Total		16,663.00 -		
	<u>Civil Aviation</u>				
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013
	Total		3,750.51 -		
	<u>Coal</u>				
5	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	03/2013 -	03/2013
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
7	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	03/2013 -	-
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	03/2012 -	-
	Total		2,324.09 -		
	<u>Petroleum</u>				
9	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	- -	03/2013
10	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE - - [N16000070]GAIL,Multi State	07/2009	238.68 -	01/2012 -	-
11	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	09/2012 -	-
12	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-
13	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	07/2012 07/2012	-
14	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	12/2012 -	-
15	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	-
	Total		8,339.17 -		

Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised DOC	Anticipated DOC
1	2	3	4	5	6
	<u>Power</u>				
16	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	03/2013
17	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,Jammu and Kashmir	08/2006	621.26 -	02/2011 10/2012	01/2013
18	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
19	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	08/2012 -	03/2013
20	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	10/2012 -	03/2013
21	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	03/2007 09/2012	04/2013
22	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		15,617.89 -		
	<u>Railways</u>				
23	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005
24	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
25	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
26	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
27	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
28	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
29	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
30	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011
31	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
32	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
33	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012
34	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
35	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
36	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
37	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
38	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012

Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised DOC	Anticipated DOC
1	2	3	4	5	6
39	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
40	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
41	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
42	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
43	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
44	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012
45	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
46	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
47	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
48	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
49	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013
50	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
51	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013
52	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013
53	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013
54	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013
55	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
56	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013
57	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013
58	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013
59	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013
60	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013
61	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
62	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
63	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-

Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised DOC	Anticipated DOC
1	2	3	4	5	6
64	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Odisha	04/1996	301.64 -	- 09/2009	-
65	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-
66	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
67	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 380.00	03/2009 11/2012	-
68	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
69	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL, Chhatisgarh	09/2006	324.90 -	03/2010 -	-
70	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, Uttar Pradesh	03/2013	307.00 -	- -	-
71	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, Multi State	03/2007	243.78 -	- -	-
72	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, Uttar Pradesh	03/2008	195.64 -	- -	-
73	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, Uttar Pradesh	03/2012	160.89 -	- -	-
74	CHHAPRA-BALLIA UP - [N22000134]NER, Multi State	03/2013	295.00 -	- -	-
75	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, Uttar Pradesh	03/2013	643.00 -	- -	-
76	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-
77	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 514.68	- -	-
78	NANGALDAM-TALWARA(NL), NR - [220100188]NR, Multi State	03/1981	37.68 450.00	07/2012 -	-
79	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1997	227.00 997.58	- -	-
80	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
81	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	-
82	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
83	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, Bihar	04/1997	78.23 162.87	- -	-
84	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 100.00	- -	-
85	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
86	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 901.62	- -	-
87	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66 528.65	- -	-
88	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, Bihar	04/2001	104.79 -	- -	-

Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised DOC	Anticipated DOC
1	2	3	4	5	6
89	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
90	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
91	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
92	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
93	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
94	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
95	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
96	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-
97	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
98	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		22,404.56 -		
	<u>Road Transport & Highways</u>				
99	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008
100	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013
101	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	- -	04/2013
	Total		1,071.27 -		
	<u>Shipping & Ports</u>				
102	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	- 01/2009	12/2010
103	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
104	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 09/2011	09/2011
105	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
106	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	08/2012
107	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
108	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
109	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012

Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised DOC	Anticipated DOC
1	2	3	4	5	6
110	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013
111	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		6,569.48 -		
	<u>Telecommunications</u>				
112	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
113	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
114	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013
115	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	-
116	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
117	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
118	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
119	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	-
	Total		2,764.39 -		
	<u>Urban Development</u>				
120	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	06/2011 -	03/2013
121	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>Water Resources</u>				
122	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		86,556.44		

List of On schedule Projects w.r.t. Original Schedule

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065]	9/2008	626.00 -	626.00	376.97	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	102.76	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	479.73		
	<u>Coal</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	159.13	03/2015 03/2015	03/2015
4	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]	11/2006	168.97 -	168.97	43.29	03/2014 03/2014	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042]	2/2008	395.87 -	395.87	84.50	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	35.71	03/2015 -	03/2015
8	Rajrappa RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	259.21	03/2016 -	03/2016
9	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	0.02	07/2016 -	07/2016
11	RAMAGUNDUM OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	50.53	03/2016 -	03/2016
13	Moonidih XV Seam UG - [N06000098]	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
14	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	7/2011	447.06 -	447.06	14.02	03/2015 -	03/2015
16	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
17	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	4.68	03/2018 03/2018	03/2018
18	KARMA OCP (1.0MTY) - [N06000088]	6/2009	162.46 -	162.46	34.71	03/2014 -	03/2014

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
19	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	81.18	03/2016 -	03/2016
20	Batura OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
21	TALABIRA OCP - [N06000043]	3/2008	447.72 -	447.72	44.50	03/2016 -	03/2016
22	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	123.40	03/2017 -	03/2017
23	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	438.86	03/2016 03/2016	03/2016
	Total		9,880.90 -	9,509.56	1,376.22		
	<u>Petroleum</u>						
24	Wax Project - [N16000101]	6/2010	576.60 -	576.60	34.77	12/2013 -	12/2013
25	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	712.11	05/2015 -	05/2015
26	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	309.81	-	08/2014 -	08/2014
27	Mounded Bullet Project at CPCL - [N16000154]	12/2012	279.00 -	279.00	-	12/2014 -	12/2014
28	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeline - [N16000153]	4/2011	152.89 -	152.89	3.79	06/2013 -	06/2013
29	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]	2/2011	913.00 -	913.00	30.60	07/2015 -	07/2015
30	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]	6/2009	486.00 -	486.00	52.05	09/2013 -	09/2013
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	666.00	-	11/2015 -	11/2015
32	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	61.81	11/2015 -	11/2015
33	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]	1/1999	1,419.00 -	1,419.00	4.89	12/2014 -	12/2014
34	BUTENE-1 PROJECT AT PANIPAT - [N16000139]	2/2012	190.00 -	190.00	48.09	03/2014 -	03/2014
35	Pipeline Replacement Project-3 - [N16000137]	4/2012	2,547.26 -	1,417.00	336.94	05/2014 -	05/2014
36	Development of Western Periphery of MH South Field - [N16000136]	4/2012	600.17 -	600.17	51.17	12/2014 -	12/2014
37	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
38	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,665.65	113.16	03/2015 -	03/2015
39	Development of WO-16 Cluster Fields - [N16000105]	6/2010	2,523.00 -	2,523.00	883.68	01/2014 -	01/2014

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
40	Ahmedabad Redevelopment - [N16000120]	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2014
41	Mehesana Redevelopment - [N16000121]	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
42	Ankleswar Redevelopment - [N16000122]	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2014
43	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]	8/2010	8,140.00 -	8,140.00	894.36	02/2014 -	02/2014
	Total		38,202.30 -	37,678.06	5,752.09		
	<u>Power</u>						
44	Transm System for development of Pooling strn. in NR part of West Bengal & Transfer of power from BHU - [N18000077]	4/2010	4,404.57 -	4,404.57	373.68	01/2015 -	01/2015
45	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]	8/2011	425.51 -	425.51	290.84	10/2013 -	10/2013
46	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	9/2012	871.35 -	871.35	-	03/2015 -	03/2015
47	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	98.76	06/2015 -	06/2015
48	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
49	COMMON TR. SYS. ASSOCIATED WITH EAST COAST & NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
50	Lata-Tapovan Hydro Electric Power Project 3x57 MW - [N18000142]	7/2012	1,527.00 -	1,527.00	65.92	08/2017 -	08/2017
51	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 x 800 MW) - [N18000140]	11/2012	11,846.00 -	11,846.00	1,056.00	05/2017 -	05/2017
52	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
53	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
54	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	70.26	03/2015 -	03/2015

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
55	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	286.00	08/2015 -	08/2015
56	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	1,470.00	11/2016 -	11/2016
57	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	942.00	09/2016 -	09/2016
58	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	1,573.00	12/2016 -	12/2016
59	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	143.37	11/2014 -	11/2014
60	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129	2/2012	3,201.44 -	3,201.44	541.70	10/2014 -	10/2014
61	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	136.63	11/2014 -	11/2014
62	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117	1/2012	1,422.85 -	1,422.85	270.30	01/2015 -	01/2015
63	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116	12/2011	1,746.65 -	1,746.65	87.59	08/2014 -	08/2014
64	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	99.60	08/2014 -	08/2014
65	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114	12/2011	552.44 -	552.44	-	02/2014 -	02/2014
66	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113	12/2011	2,422.66 -	2,422.66	281.68	08/2014 -	08/2014
67	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112	11/2011	2,127.51 -	2,127.51	759.70	07/2014 -	07/2014
68	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111	8/2011	1,637.34 -	1,637.34	699.90	08/2014 -	08/2014
69	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	145.70	06/2014 -	06/2014
70	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107	8/2011	1,391.97 -	1,391.97	928.77	12/2013 -	12/2013
71	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS [N18000127	12/2011	901.77 -	901.77	216.50	08/2014 -	08/2014
72	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126	3/2012	206.44 -	206.44	39.21	06/2014 -	06/2014

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
73	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	701.90	06/2015 -	06/2015
74	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
75	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
76	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122	2/2012	1,927.16 -	1,927.16	252.96	10/2014 -	10/2014
77	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121	2/2012	324.33 -	324.33	19.50	08/2014 -	08/2014
78	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120	2/2012	1,310.85 -	1,310.85	289.64	02/2015 -	02/2015
79	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	85.88	01/2014 -	01/2014
80	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	578.32	12/2013 -	12/2013
81	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	1,090.11	08/2013 -	08/2013
82	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	892.93	05/2014 -	05/2014
83	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102	7/2011	181.93 -	181.93	107.52	07/2013 -	07/2013
84	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103	9/2011	1,940.13 -	1,940.13	845.25	09/2014 -	09/2014
85	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096	3/2011	2,569.25 -	2,569.25	1,505.63	03/2014 -	03/2014
	Total		102,743.78 -	102,743.78	16,950.35		
	<u>Railways</u>						
86	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	84.10	02/2015 -	02/2015
87	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
88	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111	4/2010	2,619.02 -	2,913.51	286.84	03/2016 -	03/2016
89	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113	4/2008	653.19 -	653.46	246.74	03/2014 -	03/2014
90	Suratpura - Hanumangarh - Sriganaganagar Guage Conversion (NWR) - [N22000114	4/2008	516.23 -	516.23	360.79	03/2014 -	03/2014
91	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	575.05	03/2014 -	03/2014
92	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112	4/2008	829.74 -	829.74	24.79	03/2015 -	03/2015
93	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) - [N22000110	4/2010	3,951.98 -	3,951.98	116.43	03/2016 -	03/2016
	Total		15,017.59 -	15,947.41	1,694.74		
	<u>Road Transport & Highways</u>						
94	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
95	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,213.00	08/2013 -	08/2013
96	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	122.70	01/2014 -	01/2014
97	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	427.00	02/2014 -	02/2014
98	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	160.70	05/2014 -	05/2014
99	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
100	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	616.00	11/2013 -	11/2013
101	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	712.90	07/2013 -	07/2013
102	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
103	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	604.50	03/2014 -	03/2014
104	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	1,085.00	05/2014 -	05/2014
105	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	177.50	06/2014 -	06/2014
106	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	162.80	06/2015 -	06/2015

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
107	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]	4/2012	624.00 -	624.00	167.10	04/2014 -	04/2014
108	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
109	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	34.70	10/2014 -	10/2014
110	KRISHNANAGAR-BERHAMPUR - [N24000209]	2/2012	702.16 -	702.16	430.90	07/2014 -	07/2014
111	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	291.36	62.81	01/2014 -	01/2014
112	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	754.50	09/2014 -	09/2014
113	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]	12/2011	1,047.00 -	1,047.00	201.60	06/2014 -	06/2014
114	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
115	SAMAIKHALI GANDHIDHAM - [N24000223]	9/2010	805.39 -	805.39	543.70	12/2013 -	12/2013
116	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	30.19	12/2015 -	12/2015
117	2 LANING WITH PS KANPUR KABRAI - [N24000221]	1/2013	373.47 -	373.47	38.08	07/2014 -	07/2014
118	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	108.20	10/2014 -	10/2014
119	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	13.39	09/2015 -	09/2015
120	FOUR LANING OF ORISSA CHATTISHGARH BORDER [N24000218]	2/2013	1,232.00 -	1,232.00	119.60	08/2015 -	08/2015
121	4-laning of Raiganj-Dalkola - [N24000204]	2/2011	580.43 -	580.43	218.50	08/2013 -	08/2013
122	4-laning of Brahampore-Faraka - [N24000203]	2/2011	998.79 -	998.79	1,088.00	08/2013 -	08/2013
123	4-laning of Faraka-Raiganj - [N24000202]	2/2011	1,078.84 -	1,078.84	1,134.00	08/2013 -	08/2013
124	BAREILY-SITAPUR - [N24000200]	3/2011	1,046.00 -	1,046.00	325.70	09/2013 -	09/2013
125	BEAWAR-PALI-PINDWARA - [N24000199]	12/2011	2,388.00 -	2,388.00	1,118.00	06/2014 -	06/2014
126	PANIKHOLI-RIMOLI - [N24000197]	3/2012	1,410.00 -	1,410.00	153.70	09/2014 -	09/2014
127	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]	11/2011	909.00 -	909.00	867.50	05/2014 -	05/2014
128	BHUBANESWAR TO PURI - [N24000195]	3/2011	500.29 -	500.29	450.90	08/2013 -	08/2013

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
129	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	788.00	03/2014 -	03/2014
130	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	129.80	02/2014 -	02/2014
131	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	333.90	01/2014 -	01/2014
132	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
133	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
134	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
135	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	14.58	12/2013 -	12/2013
136	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
137	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,025.00	11/2013 -	11/2013
138	DEOLI-KOTA - [N24000148	1/2011	593.00 -	593.00	524.00	07/2013 -	07/2013
139	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,431.00	06/2013 -	06/2013
140	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,284.00	06/2013 -	06/2013
141	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	797.00	08/2013 -	08/2013
142	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,262.00	10/2014 -	10/2014
143	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	1,110.00	11/2013 -	11/2013
	Total		46,303.02 -	46,303.02	22,854.78		
	<u>Shipping & Ports</u>						
144	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
145	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060	2/2011	830.00 -	621.53	-	05/2013 -	05/2013
	Total		1,796.46 -	1,616.35	363.20		
	<u>Steel</u>						

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
146	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078]	7/2012	332.65 -	332.65	54.07	08/2014 -	08/2014
147	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]	1/2012	254.90 -	254.90	2.88	12/2014 -	12/2014
	Total		587.55 -	587.55	56.95		
	<u>Urban Development</u>						
148	DELHI MRTS PHASE-III - [N28000056]	9/2011	35,242.00 -	35,242.00	3,222.85	03/2016 -	03/2016
149	FARIDABAD EXTENSION - [N28000057]	9/2011	2,494.00 -	2,494.00	264.96	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	3,487.81		
	Grand Total		253,345.60	253,199.73	53,015.87		

List of Delayed Project w.r.t. Original Schedule

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	2,771.00	12/2015 -	11/2016	11	-
2	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	1,937.00	12/2016 -	03/2017	3	-
	Total		23,779.00 -	23,779.00	4,708.00				
	<u>Civil Aviation</u>								
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	215.29	05/2012 -	06/2013	13	-
4	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	226.70	01/2011 04/2013	12/2014	47	20
	Total		645.07 -	645.07	441.99				
	<u>Coal</u>								
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,714.27	06/2009 -	01/2014	55	-
6	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	109.05	03/2010 -	03/2014	48	-
7	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.49	03/2011 -	03/2014	36	-
8	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	366.34	03/2013 -	03/2014	12	-
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,284.55	03/2012 -	03/2014	24	-
10	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	102.56	03/2012 -	03/2014	24	-
11	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	704.25	03/2013 09/2012	10/2014	19	25

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
12	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, Madhya Pradesh	10/2007	259.40 -	259.40	6.26	03/2012 -	03/2015	36	-
13	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL, Odisha	12/2007	457.77 -	457.77	113.13	03/2013 -	03/2015	24	-
14	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL, Odisha	12/2007	172.08 -	172.08	119.73	03/2010 -	03/2015	60	-
15	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL, Odisha	11/2008	479.63 -	479.63	126.19	03/2013 -	03/2015	24	-
16	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, Andhra Pradesh	03/2010	181.19 -	181.19	34.29	03/2012 -	03/2015	36	-
17	Purnadih OCP (3.0 MTY) - [N06000085]CCL, Jharkhand	07/2008	210.98 -	210.98	89.20	03/2013 -	03/2015	24	-
18	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL, Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,406.74	03/2014 -	03/2016	24	-
19	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL, Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,240.49	03/2014 -	03/2016	24	-
20	MAGADH OC 20 MTY (CCL) - [N06000015]CCL, Jharkhand	08/2008	469.78 -	706.40	24.38	07/2012 -	03/2016	44	-
21	CHURCHA ROUG (1.35 MTY) - [N06000046]SECL, Chhatisgarh	06/2008	462.35 -	462.35	264.13	03/2014 -	03/2016	24	-
22	KAKATIYA LONGWALL - [N06000048]SCCL, Andhra Pradesh	12/2008	453.63 -	453.63	85.21	12/2012 -	03/2016	39	-
23	RAJMAHAL OC EXP. - [N06000056]ECL, Jharkhand	09/2009	153.82 -	153.82	24.89	03/2014 -	03/2016	24	-
24	PENGANGA OC - [N06000066]WCL, Maharashtra	10/2008	339.77 -	339.77	1.01	03/2014 -	03/2016	24	-
25	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL, Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
26	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL, Chhatisgarh	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016	24	-
27	Churi Benti UG (0.81 MTY) - [N06000083]CCL, Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
28	Tapin OCP (2.5 MTY) - [N06000086]CCL, Jharkhand	08/2008	264.68 -	264.68	117.18	03/2012 -	03/2016	48	-
29	JHANJRA R-VI SEAM PSLW - [N06000020]ECL, West Bengal	11/2006	287.18 -	287.17	0.92	03/2011 -	03/2017	72	-

						(May, 2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
30	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL, Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
31	North Urimari OCP (3.0 MTY) - [N06000084]JCL, Jharkhand	12/2007	179.87 -	179.87	55.54	03/2012 -	03/2017	60	-
32	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC, Tamil Nadu	06/2011	5,907.11 -	5,907.11	29.84	12/2015 -	12/2017	24	-
	Total		24,633.81 -	28,090.60	12,373.63				
	<u>Steel</u>								
33	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	258.32	02/2011 -	06/2013	28	-
34	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	252.86	08/2010 -	06/2013	34	-
35	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	10,366.21	10/2009 -	07/2013	45	-
36	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	140.71	10/2012 -	08/2013	10	-
37	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	450.00	246.54	05/2012 -	08/2013	15	-
38	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, Karnataka	02/2011	898.55 -	898.55	198.57	05/2013 11/2013	11/2013	6	0
39	Bailadila Iron Ore Project Deposit-11B (NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	350.85	12/2011 03/2012	12/2013	24	21
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,087.79	12/2011 -	12/2013	24	-
41	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00 -	6,325.00	2,624.65	12/2011 -	12/2013	24	-
42	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Odisha	09/2008	11,812.00 11,812.00	11,812.00	6,841.66	03/2013 -	12/2013	9	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
43	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	291.02	04/2013 12/2013	12/2013	8	0
44	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	750.85	12/2012 -	12/2013	12	-
45	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	5,179.68	03/2013 -	03/2014	12	-
46	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	4.29	11/2013 -	03/2014	4	-
47	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	70.98	10/2013 -	03/2014	5	-
	Total		64,698.32 -	70,855.86	40,664.98				
	<u>Petrochemicals</u>								
48	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	4,510.51				
	<u>Petroleum</u>								
49	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 973.79	973.79	729.51	03/2011 05/2011	05/2013	26	24
50	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	296.85	03/2006 03/2013	06/2013	87	3
51	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	06/2013	54	2
52	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,881.73	09/2010 03/2012	06/2013	33	15
53	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	06/2013	37	3
54	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,663.16	09/2011 03/2012	06/2013	21	15

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
55	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,441.01	09/2011 05/2012	06/2013	21	13
56	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013	2	-
57	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	06/2013	12	-
58	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	170.77	08/2012 -	06/2013	10	-
59	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	215.02	03/2013 -	06/2013	3	-
60	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	176.83	04/2012 -	06/2013	14	-
61	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	704.59	03/2010 03/2012	07/2013	40	16
62	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	920.79	07/2010 05/2012	07/2013	36	14
63	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	726.73	12/2011 -	07/2013	19	-
64	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	180.06	02/2013 -	07/2013	5	-
65	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,295.14	01/2012 -	07/2013	18	-
66	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,124.72	09/2012 -	09/2013	12	-
67	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	541.27	01/2013 -	09/2013	8	-
68	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	95.34	09/2012 -	09/2013	12	-
69	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	701.47	07/2012 -	10/2013	15	-
70	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	215.26	11/2012 -	10/2013	11	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
71	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
72	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	273.53	05/2013 -	11/2013	6	-
73	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	4,464.10	08/2010 03/2012	12/2013	40	21
74	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.95	09/2011 -	12/2013	27	-
75	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	249.68	03/2012 -	12/2013	21	-
76	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	-	10/2011 -	12/2013	26	-
77	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	-	10/2011 -	12/2013	26	-
78	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	35.90	08/2013 -	01/2014	5	-
79	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
80	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	637.21	03/2007 03/2014	03/2014	84	0
81	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	21,762.00	11/2012 -	03/2014	16	-
82	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,410.63	03/2013 -	03/2014	12	-
83	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	-	06/2012 -	03/2014	21	-
84	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	5,916.65	1,301.61	03/2013 03/2014	04/2014	13	1
85	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	04/2014	1	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.49	10/2010 -	12/2014	50	-
87	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	586.00	5.55	07/2015 -	08/2015	1	-
88	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.36	01/2013 -	12/2015	35	-
89	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	20.90	12/2015 -	05/2016	5	-
90	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.44	03/2007 03/2017	03/2017	120	0
	Total		118,653.05 -	133,286.25	72,140.77				
	<u>Power</u>								
91	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 -	758.75	639.43	01/2010 -	06/2013	41	-
92	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	1,738.26	11/2009 02/2013	07/2013	44	5
93	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	149.17	06/2012 -	07/2013	13	-
94	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	76.74	10/2012 -	07/2013	9	-
95	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	-	10/2011 -	07/2013	21	-
96	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	156.80	11/2011 -	09/2013	22	-
97	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	817.81	05/2012 -	09/2013	16	-
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	130.43	01/2013 -	09/2013	8	-
99	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	84.64	04/2013 -	09/2013	5	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
100	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, Assam	08/2008	144.02 -	204.29	-	06/2012 -	09/2013	15	-
101	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL, Assam	08/2008	126.18 -	159.54	-	06/2012 -	09/2013	15	-
102	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC, Jammu and Kashmir	08/2006	611.01 -	936.00	739.41	08/2010 01/2013	10/2013	38	9
103	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC, Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,301.00	10/2012 -	11/2013	13	-
104	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL, Multi State	10/2006	975.96 -	975.96	881.79	10/2009 -	12/2013	50	-
105	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL, Multi State	12/2008	7,031.88 -	7,031.88	4,456.16	12/2012 -	12/2013	12	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL, Multi State	02/2009	509.66 -	509.66	362.90	11/2011 -	12/2013	25	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL, Multi State	02/2009	410.29 -	410.29	266.41	02/2012 -	12/2013	22	-
108	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC, Himachal Pradesh	10/2005	2,304.56 -	2,716.00	1,805.96	10/2010 01/2013	03/2014	41	14
109	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,420.93	01/2012 -	03/2014	26	-
110	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL, Multi State	10/2008	4,824.12 -	4,824.12	3,388.27	10/2012 -	03/2014	17	-
111	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL, Multi State	08/2008	2,360.95 -	2,580.90	2,050.21	08/2012 -	03/2014	19	-
112	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL, Multi State	08/2008	7,075.33 -	7,075.33	5,797.73	08/2012 -	03/2014	19	-
113	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL, Multi State	02/2010	2,144.00 -	2,144.00	1,278.57	12/2012 -	03/2014	15	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
114	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	550.64	11/2012 -	03/2014	16	-
115	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,027.69	03/2013 -	03/2014	12	-
116	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,492.08	12/2013 -	03/2014	3	-
117	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	264.68	07/2013 -	03/2014	8	-
118	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	812.28	04/2013 -	03/2014	11	-
119	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,130.75	09/2009 06/2013	05/2014	56	11
120	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	866.87	08/2012 -	06/2014	22	-
121	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	352.26	11/2011 -	07/2014	32	-
122	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,358.91	4,968.00	04/2009 -	09/2014	65	-
123	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 -	573.99	565.32	08/2012 08/2013	09/2014	25	13
124	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,000.00	08/2013 -	09/2014	13	-
125	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	639.72	11/2012 -	09/2014	22	-
126	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	237.25	11/2013 -	09/2014	10	-
127	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	62.70	01/2013 -	12/2014	23	-
128	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	887.65	11/2013 -	12/2014	13	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	418.04	07/2014 -	02/2015	7	-
130	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,413.59	11/2012 -	03/2015	28	-
131	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	23.70	04/2015 -	05/2015	1	-
132	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,911.99	08/2013 -	06/2015	22	-
133	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,837.00	07/2011 -	10/2015	51	-
134	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	2,978.48	1,827.00	03/2013 -	03/2016	36	-
135	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,422.44	349.34	07/2014 -	05/2016	22	-
136	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 -	2,978.86	483.98	07/2010 -	11/2016	76	-
137	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	1,497.94	01/2016 01/2016	11/2016	10	10
138	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,457.00	12/2009 -	02/2017	86	-
139	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	2,496.90	2,270.21	05/2013 06/2016	03/2017	46	9
140	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	5,668.68	09/2010 08/2014	12/2017	87	40
141	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	3,455.29	09/2009 07/2014	03/2018	102	44
	Total		120,802.22 -	134,161.74	88,014.27				
	<u>Railways</u>								

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
142	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	221.82	03/2002 -	07/2013	136	-
143	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	548.65	03/1994 -	10/2013	235	-
144	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	250.82	12/2009 03/2011	10/2013	46	31
145	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	126.50	12/2011 11/2013	11/2013	23	0
146	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	165.13	12/2012 -	12/2013	12	-
147	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
148	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	469.03	03/2013 -	03/2014	12	-
149	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	261.70	116.77	02/2006 -	06/2014	100	-
150	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014	66	66
151	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	206.41	03/2009 03/2009	08/2014	65	65
152	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	210.67	12/2008 -	09/2014	69	-
153	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,062.20	03/2009 12/2012	12/2014	69	24
154	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	246.22	06/2013 06/2013	12/2014	18	18
155	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	176.41	03/2007 03/2007	03/2015	96	96
156	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.20	12/2010 12/2010	03/2015	51	51
157	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,443.16	12/2008 -	03/2015	75	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
158	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	124.38	12/2012 -	03/2015	27	-
159	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,498.06	03/2009 -	03/2015	72	-
160	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.65	2,735.50	04/2008 03/2014	12/2015	92	21
161	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,801.39	10/2007 12/2012	12/2015	98	36
162	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	529.23	249.36	02/2010 11/2012	12/2015	70	37
163	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015	69	-
164	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	475.23	03/2014 -	12/2015	21	-
165	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	223.23	03/2004 12/2010	03/2016	144	63
166	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	54.51	03/2014 -	03/2016	24	-
167	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	443.71	06/2005 07/2011	06/2016	132	59
168	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	44.65	03/2016 -	06/2016	3	-
169	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,423.98	478.51	03/2005 12/2008	12/2016	141	96
170	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,207.39	03/2014 03/2016	12/2016	33	9
171	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,438.50	03/2011 03/2014	03/2017	72	36
172	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	205.54	03/2010 03/2017	03/2017	84	0
173	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	89.40	04/2014 -	03/2017	35	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
174	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017	15	-
175	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,446.81	8.45	03/2015 -	03/2017	24	-
176	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	03/2001 -	12/2017	201	-
	Total		26,532.81 -	73,528.38	29,076.52				
	<u>Road Transport & Highways</u>								
177	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013	110	-
178	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	326.80	10/2008 -	06/2013	56	-
179	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	286.60	06/2011 06/2011	06/2013	24	24
180	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	06/2013	54	-
181	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	06/2013	48	-
182	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.26	02/2004 -	06/2013	112	-
183	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	303.02	10/2009 -	06/2013	44	-
184	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	501.90	09/2009 -	06/2013	45	-
185	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	06/2013	112	-
186	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	646.60	05/2010 -	06/2013	37	-
187	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,293.00	07/2012 -	06/2013	11	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
188	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,056.00	05/2012 -	06/2013	13	-
189	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,686.00	08/2011 -	06/2013	22	-
190	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	772.60	10/2011 -	06/2013	20	-
191	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,959.00	12/2012 -	06/2013	6	-
192	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	944.50	01/2013 -	06/2013	5	-
193	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	16	-
194	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	1,259.00	11/2012 -	06/2013	7	-
195	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	630.40	02/2013 -	07/2013	5	-
196	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	195.57	08/2004 07/2010	08/2013	108	37
197	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	195.90	08/2004 -	08/2013	108	-
198	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	08/2013	65	-
199	SALEM - U / UNDRUPET(BOT - 1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	08/2013	31	-
200	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013	21	-
201	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	797.20	03/2013 -	08/2013	5	-
202	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	114.70	05/2013 -	08/2013	3	-
203	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	294.30	05/2008 -	09/2013	64	-
204	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.83	10/2008 -	09/2013	59	-
205	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	283.10	06/2008 -	09/2013	63	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
206	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	258.40	06/2008 -	09/2013	63	-
207	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	200.00	246.20	06/2008 -	09/2013	63	-
208	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	09/2013	4	-
209	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
210	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	608.10	02/2013 -	10/2013	8	-
211	BHOPAL-SANCHI - [N24000192]NHAI, Madhya Pradesh	10/2011	209.00 -	209.00	13.80	01/2013 -	10/2013	9	-
212	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
213	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	231.80	09/2007 -	12/2013	75	-
214	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	294.90	10/2008 -	12/2013	62	-
215	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	264.30	01/2009 -	12/2013	59	-
216	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	441.45	09/2008 -	12/2013	63	-
217	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	299.20	06/2008 -	12/2013	66	-
218	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	202.90	05/2008 -	12/2013	67	-
219	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya Pradesh	12/2003	407.60 -	407.60	186.40	06/2010 -	12/2013	42	-
220	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
221	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	1,675.00	09/2012 -	12/2013	15	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
222	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70 -	1,673.70	2,836.00	10/2011 -	12/2013	26	-
223	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
224	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	805.39	563.30	03/2013 -	12/2013	9	-
225	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45 -	232.45	295.40	09/2010 -	01/2014	40	-
226	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00 -	325.00	447.50	05/2013 -	02/2014	9	-
227	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014	66	-
228	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	236.50	06/2005 -	03/2014	105	-
229	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	237.30	06/2008 -	03/2014	69	-
230	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	279.80	06/2008 -	03/2014	69	-
231	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	182.50	04/2008 -	03/2014	71	-
232	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	242.40	04/2008 -	03/2014	71	-
233	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	465.50	225.70	09/2007 -	03/2014	78	-
234	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	855.90	07/2010 -	03/2014	44	-
235	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	353.37	403.50	10/2011 -	03/2014	29	-
236	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	193.45	47.41	11/2012 -	03/2014	16	-
237	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	351.54	392.70	05/2013 -	03/2014	10	-
238	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	512.10	03/2013 -	03/2014	12	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
239	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	245.40	10/2013 -	03/2014	5	-
240	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	-	10/2013 -	03/2014	5	-
241	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014	79	-
242	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,127.00	03/2013 -	04/2014	13	-
243	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	464.10	02/2014 -	04/2014	2	-
244	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	303.30	02/2009 03/2014	05/2014	63	2
245	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	296.80	04/2008 -	05/2014	73	-
246	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	132.70	07/2009 -	05/2014	58	-
247	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.84	10/2008 -	06/2014	68	-
248	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	114.80	11/2008 -	06/2014	67	-
249	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
250	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	588.50	07/2013 -	06/2014	11	-
251	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014	53	-
252	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	38.55	09/2013 -	07/2014	10	-
253	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	101.10	07/2012 -	07/2014	24	-
254	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.80	09/2009 -	09/2014	60	-
255	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	272.50	04/2010 -	11/2014	55	-

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
256	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014	68	-
257	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	45.43	11/2008 -	12/2014	73	-
258	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	141.80	04/2009 -	12/2014	68	-
259	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-
260	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	932.30	02/2010 -	12/2014	58	-
261	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
262	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	307.90	08/2013 -	02/2015	18	-
263	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
264	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,718.00	08/2014 -	07/2015	11	-
265	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
266	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	843.40	07/2015 -	06/2016	11	-
	Total		50,425.79 -	52,337.58	48,232.63				
	<u>Shipping & Ports</u>								
267	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2013	06/2013	87	0
268	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	5	0
269	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	07/2013	18	10

						(May,2013)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
270	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	418.64	12/2012 10/2013	10/2013	10	0
271	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	946.21	12/2010 09/2012	04/2014	40	19
272	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
	Total		6,223.08 -	7,475.19	5,371.63				
	<u>Telecommunications</u>								
273	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9
274	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	178.11	05/2011 -	09/2013	28	-
275	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	80.05	06/2009 -	12/2013	54	-
276	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
277	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
	Total		2,934.85 -	2,774.50	1,280.59				
	Grand Total		444,788.61	535,854.17	306,815.52				

List of Projects Without Milestones w.r.t. Original Schedule

				(May,2013)		
<u>Date of Commissioning</u>						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Civil Aviation</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	06/2013	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	12/2014	0/0
6	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00 -	03/2015 -	03/2015	0/0
	Total		5,473.58 -			0/0
	<u>Coal</u>					
7	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	04/2014 -	04/2014	0/0
8	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
9	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,Andhra Pradesh	06/2012	365.01 -	06/2015 -	06/2015	0/0
10	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	- -	03/2016	0/0
11	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,Andhra Pradesh	07/2012	417.33 -	07/2016 -	07/2016	0/0
	Total		2,782.63 -			0/0
	<u>Steel</u>					
12	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	08/2014 -	08/2014	0/0
13	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		587.55 -			0/0
	<u>Petroleum</u>					
14	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 973.79	03/2011 05/2011	05/2013	0/0
15	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	06/2013	0/0
16	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	06/2013	0/0

(May,2013)

Date of Commissioning

Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
17	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	06/2013	0/0
18	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	06/2012 -	06/2013	0/0
19	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	06/2013	0/0
20	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	06/2013	0/0
21	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012 -	06/2013	0/0
22	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
23	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	07/2013	0/0
24	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	07/2013	0/0
25	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	07/2013	0/0
26	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
27	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
28	DBPL-II - [N16000147]GAIL,Multi State	06/2009	486.00 -	09/2013 -	09/2013	0/0
29	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
30	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
31	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	11/2013	0/0
32	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
33	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2013	0/0
34	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0
35	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	10/2011 -	12/2013	0/0
36	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	10/2011 -	12/2013	0/0
37	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
38	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
39	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	02/2014	0/0
40	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
41	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
42	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	03/2014	0/0
43	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 5,916.65	03/2013 03/2014	04/2014	0/0
44	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	04/2014	0/0
45	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
46	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
47	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	08/2014 -	08/2014	0/0
48	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
49	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0
50	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2014	0/0
51	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	12/2014 -	12/2014	0/0
52	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
53	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
54	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	03/2015 -	03/2015	0/0
55	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	04/2015	0/0
56	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	05/2015 -	05/2015	0/0
57	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
58	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	07/2015 -	08/2015	0/0
59	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0
60	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
61	IREF - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
62	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
63	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	-	0/0
	Total		103,729.59 -			0/0
	Power					
64	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	10/2011 -	07/2013	0/0

(May,2013)

Date of Commissioning

Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
65	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	06/2012 -	09/2013	0/0
66	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	06/2012 -	09/2013	0/0
67	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	05/2014	0/0
68	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
69	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
70	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	11/2014	0/0
71	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	03/2015 -	03/2015	0/0
72	COMMON TR. SYS. ASSOCIATED WITH EAST A.P - [N18000143]PGCIL,Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
73	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
	Total		7,160.03 -			0/0
	<u>Railways</u>					
74	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
75	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
76	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
77	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
78	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
79	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
80	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
81	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0
82	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
83	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
84	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
85	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
86	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
87	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
88	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
89	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
90	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
91	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
92	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
93	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
94	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
95	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
96	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
97	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
98	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
99	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
100	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
101	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
102	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
103	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
104	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
105	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
106	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
107	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
108	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
109	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
110	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013	0/0
111	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	06/2013	0/0
112	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	07/2013	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
113	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
114	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
115	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
116	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
117	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
118	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2014	0/0
119	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
120	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
121	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
122	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
123	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
124	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
125	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
126	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
127	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 261.70	02/2006 -	06/2014	0/0
128	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
129	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
130	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
131	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
132	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	12/2014	0/0
133	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	02/2015	0/0
134	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
135	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
136	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
137	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0

(May,2013)

Date of Commissioning

Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
138	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2015	0/0
139	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
140	Himmatnagar - Udaipur Gauge Convesion (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
141	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0
142	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	03/2015	0/0
143	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
144	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
145	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 529.23	02/2010 11/2012	12/2015	0/0
146	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2015	0/0
147	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	12/2015	0/0
148	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2016	0/0
149	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2016	0/0
150	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0
151	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
152	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	03/2016 -	03/2016	0/0
153	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
154	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
155	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	12/2016	0/0
156	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
157	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
158	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2017	0/0
160	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	03/2017	0/0
161	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2017	0/0
162	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0

			(May,2013)			
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
163	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
164	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
165	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-	0/0
166	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
167	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
168	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
169	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 380.00	03/2009 11/2012	-	0/0
170	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
171	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
172	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-	0/0
173	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-	0/0
174	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-	0/0
175	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-	0/0
176	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-	0/0
177	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-	0/0
178	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
179	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-	0/0
180	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
181	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
182	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
183	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
184	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
185	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
186	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
187	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
188	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
189	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
190	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
191	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
192	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
193	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
194	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
195	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
196	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
197	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
198	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
199	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
200	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		66,387.42 -			0/0
	Road Transport & Highways					
201	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008	0/0
202	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
203	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	06/2013	0/0
204	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	06/2013	0/0
205	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	06/2013	0/0
206	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	06/2013	0/0
207	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	06/2013	0/0
208	GWALIOR BYPSS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	06/2013	0/0
209	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	09/2009 -	06/2013	0/0
210	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	06/2013	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
211	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	06/2013	0/0
212	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	06/2013	0/0
213	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	06/2013	0/0
214	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	06/2013	0/0
215	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
216	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	06/2013	0/0
217	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	06/2013	0/0
218	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013	0/0
219	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
220	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
221	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
222	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
223	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	07/2013	0/0
224	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0
225	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	07/2013	0/0
226	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	08/2013	0/0
227	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	08/2013	0/0
228	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	08/2013	0/0
229	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	08/2013	0/0
230	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	11/2011 -	08/2013	0/0
231	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	03/2013 -	08/2013	0/0
232	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	08/2013	0/0
233	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	08/2013	0/0
234	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	08/2013	0/0
235	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	08/2013 -	08/2013	0/0

				(May,2013)		
<u>Date of Commissioning</u>						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
236	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	08/2013	0/0
237	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	08/2013	0/0
238	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	08/2013	0/0
239	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	09/2013	0/0
240	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	09/2013	0/0
241	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	09/2013	0/0
242	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	09/2013	0/0
243	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	09/2013	0/0
244	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
245	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	09/2013	0/0
246	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	09/2013	0/0
247	Pune-sholapur,pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
248	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	10/2013	0/0
249	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
250	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0
251	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	11/2013	0/0
252	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0
253	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013	0/0
254	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
255	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013	0/0
256	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	12/2013	0/0
257	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	12/2013	0/0
258	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2013	0/0
259	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2013	0/0
260	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	12/2013	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
261	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	12/2013	0/0
262	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	12/2013	0/0
263	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	06/2011 -	12/2013	0/0
264	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	09/2012 -	12/2013	0/0
265	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2013	0/0
266	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	04/2013 -	12/2013	0/0
267	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
268	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
269	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	12/2013	0/0
270	SAMAIKHIALI GANDHIDHAM - [N24000223]NHAI,Gujarat	09/2010	805.39 -	12/2013 -	12/2013	0/0
271	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	01/2014	0/0
272	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
273	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
274	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
275	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
276	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
277	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
278	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2014	0/0
279	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
280	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
281	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
282	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0
283	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
284	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
285	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2014	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
286	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
287	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
288	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
289	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
290	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
291	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
292	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
293	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	03/2014	0/0
294	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
295	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
296	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
297	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
298	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
299	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
300	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
301	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
302	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
303	2laning with PS Gopalganj-Chhapra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
304	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
305	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
306	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
307	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
308	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
309	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
310	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0

				(May,2013)		
Date of Commissioning						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
311	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
312	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
313	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2014	0/0
314	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
315	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
316	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
317	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
318	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
319	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
320	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
321	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
322	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
323	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
324	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0
325	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	11/2014	0/0
326	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
327	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
328	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
329	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2014	0/0
330	NH CONNECTIVITY TO ICTT VALLARPADAEU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
331	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	12/2014	0/0
332	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	02/2015	0/0
333	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
334	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
335	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0

(May,2013)

Date of Commissioning

Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
336	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
337	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
338	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
339	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0
340	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
341	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		96,923.58 -			0/0
	Shipping & Ports					
342	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
343	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 09/2011	09/2011	0/0
344	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
345	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	08/2012	0/0
346	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
347	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
348	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
349	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
350	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013	0/0
351	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
352	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
353	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	07/2013	0/0
354	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 10/2013	10/2013	0/0
355	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
356	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
357	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	04/2014	0/0
358	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0

Date of Commissioning

Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
359	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
	Total		15,462.28 -			0/0
	<u>Telecommunications</u>					
360	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
361	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
362	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
363	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhy Pradesh	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
364	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	09/2013	0/0
365	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	12/2013	0/0
366	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2013	0/0
367	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	12/2013	0/0
368	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	-	0/0
369	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
370	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
371	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
372	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 -	-	0/0
	Total		5,699.24 -			0/0
	<u>Urban Development</u>					
373	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
374	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
375	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
	<u>Water Resources</u>					
376	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0

				(May,2013)		
<u>Date of Commissioning</u>						
Sl.No	Project	Date of Approval	Original/Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Grand Total		342,598.98			0/0

List of ongoing projects having cost overrun w.r.t. to original schedule

							(May,2013)
						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	17,270.00	16,007.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044	09/2003	3,492.00 -	5,677.00	4,080.48	09/2010 -	-
	Total		16,663.00 -	22,947.00	20,087.48		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037	08/2008	1,942.51 -	2,325.00	2,462.87	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038	08/2008	1,808.00 -	2,015.00	1,903.36	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	24,453.71		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,714.27	06/2009 -	01/2014
6	MAGADH OC 20 MTY (CCL) - [N06000015	08/2008	469.78 -	706.40	24.38	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	977.53	704.25	03/2013 -	10/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	123.40	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047	05/2008	4,904.54 -	6,540.93	4,284.55	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	209.87	03/2014 -	03/2016
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	81.18	03/2016 -	03/2016
	Total		8,579.45 -	39,549.64	32,595.61		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106	04/2006	5,460.61 -	8,920.00	4,510.51	04/2012 -	12/2013
	Total		5,460.61 -	48,469.64	37,106.12		

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	637.21	03/2007 -	03/2014
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.44	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	296.85	03/2006 -	06/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	02/2014
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	06/2013
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,881.73	09/2010 03/2012	06/2013
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,464.10	08/2010 03/2012	12/2013
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,204.61	05/2010 -	06/2013
21	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057	01/2009	756.00 -	898.00	913.72	- -	08/2013
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	21,762.00	11/2012 -	03/2014
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066	01/2008	224.00 -	394.00	312.61	- -	03/2013
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I - [N16000070	07/2009	238.68 -	312.00	289.64	01/2012 -	-
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	513.57	04/2013 -	06/2013
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	1,557.08	06/2012 -	06/2013
27	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	973.79	729.51	03/2011 -	05/2013
28	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	5,916.65	1,301.61	03/2013 -	04/2014
29	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	113.16	03/2015 -	03/2015
30	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	176.83	04/2012 -	06/2013
31	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	-	10/2011 -	12/2013

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
32	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	-	10/2011 -	12/2013
	Total		57,284.77 -	125,610.52	85,521.70		
	<u>Power</u>						
33	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	3,455.29	09/2009 -	03/2018
34	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,358.91	4,968.00	04/2009 -	09/2014
35	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	5,668.68	09/2010 -	12/2017
36	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) - [180100222]	10/2003	768.92 -	1,628.00	1,467.53	03/2007 -	04/2013
37	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	8,457.00	12/2009 -	02/2017
38	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	1,130.75	09/2009 -	05/2014
39	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	899.72	12/2007 -	-
40	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	1,805.96	10/2010 -	03/2014
41	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	1,738.26	11/2009 -	07/2013
42	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	1,868.68	09/2008 -	03/2013
43	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	739.41	08/2010 -	10/2013
44	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26 -	913.00	731.93	02/2011 -	01/2013
45	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	483.98	07/2010 -	11/2016
46	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATH-III HEP - [N18000018]	07/2006	557.24 -	758.75	639.43	01/2010 -	06/2013
47	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	1,497.94	01/2016 -	11/2016
48	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,422.44	349.34	07/2014 -	05/2016
49	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
50	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	2,050.21	08/2012 -	03/2014
51	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	527.59	- -	07/2013
52	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	-	06/2012 -	09/2013
53	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	-	06/2012 -	09/2013
	Total		48,353.13 -	190,018.52	128,057.40		
	<u>Railways</u>						
54	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	580.83	548.65	03/1994 -	10/2013
55	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	550.42	03/1995 -	03/2013
56	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	356.87	198.99	- 03/2010	-
57	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 -	925.30	606.94	- -	03/2012
58	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 175.30	725.00	551.15	06/1999 -	03/2011
59	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	8,822.50	03/2001 -	12/2017
60	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135]	04/1983	36.80 274.41	703.17	249.90	- -	03/2015
61	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	221.82	03/2002 -	07/2013
62	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]	04/1995	304.00 -	968.60	126.84	12/2012 -	-
63	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	579.37	599.40	- -	02/2012
64	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,512.86	223.23	03/2004 -	03/2016
65	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 -	900.05	688.14	12/2011 12/2010	03/2013
66	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08 -	2,820.00	113.86	- -	-
67	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	636.65	- -	01/2013

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
68	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	216.92	- -	03/2014
69	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
70	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	356.76	07/2012 -	-
71	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	300.79	03/2012 -	03/2013
72	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	775.36	760.40	- -	10/2012
73	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	480.00	655.91	02/2009 -	03/2012
74	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	100.89	- -	-
75	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	1,444.63	- -	03/2013
76	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.65	2,735.50	04/2008 12/2011	12/2015
77	MUNEERABAD- MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	189.54	- -	03/2012
78	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	176.41	03/2007 03/2007	03/2015
79	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	352.05	- -	12/2012
80	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.00	329.21	06/2004 -	12/2012
81	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.44	07/2008 -	07/2008
82	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,523.57	07/2005 -	-
83	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	377.65	05/2008 -	-
84	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	699.67	03/2012 -	-
85	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	954.23	12/2012 -	04/2013
86	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	250.82	12/2009 -	10/2013
87	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	741.20	12/2010 -	03/2015
88	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	116.70	- -	-

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
89	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	342.66	- 05/2009	05/2009
90	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255	03/2002	381.17 -	863.23	672.57	- -	03/2012
91	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	508.81	- -	03/2014
92	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	116.29	- -	-
93	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	836.10	06/2007 -	06/2007
94	TIRUCHIRAPPALI-NAGORE- KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	714.05	544.88	- -	-
95	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.92	803.33	- -	03/2013
96	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
97	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,443.16	12/2008 -	03/2015
98	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,429.24	12/2006 -	08/2010
99	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	280.09	02/2011 -	03/2013
100	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	620.77	- 12/2009	02/2012
101	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	489.69	12/2012 12/2012	02/2013
102	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.35	- -	-
103	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	478.51	03/2005 12/2008	12/2016
104	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	693.39	442.99	03/2012 -	12/2012
105	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	251.70	- -	03/2014
106	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	195.65	- 09/2009	-
107	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014
108	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,453.50	1,438.50	03/2011 -	03/2017

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
109	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	186.95	- -	-
110	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	341.41	288.14	03/2012 -	03/2013
111	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	768.87	479.24	- -	03/2010
112	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	1,062.20	03/2009 -	12/2014
113	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	1,801.39	10/2007 -	12/2015
114	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	406.92	97.07	- -	-
115	RAMGANJ-MUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	1,225.90	226.32	- -	-
116	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]	01/2004	915.70 -	2,232.50	1,954.09	- -	03/2014
117	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	218.19 -	472.00	172.27	- -	02/2013
118	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70 -	245.39	210.67	12/2008 -	09/2014
119	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 -	639.97	175.75	03/1998 08/2005	08/2005
120	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	194.91	- -	12/2013
121	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	818.29	84.10	02/2015 -	02/2015
122	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	206.41	03/2009 03/2009	08/2014
123	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 -	810.78	126.01	- -	-
124	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 -	289.93	257.91	12/2007 03/2010	-
125	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	114.01 283.95	477.88	433.30	03/2012 -	03/2013
126	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N220000027]	04/2005	240.00 -	355.00	334.59	03/2009 12/2009	-
127	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032]	04/2006	378.56 -	791.59	0.76	- -	-
128	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045]	03/1997	186.92 -	261.70	116.77	02/2006 -	06/2014
129	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049]	07/2006	743.00 -	1,117.11	437.69	03/2008 06/2008	-

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
130	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU - [N22000052]	04/2003	98.74 -	337.30	222.07	- -	03/2012
131	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
132	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	233.73	03/2010 -	-
133	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 -	529.23	249.36	02/2010 -	12/2015
134	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015
135	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,190.05	309.37	- -	-
136	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	634.48	- -	12/2012
137	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	435.87	396.76	03/2011 -	03/2011
138	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	406.40	331.85	- -	06/2013
139	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	56.06	- -	-
140	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	170.05	- -	-
141	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	385.20	135.06	- -	03/2015
142	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	40.88	- -	-
143	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	205.54	03/2010 -	03/2017
144	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	225.88	12/2010 -	03/2011
145	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	6,220.15	1,207.39	03/2014 -	12/2016
146	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	246.44	141.55	03/2012 -	03/2014
147	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	443.71	06/2005 -	06/2016

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
148	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	475.23	03/2014 -	12/2015
149	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,384.34	89.40	04/2014 -	03/2017
150	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
151	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017
152	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	469.03	03/2013 -	03/2014
153	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]	04/2010	2,069.60 -	2,298.42	54.51	03/2014 -	03/2016
154	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	286.84	03/2016 -	03/2016
155	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	246.74	03/2014 -	03/2014
156	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	96.15	12/2011 -	02/2012
157	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	126.50	12/2011 -	11/2013
158	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	139.01	12/2010 -	12/2010
159	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	404.39	17.21	03/2013 -	03/2013
160	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) [N22000123]	04/2008	318.24 -	468.62	1.72	03/2012 -	-
161	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,446.81	8.45	03/2015 -	03/2017
162	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95	191.35	03/2011 -	-
163	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	4,255.37	3,498.06	03/2009 -	03/2015
164	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	36.94	- -	-
	Total		48,954.66 -	329,518.95	189,623.54		
	<u>Road Transport & Highways</u>						
165	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
166	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014
167	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	194.20	03/2008 -	02/2008
168	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	294.30	05/2008 -	09/2013
169	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014
170	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	114.80	11/2008 -	06/2014
171	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014
172	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	132.70	07/2009 -	05/2014
173	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
174	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	225.70	09/2007 -	03/2014
175	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) [N24000133	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013
	Total		3,324.28 -	334,964.15	194,678.39		
	<u>Shipping & Ports</u>						
176	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,370.00	5.75	10/2008 -	08/2012
177	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	221.58	- 01/2009	12/2010
178	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	946.21	12/2010 -	04/2014
179	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	139.80	03/2006 -	06/2013
180	Construction of berthing and allied facilities off Tekra near Tuna, Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
181	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013

(May,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
182	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048	03/2009	3,500.00 -	4,150.00	3,661.95	01/2012 -	07/2013
183	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
184	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059	03/2007	245.67 -	373.22	371.18	04/2009 -	02/2011
	Total		8,628.97 -	345,981.05	200,607.99		
	<u>Steel</u>						
185	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10,366.21	10/2009 -	07/2013
186	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	350.85	12/2011 06/2010	12/2013
187	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	140.71	10/2012 -	08/2013
188	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	13,087.79	12/2011 -	12/2013
189	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00 -	343.58	258.32	02/2011 -	06/2013
190	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00 -	350.00	252.86	08/2010 -	06/2013
	Total		24,028.89 -	376,197.48	225,064.73		
	<u>Telecommunications</u>						
191	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	80.05	06/2009 -	12/2013
192	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013
193	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70 -	930.60	828.80	11/2010 -	09/2013
	Total		1,393.98 -	377,678.93	226,138.16		
	<u>Urban Development</u>						
194	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	2,482.18	06/2011 -	03/2013

						(May,2013)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original /Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
195	C/o office building for IDBI at bandra Kurla Complex, Mumbai - [N28000048	11/2006	114.18 173.08	173.08	-	04/2009 -	-
	Total		6,509.18 -	389,461.01	228,620.34		
	<u>Water Resources</u>						
196	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012
	Total		542.90 -	390,648.01	228,655.83		
	Grand Total		233,474.33	2,998,331.90	1,821,211.00		

List of ongoing projects having time and cost overrun w.r.to original

(May,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Coal</u>						
1	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,714.27	06/2009	01/2014
2	MAGADH OC 20 MTY (CCL) - [N06000015	08/2008	469.78 -	706.40	24.38	07/2012	03/2016
3	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	977.53	704.25	03/2013	10/2014
4	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047	05/2008	4,904.54 -	6,540.93	4,284.55	03/2012	03/2014
5	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	209.87	03/2014	03/2016
	Total		7,938.86 -	11,573.95	7,937.32		
	<u>Petrochemicals</u>						
6	Assam gas Cracker project - [N16000106	04/2006	5,460.61 -	8,920.00	4,510.51	04/2012	12/2013
	Total		5,460.61 -	20,493.95	12,447.83		
	<u>Petroleum</u>						
7	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	637.21	03/2007	03/2014
8	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.44	03/2007	03/2017
9	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	296.85	03/2006	06/2013
10	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006	02/2014
11	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008	06/2013
12	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,881.73	09/2010 03/2012	06/2013
13	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	4,464.10	08/2010 03/2012	12/2013
14	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,204.61	05/2010	06/2013
15	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	21,762.00	11/2012	03/2014
16	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	513.57	04/2013	06/2013
17	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	1,557.08	06/2012	06/2013

(May,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
18	North Tapti Gas Field Development - [N16000096]	07/2008	589.70 755.56	973.79	729.51	03/2011	05/2013
19	Development of Cluster-7 Fields - [N16000104]	03/2010	3,241.03 -	5,916.65	1,301.61	03/2013	04/2014
20	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	176.83	04/2012	06/2013
21	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	-	10/2011	12/2013
22	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	-	10/2011	12/2013
	Total		54,006.46 -	93,365.18	59,234.28		
<u>Power</u>							
23	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	3,455.29	09/2009	03/2018
24	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,358.91	4,968.00	04/2009	09/2014
25	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	5,668.68	09/2010	12/2017
26	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	8,457.00	12/2009	02/2017
27	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	1,130.75	09/2009	05/2014
28	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	1,805.96	10/2010	03/2014
29	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	1,738.26	11/2009	07/2013
30	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	739.41	08/2010	10/2013
31	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	483.98	07/2010	11/2016
32	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]	07/2006	557.24 -	758.75	639.43	01/2010	06/2013
33	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	1,497.94	01/2016	11/2016
34	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,422.44	349.34	07/2014	05/2016
35	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	2,050.21	08/2012	03/2014
36	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	-	06/2012	09/2013
37	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	-	06/2012	09/2013
	Total		38,706.92 -	145,431.62	92,218.53		

(May,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Railways</u>						
38	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	548.65	03/1994 -	10/2013
39	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,822.50	03/2001 -	12/2017
40	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	221.82	03/2002 -	07/2013
41	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	223.23	03/2004 -	03/2016
42	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.65	2,735.50	04/2008 12/2011	12/2015
43	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	176.41	03/2007 03/2007	03/2015
44	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	250.82	12/2009 -	10/2013
45	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	741.20	12/2010 -	03/2015
46	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,443.16	12/2008 -	03/2015
47	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	478.51	03/2005 12/2008	12/2016
48	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	271.99	02/2009 02/2009	08/2014
49	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,453.50	1,438.50	03/2011 -	03/2017
50	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	1,062.20	03/2009 -	12/2014
51	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,801.39	10/2007 -	12/2015
52	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	210.67	12/2008 -	09/2014
53	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	206.41	03/2009 03/2009	08/2014
54	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	186.92 -	261.70	116.77	02/2006 -	06/2014
55	PANSPURA-KHARAGPUR 3D LINE - [N22000076	09/2007	252.50 -	529.23	249.36	02/2010 -	12/2015
56	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	718.89	03/2010 -	12/2015
57	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	205.54	03/2010 -	03/2017
58	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,220.15	1,207.39	03/2014 -	12/2016
59	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	141.55	03/2012 -	03/2014
60	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.47	443.71	06/2005 -	06/2016
61	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,141.75	475.23	03/2014 -	12/2015

(May,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
62	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,384.34	89.40	04/2014 -	03/2017
63	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	58.79	12/2015 -	03/2017
64	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	469.03	03/2013 -	03/2014
65	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) - [N22000109]	04/2010	2,069.60 -	2,298.42	54.51	03/2014 -	03/2016
66	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	126.50	12/2011 -	11/2013
67	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,446.81	8.45	03/2015 -	03/2017
68	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	4,255.37	3,498.06	03/2009 -	03/2015
	Total		23,203.93 -	215,636.01	120,714.67		
<u>Road Transport & Highways</u>							
69	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00 -	241.53	161.45	04/2004 -	06/2013
70	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	142.60	09/2008 -	03/2014
71	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]	12/2003	284.00 -	359.00	294.30	05/2008 -	09/2013
72	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	83.98	04/2009 -	12/2014
73	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	114.80	11/2008 -	06/2014
74	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	59.89	09/2007 -	04/2014
75	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	132.70	07/2009 -	05/2014
76	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	179.23	02/2010 -	07/2014
77	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	225.70	09/2007 -	03/2014
78	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	08/2013
	Total		3,158.01 -	220,888.11	125,575.32		
<u>Shipping & Ports</u>							
79	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	946.21	12/2010 -	04/2014
80	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	139.80	03/2006 -	06/2013

(May,2013)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048	03/2009	3,500.00	4,150.00	3,661.95	01/2012	07/2013
	Total		4,878.00	227,098.11	130,323.28		
			-				
	<u>Steel</u>						
82	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00	12,291.00	10,366.21	10/2009	07/2013
			-			-	
83	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89	607.17	350.85	12/2011	12/2013
			-			06/2010	
84	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00	216.68	140.71	10/2012	08/2013
			-			-	
85	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00	16,408.00	13,087.79	12/2011	12/2013
			-			-	
86	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00	343.58	258.32	02/2011	06/2013
			-			-	
87	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069	07/2007	260.00	350.00	252.86	08/2010	06/2013
			-			-	
	Total		24,028.89	257,314.54	154,780.02		
			-				
	<u>Telecommunications</u>						
88	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15	158.72	80.05	06/2009	12/2013
			-			-	
89	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70	930.60	828.80	11/2010	09/2013
			-			-	
	Total		1,065.85	258,403.86	155,688.87		
			-				
	Grand Total		162,447.53	1,450,205.33	858,920.12		
