

**313th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
November, 2011**



RVNL – KHURDA ROAD PROJECT



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for November 2011 contains information on the status of the 582 Central Sector Infrastructure Projects, costing ₹ 150 Crores and above. During November 2011, three projects, namely “Western Region Strengthening Scheme-IX of PGCIL”, “Ringbunds to Jhajhanpur(BR-6) of NHAI” and “Thrissur to Angamali (NH-47) of NHAI” have reported completion.

The online reporting of the implementation status of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month. During November 2011, forty-two (42) projects have reported additional delays, vis-à-vis the date of completion reported in the previous month. The additional delays are in the range of 1 to 16 months, in respect of projects relating to Coal, Petroleum, Power, Road Transport and Highways, Telecommunications, Steel, Fertiliser and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	132	0
2.	ROAD TRANSPORT & HIGHWAYS	136	9
3.	POWER	91	13
4.	PETROLEUM	70	3
5.	COAL	50	1
6.	TELECOMMUNICATION	40	9
7.	SHIPPING & PORTS	25	0
8.	STEEL	16	5
9.	FERTILISERS	6	1
10.	CIVIL AVIATION	5	0
11.	ATOMIC ENERGY	4	1
12.	URBAN DEVELOPMENT	4	0
13.	MINES	1	0
14.	WATER RESOURCES	1	0
15.	PETROCHEMICALS	1	0
Total		582	42

3. The total original cost of implementation of the 582 projects was about ₹ 7, 12,007.92 Crores and their anticipated completion cost is likely to be ₹ 8, 21,529.93 Crores, which reflects an overall cost overrun of 15.38 %. The expenditure incurred on these projects till November, 2011 is ₹ 3, 48,301.14 Crores, which is 42.4 % of the revised cost of the projects.

4. Out of the 582 projects, 6 projects are ahead of schedule, 169 are on schedule, 242 projects are delayed and 115 projects have been sanctioned without any commissioning schedule/date Further, in case of 50 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized.

5. During the month under reference the projects reporting delays have marginally increased to 242 from 235 in October'2011. Out of 242 delayed projects, 45 projects had overall delay in the range of 1 to 12 months, 63 projects had a delay in the range of 13 to 24 months, 100 projects had a delay in the range of 25 to 60 months and 34 projects had a delay of 61 months and above.

6. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

7. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, law and order problems, delays in engineering designs, change of scope delays in pre-project activity, Maoist problems and forest and environment clearances etc. Brief reasons for cost overruns are mainly due to inflation, fluctuation of exchange rate, higher tender value, change of scope etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various

infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

The Sector-wise details of additional delays are as under:-

i) In the **Coal sector**, Tuticorin Thermal Power Project, NLC, Tamil Nadu has reported an additional delay of 4 months due to delay in issue of LOI, slow pacing of civil works and inadequate mobilization by the contractor.

ii) In the **Fertilizer sector**, Thal Ammonia Revamp Project, RCF, Haryana has reported an additional delay of 5 months due to poor performance by the contractor.

iii) In the **Petroleum Sector**, 3 projects have reported additional delays in the range of 2-4 months. Karanpur Moradabad-Kashipur-Rudrapur Pipeline Project, GAIL, has reported an additional delay of 2 months as the land owners are demanding for high compensation, Bawana Nangal Pipeline Project, GAIL, has reported an additional delay of 3 months due to delay in RoW acquisition for construction of the pipeline and Development of C- Series Fields, ONGC, has reported an additional delay of 4 months (overall delay of 39 months) however; no reason has been reported by the project authority.

iv) In the **Power Sector**, 13 projects have reported additional delays in the range of 1-16 months. Two projects have reported an additional delay of 1 month each, two projects have reported an additional delay of 2 months each and six projects have reported an additional delay of 3 months each. Mouda STPP, NTPC project has reported an additional delay of 4 months (overall delay of 7 months), for which no reasons have been reported by the project authority. The project, 765 KV System for Central Part of Northern Grid, PGCIL, has reported an additional delay of 13 months due to delay in land acquisition and project, Subansiri Lower HEP, NHPC has reported an additional delay of 16 months (overall delay of 63 months) due to cut-off wall issue and bridged damage at Ranganadi River.

v) In the **Atomic Energy Sector**, Kudankulam APP, NPCIL has reported an additional delay of 6 months (overall delay of 50 months) due to slippage of commitments by Atom Story Export (ASE).

vi) In Steel sector, 5 projects have reported additional delays in the range of 1-7 months. The project, Rebuilding of Coke Oven Battery No. 1 and 2, SAIL, has reported an additional delay of one month due to initial delay in design and engineering, 330 TPH Boiler -6 and Auxiliary System, RINL, has reported an additional delay of 2 months (overall delay of 19 months) due to delay in supply of equipments, Expansion of Bhilai Steel Plant, SAIL, has reported an additional delay of 3 months, for which reason has not been reported by the project authority, 67.5 MW TG-5 Auxiliary System Emergency Power Requirement, RINL, has reported an additional delay of 3 months (overall delay of 14 months) due to delay in supply of equipments and Augmentation of Iron Ore Storage in RMHP, RINL, has reported an additional delay of 7 months due to delay in appointment of consultant.

vii) In the Road Transport and Highways Sector, 9 projects have reported additional delays in the range of 1-12 months. 5 projects have reported additional delay of 1 month each due to slow progress of work by the contractor. Sunakhala-Ganjam(GQ), NH-5, NHAI and Salem-Undrupet (BOT), NH-68-B, NHAI have reported an additional delay of 3 months each due to delay in land acquisition. Rajmarg Choraha to Lakhnadon, KM 351 to KM 405.7, NHAI has reported an additional delay of 9 months (overall delay of 47 months) due to delay in obtaining clearance for tree cutting and Rajmarg Choraha to Lakhnadon, KM 297 – 351, NHAI has reported an additional delay of 12 months (overall delay of 50 months) due to delay in land acquisition .

viii) In Telecom sector, 9 projects have reported additional delays in the range of 4-10 months. ERP implementation in BSNL on Turnkey basis, BSNL has reported an additional delay of 4 months due to non-acceptance of APO for security stock and GSM equipment of 1867000 lines (2G) 383000 lines-3, BSNL and GSM equipment of 1625000 lines (2G) 325000 lines-3, BSNL have reported an additional delay of 9 months each due to delay in supply of equipment. Six projects have reported an

additional delay of 10 months each due to various reasons like problem of VSAT media in 2G case, delay in EB connection, delay in supply of equipment and poor performance by the contractor.

The status as on 01.12.2011 in respect of completion of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.



(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	136	9
2	Railways	132	0
3	Power	91	13
4	Petroleum	70	3
5	Coal	50	1
6	Telecommunications	40	9
7	Shipping & Ports	25	0
8	Steel	16	5
9	Fertilisers	6	1
10	Civil Aviation	5	0
11	Atomic Energy	4	1
12	Urban Development	4	0
13	Mines	1	0
14	Petrochemicals	1	0
15	Water Resources	1	0
	Total	582	42

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING crp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May,2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00
July,2011				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
August,2011				
<u>Power</u>				
30	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
31	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
32	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
33	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
34	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
35	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

September,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Petroleum</u>				
36	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
37	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
38	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
39	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH- 28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26
October,2011				
<u>Power</u>				
40	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA- III(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000043]	204.07	06/2011	129.60
November,2011				
41	WESTERN REGION STRENGTHENING SCHEME-IX(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000050]	230.89	01/2011	98.20
<u>Road Transport & Highways</u>				
42	RINGBUNDS TO JHAJHANPUR (BR-6)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000030]	340.00	06/2008	570.00
43	THRISSUR TO ANGAMALI (NH-47)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000037]	312.50	03/2009	604.40

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2011				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97


Summary of projects in the Flash Report for the month of November, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	584
Number of Projects completed/dropped/frozen in Previous Month	1
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects with Anticipated Less than Rs. 150 Cr. in Current Month	1
Number of Projects Added in Current Month	3
Number of Projects in Current Month	582


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 582 projects, 6 projects are ahead of schedule, 169 projects are on schedule and 242 projects are delayed. Of the balance, 115 projects do not have fixed dates of commissioning while 50 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

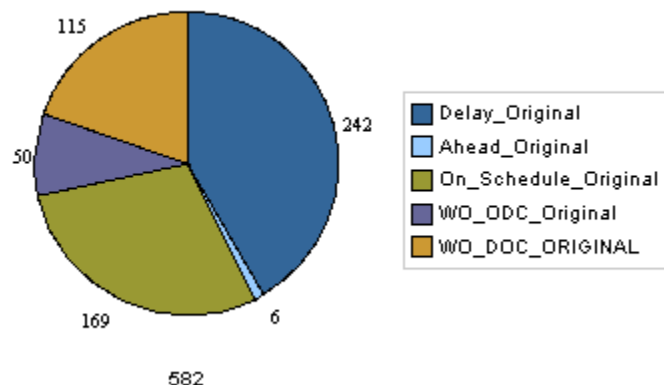

III. Investment Scenario

The Total Original cost of implementation of 582 projects when sanctioned, was of the order of Rs. 712007.92 crore but this was subsequently revised to Rs. 821529.93 crore implying a cost overrun of 15.4%. The expenditure incurred on these projects till November, 2011 is Rs. 348301.14 crore, which is 42.4% of the revised cost of the projects.

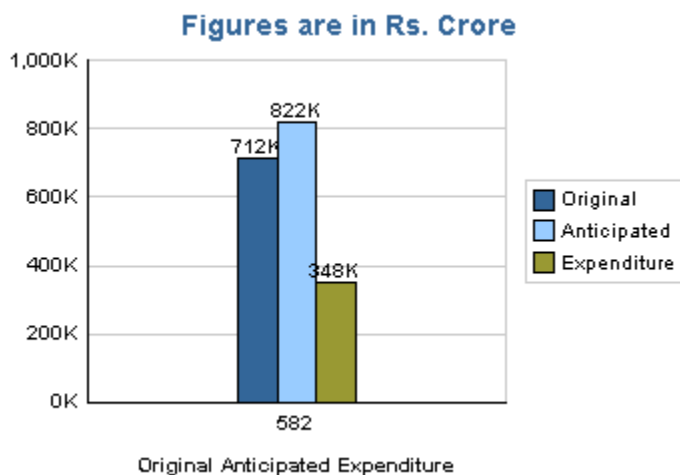

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	584
No of Projects Completed/Dropped/Frozen in Previous Month	1
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects with Anticipated Cost Less than Rs.150 Cr. In Current Month	1
No of Projects added in Current Month	3
No of Projects in Current Month	582

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	243	6	169	49	115	582	41.75
Latest Approved (Date)	255	9	208	32	79	582	43.81

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	474	571,580.60	606,822.79	230,265.63	37.90	35,242.19	6.20
Latest Approved (RCE)	108	187,735.50	214,707.14	118,035.51	55.00	26,971.64	14.40
Total (RCE)	582	759,316.10	821,529.93	348,301.14	42.40	62213.83	8.19
Original Cost of All Projects							
Original Cost	582	712,007.92	821,529.93	348,301.14	42.40	109,522.01	15.40

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	243	344,446.11	413,415.79	226,863.03	54.90	68,969.68	20.00
Latest Approved (RCE)	255	341,194.33	384,053.00	216,295.71	56.30	42,858.67	12.60

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	42	95,887.39	98,446.34	60,081.15	61.00	2,558.95	2.70

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	50	28,811.6	32,198.7	11.8	12	13,742.8	17,727.6	29.0
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	16	65,244.8	71,412.4	9.5	6	24,028.9	30,216.4	25.8
7	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
8	Petroleum	70	154,794.1	162,721.8	5.1	17	52,273.3	68,974.3	31.9
9	Power	91	190,920.1	197,203.7	3.3	10	23,524.6	29,873.1	27.0
10	Railways	132	65,054.7	132,323.5	103.4	101	37,121.1	104,446.7	181.4
11	Road Transport & Highways	136	75,509.8	77,315.0	2.4	13	3,890.9	6,265.2	61.0
12	Shipping & Ports	25	18,052.2	19,035.7	5.4	11	6,524.5	7,709.1	18.2
13	Telecommunications	40	19,713.1	20,297.7	3.0	5	2,114.4	2,781.7	31.6
14	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		582	712,007.9	821,529.9	15.4	184	200,238.2	320,125.8	59.9

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	3	28,122.0	32,960.0	11 - 50
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 17
3	Coal	50	28,811.6	32,198.7	11.8	17	11,824.7	14,752.2	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	0	0.0	0.0	-
6	Steel	16	65,244.8	71,412.4	9.5	3	40,400.0	45,964.0	3 - 36
7	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
8	Petroleum	70	154,794.1	162,721.8	5.1	30	72,263.2	82,263.7	2 - 120
9	Power	91	190,920.1	197,203.7	3.3	47	111,027.2	117,375.3	5 - 90
10	Railways	132	65,054.7	132,323.5	103.4	26	22,320.7	51,989.0	2 - 213
11	Road Transport & Highways	136	75,509.8	77,315.0	2.4	88	31,347.4	33,512.7	4 - 97
12	Shipping & Ports	25	18,052.2	19,035.7	5.4	10	8,208.4	9,033.6	2 - 93
13	Telecommunications	40	19,713.1	20,297.7	3.0	10	5,357.5	5,542.5	13 - 72
14	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		582	712,007.9	821,529.9	15.4	243	344,446.1	413,415.8	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	4	29,228.3	34,066.3	0 - 50
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 17
3	Coal	50	28,811.6	32,198.7	11.8	17	11,824.7	14,752.2	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	30 - 30
6	Steel	16	65,244.8	71,412.4	9.5	7	33,206.8	35,666.7	0 - 5
7	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
8	Petroleum	70	154,794.1	162,721.8	5.1	18	48,610.1	53,312.4	2 - 73
9	Power	91	190,920.1	197,203.7	3.3	40	102,917.3	105,792.9	5 - 83
10	Railways	132	65,054.7	132,323.5	103.4	37	27,127.7	60,802.5	0 - 213
11	Road Transport & Highways	136	75,509.8	77,315.0	2.4	88	31,347.4	33,512.7	4 - 97
12	Shipping & Ports	25	18,052.2	19,035.7	5.4	11	8,281.2	9,187.2	2 - 93
13	Telecommunications	40	19,713.1	20,297.7	3.0	23	12,227.9	12,535.7	5 - 72
14	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		582	712,007.9	821,529.9	15.4	255	322,438.0	384,053.0	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	50	30,528.6	32,198.7	5.5	6	4,961.1	7,098.9	43.1
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,401.8	4,401.8	0.0	0	0.0	0.0	0.0
6	Steel	16	71,120.1	71,412.4	0.4	3	598.0	910.3	52.2
7	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
8	Petroleum	70	167,529.7	162,721.8	-2.9	4	32,736.9	35,849.3	9.5
9	Power	91	195,734.8	197,203.7	0.8	3	15,453.8	16,987.6	9.9
10	Railways	132	82,773.4	132,323.5	59.9	88	42,723.4	92,333.9	116.1
11	Road Transport & Highways	136	75,509.8	77,315.0	2.4	13	3,890.9	6,265.2	61.0
12	Shipping & Ports	25	18,431.5	19,035.7	3.3	9	6,498.8	7,204.5	10.9
13	Telecommunications	40	19,745.3	20,297.7	2.8	3	1,287.5	1,903.1	47.8
14	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		582	759,316.1	821,529.9	8.2	134	133,693.9	205,174.7	53.5

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.07	11.74	0	0.00	0.00	0- 0
3	Coal	50	28,811.62	32,198.65	11.76	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	16	65,244.82	71,412.36	9.45	1	8,692.00	12,291.00	36- 36
7	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
8	Petroleum	70	154,794.07	162,721.78	5.12	14	19,581.72	34,561.21	3- 120
9	Power	91	190,920.07	197,203.66	3.29	5	5,281.85	9,165.13	18- 90
10	Railways	132	65,054.74	132,323.46	103.40	5	2,285.97	7,657.76	0- 80
11	Road Transport & Highways	136	75,509.76	77,315.01	2.39	0	0.00	0.00	0- 0
12	Shipping & Ports	25	18,052.23	19,035.72	5.45	2	567.88	582.03	5- 7
13	Telecommunications	40	19,713.13	20,297.68	2.97	0	0.00	0.00	0- 0
14	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
15	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		582	712007.92	821529.93	15.38	29	40970.71	69365.29	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	2	16,663.00	21,501.00	16- 50
2	Civil Aviation	5	5,021.58	5,611.07	11.74	2	3,750.51	4,340.00	10- 11
3	Coal	50	28,811.62	32,198.65	11.76	7	6,813.24	10,338.47	9- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	16	65,244.82	71,412.36	9.45	2	23,135.00	28,699.00	3- 36
7	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
8	Petroleum	70	154,794.07	162,721.78	5.12	17	52,273.26	68,974.31	3- 120
9	Power	91	190,920.07	197,203.66	3.29	8	21,271.16	25,887.04	7- 90
10	Railways	132	65,054.74	132,323.46	103.40	19	10,615.66	40,632.69	12- 213
11	Road Transport & Highways	136	75,509.76	77,315.01	2.39	13	3,890.90	6,265.24	7- 95
12	Shipping & Ports	25	18,052.23	19,035.72	5.45	7	3,728.52	4,751.17	6- 93
13	Telecommunications	40	19,713.13	20,297.68	2.97	4	1,354.24	1,681.67	17- 72
14	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
15	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		582	712007.92	821529.93	15.38	84	154524.9	230268.35	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
WESTERN REGION STRENGHTENING SCHEME-IX	04/2008	230.89	01/2011	230.89	11/2011	98.20
<u>Road Transport & Highways</u>						
RINGBUNDS TO JHAJHANPUR (BR-6)	12/2003	340.00	06/2008	340.00	11/2011	570.00
THRISSUR TO ANGAMALI (NH-47)	12/2003	312.50	03/2009	312.50	11/2011	604.40

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Coal</u>					
Muraidih UG	2/2011	339.88	4/2014	339.88	4/2014
Moonidih XV Seam UG	8/2011	1,230.27	4/2015	1,230.27	4/2015
<u>Steel</u>					
ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES	11/2011	254.55	11/2013	254.55	11/2013

VII. Milestones (Cumulative due & achieved)

Total	2333
Achieved up to month	1002

VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	08/2012	02/2013	6
<u>Coal</u>						
TUTICORIN THERMAL POWER PROJECT NLC	4,904.54	4,909.54	N.A.	10/2012	02/2013	4
<u>Fertilisers</u>						
THAL AMMONIA REVAMP PROJECT RCF	488.75	488.75	N.A.	11/2011	04/2012	5
<u>Steel</u>						
Rebuilding of coke oven battery No.1 and 2 (Bokar SAIL	500.90	500.90	N.A.	12/2011	01/2012	1
330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	N.A.	01/2012	03/2012	2
EXPANSION OF BHILAI STEEL PLANT SAIL	17,265.00	17,265.00	03/2013	03/2013	06/2013	3
67.5 MW TG-5 AUX. S'STEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	N.A.	01/2012	04/2012	3
Augmentation of Iron Ore Storage in RMHP RINL	480.00	460.00	N.A.	05/2012	12/2012	7
<u>Petroleum</u>						
KARANPUR MORADABAD- KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- GAIL	238.68	204.00	01/2012	01/2012	03/2012	2
BAWANA NANGAL PIPE LINE PROJECT GAIL	1,816.07	1,385.00	10/2010	12/2011	03/2012	3
DEVELOPMENT OF C- SERIES FIELDS ONGC	3,195.16	2,800.00	12/2008	11/2011	03/2012	4
<u>Power</u>						
BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	09/2014	10/2014	1
TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II PGCIL	238.25	238.25	05/2011	11/2011	12/2011	1
URI H.E.P STAGE -II (NHPC) NHPC	1,724.79	1,724.79	11/2009	02/2012	04/2012	2


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
WESTERN REGION STRENGTHENING SCHEME- II PGCIL	5,221.23	5,221.23	07/2010	12/2011	02/2012	2
PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.52	2,304.52	10/2010	03/2012	06/2012	3
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	557.24	01/2010	03/2012	06/2012	3
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII PGCIL	317.69	317.69	11/2011	03/2012	06/2012	3
TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP PGCIL	297.37	297.91	07/2011	12/2011	03/2012	3
VINDHYACHAL STTP STAGE-IV (NTPC) NTPC	5,915.00	5,915.00	10/2012	12/2012	03/2013	3
RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	12/2012	03/2013	3
MOUDA STTP (NTPC) NTPC	5,459.28	6,010.89	08/2012	11/2012	03/2013	4
765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA PGCIL	1,347.32	1,347.32	02/2012	02/2012	03/2013	13
SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	6,285.33	09/2010	08/2014	12/2015	16
<u>Road Transport & Highways</u>						
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	11/2011	12/2011	1
LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) NHAI	225.00	225.00	10/2008	11/2011	12/2011	1
JHANSI TO LALITPUR, NH-26 NHAI	276.09	276.09	09/2009	11/2011	12/2011	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	11/2011	12/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	11/2011	12/2011	1
SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	12/2011	03/2012	3
SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 NHAI	941.00	941.00	01/2011	12/2011	03/2012	3
RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA NHAI	229.91	229.91	10/2008	12/2011	09/2012	9
RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) NHAI	251.03	251.03	10/2008	12/2011	12/2012	12
<u>Telecommunications</u>						


VIII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	03/2012	07/2012	4
GSM equipment of 1867000Lines (2G) 383000 lines 3(BSNL	868.00	868.00	08/2009	03/2011	12/2011	9
GSM equipment of 1625000Lines (2G) 325000 lines 3(BSNL	916.70	916.70	11/2010	03/2011	12/2011	9
UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) BSNL	149.15	158.72	06/2009	02/2011	12/2011	10
Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	02/2011	12/2011	10
GSM equipment of 945000Lines (2G) 225000lines 3(G) BSNL	366.00	366.00	10/2008	02/2011	12/2011	10
GSM equipment of 1500000Lines (2G) 264700lines 3(G) BSNL	922.91	922.91	01/2010	02/2011	12/2011	10
GSM equipment of 1900000Lines (2G) 335500lines 3(G) BSNL	848.70	848.70	01/2010	02/2011	12/2011	10
GSM equipment of 614000Lines (2G) 150000lines 3(G) BSNL	315.19	315.19	01/2010	02/2011	12/2011	10
Number of projects reporting additional delay = 42						

Trend and Graphical Analysis of All Projects

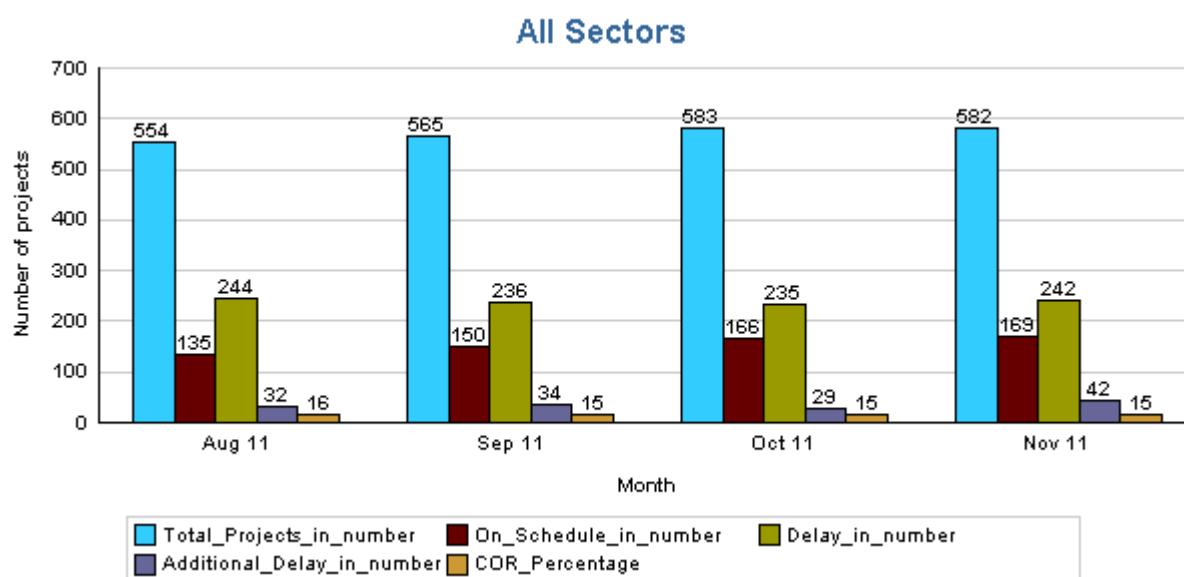


All Sectors Break-up of 242 Delayed projects in November 2011

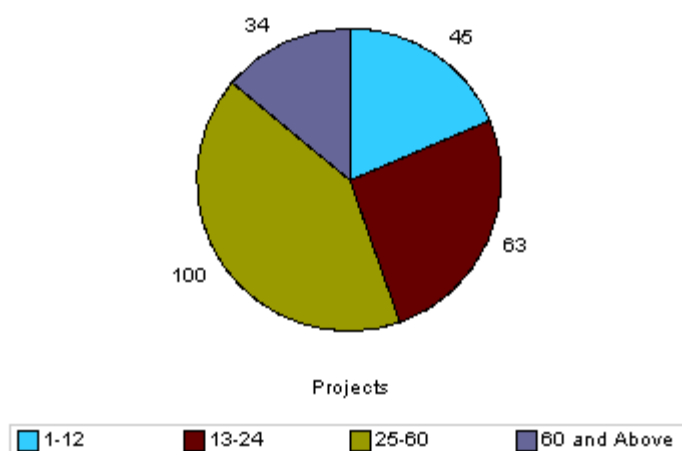


Trend and Graphical Analysis


Telecommunications Sector

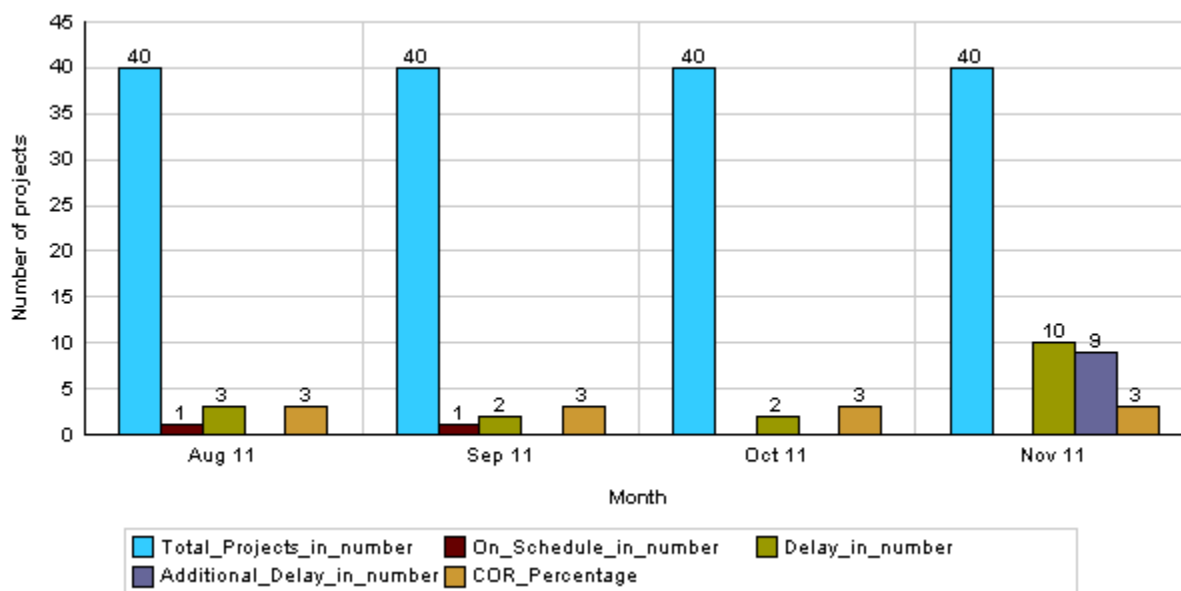


Telecommunications Sector Break-up of 10 Delayed projects in November 2011

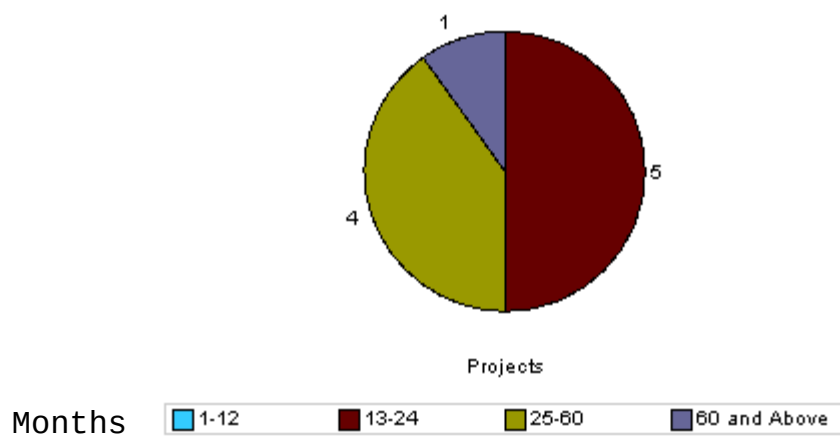


Trend and Graphical Analysis Shipping and Ports Sector

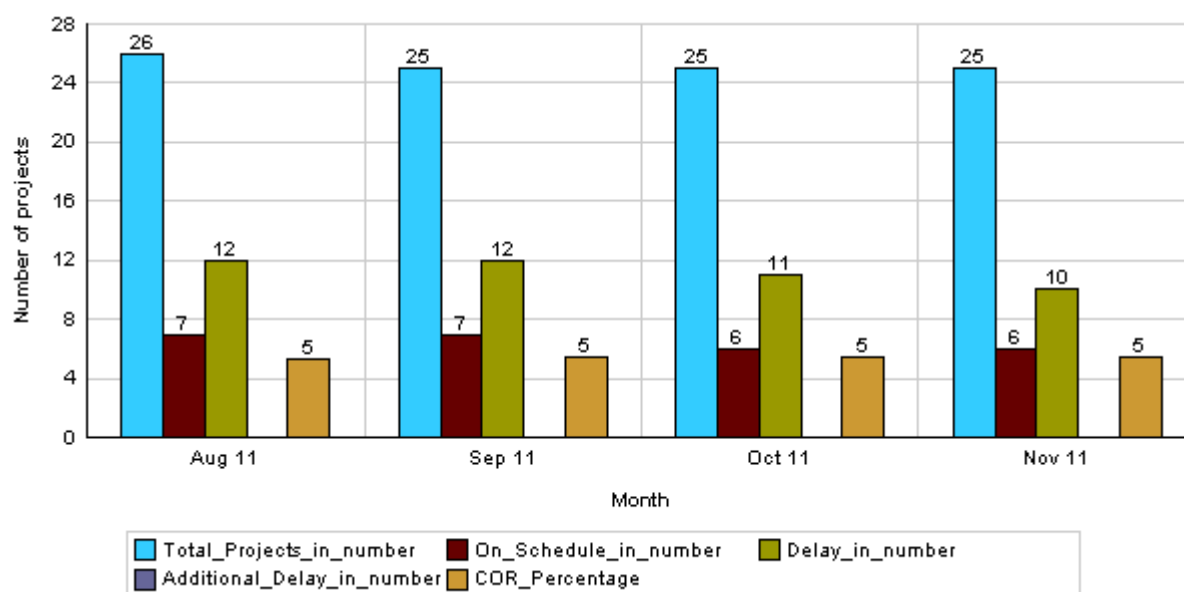


Sector Break-up of 10 Delayed projects in November 2011

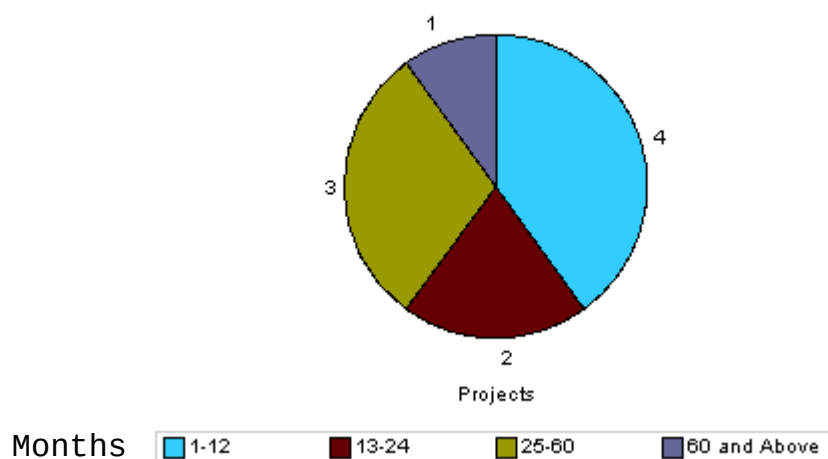

Trend and Graphical Analysis Road Transport and Highways Sector

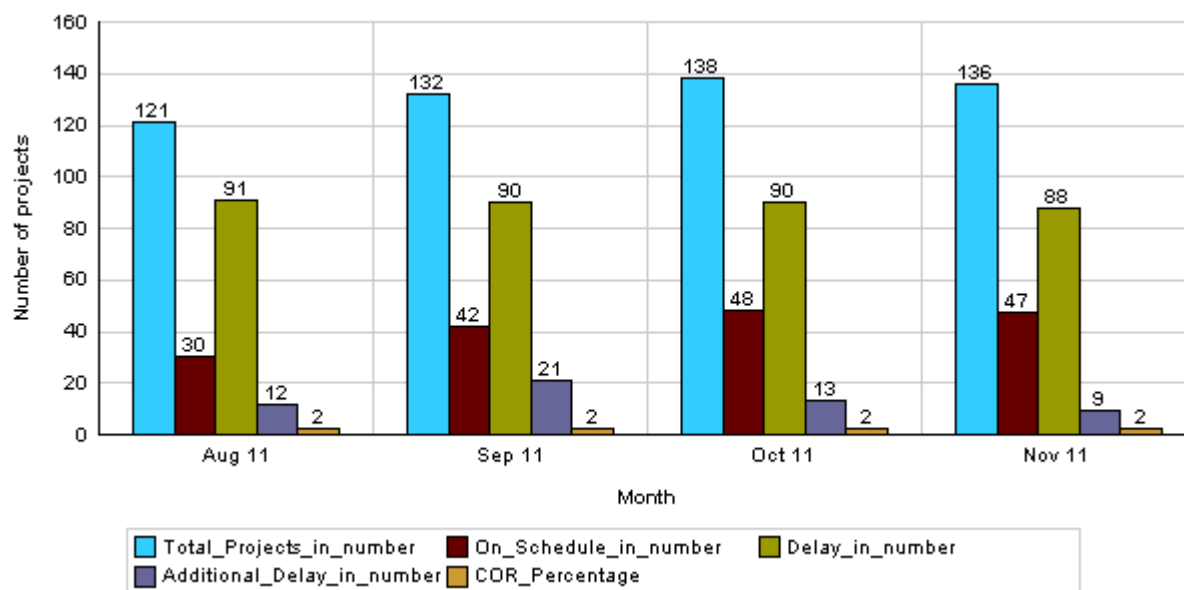


Sector Break-up of 88 Delayed projects in November 2011

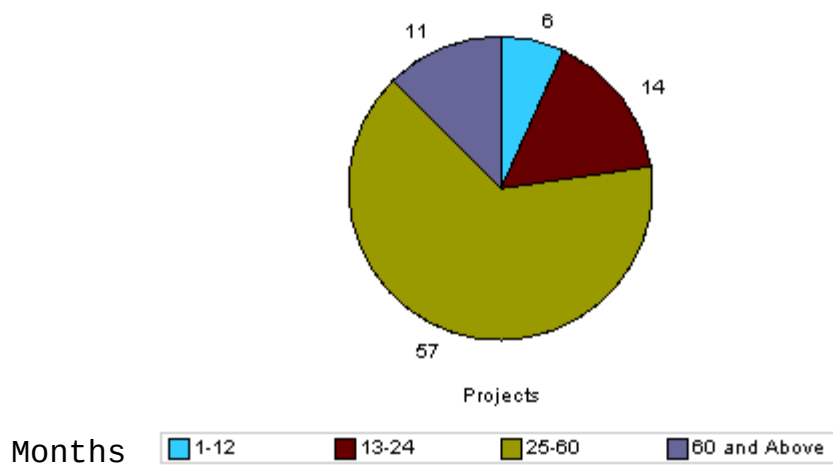


Trend and Graphical Analysis

Railways Sector

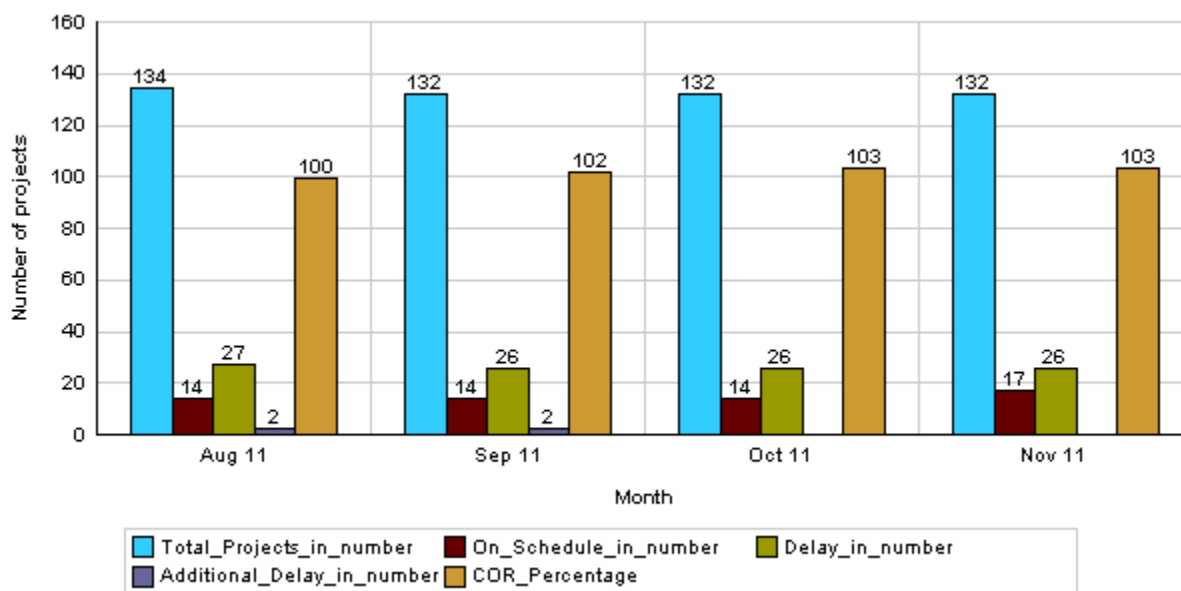


Railways Sector Sector Break-up of 26 Delayed projects in November 2011

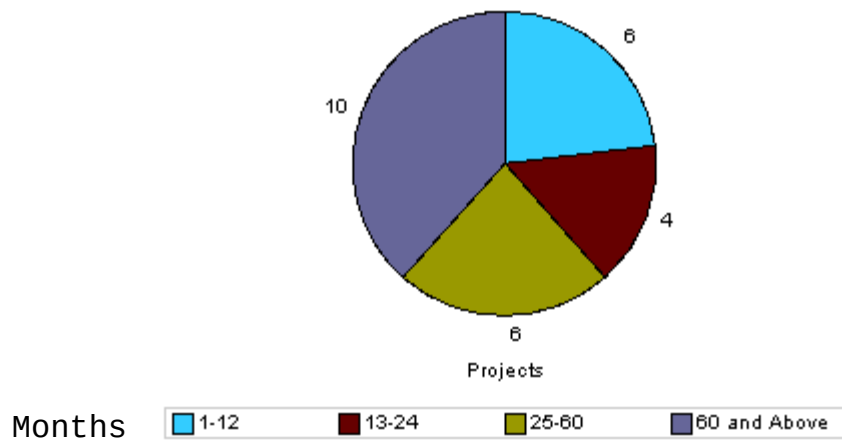


Trend and Graphical Analysis

Power Sector

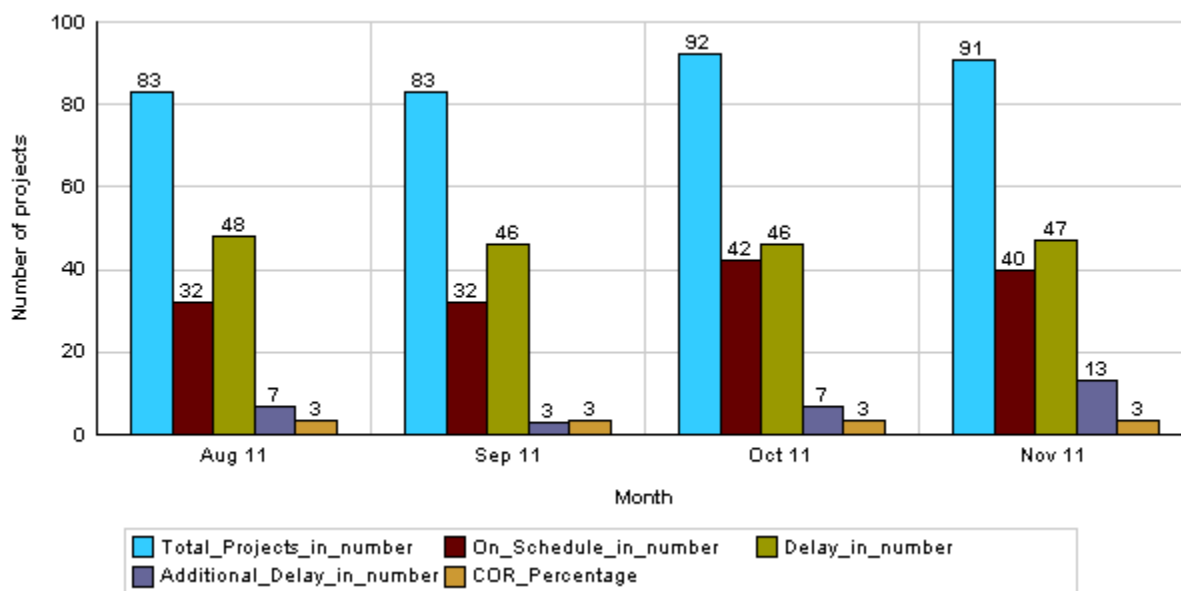


Power Sector Sector Break-up of 47 Delayed projects in November 2011

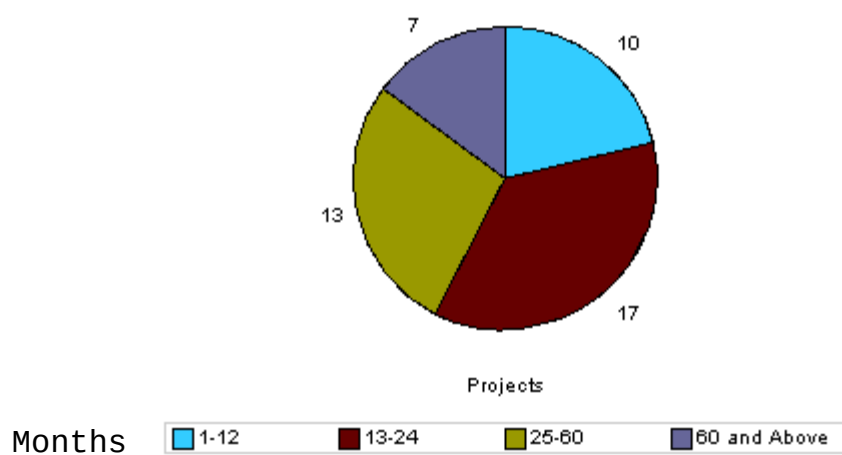


Trend and Graphical Analysis

Petroleum Sector

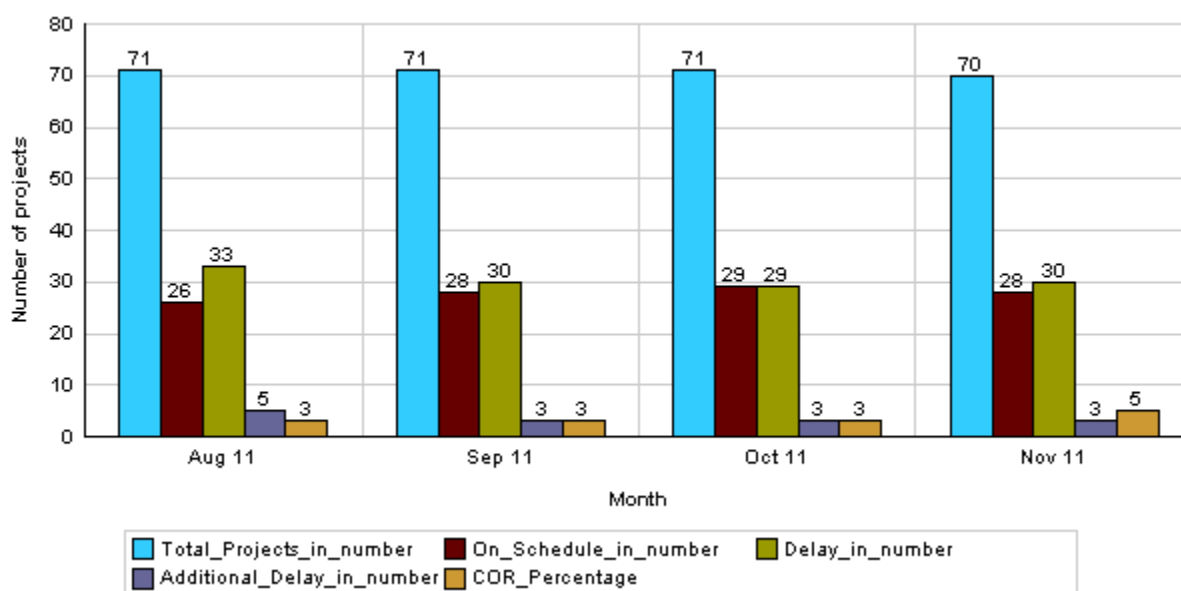


Petroleum Sector Sector Break-up of 30 Delayed projects in November 2011

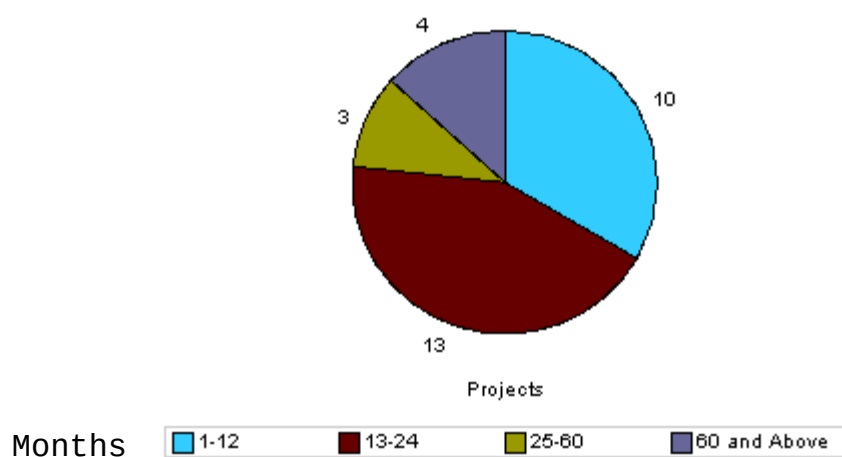


Trend and Graphical Analysis

Steel Sector

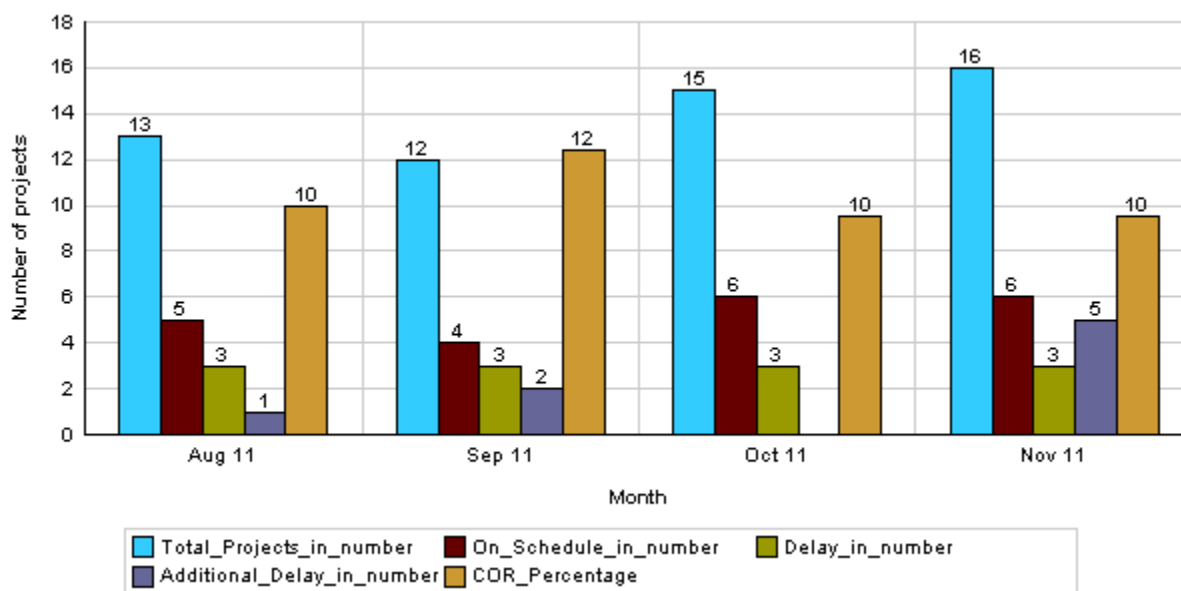


Steel Sector Break-up of 3 Delayed projects in November 2011

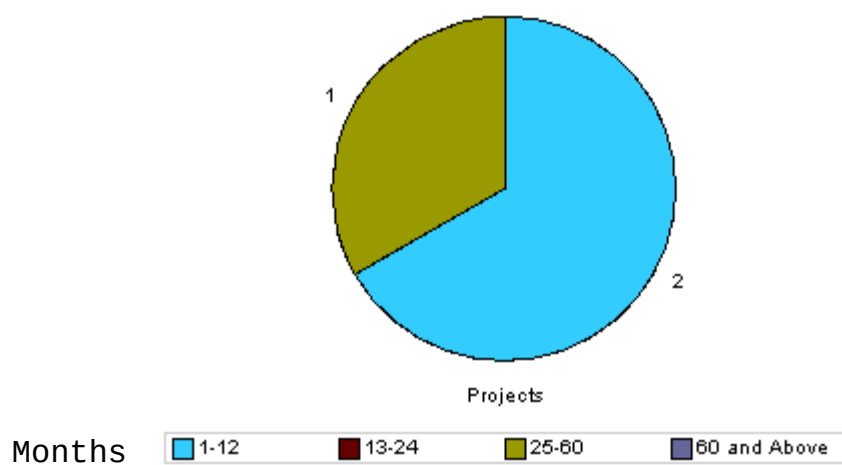


Trend and Graphical Analysis

Fertilisers Sector

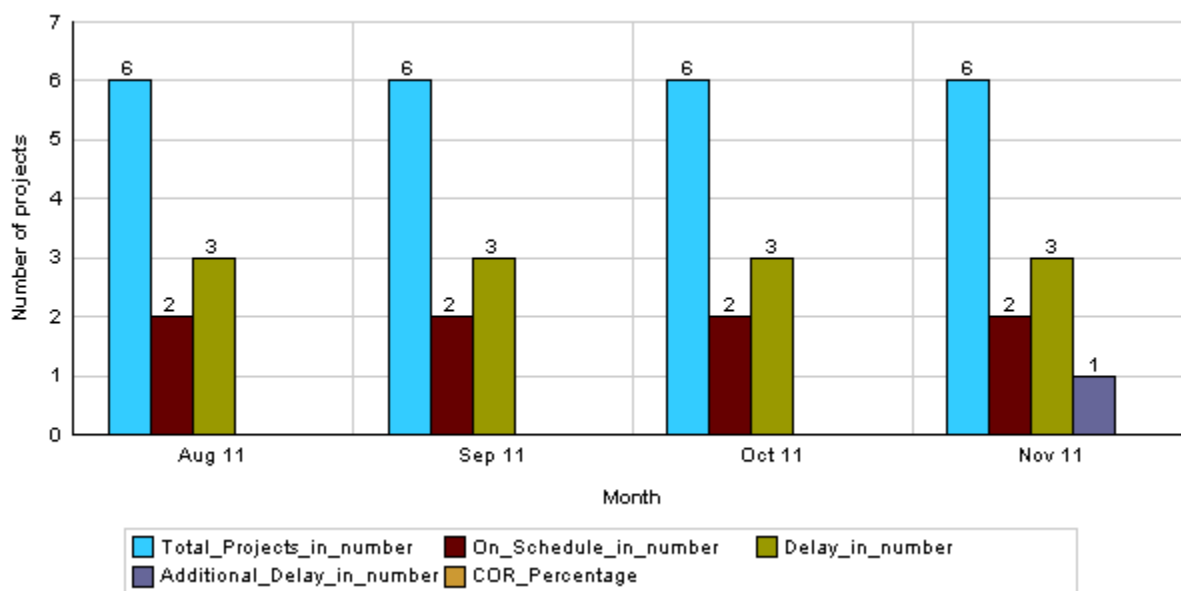


Fertilisers Sector Sector Break-up of 3 Delayed projects in November 2011

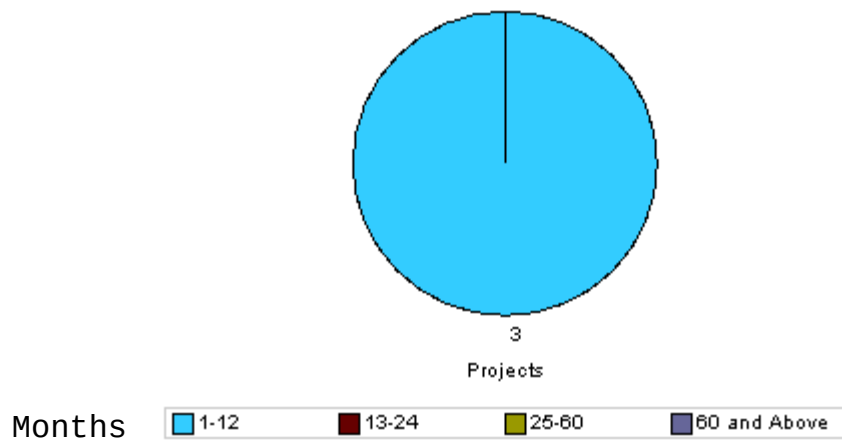


Trend and Graphical Analysis

Coal Sector

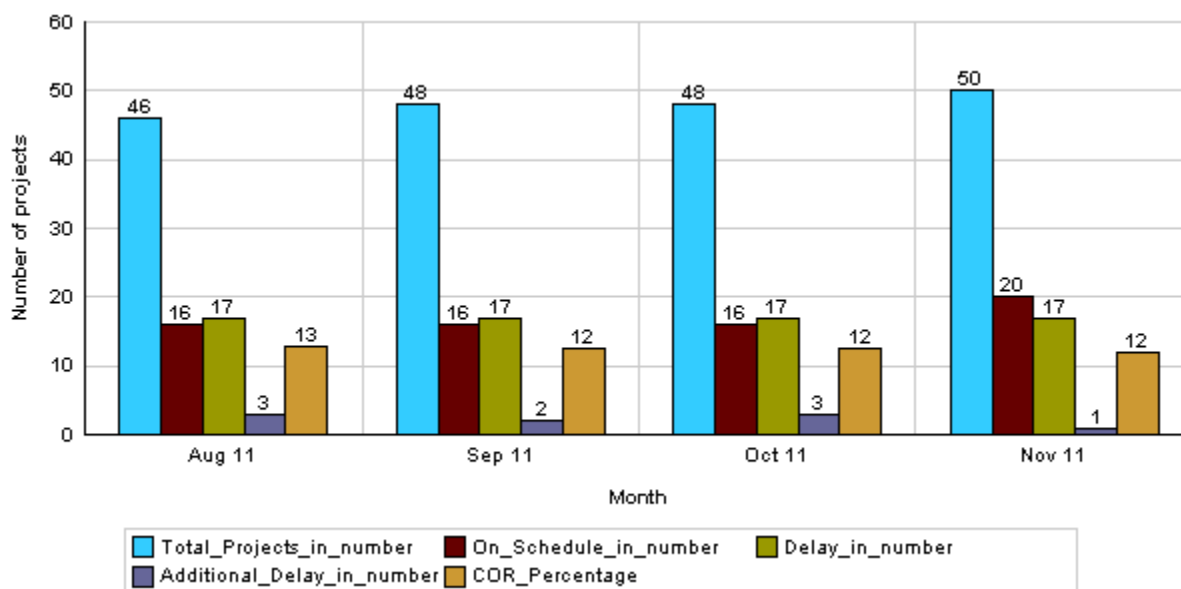


Coal Sector Sector Break-up of 17 Delayed projects in November 2011

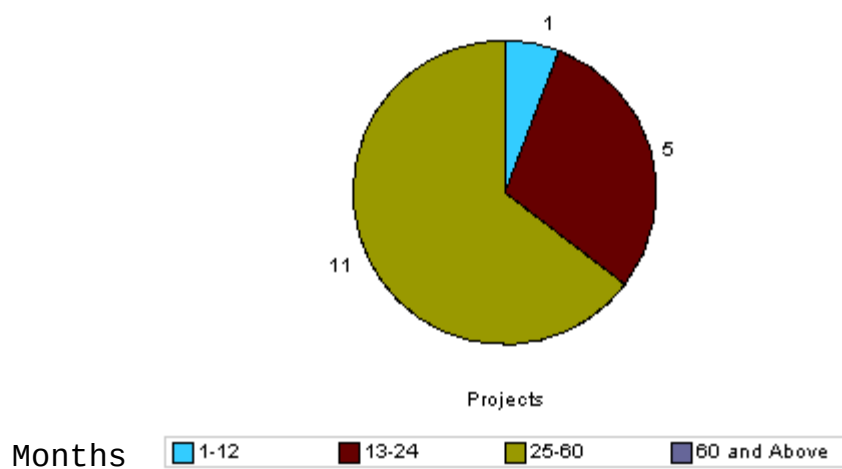


Trend and Graphical Analysis

Civil Aviation Sector

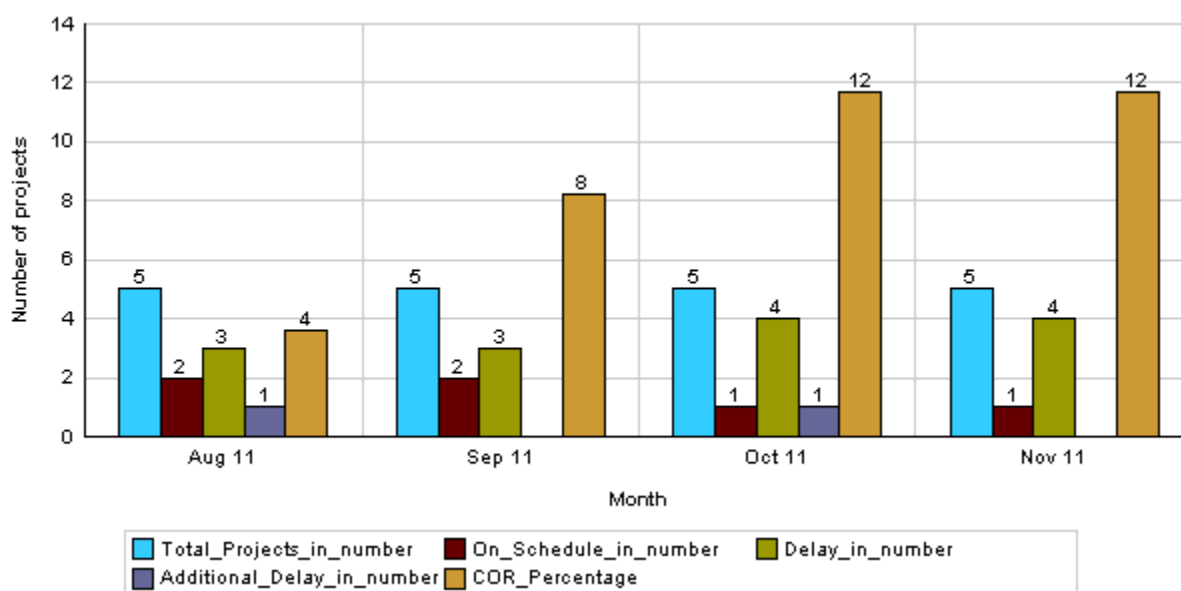


Civil Aviation Sector Break-up of 4 Delayed projects in November 2011

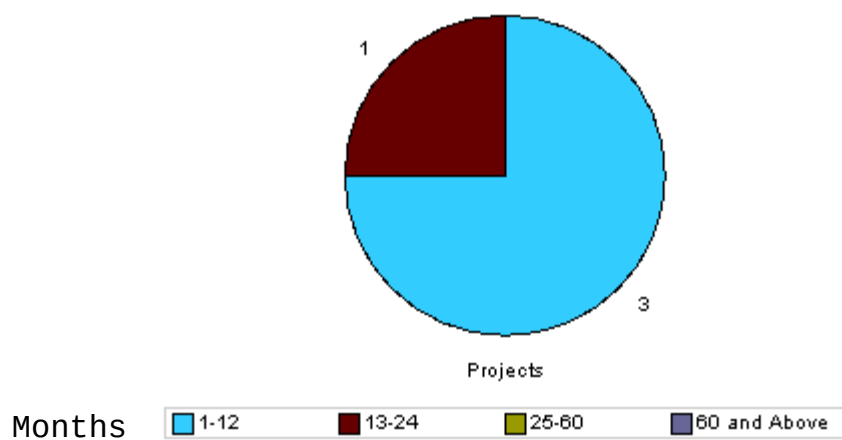

Trend and Graphical Analysis

Atomic Energy Sector

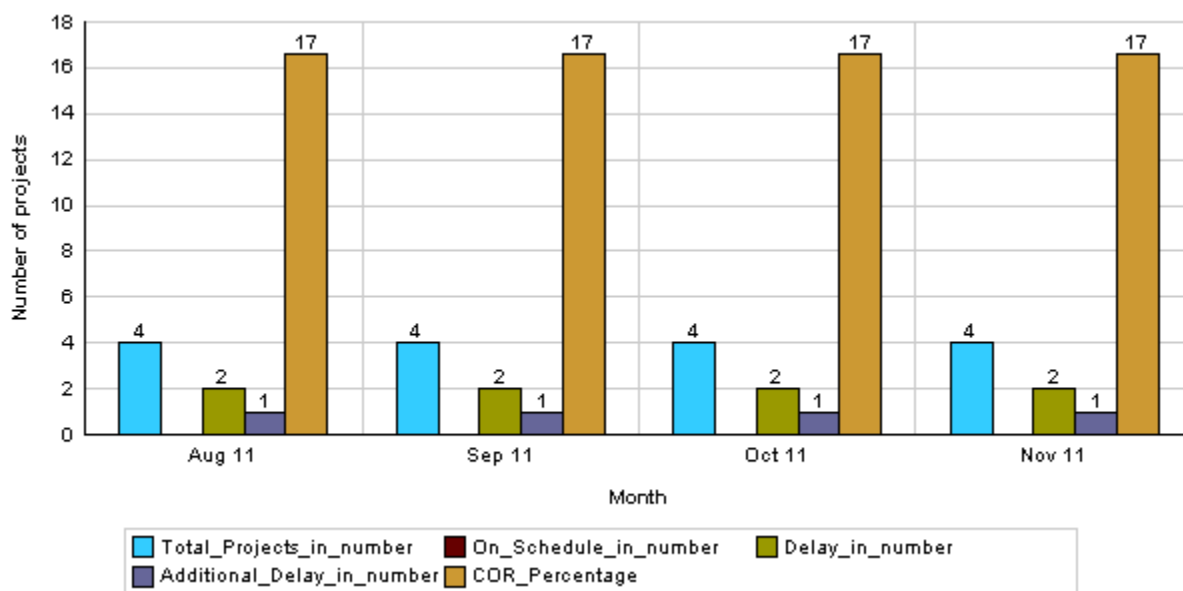

Atomic Energy Sector Sector Break-up of 2 Delayed projects in November 2011



Months



Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	29,228.29	29,228.29	34,066.29
Civil Aviation	5	5,021.58	5,228.58	5,611.07
Coal	50	28,811.62	30,528.57	32,198.65
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	16	65,244.82	71,120.10	71,412.36
Petrochemicals	1	5,460.61	8,920.00	8,920.00
Petroleum	70	154,794.07	167,529.73	162,721.78
Power	91	190,920.07	195,734.75	197,203.66
Railways	132	65,054.74	82,773.37	132,323.46
Road Transport & Highways	136	75,509.76	75,509.76	77,315.01
Shipping & Ports	25	18,052.23	18,431.54	19,035.72
Telecommunications	40	19,713.13	19,745.26	20,297.68
Urban Development	4	44,245.18	44,304.08	49,518.08
Water Resources	1	542.90	542.90	1,187.00
Grand total	582	712,007.92	759,316.10	821,529.93

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	3,333.91	09/2010	01/2012	16(O)	5/80
2	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	15,824.00	14,159.00	12/2008	02/2013	50(O)	60/119
4	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,180.00	12/2015 05/2016	11/2016	6(R1)	0/70
Total			29,228.29	34,066.29	19,673.61				65/270
<u>Civil Aviation</u>									
5	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,572.92	01/2011	12/2011	11(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	1,625.49	05/2011	03/2012	10(O)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	153.41	01/2011	06/2012	17(O)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	57.03	05/2012	08/2012	3(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	324.99	06/2013	06/2013	0(O)	0/0
Total			5,021.58	5,611.07	3,733.84				0/0
<u>Coal</u>									
10	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,683.04	06/2009	12/2011	30(O)	25/26
11	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96	302.96	87.24	03/2010	03/2012	24(O)	9/11
12	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	41.03	03/2012 03/2012	03/2012	0(R3)	11/42

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
13	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, Madhya Pradesh	10/2007	259.40 -	259.40	1.51	03/2012 -	03/2012	0(O)	0/1
14	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL, Orissa	12/2007	172.08 -	172.08	96.49	- -	03/2012	-	4/4
15	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL, Orissa	08/2008	207.28 -	207.28	68.11	- -	03/2012	-	5/7
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL, Andhra Pradesh	12/2009	418.97 -	418.97	78.59	03/2012 -	03/2012	0(O)	21/27
17	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL, Andhra Pradesh	03/2010	181.19 -	181.19	21.20	03/2012 03/2012	03/2012	0(R3)	8/34
18	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,304.10	06/2009 -	07/2012	37(O)	19/24
19	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC, Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,291.14	- -	02/2013	-	0/37
20	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL, Jharkhand	04/2006	471.66 341.63	341.63	110.02	03/2011 03/2012	03/2013	12(R3)	0/2
21	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, Madhya Pradesh	05/2006	789.88 -	741.62	288.78	03/2010 -	03/2013	36(O)	2/2
22	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL, Chhatisgarh	06/2006	737.65 -	1,188.31	569.86	- -	03/2013	-	0/8
23	JALLARAM SHAFT PROJECT - [N06000025]SCCL, Andhra Pradesh	03/2013	467.78 -	467.78	12.31	03/2013 03/2013	03/2013	0(R3)	3/83
24	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL, Orissa	12/2007	457.77 -	457.77	113.54	- -	03/2013	-	6/11
25	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, Orissa	11/2008	475.93 -	479.63	81.70	- -	03/2013	-	5/7
26	Purnadih OCP - [N06000085]CCL, Jharkhand	07/2008	210.98 -	210.98	24.25	03/2013 -	03/2013	0(O)	0/2
27	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL, Multi State	11/2006	168.97 -	168.97	37.71	03/2014 -	11/2013	-4(O)	1/2
28	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, Andhra Pradesh	09/2006	212.34 779.26	779.26	212.40	03/2013 09/2012	12/2013	15(R3)	5/22
29	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL, Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,279.57	03/2010 -	03/2014	48(O)	0/15
30	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL, Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,115.23	03/2010 -	03/2014	48(O)	0/13
31	CHURCHA RO UG (1.35MTY) - [N06000046]SECL, Chhatisgarh	06/2008	462.35 -	462.35	257.35	- -	03/2014	-	0/4
32	RAJMAHAL OC EXP. - [N06000056]ECL, Multi State	02/2006	50.08 153.82	153.82	19.76	03/2011 -	03/2014	36(O)	0/3
33	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL, Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
34	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL, Chhatisgarh	11/2009	321.42 -	321.50	203.26	- -	03/2014	-	0/5

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
35	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51	163.51	33.57	03/2011 03/2012	03/2014	24(R3)	1/2
36	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87	179.87	66.45	03/2012 03/2012	03/2014	24(R3)	0/2
37	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	76.05	03/2012 03/2013	03/2014	12(R3)	0/2
38	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	26.36	03/2014 -	03/2014	0(O)	0/0
39	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	339.88	-	04/2014 -	04/2014	0(O)	0/0
40	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77	339.77	0.65	- -	10/2014	-	0/1
41	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	140.21	03/2012 -	03/2015	36(O)	2/2
42	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011 -	03/2015	48(O)	1/5
43	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	58.80	- -	03/2015	-	2/12
44	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015 -	03/2015	0(O)	0/1
45	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	70.91	12/2012 -	03/2015	27(O)	7/44
46	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015 -	03/2015	0(O)	0/1
47	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015 -	03/2015	0(O)	1/1
48	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	19.26	03/2015 03/2015	03/2015	0(R3)	4/31
49	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015 -	03/2015	0(O)	0/28
50	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.16	03/2015 -	03/2015	0(O)	0/0
51	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015 03/2015	03/2015	0(R3)	0/0
52	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	1,230.27	-	04/2015 -	04/2015	0(O)	0/0
53	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	224.99	03/2014 -	03/2016	24(O)	2/2
54	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.21	07/2012 03/2014	03/2016	24(R3)	1/2
55	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.21	- -	03/2016	-	1/12
56	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	90.98	03/2016 -	03/2016	0(O)	0/1
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.44	03/2016 -	03/2016	0(O)	1/2
58	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	99.74	- -	03/2017	-	6/12

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NFL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 -	03/2018	0(O)	0/0
	Total		28,811.62	32,198.65	12,249.18				153/556
	<u>Fertilisers</u>								
60	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	84.31	07/2011 -	11/2011	4(O)	0/0
61	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	105.79	07/2011 -	03/2012	8(O)	0/0
62	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75 -	488.75	199.56	- 04/2012	04/2012	0(R3)	6/22
63	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84 -	1,292.84	234.32	01/2013 -	01/2013	0(O)	0/5
64	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19 -	1,294.19	233.52	01/2013 -	01/2013	0(O)	0/5
65	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	298.10	12/2012 -	01/2013	1(O)	8/8
	Total		5,317.41 -	5,317.41	1,155.60				14/40
	<u>Mines</u>								
66	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51 4,401.76	4,401.76	4,183.00	12/2008 01/2011	06/2011	5(R3)	98/110
	Total		4,091.51 -	4,401.76	4,183.00				98/110
	<u>Steel</u>								
67	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 232.93	232.93	173.27	05/2011 -	10/2011	5(O)	1/1
68	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhandd	01/2008	6,325.00 6,325.00	6,325.00	2,255.21	12/2011 12/2011	12/2011	0(R3)	10/11
69	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90 -	500.90	339.13	- -	01/2012	-	3/3
70	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	311.86	- 12/2011	03/2012	3(R3)	15/21
71	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	12,055.92	12/2011 -	03/2012	3(O)	13/14
72	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	223.14	- 08/2010	03/2012	19(R3)	1/2

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
73	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00	343.58	235.57	- 02/2011	04/2012	14(R3)	2/3
74	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	8,979.54	10/2009 10/2012	10/2012	0(R3)	56/59
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00	216.68	53.66	- 10/2012	10/2012	0(R3)	3/4
76	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00	460.00	155.33	- 05/2012	12/2012	7(R3)	1/2
77	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, Chhatisgarh	06/2009	2,875.00	2,875.00	341.72	12/2012	12/2012	0(O)	3/6
78	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, Chhatisgarh	09/2008	11,812.00 11,812.00	11,812.00	5,758.78	03/2013	03/2013	0(O)	2/8
79	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC, Karnataka	04/2011	572.00	572.00	-	04/2013	04/2013	0(O)	0/0
80	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC, Karnataka	02/2011	898.55	898.55	-	05/2013	05/2013	0(O)	0/0
81	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00	17,265.00	3,998.29	03/2013	06/2013	3(O)	14/20
82	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55	254.55	-	11/2013	11/2013	0(O)	0/0
Total			65,244.82	71,412.36	34,881.42				124/154
<u>Petrochemicals</u>									
83	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	3,145.56	- 12/2013	-	-	0/30
Total			5,460.61	8,920.00	3,145.56				0/30
<u>Petroleum</u>									
84	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	755.76	530.44	03/2011 05/2011	06/2011	1(R3)	0/0
85	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54	727.88	671.52	12/2010	06/2011	6(O)	0/0
86	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009	08/2011	23(O)	0/0
87	CONSTRUCTION OF NEW TERMINAL AT ENnore CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	299.00	263.64	02/2011 08/2011	08/2011	0(R3)	0/0
88	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00	3,284.00	-	09/2011	09/2011	0(O)	0/0
89	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40	304.40	258.31	06/2010	09/2011	15(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
91	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	659.96	04/2011 12/2011	12/2011	0(R3)	2/2
92	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	655.76	04/2010 -	12/2011	20(O)	0/0
93	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	267.17	04/2011 -	12/2011	8(O)	0/0
94	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,735.01	- -	12/2011	-	0/116
95	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,307.92	01/2012 -	01/2012	0(O)	0/0
96	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	71.64	03/2009 02/2012	02/2012	0(R3)	0/0
97	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	03/2012	39(R3)	0/0
98	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
99	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	0(R3)	0/0
100	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 -	1,385.00	1,009.93	10/2010 12/2011	03/2012	3(R3)	0/1
101	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	759.98	09/2011 03/2012	03/2012	0(R3)	0/0
102	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	03/2012	0(R3)	0/0
103	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	204.00	144.60	01/2012 -	03/2012	2(O)	3/8
104	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,	06/2009	3,032.00 -	261.00	174.49	- 08/2012	03/2012	-5(R3)	1/4
105	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	1.63	01/2013 -	03/2012	-10(O)	0/0
106	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	171.96	06/2011 03/2012	03/2012	0(R3)	9/9
107	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
108	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
109	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,968.18	05/2010 05/2012	05/2012	0(R3)	0/0
110	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	74.11	05/2010 04/2012	05/2012	1(R3)	0/0
111	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	240.88	07/2010 05/2012	05/2012	0(R3)	0/0
112	CDU/VDU-II - [N16000110]CPCL, Tamil Nadu	03/2010	333.99 -	333.99	76.90	05/2012 -	05/2012	0(O)	21/36
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,907.34	08/2010 03/2012	06/2012	3(R3)	0/0
114	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	567.62	06/2012 -	06/2012	0(O)	0/0
115	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL, Orissa	12/2009	1,492.33 -	1,492.33	729.44	06/2012 -	06/2012	0(O)	6/9
116	Wind Power Project - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
117	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	97.48	04/2011 -	07/2012	15(O)	0/0
118	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	460.70	166.10	06/2011 07/2012	07/2012	0(R2)	9/9
119	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	491.22	07/2012 -	07/2012	0(O)	0/0
120	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,401.09	03/2012 08/2012	08/2012	0(R3)	0/3
121	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	131.65	08/2012 -	08/2012	0(O)	0/0
122	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	2,467.12	09/2012 -	09/2012	0(O)	0/0
123	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]IOCL, Multi State	08/2009	1,793.00 -	1,793.00	492.71	09/2012 -	09/2012	0(O)	0/15
124	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL, Gujarat	02/2009	267.00 -	267.00	184.31	09/2012 -	09/2012	0(O)	0/0
125	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	302.26	23.44	09/2012 -	09/2012	0(O)	0/0
126	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.71	09/2011 -	12/2012	15(O)	0/0
127	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	2,915.00	206.91	10/2012 12/2012	12/2012	0(R3)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
128	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35	977.00	91.09	12/2011	01/2013	13(O)	0/0
129	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00	1,000.00	36.99	01/2013	01/2013	0(O)	13/18
130	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44	410.44	-	11/2012	01/2013	2(O)	0/0
131	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50	341.50	30.78	02/2013	02/2013	0(O)	19/42
132	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90	438.85	258.24	03/2006 03/2013	03/2013	0(R3)	6/6
133	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03	8,813.41	6,772.36	05/2010 03/2013	03/2013	0(R3)	0/0
134	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00	250.00	214.27	03/2013	03/2013	0(R1)	0/0
135	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15	2,378.86	398.22	03/2013	03/2013	0(O)	0/0
136	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64	723.64	-	03/2013	03/2013	0(O)	0/0
137	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03	3,241.03	1.50	03/2013	03/2013	0(O)	0/0
138	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11	372.11	-	03/2013	03/2013	0(O)	0/0
139	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	04/2008	825.00	1,827.00	315.69	12/2011 04/2013	04/2013	0(R3)	202/203
140	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79	861.79	-	05/2013	05/2013	0(O)	0/0
141	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	11,345.73	11/2012	06/2013	7(O)	0/100
142	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20	331.20	-	08/2013	08/2013	0(O)	0/0
143	Wax Project - [N16000101]NRL,Assam	06/2010	576.60	576.60	17.35	12/2013 12/2013	12/2013	0(R3)	0/0
144	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00	2,523.00	-	01/2014	01/2014	0(O)	0/0
145	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94	202.94	-	01/2014	01/2014	0(O)	0/0
146	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	300.76	02/2014	02/2014	0(O)	0/0
147	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10	663.69	595.79	03/2007 03/2014	03/2014	0(R3)	3/3

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10	1,916.10	-	12/2014	12/2014	0(O)	0/0
149	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	2,189.63	-	12/2014	12/2014	0(O)	0/0
150	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	-	04/2015	04/2015	0(O)	0/0
151	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09	1,674.11	1,413.90	03/2007	03/2017	0(R3)	6/6
152	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	3.29	10/2010	-	-	0/0
153	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	1,584.00	6.38	-	-	-	0/0
Total			154,794.07	162,721.78	59,979.23				300/590
Power									
154	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25	238.25	218.42	05/2011	12/2011	7(R3)	0/0
155	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52	227.52	137.60	06/2010	12/2011	18(O)	0/0
156	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63	1,405.63	1,702.21	08/2010	02/2012	18(O)	0/0
157	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,000.40	07/2010	02/2012	19(O)	20/20
158	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	313.20	02/2012	02/2012	0(O)	0/0
159	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	62.00	02/2012	02/2012	0(O)	0/0
160	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	165.60	08/2011	02/2012	6(O)	0/0
161	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	213.60	07/2010	02/2012	0(R3)	0/0
162	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	88.50	07/2011	02/2012	7(O)	0/0
163	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56	2,283.69	2,533.29	04/2005	03/2012	83(O)	7/11
164	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,485.00	12/2009	03/2012	27(O)	50/60
165	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,779.46	3,510.70	09/2009	03/2012	30(O)	11/30

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
166	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.66	710.80	10/2009 -	03/2012	29(O)	20/20
167	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28 -	621.28	707.14	02/2011 -	03/2012	13(O)	1/1
168	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,192.00	- -	03/2012	-	1/6
169	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	305.73	07/2011 -	03/2012	8(O)	0/0
170	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	215.86	129.00	06/2012 -	03/2012	-3(O)	0/0
171	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	1,724.79	1,603.83	11/2009 -	04/2012	29(O)	0/0
172	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	108.60	04/2012 -	04/2012	0(O)	0/0
173	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	768.92	1,399.53	03/2007 -	05/2012	62(O)	25/25
174	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	374.90	05/2012 -	05/2012	0(O)	0/0
175	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52 -	2,304.52	1,604.48	10/2010 -	06/2012	20(O)	0/0
176	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	512.20	01/2010 -	06/2012	29(O)	0/22
177	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	64.50	11/2011 -	06/2012	7(O)	0/0
178	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	517.90	06/2012 -	06/2012	0(O)	0/0
179	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	13.78	06/2012 -	06/2012	0(O)	0/0
180	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,738.00	08/2012 -	08/2012	0(O)	0/0
181	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	4,300.80	08/2012 -	08/2012	0(O)	0/0
182	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	473.50	08/2012 -	08/2012	0(O)	0/0
183	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	2,229.20	10/2012 -	10/2012	0(O)	0/0
184	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	469.38	196.20	10/2012 -	10/2012	0(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
185	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32	160.32	14.50	10/2012	10/2012	0(O)	0/0
186	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	692.51	08/2010	11/2012	27(O)	0/0
187	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	428.70	11/2012	11/2012	0(O)	0/0
188	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58	965.58	280.10	11/2012	11/2012	0(O)	0/0
189	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80	1,272.80	12.00	11/2012	11/2012	0(O)	0/0
190	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	1,045.69	09/2009	12/2012	39(O)	0/0
191	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,779.29	1,751.18	11/2008	12/2012	49(O)	20/38
192	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	684.00	11/2011	12/2012	13(O)	6/34
193	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88	7,031.88	2,758.30	12/2012	12/2012	0(O)	0/0
194	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	239.90	11/2011	12/2012	13(O)	0/0
195	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	304.00	11/2011	12/2012	13(O)	0/0
196	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	149.50	02/2012	12/2012	10(O)	0/0
197	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	452.60	12/2012	12/2012	0(O)	0/0
198	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68	182.68	26.80	01/2013	01/2013	0(O)	0/0
199	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	22.90	01/2013	01/2013	0(O)	0/0
200	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,921.00	04/2009	03/2013	47(O)	0/9
201	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	382.80	09/2010	03/2013	30(O)	0/0
202	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	3,090.00	08/2012	03/2013	7(O)	4/16

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
203	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	922.20	02/2012	03/2013	13(O)	0/0
204	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00	5,915.00	2,429.00	10/2012	03/2013	5(O)	2/15
205	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	2,247.00	10/2012	03/2013	5(O)	3/16
206	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	211.30	03/2013	03/2013	0(O)	0/0
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57	1,677.57	136.00	04/2013	04/2013	0(O)	0/0
208	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36	170.36	11.00	04/2013	04/2013	0(O)	0/0
209	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01	623.44	79.38	01/2012 07/2013	07/2013	0(R3)	0/0
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	86.60	07/2013	07/2013	0(O)	0/0
211	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
212	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya Pradesh	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
213	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99	573.99	247.01	08/2012 08/2013	08/2013	0(R3)	8/18
214	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	129.10	08/2013	08/2013	0(O)	0/0
215	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	20.60	08/2013	08/2013	0(O)	0/0
216	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	148.10	08/2013	08/2013	0(O)	0/0
217	RAMPUR HEP(412 MW) - [N18000024]SJVN,L,Himachal Pr.	01/2007	2,047.03	2,047.03	1,399.75	01/2012	09/2013	20(O)	2/10
218	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	134.30	11/2011	09/2013	22(O)	0/0
219	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35	4,375.35	2,534.00	06/2011	10/2013	28(O)	0/29
220	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04	7,341.04	3,094.00	-	10/2013	-	4/18

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
221	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51 -	425.51	-	10/2013 -	10/2013	0(O)	0/0
222	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State	03/2011	1,585.12 -	1,585.12	86.10	11/2013 -	11/2013	0(O)	0/0
223	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26 -	558.26	-	11/2013 -	11/2013	0(O)	0/0
224	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL, Multi State	08/2011	1,391.97 -	1,391.97	-	12/2013 -	11/2013	-1(O)	0/0
225	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19 -	2,743.19	191.40	12/2013 -	12/2013	0(O)	0/0
226	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34 -	1,366.34	-	12/2013 -	12/2013	0(O)	0/0
227	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL, Chhatisgarh	08/2011	1,391.97 -	1,391.97	-	12/2013 -	12/2013	0(O)	0/0
228	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72 913.63	913.63	286.86	07/2006 01/2014	01/2014	0(R3)	5/5
229	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25 -	2,569.25	52.50	03/2014 -	03/2014	0(O)	0/0
230	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL, Chhatisgarh	05/2011	1,961.87 -	1,961.87	31.00	05/2014 -	05/2014	0(O)	0/0
231	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal	11/2006	2,978.48 -	2,978.48	1,206.00	03/2013 -	06/2014	15(O)	1/13
232	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, Multi State	10/2011	487.49 -	487.49	-	06/2014 -	06/2014	0(O)	0/0
233	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL, Andhra Pradesh	08/2011	1,637.34 -	1,637.34	-	08/2014 -	08/2014	0(O)	0/0
234	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	3,161.00	08/2013 -	09/2014	13(O)	0/0
235	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL, Tamil Nadu	09/2011	1,940.13 -	1,940.13	-	09/2014 -	09/2014	0(O)	0/0
236	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97 -	8,693.00	6,287.00	12/2009 -	10/2014	58(O)	45/70
237	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,383.56	09/2009 -	12/2014	63(O)	1/20

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
239	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33	6,285.33	5,216.33	09/2010	12/2015	63(O)	11/11
240	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67	3,642.04	1,034.24	07/2014	01/2016	0(R3)	0/0
241	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90	2,496.90	1,654.09	05/2013	06/2016	0(R3)	2/22
242	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttaranchal	08/2008	2,491.58	3,422.44	208.64	07/2014	07/2016	24(O)	4/7
243	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45	1,007.16	812.90	12/2007	03/2013	39(R3)	0/18
244	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL, Uttar Pradesh	07/2006	1,657.00	2,978.86	277.93	07/2010	02/2016	0(R3)	0/10
Total			190,920.07	197,203.66	94,587.98				253/574
Railways									
245	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	234.56	-	12/2010	22(R1)	0/0
246	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41	211.90	189.01	-	12/2010	21(R1)	0/0
247	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	221.90	163.57	12/2007	12/2010	9(R1)	0/0
248	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73	399.50	-	03/2009	12/2010	24(R1)	0/0
249	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL, Gujarat	09/2005	200.80	200.80	269.02	-	12/2010	-	0/0
250	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	273.00	301.50	-	03/2011	24(R1)	0/0
251	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	329.70	-	03/2009	03/2011	15(R1)	0/0
252	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP, Maharashtra	04/2003	3,125.20	4,501.80	4,207.75	-	06/2011	6(R3)	1/1
253	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50	252.50	-	02/2010	11/2011	21(O)	0/0
254	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77	540.96	558.07	03/1994	12/2011	213(O)	0/0
255	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00	207.66	189.00	03/2002	12/2011	117(O)	0/0
256	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74	840.32	492.50	02/2009	12/2011	34(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	179.50	- -	12/2011	-	0/0
258	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	198.92	- 09/2009	12/2011	27(R1)	0/0
259	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	254.35	03/2013 -	12/2011	-15(O)	0/0
260	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,197.67	- -	02/2012	-	0/0
261	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	431.31	- 12/2009	02/2012	26(R1)	0/0
262	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	67.74	12/2011 -	02/2012	2(O)	0/0
263	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	544.29	03/1995 -	03/2012	204(O)	0/0
264	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	524.97	- -	03/2012	-	0/0
265	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	471.19	- 12/2011	03/2012	3(R3)	0/0
266	KADUR-CHIKMAGALUR-SAKLESHIPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	210.75	- 03/2012	03/2012	0(R3)	0/0
267	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	422.82	- -	03/2012	-	0/0
268	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	569.83	- -	03/2012	-	0/0
269	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	342.61	- 03/2011	03/2012	12(R3)	0/0
270	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
271	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0
272	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	188.17	03/2010 -	03/2012	24(O)	0/0
273	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	210.59	- -	03/2012	-	0/0
274	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	139.66	03/2012 -	03/2012	0(O)	0/0
275	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	223.95	03/2011 -	03/2012	12(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
276	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97	723.27	383.13	06/2005 07/2011	03/2012	8(R3)	0/0
277	Tinpahar - Sahibganj (ER) - [N22000115]ER, Jharkhand	04/2008	167.73	167.73	38.09	03/2012	03/2012	0(O)	0/0
278	Bhuj-Naliya (GC) with extension from naliya to vador - [N22000123]WR, Gujarat	04/2008	318.24	468.62	2.29	03/2012	03/2012	0(O)	0/0
279	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, West Bengal	04/1974	31.42 154.30	499.16	146.26	03/2007 03/2007	06/2012	63(R1)	0/0
280	NANGALDAM-TALWARA (NL), NR - [220100188](NR), Multi State	03/1981	37.68 450.00	730.00	327.68	- 07/2012	07/2012	0(R3)	0/0
281	DALLI-RAJHARA - RAOGHAT (PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00	968.60	87.13	12/2012	12/2012	0(O)	0/0
282	CONV. OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	273.67 1,160.52	1,302.12	590.40	- -	12/2012	-	0/0
283	CHANDIGARH-LUDHIANA (NEW BG LINE), NR - [220100241](NR), Punjab	07/1998	248.44 576.27	1,104.40	799.58	12/2012	12/2012	0(O)	0/0
284	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90	1,211.22	396.24	03/2005 12/2008	12/2012	48(R1)	0/0
285	JIND-SONEPAT (NL), NR - [220100280](NR), Haryana	01/2004	190.81 238.56	401.83	354.41	- 03/2012	12/2012	9(R3)	0/0
286	KOSI BRIDGE (NL), ECR - [220100304]ECR, Bihar	04/2002	323.41	341.41	242.37	- -	12/2012	-	0/0
287	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR, Bihar	04/2002	921.00	981.00	556.40	03/2009	12/2012	45(O)	0/0
288	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47	1,389.98	1,137.14	10/2007	12/2012	62(O)	0/0
289	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL, Madhya Pradesh	09/2007	687.20	687.20	427.67	03/2010	12/2012	33(O)	0/0
290	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER, West Bengal	04/1999	207.52	207.52	106.28	12/2012	12/2012	0(O)	0/0
291	DAUSA-GANGAPUR CITY (NL), NWR - [220100184]NWR, Rajasthan	02/1997	151.84 410.08	410.08	155.97	- -	03/2013	-	0/0
292	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR (SR) (GC) - [220100263]SR, Multi State	03/1998	280.00	1,029.00	705.93	- -	03/2013	-	0/0
293	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR, Madhya Pradesh	04/2008	603.04	603.04	48.10	03/2012	03/2013	12(O)	0/0
294	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR, Gujarat	04/2008	394.13	394.14	0.49	03/2013	03/2013	0(O)	0/0
295	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRT, Tamil Nadu	04/2006	495.74 495.74	495.74	138.24	- 06/2013	06/2013	0(R3)	0/0
296	Ghatisarif-Canning (ER) - [N22000117]ER, West Bengal	04/2009	189.97	189.97	71.51	12/2011	11/2013	23(O)	0/0
297	CHHINDWARA - NAGPUR (GC) (SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79	585.93	180.24	- -	12/2013	-	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
298	Katakhal to Bhairabi - [N22000126]NEFR, Assam	04/1998	227.90	223.01	83.63	12/2012	12/2013	12(O)	0/0
299	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR, Assam	04/1996	1,676.31	4,091.33	2,859.96	03/2009	12/2013	57(O)	0/0
300	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00	1,655.80	904.98	12/2008	03/2014	63(O)	0/0
301	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70	1,717.29	819.96	-	03/2014	-	0/0
302	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR, Tripura	04/2008	813.34	1,141.75	223.61	03/2014	03/2014	0(O)	0/0
303	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34	2,393.49	3.61	04/2014	03/2014	-1(O)	0/0
304	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR, Rajasthan	04/2008	653.19	653.19	30.98	03/2014	03/2014	0(O)	0/0
305	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR, Rajasthan	04/2008	516.23	516.23	96.46	03/2014	03/2014	0(O)	0/0
306	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR, Gujarat	04/2008	1,389.62	1,389.62	200.08	03/2014	03/2014	0(O)	0/0
307	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00	369.90	109.77	03/2010 06/2014	06/2014	0(R3)	0/0
308	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	3,230.01	2,259.20	04/2008 03/2014	12/2014	9(R3)	0/0
309	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23	638.00	29.10	02/2015	02/2015	0(O)	0/0
310	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66	324.66	168.18	-	03/2015	-	0/0
311	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP, Maharashtra	04/2008	5,300.00	5,300.00	323.57	03/2014	03/2015	12(O)	0/0
312	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR, Rajasthan	04/2008	829.74	829.74	-	03/2015	03/2015	0(O)	0/0
313	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00	850.00	8.44	03/2015	03/2015	0(O)	0/0
314	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48	3,380.57	52.63	12/2015	12/2015	0(O)	0/0
315	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	3,056.85	507.55	03/2011 03/2014	03/2016	24(R3)	0/0
316	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60	2,069.60	-	03/2014	03/2016	24(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98	3,951.98	-	03/2016	03/2016	0(O)	0/0
318	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02	2,619.02	-	03/2016	03/2016	0(O)	0/0
319	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72	2,397.72	17.12	03/2016	06/2016	3(O)	0/0
320	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00	20,000.00	7,333.52	03/2001	12/2017	201(O)	0/0
321	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66	356.87	147.40	-	-	-	0/0
322	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	04/1983	36.80	415.23	234.78	03/2010	-	-	0/0
323	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00	579.37	595.35	-	-	-	0/0
324	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08	1,010.00	105.35	-	-	-	0/0
325	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00	944.55	479.98	-	-	-	0/0
326	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30	1,038.00	570.21	03/1998	-	-	0/0
327	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55	945.73	636.64	-	-	-	0/0
328	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1995	227.00	997.58	67.82	-	-	-	0/0
329	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, Multi State	04/1997	218.24	537.47	95.13	-	-	-	0/0
330	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00	458.26	0.35	07/2008	-	-	0/0
331	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19	1,099.20	1,154.94	07/2005	-	-	0/0
332	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00	1,214.00	71.16	-	-	-	0/0
333	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42	776.00	270.69	05/2009	-	-	0/0
334	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, Bihar	04/1997	78.23	162.87	87.26	-	-	-	0/0
335	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00	847.76	818.01	06/2007	-	-	0/0
336	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34	296.20	310.56	04/2003	-	-	0/0
337	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00	548.96	485.24	03/2010	-	-	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
338	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	695.00	9.41	-	-	-	0/0
339	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00	607.09	344.96	-	-	-	0/0
340	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
341	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91	418.17	78.06	-	-	-	0/0
342	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13	1,225.00	209.85	-	-	-	0/0
343	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	258.80	03/2008	-	-	0/0
344	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	173.49	176.57	03/1998	-	-	0/0
345	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56	791.60	0.76	-	-	-	0/0
346	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92	261.70	-	02/2006	-	-	0/0
347	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00	732.80	316.05	03/2008	-	-	0/0
348	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19	900.00	216.45	-	-	-	0/0
349	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17	900.00	452.07	-	-	-	0/0
350	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00	227.40	24.19	-	-	-	0/0
351	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00	582.83	90.44	-	-	-	0/0
352	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00	529.88	37.16	-	-	-	0/0
353	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97	196.97	180.66	03/2011	-	-	0/0
354	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92	359.86	0.71	-	-	-	0/0
355	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36	196.95	174.86	03/2011	-	-	0/0
356	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90	548.95	472.58	06/1999	-	-	0/0
357	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81	495.44	170.02	03/2004	-	-	0/0
358	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94	302.23	330.27	-	-	-	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
359	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	289.43	06/2004 04/2005	-	-	0/0
360	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
361	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
362	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.57	- 12/2010	-	-	0/0
363	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	441.63	- -	-	-	0/0
364	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	455.90	- -	-	-	1/1
365	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,191.56	12/2006 08/2010	-	-	0/0
366	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	270.00	238.70	- 02/2011	-	-	0/0
367	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	476.79	02/2010 02/2011	-	-	0/0
368	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	378.83	- -	-	-	0/0
369	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	239.89	- 03/2011	-	-	0/0
370	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	140.28	- -	-	-	0/0
371	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	135.16	- -	-	-	0/0
372	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	86.35	- -	-	-	0/0
373	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	365.15	- 03/2011	-	-	0/0
374	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	80.40	- -	-	-	0/0
375	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	172.72	12/2010 03/2011	-	-	0/0
376	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	131.10	- 12/2010	-	-	0/0
Total			65,054.74 -	132,323.46	54,815.19				2/2
Road Transport & Highways									
377	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	200.70	10/2011 -	10/2011	0(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	163.47	08/2004 07/2010	12/2011	17(R3)	0/0
379	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	170.39	08/2004 -	12/2011	88(O)	0/0
380	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2011	81(O)	0/0
381	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	12/2011	81(O)	0/0
382	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	298.70	09/2007 -	12/2011	51(O)	0/0
383	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	254.10	09/2007 -	12/2011	51(O)	0/0
384	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	437.30	11/2007 -	12/2011	49(O)	0/0
385	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	208.70	06/2005 -	12/2011	78(O)	0/0
386	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	183.90	03/2008 -	12/2011	45(O)	0/0
387	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	193.10	154.20	03/2008 -	12/2011	45(O)	0/0
388	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	403.60	10/2008 -	12/2011	38(O)	0/0
389	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	12/2011	35(O)	0/0
390	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	12/2011	13(O)	0/0
391	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	229.60	02/2009 -	12/2011	34(O)	0/0
392	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	83.75	04/2009 -	12/2011	32(O)	0/0
393	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	176.20	06/2008 -	12/2011	42(O)	0/0
394	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	242.00	427.60	12/2008 -	12/2011	36(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
395	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	375.50	12/2008 -	12/2011	36(O)	0/0
396	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	208.10	06/2008 -	12/2011	42(O)	0/0
397	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	277.40	10/2008 -	12/2011	38(O)	0/0
398	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	198.00	187.30	11/2008 -	12/2011	37(O)	0/0
399	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	257.50	10/2008 -	12/2011	38(O)	0/0
400	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30 -	151.30	174.00	10/2008 -	12/2011	38(O)	0/0
401	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	340.00	452.90	09/2008 -	12/2011	39(O)	0/0
402	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	263.40	06/2008 -	12/2011	42(O)	0/0
403	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00 -	322.00	553.70	06/2009 -	12/2011	30(O)	0/0
404	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	196.50	236.60	06/2008 -	12/2011	42(O)	0/0
405	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	255.10	06/2008 -	12/2011	42(O)	0/0
406	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	489.10	03/2008 -	12/2011	45(O)	0/0
407	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	179.10	06/2008 -	12/2011	42(O)	0/0
408	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	219.30	04/2008 -	12/2011	44(O)	0/0
409	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	128.60	05/2008 -	12/2011	43(O)	0/0
410	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	195.60	06/2008 -	12/2011	42(O)	0/0
411	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	580.70	06/2009 -	12/2011	30(O)	0/0
412	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24 -	600.24	712.00	10/2009 -	12/2011	26(O)	0/0
413	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04 -	418.04	336.20	03/2010 -	12/2011	21(O)	0/0
414	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09 -	276.09	295.40	09/2009 -	12/2011	27(O)	0/0
415	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	660.10	07/2010 -	12/2011	17(O)	0/0
416	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	359.40	07/2010 -	12/2011	17(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
417	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	935.50	07/2010	12/2011	17(O)	0/0
418	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	345.50	05/2010	12/2011	19(O)	0/0
419	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	173.06	02/2004	12/2011	94(O)	0/0
420	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	627.70	08/2010	12/2011	16(O)	0/0
421	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	420.00	01/2011	12/2011	11(O)	0/0
422	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	558.60	05/2010	12/2011	19(O)	0/0
423	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,605.00	08/2011	12/2011	4(O)	0/0
424	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	252.70	11/2008	01/2012	38(O)	0/0
425	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	454.00	12/2008	01/2012	37(O)	0/0
426	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	295.00	09/2009	02/2012	29(O)	0/0
427	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56	390.56	511.40	02/2012	02/2012	0(O)	0/0
428	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	183.10	09/2007	03/2012	54(O)	0/0
429	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	82.92	04/2004	03/2012	95(O)	0/0
430	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	280.20	10/2008	03/2012	41(O)	0/0
431	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68	340.68	358.70	03/2008	03/2012	48(O)	0/0
432	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	257.60	06/2008	03/2012	45(O)	0/0
433	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	297.30	09/2008	03/2012	42(O)	0/0
434	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	213.90	10/2008	03/2012	41(O)	0/0
435	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	122.90	04/2008	03/2012	47(O)	0/0
436	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	183.80	04/2008	03/2012	47(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
437	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	256.68	02/2004	03/2012	97(O)	0/0
438	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	157.90	04/2010	03/2012	23(O)	0/0
439	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	03/2012	20(O)	0/0
440	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	03/2012	14(O)	0/0
441	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
442	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0
443	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	833.10	05/2012	05/2012	0(O)	0/0
444	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	372.30	05/2012	05/2012	0(O)	0/0
445	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	92.14	09/2008	06/2012	45(O)	0/0
446	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.20	10/2008	06/2012	44(O)	0/0
447	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.40	10/2009	06/2012	32(O)	0/0
448	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.70	12/2009	06/2012	30(O)	0/0
449	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	172.20	09/2010	06/2012	21(O)	0/0
450	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	396.80	06/2012	06/2012	0(O)	0/0
451	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8(O)	0/0
452	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,735.00	11/2011	06/2012	7(O)	0/0
453	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	330.60	07/2012	07/2012	0(O)	0/0
454	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	139.90	05/2008	08/2012	51(O)	0/0
455	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	510.50	10/2011	08/2012	10(O)	0/0
456	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	227.30	10/2008	09/2012	47(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
457	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	1,032.00	09/2012	09/2012	0(O)	0/0
458	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60	407.60	184.60	06/2010	10/2012	28(O)	0/0
459	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17	263.17	233.40	09/2009	10/2012	37(O)	0/0
460	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
461	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,060.00	10/2012	10/2012	0(O)	0/0
462	WADNER-DEVDHARI (NS-60/MH) (KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
463	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
464	RAJMARG CHORAH TO LAKHNAADON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	283.20	10/2008	12/2012	50(O)	0/0
465	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	177.40	07/2008	12/2012	53(O)	0/0
466	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	395.80	12/2012	12/2012	0(O)	0/0
467	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0
468	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	117.20	02/2013	02/2013	0(O)	0/0
469	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	1,214.00	09/2010	03/2013	30(O)	0/0
470	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	778.50	03/2013	03/2013	0(O)	0/0
471	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	354.00	03/2013	03/2013	0(O)	0/0
472	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
473	PUNE-SATARA (NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
474	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	11.39	03/2013	03/2013	0(O)	0/0
475	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
476	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	291.90	05/2013	05/2013	0(O)	0/0
477	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	152.30	05/2013	05/2013	0(O)	0/0
478	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
479	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	3.12	05/2013	05/2013	0(O)	0/0
480	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	23.62	05/2013	05/2013	0(O)	0/0
481	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	118.00	09/2007	06/2013	69(O)	0/0
482	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
483	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
484	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	97.17	06/2013	06/2013	0(O)	0/0
485	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	697.80	06/2013	06/2013	0(O)	0/0
486	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.86	06/2013	06/2013	0(O)	0/0
487	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	32.31	04/2009	07/2013	51(O)	0/0
488	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	52.97	11/2008	07/2013	56(O)	0/0
489	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41(O)	0/0
490	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	73.02	07/2013	07/2013	0(O)	0/0
491	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J & K	07/2010	1,813.76	1,813.76	-	07/2013	07/2013	0(O)	0/0
492	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	22.46	07/2013	07/2013	0(O)	0/0
493	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
494	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	338.20	08/2013	08/2013	0(O)	0/0
495	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	182.50	08/2013	08/2013	0(O)	0/0
496	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	-	08/2013	08/2013	0(O)	0/0
497	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	5.11	09/2013	09/2013	0(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
498	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	12.41	09/2013	09/2013	0(O)	0/0
499	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
500	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
501	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	193.90	11/2013	11/2013	0(O)	0/0
502	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0
503	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	45.39	11/2013	11/2013	0(O)	0/0
504	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
505	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
506	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
507	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	1.79	09/2007	04/2014	79(O)	0/0
508	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	0.36	07/2009	04/2014	57(O)	0/0
509	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
510	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	456.00	10/2014	10/2014	0(O)	0/0
511	NASHRI CHANANI - [N24000162]NHAI,J & K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
512	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J & K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
	Total		75,509.76	77,315.01	47,067.43				0/0
Shipping & Ports									
513	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	294.09	04/2009	02/2011	22(O)	0/0
514	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
515	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
516	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	241.50	157.81	09/2011 -	09/2011	0(O)	0/0
517	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	124.37	12/2005 01/2008	10/2011	45(R3)	0/0
518	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.79	04/2011 06/2011	11/2011	5(R3)	0/0
519	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
520	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	680.54	03/2012 -	03/2012	0(O)	0/0
521	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
522	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
523	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	0(R3)	0/0
524	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	610.00	12/2010 -	09/2012	21(O)	0/0
525	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	252.85	09/2012 -	09/2012	0(O)	0/0
526	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
527	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	20.75	12/2012 -	12/2012	0(O)	0/0
528	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
529	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
530	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
531	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	6.00	03/2006 -	12/2013	93(O)	0/0
532	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 -	12/2013	0(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
533	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46	994.82	189.92	02/2014	02/2014	0(O)	0/0
534	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.75	10/2008	-	-	0/0
535	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	-	12/2007 01/2009	-	-	0/0
536	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010	-	-	0/0
537	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	821.48	10/2008	-	-	0/0
	Total		18,052.23	19,035.72	4,500.37				0/0
Telecommunications									
538	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	-	09/2009	02/2010	5(O)	0/0
539	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	10/2010	7(O)	0/0
540	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	119.45	03/2009	02/2011	23(O)	0/0
541	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	206.79	12/2008	02/2011	26(O)	0/0
542	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	308.13	03/2009	02/2011	23(O)	0/0
543	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20	1,100.00	815.00	- 03/2011	02/2011	-1(R3)	0/1
544	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49	601.49	496.20	12/2008	03/2011	27(O)	0/0
545	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91	335.91	182.45	03/2009	03/2011	24(O)	0/0
546	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49	241.49	123.76	09/2009	03/2011	18(O)	0/0
547	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	17(O)	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
548	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33	584.33	403.71	02/2009	03/2011	25(O)	0/0
549	GSM equipment of 1700000Lines (2G) 234100 lines 3(G) - [N26000092]BSNL,Karnataka	10/2008	677.75	719.90	461.56	10/2009	03/2011	17(O)	0/0
550	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00	229.41	66.20	02/2007	08/2011	54(O)	0/0
551	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00	247.00	75.89	02/2007	08/2011	54(O)	0/0
552	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
553	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	168.31	12/2005	12/2011	72(O)	0/0
554	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15	158.72	76.55	06/2009	12/2011	30(O)	0/0
555	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81	336.81	155.71	01/2009	12/2011	35(O)	0/0
556	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00	366.00	227.39	10/2008	12/2011	38(O)	0/0
557	GSM equipment of 1867000Lines (2G) 383000 lines 3(G) - [N26000089]BSNL,Gujarat	08/2008	868.00	868.00	362.62	08/2009	12/2011	28(O)	0/0
558	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) - [N26000090]BSNL,Madhya pradesh	11/2009	916.70	916.70	280.72	11/2010	12/2011	13(O)	0/0
559	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91	922.91	346.90	01/2010	12/2011	23(O)	0/0
560	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70	848.70	712.86	01/2010	12/2011	23(O)	0/0
561	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19	315.19	142.07	01/2010	12/2011	23(O)	0/0
562	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	21.82	10/2010 03/2012	07/2012	4(R3)	0/0
563	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
564	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
565	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
566	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0
567	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
568	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	-	-	0/0
569	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	-	-	0/0
570	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	-	-	0/0
571	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	-	-	0/0
572	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
573	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	-	-	0/0
574	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	-	-	0/0
575	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	-	-	0/0
576	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	-	06/2009	-	-	0/0
577	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
Total			19,713.13	20,297.68	5,957.48				0/1
<u>Urban Development</u>									
578	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	12/2011	12/2013	24(O)	6/6
579	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
580	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	68.19	03/2016	03/2016	0(O)	0/0
581	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
Total			44,245.18	49,518.08	2,335.76				6/6
<u>Water Resources</u>									

Sector Wise Details

(Nov,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
582	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
			-			-			
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			712,007.92	821,529.93	348,301.14				1015/2333

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **40**

Number of Projects Delayed **10**

Number of Projects Without Date Of Commissioning **30**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 40 projects, 10 projects are delayed .30 projects do not have fixed dates of commissioning.

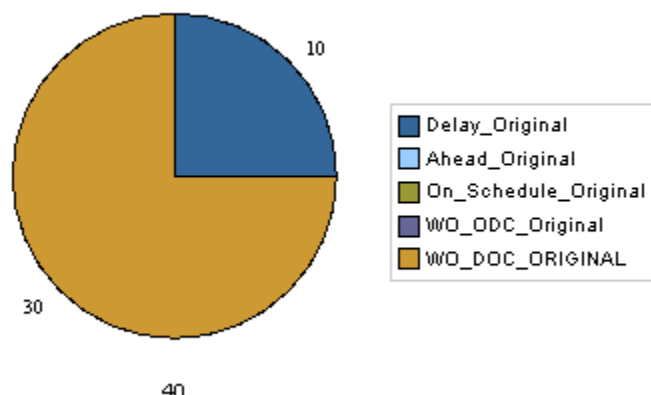

III. Investment Scenario

The Total Original cost of implementation of 40 projects when sanctioned, was of the order of Rs. 19713.13 crore but this was subsequently revised to Rs. 20297.68 crore implying a cost overrun of 3%. The expenditure incurred on these projects till November, 2011 is Rs. 5957.48 crore, which is 29.4% of the revised cost of the projects.

Figures are in Rs. Crore

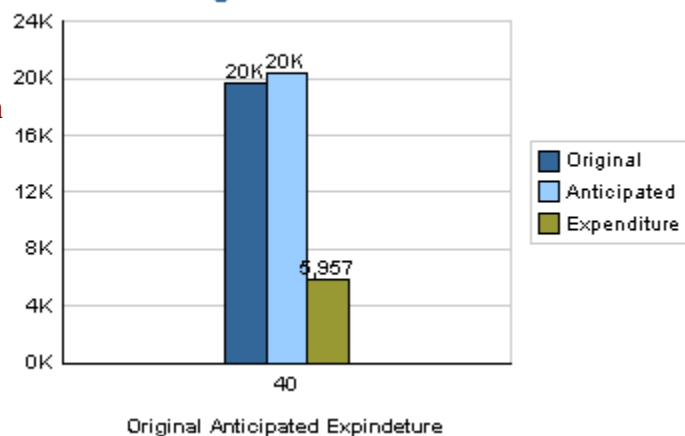

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	25
Number of Projects On Schedule	6
Number of Projects Delayed	10

Number of Projects Without Date Of Commissioning 9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 6 projects are on schedule and 10 projects are delayed .9 projects do not have fixed dates of commissioning.

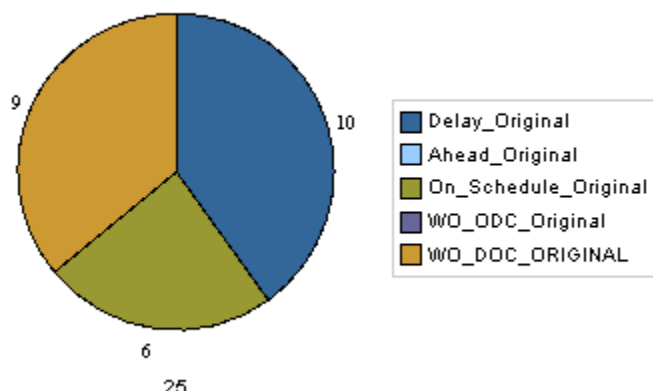

III. Investment Scenario

The Total Original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 18052.23 crore but this was subsequently revised to Rs. 19035.72 crore implying a cost overrun of 5.4%. The expenditure incurred on these projects till November, 2011 is Rs. 4500.37 crore, which is 23.6% of the revised cost of the projects.

Figures are in Rs. Crore

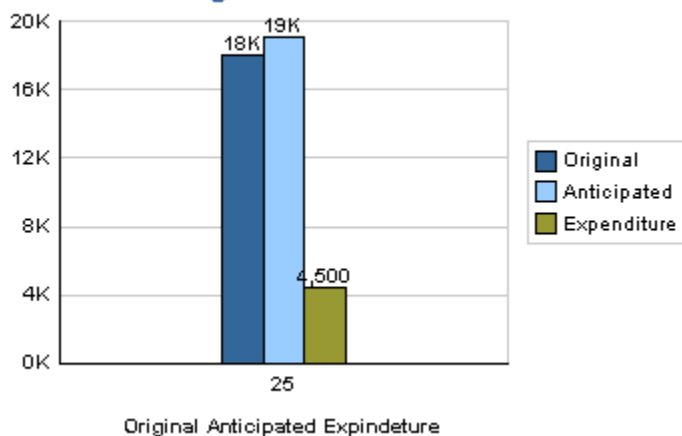

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	136
Number of Projects On Schedule	47
Number of Projects Delayed	88

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 136 projects, 47 projects are on schedule and 88 projects are delayed .1 project do not have fixed dates of commissioning.

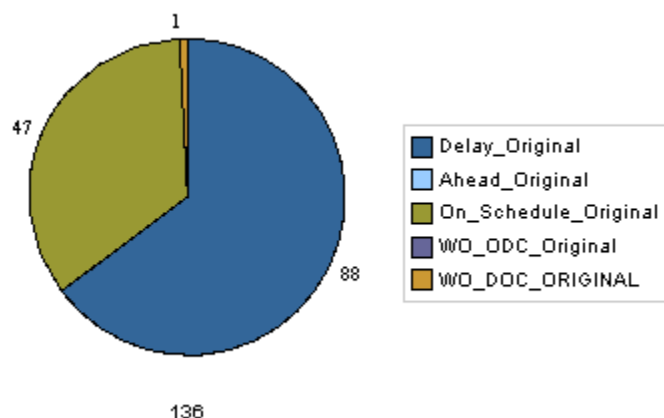

III. Investment Scenario

The Total Original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 75509.76 crore but this was subsequently revised to Rs. 77315.01 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till November, 2011 is Rs. 47067.43 crore, which is 60.9% of the revised cost of the projects.

Figures are in Rs. Crore

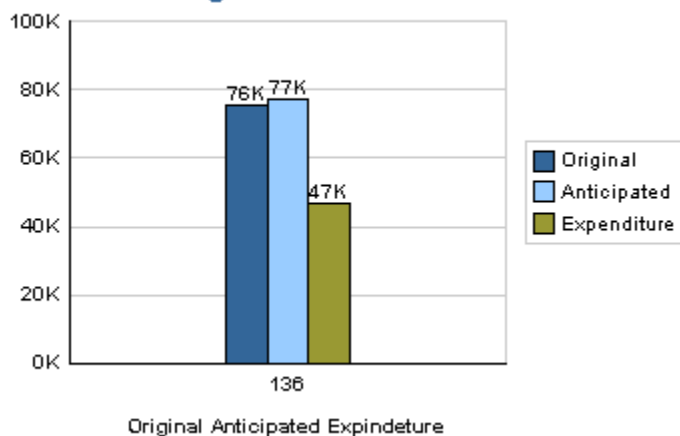

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	132
Number of Projects On Schedule	17
Number of Projects Delayed	26
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	24
Number of Projects Without Date Of Commissioning	63

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 2 projects are ahead of schedule, 17 projects are on schedule and 26 projects are delayed. 63 projects do not have fixed dates of commissioning. 24 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

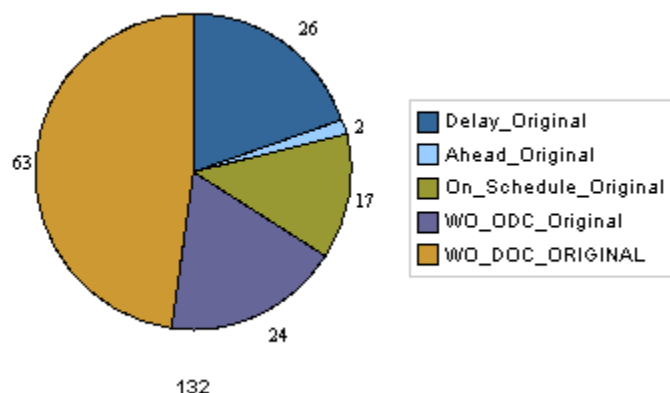

III. Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 65054.74 crore but this was subsequently revised to Rs. 132323.46 crore implying a cost overrun of 103.4%. The expenditure incurred on these projects till November, 2011 is Rs. 54815.19 crore, which is 41.4% of the revised cost of the projects.

Figures are in Rs. Crore

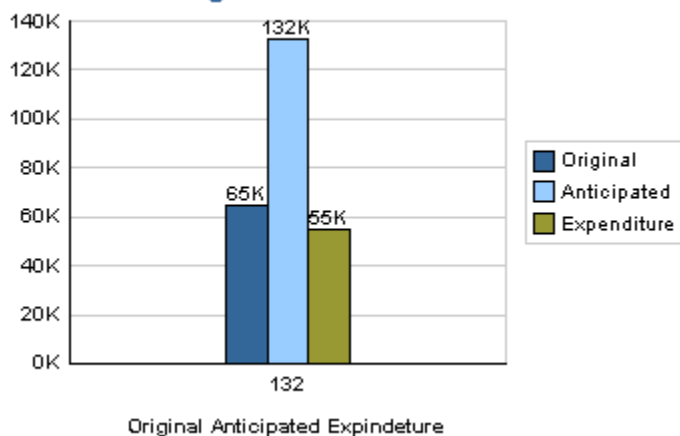

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	91
Number of Projects On Schedule	40
Number of Projects Delayed	47
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 91 projects, 2 projects are ahead of schedule, 40 projects are on schedule and 47 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

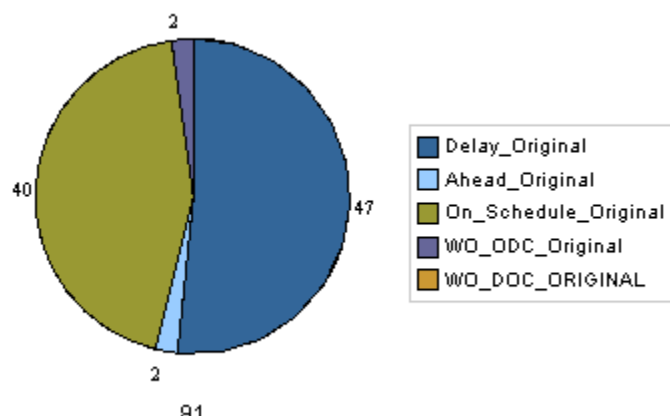

III. Investment Scenario

The Total Original cost of implementation of 91 projects when sanctioned, was of the order of Rs. 190920.07 crore but this was subsequently revised to Rs. 197203.66 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till November, 2011 is Rs. 94587.98 crore, which is 48% of the revised cost of the projects.

Figures are in Rs. Crore

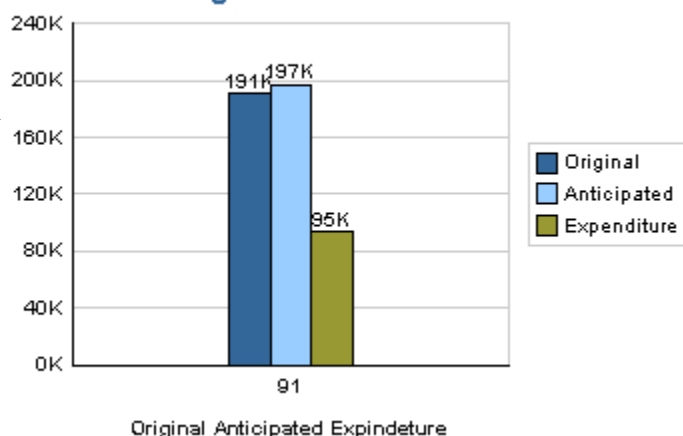

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	70
Number of Projects On Schedule	28
Number of Projects Delayed	30
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 70 projects, 1 project are ahead of schedule, 28 projects are on schedule and 30 projects are delayed .9 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

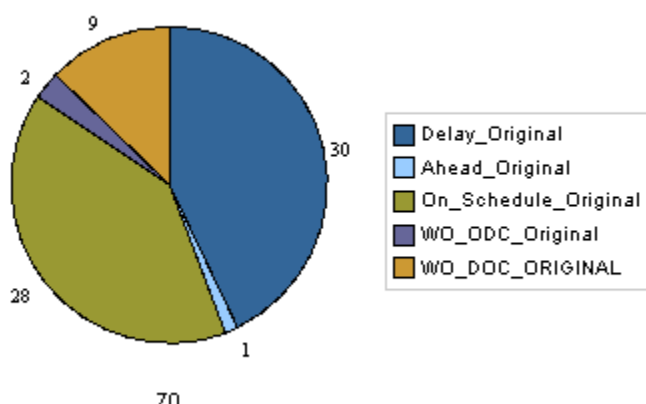

III. Investment Scenario

The Total Original cost of implementation of 70 projects when sanctioned, was of the order of Rs. 154794.07 crore but this was subsequently revised to Rs. 162721.78 crore implying a cost overrun of 5.1%. The expenditure incurred on these projects till November, 2011 is Rs. 59979.23 crore, which is 36.9% of the revised cost of the projects.

Figures are in Rs. Crore

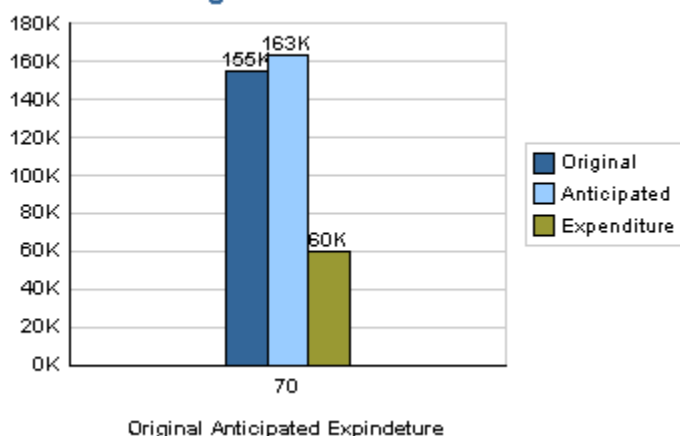

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	16
Number of Projects On Schedule	6
Number of Projects Delayed	3

Number of Projects Without Original Date of Commissioning	6
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 16 projects, 6 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

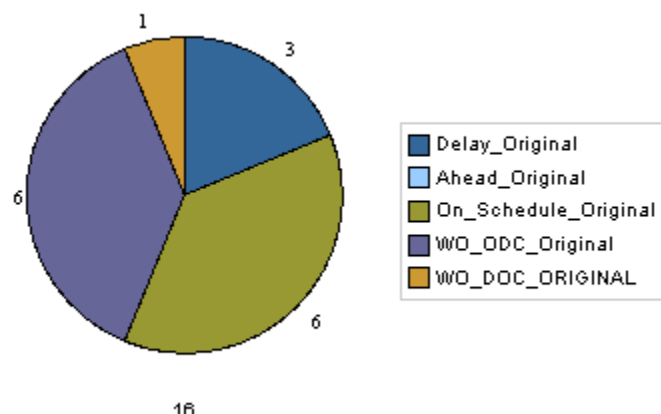

III. Investment Scenario

The Total Original cost of implementation of 16 projects when sanctioned, was of the order of Rs. 65244.82 crore but this was subsequently revised to Rs. 71412.36 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till November, 2011 is Rs. 34881.42 crore, which is 48.8% of the revised cost of the projects.

Figures are in Rs. Crore

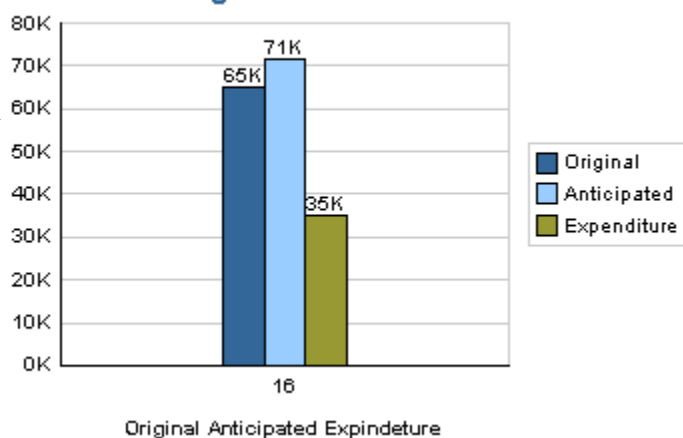

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

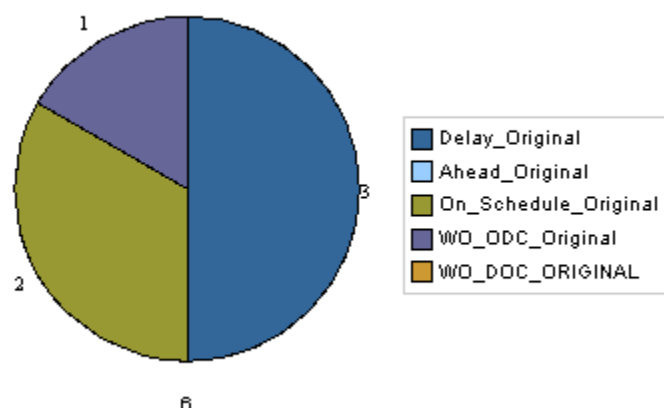

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till November, 2011 is Rs. 1155.6 crore, which is 21.7% of the revised cost of the projects.

Figures are in Rs. Crore

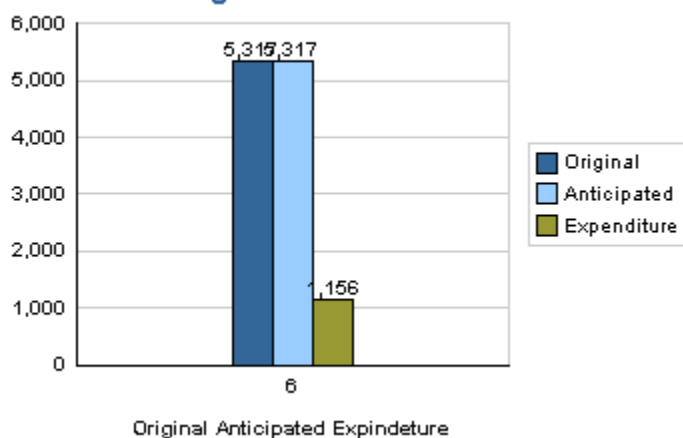

Sector wise current status of projects on theFlash Report


Coal

I. Current Status:

Number of Projects	50
Number of Projects On Schedule	20
Number of Projects Delayed	17
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	12

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 50 projects, 1 project are ahead of schedule, 20 projects are on schedule and 17 projects are delayed .12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

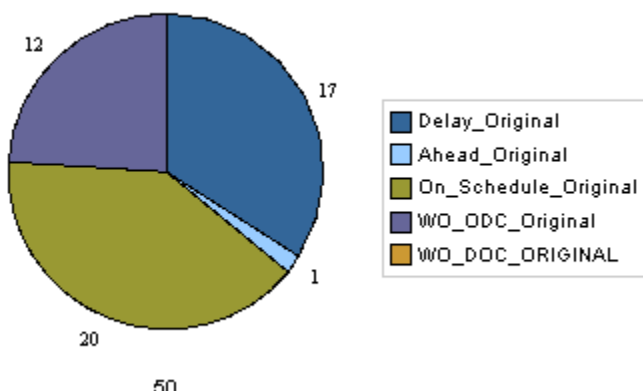

III. Investment Scenario

The Total Original cost of implementation of 50 projects when sanctioned, was of the order of Rs. 28811.62 crore but this was subsequently revised to Rs. 32198.65 crore implying a cost overrun of 11.8%. The expenditure incurred on these projects till November, 2011 is Rs. 12249.18 crore, which is 38% of the revised cost of the projects.

Figures are in Rs. Crore

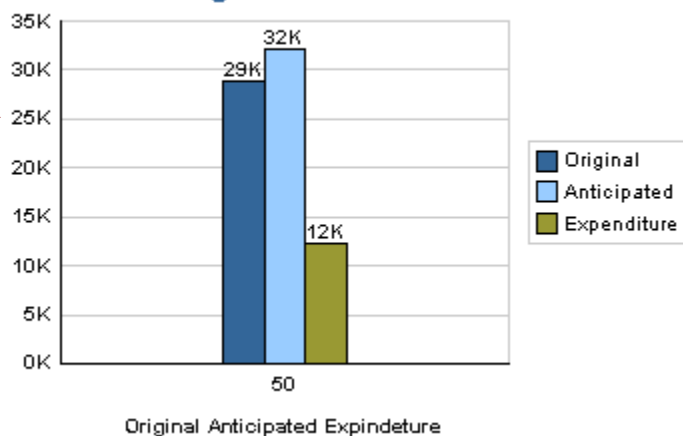

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 4 projects are delayed .

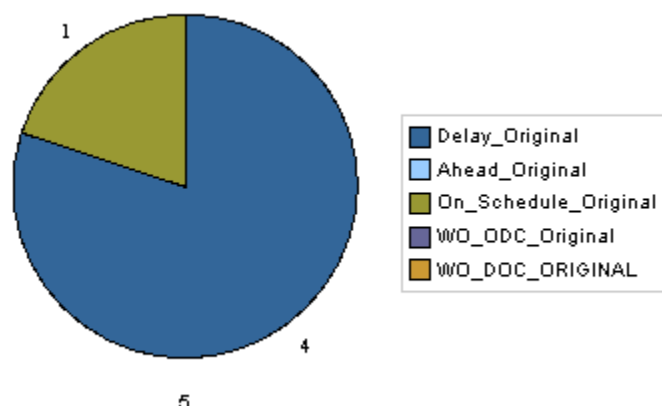

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.07 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till November, 2011 is Rs. 3733.84 crore, which is 66.5% of the revised cost of the projects.

Figures are in Rs. Crore

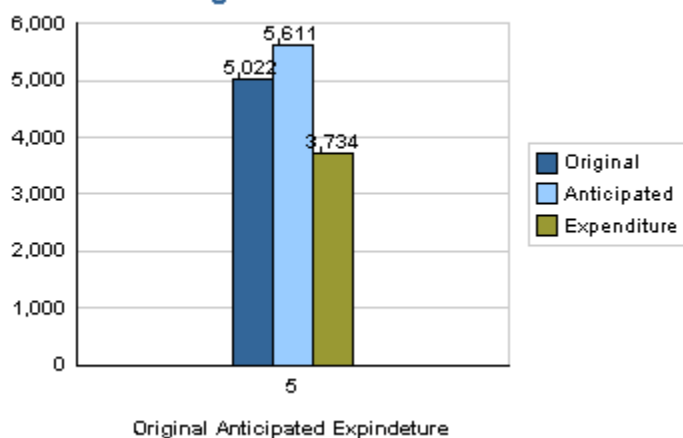

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	2
Number of Projects Without Original Date of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed .2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

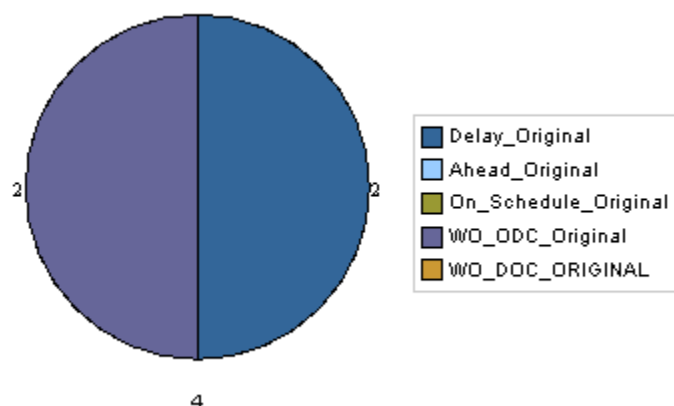

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till November, 2011 is Rs. 19673.61 crore, which is 57.8% of the revised cost of the projects.

Figures are in Rs. Crore

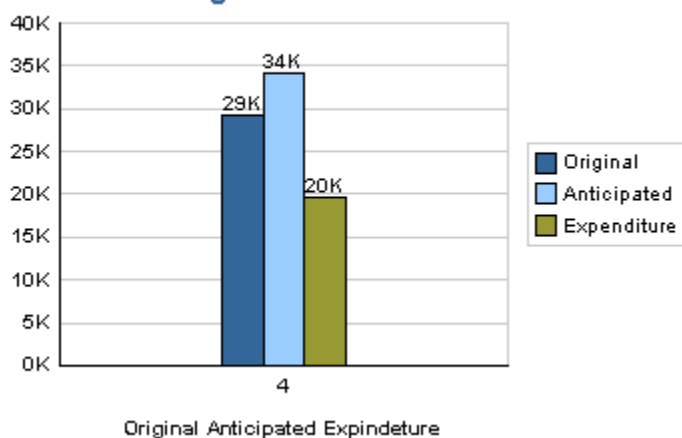

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	33	32855.21	39144.12	21548.37
2	Arunachal Pr.	4	9512.22	9610.51	7328.02
3	Assam	37	23895.78	35572.29	19104.24
4	Bihar	28	28362.95	33110.23	21176.35
5	Chhatisgarh	23	52747.27	55978.62	22988.07
6	Delhi	3	37985.00	37965.41	134.39
7	Goa	1	335.61	335.61	57.03
8	Gujarat	26	31711.98	32319.13	6031.04
9	Haryana	11	5987.83	7704.75	5168.20
10	Himachal Pr.	6	14761.16	14761.16	12523.20
11	J & K	11	14253.13	33156.54	11927.76
12	Jharkhandd	22	14396.48	15978.48	6478.81
13	Karnataka	27	31565.39	39928.36	17107.86
14	Kerala	8	6934.87	7548.87	2321.32
15	Madhya pradesh	25	17533.55	17765.86	6580.17
16	Maharashtra	52	72470.80	86887.47	39214.91
17	Manipur	1	727.56	3056.85	507.55
18	Mizoram	2	988.06	3307.12	290.47
19	Multi State	103	128507.92	131472.90	42505.32
20	Nagaland	1	850.00	850.00	8.44
21	Orissa	28	46896.69	50170.60	19406.15
22	Punjab	8	4854.69	5840.65	2993.65
23	Rajasthan	15	13638.67	14145.20	7627.06
24	Sikkim	2	1648.94	3690.03	206.04
25	Tamil Nadu	38	48500.48	57359.08	36980.31
26	Tripura	3	1522.39	2053.23	434.64
27	Uttar Pradesh	31	20197.31	23684.27	10138.24
28	Uttaranchal	6	10025.65	11948.21	4727.74
29	West Bengal	27	38340.33	46184.38	22785.79
TOTAL		582	712007.92	821529.93	348301.14

List of Projects In Which Expenditure is More then Cost

SN	PROJ_TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	13171.00	0.00	14159.00
2	BARSINGSAR TPS (2X125MW) (NLC)	Coal	1114.18	1626.09	1683.04
3	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	Petroleum	2305.30	700.00	2416.96
4	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	613.54	0.00	671.52
5	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	768.92	0.00	1399.53
6	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	611.02	0.00	692.51
7	CHAMERA,STAGE-III (NHPC)	Power	1405.63	0.00	1702.21
8	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	Power	621.28	0.00	707.14
9	KOTESHWAR HEP(THDC)	Power	1301.56	0.00	2533.29
10	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	297.37	297.91	305.73
11	GUNA-ETAWAH(NCR), NL	Railways	158.77	432.46	558.07
12	CALICUT-MANGALORE (DL) (SR)	Railways	240.00	0.00	595.35
13	KARUR-SALEM(NL),SR	Railways	155.55	0.00	636.64
14	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	100.00	322.29	422.82
15	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	491.19	1099.20	1154.94
16	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	248.44	576.27	799.58
17	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	184.00	254.07	471.19
18	KODERMA GIRIDH (NL), ECR	Railways	371.36	0.00	378.83
19	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	100.00	142.90	189.00
20	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	114.01	283.95	342.61
21	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	343.17	0.00	452.07
22	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	136.62	0.00	163.57
23	RUPSA-BANGRIPOSI (GC)(SER)	Railways	57.94	0.00	176.57
24	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	Railways	148.61	0.00	258.80
25	BILASPUR-URKURA (DL)	Railways	151.52	0.00	301.50
26	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	1676.31	0.00	2859.96
27	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	156.00	0.00	210.59
28	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	170.00	170.00	365.15
29	PATNA GANGA BRIDGE (NL), ECR	Railways	624.47	0.00	1137.14
30	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	733.00	0.00	904.98
31	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	Railways	78.23	0.00	87.26
32	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	108.00	214.09	250.82
33	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	233.00	335.77	569.83
34	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	1000.00	1500.00	2259.20
35	AMRAVATI-NARKHER NL(CR)	Railways	120.90	284.27	472.58
36	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	124.43	407.78	524.97
37	NANDYAL-YERRAGUNTALA(NL),SCR	Railways	155.74	164.36	492.50
38	ELECTRIFICATION OF MORADABAD-ROZA	Railways	129.17	0.00	223.95
39	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	200.80	0.00	269.02
40	RENIGUNTA-GUNTAKAL(RE)	Railways	168.34	0.00	310.56
41	RAJATGARH-BARANG(LD),ECOR	Railways	166.16	0.00	234.56
42	REWARI-ROHTAK (NL),NR	Railways	149.38	330.23	476.79

SN	PROJ_TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
43	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	409.00	625.30	818.01
44	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	323.40	0.00	455.90
45	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	395.00	1062.36	1197.67
46	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	100.00	0.00	485.24
47	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	295.00	0.00	479.98
48	KOTTUR-HARIHAR(NL),(SWR)	Railways	65.94	281.20	330.27
49	RANCHI-LOHARDAGA(GC),SER	Railways	194.07	0.00	289.43
50	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	293.97	0.00	383.13
51	GONDIA-JABALPUR(GC),(SECR)	Railways	386.30	0.00	570.21
52	KATIHAR - JOGBANI (GC)(NEFR)	Railways	100.00	492.98	720.57
53	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	Railways	280.00	0.00	705.93
54	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	907.69	1032.76	3191.56
55	GADWAL - RAICHUR (NL), SCR	Railways	92.63	108.91	238.70
56	BANKURA - DAMODAR (GC) (SER)	Railways	111.90	0.00	396.24
57	JIND-SONEPAT (NL),NR	Railways	190.81	238.56	354.41
58	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	412.78	0.00	437.30
59	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	240.00	0.00	280.20
60	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	557.00	0.00	930.90
61	NEW MANGALORE PORT NH-17 AND 48	Road Transport & Highways	196.50	0.00	236.60
62	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	1693.75	0.00	2605.00
63	SITAPUR-LUCKNOW	Road Transport & Highways	322.00	0.00	553.70
64	TRICHY - KORUR NH-67	Road Transport & Highways	516.00	0.00	594.20
65	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	280.00	0.00	580.70
66	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	941.00	0.00	1901.00
67	TRICHY - DINDIGUAL NH-45	Road Transport & Highways	576.00	0.00	660.10
68	AMRITSAR-PATHANKOT	Road Transport & Highways	705.00	0.00	846.50
69	Pune-sholapur, pkg1	Road Transport & Highways	1110.00	0.00	1802.00
70	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	441.00	0.00	935.50
71	Hazaribagh-Ranchi	Road Transport & Highways	625.07	0.00	666.00
72	Bijapur-Hungund Section	Road Transport & Highways	748.00	0.00	1214.00
73	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	1108.00	0.00	2735.00
74	Kishangarh-Ajmer-Beawer	Road Transport & Highways	795.00	0.00	833.10
75	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	168.00	0.00	454.00

SN	PROJ_TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
76	PONDICHERY - TINDIVANAU NH-66	Road Transport & Highways	285.00	0.00	359.40
77	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	600.24	0.00	712.00
78	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	251.03	0.00	283.20
79	KASIA TO GORAKHPUR (NH-28)(NHAI)	Road Transport & Highways	242.00	0.00	427.60
80	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	227.00	0.00	375.50
81	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	225.00	0.00	257.60
82	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	486.00	0.00	558.60
83	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	229.00	0.00	345.50
84	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	295.00	0.00	627.70
85	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	190.00	0.00	227.00
86	Armur to kadloor yellareddy	Road Transport & Highways	390.56	0.00	511.40
87	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	203.43	0.00	213.90
88	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	151.30	0.00	174.00
89	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	225.00	0.00	257.50
90	JHANSI TO LALITPUR, NH-26	Road Transport & Highways	276.09	0.00	295.40
91	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	275.00	0.00	277.40
92	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	340.68	0.00	358.70
93	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	340.00	0.00	452.90
94	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	221.82	0.00	252.70
95	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	200.00	0.00	263.40
96	NALBARI T BIJNI (AS-7)	Road Transport & Highways	208.00	0.00	219.30
97	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	245.00	0.00	489.10
98	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	220.00	0.00	254.10
99	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	275.00	0.00	298.70
100	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	273.00	0.00	475.60
101	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	367.49	0.00	453.68
102	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	157.47	0.00	183.10

SN	PROJ_TITLE	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
103	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	Road Transport & Highways	227.00	0.00	403.60
104	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	Road Transport & Highways	629.00	0.00	910.00
105	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	245.67	0.00	294.09
106	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	230.00	0.00	235.57
107	GSM equipment of 1900000Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	Telecommunications	760.20	0.00	815.00
108	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	Telecommunications	277.34	0.00	308.13

List of project Without Original Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning	
						Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL, Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,000.70	- 04/2011	04/2012
2	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,	10/2009	11,459.00 -	11,459.00	1,180.00	- 05/2016	11/2016
	Total		12,565.29 -	12,565.29	2,180.70		
	<u>Coal</u>						
3	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL, Orissa	12/2007	172.08 -	172.08	96.49	- -	03/2012
4	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL, Orissa	08/2008	207.28 -	207.28	68.11	- -	03/2012
5	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC, Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,291.14	- -	02/2013
6	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL, Chhatisgarh	06/2006	737.65 -	1,188.31	569.86	- -	03/2013
7	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL, Orissa	12/2007	457.77 -	457.77	113.54	- -	03/2013
8	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, Orissa	11/2008	475.93 -	479.63	81.70	- -	03/2013
9	CHURCHA RO UG (1.35MTY) - [N06000046]SECL, Chhatisgarh	06/2008	462.35 -	462.35	257.35	- -	03/2014
10	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL, Chhatisgarh	11/2009	321.42 -	321.50	203.26	- -	03/2014
11	PENGANGA OC - [N06000066]WCL, Orissa	10/2008	339.77 -	339.77	0.65	- -	10/2014
12	GOPAL PRASAD OCP - [N06000042]MCL, Orissa	02/2008	395.87 -	395.87	58.80	- -	03/2015
13	TALABIRA OCP - [N06000043]MCL, Orissa	03/2008	447.72 -	447.72	35.21	- -	03/2016
14	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL, Orissa	12/2007	490.00 -	490.10	99.74	- -	03/2017
	Total		9,412.38 -	9,871.92	3,875.85		
	<u>Fertilisers</u>						
15	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF, Haryana	01/2009	488.75 -	488.75	199.56	- 04/2012	04/2012
	Total		488.75 -	488.75	199.56		
	<u>Steel</u>						

List of project Without Original Date of Commissioning

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
16	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,Jharkhandd	10/2007	500.90 -	500.90	339.13	- -	01/2012
17	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	311.86	- 12/2011	03/2012
18	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 -	350.00	223.14	- 08/2010	03/2012
19	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 -	343.58	235.57	- 02/2011	04/2012
20	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	53.66	- 10/2012	10/2012
21	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	460.00	155.33	- 05/2012	12/2012
	Total		1,874.79 -	2,478.33	1,318.69		
<u>Petrochemicals</u>							
22	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	3,145.56	- 12/2013	-
	Total		5,460.61 -	8,920.00	3,145.56		
<u>Petroleum</u>							
23	EURO-IV DHD - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,735.01	- -	12/2011
24	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,	06/2009	3,032.00 -	261.00	174.49	- 08/2012	03/2012
	Total		5,647.69 -	2,876.69	1,909.50		
<u>Power</u>							
25	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,192.00	- -	03/2012
26	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,094.00	- -	10/2013
	Total		12,444.43 -	12,379.87	7,286.00		
<u>Railways</u>							
27	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	179.50	- -	12/2011
28	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	198.92	- 09/2009	12/2011
29	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,197.67	- -	02/2012

List of project Without Original Date of Commissioning

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
30	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 762.33	762.33	431.31	- 12/2009	02/2012
31	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 407.78	725.90	524.97	- -	03/2012
32	MANDARHILL-DUMKA-RAMPURHAT (NL), ER - [220100168]ER, Jharkhand	04/1995	184.00 254.07	675.00	471.19	- 12/2011	03/2012
33	KADUR-CHIKMAGALUR-SAKLESHPUR (NL), (SWR) - [220100190]SWR, Karnataka	04/1996	157.00 262.82	262.82	210.75	- 03/2012	03/2012
34	MUZAFFARPUR-SITAMARHI(NL), ECR - [220100194]ECR, Bihar	04/1997	100.00 322.29	411.22	422.82	- -	03/2012
35	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]ECR, Bihar	04/1997	233.00 335.77	903.56	569.83	- -	03/2012
36	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, Bihar	04/1996	114.01 283.95	427.89	342.61	- 03/2011	03/2012
37	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO 50 COAC - [N22000052]WS&PU, Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012
38	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU, Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012
39	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR, Arunachal Pr.	09/1996	156.00 -	254.29	210.59	- -	03/2012
40	NANGALDAM-TALWARA(NL), NR - [220100188](NR), Multi State	03/1981	37.68 450.00	730.00	327.68	- 07/2012	07/2012
41	CONV.OF 1500V DC TRACTION TO 25 KV AC, WR - [220100233]RE, Maharashtra	07/1996	273.67 1,160.52	1,302.12	590.40	- -	12/2012
42	JIND-SONEPAT (NL), NR - [220100280](NR), Haryana	01/2004	190.81 238.56	401.83	354.41	- 03/2012	12/2012
43	KOSI BRIDGE (NL), ECR - [220100304]ECR, Bihar	04/2002	323.41 -	341.41	242.37	- -	12/2012
44	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, Rajasthan	02/1997	151.84 410.08	410.08	155.97	- -	03/2013
45	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 -	1,029.00	705.93	- -	03/2013
46	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, Tamil Nadu	04/2006	495.74 495.74	495.74	138.24	- 06/2013	06/2013
47	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, Madhya Pradesh	04/2005	383.79 -	585.93	180.24	- -	12/2013
48	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR, Multi State	01/2004	915.70 -	1,717.29	819.96	- -	03/2014
49	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66 -	324.66	168.18	- -	03/2015

List of project Without Original Date of Commissioning

						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
50	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	344.96	- 12/2012	-
	Total		6,362.55	17,535.99	9,917.40		
			-				
Grand Total			54,256.49	67,116.84	29,833.26		

List of project Without Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
<u>Mines</u>					
1	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]NALCO, Orissa	10/2004	4,091.51 4,401.76	12/2008 01/2011	06/2011
	Total		4,091.51 -		
<u>Steel</u>					
2	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL, Chhatisgarh	07/2007	232.93 232.93	05/2011 -	10/2011
	Total		232.93 -		
<u>Petroleum</u>					
3	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70 755.76	03/2011 05/2011	06/2011
4	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54 -	12/2010 -	06/2011
5	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91 1,646.39	09/2009 -	08/2011
6	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 299.00	02/2011 08/2011	08/2011
7	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00 -	09/2011 -	09/2011
8	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40 -	06/2010 -	09/2011
9	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC, Maharashtra	09/2006	2,305.30 700.00	06/2010 06/2010	10/2011
10	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	10/2010 -	-
11	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	- -	-
	Total		10,617.92 -		
<u>Railways</u>					
12	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16 -	- 02/2009	12/2010
13	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41 207.00	- 03/2009	12/2010
14	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
15	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73 399.73	03/2009 12/2008	12/2010

List of project Without Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
16	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80 -	- -	12/2010
17	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
18	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
19	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,501.80	- 12/2010	06/2011
20	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	- 03/2010	-
21	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	-
22	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	-
23	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	- -	-
24	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	- -	-
25	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	03/1998 -	-
26	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	- -	-
27	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-
28	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	-
29	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	07/2008 -	-
30	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	07/2005 -	-
31	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
32	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	-
33	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	- -	-
34	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	-
35	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
36	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-
37	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	- -	-
38	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-

List of project Without Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
39	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	- -	-
40	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
41	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	03/2008 03/2009	-
42	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	03/1998 08/2005	-
43	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
44	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	02/2006 -	-
45	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
46	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-
48	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-
49	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	- -	-
50	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
51	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	-
52	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	-
53	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
54	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	-
55	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 -	-
56	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	- 03/2011	-
57	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	06/2004 04/2005	-
58	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
59	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	-
60	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	- 12/2010	-
61	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	-

List of project Without Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
62	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	- -	-
63	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	12/2006 08/2010	-
64	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	- 02/2011	-
65	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	-
66	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 -	- -	-
67	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	- 03/2011	-
68	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-
69	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-
70	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	-
71	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	- 03/2011	-
72	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	- -	-
73	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	12/2010 03/2011	-
74	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	- 12/2010	-
	Total		20,313.21 -		
<u>Road Transport & Highways</u>					
75	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	10/2011
	Total		353.37 -		
<u>Shipping & Ports</u>					
76	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -	04/2009 -	02/2011
77	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	12/2010 -	06/2011
78	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011
79	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	09/2011 -	09/2011
80	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	12/2005 01/2008	10/2011

List of project Without Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
81	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	-
82	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	12/2007 01/2009	-
83	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-
84	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-
	Total		4,830.66 -		
Telecommunications					
85	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	09/2009 -	02/2010
86	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010
87	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	03/2009 -	02/2011
88	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	02/2011
89	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	03/2009 -	02/2011
90	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20 -	- 03/2011	02/2011
91	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49 -	12/2008 -	03/2011
92	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	03/2009 -	03/2011
93	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49 -	09/2009 -	03/2011
94	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
95	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33 -	02/2009 -	03/2011
96	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	10/2009 -	03/2011
97	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 -	08/2011
98	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	08/2011

List of project Without Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	7	8
99	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	09/2011	09/2011
100	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	10/2007	-
101	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	-	-
102	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	03/2009	-
103	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	03/2009	-
104	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	03/2009	-
105	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	03/2010	-
106	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	03/2010	-
107	Procurement of STM-16 ADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	03/2010	-
108	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	03/2010	-
109	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	03/2010	-
110	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	03/2010	-
111	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	02/2010	-
112	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	09/2010	-
113	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	06/2009	-
114	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	03/2009	-
	Total		14,355.67		
			-		
	<u>Urban Development</u>				
115	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	04/2009	-
			173.08	-	
	Total		114.18		
			-		
Grand Total			54,909.45		

List of Delay Project

(Nov,2011)

						Date of Commissioning		Delay w.r.t. Original (in months)
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
<u>Atomic Energy</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,333.91	09/2010 -	01/2012	16
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,159.00	12/2008 -	02/2013	50
Total			16,663.00 -	21,501.00	17,492.91			
<u>Civil Aviation</u>								
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,572.92	01/2011 -	12/2011	11
4	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,625.49	05/2011 -	03/2012	10
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	153.41	01/2011 -	06/2012	17
6	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	57.03	05/2012 -	08/2012	3
Total			4,395.58 -	4,985.07	3,408.85			
<u>Coal</u>								
7	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,683.04	06/2009 -	12/2011	30
8	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	87.24	03/2010 -	03/2012	24
9	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,304.10	06/2009 -	07/2012	37
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	110.02	03/2011 03/2012	03/2013	24
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.62	288.78	03/2010 -	03/2013	36
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	212.40	03/2013 09/2012	12/2013	9
13	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,279.57	03/2010 -	03/2014	48
14	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,115.23	03/2010 -	03/2014	48
15	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.76	03/2011 -	03/2014	36
16	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.57	03/2011 03/2012	03/2014	36
17	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.45	03/2012 03/2012	03/2014	24

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
18	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	76.05	03/2012 03/2013	03/2014	24
19	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	140.21	03/2012	03/2015	36
20	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48
21	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	70.91	12/2012	03/2015	27
22	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	224.99	03/2014	03/2016	24
23	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.21	07/2012 03/2014	03/2016	44
	Total		11,824.69	14,752.18	7,728.53			
			-					
	Fertilisers							
24	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4
25	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8
26	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	298.10	12/2012	01/2013	1
	Total		2,241.63	2,241.63	488.20			
			-					
	Steel							
27	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	12,055.92	12/2011	03/2012	3
28	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	8,979.54	10/2009 10/2012	10/2012	36
29	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	3,998.29	03/2013	06/2013	3
	Total		40,400.00	45,964.00	25,033.75			
			-					
	Petroleum							
30	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00	798.00	659.96	04/2011 12/2011	12/2011	8
31	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	706.70	655.76	04/2010	12/2011	20
32	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	305.08	267.17	04/2011	12/2011	8
33	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	71.64	03/2009 02/2012	02/2012	35
34	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	12/2008 12/2008	03/2012	39

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
35	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	24
36	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	18
37	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 -	1,385.00	1,009.93	10/2010 12/2011	03/2012	17
38	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	759.98	09/2011 03/2012	03/2012	6
39	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	03/2012	6
40	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	204.00	144.60	01/2012 -	03/2012	2
41	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	171.96	06/2011 03/2012	03/2012	9
42	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	73
43	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,968.18	05/2010 05/2012	05/2012	24
44	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	74.11	05/2010 04/2012	05/2012	24
45	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	240.88	07/2010 05/2012	05/2012	22
46	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,907.34	08/2010 03/2012	06/2012	22
47	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	97.48	04/2011 -	07/2012	15
48	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	166.10	06/2011 07/2012	07/2012	13
49	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,401.09	03/2012 08/2012	08/2012	5
50	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.71	09/2011 -	12/2012	15
51	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	206.91	10/2012 12/2012	12/2012	2
52	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	91.09	12/2011 -	01/2013	13

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
53	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2
54	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	258.24	03/2006 03/2013	03/2013	84
55	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,772.36	05/2010 03/2013	03/2013	34
56	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	315.69	12/2011 04/2013	04/2013	16
57	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	11,345.73	11/2012 -	06/2013	7
58	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	595.79	03/2007 03/2014	03/2014	84
59	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,413.90	03/2007 03/2017	03/2017	120
	Total		72,263.16 -	82,263.74	38,848.56			
Power								
60	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25 -	238.25	218.42	05/2011 05/2011	12/2011	7
61	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	137.60	06/2010 -	12/2011	18
62	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,702.21	08/2010 -	02/2012	18
63	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,000.40	07/2010 -	02/2012	19
64	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	165.60	08/2011 -	02/2012	6
65	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	213.60	07/2010 02/2012	02/2012	19
66	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	88.50	07/2011 -	02/2012	7
67	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 -	2,283.69	2,533.29	04/2005 -	03/2012	83
68	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39 -	8,323.39	7,485.00	12/2009 -	03/2012	27
69	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46 -	3,779.46	3,510.70	09/2009 -	03/2012	30
70	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.66	710.80	10/2009 -	03/2012	29
71	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28 -	621.28	707.14	02/2011 -	03/2012	13

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
72	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	297.91	305.73	07/2011 -	03/2012	8
73	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	1,724.79	1,603.83	11/2009 -	04/2012	29
74	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	768.92	1,399.53	03/2007 -	05/2012	62
75	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52 -	2,304.52	1,604.48	10/2010 -	06/2012	20
76	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	557.24	512.20	01/2010 -	06/2012	29
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	317.69	64.50	11/2011 -	06/2012	7
78	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	692.51	08/2010 -	11/2012	27
79	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	1,045.69	09/2009 -	12/2012	39
80	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,779.29	1,751.18	11/2008 -	12/2012	49
81	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	684.00	11/2011 -	12/2012	13
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	239.90	11/2011 -	12/2012	13
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	304.00	11/2011 -	12/2012	13
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	149.50	02/2012 -	12/2012	10
85	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,921.00	04/2009 -	03/2013	47
86	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	382.80	09/2010 -	03/2013	30
87	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	3,090.00	08/2012 -	03/2013	7
88	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	922.20	02/2012 -	03/2013	13
89	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00 -	5,915.00	2,429.00	10/2012 -	03/2013	5
90	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,247.00	10/2012 -	03/2013	5
91	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	79.38	01/2012 07/2013	07/2013	18

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
92	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	247.01	08/2012 08/2013	08/2013	12
93	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,399.75	01/2012 -	09/2013	20
94	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	134.30	11/2011 -	09/2013	22
95	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,534.00	06/2011 -	10/2013	28
96	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	286.86	07/2006 01/2014	01/2014	90
97	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,206.00	03/2013 -	06/2014	15
98	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	3,161.00	08/2013 -	09/2014	13
99	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,287.00	12/2009 -	10/2014	58
100	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,383.56	09/2009 -	12/2014	63
101	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	6,285.33	5,216.33	09/2010 -	12/2015	63
102	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67 3,642.04	3,642.04	1,034.24	07/2014 01/2016	01/2016	18
103	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,654.09	05/2013 06/2016	06/2016	37
104	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	208.64	07/2014 -	07/2016	24
105	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	812.90	12/2007 12/2009	03/2013	63
106	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	277.93	07/2010 02/2016	02/2016	67
Total			111,027.19 -	117,375.34	71,745.30			
<u>Railways</u>								
107	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	-	02/2010 -	11/2011	21
108	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213
109	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	207.66	189.00	03/2002 -	12/2011	117
110	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	840.32	492.50	02/2009 -	12/2011	34
111	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	67.74	12/2011 -	02/2012	2
112	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	544.29	03/1995 -	03/2012	204

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
113	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90	324.90	188.17	03/2010	03/2012	24
114	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17	250.00	223.95	03/2011	03/2012	12
115	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97	723.27	383.13	06/2005 07/2011	03/2012	81
116	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	146.26	03/2007 03/2007	06/2012	63
117	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90	1,211.22	396.24	03/2005 12/2008	12/2012	93
118	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00	981.00	556.40	03/2009	12/2012	45
119	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47	1,389.98	1,137.14	10/2007	12/2012	62
120	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	687.20	427.67	03/2010	12/2012	33
121	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04	603.04	48.10	03/2012	03/2013	12
122	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97	189.97	71.51	12/2011	11/2013	23
123	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90	223.01	83.63	12/2012	12/2013	12
124	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31	4,091.33	2,859.96	03/2009	12/2013	57
125	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00	1,655.80	904.98	12/2008	03/2014	63
126	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00	369.90	109.77	03/2010 06/2014	06/2014	51
127	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,259.20	04/2008 03/2014	12/2014	80
128	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	323.57	03/2014	03/2015	12
129	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	507.55	03/2011 03/2014	03/2016	60
130	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	-	03/2014	03/2016	24
131	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	17.12	03/2016	06/2016	3
132	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,333.52	03/2001	12/2017	201
Total			22,320.65	51,989.04	19,829.47			

Road Transport & Highways

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
133	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	163.47	08/2004 07/2010	12/2011	88
134	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	170.39	08/2004 -	12/2011	88
135	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2011	81
136	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	12/2011	81
137	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	298.70	09/2007 -	12/2011	51
138	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	254.10	09/2007 -	12/2011	51
139	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	437.30	11/2007 -	12/2011	49
140	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	208.70	06/2005 -	12/2011	78
141	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	183.90	03/2008 -	12/2011	45
142	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27 -	193.10	154.20	03/2008 -	12/2011	45
143	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	403.60	10/2008 -	12/2011	38
144	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	12/2011	35
145	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	12/2011	13
146	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	229.60	02/2009 -	12/2011	34
147	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	83.75	04/2009 -	12/2011	32
148	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	176.20	06/2008 -	12/2011	42
149	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00 -	242.00	427.60	12/2008 -	12/2011	36
150	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00 -	227.00	375.50	12/2008 -	12/2011	36

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
151	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	208.10	06/2008	12/2011	42
152	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	277.40	10/2008	12/2011	38
153	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	187.30	11/2008	12/2011	37
154	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00	225.00	257.50	10/2008	12/2011	38
155	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	174.00	10/2008	12/2011	38
156	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	452.90	09/2008	12/2011	39
157	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	263.40	06/2008	12/2011	42
158	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	12/2011	30
159	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	236.60	06/2008	12/2011	42
160	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	255.10	06/2008	12/2011	42
161	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	489.10	03/2008	12/2011	45
162	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	179.10	06/2008	12/2011	42
163	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	219.30	04/2008	12/2011	44
164	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	128.60	05/2008	12/2011	43
165	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	195.60	06/2008	12/2011	42
166	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30
167	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	712.00	10/2009	12/2011	26
168	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	336.20	03/2010	12/2011	21
169	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09	276.09	295.40	09/2009	12/2011	27
170	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00	576.00	660.10	07/2010	12/2011	17
171	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00	285.00	359.40	07/2010	12/2011	17
172	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	935.50	07/2010	12/2011	17
173	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	345.50	05/2010	12/2011	19

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
174	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	173.06	02/2004	12/2011	94
175	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	627.70	08/2010	12/2011	16
176	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	420.00	01/2011	12/2011	11
177	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	558.60	05/2010	12/2011	19
178	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,605.00	08/2011	12/2011	4
179	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	252.70	11/2008	01/2012	38
180	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	454.00	12/2008	01/2012	37
181	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	295.00	09/2009	02/2012	29
182	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	183.10	09/2007	03/2012	54
183	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	82.92	04/2004	03/2012	95
184	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	280.20	10/2008	03/2012	41
185	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	358.70	03/2008	03/2012	48
186	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	257.60	06/2008	03/2012	45
187	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	332.94	297.30	09/2008	03/2012	42
188	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	213.90	10/2008	03/2012	41
189	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	175.96	122.90	04/2008	03/2012	47
190	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	198.16	183.80	04/2008	03/2012	47
191	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	256.68	02/2004	03/2012	97
192	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	157.90	04/2010	03/2012	23
193	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	03/2012	20
194	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	03/2012	14

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
195	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27
196	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	92.14	09/2008	06/2012	45
197	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.20	10/2008	06/2012	44
198	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.40	10/2009	06/2012	32
199	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.70	12/2009	06/2012	30
200	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	172.20	09/2010	06/2012	21
201	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8
202	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,735.00	11/2011	06/2012	7
203	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	139.90	05/2008	08/2012	51
204	Chilkaluript-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	510.50	10/2011	08/2012	10
205	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	227.30	10/2008	09/2012	47
206	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	184.60	06/2010	10/2012	28
207	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.40	09/2009	10/2012	37
208	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16
209	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	283.20	10/2008	12/2012	50
210	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	177.40	07/2008	12/2012	53
211	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	1,214.00	09/2010	03/2013	30
212	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	118.00	09/2007	06/2013	69
213	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
214	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	32.31	04/2009 -	07/2013	51
215	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	52.97	11/2008 -	07/2013	56
216	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.20	02/2010 -	07/2013	41
217	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	10/2013	14
218	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	40.71	11/2008 -	12/2013	61
219	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	1.79	09/2007 -	04/2014	79
220	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	0.36	07/2009 -	04/2014	57
Total			31,347.43 -	33,512.68	34,947.64			
Shipping & Ports								
221	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.79	04/2011 06/2011	11/2011	7
222	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	7
223	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2
224	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	5
225	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	610.00	12/2010 -	09/2012	21
226	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29
227	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25
228	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24
229	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52
230	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	6.00	03/2006 -	12/2013	93
Total			8,208.42 -	9,033.57	1,361.81			

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)
						Original / Revised	Anticipated	
1	2	3	4	5	6	7	8	9
<u>Telecommunications</u>								
231	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	168.31	12/2005 -	12/2011	72
232	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	12/2011	30
233	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	12/2011	35
234	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.39	10/2008 -	12/2011	38
235	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	362.62	08/2009 -	12/2011	28
236	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	280.72	11/2010 -	12/2011	13
237	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	12/2011	23
238	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70 -	848.70	712.86	01/2010 -	12/2011	23
239	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19 -	315.19	142.07	01/2010 -	12/2011	23
240	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	21.82	10/2010 03/2012	07/2012	21
Total			5,357.46 -	5,542.54	2,494.95			
<u>Urban Development</u>								
241	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24
Total			6,395.00 -	11,609.00	2,267.57			
<u>Water Resources</u>								
242	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60
Total			542.90 -	1,187.00	35.49			
Grand Total			332,987.11	401,956.79	225,683.03			

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
<u>Civil Aviation</u>							
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 -	12/2011		0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2012		0/0
3	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 -	06/2012		0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	08/2012		0/0
5	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013		0/0
	Total		5,021.58 -				0/0
<u>Coal</u>							
6	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	03/2014 -	03/2014		0/0
7	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	04/2014 -	04/2014		0/0
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	03/2015 -	03/2015		0/0
9	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	03/2015 03/2015	03/2015		0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	04/2015 -	04/2015		0/0
11	KHADIA EXPANSION OPENCASE PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 -	03/2018		0/0
	Total		3,473.71 -				0/0
<u>Fertilisers</u>							
12	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	11/2011		0/0
13	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	03/2012		0/0
	Total		763.00 -				0/0
<u>Steel</u>							
14	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	04/2013 -	04/2013		0/0
15	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	05/2013 -	05/2013		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
16	ENHANCEMENT OF PROD. CAP. AT BOLANI I/O MINES - [N12000075]SAIL, Orissa	11/2011	254.55	11/2013	11/2013		0/0
	Total		1,725.10				0/0
			-				
	Petroleum						
17	North Tapti Gas Field Development - [N16000096]ONGC, Multi State	07/2008	589.70	03/2011	06/2011		0/0
			755.76	05/2011			
18	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL, Bihar	06/2009	613.54	12/2010	06/2011		0/0
			-	-			
19	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]BRPL, Assam	06/2006	1,431.91	09/2009	08/2011		0/0
			1,646.39	-			
20	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00	02/2011	08/2011		0/0
			299.00	08/2011			
21	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL, Maharashtra	03/2009	3,284.00	09/2011	09/2011		0/0
			-	-			
22	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL, Maharashtra	06/2008	304.40	06/2010	09/2011		0/0
			-	-			
23	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC, Maharashtra	09/2006	2,305.30	06/2010	10/2011		0/0
			700.00	06/2010			
24	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70	04/2010	12/2011		0/0
			-	-			
25	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08	04/2011	12/2011		0/0
			-	-			
26	MRPL Phase-III Expansion - [N16000114]Mangalore Refin, Karnataka	08/2008	12,412.00	01/2012	01/2012		0/0
			12,160.26	-			
27	MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21	03/2009	02/2012		0/0
			-	02/2012			
28	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC, Maharashtra	08/2006	3,195.16	12/2008	03/2012		0/0
			-	12/2008			
29	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02	03/2010	03/2012		0/0
			-	03/2012			
30	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40	09/2010	03/2012		0/0
			2,920.82	03/2012			
31	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00	09/2011	03/2012		0/0
			898.00	03/2012			
32	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00	09/2011	03/2012		0/0
			2,730.00	03/2012			
33	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, Multi State	07/2009	7,596.18	01/2013	03/2012		0/0
			-	-			

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
34	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	03/2012 -	03/2012		0/0
35	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	04/2006 05/2011	05/2012		0/0
36	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	05/2012		0/0
37	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	05/2010 04/2012	05/2012		0/0
38	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2012		0/0
39	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	06/2012		0/0
40	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2012		0/0
41	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	06/2012		0/0
42	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	07/2012		0/0
43	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	07/2012 -	07/2012		0/0
44	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	08/2012		0/0
45	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2012		0/0
46	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 -	09/2012		0/0
47	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2012		0/0
48	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2012		0/0
49	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	10/2012 12/2012	12/2012		0/0
50	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013		0/0
51	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	01/2013		0/0
52	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013		0/0
53	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	03/2013 03/2013	03/2013		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
54	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	03/2013	03/2013		0/0
55	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64	03/2013	03/2013		0/0
56	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03	03/2013	03/2013		0/0
57	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11	03/2013	03/2013		0/0
58	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79	05/2013	05/2013		0/0
59	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20	08/2013	08/2013		0/0
60	Wax Project - [N16000101]NRL, Assam	06/2010	576.60	12/2013	12/2013		0/0
61	Development of WO-16 Cluster Fields - [N16000105]ONGC, Multi State	06/2010	2,523.00	01/2014	01/2014		0/0
62	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94	01/2014	01/2014		0/0
63	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00	02/2014	02/2014		0/0
64	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	12/2014	12/2014		0/0
65	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	12/2014	12/2014		0/0
66	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00	04/2015	04/2015		0/0
67	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07	10/2010	-		0/0
68	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00	-	-		0/0
	Total		103,965.05				0/0
	Power						
69	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL, J & K	10/2006	238.25	05/2011	12/2011		0/0
70	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL, Multi State	12/2007	227.52	06/2010	12/2011		0/0
71	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63	08/2010	02/2012		0/0
72	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL, Multi State	02/2009	664.96	02/2012	02/2012		0/0
73	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL, Multi State	02/2009	409.50	02/2012	02/2012		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	08/2011 -	02/2012		0/0
75	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	07/2010 02/2012	02/2012		0/0
76	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	07/2011 -	02/2012		0/0
77	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 297.91	07/2011 -	03/2012		0/0
78	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86 -	06/2012 -	03/2012		0/0
79	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	11/2009 -	04/2012		0/0
80	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	04/2012 -	04/2012		0/0
81	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	05/2012 -	05/2012		0/0
82	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52 -	10/2010 -	06/2012		0/0
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69 -	11/2011 -	06/2012		0/0
84	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	06/2012 -	06/2012		0/0
85	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	06/2012 -	06/2012		0/0
86	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	08/2012 -	08/2012		0/0
87	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	08/2012 -	08/2012		0/0
88	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	08/2012 -	08/2012		0/0
89	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	10/2012 -	10/2012		0/0
90	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38 -	10/2012 -	10/2012		0/0
91	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	10/2012 -	10/2012		0/0
92	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	08/2010 -	11/2012		0/0
93	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	11/2012 -	11/2012		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
94	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	11/2012 -	11/2012		0/0
95	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	11/2012 -	11/2012		0/0
96	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC, West Bengal	09/2005	1,061.38 -	09/2009 -	12/2012		0/0
97	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	12/2012 -	12/2012		0/0
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	11/2011 -	12/2012		0/0
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	11/2011 -	12/2012		0/0
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	02/2012 -	12/2012		0/0
101	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	12/2012 -	12/2012		0/0
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	01/2013 -	01/2013		0/0
103	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	01/2013 -	01/2013		0/0
104	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	09/2010 -	03/2013		0/0
105	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	02/2012 -	03/2013		0/0
106	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	03/2013 -	03/2013		0/0
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	04/2013 -	04/2013		0/0
108	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	04/2013 -	04/2013		0/0
109	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	01/2012 07/2013	07/2013		0/0
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	07/2013 -	07/2013		0/0
111	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	07/2013 -	07/2013		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
112	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya pradesh	07/2011	181.93 -	07/2013 -	07/2013		0/0
113	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	08/2013 -	08/2013		0/0
114	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	08/2013 -	08/2013		0/0
115	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	08/2013 -	08/2013		0/0
116	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	11/2011 -	09/2013		0/0
117	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	10/2013 -	10/2013		0/0
118	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	11/2013 -	11/2013		0/0
119	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26 -	11/2013 -	11/2013		0/0
120	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97 -	12/2013 -	11/2013		0/0
121	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19 -	12/2013 -	12/2013		0/0
122	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	12/2013 -	12/2013		0/0
123	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	12/2013 -	12/2013		0/0
124	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	03/2014 -	03/2014		0/0
125	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	05/2014 -	05/2014		0/0
126	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	06/2014 -	06/2014		0/0
127	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	08/2014 -	08/2014		0/0
128	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	08/2013 -	09/2014		0/0
129	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	09/2014 -	09/2014		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
130	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	01/2015	01/2015		0/0
131	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67	07/2014	01/2016		0/0
			3,642.04	01/2016			
	Total		93,636.58				0/0
			-				
<u>Railways</u>							
132	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Orissa	04/1999	166.16	-	12/2010		0/0
			-	02/2009			
133	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41	-	12/2010		0/0
			207.00	03/2009			
134	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	12/2007	12/2010		0/0
			-	03/2010			
135	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73	03/2009	12/2010		0/0
			399.73	12/2008			
136	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL, Gujarat	09/2005	200.80	-	12/2010		0/0
			-	-			
137	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	-	03/2011		0/0
			-	03/2009			
138	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	03/2009	03/2011		0/0
			-	12/2009			
139	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50	02/2010	11/2011		0/0
			-	-			
140	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77	03/1994	12/2011		0/0
			432.46	-			
141	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR, Orissa	04/1993	100.00	03/2002	12/2011		0/0
			142.90	-			
142	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74	02/2009	12/2011		0/0
			164.36	-			
143	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, Orissa	04/1994	355.38	-	12/2011		0/0
			470.21	-			
144	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64	-	12/2011		0/0
			-	09/2009			
145	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR, Karnataka	04/2007	482.00	03/2013	12/2011		0/0
			-	-			
146	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER, Uttar Pradesh	03/1997	395.00	-	02/2012		0/0
			1,062.36	-			
147	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96	-	02/2012		0/0
			762.33	12/2009			
148	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER, West Bengal	04/2009	259.51	12/2011	02/2012		0/0
			-	-			
149	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS, Multi State	03/1984	520.00	03/1995	03/2012		0/0
			637.46	-			

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
150	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	- -	03/2012		0/0
151	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	- 12/2011	03/2012		0/0
152	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	- 03/2012	03/2012		0/0
153	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	- -	03/2012		0/0
154	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	- -	03/2012		0/0
155	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	- 03/2011	03/2012		0/0
156	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012		0/0
157	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012		0/0
158	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012		0/0
159	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	- -	03/2012		0/0
160	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012		0/0
161	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012		0/0
162	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	06/2005 07/2011	03/2012		0/0
163	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	03/2012 -	03/2012		0/0
164	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	03/2012		0/0
165	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	03/2007 03/2007	06/2012		0/0
166	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	- 07/2012	07/2012		0/0
167	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	12/2012		0/0
168	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	- -	12/2012		0/0
169	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 -	12/2012		0/0
170	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	03/2005 12/2008	12/2012		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
171	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	- 03/2012	12/2012		0/0
172	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	- -	12/2012		0/0
173	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	03/2009 -	12/2012		0/0
174	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	10/2007 -	12/2012		0/0
175	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012		0/0
176	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	12/2012 -	12/2012		0/0
177	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013		0/0
178	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	- -	03/2013		0/0
179	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	03/2012 -	03/2013		0/0
180	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	03/2013 -	03/2013		0/0
181	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,Tamil Nadu	04/2006	495.74 495.74	- 06/2013	06/2013		0/0
182	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	12/2011 -	11/2013		0/0
183	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013		0/0
184	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	12/2012 -	12/2013		0/0
185	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	03/2009 -	12/2013		0/0
186	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	12/2008 -	03/2014		0/0
187	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	- -	03/2014		0/0
188	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	03/2014 -	03/2014		0/0
189	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	04/2014 -	03/2014		0/0
190	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	03/2014 -	03/2014		0/0
191	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	03/2014 -	03/2014		0/0
192	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
193	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR), Uttar Pradesh	04/2006	325.00 -	03/2010 06/2014	06/2014		0/0
194	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR, Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2014		0/0
195	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL, Orissa	04/1998	183.23 -	02/2015 -	02/2015		0/0
196	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66 -	- -	03/2015		0/0
197	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 -	03/2014 -	03/2015		0/0
198	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112]NWR, Rajasthan	04/2008	829.74 -	03/2015 -	03/2015		0/0
199	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 -	03/2015 -	03/2015		0/0
200	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015		0/0
201	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2016		0/0
202	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	03/2014 -	03/2016		0/0
203	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016		0/0
204	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016		0/0
205	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016		0/0
206	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J & K	03/1995	2,500.00 8,000.00	03/2001 -	12/2017		0/0
207	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 -	- 03/2010	-		0/0
208	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	04/1983	36.80 274.41	- -	-		0/0
209	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	-		0/0
210	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08 462.67	- -	-		0/0
211	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR - [220100183]SWR, Karnataka	02/1997	295.00 -	- -	-		0/0
212	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 -	03/1998 -	-		0/0
213	KARUR-SALEM(NL), SR - [220100191]SR, Tamil Nadu	02/1997	155.55 -	- -	-		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
214	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	- -	-		0/0
215	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	-		0/0
216	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	07/2008 -	-		0/0
217	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	07/2005 -	-		0/0
218	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-		0/0
219	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	-		0/0
220	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	- -	-		0/0
221	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	-		0/0
222	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-		0/0
223	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	- -	-		0/0
224	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	- -	-		0/0
225	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	- 12/2012	-		0/0
226	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	- -	-		0/0
227	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	- -	-		0/0
228	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-		0/0
229	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	03/2008 03/2009	-		0/0
230	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	03/1998 08/2005	-		0/0
231	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-		0/0
232	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	02/2006 -	-		0/0
233	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-		0/0
234	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	- -	-		0/0
235	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	- -	-		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
236	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	- -	-		0/0
237	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	- -	-		0/0
238	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-		0/0
239	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	03/2011 -	-		0/0
240	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	- -	-		0/0
241	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-		0/0
242	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	-		0/0
243	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 -	-		0/0
244	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	- 03/2011	-		0/0
245	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	06/2004 04/2005	-		0/0
246	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-		0/0
247	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	-		0/0
248	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	- 12/2010	-		0/0
249	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	-		0/0
250	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	12/2006 08/2010	-		0/0
251	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	- 02/2011	-		0/0
252	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	-		0/0
253	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	- -	-		0/0
254	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	- 03/2011	-		0/0
255	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	- -	-		0/0
256	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	- -	-		0/0
257	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	-		0/0
258	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	- 03/2011	-		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
259	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR, Assam	09/2006	200.00	-	-		0/0
260	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER, West Bengal	04/2007	245.15	12/2010	-		0/0
261	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68	-	-		0/0
	Total		61,606.14				0/0
	Road Transport & Highways						
262	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	10/2011	10/2011		0/0
263	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	08/2004	12/2011		0/0
264	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	08/2004	12/2011		0/0
265	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	03/2005	12/2011		0/0
266	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00	03/2005	12/2011		0/0
267	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00	09/2007	12/2011		0/0
268	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	09/2007	12/2011		0/0
269	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78	11/2007	12/2011		0/0
270	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	06/2005	12/2011		0/0
271	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K	12/2003	193.09	03/2008	12/2011		0/0
272	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27	03/2008	12/2011		0/0
273	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00	10/2008	12/2011		0/0
274	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	01/2009	12/2011		0/0
275	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI, Tamil Nadu	03/2005	629.00	11/2010	12/2011		0/0
276	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	02/2009	12/2011		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
277	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2011		0/0
278	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	12/2011		0/0
279	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00 -	12/2008 -	12/2011		0/0
280	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	12/2008 -	12/2011		0/0
281	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2011		0/0
282	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	12/2011		0/0
283	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00 -	11/2008 -	12/2011		0/0
284	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	10/2008 -	12/2011		0/0
285	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	10/2008 -	12/2011		0/0
286	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	12/2011		0/0
287	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2011		0/0
288	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00 -	06/2009 -	12/2011		0/0
289	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 -	06/2008 -	12/2011		0/0
290	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	12/2011		0/0
291	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	12/2011		0/0
292	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	06/2008 -	12/2011		0/0
293	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2011		0/0
294	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	05/2008 -	12/2011		0/0
295	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2011		0/0
296	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	12/2011		0/0
297	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24 -	10/2009 -	12/2011		0/0
298	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04 -	03/2010 -	12/2011		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
299	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09	09/2009	12/2011		0/0
300	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00	07/2010	12/2011		0/0
301	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00	07/2010	12/2011		0/0
302	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	07/2010	12/2011		0/0
303	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	05/2010	12/2011		0/0
304	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	02/2004	12/2011		0/0
305	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	08/2010	12/2011		0/0
306	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	01/2011	12/2011		0/0
307	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	05/2010	12/2011		0/0
308	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	08/2011	12/2011		0/0
309	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	11/2008	01/2012		0/0
310	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	12/2008	01/2012		0/0
311	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	09/2009	02/2012		0/0
312	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	02/2012	02/2012		0/0
313	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	09/2007	03/2012		0/0
314	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	04/2004	03/2012		0/0
315	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	10/2008	03/2012		0/0
316	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	03/2008	03/2012		0/0
317	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	06/2008	03/2012		0/0
318	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94	09/2008	03/2012		0/0
319	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	10/2008	03/2012		0/0
320	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96	04/2008	03/2012		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
321	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16	04/2008	03/2012		0/0
322	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	02/2004	03/2012		0/0
323	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	04/2010	03/2012		0/0
324	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	07/2010	03/2012		0/0
325	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	01/2011	03/2012		0/0
326	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	02/2010	05/2012		0/0
327	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	05/2012	05/2012		0/0
328	Kishangarh-Ajmer-Beawer - [N24000128]NHAI, Rajasthan	11/2009	795.00	05/2012	05/2012		0/0
329	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	05/2012	05/2012		0/0
330	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, Uttar Pradesh	12/2003	155.00	09/2008	06/2012		0/0
331	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00	10/2008	06/2012		0/0
332	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	10/2009	06/2012		0/0
333	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	12/2009	06/2012		0/0
334	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI, Multi State	12/2003	232.45	09/2010	06/2012		0/0
335	MP/Maharashtra Border-Dhula - [N24000126]NHAI, Maharashtra	12/2009	835.00	06/2012	06/2012		0/0
336	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	10/2011	06/2012		0/0
337	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	11/2011	06/2012		0/0
338	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	07/2012	07/2012		0/0
339	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	05/2008	08/2012		0/0
340	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30	10/2011	08/2012		0/0
341	RAJMARG CHORHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA - [240106305]NHAI, Madhya Pradesh	12/2003	229.91	10/2008	09/2012		0/0
342	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	09/2012	09/2012		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
343	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI, Madhya pradesh	12/2003	407.60 -	06/2010 -	10/2012		0/0
344	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya pradesh	12/2003	263.17 -	09/2009 -	10/2012		0/0
345	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	06/2011 -	10/2012		0/0
346	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	10/2012		0/0
347	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI, Maharashtra	02/2011	193.45 -	11/2012 -	11/2012		0/0
348	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00 -	11/2012 -	11/2012		0/0
349	RAJMARG CHORAH TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012		0/0
350	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	07/2008 -	12/2012		0/0
351	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06 -	12/2012 -	12/2012		0/0
352	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhandd	08/2010	625.07 -	01/2013 -	01/2013		0/0
353	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	02/2013 -	02/2013		0/0
354	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00 -	09/2010 -	03/2013		0/0
355	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00 -	03/2013 -	03/2013		0/0
356	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013		0/0
357	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00 -	03/2013 -	03/2013		0/0
358	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013		0/0
359	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	03/2013		0/0
360	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya pradesh	10/2010	1,175.00 -	04/2013 -	04/2013		0/0
361	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013		0/0
362	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00 -	05/2013 -	05/2013		0/0
363	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	05/2013 -	05/2013		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
364	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	05/2013	05/2013		0/0
365	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	05/2013	05/2013		0/0
366	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	09/2007	06/2013		0/0
367	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	11/2012	06/2013		0/0
368	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	06/2013	06/2013		0/0
369	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	06/2013	06/2013		0/0
370	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	06/2013	06/2013		0/0
371	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00	06/2013	06/2013		0/0
372	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	04/2009	07/2013		0/0
373	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	11/2008	07/2013		0/0
374	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	02/2010	07/2013		0/0
375	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	07/2013	07/2013		0/0
376	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J & K	07/2010	1,813.76	07/2013	07/2013		0/0
377	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	07/2013	07/2013		0/0
378	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	08/2013	08/2013		0/0
379	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	08/2013	08/2013		0/0
380	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013		0/0
381	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00	08/2013	08/2013		0/0
382	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	09/2013	09/2013		0/0
383	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	09/2013	09/2013		0/0
384	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	08/2012	10/2013		0/0
385	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	10/2013	10/2013		0/0
386	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	11/2013	11/2013		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
387	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	11/2013 -	11/2013		0/0
388	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54 -	11/2013 -	11/2013		0/0
389	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2013		0/0
390	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013		0/0
391	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013		0/0
392	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014		0/0
393	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	04/2014		0/0
394	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014		0/0
395	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014		0/0
396	NASHRI CHANANI - [N24000162]NHAI,J & K	06/2010	2,159.00 -	06/2015 -	06/2015		0/0
397	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J & K	07/2010	1,987.00 -	07/2015 -	07/2015		0/0
	Total		75,509.76 -				0/0
Shipping & Ports							
398	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 -	04/2009 -	02/2011		0/0
399	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00 -	12/2010 -	06/2011		0/0
400	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25 -	06/2006 09/2011	09/2011		0/0
401	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50 -	09/2011 -	09/2011		0/0
402	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	12/2005 01/2008	10/2011		0/0
403	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 06/2011	11/2011		0/0
404	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	06/2011 01/2012	01/2012		0/0
405	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	03/2012 -	03/2012		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
406	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	01/2012 -	03/2012		0/0
407	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012		0/0
408	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	12/2011 05/2012	05/2012		0/0
409	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	12/2010 -	09/2012		0/0
410	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 -	09/2012		0/0
411	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012		0/0
412	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 -	12/2012		0/0
413	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	03/2013		0/0
414	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013		0/0
415	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	01/2009 -	05/2013		0/0
416	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	03/2006 -	12/2013		0/0
417	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 -	12/2013		0/0
418	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014		0/0
419	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	10/2008 -	-		0/0
420	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	12/2007 01/2009	-		0/0
421	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	08/2010 -	-		0/0
422	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 -	-		0/0
	Total		18,052.23 -				0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
<u>Telecommunications</u>							
423	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	09/2009 -	02/2010		0/0
424	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	10/2010		0/0
425	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	03/2009 -	02/2011		0/0
426	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	02/2011		0/0
427	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	03/2009 -	02/2011		0/0
428	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49 -	12/2008 -	03/2011		0/0
429	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	03/2009 -	03/2011		0/0
430	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49 -	09/2009 -	03/2011		0/0
431	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011		0/0
432	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33 -	02/2009 -	03/2011		0/0
433	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	10/2009 -	03/2011		0/0
434	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 -	08/2011		0/0
435	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 -	08/2011		0/0
436	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	09/2011 -	09/2011		0/0
437	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	12/2005 -	12/2011		0/0
438	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	12/2011		0/0
439	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2011		0/0
440	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	10/2008 -	12/2011		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
441	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	08/2009 -	12/2011		0/0
442	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 -	12/2011		0/0
443	GSM equipment of 1500000Lines (2G) 264700lines 3(G - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	01/2010 -	12/2011		0/0
444	GSM equipment of 1900000Lines (2G) 335500lines 3(G - [N26000094]BSNL,Kerala	01/2009	848.70 -	01/2010 -	12/2011		0/0
445	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19 -	01/2010 -	12/2011		0/0
446	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	07/2012		0/0
447	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-		0/0
448	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	-	-		0/0
449	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-		0/0
450	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	03/2009 -	-		0/0
451	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	03/2009 -	-		0/0
452	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	03/2010 -	-		0/0
453	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	03/2010 -	-		0/0
454	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	03/2010 -	-		0/0
455	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	03/2010 -	-		0/0
456	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-		0/0
457	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	03/2010 -	-		0/0
458	GSM equipment of 975000Lines (2G) 325000 lines 3(G - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53 -	02/2010 -	-		0/0
459	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75 -	09/2010 -	-		0/0
460	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	06/2009 -	-		0/0

List of Projects Without Milestones

S.No	Project	Date of Approval	Original / Revised Cost	DOC Original / Revised	DOC Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	7	8	9	10
461	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	-		0/0
	Total		18,952.93 -				0/0
Urban Development							
462	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014		0/0
463	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016		0/0
464	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-		0/0
	Total		37,850.18 -				0/0
Water Resources							
465	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012		0/0
	Total		542.90 -				0/0
Grand Total			421,099.16				0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
