

**324th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 Crores and above)
October, 2012**



Paradip Refinery Project



**Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in**

Contents

Executive Summary in Hindi	1 -5
Executive Summary in English	6-11
Month wise list of completed projects Costing Rs. 1000 Crore and Above During 2010-11	2-14
Summary of Projects	15-28
Trend and Graphical Analysis of Projects	29-41
Sector wise analysis of projects	42-42
List of All Ongoing Projects	43-70
Sector wise Graph	71-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-95
List of Projects with out date of Commissioning	96-100
List of On schedule Projects	101-109
List of Projects without Milestones	110-127
List of Delayed Projects w.r.t Original and Revised	128-148
List of Projects Having cost overrun w.r.t original	149-158
List of Projects Having cost and time overrun w.r.t original	159-163
Abbreviations	164-165

कार्यकारी सारांश

अक्टूबर, 2012 की फ्लैश रिपोर्ट में 150 करोड़ रुपए और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 563 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अक्टूबर, 2012 के दौरान सड़क परिवहन तथा राजमार्ग की 2 परियोजनाओं के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 563 परियोजनाओं में से 260 परियोजनाओं में नवीनतम समय-सारणी की तुलना में विलंब हुआ तथा 49 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 49 परियोजनाओं में से, 19 परियोजनाएं 1000 करोड़ रु. और अधिक लागत वाली बड़ी परियोजनाएं हैं। सड़क परिवहन और राजमार्ग, नागर विमानन, पोत परिवहन तथा पत्तन, रेलवे, विद्युत, पेट्रोलियम, इस्पात तथा दूरसंचार क्षेत्रों से संबंधित परियोजनाओं के संबंध में 1 से 23 महीनों तक का अतिरिक्त विलंब हुआ है।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	127	38	5	1
2.	सड़क परिवहन एवं राजमार्ग	146	85	12	3
3.	विद्युत	98	49	13	10
4.	पेट्रोलियम	69	34	7	4
5.	कोयला	51	20	0	0
6.	दूरसंचार	13	8	5	0
7.	पोत परिवहन एवं पत्तन	19	6	2	0
8.	इस्पात	17	10	4	0
9.	उर्वरक	6	3	0	0
10.	नागर विमानन	6	2	1	1
11.	परमाणु ऊर्जा	5	3	0	0
12.	शहरी विकास	4	1	0	0
13.	जल संसाधन	1	1	0	0
14.	पेट्रोरसायन	1	0	0	0
कुल		563	260	49	19

3. 563 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग 7,90,096.46 करोड़ रुपए थी तथा उनके पूरा होने की अनुमानित लागत 9,23,916.38 करोड़ रुपए होने की संभावना है जो 1,33,819.92 करोड़ रुपए (मूल लागत का 16.90%) की समग्र लागत वृद्धि को दर्शाता है। अक्टूबर, 2012 तक इन परियोजनाओं पर वहन किया गया व्यय 4,24,502.42 करोड़ रुपए है जो परियोजनाओं की अनुमानित लागत का 45.9% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.10.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	एजेंसी	अनुमोदन की तारीख	परियोजना की लागत (रु. करोड़)			लागत-वृद्धि (% में)
					मूल	संशोधित	अनुमानित	
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	एनआर	03/1981	37.68	450	730	1837.37
2	गाजोले-ईटाहार सहित इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	एनईएफआर	04/1983	36.8	274.41	703.17	1810.79
3	हावड़ा-आमता-चेपादंगा एनएल (एसईआर)	रेलवे	एसईआर	04/1974	31.42	393.46	499.16	1488.67
4	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	एसईआर	03/1998	111.9	1028.05	1412.74	1162.5
5	रूपसा-बांगरीपोसी (जीसी) (एसईआर)	रेलवे	एसईआर	02/1996	57.94	604.04	639.97	1004.54

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. 563 परियोजनाओं में से, 4 परियोजनाएं समय से पहले चल रही हैं, 222 समय पर तथा 260 परियोजनाएं नवीनतम समय-सारणी की तुलना में विलंबित हैं। तथापि, विलंबित परियोजनाओं की संख्या 272 तक और बढ़ जाती है यदि समापन की मूल समय-सारणी के आधार पर गणना की जाती है। इसके अलावा, 37 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 40 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनुमानित रूप से पूरा होने का समय सूचित किया

गया है । 260 विलंबित परियोजनाओं में से, 79 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ, 55 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ, 95 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 31 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.10.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	एजेंसी	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
					मूल	अनुमानित	
1	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	एफओआईएस	03/1984	03/1995	03/2013	216
2	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	एनआर	03/1995	03/2001	12/2017	201
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	एसईआर	03/1998	03/2005	06/2016	135
4	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	एसईआर	03/1984	06/2005	06/2016	132
5	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	ईसीओआर	04/1993	03/2002	01/2013	130

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की समीक्षा करेंगे ।

5. विभिन्न परियोजना कार्यान्वयनकर्ता एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण, नगरपालिका की अनुमति में विलंब/खराब मौसम/दुष्कर क्षेत्रों के कारण सामग्री ले जाने में विलंब, दूरस्थ क्षेत्रों में सुरक्षा संबंधी मामले, बार-बार हड़ताल, नक्सलवादी गतिविधियां, उपयुक्त स्थलों की अनुपलब्धता, मेसर्स बीएचईएल द्वारा सामग्री की आपूर्ति में विलंब, कार्य प्रदान करने में देरी, सिविल कार्यों में विलंब/कार्य की धीमी गति, परामर्शदाता की नियुक्ति में विलंब, निधि का व्यवरोध, कानून और व्यवस्था की समस्या आदि शामिल हैं ।

6. मंत्रालय की ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। पहले शुरू की गई 5 परियोजनाओं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दिए गए हैं:-

बिना लक्ष्यों वाली पहली 5 परियोजनाओं की सूची (31.10.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	एजेंसी	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)	शुरू करने की तारीख		लक्ष्य
					मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	एसईआर	अप्रै-74	31.42	499.16	169.68	03/2007	03/2015	0
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	(एनआर)	मार्च-81	37.68	730	352.01	07/2012	उ.न.	0
3	इकलाखी से बलूरघाट तक नई बी जी लाइन रेलवे लाइन (एनएल) एनईएफआर	रेलवे	एनईएफ आर	अप्रै-83	36.8	703.17	242.39	उ.न.	03/2015	0
4	फ्रेट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	एफओआई एस	मार्च-84	520	634.13	555.27	03/1995	03/2013	0
5	तामलुक दीघा, लाइन का दोहरीकरण (एसईआर)	रेलवे	एसईआर	मार्च-84	293.97	1086.41	427.98	06/2005	06/2016	0

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

7. यह पाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं। पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.10.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	एजेंसी	अनुमोदन की तारीख	परियोजना की लागत (करोड़ रु.)		संचयी व्यय (करोड़ रु.)
					मूल	अनुमानित	
1	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	रेलवे	एनसीआर	04/1985	158.77	432.46	558.07
2	लांझीगढ़-जूनागढ़ एनएल (ईसीओआर)	रेलवे	ईसीओआर	04/1993	100.00	142.98	205.16
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	सीआर	06/1994	120.90	284.27	538.10
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	एससीआर	12/1994	124.43	495.68	590.02
5	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	एनआर	03/1995	2500.00	2500.00	8521.82

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/को प्रदान नहीं करा रही हैं, नीचे दिए गए हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.10.2012 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	एजेंसी	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
					मूल	संशोधित	अनुमानित
1	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	एनआर	03/1981	07/2012	उ.न.	उ.न.
2	ललितपुर-सतना-रीवा-सिंगरुली एनएल, (एनसीआर)	रेलवे	एनसीआर	04/1985	03/1994	उ.न.	12/2011
3	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	डब्ल्यूआर	04/1990	उ.न.	03/2010	उ.न.
4	अमरावती-नरखेर एनएल (सीआर)	रेलवे	सीआर	06/1994	06/1999	03/2011	03/2011
5	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	एससीआर	12/1994	उ.न.	उ.न.	03/2012

टिप्पणी: परियोजना कार्यान्वयनकर्ता एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

8. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है :-

(i) दूरसंचार क्षेत्र में, 13 परियोजनाओं में से 8 परियोजनाएं विलंबित हैं । माह के दौरान 5 परियोजनाओं के संबंध में प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । 390-के लाइन (2जी) तथा 130-के लाइन (3जी) बीएसएनएल के जीएसएम उपस्कर, 283000 लाइन (2जी) 75000 लाइन, बीएसएनएल के जीएसएम उपस्कर, असम टेलीकॉम सर्किल, चरण-VI, 2 जी तथा 3जी, बीएसएनएल, 799000 लाइन (2जी) 101000 लाइन 3 (जी), बीएसएनएल के जीएसएम उपस्कर एवं टर्न कुंजी आधार पर बीएसएनएल में ईआरपी कार्यान्वयन, बीएसएनएल परियोजनाओं के संबंध में नगरपालिका की अनुमति, खराब मौसम/दुष्कर क्षेत्रों की वजह से परिवहन में विलंब, दूरस्थ क्षेत्र में सुरक्षा संबंधी मामलों, बार-बार हड़तालों, लक्सलवाद प्रभावित क्षेत्र तथा उपयुक्त स्थलों की अनुपलब्धता एवं सुरक्षा स्टैक तथा यूपीएस के लिए एचसीएल का एपीओ को स्वीकार न करने के कारण प्रत्येक में 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(ii) **पोत परिवहन तथा पत्तन क्षेत्र** में, 19 परियोजनाओं में से 6 परियोजनाएं विलंबित हैं। माह के दौरान, 2 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '80655 डी डब्ल्यू टी पानामैक्स बल्क सीए' पोत परिवहन के 4 अधिग्रहण तथा '3060 डी डब्ल्यू टी, पोत परिवहन के दो अधिग्रहण' परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना दी गई है। तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई सुस्पष्ट कारण सूचित नहीं किया गया है।

(iii) **नागर विमानन क्षेत्र** में, 6 परियोजनाओं में से 2 परियोजनाएं विलंबित हैं। माह के दौरान 'सी/ओ एकीकृत यात्री टर्मिनल विल्डिंग, एन.एस.सी बी आई विमानन पत्तन, ए ए आई' परियोजना जो एक बड़ी परियोजना है, के संबंध में विभिन्न पैकेजों के प्रदान न किए जाने के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(iv) **पेट्रोलियम क्षेत्र** में, 69 परियोजनाओं में से 34 परियोजनाएं विलंबित हैं। माह के दौरान, 7 परियोजनाओं के संबंध में 1-5 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 4 बड़ी परियोजनाएं हैं। 4 परियोजनाओं के संबंध में प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'पॉलीप्रोपाइलिन यूनिट मेंगलोर रिफाइनरी' के संबंध में सिविल कार्यों की धीमी गति के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 'एमपीआरएल चरण-III विस्तार मेंगलोर रिफाइनरी' के परियोजना के संबंध में परियोजना-विस्थापित परिवारों को हटाने के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, तथा वीकेपीएल उन्नयन एवं स्पुरलाइन बिछाने (भीलवाड़ा तथा सीएचआई), जीएआईएल के संबंध में भूमि के अधिग्रहण में विलंब के कारण 5 माह के विलंब की सूचना प्राप्त हुई है।

(V) **विद्युत क्षेत्र** में, 98 परियोजनाओं में से 49 परियोजनाएं विलंबित हैं। माह के दौरान 13 परियोजनाओं के संबंध में 1-15 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, इनमें से 10 परियोजनाएं बड़ी परियोजनाएं हैं। 1 परियोजना के संबंध में क्रमशः प्रत्येक में 1 माह तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 4 परियोजनाओं के संबंध में प्रत्येक में 2 माह के विलंब की सूचना प्राप्त हुई है तथा 2 परियोजनाओं के संबंध में प्रत्येक में 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'बोंगाइगांव ताप विद्युत परियोजना, एनटीपीसी' तथा 'तपोवन-विष्णुगढ़ एचईपी (4X130 मे.वा.), एनटीपीसी' परियोजना के संबंध में मुख्य सिविल एजेंसी के खराब कार्य निष्पादन के कारण क्रमशः 7 तथा 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है। बीएआरएच एसटीपीपी चरण-II, एनटीपीसी' के संबंध में बीएचईएल द्वारा आपूर्ति में विलंब के कारण 8 माह अतिरिक्त विलंब की सूचना प्राप्त हुई है। 'कोल्डम एचईपी, एनटीपीसी' के संबंध में मुख्य बांध में रिसाव के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है एवं 'बीएआरएच एसटीपीसी' चरण-I (3X660 मे.वा.) एनटीपीसी के संबंध में बायलर और टारबाइन की आपूर्ति में विलंब के कारण 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

(VI) **इस्पात क्षेत्र** में, 17 परियोजनाओं में से 10 परियोजनाएं विलंबित हैं। माह के दौरान 4 परियोजनाओं के संबंध में 1-6 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है। '67.5 एमडब्ल्यूटी जी -5 सहायक

प्रणाली आपात विद्युत मांग, आरआईएनएल' तथा '330 टीपीएच बॉयलर 6 और सहायक प्रणाली, आरआईएनए परियोजना के संबंध में मेसर्स बीएचईल द्वारा विलंबित पैकेजों तथा शेष सामग्री की आपूर्ति में देरी के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । ' 'आरएमएचपी में लौह अयस्क भण्डारण के संवर्धन, आरआईएनएल के संबंध में परामर्शदाता की नियुक्ति में देरी के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । ' 7.0 एमटीपीए कुमार स्वामी लौह अयस्क खान परियोजना एनएमडीसी के संबंध में 6 माह के विलंब की सूचना प्राप्त हुई है । तथापि, इस परियोजना में विलंब के लिए परियोजना प्राधिकारियों द्वारा किसी विशेष कारणों की सूचना नहीं दी गई है ।

(vi) रेलवे क्षेत्र में, 127 परियोजनाओं में से 38 परियोजनाएं विलंबित हैं। माह के दौरान 5 परियोजनाओं के संबंध में 3-21 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 1 बड़ी परियोजना है। 'कादुर-चिकमगलूर- सकलेशपुर (एनएल) एसडब्ल्यूआर', प्रतिस्थापन ने नया रेल पुल 'वनडेल-नेहाटी, ईआर' तथा 'तिन्पहार-साहिबगंज ईआर' परियोजनाओं के संबंधमें धीमी प्रगति के कारण क्रमशः 5,7, तथा 11 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है तथा 'कोतूर-हरिहर (एनएल), एसडब्ल्यूआर' परियोजना के संबंध में निधि व्यवरोध तथा कानून और व्यवस्था की समस्या के कारण 21 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

(vii) सड़क परिवहन एवं राजमार्ग क्षेत्र में, 146 परियोजनाओं में से 85 परियोजनाएं विलंबित हैं । माह के दौरान 12 परियोजनाओं के संबंध में 1-23 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें 3 परियोजनाएं बड़ी परियोजनाएं हैं । 7 परियोजनाओं के संबंध में प्रत्येक में एक माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, 3 परियोजनाओं के संबंध में प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । मध्य प्रदेश/महाराष्ट्र सीमा से नागपुर तक चार लेन बनाना, भारतीय राष्ट्रीय राजमार्ग प्राधिकरण (एनएचएआई) तथा लखनादोन से मध्यप्रदेश/महाराष्ट्र सीमा, 596.75-653 किमी. (एनएस-1/बीओटी/एमपी-2), एनएच-7, एनएचएआई परियोजनाओं के संबंध में क्रमशः 14 तथा 23 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना कार्यान्वयनकर्ता एजेंसी ने इन परियोजनाओं के विलंब के लिए किसी विशेष कारण का उल्लेख नहीं किया है । तथापि, इन परियोजनाओं में विलंब के कारण भूमि अधिग्रहण, वन तथा पर्यावरण अनुमति में विलंब, जनसुविधा स्थानांतरित करने की समस्या, ठेकेदार का खराब कार्य निष्पादन आदि है ।

9. दिनांक 31.10.2012 की स्थिति के अनुसार, विभिन्न क्षेत्रों में 150 करोड़ रुपए तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है ।

10. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है ।

EXECUTIVE SUMMARY

1. The Flash Report for October 2012 contains information on the status of the 563 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During October 2012, 2 projects of Road Transport & Highways have reported completion.

2. During the reference month, out of 563 projects, 260 projects are delayed w.r.t latest schedule and 49 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 49 projects, 19 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 23 months, in respect of projects relating to Road Transport & Highways, Civil Aviation, Shipping & Ports, Railways, Power, Petroleum, Steel and Telecommunication Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest Schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	127	38	5	1
2.	ROAD TRANSPORT & HIGHWAYS	146	85	12	3
3.	POWER	98	49	13	10
4.	PETROLEUM	69	34	7	4
5.	COAL	51	20	0	0
6.	TELECOMMUNICATION	13	8	5	0
7.	SHIPPING & PORTS	19	6	2	0
8.	STEEL	17	10	4	0
9.	FERTILISERS	6	3	0	0
10.	CIVIL AVIATION	6	2	1	1
11.	ATOMIC ENERGY	5	3	0	0
12.	URBAN DEVELOPMENT	4	1	0	0
13.	WATER RESOURCES	1	1	0	0
14.	PETROCHEMICALS	1	0	0	0
Total		563	260	49	19

3. The total original cost of implementation of the 563 projects was about ₹ 7,90,096.46 crore and their anticipated completion cost is likely to be ₹ 9,23,916.38 crore, which reflects an overall cost overrun of ₹ 1,33,819.92 crore (16.90 % of original cost). The expenditure incurred on these projects till October 2012 is ₹ 4,24,502.42 crore, which is 45.9 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUN (as on 31-10-2012)

SN	PROJECT	SECTOR	AGENCY	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUN (in %)
					ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	NR	03/1981	37.68	450	730	1837.37
2	NEW BG LINE RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	NEFR	04/1983	36.8	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	SER	04/1974	31.42	393.46	499.16	1488.67
4	BANKURA - DAMODAR (GC) (SER)	Railways	SER	03/1998	111.9	1028.05	1412.74	1162.5
5	RUPSA-BANGRIPOSI (GC)(SER)	Railways	SER	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. Out of the 563 projects, 4 projects are ahead of schedule, 222 are on schedule and 260 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 272 if delay is calculated on the basis of original schedule of completion. Further, 37 projects have been sanctioned without any commissioning schedule/date and for 40 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 260 delayed projects, 79 projects have overall delay in the range of 1 to 12 months, 55 projects have a delay in the range of 13 to 24 months, 95 projects have a delay in the range of 25 to 60 months and 31 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUN (as on 31-10-2012)

SN	PROJECT	SECTOR	AGENCY	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUN IN MONTHS
					ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	FOIS	03/1984	03/1995	03/2013	216
2	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	(NR)	03/1995	03/2001	12/2017	201
3	BANKURA - DAMODAR (GC) (SER)	Railways	SER	03/1998	03/2005	06/2016	135
4	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	SER	03/1984	06/2005	06/2016	132
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	04/1993	03/2002	01/2013	130

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

5. The brief reasons for time overruns as reported by various project implementing agencies are land acquisition, delay in municipal permission, delay in transportation due to bad weather/difficult terrain, security issue in remote area, frequent strikes, naxal activities, non-availability of suitable sites, delay in supply of material by M/s BHEL, delay in award of work, delay in civil work/slow progress of work, delay in appointment of consultant, fund constraint, law & order problem, etc.

6. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestone are as below:-

List of 5 Earliest Projects without Milestones (as on 31.10.2012)

SN	PROJECT	SECTOR	AGENCY	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONE
					ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	SER	Apr-74	31.42	499.16	169.68	03/2007	03/2015	0
2	NANGALDAM-TALWARA(NL),NR	Railways	(NR)	Mar-81	37.68	730	352.01	07/2012	N.A.	0
3	NEW BG LINE RLY LINE FROM EKLAKHI-BALURGHAT	Railways	NEFR	Apr-83	36.8	703.17	242.39	N.A.	03/2015	0
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	FOIS	Mar-84	520	634.13	555.27	03/1995	03/2013	0
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	SER	Mar-84	293.97	1086.41	427.98	06/2005	06/2016	0

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

7. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:

List of 5 Earliest Projects without Revised Cost Estimates (as on 31.10.2012)

SN	PROJECT	SECTOR	AGENCY	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)
					ORIGINAL	ANTICIPATED	
1	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	NCR	04/1985	158.77	432.46	558.07
2	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	ECOR	04/1993	100.00	142.98	205.16
3	AMRAVATI-NARKHER NL(CR)	Railways	CR	06/1994	120.90	284.27	538.10

4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	12/1994	124.43	495.68	590.02
5	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	NR	03/1995	2500.00	2500.00	8521.82

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:

**List of 5 Earliest Projects without Revised Commissioning Schedule
(as on 31.10.2012)**

SN	PROJECT	SECTOR	AGENCY	DATE OF APPROVAL	DATE OF COMMISSIONING		
					ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	NR	03/1981	07/2012	N.A.	N.A.
2	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	Railways	NCR	04/1985	03/1994	N.A.	12/2011
3	VIRAMGAM-BHILDI(WR),GC	Railways	WR	04/1990	N.A.	03/2010	N.A.
4	AMRAVATI-NARKHER NL(CR)	Railways	CR	06/1994	06/1999	03/2011	03/2011
5	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	SCR	12/1994	N.A.	N.A.	03/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

8. The Sector-wise details of delays/additional delays are as under:-

i) In the **Telecommunications sector**, out of 13 projects, 08 projects are delayed. During the month 5 projects have reported additional delays of 3 months each. The projects GSM Equipment of 390K Lines'(2G) and 130K Lines(3G), BSNL', 'GSM Equipment of 283000 Lines (2G) and 75000 Lines, BSNL', 'Assam Telecom Circle, Phase-V.I, 2G & 3G, BSNL', 'GSM Equipment of 799000 Lines (2G) 101000 Lines 3(G), BSNL' and 'ERP Implementation in BSNL on Turnkey Basis, BSNL' have reported additional delays of 3 months each due to delay in municipal permission, delay in transportation due to bad weather/difficult terrain, security issue in remote area, frequent strikes, naxal-affected area & non-availability of suitable sites and due to HCL

not accepting the APO for security stack and UPS.

ii) In the **Shipping & Ports sector**, out of 19 projects, 6 projects are delayed. During the month 2 projects have reported additional delays of 1 month each. The projects 'Acquisition of 4 Nos. of 80655 DWT Panamax Bulk CA, Shipping' and 'Acquisition of Two nos. of 3060 DWT, Shipping' have reported additional delay of 1 month each. However, no specific reasons have been reported by the project authorities for delay in these projects.

iii) In the **Civil Aviation sector**, out of 6 projects, 2 projects are delayed. During the month the project 'C/O Integrated Passenger Ter. Buld. NSCBI Airport, AAI', a Mega project, has reported additional delay of 5 months due to non-award of various packages.

iv) In the **Petroleum Sector**, out of 69 projects, 34 projects are delayed. During the month 7 projects have reported additional delays in the range of 1-5 months, out of which 4 are Mega Projects. 4 projects have reported additional delays of 1 month each. The project 'Polypropylene unit Mangalore Refinery' has reported additional delay of 2 months due to slow progress of civil works, 'MRPL Phase-III Expansion Mangalore Refinery' has reported additional delay of 4 months due to delay in evacuation of the project displaced family and 'VKPL Upgradation and Laying of Spurline (To Bhilwara and Chi.), GAIL' has reported additional delay of 5 months due to delay in land acquisition.

v) In the **Power Sector**, out of 98 projects, 49 projects are delayed. During the month 13 projects have reported additional delays in the range of 1-15 months, out of which 10 are Mega Projects. 1 project each has reported additional delays of 1 and 3 months respectively, 4 projects have reported additional delay of 2 months each and 2 projects have reported additional delay of 6 months each. The projects 'Bongaigaon Thermal Power Project, NTPC' and 'Tapovan-Vishnugad HEP (4x130MW), NTPC' have reported additional delay of 7 and 15 months respectively due to poor performance of main civil agency, 'Barh STPP Stage-II, NTPC' has reported additional delay of 8 months due to delay in supply by BHEL, 'Koldam HEP, NTPC' has reported additional delay of 12 months due to seepage problem in main Dam and 'BARH STPP STAGE I (3X660MW), NTPC' has reported additional delay of 15 months due to delay in supply of boiler & turbine.

vi) In the **Steel sector**, out of 17 projects, 10 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-6 months. The projects '67.5 MW TG-5 AUX. STEM Emergency Power Requirement, RINL' and '330 TPH Boiler-6 and Auxiliary System, RINL' have reported additional delay of 1 month each due to packages delayed by M/s BHEL and delay in supply of balance materials. 'Augmentation of Iron Ore Storage in RMHP, RINL' has reported additional delay of 4 months due to delay in appointment of consultant. The project '7.0 MTPA Kumaraswamy Iron ORE Mine Project, NMDC' has reported additional delay of 6 months. However, no specific reasons have been reported by the project authorities for delay in this project.

vii) In the **Railways sector**, out of 127 projects, 38 projects are delayed. During the month 5 projects have reported additional delays in the range of 5-21 months, out of which 1 is a Mega Project. The projects 'Kadur-Chikmagalur-Sakleshpur (NL) SWR', 'Bandel-Naihati new rail bridge in replacement, ER' and 'Tinpahar-Sahibganj, ER' have reported additional delay of 5, 7 and 11 months respectively due to slow progress and 'Kottur-Harihar (NL), SWR' has reported additional delay of 21 months due to fund constraint and law & order problem. The project 'Kanpur-Kasganj-Mathura (GC), NER' has reported additional delay of 12 months. However, no specific reasons have been reported by the project authorities for delay in this project.

viii) In the **Road Transport & Highways Sector**, out of 146 projects, 85 are delayed. During the month 12 projects have reported additional delays in the range of 1-23 months, out of which 3 are Mega Projects. 7 projects have reported additional delays of 1 month each, 3 projects have reported additional delays of 2 months each. The projects 'Four Lanning from MP/Maharashtra Border to Nagpur, NHAI' and 'Lakhnaadon to MP/MH Border, KM 596.75-653 (NS-1/BOT/MP-2), NH7, NHAI' have reported additional delays of 14 and 23 months respectively. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, forest & environment clearance, utility shifting problem, poor performance of contractor, etc.

9. The status as on 31.10.2012 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

10. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	146	12
2	Railways	127	5
3	Power	98	13
4	Petroleum	69	7
5	Coal	51	0
6	Shipping & Ports	19	2
7	Steel	17	4
8	Telecommunications	13	5
9	Civil Aviation	6	1
10	Fertilisers	6	0
11	Atomic Energy	5	0
12	Urban Development	4	0
13	Petrochemicals	1	0
14	Water Resources	1	0
	Total	563	49

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April, 2012				
<u>Power</u>				
1	KOTESHWAR HEP (THDC) (TEHRI HYDRO DEVELOPMENT CORPORATION LIMITED) - [180100184]	1,301.56	04/2005	2635.39
2	WESTERN REGION STRENGTHENING SCHEME-X (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000049]	664.96	02/2012	362.1
<u>Road Transport & Highways</u>				
3	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000085]	600.24	10/2009	805.1
4	Bijapur-Hungund Section (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000137]	748.00	-	N.A.
<u>Shipping & Ports</u>				
5	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C (SHIPPING corp. of india) - [N25000033]	1,061.96	03/2012	1284.15
6	ACQUISITION OF TWO NOS OF 120 B.P BY 077 & 078 (AH (SHIPPING corp. of india) - [N25000058]	241.50	09/2011	262.8
<u>Telecommunications</u>				
7	GSM EQUIPMENT OF 700K LINES (2G) AND 150K LINES (3G) (BHARAT SANCHAR NIGAM LIMITED) - [N26000046]	277.34	03/2009	308.13
8	GSM equipment of 1867000 Lines (2G) 383000 lines 3 (BHARAT SANCHAR NIGAM LIMITED) - [N26000089]	868.00	08/2009	558.78
May, 2012				
<u>Fertilisers</u>				
9	THAL AMMONIA REVAMP PROJECT (RASHTRIYA CHEMICAL & FERTILISER LIMITED) - [N08000003]	488.75	04/2012	307.89
<u>Petroleum</u>				
10	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON (BONGAIGAON REFINERY PETROLEUM LIMITED) - [N16000009]	1,431.91	09/2009	1596.8
<u>Power</u>				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
11	MAUDA TRANSMISSION SYSTEM(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000084]	469.38	10/2012	224.6
	<u>Railways</u>			
12	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000034]	230.73	03/2009	328.83
13	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION(RAIL VIKAS NIGAM LTD.) - [N22000081]	200.80	-	323.35
	<u>Road Transport & Highways</u>			
14	HALDIA PORT (PORT CONNECTIVITY) (NH-41)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240104196]	273.00	03/2005	475.55
15	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000103]	441.00	-	958.09
	<u>Shipping & Ports</u>			
16	MARINE LIQUID TERMINALS(ENNORE TANK TERMINAL PVT.LTD.) - [N25000054]	196.25	06/2006	250.77
17	DEVELOPMENT OF COAL TERMINAL(ENNORE PORT LTD.) - [N25000055]	399.13	08/2010	351.08
18	DEVELOPMENT OF IRON ORE TERMINAL(ENNORE PORT LTD.) - [N25000056]	370.00	08/2010	351.61
	June,2012			
	<u>Steel</u>			
19	INSTALLATION OF 700TPD AIR SEPARATION UNIT-4 AT O(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000023]	232.93	05/2011	191.83
	<u>Power</u>			
20	CHAMERA,STAGE-III (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100241]	1,405.63	08/2010	1842.24
21	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100260]	3,779.46	09/2009	N.A.
22	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000082]	215.86	06/2012	179.7
	<u>Railways</u>			
23	MUZAFFARPUR-SITAMARHI(NL),ECR(EAST CENTRAL RAILWAYS) - [220100194]	100.00	03/2012	466.7
24	SRIGANGANAGAR-SARUPSAR (GC), NWR(NORTH WESTERN RAILWAY) - [220100313]	143.92	03/2011	235.37
	<u>Road Transport & Highways</u>			
25	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106292]	227.00	12/2008	383.2

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
26	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHA)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106300] July,2012	225.00	10/2008	261.9
	<u>Power</u>			
27	WESTERN REGION SYSTEM STRENGTHENING SCHEME- XI(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000051]	409.50	02/2012	123.5
	<u>Railways</u>			
28	RAJPIPLA-ANKELASHWAR, WR (GC)(WESTERN RAILWAY) - [N22000096] August,2012	196.97	03/2011	218.66
	<u>Steel</u>			
29	REBUILDING OF COKE OVEN BATTERIES No. 1 & 2 (BOKA(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000033]	500.90	-	355.21
	<u>Power</u>			
30	SIPAT STPP STAGE - I (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100229]	8,323.39	12/2009	8230
31	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000054]	317.69	11/2011	199.5
32	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000067]	196.10	07/2011	139.1
	<u>Road Transport & Highways</u>			
33	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106235] September,2012	193.09	03/2008	189.15
	<u>Petroleum</u>			
34	REVAMPING OF WIN PLATFORM AT MH ASSET(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000044]	333.40	05/2010	680.85
	<u>Telecommunications</u>			
35	PROJ.III OF NIB-II OF MESSAGING STORAGE(BHARAT SANCHAR NIGAM LIMITED) - [260100099]	250.00	12/2005	80.47
36	NIB Project Capacity Expansion(BHARAT SANCHAR NIGAM LIMITED) - [N26000098]	175.52	12/2008	60.84

Month wise List of Completed Project Costing Rs. 150 Crore and above during
2012-2013

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
October,2012				
<u>Road Transport & Highways</u>				
37	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106204]	275.00	09/2007	306.65
38	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106301]	151.30	10/2008	190.61


Summary of projects in the Flash Report for the month of October, 2012

I. Project Implementation - Current Status:

Number of Projects in Previous Month	569
Number of Projects completed/dropped/frozen in Previous Month	3
Number of Projects completed/dropped/frozen in Current Month	2
Number of Projects are not Reported in Current Month	1
Number of Projects in Current Month	563


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 563 projects, 5 projects are ahead of schedule, 170 projects are on schedule and 272 projects are delayed. Of the balance, 85 projects do not have fixed dates of commissioning while 31 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

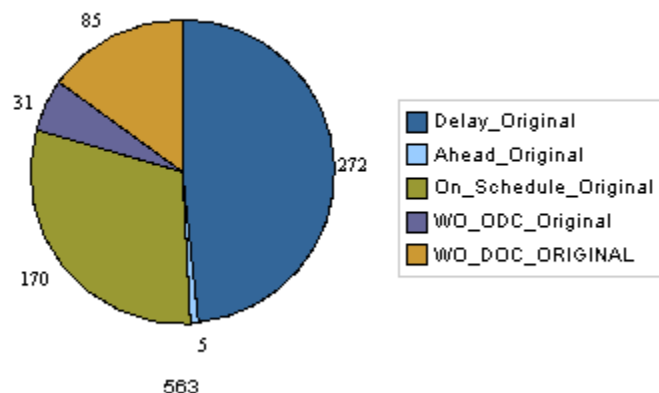

III. Investment Scenario

The Total Original cost of implementation of 563 projects when sanctioned, was of the order of Rs. 790096.46 crore but this was subsequently revised to Rs. 923916.38 crore implying a cost overrun of 16.9%. The expenditure incurred on these projects till October, 2012 is Rs. 425125.55 crore, which is 46% of the revised cost of the projects.

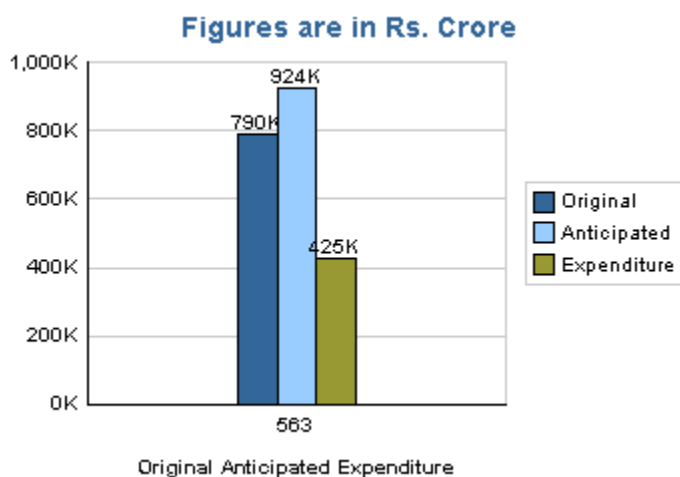

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	569
No of Projects Completed/Dropped/Frozen in Previous Month	3
No of Projects Completed/Dropped/Frozen in Current Month	2
No of Projects not reported in current months	1
No of Projects added in Current Month	0
No of Projects in Current Month	563

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	272	5	170	31	85	563	48.31
Latest Approved (Date)	260	4	222	37	40	563	46.18

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	412	645,173.89	677,122.38	278,883.25	41.20	31,948.49	5.00
Latest Approved (RCE)	151	200,699.69	246,794.00	146,242.30	59.30	46,094.31	23.00
Total (RCE)	563	845,873.58	923,916.38	425,125.55	46.01	78042.8	9.23
Original Cost of All Projects							
Original Cost	563	790,096.46	923,916.38	425,125.55	46.00	133,819.92	16.90

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	272	445,810.95	536,536.62	317,150.62	59.10	90,725.67	20.40
Latest Approved (RCE)	260	407,320.37	462,155.81	271,720.81	58.80	54,835.44	13.50

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost			Cost overrun		
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	50	83,492.51	90,909.72	66,691.85	73.40	7,417.21	8.90

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	3,750.5	4,340.0	15.7
3	Coal	51	36,056.5	37,312.3	3.5	7	8,579.5	10,433.0	21.6
4	Fertilisers	6	5,153.7	5,153.7	0.0	0	0.0	0.0	0.0
5	Steel	17	65,285.9	71,443.4	9.4	6	24,028.9	30,216.4	25.8
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
7	Petroleum	69	174,399.2	182,915.6	4.9	15	51,023.0	67,509.5	32.3
8	Power	98	231,379.5	245,377.2	6.0	18	41,492.2	55,490.7	33.7
9	Railways	127	64,518.7	148,474.8	130.1	107	44,312.9	128,315.6	189.6
10	Road Transport & Highways	146	94,054.5	95,488.7	1.5	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	11	9,532.5	12,151.1	27.5
12	Telecommunications	13	5,735.5	5,676.3	-1.0	2	1,065.9	1,089.3	2.2
13	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		563	790,096.5	923,916.4	16.9	185	216,285.2	359,827.0	66.4

Extent of cost overrun in projects with respect to original schedule(State Wise)

S.No.	State	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Andhra Pradesh	37	31,485.3	38,910.9	23.6	14	12,420.0	20,712.6	66.8
2	Arunachal Pr.	4	9,512.2	14,152.7	48.8	2	6,441.3	11,082.7	72.1
3	Assam	35	22,260.9	33,844.4	52.0	12	10,491.8	22,169.3	111.3
4	Bihar	30	26,901.2	34,657.0	28.8	13	12,343.6	20,099.4	62.8
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	22	31,111.6	31,313.5	0.6	5	2,413.7	2,885.5	19.5
7	Haryana	10	5,496.6	7,438.4	35.3	3	1,448.2	3,390.0	134.1
8	Himachal Pr.	5	13,355.6	15,414.9	15.4	3	6,781.4	8,840.8	30.4
9	J and K	10	14,927.0	34,825.6	133.3	6	7,866.5	27,765.1	253.0
10	Karnataka	24	44,634.8	54,121.3	21.3	9	8,598.8	18,491.8	115.1
11	Kerala	6	19,694.7	21,136.2	7.3	3	4,295.7	5,737.2	33.6
12	Madhya pradesh	24	19,741.9	19,892.0	0.8	3	2,027.6	2,741.5	35.2
13	Maharashtra	54	97,399.5	113,680.2	16.7	18	32,285.0	51,040.2	58.1
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	510.8
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,307.1	115.7	1	619.3	2,393.5	286.5
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	0.0
18	Orissa	30	57,409.1	60,949.0	6.2	12	32,671.6	36,211.5	10.8
19	Punjab	7	4,836.2	5,778.0	19.5	2	532.4	1,474.2	176.9
20	Rajasthan	14	26,544.1	26,138.3	-1.5	3	1,080.0	1,344.9	24.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	14	29,143.5	39,923.4	37.0
23	Tripura	3	1,522.4	2,053.2	34.9	2	1,234.4	1,765.2	43.0
24	Uttar Pradesh	23	18,822.9	22,660.7	20.4	8	3,498.5	7,384.5	111.1
25	West Bengal	27	42,286.1	54,607.6	29.1	16	25,364.5	37,685.9	48.6
26	Delhi	5	38,572.6	38,553.0	-0.1	0	0.0	0.0	0.0
27	Chhatisgarh	24	46,715.2	47,998.3	2.7	6	1,548.3	2,831.4	82.9
28	Jharkhandd	23	14,447.4	18,429.0	27.6	6	1,897.3	6,050.7	218.9
29	Uttaranchal	3	5,619.2	6,559.6	16.7	2	2,640.7	3,581.2	35.6
30	Multi State	102	139,667.0	145,358.2	4.1	20	6,574.0	16,400.0	149.5
Total		563	790,096.5	923,916.4	16.9	185	216,285.2	359,827.0	66.4

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	3	2,587.6	2,970.1	7 - 27
3	Coal	51	36,056.5	37,312.3	3.5	20	17,557.6	19,232.9	16 - 60
4	Fertilisers	6	5,153.7	5,153.7	0.0	0	0.0	0.0	-
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
7	Petroleum	69	174,399.2	182,915.6	4.9	40	110,647.2	120,282.0	1 - 120
8	Power	98	231,379.5	245,377.2	6.0	51	135,624.0	149,008.5	2 - 99
9	Railways	127	64,518.7	148,474.8	130.1	39	25,689.1	68,485.8	1 - 216
10	Road Transport & Highways	146	94,054.5	95,488.7	1.5	86	41,423.1	43,217.3	1 - 106
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	10	9,222.2	10,702.1	1 - 87
12	Telecommunications	13	5,735.5	5,676.3	-1.0	7	2,737.7	2,741.6	25 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		563	790,096.5	923,916.4	16.9	272	445,811.0	536,536.6	

Extent of the time overrun in projects with respect to original schedule(State Wise)

S. No	State	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Andhra Pradesh	37	31,485.3	38,910.9	23.6	14	17,688.1	21,299.3	1 - 41
2	Arunachal Pr.	4	9,512.2	14,152.7	48.8	3	9,356.2	13,737.0	25 - 78
3	Assam	35	22,260.9	33,844.4	52.0	33	21,484.3	32,882.6	12 - 120
4	Bihar	30	26,901.2	34,657.0	28.8	14	20,578.4	26,451.2	2 - 75
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	7 - 7
6	Gujarat	22	31,111.6	31,313.5	0.6	6	15,224.5	15,394.7	6 - 24
7	Haryana	10	5,496.6	7,438.4	35.3	4	2,065.9	3,555.1	9 - 50
8	Himachal Pr.	5	13,355.6	15,414.9	15.4	5	13,355.6	15,414.9	20 - 99
9	J and K	10	14,927.0	34,825.6	133.3	9	13,826.3	33,724.9	10 - 201
10	Karnataka	24	44,634.8	54,121.3	21.3	9	22,364.3	27,349.0	10 - 99
11	Kerala	6	19,694.7	21,136.2	7.3	3	4,674.0	5,324.0	11 - 58
12	Madhya pradesh	24	19,741.9	19,892.0	0.8	13	10,571.4	10,440.9	5 - 60
13	Maharashtra	54	97,399.5	113,680.2	16.7	24	48,186.8	58,950.8	1 - 120
14	Manipur	1	727.6	4,444.0	510.8	1	727.6	4,444.0	60 - 60
15	Meghalaya	2	762.0	762.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,307.1	115.7	2	1,533.0	3,307.1	7 - 11
17	Nagaland	1	850.0	850.0	0.0	0	0.0	0.0	-
18	Orissa	30	57,409.1	60,949.0	6.2	11	33,068.2	34,030.5	9 - 130
19	Punjab	7	4,836.2	5,778.0	19.5	4	1,611.4	2,553.2	1 - 58
20	Rajasthan	14	26,544.1	26,138.3	-1.5	6	19,992.2	19,687.9	3 - 52
21	Sikkim	2	1,648.9	3,690.0	123.8	1	309.5	309.5	27 - 27
22	Tamil Nadu	32	51,276.0	62,055.8	21.0	11	30,528.8	36,459.4	9 - 87
23	Tripura	3	1,522.4	2,053.2	34.9	1	288.0	288.0	7 - 7
24	Uttar Pradesh	23	18,822.9	22,660.7	20.4	11	11,635.1	13,616.4	5 - 93
25	West Bengal	27	42,286.1	54,607.6	29.1	15	27,126.9	33,984.7	3 - 135
26	Delhi	5	38,572.6	38,553.0	-0.1	1	249.0	229.4	72 - 72
27	Chhatisgarh	24	46,715.2	47,998.3	2.7	6	18,545.8	18,857.0	6 - 47
28	Jharkhandd	23	14,447.4	18,429.0	27.6	10	8,748.4	9,833.4	11 - 102
29	Uttaranchal	3	5,619.2	6,559.6	16.7	3	5,619.2	6,559.6	22 - 45
30	Multi State	102	139,667.0	145,358.2	4.1	51	86,116.6	87,516.6	1 - 216
Total		563	790,096.5	923,916.4	16.9	272	445,811.0	536,536.6	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.3	47,832.3	15.1	3	36,950.0	41,049.0	3 - 51
2	Civil Aviation	6	5,473.6	6,063.1	10.8	2	2,278.1	2,660.6	7 - 22
3	Coal	51	36,056.5	37,312.3	3.5	20	17,557.6	19,232.9	16 - 60
4	Fertilisers	6	5,153.7	5,153.7	0.0	3	1,088.0	1,088.0	9 - 23
5	Steel	17	65,285.9	71,443.4	9.4	10	50,973.9	57,131.4	2 - 41
6	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
7	Petroleum	69	174,399.2	182,915.6	4.9	34	70,376.6	73,981.3	0 - 86
8	Power	98	231,379.5	245,377.2	6.0	49	130,485.8	143,545.3	2 - 99
9	Railways	127	64,518.7	148,474.8	130.1	38	17,027.9	56,412.7	0 - 216
10	Road Transport & Highways	146	94,054.5	95,488.7	1.5	85	41,143.1	42,937.3	1 - 106
11	Shipping & Ports	19	16,242.5	18,554.1	14.2	6	7,001.8	8,242.8	11 - 34
12	Telecommunications	13	5,735.5	5,676.3	-1.0	8	3,074.6	3,078.4	17 - 72
13	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	21 - 21
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		563	790,096.5	923,916.4	16.9	260	384,895.3	462,155.8	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	5	41,548.3	47,832.3	15.1	2	16,663.0	22,947.0	37.7
2	Civil Aviation	6	5,680.6	6,063.1	6.7	1	1,942.5	2,325.0	19.7
3	Coal	51	37,022.5	37,312.3	0.8	5	6,336.3	6,626.1	4.6
4	Fertilisers	6	5,153.7	5,153.7	0.0	0	0.0	0.0	0.0
5	Steel	17	67,562.2	71,443.4	5.7	4	9,290.0	13,201.3	42.1
6	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
7	Petroleum	69	187,851.7	182,915.6	-2.6	2	30,533.0	31,324.0	2.6
8	Power	98	235,186.7	245,377.2	4.3	12	34,502.4	44,693.8	29.5
9	Railways	127	94,031.1	148,474.8	57.9	83	50,348.8	105,003.2	108.6
10	Road Transport & Highways	146	94,221.0	95,488.7	1.3	11	3,324.3	5,445.2	63.8
11	Shipping & Ports	19	18,109.6	18,554.1	2.5	8	4,615.6	5,370.0	16.3
12	Telecommunications	13	5,739.4	5,676.3	-1.1	0	0.0	0.0	0.0
13	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
14	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		563	845,873.6	923,916.4	9.2	130	164,493.8	249,731.6	51.8

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	0	0.00	0.00	0- 0
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,808.00	2,015.00	13- 13
3	Coal	51	36,056.46	37,312.25	3.48	0	0.00	0.00	0- 0
4	Fertilisers	6	5,153.66	5,153.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	1	295.89	607.17	13- 13
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	69	174,399.19	182,915.59	4.88	11	20,638.48	35,088.71	24- 120
8	Power	98	231,379.54	245,377.17	6.05	2	2,253.45	3,986.02	0- 73
9	Railways	127	64,518.68	148,474.81	130.13	16	8,942.50	25,057.24	1- 141
10	Road Transport & Highways	146	94,054.50	95,488.69	1.52	0	0.00	0.00	0- 0
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	6	6,013.42	7,487.89	5- 87
12	Telecommunications	13	5,735.48	5,676.27	-1.03	0	0.00	0.00	0- 0
13	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
14	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		563	790096.46	923916.38	16.94	38	45412.35	83162.03	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	5	41,548.29	47,832.29	15.12	1	13,171.00	17,270.00	51- 51
2	Civil Aviation	6	5,473.58	6,063.07	10.77	1	1,942.51	2,325.00	22- 22
3	Coal	51	36,056.46	37,312.25	3.48	4	7,617.44	9,422.79	16- 45
4	Fertilisers	6	5,153.66	5,153.66	0.00	0	0.00	0.00	0- 0
5	Steel	17	65,285.87	71,443.41	9.43	6	24,028.89	30,216.43	2- 41
6	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
7	Petroleum	69	174,399.19	182,915.59	4.88	12	49,217.95	64,390.50	10- 120
8	Power	98	231,379.54	245,377.17	6.05	16	40,474.74	53,860.13	7- 99
9	Railways	127	64,518.68	148,474.81	130.13	31	15,602.29	58,403.81	1- 216
10	Road Transport & Highways	146	94,054.50	95,488.69	1.52	11	3,324.28	5,445.20	21- 104
11	Shipping & Ports	19	16,242.52	18,554.09	14.23	6	7,074.72	8,653.14	5- 87
12	Telecommunications	13	5,735.48	5,676.27	-1.03	2	1,065.85	1,089.32	25- 45
13	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	21- 21
14	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		563	790096.46	923916.38	16.94	93	175918.18	272792.32	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		Final
S.no	Project	DOA	Cost	DOC	Cost	DOC	Expenditure
<u>Road Transport & Highways</u>							
1	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	12/2003	275.00	09/2007	275.00	10/2012	306.65
2	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	12/2003	151.30	10/2008	151.30	10/2012	190.61

VI. List of projects added

(All Cost in Rs. crore)

S.no	Project	DOA	Original		Anticipated	
			Cost	DOC	Cost	DOC

VII. Milestones (Cumulative due & achieved)

Total	3377
Achieved up to month	1190

VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
<u>Civil Aviation</u>							
1							
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT AAI	1,942.51	2,325.00	05/2011	10/2012	03/2013	5
<u>Steel</u>							
3	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREM RINL	230.00	343.58	02/2011	12/2012	01/2013	1
4	330 TPH BOILER-6 AND AUXILIARY SYSTEM RINL	260.00	350.00	08/2010	11/2012	12/2012	1
5	Augmentation of Iron Ore Storage in RMHP RINL	480.00	450.00	05/2012	02/2013	06/2013	4
6	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) NMDC	898.55	898.55	N.A.	05/2013	11/2013	6
<u>Petroleum</u>							
7	CONSTRUCTION OF NEW PROCESS COMPLEX MHN ONGC	2,853.29	6,326.40	05/2010	10/2012	11/2012	1
8	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA ONGC	370.11	370.11	04/2011	10/2012	11/2012	1
9	KARANPUR MORADABAD-KASHIPUR- RUDRAPUR PIPELINE PROJECT PHASE- GAIL	238.68	312.00	01/2012	11/2012	12/2012	1
10	EURO-IV DHDT CPCL	2,615.69	2,615.69	N.A.	10/2012	11/2012	1
11	Polypropylene unit Mangalore Refin	1,803.78	1,803.78	07/2012	04/2013	06/2013	2
12	MRPL Phase-III Expansion Mangalore Refin	12,412.00	12,160.26	01/2012	11/2012	03/2013	4
13	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI GAIL	463.32	330.47	03/2012	10/2012	03/2013	5
<u>Power</u>							
14	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.26	913.00	02/2011	10/2012	11/2012	1
15	TEESTA LOW DAM HEP, STAGE-IV (NHPC) NHPC	1,061.38	1,501.75	09/2009	10/2013	12/2013	2
16	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME PGCIL	7,031.88	7,031.88	12/2012	12/2012	02/2013	2
17	RIHAND STTP STAGE-III (2X500MW) (NTPC) NTPC	6,230.81	6,230.81	10/2012	03/2013	05/2013	2
18	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	10/2012	12/2012	2
19	PARBATI H.E.P. STAGE -III (NHPC) NHPC	2,304.56	2,716.00	10/2010	06/2013	09/2013	3
20	TEHRI PUMPED STORAGE PLANT(1000MW) THDCL	1,657.00	2,978.86	07/2010	02/2016	08/2016	6
21	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP PGCIL	184.19	184.19	11/2011	03/2013	09/2013	6


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
22	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	07/2011	04/2014	11/2014	7
23	BARH STPP STAGE -II NTPC	7,341.04	7,341.04	08/2013	01/2014	09/2014	8
24	KOLDAM HEP (NTPC) NTPC	4,527.15	4,527.15	04/2009	03/2013	03/2014	12
25	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	12/2014	03/2016	15
26	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	2,978.48	03/2013	06/2014	09/2015	15
<u>Railways</u>							
27	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) SWR	157.00	333.50	03/2012	10/2012	03/2013	5
28	Bandel-Naihati new rail bridge in replacement of j ER	207.52	207.52	12/2012	05/2013	12/2013	7
29	Tinpahar - Sahibganj (ER) ER	167.73	167.73	03/2012	03/2012	02/2013	11
30	KANPUR-KASGANJ-MATHURA(GC),NER NER	395.00	1,577.46	N.A.	03/2012	03/2013	12
31	KOTTUR-HARIHAR(NL),(SWR) SWR	65.94	302.23	N.A.	03/2011	12/2012	21
<u>Road Transport & Highways</u>							
32	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) NHAI	241.00	196.65	08/2004	10/2012	11/2012	1
33	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) NHAI	318.00	207.56	08/2004	10/2012	11/2012	1
34	ASSAM/WB BORDER TO GAIRKATTA (WB-1) NHAI	221.82	221.82	11/2008	10/2012	11/2012	1
35	Surat- Dahisar(Six Lane) Km 263 to Km 502 NHAI	1,693.75	1,693.75	08/2011	10/2012	11/2012	1
36	Hyderabad-Vijaywada Km. 40 to 221.50 Km NHAI	1,740.00	1,740.00	10/2012	10/2012	11/2012	1
37	Hyderabad-yadgiri N.H no-202 NHAI	388.00	388.00	05/2012	10/2012	11/2012	1
38	Armur to kadloor yellareddy NHAI	390.56	390.56	02/2012	10/2012	11/2012	1
39	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) NHAI	367.49	367.49	03/2005	10/2012	12/2012	2
40	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 NHAI	220.00	220.00	09/2007	10/2012	12/2012	2
41	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 NHAI	166.27	193.10	03/2008	10/2012	12/2012	2
42	Four Lanning from MP/Maharashtra Border to nagpur NHAI	1,170.52	1,170.52	06/2011	10/2012	12/2013	14
43	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 NHAI	407.60	263.17	06/2010	10/2012	09/2014	23
<u>Shipping & Ports</u>							
44	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA SHIPP.	1,066.91	968.35	09/2012	09/2012	10/2012	1
45	Acquisition of Two nos. of 3060 DWT SHIPP.	277.03	277.03	12/2011	09/2012	10/2012	1
<u>Telecommunications</u>							


VIII. List of projects reporting additional delays

S.no	Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
46	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) BSNL	373.94	373.94	12/2008	12/2012	03/2013	3
47	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES BSNL	149.15	158.72	06/2009	12/2012	03/2013	3
48	Assam Telecom Circle, Phase-V.I, 2G & 3G BSNL	336.81	336.81	01/2009	03/2013	06/2013	3
49	GSM equipment of 799000Lines (2G) 101000 lines 3(G BSNL	328.13	328.12	03/2009	12/2012	03/2013	3
50	ERP implementation in BSNL on Turnkey basis BSNL	384.00	384.00	10/2010	03/2013	06/2013	3

Trend and Graphical Analysis of All Projects

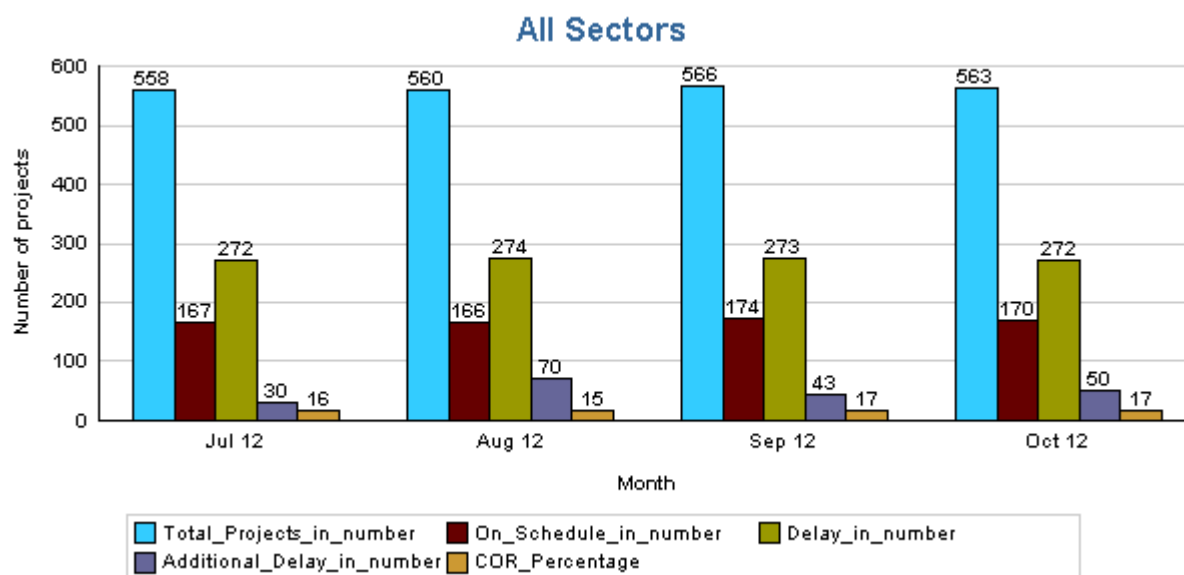


All Sectors Break-up of 272 Delayed projects in October 2012

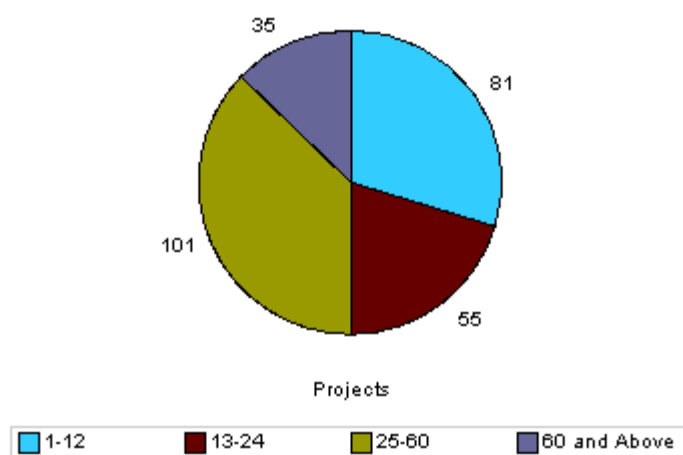


Trend and Graphical Analysis

Urban Development Sector

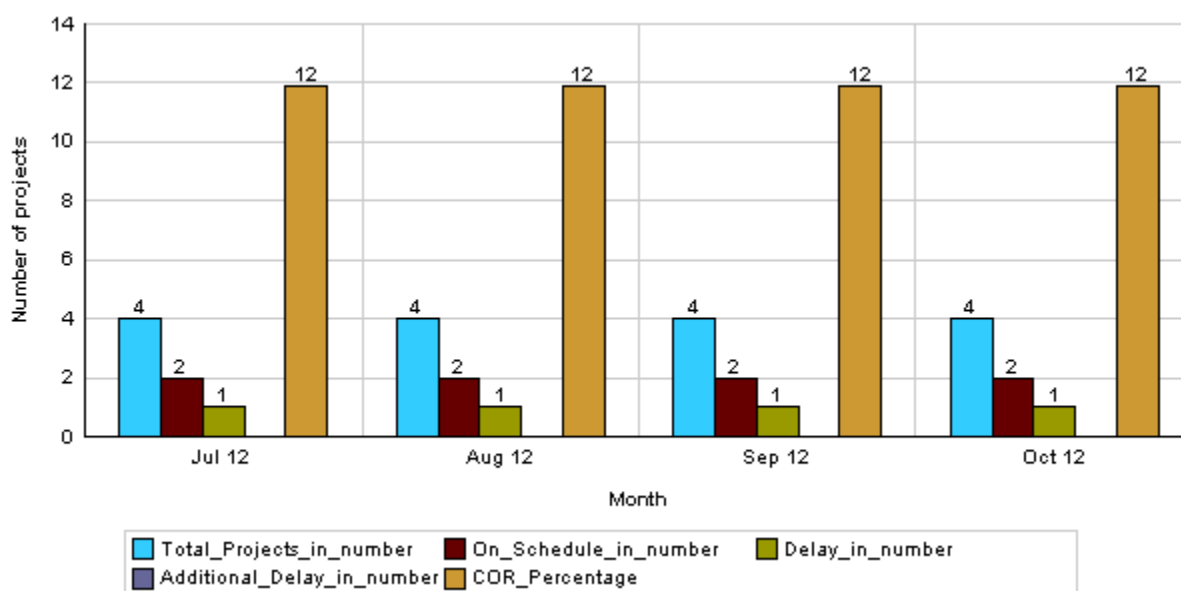


Urban Development Sector Break-up of 1 Delayed projects in October 2012

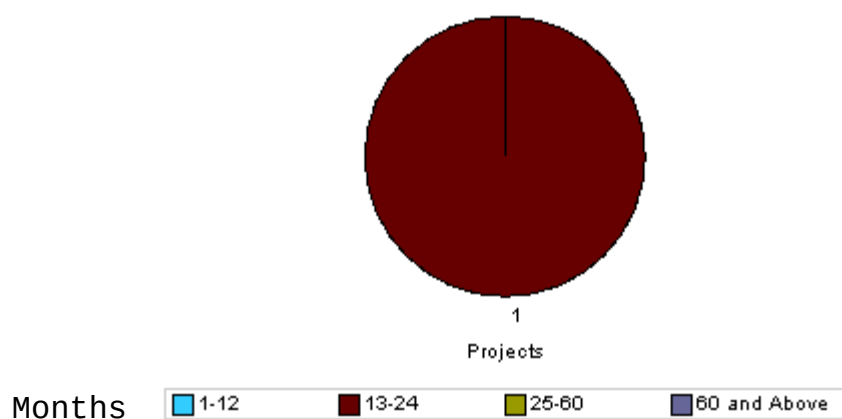


Trend and Graphical Analysis


Telecommunications Sector

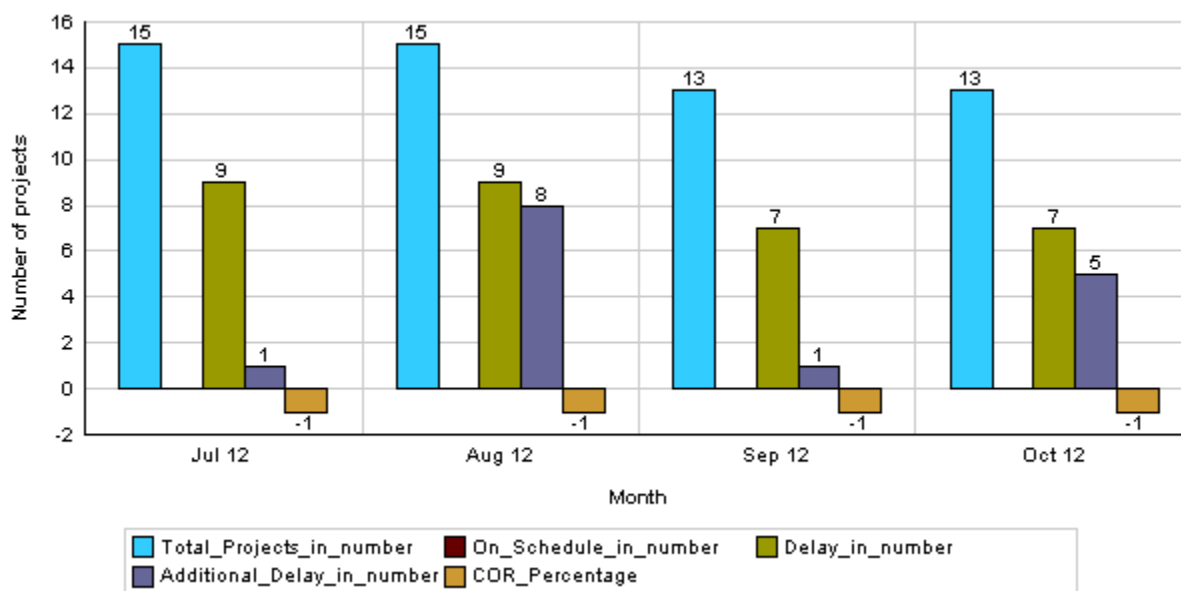


Telecommunications Sector Break-up of 7 Delayed projects in October 2012

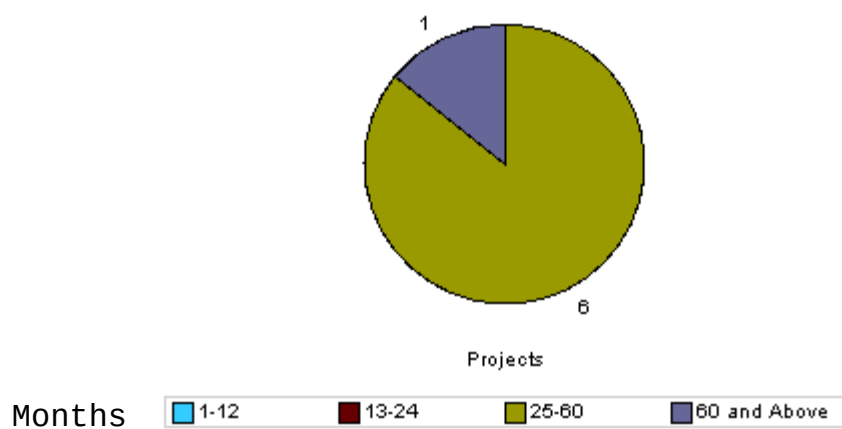


Trend and Graphical Analysis Shipping and Ports Sector

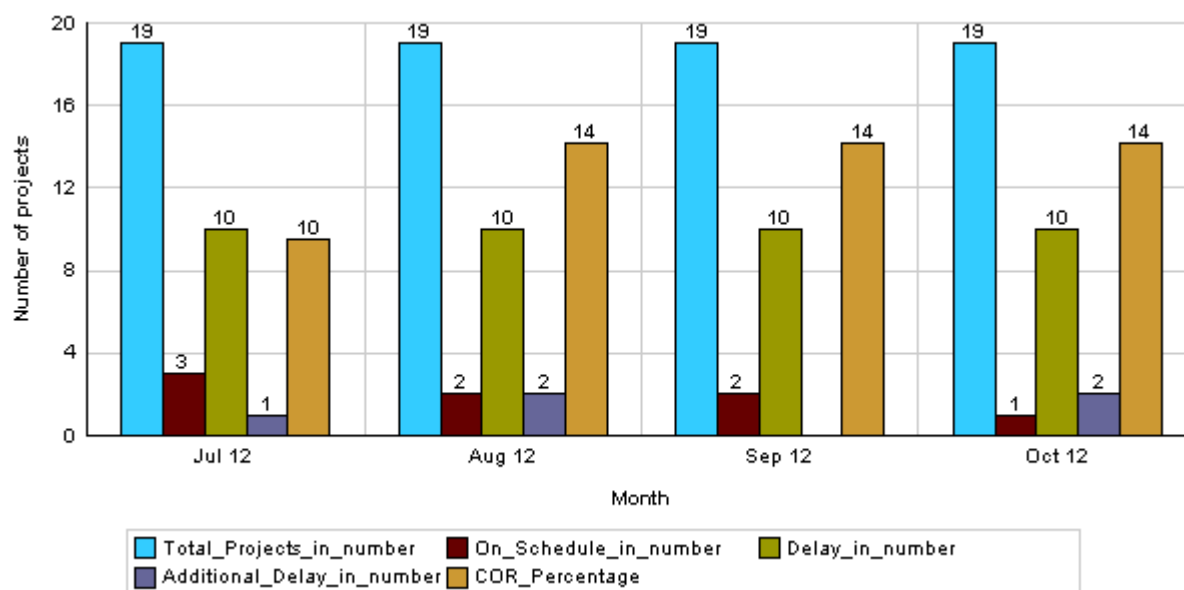


Sector Break-up of 10 Delayed projects in October 2012

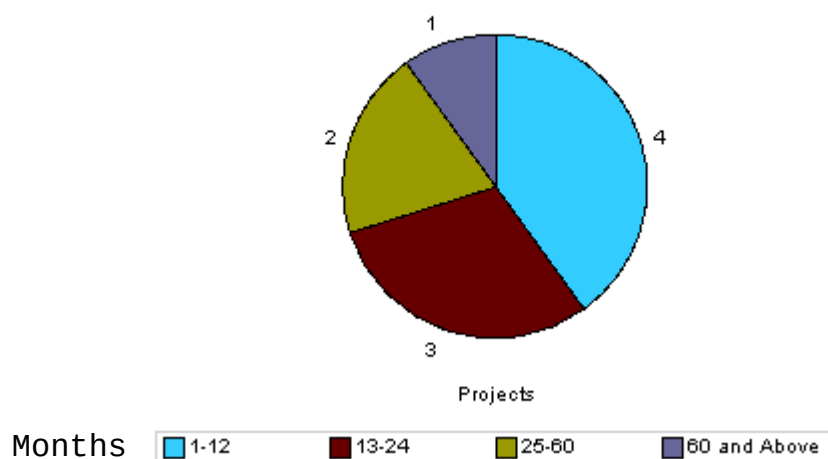

Trend and Graphical Analysis Road Transport and Highways Sector

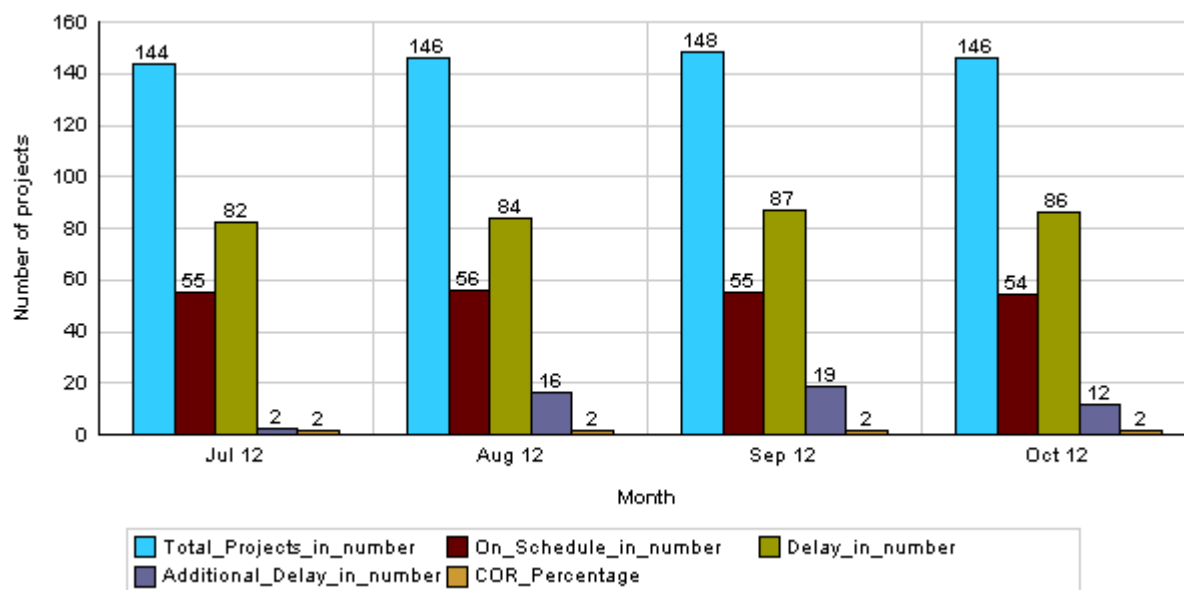


Sector Break-up of 86 Delayed projects in October 2012

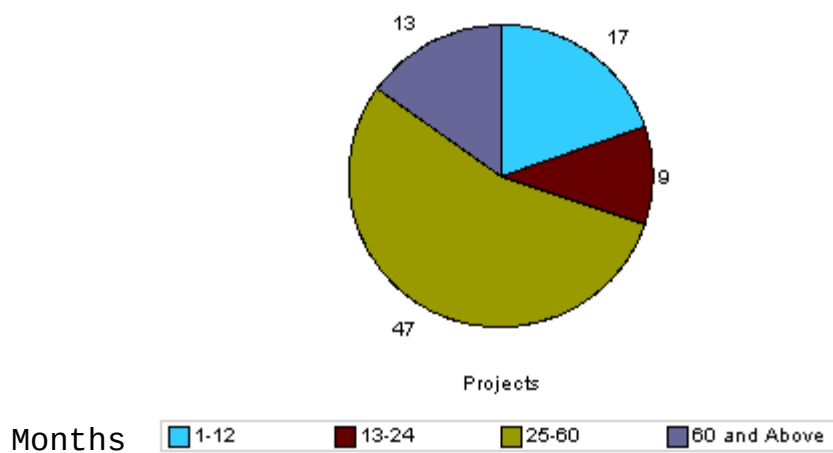


Trend and Graphical Analysis

Railways Sector

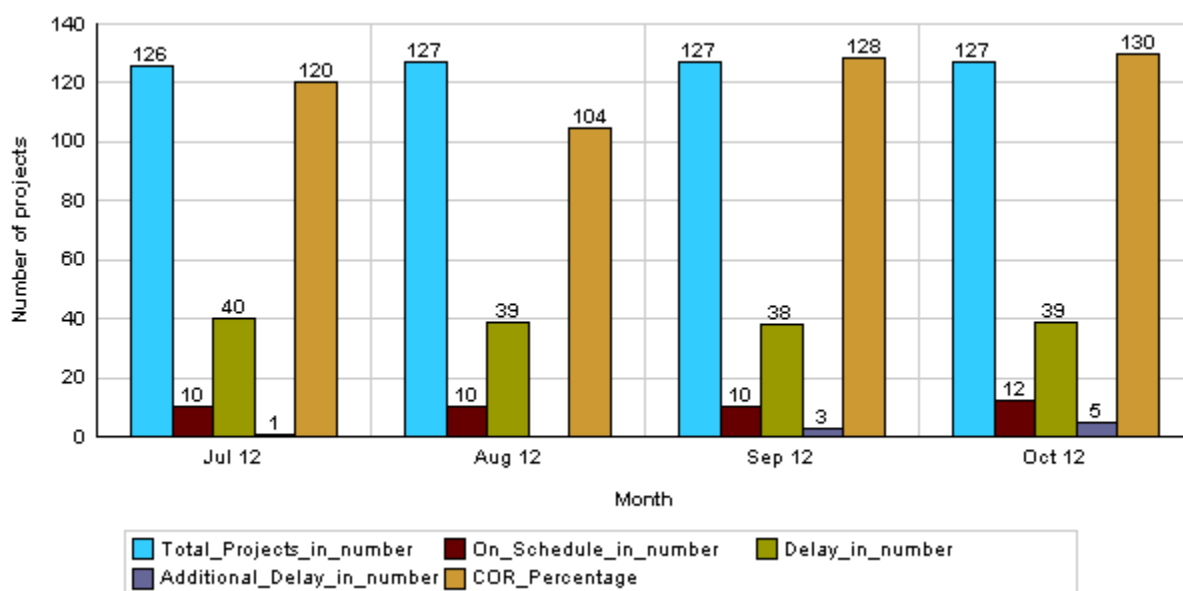


Railways Sector Sector Break-up of 39 Delayed projects in October 2012

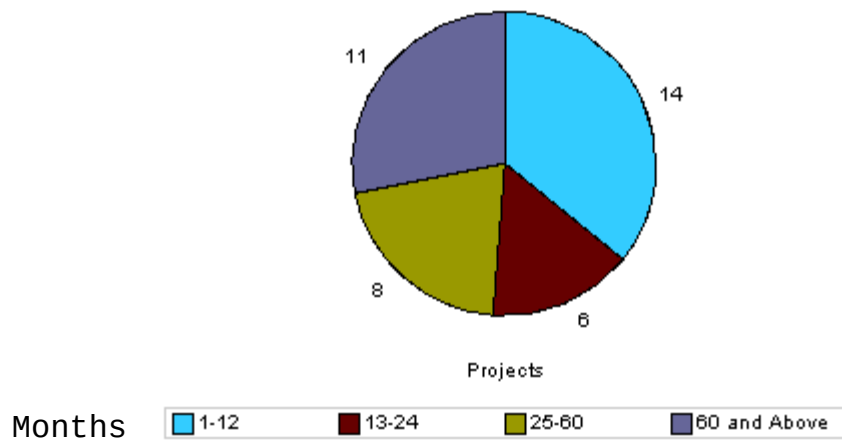


Trend and Graphical Analysis

Power Sector

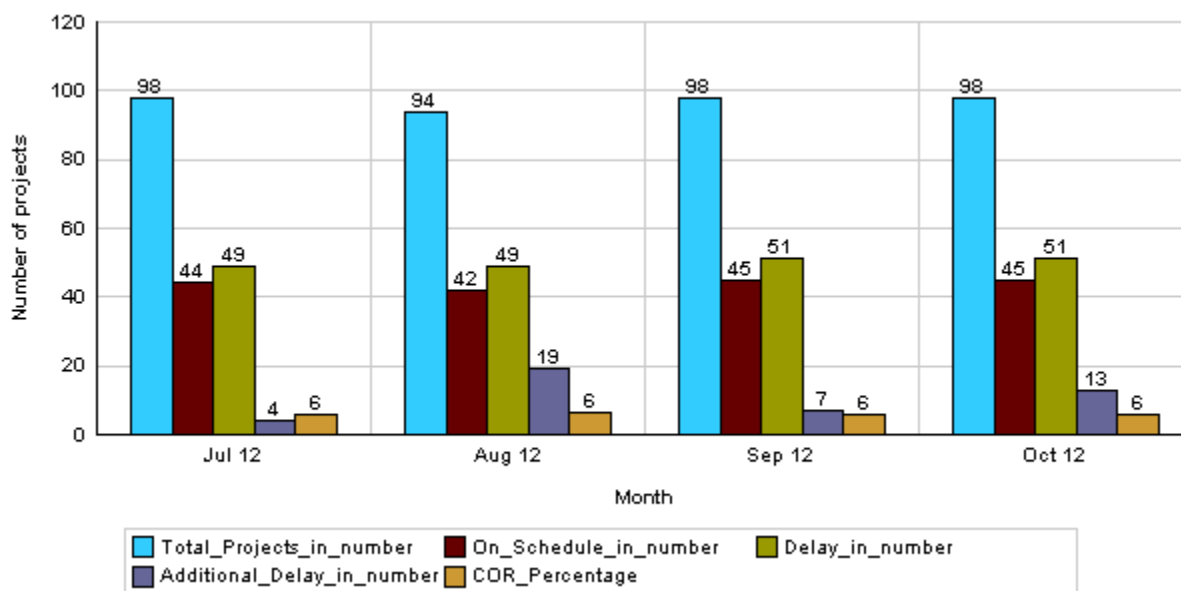


Power Sector Sector Break-up of 51 Delayed projects in October 2012

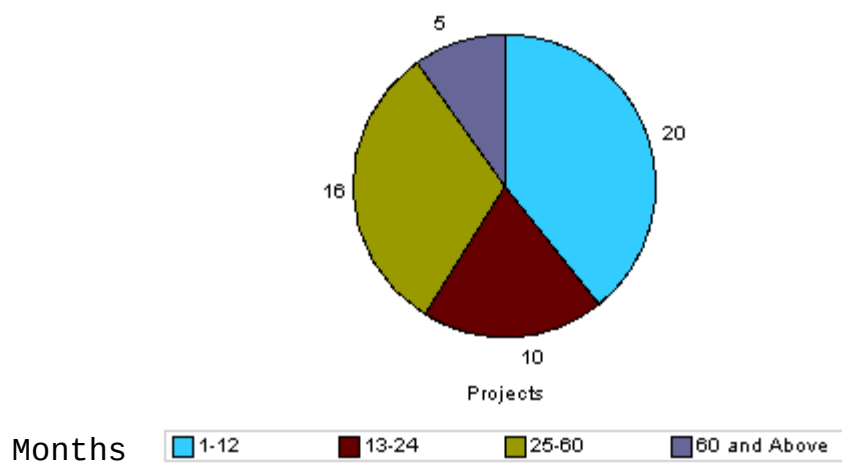


Trend and Graphical Analysis

Petroleum Sector

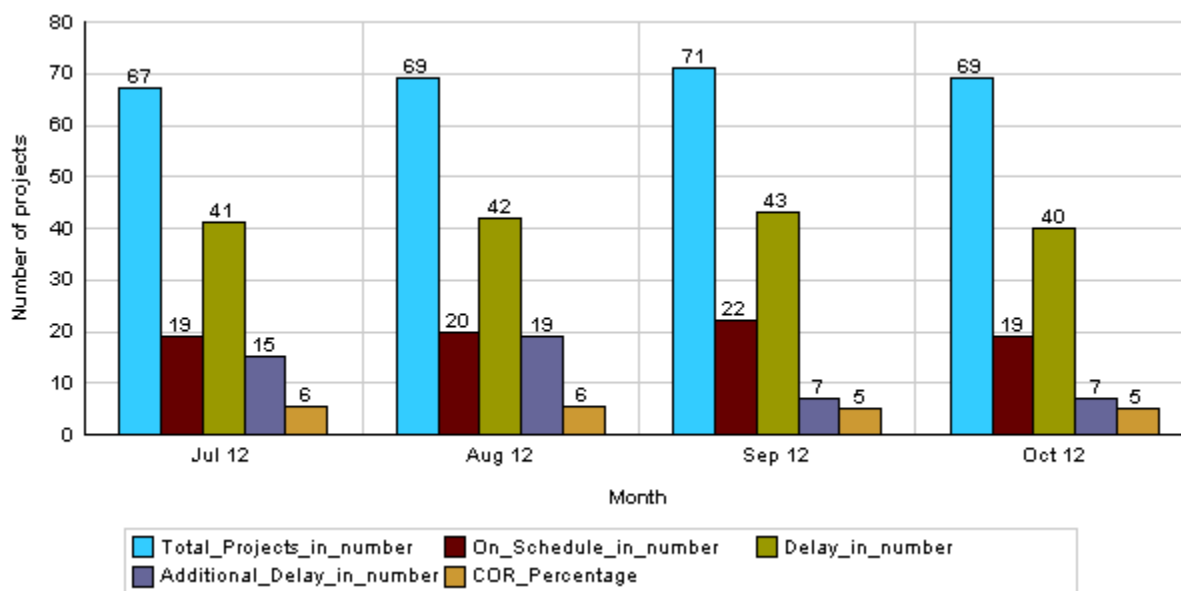


Petroleum Sector Break-up of 40 Delayed projects in October 2012

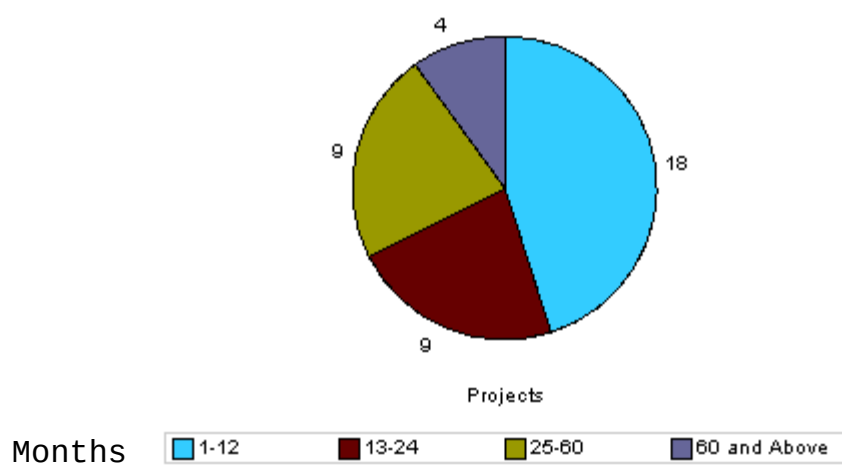


Trend and Graphical Analysis

Steel Sector

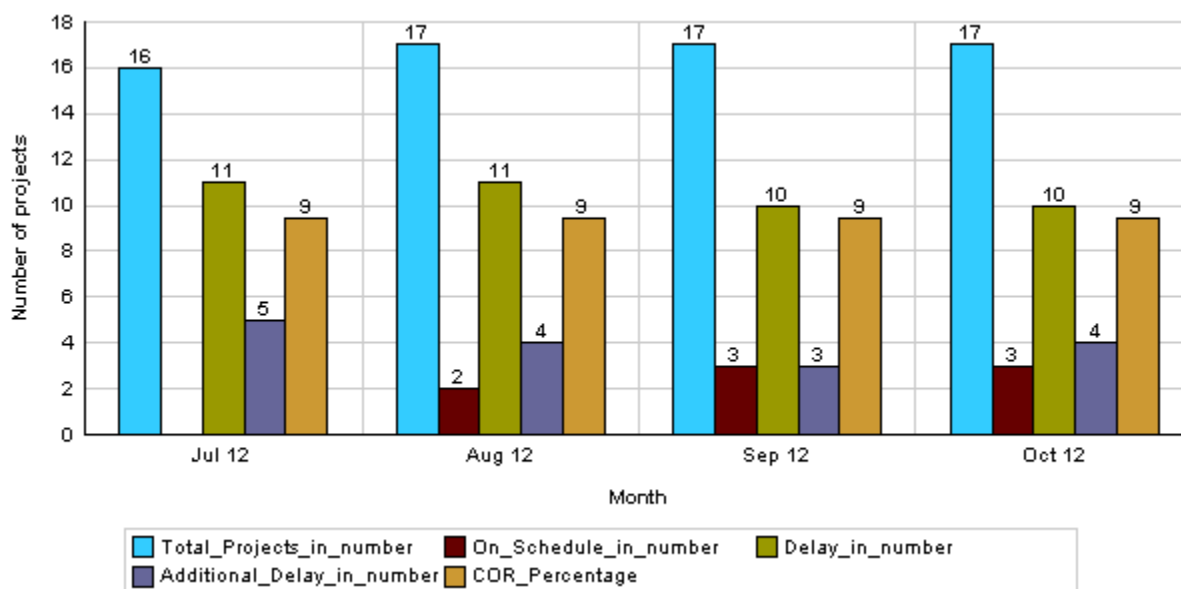


Steel Sector Sector Break-up of 10 Delayed projects in October 2012

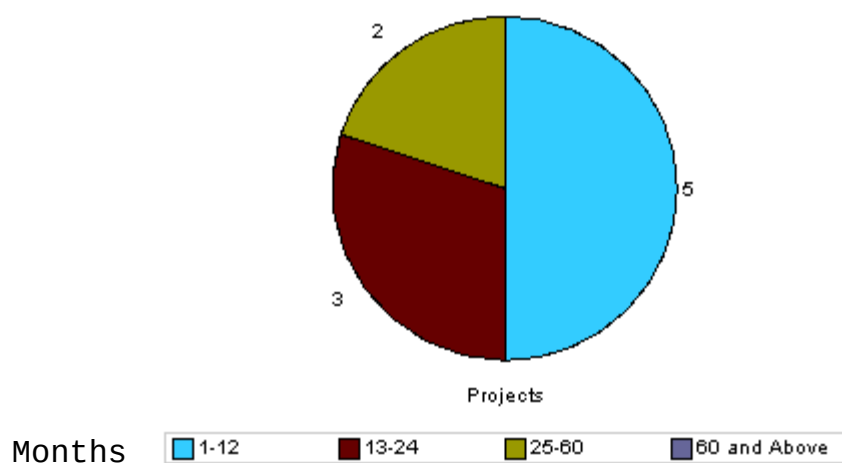


Trend and Graphical Analysis

Fertilisers Sector

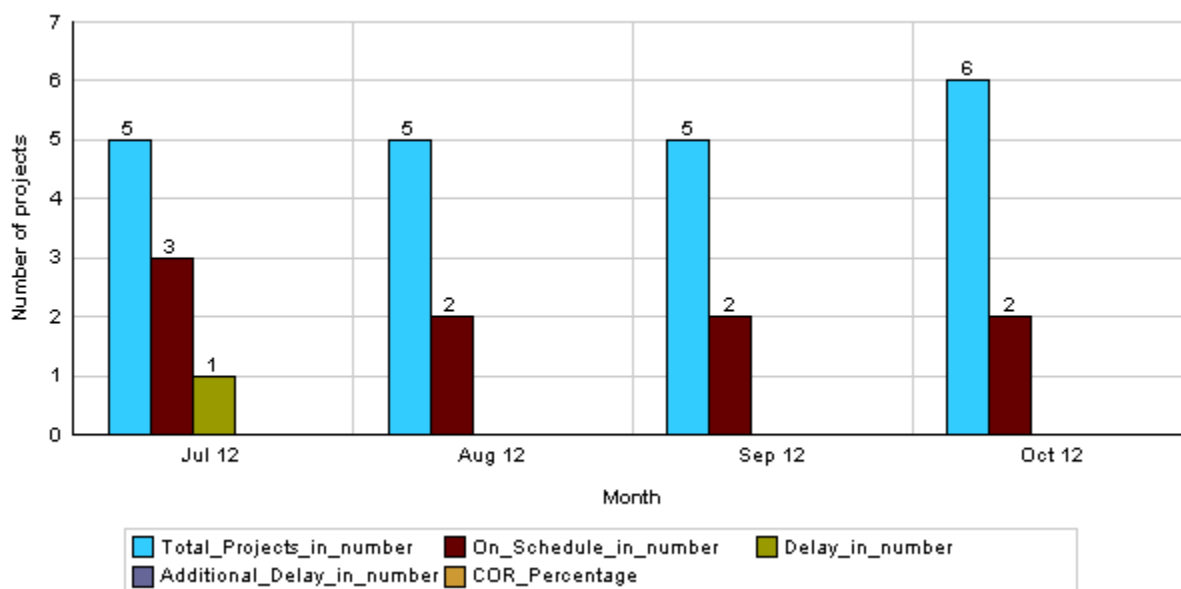


Fertilisers Sector Break-up of 0 Delayed projects in October 2012




Trend and Graphical Analysis

Coal Sector

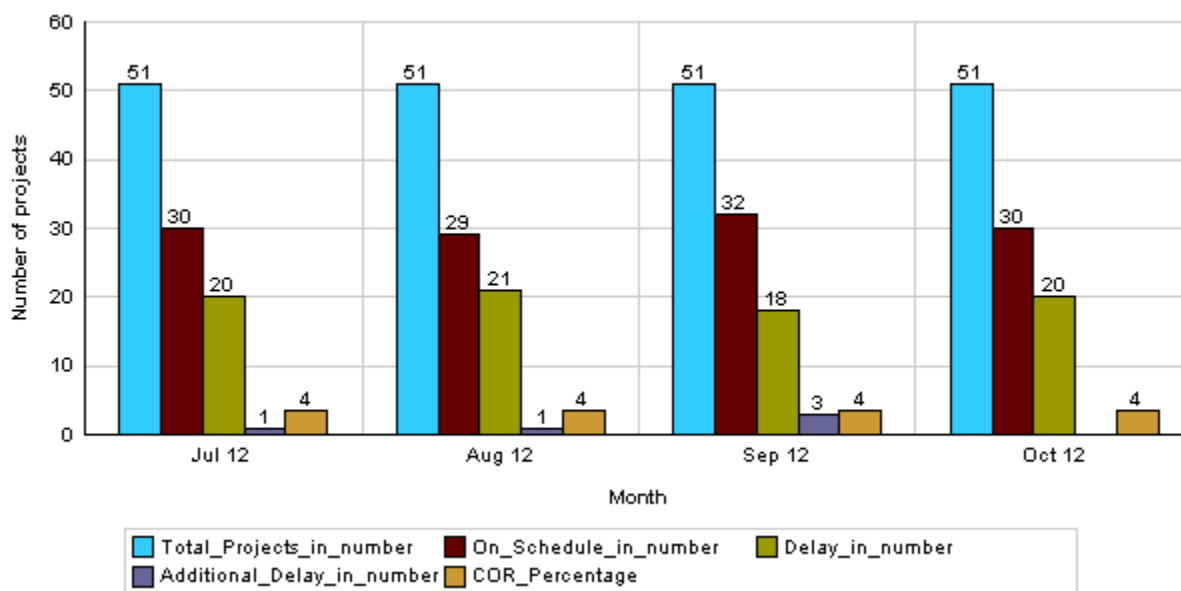


Coal Sector Break-up of 20 Delayed projects in October 2012

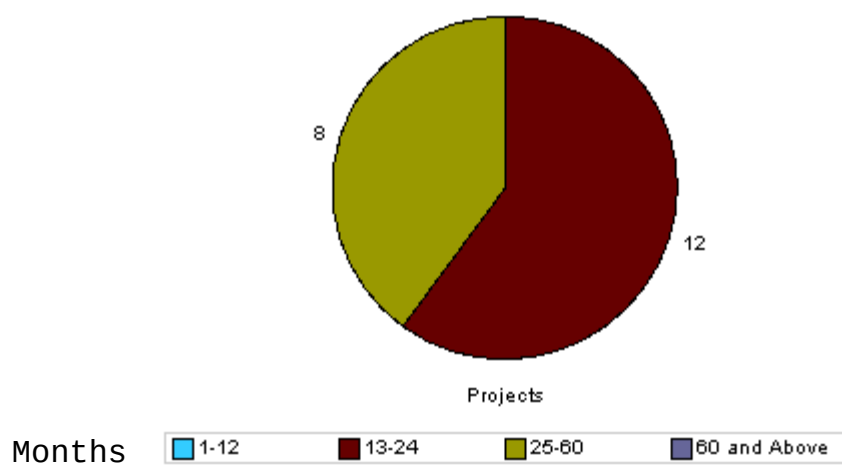


Trend and Graphical Analysis

Civil Aviation Sector

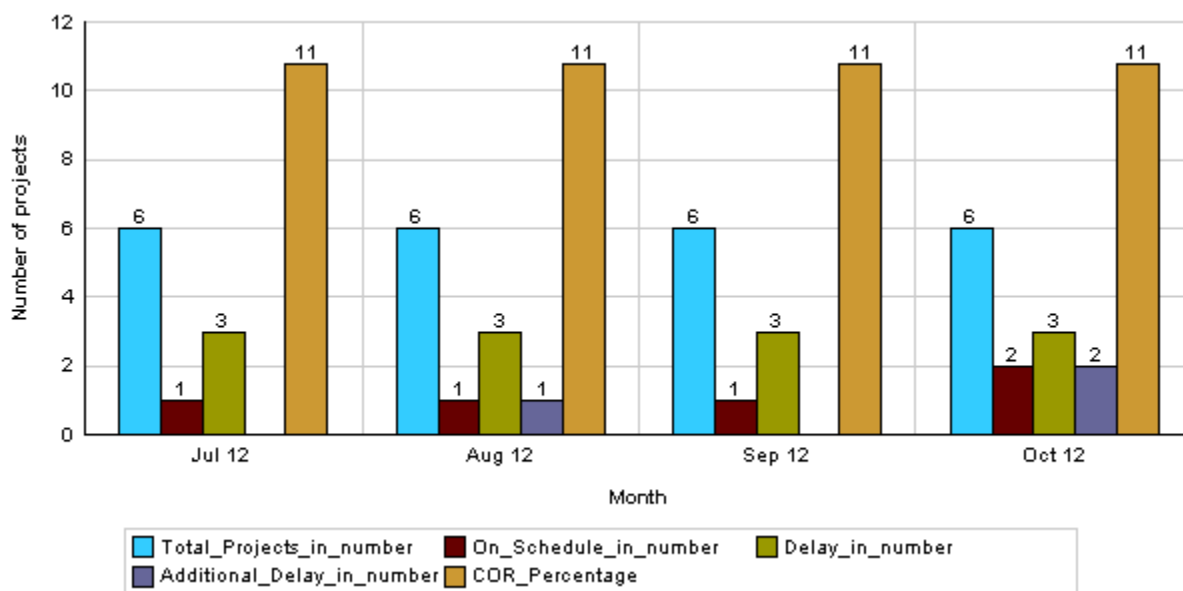


Civil Aviation Sector Break-up of 3 Delayed projects in October 2012

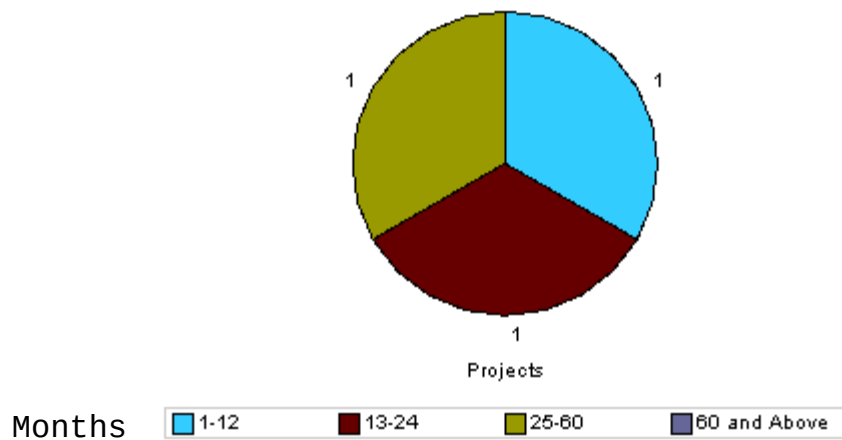


Trend and Graphical Analysis

Atomic Energy Sector

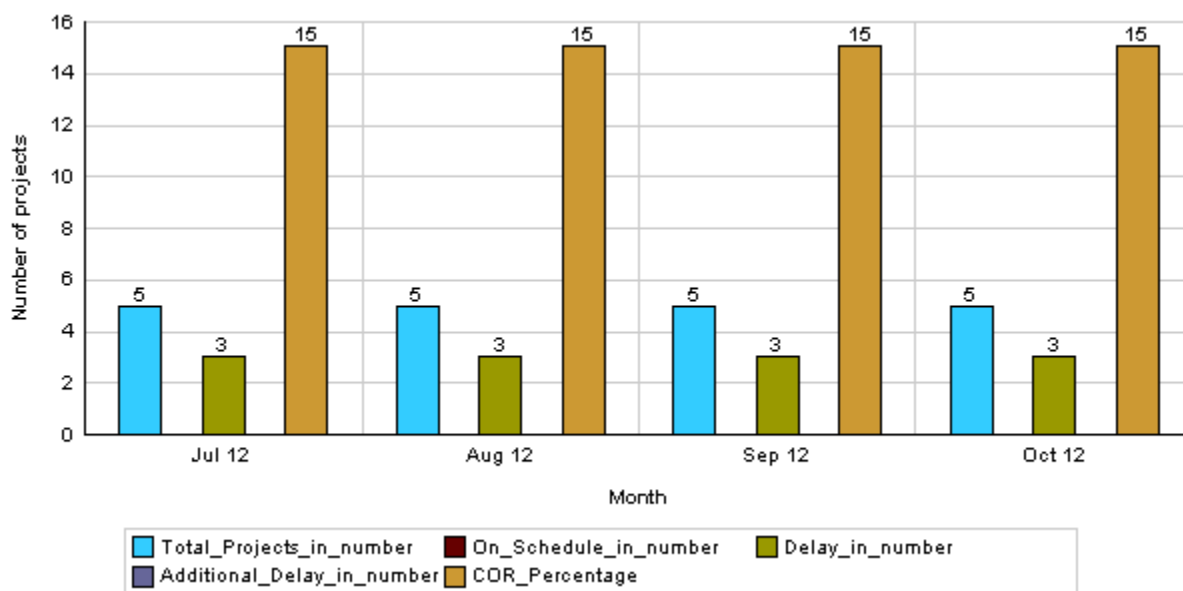

Atomic Energy Sector Sector Break-up of 3 Delayed projects in October 2012

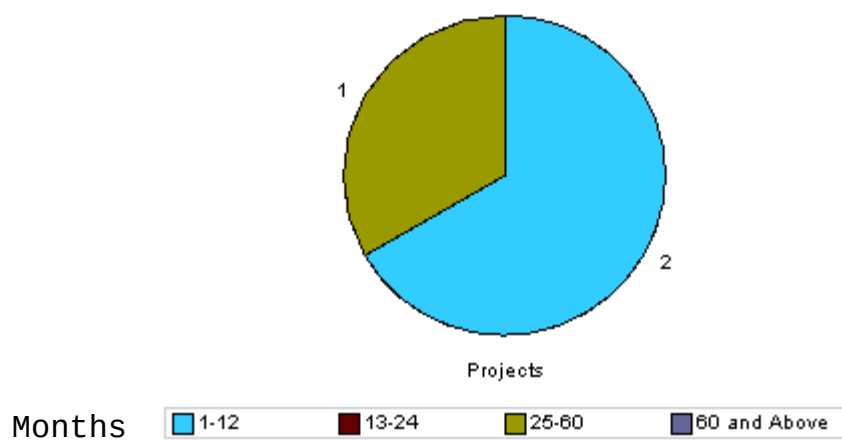

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)			
		Original	Latest	Anticipated	Cumm Expenditure
Atomic Energy	5	41,548.29	41,548.29	47,832.29	19,269.24
Civil Aviation	6	5,473.58	5,680.58	6,063.07	4,593.91
Coal	51	36,056.46	37,022.46	37,312.25	13,173.90
Fertilisers	6	5,153.66	5,153.66	5,153.66	2,875.03
Steel	17	65,285.87	67,562.15	71,443.41	44,375.57
Petrochemicals	1	5,460.61	8,920.00	8,920.00	5,669.55
Petroleum	69	174,399.19	187,851.70	182,915.59	82,606.87
Power	98	231,379.54	235,186.69	245,377.17	106,612.44
Railways	127	64,518.68	94,031.07	148,474.81	64,231.67
Road Transport & Highways	146	94,054.50	94,221.00	95,488.69	68,405.81
Shipping & Ports	19	16,242.52	18,109.64	18,554.09	8,357.06
Telecommunications	13	5,735.48	5,739.36	5,676.27	1,658.81
Urban Development	4	44,245.18	44,304.08	49,518.08	3,260.20
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	563	790,096.46	845,873.58	923,916.38	425,125.55

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,956.00	12/2015	11/2016	11(O)	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,030.00	12/2008	03/2013	51(O)	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00	5,677.00	-	09/2010	-	-	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,199.00	12/2016	03/2017	3(O)	0/69
5	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,084.24	04/2011	-	-	0/0
Total			41,548.29	47,832.29	19,269.24				47/327
<u>Civil Aviation</u>									
6	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,143.57	05/2011 03/2012	03/2013	22(O) 12(R)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	185.20	01/2011 04/2013	04/2013	27(O) 0(R)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	146.09	05/2012	12/2012	7(O)	0/0
9	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,724.62	01/2011 02/2012	02/2012	-	0/0
10	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	452.00	21.36	03/2015	03/2015	0(O)	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	626.00	373.07	06/2013	06/2013	0(O)	0/0
Total			5,473.58	6,063.07	4,593.91				0/0
<u>Coal</u>									
12	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	779.26	456.78	03/2013 09/2012	07/2014	16(O) 22(R)	7/22
13	AMLAI OC EXPANSION SECTOR 1.50 MTY - [N06000082]SECL,Chhatisgarh	11/2009	150.59	198.59	89.50	03/2016	03/2016	0(O)	2/6

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	374.26	03/2016 03/2016	03/2016	0(O) 0(R)	2/2
15	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	100.02	03/2012 -	03/2014	24(O) -	5/7
16	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	12/2007	471.66 341.63	341.63	108.61	03/2011 -	03/2013	24(O) -	0/2
17	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	118.51	03/2010 -	03/2015	60(O) -	4/4
18	BAROUD OC EXPANSION (RCE)-3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	39.81	03/2016 -	03/2016	0(O) -	0/0
19	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00 -	490.10	115.91	03/2017 -	03/2017	0(O) -	6/12
20	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 168.97	168.97	40.35	03/2014 03/2014	03/2014	0(O) 0(R)	1/2
21	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	535.10	162.06	03/2015 03/2015	03/2015	0(O) 0(R)	0/0
22	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/1
23	CHURCHA ROUG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	263.73	03/2014 -	03/2014	0(O) -	2/7
24	Churi Benti UG - [N06000083]CCL,Jharkhandd	08/2007	163.51 -	163.51	34.58	03/2011 -	03/2014	36(O) -	1/2
25	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,231.48	03/2014 -	03/2014	0(O) -	6/12
26	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,391.20	03/2014 -	03/2014	0(O) -	10/15
27	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Orissa	02/2008	395.87 -	395.87	70.82	03/2015 -	03/2015	0(O) -	2/12
28	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	479.63 -	479.63	110.91	03/2013 -	03/2013	0(O) -	5/7
29	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/6
30	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 -	03/2015	0(O) -	4/31
31	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	03/2013	0(O) -	4/83
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	0.82	03/2011 -	03/2015	48(O) -	0/1
33	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	81.94	12/2012 -	03/2015	27(O) -	8/44
34	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	111.49	03/2013 -	03/2013	0(O) -	6/11
35	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46 -	162.46	30.89	03/2014 -	03/2014	0(O) -	0/0
36	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/6

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
37	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	1.51	03/2018 03/2018	03/2018	0(O) 0(R)	0/0
38	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 741.62	741.62	334.67	03/2013 -	03/2013	0(O) -	2/2
39	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	105.97	03/2010 -	03/2014	48(O) -	9/11
40	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	674.36	03/2013 -	03/2013	0(O) -	0/8
41	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
42	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016	44(O) -	1/2
43	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	204.70	03/2014 -	03/2014	0(O) -	1/5
44	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	39.31	03/2012 -	03/2014	24(O) -	10/34
45	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
46	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
47	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	23.99	12/2015 -	08/2017	20(O) -	0/33
48	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.73	03/2012 -	03/2015	36(O) -	0/1
49	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	60.74	03/2012 -	03/2014	24(O) -	0/2
50	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
51	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	0.88	03/2014 -	03/2016	24(O) -	0/1
52	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	87.89	03/2013 -	03/2013	0(O) -	0/2
53	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhandd	09/2009	153.82 -	153.82	24.39	03/2014 -	03/2014	0(O) -	0/1
54	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	114.59	03/2012 -	03/2014	24(O) -	24/27
55	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
56	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	27.95	03/2015 -	03/2015	0(O) -	4/31
57	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016	0(O) -	1/2
58	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	48.63	03/2012 -	-	-	11/42

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
59	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	44.49	03/2016	03/2016	0(O)	1/12
60	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,497.44	06/2009	03/2013	45(O)	19/24
61	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,537.30	03/2012	03/2014	24(O)	0/39
62	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68	264.68	106.67	03/2012	03/2014	24(O)	0/2
	Total		36,056.46	37,312.25	13,173.90				166/634
	Fertilisers								
63	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	769.00	01/2013	01/2013	0(O)	0/5
64	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	239.93	07/2011	07/2012	-	0/0
65	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	185.10	07/2011	04/2012	-	0/0
66	DUMMY PROJECT FOR FERTILISERS - [N08000002]RCF,Multi State	04/2007	325.00	325.00	-	11/2009	10/2011	-	0/0
67	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	890.00	01/2013 12/2012	12/2012	-1(O) 0(R)	8/8
68	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	791.00	01/2013	01/2013	0(O)	0/5
	Total		5,153.66	5,153.66	2,875.03				8/18
	Steel								
69	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	196.51	-	04/2013	-	13/19
70	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	249.29	08/2010	12/2012	28(O)	0/1
71	67.5 MW TG-5 AUX. S'EM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	253.16	02/2011	01/2013	23(O)	2/3
72	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	124.66	-	11/2013	-	11/21
73	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	220.90	05/2012	06/2013	13(O)	1/2

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
74	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	341.42	12/2011 03/2012	01/2013	13(O) 10(R)	16/21
75	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	116.79	10/2012 -	12/2012	2(O) -	3/4
76	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]SAIL, Delhi	07/2012	332.65 -	332.65	-	08/2014 -	08/2014	0(O) -	0/0
77	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL, Orissa	11/2011	254.55 -	254.55	11.73	11/2013 -	11/2013	0(O) -	1/1
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, Chhatisgarh	09/2008	17,265.00 -	17,265.00	6,832.86	03/2013 -	09/2013	6(O) -	20/27
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, Jharkhand	01/2008	6,325.00 -	6,325.00	3,082.76	12/2011 -	12/2012	12(O) -	11/16
80	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, West Bengal	06/2009	2,875.00 -	2,875.00	1,186.14	12/2012 -	03/2013	3(O) -	9/12
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,891.89	12/2011 -	12/2012	12(O) -	17/19
82	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL, Andhra Pradesh	10/2005	8,692.00 -	12,291.00	9,838.39	10/2009 -	03/2013	41(O) -	62/64
83	Expansion of Rourkela Steel Plant - [N12000056]SAIL, Orissa	09/2008	11,812.00 11,812.00	11,812.00	8,028.81	11/2013 -	03/2013	-8(O) -	8/14
84	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL, Maharashtra	12/2011	187.33 -	187.33	-	- -	12/2013	- -	0/1
85	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL, Delhi	01/2012	254.90 -	254.90	0.26	12/2014 -	12/2014	0(O) -	0/0
Total			65,285.87 -	71,443.41	44,375.57				174/225
Petrochemicals									
86	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	5,669.55	04/2012 12/2013	12/2013	20(O) 0(R)	13/29
Total			5,460.61 -	8,920.00	5,669.55				13/29
Petroleum									
87	102 MW WIND POWER PROJECT - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16(O) -	0/0
88	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12(O) -	0/0
89	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	254.36	04/2011 -	11/2012	19(O) -	0/0
90	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	542.37	12/2011 -	01/2013	13(O) -	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
91	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15	2,378.86	1,001.96	03/2013	03/2014	12(O)	0/0
92	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10	1,916.10	614.17	12/2014	12/2014	0(O)	0/0
93	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63	2,189.63	4.84	12/2014	12/2014	0(O)	0/0
94	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92	460.70	257.66	07/2012 07/2012	06/2013	11(O) 11(R)	0/16
95	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL, Haryana	11/2009	341.50	341.50	140.89	02/2013	02/2013	0(O)	38/42
96	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00	190.00	13.17	03/2014	03/2014	0(O)	0/0
97	CDU/VDU-II - [N16000110]CPCL, Tamil Nadu	03/2010	333.99	333.99	210.76	-	09/2012	-	36/36
98	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00	798.00	742.54	04/2011 12/2011	10/2012	18(O) 10(R)	2/2
99	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, Multi State	06/2007	736.65	736.65	344.37	09/2011	08/2013	23(O)	0/0
100	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,582.27	05/2010 05/2012	11/2012	30(O) 6(R)	0/0
101	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 394.00	394.00	368.23	- 08/2011	-	-	0/22
102	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79	756.65	75.23	05/2013	05/2013	0(O)	0/0
103	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20	269.10	-	08/2013	01/2014	5(O)	0/0
104	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26	240.95	46.73	09/2012	09/2013	12(O)	0/0
105	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64	723.64	-	03/2013	11/2013	8(O)	0/0
106	Construction of tanks and blending facility at Vad - [N16000115]IOCL, Gujarat	02/2009	267.00	267.00	215.27	09/2012	09/2012	-	0/0
107	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,934.89	03/2012 08/2012	12/2012	9(O) 4(R)	0/17
108	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip) - [N16000089]IOCL, Maharashtra	12/2009	1,584.00	1,584.00	46.69	-	-	-	0/0
109	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86(O) 12(R)	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,851.49	08/2010 03/2012	12/2013	40(O) 21(R)	0/0
111	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31(O) 13(R)	0/0
112	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34(O) 12(R)	0/0
113	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52(O) 0(R)	0/0
114	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,203.81	09/2011 09/2012	09/2012	-	0/76
115	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,352.39	09/2011 03/2012	11/2012	14(O) 8(R)	0/0
116	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	83.49	03/2013 -	04/2013	1(O) -	0/0
117	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014	0(O) -	0/0
118	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	481.95	03/2013 -	04/2014	13(O) -	0/0
119	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	62.72	11/2012 -	10/2013	11(O) -	0/0
120	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	336.22	01/2014 -	01/2014	0(O) -	0/0
121	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	-	12/2014 -	12/2014	0(O) -	0/0
122	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,965.44	- -	11/2012	- -	114/116
123	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	281.04	01/2013 -	06/2013	5(O) -	18/18
124	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	611.55	04/2013 04/2013	04/2013	0(O) 0(R)	0/167
125	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015	0(O) -	0/0
126	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL,Orissa	12/2009	1,492.33 -	1,492.33	1,164.61	06/2012 03/2013	03/2013	9(O) 0(R)	8/8
127	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.00	03/2007 03/2017	03/2017	120(O) 0(R)	6/6
128	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	634.47	03/2007 03/2014	03/2014	84(O) 0(R)	3/3
129	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	-	03/2014 -	03/2014	0(O) -	0/0
130	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	277.79	03/2006 03/2013	03/2013	84(O) 0(R)	6/6

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
131	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00	14,225.00	9.21	12/2015	12/2015	0(O)	0/0
132	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	2,059.63	-	03/2015	03/2015	0(O)	0/0
133	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	7,596.18	2.54	01/2013	07/2015	30(O)	0/0
134	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07	281.07	4.49	10/2010	12/2014	50(O)	0/0
135	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 312.00	312.00	266.34	01/2012 01/2012	12/2012	11(O) 11(R)	0/1
136	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00	2,915.00	1,080.01	12/2012 12/2012	12/2013	12(O) 12(R)	0/21
137	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00	261.00	202.27	03/2012 08/2012	-	-	2/4
138	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	9,397.26	01/2012 -	03/2013	14(O) -	0/108
139	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39	6,855.93	4,258.26	09/2012 -	09/2013	12(O) -	0/0
140	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.54	05/2010 03/2013	03/2013	34(O) 0(R)	0/0
141	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	3,823.00	701.81	04/2015 -	04/2015	0(O) -	0/0
142	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	679.99	03/2011 05/2011	03/2013	24(O) 22(R)	0/0
143	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	539.45	03/2010 03/2012	05/2013	38(O) 14(R)	0/0
144	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00	30,426.00	18,612.00	11/2012 09/2013	09/2013	10(O) 0(R)	60/100
145	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00	1,793.00	700.55	09/2012 -	09/2012	-	0/11
146	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00	8,140.00	2,015.84	02/2014 -	02/2014	0(O) -	0/0
147	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	246.81	184.00	04/2012 -	-	-	0/0
148	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26	1,417.00	17.28	05/2014 -	05/2014	0(O) -	0/0
149	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78	1,803.78	630.38	07/2012 -	06/2013	11(O) -	0/31
150	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	898.00	904.59	- 03/2012	08/2012	-	0/53

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
151	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014	0(O) -	0/0
152	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016	0(O) -	0/0
153	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7(O) -	0/0
154	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	234.59	03/2012 -	03/2013	12(O) -	13/20
155	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	82.54	12/2013 12/2013	12/2013	0(O) 0(R)	0/0
Total			174,399.19 -	182,915.59	82,606.87				306/884
Power									
156	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,442.10	08/2012 -	03/2013	7(O) -	0/11
157	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,112.70	02/2012 -	11/2012	9(O) -	0/7
158	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	665.60	05/2012 -	12/2012	7(O) -	0/11
159	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,029.30	06/2012 -	11/2012	5(O) -	0/4
160	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,720.00	08/2013 -	09/2014	13(O) -	7/19
161	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,510.00	12/2009 12/2014	03/2016	75(O) 15(R)	26/47
162	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,385.00	07/2011 -	11/2014	40(O) -	4/28
163	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.00	764.03	02/2011 10/2012	11/2012	21(O) 1(R)	2/4
164	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	300.60	08/2014 -	08/2014	0(O) -	0/20
165	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	25.50	06/2014 -	06/2014	0(O) -	0/20
166	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	339.90	09/2014 -	09/2014	0(O) -	8/19

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
167	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	867.25	10/2009 -	03/2013	41(O) -	20/20
168	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	450.20	11/2012 -	03/2014	16(O) -	3/11
169	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
170	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	449.10	05/2014 -	05/2014	0(O) -	0/16
171	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	703.70	08/2013 -	08/2013	0(O) -	0/14
172	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	64.50	08/2014 -	08/2014	0(O) -	0/21
173	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	495.80	12/2013 -	12/2013	0(O) -	0/13
174	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	55.00	10/2012 -	03/2013	5(O) -	0/15
175	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	850.63	12/2007 12/2009	-	-	0/10
176	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.00	2,034.59	05/2013 06/2016	03/2017	46(O) 9(R)	4/22
177	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,751.05	01/2016 01/2016	11/2016	10(O) 10(R)	0/2
178	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,548.00	04/2009 03/2014	03/2014	59(O) 0(R)	0/9
179	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	987.00	12/2016 -	12/2016	0(O) -	0/0
180	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,841.11	09/2008 -	03/2013	54(O) -	17/37
181	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,527.00	08/2012 -	03/2013	7(O) -	11/16
182	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	582.00	09/2016 -	09/2016	0(O) -	0/0
183	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	794.58	08/2010 01/2013	01/2013	29(O) 0(R)	0/3
184	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,182.30	08/2013 -	09/2014	13(O) -	0/17
185	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	246.10	02/2012 -	12/2013	22(O) -	0/14

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	329.90	11/2011 -	12/2013	25(O) -	0/11
187	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	343.50	11/2011 -	12/2013	25(O) -	0/14
188	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	61.30	01/2013 -	01/2013	0(O) -	0/7
189	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	212.30	07/2013 -	07/2013	0(O) -	0/12
190	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	570.80	04/2013 -	10/2013	6(O) -	0/12
191	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	95.20	08/2013 -	08/2013	0(O) -	0/16
192	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	44.00	11/2014 -	11/2014	0(O) -	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	-	03/2015 -	03/2015	0(O) -	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	-	04/2015 -	04/2015	0(O) -	0/0
195	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	453.90	11/2012 -	03/2013	4(O) -	0/10
196	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,960.04	10/2010 01/2013	09/2013	35(O) 8(R)	0/0
197	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,627.99	09/2009 07/2014	12/2017	99(O) 41(R)	1/20
198	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 -	573.99	400.67	08/2012 08/2013	09/2014	25(O) 13(R)	14/21
199	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	2,004.41	01/2012 -	09/2013	20(O) -	0/0
200	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,670.00	10/2012 -	05/2013	7(O) -	10/16
201	SOLAPUR STTP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	820.00	11/2016 -	11/2016	0(O) -	0/0
202	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,830.23	09/2010 08/2014	03/2017	78(O) 31(R)	11/11
203	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	51.60	04/2013 -	04/2013	0(O) -	0/15
204	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,983.70	08/2012 -	03/2013	7(O) -	0/7

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
205	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35	1,935.35	-	12/2014	12/2014	0(O)	0/0
206	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	213.78	-	03/2014	03/2014	0(O)	0/0
207	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65	1,746.65	50.40	08/2014	08/2014	0(O)	0/20
208	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85	1,310.85	105.10	02/2015	02/2015	0(O)	0/0
209	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26	1,263.26	53.40	11/2014	11/2014	0(O)	0/0
210	SYSTEM STRENGTHENING IN RAIPUR- WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85	1,422.85	125.90	01/2015	01/2015	0(O)	0/19
211	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33	297.33	22.90	08/2014	08/2014	0(O)	0/20
212	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	63.60	06/2014	06/2014	0(O)	0/19
213	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	158.70	04/2012	10/2012	6(O)	0/0
214	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	127.08	06/2012	12/2012	6(O)	0/9
215	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	780.40	08/2012	12/2013	16(O)	0/11
216	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48	2,978.48	1,591.00	03/2013	09/2015	30(O)	2/14
217	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,501.75	1,212.87	09/2009 06/2013	12/2013	51(O) 6(R)	0/0
218	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	1,628.00	1,598.46	03/2007 09/2012	02/2013	71(O) 5(R)	25/25
219	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	382.46	07/2010 02/2016	08/2016	73(O) 6(R)	1/10
220	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28	259.28	23.50	01/2014	01/2014	0(O)	0/17
221	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	2,422.66	83.20	08/2014	08/2014	0(O)	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	68.70	10/2014 -	10/2014	0(O) -	0/21
223	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.37	386.37	332.13	07/2011 -	11/2012	16(O) -	0/5
224	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,024.70	10/2012 -	09/2013	11(O) -	0/12
225	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	336.00	01/2015 -	01/2015	0(O) -	0/20
226	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	781.50	03/2014 -	03/2014	0(O) -	0/15
227	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	599.30	08/2013 -	08/2013	0(O) -	0/14
228	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	2.20	08/2014 -	08/2014	0(O) -	0/20
229	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	37.10	10/2014 -	10/2014	0(O) -	0/20
230	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013	37(O) -	0/22
231	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	152.00	11/2011 -	09/2013	22(O) -	0/7
232	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,008.20	12/2012 -	02/2013	2(O) -	0/11
233	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	90.20	02/2014 -	02/2014	0(O) -	0/20
234	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	110.50	10/2013 -	10/2013	0(O) -	0/18
235	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	50.80	07/2013 -	07/2013	0(O) -	0/0
236	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	258.30	12/2013 -	12/2013	0(O) -	0/18
237	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	72.30	11/2013 -	11/2013	0(O) -	0/20

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86	2,074.86	721.00	03/2013	03/2013	0(O)	0/14
239	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	896.20	12/2013	12/2013	0(O)	0/13
240	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99	4,672.99	1,659.20	11/2012	06/2013	7(O)	0/15
241	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51	2,127.51	263.20	07/2014	07/2014	0(O)	0/19
242	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	368.16	- 07/2013	07/2013	- 0(R)	6/29
243	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	352.38	07/2014 -	02/2015	7(O) -	0/16
244	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00	2,144.00	940.40	12/2012	12/2013	12(O)	0/11
245	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	443.50	11/2013	11/2013	0(O)	0/15
246	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03	250.03	58.40	01/2013	11/2013	10(O)	0/16
247	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29	2,081.00	1,825.39	11/2009 02/2013	03/2013	40(O) 1(R)	0/4
248	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40	3,180.40	145.00	08/2015	08/2015	0(O)	0/0
249	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	3,924.00	10/2012	03/2013	5(O)	9/15
250	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	323.33	07/2014 -	05/2016	22(O) -	1/3
251	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23	5,221.23	3,163.50	07/2010	12/2012	29(O)	20/20
252	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69	477.69	419.00	09/2010	03/2013	30(O)	0/9
253	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76	9,569.76	27.70	06/2015	06/2015	0(O)	0/24
Total			231,379.54	245,377.17	106,612.44				202/1232

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Railways									
254	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,141.75	426.35	03/2014 -	03/2014	0(O) -	0/0
255	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	03/2011	-	0/0
256	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	176.76	- -	03/2013	- -	0/0
257	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	453.04	392.85	03/2011 03/2011	03/2011	-	0/0
258	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	538.10	06/1999 03/2011	03/2011	-	0/0
259	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	96.96	- -	-	-	0/0
260	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	404.39	3.77	03/2013 -	03/2013	0(O) -	0/0
261	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.29	- -	-	-	0/0
262	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	451.90	03/2005 12/2008	06/2016	135(O) 90(R)	0/0
263	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	205.28	12/2010 03/2011	03/2011	-	0/0
264	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MTP,Maharashtra	03/1996	401.81 495.44	1,512.86	204.95	03/2004 12/2010	03/2014	120(O) 39(R)	0/0
265	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	12.87	04/2014 -	03/2015	11(O) -	0/0
266	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	668.82	03/2010 -	12/2012	33(O) -	0/0
267	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	350.00	327.08	- 03/2009	03/2011	-	0/0
268	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.02	2,501.02	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
269	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	145.89	12/2012 -	12/2013	12(O) -	0/0
270	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	192.81	03/2011 -	-	-	0/0
271	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	1.00	03/2012 -	-	-	0/0
272	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	600.41	- -	02/2012	-	0/0
273	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	897.49	12/2012 01/2013	01/2013	1(O) 0(R)	0/0
274	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
275	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	- -	0/0
276	CHURCHGATE-VIRAR:CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	1,302.12	608.97	06/2013 06/2013	06/2013	0(O) 0(R)	0/0
277	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	415.73	279.98	- -	12/2012	- -	0/0
278	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	118.28	12/2012 -	12/2012	0(O) -	0/0
279	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	83.11	- -	-	-	0/0
280	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	202.01	- -	03/2013	-	0/0
281	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	420.44	12/2012 12/2012	02/2013	2(O) 2(R)	0/0
282	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	569.32	- -	12/2012	-	0/0
283	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	89.02	12/2011 02/2012	02/2012	-	0/0
284	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	141.55	03/2012 -	03/2012	-	0/0
285	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012	-	0/0
286	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	174.33	06/2013 06/2013	03/2014	9(O) 9(R)	0/0
287	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216(O) -	0/0
288	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.33	02/2011 02/2011	02/2013	24(O) 24(R)	0/0
289	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	82.89	02/2006 -	-	-	0/0
290	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	863.23	603.58	- -	03/2012	-	0/0
291	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
292	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	348.55	- 05/2009	05/2009	-	0/0
293	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	108.12	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
294	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	324.66	182.55	- -	-	-	0/0
295	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	221.60	- 09/2009	-	-	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
296	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
297	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	542.29	- -	01/2013	- -	0/0
298	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	146.32	- -	03/2014	- -	0/0
299	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	169.68	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
300	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	69.70	- -	-	-	0/0
301	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	7.89	03/2015 -	03/2015	0(O) -	0/0
302	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.75	835.55	06/2007 -	06/2007	-	0/0
303	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	662.51	03/2012 08/2012	02/2013	11(O) 6(R)	0/0
304	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	425.36	03/2012 03/2012	12/2012	9(O) 9(R)	0/0
305	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	937.59	03/2011 03/2014	03/2016	60(O) 24(R)	0/0
306	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.46	215.94	03/2014 -	03/2014	0(O) -	0/0
307	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	249.19	03/2012 03/2012	03/2013	12(O) 12(R)	0/0
308	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,389.02	- -	03/2013	- -	0/0
309	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	506.14	- -	03/2014	- -	1/1
310	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	737.02	- -	10/2012	- -	0/0
311	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	732.83	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
312	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	96.67	- -	03/2013	- -	0/0
313	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013	49(O) 49(R)	0/0
314	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	237.18	- -	03/2013	- -	0/0
315	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
316	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	768.87	436.14	- 03/2010	03/2010	-	0/0
317	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	2,957.21	1,321.44	07/2005 -	-	-	0/0
318	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	418.17	126.50	- -	-	-	0/0
319	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	274.73	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
320	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
321	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	335.74	- -	12/2012	-	0/0
322	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	114.08	12/2012 -	03/2014	15(O) -	0/0
323	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	319.01	05/2008 03/2011	03/2011	-	0/0
324	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	-	0/0
325	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	205.16	03/2002 -	01/2013	130(O) -	0/0
326	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,195.95	03/2009 -	12/2013	57(O) -	0/0
327	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.35	07/2008 -	07/2008	-	0/0
328	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.46	- -	02/2013	-	0/0
329	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	555.40	12/2011 12/2011	03/2013	15(O) 15(R)	0/0
330	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
331	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	401.54	03/2012 03/2013	03/2013	12(O) 0(R)	0/0
332	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	900.00	280.18	- -	-	-	0/0
333	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	4,501.80	4,334.00	06/2011 03/2012	03/2012	-	0/0
334	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	920.70	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
335	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	139.79	- -	03/2012	-	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
336	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 429.49	883.00	634.02	02/2009 -	03/2012	-	0/0
337	NANGALDAM-TALWARA(NL), NR - [220100188](NR), Multi State	03/1981	37.68 450.00	730.00	352.01	07/2012 -	-	-	0/0
338	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR, Bihar	09/2006	300.00 300.00	532.87	39.45	- -	-	-	0/0
339	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR, Assam	09/2006	200.00 200.00	385.20	114.85	- -	03/2014	-	0/0
340	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR, Multi State	04/2000	733.00 733.00	1,655.81	1,298.65	12/2008 -	03/2014	63(O) -	0/0
341	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	04/1983	36.80 274.41	703.17	242.39	- -	03/2015	-	0/0
342	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	850.00	8.45	03/2015 -	03/2015	0(O) -	0/0
343	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	2,913.51	171.51	03/2016 -	03/2016	0(O) -	0/0
344	New Work for Construction of Metro railway from Ba - [N22000109]RVNL, West Bengal	04/2010	2,069.60 -	2,298.42	33.46	03/2014 03/2016	03/2016	24(O) 0(R)	0/0
345	New Work for Construction of Metro railway from NS - [N22000110]RVNL, West Bengal	04/2010	3,951.98 -	3,951.98	35.50	03/2016 -	03/2016	0(O) -	0/0
346	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	30.85	03/2016 -	06/2016	3(O) -	0/0
347	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	1,117.11	448.67	03/2008 06/2008	-	-	0/0
348	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	355.00	413.37	03/2009 12/2009	03/2011	-	0/0
349	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 -	252.50	247.35	02/2010 -	-	-	0/0
350	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, Bihar	04/2001	624.47 2,921.00	2,921.00	1,563.17	10/2007 12/2012	12/2012	62(O) 0(R)	0/0
351	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 495.68	925.30	590.02	- -	03/2012	-	0/0
352	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	293.74	137.07	12/2010 12/2010	12/2010	-	0/0
353	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR, Multi State	03/1998	280.00 842.35	1,029.00	769.62	- -	03/2013	-	0/6
354	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	221.90	236.81	12/2007 03/2010	12/2010	-	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
355	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	863.38	03/2009 12/2012	12/2012	45(O) 0(R)	0/0
356	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013	50(O) 50(R)	0/0
357	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	240.93	- -	-	-	0/0
358	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	456.45	301.82	06/2004 -	12/2012	102(O) -	0/0
359	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,476.55	- -	03/2013	- -	0/0
360	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	370.00	358.98	04/2003 03/2010	-	-	0/0
361	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	602.00	494.36	02/2010 02/2011	02/2011	-	0/0
362	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	639.97	174.53	03/1998 08/2005	08/2005	-	0/0
363	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	394.08	03/2013 -	03/2014	12(O) -	0/0
364	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	105.72	03/2012 -	03/2013	12(O) -	0/0
365	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	228.77	03/2010 -	03/2012	-	0/0
366	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015	0(O) -	0/0
367	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	818.29	75.05	02/2015 -	02/2015	0(O) -	0/0
368	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	288.62	03/2014 -	03/2014	0(O) -	0/0
369	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	115.80	- -	03/2013	- -	0/0
370	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	427.98	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
371	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	530.19	- 12/2009	02/2012	-	0/0
372	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	136.04	- -	-	-	0/0
373	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	39.04	- -	-	-	0/0
374	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	548.96	518.10	- -	-	-	0/0
375	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,225.24	12/2006 08/2010	08/2010	-	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
376	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	167.73	48.02	03/2012 -	02/2013	11(O) -	0/0
377	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	20,000.00	8,521.82	03/2001 -	12/2017	201(O) -	0/0
378	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	820.40	158.14	03/2010 06/2014	06/2014	51(O) 0(R)	0/0
379	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	397.15	03/2014 -	03/2013	-12(O) -	0/0
380	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	356.87	171.77	- 03/2010	-	-	0/0
Total			64,518.68 -	148,474.81	64,231.67				1/7
Road Transport & Highways									
381	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	352.68	05/2013 -	03/2014	10(O) -	0/0
382	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	269.32	11/2013 -	11/2013	0(O) -	0/0
383	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	10.49	01/2014 -	01/2014	0(O) -	0/0
384	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	248.04	02/2014 -	02/2014	0(O) -	0/0
385	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	223.55	02/2014 -	04/2014	2(O) -	0/0
386	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014	0(O) -	0/0
387	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	131.22	05/2014 -	05/2014	0(O) -	0/0
388	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	847.12	08/2014 -	08/2014	0(O) -	0/0
389	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013	0(O) -	0/0
390	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	34.42	09/2013 -	07/2014	10(O) -	0/0
391	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	590.69	08/2013 -	08/2013	0(O) -	0/0
392	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	456.17	07/2013 -	07/2013	0(O) -	0/0
393	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhandd	02/2012	398.00 -	398.00	286.35	02/2014 -	02/2014	0(O) -	0/0
394	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	560.95	08/2013 -	08/2013	0(O) -	0/0
395	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	729.12	08/2013 -	08/2013	0(O) -	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
396	4-laning of Raiganj-Dalkola - [N24000204]NHAI, Multi State	02/2011	580.43	580.43	218.49	08/2013	08/2013	0(O)	0/0
397	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, West Bengal	04/2012	1,396.18	1,396.18	463.57	09/2014	09/2014	0(O)	0/0
398	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	465.50	184.79	09/2007	03/2014	78(O)	0/0
399	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2012	93(O)	0/0
400	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	1,161.20	11/2012	06/2013	7(O)	0/0
401	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	289.52	11/2008	11/2012	48(O)	0/0
402	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00	190.00	260.19	01/2009	12/2012	47(O)	0/0
403	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	631.65	02/2012	11/2012	9(O)	0/0
404	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	194.42	02/2004	12/2012	106(O)	0/0
405	BAREILLY-SITAPUR - [N24000200]NHAI, Uttar Pradesh	03/2011	1,046.00	1,046.00	176.48	09/2013	09/2013	0(O)	0/0
406	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan	12/2011	2,388.00	2,388.00	470.08	06/2014	06/2014	0(O)	0/0
407	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	418.89	-	10/2013	-	2/2
408	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00	209.00	3.82	01/2013	10/2013	9(O)	0/0
409	BHUBANESWAR TO PURI - [N24000195]NHAI, Orissa	03/2011	500.29	500.29	440.64	08/2013	08/2013	0(O)	0/0
410	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80	237.80	251.66	06/2008	12/2012	54(O)	0/0
411	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00	195.00	209.66	06/2008	03/2013	57(O)	0/0
412	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00	230.00	227.91	06/2005	03/2013	93(O)	0/0
413	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61	217.61	225.26	04/2010	12/2012	32(O)	0/0
414	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	179.23	02/2010	12/2013	46(O)	0/0
415	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	743.61	03/2013	03/2013	0(O)	0/0
416	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	355.13	-	12/2013	-	0/1

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
417	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	957.75	05/2013	05/2013	0(O)	0/0
418	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37	353.37	376.65	10/2011	03/2014	29(O)	0/0
419	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	712.18	10/2011	06/2013	20(O)	0/0
420	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00	225.00	282.86	06/2008	12/2012	54(O)	0/0
421	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	175.59	10/2008	03/2014	65(O)	0/0
422	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	593.31	05/2010	12/2012	31(O)	0/0
423	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	390.90	07/2013	07/2013	0(O)	0/0
424	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	75.85	06/2013	06/2013	0(O)	0/0
425	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	351.33	-	06/2013	-	1/1
426	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	231.15	06/2008	03/2013	57(O)	0/0
427	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	187.69	05/2008	03/2013	58(O)	0/0
428	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	274.33	09/2010	12/2012	27(O)	0/0
429	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	85.41	08/2013	08/2013	0(O)	0/0
430	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	535.49	01/2011	12/2012	23(O)	0/0
431	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	399.87	09/2008	12/2012	51(O)	0/0
432	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	12/2013	30(O)	0/0
433	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	134.12	09/2008	03/2013	54(O)	0/0
434	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	271.86	02/2004	12/2012	106(O)	0/0
435	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	697.65	08/2013	08/2013	0(O)	0/0
436	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	211.16	04/2008	12/2012	56(O)	0/0
437	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	152.14	04/2008	12/2012	56(O)	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
438	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI, Madhya Pradesh	12/2003	300.93	300.93	302.72	10/2009	12/2012	38(O)	0/0
439	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00	604.00	494.29	12/2009	07/2013	43(O)	0/0
440	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10	1,509.10	1,427.90	09/2012	03/2013	6(O)	0/0
441	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI, Multi State	04/2009	1,673.70	1,673.70	2,731.00	10/2011	12/2012	14(O)	0/0
442	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00	220.00	279.21	09/2007	12/2012	63(O)	0/0
443	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00	280.00	278.20	02/2009 03/2014	03/2013	49(O) -12(R)	0/0
444	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	51.63	07/2009	04/2014	57(O)	0/0
445	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	28.21	09/2007	04/2014	79(O)	0/0
446	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00	207.56	187.68	08/2004	11/2012	99(O)	0/0
447	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00	196.65	181.42	08/2004 07/2010	11/2012	99(O) 28(R)	0/0
448	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	862.54	01/2013	01/2013	0(O)	0/0
449	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	1,394.40	-	03/2013	-	3/3
450	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI, Andhra Pradesh	04/2010	1,740.00	1,740.00	1,903.30	10/2012	11/2012	1(O)	0/0
451	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI, Andhra Pradesh	08/2010	388.00	388.00	515.85	05/2012	11/2012	6(O)	0/0
452	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	325.00	387.71	05/2013	02/2014	9(O)	0/0
453	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.67	04/2013	04/2013	0(O)	0/0
454	JAIPUR-REENGUS - [N24000198]NHAI, Rajasthan	08/2010	267.81	267.81	541.88	02/2013	02/2013	0(O)	0/0
455	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76	1,813.76	-	07/2013	06/2014	11(O)	0/0
456	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00	340.00	575.27	09/2008	12/2012	51(O)	0/0
457	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	499.70	09/2009	03/2013	42(O)	0/0
458	JORBAT - BARAPANI - [N24000180]NHAI, Meghalaya	01/2011	536.00	536.00	404.05	01/2014	01/2014	0(O)	0/0
459	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	1,517.00	12/2012	12/2012	0(O)	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
460	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	279.36	10/2008	02/2013	52(O)	0/0
461	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	294.29	10/2008	03/2013	53(O)	0/0
462	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16	702.16	183.38	07/2014	07/2014	0(O)	0/0
463	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	737.54	-	03/2013	-	2/3
464	Kishangarh-Ajmer-Beaver - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	1,037.50	05/2012	12/2012	7(O)	0/0
465	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	263.17	233.77	06/2010	09/2014	51(O)	0/0
466	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.77	09/2009	09/2014	60(O)	0/0
467	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90	635.90	-	07/2012	07/2014	24(O)	0/0
468	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	93.99	11/2008	07/2013	56(O)	0/0
469	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	62.08	04/2009	07/2013	51(O)	0/0
470	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	21.35	11/2008	01/2014	62(O)	0/0
471	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	118.02	04/2009	03/2013	47(O)	0/0
472	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	1,068.70	06/2012	12/2012	6(O)	0/0
473	MURADABAD-BAREILLY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	1,264.30	06/2013	06/2013	0(O)	0/0
474	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00	754.00	426.01	03/2013	03/2014	12(O)	0/0
475	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	269.32	11/2013	11/2013	0(O)	0/0
476	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	287.75	06/2008	03/2013	57(O)	0/0
477	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	457.30	12/2008	12/2012	48(O)	0/0
478	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19	484.19	25.36	10/2014	10/2014	0(O)	0/0
479	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	270.92	04/2008	12/2012	56(O)	0/0
480	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	248.90	06/2008	03/2013	57(O)	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
481	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00	200.00	276.00	06/2008	12/2012	54(O)	0/0
482	NASHRI CHANANI - [N24000162]NHAI, J and K	06/2010	2,159.00	2,159.00	-	06/2015	05/2016	11(O)	0/0
483	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50	196.50	257.43	06/2011	12/2012	18(O)	0/2
484	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00	557.00	930.92	02/2010	12/2014	58(O)	0/0
485	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00	586.00	237.55	01/2014	01/2014	0(O)	0/0
486	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	436.70	09/2013	09/2013	0(O)	0/0
487	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	388.01	03/2008	03/2013	60(O)	0/0
488	PANIKHOLI-RIMOLI - [N24000197]NHAI, Orissa	03/2012	1,410.00	1,410.00	152.77	09/2014	09/2014	0(O)	0/0
489	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	931.51	10/2014	10/2014	0(O)	0/0
490	PATHANKOT- BHOGPUR, KM.26- KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00	359.00	230.13	05/2008	03/2013	58(O)	0/0
491	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00	574.00	425.90	03/2014	03/2014	0(O)	0/0
492	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	588.61	02/2013	02/2013	0(O)	0/0
493	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, Maharashtra	03/2005	940.00	940.00	1,158.80	07/2012	12/2012	5(O)	0/0
494	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	1,028.20	03/2013	03/2013	0(O)	0/0
495	PUNE-SHOLAPUR, Pkg-II - [N24000193]NHAI, Maharashtra	09/2011	835.00	835.00	104.67	01/2014	01/2014	0(O)	0/0
496	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00	2,288.00	3,462.40	11/2011	08/2013	21(O)	0/0
497	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00	1,110.00	1,802.10	05/2012	10/2013	17(O)	0/0
498	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J and K	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11(O)	0/0
499	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHA) - [240106304]NHAI, Madhya pradesh	12/2003	251.03	251.03	312.76	10/2008	12/2012	50(O)	0/0
500	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91	229.91	267.50	10/2008	12/2012	50(O)	0/0
501	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	650.00	751.40	11/2013	11/2013	0(O)	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
502	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43	203.43	240.12	10/2008	12/2012	50(O)	0/0
503	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	02/2013	25(O)	0/0
504	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	360.85	03/2013	03/2013	0(O)	0/0
505	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00	909.00	844.05	05/2014	05/2014	0(O)	0/0
506	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	206.78	09/2007	03/2013	66(O)	0/0
507	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	186.36	07/2008	12/2012	53(O)	0/0
508	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
509	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	12.48	12/2013	12/2013	0(O)	0/0
510	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00	1,535.00	822.95	05/2014	05/2014	0(O)	0/0
511	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.52	08/2012	03/2014	19(O)	0/0
512	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70	1,100.70	-	06/2014	06/2014	0(O)	0/0
513	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00	245.00	491.21	03/2008	03/2013	60(O)	0/0
514	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00	241.53	141.38	04/2004	12/2012	104(O)	0/0
515	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,674.90	08/2011	11/2012	15(O)	0/0
516	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	581.49	06/2009	11/2012	41(O)	0/0
517	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00	516.00	760.07	07/2010	03/2013	32(O)	0/0
518	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	731.28	11/2013	11/2013	0(O)	0/0
519	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
520	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	78.28	05/2013	05/2013	0(O)	0/0
521	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI, Karnataka	11/2010	680.00	680.00	166.98	-	04/2013	-	2/2

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
522	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	686.10	03/2014 -	03/2014	0(O) -	0/0
523	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012	57(O) -	0/0
524	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	33.97	11/2012 -	11/2012	0(O) -	0/0
525	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	419.59	07/2013 -	07/2013	0(O) -	0/0
526	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	148.81	06/2014 -	06/2014	0(O) -	0/0
	Total		94,054.50 -	95,488.69	68,405.81				10/14
Shipping & Ports									
527	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 10/2012	10/2012	18(O) 0(R)	0/0
528	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	777.97	09/2012 10/2012	10/2012	1(O) 0(R)	0/0
529	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	294.84	12/2012 05/2013	05/2013	5(O) 0(R)	0/0
530	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	188.88	12/2011 10/2012	10/2012	10(O) 0(R)	0/0
531	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	305.00	194.14	06/2011 09/2012	09/2012	-	0/0
532	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014	0(O) -	0/0
533	Acquistion of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 10/2013	10/2013	-2(O) 0(R)	0/0
534	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	894.93	12/2010 09/2012	10/2013	34(O) 13(R)	0/0
535	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O) -	0/0
536	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	22(O) -	0/0
537	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	10/2008	-	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
538	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST, Orissa	12/2005	154.84 -	253.36	-	- 01/2009	01/2009	-	0/1
539	ENNORE MANALI EXPRESS WAY, F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST, Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87(O) 0(R)	0/0
540	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST, Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O) -	0/0
541	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
542	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67 298.17	373.22	326.08	04/2009 11/2009	02/2011	-	0/0
543	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST, Tamil Nadu	06/2005	2,427.40 -	2,427.40	830.41	10/2008 11/2010	-	-	0/0
544	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,534.95	01/2012 09/2012	12/2012	11(O) 3(R)	0/0
545	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST, Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	03/2013	-2(O) -	0/0
Total			16,242.52 -	18,554.09	8,357.06				0/1
Telecommunications									
546	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL, Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53(O) -	0/0
547	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL, Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
548	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL, Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72(O) 11(R)	0/0
549	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL, Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	06/2013	32(O) 15(R)	0/0
550	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL, Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
551	Execution of telecom network requirement of defence - [N26000065]BSNL, Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
552	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL, Uttaranchal	01/2009	149.15 158.72	158.72	80.05	06/2009 -	03/2013	45(O) -	0/0

Sector Wise Details

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
553	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	232.00	12/2008	03/2013	51(O)	0/0
554	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	815.91	11/2010	12/2012	25(O)	0/0
555	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84	336.84	35.75	10/2009	03/2011	-	0/0
556	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	03/2013	48(O)	0/0
557	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
558	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010	-	-	0/0
	Total		5,735.48	5,676.27	1,658.81				0/0
	Urban Development								
559	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00	11,609.00	2,267.57	06/2011	03/2013	21(O)	6/6
560	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
561	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	923.05	03/2016	03/2016	0(O)	0/0
562	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	69.58	09/2014	09/2014	0(O)	0/0
	Total		44,245.18	49,518.08	3,260.20				6/6
	Water Resources								
563	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
Grand Total			790,096.46	923,916.38	425,125.55				933/3377

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

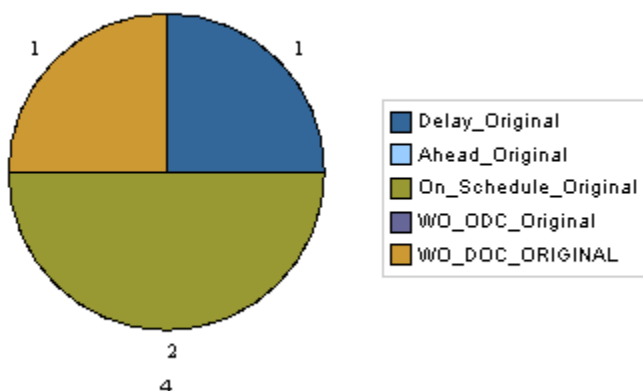

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till October, 2012 is Rs. 3260.2 crore, which is 6.6% of the revised cost of the projects.

Figures are in Rs. Crore

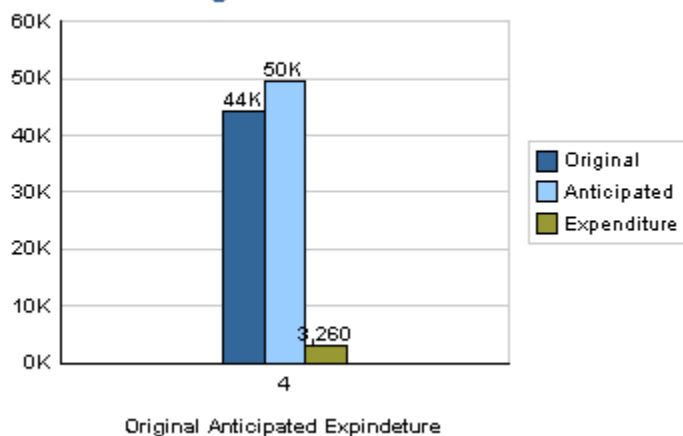

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **13**

Number of Projects Delayed **7**

Number of Projects Without Date Of Commissioning **6**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 7 projects are delayed .6 projects do not have fixed dates of commissioning.

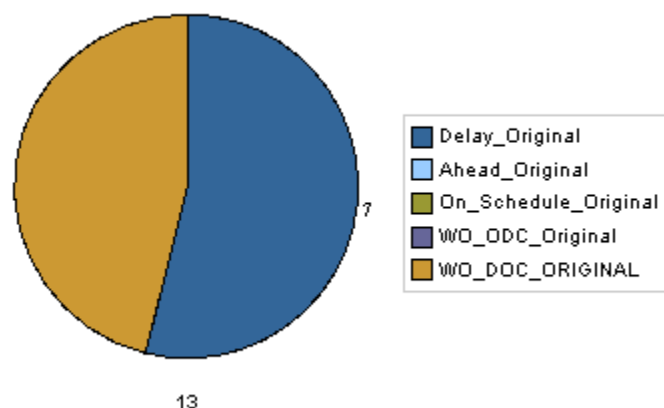

III. Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5735.48 crore but this was subsequently revised to Rs. 5676.27 crore implying a cost overrun of -1%. The expenditure incurred on these projects till October, 2012 is Rs. 1658.81 crore, which is 29.2% of the revised cost of the projects.

Figures are in Rs. Crore

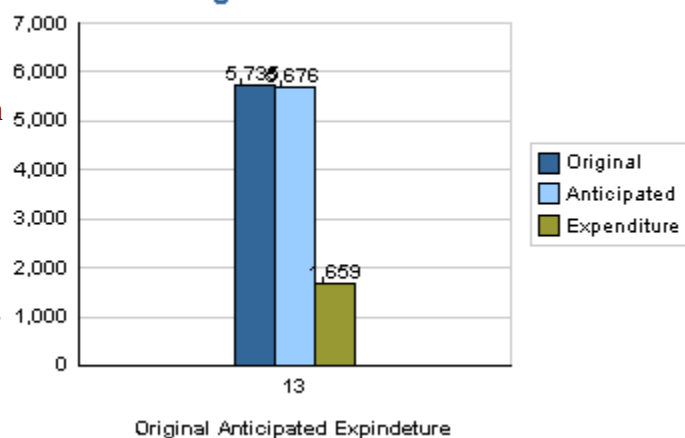

Sector wise current status of projects on theFlash Report


Shipping & Ports

I. Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	10
Number of Projects Ahead	2
Number of Projects Without Date Of Commissioning	6

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 2 projects are ahead of schedule, 1 project are on schedule and 10 projects are delayed .6 projects do not have fixed dates of commissioning.

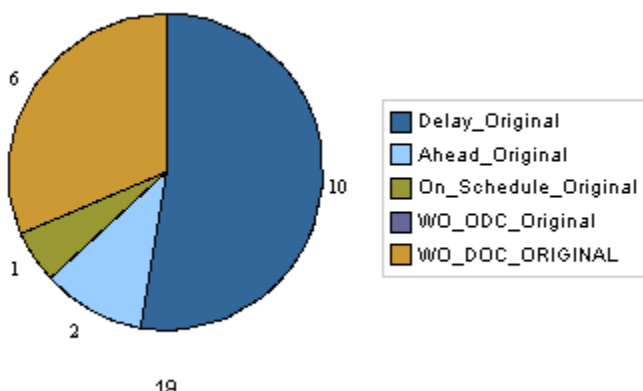

III. Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 16242.52 crore but this was subsequently revised to Rs. 18554.09 crore implying a cost overrun of 14.2%. The expenditure incurred on these projects till October, 2012 is Rs. 8357.06 crore, which is 45% of the revised cost of the projects.

Figures are in Rs. Crore

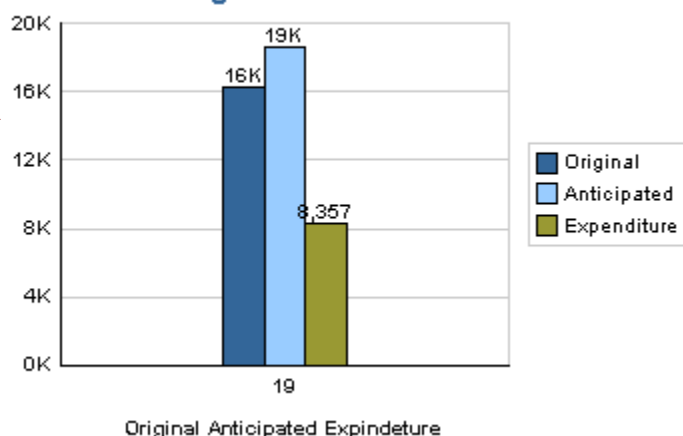

Sector wise current status of projects on theFlash Report

Road Transport & Highways


I. Current Status:

Number of Projects	146
Number of Projects On Schedule	54
Number of Projects Delayed	86

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 146 projects, 54 projects are on schedule and 86 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

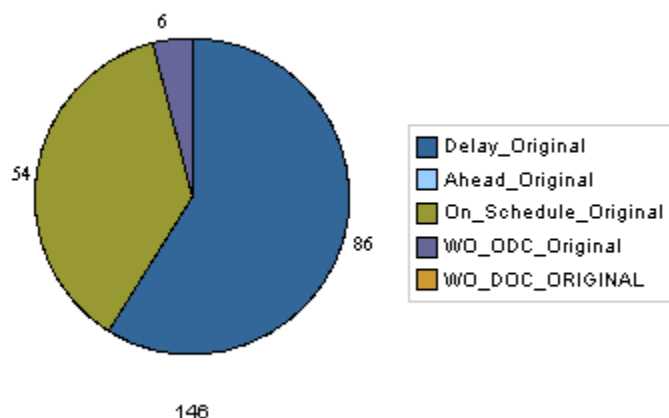

III. Investment Scenario

The Total Original cost of implementation of 146 projects when sanctioned, was of the order of Rs. 94054.5 crore but this was subsequently revised to Rs. 95488.69 crore implying a cost overrun of 1.5%. The expenditure incurred on these projects till October, 2012 is Rs. 68405.81 crore, which is 71.6% of the revised cost of the projects.

Figures are in Rs. Crore

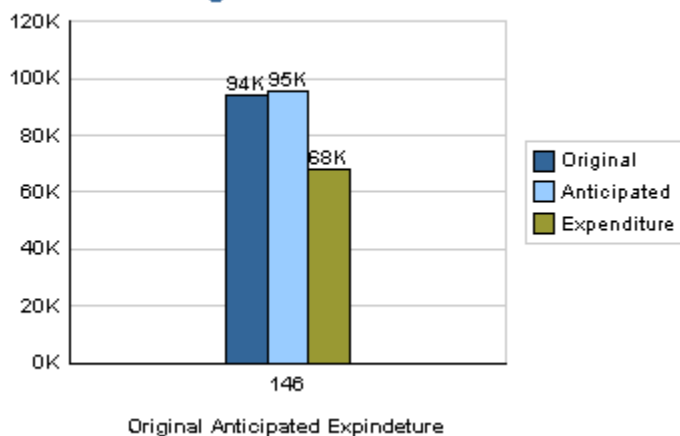

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	127
Number of Projects On Schedule	12
Number of Projects Delayed	39
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	20
Number of Projects Without Date Of Commissioning	55

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 127 projects, 1 project are ahead of schedule, 12 projects are on schedule and 39 projects are delayed .55 projects do not have fixed dates of commissioning.20 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

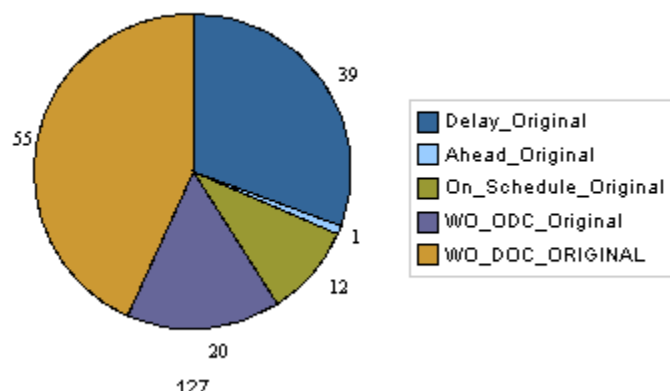

III. Investment Scenario

The Total Original cost of implementation of 127 projects when sanctioned, was of the order of Rs. 64518.68 crore but this was subsequently revised to Rs. 148474.81 crore implying a cost overrun of 130.1%. The expenditure incurred on these projects till October, 2012 is Rs. 64231.67 crore, which is 43.3% of the revised cost of the projects.

Figures are in Rs. Crore

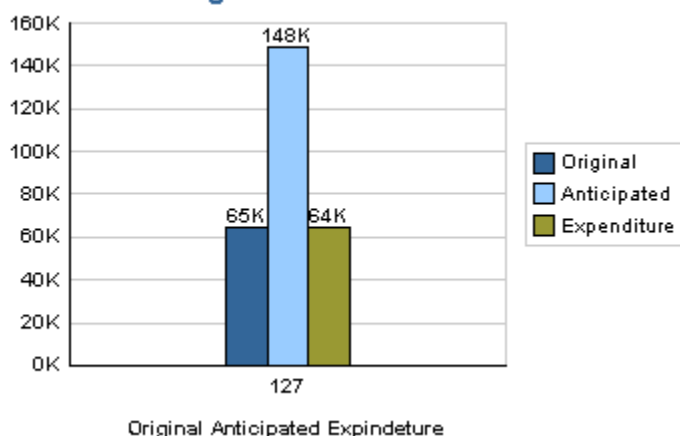

Sector wise current status of projects on theFlash Report

Power


I. Current Status:

Number of Projects	98
Number of Projects On Schedule	45
Number of Projects Delayed	51

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 98 projects, 45 projects are on schedule and 51 projects are delayed .1 project do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

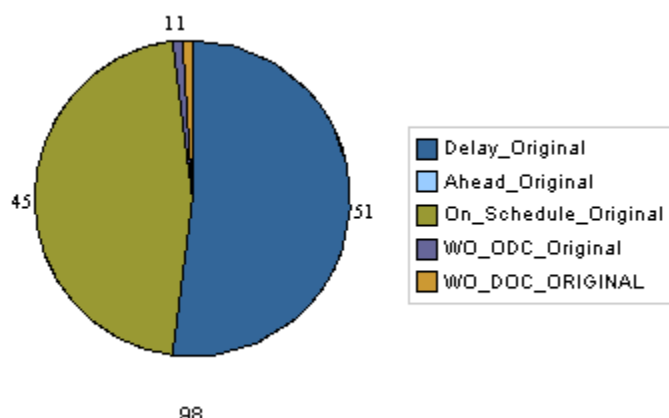

III. Investment Scenario

The Total Original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 231379.54 crore but this was subsequently revised to Rs. 245377.17 crore implying a cost overrun of 6%. The expenditure incurred on these projects till October, 2012 is Rs. 106612.44 crore, which is 43.4% of the revised cost of the projects.

Figures are in Rs. Crore

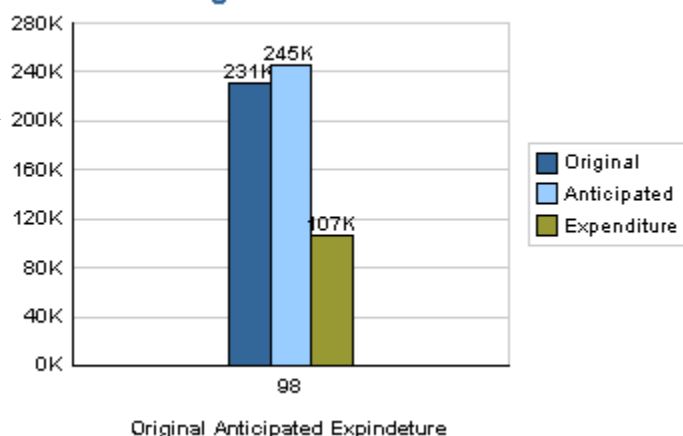

Sector wise current status of projects on theFlash Report

Petroleum


I. Current Status:

Number of Projects	69
Number of Projects On Schedule	19
Number of Projects Delayed	40

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	9

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 69 projects, 19 projects are on schedule and 40 projects are delayed .9 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

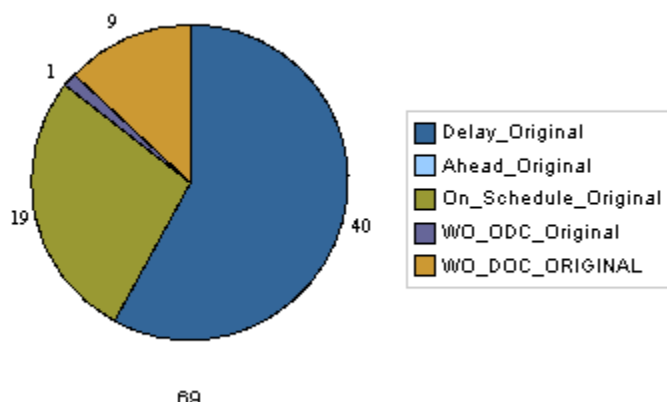

III. Investment Scenario

The Total Original cost of implementation of 69 projects when sanctioned, was of the order of Rs. 174399.19 crore but this was subsequently revised to Rs. 182915.59 crore implying a cost overrun of 4.9%. The expenditure incurred on these projects till October, 2012 is Rs. 82606.87 crore, which is 45.2% of the revised cost of the projects.

Figures are in Rs. Crore

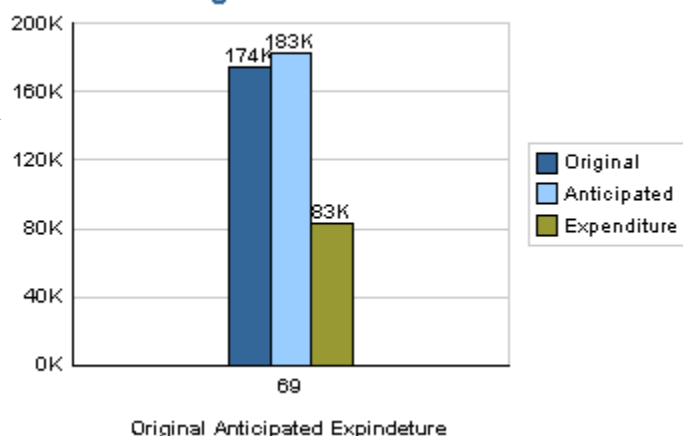

Sector wise current status of projects on theFlash Report


Steel

I. Current Status:

Number of Projects	17
Number of Projects On Schedule	3
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 17 projects, 1 project are ahead of schedule, 3 projects are on schedule and 10 projects are delayed .3 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

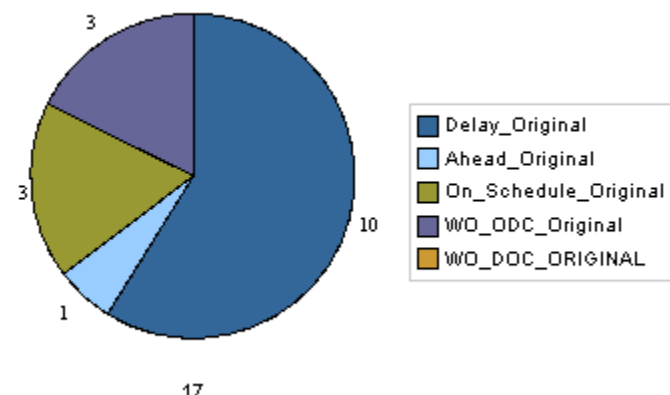

III. Investment Scenario

The Total Original cost of implementation of 17 projects when sanctioned, was of the order of Rs. 65285.87 crore but this was subsequently revised to Rs. 71443.41 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till October, 2012 is Rs. 44375.57 crore, which is 62.1% of the revised cost of the projects.

Figures are in Rs. Crore

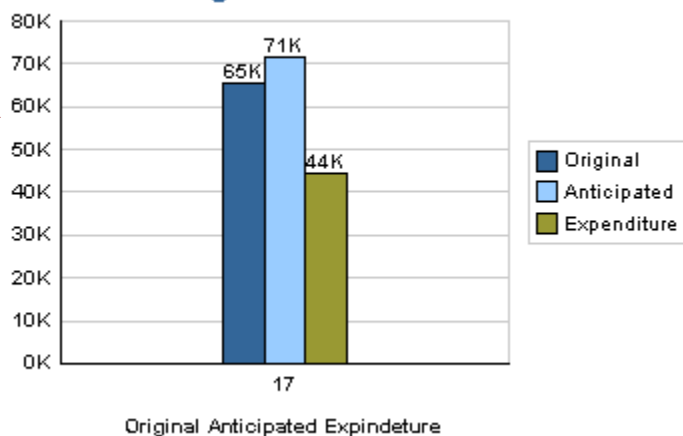

Sector wise current status of projects on theFlash Report


Fertilisers

I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 1 project are ahead of schedule, 2 projects are on schedule and 3 projects do not have fixed dates of commissioning.

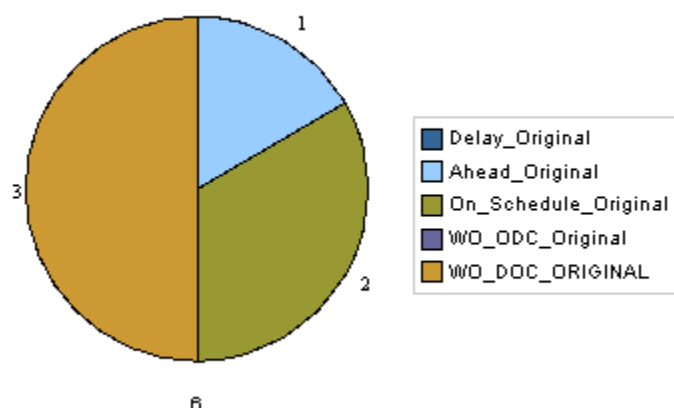

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5153.66 crore but this was subsequently revised to Rs. 5153.66 crore implying a cost overrun of 0%. The expenditure incurred on these projects till October, 2012 is Rs. 2875.03 crore, which is 55.8% of the revised cost of the projects.

Figures are in Rs. Crore

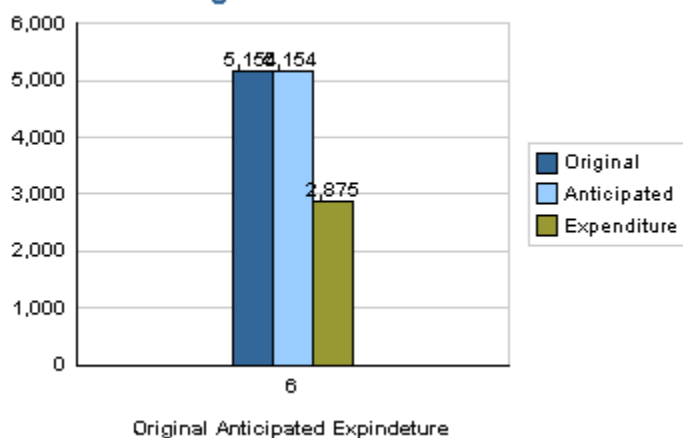

Sector wise current status of projects on theFlash Report

Coal


I. Current Status:

Number of Projects	51
Number of Projects On Schedule	30
Number of Projects Delayed	20

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 51 projects, 30 projects are on schedule and 20 projects are delayed .1 project do not have fixed dates of commissioning.

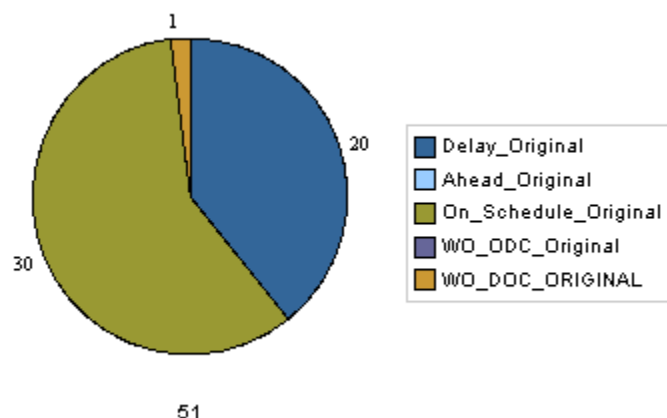

III. Investment Scenario

The Total Original cost of implementation of 51 projects when sanctioned, was of the order of Rs. 36056.46 crore but this was subsequently revised to Rs. 37312.25 crore implying a cost overrun of 3.5%. The expenditure incurred on these projects till October, 2012 is Rs. 13173.9 crore, which is 35.3% of the revised cost of the projects.

Figures are in Rs. Crore

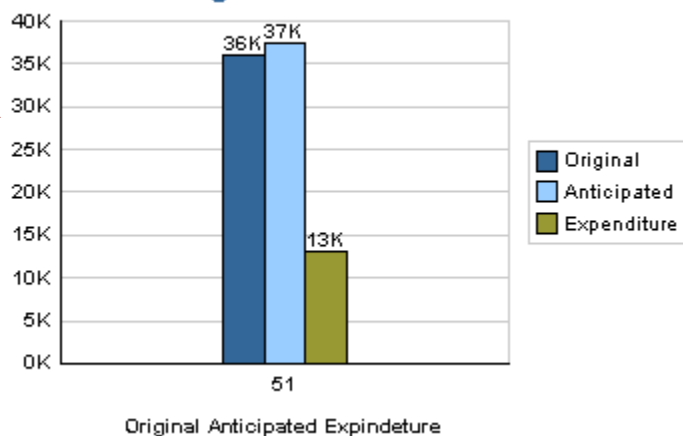

Sector wise current status of projects on theFlash Report

Civil Aviation


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project do not have fixed dates of commissioning.

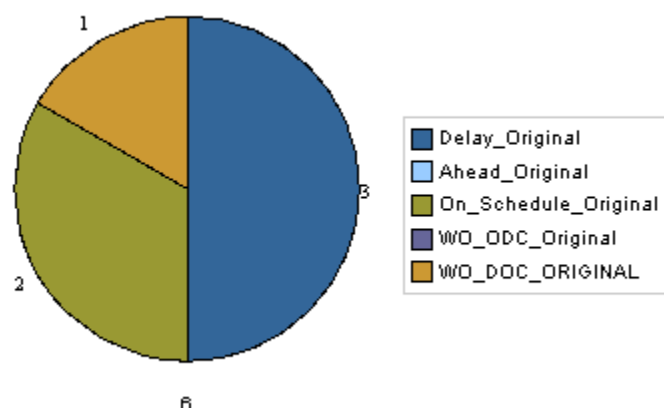

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5473.58 crore but this was subsequently revised to Rs. 6063.07 crore implying a cost overrun of 10.8%. The expenditure incurred on these projects till October, 2012 is Rs. 4593.91 crore, which is 75.8% of the revised cost of the projects.

Figures are in Rs. Crore

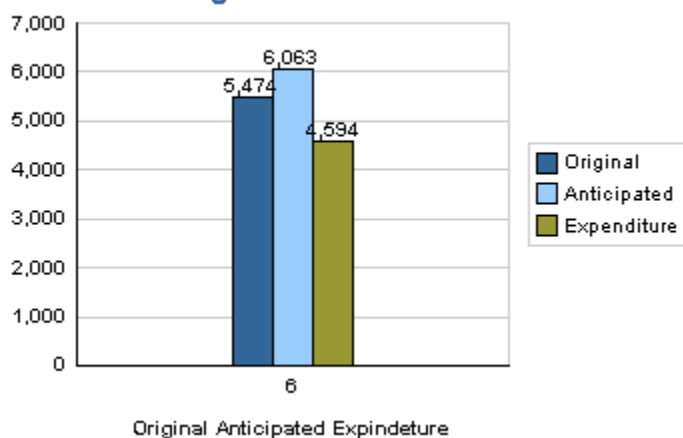

Sector wise current status of projects on theFlash Report

Atomic Energy

I. Current Status:


Number of Projects 5

Number of Projects Delayed 3

Number of Projects Without Date Of Commissioning 2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 3 projects are delayed .2 projects do not have fixed dates of commissioning.

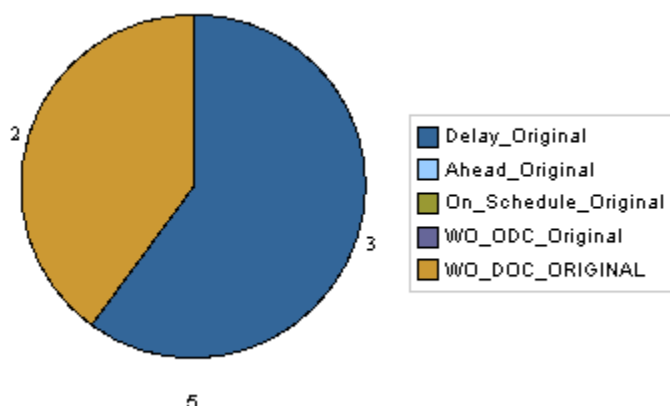

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 41548.29 crore but this was subsequently revised to Rs. 47832.29 crore implying a cost overrun of 15.1%. The expenditure incurred on these projects till October, 2012 is Rs. 19269.24 crore, which is 40.3% of the revised cost of the projects.

Figures are in Rs. Crore

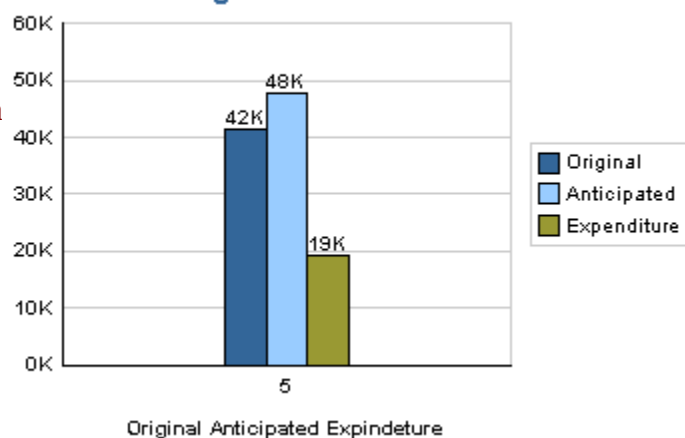

ANNEXURES

CENTRAL SECTOR PROJECTS as on 01.11.2012

SN	STATE_NAME	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	37	31485.25	38910.85	23370.24
2	Arunachal Pr.	4	9512.22	14152.72	8545.47
3	Assam	35	22260.93	33844.43	23141.21
4	Bihar	30	26901.24	34657.04	22796.18
5	Chhatisgarh	24	46715.19	47998.27	14654.67
6	Delhi	5	38572.55	38552.96	1060.09
7	Goa	1	335.61	335.61	146.09
8	Gujarat	22	31111.55	31313.49	8618.58
9	Haryana	10	5496.60	7438.41	7607.89
10	Himachal Pr.	5	13355.57	15414.93	12735.44
11	J and K	10	14926.96	34825.56	13820.30
12	Jharkhandd	23	14447.40	18428.98	8082.74
13	Karnataka	24	44634.83	54121.25	20479.07
14	Kerala	6	19694.67	21136.22	5052.64
15	Madhya pradesh	24	19741.92	19891.96	9289.71
16	Maharashtra	54	97399.54	113680.17	52347.30
17	Manipur	1	727.56	4444.00	937.59
18	Meghalaya	2	762.00	762.00	652.09
19	Mizoram	2	1532.97	3307.11	365.25
20	Multi State	102	139667.04	145358.21	65249.58
21	Nagaland	1	850.00	850.00	8.45
22	Orissa	30	57409.06	60948.97	33996.56
23	Punjab	7	4836.20	5777.97	4201.18
24	Rajasthan	14	26544.10	26138.31	9492.91
25	Sikkim	2	1648.94	3690.04	237.83
26	Tamil Nadu	32	51275.95	62055.82	35984.77
27	Tripura	3	1522.39	2053.23	948.88
28	Uttar Pradesh	23	18822.90	22660.67	11564.45
29	Uttaranchal	3	5619.21	6559.64	1994.38
30	West Bengal	27	42286.11	54607.56	27744.01
TOTAL		563	790096.46	923916.38	425125.55

LIST OF PROJECTS MORE THAN COST

SN	PROJECT_TITLE	AGENCY	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	NPCIL	Atomic Energy	13171.00	0.00	15030.00
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	AAI	Civil Aviation	1942.51	0.00	2143.57
3	RESITMENT OF MARKETING INSTALATION AT VISAKH	HPCL	Petroleum	756.00	0.00	904.59
4	CHUTAK HYDRO-ELECTRIC PROJECT	NHPC	Power	621.26	0.00	764.03
5	NIMOO BAZGO HYDROELECTRIC PROJECT	NHPC	Power	611.01	0.00	794.58
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	NHPC	Power	1061.38	0.00	1212.87
7	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	NHPC	Power	768.92	0.00	1598.46
8	URI H.E.P STAGE -II (NHPC)	NHPC	Power	1729.29	0.00	1825.39
9	KOLDAM HEP (NTPC)	NTPC	Power	4527.15	0.00	4548.00
10	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP	PGCIL	Power	557.24	0.00	595.00
11	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	(NR)	Railways	248.44	576.27	897.49
12	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	(NR)	Railways	409.00	625.30	835.55
13	JIND-SONEPAT (NL),NR	(NR)	Railways	190.81	238.56	425.36
14	REWARI-ROHTAK (NL),NR	(NR)	Railways	149.38	330.23	494.36
15	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	(NR)	Railways	2500.00	2500.00	8521.82
16	AMRAVATI-NARKHER NL(CR)	CR	Railways	120.90	284.27	538.10
17	LANJHIGARH-JUNAGARH NL(ECOR)	ECOR	Railways	100.00	142.98	205.16
18	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	ECR	Railways	233.00	501.69	662.51
19	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	Railways	114.01	332.92	401.54
20	MUMBAI URBAN TRANSPORT PROJECT PHASE-I	MRTP	Railways	3125.20	4174.40	4334.00
21	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	MRTP	Railways	907.69	3156.32	3225.24
22	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	NCR	Railways	108.00	214.09	250.82
23	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	NCR	Railways	158.77	432.46	558.07
24	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	NEFR	Railways	170.00	170.00	392.85
25	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	NEFR	Railways	1000.00	1500.00	2501.02

26	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	NEFR	Railways	156.00	156.00	279.98
27	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NEFR	Railways	727.56	727.53	937.59
28	KATIHAR - JOGBANI (GC)(NEFR)	NEFR	Railways	100.00	492.98	732.83
29	Lumding-SILCHAR Jiribam, Badarpur- Baraigram Kumarghat national project	NEFR	Railways	1676.31	1676.31	3195.95
30	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NEFR	Railways	733.00	733.00	1298.65
31	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	NEFR	Railways	915.70	915.70	1476.55
32	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER)	NER	Railways	381.17	381.17	603.58
33	KANPUR-KASGANJ-MATHURA(GC),NER	NER	Railways	395.00	1062.36	1389.02
34	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	NER	Railways	323.40	323.40	506.14
35	ELECTRIFICATION OF MORADABAD-ROZA	RE	Railways	129.17	0.00	227.48
36	BILASPUR-URKURA (DL)	RVNL	Railways	151.52	0.00	327.08
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	Railways	133.41	207.00	218.22
38	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	RVNL	Railways	240.00	0.00	413.37
39	RAICHUR-GUNTAKAL(DL)(SCR)	RVNL	Railways	136.62	0.00	236.81
40	RAJATGARH-BARANG(LD),ECOR	RVNL	Railways	166.16	0.00	253.88
41	RENIGUNTA-GUNTAKAL(RE)	RVNL	Railways	168.34	0.00	358.98
42	GADWAL - RAICHUR (NL), SCR	SCR	Railways	92.63	228.09	260.33
43	NANDYAL-YERRAGUNTALA(NL),SCR	SCR	Railways	155.74	429.49	634.02
44	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	SCR	Railways	124.43	495.68	590.02
45	RANCHI-LOHARDAGA(GC),SER	SER	Railways	194.07	194.07	301.82
46	CALICUT-MANGALORE (DL) (SR)	SR	Railways	240.00	0.00	600.41
47	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	SR	Railways	343.17	343.17	569.32
48	KARUR-SALEM(NL),SR	SR	Railways	155.55	155.00	737.02
49	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	Railways	100.00	100.00	518.10
50	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	SWR	Railways	295.00	412.91	542.29
51	KOTTUR-HARIHAR(NL),(SWR)	SWR	Railways	65.94	302.23	335.74
52	2 LANNING OF MOKAMA-MUNGER	NHAI	Road Transport & Highways	351.54	0.00	352.68
53	2-LANNING OF SHILONG BYPASS	NHAI	Road Transport & Highways	226.00	0.00	248.04

54	4 LANNING OF AHMEDABAD TO GODHARA	NHAI	Road Transport & Highways	1008.50	0.00	1097.80
55	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	NHAI	Road Transport & Highways	367.49	0.00	453.68
56	AMRITSAR-PATHANKOT	NHAI	Road Transport & Highways	705.00	0.00	1161.20
57	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	NHAI	Road Transport & Highways	221.82	0.00	289.52
58	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	NHAI	Road Transport & Highways	190.00	0.00	260.19
59	Armur to kadloor yellareddy	NHAI	Road Transport & Highways	390.56	0.00	631.65
60	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	NHAI	Road Transport & Highways	237.80	0.00	251.66
61	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	NHAI	Road Transport & Highways	195.00	0.00	209.66
62	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	Road Transport & Highways	217.61	0.00	225.26
63	Chennai-Tada(Six lane)	NHAI	Road Transport & Highways	353.37	0.00	376.65
64	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	NHAI	Road Transport & Highways	572.30	0.00	712.18
65	DAKOBA TO NAGAON (NH-36)(NHAI)	NHAI	Road Transport & Highways	225.00	0.00	282.86
66	DELHI/ HARYANA BORDER TO ROHTAK	NHAI	Road Transport & Highways	486.00	0.00	593.31

67	DHARAMTUL TO SONAPUR (AS-19)	NHAI	Road Transport & Highways	200.00	0.00	231.15
68	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	NHAI	Road Transport & Highways	160.00	0.00	187.69
69	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	NHAI	Road Transport & Highways	232.45	0.00	274.33
70	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER	NHAI	Road Transport & Highways	464.00	0.00	535.49
71	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	NHAI	Road Transport & Highways	332.94	0.00	399.87
72	GANJAM-ICCHAPURUM,NH-5(NHAI)	NHAI	Road Transport & Highways	263.27	0.00	271.86
73	GUWAHATI TO NALBARI (AS-5)	NHAI	Road Transport & Highways	198.16	0.00	211.16
74	GWALIOR BYPASS, NH-75,3	NHAI	Road Transport & Highways	300.93	0.00	302.72
75	Gurgaon-Kotputli Km 42.70 to 54.4 Km	NHAI	Road Transport & Highways	1673.70	0.00	2731.00
76	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	NHAI	Road Transport & Highways	220.00	0.00	279.21
77	Hazaribagh-Ranchi	NHAI	Road Transport & Highways	625.07	0.00	862.54
78	Hungund-Surathkal and Mangalore-Knt/Kerala Border	NHAI	Road Transport & Highways	946.00	0.00	1394.40
79	Hyderabad-Vijaywada Km. 40 to 221.50 Km	NHAI	Road Transport & Highways	1740.00	0.00	1903.30

80	Hyderabad-yadgiri N.H no-202	NHAI	Road Transport & Highways	388.00	0.00	515.85
81	INDORE-DEWAS(NH-3)	NHAI	Road Transport & Highways	325.00	0.00	387.71
82	JAIPUR-REENGUS	NHAI	Road Transport & Highways	267.81	0.00	541.88
83	JHAJHARPUR TO DARBANGA (BR-7)	NHAI	Road Transport & Highways	340.00	0.00	575.27
84	JHANSI TO LALITPUR, NH-25,26	NHAI	Road Transport & Highways	355.06	0.00	499.70
85	Jaipur-Tonk-Deoli	NHAI	Road Transport & Highways	792.06	0.00	1517.00
86	KOTA BYPASS,RJ-4, NH-76 (NHAI)	NHAI	Road Transport & Highways	275.00	0.00	279.36
87	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	NHAI	Road Transport & Highways	240.00	0.00	294.29
88	KUNDUPUR-SURATHKAL & MANGLORE	NHAI	Road Transport & Highways	671.00	0.00	737.54
89	Kishangarh-Ajmer-Beawer	NHAI	Road Transport & Highways	795.00	0.00	1037.50
90	MP/Maharashtra Border-Dhula	NHAI	Road Transport & Highways	835.00	0.00	1068.70
91	NAGAON TO DHARAMTUL (AS-2)	NHAI	Road Transport & Highways	264.72	0.00	287.75
92	NAGPUR-KONDHALI,NH-6(NHAI)	NHAI	Road Transport & Highways	168.00	0.00	457.30

93	NALBARI T BIJNI (AS-7)	NHAI	Road Transport & Highways	208.00	0.00	270.92
94	NALBARI TO BIJNI (AS-6)	NHAI	Road Transport & Highways	225.00	0.00	248.90
95	NALBARI TO BIJNI (AS-8)	NHAI	Road Transport & Highways	200.00	0.00	276.00
96	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	NHAI	Road Transport & Highways	557.00	0.00	930.92
97	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0	NHAI	Road Transport & Highways	340.68	0.00	388.01
98	PANIPAT-ROHTAK	NHAI	Road Transport & Highways	807.00	0.00	931.51
99	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	NHAI	Road Transport & Highways	940.00	0.00	1158.80
100	Panipat-Jalandhar 6 lane (Km 96 to 387.1 km)	NHAI	Road Transport & Highways	1108.00	0.00	3462.40
101	Pune-sholapur, pkg1	NHAI	Road Transport & Highways	1110.00	0.00	1802.10
102	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	NHAI	Road Transport & Highways	251.03	0.00	312.76
103	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA)	NHAI	Road Transport & Highways	229.91	0.00	267.50
104	ROHTAK-BAWAL	NHAI	Road Transport & Highways	650.00	0.00	751.40
105	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI)	NHAI	Road Transport & Highways	203.43	0.00	240.12

106	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	NHAI	Road Transport & Highways	941.00	0.00	1901.00
107	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	NHAI	Road Transport & Highways	157.47	0.00	206.78
108	SONAPUR TO GUWAHTI (AS-3)	NHAI	Road Transport & Highways	245.00	0.00	491.21
109	Surat- Dahisar(Six Lane) Km 263 to Km 502	NHAI	Road Transport & Highways	1693.75	0.00	2674.90
110	THANJAUR-TRICHY,NH-67(NHAI)	NHAI	Road Transport & Highways	280.00	0.00	581.49
111	TRICHY - KORUR NH-67	NHAI	Road Transport & Highways	516.00	0.00	760.07
112	Talegaon-amravati	NHAI	Road Transport & Highways	567.00	0.00	731.28
113	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	RVNL	Shipping & Ports	245.67	298.17	326.08
114	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT	RINL	Steel	230.00	0.00	253.16
115	COKE OVEN BATTERY NO. 4 PHASE-II	RINL	Steel	108.00	0.00	116.79
116	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL)	RINL	Steel	8692.00	0.00	9838.39
	TOTAL			82907.95	24813.75	125058.96

Sectorwise Summary of Project Without Original Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Petroleum	1	2,615.69	.00	2,615.69	1,965.44
Power	1	421.01	623.44	623.44	368.16
Railways	20	5,946.98	8,582.61	16,135.26	8,299.25
Road Transport & Highways	6	4,069.00	.00	4,069.00	3,424.27
Steel	3	1,657.88	.00	1,657.88	321.17
Grand total	31	14,710.56	9,206.05	25,101.27	14,378.29

List of project Without Original Date of Commissioning

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Steel</u>								
1	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00	572.00	196.51	-	04/2013	-	13/19
2	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55	898.55	124.66	-	11/2013	-	17/21
3	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33	187.33	-	-	12/2013	-	0/1
	Total		1,657.88	1,657.88	321.17				30/41
	<u>Petroleum</u>								
4	EURO-IV DHD T - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69	2,615.69	1,965.44	-	11/2012	-	116/116
	Total		2,615.69	2,615.69	1,965.44				116/116
	<u>Power</u>								
5	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	368.16	- 07/2013	07/2013	0(R3)	6/29
	Total		421.01	623.44	368.16				6/29
	<u>Railways</u>								
6	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	712.00	737.02	-	10/2012	-	0/0
7	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	335.74	-	12/2012	-	0/0
8	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	900.00	569.32	-	12/2012	-	0/0
9	CONSTRUCTION OF NEW LINE FROM HARMATHI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	415.73	279.98	-	12/2012	-	0/0
10	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	944.55	542.29	-	01/2013	-	0/0
11	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	218.19	165.46	-	02/2013	-	0/0
12	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	2,820.00	176.76	-	03/2013	-	0/0
13	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	202.01	-	03/2013	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,389.02	- -	03/2013	-	0/0
15	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	96.67	- -	03/2013	-	0/0
16	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.00	769.62	- -	03/2013	-	0/6
17	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	1,100.00	237.18	- -	03/2013	-	0/0
18	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	1,717.29	1,476.55	- -	03/2013	-	0/0
19	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	115.80	- -	03/2013	-	0/0
20	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
21	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	750.89	506.14	- -	03/2014	-	0/1
22	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	146.32	- -	03/2014	-	0/0
23	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	114.85	- -	03/2014	-	0/0
24	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	242.39	- -	03/2015	-	0/0
25	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
Total			5,946.98 -	16,135.26	8,299.25				0/7
<u>Road Transport & Highways</u>									
26	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,394.40	- -	03/2013	-	3/3
27	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	737.54	- -	03/2013	-	2/3
28	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	166.98	- -	04/2013	-	2/2
29	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	351.33	- -	06/2013	-	1/1
30	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	418.89	- -	10/2013	-	2/2
31	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	355.13	- -	12/2013	-	0/1
Total			4,069.00 -	4,069.00	3,424.27				10/12

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Grand Total			14,710.56	25,101.27	14,378.29				162/205

Sectorwise Summary Without Date of Commissioning

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	2	4,598.29	.00	6,783.29	1,084.24
Civil Aviation	1	1,808.00	2,015.00	2,015.00	1,724.62
Coal	1	249.03	.00	249.03	48.63
Fertilisers	3	1,088.00	.00	1,088.00	425.03
Petroleum	9	8,836.80	2,568.00	7,951.80	4,036.17
Power	1	596.45	1,007.16	1,007.16	850.63
Railways	55	18,384.75	29,617.92	44,733.51	24,056.97
Shipping & Ports	6	4,195.76	1,869.77	5,207.58	1,356.59
Telecommunications	6	2,997.75	.00	2,934.67	111.64
Urban Development	1	114.18	173.08	173.08	0.00
Grand total	85	42,869.01	37,250.93	72,143.12	33,694.52

List of project Without Date of Commissioning

Date of Commissioning					
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
<u>Atomic Energy</u>					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVINI,Tamil Nadu	09/2003	3,492.00	09/2010	-
2	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-
	Total		4,598.29		
<u>Civil Aviation</u>					
3	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00	01/2011	02/2012
	Total		2,015.00	02/2012	
<u>Coal</u>					
4	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	03/2012	-
	Total		249.03		
<u>Fertilisers</u>					
5	DUMMY PROJECT FOR FERTILISERS - [N08000002]RCF,Multi State	04/2007	325.00	11/2009	10/2011
6	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	07/2011	04/2012
7	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	07/2011	07/2012
	Total		1,088.00		
<u>Petroleum</u>					
8	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00	-	08/2012
9	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	03/2012	09/2012
10	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	2,174.00	09/2012	09/2012
11	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	1,793.00	-	09/2012
12	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	333.99	-	09/2012
13	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	267.00	09/2012	09/2012
14	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	1,584.00	-	-
15	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	246.81	04/2012	-
			224.00	-	-
			394.00	08/2011	

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
16	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL, Multi State	06/2009	348.00 -	03/2012 08/2012	-
	Total		8,836.80 -		
<u>Power</u>					
17	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		596.45 -		
<u>Railways</u>					
18	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005
19	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258](NR), Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
20	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
21	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
22	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
23	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRT, West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
24	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010
25	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
26	REWARI-ROHTAK (NL), NR - [220100279](NR), Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011
27	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011
28	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR, Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011
29	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR, Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011
30	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011
31	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011
32	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
33	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
34	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR, Multi State	04/1985	158.77 432.46	03/1994 -	12/2011
35	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012
36	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012
37	Dakshin-barasal-lakshmikantapur - [N22000116]ER, West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
38	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012
39	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
40	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
41	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012
42	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
43	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
44	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012
45	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012
46	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012
47	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012
48	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-
49	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	- -	-
50	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-
51	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	- 09/2009	-
52	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 418.17	- -	-
53	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	02/2006 -	-
54	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
55	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	02/2010 -	-
56	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-
57	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	07/2012 -	-
58	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
59	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 2,957.21	07/2005 -	-
60	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
61	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
62	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
63	HAPIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
64	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
65	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
66	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
67	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
68	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
69	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
70	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
71	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
72	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
	Total		18,384.75 -		
<u>Shipping & Ports</u>					
73	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008
74	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	- 01/2009	01/2009
75	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
76	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
77	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 09/2012	09/2012
78	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
	Total		4,195.76 -		
<u>Telecommunications</u>					
79	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011
80	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-
81	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-
82	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
83	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-
84	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
	Total		2,997.75 -		
<u>Urban Development</u>					

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated
1	2	3	4	5	6
85	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		114.18 -		
Grand Total			42,869.01		

List of Projects Ahead of Schedule

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Fertilisers</u>						
1	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT [N08000006]	1/2010	1,478.63 -	1,478.63	890.00	01/2013 12/2012	12/2012
	Total		1,478.63 -	1,478.63	890.00		
	<u>Steel</u>						
2	Expansion of Rourkela Steel Plant - [N12000056]	9/2008	11,812.00 11,812.00	11,812.00	8,028.81	11/2013 -	03/2013
	Total		11,812.00 -	11,812.00	8,028.81		
	<u>Railways</u>						
3	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]	4/2008	1,389.62 -	1,389.62	397.15	03/2014 -	03/2013
	Total		1,389.62 -	1,389.62	397.15		
	<u>Shipping & Ports</u>						
4	Acquistion of three(3) nos of 6500TEU Cellular container vessels from M/S stx shipbuilding co. ltd. - [N25000052]	10/2010	1,028.10 1,012.23	1,028.10	371.96	12/2013 10/2013	10/2013
5	Setting up of Single Point Mooring (SPM) and allied facilities off Veera in Gulf of Kutch on BOT bas - [N25000060]	2/2011	830.00 -	621.53	-	05/2013 -	03/2013
	Total		1,858.10 -	1,649.63	371.96		
	Grand Total		16,538.35	16,329.88	9,687.92		

Sectorwise Summary On Schedule

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Civil Aviation	2	1,078.00	.00	1,078.00	394.43
Coal	30	18,249.83	.00	17,830.31	5,716.16
Fertilisers	2	2,587.03	.00	2,587.03	1,560.00
Petroleum	19	52,299.48	.00	52,066.08	4,623.82
Power	45	94,738.12	.00	94,738.12	10,664.00
Railways	12	13,108.19	654.51	17,730.65	2,012.96
Road Transport & Highways	54	48,562.38	.00	48,202.38	23,989.98
Shipping & Ports	1	966.46	.00	994.82	248.23
Steel	3	842.10	.00	842.10	11.99
Urban Development	2	37,736.00	.00	37,736.00	992.63
Grand total	170	270,167.59	654.51	273,805.49	50,214.20

List of On schedule Projects

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	GAGAN PROJECT - [N04000065	9/2008	626.00 -	626.00	373.07	06/2013 -	06/2013
2	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070	2/2011	452.00 -	452.00	21.36	03/2015 -	03/2015
	Total		1,078.00 -	1,078.00	394.43		
	<u>Coal</u>						
3	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093	6/2010	2,675.67 -	2,675.67	1,391.20	03/2014 -	03/2014
4	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094	12/2009	1,943.66 -	1,943.66	1,231.48	03/2014 -	03/2014
5	KRISHNASHILA (NCL) (4MTY) - [N06000007	6/2011	789.88 -	741.62	334.67	03/2013 -	03/2013
6	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	162.06	03/2015 03/2015	03/2015
7	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	40.35	03/2014 03/2014	03/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	115.91	03/2017 -	03/2017
9	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	70.82	03/2015 -	03/2015
10	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	89.50	03/2016 -	03/2016
11	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081	12/2009	321.42 -	321.50	204.70	03/2014 -	03/2014
12	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	27.95	03/2015 -	03/2015
13	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.63 -	479.63	110.91	03/2013 -	03/2013
14	RAJMAHAL OC EXP. - [N06000056	9/2009	153.82 -	153.82	24.39	03/2014 -	03/2014
15	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
16	CHURCHA UG - [N06000046	6/2008	462.35 -	462.35	263.73	03/2014 -	03/2014
17	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
18	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.49	03/2016 -	03/2016
19	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	39.81	03/2016 -	03/2016
20	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
21	Muraidih UG Turn-key Project - [N06000096]	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
22	JALAGAM VENGALA RAO OCP - [N06000094]	7/2011	447.06 -	447.06	-	03/2015 -	03/2015
23	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
24	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	1.51	03/2018 03/2018	03/2018
25	Kistaram OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
26	KARMA OCP - [N06000088]	6/2009	162.46 -	162.46	30.89	03/2014 -	03/2014
27	Rajrappa RCE OCP - [N06000087]	12/2009	510.85 -	510.85	269.00	03/2016 -	03/2016
28	Purnadih OCP - [N06000085]	7/2008	210.98 -	210.98	87.89	03/2013 -	03/2013
29	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]	12/2007	457.77 -	457.77	111.49	03/2013 -	03/2013
30	JALLARAM SHAFT PROJECT - [N06000025]	9/2007	467.78 -	467.78	12.31	03/2013 -	03/2013
31	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	374.26	03/2016 03/2016	03/2016
32	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	6/2008	1,188.31 -	1,188.31	674.36	03/2013 -	03/2013
	Total		18,249.83 -	17,830.31	5,716.16		
<u>Fertilisers</u>							
33	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT - [N08000004]	1/2010	1,292.84 -	1,292.84	791.00	01/2013 -	01/2013
34	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGEOVER PROJECT - [N08000005]	1/2010	1,294.19 -	1,294.19	769.00	01/2013 -	01/2013
	Total		2,587.03 -	2,587.03	1,560.00		
<u>Petroleum</u>							
35	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]	4/2008	825.00 -	1,827.00	611.55	04/2013 04/2013	04/2013
36	Development of WO-16 Cluster Fields - [N16000105]	6/2010	2,523.00 -	2,523.00	336.22	01/2014 -	01/2014
37	Development of C-26 Cluster Fields - [N16000133]	3/2012	2,592.17 -	2,592.17	-	05/2014 -	05/2014
38	Heera and South Heera Redevelopment Ph-II - [N16000132]	3/2012	5,608.40 -	5,608.40	-	05/2015 -	05/2015
39	Integrated Development of B-127 fields - [N16000131]	12/2011	2,059.63 -	2,059.63	-	03/2015 -	03/2015

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	3/2011	861.79 -	756.65	75.23	05/2013 -	05/2013
41	Ankleswar Redevelopment - [N16000122	11/2010	2,189.63 -	2,189.63	4.84	12/2014 -	12/2014
42	Mehesana Redevelopment - [N16000121	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	04/2015
43	Ahmedabad Redevelopment - [N16000120	11/2010	1,916.10 -	1,916.10	614.17	12/2014 -	12/2014
44	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112	8/2010	8,140.00 -	8,140.00	2,015.84	02/2014 -	02/2014
45	Butadiene Extraction Unit(BDEU) at Panipat - [N16000108	11/2009	341.50 -	341.50	140.89	02/2013 -	02/2013
46	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	-	06/2016 -	06/2016
47	Integrated Refinery Expansion Project - [N16000143	1/1999	14,225.00 -	14,225.00	9.21	12/2015 -	12/2015
48	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	1.07	12/2014 -	12/2014
49	IOR of B-173A Field - [N16000140	1/2012	352.49 -	352.49	-	03/2014 -	03/2014
50	BUTENE-1 PROJECT AT PANIPAT - [N16000139	2/2012	190.00 -	190.00	13.17	03/2014 -	03/2014
51	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	17.28	05/2014 -	05/2014
52	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	-	12/2014 -	12/2014
53	Wax Project - [N16000101	6/2010	576.60 -	576.60	82.54	12/2013 12/2013	12/2013
	Total		52,299.48 -	52,066.08	4,623.82		
Power							
54	Transm System for development of Pooling stn. in NR part of West Bengal & Transfer of power from BHU - [N18000077	4/2010	4,404.57 -	4,404.57	336.00	01/2015 -	01/2015
55	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087	9/2010	2,074.86 -	2,074.86	721.00	03/2013 -	03/2013
56	Northern Region system strengthening scheme-XXII - [N18000091	12/2010	209.78 -	209.78	95.20	08/2013 -	08/2013
57	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092	12/2010	1,719.52 -	1,719.52	703.70	08/2013 -	08/2013
58	Transmission system associated with krishnapatnam- Part-A - [N18000090	12/2010	779.21 -	779.21	599.30	08/2013 -	08/2013
59	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088	10/2010	182.68 -	182.68	61.30	01/2013 -	01/2013

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
60	Transmission system for phase-I generation projects in orissa-part B - [N18000093]	12/2010	2,743.19 -	2,743.19	896.20	12/2013 -	12/2013
61	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]	3/2011	2,569.25 -	2,569.25	781.50	03/2014 -	03/2014
62	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]	1/2012	1,422.85 -	1,422.85	125.90	01/2015 -	01/2015
63	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]	12/2011	1,746.65 -	1,746.65	50.40	08/2014 -	08/2014
64	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV [N18000115]	12/2011	297.33 -	297.33	22.90	08/2014 -	08/2014
65	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]	12/2011	552.44 -	552.44	90.20	02/2014 -	02/2014
66	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]	12/2011	2,422.66 -	2,422.66	83.20	08/2014 -	08/2014
67	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPs GENERATION PROJECTS IN CHATTISGARH - [N18000112]	11/2011	2,127.51 -	2,127.51	263.20	07/2014 -	07/2014
68	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]	8/2011	1,637.34 -	1,637.34	300.60	08/2014 -	08/2014
69	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	487.49	63.60	06/2014 -	06/2014
70	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]	8/2011	1,391.97 -	1,391.97	495.80	12/2013 -	12/2013
71	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]	12/2011	901.77 -	901.77	64.50	08/2014 -	08/2014
72	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]	3/2012	206.44 -	206.44	25.50	06/2014 -	06/2014
73	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]	3/2012	9,569.76 -	9,569.76	27.70	06/2015 -	06/2015
74	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
75	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
76	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	37.10	10/2014 -	10/2014
77	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]	2/2012	324.33 -	324.33	2.20	08/2014 -	08/2014
78	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	105.10	02/2015 -	02/2015

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
79	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118	1/2012	259.28 -	259.28	23.50	01/2014 -	01/2014
80	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	-	12/2014 -	12/2014
81	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	-	03/2015 -	03/2015
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135	9/2012	524.40 -	524.40	-	04/2015 -	04/2015
83	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	145.00	08/2015 -	08/2015
84	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	820.00	11/2016 -	11/2016
85	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	582.00	09/2016 -	09/2016
86	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	987.00	12/2016 -	12/2016
87	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	53.40	11/2014 -	11/2014
88	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129	2/2012	3,201.44 -	3,201.44	68.70	10/2014 -	10/2014
89	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	44.00	11/2014 -	11/2014
90	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106	8/2011	425.51 -	425.51	110.50	10/2013 -	10/2013
91	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105	9/2011	1,366.34 -	1,366.34	258.30	12/2013 -	12/2013
92	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104	10/2011	558.26 -	558.26	72.30	11/2013 -	11/2013
93	Common System Associated with Coastal Energen Private Limited and Ind-Barath Power(Madras) Limited L - [N18000103	9/2011	1,940.13 -	1,940.13	339.90	09/2014 -	09/2014
94	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102	7/2011	181.93 -	181.93	50.80	07/2013 -	07/2013
95	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101	5/2011	1,961.87 -	1,961.87	449.10	05/2014 -	05/2014
96	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099	3/2011	1,585.12 -	1,585.12	443.50	11/2013 -	11/2013
97	Supplementary transmission associated with vellur TPS - [N18000097	8/2010	170.36 -	170.36	51.60	04/2013 -	04/2013

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
98	Northern region system strengthening scheme XVI - [N18000094 Total	7/2010	752.64 - 94,738.12	752.64 - 94,738.12	212.30 - 10,664.00	07/2013 - -	07/2013 - -
<u>Railways</u>							
99	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	4/1995	304.00 -	968.60 -	118.28 -	12/2012 -	12/2012 -
100	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	7/1996	653.84 654.51	1,302.12 -	608.97 -	06/2013 06/2013	06/2013 -
101	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29 -	75.05 -	02/2015 -	02/2015 -
102	SEVOK RANGPO, NEFR - [N22000102	4/2008	1,339.48 -	3,380.58 -	52.63 -	12/2015 -	12/2015 -
103	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. [N22000111	4/2010	2,619.02 -	2,913.51 -	171.51 -	03/2016 -	03/2016 -
104	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) [N22000113	4/2008	653.19 -	653.46 -	215.94 -	03/2014 -	03/2014 -
105	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121	4/2008	394.14 -	404.39 -	3.77 -	03/2013 -	03/2013 -
106	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124	4/2006	850.00 -	850.00 -	8.45 -	03/2015 -	03/2015 -
107	Suratpura - Hanumangarh - Sriganganagar Guage Conversion (NWR) [N22000114	4/2008	516.23 -	516.23 -	288.62 -	03/2014 -	03/2014 -
108	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112	4/2008	829.74 -	829.74 -	7.89 -	03/2015 -	03/2015 -
109	New Work for Construction of Metro railway from NSCB Airport to New Garia VIA Rajarhat (MTP) [N22000110	4/2010	3,951.98 -	3,951.98 -	35.50 -	03/2016 -	03/2016 -
110	AGARTALA SABROOM, NL, NEFR - [N22000099 Total	4/2008	813.34 - 13,108.19	1,141.75 - 17,730.65	426.35 - 2,012.96	03/2014 - -	03/2014 - -
<u>Road Transport & Highways</u>							
111	Jaipur-Tonk-Deoli - [N24000135	6/2010	792.06 -	792.06 -	1,517.00 -	12/2012 -	12/2012 -
112	Hazaribagh-Ranchi - [N24000141	8/2010	625.07 -	625.07 -	862.54 -	01/2013 -	01/2013 -
113	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750- 356.502 KM [N24000145	11/2010	1,585.00 -	1,585.00 -	957.75 -	05/2013 -	05/2013 -
114	4-laning of Raiganj-Dalkola - [N24000204	2/2011	580.43 -	580.43 -	218.49 -	08/2013 -	08/2013 -
115	4-laning of Brahampore-Faraka - [N24000203	2/2011	998.79 -	998.79 -	560.95 -	08/2013 -	08/2013 -

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
116	4-laning of Faraka-Raiganj - [N24000202	2/2011	1,078.84 -	1,078.84	729.12	08/2013 -	08/2013
117	BAREILY-SITAPUR - [N24000200	3/2011	1,046.00 -	1,046.00	176.48	09/2013 -	09/2013
118	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	470.08	06/2014 -	06/2014
119	JAIPUR-REENGUS - [N24000198	8/2010	267.81 -	267.81	541.88	02/2013 -	02/2013
120	PANIKHOLI-RIMOLI - [N24000197	3/2012	1,410.00 -	1,410.00	152.77	09/2014 -	09/2014
121	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER [N24000196	11/2011	909.00 -	909.00	844.05	05/2014 -	05/2014
122	BHUBANESWAR TO PURI - [N24000195	3/2011	500.29 -	500.29	440.64	08/2013 -	08/2013
123	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	25.36	10/2014 -	10/2014
124	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	183.38	07/2014 -	07/2014
125	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	10.49	01/2014 -	01/2014
126	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	463.57	09/2014 -	09/2014
127	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	148.81	06/2014 -	06/2014
128	NIROLI-ROXY-RAJAMUNDA - [N24000194	7/2011	586.00 -	586.00	237.55	01/2014 -	01/2014
129	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	104.67	01/2014 -	01/2014
130	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	286.35	02/2014 -	02/2014
131	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	131.22	05/2014 -	05/2014
132	SRINAGAR TO BANIHAL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
133	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
134	4-LANNING OF CHAPRA-HAJIPUR - [N24000187	1/2011	575.00 -	575.00	456.17	07/2013 -	07/2013
135	4 LANNING OF GODHARA TO GUJARAT/MP BORDER [N24000168	3/2011	785.50 -	785.50	590.69	08/2013 -	08/2013
136	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167	12/2010	1,008.50 -	1,008.50	1,097.80	06/2013 -	06/2013
137	PATNA-MUZZAFFARPUR - [N24000165	8/2010	671.30 -	671.30	588.61	02/2013 -	02/2013
138	PUNE-SATARA(NH-4) - [N24000156	10/2010	1,724.55 -	1,724.55	1,028.20	03/2013 -	03/2013
139	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	847.12	08/2014 -	08/2014
140	MURADABAD-BAREILY - [N24000154	4/2010	1,267.00 -	1,267.00	1,264.30	06/2013 -	06/2013

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
141	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	931.51	10/2014 -	10/2014
142	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150	2/2011	193.45 -	193.45	33.97	11/2012 -	11/2012
143	DEOLI-KOTA - [N24000148	1/2011	953.00 -	593.00	390.90	07/2013 -	07/2013
144	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	40.11	04/2014 -	04/2014
145	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	425.90	03/2014 -	03/2014
146	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	822.95	05/2014 -	05/2014
147	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	686.10	03/2014 -	03/2014
148	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	248.04	02/2014 -	02/2014
149	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	404.05	01/2014 -	01/2014
150	SAMAIKHALI - GANDHIDHAM - [N24000179	9/2010	805.39 -	805.39	360.85	03/2013 -	03/2013
151	Tirupati - Tiruthani - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
152	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177	9/2011	485.00 -	485.00	85.41	08/2013 -	08/2013
153	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176	5/2010	374.00 -	374.00	78.28	05/2013 -	05/2013
154	Kandla - Mundra port - [N24000175	1/2011	953.88 -	953.88	419.59	07/2013 -	07/2013
155	2 Laning of Muzaffarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	269.32	11/2013 -	11/2013
156	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173	6/2011	600.00 -	600.00	75.85	06/2013 -	06/2013
157	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	12.48	12/2013 -	12/2013
158	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
159	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	697.65	08/2013 -	08/2013
160	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	751.40	11/2013 -	11/2013
161	CHENGAPALLI TO COIMBATORE BYPASS KM- 102.035-144.740 KM [N24000144	9/2010	852.00 -	852.00	743.61	03/2013 -	03/2013
162	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	731.28	11/2013 -	11/2013
163	Indore-Jhabua-Gujrat/MP - [N24000136	10/2010	1,175.00 -	1,175.00	138.67	04/2013 -	04/2013

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
164	New 4 Lane elevated road from chennai airport-maduravoyal NH no.4 - [N24000139]	9/2010	1,655.00 -	1,655.00	436.70	09/2013 -	09/2013
	Total		48,562.38 -	48,202.38	23,989.98		
<u>Shipping & Ports</u>							
165	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
	Total		966.46 -	994.82	248.23		
<u>Steel</u>							
166	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]	11/2011	254.55 -	254.55	11.73	11/2013 -	11/2013
167	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chattisgarh - [N12000078]	7/2012	332.65 -	332.65	-	08/2014 -	08/2014
168	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]	1/2012	254.90 -	254.90	0.26	12/2014 -	12/2014
	Total		842.10 -	842.10	11.99		
<u>Urban Development</u>							
169	DELHI MRTS PHASE-III - [N28000056]	9/2011	35,242.00 -	35,242.00	923.05	03/2016 -	03/2016
170	FARIDABAD EXTENSION - [N28000057]	9/2011	2,494.00 -	2,494.00	69.58	09/2014 -	09/2014
	Total		37,736.00 -	37,736.00	992.63		
	Grand Total		270,167.59	273,805.49	50,214.20		

List of Delay Project

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
<u>Atomic Energy</u>									
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00	17,270.00	15,030.00	12/2008	03/2013	51	-
2	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00	11,459.00	1,956.00	12/2015	11/2016	11	-
3	RAJASTHAN ATOMIC POWER PROJECT - 7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00	12,320.00	1,199.00	12/2016	03/2017	3	-
Total			36,950.00	41,049.00	18,185.00				
<u>Civil Aviation</u>									
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	335.61	146.09	05/2012	12/2012	7	-
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	2,325.00	2,143.57	05/2011 03/2012	03/2013	22	12
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	309.46	185.20	01/2011 04/2013	04/2013	27	0
Total			2,587.58	2,970.07	2,474.86				
<u>Coal</u>									
7	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,497.44	06/2009	03/2013	45	-
8	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.61	03/2011	03/2013	24	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Orissa	01/2005	302.96	302.96	105.97	03/2010	03/2014	48	-
10	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54	4,909.54	3,537.30	03/2012	03/2014	24	-

(Oct,2012)

S.No Project		Date of Approval	Original / Revised Cost		Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
							Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10	11
11	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Orissa	08/2008	207.28	207.28	100.02	03/2012	03/2014	24	-	-
12	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97	418.97	114.59	03/2012	03/2014	24	-	-
13	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19	181.19	39.31	03/2012	03/2014	24	-	-
14	Churi Benti UG - [N06000083]CCL,Jharkhand	08/2007	163.51	163.51	34.58	03/2011	03/2014	36	-	-
15	North Urimari OCP - [N06000084]CCL,Jharkhand	12/2007	179.87	179.87	60.74	03/2012	03/2014	24	-	-
16	Tapin OCP - [N06000086]CCL,Jharkhand	08/2008	264.68	264.68	106.67	03/2012	03/2014	24	-	-
17	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	779.26	456.78	03/2013 09/2012	07/2014	16	22	-
18	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	0.82	03/2011	03/2015	48	-	-
19	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya Pradesh	10/2007	259.40	259.40	1.73	03/2012	03/2015	36	-	-
20	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	118.51	03/2010	03/2015	60	-	-
21	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63	453.63	81.94	12/2012	03/2015	27	-	-
22	MAGADH OC (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78	706.40	19.23	07/2012	03/2016	44	-	-
23	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77	339.77	0.88	03/2014	03/2016	24	-	-
24	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44	178.44	-	03/2014	03/2016	24	-	-
25	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2017	24	-	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
26	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11	5,907.11	23.99	12/2015	08/2017	20	-
	Total		17,557.60	19,232.91	7,409.11				
	Steel								
27	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00	216.68	116.79	10/2012	12/2012	2	-
28	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	13,891.89	12/2011	12/2012	12	-
29	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00	6,325.00	3,082.76	12/2011	12/2012	12	-
30	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	249.29	08/2010	12/2012	28	-
31	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	341.42	12/2011 03/2012	01/2013	13	10
32	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	253.16	02/2011	01/2013	23	-
33	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00	12,291.00	9,838.39	10/2009	03/2013	41	-
34	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00	2,875.00	1,186.14	12/2012	03/2013	3	-
35	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	450.00	220.90	05/2012	06/2013	13	-
36	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00	17,265.00	6,832.86	03/2013	09/2013	6	-
	Total		50,973.89	57,131.43	36,013.60				
	Petrochemicals								

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	0
37	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	5,669.55	04/2012 12/2013	12/2013	20	0
	Total		5,460.61	8,920.00	5,669.55				
			-						
	<u>Petroleum</u>								
38	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	742.54	04/2011 12/2011	10/2012	18	10
39	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	5,582.27	05/2010 05/2012	11/2012	30	6
40	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	254.36	04/2011 -	11/2012	19	-
41	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,352.39	09/2011 03/2012	11/2012	14	8
42	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL, Multi State	07/2009	238.68 312.00	312.00	266.34	01/2012 01/2012	12/2012	11	11
43	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,934.89	03/2012 08/2012	12/2012	9	4
44	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	542.37	12/2011 -	01/2013	13	-
45	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC, Assam	09/2001	113.90 438.85	438.85	277.79	03/2006 03/2013	03/2013	84	0
46	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,084.54	05/2010 03/2013	03/2013	34	0
47	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]IOCL, Orissa	12/2009	1,492.33 -	1,492.33	1,164.61	06/2012 03/2013	03/2013	9	0
48	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	234.59	03/2012 -	03/2013	12	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
49	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	679.99	03/2011 05/2011	03/2013	24	22
50	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	154.37	08/2012 -	03/2013	7	-
51	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	9,397.26	01/2012 -	03/2013	14	-
52	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	04/2013	52	0
53	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,858.42	09/2010 03/2012	04/2013	31	13
54	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	83.49	03/2013 -	04/2013	1	-
55	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	539.45	03/2010 03/2012	05/2013	38	14
56	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	872.82	07/2010 05/2012	05/2013	34	12
57	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	06/2013	86	12
58	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	1,147.97	06/2012 -	06/2013	12	-
59	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	257.66	07/2012 07/2012	06/2013	11	11
60	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	281.04	01/2013 -	06/2013	5	-
61	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	630.38	07/2012 -	06/2013	11	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
62	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	344.37	09/2011 -	08/2013	23	-
63	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	18,612.00	11/2012 09/2013	09/2013	10	0
64	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	4,258.26	09/2012 -	09/2013	12	-
65	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	46.73	09/2012 -	09/2013	12	-
66	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	62.72	11/2012 -	10/2013	11	-
67	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	820.00	-	06/2012 -	10/2013	16	-
68	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	11/2013	8	-
69	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	3,851.49	08/2010 03/2012	12/2013	40	21
70	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	1,080.01	12/2012 12/2012	12/2013	12	12
71	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	-	08/2013 -	01/2014	5	-
72	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	634.47	03/2007 03/2014	03/2014	84	0
73	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,001.96	03/2013 -	03/2014	12	-
74	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	481.95	03/2013 -	04/2014	13	-
75	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.49	10/2010 -	12/2014	50	-
76	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	2.54	01/2013 -	07/2015	30	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	0
77	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,556.00	03/2007 03/2017	03/2017	120	0
	Total		110,647.22	120,282.02	71,981.44				
			-						
	<u>Power</u>								
78	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61 -	276.61	158.70	04/2012 -	10/2012	6	-
79	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J and K	08/2006	621.26 -	913.00	764.03	02/2011 10/2012	11/2012	21	1
80	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 386.37	386.37	332.13	07/2011 -	11/2012	16	-
81	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	1,112.70	02/2012 -	11/2012	9	-
82	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36 -	1,736.36	1,029.30	06/2012 -	11/2012	5	-
83	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	5,221.23	3,163.50	07/2010 -	12/2012	29	-
84	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	665.60	05/2012 -	12/2012	7	-
85	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	127.08	06/2012 -	12/2012	6	-
86	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J and K	08/2006	611.01 -	936.00	794.58	08/2010 01/2013	01/2013	29	0
87	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92 -	1,628.00	1,598.46	03/2007 09/2012	02/2013	71	5

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
88	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013	37	-
89	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	4,008.20	12/2012 -	02/2013	2	-
90	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J and K	08/2005	1,729.29 -	2,081.00	1,825.39	11/2009 02/2013	03/2013	40	1
91	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,841.11	09/2008 -	03/2013	54	-
92	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	867.25	10/2009 -	03/2013	41	-
93	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	419.00	09/2010 -	03/2013	30	-
94	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,527.00	08/2012 -	03/2013	7	-
95	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 -	2,360.95	1,983.70	08/2012 -	03/2013	7	-
96	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,442.10	08/2012 -	03/2013	7	-
97	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya Pradesh	01/2009	5,915.00 -	5,915.00	3,924.00	10/2012 -	03/2013	5	-
98	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	453.90	11/2012 -	03/2013	4	-
99	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	55.00	10/2012 -	03/2013	5	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
100	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	3,670.00	10/2012 -	05/2013	7	-
101	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	1,659.20	11/2012 -	06/2013	7	-
102	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56 -	2,716.00	1,960.04	10/2010 01/2013	09/2013	35	8
103	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	2,004.41	01/2012 -	09/2013	20	-
104	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,024.70	10/2012 -	09/2013	11	-
105	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	152.00	11/2011 -	09/2013	22	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	570.80	04/2013 -	10/2013	6	-
107	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	58.40	01/2013 -	11/2013	10	-
108	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,212.87	09/2009 06/2013	12/2013	51	6
109	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	329.90	11/2011 -	12/2013	25	-
110	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	343.50	11/2011 -	12/2013	25	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
111	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	246.10	02/2012 -	12/2013	22	-
112	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	940.40	12/2012 -	12/2013	12	-
113	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	780.40	08/2012 -	12/2013	16	-
114	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	4,548.00	04/2009 03/2014	03/2014	59	0
115	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	450.20	11/2012 -	03/2014	16	-
116	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunchal Pr.	12/2008	573.99 -	573.99	400.67	08/2012 08/2013	09/2014	25	13
117	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	4,720.00	08/2013 -	09/2014	13	-
118	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	5,182.30	08/2013 -	09/2014	13	-
119	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	3,385.00	07/2011 -	11/2014	40	-
120	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 913.63	913.63	352.38	07/2014 -	02/2015	7	-
121	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,591.00	03/2013 -	09/2015	30	-
122	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	7,510.00	12/2009 12/2014	03/2016	75	15
123	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 2,491.58	3,422.44	323.33	07/2014 -	05/2016	22	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	6
124	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	382.46	07/2010 02/2016	08/2016	73	6
125	KISHANGANGA HEP - [N18000031]NHPC,J and K	07/2007	2,238.67 3,642.04	3,642.00	1,751.05	01/2016 01/2016	11/2016	10	10
126	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	10,667.00	5,830.23	09/2010 08/2014	03/2017	78	31
127	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.00	2,034.59	05/2013 06/2016	03/2017	46	9
128	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	5,366.00	3,627.99	09/2009 07/2014	12/2017	99	41
Total			135,623.96	149,008.45	94,729.65				
Railways									
129	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	456.45	301.82	06/2004 -	12/2012	102	-
130	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	500.00	425.36	03/2012 03/2012	12/2012	9	9
131	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	863.38	03/2009 12/2012	12/2012	45	0
132	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,563.17	10/2007 12/2012	12/2012	62	0
133	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya Pradesh	09/2007	687.20 -	687.20	668.82	03/2010 -	12/2012	33	-
134	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	227.94	205.16	03/2002 -	01/2013	130	-
135	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,115.21	897.49	12/2012 01/2013	01/2013	1	0
136	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	662.51	03/2012 08/2012	02/2013	11	6
137	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	260.33	02/2011 02/2011	02/2013	24	24

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
138	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	420.44	12/2012 12/2012	02/2013	2	2
139	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	167.73	48.02	03/2012 -	02/2013	11	-
140	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	634.13	555.27	03/1995 -	03/2013	216	-
141	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	900.05	555.40	12/2011 12/2011	03/2013	15	15
142	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	249.19	03/2012 03/2012	03/2013	12	12
143	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	274.73	03/2012 03/2013	03/2013	12	0
144	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	401.54	03/2012 03/2013	03/2013	12	0
145	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	603.04	105.72	03/2012 -	03/2013	12	-
146	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013	50	50
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013	49	49
148	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	108.12	12/2011 11/2013	11/2013	23	0
149	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	145.89	12/2012 -	12/2013	12	-
150	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	4,255.37	3,195.95	03/2009 -	12/2013	57	-
151	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,512.86	204.95	03/2004 12/2010	03/2014	120	39
152	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	1,655.81	1,298.65	12/2008 -	03/2014	63	-

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	9
153	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	174.33	06/2013 06/2013	03/2014	9	9
154	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	394.08	03/2013 -	03/2014	12	-
155	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	114.08	12/2012 -	03/2014	15	-
156	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	820.40	158.14	03/2010 06/2014	06/2014	51	0
157	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	499.16	169.68	03/2007 03/2007	03/2015	96	96
158	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	732.83	12/2010 12/2010	03/2015	51	51
159	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	2,393.48	12.87	04/2014 -	03/2015	11	-
160	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.02	2,501.02	04/2008 03/2014	12/2015	92	21
161	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,444.00	937.59	03/2011 03/2014	03/2016	60	24
162	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	920.70	03/2014 03/2016	03/2016	24	0
163	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,298.42	33.46	03/2014 03/2016	03/2016	24	0
164	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,028.05	1,412.74	451.90	03/2005 12/2008	06/2016	135	90
165	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,086.41	427.98	06/2005 07/2011	06/2016	132	59
166	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	30.85	03/2016 -	06/2016	3	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
167	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J and K	03/1995	2,500.00 2,500.00	20,000.00	8,521.82	03/2001 -	12/2017	201	-
	Total		25,689.14	68,485.77	29,465.34				
			-						
	<u>Road Transport & Highways</u>								
168	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	181.42	08/2004 07/2010	11/2012	99	28
169	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	187.68	08/2004 -	11/2012	99	-
170	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	289.52	11/2008 -	11/2012	48	-
171	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.49	06/2009 -	11/2012	41	-
172	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,674.90	08/2011 -	11/2012	15	-
173	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	1,740.00	1,903.30	10/2012 -	11/2012	1	-
174	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	388.00	515.85	05/2012 -	11/2012	6	-
175	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	631.65	02/2012 -	11/2012	9	-
176	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	141.38	04/2004 -	12/2012	104	-
177	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2012	93	-
178	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	279.21	09/2007 -	12/2012	63	-
179	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012	57	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
180	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	260.19	01/2009 -	12/2012	47	-
181	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	225.00	282.86	06/2008 -	12/2012	54	-
182	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	251.66	06/2008 -	12/2012	54	-
183	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	399.87	09/2008 -	12/2012	51	-
184	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	240.12	10/2008 -	12/2012	50	-
185	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya Pradesh	12/2003	251.03 -	251.03	312.76	10/2008 -	12/2012	50	-
186	RAJMARG CHORAHA TO LAKHNANDON, KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya Pradesh	12/2003	229.91 -	229.91	267.50	10/2008 -	12/2012	50	-
187	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00 -	225.00	186.36	07/2008 -	12/2012	53	-
188	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	575.27	09/2008 -	12/2012	51	-
189	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	276.00	06/2008 -	12/2012	54	-
190	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	152.14	04/2008 -	12/2012	56	-
191	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	257.43	06/2011 06/2011	12/2012	18	18
192	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	211.16	04/2008 -	12/2012	56	-
193	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	270.92	04/2008 -	12/2012	56	-
194	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	12/2012	48	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
195	GANJAM- ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	271.86	02/2004 -	12/2012	106	-
196	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	225.26	04/2010 -	12/2012	32	-
197	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	302.72	10/2009 -	12/2012	38	-
198	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	274.33	09/2010 -	12/2012	27	-
199	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	228.70	194.42	02/2004 -	12/2012	106	-
200	END OF DURG BYPASS- CHHATISGARH/MAHARAS HTRA BORDER - [N24000118]NHAI,Chhatisga rh	01/2008	464.00 -	464.00	535.49	01/2011 -	12/2012	23	-
201	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	593.31	05/2010 -	12/2012	31	-
202	PIMPALGAON-NASIK- GONDE, NH-3 (NHDP- PHASE-III) - [N24000123]NHAI,Maharash tra	03/2005	940.00 -	940.00	1,158.80	07/2012 -	12/2012	5	-
203	MP/Maharashtra Border- Dhula - [N24000126]NHAI,Maharash tra	12/2009	835.00 -	835.00	1,068.70	06/2012 -	12/2012	6	-
204	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,037.50	05/2012 -	12/2012	7	-
205	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,731.00	10/2011 -	12/2012	14	-
206	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	279.36	10/2008 -	02/2013	52	-
207	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	02/2013	25	-
208	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	206.78	09/2007 -	03/2013	66	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
209	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	134.12	09/2008 -	03/2013	54	-
210	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	227.91	06/2005 -	03/2013	93	-
211	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	230.13	05/2008 -	03/2013	58	-
212	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	294.29	10/2008 -	03/2013	53	-
213	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	388.01	03/2008 -	03/2013	60	-
214	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	278.20	02/2009 03/2014	03/2013	49	-12
215	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	118.02	04/2009 -	03/2013	47	-
216	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	209.66	06/2008 -	03/2013	57	-
217	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	287.75	06/2008 -	03/2013	57	-
218	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.21	03/2008 -	03/2013	60	-
219	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	248.90	06/2008 -	03/2013	57	-
220	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	187.69	05/2008 -	03/2013	58	-
221	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	231.15	06/2008 -	03/2013	57	-
222	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	499.70	09/2009 -	03/2013	42	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
223	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	760.07	07/2010 -	03/2013	32	-
224	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	1,509.10	1,427.90	09/2012 -	03/2013	6	-
225	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	572.30	712.18	10/2011 -	06/2013	20	-
226	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	705.00	1,161.20	11/2012 -	06/2013	7	-
227	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	62.08	04/2009 -	07/2013	51	-
228	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	93.99	11/2008 -	07/2013	56	-
229	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	604.00	494.29	12/2009 -	07/2013	43	-
230	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI, Haryana	05/2009	1,108.00 -	2,288.00	3,462.40	11/2011 -	08/2013	21	-
231	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.10	05/2012 -	10/2013	17	-
232	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00 -	209.00	3.82	01/2013 -	10/2013	9	-
233	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013	46	-
234	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI, Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
235	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	21.35	11/2008 -	01/2014	62	-
236	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	325.00	387.71	05/2013 -	02/2014	9	-
237	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	300.00	175.59	10/2008 -	03/2014	65	-

(Oct,2012)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
238	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	184.79	09/2007 -	03/2014	78	-
239	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	376.65	10/2011 -	03/2014	29	-
240	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.52	08/2012 -	03/2014	19	-
241	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	352.68	05/2013 -	03/2014	10	-
242	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	426.01	03/2013 -	03/2014	12	-
243	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014	79	-
244	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	51.63	07/2009 -	04/2014	57	-
245	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	223.55	02/2014 -	04/2014	2	-
246	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J and K	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
247	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	34.42	09/2013 -	07/2014	10	-
248	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	-	07/2012 -	07/2014	24	-
249	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	263.17	233.77	06/2010 -	09/2014	51	-
250	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.77	09/2009 -	09/2014	60	-
251	NH CONNECTIVITY TO ICTT VALLARPADAUEU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.92	02/2010 -	12/2014	58	-
252	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
253	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00	1,987.00	-	07/2015	06/2016	11	-
	Total		41,423.12	43,217.31	40,991.56				
	Shipping & Ports								
254	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44	359.44	358.78	04/2011 10/2012	10/2012	18	0
255	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91	968.35	777.97	09/2012 10/2012	10/2012	1	0
256	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	188.88	12/2011 10/2012	10/2012	10	0
257	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10	444.10	-	06/2010	11/2012	29	-
258	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00	1,060.00	0.93	02/2011	12/2012	22	-
259	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,534.95	01/2012 09/2012	12/2012	11	3
260	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00	755.50	219.00	03/2011	03/2013	24	-
261	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	294.84	12/2012 05/2013	05/2013	5	0
262	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	110.00	03/2006 06/2013	06/2013	87	0
263	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	894.93	12/2010 09/2012	10/2013	34	13

(Oct,2012)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	
	Total		9,222.20	10,702.06	6,380.28				
				-					
	<u>Telecommunications</u>								
264	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	930.60	815.91	11/2010 -	12/2012	25	-
265	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	67.20	02/2007 03/2012	02/2013	72	11
266	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	232.00	12/2008 -	03/2013	51	-
267	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	80.05	06/2009 -	03/2013	45	-
268	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	328.12	164.58	03/2009 -	03/2013	48	-
269	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	157.98	01/2009 -	06/2013	53	-
270	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	06/2013	32	15
	Total		2,737.73	2,741.60	1,547.17				
				-					
	<u>Urban Development</u>								
271	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	21	-
	Total		6,395.00	11,609.00	2,267.57				
				-					
	<u>Water Resources</u>								
272	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	-
	Total		542.90	1,187.00	35.49				
				-					
Grand Total			445,810.95	536,536.62	317,150.62				

List of ongoing projects having cost overrun w.r.to original

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	15,030.00	12/2008 -	03/2013
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	-	09/2010 -	-
	Total		16,663.00 -	22,947.00	15,030.00		
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	2,143.57	05/2011 -	03/2013
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) [N04000038]	08/2008	1,808.00 -	2,015.00	1,724.62	01/2011 -	02/2012
	Total		3,750.51 -	27,287.00	18,898.19		
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	2,497.44	06/2009 -	03/2013
6	MAGADH OC (CCL) - [N06000015]	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	779.26	456.78	03/2013 -	07/2014
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	115.91	03/2017 -	03/2017
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	4,909.54	3,537.30	03/2012 -	03/2014
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	204.70	03/2014 -	03/2014
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	89.50	03/2016 -	03/2016
	Total		8,579.45 -	37,719.98	25,819.05		
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	5,669.55	04/2012 -	12/2013
	Total		5,460.61 -	46,639.98	31,488.60		
	<u>Petroleum</u>						
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	663.69	634.47	03/2007 -	03/2014

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.00	03/2007 -	03/2017
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	277.79	03/2006 -	03/2013
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
18	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,582.27	05/2010 -	11/2012
19	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
20	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,851.49	08/2010 03/2012	12/2013
21	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,084.54	05/2010 -	03/2013
22	RESITMENT OF MARKETING INSTALATION AT VISAKH [N16000057	01/2009	756.00 -	898.00	904.59	- -	08/2012
23	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	18,612.00	11/2012 -	09/2013
24	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI [N16000066	01/2008	224.00 -	394.00	368.23	- -	-
25	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	266.34	01/2012 -	12/2012
26	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY [N16000081	04/2008	825.00 -	1,827.00	611.55	04/2013 -	04/2013
27	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	679.99	03/2011 -	03/2013
	Total		51,022.95 -	114,149.48	78,481.19		
Power							
28	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,627.99	09/2009 -	12/2017
29	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,830.23	09/2010 -	03/2017
30	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,598.46	03/2007 -	02/2013
31	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,510.00	12/2009 -	03/2016
32	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,212.87	09/2009 -	12/2013
33	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	850.63	12/2007 -	-
34	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,960.04	10/2010 -	09/2013

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
35	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,825.39	11/2009 -	03/2013
36	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,841.11	09/2008 -	03/2013
37	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	794.58	08/2010 -	01/2013
38	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	764.03	02/2011 -	11/2012
39	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	382.46	07/2010 -	08/2016
40	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013
41	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,751.05	01/2016 -	11/2016
42	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	323.33	07/2014 -	05/2016
43	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,527.00	08/2012 -	03/2013
44	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.37	332.13	07/2011 -	11/2012
45	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	368.16	- -	07/2013
	Total		41,492.20 -	169,640.21	114,575.65		
<u>Railways</u>							
46	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007	04/1985	158.77 274.56	540.96	558.07	03/1994 -	12/2011
47	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	634.13	555.27	03/1995 -	03/2013
48	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	356.87	171.77	- 03/2010	-
49	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	590.02	- -	03/2012
50	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	548.95	538.10	06/1999 -	03/2011
51	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	8,521.82	03/2001 -	12/2017
52	New BG line Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	242.39	- -	03/2015
53	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	205.16	03/2002 -	01/2013
54	DALLI-RAJHARA - RAOGHAT(PART OF DALLI- RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	118.28	12/2012 -	12/2012
55	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	600.41	- -	02/2012
56	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,512.86	204.95	03/2004 -	03/2014

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
57	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	555.40	12/2011 12/2010	03/2013
58	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	176.76	- -	03/2013
59	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	944.55	542.29	- -	01/2013
60	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	202.01	- -	03/2013
61	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	590.26	03/1998 -	-
62	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	730.00	352.01	07/2012 -	-
63	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	249.19	03/2012 -	03/2013
64	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	712.00	737.02	- -	10/2012
65	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	634.02	02/2009 -	03/2012
66	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	69.70	- -	-
67	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,577.46	1,389.02	- -	03/2013
68	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	3,230.02	2,501.02	04/2008 12/2011	12/2015
69	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	139.79	- -	03/2012
70	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	499.16	169.68	03/2007 03/2007	03/2015
71	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	335.74	- -	12/2012
72	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	456.45	301.82	06/2004 -	12/2012
73	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	0.35	07/2008 -	07/2008
74	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	1,321.44	07/2005 -	-
75	CHURCHGATE-VIRAR CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233	07/1996	653.84 654.51	1,302.12	608.97	06/2013 -	06/2013
76	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR [220100240	04/1997	233.00 335.77	1,043.56	662.51	03/2012 -	02/2013
77	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	897.49	12/2012 -	01/2013
78	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	227.42	250.82	12/2009 -	03/2011
79	KATI HAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	732.83	12/2010 -	03/2015
80	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,214.00	96.96	- -	-

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
81	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	776.00	348.55	- 05/2009	05/2009
82	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	603.58	- -	03/2012
83	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	750.89	506.14	- -	03/2014
84	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	96.67	- -	03/2013
85	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	835.55	06/2007 -	06/2007
86	RENIGUNTA-GUNTAKAL(RE) - [220100260	06/2000	168.34 -	370.00	358.98	04/2003 03/2010	-
87	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	548.96	518.10	- -	-
88	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) - [220100263	03/1998	280.00 -	1,029.00	769.62	- -	03/2013
89	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	9.41	- -	-
90	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	1,655.81	1,298.65	12/2008 -	03/2014
91	TOLLYGANJ-GARIA with extension to Dum Dum- Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	3,225.24	12/2006 -	08/2010
92	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	260.33	02/2011 -	02/2013
93	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	530.19	- 12/2009	02/2012
94	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	420.44	12/2012 12/2012	02/2013
95	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	0.29	- -	-
96	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,412.74	451.90	03/2005 12/2008	06/2016
97	REWARI-ROHTAK (NL),NR - [220100279	01/2004	149.38 -	602.00	494.36	02/2010 -	02/2011
98	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	500.00	425.36	03/2012 -	12/2012
99	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,100.00	237.18	- -	03/2013
100	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	735.10	221.60	- 09/2009	-
101	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013
102	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,444.00	937.59	03/2011 -	03/2016
103	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	274.73	03/2012 -	03/2013
104	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	436.14	- -	03/2010

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
105	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	863.38	03/2009 -	12/2012
106	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	1,563.17	10/2007 -	12/2012
107	DANIAWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	83.11	- -	-
108	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.00	240.93	- -	-
109	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR [220100315	01/2004	915.70 -	1,717.29	1,476.55	- -	03/2013
110	BILASPUR-URKURA (DL) - [220100321	04/1997	151.52 -	350.00	327.08	- 03/2009	03/2011
111	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	174.53	03/1998 08/2005	08/2005
112	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	194.91	- -	12/2013
113	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	75.05	02/2015 -	02/2015
114	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013
115	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	726.96 -	810.78	115.80	- -	03/2013
116	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	221.90	236.81	12/2007 03/2010	12/2010
117	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	401.54	03/2012 -	03/2013
118	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N220000027	04/2005	240.00 -	355.00	413.37	03/2009 12/2009	03/2011
119	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.60	0.76	- -	-
120	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	82.89	02/2006 -	-
121	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	448.67	03/2008 06/2008	-
122	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS&PU [N220000052	04/2003	98.74 -	337.30	222.07	- -	03/2012
123	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N220000053	03/2005	470.09 -	1,417.97	1,011.09	- -	03/2012
124	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	228.77	03/2010 -	03/2012
125	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI [N220000079	09/2007	404.19 -	900.00	280.18	- -	-
126	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE [N220000080	09/2006	343.17 -	900.00	569.32	- -	12/2012
127	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082	12/2006	170.00 -	453.04	392.85	03/2011 -	03/2011

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
128	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR - [N22000083]	09/1996	156.00 -	415.73	279.98	- -	12/2012
129	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	227.40	39.04	- -	-
130	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	582.83	136.04	- -	-
131	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	200.00 -	385.20	114.85	- -	03/2014
132	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	300.00 -	532.87	39.45	- -	-
133	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	820.40	158.14	03/2010 -	06/2014
134	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	1,106.62	205.28	12/2010 -	03/2011
135	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,501.80	4,334.00	06/2011 -	03/2012
136	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	12/2004	129.17 -	250.00	227.48	03/2011 -	03/2012
137	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,086.41	427.98	06/2005 -	06/2016
138	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,141.75	426.35	03/2014 -	03/2014
139	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	12.87	04/2014 -	03/2015
140	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	1.22	- -	03/2015
141	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	52.63	12/2015 -	12/2015
142	Ramanagram-Mysore doubling with electrification of Kengesli- Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	394.08	03/2013 -	03/2014
143	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineswar (MTP) [N22000109]	04/2010	2,069.60 -	2,298.42	33.46	03/2014 -	03/2016
144	New Work for Construction of Metro railway from Joka to Binoy Badal Dinesh Bagh. - [N22000111]	04/2010	2,619.02 -	2,913.51	171.51	03/2016 -	03/2016
145	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.46	215.94	03/2014 -	03/2014
146	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	89.02	12/2011 -	02/2012
147	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	108.12	12/2011 -	11/2013
148	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	137.07	12/2010 -	12/2010
149	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	404.39	3.77	03/2013 -	03/2013
150	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	468.62	1.00	03/2012 -	-
151	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95	192.81	03/2011 -	-

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project [N22000127	04/1996	1,676.31 -	4,255.37	3,195.95	03/2009 -	12/2013
	Total		44,312.87 -	297,955.84	174,532.56		
<u>Road Transport & Highways</u>							
153	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	141.38	04/2004 -	12/2012
154	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 [240106221	12/2003	155.00 -	201.66	134.12	09/2008 -	03/2013
155	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012
156	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	230.13	05/2008 -	03/2013
157	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	62.08	04/2009 -	07/2013
158	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	93.99	11/2008 -	07/2013
159	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014
160	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	51.63	07/2009 -	04/2014
161	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
162	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	184.79	09/2007 -	03/2014
163	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,462.40	11/2011 -	08/2013
	Total		3,324.28 -	303,401.04	179,263.95		
<u>Shipping & Ports</u>							
164	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	5.75	10/2008 -	10/2008
165	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	-	- 01/2009	01/2009
166	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	894.93	12/2010 -	10/2013
167	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013
168	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
169	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
170	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042	04/2009	290.85 -	305.00	194.14	06/2011 -	09/2012

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,534.95	01/2012 -	12/2012
172	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]	08/2010	612.72 -	627.64	294.84	12/2012 -	05/2013
173	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	248.23	02/2014 -	02/2014
174	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	326.08	04/2009 -	02/2011
	Total		9,532.54 -	315,552.18	185,092.80		
<u>Steel</u>							
175	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	9,838.39	10/2009 -	03/2013
176	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	341.42	12/2011 06/2010	01/2013
177	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	116.79	10/2012 -	12/2012
178	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	13,891.89	12/2011 -	12/2012
179	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	230.00 -	343.58	253.16	02/2011 -	01/2013
180	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	350.00	249.29	08/2010 -	12/2012
	Total		24,028.89 -	345,768.61	209,783.74		
<u>Telecommunications</u>							
181	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013
182	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]	11/2009	916.70 -	930.60	815.91	11/2010 -	12/2012
	Total		1,065.85 -	346,857.93	210,679.70		
<u>Urban Development</u>							
183	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013
184	C/o office building for IDBI at bandra Kurla Complex, Mumbai - [N28000048]	11/2006	114.18 173.08	173.08	-	04/2009 -	-
	Total		6,509.18 -	358,640.01	212,947.27		

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Water Resources</u>						
185	PAGLADIYA DAM PROJECT	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	- [300100001		-			-	
	Total		542.90	359,827.01	212,982.76		
			-				
	Grand Total		216,285.23	2,746,386.27	1,669,575.46		

List of ongoing projects having time and cost overrun w.r.to original

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040	12/2001	13,171.00 -	17,270.00	15,030.00	12/2008 -	03/2013
	Total		13,171.00 -	17,270.00	15,030.00		
	<u>Civil Aviation</u>						
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037	08/2008	1,942.51 -	2,325.00	2,143.57	05/2011 -	03/2013
	Total		1,942.51 -	19,595.00	17,173.57		
	<u>Coal</u>						
3	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087	10/2004	2,030.78 -	3,027.59	2,497.44	06/2009 -	03/2013
4	MAGADH OC (CCL) - [N06000015	08/2008	469.78 -	706.40	19.23	07/2012 -	03/2016
5	ADRIYALA SHAFT PROJECT - [N06000016	12/2009	212.34 -	779.26	456.78	03/2013 -	07/2014
6	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047	05/2008	4,904.54 -	4,909.54	3,537.30	03/2012 -	03/2014
	Total		7,617.44 -	29,017.79	23,684.32		
	<u>Petrochemicals</u>						
7	Assam gas Cracker project - [N16000106	04/2006	5,460.61 -	8,920.00	5,669.55	04/2012 -	12/2013
	Total		5,460.61 -	37,937.79	29,353.87		
	<u>Petroleum</u>						
8	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	663.69	634.47	03/2007 -	03/2014
9	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	1,556.00	03/2007 -	03/2017
10	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	277.79	03/2006 -	03/2013
11	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	2,184.00	04/2006 -	06/2013
12	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	2,520.91	12/2008 -	04/2013
13	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030	01/2007	2,853.29 -	6,326.40	5,582.27	05/2010 -	11/2012

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Apenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
14	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	1,858.42	09/2010 03/2012	04/2013
15	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	3,851.49	08/2010 03/2012	12/2013
16	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	7,084.54	05/2010 -	03/2013
17	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	30,426.00	18,612.00	11/2012 -	09/2013
18	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	266.34	01/2012 -	12/2012
19	North Tapti Gas Field Development - [N16000096	07/2008	589.70 755.56	755.76	679.99	03/2011 -	03/2013
	Total		49,217.95 -	102,328.29	74,462.09		
<u>Power</u>							
20	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	3,627.99	09/2009 -	12/2017
21	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	5,830.23	09/2010 -	03/2017
22	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC) [180100222	10/2003	768.92 -	1,628.00	1,598.46	03/2007 -	02/2013
23	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	7,510.00	12/2009 -	03/2016
24	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	1,212.87	09/2009 -	12/2013
25	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	1,960.04	10/2010 -	09/2013
26	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	1,825.39	11/2009 -	03/2013
27	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	1,841.11	09/2008 -	03/2013
28	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	794.58	08/2010 -	01/2013
29	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007	08/2006	621.26 -	913.00	764.03	02/2011 -	11/2012
30	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	382.46	07/2010 -	08/2016
31	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP [N18000018	07/2006	557.24 -	758.75	595.00	01/2010 -	02/2013
32	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	1,751.05	01/2016 -	11/2016
33	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042	08/2008	2,491.58 -	3,422.44	323.33	07/2014 -	05/2016
34	MOUDA STPP - [N18000048	11/2008	5,459.28 -	6,010.89	4,527.00	08/2012 -	03/2013
35	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064	04/2008	297.37 -	386.37	332.13	07/2011 -	11/2012

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		40,474.74 -	156,188.42	109,337.76		
	<u>Railways</u>						
36	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	555.27	03/1995	03/2013
37	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	20,000.00	8,521.82	03/2001	12/2017
38	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 119.29	227.94	205.16	03/2002	01/2013
39	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,512.86	204.95	03/2004	03/2014
40	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 -	900.05	555.40	12/2011 12/2010	03/2013
41	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	333.50	249.19	03/2012	03/2013
42	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]	09/1997	1,000.00 -	3,230.02	2,501.02	04/2008 12/2011	12/2015
43	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	499.16	169.68	03/2007 03/2007	03/2015
44	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	456.45	301.82	06/2004	12/2012
45	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	1,043.56	662.51	03/2012	02/2013
46	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1998	248.44 -	1,115.21	897.49	12/2012	01/2013
47	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 -	1,041.79	732.83	12/2010	03/2015
48	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	733.00 -	1,655.81	1,298.65	12/2008	03/2014
49	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 -	270.00	260.33	02/2011	02/2013
50	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 240.59	607.09	420.44	12/2012 12/2012	02/2013
51	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 -	1,412.74	451.90	03/2005 12/2008	06/2016
52	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 -	500.00	425.36	03/2012	12/2012
53	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	243.40	253.88	02/2009 02/2009	04/2013
54	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	4,444.00	937.59	03/2011	03/2016
55	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	341.41	274.73	03/2012	03/2013
56	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	2,363.00	863.38	03/2009	12/2012
57	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	1,563.17	10/2007	12/2012

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
58	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	225.00	218.22	03/2009 03/2009	04/2013
59	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	401.54	03/2012 -	03/2013
60	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	820.40	158.14	03/2010 -	06/2014
61	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,086.41	427.98	06/2005 -	06/2016
62	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,393.48	12.87	04/2014 -	03/2015
63	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	394.08	03/2013 -	03/2014
64	New Work for Construction of Metro railway from Baranagar to Barrackpore and Dakshineshwar (MTP) - [N22000109	04/2010	2,069.60 -	2,298.42	33.46	03/2014 -	03/2016
65	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	108.12	12/2011 -	11/2013
66	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	4,255.37	3,195.95	03/2009 -	12/2013
	Total		15,602.29 -	214,592.23	136,594.69		
Road Transport & Highways							
67	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	141.38	04/2004 -	12/2012
68	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH- 25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	134.12	09/2008 -	03/2013
69	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	163.43	03/2008 -	12/2012
70	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	230.13	05/2008 -	03/2013
71	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	62.08	04/2009 -	07/2013
72	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	93.99	11/2008 -	07/2013
73	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	28.21	09/2007 -	04/2014
74	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	51.63	07/2009 -	04/2014
75	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	179.23	02/2010 -	12/2013
76	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	184.79	09/2007 -	03/2014
77	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	3,462.40	11/2011 -	08/2013
	Total		3,324.28 -	220,037.43	141,326.08		
Shipping & Ports							

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	1,460.00	894.93	12/2010 -	10/2013
79	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) [N25000035]	10/2002	150.00 -	600.00	110.00	03/2006 -	06/2013
80	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012
81	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA [N25000039]	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013
82	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN [N25000048]	03/2009	3,500.00 -	4,150.00	3,534.95	01/2012 -	12/2012
83	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries [N25000051]	08/2010	612.72 -	627.64	294.84	12/2012 -	05/2013
	Total		7,074.72 -	228,690.57	146,380.73		
<u>Steel</u>							
84	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	9,838.39	10/2009 -	03/2013
85	Bailadilla Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	341.42	12/2011 06/2010	01/2013
86	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	116.79	10/2012 -	12/2012
87	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	13,891.89	12/2011 -	12/2012
88	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT [N12000068]	07/2007	230.00 -	343.58	253.16	02/2011 -	01/2013
89	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	350.00	249.29	08/2010 -	12/2012
	Total		24,028.89 -	258,907.00	171,071.67		
<u>Telecommunications</u>							
90	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL [N26000058]	01/2009	149.15 -	158.72	80.05	06/2009 -	03/2013
91	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle [N26000090]	11/2009	916.70 -	930.60	815.91	11/2010 -	12/2012
	Total		1,065.85 -	259,996.32	171,967.63		
<u>Urban Development</u>							
92	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013

(Oct,2012)

Date of
Commissioning

S.No	Project	Date of Approval	Original /Revised Cost	Anticipated	Cumulative Expenditure	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		6,395.00	271,605.32	174,235.20		
			-				
	<u>Water Resources</u>						
93	PAGLADIYA DAM PROJECT	01/2001	542.90	1,187.00	35.49	12/2007	12/2012
	- [300100001		-			-	
	Total		542.90	272,792.32	174,270.69		
			-				
	Grand Total		175,918.18	2,088,958.48	1,384,888.30		

Sectorwise Summary of Project Without Milestone

Sector	Number of projects	Cost of project			Total Cumm Expenditure
		Original	Revised	Anticipated	
Atomic Energy	1	1,106.29	.00	1,106.29	1,084.24
Civil Aviation	6	5,473.58	2,015.00	6,063.07	4,593.91
Coal	6	3,868.49	1,666.38	3,657.55	234.27
Fertilisers	3	1,088.00	.00	1,088.00	425.03
Petroleum	46	106,675.46	35,350.85	115,502.22	39,229.20
Power	18	50,930.65	.00	51,782.46	8,206.52
Railways	125	63,915.28	66,634.04	146,694.92	62,955.91
Road Transport & Highways	139	89,789.00	.00	91,223.19	64,724.11
Shipping & Ports	18	16,087.68	9,708.64	18,300.73	8,357.06
Steel	2	587.55	.00	587.55	0.26
Telecommunications	13	5,735.48	1,318.73	5,676.27	1,658.81
Urban Development	3	37,850.18	173.08	37,909.08	992.63
Water Resources	1	542.90	.00	1,187.00	35.49
Grand total	381	383,650.54	116,866.72	480,778.33	192,497.44

List of Projects Without Milestones

(Oct,2012)

Date of Commissioning						
S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
<u>Atomic Energy</u>						
1	URANIUM ORE MINE and PROCESSING PLANT AT TUMMALAP - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	04/2011	-	0/0
	Total		1,106.29			0/0
<u>Civil Aviation</u>						
2	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
3	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61	05/2012	12/2012	0/0
4	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51	05/2011 03/2012	03/2013	0/0
5	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46	01/2011 04/2013	04/2013	0/0
6	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00	06/2013	06/2013	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Punjab	02/2011	452.00	03/2015	03/2015	0/0
	Total		5,473.58			0/0
<u>Coal</u>						
8	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	03/2014	03/2014	0/0
9	Muraidih UG - [N06000096]BCCL,Jharkhandd	02/2011	339.88	04/2014	04/2014	0/0
10	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 535.10	03/2015 03/2015	03/2015	0/0
11	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhandd	08/2011	1,230.27	04/2015	04/2015	0/0
12	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56	03/2016	03/2016	0/0
13	KHADIA EXPANSION OPENCASE PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	03/2018 03/2018	03/2018	0/0
	Total		3,868.49			0/0
<u>Fertilisers</u>						
14	DUMMY PROJECT FOR FERTILISERS - [N08000002]RCF,Multi State	04/2007	325.00	11/2009	10/2011	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	07/2011 -	04/2012	0/0
16	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	07/2011 -	07/2012	0/0
	Total		1,088.00 -			0/0
Steel						
17	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisgarh - [N12000078]SAIL,Delhi	07/2012	332.65 -	08/2014 -	08/2014	0/0
18	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Odisha - [N12000079]SAIL,Delhi	01/2012	254.90 -	12/2014 -	12/2014	0/0
	Total		587.55 -			0/0
Petroleum						
19	Construction of tanks and blending facility at Vad - [N16000115]IOCL,Gujarat	02/2009	267.00 -	09/2012 -	09/2012	0/0
20	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	05/2010 05/2012	11/2012	0/0
21	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	04/2011 -	11/2012	0/0
22	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	11/2012	0/0
23	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	12/2011 -	01/2013	0/0
24	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2013	0/0
25	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	03/2011 05/2011	03/2013	0/0
26	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	08/2012 -	03/2013	0/0
27	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	04/2013	0/0
28	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	04/2013	0/0
29	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	03/2013 -	04/2013	0/0
30	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	05/2013	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
31	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	05/2013	0/0
32	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	05/2013 -	05/2013	0/0
33	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	06/2013	0/0
34	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	06/2012 -	06/2013	0/0
35	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	08/2013	0/0
36	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	09/2013	0/0
37	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	09/2013	0/0
38	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	11/2012 -	10/2013	0/0
39	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	06/2012 -	10/2013	0/0
40	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	11/2013	0/0
41	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	08/2010 03/2012	12/2013	0/0
42	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 12/2013	12/2013	0/0
43	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	01/2014 -	01/2014	0/0
44	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	08/2013 -	01/2014	0/0
45	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
46	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	03/2013 -	03/2014	0/0
47	Butene-1 at Panipat - [N16000139]IOCL,Haryana	02/2012	190.00 -	03/2014 -	03/2014	0/0
48	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	03/2014 -	03/2014	0/0
49	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	03/2013 -	04/2014	0/0
50	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	05/2014 -	05/2014	0/0
51	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	05/2014 -	05/2014	0/0
52	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
53	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2014	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
54	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63	12/2014	12/2014	0/0
55	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17	12/2014	12/2014	0/0
56	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00	12/2014	12/2014	0/0
57	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63	03/2015	03/2015	0/0
58	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00	04/2015	04/2015	0/0
59	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40	05/2015	05/2015	0/0
60	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	01/2013	07/2015	0/0
61	I REP - [N16000143]BPCL,Kerala	01/1999	14,225.00	12/2015	12/2015	0/0
62	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74	06/2016	06/2016	0/0
63	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00	-	-	0/0
64	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81	04/2012	-	0/0
Total			106,675.46			0/0
			-			
Power						
65	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	04/2012	10/2012	0/0
66	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	07/2013	07/2013	0/0
67	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.56	10/2010	09/2013	0/0
68	RAMPUR HEP(412 MW) - [N18000024]SJVN,Himachal Pr.	01/2007	2,047.03	01/2012	09/2013	0/0
69	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	09/2009	12/2013	0/0
70	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78	03/2014	03/2014	0/0
71	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66	08/2014	08/2014	0/0
72	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63	09/2014	09/2014	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
73	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	11/2014 -	11/2014	0/0
74	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	11/2014 -	11/2014	0/0
75	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	12/2014	0/0
76	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	02/2015 -	02/2015	0/0
77	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	03/2015 -	03/2015	0/0
78	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	04/2015 -	04/2015	0/0
79	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	08/2015 -	08/2015	0/0
80	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	09/2016 -	09/2016	0/0
81	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	11/2016 -	11/2016	0/0
82	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	12/2016 -	12/2016	0/0
	Total		50,930.65 -			0/0
<u>Railways</u>						
83	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0
84	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
85	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
86	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
87	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
88	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
89	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	12/2010	0/0
90	Pandabeswar-Chinpa doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
91	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	02/2010 02/2011	02/2011	0/0
92	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	06/1999 03/2011	03/2011	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
93	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	03/2011	0/0
94	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	12/2009 03/2011	03/2011	0/0
95	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52 -	- 03/2009	03/2011	0/0
96	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00 -	03/2009 12/2009	03/2011	0/0
97	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
98	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
99	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100007]NCR,Multi State	04/1985	158.77 432.46	03/1994 -	12/2011	0/0
100	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
101	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
102	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
103	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	03/2012	0/0
104	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
105	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
106	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 381.17	- -	03/2012	0/0
107	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
108	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
109	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	03/2012	0/0
110	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]MRTP,Maharashtra	04/2003	3,125.20 4,174.40	06/2011 03/2012	03/2012	0/0
111	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	03/2012 -	03/2012	0/0
112	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	03/2011 -	03/2012	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
113	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
114	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	12/2012	0/0
115	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
116	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 194.07	06/2004 -	12/2012	0/0
117	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
118	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2012	0/0
119	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2012	0/0
120	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	03/2010 -	12/2012	0/0
121	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
122	CONSTRUCTION OF NEW LINE FROM HARMATHITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 156.00	- -	12/2012	0/0
123	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.98	03/2002 -	01/2013	0/0
124	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
125	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	12/2012 01/2013	01/2013	0/0
126	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	02/2013	0/0
127	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	02/2013	0/0
128	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
129	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
130	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 167.73	03/2012 -	02/2013	0/0
131	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 634.13	03/1995 -	03/2013	0/0
132	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
133	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 1,010.00	- -	03/2013	0/0
134	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2013	0/0
135	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
136	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	- -	03/2013	0/0
137	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	03/2013	0/0
138	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38 470.21	- -	03/2013	0/0
139	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
140	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2013	0/0
141	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	- -	03/2013	0/0
142	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
143	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	03/2013	0/0
144	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
145	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2013	0/0
146	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16 -	02/2009 02/2009	04/2013	0/0
147	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41 207.00	03/2009 03/2009	04/2013	0/0
148	CHURCHGATE-VIRAR: CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	653.84 1,302.12	06/2013 06/2013	06/2013	0/0
149	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
150	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
151	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
152	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2013	0/0
153	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	03/2014	0/0
154	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2014	0/0
155	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
156	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	03/2014	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
157	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2014	0/0
158	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014 -	03/2014	0/0
159	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
160	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
161	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
162	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2014	0/0
163	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 325.00	03/2010 06/2014	06/2014	0/0
164	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	02/2015 -	02/2015	0/0
165	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
166	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
167	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
168	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 619.34	04/2014 -	03/2015	0/0
169	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
170	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
171	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015 -	03/2015	0/0
172	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
173	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	12/2015 -	12/2015	0/0
174	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2016	0/0
175	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	03/2014 03/2016	03/2016	0/0
176	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 03/2016	03/2016	0/0
177	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	03/2016 -	03/2016	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
178	New Work for Construction of Metro railway - [N22000111]RVNL, West Bengal	04/2010	2,619.02 -	03/2016 -	03/2016	0/0
179	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,028.05	03/2005 12/2008	06/2016	0/0
180	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
181	New Work for Construction of Metro railway from No - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	03/2016 -	06/2016	0/0
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133](NR), J and K	03/1995	2,500.00 2,500.00	03/2001 -	12/2017	0/0
183	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
184	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, Kerala	10/1998	550.00 -	- -	-	0/0
185	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL, Andhra Pradesh	06/2000	168.34 -	04/2003 03/2010	-	0/0
186	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 -	- 09/2009	-	0/0
187	KODERMA-TILAIYA (NL), ECR - [220100305]ECR, Jharkhand	04/2002	459.91 418.17	- -	-	0/0
188	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER, Jharkhand	03/1997	186.92 -	02/2006 -	-	0/0
189	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
190	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50 -	02/2010 -	-	0/0
191	VIRAMGAM-BHILDI(WR), GC - [220100062]WR, Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
192	NANGALDAM-TALWARA(NL), NR - [220100188](NR), Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
193	HUBLI-ANKOLA(NL), SWR - [220100193]SWR, Karnataka	04/1997	227.00 997.58	- -	-	0/0
194	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR, Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
195	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
196	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
197	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR, Karnataka	02/1999	138.00 901.62	- -	-	0/0
198	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR, Bihar	04/2003	324.66 528.65	- -	-	0/0
199	DANIWAN-BIHARSARIF (NL), ECR - [220100311]ECR, Bihar	04/2001	104.79 -	- -	-	0/0
200	RAMGANJMUUNDI-BHOPAL (NL), WCR - [220100314]WCR, Madhya Pradesh	04/2001	727.13 727.13	- -	-	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
201	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
202	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
203	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
204	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0
205	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
206	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
207	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
	Total		63,915.28 -			0/0
Road Transport & Highways						
208	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	11/2012	0/0
209	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	11/2012	0/0
210	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82 -	11/2008 -	11/2012	0/0
211	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	11/2012	0/0
212	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	08/2011 -	11/2012	0/0
213	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00 -	10/2012 -	11/2012	0/0
214	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00 -	05/2012 -	11/2012	0/0
215	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	11/2012	0/0
216	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	11/2012	0/0
217	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	04/2004 -	12/2012	0/0
218	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	03/2005 -	12/2012	0/0
219	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	12/2012	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
220	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J and K	12/2003	166.27 -	03/2008 -	12/2012	0/0
221	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	01/2009 -	12/2012	0/0
222	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	06/2008 -	12/2012	0/0
223	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	12/2012	0/0
224	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	09/2008 -	12/2012	0/0
225	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	10/2008 -	12/2012	0/0
226	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	12/2012	0/0
227	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91 -	10/2008 -	12/2012	0/0
228	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	12/2012	0/0
229	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00 -	09/2008 -	12/2012	0/0
230	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	06/2008 -	12/2012	0/0
231	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	12/2012	0/0
232	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	12/2012	0/0
233	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	12/2012	0/0
234	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	12/2012	0/0
235	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	02/2004 -	12/2012	0/0
236	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2012	0/0
237	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	10/2009 -	12/2012	0/0
238	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	12/2012	0/0
239	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70 -	02/2004 -	12/2012	0/0
240	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00 -	01/2011 -	12/2012	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
241	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	12/2012	0/0
242	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	07/2012 -	12/2012	0/0
243	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00 -	06/2012 -	12/2012	0/0
244	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	05/2012 -	12/2012	0/0
245	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	10/2011 -	12/2012	0/0
246	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	12/2012	0/0
247	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhandd	08/2010	625.07 -	01/2013 -	01/2013	0/0
248	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	10/2008 -	02/2013	0/0
249	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	01/2011 -	02/2013	0/0
250	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	02/2013	0/0
251	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	02/2013	0/0
252	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2013	0/0
253	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2013	0/0
254	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2013	0/0
255	PATHANKOT- BHOGPUR, KM.26- KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	05/2008 -	03/2013	0/0
256	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	10/2008 -	03/2013	0/0
257	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	03/2008 -	03/2013	0/0
258	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	03/2013	0/0
259	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	03/2013	0/0
260	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2013	0/0
261	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2013	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
262	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	03/2008 -	03/2013	0/0
263	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	06/2008 -	03/2013	0/0
264	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	05/2008 -	03/2013	0/0
265	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00 -	06/2008 -	03/2013	0/0
266	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	09/2009 -	03/2013	0/0
267	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2013	0/0
268	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI, Gujarat	03/2010	1,509.10 -	09/2012 -	03/2013	0/0
269	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00 -	03/2013 -	03/2013	0/0
270	PUNE-SATARA (NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55 -	03/2013 -	03/2013	0/0
271	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39 -	03/2013 -	03/2013	0/0
272	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00 -	04/2013 -	04/2013	0/0
273	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00 -	05/2013 -	05/2013	0/0
274	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00 -	05/2013 -	05/2013	0/0
275	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI, Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2013	0/0
276	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00 -	11/2012 -	06/2013	0/0
277	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	06/2013	0/0
278	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50 -	06/2013 -	06/2013	0/0
279	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	06/2013 -	06/2013	0/0
280	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	04/2009 -	07/2013	0/0
281	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	11/2008 -	07/2013	0/0
282	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, Multi State	12/2003	604.00 -	12/2009 -	07/2013	0/0
283	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00 -	07/2013 -	07/2013	0/0
284	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88 -	07/2013 -	07/2013	0/0
285	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, Bihar	01/2011	575.00 -	07/2013 -	07/2013	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
286	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	11/2011	08/2013	0/0
287	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	08/2013	08/2013	0/0
288	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	08/2013	08/2013	0/0
289	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	08/2013	08/2013	0/0
290	BHUBANESWAR TO PURI - [N24000195]NHAI,Orissa	03/2011	500.29	08/2013	08/2013	0/0
291	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84	08/2013	08/2013	0/0
292	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79	08/2013	08/2013	0/0
293	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43	08/2013	08/2013	0/0
294	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	09/2013	09/2013	0/0
295	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00	09/2013	09/2013	0/0
296	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	05/2012	10/2013	0/0
297	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	10/2013	10/2013	0/0
298	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00	01/2013	10/2013	0/0
299	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	11/2013	11/2013	0/0
300	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
301	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
302	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
303	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	02/2010	12/2013	0/0
304	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
305	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	12/2013	12/2013	0/0
306	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	12/2013	12/2013	0/0
307	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	11/2008	01/2014	0/0
308	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00	01/2014	01/2014	0/0
309	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00	01/2014	01/2014	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
310	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Orissa	07/2011	586.00 -	01/2014 -	01/2014	0/0
311	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
312	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
313	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI, Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
314	4-laning of Barhi-Hazaribagh - [N24000191]NHAI, Jharkhandd	02/2012	398.00 -	02/2014 -	02/2014	0/0
315	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI, Bihar	12/2003	300.00 -	10/2008 -	03/2014	0/0
316	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
317	Chennai-Tada(Six lane) - [N24000129]NHAI, Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
318	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00 -	08/2012 -	03/2014	0/0
319	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
320	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI, Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
321	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
322	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
323	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
324	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00 -	07/2009 -	04/2014	0/0
325	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI, Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
326	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
327	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI, Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
328	2laning with PS Gopalganj-Chappra - [N24000190]NHAI, Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0
329	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, Orissa	11/2011	909.00 -	05/2014 -	05/2014	0/0
330	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J and K	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
331	SNG toBANL - [N24000189]NHAI, J and K	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
332	BEAWAR-PALI-PINDWARA - [N24000199]NHAI, Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
333	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
334	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
335	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
336	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
337	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	08/2014	0/0
338	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	06/2010 -	09/2014	0/0
339	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
340	PANIKHOLI-RIMOLI - [N24000197]NHAI,Orissa	03/2012	1,410.00 -	09/2014 -	09/2014	0/0
341	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
342	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
343	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
344	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
345	NASHRI CHANANI - [N24000162]NHAI,J and K	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
346	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J and K	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		89,789.00 -			0/0
Shipping & Ports						
347	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	10/2008	0/0
348	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
349	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
350	Acquisition of two nos. of 120 B.P BY 079& 080 - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 -	06/2011 09/2012	09/2012	0/0
351	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 10/2012	10/2012	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
352	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	09/2012 10/2012	10/2012	0/0
353	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
354	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
355	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
356	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	12/2012	0/0
357	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
358	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	03/2013	0/0
359	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	12/2012 05/2013	05/2013	0/0
360	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 06/2013	06/2013	0/0
361	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	10/2013	0/0
362	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 10/2013	10/2013	0/0
363	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
364	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
Total			16,087.68 -			0/0
Telecommunications						
365	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	10/2009 -	03/2011	0/0
366	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 930.60	11/2010 -	12/2012	0/0
367	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	02/2007 03/2012	02/2013	0/0

(Oct,2012)

Date of Commissioning

S.No	Project	Date of Approval	Original / Revised Cost	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
368	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	03/2013	0/0
369	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	06/2009 -	03/2013	0/0
370	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	03/2009 -	03/2013	0/0
371	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	06/2013	0/0
372	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	06/2013	0/0
373	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	10/2007 -	-	0/0
374	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	03/2009 -	-	0/0
375	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
376	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
377	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
	Total		5,735.48 -			0/0
Urban Development						
378	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	09/2014	0/0
379	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
380	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
Water Resources						
381	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
Grand Total			383,650.54			0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
