



288th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(Rs.100 Crore and above)
OCTOBER, 2009

Ministry of Statistics & Programme Implementation
Sardar Patel Bhawan, New Delhi
Website:- www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 100 Crore and Above During 2008-09	6-10
Summary of Projects	1-17
Sector wise analysis of projects	18-52

EXECUTIVE SUMMARY

The 288th Flash Report for October' 2009, that contains information on the status of 591 projects in the Central Sector, each costing Rs. 100 crores and above. During October' 2009, four projects reported completion and have been dropped from the monitor of this Ministry. During the month under reference, 4 new projects have been added. Sector-wise number of ongoing projects is given below:

S. No.	Sector	Projects on monitor
1.	ROAD TRANSPORT & HIGHWAYS	155
2.	RAILWAYS	150
3.	POWER	83
4.	PETROLEUM	64
5.	COAL	43
6.	TELECOMMUNICATION	29
7.	STEEL	29
8.	SHIPPING & PORTS	18
9.	CIVIL AVIATION	9
10.	ATOMIC ENERGY	5
11.	URBAN DEVELOPMENT	3
12.	MINES	1
13.	HEALTH & FW	1
14.	WATER RESOURCES	1
Total		591

2. Forty (40) projects have reported additional delays compared to the completion dates in the previous month. There have been slippages in the range of 1-36 months in respect of

projects relating to Atomic Energy, Civil Aviation, Coal, Steel, Petroleum, Power, Road Transport and Highways, Shipping & Port and Telecommunications sectors.

3. In the **Atomic Energy Sector**, 4 projects have reported additional delays as compared to the position in the previous month. Kaiga Atomic Power Project units 3&4, Kaiga and Rajasthan Atomic Power Project units 5&6, Rawatbhata, have reported additional delays of 2 month and 1 month respectively because of non - availability of fuel. Kudankulam APP (NPCIL), has reported additional delay of 3 months due to slippage of commitment of M/s Atom Stroy Export (ASE) Russia. Prototype Fast Breeder Reactor Kalpakkam, Tamilnadu has reported additional delay of 12 months, however, no specific reasons have been provided by the project authorities.

4. In the **Civil Aviation Sector**, Construction of New International Terminal Building Thiruvananthapuram, Kerala, has reported additional delay of 1 month, however no specific reason has been provided by project authorities.

5. In the **Coal sector**, 6 projects have reported additional delays in the range of 1-36 months. Pelma UG and Batura OC have reported additional delays of 36 months and 24 months respectively due to delay in acquisition of land. Sarpi Augmentation (UG) has reported additional delays of 12 months due to revision of design and diversion of fund. Jhanjra Continous Miner (2nd Set) has reported additional delay of 36 months, however, no specific reason has been reported by the project authorities. Barsingsar Lignite Mine has reported additional delay of 1 month due to inadequate mobilization of labour by the contractor. TRS-II Expansion (1470MW to 1970MW) (NLC) has reported additional delay of 3 months due to delay in erection of equipments.

6. In the **Steel Sector**, 2 projects have reported additional delays in the range of 1-2 months. Installation of 700 Tonnes per Day Oxygen Plant, Orissa, has reported additional delay of 1 month due to delay in supply of Booster Air Compressor. Simultaneous Blowing of Blast Furnace Converter of SMS-II, Orissa has reported additional delays of 2 months due to delay in civil work and supply of other equipments.

7. In the **Petroleum Sector**, Installation of FCC Gasoline Desulphurisation Unit at Mathura Refinery has reported additional delay of 1 month due to delay in supply of compressor's piping auxiliaries and instrumentation items by BPCL.

8. In the **Power Sector**, 3 projects have reported additional delays in the range of 1-7 months. Sipat STPP Stage-I, 3x660 MW at Bilaspur, Chattisgarh has reported additional delay of 7 months due to delay in supply of equipments by M/s Power Machine, Russia. System Strengthening-VII of Southern Region (248 CKM) Tamil Nadu has reported additional delay of 1 month due to delay in construction of downstream bay, Northern Region System Strengthening Scheme-V (1222 CKM) has reported additional delay of 3 months to match with the linked deposited.

9. In the **Road Transport and Highways Sector**, 19 projects have reported additional delays in the range of 1-12 months. The concerned project authorities have not indicated specific reasons for such delays.

10. In the **Shipping & Ports Sector**, Rail Connectivity to Intergrated Container Terminal at Vallarpadam has reported additional delays of 12 months due to revision of cost.

11. In the **Telecommunication Sector**, 3 projects have reported additional delays in the range of 1-2 months. GSM based network Expansion Plan, Phase-IV, Chattisgarh has reported additional delay of 2 months due to delay in Execution of work by M/s ITI Ltd. Assam Telecom Circle, Phase-V.I, 2G & 3G has reported additional delay of 1 months due to delay in supply of equipment. Kolkata Telecom District, Phase-IV has reported additional delay of 2 months due to revision of works.

Status as on 01.11.2009 in respect of completion of projects costing Rs.100 crore and above in different sectors during 2009-10 is indicated in the following tables.

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Delayed
1	Road Transport & Highways	155	19
2	Railways	150	0
3	Power	83	3
4	Petroleum	64	1
5	Coal	43	6
6	Steel	29	2
7	Telecommunications	29	3
8	Shipping & Ports	18	1
9	Civil Aviation	9	1
10	Atomic Energy	5	4
11	Urban Development	3	0
12	Mines	1	0
13	Health & Family Welfare	1	0
14	Water Resources	1	0
	Total	591	40

ANNEXURE-I

Month wise List of Completed Project Costing Rs.100 Crore and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April,2009				
<u>Steel</u>				
1	COKE OVEN BATTERY NO. 4(PHASE-1) (RINL)(RASTRIYA ISPAT NIGAM LIMITED) - [120100061]	286.63	12/2006	301.25
May,2009				
<u>Petroleum</u>				
2	AUGMENTATION OF MUNDRA-PANIPAT CRUDE OIL PIPELINE(INDIAN OIL CORPORATION LIMITED) - [160100291]	205.00	03/2008	140.55
<u>Road Transport & Highways</u>				
3	JHANSI-SHIVPURI ,NH-25,NH-25 KM-91-50(NHDP,P) - [240106251]	220.31	05/2008	149.02
4	BHARATPUR MAHAHA, NH-11, KM.63 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106259]	250.00	01/2010	341.10
5	AMBALA-ZIRAKPUR, NH-21AND22, KM.5/735 TO KM.39/961(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106261]	298.00	11/2010	364.62
6	KONDHALI-TELEGAON(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000041]	212.00	03/2010	331.87
<u>Telecommunications</u>				
7	GSM BASED NETWORK EXPANSION PH-IV (BSNL) (U.P. WEST)(BHARAT SANCHAR NIGAM LIMITED) - [260100081]	359.07	06/2009	36.19
8	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(PUNJAB)(BHARAT SANCHAR NIGAM LIMITED) - [260100089]	508.63	06/2010	365.16
9	GSM BASED NETWORK EXPANSION PH-IV (BSNL)(RAJASTHAN)(BHARAT SANCHAR NIGAM LIMITED) - [260100090]	448.91	06/2009	154.52
10	GSM BASED NETWORK(PH-IV)(BSNL) ORISSA(BHARAT SANCHAR NIGAM LIMITED) - [260100093]	164.06	12/2009	89.29
11	GSM-NETWORK EXPANSION(PH-IV) (BSNL) W. BENGAL(BHARAT SANCHAR NIGAM LIMITED) - [260100094]	428.00	06/2009	200.00
June,2009				
<u>Petroleum</u>				
12	GREEN FUELS & EMISSION CONTROL (HPCL) MUMBAI REF.(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [160100236]	1,152.00	06/2009	1,551.79
<u>Railways</u>				

Month wise List of Completed Project Costing Rs.100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
13	THANE-TURBHE-NERUL-VASHI(MTP)(METROPOLITAN TRANSPORT PROJECTS) - [220100159]	403.39	03/2000	400.60
<u>Road Transport & Highways</u>				
14	PARADIP PORT,NH-5A (PORT CONNECTIVITY) KM 0 - KM 77(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240100202]	428.00	02/2007	459.38
15	SWAROOPGANJ TO BAKARIA (RJ-1) PH.II, KM.29-KM.0 (NH-76)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106229]	220.00	04/2010	244.47
16	RAJASTHAN/MP BORDER TO KOTA(RJ-10), KM.509- 449.15, NH-76(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106254]	378.22	04/2008	365.05
17	RJ/MP BORDER TO KOTA(RJ-9) NH-76, KM.449.15 TO KM.406(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106255]	297.72	04/2008	289.88
18	AGRA-BHARATPUR(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000027]	195.00	03/2009	192.10
19	PALANPUR TO SWAROOPGANJ,NH-14(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000067]	498.00	03/2009	82.09
July,2009				
<u>Power</u>				
20	KAHAL GAON STPP STAGE - II (NTPC)(NATIONAL THERMAL POWER CORPORATION) - [180100230]	5,868.31	05/2007	4,881.17
<u>Road Transport & Highways</u>				
21	GARAMORE TO BAMANBORE (PACK.-III) PH.-II, KM.254-KM.182.60(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106215]	360.70	11/2007	334.72
22	TINDIVANAM-UIUNDURPET,KM 121-192.25 NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000082]	480.00	03/2009	1,130.80
<u>Telecommunications</u>				
23	COMM. OF GSM EQU. OF 600K LINES(PH-4)(BHARAT SANCHAR NIGAM LIMITED) - [N26000032]	214.00	01/2007	120.48
24	PROJECT NIB-II BROADBAND MULTIPLY(BHARAT SANCHAR NIGAM LIMITED) - [N26000047]	1,008.00	03/2009	337.50
August,2009				
<u>Power</u>				
25	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VIII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000025]	220.69	04/2009	131.26
<u>Railways</u>				
26	MADURAI-DINDIGUL,(LD)(SR)(SR) - [N22000047]	73.19	-	181.81

Month wise List of Completed Project Costing Rs.100 Crore and above during

2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Road Transport & Highways</u>				
27	TIRUNELVEI-PANAGUDI, KM 160-203(T.N)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106242]	423.54	03/2008	220.40
28	SALEM TO KARUR (NS-21 OF TN-2), KM.207.050-KM.248.625, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106270]	253.50	01/2009	333.34
29	SALEM TO KARUR, KM.258-645 TO KM.292.6(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106271]	205.60	08/2008	323.94
30	SALEM TO KERALA BORDER SEC. (TN-7), KM.53 TO KM.100, NH-47(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106274]	379.80	12/2008	453.20
September,2009				
31	MADURAI-KANNIAKUMARI, KM.42 TO KM.80, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106238]	474.21	03/2008	246.20
32	MADURAI-TIRUNVELI SECTION INCLUDING MADURAI-BYPASS, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106239]	567.38	03/2008	382.50
33	MAHUA-JAIPUR, NH-11, KM.120 TO KM.228(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106258]	483.00	03/2009	578.30
34	KARUR TO MADURAI (TN-5), KM.373.275 TO KM.426.6, NH-7(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106275]	283.50	12/2008	448.30
35	INDORE-KALAGHAT(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000034]	472.00	09/2009	663.90
36	Bharuch-Surat Package BOT-II(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000070]	492.00	07/2009	448.87
37	Vadodara-Bharuch Package BOT-I(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000071]	660.00	07/2009	789.84
38	UIUWDURPET-PADALUR,NH-45(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000084]	460.00	06/2009	799.19
<u>Shipping & Ports</u>				
39	ACQUISITION OF 2-300,000 DWT VERY LARGE CRUDE CARRIERS(SHIPPING) - [250100174]	1,136.08	09/2009	1,196.24
October,2009				
<u>Petroleum</u>				
40	DEVELOPMENT OF BASSEIN EAST (ONGCL)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100232]	985.17	03/2006	1,568.46
<u>Railways</u>				
41	2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)(RAIL VIKAS NIGAM LTD.) - [220100221]	93.10	-	126.11
<u>Telecommunications</u>				
42	GSM EQUIPMENT OF 1015K LINES PH-4.5(BHARAT SANCHAR NIGAM LIMITED) - [N26000044]	350.84	11/2008	182.06
43	ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM(BHARAT SANCHAR NIGAM LIMITED) - [N26000059]	567.40	06/2009	241.85

Month wise List of Completed Project Costing Rs.100 Crore and above during
2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
---------	-----------------	------------------------------	--------------------------------------	--

ANNEXURE-I

Month wise List of Deleted Project Costing Rs.100 Crore and above during 2009-2010

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2009				
<u>Telecommunications</u>				
1	500K BROAD BAND ACCESS N/W PH-III(MAHANAGAR TELEPHONE NIGAM LIMITED) - [120100061]	134.25	10/2009	31.95


Summary of projects on the Flash Report for the month of October, 2009

I. Project Implementation – Current Status:

Number of Projects Previous Month	600
Number of Projects Completed/Dropped/Frozen in Previous Month	9
Number of Projects Completed/Dropped/Frozen in Current month	4
Number of Projects Added in Current month	4
Number of Projects in Current Month	591

II. Brief Analysis


a) **Project Status w.r.t Original Schedule:** Out of 591 projects, 14 projects are ahead of schedule, 136 projects are on schedule and 321 projects are delayed. Of the balance, 79 projects do not have fixed dates of commissioning while 41 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

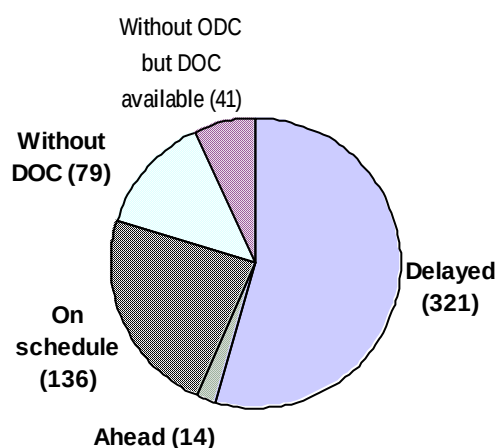

III. Investment Scenario

Figures are in Rs. Crore

The total cost of implementation of 591 projects when sanctioned, was of the order of Rs. 542317.48 crore but this was subsequently revised to Rs. 596302.41 crore implying a cost overrun of 9.95%. The expenditure incurred on these projects till October, 2009 is Rs. 240955.15 crore, which is 40.41% of the revised cost of the projects.

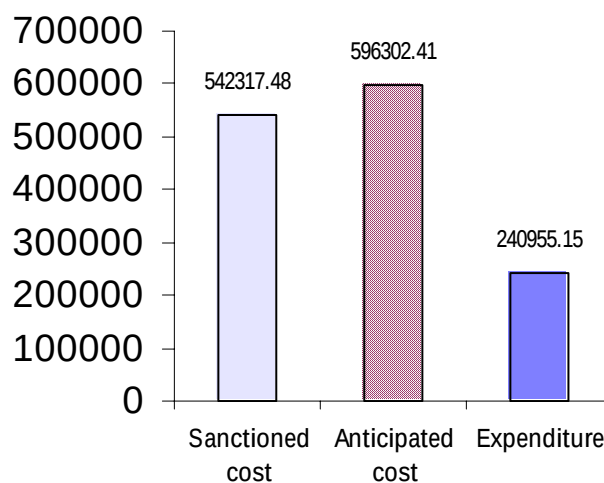

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	600
No of Projects Completed/Dropped/Frozen in Previous Month	9
No of Projects Completed/Dropped/Frozen in Current Month	4
No of Projects added in Current Month	4
No of Projects in Current Month	591

II. Project status

With Respect To	Number of Projects						Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	
Original	321	14	136	41	79	591	54.31
Latest Approved	336	15	140	28	72	591	56.85

III. Project cost

With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Rs. Crore)	%
Original	500	488,971.75	529,365.08	204,261.89	38.60	40,393.33	8.30
Latest Approved	91	53,345.73	66,937.33	36,693.26	54.80	13,591.60	25.50
Total	591	542,317.48	596,302.41	240,955.15	40.41	53984.93	9.95

IV. List of projects completed/dropped current month

IV. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Telecommunications</u>						
GSM EQUIPMENT OF 1015K LINES PH-4.5	10/2008	350.84	11/2008	350.84	09/2009	182.06
<u>Railways</u>						
2ND BRIDGE ON BIRUPA AND MAHANADI(B and S) (ECOR)	04/1997	93.10	N.A.	122.00	N.A.	126.11
<u>Petroleum</u>						
DEVELOPMENT OF BASSEIN EAST (ONGCL)	04/2003	985.17	03/2006	1,688.38	09/2009	1,568.46

IV. List of projects completed/dropped current month

(Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Telecommunications</u>						
ANDHRA PRADESH TELECOM CIRCLE PHASE-IV GSM	03/2008	567.40	06/2009	482.29	10/2009	241.85

V. List of projects added

(Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Coal</u>					
KARTALI (EAST) OC	7/2008	178.44	3/2014	178.44	3/2014
<u>Road Transport & Highways</u>					
PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	3/2005	940.00	7/2012	940.00	7/2012
<u>Coal</u>					
JAGANNATHPOR OC	9/2008	152.43	3/2015	152.43	3/2015
KTK OC Sector-I	1/2008	91.50	9/2010	128.16	3/2010

VI. Milestones (Cumulative due & achieved)

Total	1991
Achieved up to month	715

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay
	Original	Anticipated	Original	Last month	This month	(in months)
<u>Atomic Energy</u>						
RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL)	3,072.00	3,072.00	02/2008	01/2010	02/2010	1
KAIGA 3 and 4 UNITS (NPCIL)	4,213.00	3,282.00	10/2009	01/2010	03/2010	2
KUDANKULAM APP (NPCIL)	13,171.00	13,171.00	12/2008	12/2010	03/2011	3
PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	3,492.00	5,677.00	09/2010	09/2010	09/2011	12
<u>Civil Aviation</u>						
CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING	245.58	245.58	12/2008	10/2009	11/2009	1
<u>Coal</u>						
BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC)	254.07	254.60	06/2009	11/2009	12/2009	1
TPS-II EXPANSION (1470MW TO 1970MW) (NLC)	2,030.78	2,453.57	06/2009	11/2010	02/2011	3
AUGMENTATION OF PRODUCTION AT SAPRI UG MINE	147.86	147.86	03/2012	03/2011	03/2012	12
Batura OC	203.82	203.82	03/2013	03/2013	03/2015	24
PELMA OC	448.32	448.32	03/2012	03/2012	03/2015	36
JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II	122.35	122.35	03/2010	03/2010	03/2013	36
<u>Steel</u>						
INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA	302.70	302.70	06/2009	12/2009	01/2010	1
SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II	197.66	197.66	10/2009	11/2009	01/2010	2
<u>Petroleum</u>						
INST. OF FCC GASOLINE DESULPHUN UNIT AT MATHURA RE	348.00	348.00	12/2009	12/2009	01/2010	1
<u>Power</u>						
SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL)	279.30	340.14	07/2009	10/2009	11/2009	1

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
NORTHERN REGION SYSTEM STRENGTHENING SCHEME-V	721.25	721.25	06/2009	12/2009	03/2010	3
SIPAT STPP STAGE - I (NTPC)	8,323.39	8,323.39	12/2009	03/2011	10/2011	7
Road Transport & Highways						
ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2	440.93	440.93	12/2006	10/2009	11/2009	1
ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2	534.39	534.39	05/2007	10/2009	11/2009	1
VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2)	467.93	467.93	03/2005	12/2009	01/2010	1
GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH- 2)	399.75	399.75	03/2005	10/2009	11/2009	1
HYDERABAD BANGALORE SECTION(NH-7)(NHAI)	611.44	592.00	03/2009	10/2009	11/2009	1
TRICHY BYPASS END TO TOVARAMKURCHI (NH- 45B)(NHAI)	261.00	261.00	08/2008	11/2009	12/2009	1
TOVARAMKURCHI- MADURAI,NH45B (NHAI)	263.00	263.00	08/2008	11/2009	12/2009	1
PANIPAT TO PANCHI GUJRAN, NH-1	109.00	109.00	10/2008	10/2009	11/2009	1
ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT	450.00	450.00	07/2008	10/2009	11/2009	1
ORAI TO JHANSI (UP-4),NH- 25, KM.170.0 TO KM.104.0	451.97	451.97	04/2008	03/2010	06/2010	3
LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS- 1/BOT/MP-2),NH7	407.60	407.60	06/2010	06/2010	09/2010	3
JHANSI TO LALITPUR, NH-26	276.09	276.09	09/2009	06/2010	09/2010	3
JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1	263.00	263.00	02/2009	10/2009	03/2010	5
ORAI TO JHANSI (UP-5),NH- 25, KM.220.0 TO KM.170.0	340.68	340.68	03/2008	06/2010	12/2010	6
KASIA TO GORAKHPUR (NH- 28)(NHAI)	242.00	242.00	12/2008	06/2010	12/2010	6
UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	227.00	227.00	12/2008	06/2010	12/2010	6
GARHMUKTESHWAR- MURADABAD (NHAI) OTHERS KM.93-149.25, NH- 24	275.00	275.00	09/2007	12/2009	12/2010	12
HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24	220.00	220.00	09/2007	12/2009	12/2010	12

VII. List of projects reporting additional delays

Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A	284.00	284.00	05/2008	12/2009	12/2010	12
<u>Shipping & Ports</u>						
RAIL CONNECTIVITY TO ICTT AT VALLARPADAM	245.67	298.17	04/2009	11/2009	11/2010	12
<u>Telecommunications</u>						
Assam Telecom Circle, Phase- V.I, 2G & 3G	336.81	174.36	01/2009	10/2009	11/2009	1
GSM BASED NETWORK EXPANSION PLAN PH-4	239.19	239.19	04/2008	10/2009	12/2009	2
KOLKATA TELECOM DISTRICT PH-4	208.50	208.50	09/2008	10/2009	12/2009	2
Number of projects reporting additional delay = 40						

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	5	25,054.29	25,054.29	26,308.29
Civil Aviation	9	4,832.24	4,881.66	4,832.24
Coal	43	26,110.40	26,216.99	27,522.73
Mines	1	4,091.51	4,091.51	4,091.51
Steel	29	45,596.58	45,596.58	49,353.10
Petroleum	64	136,018.51	136,018.51	144,969.18
Power	83	153,835.15	155,649.23	159,742.28
Health & Family Welfare	1	71.18	422.60	443.15
Railways	150	50,032.77	57,528.71	93,320.47
Road Transport & Highways	155	45,226.22	45,226.22	45,431.53
Shipping & Ports	18	12,475.83	12,475.83	12,747.59
Telecommunications	29	11,765.42	11,765.42	11,147.31
Urban Development	3	14,596.67	16,847.03	15,206.03
Water Resources	1	542.90	542.90	1,187.00
Grand total	591	530,249.67	542,317.48	596,302.41


Sector wise Current Status of Projects on the Flash Report

1. Sector: - Atomic Energy

Number of Projects	5
Number of Projects on schedule	1
Number of Projects Delayed	4

Brief Analysis


Project Status w.r.t Original Schedule: Out of 5 projects, 1 projects are on schedule and 4 projects are delayed.



Investment Scenario

Figures are in Rs. Crores

The total cost of implementation of 5 projects when sanctioned, was of the order of Rs. 25054.29 Crores but this was subsequently revised to Rs. 26308.29 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 19321.61 Crores.

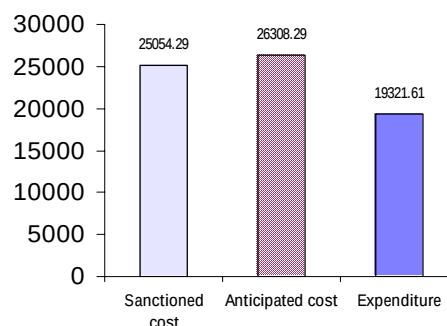


2. Sector: - Civil Aviation

Number of Projects	9
Number of Projects on schedule	3
Number of Projects Delayed	5
Number of Projects Ahead	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 9 projects, 3 projects are on schedule, 5 projects are delayed and 1 project is ahead.



Investment Scenario

The total cost of implementation of 9 projects when sanctioned, was of the order of Rs. 4832.24 Crores but this was subsequently revised to Rs. 4832.24 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 823.93 Crores.

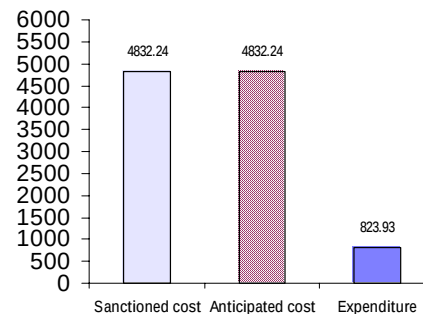


3. Sector: - Coal


Number of Projects	43
Number of Projects on schedule	18
Number of Projects Delayed	21
Number of Projects Ahead	4

Brief Analysis

Project Status w.r.t Original Schedule: Out of 43 projects, 18 projects are on schedule, 21 projects are delayed and 4 projects are ahead.



Investment Scenario

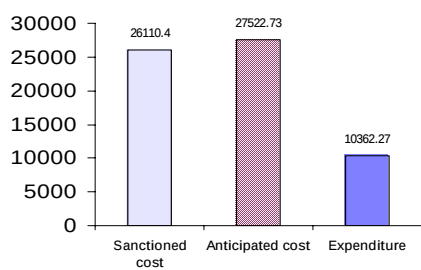


The total cost of implementation of 43 projects when sanctioned, was of the order of Rs. 26110.4 Crores but this was subsequently revised to Rs. 27522.73 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 10362.27 Crores

4. Sector: - Petroleum

Number of Projects	64
Number of Projects on schedule	28
Number of Projects Delayed	33
Number of Projects Ahead	3


Brief Analysis

Project Status w.r.t Original Schedule: Out of 64 projects, 28 projects are on schedule, 33 projects are delayed and 3 projects are ahead .



Investment Scenario

The total cost of implementation of 64 projects when sanctioned, was of the order of Rs. 136018.51 Crores but this was subsequently revised to Rs. 144969.18 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 40790.50 Crores.

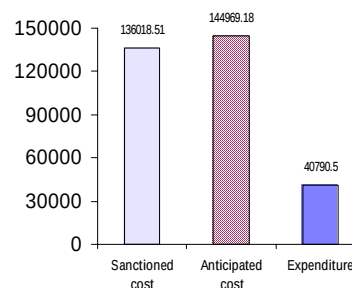


5. Sector: - Power

Number of Projects	83
Number of Projects on schedule	46
Number of Projects Delayed	35
Number of Projects Wo_Doc_Original	1
Number of Projects Wo_Odc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 83 projects, 46 projects are on schedule, 35 projects are delayed, 1 projects is Wo_Doc_Original and 1 projects is Wo_Odc_Original



Investment Scenario

The total cost of implementation of 83 projects when sanctioned, was of the order of Rs. 153835.15 Crores but this was subsequently revised to Rs. 159743.76 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 54428.51 Crores.

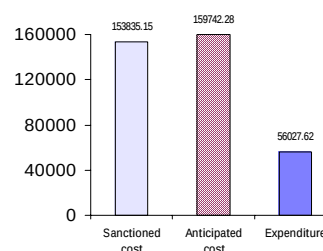


6. Sector: - Railways

Number of Projects	150
Number of Projects on schedule	8
Number of Projects Delayed	40
Number of Projects Ahead	1
Number of Projects Wo_Doc_Original	41
Number of Projects Wo_Odc_Original	60


Brief Analysis

Project Status w.r.t Original Schedule: Out of 150 projects, 8 projects are on schedule, 40 projects are delayed, 1 projects is ahead. 41 projects are Wo_Doc_Original and 60 projects are Wo_Odc_Original



Investment Scenario

The total cost of implementation of 150 projects when sanctioned, was of the order of Rs. 50032.77 Crores but this was subsequently revised to Rs. 93320.47 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 41035.47 Crores.

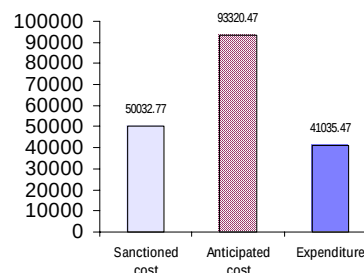


7. Sector: - Road Transport and Highways

Number of Projects	155
Number of Projects on schedule	15
Number of Projects Delayed	135
Number of Projects Ahead	3
Number of Projects Wo_Doc_Original	1


Brief Analysis

Project Status w.r.t Original Schedule: Out of 155 projects, 15 projects are on schedule, 136 projects are delayed, 3 projects are ahead and 1 projects is Wo_Doc_Original.



Investment Scenario

The total cost of implementation of 154 projects when sanctioned, was of the order of Rs. 45226.22 Crores but this was subsequently revised to Rs. 45431.53 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 34054.12 Crores.

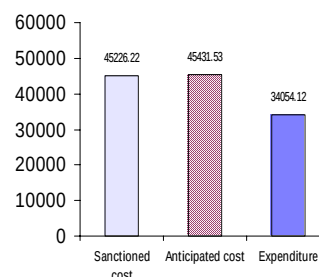


8. Sector: - Shipping and Ports

Number of Projects	18
Number of Projects on schedule	9
Number of Projects Delayed	5
Number of Projects Ahead	2
Number of Projects Wo_Doc_Original	3


Brief Analysis

Project Status w.r.t Original Schedule: Out of 18 projects, 9 projects are on schedule, 5 projects are delayed, 2 projects are ahead and 3 projects are Wo_Doc_Original.

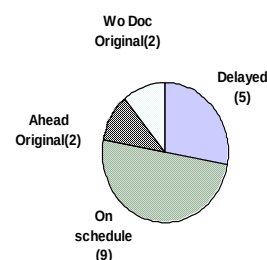

Investment Scenario

The total cost of implementation of 18 projects when sanctioned, was of the order of Rs.12475.83 Crores but this was subsequently revised to Rs. 12747.59 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 3105.88 Crores.

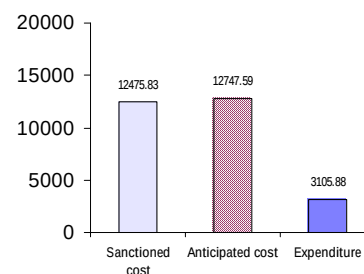


9. Sector: - Steel


Number of Projects	29
Number of Projects on schedule	4
Number of Projects Delayed	23
Number of Projects Wo_Doc_Original	2

Brief Analysis

Project Status w.r.t Original Schedule:
Out of 29 projects, 4 projects are on schedule, 23 projects are delayed and 2 projects are Wo_Doc_Original .



Investment Scenario

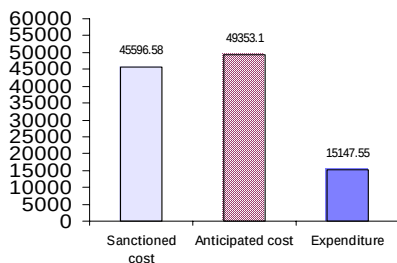


The total cost of implementation of 29 projects when sanctioned, was of the order of Rs. 45596.58 Crores but this was subsequently revised to Rs. 49353.10 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 15147.55 Crores.

10. Sector: - Telecommunications

Number of Projects	29
Number of Projects on schedule	2
Number of Projects Delayed	22
Number of Projects Wo_Doc_Original	5


Brief Analysis

Project Status w.r.t Original Schedule:
Out of 29 projects, 2 projects are on schedule, 22 projects are delayed and 5 projects are Wo_Doc_Original .

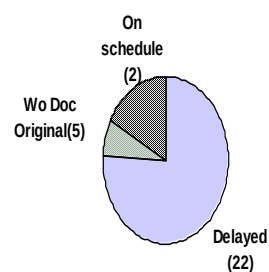

Investment Scenario

The total cost of implementation of 29 projects when sanctioned, was of the order of Rs. 11765.42 Crores but this was subsequently revised to Rs. 11147.31 Crores. The expenditure incurred on these projects till October, 2009 is Rs. 3635.77 Crores.

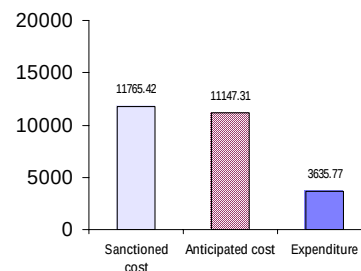

(Oct,2009)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	RAJASTHAN ATOMIC POWER PROJECT 5 and 6 (NPCIL) - [020100042]	04/2002	3,072.00	3,072.00	2,058.00	02/2008	02/2010	1	61/75
2	KAIGA 3 and 4 UNITS (NPCIL) - [020100041]	05/2001	4,213.00	3,282.00	2,465.00	10/2009 09/2007	03/2010	2	71/75
3	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00	13,171.00	12,392.00	12/2008	03/2011	3	61/119
4	URANIUM ORE MINE & PROCESSING PLANT AT TUMMALAPALL - [N02000007]	09/2007	1,106.29	1,106.29	356.94	04/2011	04/2011	0	0/0
5	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	5,677.00	2,049.67	09/2010	09/2011	12	8/80
Total			25,054.29	26,308.29	19,321.61				201/349
<u>Civil Aviation</u>									
6	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BLDG. A - [N04000017]	02/2007	290.92	290.92	146.12	02/2009	10/2009	0	1/24
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING - [N04000016]	10/2006	245.58 295.00	245.58	26.26	12/2008	11/2009	1	1/28
8	C/O NEW EXPANDABLE MODULAR INTEGRATED BLDG. RAIPUR - [N04000034]	03/2008	129.65	129.65	28.90	09/2009	12/2009	0	0/0
9	C/O EXPANDABLE MODULAR INTEGRATED TER. BULD. RAJA - [N04000035]	03/2008	135.04	135.04	43.42	09/2009	12/2009	0	0/0
10	C/O INTEGRATED CARGO COMPLEX(PH-III) AT CHENNAI A - [N04000039]	08/2008	144.94	144.94	18.66	04/2010	01/2010	0	0/0
11	C/O EXPANDABLE MODULAR TER. BULD. AT DABH INDORE - [N04000036]	02/2008	135.60	135.60	29.54	10/2009	02/2010	0	0/0
12	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA - [N04000040]	01/2008	535.00	535.00	116.05	06/2010	06/2010	0	0/0
13	D/O KAMARAJ DOMESTIC TER-PH-II & EXP. ANNA INT. TE - [N04000038]	08/2008	1,273.00	1,273.00	205.18	01/2011	01/2011	0	0/0
14	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]	08/2008	1,942.51	1,942.51	209.80	05/2011	05/2011	0	0/0
Total			4,832.24	4,832.24	823.93				2/52
<u>Coal</u>									
15	BARSINGSAR MINE 2.10 MTPA LIGNITE (NLC) - [060100090]	12/2004	254.07	254.60	205.89	06/2009	12/2009	1	11/21
16	EXPANSION OF MINE-II (10.5 MTPA TO 15.0 MTPA) (NLC) - [060100088]	10/2004	2,161.28	2,295.93	1,683.47	06/2009	02/2010	0	25/23

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]	12/2004	1,114.18	1,626.09	1,318.57	06/2009	03/2010	0	22/26
18	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]	07/2005	1,667.55	1,667.55	855.38	03/2010	03/2010	0	3/7
19	DIPKA EXPANSION OCP (SECL) (20 MTY) - [060100094]	07/2005	1,268.53	1,268.53	749.26	03/2010	03/2010	0	2/6
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]	05/2006	789.88	789.88	134.44	03/2010	03/2010	0	0/1
21	BHARATPUR OC EXPANSION PHASE-III PROJECT - [N06000030]	02/2007	131.39	131.39	358.84	03/2010	03/2010	0	0/0
22	BALRAM OCP EXTENSION - [N06000044]	12/2007	172.08	172.08	471.91	03/2009	03/2010	0	0/0
23	KTK OC Sector-I - [N06000077]	01/2008	91.50	128.16	128.16	09/2010	03/2010	0	0/0
24	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78	2,453.57	1,831.44	06/2009	02/2011	3	18/24
25	LAKHANPUR OC EXP. PROJECT PH-II - [N06000069]	03/2004	98.74	116.54	245.70	03/2007	03/2011	0	0/0
26	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]	01/2005	302.96	302.96	55.66	03/2010	03/2012	0	0/4
27	ASHOK EXPN.OCP -CCL (5 MTY) - [060100096]	04/2006	471.66	471.66	100.37	03/2011	03/2012	0	0/0
28	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	06/2006	746.04	746.04	134.20	03/2012	03/2012	0	0/1
29	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]	10/2006	249.03	249.03	28.42	03/2012	03/2012	0	0/0
30	JHANJRA LONGWAL UG PHASE II - [N06000020]	11/2006	287.18	287.17	-	11/2009	03/2012	0	0/0
31	NIGAIH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]	10/2007	529.40	259.40	-	03/2012	03/2012	0	0/0
32	AUGMENTATION OF PRODUCTION AT SAPRI UG MINE - [N06000058]	09/1987	147.86	147.86	25.50	03/2012	03/2012	12	0/0
33	ANANTA OC EXPANSION PH-II - [N06000067]	08/2008	207.28	207.28	244.40	03/2012	03/2012	0	0/0
34	ADRIYALA SHAFT PROJECT - [N06000016]	09/2006	212.34	212.34	17.34	03/2013	09/2012	0	2/11
35	TUTICORIN THERMAL POWER PROJECT - [N06000047]	05/2008	4,904.54	4,904.54	449.28	08/2012	09/2012	0	0/0
36	KAKATIYA LAONGWALL - [N06000048]	12/2008	453.63	453.63	40.54	12/2012	12/2012	0	0/0
37	KUSMUNDA EXPN.OCP(SECL)(10MTY) - [N06000008]	06/2006	737.65	1,188.31	581.04	03/2011 03/2013	03/2013	0	0/4
38	MAGADH OC (CCL) - [N06000015]	07/2006	469.78 706.40	469.78	12.12	07/2012	03/2013	0	0/0
39	JALLARAM SHAFT PROJECT - [N06000025]	03/2013	467.78	467.78	10.37	03/2013	03/2013	0	0/7
40	KANIHA OCP - [N06000035]	12/2007	457.77	457.77	48.96	03/2012	03/2013	0	0/0
41	JHANJRA CONTINEOUS MINAR FOR JHANJRA UG-II - [N06000057]	02/2009	122.35	122.35	-	03/2010	03/2013	36	0/0
42	NARAYANKURI UG - [N06000059]	02/2009	149.06	149.06	-	03/2013	03/2013	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
43	CHITRA EAST OCP - [N06000060]	08/2007	112.69	112.69	-	11/2010	03/2013	0	0/0
44	HINGULA OC-II EXP. PH-II (15 MTY) - [N06000068]	11/2008	475.93	479.53	171.63	03/2013	03/2013	0	0/0
45	BINA EXTN. PROJ - [N06000019]	11/2006	168.97	168.97	88.05	03/2014	11/2013	0	1/1
46	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]	05/2006	1,352.04	1,352.04	26.92	03/2014	03/2014	0	1/1
47	CHURCHA UG - [N06000046]	06/2008	462.35	462.35	235.14	06/2014	03/2014	0	0/0
48	RAJMAHAL OC EXP. - [N06000056]	02/2006	50.08	153.82	2.76	03/2010	03/2014	0	0/0
49	PENGANGA OC - [N06000066]	10/2008	339.77	339.77	-	03/2014	03/2014	0	0/0
50	KARTALI (EAST) OC - [N06000076]	07/2008	178.44	178.44	-	03/2014	03/2014	0	0/0
51	GOPAL PRASAD OCP - [N06000042]	02/2008	395.87	395.87	23.23	03/2013	03/2015	0	0/0
52	PELMA OC - [N06000045]	07/2008	448.32	448.32	-	03/2012	03/2015	36	0/0
53	Batura OC - [N06000049]	09/2008	203.82	203.82	-	03/2013	03/2015	24	0/0
54	BAROUD OC EXPANSION - [N06000065]	07/2008	135.58	135.58	23.26	03/2015	03/2015	0	0/0
55	JAGANNATHPOR OC - [N06000075]	09/2008	152.43	152.43	-	03/2015	03/2015	0	0/0
56	BHUBANESWARI OCP - [N06000034]	12/2007	490.10	490.10	54.70	03/2014	03/2016	0	0/0
57	TALABIRA OCP - [N06000043]	03/2008	447.72	447.72	5.32	03/2015	03/2016	0	0/0
Total			26,110.40	27,522.73	10,362.27				85/137
<u>Mines</u>									
58	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM, SMELTER AND POWE - [100100054]	10/2004	4,091.51	4,091.51	3,316.00	12/2008	11/2009	0	18/111
Total			4,091.51	4,091.51	3,316.00				18/111
<u>Steel</u>									
59	Deve. of Bailadila Iron Ore Deposit-II(B)(NMDCL) - [N12000018]	01/2003	295.89	607.17	196.14	10/2009	10/2009	0	2/21
60	INSTALLATION OF NEW COKE OVEN GAS HOLDER, ROURKELA - [N12000024]	07/2007	123.22	123.22	75.75	06/2009	10/2009	0	0/0
61	REBUILDING OF COKE OVEN BATTERY NO.-4 - [N12000021]	05/2007	248.94	248.94	147.87	08/2009	12/2009	0	0/0
62	INSTALLATION OF 700 TPD OXYGEN PLANT, ROURKELA - [N12000025]	07/2007	302.70	302.70	199.77	06/2009	01/2010	1	0/0
63	SIMULTANEOUS BLOWING OF BOF CONVERTER OF SMS-II - [N12000036]	01/2008	197.66	197.66	78.69	10/2009	01/2010	2	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
64	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP) - [N12000054]	07/2008	172.78	191.00	48.33	01/2010	01/2010	0	0/0
65	ENHANCEMENT OF LOADING CAPACITY AT BOLANI IRON ORE - [N12000049]	06/2008	124.88	119.88	36.08	12/2009	02/2010	0	0/0
66	COAL DUST INJECTION IN BF-2 and 3 - [120100069]	04/2006	132.73	133.92	84.05	05/2008	03/2010	0	0/2
67	REBUILDING OF COKE OVEN BATTERY-10 - [N12000016]	03/2007	416.50	416.50	206.34	09/2009	03/2010	0	0/0
68	REBUILDING OF BLAST FURNANCE NO.2(BOKARO STEEL PL - [N12000035]	10/2007	892.32	892.32	446.10	08/2009	03/2010	0	0/0
69	Pulverised coal injection system for bf-1&2 - [N12000037]	11/2007	125.00	130.00	32.75	09/2009	03/2010	0	0/0
70	EXPANSION OF SALEM STEEL PLANT - [N12000050]	01/2008	1,902.00	1,902.00	1,031.35	03/2010	06/2010	0	0/0
71	AIR SEPARATION PLANT (ASU-4) - [N12000060]	03/2008	96.00	170.00	40.52	06/2010	06/2010	0	0/0
72	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00	353.00	79.91	02/2010	08/2010	0	0/0
73	Rebuilding of coke oven battery No.1 & 2 (Bokaro S - [N12000033]	10/2007	500.90	500.90	112.24	04/2010	10/2010	0	0/0
74	Air Separation Plant(ASU-5) - [N12000052]	06/2008	129.50	129.50	3.32	12/2010	12/2010	0	0/0
75	POWER PLANT-I - [N12000039]	09/2007	462.00	350.00	81.97	12/2009	01/2011	0	0/0
76	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]	07/2007	230.00	358.00	96.14	02/2010	01/2011	0	0/0
77	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]	07/2007	244.30	232.93	45.23	07/2009	05/2011	0	0/0
78	INSTALLATION OF NEW TURBO BLOWER IN TURBO BLOWER S - [N12000034]	10/2007	105.33	116.33	9.68	08/2009	05/2011	0	0/0
79	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]	10/2005	8,692.00	12,228.00	4,620.00	10/2009	06/2011	0	0/126
80	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00	168.95	11.69	10/2009	06/2011	0	0/0
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00	14,443.00	4,633.69	07/2010	06/2011	0	0/0
82	EXPANSION OF BOKARO STEEL PLANT - [N12000055]	01/2008	3,316.00	3,316.00	530.12	12/2010	10/2011	0	0/0
83	Augmentation of Iron Ore Storage in RMHP - [N12000053]	05/2008	480.00	480.84	-	09/2010	12/2011	0	0/0
84	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]	09/2008	6,133.00	6,171.00	884.34	02/2011	03/2012	0	0/0
85	EXPANSION OF BHILAI STEEL PLANT - [N12000057]	09/2008	5,185.00	4,792.00	1,207.54	05/2011	09/2012	0	0/0
86	COKING COAL FACILITIES IN COAL HANDLING PLANT - [N12000010]	09/2006	133.91	134.32	103.45	03/2008	-	-	0/3
87	INSTALLATION OF MSDS-V AND TRANSMISSION NETWORK F - [N12000022]	05/2007	143.02	143.02	104.49	11/2008	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		45,596.58	49,353.10	15,147.55				2/152
	<u>Petroleum</u>								
88	CLEAN FUELS PROJECT AT VISAKH REFINERY(HPCL) - [160100281]	04/2003	1,635.00	2,147.79	2,095.36	05/2006	12/2009	0	29/45
89	INST. OF FACILITIES FOR IMPROVEMENT IN DIESEL QUALITY (IOCL) - [160100289]	11/2005	1,876.00	2,869.00	2,327.46	04/2009 12/2009	12/2009	0	31/36
90	DADRI- PANIPAT R-LNG SPUR PIPELINE - [N16000018]	06/2005	250.66	350.00	297.16	06/2008	12/2009	0	0/0
91	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]	08/2006	3,195.16	1,800.00	1,518.89	12/2008	12/2009	0	0/0
92	CRUDE OIL RECEIPT FACILITIES,KOCHI REFINERY - [N16000028]	04/2006	2,591.80	3,941.41	1,793.09	09/2009	12/2009	0	0/0
93	CHENNAI-BANGALORE PIPELINE - [N16000029]	07/2007	232.11	273.00	184.87	07/2009	12/2009	0	0/0
94	MSQ UPGRADATION PROJECT AT PANIPAT REFINERY - [N16000035]	01/2008	1,131.00	1,131.00	661.95	12/2009	12/2009	0	0/0
95	LPG PROCESSING & COMPRESSION - [N16000041]	08/2007	142.00	139.07	32.13	10/2009	12/2009	0	0/0
96	CHAINSA-JHAJJAR PIPE LINE PROJECT - [N16000047]	11/2007	967.77	510.00	301.29	09/2009	12/2009	0	0/0
97	RESIDUE UPGRADATION AND MS/HSD QUALITY IMPROVEMENT - [N16000021]	01/2007	5,693.00	5,882.00	4,200.02	01/2010	01/2010	0	0/0
98	INST. OF FCC GASOLINE DESULPHUR UNIT AT MATHURA RE - [N16000034]	01/2008	348.00	348.00	153.27	12/2009	01/2010	1	0/0
99	PANIPAT NAPHTHA CRACKER PROJECT - [160100292]	04/2006	12,138.00	14,439.00	10,360.48	09/2009 11/2009	02/2010	0	61/101
100	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10	429.38	483.40	03/2007	03/2010	0	3/3
101	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90	219.22	134.54	03/2006	03/2010	0	6/6
102	SULTANPUR NEEMRANA PIPE LINE PROJECT - [N16000049]	11/2007	396.13	396.13	44.46	10/2009	03/2010	0	0/0
103	VIJAPUR DADRI-BAWANA PIPE LINE PROJECT - [N16000048]	11/2007	5,595.31	3,860.00	2,856.20	11/2009	04/2010	0	0/0
104	HEERA RECONSTRUCTION - [N16000062]	05/2008	706.70	706.70	43.20	04/2010	04/2010	0	0/0
105	LUBDE OIL BASE STOCK QUALITY UPGRADATION AT MUMBAI - [N16000026]	10/2006	638.90	1,030.00	422.98	04/2009	05/2010	0	0/0
106	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]	05/2008	333.40	330.40	0.35	05/2010	05/2010	0	0/0
107	MNW-NF BRIDGE PROJECT - [N16000045]	05/2008	175.21	162.12	58.19	03/2009	05/2010	0	0/0
108	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]	06/2007	1,436.21	1,436.21	-	07/2010	05/2010	0	0/0
109	BARGE BUMPER-BOAT LANDING-RISER PROTECTOR PROJECT - [N16000055]	05/2008	289.60	289.60	156.92	05/2010	05/2010	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	INSTALLATION OF FCCV AT MUMBAI REFINERY - [N16000056]	03/2007	900.47	900.47	396.73	09/2009	05/2010	0	0/0
111	SINGLE POINT MOORING PROJECT AT VISAKHAPATNAM - [N16000067]	11/2008	643.46	643.46	96.17	05/2010	05/2010	0	0/0
112	DIESEL HYDRO TREATMENT PROJECT, BRPL DHALIGAON - [N16000009]	06/2006	1,431.91	1,646.39	1,162.57	09/2009	06/2010	0	0/0
113	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]	09/2006	2,305.30	1,339.25	1,131.39	06/2010	06/2010	0	0/0
114	MSQ UPGRADATION PROJECT AT GUWAHATI REFINERY - [N16000036]	04/2008	372.00	372.00	84.39	02/2010	06/2010	0	0/0
115	MSQ UPGRADATION PROJECT AT DIGBOI REFINERY - [N16000037]	04/2008	356.00	356.00	90.19	02/2010	06/2010	0	0/0
116	MSQ UPGRADATION PROJECT AT BARAUNI REFINERY - [N16000038]	04/2008	1,492.00	1,492.00	345.77	04/2010	06/2010	0	0/0
117	MSQ IMPROVMENT PROJECT - [N16000040]	04/2008	293.60	293.60	73.85	12/2009	06/2010	0	0/0
118	TWO PIPELINE REPLACEMENT PROJECT AT AHMEDABAD MEHS - [N16000042]	03/2008	188.18	143.84	81.80	06/2010	06/2010	0	0/0
119	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC) - [160100168]	12/2003	900.92	1,493.49	595.22	06/2006	07/2010	0	0/2
120	EXPANSION OF PANIPAT REFINERY FROM 12 TO 15 MMTPA - [N16000017]	06/2005	806.00	1,007.83	503.16	03/2008	08/2010	0	18/48
121	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]	10/2010	1,816.07	1,816.07	6.36	10/2010	10/2010	0	0/0
122	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]	11/2007	281.07	281.07	1.12	10/2010	10/2010	-14	0/0
123	DAHEJ-VIJAYPUR PIPE LINE PROJECT - [N16000052]	11/2007	4,429.38	3,000.00	14.65	10/2010	10/2010	0	0/0
124	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I - [N16000053]	11/2007	1,512.00	1,512.00	6.35	10/2011	10/2010	0	0/0
125	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]	01/2008	224.00	224.00	32.76	12/2010	12/2010	0	0/0
126	Guru Govind Singh Refinery Product Evacuation - [N16000076]	01/2009	605.40	605.40	-	12/2010	12/2010	0	0/0
127	CAPACITY AUGMENTATION OF AGRA& FERIZABAD REGION - [N16000074]	07/2009	199.57	199.57	-	01/2011	01/2011	0	0/0
128	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09	834.90	929.54	03/2007	03/2011	0	6/6
129	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]	06/2007	1,252.75	8,061.42	3,374.84	06/2009	04/2011	0	0/0
130	COMPRESSOR STATIONS (KAILARAS & CHAINSA) - [N16000054]	11/2007	1,061.93	1,061.93	1.10	11/2011	04/2011	0	0/0
131	NEELAM RECONSTRUCTION - [N16000063]	05/2008	305.08	305.08	18.57	04/2011	04/2011	0	0/0
132	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]	04/2003	429.82	1,262.93	1,080.22	03/2005	05/2011	0	0/0
133	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]	02/2009	349.00	349.00	2.40	08/2011	08/2011	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
134	Construction of Tank and Blending Facility at Vadi - [N16000075]	02/2009	267.00	349.00	5.17	08/2011	08/2011	0	0/0
135	Construction of Tanks and Blending Facility at Vad - [N16000077]	02/2009	267.00	349.00	-	08/2011	08/2011	0	0/0
136	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]	03/2009	3,597.00	3,597.00	47.79	09/2011	09/2011	0	0/0
137	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]	03/2009	3,284.00	3,284.00	36.58	09/2011	09/2011	0	0/0
138	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057]	01/2009	756.00	756.00	90.33	12/2011	12/2011	0	0/0
139	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]	10/2008	1,797.35	1,797.35	-	12/2011	12/2011	0	0/0
140	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]	02/2008	370.11	370.11	-	04/2011	12/2011	0	0/0
141	MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT - [N16000070]	07/2009	238.68	238.68	-	01/2012	01/2012	0	0/0
142	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]	01/2007	740.02	740.02	243.50	03/2010 03/2012	03/2012	0	0/0
143	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78	2,710.10	0.61	03/2010 08/2010	03/2012	0	0/0
144	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]	01/2007	1,552.63	1,849.50	5.24	02/2009 09/2010	04/2012	0	0/0
145	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]	01/2007	2,853.29	2,853.29	0.54	05/2010	05/2012	0	0/0
146	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]	01/2009	6,855.93	6,855.93	0.54	09/2012	09/2012	0	0/0
147	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00	29,777.00	2,204.84	03/2012	11/2012	0	0/0
148	KOCHI-KANJIRKOD BANGALORE-MANGALORE PIPELINE PROJE - [N16000071]	06/2009	3,032.00	3,032.00	-	12/2012	12/2012	0	0/0
149	DHABOL-BANGALORE PIPELINE PROJECT - [N16000073]	06/2009	4,543.43	4,543.43	-	12/2012	12/2012	0	0/0
150	JAGDISHPUR-HALDIA PIPELINE PROJECT - [N16000072]	07/2009	7,596.18	7,596.18	-	01/2013	01/2013	0	0/0
151	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]	03/2009	2,465.15	2,378.86	-	03/2013	03/2013	0	0/0
Total			136,018.51	144,969.18	40,790.50				154/247
Power									
152	SYSTEM STRENGTHENING - VII OF SOUTHERN REGION (PGCIL) - [180100253]	05/2005	279.30	340.14	278.85	07/2009	11/2009	1	5/18
153	SIPAT-II SUPP. TRANS. SYSTEM (PGCIL) - [180100257]	06/2005	813.67	820.45	778.34	06/2008	11/2009	0	9/22
154	KOLDAM HEP TRANSMISSION LINE (PGCIL) - [180100263]	09/2005	464.91	464.91	158.53	09/2008 09/2008	11/2009	0	9/22
155	SEWA- II H.E.P (NHPC) - [180100220]	09/2003	665.46	1,018.98	874.82	09/2007	12/2009	0	8/36

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
156	SYSTEM STRENGTHENING IN SOUTH-WESTERN PART-B NORTHERN - [N18000020]	10/2006	150.26 -	153.54	107.02	10/2009 -	12/2009	0	5/20
157	ENHANCEMENT OF TRANSMISSION CAPACITY IN EAST-WEST - [N18000026]	10/2006	103.80 -	103.80	63.65	06/2009 -	12/2009	0	0/0
158	NEYVELI TS-II TRANSMISSION SYSTEM (PGCIL) - [180100247]	01/2005	691.83 -	913.35	699.21	12/2007 -	02/2010	0	13/20
159	KUNADANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	1,896.65	1,434.10	11/2008 -	02/2010	0	20/38
160	KORBA STPP STAGE-III - [N18000011]	08/2006	2,448.50 -	2,448.49	1,690.19	02/2010 -	02/2010	0	2/24
161	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-VI - [N18000021]	01/2007	186.95 -	186.95	120.55	07/2009 -	02/2010	0	2/21
162	TUIRIAL HE PROJECT(NEEPCO) - [180100165]	07/1998	368.72 -	836.14	318.39	07/2006 -	03/2010	0	2/5
163	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 1,007.16	1,007.16	694.59	12/2007 -	03/2010	0	7/18
164	KOTESWAR TRANSMISSION SYSTEM (PGCIL) - [180100256]	06/2006	260.34 -	266.61	124.54	06/2008 -	03/2010	0	6/20
165	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]	12/2005	3,779.46 -	3,779.46	3,115.42	09/2009 -	03/2010	0	11/30
166	EAST-WEST TRANSMISSION CORRIDOR STRENGTHENING SCHEME - [260100100]	06/2006	803.70 -	803.76	507.68	06/2009 -	03/2010	0	0/20
167	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]	10/2006	975.96 -	975.96	484.59	10/2009 -	03/2010	0	2/20
168	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-V - [N18000017]	06/2006	721.25 -	721.25	547.48	06/2009 -	03/2010	3	4/19
169	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB G - [N18000037]	04/2008	290.49 -	290.49	193.84	04/2010 -	04/2010	0	0/0
170	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]	12/2007	227.52 -	227.52	83.26	06/2010 -	06/2010	0	0/0
171	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]	07/2006	5,221.23 -	5,221.23	1,666.79	07/2010 -	07/2010	0	2/20
172	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]	02/2009	353.57 -	353.57	19.81	07/2010 -	07/2010	0	0/0
173	CHAMERA, STAGE-III (NHPC) - [180100241]	08/2005	1,405.63 -	1,584.35	980.23	08/2010 -	08/2010	0	0/0
174	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	796.00	363.76	08/2010 -	08/2010	0	0/0
175	Farakka STPP Stage-III - [N18000016]	07/2006	2,570.44 -	2,570.44	1,341.89	08/2010 -	08/2010	0	10/26
176	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]	12/2007	477.69 -	477.69	171.57	09/2010 -	09/2010	0	0/0
177	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER - [N18000040]	09/2007	262.10 -	262.10	125.03	09/2010 -	09/2010	0	0/0
178	National Capital Thermal Power Project Stage-II - [N18000013]	10/2006	5,135.33 -	5,135.33	3,288.23	10/2010 -	10/2010	0	8/40

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
179	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56	2,217.00	836.30	10/2010	11/2010	0	0/0
180	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HE - [N18000018]	07/2006	557.24	557.24	228.80	01/2010	11/2010	0	0/22
181	WESTERN REGION STRENGTHENING SCHEME-VI - [N18000038]	02/2008	340.72	340.72	75.70	11/2010	11/2010	0	0/0
182	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XII - [N18000039]	02/2008	261.55	261.55	55.51	11/2010	11/2010	0	0/0
183	SYSTEM STRENGTHENING SCHEME-VIII OF SOUTHERN REGION - [N18000070]	02/2008	105.84	105.84	30.36	11/2010	11/2010	0	0/0
184	KOTESHWAR HEP (THDC) - [180100184]	04/2000	1,301.56	1,301.56	1,487.95	04/2005	12/2010	0	0/0
185	NORTHERN REGION SYSTEM STRENGTHENING-XI - [N18000034]	12/2007	417.76	417.76	190.49	12/2010	12/2010	0	0/0
186	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-X - [N18000036]	12/2007	408.36	408.36	207.06	12/2010	12/2010	0	0/0
187	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]	04/2008	230.89	230.89	4.88	01/2011	01/2011	0	0/0
188	TESSTA LOW DAM STAGE - II, III (NHPC) - [180100222]	10/2003	768.92	1,279.40	1,009.68	03/2007	02/2011	0	1/25
189	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29	1,724.79	935.65	11/2009	02/2011	0	0/0
190	CHUTAK HYDRO-ELECTRIC PROJECT - [N18000007]	08/2006	621.26	802.00	307.83	02/2011	02/2011	0	0/0
191	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]	10/2006	238.25	238.25	155.73	-	05/2011	0	0/0
192	SIMHADRI STPP STAGE -II - [N18000032]	08/2007	5,103.39	5,038.53	2,002.73	05/2011	05/2011	0	0/0
193	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III - [N18000043]	12/2008	204.07	204.07	24.96	06/2011	06/2011	0	0/0
194	TR. SYSTEM ASSOCIATED WITH CORBA III GENERATION PR - [N18000059]	02/2009	276.61	276.61	28.14	06/2011	06/2011	0	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-IX - [N18000055]	07/2008	525.14	525.14	244.78	07/2011	07/2011	0	0/0
196	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]	04/2008	297.37	297.37	105.46	07/2011	07/2011	0	0/0
197	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]	03/2009	196.10	196.10	3.58	07/2011	07/2011	0	0/0
198	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38	1,061.38	578.62	09/2009	08/2011	0	0/0
199	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIV - [N18000057]	02/2009	132.19	132.19	9.62	08/2011	08/2011	0	0/0
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]	02/2009	210.79	210.79	-	08/2011	08/2011	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
201	SYSTEM STRENGTHENING IN NR GRID FOR KARCHAM WANGTO - [N18000044]	12/2008	328.97 -	328.97	27.73	09/2011 -	09/2011	0	0/0
202	SIPAT STPP STAGE - I (NTPC) - [180100229]	12/2003	8,323.39 -	8,323.39	6,287.18	12/2009 -	10/2011	7	33/56
203	BONGAIGAON THERMAL POWER PROJECT - [N18000041]	01/2008	4,375.35 -	4,375.35	624.96	07/2011 -	11/2011	0	0/0
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]	02/2009	520.48 -	520.48	86.18	11/2011 -	11/2011	0	0/0
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]	02/2009	509.66 -	509.66	5.33	11/2011 -	11/2011	0	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]	02/2009	317.69 -	317.69	0.37	11/2011 -	11/2011	0	0/0
207	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]	02/2009	184.19 -	184.19	11.86	11/2011 -	11/2011	0	0/0
208	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	4,527.15	2,854.83	04/2009 -	12/2011	0	19/41
209	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	421.01	60.08	01/2012 -	01/2012	0	0/0
210	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]	02/2009	664.96 -	664.96	18.55	02/2012 -	02/2012	0	0/0
211	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]	02/2009	409.50 -	409.50	-	02/2012 -	02/2012	0	0/0
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]	02/2009	410.29 -	410.29	5.50	02/2012 -	02/2012	0	0/0
213	SYSTEM STRENGTHENING SCHEME-IX OF SOUTHERN REGION - [N18000060]	02/2009	120.62 -	120.62	3.25	02/2012 -	02/2012	0	0/0
214	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]	02/2009	1,347.32 -	1,347.32	72.38	02/2012 -	02/2012	0	0/0
215	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	2,047.03	710.65	01/2012 -	03/2012	0	2/10
216	PARA HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	573.99	58.78	08/2012 -	08/2012	0	0/0
217	MOUDA STPP - [N18000048]	11/2007	5,459.28 -	5,459.28	560.60	02/2012 -	08/2012	0	0/0
218	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]	08/2008	2,360.95 -	2,360.95	479.54	08/2012 -	08/2012	0	0/0
219	765 KV POOLING STATION & NETWORK WITH DVC AND MAIT - [N18000069]	08/2008	7,075.33 -	7,075.33	1,096.25	08/2012 -	08/2012	0	0/0
220	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER - [N18000061]	10/2008	4,824.12 -	4,824.12	149.26	10/2012 -	10/2012	0	0/0
221	LOWER SUBANSIRI H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	7,452.00	3,460.71	09/2010 -	12/2012	0	2/11

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
222	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI = II HEP - [180100261]	12/2005	358.42	358.42	6.09	12/2008 09/2010	12/2012	0	0/15
223	LOHARINAG-PAL HEP(4x150MW) - [N18000005]	06/2006	2,895.10	2,895.10	507.06	11/2011	12/2012	0	6/34
224	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]	12/2008	7,031.88	7,031.88	214.40	12/2012	12/2012	0	0/0
225	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59	3,954.00	2,557.95	09/2009	03/2013	0	1/20
226	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48	2,978.48	625.97	03/2013	03/2013	0	5/31
227	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00	1,657.60	252.91	07/2010	04/2013	0	0/0
228	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90	3,253.22	988.29	12/2009 03/2011	05/2013	0	37/165
229	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58	2,491.58	74.87	06/2013	06/2013	0	0/0
230	BARH STPP STAGE -II - [N18000047]	02/2008	7,341.04	7,341.04	582.17	08/2013	08/2013	0	0/0
231	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19	11,130.19	282.36	08/2013	08/2013	0	0/0
232	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97	8,692.97	4,388.01	11/2010	10/2013	0	15/51
233	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 3,642.04	3,642.04	189.03	07/2014	01/2016	0	0/0
234	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62	578.62	28.33	06/2006	-	-	0/0
Total			153,835.15	159,742.28	56,027.62				246/920
Health & Family Welfare									
235	NORTH EAST INDIRA GANDHI INSTITUTE OF HEALTH & MS - [210100001]	05/1986	71.18 422.60	443.15	381.31	03/1999 03/2005	-	-	7/16
Total			71.18	443.15	381.31				7/16
Railways									
236	RAJKOT-VERAVAL & WANSJALIYA-JETALSAR GC(WR) - [220100116]	04/1992	112.53 193.61	564.50	458.37	03/1996 06/2009	08/2009	-	0/0
237	RAJGIR-TILAIYA (NL), ECR - [220100312]	04/2001	180.82 180.82	180.82	230.44	03/2006	09/2009	-	0/0
238	VALLAPARPADM-IDAPALLY (NL)(RVNL) - [N22000048]	07/2006	246.50 246.50	246.50	288.90	03/2009 03/2009	11/2009	0	0/0
239	AGRA-ETAWAH VIA FATEBAD & BAD (NL),NCR - [220100243]	04/1999	108.00 214.09	214.09	112.17	12/2009	12/2009	0	0/0
240	KURLA-BHANDUP,5 AND 6TH P.I.,MUMBAI,CR - [220100300]	04/1995	49.84 102.90	136.45	114.25	03/2002	12/2009	0	0/0
241	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	129.70 129.70	142.48	98.84	12/2008	12/2009	0	0/0
242	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN - [N22000002]	04/1996	114.01 283.95	322.87	229.01	-	12/2009	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
243	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]	04/2003	98.74 -	224.51	41.39	- -	12/2009	0	0/0
244	ABOHAR- FAZILKA - [N22000055]	09/2001	86.44 -	209.57	151.37	03/2009 -	02/2010	0	0/0
245	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	634.13	430.25	03/1995 -	03/2010	0	0/0
246	AMBALA-MORADABAD(RE) - [220100131]	03/1993	152.21 157.76	265.00	265.33	03/1998 -	03/2010	0	0/0
247	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]	04/1993	100.00 142.98	170.00	93.24	03/2002 -	03/2010	0	0/0
248	CALICUT-MANGALORE (DL) (SR) - [220100151]	02/1996	240.00 -	571.51	561.78	- -	03/2010	0	0/0
249	MIRAJ-LATUR ROAD(GC),CR - [220100162]	04/1993	225.00 360.63	816.40	649.60	03/2001 -	03/2010	0	0/0
250	KOTTUR-HARIHAR(NL),(SWR) - [220100212]	04/1995	65.94 -	281.20	250.47	- -	03/2010	0	0/0
251	NEW JALPAIGURI-NEW BONGAIGAON (GC),NEFR - [220100224]	11/1998	536.85 523.17	960.48	966.83	03/2003 -	03/2010	0	0/0
252	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	233.00 335.77	501.69	278.12	- -	03/2010	0	0/0
253	TAHANJAVUR-VILLUPURAM GAUGE CONVERSION (G.C)(SR) - [220100244]	10/2001	223.00 356.90	356.90	548.69	- 11/2008	03/2010	0	0/0
254	VILLUPURAM-KATPADI (GC)(SR) - [220100251]	02/2000	175.00 175.00	502.14	426.97	- -	03/2010	0	0/0
255	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	409.00 625.30	639.54	738.64	06/2007 -	03/2010	0	0/0
256	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER) - [220100264]	02/1999	180.73 320.66	335.00	298.11	12/2006 12/2008	03/2010	0	0/0
257	TOLLYGANJ-GARIA(MTP) - [220100268]	03/2000	907.69 -	1,032.76	754.17	12/2006 -	03/2010	0	0/0
258	DHARMAVARAM-PAKALA (GC), SCR - [220100282]	04/1997	200.00 294.99	546.49	498.12	- 02/2009	03/2010	0	0/0
259	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 243.20	243.40	179.76	- 02/2009	03/2010	0	0/0
260	BHILDI-SAMDARI (GC) - [220100291]	04/1999	244.74 479.00	479.00	448.87	- 03/2009	03/2010	0	0/0
261	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]	04/1997	143.92 -	168.80	4.77	- -	03/2010	0	0/0
262	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]	04/2005	148.61 227.52	227.52	218.20	03/2008 03/2009	03/2010	0	0/0
263	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]	02/1996	57.94 137.56	137.57	131.08	03/1998 08/2005	03/2010	0	0/0
264	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 211.90	211.90	124.12	- 03/2009	03/2010	0	0/0
265	PODAPAHAR-BANSPANI,(LD)(SER) - [N22000046]	04/2006	129.74 129.74	129.74	123.13	03/2006 -	03/2010	0	0/0
266	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 732.80	732.80	142.90	03/2008 06/2008	03/2010	0	0/0
267	SHIMOGA-TALAGUPPA - [N22000056]	12/1992	46.00 -	158.95	204.77	- -	03/2010	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
268	NEW GUWAHATI-DIGARU PATCH DOUBLING PH-I - [N22000078]	09/2007	99.84 99.84	110.94	61.84	03/2010 -	03/2010	0	0/0
269	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]	07/1996	273.67 648.76	1,160.52	423.33	- 12/2009	06/2010	0	0/0
270	REINGUNTA-GUNTAKAL(RE) - [220100260]	06/2000	168.34 296.20	296.20	201.06	04/2003 03/2010	06/2010	0	0/0
271	BARAMATI - LONAND (NL), CR - [220100271]	03/1998	75.00 -	138.48	35.14	- -	06/2010	0	0/0
272	CUTTACK - BARANG (LD) - [220100326]	04/1995	127.13 135.10	135.00	113.34	- -	06/2010	0	0/0
273	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]	04/2005	240.00 329.70	330.00	212.56	03/2009 12/2009	06/2010	0	0/0
274	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]	04/2003	136.62 221.90	221.90	82.22	12/2007 03/2010	07/2010	0	0/0
275	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	881.19	86.35	- -	07/2010	0	0/0
276	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]	09/2005	200.80 200.80	200.80	65.98	- -	09/2010	0	0/0
277	BILASPUR-URKURA (DL) - [220100321]	04/1997	151.52 273.00	273.00	253.45	- 03/2009	11/2010	0	0/0
278	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	183.23 -	638.00	0.81	02/2015 -	11/2010	0	0/0
279	BELAPUR-SEAWOOD-URAN ELECTRIF-IED DOUBLE LINE(MTP)-PH-I - [220100164]	03/1996	401.81 -	495.44	129.80	03/2004 -	12/2010	0	0/0
280	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	100.00 492.98	672.38	638.51	- -	12/2010	0	0/0
281	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	157.96 -	567.00	157.19	- 12/2009	12/2010	0	0/0
282	AJMER-PHULERA-RINGUS-REWARI (G.C.)(NWR)(RVNL) - [N22000033]	04/2005	352.00 718.30	718.30	602.55	03/2008 03/2009	12/2010	0	0/0
283	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]	04/2003	230.73 399.73	399.50	253.34	03/2009 12/2009	12/2010	0	0/0
284	BARDHAMAN-KATWA (GC) - [N22000091]	04/2007	245.15 -	245.15	7.53	12/2010 -	12/2010	0	0/0
285	MUMBAI URBAN TRANSPORT PROJECT PHASE-I - [N22000093]	04/2003	3,125.20 -	4,174.00	2,953.68	12/2010 -	12/2010	0	0/0
286	REWARI-ROHTAK (NL),NR - [220100279]	01/2004	149.38 330.23	457.17	292.96	02/2010 -	02/2011	0	0/0
287	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	04/1994	355.38 -	1,000.00	79.07	- -	02/2011	0	0/0
288	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]	04/2005	726.96 810.78	810.78	32.36	- -	02/2011	0	0/0
289	VIRAMGAM-BHILDI(WR),GC - [220100062]	04/1990	155.66 -	356.87	179.71	- 03/2010	03/2011	0	0/0
290	AMRAVATI-NARKHER NL(CR) - [220100118]	06/1994	120.90 175.30	284.27	247.17	06/1999 -	03/2011	0	0/0
291	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]	03/1997	100.00 -	332.75	213.38	- -	03/2011	0	0/0
292	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	193.78 194.07	449.83	237.53	06/2004 -	03/2011	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
293	GOOTY- RENIGUNTA PATCH DOUBLING PH-II (DL) (SCR) - [220100267]	05/2002	304.50 306.00	306.00	329.73	- 06/2009	03/2011	0	0/0
294	KODERMA GIRIDH (NL), ECR - [220100306]	04/1996	371.36 -	371.36	234.34	- -	03/2011	0	0/0
295	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]	02/2008	171.10 -	171.10	43.83	03/2011 -	03/2011	0	0/0
296	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]	03/2006	258.35 -	258.35	9.30	03/2011 -	03/2011	0	0/0
297	RAJPIPLA-ANKELASHWAR (GC) - [N22000096]	04/2006	196.97 -	196.97	12.90	03/2011 -	03/2011	0	0/0
298	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]	04/1995	184.00 -	676.00	267.34	- 12/2010	06/2011	0	0/0
299	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	324.66 -	528.65	98.24	- -	06/2011	0	0/0
300	SITAMARHI-RAXAUL-NARKATIAGANJ (GC) - [N22000089]	04/1997	501.69 -	501.69	278.85	03/2010 -	06/2011	0	0/0
301	PANSPURA-KHARAGPUR 3D LINE - [N22000076]	09/2007	252.50 252.50	252.50	23.85	02/2010 -	11/2011	0	0/0
302	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]	07/1997	248.44 576.27	587.08	615.71	- -	12/2011	0	0/0
303	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	301.64 735.10	735.10	175.32	- 09/2009	12/2011	0	0/0
304	UTRATIA-ZAFRABAD (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	469.03	26.42	03/2010 -	12/2011	0	0/0
305	LUMDING-SILCHAR(GC),NEFR - [220100170]	04/1996	648.00 1,520.00	4,074.10	1,849.86	03/2009 -	03/2012	0	0/0
306	DLW GM 4000 / 3000 HP DIESEL LOCOS - [220100226]	04/1999	155.54 -	141.40	103.18	03/2003 -	03/2012	0	0/0
307	JIND-SONEPAT (NL),NR - [220100280]	01/2004	190.81 238.56	234.45	53.70	- -	03/2012	0	0/0
308	KOSI BRIDGE (NL), ECR - [220100304]	04/2002	323.41 -	322.95	101.09	- -	03/2012	0	0/0
309	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS - [N22000028]	04/2006	415.59 -	495.74	47.96	- -	03/2012	0	0/0
310	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 324.90	324.90	54.03	03/2010 -	03/2012	0	0/0
311	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	11,270.00	5,735.26	03/2001 -	12/2012	0	0/0
312	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	353.08 353.08	462.67	43.39	- -	12/2012	0	0/0
313	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	138.00 258.24	607.09	121.77	- 12/2012	12/2012	0	0/0
314	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]	04/2002	921.00 -	921.00	236.87	03/2009 -	12/2012	0	0/0
315	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	1,480.71	445.84	10/2007 -	12/2012	0	0/0
316	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	687.20	30.14	03/2010 -	12/2012	0	0/0
317	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]	03/1998	280.00 280.00	900.00	504.26	- -	03/2013	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
318	RANGIA-MURKONGSELEK, (GC) NEFR - [220100315]	01/2004	912.70 915.70	1,556.23	100.71	- -	03/2013	0	0/0
319	BRAHAMAPUTRA BRIDGE AT BOGIBIL & LINK LINES, NEFR - [220100201]	04/1996	1,000.00 1,500.00	3,087.44	1,586.31	04/2008 12/2011	03/2014	0	0/0
320	MAYNAGURI TO JOGIGHOPA VIA CHANGRA (NL), NEFR - [220100266]	02/2000	733.00 733.00	1,502.29	391.56	12/2008 -	03/2014	0	0/0
321	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]	09/1996	156.00 156.00	160.48	57.57	- -	03/2014	0	0/0
322	NEW B.G. LINE FROM AZARA TO BYRNIHAT (NATINAL PROJ - [N22000086]	09/2006	200.00 200.00	546.47	0.48	- -	03/2014	0	0/0
323	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	5,300.00	60.00	03/2014 -	03/2014	0	0/0
324	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 727.53	2,492.53	112.77	03/2011 -	03/2016	0	0/0
325	GUNA-ETAWAH(NCR), NL - [220100007]	04/1985	158.77 274.56	432.46	425.40	03/1994 -	-	-	0/0
326	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]	12/1994	124.43 408.43	517.63	309.11	- -	-	-	0/0
327	HOTGI-GADAG(GC),SWR - [220100125]	04/1994	180.00 -	318.66	452.61	03/1999 03/2003	-	-	0/0
328	EKLAKHI-BALURGHAT(NL),NEFR - [220100135]	01/1986	36.80 274.41	285.93	229.64	- -	-	-	0/0
329	DALLIRAJHARA-JAGDALPUR,NL,SECR - [220100149]	04/1995	369.00 -	968.60	0.43	- -	-	-	0/0
330	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]	02/1997	295.00 -	412.91	339.75	- -	-	-	0/0
331	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	151.84 -	208.83	30.98	- -	-	-	0/0
332	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR - [220100185]	09/1996	262.00 433.39	456.00	470.63	- 03/2000	-	-	0/0
333	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	356.00 -	511.86	413.02	03/1998 -	-	-	0/0
334	SURENDRANAGAR-BHAVNAGAR(GC),WR - [220100187]	03/1997	437.40 -	563.25	518.92	03/2004 03/2005	-	-	0/0
335	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 -	730.00	210.82	- -	-	-	0/0
336	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]	04/1996	157.00 -	274.29	71.76	- -	-	-	0/0
337	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 155.00	613.11	271.78	- -	-	-	0/0
338	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1997	155.74 164.36	429.49	234.29	02/2009 -	-	-	0/0
339	HUBLI-AKOLA(NL),SWR - [220100193]	04/1995	227.00 -	103.72	49.28	- -	-	-	0/0
340	HOSPET-GUNTAKAL(LD),SCR - [220100195]	03/1996	105.22 268.00	268.00	275.41	12/1999 03/2008	-	-	0/0
341	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	395.00 598.98	661.72	510.14	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
342	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1996	377.32 218.24	497.47	53.80	- -	-	-	0/0
343	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	31.42 154.30	154.30	88.77	03/2007 03/2007	-	-	0/0
344	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	243.17	0.27	07/2008 -	-	-	0/0
345	KODERMA-RANCHI VIA BARKAKHANA (NL),ECR - [220100222]	03/1999	491.19 -	1,099.20	540.09	07/2005 -	-	-	0/0
346	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	925.00 925.00	925.00	311.43	05/2008 -	-	-	0/0
347	KUTTIPURAM-CALICUT INCLD. SHORANUR-M-LORE (DL) (SR) - [220100249]	03/2001	178.76 178.71	219.94	190.49	- -	-	-	0/0
348	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 550.00	550.00	60.58	- -	-	-	0/0
349	PURNA-AKOLA (G.C), SCR - [220100253]	02/2000	228.00 -	497.63	477.14	- -	-	-	0/0
350	BIDAR-GULBARGA,SCR(NL) - [220100254]	02/1999	242.42 369.70	369.70	121.44	- 05/2009	-	-	0/0
351	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]	03/2002	383.15 -	381.17	80.12	- -	-	-	0/0
352	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]	09/2001	320.10 -	320.10	108.05	- -	-	-	0/0
353	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]	03/1997	78.23 -	162.87	57.03	- -	-	-	0/0
354	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	548.96	353.63	- -	-	-	0/0
355	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 329.05	695.00	9.41	- -	-	-	0/0
356	GADWAL - RAICHUR (NL), SCR - [220100270]	04/1998	92.63 108.91	207.80	107.83	- -	-	-	0/0
357	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	02/1999	138.00 -	901.62	0.99	- -	-	-	0/0
358	BANKURA - DAMODAR (GC) (SER) - [220100277]	03/1998	111.90 111.90	111.90	274.56	03/2005 12/2008	-	-	0/0
359	HAPUR-KANKATHER (LD),NR - [220100278]	04/2003	106.64 117.31	106.64	138.89	03/2007 -	-	-	0/0
360	SURAT-KOSAMBA (LD),WR - [220100281]	04/2000	133.00 -	133.00	-	- -	-	-	0/0
361	TANUR (KUTTIPURAM) GURUVAYUR (NL) (SR) - [220100283]	04/1995	40.00 -	137.71	8.69	- -	-	-	0/0
362	REWARI-SADULPUR-HISSAR (GC),NWR - [220100290]	04/1997	198.96 -	364.19	77.05	- -	-	-	0/0
363	KODERMA-TILAIYA (NL), ECR - [220100305]	04/2002	459.91 -	459.91	36.40	- -	-	-	0/0
364	BARBIGHA - SHEKHPURA + NEORA-DANIAWAN (NL), ECR - [220100309]	04/2002	120.23 -	120.23	220.17	- -	-	-	0/0
365	BIHARSHARIFF-BARBIGHA (NL), ECR - [220100310]	04/2001	103.86 -	103.86	28.93	- -	-	-	0/0
366	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]	04/2001	104.79 -	104.79	34.13	- -	-	-	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
367	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	727.13 727.13	726.05	102.66	- -	-	-	0/0
368	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]	04/2003	104.10 -	113.75	40.35	- -	-	-	0/0
369	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	165.67 -	165.67	0.15	- -	-	-	0/0
370	HATHUA-BHATNI (N L) (NER) - [220100319]	04/2005	200.73 -	230.03	45.76	- -	-	-	0/0
371	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]	04/2005	383.79 -	585.93	102.78	- -	-	-	0/0
372	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR) - [220100330]	04/1992	458.45 -	573.12	555.49	- -	-	-	0/0
373	BHATNI-JIRADEI PATCH DOUBLING (NER) - [N22000029]	04/2006	100.27 -	100.27	0.01	- -	-	-	0/0
374	MUNDERWA-BABHNAN PATCH DOUBLING(NER) - [N22000030]	04/2006	102.10 -	102.10	22.75	- -	-	-	0/0
375	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]	04/2006	378.56 -	670.00	0.43	- -	-	-	0/0
376	GAELKERA-MANOHARPUR,(LD)(SER) - [N22000045]	03/1998	186.92 261.70	261.70	0.08	02/2006 -	-	-	0/0
377	SETTING UP EAST COAST RLY.ZN. (SER) - [N22000054]	04/1997	41.67 -	129.78	90.84	- -	-	-	0/0
378	PATTABIRAM-ARAKKONAM,SR - [N22000057]	04/2002	71.94 -	124.00	151.76	03/2004 07/2008	-	-	0/0
379	AMROHA-KANKATHER,NR - [N22000058]	04/2000	57.00 107.29	103.57	106.12	03/2005 -	-	-	0/0
380	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]	09/2007	404.19 404.19	711.15	24.47	- -	-	-	0/0
381	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 343.17	639.00	128.61	- -	-	-	0/0
382	ALUABARI ROAD SILIGURI JANCTION VIA GALGALIA - [N22000082]	12/2006	170.00 170.00	255.96	50.12	- -	-	-	0/0
383	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 125.00	227.40	9.64	- -	-	-	0/0
384	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 456.00	582.83	15.18	- -	-	-	0/0
385	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]	09/2006	300.00 300.00	529.88	18.31	- -	-	-	0/0
Total			50,032.77 -	93,320.47	41,035.47				0/0
Road Transport & Highways									
386	CHITTORGARH BYPASS(RJ-6) NH-76 KM.159 TO KM.213 - [240106232]	03/2005	133.03 -	133.03	244.80	08/2005 -	10/2009	0	0/0
387	JAWAHARLAL NEHRU PORT PHASE-II,SH-54 - [N24000039]	04/2000	143.00 -	143.00	120.30	05/2007 -	10/2009	0	0/0
388	ALLAHABAD BYPASS (KM.158-KM.198) GQ, NH-2 - [240100203]	04/2000	440.93 -	440.93	592.61	12/2006 -	11/2009	1	0/0
389	ALLAHABAD BYPASS (KM.198-KM.242.708) GQ, NH-2 - [240100204]	04/2000	534.39 -	534.39	638.17	05/2007 -	11/2009	1	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
390	GORHAR-BARWA ADDA (GQ) KM.320-KM.398.75 (NH-2) - [240101187]	04/2000	399.75	399.75	386.90	03/2005	11/2009	1	0/0
391	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]	12/2003	412.78	479.54	404.90	11/2007	11/2009	0	0/0
392	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120 - [240106240]	12/2003	323.36	323.36	189.50	03/2008	11/2009	0	0/0
393	MADURAI -KANNIAKUMARI SEC. (NS-42/TN) NH-7, KM.120 TO KM.160 - [240106241]	12/2003	507.49	507.49	283.70	03/2008	11/2009	0	0/0
394	KARUR TO MADURAI (NH-7), KM.305.6 TO KM.373.275, NH-7 - [240106272]	12/2003	327.20	327.20	457.60	01/2009	11/2009	0	0/0
395	SALEM TO KERALA BORDER SEC(TN6), KM.203.96 NH7 TO KM 53 NH47 - [240106273]	12/2003	469.80	469.80	665.80	12/2008	11/2009	0	0/0
396	HYDERABAD BANGALORE SECTION(NH-7)(NHAI) - [240106284]	12/2003	611.44	592.00	834.20	03/2009	11/2009	1	0/0
397	AP/KARNATKA BORDER-NANDI HILL CROSSING AND DEVANHA - [N24000060]	12/2003	402.80	402.80	453.50	03/2009	11/2009	0	0/0
398	PANIPAT TO PANCHI GUJRAN, NH-1 - [N24000066]	12/2003	109.00	109.00	130.30	10/2008	11/2009	1	0/0
399	PADALUR-TRICHY, NH-45 - [N24000083]	03/2005	320.00	320.00	596.90	05/2009	11/2009	0	0/0
400	SIX LANING OF BANGLORE-HOSUR SECTION OF NH-7, PHAS - [N24000086]	03/2005	110.00	110.00	107.30	07/2008	11/2009	0	0/0
401	KADAL TO ARMUR, NH-7 - [N24000092]	12/2003	271.73	271.73	303.80	11/2009	11/2009	0	0/0
402	ELEVATED HIGHWAY FROM SILK BOARD JUNCTION TO ELECT - [N24000105]	03/2005	450.00	450.00	833.20	07/2008	11/2009	1	0/0
403	BHUBANESWAR-KHURDA (GQ) KM.387.7-KM.418 (NH-5) - [240101151]	04/2000	140.85	140.85	148.01	01/2004	12/2009	0	0/0
404	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]	04/2000	225.00	225.00	145.54	04/2004	12/2009	0	0/0
405	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]	04/2000	367.49	367.49	416.18	03/2005	12/2009	0	0/0
406	FATEHPUR-KHAGA (GQ) KM.38-KM.115 (NH-2) - [240101178]	04/2000	372.40	372.40	380.72	07/2004	12/2009	0	0/0
407	CHENNAI BYPASS (NHAI) OTHERS, NH-45, 4 & 5 - [240106202]	12/2003	480.00	480.00	742.90	11/2007	12/2009	0	0/0
408	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS - [240106203]	12/2003	210.00	210.00	576.60	04/2007	12/2009	0	0/0
409	JHANSI BYPASS (UP-3), KM.104-KM.91, NH-25 - [240106220]	12/2003	158.06	158.06	135.10	08/2005	12/2009	0	0/0
410	PURNEA-FORBESGANJ (BR-1) PHASE-II, KM.309 TO 268, NH-57 - [240106227]	12/2003	276.00	276.00	309.30	04/2008	12/2009	0	0/0
411	PURNEA-FORBESGANJ (BR-2) PHASE-II, KM.268 TO 230, NH-57 - [240106228]	12/2003	310.00	310.00	321.00	04/2008	12/2009	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
412	GOGUNDA TO UDAIPUR (RJ-3) NH.76 KM.104 TO KM.73 - [240106231]	12/2003	266.00	288.06	307.10	08/2007	12/2009	0	0/0
413	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00 - [240106256]	03/2005	359.00	359.00	448.30	03/2009	12/2009	0	0/0
414	DHULE-PIMPALGAON, NH-3, KM.380 TOKM. 265 - [240106257]	03/2005	556.00	556.00	568.50	03/2009	12/2009	0	0/0
415	TRICHY BYPASS END TO TOVARAMKURCHI (NH-45B)(NHAI) - [240106285]	03/2005	261.00	261.00	275.20	08/2008	12/2009	1	0/0
416	SAGAR - RAJMARG CHORAH, KM 255-297, NH-26 (NHAI) - [240106302]	12/2003	206.96	206.96	51.79	10/2008	12/2009	0	0/0
417	SIMRAHI TO RING-BUND (MISSIONG LINE) (BR-4) - [N24000029]	12/2003	100.50	100.50	145.90	04/2008	12/2009	0	0/0
418	THRISSUR TO ANGAMALI (NH-47) - [N24000037]	12/2003	312.50	312.50	477.00	03/2009	12/2009	0	0/0
419	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]	04/2000	196.50	196.50	132.44	06/2008	12/2009	0	0/0
420	TOVARAMKURCHI-MADURAI, NH45B (NHAI) - [N24000054]	04/2000	263.00	263.00	304.00	08/2008	12/2009	1	0/0
421	NAGPUR-KONDHALI, NH-6 (NHAI) - [N24000055]	03/2005	168.00	168.00	227.74	12/2008	12/2009	0	0/0
422	BARA TO ORAI, NH-2, 25 - [N24000069]	12/2003	465.00	465.00	23.82	04/2009	12/2009	0	0/0
423	PATHANKOT BHOGPUR NH-1A - [N24000115]	12/2003	229.00	229.00	-	05/2010	12/2009	0	0/0
424	VARANASI-MOHANIA (GQ) KM.317-329 & KM.0-KM.65 (NH-2) - [240101181]	04/2000	467.93	467.93	447.07	03/2005	01/2010	1	0/0
425	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]	03/2005	629.00	629.00	698.80	11/2010	01/2010	0	0/0
426	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]	03/2005	190.00	190.00	197.00	01/2009	02/2010	0	0/0
427	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]	03/2005	557.00	557.00	726.30	02/2010	02/2010	0	0/0
428	KUNJWANI-VIJAYPUR (NS-15) (NS & EW-PH-I) KM.80-KM.97.20, NH-1A - [240102193]	04/2000	110.00	110.00	139.20	12/2004	03/2010	0	0/0
429	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31 - [240103191]	04/2000	205.73	205.73	240.90	07/2004	03/2010	0	0/0
430	DEVDHARI-KELAPUR - [240106207]	12/2003	144.00	144.00	95.12	07/2005	03/2010	0	0/0
431	BORKHEDI-JAM (NS-22/MH) PH.II KM.36.6 TO KM.64.0, NH-7 - [240106210]	12/2003	110.00	110.00	105.70	06/2005	03/2010	0	0/0
432	JALANDAR-AMRITSAR, KM.407/100 TO KM.456/100, NH-1 - [240106268]	03/2005	263.00	263.00	334.50	02/2009	03/2010	5	0/0
433	NAGAON BYPASS (NH-37)(NHAI) - [240106289]	12/2003	230.00	230.00	137.10	06/2008	03/2010	0	0/0
434	THANJAUR-TRICHY, NH-67 (NHAI) - [N24000056]	03/2005	280.00	280.00	524.60	06/2009	03/2010	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
435	MAHARASHTRA/AP BORDER TO ISLAM NAGAR,(NS-2/BOT/AP-6),NH-7 - [N24000093]	12/2003	360.42	360.42	308.80	11/2009	03/2010	0	0/0
436	BANGALORE-NEELAMANGLALA NH-4 - [N24000104]	03/2005	445.00	445.00	630.60	07/2010	03/2010	0	0/0
437	COCHIN PORT, NH-47 (PORT CONNECTIVITY) KMS 348 - KMS 358 - [240100206]	04/2000	106.00	193.00	80.71	08/2006	04/2010	0	0/0
438	KANYAKUMARI-PANAGUDI (NS CORR. PH-II) (KM 203-233.60), NH-7 - [240102202]	01/2004	120.00	120.00	47.27	09/2006	04/2010	0	0/0
439	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]	12/2003	166.27	166.27	79.54	03/2008	04/2010	0	0/0
440	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 251-293 - [N24000076]	12/2003	208.46	208.46	145.10	08/2009	04/2010	0	0/0
441	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 376-418 - [N24000079]	12/2003	205.92	205.92	148.90	08/2009	04/2010	0	0/0
442	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 418-463 - [N24000080]	12/2003	243.64	243.64	197.60	08/2009	04/2010	0	0/0
443	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 211-251 - [N24000081]	12/2003	194.80	194.80	127.40	08/2009	04/2010	0	0/0
444	CHITRADURGA BY PASS (GQ) KM.207-KM.189 (NH-4) - [240101134]	04/2000	104.00	104.00	138.91	08/2004	05/2010	0	0/0
445	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]	12/2003	193.09	193.09	104.20	03/2008	05/2010	0	0/0
446	GONDE-VADAPE(THANE), NH-3, KM.440/000 TO KM.539/500 - [240106262]	03/2005	579.00	579.00	480.24	04/2009	05/2010	0	0/0
447	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]	12/2003	225.00	225.00	123.50	10/2008	05/2010	0	0/0
448	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]	04/2007	486.00	486.00	64.42	05/2010	05/2010	0	0/0
449	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]	12/2003	157.47	154.57	112.40	09/2007	06/2010	0	0/0
450	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]	04/2000	318.00	207.56	35.11	08/2004	06/2010	0	0/0
451	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2 - [240106222]	12/2003	193.00	193.00	243.60	10/2008	06/2010	0	0/0
452	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH-28 - [240106225]	12/2003	217.00	217.00	271.90	10/2008	06/2010	0	0/0
453	GORAKHPUR-AYODHYA (LMNHP-6),NH-28, KM.251.70 TO KM.208.00 - [240106245]	12/2003	239.00	239.00	282.20	10/2008	06/2010	0	0/0
454	GORAKHPUR-AYODHYA (LMNHP-4),NH-28, KM.164.00 TO KM.135.00 - [240106247]	12/2003	205.00	205.00	224.20	10/2008	06/2010	0	0/0
455	AYODHYA-LUCKNOW (LMNHP-3),NH-28, KM.135.000 TO KM.93.075 - [240106248]	12/2003	212.00	212.00	268.60	10/2008	06/2010	0	0/0
456	ORAI TO JHANSI (UP-4),NH-25, KM.170.0 TO KM.104.0 - [240106249]	12/2003	451.97	451.97	374.40	04/2008	06/2010	3	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
457	DARBHANGA-MUZAFFARPUR, NH-57 (NHAI) - [240106295]	12/2003	305.00	305.00	314.30	06/2008	06/2010	0	0/0
458	DARBHANGA-MUZAFFARPUR(KM 30 TO KM 0), NH-57 (NHAI) - [240106296]	12/2003	291.80	291.80	334.20	06/2008	06/2010	0	0/0
459	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]	12/2003	275.00	250.39	153.00	10/2008	06/2010	0	0/0
460	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]	12/2003	225.00	225.00	134.70	07/2008	06/2010	0	0/0
461	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]	12/2003	340.00	340.00	363.50	06/2008	06/2010	0	0/0
462	NALBARI TO BIJNI (AS-8) - [N24000035]	12/2003	200.00	200.00	129.00	06/2008	06/2010	0	0/0
463	SITAPUR-LUCKNOW - [N24000036]	03/2005	322.00	322.00	171.20	06/2009	06/2010	0	0/0
464	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]	12/2003	221.82	221.82	139.40	11/2008	06/2010	0	0/0
465	NALBARI TO BIJNI (AS-9) - [N24000050]	12/2003	142.00	142.00	100.90	06/2008	06/2010	0	0/0
466	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]	04/2000	263.27	263.27	182.92	02/2004	06/2010	0	0/0
467	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 293.4-3 - [N24000077]	12/2003	239.19	239.19	159.90	09/2009	06/2010	0	0/0
468	HYDERABAD-BANGALORE SEC.(NS CORR.PH-II)[KM 336-376 - [N24000078]	12/2003	243.38	243.38	163.80	09/2008	06/2010	0	0/0
469	KURALI-KIRATPUR, NH-21 - [N24000087]	03/2005	309.00	309.00	215.60	06/2010	06/2010	0	0/0
470	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]	12/2003	418.04	418.04	218.40	03/2010	06/2010	0	0/0
471	JHANSI TO LALITPUR, NH-25,26 - [N24000096]	12/2003	355.06	355.06	238.40	09/2009	06/2010	0	0/0
472	AMRITSAR-WAGHA BORDER - [N24000121]	06/2008	205.88	205.88	108.20	06/2010	06/2010	0	0/0
473	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]	04/2000	241.00	196.65	31.19	08/2004	07/2010	0	0/0
474	TRICHY - DINDIGUAL NH-45 - [N24000099]	03/2005	576.00	576.00	168.40	07/2010	07/2010	0	0/0
475	PONDICHERY - TINDIVANAU NH-66 - [N24000100]	03/2005	285.00	285.00	204.40	07/2010	07/2010	0	0/0
476	TRICHY - KORUR NH-67 - [N24000101]	03/2005	516.00	516.00	213.30	07/2010	07/2010	0	0/0
477	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]	03/2005	441.00	441.00	321.10	07/2010	07/2010	0	0/0
478	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4 - [N24000106]	03/2005	565.00	565.00	535.10	07/2010	07/2010	0	0/0
479	ISLAM NAGAR TO KADTAL - [N24000109]	12/2003	546.83	546.83	448.20	03/2010	07/2010	0	0/0
480	LANKA TO DABOKA (NH-54)(NHAI) - [240106286]	12/2003	225.00	225.00	99.85	06/2008	08/2010	0	0/0
481	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]	02/2008	295.00	295.00	182.10	08/2010	08/2010	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
482	LUCKNOW-BYPASS (EW) (NS & EW-PH-I) NH-25 & NH-28 VIA NH-56 - [240103192]	04/2000	182.52 -	111.78	0.59	06/2004 -	09/2010	0	0/0
483	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]	04/2000	273.00 -	522.00	220.80	03/2005 -	09/2010	0	0/0
484	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]	12/2003	198.00 -	198.00	66.84	11/2008 -	09/2010	0	0/0
485	LAKHNAADON TO MP/MH BORDER, KM 596.75-653 (NS-1/BOT/MP-2), NH7 - [N24000094]	12/2003	407.60 -	407.60	177.60	06/2010 -	09/2010	3	0/0
486	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]	12/2003	263.17 -	263.17	214.80	09/2009 -	09/2010	0	0/0
487	JHANSI TO LALITPUR, NH-26 - [N24000097]	12/2003	276.09 -	276.09	183.20	09/2009 -	09/2010	3	0/0
488	LUMDING TO DABOKA - [N24000110]	12/2003	130.00 -	130.00	27.22	08/2010 -	09/2010	0	0/0
489	WAINGANGA BRIDGE - CHHATISGARH-MAHARASHTRA - [N24000120]	03/2008	424.00 -	424.00	275.60	09/2010 -	09/2010	0	0/0
490	GWALIOR BYPASS, NH-75,3 - [N24000088]	12/2003	300.93 -	300.93	170.80	10/2009 -	10/2010	0	0/0
491	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]	12/2003	275.00 -	275.00	247.90	09/2007 -	12/2010	12	0/0
492	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]	03/2005	220.00 -	220.00	112.50	09/2007 -	12/2010	12	0/0
493	JAM-WADNER - [240106209]	12/2003	145.00 -	145.00	68.18	07/2005 -	12/2010	0	0/0
494	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]	12/2003	230.00 -	230.00	87.70	06/2005 -	12/2010	0	0/0
495	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]	12/2003	284.00 -	284.00	268.80	05/2008 -	12/2010	12	0/0
496	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]	12/2003	227.00 -	227.00	188.70	10/2008 -	12/2010	0	0/0
497	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]	12/2003	340.68 -	340.68	192.20	03/2008 -	12/2010	6	0/0
498	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	280.00	98.44	02/2009 -	12/2010	0	0/0
499	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	199.81	27.54	04/2009 -	12/2010	0	0/0
500	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	167.64	39.49	11/2008 -	12/2010	0	0/0
501	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	155.04	27.96	11/2008 -	12/2010	0	0/0
502	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]	12/2003	200.00 -	200.00	36.15	04/2009 -	12/2010	0	0/0
503	DAKOPA TO NAGAON (NH-36)(NHAI) - [240106288]	12/2003	225.00 -	225.00	86.47	06/2008 -	12/2010	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
504	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]	12/2003	195.00	195.00	68.72	06/2008	12/2010	0	0/0
505	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]	12/2003	242.00	242.00	261.80	12/2008	12/2010	6	0/0
506	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]	12/2003	227.00	227.00	231.50	12/2008	12/2010	6	0/0
507	BIJNI TO ASSAM /WB BORDER (NH-31.C)(2)(NHAI) - [240106293]	12/2003	237.80	237.80	66.24	06/2008	12/2010	0	0/0
508	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]	12/2003	332.94	332.94	124.40	09/2008	12/2010	0	0/0
509	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]	12/2003	151.30	151.30	83.78	10/2008	12/2010	0	0/0
510	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]	12/2003	203.43	203.43	63.28	10/2008	12/2010	0	0/0
511	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]	12/2003	251.03	251.03	62.13	10/2008	12/2010	0	0/0
512	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]	12/2003	229.91	229.91	29.18	10/2008	12/2010	0	0/0
513	GUWHATI TO NALBARI (AS-4) - [N24000038]	12/2003	175.96	175.96	48.12	04/2008	12/2010	0	0/0
514	NAGAON TO DHARAMTUL (AS-2) - [N24000042]	12/2003	264.72	264.72	75.54	06/2008	12/2010	0	0/0
515	SONAPUR TO GUWAHTI (AS-3) - [N24000044]	12/2003	245.00	245.00	181.10	03/2008	12/2010	0	0/0
516	GUWAHATI TO NALBARI (AS-5) - [N24000046]	12/2003	198.16	198.16	75.41	04/2008	12/2010	0	0/0
517	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00	225.00	106.70	06/2008	12/2010	0	0/0
518	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00	208.00	57.55	04/2008	12/2010	0	0/0
519	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]	12/2003	160.00	160.00	50.82	05/2008	12/2010	0	0/0
520	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]	12/2003	200.00	200.00	78.52	06/2008	12/2010	0	0/0
521	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00	212.00	33.73	09/2007	12/2010	0	0/0
522	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00	196.00	23.32	07/2009	12/2010	0	0/0
523	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61	217.61	58.63	04/2010	12/2010	0	0/0
524	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00	281.31	157.20	02/2010	12/2010	0	0/0
525	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]	12/2003	600.24	600.24	361.20	10/2009	12/2010	0	0/0
526	GWALIOR-JHANSI, NH-75 - [N24000089]	12/2003	604.00	604.00	188.30	12/2009	12/2010	0	0/0
527	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]	04/2000	228.70	228.70	192.36	02/2004	12/2010	0	0/0
528	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]	03/2005	941.00	941.00	266.60	01/2011	01/2011	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
529	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]	01/2008	464.00 -	464.00	169.30	01/2011 -	01/2011	0	0/0
530	AGRA-BYPASS(NS-1/UP-1),KM 176.8- 13.03 NH-2,3 - [N24000098]	12/2003	348.16 -	348.16	102.10	09/2007 -	02/2011	0	0/0
531	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28 - [240106223]	12/2003	239.00 -	239.00	179.10	07/2005 -	03/2011	0	0/0
532	MUZZAFFARPUR TO MEHSI (LMNHP- 12), KM.520 TO 480, NH-28 - [240106224]	12/2003	275.00 -	275.00	181.60	07/2005 -	03/2011	0	0/0
533	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]	12/2003	240.00 -	240.00	126.10	10/2008 -	03/2011	0	0/0
534	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]	12/2003	340.00 -	340.00	179.50	09/2008 -	03/2011	0	0/0
535	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]	12/2003	232.45 -	232.45	78.70	09/2010 -	03/2011	0	0/0
536	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70 - [N24000119]	11/2008	549.00 -	549.00	331.40	05/2010 -	05/2011	0	0/0
537	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	38.29	09/2008 -	06/2011	0	0/0
538	KELARPUR-PIMPALKATTI-KM 153 TO KM 175 - [240106283]	12/2003	117.40 -	117.40	29.83	11/2008 -	06/2011	0	0/0
539	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]	03/2005	940.00 -	940.00	0.31	07/2012 -	07/2012	0	0/0
540	DEVDHARI-WADNER - [240106208]	12/2003	145.00 -	145.00	24.71	07/2005 -	-	-	0/0
Total			45,226.22 -	45,431.53	34,054.12				0/0
<u>Shipping & Ports</u>									
541	CONSTRUCTION OF CAR /CLEAN CARGO TERMINAL - [N25000034]	01/2009	100.00 -	100.00	0.50	01/2010 -	01/2010	0	0/0
542	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]	01/2002	165.00 -	165.00	38.10	12/2005 -	03/2010	0	0/0
543	DEEPENING OF CHEENEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	99.55	06/2007 01/2009	03/2010	0	0/0
544	ACQUISITION OF TWO NOS.OF 470000 DWT MR TANKERS - [N25000013]	12/2006	411.32 -	411.32	342.92	03/2010 -	03/2010	0	0/0
545	ACQUISITION OF 6 NOS. 60470 DWT LR-I PRODUCT TANKE - [N25000029]	10/2006	1,658.59 -	1,658.59	318.24	07/2010 -	07/2010	0	0/0
546	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]	06/2005	2,427.40 -	2,427.40	809.44	10/2008 -	11/2010	0	0/0
547	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM - [N25000015]	03/2007	245.67 -	298.17	274.01	04/2009 -	11/2010	12	0/0
548	ACQUISITION OF 2 NOS. OF 105000 DWT LR-II TANKERS - [N25000030]	08/2007	586.58 -	586.58	208.02	11/2010 -	11/2010	0	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
549	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]	11/2007	366.00	366.00	1.43	12/2010	12/2010	0	0/0
550	OPERATION, MANAG. & MAINT. OF MULTI USER-JETTY FOR - [N25000038]	06/2006	230.00	230.00	-	12/2010	12/2010	0	0/0
551	C/O IMPOUNDED DOCK AT TUNA FOR HANDELLING DRAFT VE - [N25000037]	04/2005	882.00	882.00	0.16	02/2011	02/2011	0	0/0
552	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00	702.00	0.73	03/2011	03/2011	0	0/0
553	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]	10/2007	359.44	359.44	200.91	04/2011	04/2011	0	0/0
554	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR - [N25000032]	08/2008	1,108.12	1,168.42	341.48	04/2011	12/2011	0	0/0
555	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]	11/2007	1,061.96	1,061.96	219.98	03/2012	01/2012	0	0/0
556	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]	08/2008	1,066.91	968.35	222.91	09/2012	08/2012	0	0/0
557	DEEPENING AND WIDENING OF MAIN HARBOUR CHANNEL AND - [N25000003]	10/2005	800.00	800.00	4.24	10/2008	-	-	0/0
558	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]	10/2002	150.00	309.00	23.26	09/2005	-	-	0/0
Total			12,475.83	12,747.59	3,105.88				0/0
<u>Telecommunications</u>									
559	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]	06/2006	231.38	168.30	92.36	10/2007	08/2009	-	0/0
560	NIB-II PROJECT RURAL BROADBAND - [N26000037]	12/2007	312.86	353.00	119.27	02/2008	09/2009	-	0/0
561	GSM EQUIPMENT OF 1162K LINES PH-4.5 - [N26000045]	03/2008	325.00	325.00	222.00	12/2008	09/2009	-	0/0
562	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]	11/2007	277.34	277.34	177.49	03/2009	09/2009	-	0/0
563	500K BROADBAND ACCESS H/W EQUIPMENT DELHI AND MUMB - [N26000038]	04/2007	134.25	133.75	34.05	06/2008	06/2008	-14	0/0
564	COMMISSIONING OF GSM EQUIPMENT OF 650K LINES (PH- - [N26000028]	11/2006	364.52	364.52	51.44	12/2006	10/2009	0	0/0
565	GSM BASED NETWORK PH-4 - [N26000033]	11/2007	174.36	174.36	71.50	11/2007	10/2009	0	0/0
566	EXPANSION OF 750K GSM LINES - [N26000049]	10/2006	278.16	278.16	153.13	12/2008	10/2009	0	0/0
567	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]	12/2005	249.00	229.41	67.67	02/2007	11/2009	0	0/0
568	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]	06/2007	336.81	174.36	64.50	01/2009	11/2009	1	0/0

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
569	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]	01/2006	247.00	247.00	119.50	02/2007	12/2009	0	0/0
570	GSM BASED NETWORK EXPANSION PLAN PH-4 - [N26000034]	02/2007	239.19	239.19	104.48	04/2008	12/2009	2	0/0
571	KOLKATA TELECOM DISTRICT PH-4 - [N26000036]	09/2006	208.50	208.50	146.38	09/2008	12/2009	2	0/0
572	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]	06/2007	601.49	601.49	399.77	12/2008	12/2009	0	0/0
573	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]	01/2008	192.48	192.48	79.32	03/2009	12/2009	0	0/0
574	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]	02/2008	373.94	373.94	154.60	12/2008	12/2009	0	0/0
575	GSM EQUIPMENT OF 1006280 LINES IN TAMILNADU PH-4.5 - [N26000042]	06/2008	409.21	409.21	465.49	12/2008	12/2009	0	0/0
576	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]	05/2007	335.91	335.91	10.96	03/2009	12/2009	0	0/0
577	DELHI EXP. OF 1250K LINES OF 2G/3G GSM LINES - [N26000052]	02/2007	463.61	463.61	52.50	12/2009	12/2009	0	0/0
578	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]	01/2009	149.15	149.15	40.87	06/2009	12/2009	0	0/0
579	BIHAR TELECOM CIRCLE PHASE-V.1, 2G & 3G - [N26000060]	04/2007	366.00	366.00	-	09/2009	12/2009	0	0/0
580	EXPANSION OF EXISTING 2G&3G GSM N/W BY 750 KPE NO - [N26000061]	10/2008	180.53	180.53	8.08	12/2009	12/2009	0	0/0
581	NATIONAL RADIO SPECTRUM MANAGEMENT and MONIT. SY. I - [260100051]	08/2000	279.97	172.04	136.16	12/2004	02/2010	0	0/0
582	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]	09/2008	1,799.94	1,799.94	26.50	09/2009	06/2010	0	0/0
583	GSM EQUIPMENT OF 1625K LINES(2G) & 325K LINES IN M - [N26000051]	06/2008	908.30	916.70	151.70	08/2009	06/2010	0	0/0
584	GSM EXPANSION PH.IV (B) (BSNL) MAHARASHTRA - [260100095]	07/2005	1,174.75	1,174.75	371.41	03/2006	-	-	0/0
585	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]	11/2003	250.00	425.51	68.50	12/2005	-	-	0/0
586	IMPLEMENTATION AND EXECUTION OF NEW TECHNOLOGY - [N26000015]	10/2004	160.00	135.00	94.77	06/2006	-	-	0/0
587	EXP. OF 750K GSM LINES OF 2.5 GSM AND VALIDATION EQU - [N26000026]	02/2007	741.77	278.16	151.37	10/2007	-	-	0/0
Total			11,765.42	11,147.31	3,635.77				0/0
<u>Urban Development</u>									
588	C/O GENERAL POOL OFFICE COMPLEX AT INA - [N28000016]	10/2004	83.67	135.03	-	02/2010	02/2010	0	0/0
589	DELHI MRTS PHASE-II PROJECT - [280100002]	08/2005	8,118.00	8,676.00	11,281.39	06/2010	10/2010	0	0/7
590	BANGALORE METRO RAIL PROJECT - [N28000008]	05/2006	6,395.00	6,395.00	1,636.24	12/2011	12/2011	0	0/0
Total			14,596.67	15,206.03	12,917.63				0/7

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t Original (in Mon)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Water Resources</u>									
591	PAGLADIYA DAM PROJECT - [300100001]	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	0	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			530,249.67	596,302.41	240,955.15				715/1991
