

**312th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹.150 Crores and above)
October, 2011**



AAI NSCBI AIRPORT



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Contents

Executive Summary	1 -5
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2010-11	6-12
List of Delete Projects	13
Summary of Projects	14-24
Sector wise Trend and Graphicalf Analysis	25-37
Sector wise analysis of projects	38-67
Graph	68-78
Statewise Summary of All Ongoing Projects	79
List of Abbreviations	80-81

EXECUTIVE SUMMARY

The Flash Report for October 2011 contains information on the status of the 583 projects in the Central Sector costing ₹ 150 Crores and above. During October 2011, one project, “Transmission System Associated with Farakka-III, PGCIL” of Power Sector has reported completion.

The online reporting of the implementation status of the ongoing projects from the project authorities has improved considerably with majority of project authorities reporting online during the current month. NHAI, however, has been a major defaulter on this count and has not been reporting any details in the OCMS. During October 2011, twenty-seven (27) projects have reported additional delays, vis-à-vis the date of completion reported the previous month. The additional delays are in the range of 1 to 12 months, in respect of projects relating to Coal, Petroleum, Power, Road Transport and Highways, Civil Aviation, Urban Development and Atomic Energy Sectors.

S. No.	Sector	Projects on monitor	Additional delays
1.	RAILWAYS	132	0
2.	ROAD TRANSPORT & HIGHWAYS	138	13
3.	POWER	92	7
4.	PETROLEUM	71	1
5.	COAL	48	3
6.	TELECOMMUNICATION	40	0
7.	SHIPPING & PORTS	25	0
8.	STEEL	15	0
9.	FERTILISERS	6	0
10.	CIVIL AVIATION	5	1
11.	ATOMIC ENERGY	4	1
12.	URBAN DEVELOPMENT	4	1
13.	MINES	1	0
14.	WATER RESOURCES	1	0
15.	PETROCHEMICALS	1	0
Total		583	27

3. The total original cost of implementation of the 583 projects was about ₹ 7, 12,811.99 Crores and their anticipated completion cost is likely to be ₹ 8, 21,664.74 Crores, which reflects an overall cost overrun of 15.3 %. The expenditure incurred on these projects till October, 2011 is ₹ 3, 44,360.76 Crores, which is 41.9 % of the revised cost of the projects.

4. Out of the 583 projects, 7 projects are ahead of schedule, 166 are on schedule, 235 projects are delayed and 127 projects have been sanctioned without any commissioning schedule/date Further, in case of 48 projects neither the year of commissioning nor the tentative gestation period of the projects have been reported but subsequently in some of the cases, the date of completion have been finalized. The concerned ministries have been requested to fix the date of commissioning of their projects at an early date.

5. During the month under reference the projects reporting delays have marginally increased to 235 (from 234 in September'2011). Out of 235 delayed projects, 45 projects had overall delay in the range of 1 to 12 months, 57 projects had a delay in the range of 13 to 24 months, 99 projects had a delay in the range of 25 to 60 months and 34 projects had a delay of 61 months and above.

6. It may be noted that this Ministry monitors the cost & time overrun with respect to original cost estimates (OCE) and not against the RCEs, as comparison against OCE reflect the actual changes. If the time and cost overruns is measured against the revised estimates, the calculated parameters will reflect only the unregularized RCEs due to which all time and cost overrun will get regularized resulting in zero value. This will not serve the purpose of monitoring.

7. The brief reasons for time overruns as reported by various projects implementing agencies are inadequate mobilization by the contractors, law and order problems, delays in engineering designs, change of scope delays in pre-project activity, Maoist problems and forest and environment clearances etc. Brief reasons for cost overruns are mainly due to inflation, fluctuation of exchange rate, higher tender value, change of scope etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each

project, to facilitate better monitoring. However, not all the project agencies are providing the list of milestones.

The Sector-wise details of additional delays are as under:-

i) In the **Coal sector**, 3 projects have reported additional delays in the range of 2 to 12 months. TPS-II, NLC, Tamil Nadu has reported an additional delay of 2 months (overall delay of 37 months) due to delay in commissioning. Barsingsar TPS (2 X 125 MW), NLC, Rajasthan has reported an additional delay of 2 months due to delay in commissioning (overall delay of 30 months). Ashok Expansion, CCL, Jharkhand has reported an additional delay of 12 months due to delay in land acquisition and environment clearances.

ii) In the **Civil Aviation sector**, Construction of New International Terminal Building, AAI, Goa has reported an additional delays of 3 months due to change in structural design of foundation and shortage of manpower.

iii) In the **Petroleum Sector**, Construction of 12 Offshore Supply Vessels (OSV) ONGC has reported an additional delay of 12 months (overall delay of 15 months) due to delay in procurement of steel by PSL and shortage of skilled manpower at contractor's end.

iv) In the **Power Sector**, 7 projects have reported additional delays in the range of 1-3 months. Chutak HEP, NHPC, Jammu & Kashmir has reported an additional delay of 1 month (overall delay of 13 months) due to delay in supply and erection of ERM components, Eastern Region Strengthening Scheme-II,PGCIL has reported an additional delay of 1 month (overall delay of 18 months) due to slow progress by the Contractor, Transmission System Associated with Uri-II,PGCIL, Jammu & Kashmir has reported an additional delay of 2 months (overall delay of 06 months) due to poor law & order situation , Vishnugad Pipalkoti HEP, THDCL, Uttaraanchal has reported an additional delay of 2 months (overall delay of 24 months) due to poor mobilization of work, Mouda STPP (NTPC), Maharashtra has reported an additional delay of 2 months (overall delay of 05 months) due to slow progress by M/s ERA & M/s BHEL, Transmission System Associated with Parbati-III HEP,PGCIL, Himachal Pradesh has reported an additional delay of 3 months (overall delay of 26 months) due to delay in forest clearances, Chamera stage-II.,NHPC, Himachal Pradesh has reported

an additional delay of 2 months (overall delay of 18 months) due to heavy rainfall in August, 2011 .

v) In the Road Transport and Highways Sector, 13 projects have reported additional delays in the range of 1-5 months. 6 projects have reported additional delay of 1 month each due to slow progress of work by the contractor. Aurang-Raipur,, NH-66, 232 KM to 281 KM, NHAI and End of Durg Bypass – Chhatisgarh / Maharastra Border, NHAI have reported an additional delay of 2 months each due to delay in Railways clearance and poor mobilization by the contractor respectively, Forbesganj to Simrahi, NHAI and Nagpur - Kondhali (NH-6), NHAI have reported an additional delay of 3 months each due to delay in shifting of Electric lines and delay in land acquisition respectively. Haranganjo to Maibang, KM 164.08 – 190.58, NHAI and Haranganjo to Maibang (NH-54), NHAI has reported an additional delay of 4 months each due to poor law & order situation and delay in utility shifting respectively, Dakoba to Nagoan (NH-36) NHAI has reported an additional delay of 5 months (overall delay of 45 months) due to delay in land acquisition .

vii) In the Atomic Energy Sector, Kudankulam APP, NPCIL has reported an additional delay of 4 months (overall delay of 48 months) due to agitation by the local people.

viii) In Urban Development sector, Bangalore Metro Rail Project has reported an additional delay of 9 months (overall delay of 48 months) due to delay in land acquisition.

The status as on 01.11.2011 in respect of completion of projects costing ₹150 Crores and above in the various sectors is indicated in the Report.

(Pankaj Jain)
Additional Secretary
Ministry of Statistics & Programme Implementation

EXECUTIVE SUMMARY

Sl. No.	Sector	Projects on Monitor	Projects Additional Delayed
1	Road Transport & Highways	138	13
2	Railways	132	0
3	Power	92	7
4	Petroleum	71	1
5	Coal	48	3
6	Telecommunications	40	0
7	Shipping & Ports	25	0
8	Steel	15	0
9	Fertilisers	6	0
10	Civil Aviation	5	1
11	Atomic Energy	4	1
12	Urban Development	4	1
13	Mines	1	0
14	Petrochemicals	1	0
15	Water Resources	1	0
	Total	583	27

ANNEXURE-I

Month wise List of Completed Project Costing Rs. 150 Crore and above during 2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
April, 2011				
<u>Civil Aviation</u>				
1	Extension of Secondary Runway(K2)(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	230.00	01/2011	241.28
<u>Petroleum</u>				
2	SULTANPUR NEEMRANA PIPE LINE PROJECT (Spurline to CJPL)(GAS AUTHORITY OF INDIA LIMITED) - [N16000049]	396.13	10/2009	106.22
3	Guru Govind Singh Refinery Products Evacuation Project(HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000076]	605.40	12/2010	408.90
<u>Power</u>				
4	Farakka STPP Stage-III(NATIONAL THERMAL POWER CORPORATION) - [N18000016]	2,570.44	08/2010	1,896.00
<u>Railways</u>				
5	GUNTUR-GUNTAKAL-KALLURU(GL)(SCR)(SOUTH CENTRAL RAILWAY) - [220100330]	458.45	-	555.49
<u>Road Transport & Highways</u>				
6	MADURAI -KANIAKUMARI SECTION (NS-41/TN) NH-7,KM.80 TO KM.120(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106240]	323.36	03/2008	189.90
<u>Shipping & Ports</u>				
7	ACQUISITION OF 4 NOS. OF 115000 DWT CRUDE OIL CARR(SHIPPING corp. of india) - [N25000032]	1,108.12	04/2011	1,238.88
May, 2011				
<u>Civil Aviation</u>				
8	CONSTRUCTION OF RCC/PRE STRESSD CONCRETE BRIDGE K3(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000068]	213.35	09/2010	60.89
<u>Power</u>				
9	TR. SYSTEM FOR STARTUP POWER TO DVC & MAITHON RB GEN. PROJ.(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000037]	290.49	04/2010	346.80

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Railways</u>				
10	DEOGHAR-DUMKA NEW BG LINE (DOUBL.)(ER)(EASTERN RAILWAYS) - [220100264]	180.73	12/2006	352.32
11	HAPUR-KANKATHER (LD),NR(NORTHERN RAILWAY) - [220100278]	106.64	03/2007	147.32
12	SHIMOGA-TALAGUPPA (SWR), GC(SOUTH WESTERN RAILWAY) - [N22000056]	46.00	-	244.16
<u>Road Transport & Highways</u>				
13	GONDE-VADAPPE(THANE), NH-3, KM.440/000 TO KM.539/500(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106262]	579.00	04/2009	765.90
14	NAGAON BYPASS (NH-37)(NHAI)(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106289]	230.00	06/2008	312.00
15	KALGHAT-MP/MAHARASHTRA BORDER KM 16.6-84.70(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000119]	549.00	05/2010	815.00
June,2011				
<u>Petroleum</u>				
16	CAPACITY EXP. CUM MODERNISATION PH-II(BHARAT PETROLEUM CORPORATION LIMITED) - [N16000080]	2,591.80	12/2009	3,265.10
<u>Power</u>				
17	KOTESWAR TRANSMISSION SYSTEM (PGCIL)(POWER GRID CORPORATION OF INDIA LIMITED) - [180100256]	260.34	06/2008	184.25
18	EAST-WEST TRANSMISSION CORRIDOR STRENGTHNING SCHEME(POWER GRID CORPORATION OF INDIA LIMITED) - [260100100]	803.70	06/2009	667.01
19	TRANSMISSION SYSTEM ASSOCIATED WITH KORBA III GENE(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000059]	276.61	06/2011	199.16
<u>Railways</u>				
20	VILLUPURAM-KATPADI (GC)(SR)(SOUTHERN RAILWAY) - [220100251]	175.00	-	538.69
<u>Road Transport & Highways</u>				
21	PURNEA-GOYAKOTA SEC.(EW) (NS & EW-PH-I) KM.419-KM.447, NH-31(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240103191]	205.73	07/2004	247.70
22	MEHSI TO KOTWA (LMNHP-II), PH.II, KM.480 TO KM.440, NH-28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106223]	239.00	07/2005	317.60
23	BANGLORE - HOSKOTE MUDBOGAL SECTION NH-4(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000106]	565.00	07/2010	1,080.00
July,2011				

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Steel</u>				
24	REBUILDING OF COKE OVEN BATTERY NO-6 (BSP)(STEEL AUTHORITY OF INDIA LIMITED (SAIL)) - [N12000054]	172.78	01/2010	131.95
<u>Petroleum</u>				
25	C2-C3 AND LPG RECOVERY FROM LNG, DAHEJ (ONGC)(OIL & NATURAL GAS CORPORATION LIMITED) - [160100168]	900.92	05/2008	774.32
26	COMPRESSOR STATIONS (VIJAYPUR AND JHABUA) PHASE-I(GAS AUTHORITY OF INDIA LIMITED) - [N16000053]	1,512.00	04/2011	846.61
27	Pipeline Replacement project-2(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000111]	2,553.28	05/2011	3,614.84
<u>Railways</u>				
28	SURENDRANAGAR-BHAVNAGAR(GC),WR(WESTERN RAILWAY) - [220100187]	437.40	03/2004	544.35
<u>Road Transport & Highways</u>				
29	IMPROVEMENT OF ACCESS OF GQ WITHIN CHENNAI CITY(NHAI) OTHERS(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106203]	210.00	04/2007	672.97
August,2011				
<u>Power</u>				
30	EST. OF 400/220 KV GIS POOLING STATION NEAR CHAMER(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000040]	262.10	09/2010	164.00
<u>Railways</u>				
31	AJMER-UDAIPUR-CHITTAURGARH (GC),NWR(NORTH WESTERN RAILWAY) - [220100185]	262.00	-	548.54
<u>Road Transport & Highways</u>				
32	AYODHYA - LUCKNOW (LMNHP-I) NH-28, KM.45 TO KM.8.2(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106222]	193.00	10/2008	338.70
33	MEERUT-MUZAFFARNAGAR, NH-58 PHASE-III, KM.52.25 TO KM.131.00(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106256]	359.00	03/2009	870.60
<u>Telecommunications</u>				
34	NIB-II PROJECT RURAL BROADBAND(BHARAT SANCHAR NIGAM LIMITED) - [N26000037]	312.86	02/2008	204.43
<u>Urban Development</u>				
35	DELHI MRTS PHASE-II PROJECT(DELHI METRO RAIL CORPORATION) - [280100002]	8,676.00	06/2010	18,304.30

September,2011

**Month wise List of Completed Project Costing Rs. 150 Crore and above during
2011-2012**

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
<u>Petroleum</u>				
36	MSQ QUALITY UP GRADATION PROJECT AT BONGAIGAON REF(INDIAN OIL CORPORATION LIMITED) - [N16000040]	293.60	12/2009	234.81
<u>Railways</u>				
37	RAJKOT-VERAVAL (GC) AND WANSJALIYA-JETALSAR GC AN(WESTERN RAILWAY) - [220100116]	112.53	03/1996	509.57
38	Sadulpur-Bikaner and Ratangarh-Degana Gauge Canves(NORTH WESTERN RAILWAY) - [N22000106]	643.36	03/2011	786.54
<u>Road Transport & Highways</u>				
39	AYODHYA - LUCKNOW (LMNHP-II) KM.93.075 TO KM.45, NH- 28(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106225]	217.00	10/2008	352.26
October,2011				
<u>Power</u>				
40	TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA- III(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000043]	204.07	06/2011	129.60

ANNEXURE-I

Month wise List of Deleted Project Costing Rs. 150 Crore and above during
2011-2012

Sl. No.	Project Name	Original Cost (Rs. Crore)	Original Date Of Commissioning	Cumulative Expenditure (Rs. Crore)
May,2011				
<u>Civil Aviation</u>				
1	D/O OF TERMINAL BLDG. AND PAVEMENT WORKS AT CHENNA(AIRPORT AUTHORITY OF INDIA LIMITED) - [N04000056]	535.00	06/2010	143.97


Summary of projects in the Flash Report for the month of October, 2011

I. Project Implementation - Current Status:

Number of Projects in Previous Month	569
Number of Projects completed/dropped/frozen in Previous Month	4
Number of Projects completed/dropped/frozen in Current Month	1
Number of Projects with Anticipated greater than Rs. 150 Cr. in Current Month	3
Number of Projects Added in Current Month	16
Number of Projects in Current Month	583


II. Brief Analysis

Project Status with respect to Original Schedule: Out of 583 projects, 7 projects are ahead of schedule, 166 projects are on schedule and 235 projects are delayed. Of the balance, 127 projects do not have fixed dates of commissioning while 48 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

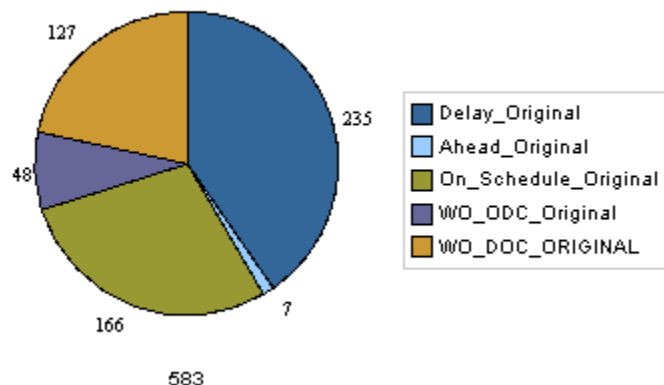

III. Investment Scenario

The Total Original cost of implementation of 583 projects when sanctioned, was of the order of Rs. 712811.99 crore but this was subsequently revised to Rs. 821664.74 crore implying a cost overrun of 15.3%. The expenditure incurred on these projects till October, 2011 is Rs. 344360.76 crore, which is 41.9% of the revised cost of the projects.

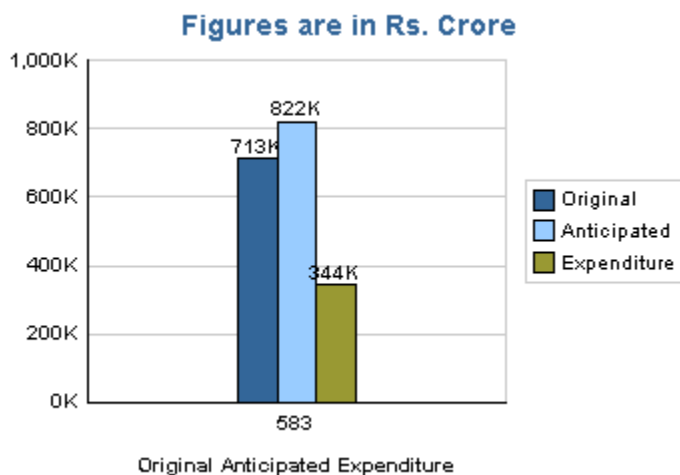

I. Project Added / Completed / Dropped / Frozen

No of Projects in Previous Month	569
No of Projects Completed/Dropped/Frozen in Previous Month	4
No of Projects Completed/Dropped/Frozen in Current Month	1
No of Projects with Anticipated Cost Greater than Rs.150 Cr. In Current Month	3
No of Projects added in Current Month	16
No of Projects in Current Month	583

II. Project status

With Respect To	Number of Projects					Total	Delay (%)
	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C		
Original (Date)	235	6	167	48	127	583	40.31
Latest Approved (Date)	254	13	204	30	85	583	43.57

III. (A) Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	474	565,353.49	598,999.42	227,436.14	38.00	33,645.93	6.00
Latest Approved (RCE)	109	195,748.27	222,665.32	116,924.62	52.50	26,917.05	13.80
Total (RCE)	583	761,101.76	821,664.74	344,360.76	41.91	60562.98	7.96
Original Cost of All Projects							
Original Cost	583	712,811.99	821,664.74	344,360.76	41.90	108,852.75	15.30

III. (B) Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Original (OCE)	235	320,056.39	390,393.26	218,197.05	55.90	70,336.87	22.00
Latest Approved (RCE)	254	334,757.09	376,830.44	212,635.39	56.40	42,073.35	12.60

IV. Additional Delayed Project cost

(All Cost/ Expenditure in Rs. crore)							
With Respect to	No. of Projects	Cost				Cost overrun	
		Sanctioned	Anticipated	Expenditure	%	(Crore)	%
Latest Approved	27	39,461.10	50,003.53	32,086.00	64.20	10,542.43	26.70

Extent of cost overrun in projects with respect to original schedule

S.No.	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Original	Anticipated cost	Cost overrun (%)	No .	Original cost	Anticipated cost	% Incr Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,021.6	5,611.1	11.7	2	3,750.5	4,340.0	15.7
3	Coal	48	27,241.5	30,628.5	12.4	12	13,742.8	17,727.6	29.0
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	7.6
6	Steel	15	64,990.3	71,157.8	9.5	6	24,028.9	30,216.4	25.8
7	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
8	Petroleum	71	156,539.5	164,117.8	4.8	17	52,273.3	68,974.3	31.9
9	Power	92	191,151.0	197,235.0	3.2	11	25,563.8	32,102.3	25.6
10	Railways	132	65,054.7	132,203.1	103.2	101	37,121.1	104,326.3	181.0
11	Road Transport & Highways	138	76,162.3	77,967.5	2.4	13	3,890.9	6,265.2	61.0
12	Shipping & Ports	25	18,052.2	19,035.7	5.4	11	6,524.5	7,709.1	18.2
13	Telecommunications	40	19,713.1	20,297.7	3.0	5	2,114.4	2,781.7	31.6
14	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		583	712,812.0	821,664.7	15.3	185	202,277.4	322,234.7	59.3

Extent of the time overrun in projects with respect to original schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	3	28,122.0	32,960.0	11 - 48
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 17
3	Coal	48	27,241.5	30,628.5	12.4	17	11,824.7	14,752.2	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	0	0.0	0.0	-
6	Steel	15	64,990.3	71,157.8	9.5	3	23,367.9	28,931.9	5 - 36
7	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
8	Petroleum	71	156,539.5	164,117.8	4.8	29	70,732.8	82,335.0	2 - 120
9	Power	92	191,151.0	197,235.0	3.2	45	109,105.9	115,254.5	2 - 90
10	Railways	132	65,054.7	132,203.1	103.2	26	22,320.7	51,963.7	2 - 213
11	Road Transport & Highways	138	76,162.3	77,967.5	2.4	90	31,999.9	34,165.2	4 - 106
12	Shipping & Ports	25	18,052.2	19,035.7	5.4	11	8,373.4	9,198.6	2 - 93
13	Telecommunications	40	19,713.1	20,297.7	3.0	2	634.0	809.5	17 - 72
14	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		583	712,812.0	821,664.7	15.3	235	320,056.4	390,393.3	

Extent of the time overrun in projects with respect to latest schedule

S. No	Sector	No. of Projects	Total cost (Rs. Cr.)			Projects with time overrun			
			Original	Anticipated cost	Cost overrun (%)	No.	Original cost	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.3	34,066.3	16.6	4	29,228.3	34,066.3	0 - 48
2	Civil Aviation	5	5,021.6	5,611.1	11.7	4	4,395.6	4,985.1	3 - 17
3	Coal	48	27,241.5	30,628.5	12.4	17	11,824.7	14,752.2	9 - 48
4	Fertilisers	6	5,317.4	5,317.4	0.0	3	2,241.6	2,241.6	1 - 8
5	Mines	1	4,091.5	4,401.8	7.6	1	4,091.5	4,401.8	30 - 30
6	Steel	15	64,990.3	71,157.8	9.5	5	15,461.8	17,941.7	0 - 6
7	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
8	Petroleum	71	156,539.5	164,117.8	4.8	17	49,470.3	54,638.4	2 - 73
9	Power	92	191,151.0	197,235.0	3.2	40	112,712.9	114,342.3	0 - 63
10	Railways	132	65,054.7	132,203.1	103.2	37	27,127.7	60,777.1	0 - 213
11	Road Transport & Highways	138	76,162.3	77,967.5	2.4	90	31,999.9	34,165.2	4 - 106
12	Shipping & Ports	25	18,052.2	19,035.7	5.4	11	8,281.2	9,187.2	2 - 93
13	Telecommunications	40	19,713.1	20,297.7	3.0	23	12,227.9	12,535.7	4 - 72
14	Urban Development	4	44,245.2	49,518.1	11.9	1	6,395.0	11,609.0	24 - 24
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	60 - 60
Total		583	712,812.0	821,664.7	15.3	254	316,001.3	376,830.4	

Extent of cost overrun in projects with respect to latest schedule

S.No.	Sector	No. of projects	Total cost (Rs. Cr.)			Projects with cost overrun			
			Latest approved	Anticipated cost	Cost overrun (%)	No .	Latest approved	Anticipated cost	% Increase Base
1	Atomic Energy	4	29,228.3	34,066.3	16.6	2	16,663.0	21,501.0	29.0
2	Civil Aviation	5	5,228.6	5,611.1	7.3	1	1,942.5	2,325.0	19.7
3	Coal	48	28,958.4	30,628.5	5.8	6	4,961.1	7,098.9	43.1
4	Fertilisers	6	5,317.4	5,317.4	0.0	0	0.0	0.0	0.0
5	Mines	1	4,401.8	4,401.8	0.0	0	0.0	0.0	0.0
6	Steel	15	70,865.6	71,157.8	0.4	3	598.0	910.3	52.2
7	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
8	Petroleum	71	169,275.1	164,117.8	-3.0	4	32,736.9	35,849.3	9.5
9	Power	92	196,947.2	197,235.0	0.1	4	16,488.8	17,290.3	4.9
10	Railways	132	82,773.4	132,203.1	59.7	88	42,723.4	92,213.5	115.8
11	Road Transport & Highways	138	76,162.3	77,967.5	2.4	13	3,890.9	6,265.2	61.0
12	Shipping & Ports	25	18,431.5	19,035.7	3.3	9	6,498.8	7,204.5	10.9
13	Telecommunications	40	19,745.3	20,297.7	2.8	3	1,287.5	1,903.1	47.8
14	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
15	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		583	761,101.8	821,664.7	8.0	135	134,728.8	205,357.0	52.4

Extent of time & cost overrun in projects with respect to latest schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	0	0.00	0.00	0- 0
2	Civil Aviation	5	5,021.58	5,611.06	11.74	0	0.00	0.00	0- 0
3	Coal	48	27,241.47	30,628.50	12.43	1	469.78	706.40	44- 44
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	15	64,990.27	71,157.81	9.49	1	8,692.00	12,291.00	36- 36
7	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
8	Petroleum	71	156,539.45	164,117.82	4.84	14	19,581.72	34,561.21	3- 120
9	Power	92	191,150.96	197,235.03	3.18	6	6,583.41	11,389.62	18- 90
10	Railways	132	65,054.74	132,203.07	103.22	5	2,285.97	7,657.76	0- 80
11	Road Transport & Highways	138	76,162.26	77,967.51	2.37	0	0.00	0.00	0- 0
12	Shipping & Ports	25	18,052.23	19,035.72	5.45	2	567.88	582.03	5- 7
13	Telecommunications	40	19,713.13	20,297.68	2.97	0	0.00	0.00	0- 0
14	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
15	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		583	712811.99	821664.74	15.27	30	42272.27	71589.78	

Extent of time & cost overrun in projects with respect to original schedule

S No.	Sector	No. of projects	Total Cost (Rs. Cr.)			Projects with time & cost overrun			
			Original	Anticipated Cost	Cost overrun(%)	No.	Original	Anticipated cost	Range (Months)
1	Atomic Energy	4	29,228.29	34,066.29	16.55	2	16,663.00	21,501.00	16- 48
2	Civil Aviation	5	5,021.58	5,611.06	11.74	2	3,750.51	4,340.00	10- 11
3	Coal	48	27,241.47	30,628.50	12.43	7	6,813.24	10,338.47	9- 48
4	Fertilisers	6	5,317.41	5,317.41	0.00	0	0.00	0.00	0- 0
5	Mines	1	4,091.51	4,401.76	7.58	1	4,091.51	4,401.76	30- 30
6	Steel	15	64,990.27	71,157.81	9.49	2	23,135.00	28,699.00	6- 36
7	Petrochemicals	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
8	Petroleum	71	156,539.45	164,117.82	4.84	16	51,517.26	68,076.31	3- 120
9	Power	92	191,150.96	197,235.03	3.18	11	25,563.77	32,102.32	5- 90
10	Railways	132	65,054.74	132,203.07	103.22	19	10,615.66	40,607.30	12- 213
11	Road Transport & Highways	138	76,162.26	77,967.51	2.37	13	3,890.90	6,265.24	7- 92
12	Shipping & Ports	25	18,052.23	19,035.72	5.45	7	3,728.52	4,751.17	6- 93
13	Telecommunications	40	19,713.13	20,297.68	2.97	4	1,354.24	1,681.67	17- 72
14	Urban Development	4	44,245.18	49,518.08	11.92	1	6,395.00	11,609.00	24- 24
15	Water Resources	1	542.90	1,187.00	118.64	1	542.90	1,187.00	60- 60
Total		583	712811.99	821664.74	15.27	86	158061.51	235560.24	

V. List of projects completed/dropped/Frozen current month

(All Cost /Expenditure in Rs. crore)

Project	DOA	Original		Now anticipated		Final
		Cost	DOC	Cost	DOC	Expenditure
<u>Power</u>						
TRANSMISSION SYSTEM ASSOCIATED WITH FARAKKA-III	12/2008	204.07	06/2011	204.07	08/2011	129.60

VI. List of projects added

(All Cost in Rs. crore)

Project	DOA	Original		Anticipated	
		Cost	DOC	Cost	DOC
<u>Power</u>					
TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK	10/2011	558.26	11/2013	558.26	11/2013
Common System Associated with Coastal Energen Priv	9/2011	1,940.13	9/2014	1,940.13	9/2014
TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH	9/2011	1,366.34	12/2013	1,366.34	12/2013
TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED	8/2011	425.51	10/2013	425.51	10/2013
INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P	8/2011	1,391.97	12/2013	1,391.97	12/2013
TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT	7/2011	181.93	7/2013	181.93	7/2013
SYTEM STRENGTHENING XIII OF SR GRID	10/2011	487.49	6/2014	487.49	6/2014
INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P	8/2011	1,391.97	11/2013	1,391.97	11/2013
COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA	8/2011	1,637.34	8/2014	1,637.34	8/2014
<u>Road Transport & Highways</u>					
Muzafarpur - Sonbarsa	5/2011	511.54	11/2013	511.54	11/2013
kandla - Mundra port	1/2011	953.88	7/2013	953.88	7/2013
Trichy Bypass	5/2010	374.00	5/2013	374.00	5/2013
Dindigul - Kumli	9/2011	485.00	8/2013	485.00	8/2013
Tirupati - Chennai	4/2011	571.00	10/2013	571.00	10/2013
SAMAIKHALI - GANDHIDHAM	9/2010	805.39	3/2013	805.39	3/2013
<u>Steel</u>					
EXPANSION OF DURGAPUR STEEL PLANT	6/2009	2,875.00	12/2012	2,875.00	12/2012

VII. Milestones (Cumulative due & achieved)

Total	2334
Achieved up to month	982

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
<u>Atomic Energy</u>						
KUDANKULAM APP (NPCIL) NPCIL	13,171.00	15,824.00	12/2008	08/2012	12/2012	4
<u>Civil Aviation</u>						
Construction of New International Terminal Building AAI	335.61	335.61	05/2012	05/2012	08/2012	3
<u>Coal</u>						
TPS-II EXPANSION (1470MW TO 1970MW) (NLC) NLC	2,030.78	2,453.57	06/2009	05/2012	07/2012	2
BARSINGSAR TPS (2X125MW) (NLC) NLC	1,114.18	1,626.09	06/2009	10/2011	12/2011	2
ASHOK EXPN.OCP -CCL (10 MTY) CCL	471.66	341.63	03/2011	03/2012	03/2013	12
<u>Petroleum</u>						
CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) ONGC	736.65	736.65	09/2011	12/2011	12/2012	12
<u>Power</u>						
CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) NHPC	621.28	621.28	02/2011	02/2012	03/2012	1
EASTERN REGION STRENGTHENING SCHEME- II PGCIL	227.52	227.52	06/2010	11/2011	12/2011	1
CHAMERA,STAGE-III (NHPC) NHPC	1,405.63	1,405.63	08/2010	12/2011	02/2012	2
TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II PGCIL	238.25	227.03	05/2011	09/2011	11/2011	2
VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCL	2,491.58	3,422.44	07/2014	05/2016	07/2016	2
MOUDA STPP (NTPC) NTPC	5,459.28	6,010.89	08/2012	11/2012	01/2013	2
TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP PGCIL	557.24	639.52	01/2010	12/2011	03/2012	3
<u>Road Transport & Highways</u>						
MADURAI-ARUPKOTTAI- TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B NHAI	629.00	629.00	11/2010	10/2011	11/2011	1

VIII. List of projects reporting additional delays


Project name	Cost (Rs. Crore)		DOC reported			Delay (in months)
	Original	Anticipated	Original	Last month	This month	
KOTA BYPASS,RJ-4, NH-76 (NHAI) NHAI	275.00	250.39	10/2008	11/2011	12/2011	1
RINGBUNDS TO JHAJHANPUR (BR-6) NHAI	340.00	340.00	06/2008	10/2011	11/2011	1
THRISSUR TO ANGAMALI (NH-47) NHAI	312.50	312.50	03/2009	10/2011	11/2011	1
TRICHY - DINDIGUAL NH-45 NHAI	576.00	576.00	07/2010	10/2011	11/2011	1
PONDICHERY - TINDIVANAU NH-66 NHAI	285.00	285.00	07/2010	10/2011	11/2011	1
AURANG-RAIPUR, NH-6, KM.232 TO KM.281 NHAI	190.00	190.00	01/2009	10/2011	12/2011	2
END OF DURG BYPASS- CHHATISGARH/MAHARASHT RA BORDER NHAI	464.00	464.00	01/2011	10/2011	12/2011	2
FORBESGANJ TO SIMRAHI (NH-57)(NHAI) NHAI	332.94	332.94	09/2008	12/2011	03/2012	3
NAGPUR-KONDHALI,NH- 6(NHAI) NHAI	168.00	168.00	12/2008	10/2011	01/2012	3
HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 NHAI	212.00	386.10	09/2007	12/2013	04/2014	4
HARANGAJO TO MAIBANG, NH-54 NHAI	196.00	363.74	07/2009	12/2013	04/2014	4
DAKOBA TO NAGAON (NH- 36)(NHAI) NHAI	225.00	225.00	06/2008	10/2011	03/2012	5
<u>Urban Development</u>						
BANGALORE METRO RAIL PROJECT MRTD	6,395.00	11,609.00	12/2011	03/2013	12/2013	9

Number of projects reporting additional delay = 27

Trend and Graphical Analysis of All Projects

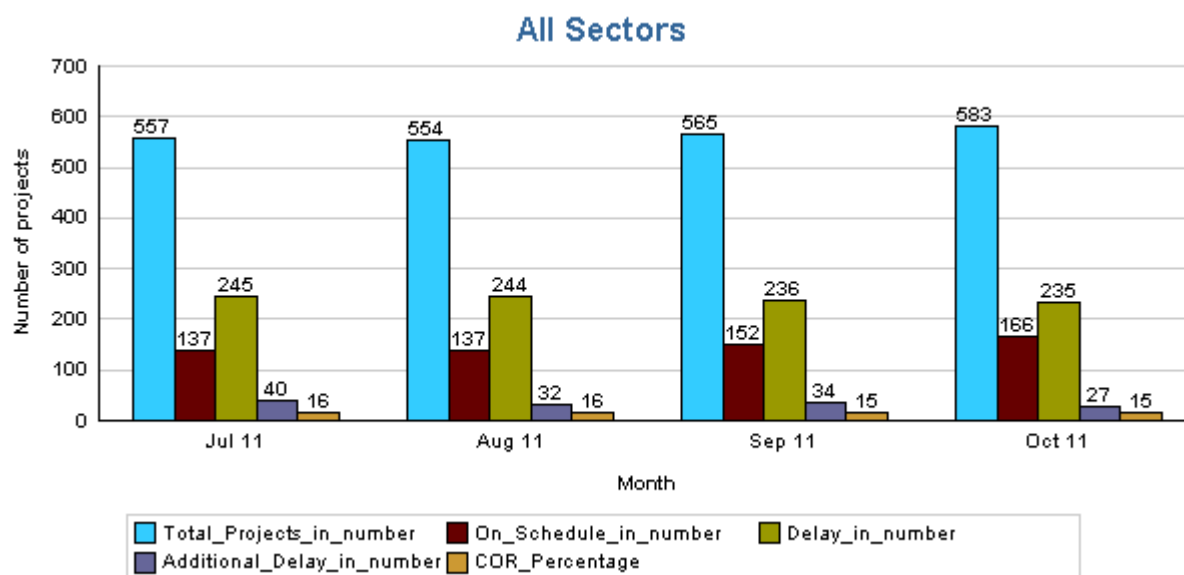


All Sectors Break-up of 235 Delayed projects in October 2011

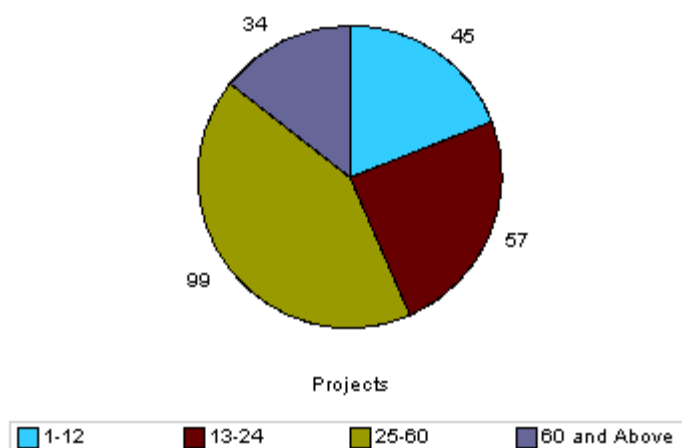


Trend and Graphical Analysis


Urban Development Sector

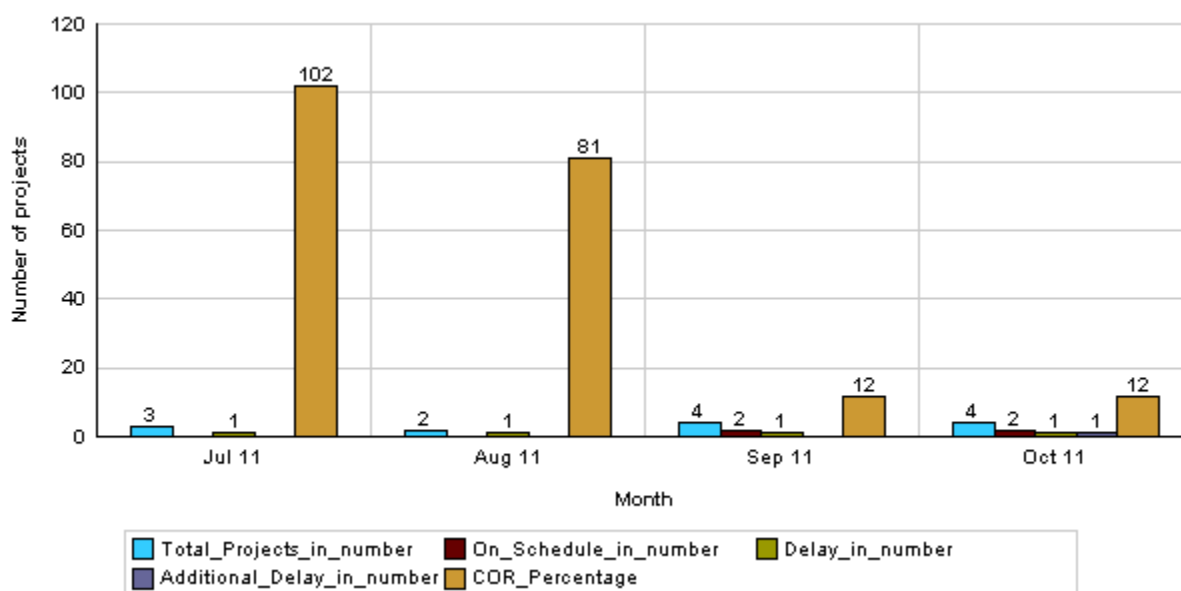


Urban Development Sector Break-up of 1 Delayed projects in October 2011

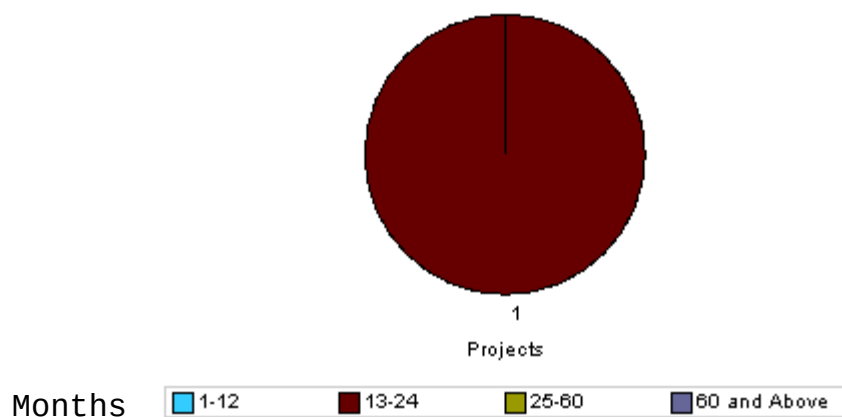


Trend and Graphical Analysis Telecommunications Sector

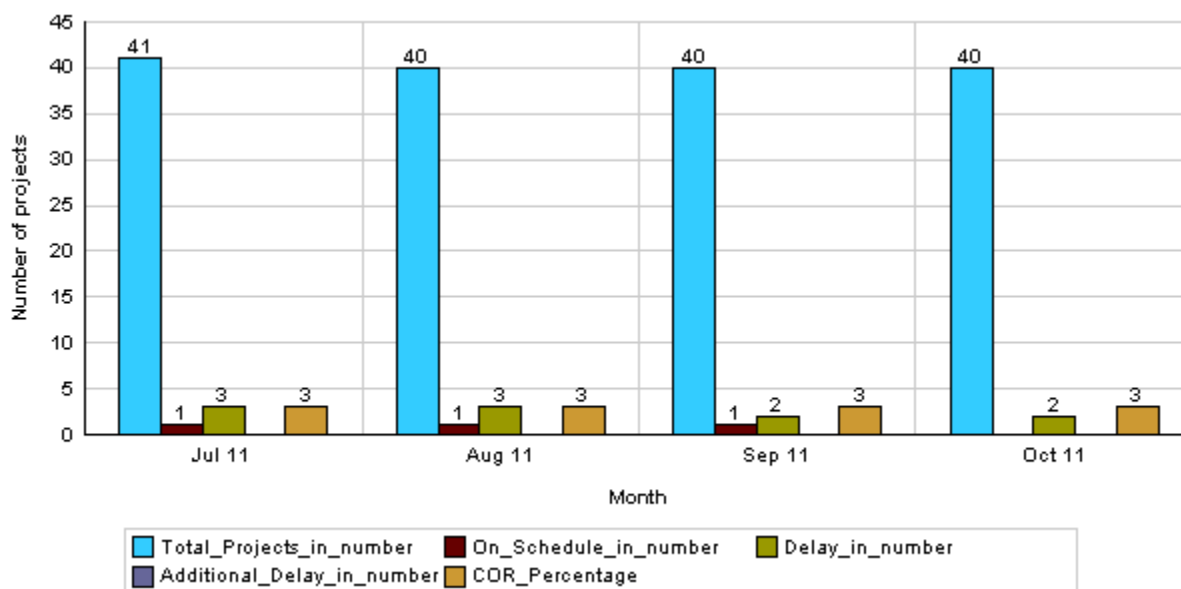


Telecommunications Sector Break-up of 2 Delayed projects in October 2011

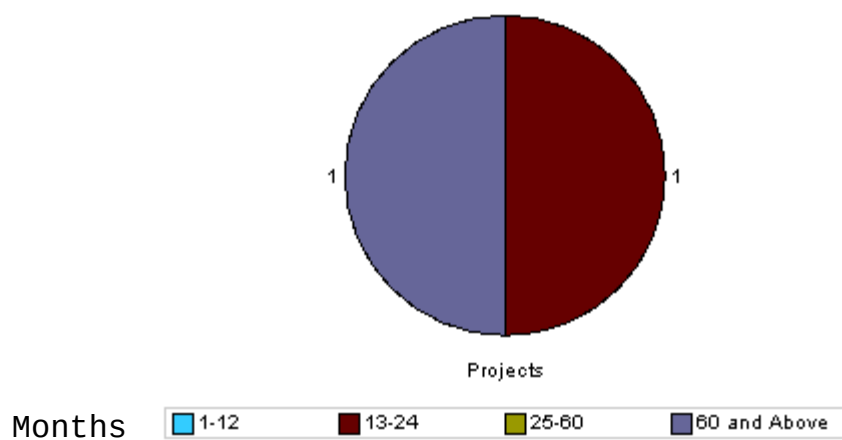


Trend and Graphical Analysis Shipping and Ports Sector

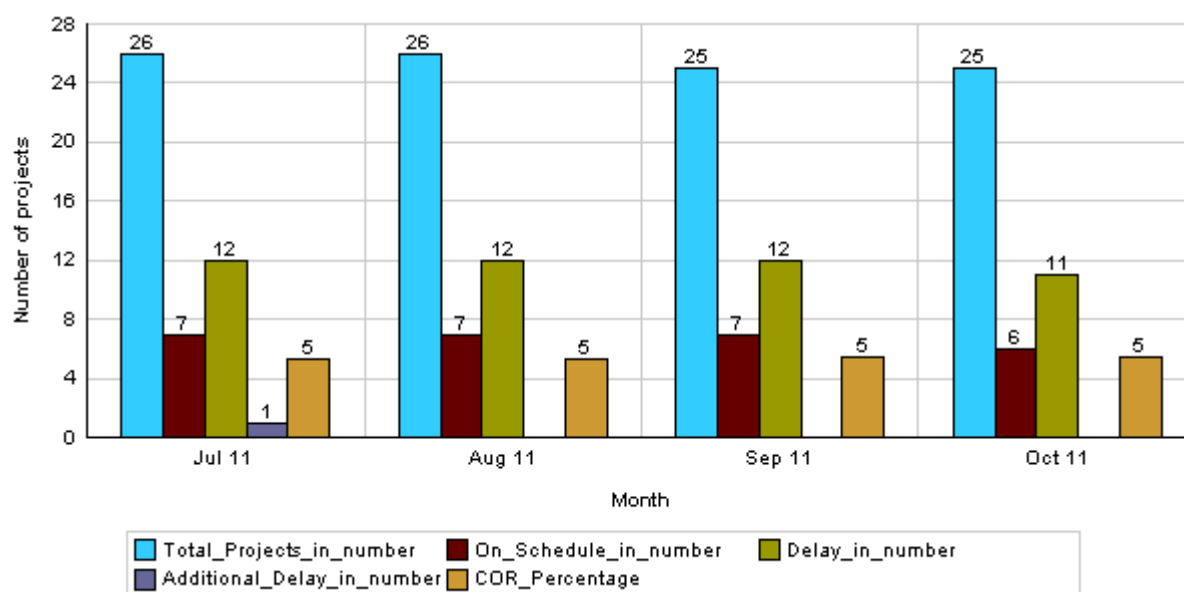


Sector Break-up of 11 Delayed projects in October 2011

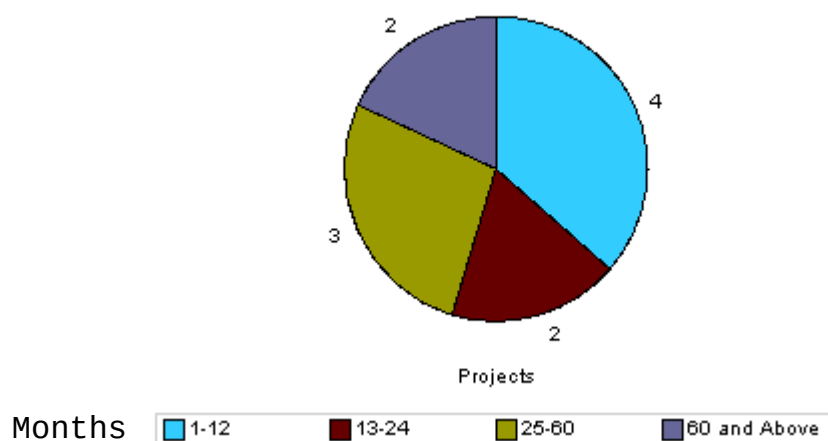

Trend and Graphical Analysis Road Transport and Highways Sector

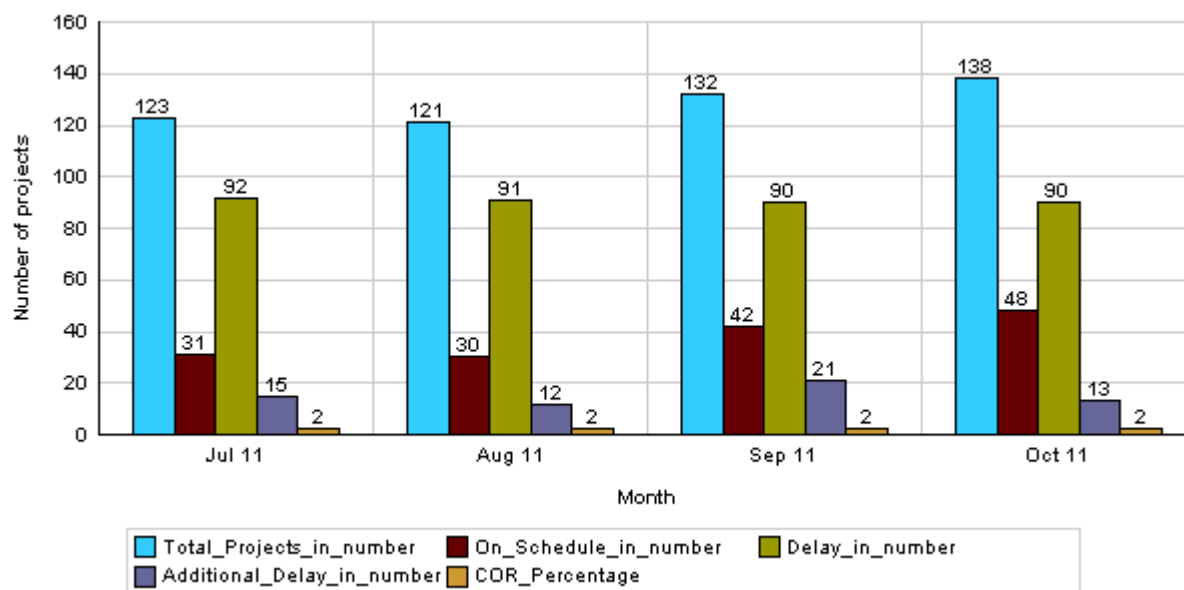


Sector Break-up of 90 Delayed projects in October 2011

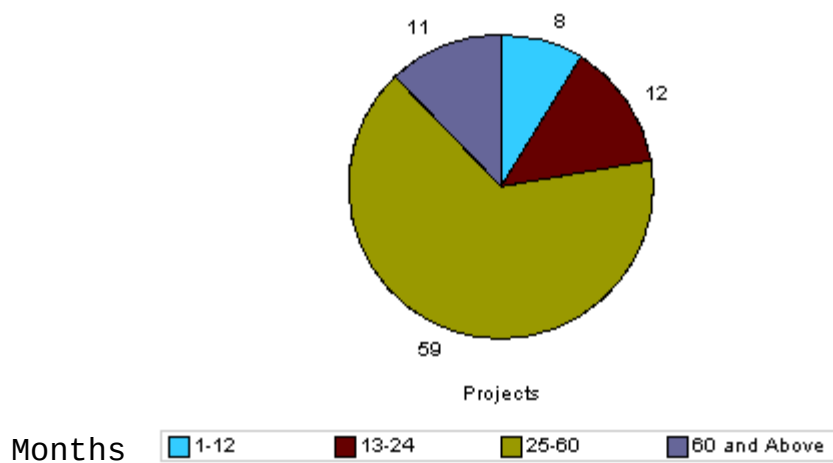


Trend and Graphical Analysis

Railways Sector

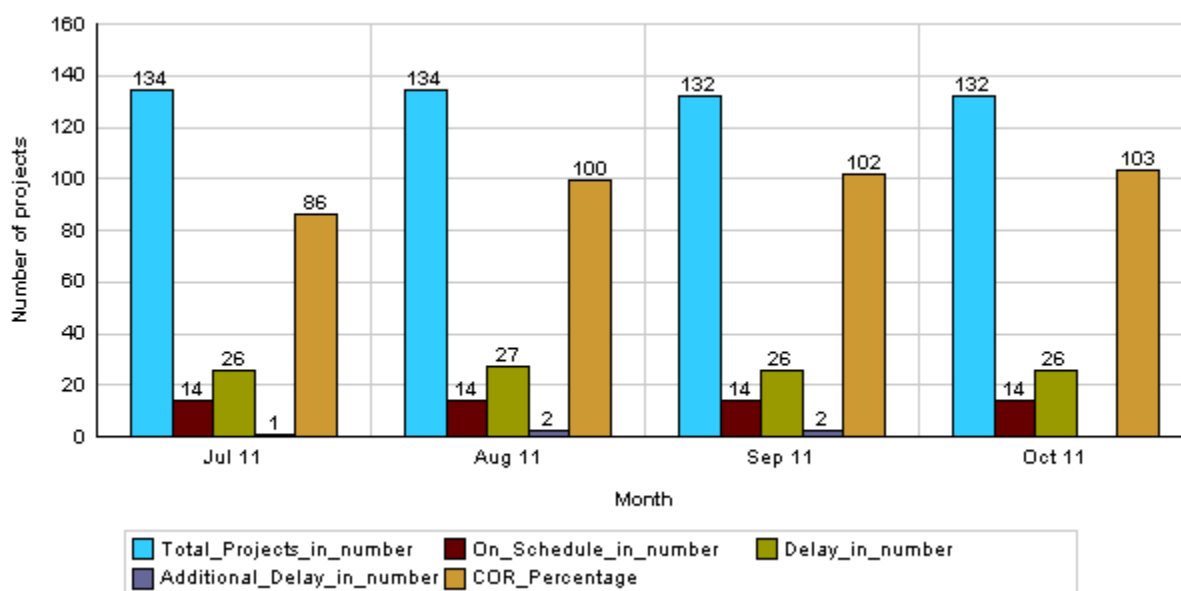


Railways Sector Sector Break-up of 26 Delayed projects in October 2011

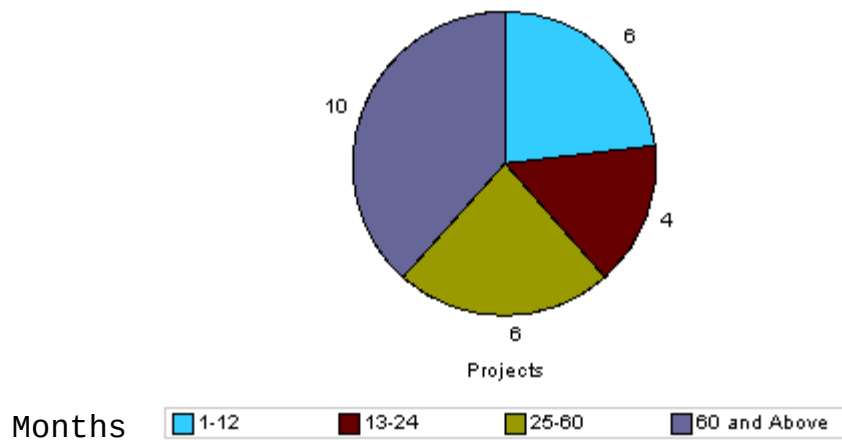


Trend and Graphical Analysis

Power Sector

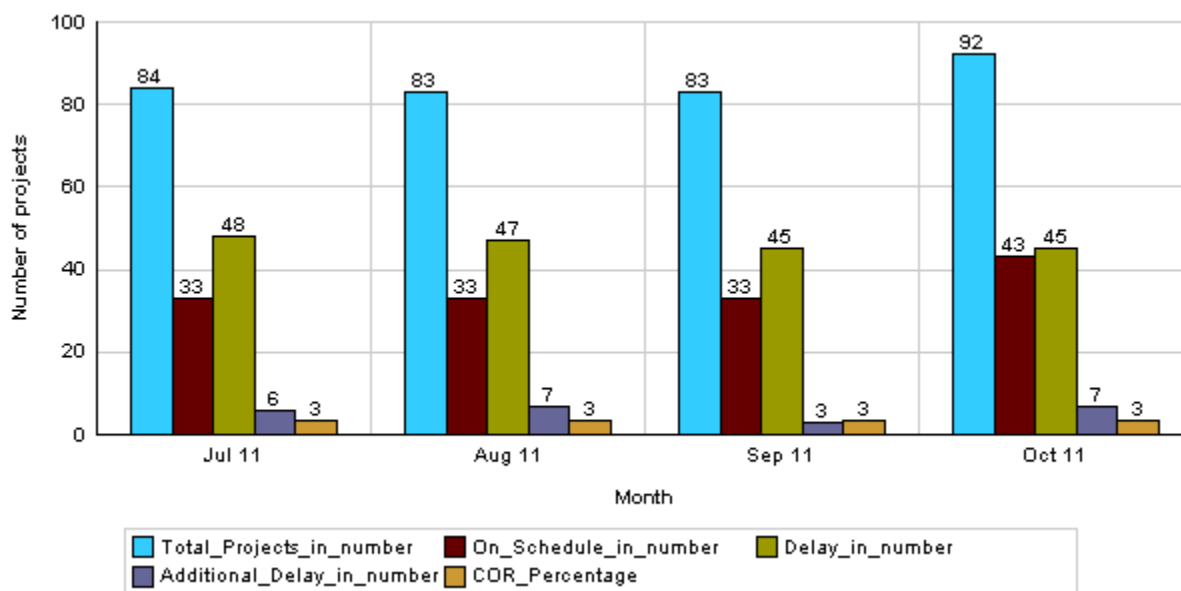

Power Sector Sector Break-up of 45 Delayed projects in October 2011

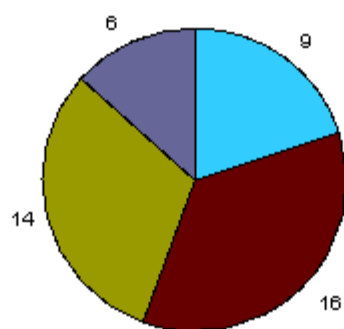


Months




Trend and Graphical Analysis

Petroleum Sector

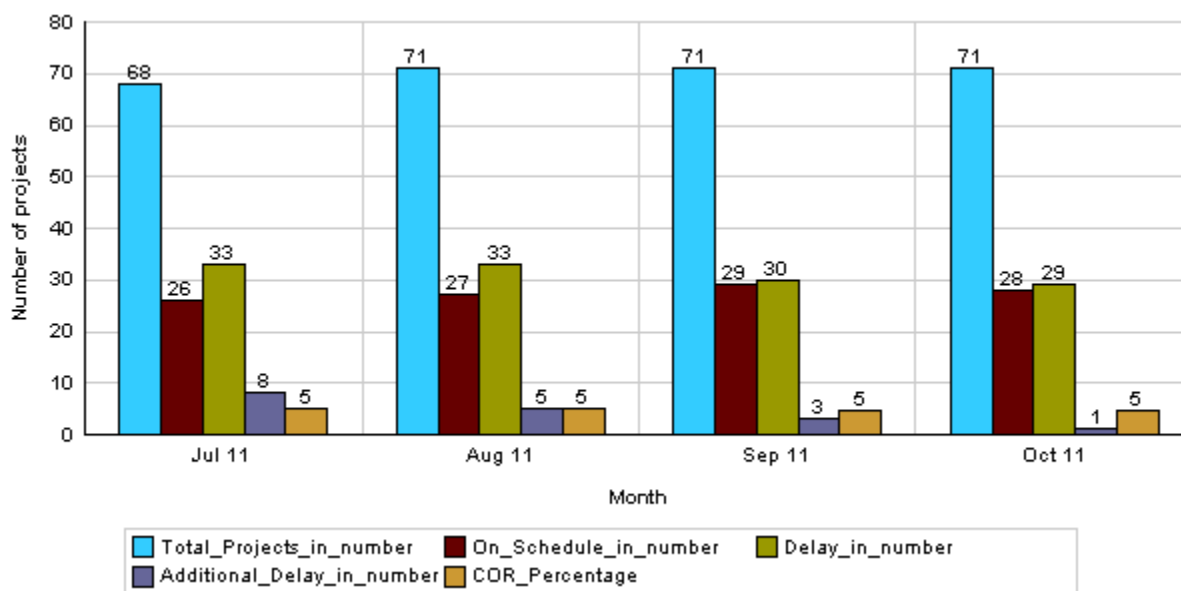


Petroleum Sector Sector Break-up of 29 Delayed projects in October 2011

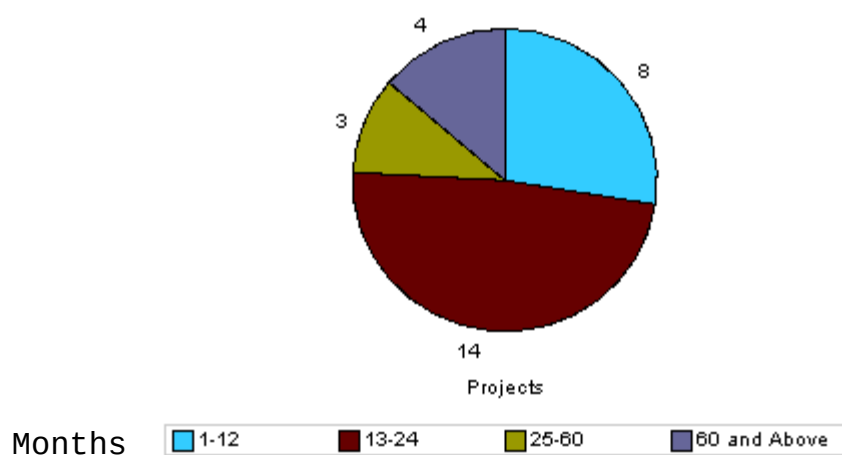


Trend and Graphical Analysis

Steel Sector

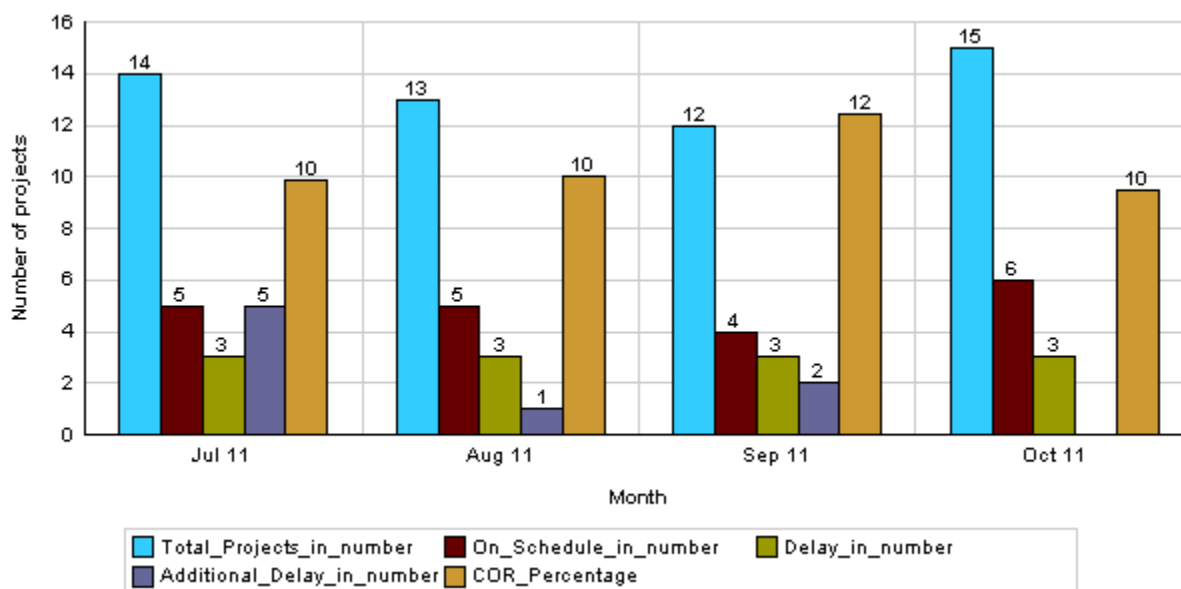


Steel Sector Break-up of 3 Delayed projects in October 2011

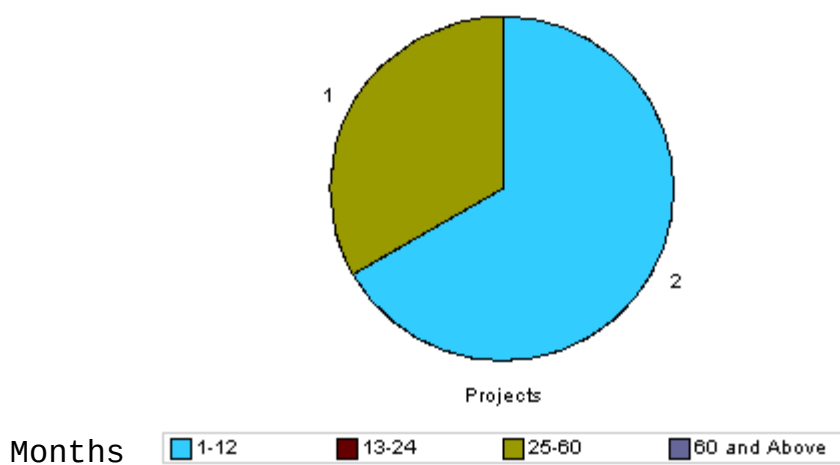


Trend and Graphical Analysis

Fertilisers Sector

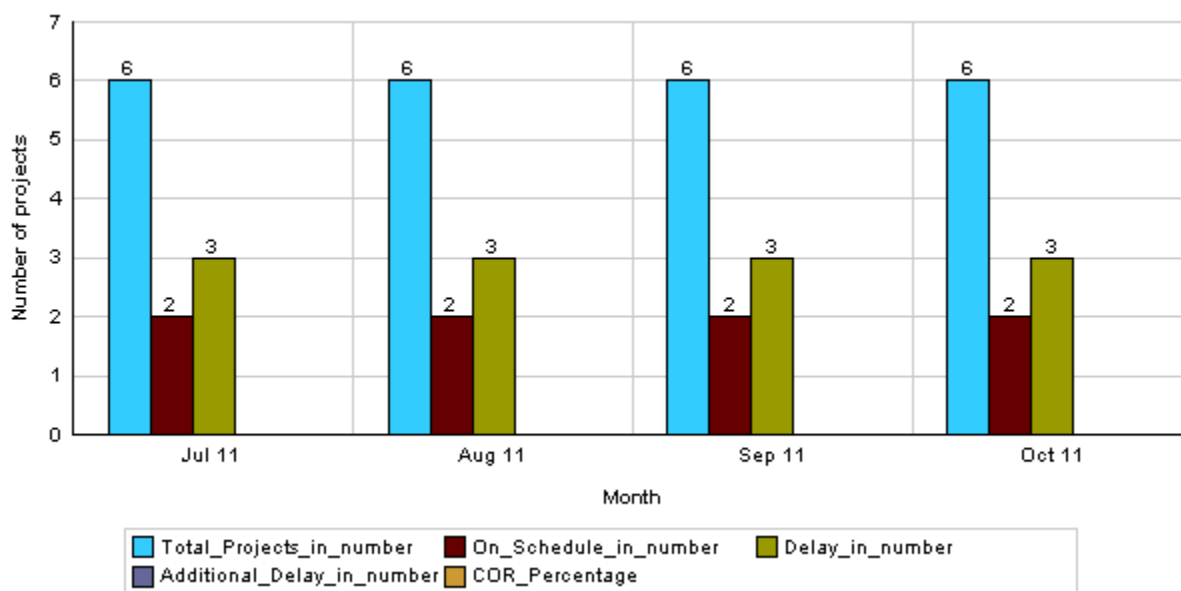


Fertilisers Sector Break-up of 3 Delayed projects in October 2011

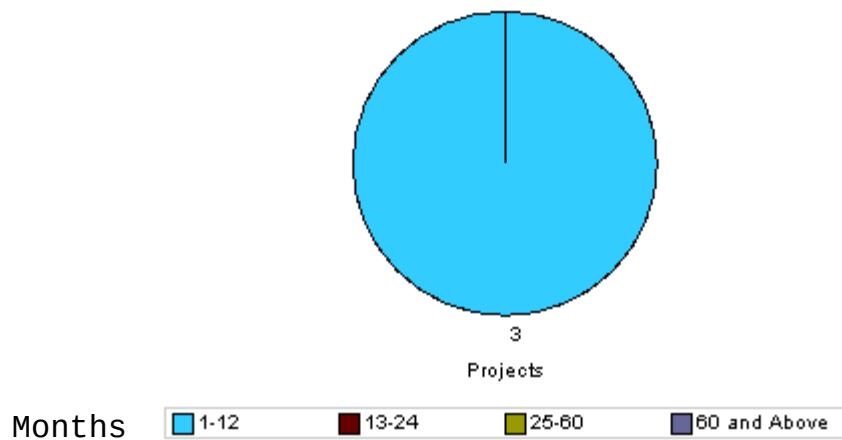


Trend and Graphical Analysis

Coal Sector

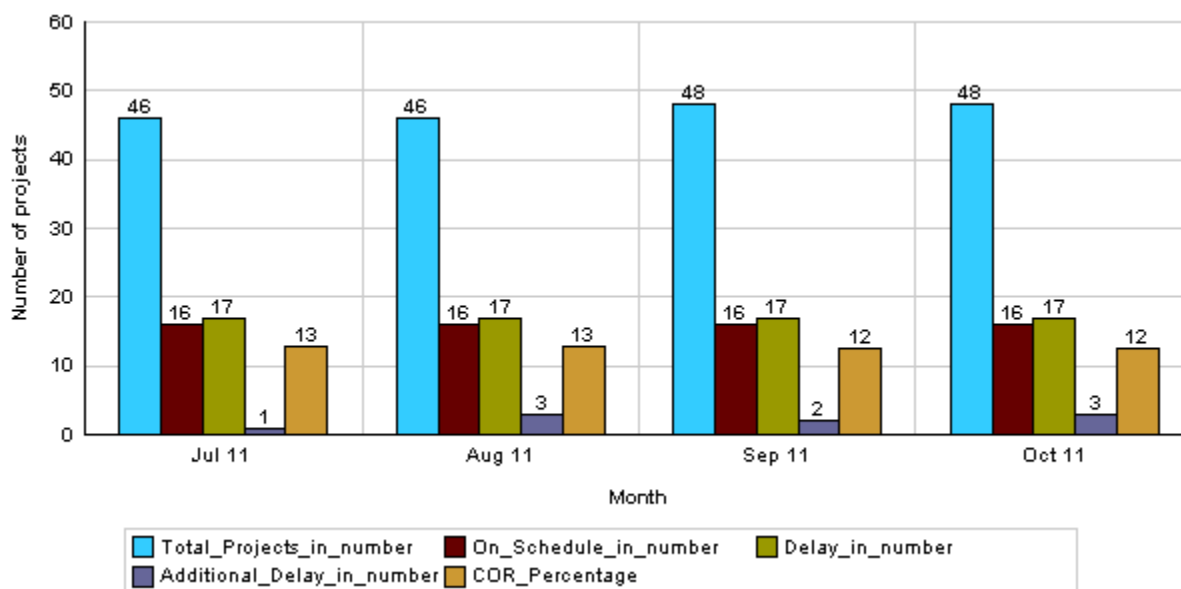


Coal Sector Sector Break-up of 17 Delayed projects in October 2011

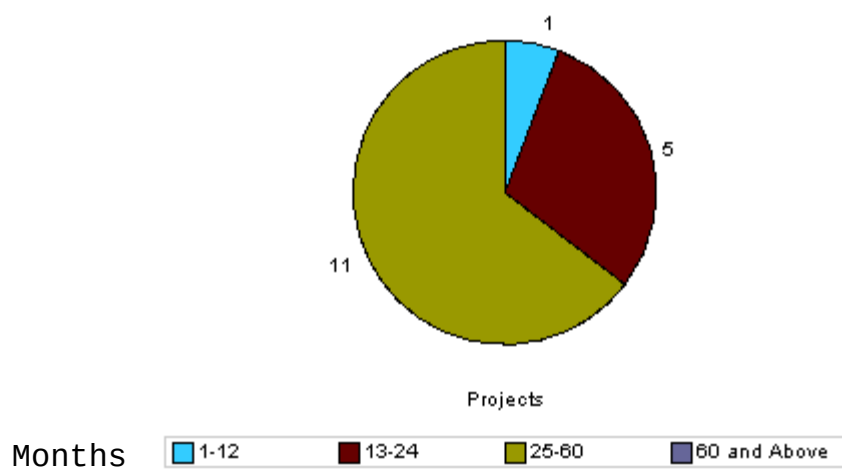


Trend and Graphical Analysis

Civil Aviation Sector

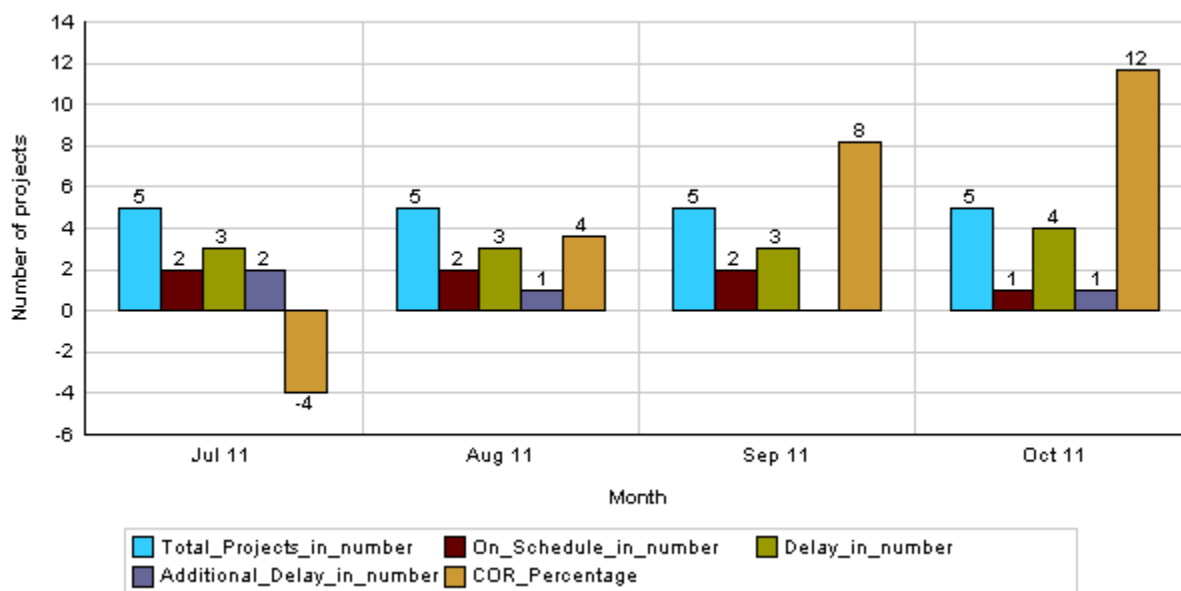


Civil Aviation Sector Break-up of 4 Delayed projects in October 2011

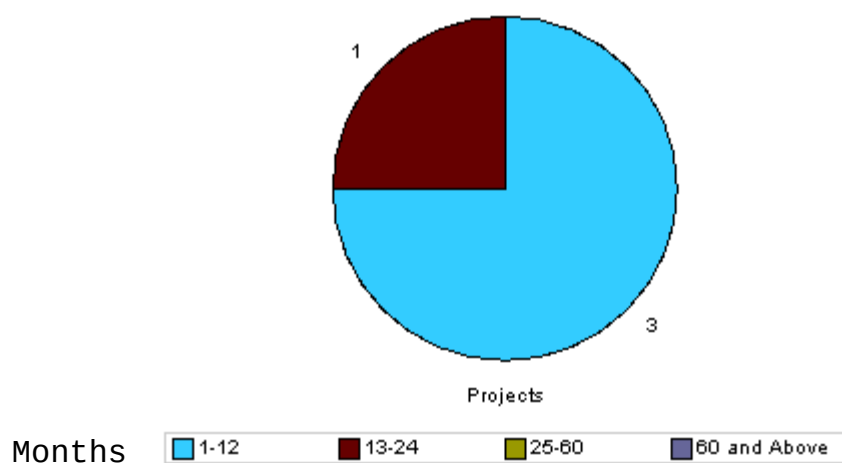


Trend and Graphical Analysis

Atomic Energy Sector

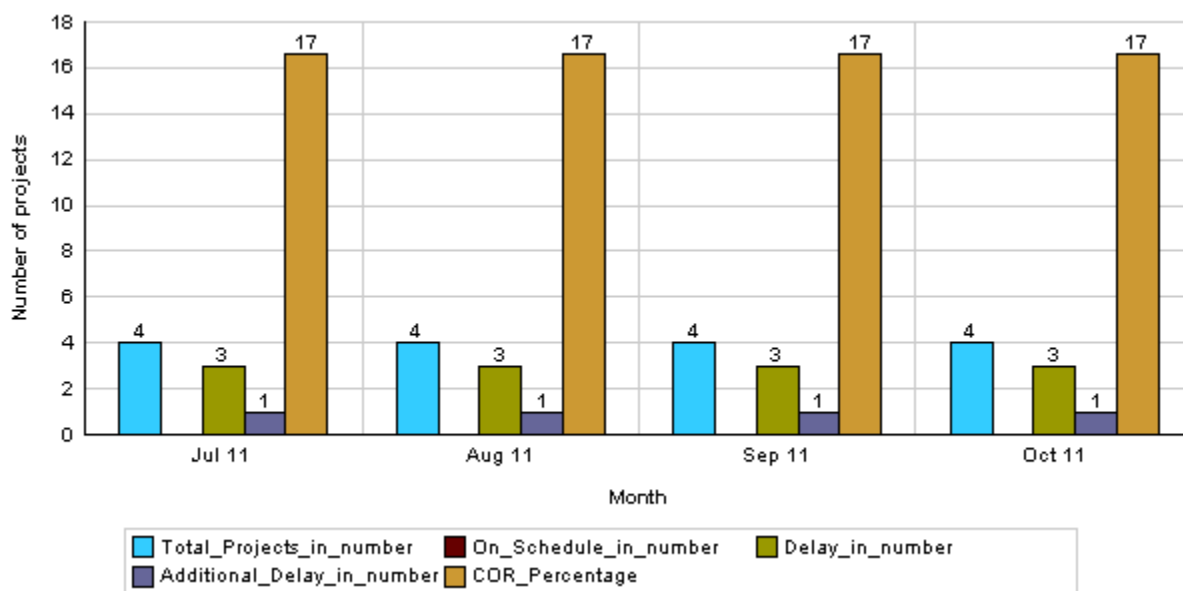

Atomic Energy Sector Sector Break-up of 3 Delayed projects in October 2011

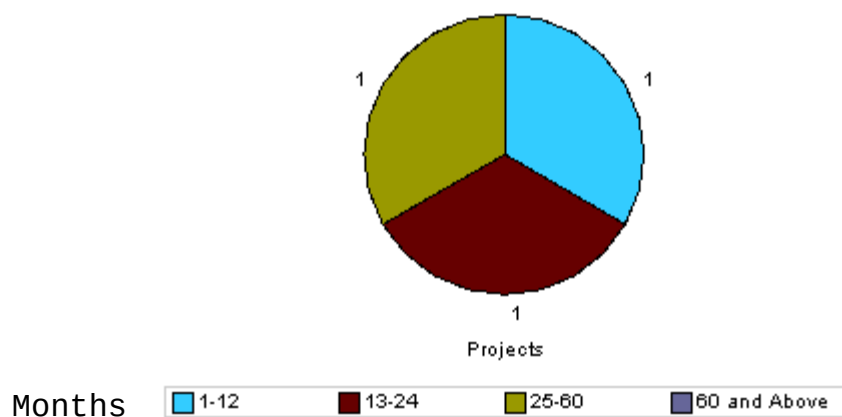

Sectorwise analysis of projects

Sector	Number of projects	Cost (Rs. Crore)		
		Original	Latest	Anticipated
Atomic Energy	4	29,228.29	29,228.29	34,066.29
Civil Aviation	5	5,021.58	5,228.58	5,611.06
Coal	48	27,241.47	28,958.42	30,628.50
Fertilisers	6	5,317.41	5,317.41	5,317.41
Mines	1	4,091.51	4,401.76	4,401.76
Steel	15	64,990.27	70,865.55	71,157.81
Petrochemicals	1	5,460.61	8,920.00	8,920.00
Petroleum	71	156,539.45	169,275.11	164,117.82
Power	92	191,150.96	196,947.23	197,235.03
Railways	132	65,054.74	82,773.37	132,203.07
Road Transport & Highways	138	76,162.26	76,162.26	77,967.51
Shipping & Ports	25	18,052.23	18,431.54	19,035.72
Telecommunications	40	19,713.13	19,745.26	20,297.68
Urban Development	4	44,245.18	44,304.08	49,518.08
Water Resources	1	542.90	542.90	1,187.00
Grand total	583	712,811.99	761,101.76	821,664.74

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	3,281.47	09/2010 -	01/2012	16(O)	5/80
2	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29 -	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/1
3	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 -	15,824.00	14,122.00	12/2008 -	12/2012	48(O)	60/119
4	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	1,059.00	12/2015 05/2016	11/2016	6(R1)	0/70
	Total		29,228.29 -	34,066.29	19,463.17				65/270
	<u>Civil Aviation</u>								
5	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,552.74	01/2011 -	12/2011	11(O)	0/0
6	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,530.56	05/2011 -	03/2012	10(O)	0/0
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.45	153.41	01/2011 -	06/2012	17(O)	0/0
8	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	52.75	05/2012 -	08/2012	3(O)	0/0
9	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	324.99	06/2013 -	06/2013	0(O)	0/0
	Total		5,021.58 -	5,611.06	3,614.45				0/0
	<u>Coal</u>								
10	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC,Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,669.83	06/2009 -	12/2011	30(O)	24/26
11	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL,Orissa	01/2005	302.96 -	302.96	86.63	03/2010 -	03/2012	24(O)	9/11
12	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	1.51	03/2012 -	03/2012	0(O)	0/1
13	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08 -	172.08	95.91	- -	03/2012	-	4/4

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Orissa	08/2008	207.28 -	207.28	68.10	- -	03/2012	-	5/7
15	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	78.21	03/2012 -	03/2012	0(O)	21/27
16	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	21.20	03/2012 03/2012	03/2012	0(R3)	8/34
17	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,291.10	06/2009 -	07/2012	37(O)	19/24
18	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,225.93	- -	02/2013	-	0/23
19	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhandd	04/2006	471.66 341.63	341.63	101.43	03/2011 03/2012	03/2013	12(R3)	0/2
20	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Madhya pradesh	05/2006	789.88 -	741.62	288.78	03/2010 -	03/2013	36(O)	2/2
21	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65 -	1,188.31	569.86	- -	03/2013	-	0/8
22	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77 -	457.77	110.21	- -	03/2013	-	6/11
23	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93 -	479.63	76.95	- -	03/2013	-	5/7
24	Purnadih OCP - [N06000085]CCL,Jharkhandd	07/2008	210.98 -	210.98	24.25	03/2013 -	03/2013	0(O)	0/2
25	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	37.71	03/2014 -	11/2013	-4(O)	1/2
26	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	09/2006	212.34 779.26	779.26	201.30	03/2013 09/2012	12/2013	15(R3)	5/22
27	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL,Chhatisgarh	07/2005	1,667.55 -	2,675.67	1,279.57	03/2010 -	03/2014	48(O)	0/15
28	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL,Chhatisgarh	07/2005	1,268.53 -	1,943.66	1,109.47	03/2010 -	03/2014	48(O)	0/13
29	CHURCHA RO UG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	257.30	- -	03/2014	-	0/4
30	RAJMAHAL OC EXP. - [N06000056]ECL,Multi State	02/2006	50.08 153.82	153.82	19.74	03/2011 -	03/2014	36(O)	0/3
31	KARTALI (EAST) OCP(2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2014	0(O)	0/1
32	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42 -	321.50	203.23	- -	03/2014	-	0/5
33	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.57	03/2011 03/2012	03/2014	24(R3)	1/2
34	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.45	03/2012 03/2012	03/2014	24(R3)	0/2
35	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	76.05	03/2012 03/2013	03/2014	12(R3)	0/2

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	KARMA OCP - [N06000088]CCL,Jharkhandd	06/2009	162.46	162.46	26.36	03/2014	03/2014	0(O)	0/0
37	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77	339.77	0.65	-	10/2014	-	0/1
38	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04	535.10	140.21	03/2012	03/2015	36(O)	2/2
39	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18	287.17	-	03/2011	03/2015	48(O)	1/5
40	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	58.80	-	03/2015	-	2/12
41	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32	448.32	-	03/2015	03/2015	0(O)	0/1
42	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63	453.63	69.64	12/2012	03/2015	27(O)	7/44
43	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82	203.82	-	03/2015	03/2015	0(O)	0/1
44	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43	152.43	-	03/2015	03/2015	0(O)	1/1
45	RKP OCP PHASE-I - [N06000079]SCCL,Uttaranchal	03/2010	209.78	209.78	18.88	03/2015 03/2015	03/2015	0(R3)	4/31
46	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29	242.29	-	03/2015	03/2015	0(O)	0/28
47	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76	162.76	1.14	03/2015	03/2015	0(O)	0/0
48	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06	447.06	-	03/2015 03/2015	03/2015	0(R3)	0/0
49	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04	1,143.54	225.00	03/2014	03/2016	24(O)	2/2
50	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.21	07/2012 03/2014	03/2016	24(R3)	1/2
51	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.20	-	03/2016	-	1/12
52	AMLAI OC EXPANSION SECTOR 'B' (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	198.59	198.59	90.98	03/2016	03/2016	0(O)	0/1
53	Rajrappa RCE OCP - [N06000087]CCL,Jharkhandd	12/2009	510.85	510.85	290.44	03/2016	03/2016	0(O)	1/2
54	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	99.19	-	03/2017	-	6/12
55	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018	03/2018	0(O)	0/0
56	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03	249.03	40.95	03/2012 03/2012	-	-	11/42
57	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78	467.78	12.31	03/2013 03/2013	-	-	3/83
Total			27,241.47	30,628.50	12,120.25				152/542

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
Fertilisers									
58	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	195.63	- 11/2011	11/2011	0(R3)	6/22
59	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00	325.00	84.31	07/2011	11/2011	4(O)	0/0
60	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00	438.00	105.79	07/2011	03/2012	8(O)	0/0
61	PANIPAT - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJE - [N08000004]NFL,Haryana	01/2010	1,292.84	1,292.84	175.88	01/2013	01/2013	0(O)	0/5
62	BATHINDA - AMMONIA PLANT FEEDSTOCK CHANGE OVER PROJ - [N08000005]NFL,Punjab	01/2010	1,294.19	1,294.19	177.02	01/2013	01/2013	0(O)	0/5
63	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63	1,478.63	223.57	12/2012	01/2013	1(O)	8/8
Total			5,317.41	5,317.41	962.20				14/40
Mines									
64	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51 4,401.76	4,401.76	4,183.00	12/2008 01/2011	06/2011	5(R3)	98/110
Total			4,091.51	4,401.76	4,183.00				98/110
Steel									
65	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 232.93	232.93	168.44	05/2011 -	10/2011	5(O)	1/1
66	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 6,325.00	6,325.00	2,192.30	12/2011 12/2011	12/2011	0(R3)	8/11
67	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,	10/2007	500.90	500.90	326.23	- -	01/2012	-	3/3
68	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00	343.58	235.40	- 02/2011	01/2012	11(R3)	2/3
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00	350.00	223.06	- 08/2010	01/2012	17(R3)	1/2
70	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	311.45	- 12/2011	03/2012	3(R3)	15/21
71	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00	460.00	144.07	- 05/2012	05/2012	0(R3)	1/2
72	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	11,870.83	12/2011 12/2011	06/2012	6(R3)	12/14

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
73	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	8,911.27	10/2009 10/2012	10/2012	0(R3)	54/59
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 -	216.68	50.87	- 10/2012	10/2012	0(R3)	3/4
75	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,	06/2009	2,875.00 -	2,875.00	323.94	12/2012 -	12/2012	0(O)	3/6
76	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,	09/2008	11,812.00 -	11,812.00	5,551.34	03/2013 -	03/2013	0(O)	1/8
77	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 17,265.00	17,265.00	3,788.27	03/2013 03/2013	03/2013	0(R3)	14/20
78	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
79	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		64,990.27 -	71,157.81	34,097.47				118/154
Petrochemicals									
80	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	3,145.56	- 12/2013	04/2012	-20(R3)	0/30
	Total		5,460.61 -	8,920.00	3,145.56				0/30
Petroleum									
81	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	-	06/2010 -	09/2011	15(O)	0/0
82	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	528.92	03/2011 05/2011	06/2011	1(R3)	0/0
83	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
84	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
85	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	258.42	02/2011 08/2011	08/2011	0(R3)	0/0
86	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 -	2,340.00	2,273.78	10/2010 09/2011	09/2011	0(R2)	0/0
87	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
88	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
89	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0

Sector Wise Details

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL,Multi State	11/2007	1,816.07 -	1,385.00	998.86	10/2010 12/2011	12/2011	0(R3)	0/1
91	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL,Multi State	11/2007	1,167.00 -	798.00	647.70	04/2011 12/2011	12/2011	0(R3)	2/2
92	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]OCL,Gujarat	02/2009	250.00 349.00	250.00	207.27	03/2013 03/2013	12/2011	-15(R1)	0/0
93	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70 -	706.70	648.52	04/2010 -	12/2011	20(O)	0/0
94	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08 -	305.08	261.78	04/2011 -	12/2011	8(O)	0/0
95	EURO-IV DHDT - [N16000109]CPCL,Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,710.90	- -	12/2011	-	0/116
96	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]OCL,Gujarat	02/2009	267.00 -	267.00	181.30	09/2012 -	12/2011	-9(O)	0/0
97	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- [N16000070]GAIL,Multi State	07/2009	238.68 -	204.00	142.75	01/2012 -	01/2012	0(O)	3/8
98	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,080.12	01/2012 -	01/2012	0(O)	0/0
99	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21 -	162.12	71.60	03/2009 02/2012	02/2012	0(R3)	0/0
100	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
101	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	0(R3)	0/0
102	KOCHI-KOOTANAD BANGALORE-MANGALORE PIPELINE PROJEC - [N16000071]GAIL,Multi State	06/2009	348.00 -	261.00	173.40	03/2012 08/2012	03/2012	-5(R3)	1/12
103	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	6,652.22	0.26	01/2013 -	03/2012	-10(O)	0/0
104	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	160.47	06/2011 03/2012	03/2012	0(R3)	9/9
105	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00 -	616.00	-	03/2012 -	03/2012	0(O)	0/0
106	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
107	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC,Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,771.00	05/2010 05/2012	05/2012	0(R3)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC,Maharashtra	05/2008	333.40 837.54	656.51	49.20	05/2010 04/2012	05/2012	1(R3)	0/0
109	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	233.77	07/2010 05/2012	05/2012	0(R3)	0/0
110	CDU/VDU-II - [N16000110]CPCL,Tamil Nadu	03/2010	333.99 -	333.99	66.17	05/2012 -	05/2012	0(O)	18/36
111	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,802.20	08/2010 03/2012	06/2012	3(R3)	0/0
112	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 -	2,163.64	554.69	06/2012 -	06/2012	0(O)	0/0
113	INTEGRATED OFFSHORE CRUDE OIL HANDLING FACILITIES - [N16000090]OCL,Orissa	12/2009	1,492.33 -	1,492.33	701.91	06/2012 -	06/2012	0(O)	6/9
114	Wind Power Project - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
115	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC,Gujarat	02/2008	370.11 -	370.11	82.78	04/2011 -	07/2012	15(O)	0/0
116	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,Multi State	12/2009	540.92 -	460.70	164.83	06/2011 07/2012	07/2012	0(R2)	9/9
117	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	433.70	07/2012 -	07/2012	0(O)	0/0
118	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL,Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,335.32	03/2012 08/2012	08/2012	0(R3)	0/10
119	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	288.04	122.65	08/2012 -	08/2012	0(O)	0/0
120	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	2,442.94	09/2012 -	09/2012	0(O)	0/0
121	PARADIP-RAIPUR-SAMBALPUR-RANCHI PIPELINE - [N16000088]OCL,Multi State	08/2009	1,793.00 -	1,793.00	479.65	09/2012 -	09/2012	0(O)	0/15
122	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	302.26	21.14	09/2012 -	09/2012	0(O)	0/0
123	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	210.53	09/2011 -	12/2012	15(O)	0/0
124	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	84.18	12/2011 -	01/2013	13(O)	0/0
125	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	33.56	01/2013 -	01/2013	0(O)	12/18
126	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
127	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT - [N16000108]IOCL,Haryana	11/2009	341.50 -	341.50	24.86	02/2013 -	02/2013	0(O)	18/42
128	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	231.94	03/2006 03/2013	03/2013	0(R3)	6/6
129	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,767.62	05/2010 03/2013	03/2013	0(R3)	0/0
130	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	398.22	03/2013 -	03/2013	0(O)	0/0
131	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
132	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 -	3,241.03	1.50	03/2013 -	03/2013	0(O)	0/0
133	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0
134	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	-	10/2012 -	03/2013	5(O)	0/0
135	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	-	12/2011 04/2013	04/2013	0(R3)	202/203
136	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	861.79	-	05/2013 -	05/2013	0(O)	0/0
137	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	10,597.63	11/2012 -	06/2013	7(O)	0/100
138	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
139	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	13.77	12/2013 12/2013	12/2013	0(R3)	0/0
140	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
141	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O)	0/0
142	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	254.69	02/2014 -	02/2014	0(O)	0/0
143	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	592.78	03/2007 03/2014	03/2014	0(R3)	3/3
144	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	-	12/2014 -	12/2014	0(O)	0/0
145	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O)	0/0
146	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	-	04/2015 -	04/2015	0(O)	0/0
147	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,375.28	03/2007 03/2017	03/2017	0(R3)	6/6

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.29	10/2010 -	-	-	0/0
149	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	748.06	09/2011 03/2012	12/2011	-3(R3)	0/0
150	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	-	-	0/0
151	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	5.76	- -	-	-	0/0
Total			156,539.45 -	164,117.82	59,678.91				295/605
Power									
152	TRANSMISSION SYSTEM ASSOCIATEDWITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25 -	227.03	213.52	05/2011 05/2011	11/2011	6(R3)	0/0
153	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	4,978.56	2,987.90	07/2010 -	12/2011	17(O)	20/20
154	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	136.10	06/2010 -	12/2011	18(O)	0/0
155	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.37	300.13	07/2011 -	12/2011	5(O)	0/0
156	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,694.56	08/2010 -	02/2012	18(O)	0/0
157	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	1,724.79	1,575.98	11/2009 -	02/2012	27(O)	0/0
158	WESTERN REGION STRENGHTENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96 -	664.96	304.39	02/2012 -	02/2012	0(O)	0/0
159	WESTERN REGION SYSTEM STRENGHTENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50 -	409.50	60.03	02/2012 -	02/2012	0(O)	0/0
160	NORTHERN REGION SYSTEM STRENGHTENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	165.10	08/2011 -	02/2012	6(O)	0/0
161	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	213.40	07/2010 02/2012	02/2012	0(R3)	0/0
162	SYSTEM STRENGHTENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	86.60	07/2011 -	02/2012	7(O)	0/0
163	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32 -	1,347.32	888.20	02/2012 -	02/2012	0(O)	0/0
164	KOTESHWAR HEP (THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 2,283.69	2,283.69	2,524.97	04/2005 03/2012	03/2012	0(R3)	5/11

Sector Wise Details

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
165	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,431.00	12/2009	03/2012	27(O)	50/60
166	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,590.26	10/2010	03/2012	17(O)	0/0
167	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,483.30	09/2009	03/2012	30(O)	11/30
168	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	710.00	10/2009	03/2012	29(O)	20/20
169	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	703.42	02/2011	03/2012	13(O)	1/1
170	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	486.40	01/2010	03/2012	26(O)	0/22
171	SIMHADRI STPP STAGE -II - [N18000032]NTPC,Andhra Pradesh	08/2007	5,103.39	5,038.83	4,162.00	- 05/2011	03/2012	10(R3)	0/6
172	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	62.30	11/2011	03/2012	4(O)	0/0
173	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	101.30	04/2012	04/2012	0(O)	0/0
174	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,385.57	03/2007	05/2012	62(O)	25/25
175	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	351.80	05/2012	05/2012	0(O)	0/0
176	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	414.30	06/2012	06/2012	0(O)	0/0
177	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	121.30	06/2012	06/2012	0(O)	0/0
178	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	10.88	06/2012	06/2012	0(O)	0/0
179	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,722.70	08/2012	08/2012	0(O)	0/0
180	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	4,226.70	08/2012	08/2012	0(O)	0/0
181	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	451.10	08/2012	08/2012	0(O)	0/0
182	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,148.00	10/2012	10/2012	0(O)	0/0
183	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	197.70	10/2012	10/2012	0(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
184	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	13.70	10/2012 -	10/2012	0(O)	0/0
185	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	683.53	08/2010 -	11/2012	27(O)	0/0
186	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	353.10	11/2012 -	11/2012	0(O)	0/0
187	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	267.20	11/2012 -	11/2012	0(O)	0/0
188	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	124.00	11/2012 -	11/2012	0(O)	0/0
189	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	1,027.42	09/2009 -	12/2012	39(O)	0/0
190	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 -	1,946.85	1,745.38	11/2008 -	12/2012	49(O)	20/38
191	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10 -	2,895.10	685.00	11/2011 -	12/2012	13(O)	6/34
192	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	2,687.00	12/2012 -	12/2012	0(O)	0/0
193	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	266.43	11/2011 -	12/2012	13(O)	0/0
194	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	266.60	11/2011 -	12/2012	13(O)	0/0
195	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	144.50	02/2012 -	12/2012	10(O)	0/0
196	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	2,329.00	10/2012 -	12/2012	2(O)	2/15
197	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	2,152.00	10/2012 -	12/2012	2(O)	2/16
198	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	412.00	12/2012 -	12/2012	0(O)	0/0
199	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	2,988.00	08/2012 -	01/2013	5(O)	3/16
200	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	25.54	01/2013 -	01/2013	0(O)	0/0
201	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	22.90	01/2013 -	01/2013	0(O)	0/0

Sector Wise Details

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
202	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15 -	4,527.15	3,884.00	04/2009 -	03/2013	47(O)	0/9
203	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	831.16	12/2007 12/2009	03/2013	39(R3)	0/18
204	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	381.90	09/2010 -	03/2013	30(O)	0/0
205	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	171.60	03/2013 -	03/2013	0(O)	0/0
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	107.00	04/2013 -	04/2013	0(O)	0/0
207	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	8.71	04/2013 -	04/2013	0(O)	0/0
208	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	74.52	01/2012 07/2013	07/2013	0(R3)	0/0
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	83.30	07/2013 -	07/2013	0(O)	0/0
210	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
211	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhy Pradesh	07/2011	181.93 -	181.93	-	07/2013 -	07/2013	0(O)	0/0
212	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pr.	12/2008	573.99 573.99	573.99	232.22	08/2013 08/2013	08/2013	0(R3)	7/17
213	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21 -	779.21	116.00	08/2013 -	08/2013	0(O)	0/0
214	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78 -	209.78	18.55	08/2013 -	08/2013	0(O)	0/0
215	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	135.80	08/2013 -	08/2013	0(O)	0/0
216	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,399.75	01/2012 -	09/2013	20(O)	2/10
217	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	132.80	11/2011 -	09/2013	22(O)	0/0
218	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,447.00	06/2011 -	10/2013	28(O)	0/29
219	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	3,026.00	- 08/2013	10/2013	2(R3)	2/18

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
220	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL, Madhya Pradesh	08/2011	425.51 -	425.51	-	10/2013 -	10/2013	0(O)	0/0
221	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL, Multi State	03/2011	1,585.12 -	1,585.12	66.40	11/2013 -	11/2013	0(O)	0/0
222	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL, Jharkhand	10/2011	558.26 -	558.26	-	11/2013 -	11/2013	0(O)	0/0
223	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL, Multi State	08/2011	1,391.97 -	1,391.97	-	11/2013 -	11/2013	0(O)	0/0
224	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL, Orissa	12/2010	2,743.19 -	2,743.19	216.21	12/2013 -	12/2013	0(O)	0/0
225	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL, Multi State	09/2011	1,366.34 -	1,366.34	-	12/2013 -	12/2013	0(O)	0/0
226	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL, Chhattisgarh	08/2011	1,391.97 -	1,391.97	-	12/2013 -	12/2013	0(O)	0/0
227	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO, Mizoram	07/1998	368.72 913.63	913.63	268.89	07/2006 01/2014	01/2014	0(R3)	5/5
228	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL, Multi State	03/2011	2,569.25 -	2,569.25	52.50	03/2014 -	03/2014	0(O)	0/0
229	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL, Chhattisgarh	05/2011	1,961.87 -	1,961.87	31.00	05/2014 -	05/2014	0(O)	0/0
230	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC, Uttaranchal	11/2006	2,978.48 -	2,978.48	1,187.00	03/2013 -	06/2014	15(O)	1/13
231	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL, Multi State	10/2011	487.49 -	487.49	-	06/2014 -	06/2014	0(O)	0/0
232	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC, Arunachal Pr.	09/2003	6,285.33 -	6,285.33	5,184.46	09/2010 -	08/2014	47(O)	11/11
233	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL, Andhra Pradesh	08/2011	1,637.34 -	1,637.34	-	08/2014 -	08/2014	0(O)	0/0
234	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC, Bihar	12/2003	8,692.97 -	8,693.00	6,195.00	12/2009 -	09/2014	57(O)	45/70
235	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL, Multi State	02/2009	11,130.19 -	11,130.19	3,073.60	08/2013 -	09/2014	13(O)	0/0
236	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL, Tamil Nadu	09/2011	1,940.13 -	1,940.13	-	09/2014 -	09/2014	0(O)	0/0
237	PARBATI HEP (NHPC) II - [180100210]NHPC, Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,356.79	09/2009 -	12/2014	63(O)	1/20

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
238	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL, West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
239	KISHANGANGA HEP - [N18000031]NHPC, J & K	07/2007	2,238.67 3,642.04	3,642.04	999.75	07/2014 01/2016	01/2016	0(R3)	0/0
240	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,	07/2006	1,657.00 2,978.86	2,978.86	277.54	07/2010 02/2016	02/2016	0(R3)	0/10
241	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO, Arunachal Pr.	12/2004	2,496.90	2,496.90	1,626.70	05/2013 06/2016	06/2016	0(R3)	2/22
242	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL, Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	179.49	07/2014	07/2016	24(O)	4/7
243	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL, Multi State	04/2008	230.89	230.89	96.40	01/2011	-	-	0/1
Total			191,150.96	197,235.03	92,966.25				245/574
Railways									
244	RAJATGARH-BARANG(LD), ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	-	-	12/2010	22(R1)	0/0
245	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41 207.00	211.90	188.18	-	12/2010	21(R1)	0/0
246	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	221.90	161.07	12/2007 03/2010	12/2010	9(R1)	0/0
247	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73 399.73	399.50	295.24	03/2009 12/2008	12/2010	24(R1)	0/0
248	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSION - [N22000081]RVNL, Gujarat	09/2005	200.80	200.80	269.02	-	12/2010	-	0/0
249	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	273.00	-	-	03/2011	24(R1)	0/0
250	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	329.70	267.79	03/2009 12/2009	03/2011	15(R1)	0/0
251	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP, Maharashtra	04/2003	3,125.20 4,501.80	4,501.80	4,273.68	-	06/2011	6(R3)	1/1
252	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL, West Bengal	09/2007	252.50	252.50	-	02/2010	11/2011	21(O)	0/0
253	GUNA-ETAWAH(NCR), NL - [220100007]NCR, Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994	12/2011	213(O)	0/0
254	LANJHIGARH-JUNAGARH NL (ECOR) - [220100148]ECOR, Orissa	04/1993	100.00 142.90	208.68	187.44	03/2002	12/2011	117(O)	0/0
255	NANDYAL-YERRAGUNTALA(NL), SCR - [220100192]SCR, Andhra Pradesh	03/1996	155.74 164.36	843.91	492.29	02/2009	12/2011	34(O)	0/0
256	KHURDA ROAD-BOLANGIR(NL) ECOR - [220100284]ECOR, Orissa	04/1994	355.38 470.21	1,100.00	176.85	-	12/2011	-	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
257	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
258	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 -	482.70	250.13	03/2013 -	12/2011	-15(O)	0/0
259	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,190.60	- -	02/2012	-	0/0
260	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	424.94	- 12/2009	02/2012	26(R1)	0/0
261	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	66.31	12/2011 -	02/2012	2(O)	0/0
262	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	542.82	03/1995 -	03/2012	204(O)	0/0
263	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	512.65	- -	03/2012	-	0/0
264	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 254.07	675.00	466.87	- 12/2011	03/2012	3(R3)	0/0
265	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	208.83	- 03/2012	03/2012	0(R3)	0/0
266	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	422.17	- -	03/2012	-	0/0
267	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	565.87	- -	03/2012	-	0/0
268	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	340.51	- 03/2011	03/2012	12(R3)	0/0
269	HARNOUT - SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
270	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0
271	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	188.15	03/2010 -	03/2012	24(O)	0/0
272	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	202.04	- -	03/2012	-	0/0
273	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	137.47	03/2012 -	03/2012	0(O)	0/0
274	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	218.15	03/2011 -	03/2012	12(O)	0/0
275	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	383.13	06/2005 07/2011	03/2012	8(R3)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
276	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 -	167.73	36.32	03/2012 -	03/2012	0(O)	0/0
277	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	146.26	03/2007 03/2007	06/2012	63(R1)	0/0
278	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	326.92	- 07/2012	07/2012	0(R3)	0/0
279	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	579.88	- -	12/2012	-	0/0
280	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	789.49	12/2012 -	12/2012	0(O)	0/0
281	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	396.24	03/2005 12/2008	12/2012	48(R1)	0/0
282	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	338.99	- 03/2012	12/2012	9(R3)	0/0
283	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	241.91	- -	12/2012	-	0/0
284	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	556.03	03/2009 -	12/2012	45(O)	0/0
285	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	1,013.11	10/2007 -	12/2012	62(O)	0/0
286	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	400.42	03/2010 -	12/2012	33(O)	0/0
287	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	105.98	12/2012 -	12/2012	0(O)	0/0
288	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	152.76	- -	03/2013	-	0/0
289	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	697.02	- -	03/2013	-	0/0
290	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	48.10	03/2012 -	03/2013	12(O)	0/0
291	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O)	0/0
292	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	135.28	- 06/2013	06/2013	0(R3)	0/0
293	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	64.10	12/2011 -	11/2013	23(O)	0/0
294	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	180.24	- -	12/2013	-	0/0
295	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	83.63	12/2012 -	12/2013	12(O)	0/0
296	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,820.12	03/2009 -	12/2013	57(O)	0/0
297	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	834.94	12/2008 -	03/2014	63(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
298	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70	1,717.29	771.94	-	03/2014	-	0/0
299	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34	1,141.75	217.04	03/2014	03/2014	0(O)	0/0
300	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	2,393.49	3.61	04/2014	03/2014	-1(O)	0/0
301	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19	653.19	9.50	03/2014	03/2014	0(O)	0/0
302	Suratpura - Hanumangarh - Sriganaganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23	516.23	80.97	03/2014	03/2014	0(O)	0/0
303	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62	1,389.62	195.64	03/2014	03/2014	0(O)	0/0
304	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00	369.90	107.60	03/2010 06/2014	06/2014	0(R3)	0/0
305	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,240.65	04/2008 03/2014	12/2014	9(R3)	0/0
306	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66	324.66	168.07	-	03/2015	-	0/0
307	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00	5,300.00	315.09	03/2014	03/2015	12(O)	0/0
308	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74	829.74	-	03/2015	03/2015	0(O)	0/0
309	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00	850.00	8.44	03/2015	03/2015	0(O)	0/0
310	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	3,380.57	52.63	12/2015	12/2015	0(O)	0/0
311	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	493.47	03/2011 03/2014	03/2016	24(R3)	0/0
312	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60	2,069.60	-	03/2014	03/2016	24(O)	0/0
313	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98	3,951.98	-	03/2016	03/2016	0(O)	0/0
314	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02	2,619.02	-	03/2016	03/2016	0(O)	0/0
315	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	2,397.72	0.02	03/2016	06/2016	3(O)	0/0
316	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,326.12	03/2001	12/2017	201(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
317	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	356.87	149.70	- 03/2010	-	-	0/0
318	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.70	- -	-	-	0/0
319	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	87.11	12/2012 -	-	-	0/0
320	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	595.36	- -	-	-	0/0
321	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	99.45	- -	-	-	0/0
322	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 -	944.55	478.17	- -	-	-	0/0
323	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 -	1,038.00	570.21	03/1998 -	-	-	0/0
324	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 -	945.73	622.93	- -	-	-	0/0
325	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00 -	997.58	65.16	- -	-	-	0/0
326	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	93.80	- -	-	-	0/0
327	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 -	363.26	0.27	07/2008 -	-	-	0/0
328	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 1,099.20	1,099.20	1,113.09	07/2005 -	-	-	0/0
329	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 -	1,214.00	70.88	- -	-	-	0/0
330	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	269.00	- 05/2009	-	-	0/0
331	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 -	162.87	87.26	- -	-	-	0/0
332	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	815.43	06/2007 -	-	-	0/0
333	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34 -	296.20	307.08	04/2003 03/2010	-	-	0/0
334	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 -	548.96	476.32	- -	-	-	0/0
335	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
336	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	338.76	- 12/2012	-	-	0/0
337	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
338	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91 -	418.17	77.24	- -	-	-	0/0
339	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	210.90	- -	-	-	0/0
340	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61 -	227.52	258.96	03/2008 03/2009	-	-	0/0
341	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94 -	173.49	176.57	03/1998 08/2005	-	-	0/0
342	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0
343	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
344	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	261.70	24.65	02/2006 -	-	-	0/0
345	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	315.49	03/2008 06/2008	-	-	0/0
346	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' -A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	211.41	- -	-	-	0/0
347	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	443.75	- -	-	-	0/0
348	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	22.66	- -	-	-	0/0
349	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	89.12	- -	-	-	0/0
350	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	35.45	- -	-	-	0/0
351	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	178.19	03/2011 -	-	-	0/0
352	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
353	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	171.36	03/2011 -	-	-	0/0
354	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	466.60	06/1999 03/2011	-	-	0/0
355	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	167.16	03/2004 -	-	-	0/0
356	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	329.27	- 03/2011	-	-	0/0
357	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	289.43	06/2004 04/2005	-	-	0/0
358	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0

Sector Wise Details

(Oct,2011)

						Date of Commissioning		Delay w.r.t. Original /Revised (in months)	Milestones Achieved/ Total
S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
359	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
360	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.94	- 12/2010	-	-	0/0
361	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	436.49	- -	-	-	0/0
362	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	451.09	- -	-	-	1/1
363	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,076.13	12/2006 08/2010	-	-	0/0
364	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	270.00	236.09	- 02/2011	-	-	0/0
365	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	471.11	02/2010 02/2011	-	-	0/0
366	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	375.49	- -	-	-	0/0
367	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	236.84	- 03/2011	-	-	0/0
368	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	134.12	- -	-	-	0/0
369	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	134.90	- -	-	-	0/0
370	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	85.45	- -	-	-	0/0
371	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	365.15	- 03/2011	-	-	0/0
372	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.90	- -	-	-	0/0
373	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	167.66	12/2010 03/2011	-	-	0/0
374	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	130.29	- 12/2010	-	-	0/0
375	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	2.29	03/2012 -	-	-	0/0
Total			65,054.74 -	132,203.07	53,868.82				
<u>Road Transport & Highways</u>									
376	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	200.40	10/2011 -	10/2011	0(O)	0/0
377	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	11/2011	12(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
378	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI, Madhya Pradesh	12/2003	225.00 -	225.00	257.50	10/2008 -	11/2011	37(O)	0/0
379	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI, Bihar	12/2003	340.00 -	340.00	570.00	06/2008 -	11/2011	41(O)	0/0
380	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI, Kerala	12/2003	312.50 -	312.50	604.40	03/2009 -	11/2011	32(O)	0/0
381	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI, Uttar Pradesh	12/2003	276.09 -	276.09	295.30	09/2009 -	11/2011	26(O)	0/0
382	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI, Tamil Nadu	03/2005	576.00 -	576.00	658.90	07/2010 -	11/2011	16(O)	0/0
383	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI, Tamil Nadu	03/2005	285.00 -	285.00	359.30	07/2010 -	11/2011	16(O)	0/0
384	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	159.45	08/2004 07/2010	12/2011	17(R3)	0/0
385	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	167.70	08/2004 -	12/2011	88(O)	0/0
386	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Orissa	04/2000	225.00 -	241.53	82.01	04/2004 -	12/2011	92(O)	0/0
387	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI, Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2011	81(O)	0/0
388	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI, West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	12/2011	81(O)	0/0
389	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI, Uttar Pradesh	12/2003	275.00 -	275.00	298.70	09/2007 -	12/2011	51(O)	0/0
390	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	252.00	09/2007 -	12/2011	51(O)	0/0
391	GAGODHAR-GARAMORE(PK-IV, NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI, Gujarat	12/2003	412.78 -	479.54	436.90	11/2007 -	12/2011	49(O)	0/0
392	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI, Assam	12/2003	230.00 -	230.00	207.80	06/2005 -	12/2011	78(O)	0/0
393	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI, J & K	12/2003	193.09 -	166.30	183.90	03/2008 -	12/2011	45(O)	0/0
394	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27 -	193.10	153.70	03/2008 -	12/2011	45(O)	0/0
395	GORAKHPUR-AYODHYA (LMNHP-5), NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	403.50	10/2008 -	12/2011	38(O)	0/0
396	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	12/2011	35(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
397	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	228.90	02/2009 -	12/2011	34(O)	0/0
398	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	82.02	04/2009 -	12/2011	32(O)	0/0
399	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	174.80	06/2008 -	12/2011	42(O)	0/0
400	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00 -	242.00	427.20	12/2008 -	12/2011	36(O)	0/0
401	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	369.10	12/2008 -	12/2011	36(O)	0/0
402	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	204.70	06/2008 -	12/2011	42(O)	0/0
403	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	277.40	10/2008 -	12/2011	38(O)	0/0
404	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya pradesh	12/2003	198.00 -	198.00	187.30	11/2008 -	12/2011	37(O)	0/0
405	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	174.00	10/2008 -	12/2011	38(O)	0/0
406	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03 -	251.03	283.20	10/2008 -	12/2011	38(O)	0/0
407	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91 -	229.91	226.80	10/2008 -	12/2011	38(O)	0/0
408	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	447.70	09/2008 -	12/2011	39(O)	0/0
409	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	257.90	06/2008 -	12/2011	42(O)	0/0
410	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00 -	322.00	553.70	06/2009 -	12/2011	30(O)	0/0
411	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 -	196.50	236.60	06/2008 -	12/2011	42(O)	0/0
412	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	255.10	06/2008 -	12/2011	42(O)	0/0
413	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	486.20	03/2008 -	12/2011	45(O)	0/0
414	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	173.80	06/2008 -	12/2011	42(O)	0/0
415	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	212.80	04/2008 -	12/2011	44(O)	0/0
416	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI, Assam	12/2003	160.00 -	160.00	126.20	05/2008 -	12/2011	43(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
417	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI, Assam	12/2003	200.00	200.00	195.60	06/2008	12/2011	42(O)	0/0
418	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI, Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30(O)	0/0
419	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI, Uttar Pradesh	12/2003	600.24	600.24	707.10	10/2009	12/2011	26(O)	0/0
420	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI, Bihar	12/2003	418.04	418.04	328.70	03/2010	12/2011	21(O)	0/0
421	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI, Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
422	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI, Karnataka	03/2005	441.00	441.00	929.00	07/2010	12/2011	17(O)	0/0
423	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI, Punjab	12/2003	229.00	284.00	344.80	05/2010	12/2011	19(O)	0/0
424	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70	228.70	173.06	02/2004	12/2011	94(O)	0/0
425	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16(O)	0/0
426	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00	464.00	420.00	01/2011	12/2011	11(O)	0/0
427	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00	486.00	558.60	05/2010	12/2011	19(O)	0/0
428	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75	1,693.75	2,603.00	08/2011	12/2011	4(O)	0/0
429	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82	221.82	250.30	11/2008	01/2012	38(O)	0/0
430	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00	168.00	385.30	12/2008	01/2012	37(O)	0/0
431	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06	355.06	294.70	09/2009	02/2012	29(O)	0/0
432	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56	390.56	511.40	02/2012	02/2012	0(O)	0/0
433	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47	154.57	180.40	09/2007	03/2012	54(O)	0/0
434	KOTWA TO DEWAPUR (10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00	240.00	274.90	10/2008	03/2012	41(O)	0/0
435	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68	340.68	357.70	03/2008	03/2012	48(O)	0/0
436	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00	225.00	257.60	06/2008	03/2012	45(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
437	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	332.94	297.30	09/2008	03/2012	42(O)	0/0
438	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43	203.43	208.20	10/2008	03/2012	41(O)	0/0
439	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96	175.96	120.70	04/2008	03/2012	47(O)	0/0
440	GUWHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16	198.16	180.20	04/2008	03/2012	47(O)	0/0
441	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61	217.61	154.00	04/2010	03/2012	23(O)	0/0
442	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00	516.00	594.20	07/2010	05/2012	22(O)	0/0
443	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00	557.00	930.90	02/2010	05/2012	27(O)	0/0
444	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00	1,110.00	1,802.00	05/2012	05/2012	0(O)	0/0
445	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	804.30	05/2012	05/2012	0(O)	0/0
446	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	372.30	05/2012	05/2012	0(O)	0/0
447	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	90.44	09/2008	06/2012	45(O)	0/0
448	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.10	10/2008	06/2012	44(O)	0/0
449	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
450	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.70	12/2009	06/2012	30(O)	0/0
451	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	168.20	09/2010	06/2012	21(O)	0/0
452	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	396.70	06/2012	06/2012	0(O)	0/0
453	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8(O)	0/0
454	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,691.00	11/2011	06/2012	7(O)	0/0
455	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-II) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	328.20	07/2012	07/2012	0(O)	0/0
456	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	132.20	05/2008	08/2012	51(O)	0/0
457	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	510.50	10/2011	08/2012	10(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
458	Gujarat/Maharashtra Border Surat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	827.30	09/2012	09/2012	0(O)	0/0
459	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya Pradesh	12/2003	407.60	407.60	184.60	06/2010	10/2012	28(O)	0/0
460	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya Pradesh	12/2003	263.17	263.17	233.40	09/2009	10/2012	37(O)	0/0
461	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
462	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,060.00	10/2012	10/2012	0(O)	0/0
463	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
464	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0
465	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00	225.00	177.40	07/2008	12/2012	53(O)	0/0
466	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27	263.27	254.69	02/2004	12/2012	106(O)	0/0
467	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06	792.06	390.20	12/2012	12/2012	0(O)	0/0
468	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0
469	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30	671.30	116.90	02/2013	02/2013	0(O)	0/0
470	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00	748.00	1,114.00	09/2010	03/2013	30(O)	0/0
471	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00	946.00	778.50	03/2013	03/2013	0(O)	0/0
472	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	852.00	354.00	03/2013	03/2013	0(O)	0/0
473	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
474	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
475	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39	805.39	7.75	03/2013	03/2013	0(O)	0/0
476	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya Pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
477	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	1,585.00	251.90	05/2013	05/2013	0(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
478	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00	453.00	140.60	05/2013	05/2013	0(O)	0/0
479	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
480	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54	351.54	3.12	05/2013	05/2013	0(O)	0/0
481	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00	374.00	21.49	05/2013	05/2013	0(O)	0/0
482	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16	348.16	118.00	09/2007	06/2013	69(O)	0/0
483	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
484	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
485	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0
486	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50	1,008.50	596.90	06/2013	06/2013	0(O)	0/0
487	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00	600.00	72.15	06/2013	06/2013	0(O)	0/0
488	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81	385.13	31.92	04/2009	07/2013	51(O)	0/0
489	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
490	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41(O)	0/0
491	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	953.00	593.00	71.18	07/2013	07/2013	0(O)	0/0
492	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,J & K	07/2010	1,813.76	1,813.76	-	07/2013	07/2013	0(O)	0/0
493	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88	953.88	23.41	07/2013	07/2013	0(O)	0/0
494	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
495	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50	785.50	335.00	08/2013	08/2013	0(O)	0/0
496	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00	1,141.00	182.50	08/2013	08/2013	0(O)	0/0
497	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00	485.00	-	08/2013	08/2013	0(O)	0/0
498	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00	1,655.00	4.71	09/2013	09/2013	0(O)	0/0
499	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00	359.00	12.40	09/2013	09/2013	0(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
500	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
501	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
502	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00	567.00	179.60	11/2013	11/2013	0(O)	0/0
503	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0
504	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	511.54	40.39	11/2013	11/2013	0(O)	0/0
505	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
506	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
507	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
508	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00	386.10	1.76	09/2007	04/2014	79(O)	0/0
509	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00	363.74	0.34	07/2009	04/2014	57(O)	0/0
510	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
511	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00	807.00	455.70	10/2014	10/2014	0(O)	0/0
512	NASHRI CHANANI - [N24000162]NHAI,J & K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
513	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,J & K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
	Total		76,162.26	77,967.51	47,366.19				0/0
Shipping & Ports									
514	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	294.09	04/2009	02/2011	22(O)	0/0
515	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
516	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
517	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	241.50	48.10	09/2011	09/2011	0(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
518	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	124.37	12/2005 01/2008	10/2011	45(R3)	0/0
519	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.79	04/2011 06/2011	11/2011	5(R3)	0/0
520	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
521	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP.,Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	680.53	03/2012 -	03/2012	0(O)	0/0
522	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2(O)	0/0
523	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.04	03/2012 -	03/2012	0(O)	0/0
524	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	0(R3)	0/0
525	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	610.00	12/2010 -	09/2012	21(O)	0/0
526	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
527	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
528	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	83.51	12/2012 -	12/2012	0(O)	0/0
529	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
530	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
531	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
532	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
533	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
534	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
535	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
536	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
537	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
538	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.48	10/2008 -	-	-	0/0
Total			18,052.23 -	19,035.72	4,314.55				0/0
<u>Telecommunications</u>									
539	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N260000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	299.77	09/2009 -	02/2010	5(O)	0/0
540	Implementation of FTTH, the state of the art access ,gpon eq - [N260000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
541	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N260000040]BSNL,Haryana	01/2008	192.48 -	192.48	119.45	03/2009 -	02/2011	23(O)	0/0
542	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N260000041]BSNL,Punjab	02/2008	373.94 -	373.94	209.79	12/2008 -	02/2011	26(O)	0/0
543	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N260000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
544	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N260000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	02/2011	20(O)	0/0
545	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N260000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
546	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N260000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.39	10/2008 -	02/2011	28(O)	0/0
547	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N260000091]BSNL,Tamil Nadu	01/2009	760.20 -	1,100.00	815.00	- 03/2011	02/2011	-1(R3)	0/1
548	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N260000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	02/2011	13(O)	0/0
549	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N260000094]BSNL,Kerala	01/2009	848.70 -	848.70	712.86	01/2010 -	02/2011	13(O)	0/0
550	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N260000095]BSNL,Tamil Nadu	01/2009	315.19 -	315.19	142.07	01/2010 -	02/2011	13(O)	0/0

Sector Wise Details

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
551	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49 -	601.49	496.20	12/2008 -	03/2011	27(O)	0/0
552	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	335.91	182.45	03/2009 -	03/2011	24(O)	0/0
553	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49 -	241.49	123.76	09/2009 -	03/2011	18(O)	0/0
554	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	17(O)	0/0
555	GSM equipment of 849862Lines (2G) 150138 lines 3(G - [N26000087]BSNL,West Bengal	02/2008	584.33 -	584.33	403.71	02/2009 -	03/2011	25(O)	0/0
556	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	362.62	08/2009 -	03/2011	19(O)	0/0
557	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	280.72	11/2010 -	03/2011	4(O)	0/0
558	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	461.56	10/2009 -	03/2011	17(O)	0/0
559	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
560	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
561	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
562	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	141.31	12/2005 -	12/2011	72(O)	0/0
563	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	23.30	10/2010 -	03/2012	17(O)	0/0
564	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0
565	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00 -	350.00	-	- -	-	-	0/0
566	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00 -	1,077.00	-	03/2009 -	-	-	0/0
567	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00 -	424.00	-	03/2009 -	-	-	0/0
568	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10 -	590.10	-	03/2009 -	-	-	0/0

Sector Wise Details

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original / Revised (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
569	Procurement of 10G 40 CHL (12 chi equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50 -	545.50	-	03/2010 -	-	-	0/0
570	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03 -	154.03	-	03/2010 -	-	-	0/0
571	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92 -	355.92	-	03/2010 -	-	-	0/0
572	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00 -	477.00	-	03/2010 -	-	-	0/0
573	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
574	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00 -	229.00	-	03/2010 -	-	-	0/0
575	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53 -	625.53	-	02/2010 -	-	-	0/0
576	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75 -	624.75	-	09/2010 -	-	-	0/0
577	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23 -	170.23	-	06/2009 -	-	-	0/0
578	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13 -	328.12	164.58	03/2009 -	-	-	0/0
Total			19,713.13 -	20,297.68	6,234.73				0/1
<u>Urban Development</u>									
579	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24(O)	6/6
580	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	-	09/2014 -	09/2014	0(O)	0/0
581	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	42.15	03/2016 -	03/2016	0(O)	0/0
582	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
Total			44,245.18 -	49,518.08	2,309.72				6/6
<u>Water Resources</u>									
583	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60(O)	0/0
Total			542.90 -	1,187.00	35.49				0/0
Grand Total			712,811.99	821,664.74	344,360.76				995/2334

Sector wise current status of projects on theFlash Report

Telecommunications

I. Current Status:


Number of Projects **40**

Number of Projects Delayed **2**

Number of Projects Without Date Of Commissioning **38**

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 40 projects, 2 projects are delayed .38 projects do not have fixed dates of commissioning.

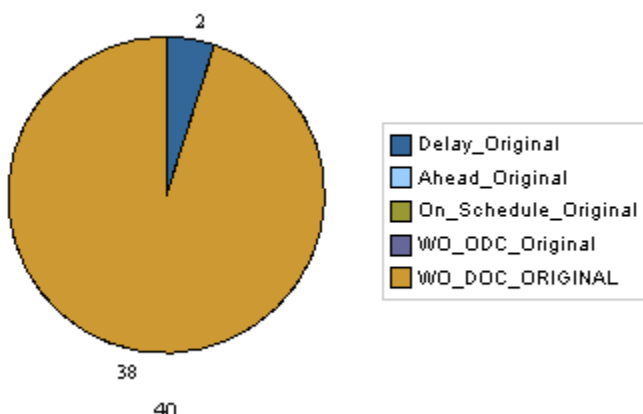

III. Investment Scenario

The Total Original cost of implementation of 40 projects when sanctioned, was of the order of Rs. 19713.13 crore but this was subsequently revised to Rs. 20297.68 crore implying a cost overrun of 3%. The expenditure incurred on these projects till October, 2011 is Rs. 6234.73 crore, which is 30.7% of the revised cost of the projects.

Figures are in Rs. Crore

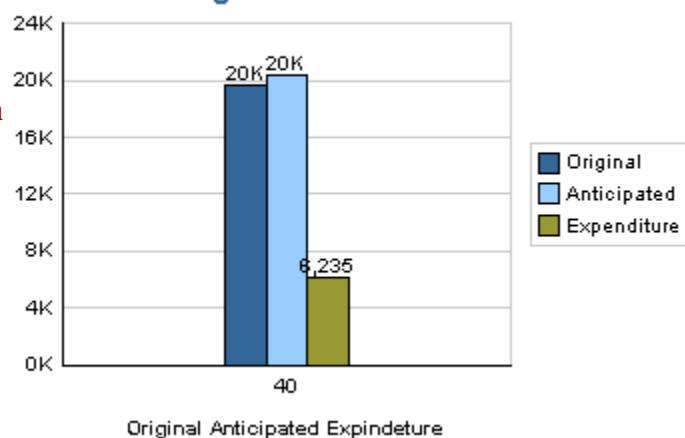

Sector wise current status of projects on theFlash Report

Shipping & Ports


I. Current Status:

Number of Projects	25
Number of Projects On Schedule	6
Number of Projects Delayed	11

Number of Projects Without Date Of Commissioning	8
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 25 projects, 6 projects are on schedule and 11 projects are delayed .8 projects do not have fixed dates of commissioning.

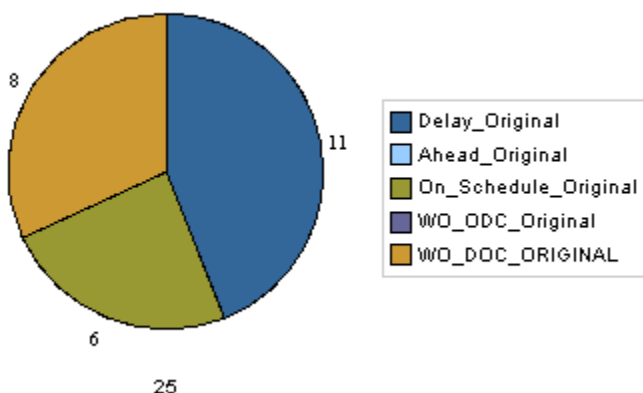

III. Investment Scenario

The Total Original cost of implementation of 25 projects when sanctioned, was of the order of Rs. 18052.23 crore but this was subsequently revised to Rs. 19035.72 crore implying a cost overrun of 5.4%. The expenditure incurred on these projects till October, 2011 is Rs. 4314.55 crore, which is 22.7% of the revised cost of the projects.

Figures are in Rs. Crore

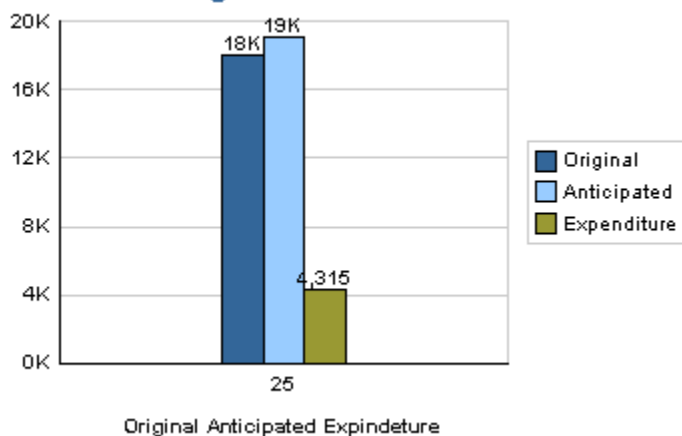

Sector wise current status of projects on theFlash Report


Road Transport & Highways

I. Current Status:

Number of Projects	138
Number of Projects On Schedule	48
Number of Projects Delayed	90

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 138 projects, 48 projects are on schedule and 90 projects are delayed .

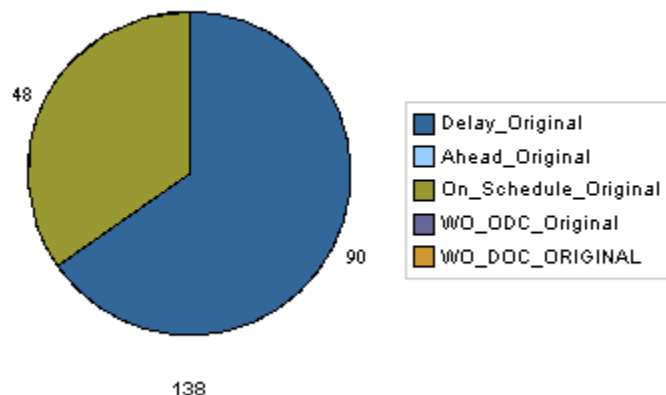

III. Investment Scenario

The Total Original cost of implementation of 138 projects when sanctioned, was of the order of Rs. 76162.26 crore but this was subsequently revised to Rs. 77967.51 crore implying a cost overrun of 2.4%. The expenditure incurred on these projects till October, 2011 is Rs. 47366.19 crore, which is 60.8% of the revised cost of the projects.

Figures are in Rs. Crore

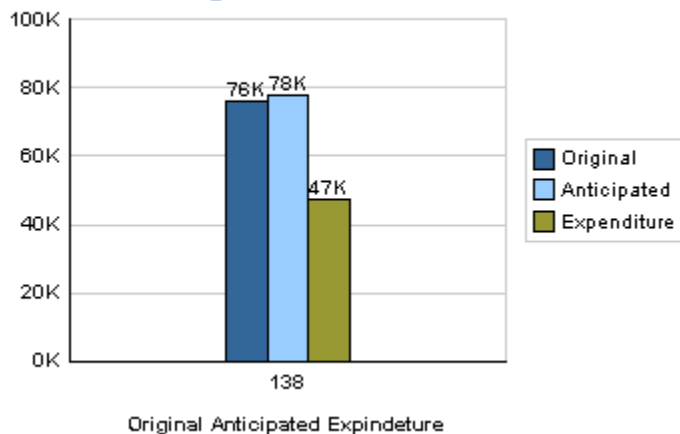

Sector wise current status of projects on theFlash Report


Railways

I. Current Status:

Number of Projects	132
Number of Projects On Schedule	14
Number of Projects Delayed	26
Number of Projects Ahead	2
Number of Projects Without Original Date of Commissioning	24
Number of Projects Without Date Of Commissioning	66

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 132 projects, 2 projects are ahead of schedule, 14 projects are on schedule and 26 projects are delayed. 66 projects do not have fixed dates of commissioning. 24 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

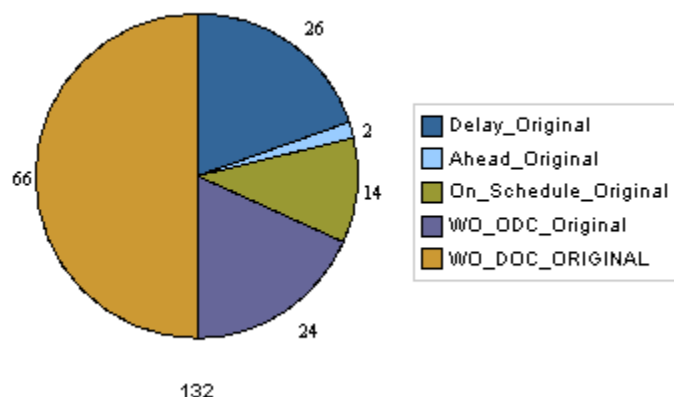

III. Investment Scenario

The Total Original cost of implementation of 132 projects when sanctioned, was of the order of Rs. 65054.74 crore but this was subsequently revised to Rs. 132203.07 crore implying a cost overrun of 103.2%. The expenditure incurred on these projects till October, 2011 is Rs. 53868.82 crore, which is 40.7% of the revised cost of the projects.

Figures are in Rs. Crore

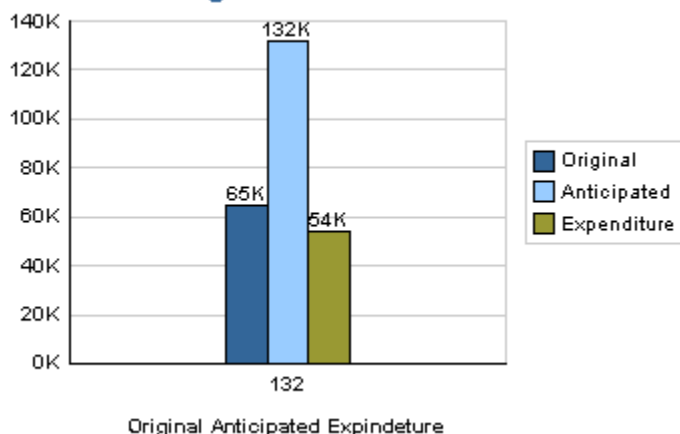

Sector wise current status of projects on theFlash Report


Power

I. Current Status:

Number of Projects	92
Number of Projects On Schedule	43
Number of Projects Delayed	45
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 92 projects, 1 project are ahead of schedule, 43 projects are on schedule and 45 projects are delayed .1 project do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

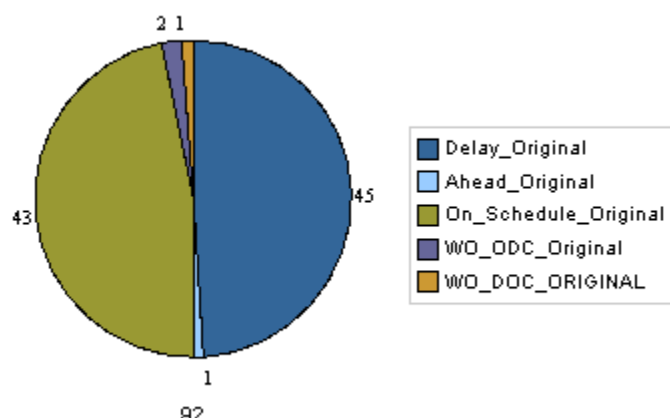

III. Investment Scenario

The Total Original cost of implementation of 92 projects when sanctioned, was of the order of Rs. 191150.96 crore but this was subsequently revised to Rs. 197235.03 crore implying a cost overrun of 3.2%. The expenditure incurred on these projects till October, 2011 is Rs. 92966.25 crore, which is 47.1% of the revised cost of the projects.

Figures are in Rs. Crore

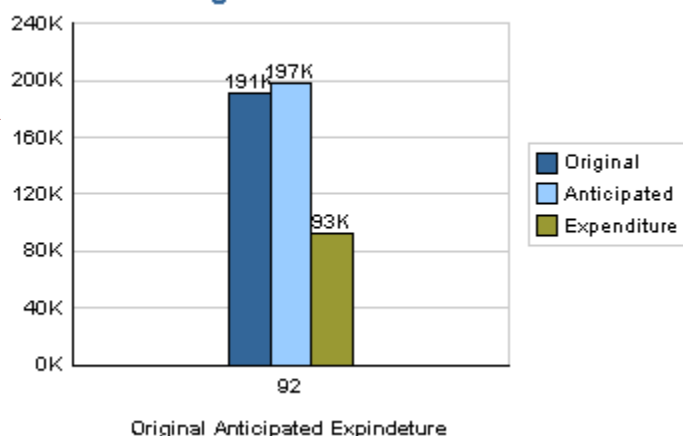

Sector wise current status of projects on theFlash Report


Petroleum

I. Current Status:

Number of Projects	71
Number of Projects On Schedule	28
Number of Projects Delayed	29
Number of Projects Ahead	3
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	10

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 71 projects, 3 projects are ahead of schedule, 28 projects are on schedule and 29 projects are delayed .10 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

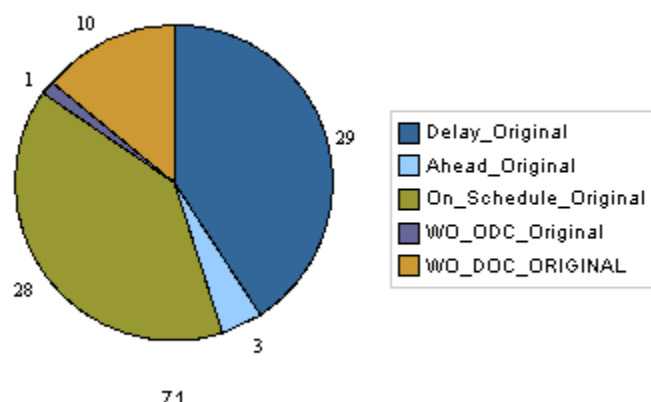

III. Investment Scenario

The Total Original cost of implementation of 71 projects when sanctioned, was of the order of Rs. 156539.45 crore but this was subsequently revised to Rs. 164117.82 crore implying a cost overrun of 4.8%. The expenditure incurred on these projects till October, 2011 is Rs. 59678.91 crore, which is 36.4% of the revised cost of the projects.

Figures are in Rs. Crore

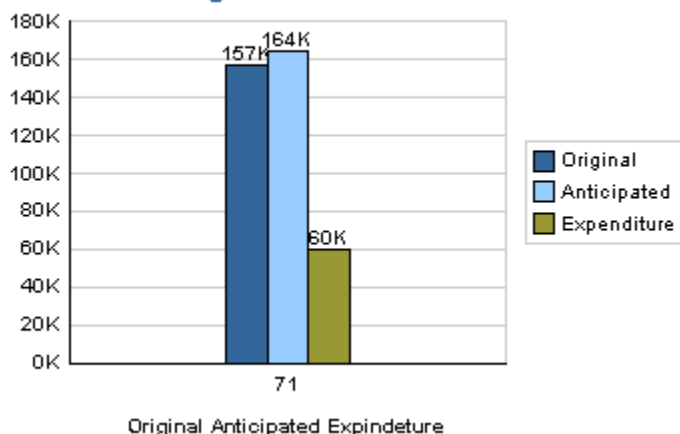

Sector wise current status of projects on theFlash Report

Steel


I. Current Status:

Number of Projects	15
Number of Projects On Schedule	6
Number of Projects Delayed	3

Number of Projects Without Original Date of Commissioning	6
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 15 projects, 6 projects are on schedule and 3 projects are delayed .6 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

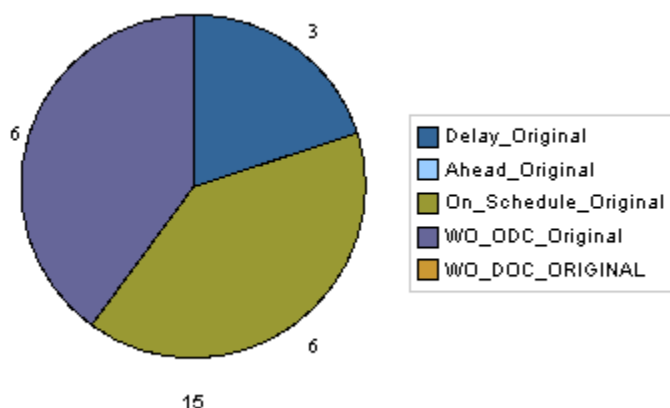

III. Investment Scenario

The Total Original cost of implementation of 15 projects when sanctioned, was of the order of Rs. 64990.27 crore but this was subsequently revised to Rs. 71157.81 crore implying a cost overrun of 9.5%. The expenditure incurred on these projects till October, 2011 is Rs. 34097.47 crore, which is 47.9% of the revised cost of the projects.

Figures are in Rs. Crore

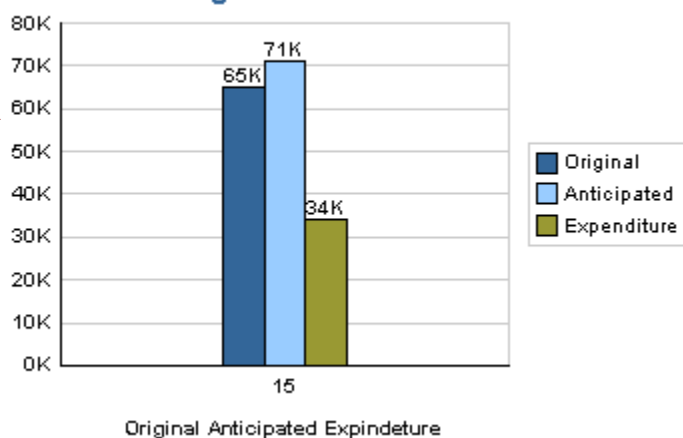

Sector wise current status of projects on theFlash Report

Fertilisers


I. Current Status:

Number of Projects	6
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Original Date of Commissioning	1
---	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 6 projects, 2 projects are on schedule and 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

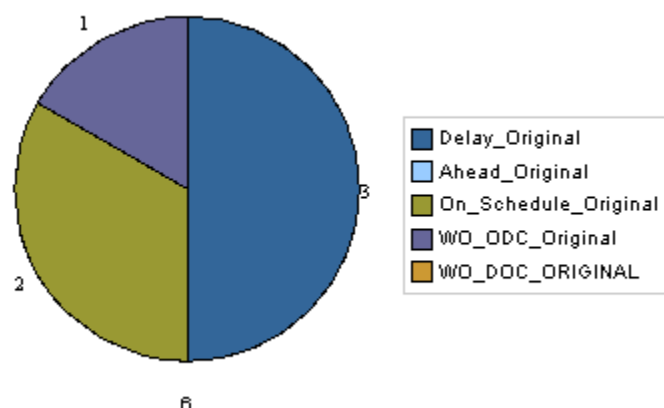

III. Investment Scenario

The Total Original cost of implementation of 6 projects when sanctioned, was of the order of Rs. 5317.41 crore but this was subsequently revised to Rs. 5317.41 crore implying a cost overrun of 0%. The expenditure incurred on these projects till October, 2011 is Rs. 962.2 crore, which is 18.1% of the revised cost of the projects.

Figures are in Rs. Crore

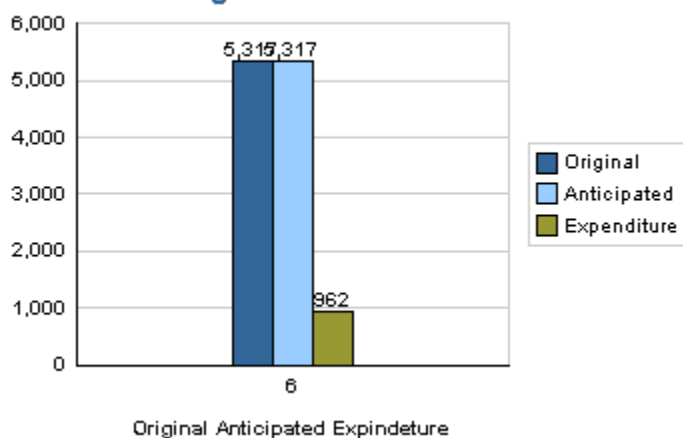

Sector wise current status of projects on theFlash Report


Coal

I. Current Status:

Number of Projects	48
Number of Projects On Schedule	16
Number of Projects Delayed	17
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	12
Number of Projects Without Date Of Commissioning	2

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 48 projects, 1 project are ahead of schedule, 16 projects are on schedule and 17 projects are delayed. 2 projects do not have fixed dates of commissioning. 12 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

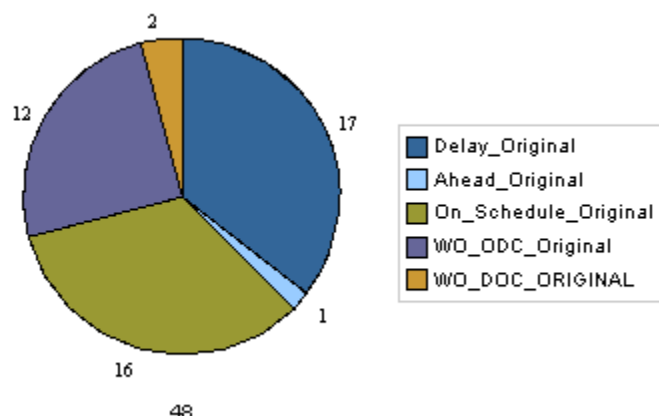

III. Investment Scenario

The Total Original cost of implementation of 48 projects when sanctioned, was of the order of Rs. 27241.47 crore but this was subsequently revised to Rs. 30628.5 crore implying a cost overrun of 12.4%. The expenditure incurred on these projects till October, 2011 is Rs. 12120.25 crore, which is 39.6% of the revised cost of the projects.

Figures are in Rs. Crore

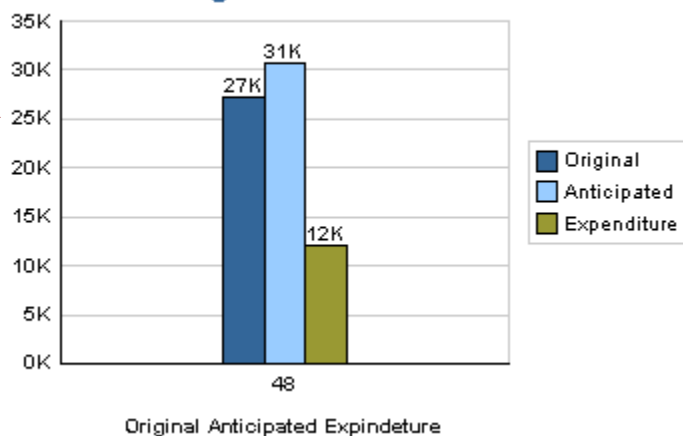

Sector wise current status of projects on theFlash Report


Civil Aviation

I. Current Status:

Number of Projects	5
Number of Projects On Schedule	1
Number of Projects Delayed	4

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 1 project are on schedule and 4 projects are delayed.

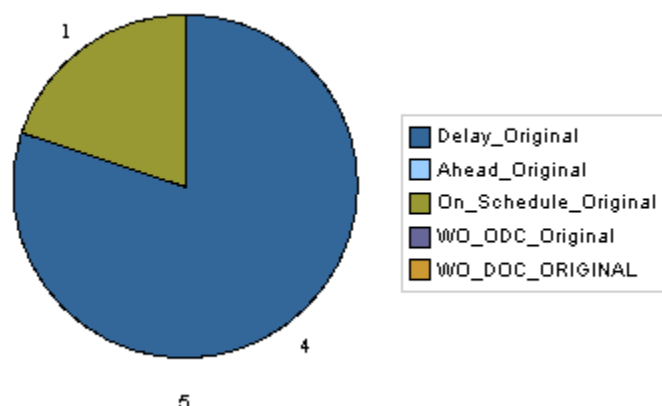

III. Investment Scenario

The Total Original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 5021.58 crore but this was subsequently revised to Rs. 5611.06 crore implying a cost overrun of 11.7%. The expenditure incurred on these projects till October, 2011 is Rs. 3614.45 crore, which is 64.4% of the revised cost of the projects.

Figures are in Rs. Crore

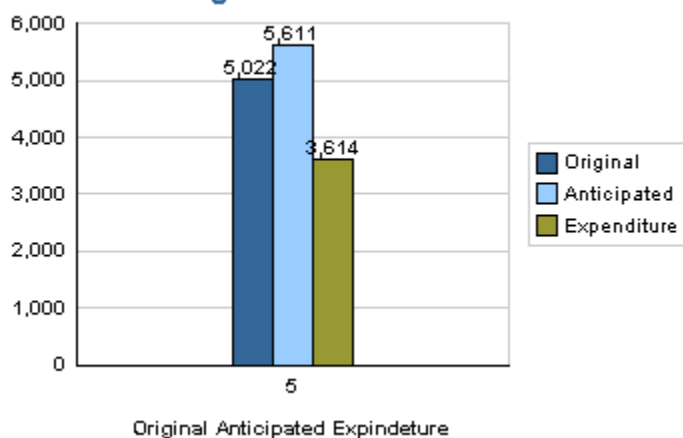

Sector wise current status of projects on theFlash Report


Atomic Energy

I. Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Original Date of Commissioning	1

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

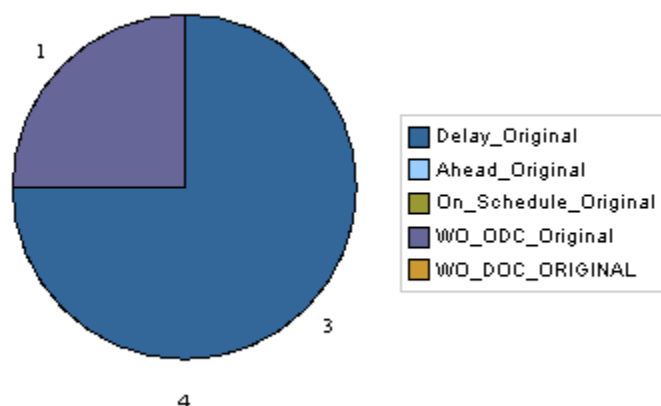

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 29228.29 crore but this was subsequently revised to Rs. 34066.29 crore implying a cost overrun of 16.6%. The expenditure incurred on these projects till October, 2011 is Rs. 19463.17 crore, which is 57.1% of the revised cost of the projects.

Figures are in Rs. Crore

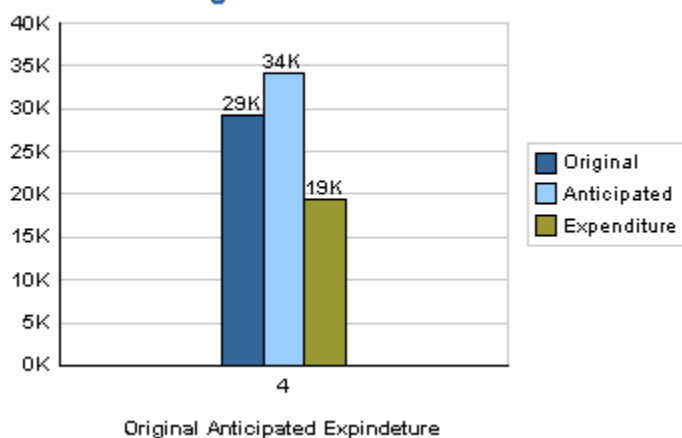

Sector wise current status of projects on theFlash Report

Urban Development


I. Current Status:

Number of Projects	4
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	1
--	---

II. Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are on schedule and 1 project are delayed .1 project do not have fixed dates of commissioning.

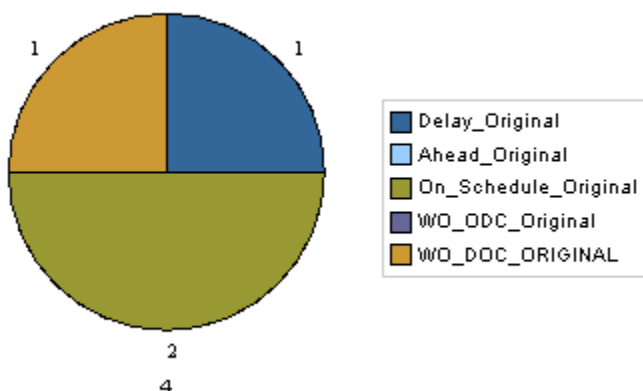

III. Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till October, 2011 is Rs. 2309.72 crore, which is 4.7% of the revised cost of the projects.

Figures are in Rs. Crore

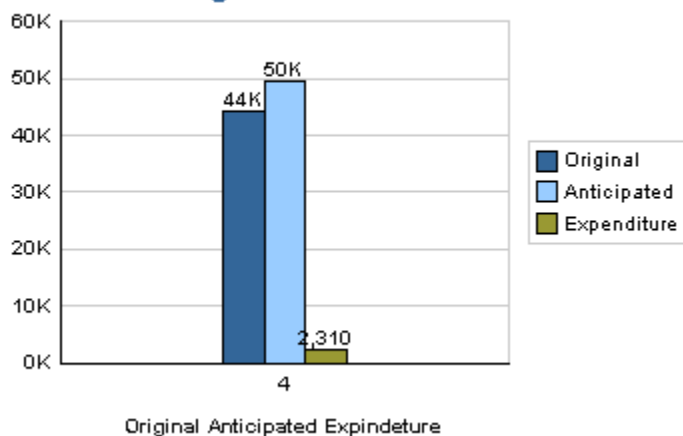

ANNEXURES

CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMMULATIVE EXPENDITURE
1	Andhra Pradesh	33	32855.21	39052.71	21351.34
2	Arunachal Pr.	4	9512.22	9610.51	7245.42
3	Assam	37	23895.78	35572.29	18826.56
4	Bihar	29	28702.95	33395.90	21388.67
5	Chhatisgarh	23	52747.27	55978.62	22173.91
6	Delhi	3	37985.00	37965.41	108.35
7	Goa	1	335.61	335.61	52.75
8	Gujarat	26	31711.98	32319.13	5560.89
9	Haryana	11	5987.83	7704.75	5034.51
10	Himachal Pr.	6	14761.16	14843.44	12411.76
11	J & K	11	14253.13	33145.32	11839.92
12	Jharkhandd	20	12826.33	14408.33	6366.96
13	Karnataka	27	31565.39	39869.16	16605.41
14	Kerala	9	7247.37	7861.37	2815.73
15	Madhya pradesh	25	17533.55	17765.86	6447.48
16	Maharashtra	52	72470.80	86887.47	38265.40
17	Manipur	1	727.56	3056.85	493.47
18	Mizoram	2	988.06	3307.12	272.50
19	Multi State	105	130484.19	133017.89	43925.85
20	Nagaland	1	850.00	850.00	8.44
21	Orissa	27	46642.14	49917.07	18134.37
22	Punjab	8	4854.69	5840.65	2847.13
23	Rajasthan	15	13638.67	13902.53	7521.38
24	Sikkim	2	1648.94	3690.02	206.04
25	Tamil Nadu	38	48500.48	57526.64	36757.98
26	Tripura	3	1522.39	2053.23	414.21
27	Uttar Pradesh	31	20197.31	23654.27	10295.29
28	Uttaranchal	6	10025.65	11948.21	4671.89
29	West Bengal	27	38340.33	46184.38	22317.15
TOTAL		583	712811.99	821664.74	344360.76

List of Projects in which Expenditure is more than cost

SN	PROJECT	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
1	KUDANKULAM APP (NPCIL)	Atomic Energy	13171.00	0.00	14122.00
2	BARSINGSAR TPS (2X125MW) (NLC)	Coal	1114.18	1626.09	1669.83
3	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli and Lauriya	Petroleum	613.54	0.00	671.52
4	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT	Petroleum	2305.30	700.00	2416.96
5	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP	Power	297.37	0.00	300.13
6	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	611.02	0.00	683.53
7	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)	Power	621.28	0.00	703.42
8	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJECT (NHPC)	Power	768.92	0.00	1385.57
9	CHAMERA,STAGE-III (NHPC)	Power	1405.63	0.00	1694.56
10	KOTESHWAR HEP(THDC)	Power	1301.56	2283.69	2524.97
11	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	Railways	78.23	0.00	87.26
12	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	136.62	0.00	161.07
13	RUPSA-BANGRIPOSI (GC)(SER)	Railways	57.94	0.00	176.57
14	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	100.00	142.90	187.44
15	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	156.00	0.00	202.04
16	ELECTRIFICATION OF MORADABAD-ROZA	Railways	129.17	0.00	218.15
17	GADWAL - RAICHUR (NL), SCR	Railways	92.63	108.91	236.09
18	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR	Railways	108.00	214.09	250.82
19	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR)	Railways	148.61	0.00	258.96
20	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)	Railways	240.00	0.00	267.79
21	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN	Railways	200.80	0.00	269.02
22	RANCHI-LOHARDAGA(GC),SER	Railways	194.07	0.00	289.43
23	RENIGUNTA-GUNTAKAL(RE)	Railways	168.34	0.00	307.08
24	KOTTUR-HARIHAR(NL),(SWR)	Railways	65.94	281.20	329.27
25	JIND-SONEPAT (NL),NR	Railways	190.81	238.56	338.99
26	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	114.01	283.95	340.51
27	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	170.00	170.00	365.15
28	KODERMA GIRIDH (NL), ECR	Railways	371.36	0.00	375.49
29	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	293.97	0.00	383.13
30	BANKURA - DAMODAR (GC) (SER)	Railways	111.90	0.00	396.24
31	MUZAFFARPUR-SITAMARHI(NL),ECR	Railways	100.00	322.29	422.17
32	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	343.17	0.00	443.75
33	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	323.40	0.00	451.09
34	AMRAVATI-NARKHER NL(CR)	Railways	120.90	284.27	466.60
35	MANDARHILL-DUMKA-RAMPURHAT (NL),ER	Railways	184.00	254.07	466.87

SN	PROJECT	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
36	REWARI-ROHTAK (NL),NR	Railways	149.38	330.23	471.11
37	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	100.00	0.00	476.32
38	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	295.00	0.00	478.17
39	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	155.74	164.36	492.29
40	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	124.43	407.78	512.65
41	GUNA-ETAWAH(NCR), NL	Railways	158.77	432.46	558.07
42	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	233.00	335.77	565.87
43	GONDIA-JABALPUR(GC),(SECR)	Railways	386.30	0.00	570.21
44	CALICUT-MANGALORE (DL) (SR)	Railways	240.00	0.00	595.36
45	KARUR-SALEM(NL),SR	Railways	155.55	0.00	622.93
46	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	Railways	280.00	0.00	697.02
47	KATIHAR - JOGBANI (GC)(NEFR)	Railways	100.00	492.98	720.94
48	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	248.44	576.27	789.49
49	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	409.00	625.30	815.43
50	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	733.00	0.00	834.94
51	PATNA GANGA BRIDGE (NL), ECR	Railways	624.47	0.00	1013.11
52	KODERMA-RANCHI VIA BARKAKANA (NL),ECR	Railways	491.19	1099.20	1113.09
53	KANPUR-KASGANJ-MATHURA(GC),NER	Railways	395.00	1062.36	1190.60
54	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDGE AT BOGIBEEL AND LINK LINES,NEFR	Railways	1000.00	1500.00	2240.65
55	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	1676.31	0.00	2820.12
56	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	907.69	1032.76	3076.13
57	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI)	Road Transport & Highways	151.30	0.00	174.00
58	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport & Highways	157.47	0.00	180.40
59	SAGAR - RAJMARG CHORAH, KM 211 TO KM 255, NH-26 (NHAI)	Road Transport & Highways	203.43	0.00	208.20
60	NALBARI T BIJNI (AS-7)	Road Transport & Highways	208.00	0.00	212.80
61	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport & Highways	190.00	0.00	227.00
62	NEW MANGALORE PORT NH-17 AND 48	Road Transport & Highways	196.50	0.00	236.60
63	ASSAM/WB BORDER TO GAIRKATTA (WB-1)	Road Transport & Highways	221.82	0.00	250.30
64	HAPUR-GARHMKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport & Highways	220.00	0.00	252.00

SN	PROJECT	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
65	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI)	Road Transport & Highways	225.00	0.00	257.50
66	DAKOBA TO NAGAON (NH-36)(NHAI)	Road Transport & Highways	225.00	0.00	257.60
67	NALBARI TO BIJNI (AS-8)	Road Transport & Highways	200.00	0.00	257.90
68	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport & Highways	240.00	0.00	274.90
69	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport & Highways	275.00	0.00	277.40
70	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport & Highways	251.03	0.00	283.20
71	JHANSI TO LALITPUR, NH-26	Road Transport & Highways	276.09	0.00	295.30
72	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24	Road Transport & Highways	275.00	0.00	298.70
73	PATHANKOT BHOGPUR NH-1A	Road Transport & Highways	229.00	0.00	344.80
74	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0	Road Transport & Highways	340.68	0.00	357.70
75	PONDICHERY - TINDIVANAU NH-66	Road Transport & Highways	285.00	0.00	359.30
76	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI)	Road Transport & Highways	227.00	0.00	369.10
77	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport & Highways	168.00	0.00	385.30
78	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00	Road Transport & Highways	227.00	0.00	403.50
79	KASIA TO GORAKHPUR (NH-28)(NHAI)	Road Transport & Highways	242.00	0.00	427.20
80	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254	Road Transport & Highways	412.78	0.00	436.90
81	JHAJHARPUR TO DARBANGA (BR-7)	Road Transport & Highways	340.00	0.00	447.70
82	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2)	Road Transport & Highways	367.49	0.00	453.68
83	HALDIA PORT (PORT CONNECTIVITY) (NH-41)	Road Transport & Highways	273.00	0.00	475.60
84	SONAPUR TO GUWAHTI (AS-3)	Road Transport & Highways	245.00	0.00	486.20
85	Armur to kadloor yellareddy	Road Transport & Highways	390.56	0.00	511.40
86	SITAPUR-LUCKNOW	Road Transport & Highways	322.00	0.00	553.70
87	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport & Highways	486.00	0.00	558.60
88	RINGBUNDS TO JHAJHANPUR (BR-6)	Road Transport & Highways	340.00	0.00	570.00

SN	PROJECT	SECTOR	COST ORIGINAL	COST REVISED	CUMMULATIVE EXPENDITURE
89	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport & Highways	280.00	0.00	580.70
90	TRICHY - KORUR NH-67	Road Transport & Highways	516.00	0.00	594.20
91	THRISSUR TO ANGAMALI (NH-47)	Road Transport & Highways	312.50	0.00	604.40
92	ZIRAKPUR(HARYANA) -PARWANOO(HIMACHAL PRADESH)	Road Transport & Highways	295.00	0.00	624.30
93	TRICHY - DINDIGUAL NH-45	Road Transport & Highways	576.00	0.00	658.90
94	Hazaribagh-Ranchi	Road Transport & Highways	625.07	0.00	666.00
95	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRIDOR	Road Transport & Highways	600.24	0.00	707.10
96	Kishangarh-Ajmer-Beawer	Road Transport & Highways	795.00	0.00	804.30
97	AMRITSAR-PATHANKOT	Road Transport & Highways	705.00	0.00	846.50
98	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B	Road Transport & Highways	629.00	0.00	910.00
99	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVIHALLI	Road Transport & Highways	441.00	0.00	929.00
100	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	Road Transport & Highways	557.00	0.00	930.90
101	Bijapur-Hungund Section	Road Transport & Highways	748.00	0.00	1114.00
102	Pune-sholapur, pkg1	Road Transport & Highways	1110.00	0.00	1802.00
103	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport & Highways	941.00	0.00	1901.00
104	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport & Highways	1693.75	0.00	2603.00
105	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport & Highways	1108.00	0.00	2691.00
106	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping & Ports	245.67	0.00	294.09
107	67.5 MW TG-5 AUX. SYSTEM EMERGENCY POWER REQUIREMENT EXP. UNIT	Steel	230.00	0.00	235.40
108	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) PH-5.1	Telecommunications	277.34	0.00	308.13
109	GSM equipment of 1900000 Lines (2G) 401700 lines 3(G)Tamil Nadu Phase V.1 Telecom Circle	Telecommunications	760.20	0.00	815.00

List of project Without Original Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	URANIUM ORE MINE AND PROCESSING PLANT AT TUMMALAPA - [N02000007]UCIL,Andhra Pradesh	09/2007	1,106.29	1,106.29	1,000.70	- 04/2011	04/2012	12(R3)	0/1
	Total		1,106.29	1,106.29	1,000.70				0/1
	<u>Coal</u>								
2	BALRAM OCP EXTENSION, MCL (8.00 Mty) - [N06000044]MCL,Orissa	12/2007	172.08	172.08	95.91	- -	03/2012	-	4/4
3	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Orissa	08/2008	207.28	207.28	68.10	- -	03/2012	-	5/7
4	TUTICORIN THERMAL POWER PROJECT - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 4,909.54	4,909.54	2,225.93	- -	02/2013	-	0/23
5	KUSMUNDA EXPN.OCP(SECL)(10-15MTY) - [N06000008]SECL,Chhatisgarh	06/2006	737.65	1,188.31	569.86	- -	03/2013	-	0/8
6	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Orissa	12/2007	457.77	457.77	110.21	- -	03/2013	-	6/11
7	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Orissa	11/2008	475.93	479.63	76.95	- -	03/2013	-	5/7
8	CHURCHA RO UG (1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35	462.35	257.30	- -	03/2014	-	0/4
9	MANIKPUR OC EXPANTION (3.50 MTY) - [N06000081]SECL,Chhatisgarh	11/2009	321.42	321.50	203.23	- -	03/2014	-	0/5
10	PENGANGA OC - [N06000066]WCL,Orissa	10/2008	339.77	339.77	0.65	- -	10/2014	-	1/1
11	GOPAL PRASAD OCP - [N06000042]MCL,Orissa	02/2008	395.87	395.87	58.80	- -	03/2015	-	2/12
12	TALABIRA OCP - [N06000043]MCL,Orissa	03/2008	447.72	447.72	35.20	- -	03/2016	-	1/12
13	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Orissa	12/2007	490.00	490.10	99.19	- -	03/2017	-	6/12
	Total		9,412.38	9,871.92	3,801.33				30/106
	<u>Fertilisers</u>								
14	THAL AMMONIA REVAMP PROJECT - [N08000003]RCF,Haryana	01/2009	488.75	488.75	195.63	- 11/2011	11/2011	0(R3)	6/22
	Total		488.75	488.75	195.63				6/22
	<u>Steel</u>								
15	Rebuilding of coke oven battery No.1 and 2 (Bokar - [N12000033]SAIL,	10/2007	500.90	500.90	326.23	- -	01/2012	-	1/3

List of project Without Original Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
16	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT - [N12000068]RINL, Andhra Pradesh	07/2007	230.00 -	343.58	235.40	- 02/2011	01/2012	11(R3)	2/3
17	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL, Andhra Pradesh	07/2007	260.00 -	350.00	223.06	- 08/2010	01/2012	17(R3)	1/2
18	Bailadila Iron Ore Deposit- IIB(NMDC) - [N12000018]NMDC, Chhatisgarh	01/2007	295.89 607.17	607.17	311.45	- 12/2011	03/2012	3(R3)	18/21
19	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL, Multi State	05/2008	480.00 -	460.00	144.07	- 05/2012	05/2012	0(R3)	1/2
20	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, Andhra Pradesh	08/2007	108.00 -	216.68	50.87	- 10/2012	10/2012	0(R3)	3/4
	Total		1,874.79 -	2,478.33	1,291.08				26/35
<u>Petrochemicals</u>									
21	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL, Assam	04/2006	5,460.61 8,920.00	8,920.00	3,145.56	- 12/2013	04/2012	-20(R3)	0/30
	Total		5,460.61 -	8,920.00	3,145.56				0/30
<u>Petroleum</u>									
22	EURO-IV DHD - [N16000109]CPCL, Tamil Nadu	09/2008	2,615.69 -	2,615.69	1,710.90	- -	12/2011	-	0/116
	Total		2,615.69 -	2,615.69	1,710.90				0/116
<u>Power</u>									
23	SIMHADRI STPP STAGE -II - [N18000032]NTPC, Andhra Pradesh	08/2007	5,103.39 -	5,038.83	4,162.00	- 05/2011	03/2012	10(R3)	0/6
24	BARH STPP STAGE -II - [N18000047]NTPC, Bihar	02/2008	7,341.04 -	7,341.04	3,026.00	- 08/2013	10/2013	2(R3)	2/18
	Total		12,444.43 -	12,379.87	7,188.00				2/24
<u>Railways</u>									
25	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR, Orissa	04/1994	355.38 470.21	1,100.00	176.85	- -	12/2011	-	0/0
26	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, Orissa	04/1996	301.64 -	735.10	-	- 09/2009	12/2011	27(R1)	0/0
27	KANPUR-KASGANJ-MATHURA(GC), NER - [220100197]NER, Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,190.60	- -	02/2012	-	0/0
28	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 762.33	762.33	424.94	- 12/2009	02/2012	26(R1)	0/0
29	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, Andhra Pradesh	12/1994	124.43 407.78	725.90	512.65	- -	03/2012	-	0/0

List of project Without Original Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
30	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	466.87	- 12/2011	03/2012	3(R3)	0/0
31	KADUR-CHIKMAGALUR-SAKLESHAPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	208.83	- 03/2012	03/2012	0(R3)	0/0
32	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	422.17	- -	03/2012	-	0/0
33	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	565.87	- -	03/2012	-	0/0
34	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	340.51	- 03/2011	03/2012	12(R3)	0/0
35	HARNOUT -SET. UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
36	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0
37	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	202.04	- -	03/2012	-	0/0
38	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	326.92	- 07/2012	07/2012	0(R3)	0/0
39	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	579.88	- -	12/2012	-	0/0
40	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	338.99	- 03/2012	12/2012	9(R3)	0/0
41	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	241.91	- -	12/2012	-	0/0
42	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	152.76	- -	03/2013	-	0/0
43	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	697.02	- -	03/2013	-	0/0
44	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	135.28	- 06/2013	06/2013	0(R3)	0/0
45	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	180.24	- -	12/2013	-	0/0
46	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	771.94	- -	03/2014	-	0/0
47	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	168.07	- -	03/2015	-	0/0
48	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	338.76	- 12/2012	-	-	0/0
Total			6,362.55 -	17,535.99	9,572.00				0/0
Grand Total			39,765.49	55,396.84	27,905.20				64/334

List of project Without Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Coal</u>									
1	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	40.95	03/2012 03/2012	-	-	13/42
2	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	03/2013	467.78 -	467.78	12.31	03/2013 03/2013	-	-	0/83
Total			716.81 -	716.81	53.26				13/125
<u>Mines</u>									
3	SECOND PHASE EXPANSION OF CAPTIVE ALUMINIUM,SMELTER AND POWE - [100100054]NALCO,Orissa	10/2004	4,091.51 4,401.76	4,401.76	4,183.00	12/2008 01/2011	06/2011	5(R3)	117/110
Total			4,091.51 -	4,401.76	4,183.00				117/110
<u>Petroleum</u>									
4	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40 -	304.40	-	06/2010 -	09/2011	15(O)	0/0
5	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	528.92	03/2011 05/2011	06/2011	1(R3)	0/0
6	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54 -	727.88	671.52	12/2010 -	06/2011	6(O)	0/0
7	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009 -	08/2011	23(O)	0/0
8	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	258.42	02/2011 08/2011	08/2011	0(R3)	0/0
9	DAHEJ-VIJAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38 -	2,340.00	2,273.78	10/2010 09/2011	09/2011	0(R2)	0/0
10	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 -	3,284.00	-	09/2011 -	09/2011	0(O)	0/0
11	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	3.29	10/2010 -	-	-	0/0
12	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	-	-	0/0
13	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	1,584.00	5.76	- -	-	-	0/0
Total			16,339.00 -	13,996.24	6,035.31				0/0
<u>Power</u>									

List of project Without Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	WESTERN REGION STRENGTHENING SCHEME-IX - [N18000050]PGCIL, Multi State	04/2008	230.89	230.89	96.40	01/2011	-	-	0/1
	Total		230.89	230.89	96.40				0/1
			-						
<u>Railways</u>									
15	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL, Orissa	04/1999	166.16	243.40	-	-	12/2010	22(R1)	0/0
			-			02/2009			
16	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, Orissa	04/2000	133.41	211.90	188.18	-	12/2010	21(R1)	0/0
			207.00			03/2009			
17	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL, Andhra Pradesh	04/2003	136.62	221.90	161.07	12/2007	12/2010	9(R1)	0/0
			-			03/2010			
18	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL, Uttar Pradesh	04/2003	230.73	399.50	295.24	03/2009	12/2010	24(R1)	0/0
			399.73			12/2008			
19	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL, Gujarat	09/2005	200.80	200.80	269.02	-	12/2010	-	0/0
			-			-			
20	BILASPUR-URKURA (DL) - [220100321]RVNL, Chhatisgarh	04/1997	151.52	273.00	-	-	03/2011	24(R1)	0/0
			-			03/2009			
21	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL, Multi State	04/2005	240.00	329.70	267.79	03/2009	03/2011	15(R1)	0/0
			-			12/2009			
22	MUMBAI URBAN TRANSPORT PROJECT PHASE-I, MTP - [N22000093]MRTP, Maharashtra	04/2003	3,125.20	4,501.80	4,273.68	-	06/2011	6(R3)	0/1
			4,501.80			12/2010			
23	VIRAMGAM-BHILDI(WR),GC - [220100062]WR, Multi State	04/1990	155.66	356.87	149.70	-	-	-	0/0
			-			03/2010			
24	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR, West Bengal	04/1983	36.80	415.23	234.70	-	-	-	0/0
			274.41			-			
25	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL, Chhatisgarh	04/1995	304.00	968.60	87.11	12/2012	-	-	0/0
			-			-			
26	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00	579.37	595.36	-	-	-	0/0
			-			-			
27	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, Maharashtra	02/1997	353.08	1,010.00	99.45	-	-	-	0/0
			462.67			-			
28	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR, Karnataka	02/1997	295.00	944.55	478.17	-	-	-	0/0
			-			-			
29	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, Multi State	02/1997	386.30	1,038.00	570.21	03/1998	-	-	0/0
			-			-			
30	KARUR-SALEM(NL),SR - [220100191]SR, Tamil Nadu	02/1997	155.55	945.73	622.93	-	-	-	0/0
			-			-			
31	HUBLI-ANKOLA(NL),SWR - [220100193]SWR, Karnataka	04/1995	227.00	997.58	65.16	-	-	-	0/0
			-			-			
32	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR, Multi State	04/1997	218.24	537.47	93.80	-	-	-	0/0
			377.32			-			
33	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0
			-			-			

List of project Without Date of Commissioning

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
34	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,113.09	07/2005 -	-	-	0/0
35	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252] SR, Kerala	10/1998	550.00 -	1,214.00	70.88	- -	-	-	0/0
36	GULBARGA-BIDAR, SCR(NL) - [220100254] SCR, Karnataka	02/1998	242.42 369.70	776.00	269.00	- 05/2009	-	-	0/0
37	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, Bihar	04/1997	78.23 -	162.87	87.26	- -	-	-	0/0
38	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258] (NR), Multi State	03/2002	409.00 625.30	847.76	815.43	06/2007 -	-	-	0/0
39	REINGUNTA-GUNTAKAL(RE) - [220100260] RVNL, Andhra Pradesh	06/2000	168.34 -	296.20	307.08	04/2003 03/2010	-	-	0/0
40	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262] SR, Tamil Nadu	09/1995	100.00 -	548.96	476.32	- -	-	-	0/0
41	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265] SCR, Andhra Pradesh	12/2001	330.00 -	695.00	9.44	- -	-	-	0/0
42	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274] SWR, Karnataka	02/1999	138.00 -	901.62	0.29	- -	-	-	0/0
43	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, Jharkhandd	04/2002	459.91 -	418.17	77.24	- -	-	-	0/0
44	RAMGANJMUNDI-BHOPAL (NL), WCR - [220100314] WCR, Madhya Pradesh	04/2001	727.13 727.13	1,225.00	210.90	- -	-	-	0/0
45	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322] WR, Gujarat	04/2005	148.61 -	227.52	258.96	03/2008 03/2009	-	-	0/0
46	RUPSA-BANGRIPOSI (GC)(SER) - [220100323] SER, Orissa	02/1996	57.94 -	173.49	176.57	03/1998 08/2005	-	-	0/0
47	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325] RVNL, Orissa	04/1998	183.23 -	638.00	-	02/2015 -	-	-	0/0
48	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032] SCR, Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
49	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045] SER, Jharkhandd	03/1997	186.92 -	261.70	24.65	02/2006 -	-	-	0/0
50	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049] RVNL, Andhra Pradesh	07/2006	743.00 -	732.80	315.49	03/2008 06/2008	-	-	0/0
51	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I-A - [N22000079] SR, Tamil Nadu	09/2007	404.19 -	900.00	211.41	- -	-	-	0/0
52	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080] SR, Tamil Nadu	09/2006	343.17 -	900.00	443.75	- -	-	-	0/0
53	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084] SR, Tamil Nadu	09/2006	125.00 -	227.40	22.66	- -	-	-	0/0
54	TIDIVANAM-NAGARI (NL) - [N22000085] SR, Tamil Nadu	09/2006	456.00 -	582.83	89.12	- -	-	-	0/0
55	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087] NEFR, Bihar	09/2006	300.00 300.00	529.88	35.45	- -	-	-	0/0

List of project Without Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
56	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	178.19	03/2011 -	-	-	0/0
57	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
58	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	171.36	03/2011 -	-	-	0/0
59	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	466.60	06/1999 03/2011	-	-	0/0
60	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]M RTP,Maharashtra	03/1996	401.81 495.44	495.44	167.16	03/2004 -	-	-	0/0
61	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	329.27	- 03/2011	-	-	0/0
62	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	289.43	06/2004 04/2005	-	-	0/0
63	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
64	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
65	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.94	- 12/2010	-	-	0/0
66	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	436.49	- -	-	-	0/0
67	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 -	522.56	451.09	- -	-	-	0/1
68	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]M RTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,076.13	12/2006 08/2010	-	-	0/0
69	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	270.00	236.09	- 02/2011	-	-	0/0
70	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	471.11	02/2010 02/2011	-	-	0/0
71	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	375.49	- -	-	-	0/0
72	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	236.84	- 03/2011	-	-	0/0
73	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	134.12	- -	-	-	0/0
74	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	134.90	- -	-	-	0/0
75	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	85.45	- -	-	-	0/0
76	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	365.15	- 03/2011	-	-	0/0
77	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.90	- -	-	-	0/0

List of project Without Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
78	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15	245.15	167.66	12/2010 03/2011	-	-	0/0
79	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68	225.68	130.29	- 12/2010	-	-	0/0
80	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24	468.62	2.29	03/2012 -	-	-	0/0
	Total		21,118.68	42,450.25	22,926.85				0/2
			-						
	Shipping & Ports								
81	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67	298.17	294.09	04/2009 -	02/2011	22(O)	0/0
82	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST,Karnataka	06/2006	230.00	272.50	219.00	12/2010 -	06/2011	6(O)	0/0
83	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK,Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
84	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP.,Kerala	12/2010	241.50	241.50	48.10	09/2011 -	09/2011	0(O)	0/0
85	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00	800.00	5.75	10/2008 -	-	-	0/0
86	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84	253.36	-	12/2007 01/2009	-	-	0/0
87	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00	370.00	-	08/2010 -	-	-	0/0
88	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40	2,427.40	821.48	10/2008 -	-	-	0/0
	Total		4,665.66	4,859.18	1,388.42				0/0
			-						
	Telecommunications								
89	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94	1,799.94	299.77	09/2009 -	02/2010	5(O)	0/0
90	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88	952.88	-	03/2010 -	10/2010	7(O)	0/0
91	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48	192.48	119.45	03/2009 -	02/2011	23(O)	0/0
92	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94	373.94	209.79	12/2008 -	02/2011	26(O)	0/0
93	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34	377.54	308.13	03/2009 -	02/2011	23(O)	0/0

List of project Without Date of Commissioning

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
94	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	02/2011	20(O)	0/0
95	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
96	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.39	10/2008 -	02/2011	28(O)	0/0
97	GSM equipment of 1900000Lines (2G) 401700 lines 3(- [N26000091]BSNL,Tamil Nadu	01/2009	760.20 -	1,100.00	815.00	- 03/2011	02/2011	-1(R3)	0/1
98	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	02/2011	13(O)	0/0
99	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70 -	848.70	712.86	01/2010 -	02/2011	13(O)	0/0
100	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19 -	315.19	142.07	01/2010 -	02/2011	13(O)	0/0
101	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49 -	601.49	496.20	12/2008 -	03/2011	27(O)	0/0
102	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	335.91	182.45	03/2009 -	03/2011	24(O)	0/0
103	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49 -	241.49	123.76	09/2009 -	03/2011	18(O)	0/0
104	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	17(O)	0/0
105	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33 -	584.33	403.71	02/2009 -	03/2011	25(O)	0/0
106	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	362.62	08/2009 -	03/2011	19(O)	0/0
107	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	280.72	11/2010 -	03/2011	4(O)	0/0
108	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	461.56	10/2009 -	03/2011	17(O)	0/0
109	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
110	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0
111	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86 -	389.86	3.06	09/2011 -	09/2011	0(O)	0/0
112	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38 -	168.30	-	10/2007 -	-	-	0/0

List of project Without Date of Commissioning

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
113	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
114	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
115	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0
116	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
117	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	-	-	0/0
118	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	-	-	0/0
119	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	-	-	0/0
120	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	-	-	0/0
121	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
122	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	-	-	0/0
123	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	-	-	0/0
124	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	-	-	0/0
125	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	-	06/2009	-	-	0/0
126	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhandd	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
Total			19,079.13	19,488.17	6,070.12				0/1
<u>Urban Development</u>									
127	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18	173.08	-	04/2009	-	-	0/0
Total			114.18	173.08	.00				0/0
Grand Total			66,355.86	86,316.38	40,753.36				130/239

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Atomic Energy</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, Tamil Nadu	09/2003	3,492.00	5,677.00	3,281.47	09/2010	01/2012	16	8/80
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL, Tamil Nadu	12/2001	13,171.00	15,824.00	14,122.00	12/2008	12/2012	48	61/119
3	KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N02000010]NPCIL, Gujarat	10/2009	11,459.00	11,459.00	1,059.00	12/2015 05/2016	11/2016	11	0/70
Total			28,122.00	32,960.00	18,462.47				69/269
<u>Civil Aviation</u>									
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI, Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,552.74	01/2011	12/2011	11	0/0
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI, West Bengal	08/2008	1,942.51	2,325.00	1,530.56	05/2011	03/2012	10	0/0
6	C/o new Airport at Pakyong (Sikkim) Airport - [N04000050]AAI, Sikkim	01/2009	309.46	309.45	153.41	01/2011	06/2012	17	0/0
7	Construction of New International Terminal Building - [N04000069]AAI, Goa	05/2010	335.61	335.61	52.75	05/2012	08/2012	3	0/0
Total			4,395.58	4,985.06	3,289.46				0/0
<u>Coal</u>									
8	BARSINGSAR TPS (2X125MW) (NLC) - [060100089]NLC, Rajasthan	12/2004	1,114.18 1,626.09	1,626.09	1,669.83	06/2009	12/2011	30	59/26
9	KULDA OCP (MAHANADI COALFIELDS LTD.) - [060100092]MCL, Orissa	01/2005	302.96	302.96	86.63	03/2010	03/2012	24	9/11
10	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, Tamil Nadu	10/2004	2,030.78 2,453.57	2,453.57	2,291.10	06/2009	07/2012	37	60/24
11	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL, Jharkhand	04/2006	471.66 341.63	341.63	101.43	03/2011 03/2012	03/2013	24	0/2
12	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL, Madhya Pradesh	05/2006	789.88	741.62	288.78	03/2010	03/2013	36	0/2
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL, Andhra Pradesh	09/2006	212.34 779.26	779.26	201.30	03/2013 09/2012	12/2013	9	2/22
14	GEVRA EXPANSION OCP (SECL) (25 MTY) - [060100093]SECL, Chhatisgarh	07/2005	1,667.55	2,675.67	1,279.57	03/2010	03/2014	48	3/15
15	DIPKA EXPANSION OCP (SECL) (20-25 MTY) - [060100094]SECL, Chhatisgarh	07/2005	1,268.53	1,943.66	1,109.47	03/2010	03/2014	48	2/13
16	RAJMAHAL OC EXP. - [N06000056]ECL, Multi State	02/2006	50.08 153.82	153.82	19.74	03/2011	03/2014	36	0/3

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
17	Churi Benti UG - [N06000083]CCL,Jharkhandd	06/2007	163.51 -	163.51	33.57	03/2011 03/2012	03/2014	36	0/2
18	North Urimari OCP - [N06000084]CCL,Jharkhandd	12/2007	179.87 -	179.87	66.45	03/2012 03/2012	03/2014	24	0/2
19	Tapin OCP - [N06000086]CCL,Jharkhandd	08/2008	264.68 -	264.68	76.05	03/2012 03/2013	03/2014	24	0/2
20	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2006	746.04 -	535.10	140.21	03/2012 -	03/2015	36	0/2
21	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	-	03/2011 -	03/2015	48	1/5
22	KAKATIYA LAONGWALL - [N06000048]SCCL,Multi State	12/2008	453.63 -	453.63	69.64	12/2012 -	03/2015	27	11/44
23	AMLOHRI EPR (NCL) (6 MTY) - [N06000010]NCL,Madhya pradesh	05/2006	1,352.04 -	1,143.54	225.00	03/2014 -	03/2016	24	1/2
24	MAGADH OC (CCL) - [N06000015]CCL,Jharkhandd	07/2006	469.78 706.40	706.40	16.21	07/2012 03/2014	03/2016	44	0/2
Total			11,824.69 -	14,752.18	7,674.98				148/179
<u>Fertilisers</u>									
25	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	84.31	07/2011 -	11/2011	4	0/0
26	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	105.79	07/2011 -	03/2012	8	0/0
27	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT - [N08000006]NFL,Punjab	01/2010	1,478.63 -	1,478.63	223.57	12/2012 -	01/2013	1	0/8
Total			2,241.63 -	2,241.63	413.67				0/8
<u>Steel</u>									
28	700TPD ARI SEPARATION UNIT-4 AT OXYGEN PLANT-II, BHILLAI - [N12000023]SAIL,Chhatisgarh	07/2007	232.93 232.93	232.93	168.44	05/2011 -	10/2011	5	0/1
29	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 16,408.00	16,408.00	11,870.83	12/2011 12/2011	06/2012	6	6/14
30	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	8,911.27	10/2009 10/2012	10/2012	36	49/59
Total			23,367.93 -	28,931.93	20,950.54				55/74
<u>Petroleum</u>									
31	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16	0/0
32	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 -	2,800.00	2,520.91	12/2008 12/2008	11/2011	35	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
33	BAWANA NANGAL PIPE LINE PROJECT - [N16000050]GAIL, Multi State	11/2007	1,816.07 -	1,385.00	998.86	10/2010 12/2011	12/2011	14	0/1
34	COMPRESSOR STATIONS (KAILARAS AND CHAINSA) - [N16000054]GAIL, Multi State	11/2007	1,167.00 -	798.00	647.70	04/2011 12/2011	12/2011	8	0/2
35	HEERA RECONSTRUCTION - [N16000062]ONGC, Maharashtra	05/2008	706.70 -	706.70	648.52	04/2010 -	12/2011	20	0/0
36	NEELAM RECONSTRUCTION - [N16000063]ONGC, Maharashtra	05/2008	305.08 -	305.08	261.78	04/2011 -	12/2011	8	0/0
37	MNW-NF BRIDGE PROJECT - [N16000045]ONGC, Maharashtra	05/2008	175.21 -	162.12	71.60	03/2009 02/2012	02/2012	35	0/0
38	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC, Maharashtra	01/2007	740.02 -	740.02	412.78	03/2010 03/2012	03/2012	24	0/0
39	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	18	0/0
40	VKPL UPGRADE AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL, Multi State	12/2009	463.32 -	330.47	160.47	06/2011 03/2012	03/2012	9	3/9
41	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	73	0/0
42	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,771.00	05/2010 05/2012	05/2012	24	0/0
43	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	49.20	05/2010 04/2012	05/2012	24	0/0
44	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	233.77	07/2010 05/2012	05/2012	22	0/0
45	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,802.20	08/2010 03/2012	06/2012	22	0/0
46	ADDITIONAL GAS PROCESSING FACILITY AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	82.78	04/2011 -	07/2012	15	0/0
47	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	460.70	164.83	06/2011 07/2012	07/2012	13	7/9
48	DABHOL-BANGALORE PIPELINE PROJECT PHASE-I - [N16000073]GAIL, Multi State	06/2009	4,543.43 4,508.38	2,300.00	1,335.32	03/2012 08/2012	08/2012	5	11/10
49	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS (OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.53	09/2011 -	12/2012	15	0/0
50	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	84.18	12/2011 -	01/2013	13	0/0
51	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
52	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	231.94	03/2006 03/2013	03/2013	84	6/6
53	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,767.62	05/2010 03/2013	03/2013	34	0/0
54	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,915.00	-	10/2012 -	03/2013	5	0/0
55	HYDROCRACKER REVAMP SETTING UP A NEW CCR AT MUMB - [N16000081]BPCL,Maharashtra	04/2008	825.00 1,827.00	1,827.00	-	12/2011 04/2013	04/2013	16	0/203
56	PARADIP REFINERY PROJECT - [N16000058]IOCL,Orissa	02/2009	29,777.00 -	30,426.00	10,597.63	11/2012 -	06/2013	7	107/100
57	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	663.69	592.78	03/2007 03/2014	03/2014	84	3/3
58	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,375.28	03/2007 03/2017	03/2017	120	6/6
59	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	748.06	09/2011 03/2012	12/2011	3	0/0
Total			70,732.78 -	82,335.04	38,598.15				143/349
Power									
60	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL,J & K	10/2006	238.25 -	227.03	213.52	05/2011 05/2011	11/2011	6	0/0
61	WESTERN REGION STRENGTHENING SCHEME-II - [N18000022]PGCIL,Rajasthan	07/2006	5,221.23 -	4,978.56	2,987.90	07/2010 -	12/2011	17	3/20
62	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL,Multi State	12/2007	227.52 -	227.52	136.10	06/2010 -	12/2011	18	0/0
63	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL,Multi State	04/2008	297.37 -	297.37	300.13	07/2011 -	12/2011	5	0/0
64	CHAMERA,STAGE-III (NHPC) - [180100241]NHPC,Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,694.56	08/2010 -	02/2012	18	0/0
65	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79 -	1,724.79	1,575.98	11/2009 -	02/2012	27	0/0
66	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79 -	210.79	165.10	08/2011 -	02/2012	6	0/0
67	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57 -	353.57	213.40	07/2010 02/2012	02/2012	19	0/0
68	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10 -	196.10	86.60	07/2011 -	02/2012	7	0/0
69	KOTESHWAR HEP(THDC) - [180100184]THDCL,Uttaranchal	04/2000	1,301.56 2,283.69	2,283.69	2,524.97	04/2005 03/2012	03/2012	83	7/11

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
70	SIPAT STPP STAGE - I (NTPC) - [180100229]NTPC,Chhatisgarh	12/2003	8,323.39	8,323.39	7,431.00	12/2009	03/2012	27	33/60
71	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,590.26	10/2010	03/2012	17	0/0
72	TRANSMISSION SY. ASSOCIATED WITH BARH GENER. PROJECT(P.GR.) - [180100260]PGCIL,Bihar	12/2005	3,779.46	3,725.13	3,483.30	09/2009	03/2012	30	15/30
73	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96	894.26	710.00	10/2009	03/2012	29	2/20
74	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC) - [N18000007]NHPC,J & K	08/2006	621.28	621.28	703.42	02/2011	03/2012	13	0/1
75	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pr.	07/2006	557.24	639.52	486.40	01/2010	03/2012	26	0/22
76	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	62.30	11/2011	03/2012	4	0/0
77	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE - [180100222]NHPC,West Bengal	10/2003	768.92	768.92	1,385.57	03/2007	05/2012	62	1/25
78	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02	611.02	683.53	08/2010	11/2012	27	0/0
79	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38	1,061.38	1,027.42	09/2009	12/2012	39	0/0
80	KUDANKULAM-APP TRANS. SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29	1,946.85	1,745.38	11/2008	12/2012	49	25/38
81	LOHARINAG-PAL HEP(4X150MW) - [N18000005]NTPC,Uttaranchal	06/2006	2,895.10	2,895.10	685.00	11/2011	12/2012	13	6/34
82	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48	520.48	266.43	11/2011	12/2012	13	0/0
83	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66	509.66	266.60	11/2011	12/2012	13	0/0
84	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29	410.29	144.50	02/2012	12/2012	10	0/0
85	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00	5,915.00	2,329.00	10/2012	12/2012	2	3/15
86	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81	6,230.81	2,152.00	10/2012	12/2012	2	3/16
87	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28	6,010.89	2,988.00	08/2012	01/2013	5	3/16
88	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pr.	10/2002	4,527.15	4,527.15	3,884.00	04/2009	03/2013	47	19/9
89	KAIGA 3&4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	947.96	831.16	12/2007 12/2009	03/2013	63	14/18

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	381.90	09/2010 -	03/2013	30	0/0
91	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	74.52	01/2012 07/2013	07/2013	18	0/0
92	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pr.	01/2007	2,047.03 -	2,047.03	1,399.75	01/2012 -	09/2013	20	2/10
93	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	132.80	11/2011 -	09/2013	22	0/0
94	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	2,447.00	06/2011 -	10/2013	28	0/29
95	TUIRIAL HE PROJECT(NEEPCO) - [180100165]NEEPCO,Mizoram	07/1998	368.72 913.63	913.63	268.89	07/2006 01/2014	01/2014	90	2/5
96	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttaranchal	11/2006	2,978.48 -	2,978.48	1,187.00	03/2013 -	06/2014	15	6/13
97	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pr.	09/2003	6,285.33 -	6,285.33	5,184.46	09/2010 -	08/2014	47	2/11
98	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	6,195.00	12/2009 -	09/2014	57	15/70
99	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	3,073.60	08/2013 -	09/2014	13	0/0
100	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pr.	09/2002	3,919.59 -	3,919.59	3,356.79	09/2009 -	12/2014	63	1/20
101	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67 3,642.04	3,642.04	999.75	07/2014 01/2016	01/2016	18	0/0
102	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,	07/2006	1,657.00 2,978.86	2,978.86	277.54	07/2010 02/2016	02/2016	67	1/10
103	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pr.	12/2004	2,496.90 -	2,496.90	1,626.70	05/2013 06/2016	06/2016	37	79/22
104	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttaranchal	08/2008	2,491.58 3,422.44	3,422.44	179.49	07/2014 -	07/2016	24	0/7
Total			109,105.88 -	115,254.51	69,538.72				242/532
<u>Railways</u>									
105	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50 -	252.50	-	02/2010 -	11/2011	21	0/0
106	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77 432.46	540.96	558.07	03/1994 -	12/2011	213	0/0
107	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00 142.90	208.68	187.44	03/2002 -	12/2011	117	0/0
108	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 164.36	843.91	492.29	02/2009 -	12/2011	34	0/0
109	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	66.31	12/2011 -	02/2012	2	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
110	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	542.82	03/1995 -	03/2012	204	0/0
111	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	188.15	03/2010 -	03/2012	24	0/0
112	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	218.15	03/2011 -	03/2012	12	0/0
113	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	383.13	06/2005 07/2011	03/2012	81	0/0
114	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	146.26	03/2007 03/2007	06/2012	63	0/0
115	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	396.24	03/2005 12/2008	12/2012	93	0/0
116	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	556.03	03/2009 -	12/2012	45	0/0
117	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	1,013.11	10/2007 -	12/2012	62	0/0
118	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	400.42	03/2010 -	12/2012	33	0/0
119	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	48.10	03/2012 -	03/2013	12	0/0
120	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	64.10	12/2011 -	11/2013	23	0/0
121	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	83.63	12/2012 -	12/2013	12	0/0
122	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,820.12	03/2009 -	12/2013	57	0/0
123	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	834.94	12/2008 -	03/2014	63	0/0
124	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	107.60	03/2010 06/2014	06/2014	51	0/0
125	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,240.65	04/2008 03/2014	12/2014	80	0/0
126	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	315.09	03/2014 -	03/2015	12	0/0
127	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	493.47	03/2011 03/2014	03/2016	60	0/0
128	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	-	03/2014 -	03/2016	24	0/0
129	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	0.02	03/2016 -	06/2016	3	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
130	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,326.12	03/2001 -	12/2017	201	0/0
	Total		22,320.65	51,963.65	19,482.26				0/0
	Road Transport & Highways								
131	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	11/2011	12	0/0
132	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya Pradesh	12/2003	225.00 -	225.00	257.50	10/2008 -	11/2011	37	0/0
133	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	570.00	06/2008 -	11/2011	41	0/0
134	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	604.40	03/2009 -	11/2011	32	0/0
135	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09 -	276.09	295.30	09/2009 -	11/2011	26	0/0
136	TRICHY - DINDIGUL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	658.90	07/2010 -	11/2011	16	0/0
137	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	359.30	07/2010 -	11/2011	16	0/0
138	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	159.45	08/2004 07/2010	12/2011	88	0/0
139	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	167.70	08/2004 -	12/2011	88	0/0
140	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00 -	241.53	82.01	04/2004 -	12/2011	92	0/0
141	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49 -	367.49	453.68	03/2005 -	12/2011	81	0/0
142	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00 -	522.00	475.60	03/2005 -	12/2011	81	0/0
143	GARHMUKTESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00 -	275.00	298.70	09/2007 -	12/2011	51	0/0
144	HAPUR-GARHMUKTESHWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	252.00	09/2007 -	12/2011	51	0/0
145	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78 -	479.54	436.90	11/2007 -	12/2011	49	0/0
146	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	207.80	06/2005 -	12/2011	78	0/0
147	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09 -	166.30	183.90	03/2008 -	12/2011	45	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
148	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI, J & K	12/2003	166.27 -	193.10	153.70	03/2008 -	12/2011	45	0/0
149	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	403.50	10/2008 -	12/2011	38	0/0
150	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI, Chhatisgarh	03/2005	190.00 -	190.00	227.00	01/2009 -	12/2011	35	0/0
151	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, Assam	12/2003	280.00 -	280.00	228.90	02/2009 -	12/2011	34	0/0
152	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	82.02	04/2009 -	12/2011	32	0/0
153	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI, Assam	12/2003	195.00 -	195.00	174.80	06/2008 -	12/2011	42	0/0
154	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI, Uttar Pradesh	12/2003	242.00 -	242.00	427.20	12/2008 -	12/2011	36	0/0
155	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI, Uttar Pradesh	12/2003	227.00 -	227.00	369.10	12/2008 -	12/2011	36	0/0
156	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI, Assam	12/2003	237.80 -	237.80	204.70	06/2008 -	12/2011	42	0/0
157	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI, Rajasthan	12/2003	275.00 -	250.39	277.40	10/2008 -	12/2011	38	0/0
158	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI, Madhya pradesh	12/2003	198.00 -	198.00	187.30	11/2008 -	12/2011	37	0/0
159	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI, Uttar Pradesh	12/2003	151.30 -	151.30	174.00	10/2008 -	12/2011	38	0/0
160	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, Madhya pradesh	12/2003	251.03 -	251.03	283.20	10/2008 -	12/2011	38	0/0
161	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI, Madhya pradesh	12/2003	229.91 -	229.91	226.80	10/2008 -	12/2011	38	0/0
162	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI, Bihar	12/2003	340.00 -	340.00	447.70	09/2008 -	12/2011	39	0/0
163	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	257.90	06/2008 -	12/2011	42	0/0
164	SITAPUR-LUCKNOW - [N24000036]NHAI, Uttar Pradesh	03/2005	322.00 -	322.00	553.70	06/2009 -	12/2011	30	0/0
165	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 -	196.50	236.60	06/2008 -	12/2011	42	0/0
166	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	255.10	06/2008 -	12/2011	42	0/0
167	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, Assam	12/2003	245.00 -	245.00	486.20	03/2008 -	12/2011	45	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
168	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	173.80	06/2008	12/2011	42	0/0
169	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	212.80	04/2008	12/2011	44	0/0
170	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	126.20	05/2008	12/2011	43	0/0
171	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	195.60	06/2008	12/2011	42	0/0
172	THANJAUR-TRICHY, NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30	0/0
173	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	707.10	10/2009	12/2011	26	0/0
174	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	328.70	03/2010	12/2011	21	0/0
175	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11	0/0
176	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	929.00	07/2010	12/2011	17	0/0
177	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	344.80	05/2010	12/2011	19	0/0
178	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Orissa	04/2000	228.70	228.70	173.06	02/2004	12/2011	94	0/0
179	ZIRAKPUR (HARYANA) - PARWANOO (HIMACHAL PRADESH) - [N24000117]NHAI,Multi State	02/2008	295.00	295.00	624.30	08/2010	12/2011	16	0/0
180	END OF DURG BYPASS-CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI,Chhatisgarh	01/2008	464.00	464.00	420.00	01/2011	12/2011	11	0/0
181	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00	486.00	558.60	05/2010	12/2011	19	0/0
182	Surat- Dahisar (Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	1,693.75	2,603.00	08/2011	12/2011	4	0/0
183	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI,West Bengal	12/2003	221.82	221.82	250.30	11/2008	01/2012	38	0/0
184	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00	168.00	385.30	12/2008	01/2012	37	0/0
185	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	355.06	294.70	09/2009	02/2012	29	0/0
186	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47	154.57	180.40	09/2007	03/2012	54	0/0
187	KOTWA TO DEWAPUR (10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	240.00	274.90	10/2008	03/2012	41	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
188	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI,Uttar Pradesh	12/2003	340.68 -	340.68	357.70	03/2008 -	03/2012	48	0/0
189	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI,Assam	12/2003	225.00 -	225.00	257.60	06/2008 -	03/2012	45	0/0
190	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	297.30	09/2008 -	03/2012	42	0/0
191	SAGAR - RAJMARG CHORAHA,KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI,Madhya pradesh	12/2003	203.43 -	203.43	208.20	10/2008 -	03/2012	41	0/0
192	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	120.70	04/2008 -	03/2012	47	0/0
193	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	180.20	04/2008 -	03/2012	47	0/0
194	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	154.00	04/2010 -	03/2012	23	0/0
195	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	594.20	07/2010 -	05/2012	22	0/0
196	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27	0/0
197	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	90.44	09/2008 -	06/2012	45	0/0
198	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	170.10	10/2008 -	06/2012	44	0/0
199	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93 -	300.93	294.10	10/2009 -	06/2012	32	0/0
200	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	412.70	12/2009 -	06/2012	30	0/0
201	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	168.20	09/2010 -	06/2012	21	0/0
202	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	1,527.00	10/2011 -	06/2012	8	0/0
203	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	2,691.00	11/2011 -	06/2012	7	0/0
204	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	132.20	05/2008 -	08/2012	51	0/0
205	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	510.50	10/2011 -	08/2012	10	0/0
206	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	184.60	06/2010 -	10/2012	28	0/0
207	LAKHNAADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	233.40	09/2009 -	10/2012	37	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
208	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	10/2012	16	0/0
209	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	177.40	07/2008 -	12/2012	53	0/0
210	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Orissa	04/2000	263.27 -	263.27	254.69	02/2004 -	12/2012	106	0/0
211	Bijapur-Hungund Section - [N24000137]NHAI,Karnataka	09/2010	748.00 -	748.00	1,114.00	09/2010 -	03/2013	30	0/0
212	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	348.16	118.00	09/2007 -	06/2013	69	0/0
213	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	846.50	11/2012 -	06/2013	7	0/0
214	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	31.92	04/2009 -	07/2013	51	0/0
215	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	39.26	11/2008 -	07/2013	56	0/0
216	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	179.20	02/2010 -	07/2013	41	0/0
217	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	10/2013	14	0/0
218	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	40.71	11/2008 -	12/2013	61	0/0
219	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	1.76	09/2007 -	04/2014	79	0/0
220	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	0.34	07/2009 -	04/2014	57	0/0
Total			31,999.93 -	34,165.18	35,771.95				0/0
<u>Shipping & Ports</u>									
221	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP.,Gujarat	01/2002	165.00 165.00	165.00	124.37	12/2005 01/2008	10/2011	70	0/0
222	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.79	04/2011 06/2011	11/2011	7	0/0
223	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP.,Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	7	0/0
224	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 -	3,500.00	-	01/2012 -	03/2012	2	0/0
225	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST,Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	5	0/0

List of Delay Project (w.r.t Original)

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
226	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 -	1,460.00	610.00	12/2010 -	09/2012	21	0/0
227	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29	0/0
228	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25	0/0
229	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24	0/0
230	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52	0/0
231	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93	0/0
	Total		8,373.42 -	9,198.57	1,547.18				0/0
Telecommunications									
232	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00 -	425.51	141.31	12/2005 -	12/2011	72	0/0
233	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	23.30	10/2010 -	03/2012	17	0/0
	Total		634.00 -	809.51	164.61				0/0
Urban Development									
234	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	12/2011 -	12/2013	24	6/6
	Total		6,395.00 -	11,609.00	2,267.57				6/6
Water Resources									
235	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	60	0/0
	Total		542.90 -	1,187.00	35.49				0/0
Grand Total			320,056.39	390,393.26	218,197.05				663/1417

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
<u>Civil Aviation</u>									
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,552.74	01/2011 -	12/2011	11(O)	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	1,530.56	05/2011 -	03/2012	10(O)	0/0
3	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.45	153.41	01/2011 -	06/2012	17(O)	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	52.75	05/2012 -	08/2012	3(O)	0/0
5	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	324.99	06/2013 -	06/2013	0(O)	0/0
	Total		5,021.58 -	5,611.06	3,614.45				0/0
<u>Coal</u>									
6	KARMA OCP - [N06000088]JCL,Jharkhand	06/2009	162.46 -	162.46	26.36	03/2014 -	03/2014	0(O)	0/0
7	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	1.14	03/2015 -	03/2015	0(O)	0/0
8	JALAGAM VENGALA RAO OCP - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	-	03/2015 03/2015	03/2015	0(R3)	0/0
9	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 1,131.28	1,131.28	-	03/2018 -	03/2018	0(O)	0/0
	Total		1,903.56 -	1,903.56	27.50				0/0
<u>Fertilisers</u>									
10	CAPACITY ENHANCEMENT OF VIJAIPUR-I PLANTS - [N08000007]NFL,Madhya pradesh	09/2008	325.00 -	325.00	84.31	07/2011 -	11/2011	4(O)	0/0
11	CAPACITY ENHANCEMENT OF AMMONIA AND UREA PLANT VIJ - [N08000008]NFL,Madhya pradesh	09/2008	438.00 -	438.00	105.79	07/2011 -	03/2012	8(O)	0/0
	Total		763.00 -	763.00	190.10				0/0
<u>Steel</u>									
12	1.2 MTPA PELLET PLANT DONIMALAI - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	-	04/2013 -	04/2013	0(O)	0/0
13	7.0 MTPA KUMARASWAMY IRON ORE MINE - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	-	05/2013 -	05/2013	0(O)	0/0
	Total		1,470.55 -	1,470.55	.00				0/0
<u>Petroleum</u>									

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
14	REFRIGERATED LPG STORAGE AT JNPT - [N16000083]BPCL,Maharashtra	06/2008	304.40	304.40	-	06/2010	09/2011	15(O)	0/0
15	North Tapti Gas Field Development - [N16000096]ONGC,Multi State	07/2008	589.70 755.76	755.76	528.92	03/2011 05/2011	06/2011	1(R3)	0/0
16	Integrated Sugar, Ethanol, Cogen Power Plant at Sugauli - [N16000102]HPCL,Bihar	06/2009	613.54	727.88	671.52	12/2010	06/2011	6(O)	0/0
17	DIESEL HYDRO TREATMENT PROJECT,BRPL DHALIGAON - [N16000009]BRPL,Assam	06/2006	1,431.91 1,646.39	1,690.13	1,596.80	09/2009	08/2011	23(O)	0/0
18	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 299.00	299.00	258.42	02/2011 08/2011	08/2011	0(R3)	0/0
19	DAHEJ-VI JAYPUR PIPE LINE PROJECT(PHASE-II) - [N16000052]GAIL,Multi State	11/2007	4,429.38	2,340.00	2,273.78	10/2010 09/2011	09/2011	0(R2)	0/0
20	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00	3,284.00	-	09/2011	09/2011	0(O)	0/0
21	HEERA AND SOUTH HEERA RE-DEVELOPMENT PROJECT - [N16000024]ONGC,Maharashtra	09/2006	2,305.30 700.00	3,005.30	2,416.96	06/2010 06/2010	10/2011	16(R3)	0/0
22	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16	2,800.00	2,520.91	12/2008 12/2008	11/2011	35(R3)	0/0
23	BRANCH PIPELINE FROM KSPL VIRAMGAON TO KANDLA - [N16000059]IOCL,Gujarat	02/2009	250.00 349.00	250.00	207.27	03/2013 03/2013	12/2011	-15(R1)	0/0
24	HEERA RECONSTRUCTION - [N16000062]ONGC,Maharashtra	05/2008	706.70	706.70	648.52	04/2010	12/2011	20(O)	0/0
25	NEELAM RECONSTRUCTION - [N16000063]ONGC,Maharashtra	05/2008	305.08	305.08	261.78	04/2011	12/2011	8(O)	0/0
26	CONSTRUCTION OF TANKS AND BLENDING FACILITY AT VAD - [N16000115]IOCL,Gujarat	02/2009	267.00	267.00	181.30	09/2012	12/2011	-9(O)	0/0
27	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 12,160.26	12,160.26	7,080.12	01/2012	01/2012	0(O)	0/0
28	MNW-NF BRIDGE PROJECT - [N16000045]ONGC,Maharashtra	05/2008	175.21	162.12	71.60	03/2009 02/2012	02/2012	0(R3)	0/0
29	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02	740.02	412.78	03/2010 03/2012	03/2012	0(R1)	0/0
30	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,173.84	09/2010 03/2012	03/2012	0(R3)	0/0
31	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18	6,652.22	0.26	01/2013	03/2012	-10(O)	0/0
32	SETTING UP 100 MW COMMERCIAL WIND ENERGY GENERATION - [N16000126]GAIL,Multi State	05/2011	616.00	616.00	-	03/2012	03/2012	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
33	INTEGRATED DEV OF G1 and GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,218.01	2,218.01	1,237.61	04/2006 05/2011	05/2012	12(R3)	0/0
34	CONSTRUCTION OF NEW PROCESS COMPLEX MHN - [N16000030]ONGC, Maharashtra	01/2007	2,853.29 6,326.40	6,326.40	3,771.00	05/2010 05/2012	05/2012	0(R3)	0/0
35	REVAMPING OF WIN PLATFORM AT MH ASSET - [N16000044]ONGC, Maharashtra	05/2008	333.40 837.54	656.51	49.20	05/2010 04/2012	05/2012	1(R3)	0/0
36	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	233.77	07/2010 05/2012	05/2012	0(R3)	0/0
37	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	1,802.20	08/2010 03/2012	06/2012	3(R3)	0/0
38	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC, Multi State	01/2010	2,163.64 -	2,163.64	554.69	06/2012 -	06/2012	0(O)	0/0
39	Wind Power Project - [N16000119]ONGC, Rajasthan	07/2010	1,106.00 -	1,106.00	-	06/2012 -	06/2012	0(O)	0/0
40	ADDITIONAL GAS PROCESSING FACILITI AT HAZIRA - [N16000065]ONGC, Gujarat	02/2008	370.11 -	370.11	82.78	04/2011 -	07/2012	15(O)	0/0
41	Polypropylene unit - [N16000113]Mangalore Refin, Karnataka	05/2009	1,803.78 -	1,803.78	433.70	07/2012 -	07/2012	0(O)	0/0
42	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC, Tripura	07/2008	288.04 288.04	288.04	122.65	08/2012 -	08/2012	0(O)	0/0
43	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC, Maharashtra	01/2009	7,133.39 -	6,855.93	2,442.94	09/2012 -	09/2012	0(O)	0/0
44	Construction of 6 ETPs - [N16000117]ONGC, Gujarat	03/2009	302.26 -	302.26	21.14	09/2012 -	09/2012	0(O)	0/0
45	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	210.53	09/2011 -	12/2012	15(O)	0/0
46	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC, Maharashtra	10/2008	1,797.35 -	977.00	84.18	12/2011 -	01/2013	13(O)	0/0
47	Development of SB-14 field - [N16000116]ONGC, Multi State	01/2011	410.44 -	410.44	-	11/2012 -	01/2013	2(O)	0/0
48	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC, Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	6,767.62	05/2010 03/2013	03/2013	0(R3)	0/0
49	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	398.22	03/2013 -	03/2013	0(O)	0/0
50	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	03/2013	0(O)	0/0
51	Development of Cluster-7 Fields - [N16000104]ONGC, Multi State	03/2010	3,241.03 -	3,241.03	1.50	03/2013 -	03/2013	0(O)	0/0
52	Development of BHE and BH-35 Area. - [N16000118]ONGC, Multi State	08/2010	372.11 -	372.11	-	03/2013 -	03/2013	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
53	KOCHI KOOTTANAD BANGLORE MANGLORE PIPELINE PH-II - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	2,915.00	-	10/2012 -	03/2013	5(O)	0/0
54	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	861.79	-	05/2013 -	05/2013	0(O)	0/0
55	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	331.20	-	08/2013 -	08/2013	0(O)	0/0
56	Wax Project - [N16000101]NRL, Assam	06/2010	576.60 -	576.60	13.77	12/2013 12/2013	12/2013	0(R3)	0/0
57	Development of WO-16 Cluster Fields - [N16000105]ONGC, Multi State	06/2010	2,523.00 -	2,523.00	-	01/2014 -	01/2014	0(O)	0/0
58	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94 -	202.94	-	01/2014 -	01/2014	0(O)	0/0
59	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL, Multi State	08/2010	8,140.00 -	8,140.00	254.69	02/2014 -	02/2014	0(O)	0/0
60	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	-	12/2014 -	12/2014	0(O)	0/0
61	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	-	12/2014 -	12/2014	0(O)	0/0
62	Mehesana Redevelopment - [N16000121]ONGC, Gujarat	11/2010	3,823.00 -	3,823.00	-	04/2015 -	04/2015	0(O)	0/0
63	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL, Haryana	11/2007	281.07 -	281.07	3.29	10/2010 -	-	-	0/0
64	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL, Andhra Pradesh	01/2009	756.00 898.00	898.00	748.06	09/2011 03/2012	12/2011	-3(R3)	0/0
65	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL, Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	696.82	09/2011 03/2012	-	-	0/0
66	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	5.76	- -	-	-	0/0
	Total		108,394.43 -	115,772.49	40,240.90				0/0
Power									
67	TRANSMISSION SYSTEM ASSOCIATED WITH URI-II - [N18000023]PGCIL, J & K	10/2006	238.25 -	227.03	213.52	05/2011 05/2011	11/2011	6(R3)	0/0
68	EASTERN REGION STRENGTHENING SCHEME-II - [N18000033]PGCIL, Multi State	12/2007	227.52 -	227.52	136.10	06/2010 -	12/2011	18(O)	0/0
69	TR. SYSTEM ASSOCIATED WITH CHAMERA III HEP - [N18000064]PGCIL, Multi State	04/2008	297.37 -	297.37	300.13	07/2011 -	12/2011	5(O)	0/0
70	CHAMERA, STAGE-III (NHPC) - [180100241]NHPC, Himachal Pr.	08/2005	1,405.63 -	1,405.63	1,694.56	08/2010 -	02/2012	18(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
71	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,J & K	08/2005	1,724.79	1,724.79	1,575.98	11/2009	02/2012	27(O)	0/0
72	WESTERN REGION STRENGTHENING SCHEME-X - [N18000049]PGCIL,Multi State	02/2009	664.96	664.96	304.39	02/2012	02/2012	0(O)	0/0
73	WESTERN REGION SYSTEM STRENGTHENING SCHEME-XI - [N18000051]PGCIL,Multi State	02/2009	409.50	409.50	60.03	02/2012	02/2012	0(O)	0/0
74	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVII - [N18000058]PGCIL,Rajasthan	02/2009	210.79	210.79	165.10	08/2011	02/2012	6(O)	0/0
75	TR. SYSTEM ASSOCIATED WITH TUTICORIN JV TPS - [N18000062]PGCIL,Multi State	02/2009	353.57	353.57	213.40	07/2010 02/2012	02/2012	0(R3)	0/0
76	SYSTEM STRENGTHENING -XI IN SOUTHERN REGION - [N18000067]PGCIL,Multi State	03/2009	196.10	196.10	86.60	07/2011	02/2012	7(O)	0/0
77	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA - [N18000068]PGCIL,Multi State	02/2009	1,347.32	1,347.32	888.20	02/2012	02/2012	0(O)	0/0
78	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pr.	10/2005	2,304.52	2,304.52	1,590.26	10/2010	03/2012	17(O)	0/0
79	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIII - [N18000054]PGCIL,Multi State	02/2009	317.69	317.69	62.30	11/2011	03/2012	4(O)	0/0
80	System Strengthening -X of SR - [N18000086]PGCIL,Multi State	12/2009	276.61	276.61	101.30	04/2012	04/2012	0(O)	0/0
81	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12	1,075.12	351.80	05/2012	05/2012	0(O)	0/0
82	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G - [N18000078]PGCIL,Multi State	07/2009	1,736.36	1,736.36	414.30	06/2012	06/2012	0(O)	0/0
83	IMMEDIATE EVACUATION SYSTEM FOR NABINAGAR TPS - [N18000082]PGCIL,Bihar	02/2010	215.86	215.86	121.30	06/2012	06/2012	0(O)	0/0
84	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34	232.34	10.88	06/2012	06/2012	0(O)	0/0
85	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95	2,360.95	1,722.70	08/2012	08/2012	0(O)	0/0
86	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33	7,075.33	4,226.70	08/2012	08/2012	0(O)	0/0
87	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83	1,216.83	451.10	08/2012	08/2012	0(O)	0/0
88	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12	4,824.12	2,148.00	10/2012	10/2012	0(O)	0/0
89	MAUDA TRANSMISSION SYSTEM - [N18000084]PGCIL,Maharashtra	02/2010	469.38	469.38	197.70	10/2012	10/2012	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
90	INTERCONNECTION BETWEEN ELECTRICAL GRIDS OF INDIA AND B - [N18000089]PGCIL,Multi State	10/2010	160.32 -	160.32	13.70	10/2012 -	10/2012	0(O)	0/0
91	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,J & K	08/2006	611.02 -	611.02	683.53	08/2010 -	11/2012	27(O)	0/0
92	TRANSMISSION SYSTEM OF VINDHYACHAL-IV AND RIHAND-I - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	353.10	11/2012 -	11/2012	0(O)	0/0
93	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	267.20	11/2012 -	11/2012	0(O)	0/0
94	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	124.00	11/2012 -	11/2012	0(O)	0/0
95	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,061.38	1,027.42	09/2009 -	12/2012	39(O)	0/0
96	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME - [N18000046]PGCIL,Multi State	12/2008	7,031.88 -	7,031.88	2,687.00	12/2012 -	12/2012	0(O)	0/0
97	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	266.43	11/2011 -	12/2012	13(O)	0/0
98	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	266.60	11/2011 -	12/2012	13(O)	0/0
99	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	144.50	02/2012 -	12/2012	10(O)	0/0
100	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	412.00	12/2012 -	12/2012	0(O)	0/0
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	25.54	01/2013 -	01/2013	0(O)	0/0
102	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	22.90	01/2013 -	01/2013	0(O)	0/0
103	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	381.90	09/2010 -	03/2013	30(O)	0/0
104	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Orissa	09/2010	2,074.86 -	2,074.86	171.60	03/2013 -	03/2013	0(O)	0/0
105	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	107.00	04/2013 -	04/2013	0(O)	0/0
106	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	8.71	04/2013 -	04/2013	0(O)	0/0
107	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 623.44	623.44	74.52	01/2012 07/2013	07/2013	0(R3)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64	752.64	83.30	07/2013	07/2013	0(O)	0/0
109	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
110	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000108]PGCIL,Madhya Pradesh	07/2011	181.93	181.93	-	07/2013	07/2013	0(O)	0/0
111	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM - [N18000090]PGCIL,Andhra Pradesh	12/2010	779.21	779.21	116.00	08/2013	08/2013	0(O)	0/0
112	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII - [N18000091]PGCIL,Multi State	12/2010	209.78	209.78	18.55	08/2013	08/2013	0(O)	0/0
113	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52	1,719.52	135.80	08/2013	08/2013	0(O)	0/0
114	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19	184.19	132.80	11/2011	09/2013	22(O)	0/0
115	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya Pradesh	08/2011	425.51	425.51	-	10/2013	10/2013	0(O)	0/0
116	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12	1,585.12	66.40	11/2013	11/2013	0(O)	0/0
117	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARK - [N18000104]PGCIL,Jharkhandd	10/2011	558.26	558.26	-	11/2013	11/2013	0(O)	0/0
118	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000110]PGCIL,Multi State	08/2011	1,391.97	1,391.97	-	11/2013	11/2013	0(O)	0/0
119	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Orissa	12/2010	2,743.19	2,743.19	216.21	12/2013	12/2013	0(O)	0/0
120	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34	1,366.34	-	12/2013	12/2013	0(O)	0/0
121	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97	1,391.97	-	12/2013	12/2013	0(O)	0/0
122	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25	2,569.25	52.50	03/2014	03/2014	0(O)	0/0
123	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87	1,961.87	31.00	05/2014	05/2014	0(O)	0/0
124	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49	487.49	-	06/2014	06/2014	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
125	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34	1,637.34	-	08/2014	08/2014	0(O)	0/0
126	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19	11,130.19	3,073.60	08/2013	09/2014	13(O)	0/0
127	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13	1,940.13	-	09/2014	09/2014	0(O)	0/0
128	TRANS SYSTEM FOR DEVELOPMENT OF POOLING STN IN NR - [N18000077]PGCIL,West Bengal	04/2010	4,404.57	4,404.57	-	01/2015	01/2015	0(O)	0/0
129	KISHANGANGA HEP - [N18000031]NHPC,J & K	07/2007	2,238.67	3,642.04	999.75	07/2014	01/2016	0(R3)	0/0
	Total		93,636.58	95,231.16	28,999.91				0/0
Railways									
130	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Orissa	04/1999	166.16	243.40	-	-	12/2010	22(R1)	0/0
131	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Orissa	04/2000	133.41	211.90	188.18	02/2009	12/2010	21(R1)	0/0
132	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62	221.90	161.07	03/2009	12/2010	9(R1)	0/0
133	ALIGARH-GAZIABAD 3RD LINE DOUBLING (RVNL) - [N22000034]RVNL,Uttar Pradesh	04/2003	230.73	399.50	295.24	03/2009	12/2010	24(R1)	0/0
134	BHARUCH-SAMNI-DAHEJ GAUGE CONVERSIN - [N22000081]RVNL,Gujarat	09/2005	200.80	200.80	269.02	12/2008	12/2010	-	0/0
135	BILASPUR-URKURA (DL) - [220100321]RVNL,Chhatisgarh	04/1997	151.52	273.00	-	-	03/2011	24(R1)	0/0
136	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL) - [N22000027]RVNL,Multi State	04/2005	240.00	329.70	267.79	03/2009	03/2011	15(R1)	0/0
137	PANSPURA-KHARAGPUR 3D LINE - [N22000076]RVNL,West Bengal	09/2007	252.50	252.50	-	12/2009	11/2011	21(O)	0/0
138	GUNA-ETAWAH(NCR), NL - [220100007]NCR,Multi State	04/1985	158.77	540.96	558.07	03/1994	12/2011	213(O)	0/0
139	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Orissa	04/1993	100.00	208.68	187.44	-	12/2011	117(O)	0/0
140	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74	843.91	492.29	02/2009	12/2011	34(O)	0/0
141	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Orissa	04/1994	355.38	1,100.00	176.85	-	12/2011	-	0/0
142	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Orissa	04/1996	301.64	735.10	-	09/2009	12/2011	27(R1)	0/0
143	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00	482.70	250.13	03/2013	12/2011	-15(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
144	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,062.36	1,577.46	1,190.60	- -	02/2012	-	0/0
145	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 762.33	762.33	424.94	- 12/2009	02/2012	26(R1)	0/0
146	Dakshin-barasat-lakshmikantapur (ER) - [N22000116]ER,West Bengal	04/2009	259.51 -	259.51	66.31	12/2011 -	02/2012	2(O)	0/0
147	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 637.46	634.13	542.82	03/1995 -	03/2012	204(O)	0/0
148	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 407.78	725.90	512.65	- -	03/2012	-	0/0
149	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhandd	04/1995	184.00 254.07	675.00	466.87	- 12/2011	03/2012	3(R3)	0/0
150	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	262.82	208.83	- 03/2012	03/2012	0(R3)	0/0
151	MUZAFFARPUR-SITAMARHI(NL),ECR - [220100194]ECR,Bihar	04/1997	100.00 322.29	411.22	422.17	- -	03/2012	-	0/0
152	JAYNAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 335.77	903.56	565.87	- -	03/2012	-	0/0
153	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 283.95	427.89	340.51	- 03/2011	03/2012	12(R3)	0/0
154	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	195.66	- -	03/2012	-	0/0
155	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	933.24	- -	03/2012	-	0/0
156	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	324.90	188.15	03/2010 -	03/2012	24(O)	0/0
157	CONSTRUCTION OF NEW LINE FROM HARMATI-TANAGAR/NAR - [N22000083]NEFR,Arunachal Pr.	09/1996	156.00 -	254.29	202.04	- -	03/2012	-	0/0
158	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR & G'BA - [N22000094]RE,Uttar Pradesh	02/2008	171.10 -	171.10	137.47	03/2012 -	03/2012	0(O)	0/0
159	ELECTRIFICATION OF MORADABAD-ROZA - [N22000095]RE,Uttar Pradesh	12/2004	129.17 -	220.00	218.15	03/2011 -	03/2012	12(O)	0/0
160	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 -	723.27	383.13	06/2005 07/2011	03/2012	8(R3)	0/0
161	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhandd	04/2008	167.73 -	167.73	36.32	03/2012 -	03/2012	0(O)	0/0
162	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 154.30	499.16	146.26	03/2007 03/2007	06/2012	63(R1)	0/0
163	NANGALDAM-TALWARA(NL),NR - [220100188](NR),Multi State	03/1981	37.68 450.00	730.00	326.92	- 07/2012	07/2012	0(R3)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
164	CONV.OF 1500V DC TRACTION TO 25 KV AC,WR - [220100233]RE,Maharashtra	07/1996	273.67 1,160.52	1,302.12	579.88	- -	12/2012	-	0/0
165	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241](NR),Punjab	07/1998	248.44 576.27	1,104.40	789.49	12/2012 -	12/2012	0(O)	0/0
166	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 -	1,211.22	396.24	03/2005 12/2008	12/2012	48(R1)	0/0
167	JIND-SONEPAT (NL),NR - [220100280](NR),Haryana	01/2004	190.81 238.56	401.83	338.99	- 03/2012	12/2012	9(R3)	0/0
168	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 -	341.41	241.91	- -	12/2012	-	0/0
169	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 -	981.00	556.03	03/2009 -	12/2012	45(O)	0/0
170	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 -	1,389.98	1,013.11	10/2007 -	12/2012	62(O)	0/0
171	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	687.20	400.42	03/2010 -	12/2012	33(O)	0/0
172	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 -	207.52	105.98	12/2012 -	12/2012	0(O)	0/0
173	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	152.76	- -	03/2013	-	0/0
174	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 -	1,029.00	697.02	- -	03/2013	-	0/0
175	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 -	603.04	48.10	03/2012 -	03/2013	12(O)	0/0
176	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.13 -	394.14	0.49	03/2013 -	03/2013	0(O)	0/0
177	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 495.74	495.74	135.28	- 06/2013	06/2013	0(R3)	0/0
178	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 -	189.97	64.10	12/2011 -	11/2013	23(O)	0/0
179	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	180.24	- -	12/2013	-	0/0
180	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 -	223.01	83.63	12/2012 -	12/2013	12(O)	0/0
181	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 -	4,091.33	2,820.12	03/2009 -	12/2013	57(O)	0/0
182	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 -	1,655.80	834.94	12/2008 -	03/2014	63(O)	0/0
183	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 -	1,717.29	771.94	- -	03/2014	-	0/0
184	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 -	1,141.75	217.04	03/2014 -	03/2014	0(O)	0/0
185	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,393.49	3.61	04/2014 -	03/2014	-1(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
186	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 -	653.19	9.50	03/2014 -	03/2014	0(O)	0/0
187	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 -	516.23	80.97	03/2014 -	03/2014	0(O)	0/0
188	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	195.64	03/2014 -	03/2014	0(O)	0/0
189	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088](NR),Uttar Pradesh	04/2006	325.00 -	369.90	107.60	03/2010 06/2014	06/2014	0(R3)	0/0
190	RAIL-CUM-ROAD BRIDGE OVER RIVER BRAHAMAPUTRA BRIDG - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	3,230.01	2,240.65	04/2008 03/2014	12/2014	9(R3)	0/0
191	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 -	324.66	168.07	- -	03/2015	-	0/0
192	MUMBAI URBAN TRANSPORT PROJECT PHASE-II, MTP - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 -	5,300.00	315.09	03/2014 -	03/2015	12(O)	0/0
193	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 -	829.74	-	03/2015 -	03/2015	0(O)	0/0
194	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 -	850.00	8.44	03/2015 -	03/2015	0(O)	0/0
195	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.57	52.63	12/2015 -	12/2015	0(O)	0/0
196	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	3,056.85	493.47	03/2011 03/2014	03/2016	24(R3)	0/0
197	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	-	03/2014 -	03/2016	24(O)	0/0
198	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	-	03/2016 -	03/2016	0(O)	0/0
199	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	-	03/2016 -	03/2016	0(O)	0/0
200	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	0.02	03/2016 -	06/2016	3(O)	0/0
201	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133](NR),J & K	03/1995	2,500.00 8,000.00	20,000.00	7,326.12	03/2001 -	12/2017	201(O)	0/0
202	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 -	356.87	149.70	- 03/2010	-	-	0/0
203	New BG line Rly line from Eklakhi-Balurghat includ - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	415.23	234.70	- -	-	-	0/0
204	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	87.11	12/2012 -	-	-	0/0

List of Projects Without Milestones

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
205	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00	579.37	595.36	-	-	-	0/0
206	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 462.67	1,010.00	99.45	-	-	-	0/0
207	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00	944.55	478.17	-	-	-	0/0
208	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30	1,038.00	570.21	03/1998	-	-	0/0
209	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55	945.73	622.93	-	-	-	0/0
210	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1995	227.00	997.58	65.16	-	-	-	0/0
211	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	537.47	93.80	-	-	-	0/0
212	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00	363.26	0.27	07/2008	-	-	0/0
213	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhandd	03/1999	491.19 1,099.20	1,099.20	1,113.09	07/2005	-	-	0/0
214	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00	1,214.00	70.88	-	-	-	0/0
215	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	776.00	269.00	-	-	-	0/0
216	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23	162.87	87.26	-	-	-	0/0
217	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258](NR),Multi State	03/2002	409.00 625.30	847.76	815.43	06/2007	-	-	0/0
218	REINGUNTA-GUNTAKAL(RE) - [220100260]RVNL,Andhra Pradesh	06/2000	168.34	296.20	307.08	04/2003 03/2010	-	-	0/0
219	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00	548.96	476.32	-	-	-	0/0
220	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00	695.00	9.44	-	-	-	0/0
221	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 519.67	607.09	338.76	-	-	-	0/0
222	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00	901.62	0.29	-	-	-	0/0
223	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhandd	04/2002	459.91	418.17	77.24	-	-	-	0/0
224	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.00	210.90	-	-	-	0/0
225	PRATAPNAGAR-CHOTA UDAIPUR (GC) (WR) - [220100322]WR,Gujarat	04/2005	148.61	227.52	258.96	03/2008 03/2009	-	-	0/0
226	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Orissa	02/1996	57.94	173.49	176.57	03/1998 08/2005	-	-	0/0
227	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Orissa	04/1998	183.23	638.00	-	02/2015	-	-	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
228	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.60	0.76	- -	-	-	0/0
229	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhandd	03/1997	186.92 -	261.70	24.65	02/2006 -	-	-	0/0
230	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	732.80	315.49	03/2008 06/2008	-	-	0/0
231	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDIL'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 -	900.00	211.41	- -	-	-	0/0
232	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 -	900.00	443.75	- -	-	-	0/0
233	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 -	227.40	22.66	- -	-	-	0/0
234	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 -	582.83	89.12	- -	-	-	0/0
235	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	529.88	35.45	- -	-	-	0/0
236	RAJPIPLA-ANKELASHWAR, WR (GC) - [N22000096]WR,Gujarat	04/2006	196.97 -	196.97	178.19	03/2011 -	-	-	0/0
237	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 -	359.86	0.71	- -	-	-	0/0
238	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	171.36	03/2011 -	-	-	0/0
239	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 284.27	548.95	466.60	06/1999 03/2011	-	-	0/0
240	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	495.44	167.16	03/2004 -	-	-	0/0
241	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 281.20	302.23	329.27	- 03/2011	-	-	0/0
242	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhandd	04/1997	194.07 -	456.45	289.43	06/2004 04/2005	-	-	0/0
243	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	925.00	504.78	05/2008 03/2011	-	-	0/0
244	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 214.09	227.42	250.82	12/2009 03/2011	-	-	0/0
245	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,015.84	720.94	- 12/2010	-	-	0/0
246	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	436.49	- -	-	-	0/0
247	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 1,032.76	3,176.10	3,076.13	12/2006 08/2010	-	-	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
248	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 108.91	270.00	236.09	- 02/2011	-	-	0/0
249	REWARI-ROHTAK (NL),NR - [220100279](NR),Haryana	01/2004	149.38 330.23	475.28	471.11	02/2010 02/2011	-	-	0/0
250	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhandd	04/1996	371.36 -	452.35	375.49	- -	-	-	0/0
251	SRIGANGANAGAR-SARUPSAR (GC), NWR - [220100313]NWR,Rajasthan	04/2001	143.92 258.60	258.60	236.84	- 03/2011	-	-	0/0
252	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 -	218.19	134.12	- -	-	-	0/0
253	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 -	230.03	134.90	- -	-	-	0/0
254	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Orissa	04/2005	726.96 810.78	810.78	85.45	- -	-	-	0/0
255	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	365.15	- 03/2011	-	-	0/0
256	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 -	384.04	76.90	- -	-	-	0/0
257	BARDHAMAN-KATWA, ER (GC) - [N22000091]ER,West Bengal	04/2007	245.15 -	245.15	167.66	12/2010 03/2011	-	-	0/0
258	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 -	225.68	130.29	- 12/2010	-	-	0/0
259	Bhuj-Naliya(GC) with extension from naliyate vayor - [N22000123]WR,Gujarat	04/2008	318.24 -	468.62	2.29	03/2012 -	-	-	0/0
	Total		61,606.14 -	127,178.71	49,144.05				0/0
<u>Road Transport & Highways</u>									
260	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	200.40	10/2011 -	10/2011	0(O)	0/0
261	MADURAI-ARUPKOTTAI-TUTICORIN, KM.138.8 TO KM.264.5, NH-45 B - [240106276]NHAI,Tamil Nadu	03/2005	629.00 -	629.00	910.00	11/2010 -	11/2011	12(O)	0/0
262	LALITPUR TO SAGAR KM 132 TO KM 187, NH-26 (NHAI) - [240106300]NHAI,Madhya pradesh	12/2003	225.00 -	225.00	257.50	10/2008 -	11/2011	37(O)	0/0
263	RINGBUNDS TO JHAJHANPUR (BR-6) - [N24000030]NHAI,Bihar	12/2003	340.00 -	340.00	570.00	06/2008 -	11/2011	41(O)	0/0
264	THRISSUR TO ANGAMALI (NH-47) - [N24000037]NHAI,Kerala	12/2003	312.50 -	312.50	604.40	03/2009 -	11/2011	32(O)	0/0
265	JHANSI TO LALITPUR, NH-26 - [N24000097]NHAI,Uttar Pradesh	12/2003	276.09 -	276.09	295.30	09/2009 -	11/2011	26(O)	0/0
266	TRICHY - DINDIGUAL NH-45 - [N24000099]NHAI,Tamil Nadu	03/2005	576.00 -	576.00	658.90	07/2010 -	11/2011	16(O)	0/0
267	PONDICHERY - TINDIVANAU NH-66 - [N24000100]NHAI,Tamil Nadu	03/2005	285.00 -	285.00	359.30	07/2010 -	11/2011	16(O)	0/0
268	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	159.45	08/2004 07/2010	12/2011	17(R3)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
269	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00	207.56	167.70	08/2004	12/2011	88(O)	0/0
270	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Orissa	04/2000	225.00	241.53	82.01	04/2004	12/2011	92(O)	0/0
271	AGRA-SHIKOHABAD (GQ) KM.199.66-KM.250.50 (NH-2) - [240101173]NHAI,Uttar Pradesh	04/2000	367.49	367.49	453.68	03/2005	12/2011	81(O)	0/0
272	HALDIA PORT (PORT CONNECTIVITY) (NH-41) - [240104196]NHAI,West Bengal	04/2000	273.00	522.00	475.60	03/2005	12/2011	81(O)	0/0
273	GARHMUKTRESHWAR-MURADABAD (NHAI) OTHERS KM.93-149.25, NH-24 - [240106204]NHAI,Uttar Pradesh	12/2003	275.00	275.00	298.70	09/2007	12/2011	51(O)	0/0
274	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00	220.00	252.00	09/2007	12/2011	51(O)	0/0
275	GAGODHAR-GARAMORE(PK-IV,NH15) KM 245 TO 281.3 AND 308 TO 254 - [240106216]NHAI,Gujarat	12/2003	412.78	479.54	436.90	11/2007	12/2011	49(O)	0/0
276	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00	230.00	207.80	06/2005	12/2011	78(O)	0/0
277	VIJAYAPUR TO PATHANKOT (J&K) NH-1A KM.16.35 TO KM.50.00 - [240106235]NHAI,J & K	12/2003	193.09	166.30	183.90	03/2008	12/2011	45(O)	0/0
278	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,J & K	12/2003	166.27	193.10	153.70	03/2008	12/2011	45(O)	0/0
279	GORAKHPUR-AYODHYA (LMNHP-5),NH-28, KM.208.00 TO KM.164.00 - [240106246]NHAI,Uttar Pradesh	12/2003	227.00	227.00	403.50	10/2008	12/2011	38(O)	0/0
280	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	190.00	227.00	01/2009	12/2011	35(O)	0/0
281	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00	280.00	228.90	02/2009	12/2011	34(O)	0/0
282	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00	200.00	82.02	04/2009	12/2011	32(O)	0/0
283	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00	195.00	174.80	06/2008	12/2011	42(O)	0/0
284	KASIA TO GORAKHPUR (NH-28)(NHAI) - [240106291]NHAI,Uttar Pradesh	12/2003	242.00	242.00	427.20	12/2008	12/2011	36(O)	0/0
285	UP/BIHAR BORDER TO KASIA (NH-28)(NHAI) - [240106292]NHAI,Uttar Pradesh	12/2003	227.00	227.00	369.10	12/2008	12/2011	36(O)	0/0
286	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80	237.80	204.70	06/2008	12/2011	42(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
287	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	250.39	277.40	10/2008	12/2011	38(O)	0/0
288	LALITPUR TO SAGAR, NH-26 (NHAI) - [240106299]NHAI,Madhya pradesh	12/2003	198.00	198.00	187.30	11/2008	12/2011	37(O)	0/0
289	SAGAR BY PASS,KM 187 TO KM 211 , NH-26 (NHAI) - [240106301]NHAI,Uttar Pradesh	12/2003	151.30	151.30	174.00	10/2008	12/2011	38(O)	0/0
290	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03	251.03	283.20	10/2008	12/2011	38(O)	0/0
291	RAJMARG CHORAHA TO LAKHNANDON,KM 351 TO KM 405.7, NH-26 (NHA) - [240106305]NHAI,Madhya pradesh	12/2003	229.91	229.91	226.80	10/2008	12/2011	38(O)	0/0
292	JHAJHARPUR TO DARBANGA (BR-7) - [N24000031]NHAI,Bihar	12/2003	340.00	340.00	447.70	09/2008	12/2011	39(O)	0/0
293	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	200.00	257.90	06/2008	12/2011	42(O)	0/0
294	SITAPUR-LUCKNOW - [N24000036]NHAI,Uttar Pradesh	03/2005	322.00	322.00	553.70	06/2009	12/2011	30(O)	0/0
295	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50	196.50	236.60	06/2008	12/2011	42(O)	0/0
296	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72	264.72	255.10	06/2008	12/2011	42(O)	0/0
297	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00	245.00	486.20	03/2008	12/2011	45(O)	0/0
298	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	225.00	173.80	06/2008	12/2011	42(O)	0/0
299	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00	208.00	212.80	04/2008	12/2011	44(O)	0/0
300	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	160.00	126.20	05/2008	12/2011	43(O)	0/0
301	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00	200.00	195.60	06/2008	12/2011	42(O)	0/0
302	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00	280.00	580.70	06/2009	12/2011	30(O)	0/0
303	GORAKHPUR BYPASS, NH-28, PHASE-II EAST-WEST CORRID - [N24000085]NHAI,Uttar Pradesh	12/2003	600.24	600.24	707.10	10/2009	12/2011	26(O)	0/0
304	KOSI BRIDGE INCLUDING APPROACHES AND GUIDE BOND AN - [N24000090]NHAI,Bihar	12/2003	418.04	418.04	328.70	03/2010	12/2011	21(O)	0/0
305	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	941.00	1,901.00	01/2011	12/2011	11(O)	0/0
306	NEELAMANGALAR JUNCTION ON NH-4 SMITH NH-48 TO DEVI - [N24000103]NHAI,Karnataka	03/2005	441.00	441.00	929.00	07/2010	12/2011	17(O)	0/0
307	PATHANKOT BHOGPUR NH-1A - [N24000115]NHAI,Punjab	12/2003	229.00	284.00	344.80	05/2010	12/2011	19(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
308	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Orissa	04/2000	228.70 -	228.70	173.06	02/2004 -	12/2011	94(O)	0/0
309	ZIRAKPUR(HARYANA) - PARWANOO(HIMACHAL PRADESH) - [N24000117]NHAI, Multi State	02/2008	295.00 -	295.00	624.30	08/2010 -	12/2011	16(O)	0/0
310	END OF DURG BYPASS- CHHATISGARH/MAHARASHTRA BORDER - [N24000118]NHAI, Chhatisgarh	01/2008	464.00 -	464.00	420.00	01/2011 -	12/2011	11(O)	0/0
311	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	558.60	05/2010 -	12/2011	19(O)	0/0
312	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI, Multi State	02/2009	1,693.75 -	1,693.75	2,603.00	08/2011 -	12/2011	4(O)	0/0
313	ASSAM/WB BORDER TO GAIRKATTA (WB-1) - [N24000045]NHAI, West Bengal	12/2003	221.82 -	221.82	250.30	11/2008 -	01/2012	38(O)	0/0
314	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	385.30	12/2008 -	01/2012	37(O)	0/0
315	JHANSI TO LALITPUR, NH-25, 26 - [N24000096]NHAI, Uttar Pradesh	12/2003	355.06 -	355.06	294.70	09/2009 -	02/2012	29(O)	0/0
316	Armur to kadloor yellareddy - [N24000143]NHAI, Andhra Pradesh	02/2010	390.56 -	390.56	511.40	02/2012 -	02/2012	0(O)	0/0
317	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, Assam	12/2003	157.47 -	154.57	180.40	09/2007 -	03/2012	54(O)	0/0
318	KOTWA TO DEWAPUR(10 LMNHP), NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI, Bihar	12/2003	240.00 -	240.00	274.90	10/2008 -	03/2012	41(O)	0/0
319	ORAI TO JHANSI (UP-5), NH-25, KM.220.0 TO KM.170.0 - [240106250]NHAI, Uttar Pradesh	12/2003	340.68 -	340.68	357.70	03/2008 -	03/2012	48(O)	0/0
320	DAKOBA TO NAGAON (NH-36)(NHAI) - [240106288]NHAI, Assam	12/2003	225.00 -	225.00	257.60	06/2008 -	03/2012	45(O)	0/0
321	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI, Bihar	12/2003	332.94 -	332.94	297.30	09/2008 -	03/2012	42(O)	0/0
322	SAGAR - RAJMARG CHORAHA, KM 211 TO KM 255, NH-26 (NHAI) - [240106303]NHAI, Madhya Pradesh	12/2003	203.43 -	203.43	208.20	10/2008 -	03/2012	41(O)	0/0
323	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI, Assam	12/2003	175.96 -	175.96	120.70	04/2008 -	03/2012	47(O)	0/0
324	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, Assam	12/2003	198.16 -	198.16	180.20	04/2008 -	03/2012	47(O)	0/0
325	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]NHAI, Assam	12/2003	217.61 -	217.61	154.00	04/2010 -	03/2012	23(O)	0/0
326	TRICHY - KORUR NH-67 - [N24000101]NHAI, Tamil Nadu	03/2005	516.00 -	516.00	594.20	07/2010 -	05/2012	22(O)	0/0
327	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	930.90	02/2010 -	05/2012	27(O)	0/0
328	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	05/2012	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
329	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	795.00	804.30	05/2012	05/2012	0(O)	0/0
330	Hyderabad-yadgiri N.H no-202 - [N24000142]NHAI,Andhra Pradesh	08/2010	388.00	388.00	372.30	05/2012	05/2012	0(O)	0/0
331	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00	201.66	90.44	09/2008	06/2012	45(O)	0/0
332	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00	300.00	170.10	10/2008	06/2012	44(O)	0/0
333	GWALIOR BYPASS, NH-75,3 - [N24000088]NHAI,Madhya pradesh	12/2003	300.93	300.93	294.10	10/2009	06/2012	32(O)	0/0
334	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00	604.00	412.70	12/2009	06/2012	30(O)	0/0
335	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45	232.45	168.20	09/2010	06/2012	21(O)	0/0
336	MP/Maharashtra Border-Dhula - [N24000126]NHAI,Maharashtra	12/2009	835.00	835.00	396.70	06/2012	06/2012	0(O)	0/0
337	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	1,673.70	1,527.00	10/2011	06/2012	8(O)	0/0
338	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	2,288.00	2,691.00	11/2011	06/2012	7(O)	0/0
339	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	940.00	328.20	07/2012	07/2012	0(O)	0/0
340	PATHANKOT- BHOGPUR, KM.26-KM.70, NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	359.00	132.20	05/2008	08/2012	51(O)	0/0
341	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30	572.30	510.50	10/2011	08/2012	10(O)	0/0
342	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	1,509.10	827.30	09/2012	09/2012	0(O)	0/0
343	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	407.60	184.60	06/2010	10/2012	28(O)	0/0
344	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17	263.17	233.40	09/2009	10/2012	37(O)	0/0
345	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	1,170.52	4.41	06/2011	10/2012	16(O)	0/0
346	Hyderabad-Vijaywada Km. 40 to 221.50 Km - [N24000134]NHAI,Andhra Pradesh	04/2010	1,740.00	1,740.00	1,060.00	10/2012	10/2012	0(O)	0/0
347	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45	193.45	29.04	11/2012	11/2012	0(O)	0/0
348	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00	680.00	-	11/2012	11/2012	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
349	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, West Bengal	12/2003	225.00	225.00	177.40	07/2008	12/2012	53(O)	0/0
350	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Orissa	04/2000	263.27	263.27	254.69	02/2004	12/2012	106(O)	0/0
351	Jaipur-Tonk-Deoli - [N24000135]NHAI, Rajasthan	06/2010	792.06	792.06	390.20	12/2012	12/2012	0(O)	0/0
352	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07	625.07	666.00	01/2013	01/2013	0(O)	0/0
353	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30	671.30	116.90	02/2013	02/2013	0(O)	0/0
354	Bijapur-Hungund Section - [N24000137]NHAI, Karnataka	09/2010	748.00	748.00	1,114.00	09/2010	03/2013	30(O)	0/0
355	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI, Karnataka	09/2010	946.00	946.00	778.50	03/2013	03/2013	0(O)	0/0
356	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI, Tamil Nadu	09/2010	852.00	852.00	354.00	03/2013	03/2013	0(O)	0/0
357	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, Karnataka	09/2010	671.00	671.00	173.20	03/2013	03/2013	0(O)	0/0
358	PUNE-SATARA(NH-4) - [N24000156]NHAI, Maharashtra	10/2010	1,724.55	1,724.55	107.60	03/2013	03/2013	0(O)	0/0
359	SAMAKHIALI - GANDHIDHAM - [N24000179]NHAI, Gujarat	09/2010	805.39	805.39	7.75	03/2013	03/2013	0(O)	0/0
360	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI, Madhya Pradesh	10/2010	1,175.00	1,175.00	138.70	04/2013	04/2013	0(O)	0/0
361	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI, Andhra Pradesh	11/2010	1,585.00	1,585.00	251.90	05/2013	05/2013	0(O)	0/0
362	DEVIHALLI-HASSAN - [N24000152]NHAI, Karnataka	12/2010	453.00	453.00	140.60	05/2013	05/2013	0(O)	0/0
363	INDORE-DEWAS(NH-3) - [N24000159]NHAI, Madhya Pradesh	11/2010	325.00	325.00	138.70	05/2013	05/2013	0(O)	0/0
364	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, Bihar	05/2011	351.54	351.54	3.12	05/2013	05/2013	0(O)	0/0
365	Trichy Bypass - [N24000176]NHAI, Tamil Nadu	05/2010	374.00	374.00	21.49	05/2013	05/2013	0(O)	0/0
366	AGRA-BYPASS(NS-1/UP-1), KM 176.8-13.03 NH-2,3 - [N24000098]NHAI, Uttar Pradesh	12/2003	348.16	348.16	118.00	09/2007	06/2013	69(O)	0/0
367	AMRITSAR-PATHANKOT - [N24000147]NHAI, Punjab	05/2010	705.00	705.00	846.50	11/2012	06/2013	7(O)	0/0
368	MURADABAD-BAREILLY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00	1,267.00	-	06/2013	06/2013	0(O)	0/0
369	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, Karnataka	12/2010	480.00	480.00	-	06/2013	06/2013	0(O)	0/0
370	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, Gujarat	12/2010	1,008.50	1,008.50	596.90	06/2013	06/2013	0(O)	0/0
371	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI - [N24000173]NHAI, Tamil Nadu	06/2011	600.00	600.00	72.15	06/2013	06/2013	0(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
372	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81	385.13	31.92	04/2009	07/2013	51(O)	0/0
373	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04	280.13	39.26	11/2008	07/2013	56(O)	0/0
374	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI, Rajasthan	12/2003	275.00	281.31	179.20	02/2010	07/2013	41(O)	0/0
375	DEOLI-KOTA - [N24000148]NHAI, Rajasthan	01/2011	953.00	593.00	71.18	07/2013	07/2013	0(O)	0/0
376	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, J & K	07/2010	1,813.76	1,813.76	-	07/2013	07/2013	0(O)	0/0
377	kandla - Mundra port - [N24000175]NHAI, Gujarat	01/2011	953.88	953.88	23.41	07/2013	07/2013	0(O)	0/0
378	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI, Karnataka	03/2011	839.00	839.00	-	08/2013	08/2013	0(O)	0/0
379	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, Gujarat	03/2011	785.50	785.50	335.00	08/2013	08/2013	0(O)	0/0
380	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, Uttar Pradesh	02/2011	1,141.00	1,141.00	182.50	08/2013	08/2013	0(O)	0/0
381	Dindigul - Kumli - [N24000177]NHAI, Tamil Nadu	09/2011	485.00	485.00	-	08/2013	08/2013	0(O)	0/0
382	New 4 Lane elevated road from chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00	1,655.00	4.71	09/2013	09/2013	0(O)	0/0
383	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI, Karnataka	03/2011	359.00	359.00	12.40	09/2013	09/2013	0(O)	0/0
384	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI, Kerala	02/2010	617.00	617.00	154.50	08/2012	10/2013	14(O)	0/0
385	Tirupati - Chennai - [N24000178]NHAI, Tamil Nadu	04/2011	571.00	571.00	-	10/2013	10/2013	0(O)	0/0
386	Talegaon-amravati - [N24000140]NHAI, Maharashtra	11/2009	567.00	567.00	179.60	11/2013	11/2013	0(O)	0/0
387	ROHTAK-BAWAL - [N24000169]NHAI, Haryana	05/2011	650.00	650.00	-	11/2013	11/2013	0(O)	0/0
388	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54	511.54	40.39	11/2013	11/2013	0(O)	0/0
389	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64	167.64	40.71	11/2008	12/2013	61(O)	0/0
390	SIX LANNING OF HOSUR-KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI, Tamil Nadu	06/2011	535.00	535.00	-	12/2013	12/2013	0(O)	0/0
391	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM. - [N24000172]NHAI, Tamil Nadu	09/2011	1,250.00	1,250.00	-	12/2013	12/2013	0(O)	0/0
392	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061]NHAI, Assam	12/2003	212.00	386.10	1.76	09/2007	04/2014	79(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
393	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, Assam	12/2003	196.00	363.74	0.34	07/2009	04/2014	57(O)	0/0
394	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, Multi State	02/2011	2,498.76	2,498.76	-	08/2014	08/2014	0(O)	0/0
395	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00	807.00	455.70	10/2014	10/2014	0(O)	0/0
396	NASHRI CHANANI - [N24000162]NHAI, J & K	06/2010	2,159.00	2,159.00	-	06/2015	06/2015	0(O)	0/0
397	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, J & K	07/2010	1,987.00	1,987.00	-	07/2015	07/2015	0(O)	0/0
	Total		76,162.26	77,967.51	47,366.19				0/0
	Shipping & Ports								
398	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL, Kerala	03/2007	245.67	298.17	294.09	04/2009	02/2011	22(O)	0/0
399	Construction & License out the OPERATION, MANAG. & - [N25000038]PORT TRUST, Karnataka	06/2006	230.00	272.50	219.00	12/2010	06/2011	6(O)	0/0
400	MARINE LIQUID TERMINALS - [N25000054]ENNORE TANK, Tamil Nadu	10/2004	196.25	196.25	-	06/2006 09/2011	09/2011	0(R2)	0/0
401	ACQUISITION OF TWO NOS OF 120 B.P (AH03TYPE) AHTS - [N25000058]SHIPP., Kerala	12/2010	241.50	241.50	48.10	09/2011	09/2011	0(O)	0/0
402	ESTABLISHMENT OF VESSEL TRAFFIC SERVICES IN GULF OF KUTCH - [250100112]SHIPP., Gujarat	01/2002	165.00 165.00	165.00	124.37	12/2005 01/2008	10/2011	45(R3)	0/0
403	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP., Maharashtra	10/2007	359.44	359.44	358.79	04/2011 06/2011	11/2011	5(R3)	0/0
404	Acquisition of two nos. of 120 B.P - [N25000042]SHIPP., Maharashtra	04/2009	290.85 305.00	305.00	86.46	06/2011 01/2012	01/2012	0(R3)	0/0
405	ACQUISITION OF 6 NOS. OF 57000 DWT HANDYMAX BULK C - [N25000033]SHIPP., Maharashtra	11/2007	1,061.96 1,077.60	1,082.06	680.53	03/2012	03/2012	0(O)	0/0
406	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST, Kerala	03/2009	3,500.00	3,500.00	-	01/2012	03/2012	2(O)	0/0
407	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST, Gujarat	06/2010	277.00	277.00	0.04	03/2012	03/2012	0(O)	0/0
408	Acquisition of Two nos. of 3060 DWT - [N25000043]PORT TRUST, Maharashtra	04/2009	277.03 280.00	277.03	81.40	12/2011 05/2012	05/2012	0(R3)	0/0
409	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00	1,460.00	610.00	12/2010	09/2012	21(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
410	ACQUISITION OF 4 NOS. OF 80655 DWT PANAMAX BULK CA - [N25000031]SHIPP.,Maharashtra	08/2008	1,066.91 -	968.35	222.91	09/2012 -	09/2012	0(O)	0/0
411	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	29(O)	0/0
412	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 627.64	627.64	83.51	12/2012 -	12/2012	0(O)	0/0
413	C/O Berthing and Allied Facilities off tekra near - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	1,060.00	0.16	02/2011 -	03/2013	25(O)	0/0
414	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	24(O)	0/0
415	SETTING UP OF AN INTERNATIONAL CRUISE TERMINAL AT - [N25000047]PORT TRUST,Kerala	03/2008	375.00 272.50	272.50	-	01/2009 -	05/2013	52(O)	0/0
416	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]SHIPP.,Tamil Nadu	10/2002	150.00 600.00	600.00	67.00	03/2006 -	12/2013	93(O)	0/0
417	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,028.10	202.04	12/2013 -	12/2013	0(O)	0/0
418	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	189.92	02/2014 -	02/2014	0(O)	0/0
419	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 -	800.00	5.75	10/2008 -	-	-	0/0
420	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Orissa	12/2005	154.84 -	253.36	-	12/2007 01/2009	-	-	0/0
421	DEVELOPMENT OF IRON ORE TERMINAL - [N25000056]ENNORE PORT LTD,Tamil Nadu	09/2006	370.00 -	370.00	-	08/2010 -	-	-	0/0
422	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	821.48	10/2008 -	-	-	0/0
	Total		18,052.23 -	19,035.72	4,314.55				0/0
Telecommunications									
423	GSM EQUIPMENT OF 3125K LINES(2G) AND 625K LINES(3 - [N26000043]BSNL,Maharashtra	09/2008	1,799.94 -	1,799.94	299.77	09/2009 -	02/2010	5(O)	0/0
424	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	10/2010	7(O)	0/0
425	GSM EQUIPMENT OF 216650 LINES(2G) PH-5.1 - [N26000040]BSNL,Haryana	01/2008	192.48 -	192.48	119.45	03/2009 -	02/2011	23(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
426	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	209.79	12/2008 -	02/2011	26(O)	0/0
427	GSM EQUIPMENT OF 700K LINES(2G) AND 150K LINES(3G) - [N26000046]BSNL,Orissa	11/2007	277.34 -	377.54	308.13	03/2009 -	02/2011	23(O)	0/0
428	UTTARANCHAL TELECOM CIRCLE PHASE-VI (2G & 3G) - [N26000058]BSNL,Uttaranchal	01/2009	149.15 158.72	158.72	76.55	06/2009 -	02/2011	20(O)	0/0
429	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	155.71	01/2009 -	02/2011	25(O)	0/0
430	GSM equipment of 945000Lines (2G) 225000lines 3(G) - [N26000086]BSNL,Bihar	10/2007	366.00 -	366.00	227.39	10/2008 -	02/2011	28(O)	0/0
431	GSM equipment of 1500000Lines (2G) 264700lines 3(G) - [N26000093]BSNL,Andhra Pradesh	01/2009	922.91 -	922.91	346.90	01/2010 -	02/2011	13(O)	0/0
432	GSM equipment of 1900000Lines (2G) 335500lines 3(G) - [N26000094]BSNL,Kerala	01/2009	848.70 -	848.70	712.86	01/2010 -	02/2011	13(O)	0/0
433	GSM equipment of 614000Lines (2G) 150000lines 3(G) - [N26000095]BSNL,Tamil Nadu	01/2009	315.19 -	315.19	142.07	01/2010 -	02/2011	13(O)	0/0
434	GSM EQUIPMENT OF 900K LINES(2G) AND 300K LINES(3G) - [N26000039]BSNL,Rajasthan	06/2007	601.49 -	601.49	496.20	12/2008 -	03/2011	27(O)	0/0
435	GSM EQUIPMENT-480K LINES(2G) & 220K LINES(3G) IN - [N26000050]BSNL,Uttar Pradesh	05/2007	335.91 -	335.91	182.45	03/2009 -	03/2011	24(O)	0/0
436	GSM equipment of 900000Lines (2G) PunjabPhase V.2 - [N26000081]BSNL,Punjab	09/2008	241.49 -	241.49	123.76	09/2009 -	03/2011	18(O)	0/0
437	GSM equipment of 200000Lines (2G) UP(West)Phase V. - [N26000082]BSNL,Uttar Pradesh	10/2008	336.84 -	336.84	35.75	10/2009 -	03/2011	17(O)	0/0
438	GSM equipment of 849862Lines (2G) 150138 lines 3(G) - [N26000087]BSNL,West Bengal	02/2008	584.33 -	584.33	403.71	02/2009 -	03/2011	25(O)	0/0
439	GSM equipment of 1867000Lines (2G) 383000 lines 3(- [N26000089]BSNL,Gujarat	08/2008	868.00 -	868.00	362.62	08/2009 -	03/2011	19(O)	0/0
440	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	916.70	280.72	11/2010 -	03/2011	4(O)	0/0
441	GSM equipment of 1700000Lines (2G) 234100 lines 3(- [N26000092]BSNL,Karnataka	10/2008	677.75 719.90	719.90	461.56	10/2009 -	03/2011	17(O)	0/0
442	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 229.41	229.41	66.20	02/2007 -	08/2011	54(O)	0/0
443	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 -	08/2011	54(O)	0/0

List of Projects Without Milestones

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
444	FTTH BO-3474 /08-09 in Mumbai - [N26000078]MTNL,Maharashtra	04/2010	389.86	389.86	3.06	09/2011	09/2011	0(O)	0/0
445	PROJ.III OF NIB-II OF MESSAGING STORAGE - [260100099]BSNL,Multi State	11/2003	250.00	425.51	141.31	12/2005	12/2011	72(O)	0/0
446	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00	384.00	23.30	10/2010	03/2012	17(O)	0/0
447	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]BSNL,Maharashtra	06/2006	231.38	168.30	-	10/2007	-	-	0/0
448	MANAGED LEASED LINE NETWORK PH-VI - [N26000063]BSNL,Multi State	11/2008	350.00	350.00	-	-	-	-	0/0
449	Execution of telecom network requirement of defence - [N26000065]BSNL,Multi State	05/2006	1,077.00	1,077.00	-	03/2009	-	-	0/0
450	Procurement of 2.5G DWDM equipment - [N26000066]BSNL,Multi State	08/2006	424.00	424.00	-	03/2009	-	-	0/0
451	Procurement of 10G (40 chl) DWDM equipment - [N26000067]BSNL,Multi State	08/2006	590.10	590.10	-	03/2009	-	-	0/0
452	Procurement of 10G 40 CHL (12 chl equipped) DWDM - [N26000068]BSNL,Multi State	12/2007	545.50	545.50	-	03/2010	-	-	0/0
453	Procurement of STM-1 SDH equipment - [N26000069]BSNL,Multi State	02/2007	154.03	154.03	-	03/2010	-	-	0/0
454	Procurement of STM-16 MADM equipment - [N26000070]BSNL,Multi State	03/2008	355.92	355.92	-	03/2010	-	-	0/0
455	Procurement of STM-16 ADM equipment - [N26000071]BSNL,Multi State	02/2007	477.00	477.00	-	03/2010	-	-	0/0
456	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65	152.65	-	03/2010	-	-	0/0
457	Procurement of DXC equipment - [N26000074]BSNL,Multi State	02/2008	229.00	229.00	-	03/2010	-	-	0/0
458	GSM equipment of 975000Lines (2G) 325000 lines 3(G) - [N26000083]BSNL,Uttar Pradesh	02/2009	625.53	625.53	-	02/2010	-	-	0/0
459	GSM equipment of 1100000Lines (2G) UP East Phase - [N26000084]BSNL,Uttar Pradesh	09/2009	624.75	624.75	-	09/2010	-	-	0/0
460	GSM equipment of 375000Lines (2G) 75000lines 3(G) - [N26000085]BSNL,West Bengal	06/2008	170.23	170.23	-	06/2009	-	-	0/0
461	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13	328.12	164.58	03/2009	-	-	0/0
Total			18,952.93	19,197.68	5,419.73				0/0

Urban Development

List of Projects Without Milestones

(Oct,2011)

S.No Project		Date of Approval	Original / Revised Cost	Anticipated Cost	Cumm. Expenditure	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
462	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00	2,494.00	-	09/2014	09/2014	0(O)	0/0
463	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00	35,242.00	42.15	03/2016	03/2016	0(O)	0/0
464	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009	-	-	0/0
	Total		37,850.18	37,909.08	42.15				0/0
			-						
	<u>Water Resources</u>								
465	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90	1,187.00	35.49	12/2007	12/2012	60(O)	0/0
	Total		542.90	1,187.00	35.49				0/0
			-						
Grand Total			424,356.34	503,227.52	179,395.02				0/0

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program
LOI	Letter of Intent

LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SSS	Sardar Swaran Singh
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vaccum Distillation Unit
WHRB	Waste Heat Recovery Boiler
