

**335th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(₹ 150 crore and above)
September 2013**



NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro
LEP	Life Extension Program

LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDSCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-29
Trend and Graphical Analysis of Projects	30-42
Sector wise analysis of projects	43-43
List of All Ongoing Projects	44-72
Sector wise Graph	73-83
ANNEXURE	84-84
Central Sector Projects	85-85
List of Projects Having Expenditure More than cost	86-91
List of Projects Ahead of Schedule	92-92
List of Projects with out Original date of Commissioning	93-94
List of Projects with out date of Commissioning	95-104
List of On schedule Projects Original Schedule	105-112
List of Delayed Projects w.r.t Original Schedule	113-125
List of Projects Having cost overrun w.r.t original	126-136
List of Projects Having cost and time overrun w.r.t original	137-141
List of Projects without Milestones	142-162
List of Projects Ahead of Schedule w.r.t Latest Schedule	163-163
List of On schedule Projects w.r.t. Latest Schedule	164-172
List of Delayed Projects w.r.t Latest Schedule	173-185

EXECUTIVE SUMMARY

1. The Flash Report for September 2013 contains information on the status of the 738 Central Sector Infrastructure Projects costing ₹ 150 crore and above. During September 2013, 3 projects (1 project each in Power, Petroleum and Road Transport & Highways Sectors respectively) have reported completion.

2. During the reference month, out of 738 projects, 290 projects are delayed with respect to latest schedule and 45 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 45 projects, 15 are Mega Projects costing ₹ 1000 crore and above. The additional delays are in the range of 1 to 24 months in respect of projects relating to Coal, Telecommunication, Steel, Civil Aviation, Petroleum, Railways, Road Transport & Highways and Power Sectors.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t latest schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	Railways	283	35	4	0
2.	Road Transport And Highways	151	101	16	2
3.	Power	98	52	15	9
4.	Petroleum	83	47	3	3
5.	Coal	55	28	1	0
6.	Shipping And Ports	19	1	0	0
7.	Steel	18	12	2	1
8.	Telecommunications	13	6	1	0
9.	Civil Aviation	8	3	3	0
10.	Atomic Energy	4	4	0	0
11.	Urban Development	4	1	0	0
12.	Petrochemicals	1	0	0	0
13.	Water Resources	1	0	0	0
Total		738	290	45	15

3. Total original cost of implementation of the 738 projects was about ₹ 9,04,955.28 crore and their anticipated completion cost is likely to be ₹ 10,78,958.46 crore, which reflects overall cost overruns of ₹ 1,74,003.18 crore (19.20 % of original cost). The expenditure incurred on these projects till September 2013 is ₹ 5,05,233.32 crore, which is 46.80 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS (as on 30-09 -2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)			COST OVERRUNS (in %)
				ORIGINAL	REVISED	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	450.00	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	Railways	04/1983	36.80	274.41	703.17	1810.79
3	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	393.46	535.40	1604.01
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	111.90	1028.05	1423.98	1172.55
5	RUPSA-BANGRIPOSI (GC) (SER)	Railways	02/1996	57.94	604.04	639.97	1004.54

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute term are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS (as on 30-09-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		
				COST ORIGINAL	COST ANTICIPATED	COST OVERRUN
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	20000.00	17500.00
2	BANGALORE METRO RAIL PROJECT	Urban Development	05/2006	6395.00	11609.00	5214.00
3	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	10667.00	4381.67
4	KUDANKULAM APP (NPCIL)	Atomic Energy	12/2001	13171.00	17270.00	4099.00
5	BPUTRA BRIDGE AT BOGIBIL & LINK LINES,NEFR	Railways	09/1997	1000.00	4996.65	3996.65

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 738 projects, 6 projects are ahead of schedule, 155 are on schedule and 290 are delayed with respect to latest schedule. However, the numbers of delayed projects further increases to 301 if delay is calculated on the basis of original schedule of completion. Further, 26 projects have been sanctioned without any commissioning schedule/date and for 261 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 290 delayed projects, 66 projects have overall delay in the range of 1 to 12 months, 78 projects have a delay in the range of 13 to 24 months, 74 projects have a delay in the range of 25 to 60 months and 72 projects have a delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 30-09-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS (in months)
				ORIGINAL	ANTICIPATED	
1	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	03/1995	03/2015	240
2	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	03/1994	10/2013	235
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	03/2001	12/2017	201
4	BANKURA - DAMODAR (GC) (SER)	Railways	03/1998	03/2005	12/2016	141
5	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	03/2002	09/2013	138

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In a review of its severely affected projects in terms of time & cost overruns, Ministry of Railways has informed that outlay for Railway projects is very low of throw forward and is insufficient even to neutralize the prevailing inflation. Due to this, Railways is not in the position to fix the targets for completion of the projects. Paucity of funds has forced Railways to scale

down the targets for 2013-14 to 1525 Km against the achievement of 2315 Km and 2337 Km in 2010-11 and 2011-12 respectively.

7. The brief reasons for time overruns as reported by various other project implementing agencies are delay in land acquisition, forest clearance, delay in supply of equipment, delay in equipment erection, change in structural design, geological surprises, transfer of technology, change in scope of work, delay in shifting of utility by State Government, change of ownership of executing agency, space constraint, mobilization by vendor, delay in award of works ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as below:-

List of 5 Earliest Projects without Milestones (as on 30-09-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		EXPENDITURE CUMMULATIVE (₹; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA,LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

N.R.: Not Reported.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as below:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 30-09-2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ crore)		EXPENDITURE CUMMULATIVE (₹ crore)
				ORIGINAL	REVISED	
1	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	211.19
2	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	120.90	284.27	541.95
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	597.99
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8549.43
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	344.29

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule (as on 30.09.2013)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

N.R.: Not Reported.

10. The Sector-wise details of delays/additional delays are as under:-

i) In the **Coal Sector**, out of 55 projects, 28 projects are delayed. The project 'Kakatiya Longwall, SCCL' has reported additional delay of 12 months (however, no specific reasons have been reported by the project authority for the delay in this project).

ii) In the **Telecommunications Sector**, out of 13 projects, 6 projects are delayed. The project 'Supply Installation Testing and Commissioning of Rural Wimax, BSNL' has reported additional delay of 3 months due to frequent bandhs and contractual issues.

iii) In the **Steel Sector**, out of 18 projects, 12 projects are delayed. During the month 2 projects have reported additional delays of 1 month each, out of which 1 is Mega project. The projects 'Expansion of RINL/VSP from 3 MTPY-6.3 MTPY of liquid Steel, RINL' and '67.5 MW TG-5 Auxiliary System Emergency Power Requirement, RINL, SAIL' have reported additional delay of 1 month each (however, no specific reasons have been reported by the project authorities for the delay in these projects).

iv) In the **Railways Sector**, out of 283 projects, 35 projects are delayed. During the month 4 projects have reported additional delays in the range of 1-24 months. The projects 'Lanjigarh-Junagarh NL, ECOR' has reported additional delay of 1 month due to CRS sanction awaited; the project 'Pedapalli-Karimnagar-Nizamabad NL, SCR' has reported additional delay of 23 months due fund constraints; the project 'Ranchi-Lohardaga (GC), SER' has reported additional delay 24 months due to law & order; and the project 'Panvel Pen Doubling CR' has reported additional delay of 1 month (however, no specific reasons have been reported by the project authority for the delay in this project).

v) In the **Civil Aviation Sector**, out of 8 projects, 3 projects are delayed. All the three projects have reported delay during this month only. The project 'Construction of New International Terminal Building, AAI' has reported delay of 2 months; the projects 'Construction of New Airport at Pakyong (Sikkim), Airport, AAI' and 'Establishment of Airport Operations Control Centres of Airport Authority of India' have reported delay of 3 months each (however, no specific reasons have been reported by the project authority for the delay in these projects).

vi) In the **Petroleum Sector**, out of 83 projects, 47 projects are delayed. During the month 3 projects, all of which are Mega projects, have reported additional delays in the range of 1-19 months. The projects 'Paradip Refinery Project, IOCL' and 'Fluidized Catalytic Cracking Unit (FCCU) Revamp, IOCL' have reported additional delay of 1 month each due to delay in delivery of Air coolers and slow progress by implementing agencies; and the project 'Development of Western Oilfield-16 Cluster Fields, ONGC' has reported additional delays of 19 months due to delay in slow work progress by pipeline contractor.

vii) In the **Power Sector**, out of 98 projects, 52 projects are delayed. During the month 15 projects have reported additional delays in the range of 1-16 months, out of which 9 are Mega projects. The project 'Barh STPP Stage I, NTPC' and 'Transmission System Associated with Rampur HEP, PGCIL' have reported additional delay of 1 month each due to delay in supply of equipment and delay in generation project; the projects 'System Strengthening – XII of SR, PGCIL' has reported additional delays of 2 months due to ongoing agitation at site; the projects 'Subansiri Lower HEP, NHPC' and 'Eastern Region Strengthening Scheme-I, PGCIL' have reported additional delays of 3 months each due to delay in ongoing agitation by different pressure groups and unit shut down respectively; the projects 'Establishment of Pooling Stations at Rajgarh, PGCIL', 'Transmission System for transfer of Power from Generation, PGCIL' and 'Transmission System for transfer of Power from Generation-Part B PGCIL' have reported additional delays of 3 months each due to bad weather condition, delay in land acquisition and high compensation demand by locals respectively; the projects 'Eastern Region Transmission System-III, PGCIL', 'Transmission System for development of Pooling station in NR part of West Bengal, PGCIL' and 'Supplementary Transmission Associated with Vallur, PGCIL' have reported additional delays of 6, 11 and 12 months respectively due to delay in land acquisition; the project 'Bangaigaon Thermal Power Project, NTPC' has reported additional delays of 8 months due to delay in frequent bandhs and contractual issues; the projects 'Tapovan – Vishnugad HEP, NTPC' and 'Vishnugad Pipalkoti Hydro Electric Project, THDCL' have reported additional delays of 16 months each due to delay in heavy rainfall and heavy current monsoon; and the project 'Northern Region System Strengthening Scheme- XX, PGCIL' has reported additional delay of 1 month (however, no specific reasons have been reported by the project authority for the delay in this project).

viii) In the **Road Transport & Highways Sector**, out of 151 projects, 101 are delayed. During the month 16 projects have reported additional delays in the range of 1-15 months, out of which 2 are Mega projects. The project 'Brahmaputra Bridge, NH No.-31, NHAI' and

‘Chambal Bridge, NH-76 (RJ-5), NHAI’ have reported additional delay of 1 month each; the projects ‘Sunakhala-Ganjam (GQ) KM.338-KM.284, NH-5, NHAI’, ‘Balasore Bhadrak KM 136.5 - 199.14, NH-5, NHAI’ and ‘Deoli- Kota, NHAI’ have reported additional delays of 2 months each; the projects ‘Pathankot- Bhogpur, KM.26-KM.70, NS-38, NH-1A, NHAI’, ‘Nagaon to Dharamtul (AS-2), NHAI’, ‘Nalbari to Bijni (AS-6), NHAI’, ‘Dharamtul to Sonapur (AS-19), NHAI’, ‘Kishangarh-Ajmer-Beawer, NHAI’, ‘Cuddapah-Mydukur-Kurnool KM-167.750-356.502 KM, NHAI’, ‘Devihalli-Hassan, NHAI’ and ‘Jaipur-Reengus, NHAI’ have reported additional delays of 3 months each; and the projects ‘Jaipur-Tonk-Deoli, NHAI’, ‘Thanjaur- Trichy, NH-67, NHAI’ and ‘Bareilly – Sitapur, NHAI’ has reported additional delay of 5, 12 and 15 months respectively. The project implementing agency has not mentioned any specific reasons for delay in these projects. However, general reasons for delay in these projects are delay in land acquisition, delay in forest & environment clearance, delay in shifting of utility, poor performance of contractor, etc.


11. The status as on 30.09.2013 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	Railways	283	4
2	Road Transport And Highways	151	16
3	Power	98	15
4	Petroleum	83	3
5	Coal	55	1
6	Shipping And Ports	19	0
7	Steel	18	2
8	Telecommunications	13	1
9	Civil Aviation	8	3
10	Atomic Energy	4	0
11	Urban Development	4	0
12	Petrochemicals	1	0
13	Water Resources	1	0
	Total	738	45

Sectoral break up of on-going infrastructure projects.

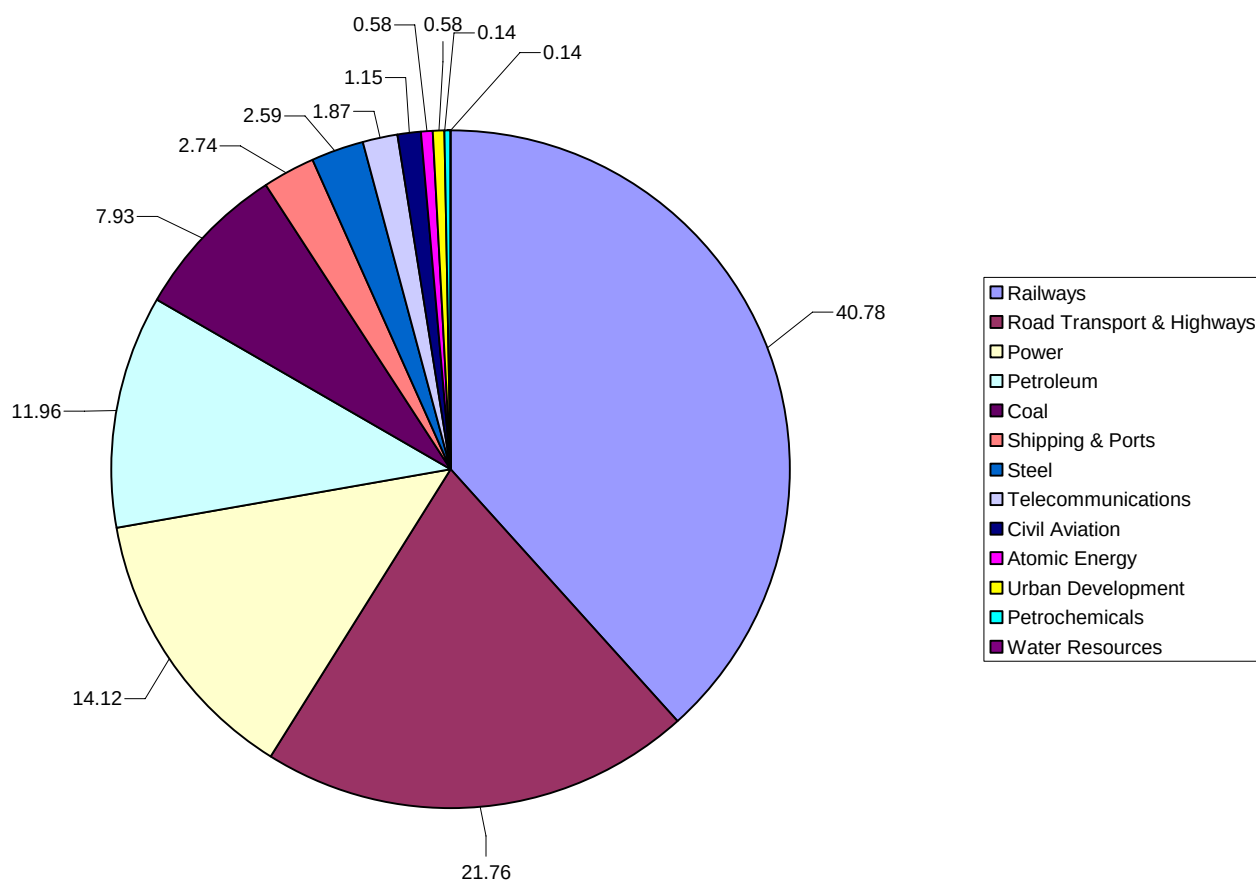

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2013-2014				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	April,2013			
	<u>Power</u>			
1	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXII(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000091]	209.78	08/2013	52.2
	<u>Railways</u>			
2	REINGUNTA-GUNTAKAL(RE)(RAIL VIKAS NIGAM LTD.) - [220100260]	168.34	04/2003	343.36
3	BILASPUR-URKURA (DL)(RAIL VIKAS NIGAM LTD.) - [220100321]	151.52	-	315
	May,2013			
	<u>Fertilisers</u>			
4	NANGAL - AMMONIA PLANT FEEDSTOCK PROJECT(NATIONAL FERTILISER LIMITED) - [N08000006]	1,478.63	01/2013	1133
	<u>Power</u>			
5	765 KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PA(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000068]	1,347.32	02/2012	1206.1
6	765KV SYSTEM FOR CENTRAL PART OF NORTHERN REGION G(POWER GRID CORPORATION OF INDIA LIMITED) - [N18000078]	1,736.36	06/2012	1240.75
	<u>Road Transport And Highways</u>			
7	ORAI TO JHANSI (UP-5),NH-25, KM.220.0 TO KM.170.0(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106250]	340.68	03/2008	400.56
	June,2013			
	<u>Railways</u>			
8	PALWAL-BHUTESWAR 3RD LINE DOUBLING(NCR)(RVNL)(RAIL VIKAS NIGAM LTD.) - [N22000027]	240.00	03/2009	334.59
9	PANSPURA-KHARAGPUR 3D LINE(RAIL VIKAS NIGAM LTD.) - [N22000076]	252.50	02/2010	249.36
	July,2013			
	<u>Petroleum</u>			
10	North Tapti Gas Field Development(OIL & NATURAL GAS CORPORATION LIMITED) - [N16000096]	589.70	03/2011	912.53
	<u>Power</u>			
11	TEESTA LOW DAM STAGE III HYDROELECTRIC POWER PROJE(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100222]	768.92	03/2007	1467.53

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2013-2014

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
12	CHUTAK HYDRO-ELECTRIC PROJECT (NHPC)(NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [N18000007]	621.26	02/2011	731.93
	August,2013			
13	INTERCONNECTION BETWEEN ELECTTRICAL GRIDS OF INDIA AND B(Power Grid Corporation of India Limited) - [N18000089]	160.32	10/2012	87.63
	<u>Railways</u>			
14	Madurai-Rameswaram-GC(Southern Railway) - [N22000200]	240.00	-	367.21
15	Krishnanagar-Bethua Dahri doubling(EASTERN RAILWAYS) - [N22000226]	151.65	03/2015	90.21
16	Dharmavaram-Pakala GC(SOUTH COST RAILWAY) - [N22000284]	294.99	-	658.53
	September,2013			
	<u>Petroleum</u>			
17	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT(INDIAN OIL CORPORATION LIMITED) - [N16000108]	341.50	02/2013	198.81
	<u>Power</u>			
18	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME(Power Grid Corporation of India Limited) - [N18000046]	7,031.88	12/2012	4591.9
	<u>Road Transport And Highways</u>			
19	GWALIOR BYPASS, NH-75,3(NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000088]	300.93	10/2009	302.7


Summary of projects in the Flash Report for the month of September, 2013

Project Implementation - Current Status:

Number of Projects in Previous Month	741
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects not Reported in current Month	1
Number of Projects Added in Current Month	1
Number of Projects in Current Month	738


Brief Analysis

Project Status with respect to Original Schedule: Out of 738 projects, 5 projects are ahead of schedule, 145 projects are on schedule and 301 projects are delayed. Of the balance, 261 projects do not have fixed dates of commissioning while 26 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

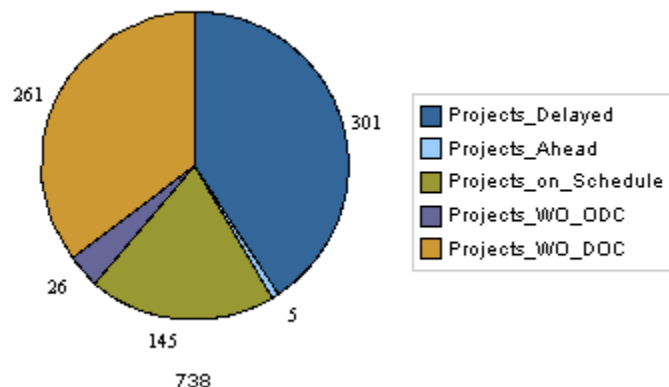

Investment Scenario

The Total Original cost of implementation of 738 projects when sanctioned, was of the order of Rs. 904955.28 crore but this was subsequently revised to Rs. 1078958.46 crore implying a cost overrun of 19.2%. The expenditure incurred on these projects till September, 2013 is Rs. 505233.32 crore, which is 46.8% of the revised cost of the projects.

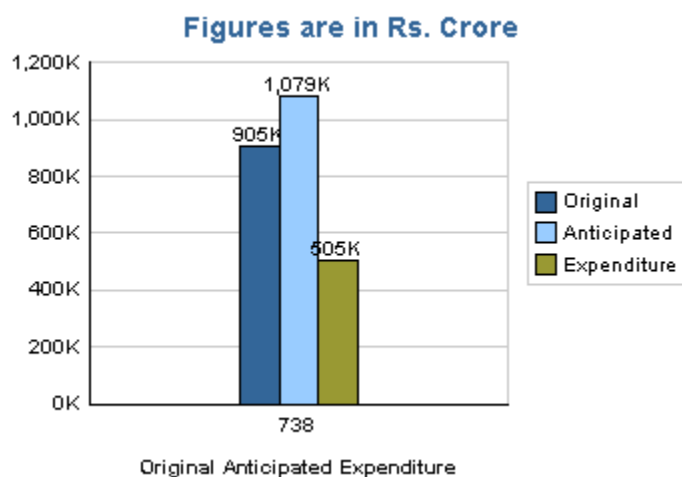

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	741
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects not Reported in Current Month	1
No of Projects added in Current Month	1
No of Projects in Current Month	738

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	301	5	145	26	261	738	40.79
Latest Approved (Date)	290	6	155	26	261	738	39.30

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	586	771,504.43	818,416.14	352,065.91	43.00	46,911.71	6.10
Latest Approved (RCE)	152	202,426.73	260,542.32	153,167.41	58.80	58,115.59	28.70
Total (RCE)	738	973,931.16	1,078,958.46	505,233.32	46.83	105027.3	10.78
Original Cost of All Projects							
Original Cost	738	904,955.28	1,078,958.46	505,233.32	46.80	174,003.18	19.20

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	301	482,375.00	587,404.51	372,204.57	63.40	105,029.51	21.80
Latest Approved (RCE)	290	502,134.52	564,578.65	362,179.45	64.20	62,444.13	12.40

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	45	88,955.85	103,349.56	73,208.42	70.80	14,393.71	16.20

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	Civil Aviation	8	6,035.5	6,625.0	9.8	2	3,750.5	4,340.0	15.7
3	Coal	55	38,127.1	41,212.5	8.1	7	8,579.5	12,262.6	42.9
4	Steel	18	65,625.2	71,782.4	9.4	6	24,028.9	30,216.1	25.7
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	Petroleum	83	183,767.3	198,154.0	7.8	24	58,175.9	78,668.0	35.2
7	Power	98	246,982.7	266,241.8	7.8	20	52,742.1	72,001.2	36.5
8	Railways	283	147,446.3	258,258.6	75.2	144	59,267.9	170,194.7	187.2
9	Road Transport And Highways	151	104,964.2	106,902.8	1.8	11	3,324.3	5,445.2	63.8
10	Shipping And Ports	19	15,617.1	17,902.4	14.6	9	8,629.0	11,218.5	30.0
11	Telecommunications	13	5,699.2	5,527.9	-3.0	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,245.2	49,518.1	11.9	2	6,509.2	11,782.1	81.0
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		738	904,955.3	1,078,958.5	19.2	232	249,067.6	430,663.8	72.9

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	Andhra Pradesh	46	37,404.6	45,444.3	21.5	15	13,556.4	22,463.1	65.7
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	4	9,512.2	17,330.3	82.2
3	Assam	41	24,155.5	38,429.7	59.1	14	10,762.0	25,130.3	133.5
4	Bihar	46	32,579.0	41,019.1	25.9	17	13,347.2	21,803.6	63.4
5	Goa	1	335.6	335.6	0.0	0	0.0	0.0	0.0
6	Gujarat	33	38,022.7	39,317.2	3.4	7	3,094.5	4,716.2	52.4
7	Haryana	9	4,399.9	6,082.5	38.2	2	1,298.8	2,981.4	129.5
8	Himachal Pradesh	6	14,402.5	20,285.8	40.8	5	12,355.4	18,238.8	47.6
9	Jammu and Kashmir	9	14,305.7	33,912.6	137.1	5	7,245.2	26,852.1	270.6
10	Karnataka	37	53,868.0	63,795.5	18.4	13	10,517.5	20,938.0	99.1
11	Kerala	10	21,010.6	22,835.4	8.7	4	4,487.4	6,312.2	40.7
12	Madhya pradesh	21	31,448.2	32,674.6	3.9	5	3,317.9	4,963.7	49.6
13	Maharashtra	56	95,785.3	109,499.3	14.3	19	33,512.3	49,685.3	48.3
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	512.1
15	Meghalaya	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	Mizoram	2	1,533.0	3,298.0	115.1	1	619.3	2,384.3	285.0
17	Nagaland	2	5,124.0	6,715.5	31.1	1	850.0	2,441.5	187.2
18	Odisha	31	56,321.5	63,614.3	12.9	13	32,821.5	40,114.2	22.2
19	Punjab	6	2,212.6	3,154.4	42.6	2	532.4	1,474.2	176.9
20	Rajasthan	25	25,256.6	25,682.6	1.7	7	2,725.5	3,637.6	33.5
21	Sikkim	2	1,648.9	3,690.0	123.8	1	1,339.5	3,380.6	152.4
22	Tamil Nadu	41	53,242.8	68,268.9	28.2	20	30,760.3	45,786.4	48.8
23	Tripura	5	2,669.4	4,021.1	50.6	3	2,129.4	3,515.4	65.1
24	Uttar Pradesh	30	22,605.7	27,184.9	20.3	10	3,831.0	8,458.5	120.8
25	West Bengal	35	49,371.9	60,370.6	22.3	14	20,053.9	31,052.6	54.8
26	Chandigarh	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	Delhi	6	38,669.3	38,649.7	-0.1	0	0.0	0.0	0.0
28	Chhatisgarh	24	58,278.3	59,362.9	1.9	5	1,396.8	2,481.4	77.6
29	Jharkhand	26	15,873.2	20,137.9	26.9	8	2,534.9	6,971.4	175.0
30	Uttarakhand	6	7,844.0	10,199.3	30.0	4	5,839.0	8,194.3	40.3
31	Multi State	173	181,049.6	203,896.0	12.6	32	19,899.8	44,902.9	125.6
Total		738	904,955.3	1,078,958.5	19.2	232	249,067.6	430,663.8	72.9

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 66
2	Civil Aviation	8	6,035.5	6,625.0	9.8	3	989.4	989.4	3 - 50
3	Coal	55	38,127.1	41,212.5	8.1	28	24,633.8	28,090.6	12 - 72
4	Steel	18	65,625.2	71,782.4	9.4	14	64,438.3	70,505.9	8 - 48
5	Petrochemicals	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	20 - 20
6	Petroleum	83	183,767.3	198,154.0	7.8	50	127,204.9	143,219.6	2 - 94
7	Power	98	246,982.7	266,241.8	7.8	52	123,653.8	141,352.8	1 - 106
8	Railways	283	147,446.3	258,258.6	75.2	37	26,070.8	75,820.7	3 - 240
9	Road Transport And Highways	151	104,964.2	106,902.8	1.8	101	61,318.7	63,230.4	2 - 117
10	Shipping And Ports	19	15,617.1	17,902.4	14.6	4	2,502.6	3,104.7	5 - 93
11	Telecommunications	13	5,699.2	5,527.9	-3.0	6	3,166.2	2,950.5	31 - 74
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		738	904,955.3	1,078,958.5	19.2	301	482,375.0	587,404.5	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Andhra Pradesh	46	37,404.6	45,444.3	21.5	9	12,706.5	17,658.9	7 - 48
2	Arunachal Pradesh	4	9,512.2	17,330.3	82.2	3	9,356.2	16,923.9	13 - 90
3	Assam	41	24,155.5	38,429.7	59.1	36	22,277.8	35,722.7	3 - 105
4	Bihar	46	32,579.0	41,019.1	25.9	12	20,814.3	25,494.6	2 - 98
5	Goa	1	335.6	335.6	0.0	1	335.6	335.6	18 - 18
6	Gujarat	33	38,022.7	39,317.2	3.4	11	24,987.1	25,008.7	4 - 24
7	Haryana	9	4,399.9	6,082.5	38.2	3	1,875.1	3,055.1	25 - 50
8	Himachal Pradesh	6	14,402.5	20,285.8	40.8	4	12,798.3	16,543.6	26 - 106
9	Jammu and Kashmir	9	14,305.7	33,912.6	137.1	7	13,038.7	32,618.8	10 - 181
10	Karnataka	37	53,868.0	63,795.5	18.4	12	19,346.4	19,349.1	8 - 179
11	Kerala	10	21,010.6	22,835.4	8.7	4	16,081.0	16,081.0	5 - 58
12	Madhya Pradesh	21	31,448.2	32,674.6	3.9	10	4,919.6	5,046.3	2 - 69
13	Maharashtra	56	95,785.3	109,499.3	14.3	26	44,594.4	52,325.7	5 - 129
14	Manipur	1	727.6	4,453.5	512.1	1	727.6	4,453.5	72 - 72
15	Meghalaya	3	4,845.0	4,845.0	0.0	0	0.0	0.0	-
16	Mizoram	2	1,533.0	3,298.0	115.1	2	1,533.0	3,298.0	35 - 103
17	Nagaland	2	5,124.0	6,715.5	31.1	1	850.0	2,441.5	24 - 24
18	Odisha	31	56,321.5	63,614.3	12.9	20	52,044.1	55,413.4	4 - 139
19	Punjab	6	2,212.6	3,154.4	42.6	2	989.0	1,064.0	13 - 67
20	Rajasthan	25	25,256.6	25,682.6	1.7	8	16,423.9	15,977.6	3 - 65
21	Sikkim	2	1,648.9	3,690.0	123.8	2	1,648.9	3,690.0	15 - 50
22	Tamil Nadu	41	53,242.8	68,268.9	28.2	15	34,552.5	43,919.7	6 - 93
23	Tripura	5	2,669.4	4,021.1	50.6	4	2,417.4	3,769.1	10 - 96
24	Uttar Pradesh	30	22,605.7	27,184.9	20.3	16	15,579.6	18,324.5	9 - 84
25	West Bengal	35	49,371.9	60,370.6	22.3	11	26,303.6	31,726.6	3 - 141
26	Chandigarh	1	452.0	452.0	0.0	0	0.0	0.0	-
27	Delhi	6	38,669.3	38,649.7	-0.1	1	2,494.0	2,494.0	8 - 8
28	Chhatisgarh	24	58,278.3	59,362.9	1.9	10	25,204.4	25,515.7	7 - 59
29	Jharkhand	26	15,873.2	20,137.9	26.9	11	9,616.7	10,125.6	9 - 126
30	Uttarakhand	6	7,844.0	10,199.3	30.0	4	6,097.2	8,228.1	5 - 54
31	Multi State	173	181,049.6	203,896.0	12.6	55	82,762.1	90,799.1	1 - 240
Total		738	904,955.3	1,078,958.5	19.2	301	482,375.0	587,404.5	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	3 - 66
2	Civil Aviation	8	6,035.5	6,625.0	9.8	3	989.4	989.4	3 - 50
3	Coal	55	38,127.1	41,212.5	8.1	28	24,633.8	28,090.6	12 - 72
4	Steel	18	65,625.2	71,782.4	9.4	12	62,967.8	69,035.3	8 - 48
5	Petrochemicals	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	Petroleum	83	183,767.3	198,154.0	7.8	47	123,228.6	134,156.5	2 - 94
7	Power	98	246,982.7	266,241.8	7.8	52	123,653.8	141,352.8	1 - 106
8	Railways	283	147,446.3	258,258.6	75.2	35	25,555.8	74,093.1	3 - 240
9	Road Transport And Highways	151	104,964.2	106,902.8	1.8	101	61,318.7	63,230.4	2 - 117
10	Shipping And Ports	19	15,617.1	17,902.4	14.6	1	1,228.0	1,460.0	48 - 48
11	Telecommunications	13	5,699.2	5,527.9	-3.0	6	3,166.2	2,950.5	31 - 74
12	Urban Development	4	44,245.2	49,518.1	11.9	1	2,494.0	2,494.0	8 - 8
13	Water Resources	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		738	904,955.3	1,078,958.5	19.2	290	469,678.1	564,578.7	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	Atomic Energy	4	44,541.0	46,726.0	4.9	1	3,492.0	5,677.0	62.6
2	Civil Aviation	8	6,242.5	6,625.0	6.1	1	1,942.5	2,325.0	19.7
3	Coal	55	40,988.6	41,212.5	0.5	5	2,211.1	2,694.1	21.8
4	Steel	18	69,847.4	71,782.4	2.8	1	14,443.0	16,408.0	13.6
5	Petrochemicals	1	8,920.0	8,920.0	0.0	0	0.0	0.0	0.0
6	Petroleum	83	197,997.0	198,154.0	0.1	9	32,985.2	37,291.3	13.1
7	Power	98	251,480.3	266,241.8	5.9	13	42,978.5	57,740.0	34.3
8	Railways	283	180,749.4	258,258.6	42.9	115	62,249.5	139,833.2	124.6
9	Road Transport And Highways	151	105,130.7	106,902.8	1.7	11	3,324.3	5,445.2	63.8
10	Shipping And Ports	19	17,488.0	17,902.4	2.4	5	3,157.6	3,783.5	19.8
11	Telecommunications	13	5,699.2	5,527.9	-3.0	3	1,394.0	1,481.5	6.3
12	Urban Development	4	44,304.1	49,518.1	11.8	1	6,395.0	11,609.0	81.5
13	Water Resources	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		738	973,931.2	1,078,958.5	10.8	166	175,115.5	285,474.8	63.0

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	0	0.00	0.00	0- 0
2	Civil Aviation	8	6,035.46	6,624.95	9.77	1	1,808.00	2,015.00	13- 13
3	Coal	55	38,127.05	41,212.50	8.09	0	0.00	0.00	0- 0
4	Steel	18	65,625.22	71,782.40	9.38	2	8,987.89	12,898.17	24- 48
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	83	183,767.28	198,154.01	7.83	11	20,683.33	35,008.63	20- 94
7	Power	98	246,982.72	266,241.78	7.80	2	2,253.45	3,986.02	0- 79
8	Railways	283	147,446.28	258,258.56	75.15	15	5,839.02	22,637.08	0- 141
9	Road Transport And Highways	151	104,964.22	106,902.84	1.85	0	0.00	0.00	0- 0
10	Shipping And Ports	19	15,617.12	17,902.42	14.63	5	5,400.70	6,860.25	10- 93
11	Telecommunications	13	5,699.24	5,527.92	-3.01	0	0.00	0.00	0- 0
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		738	904955.28	1078958.46	19.23	37	50433	92325.15	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	Atomic Energy	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 66
2	Civil Aviation	8	6,035.46	6,624.95	9.77	0	0.00	0.00	0- 0
3	Coal	55	38,127.05	41,212.50	8.09	5	7,938.86	11,573.95	19- 55
4	Steel	18	65,625.22	71,782.40	9.38	5	23,768.89	29,866.43	14- 48
5	Petrochemicals	1	5,460.61	8,920.00	63.35	1	5,460.61	8,920.00	20- 20
6	Petroleum	83	183,767.28	198,154.01	7.83	18	53,921.74	73,387.51	5- 94
7	Power	98	246,982.72	266,241.78	7.80	16	44,349.86	62,048.81	10- 106
8	Railways	283	147,446.28	258,258.56	75.15	32	22,453.88	72,208.71	9- 240
9	Road Transport And Highways	151	104,964.22	106,902.84	1.85	10	3,158.01	5,252.10	25- 115
10	Shipping And Ports	19	15,617.12	17,902.42	14.63	2	1,378.00	2,060.00	48- 93
11	Telecommunications	13	5,699.24	5,527.92	-3.01	2	1,065.85	1,089.32	34- 54
12	Urban Development	4	44,245.18	49,518.08	11.92	0	0.00	0.00	0- 0
13	Water Resources	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		738	904955.28	1078958.46	19.23	93	180158.7	289353.83	

List of projects completed/dropped/Frozen during current month

(All Cost /Expenditure in Rs. crore)

			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>Petroleum</u>						
1	BUTADIENE EXTRACTION UNIT (BDEU) AT PANIPAT	11/2009	341.50	02/2013	341.50	09/2013	198.81
	<u>Power</u>						
2	TRANSMISSION SYSTEM ASSOCIATED WITH SASAN ULTRA ME	12/2008	7,031.88	12/2012	7,031.88	09/2013	4,591.90
	<u>Road Transport And Highways</u>						
3	GWALIOR BYPASS, NH-75,3	12/2003	300.93	10/2009	300.93	06/2013	302.70

List of projects added	(All Cost in Rs. crore)
------------------------	-------------------------

			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>Road Transport And Highways</u>					
1	BARSAT-KRISHNANAGAR	8/2012	867.00	2/2015	867.00	2/2015

Milestones (Cumulative due & achieved)

Total	3714
Achieved up to month	1335


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>Civil Aviation</u>						
1	Construction of New International Terminal Building AAI	335.61	335.61	05/2012	09/2013	11/2013	2
2	C/o new Airport at Pakyong(Sikkim) Airport AAI	309.46	309.46	01/2011	12/2014	03/2015	3
3	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI AAI	344.28	344.28	03/2014	03/2014	06/2014	3
	<u>Coal</u>						
4	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
	<u>Steel</u>						
5	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL RINL	8,692.00	12,291.00	10/2009	09/2013	10/2013	1
6	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT RINL	230.00	343.58	02/2011	09/2013	10/2013	1
	<u>Petroleum</u>						
7	PARADIP REFINERY PROJECT IOCL	29,777.00	32,710.00	11/2012	04/2014	05/2014	1
8	Fluidized catalytic cracking unit(FCCU) revamp IOCL	1,000.00	1,000.00	01/2013	11/2013	12/2013	1
9	Development of WO-16 Cluster Fields ONGC	2,523.00	2,523.00	01/2014	05/2014	12/2015	19
	<u>Power</u>						
10	BARH STPP STAGE I (3X660MW) NTPC NTPC	8,692.97	8,693.00	12/2009	02/2017	03/2017	1
11	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP PGCIL	184.19	184.19	11/2011	09/2013	10/2013	1
12	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX PGCIL	182.68	182.68	01/2013	10/2013	11/2013	1
13	System Strengthening -XII of SR PGCIL	232.34	232.34	06/2012	09/2013	11/2013	2
14	SUBANSIRI LOWER H.E.P (NHPC) NHPC	6,285.33	10,667.00	09/2010	12/2017	03/2018	3
15	EASTERN REGION STRENGTHENING SCHEME-I PGCIL	975.96	975.96	10/2009	12/2013	03/2014	3
16	Establishment of pooling stations at Rajgarh PGCIL	1,719.52	1,719.52	08/2013	12/2013	03/2014	3
17	Transmission system for transfer of power from Gen. PGCIL	250.03	250.03	01/2013	12/2014	03/2015	3
18	Transmission system for transfer of power from Gen-PART B PGCIL	1,585.12	1,585.12	11/2013	12/2014	03/2015	3
19	EASTERN REGION TRANSMISSION SYSTEM-III PGCIL	1,272.80	1,272.80	11/2012	09/2014	03/2015	6
20	BONGAIGAON THERMAL POWER PROJECT NTPC	4,375.35	4,375.35	07/2011	10/2015	06/2016	8


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
21	Transm System for development of Pooling stn. in N PGCIL	4,404.57	4,404.57	01/2015	01/2015	12/2015	11
22	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR PGCIL	170.36	170.36	04/2013	12/2013	12/2014	12
23	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) NTPC	2,978.48	3,846.30	03/2013	03/2016	07/2017	16
24	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT THDCL	2,491.58	3,745.08	07/2014	05/2016	09/2017	16
	<u>Railways</u>						
25	LANJHIGARH-JUNAGARH NL(ECOR) ECOR	100.00	227.94	03/2002	09/2013	10/2013	1
26	PANVEL PEN DOUBLING CR	191.00	191.00	N.A.	12/2013	01/2014	1
27	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) SCR	124.43	925.30	N.A.	03/2012	02/2014	23
28	RANCHI-LOHARDAGA(GC),SER SER	194.07	596.35	06/2004	12/2012	12/2014	24
	<u>Road Transport And Highways</u>						
29	BRAHMPUTRA BRIDGE,NH NO-31 NHAI	217.61	217.61	04/2010	11/2014	12/2014	1
30	CHAMBAL BRIDGE, NH-76 (RJ-5) NHAI	275.00	281.31	02/2010	06/2015	07/2015	1
31	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) NHAI	225.00	241.53	04/2004	09/2013	11/2013	2
32	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 NHAI	228.70	228.70	02/2004	09/2013	11/2013	2
33	DEOLI-KOTA NHAI	593.00	593.00	07/2013	10/2013	12/2013	2
34	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A NHAI	284.00	359.00	05/2008	09/2013	12/2013	3
35	NAGAON TO DHARAMTUL (AS-2) NHAI	264.72	264.72	06/2008	12/2013	03/2014	3
36	NALBARI TO BIJNI (AS-6) NHAI	225.00	225.00	06/2008	09/2013	12/2013	3
37	DHARAMTUL TO SONAPUR (AS-19) NHAI	200.00	200.00	06/2008	12/2013	03/2014	3
38	Kishangarh-Ajmer-Beawer NHAI	795.00	795.00	05/2012	09/2013	12/2013	3
39	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM NHAI	1,585.00	1,585.00	05/2013	09/2013	12/2013	3
40	DEVIHALLI-HASSAN NHAI	453.00	453.00	N.A.	09/2013	12/2013	3
41	JAIPUR-REENGUS NHAI	267.81	267.81	02/2013	09/2013	12/2013	3
42	Jaipur-Tonk-Deoli NHAI	792.06	792.06	12/2012	09/2013	02/2014	5
43	THANJAUR-TRICHY,NH-67(NHAI) NHAI	280.00	280.00	06/2009	09/2013	09/2014	12
44	BAREILY-SITAPUR NHAI	1,046.00	1,046.00	09/2013	09/2013	12/2014	15
	<u>Telecommunications</u>						
45	Supply Installation testing and commissioning of Rural Wimax BSNL	1,148.19	964.37	05/2011	09/2013	12/2013	3
	45						

Graphical Presentation of All Projects w.r.t. Original Schedule

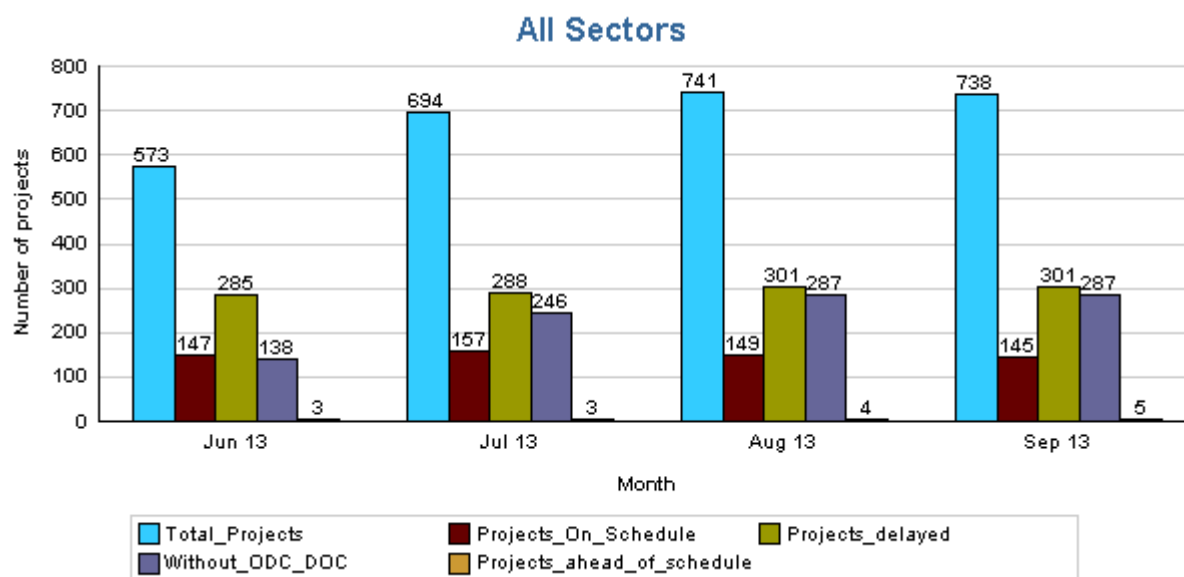

Break-up of 301 Delayed projects in September 2013

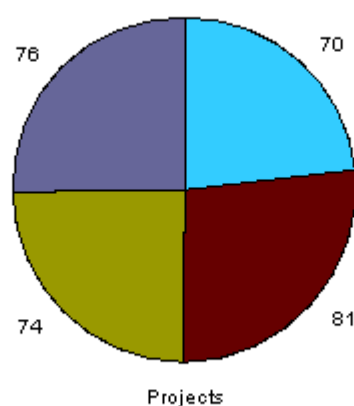


Delay in Months


Legend:

- 1-12
- 13-24
- 25-60
- 60 and Above

Graphical Presentation of All Projects w.r.t. Revised Schedule

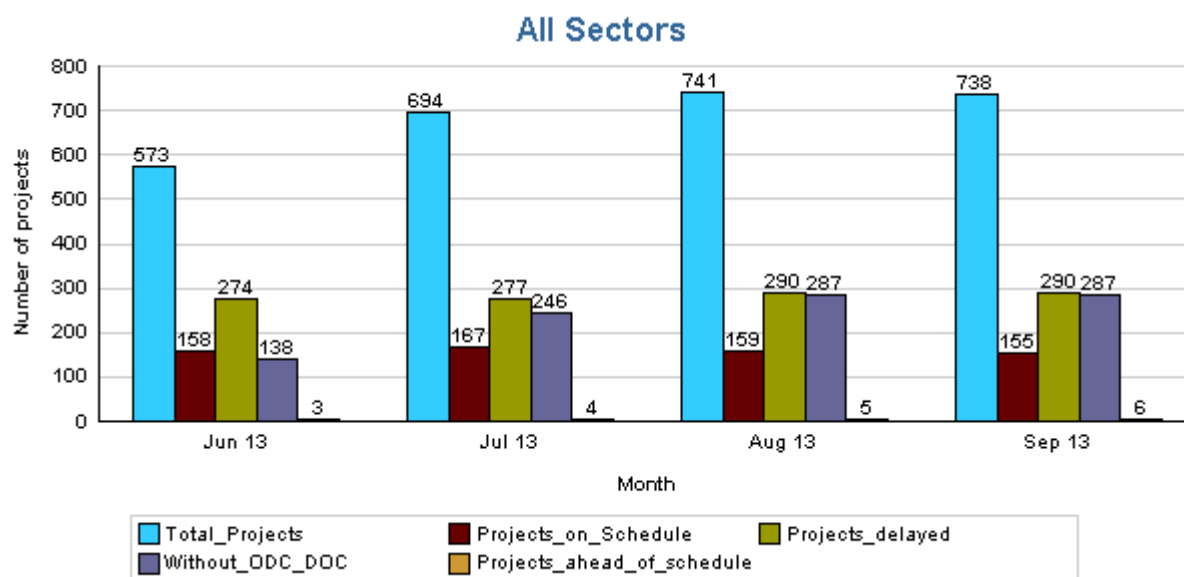


Break-up of 290 Delayed projects in September 2013

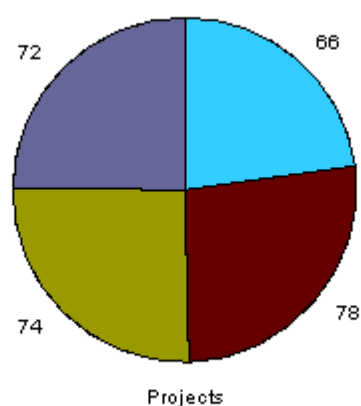


Delay in Months



Graphical Presentation of Urban Development Sector

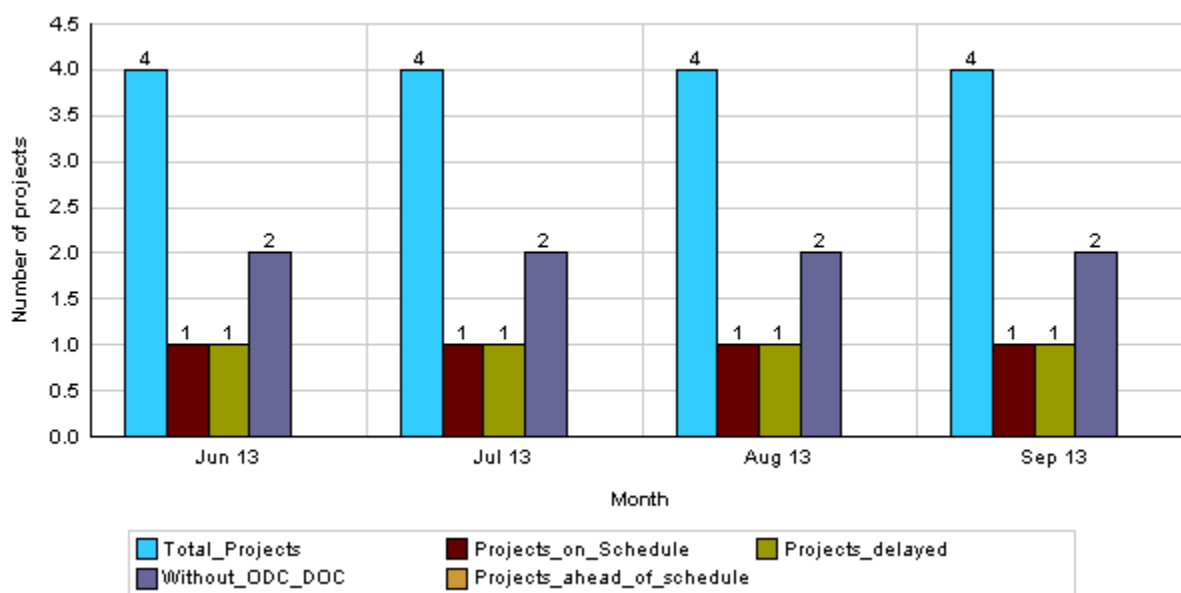


Break-up of 1 Delayed projects in September 2013




Delay in Months



Graphical Presentation of Telecommunications Sector

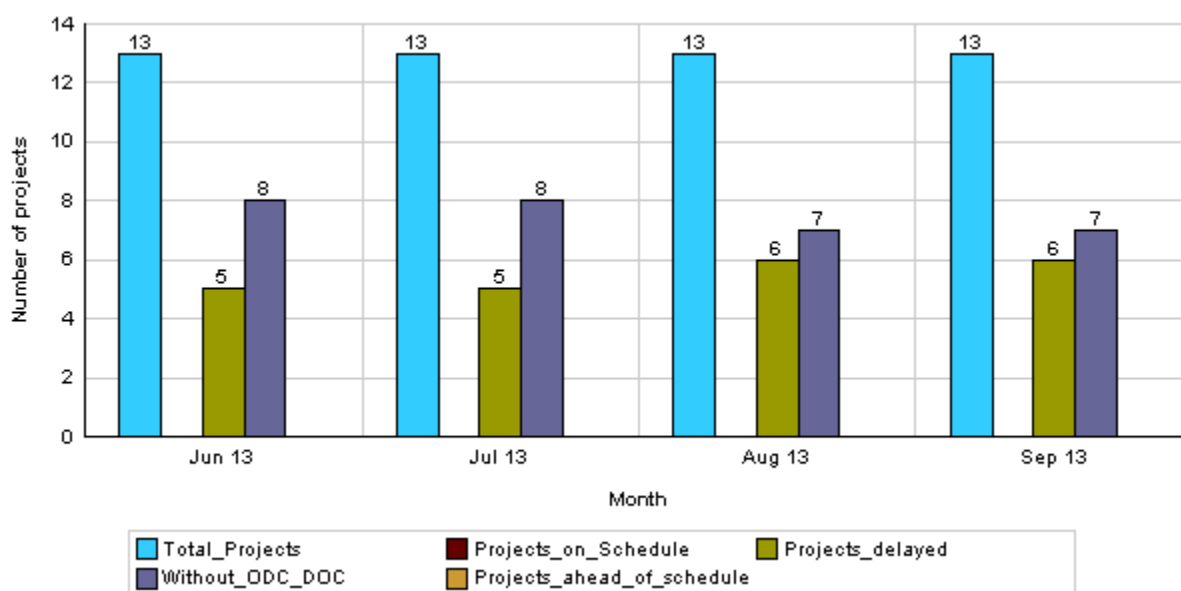


Break-up of 6 Delayed projects in September 2013

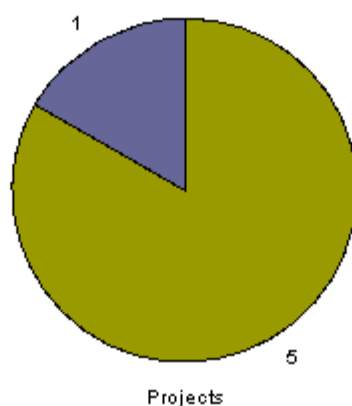


Delay in Months



Graphical Presentation of Shipping And Ports Sector

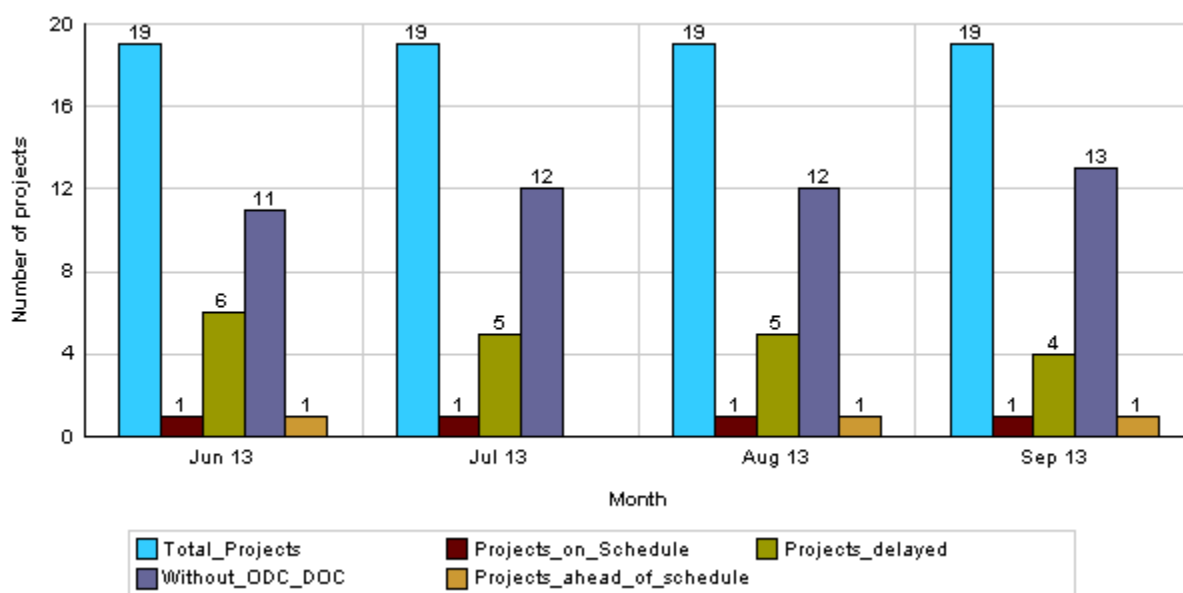


Break-up of 4 Delayed projects in September 2013

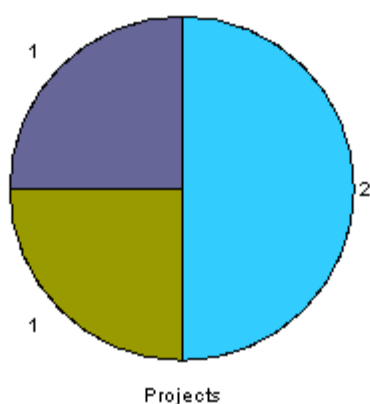


Delay in Months



Graphical Presentation of Road Transport And Highways Sector

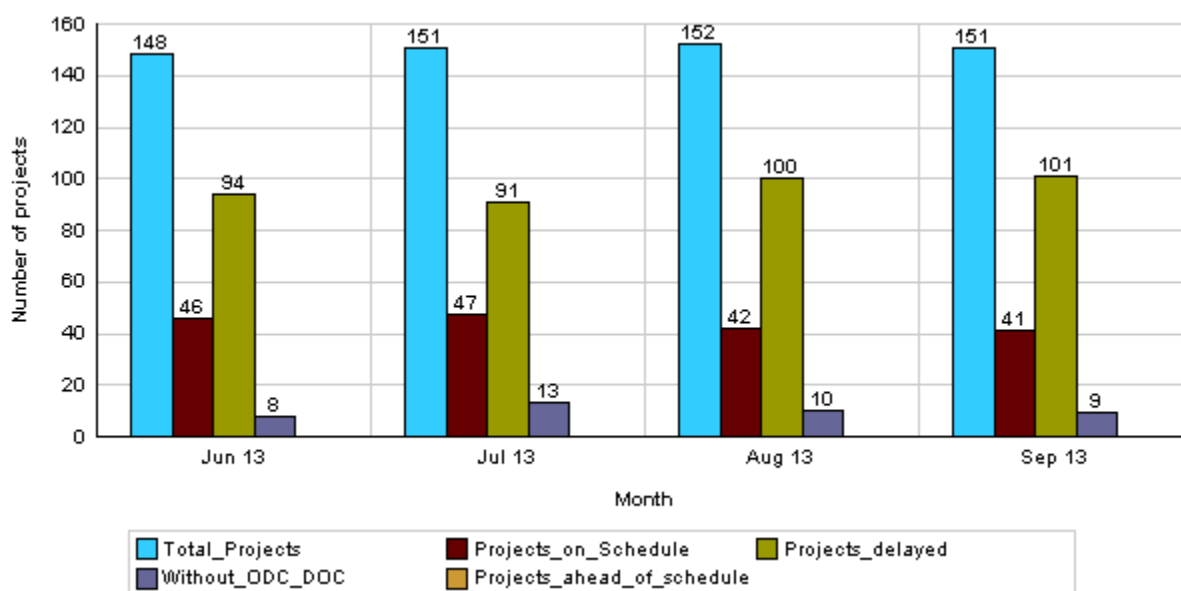


Break-up of 101 Delayed projects in September 2013

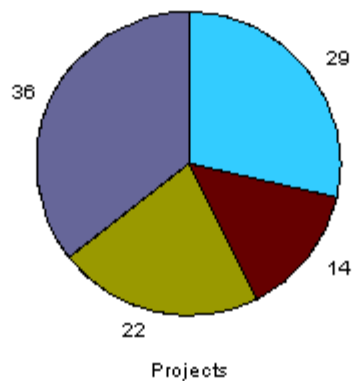


Delay in Months



Graphical Presentation of Railways Sector

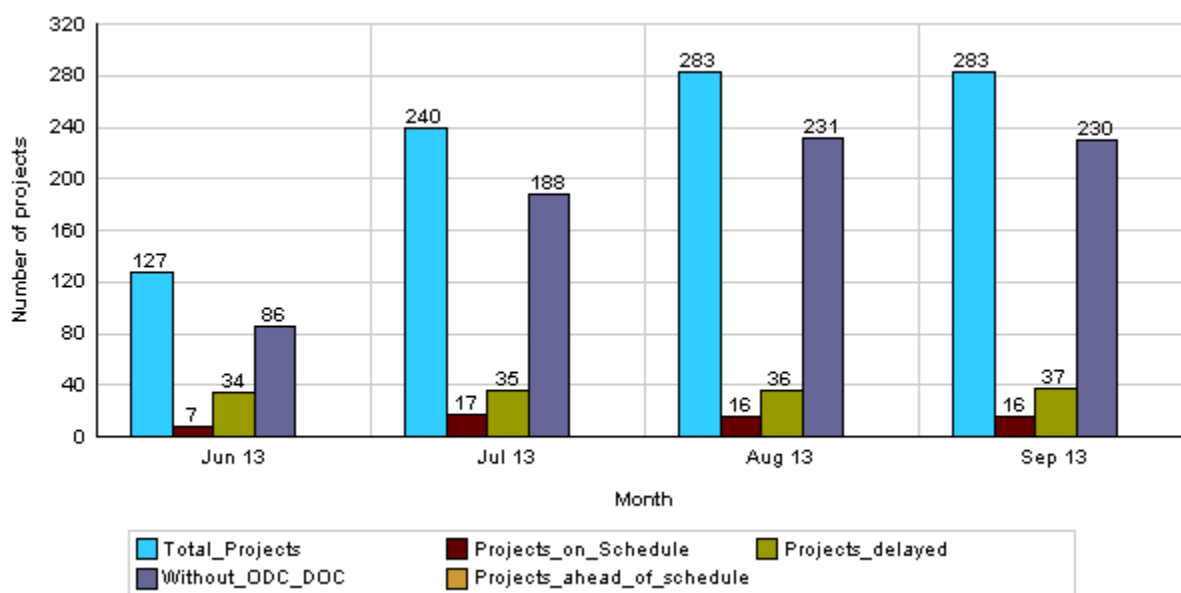


Break-up of 37 Delayed projects in September 2013

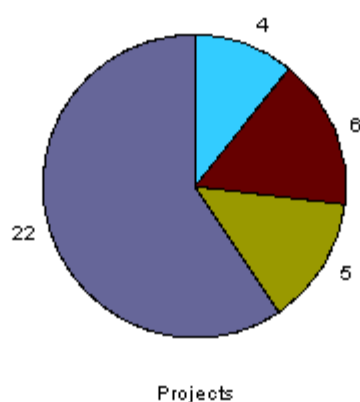


Delay in Months



Graphical Presentation of Power Sector

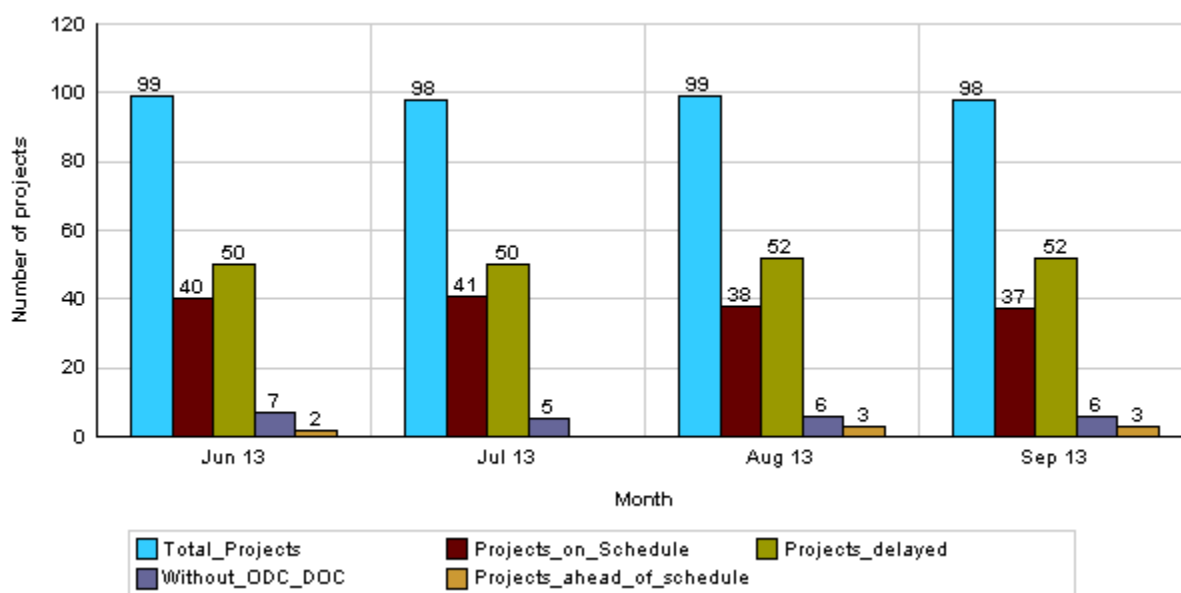


Break-up of 52 Delayed projects in September 2013

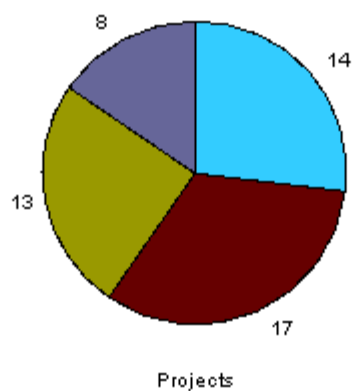


Delay in Months



Graphical Presentation of Petroleum Sector

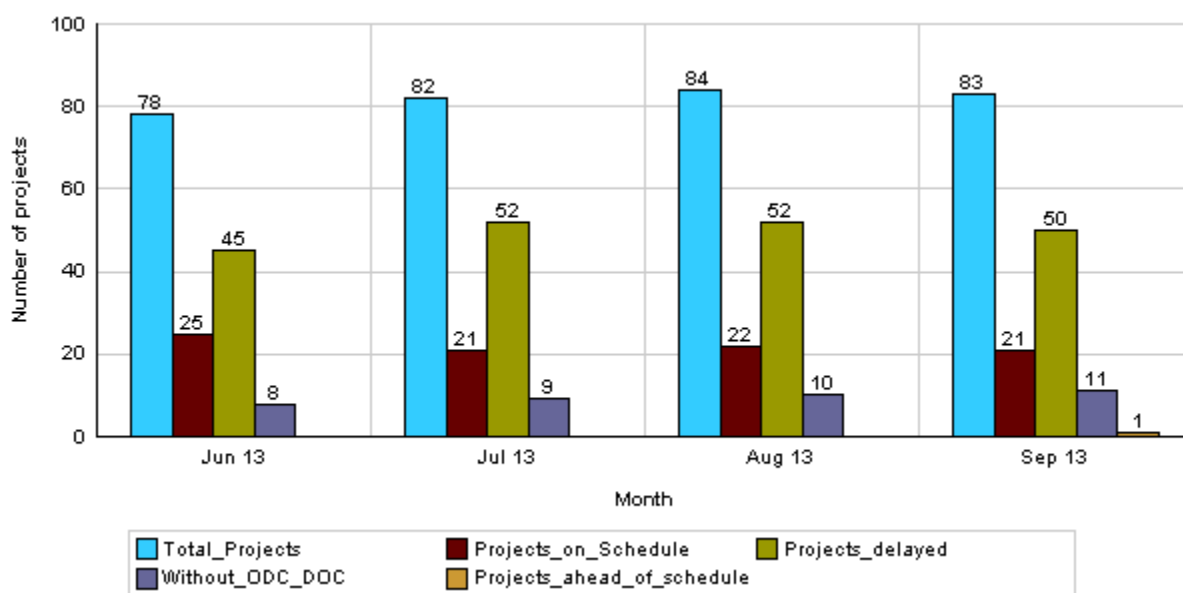


Break-up of 50 Delayed projects in September 2013

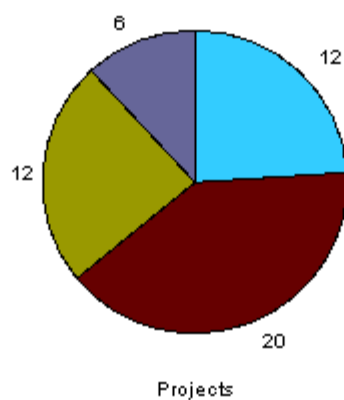


Delay in Months



Graphical Presentation of Steel Sector

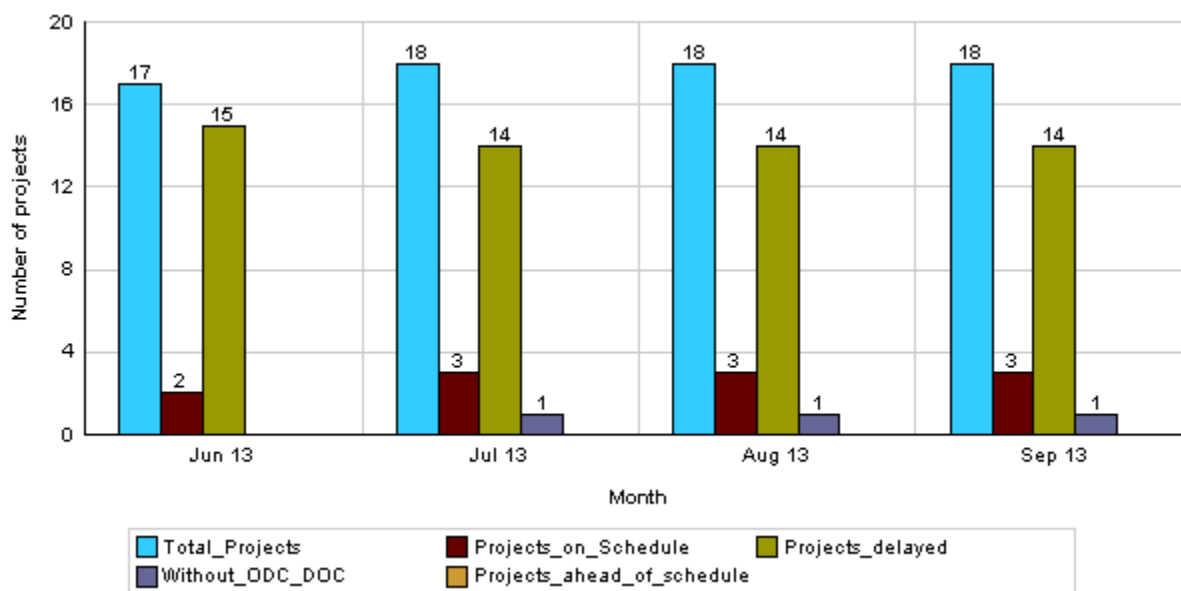


Break-up of 14 Delayed projects in September 2013

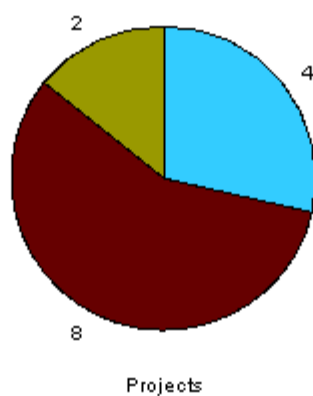


Delay in Months



Graphical Presentation of Coal Sector

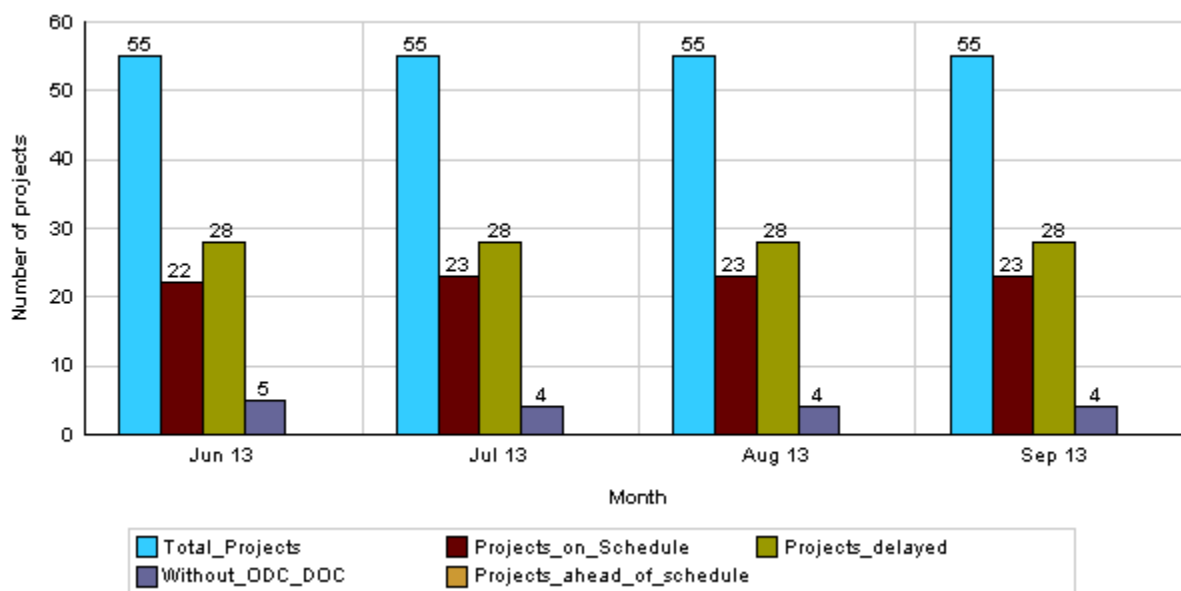


Break-up of 28 Delayed projects in September 2013

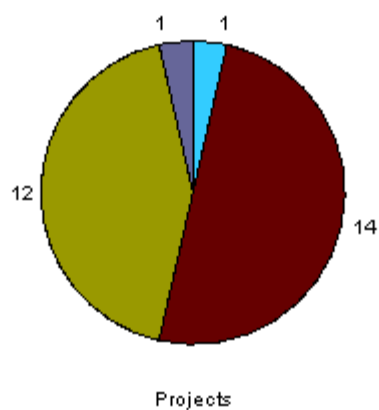


Delay in Months



Graphical Presentation of Civil Aviation Sector

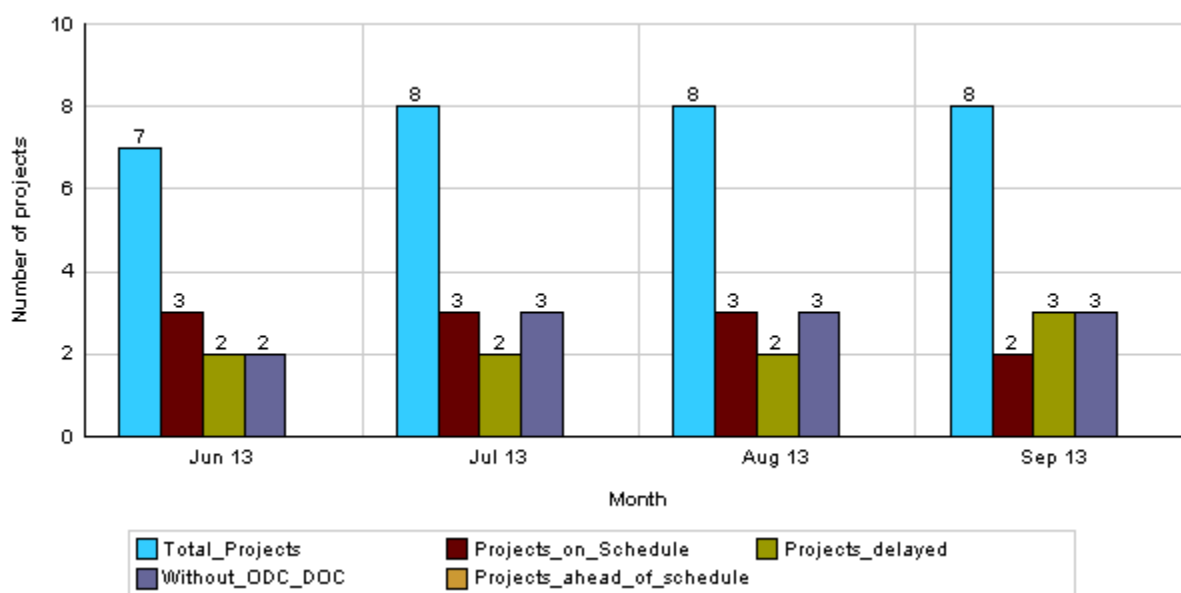


Break-up of 3 Delayed projects in September 2013

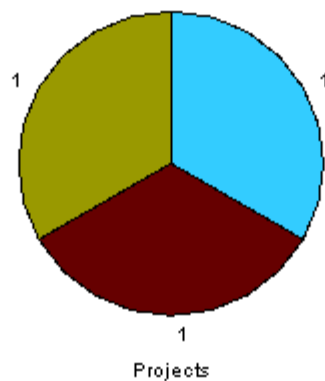


Delay in Months



Graphical Presentation of Atomic Energy Sector

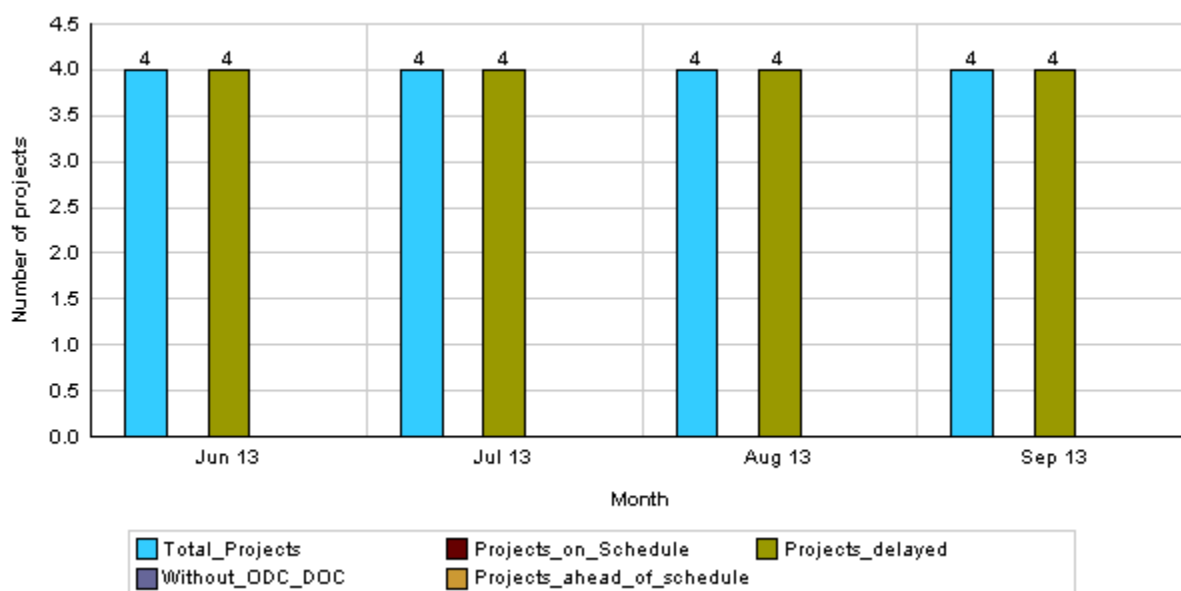

Break-up of 4 Delayed projects in September 2013

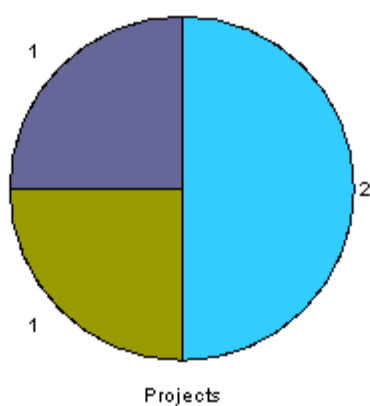

Delay in Months



Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
Atomic Energy	4	40,442.00	44,541.00	46,726.00	26,373.60
Civil Aviation	8	6,035.46	6,242.46	6,624.95	5,453.37
Coal	55	38,127.05	40,988.64	41,212.50	15,788.60
Steel	18	65,625.22	69,847.40	71,782.40	53,801.46
Petrochemicals	1	5,460.61	8,920.00	8,920.00	4,510.51
Petroleum	83	183,767.28	197,997.02	198,154.01	96,241.80
Power	98	246,982.72	251,480.33	266,241.78	126,527.06
Railways	283	147,446.28	180,749.42	258,258.56	75,461.51
Road Transport And Highways	151	104,964.22	105,130.72	106,902.84	83,933.30
Shipping And Ports	19	15,617.12	17,487.95	17,902.42	8,652.15
Telecommunications	13	5,699.24	5,699.24	5,527.92	2,032.84
Urban Development	4	44,245.18	44,304.08	49,518.08	6,421.63
Water Resources	1	542.90	542.90	1,187.00	35.49
Grand total	738	904,955.28	973,931.16	1,078,958.46	505,233.32

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(Sep,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	3,088.00	12/2015 -	11/2016	11(O) -	0/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,485.00	12/2008 -	06/2014	66(O) -	39/106
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015	54(O) -	8/82
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,119.00	12/2016 -	03/2017	3(O) -	0/69
	Total		40,442.00 -	46,726.00	26,373.60				47/327
	<u>Civil Aviation</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	2,325.00	2,474.30	05/2011 -	03/2013	-	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.71	01/2011 04/2013	03/2015	50(O) 23(R)	0/0
7	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	244.70	05/2012 -	11/2013	18(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	2,015.00	1,906.88	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Chandigarh	02/2011	452.00 -	452.00	145.42	03/2015 -	03/2015	0(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	06/2014	3(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	626.00	450.34	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,624.95	5,453.37				0/0
	<u>Coal</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	802.36	03/2013 09/2012	10/2014	19(O) 25(R)	18/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,Chhatisgarh	11/2009	150.59 -	198.59	89.92	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,Madhya pradesh	12/2009	1,352.04 1,143.54	1,143.54	579.32	03/2016 03/2016	03/2016	0(O) 0(R)	0/4
16	AMRAPALI OC - [N06000103]JCL,Jharkhand	02/2012	858.11 -	858.11	49.40	03/2020 -	03/2020	0(O) -	0/3
17	ANANTA OC EXPANSION PH-III 15.0 Mty - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	115.88	03/2012 -	03/2014	24(O) -	5/6

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.85	03/2011 -	03/2014	36(O) -	0/2
19	BALRAM OCP EXTENSION,MCL (8.00 Mty) - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.85	03/2010 -	03/2015	60(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,Chhatisgarh	04/2012	258.56 -	258.56	52.65	03/2016 -	03/2016	0(O) -	0/6
21	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]MCL,Odisha	12/2007	490.00 -	490.10	151.06	03/2017 -	03/2017	0(O) -	4/12
22	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019]NCL,Multi State	11/2006	168.97 -	168.97	45.02	03/2014 -	03/2014	0(O) -	0/2
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,Madhya pradesh	06/2011	746.04 -	535.10	161.60	03/2015 -	03/2015	0(O) -	0/3
24	Batura OCP (2.0 MTY) - [N06000049]SECL,Madhya pradesh	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	267.52	03/2014 -	03/2016	24(O) -	2/8
26	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,271.75	03/2014 -	03/2016	24(O) -	6/12
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,422.40	03/2014 -	03/2016	24(O) -	10/15
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,Odisha	02/2008	395.87 -	395.87	72.34	03/2015 -	03/2015	0(O) -	1/13
30	HINGULA OC-II EXP PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	116.91	03/2013 -	03/2015	24(O) -	3/8
31	JAGANNATHPUR OCP(3.00 MTY) - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,Andhra Pradesh	07/2011	447.06 -	447.06	14.03	03/2015 -	03/2015	0(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72(O) -	0/2
35	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	91.60	12/2012 -	03/2016	39(O) -	9/44
36	KALYANIKHANI OPENCASST PROJECT - [N06000101]SCCL,Andhra Pradesh	07/2012	417.33 -	417.33	0.09	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.85	03/2013 -	03/2015	24(O) -	5/10
38	KARMA OCP (1.0MTY) - [N06000088]CCL,Jharkhand	06/2009	162.46 -	162.46	40.81	03/2014 -	03/2014	0(O) -	0/2
39	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7
40	KHADIA EXPANSION OPENCASST PROJECT 4 TO 10 MTPA,6MT - [N06000091]NCL,Uttar Pradesh	06/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018	0(O) -	0/4
41	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 -	741.62	374.23	03/2013 -	03/2014	12(O) -	0/2
42	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.30	03/2010 -	03/2014	48(O) -	9/10
43	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	1,188.31	738.84	03/2013 -	-	-	0/9

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
44	Kistaram OCP - [N06000089]SCCL,Andhra Pradesh	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
45	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	27.60	07/2012 -	03/2016	44(O) -	0/3
46	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.96	03/2014 -	03/2016	24(O) -	1/6
47	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.67	03/2012 -	03/2015	36(O) -	4/6
48	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015	0(O) -	0/0
49	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	0(O) -	0/0
50	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	34.04	12/2015 -	02/2018	26(O) -	0/33
51	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.98	03/2012 -	03/2015	36(O) -	0/2
52	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	61.20	03/2012 -	03/2017	60(O) -	0/2
53	PELMA OCP(10.00MTY) - [N06000045]SECL,Chhatisgarh	07/2008	448.32 -	448.32	-	03/2015 -	03/2015	0(O) -	1/1
54	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.23	03/2014 -	03/2016	24(O) -	0/1
55	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.33	03/2013 -	03/2015	24(O) -	0/3
56	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	19.29	03/2014 -	03/2016	24(O) -	0/2
57	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	418.97	236.07	03/2012 -	-	-	24/27
58	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,Andhra Pradesh	07/2011	162.76 -	162.76	2.56	03/2015 -	03/2015	0(O) -	4/29
59	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,Andhra Pradesh	11/2012	430.14 -	430.14	58.90	03/2016 -	03/2016	0(O) -	4/48
60	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,Andhra Pradesh	06/2012	365.01 -	365.01	-	06/2015 -	06/2015	0(O) -	2/51
61	RKP OCP PHASE-I - [N06000079]SCCL,Andhra Pradesh	03/2010	209.78 -	209.78	51.42	03/2015 -	03/2015	0(O) -	8/31
62	Rajrappa RCE OCP (3.0 MTY) - [N06000087]CCL,Jharkhand	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016	0(O) -	0/2
63	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	249.03	56.69	03/2012 -	-	-	16/42
64	TALABIRA OCP - [N06000043]MCL,Odisha	03/2008	447.72 -	447.72	44.33	03/2016 -	03/2016	0(O) -	0/12
65	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [N060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,783.98	06/2009 -	01/2014	55(O) -	19/23
66	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,689.91	03/2012 -	03/2014	24(O) -	20/39
67	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	138.21	03/2012 -	03/2016	48(O) -	0/2
	Total		38,127.05 -	41,212.50	15,788.60				196/778
	Steel								

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
68	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	327.46	04/2013 12/2013	12/2013	8(O) 0(R)	16/18
69	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 349.64	349.64	255.83	08/2010 08/2010	06/2013	-	1/1
70	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREM - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 343.58	343.58	280.63	02/2011 02/2011	10/2013	32(O) 32(R)	3/3
71	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	222.75	05/2013 03/2014	03/2014	10(O) 0(R)	11/20
72	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	283.63	05/2012 05/2012	12/2013	19(O) 19(R)	2/2
73	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	354.04	12/2011 03/2012	12/2013	24(O) 21(R)	15/20
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 216.68	216.68	152.61	10/2012 10/2012	12/2013	14(O) 14(R)	3/4
75	Coke Oven Battery-5 - [N12000080]SAIL,West Bengal	03/2012	339.35 -	339.35	12.59	06/2015 -	06/2015	0(O) -	0/0
76	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, Chattisga - [N12000078]SAIL,Chhatisgarh	07/2012	332.65 -	332.65	-	08/2014 -	08/2014	0(O) -	0/2
77	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	74.38	11/2013 -	06/2015	19(O) -	1/3
78	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	10,590.79	03/2013 -	09/2014	18(O) -	23/32
79	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,779.97	12/2011 -	12/2013	24(O) -	18/21
80	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,841.57	12/2012 -	03/2014	15(O) -	10/16
81	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	15,038.24	12/2011 -	12/2013	24(O) -	20/23
82	EXPANSION OF RINL/VSP FROM 3 MTPY-6.3 MTPY OF LIQUID STEEL - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,554.63	10/2009 10/2012	10/2013	48(O) 12(R)	66/67
83	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,933.09	03/2013 -	12/2013	9(O) -	14/19
84	INSTALLATION OF 1x45 MVA Submerged Arc Furnace AT - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	95.71	10/2013 -	06/2014	8(O) -	0/3
85	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079]SAIL,Odisha	01/2012	254.90 -	254.90	3.54	12/2014 -	12/2014	0(O) -	0/1
	Total		65,625.22 -	71,782.40	53,801.46				203/255
	<u>Petrochemicals</u>								
86	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20(O) 0(R)	19/29
	Total		5,460.61 -	8,920.00	4,510.51				19/29
	<u>Petroleum</u>								
87	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	28.10	06/2012 -	03/2014	21(O) -	0/4
88	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23(O) -	0/0
89	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	773.81	12/2011 -	11/2013	23(O) -	0/5

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
90	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, Assam	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 -	03/2014	12(O) -	0/5
91	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL, Multi State	08/2011	586.00 -	586.00	74.77	08/2015 -	07/2015	-1(O) -	0/0
92	Ahmedabad Redevelopment - [N16000120]ONGC, Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24(O) -	0/0
93	Ankleswar Redevelopment - [N16000122]ONGC, Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24(O) -	0/0
94	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	540.92	330.96	07/2012 07/2012	-	-	0/7
95	Butene-1 at Panipat - [N16000139]IOCL, Haryana	02/2012	190.00 -	190.00	80.85	03/2014 -	03/2014	0(O) -	0/24
96	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, Assam	08/2008	144.02 -	204.29	133.48	06/2012 -	12/2013	18(O) -	0/0
97	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, Multi State	06/2007	736.65 -	736.65	445.86	09/2011 -	12/2014	39(O) -	0/0
98	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL, Assam	08/2008	126.18 -	159.54	59.74	06/2012 -	03/2014	21(O) -	0/0
99	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL, Tamil Nadu	01/2008	224.00 394.00	394.00	312.61	- -	03/2013	-	18/19
100	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER - [N16000127]ONGC, Assam	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12(O) -	0/5
101	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE - [N16000128]ONGC, Maharashtra	03/2011	861.79 -	761.68	289.87	05/2013 -	05/2014	12(O) -	0/5
102	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY - [N16000167]OIL, Multi State	08/2006	374.56 -	374.56	10.46	09/2012 -	10/2016	49(O) -	0/0
103	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL, Rajasthan	04/2011	152.89 -	152.89	118.41	06/2013 -	06/2013	-	0/0
104	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC, Multi State	11/2010	331.20 -	269.10	91.79	08/2013 -	03/2014	7(O) -	0/5
105	Construction of 6 ETps - [N16000117]ONGC, Gujarat	03/2009	302.26 -	240.95	98.72	09/2012 -	12/2013	15(O) -	0/0
106	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134]ONGC, Gujarat	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014	0(O) -	0/5
107	Construction of one Multipurpose Support Vessel - [N16000103]ONGC, Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
108	Construction of six Effluent Treatment Plants (ETP - [N16000099]ONGC, Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12(O) -	0/5
109	Construction of three ETps, Mehsana - [N16000135]ONGC, Gujarat	03/2012	260.74 -	260.74	0.52	11/2014 -	11/2014	0(O) -	0/5
110	DBPL-II - [N16000147]GAIL, Multi State	06/2009	486.00 -	486.00	61.61	09/2013 -	09/2013	0(O) -	0/1
111	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL, Maharashtra	12/2009	1,584.00 -	1,584.00	487.90	- -	-	-	0/0
112	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94(O) 20(R)	0/0
113	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,116.27	08/2010 03/2012	05/2014	45(O) 26(R)	0/10
114	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC, Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63(O) 45(R)	0/0
115	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC, Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44(O) 22(R)	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
116	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63(O) 11(R)	0/0
117	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24(O) 16(R)	6/76
118	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	2,730.00	1,697.33	09/2011 03/2012	08/2013	-	56/59
119	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	234.31	03/2013 -	12/2013	9(O) -	0/5
120	Development of C-26 Cluster Fields - [N16000133]ONGC,Maharashtra	03/2012	2,592.17 -	2,592.17	26.61	05/2014 -	05/2014	0(O) -	0/9
121	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
122	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.26	11/2012 -	10/2013	11(O) -	0/9
123	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	957.44	01/2014 -	12/2015	23(O) -	0/9
124	Development of Western Periphery of MH South Field - [N16000136]ONGC,Multi State	04/2012	600.17 -	600.17	99.87	12/2014 -	12/2014	0(O) -	0/8
125	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	711.00	0.88	- -	-	-	0/0
126	Fluidized catalytic cracking unit(FCCU) revamp - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	673.33	01/2013 -	12/2013	11(O) -	18/18
127	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26(O) -	0/9
128	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MU - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013	5(O) -	0/167
129	Heera and South Heera Redevelopment Ph-II - [N16000132]ONGC,Maharashtra	03/2012	5,608.40 -	5,608.40	1,278.32	05/2015 -	05/2015	0(O) -	0/17
130	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,727.24	03/2007 03/2017	12/2013	81(O) -39(R)	6/6
131	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	750.00	729.07	03/2007 03/2014	09/2013	78(O) -6(R)	3/3
132	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	14.71	03/2014 -	05/2014	2(O) -	0/5
133	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93(O) 9(R)	6/6
134	IROP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	508.63	12/2015 -	05/2016	5(O) -	0/0
135	Integrated Development of B-127 fields - [N16000131]ONGC,Maharashtra	12/2011	2,059.63 2,665.65	2,665.65	289.05	03/2015 -	03/2015	0(O) -	0/12
136	Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016	0(O) -	0/0
137	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35(O) -	0/0
138	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50(O) -	0/0
139	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	312.00	293.12	01/2012 -	07/2013	-	0/1
140	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL,Multi State	06/2009	2,915.00 -	2,300.00	1,239.97	12/2012 -	-	-	0/10

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
141	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015	0(O) -	0/0
142	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,773.71	01/2012 -	10/2013	21(O) -	0/108
143	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	03/2014	18(O) -	0/0
144	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46(O) 12(R)	0/0
145	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	03/2017	23(O) -	0/0
146	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	279.00	4.87	12/2014 -	12/2014	0(O) -	0/0
147	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	730.97	03/2010 03/2012	12/2013	45(O) 21(R)	0/0
148	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	913.00	37.26	07/2015 -	07/2015	0(O) -	0/0
149	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	23,278.00	11/2012 -	05/2014	18(O) -	60/100
150	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	1,793.00	885.98	09/2012 -	-	-	5/11
151	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	8,140.00	5,177.12	02/2014 -	02/2014	0(O) -	0/0
152	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	238.10	04/2012 06/2013	12/2013	20(O) 6(R)	0/0
153	Pipeline Replacement Project, Ahmedabad - [N16000159]ONGC,Gujarat	09/2011	202.25 -	160.16	-	07/2016 -	07/2016	0(O) -	0/5
154	Pipeline Replacement Project-3 - [N16000137]ONGC,Multi State	04/2012	2,547.26 -	1,417.00	515.24	05/2014 -	05/2014	0(O) -	0/5
155	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	745.49	07/2012 -	12/2013	17(O) -	0/31
156	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]OIL,Multi State	04/2010	270.00 -	270.00	-	12/2014 -	12/2014	0(O) -	0/0
157	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	898.00	913.72	-	08/2013	-	52/53
158	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,Multi State	02/2012	1,210.64 -	1,210.64	281.76	11/2015 -	11/2015	0(O) -	6/25
159	Reconstruction of BPA and BPB Platforms - [N16000161]ONGC,Maharashtra	03/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015	0(O) -	0/0
160	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	1,419.00	134.21	12/2014 -	12/2014	0(O) -	0/0
161	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20(O) -	0/0
162	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	722.53	10/2011 -	12/2013	26(O) -	0/0
163	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	904.74	10/2011 -	01/2014	27(O) -	0/0
164	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	10,281.00	0.04	-	04/2015	-	0/0
165	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUN - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3(O) -	0/5

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
166	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	309.82	48.71	10/2014 -	10/2014	0(O) -	0/0
167	Up-gradation of Konaban GGS and Pipeline Grid Project - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	199.40	08/2012 -	03/2014	19(O) -	0/5
168	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHI - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	263.46	03/2012 -	12/2013	21(O) -	13/20
169	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	576.60	306.39	12/2013 -	12/2013	0(O) -	0/0
	Total		183,767.28 -	198,154.01	96,241.80				249/912
	<u>Power</u>								
170	765 KV POOLING STATION AND NETWORK WITH DVC AND MA - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,979.25	08/2012 -	03/2014	19(O) -	0/11
171	765KV SYSTEM FOR CENTRAL PART OF NORTHERN GRID PAR - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	847.35	05/2012 -	12/2013	19(O) -	0/8
172	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,Multi State	12/2012	156.04 -	156.04	-	10/2014 -	10/2014	0(O) -	0/7
173	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,354.00	08/2013 -	09/2014	13(O) -	12/19
174	BARH STPP STAGE I (3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,704.00	12/2009 -	03/2017	87(O) -	26/54
175	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	4,050.00	07/2011 -	06/2016	59(O) -	5/28
176	COMMON SYS. ASSOCIATED PART- B - [N18000144]PGCIL,Multi State	03/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015	0(O) -	0/20
177	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	1,909.24	195.81	06/2015 -	06/2015	0(O) -	0/0
178	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNA - [N18000111]PGCIL,Andhra Pradesh	08/2011	1,637.34 -	1,637.34	937.10	08/2014 -	08/2014	0(O) -	7/20
179	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126]PGCIL,Andhra Pradesh	03/2012	206.44 -	206.44	41.42	06/2014 -	06/2014	0(O) -	0/20
180	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC - [N18000143]PGCIL,Multi State	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/0
181	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	182.80	3.60	10/2014 -	10/2014	0(O) -	0/0
182	Common System Associated with Coastal Energen Priv - [N18000103]PGCIL,Tamil Nadu	09/2011	1,940.13 -	1,940.13	1,040.50	09/2014 -	09/2014	0(O) -	7/20
183	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	885.68	10/2009 -	03/2014	53(O) -	5/15
184	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	725.71	11/2012 -	03/2015	28(O) -	2/13
185	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
186	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101]PGCIL,Chhatisgarh	05/2011	1,961.87 -	1,961.87	1,131.45	05/2014 -	05/2014	0(O) -	1/11
187	Establishment of pooling stations at Rajgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,289.56	08/2013 -	03/2014	7(O) -	1/12

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
188	Gadarwara Super Thermal Power Project Stage-I - [N18000151]NTPC,Madhya pradesh	02/2013	11,638.55 -	11,638.55	687.00	09/2017 -	09/2017	0(O) -	4/40
189	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,Bihar	12/2011	901.77 -	901.77	377.02	08/2014 -	08/2014	0(O) -	1/16
190	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107]PGCIL,Chhatisgarh	08/2011	1,391.97 -	1,391.97	1,059.23	12/2013 -	12/2013	0(O) -	1/12
191	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,Karnataka	03/2005	596.45 1,007.16	1,007.16	909.70	12/2007 12/2009	-	-	2/11
192	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,473.56	12/2009 05/2013	03/2017	87(O) 46(R)	7/22
193	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,677.22	01/2016 01/2016	11/2016	10(O) 10(R)	0/4
194	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,134.00	04/2009 -	09/2014	65(O) -	0/9
195	KUDGI STPP STAGE 1 - [N18000131]NTPC,Karnataka	12/2011	15,166.19 -	15,166.19	1,845.00	12/2016 -	12/2016	0(O) -	15/17
196	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,Tamil Nadu	05/2005	1,779.29 2,159.07	2,159.07	1,870.81	09/2008 -	03/2013	-	15/23
197	LARA STPP STAGE-I - [N18000140]NTPC,Chhatisgarh	11/2012	11,846.00 -	11,846.00	1,115.00	05/2017 -	05/2017	0(O) -	6/39
198	Lata-Tapovan HPP 3x57MW - [N18000142]NTPC,Uttarakhand	07/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017	0(O) -	0/15
199	MOUDA STPP (NTPC) - [N18000048]NTPC,Maharashtra	11/2008	5,459.28 -	6,010.89	4,056.00	08/2012 -	03/2013	-	16/16
200	MOUDA STPP STAGE 2 - [N18000132]NTPC,Maharashtra	03/2012	7,921.47 -	7,921.47	1,194.00	09/2016 -	09/2016	0(O) -	14/14
201	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	877.64	08/2010 01/2013	10/2013	38(O) 9(R)	0/3
202	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,689.59	08/2013 -	06/2015	22(O) -	0/17
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.62	02/2012 -	12/2013	22(O) -	1/13
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	363.51	11/2011 -	07/2014	32(O) -	0/11
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	385.26	11/2011 -	12/2013	25(O) -	1/14
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	134.45	01/2013 -	11/2013	10(O) -	1/6
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	327.34	07/2013 -	03/2014	8(O) -	1/11
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME- XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	891.31	04/2013 -	03/2015	23(O) -	0/11
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,Multi State	11/2011	723.63 -	723.63	195.23	11/2014 -	11/2014	0(O) -	1/12
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,Multi State	09/2013	680.69 -	680.69	-	03/2016 -	03/2016	0(O) -	0/0
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,Multi State	09/2012	803.34 -	803.34	105.74	03/2015 -	03/2015	0(O) -	0/15
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	48.69	04/2015 -	05/2015	1(O) -	0/16

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
213	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	607.55	11/2012 -	03/2014	16(O) -	0/11
214	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,184.87	10/2010 01/2013	03/2014	41(O) 14(R)	0/6
215	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	4,058.55	09/2009 07/2014	07/2018	106(O) 48(R)	1/20
216	PARE HYDRO ELECTRIC PROJECT(110 MW) - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 1,117.92	1,117.92	660.88	08/2013 08/2013	09/2014	13(O) 13(R)	17/22
217	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,763.64	01/2012 -	03/2014	26(O) -	0/28
218	RIHAND STTP STAGE-III (2X500MW) (NTPC) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,512.00	10/2012 -	10/2013	12(O) -	16/16
219	SOLAPUR STPP - [N18000133]NTPC,Maharashtra	03/2012	9,395.18 -	9,395.18	1,653.00	11/2016 -	11/2016	0(O) -	15/15
220	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,362.61	09/2010 08/2014	03/2018	90(O) 43(R)	11/11
221	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH VAALLUR - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	95.16	04/2013 -	12/2014	20(O) -	4/15
222	SUPPLEMENTRY TRANSMISSION ASSOCIATED WITH DVC AND - [N18000065]PGCIL,Multi State	08/2008	2,360.95 2,580.90	2,580.90	2,066.28	08/2012 -	03/2014	19(O) -	0/5
223	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,Multi State	09/2012	1,508.74 -	1,508.74	76.61	06/2016 -	04/2015	-14(O) -	0/20
224	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	1,935.35	271.58	12/2014 -	11/2014	-1(O) -	0/0
225	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124]PGCIL,Madhya pradesh	03/2012	213.78 -	213.78	-	03/2014 -	03/2014	0(O) -	0/7
226	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116]PGCIL,Chhatisgarh	12/2011	1,746.65 -	1,746.65	174.49	08/2014 -	08/2014	0(O) -	2/19
227	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120]PGCIL,Maharashtra	02/2012	1,310.85 -	1,310.85	464.56	02/2015 -	02/2015	0(O) -	0/14
228	SYSTEM STRENGTHENING-XVII IN SOUTHERN REGION GRID - [N18000130]PGCIL,Multi State	06/2012	1,263.26 -	1,263.26	282.68	11/2014 -	11/2014	0(O) -	0/16
229	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117]PGCIL,Chhatisgarh	01/2012	1,422.85 -	1,422.85	432.96	01/2015 -	01/2015	0(O) -	3/19
230	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,Multi State	12/2011	297.33 -	297.33	144.01	08/2014 -	08/2014	0(O) -	7/20
231	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,Multi State	10/2011	487.49 -	487.49	203.81	06/2014 -	06/2014	0(O) -	7/20
232	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	154.44	06/2012 -	11/2013	17(O) -	0/3
233	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	910.02	08/2012 -	06/2014	22(O) -	0/11
234	TAPOVAN-VISHNUGAD HEP (4x130MW) (NTPC) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	3,846.30	1,899.00	03/2013 -	07/2017	52(O) -	2/15
235	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,387.84	09/2009 06/2013	11/2014	62(O) 17(R)	0/0
236	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	518.78	07/2010 02/2016	02/2017	79(O) 12(R)	1/10
237	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118]PGCIL,Gujarat	01/2012	259.28 -	259.28	111.93	01/2014 -	01/2014	0(O) -	3/18

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
238	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113]PGCIL,Multi State	12/2011	2,422.66 -	2,422.66	520.74	08/2014 -	08/2014	0(O) -	2/19
239	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129]PGCIL,Multi State	02/2012	3,201.44 -	3,201.44	981.51	10/2014 -	09/2014	-1(O) -	2/18
240	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,539.61	10/2012 -	06/2014	20(O) -	0/11
241	TRANS SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,906.96	03/2014 -	05/2014	2(O) -	4/15
242	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121]PGCIL,Andhra Pradesh	02/2012	324.33 -	324.33	19.57	08/2014 -	08/2014	0(O) -	7/20
243	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122]PGCIL,Andhra Pradesh	02/2012	1,927.16 -	1,927.16	444.72	10/2014 -	10/2014	0(O) -	3/16
244	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL,Himachal Pradesh	07/2006	557.24 775.25	775.25	645.74	01/2010 -	07/2013	-	2/11
245	TRANSMISSION SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	159.08	11/2011 -	10/2013	23(O) -	0/4
246	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114]PGCIL,Gujarat	12/2011	552.44 -	552.44	329.39	02/2014 -	02/2014	0(O) -	3/17
247	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	331.70	10/2013 -	12/2013	2(O) -	2/13
248	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 K - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	138.63	07/2013 -	12/2013	5(O) -	0/13
249	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	785.24	12/2013 -	03/2014	3(O) -	2/13
250	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECT - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	182.18	11/2013 -	09/2014	10(O) -	7/20
251	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORI - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,248.80	03/2013 -	05/2014	14(O) -	4/15
252	TRANSMISSION SYSTEM FOR PHASE-I GEN. PROJECT IN OR - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,720.10	12/2013 -	05/2014	5(O) -	0/13
253	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112]PGCIL,Chhatisgarh	11/2011	2,127.51 -	2,127.51	1,186.02	07/2014 -	07/2014	0(O) -	2/14
254	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	645.71	07/2013 -	05/2014	10(O) -	13/29
255	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	470.13	07/2006 -	02/2015	103(O) -	1/16
256	Trans. System associated with PALLATANA GBPP & BPT - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,427.35	12/2012 -	06/2014	18(O) -	0/11
257	Transm System for development of Pooling strn. in N - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	392.18	01/2015 -	12/2015	11(O) -	0/20
258	Transmission System associated with Mauda Stage-II - [N18000153]PGCIL,Multi State	09/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016	0(O) -	0/0
259	Transmission System of Vinchuachal -IV And Rihand - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,719.39	11/2012 -	03/2015	28(O) -	0/15
260	Transmission system for transfer of power from Gen-PART B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	1,042.98	11/2013 -	03/2015	16(O) -	5/16

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
261	Transmission system for transfer of power from Gen. - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	63.45	01/2013 -	03/2015	26(O) -	5/18
262	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	2,053.70	11/2009 02/2013	10/2013	47(O) 8(R)	0/4
263	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,Madhya pradesh	12/2011	3,180.40 -	3,180.40	503.00	08/2015 -	08/2015	0(O) -	11/12
264	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC,Madhya pradesh	01/2009	5,915.00 -	5,915.00	3,401.00	10/2012 -	03/2013	-	15/15
265	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	364.22	07/2014 -	09/2017	38(O) -	1/1
266	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,Maharashtra	12/2007	477.69 -	477.69	451.73	09/2010 -	-	-	0/5
267	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,Chhatisgarh	03/2012	9,569.76 -	9,569.76	872.60	06/2015 -	06/2015	0(O) -	3/28
	Total		246,982.72 -	266,241.78	126,527.06				335/1388
	<u>Railways</u>								
268	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	184.06	0.98	- -	-	-	0/0
269	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	489.13	03/2014 -	12/2015	21(O) -	0/0
270	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	406.74	12/2009 03/2011	10/2013	46(O) 31(R)	0/0
271	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	2,820.00	141.29	- -	-	-	0/0
272	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	435.87	412.10	03/2011 03/2011	03/2011	-	0/0
273	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	725.00	559.04	06/1999 03/2011	03/2011	-	0/0
274	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	307.00	-	- -	-	-	0/0
275	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	1,566.00	120.90	- -	-	-	0/0
276	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	199.75	32.35	- -	-	-	0/0
277	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	252.00	-	- -	-	-	0/0
278	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	567.18	0.17	- -	-	-	0/0
279	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	1,215.30	35.42	03/2013 -	03/2013	-	0/0
280	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	218.39	16.50	- -	-	-	0/0
281	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	822.00	-	- -	-	-	0/0
282	Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh	04/2012	153.00 -	153.00	-	- -	-	-	0/0
283	Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State	04/2008	184.26 -	2,000.00	21.02	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
284	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	242.09	-	- -	-	-	0/0
285	Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State	04/2010	338.54 -	338.54	77.27	- -	-	-	0/0
286	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	312.12	30.77	- -	03/2015	-	0/0
287	Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi	04/2012	295.68 -	295.68	-	- -	-	-	0/0
288	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
289	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
290	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	527.00	2.88	- -	-	-	0/0
291	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	901.62	0.51	- -	-	-	0/0
292	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,039.29	1,423.98	482.85	03/2005 12/2008	12/2016	141(O) 96(R)	0/0
293	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	1,106.62	225.47	12/2010 03/2011	03/2011	-	0/0
294	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	319.75	03/2004 12/2010	12/2014	129(O) 48(R)	0/0
295	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	96.43	04/2014 -	03/2017	35(O) -	0/0
296	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	195.64	67.91	- -	-	-	0/0
297	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69(O) -	0/0
298	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.19	2,854.15	04/2008 03/2014	12/2015	92(O) 21(R)	0/0
299	Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka	04/2010	377.93 -	377.93	10.33	- -	-	-	0/0
300	Bandel-Boinchhi 3rd line - [N22000221]ER,Multi State	04/2011	288.35 -	288.35	3.99	- -	-	-	0/0
301	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	179.63	12/2012 -	12/2013	12(O) -	0/0
302	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	246.08	0.11	- -	-	-	0/0
303	Bariarpur-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	450.55	9.35	- -	-	-	0/0
304	Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal	04/2012	255.64 -	255.64	-	- -	-	-	0/0
305	Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh	04/2010	337.49 -	337.49	0.12	- -	-	-	0/0
306	Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh	04/2012	923.23 -	923.23	-	- -	-	-	0/0
307	Bhadutola-Jhargram via Lalgarh (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	289.64	0.07	- -	-	-	0/0
308	Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh	04/2008	1,046.88 -	2,966.99	37.82	- -	-	-	0/0
309	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	196.95	193.49	03/2011 -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
310	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	485.65	1.76	03/2012 -	-	-	0/0
311	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	326.20	1.69	- -	-	-	0/0
312	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	175.80	0.88	- -	-	-	0/0
313	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	267.37	33.79	- -	-	-	0/0
314	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
315	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	1,115.21	970.35	12/2012 01/2013	04/2013	-	0/0
316	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	295.00	0.06	- -	-	-	0/0
317	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
318	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
319	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	243.78	26.31	- -	-	-	0/0
320	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	358.30	- -	12/2013	-	0/0
321	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	41.85	03/2015 -	12/2015	9(O) -	0/0
322	Chandigarh-Baddi NL - [N22000296]NR,Multi State	04/2007	328.14 -	328.14	1.03	- -	-	-	0/0
323	Chandpara-Bangaon doubling with extension to Chandb - [N22000242]ER,Multi State	04/2003	337.96 -	337.96	59.07	- -	-	-	0/0
324	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	951.24	520.43	- -	-	-	0/0
325	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	222.95	91.12	- -	-	-	0/0
326	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	520.00	458.54	- -	-	-	0/0
327	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	1,200.00	1.80	- -	-	-	0/0
328	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	378.56	104.60	- -	-	-	0/0
329	Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka	04/2013	327.25 -	327.25	-	- -	-	-	0/0
330	Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka	04/2013	558.00 -	558.00	-	- -	-	-	0/0
331	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER,Multi State	04/2005	595.91 -	595.91	88.51	- -	-	-	0/0
332	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	1,347.26	139.03	- -	-	-	0/0
333	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
334	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,151.00	944.37	03/2007 -	03/2015	96(O) -	0/0
335	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	556.64	266.48	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
336	Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh	04/2013	829.00 -	829.00	-	- -	-	-	0/0
337	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
338	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	406.92	106.18	- -	-	-	0/0
339	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	233.81	- -	03/2014	-	0/0
340	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	607.09	501.62	12/2012 12/2012	02/2013	-	0/0
341	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	914.98	676.38	- -	12/2012	-	0/0
342	Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State	04/2007	1,640.04 -	1,640.04	151.56	- -	-	-	0/0
343	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	533.38	99.95	12/2011 02/2012	02/2012	-	0/0
344	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]SER,Jharkhand	04/2010	309.44 -	388.67	42.55	12/2015 -	12/2015	0(O) -	0/0
345	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER,Multi State	04/2010	296.44 -	296.44	3.21	- -	-	-	0/0
346	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	366.73	4.00	- -	-	-	0/0
347	Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
348	Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State	04/2007	336.91 -	336.91	140.59	- -	-	-	0/0
349	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	376.59	0.17	- -	-	-	0/0
350	Dholpur-Sirmuttra with extension to Gangapurcity A - [N22000158]NCR,Multi State	04/2010	622.41 2,030.50	2,030.50	1.22	02/2019 -	02/2019	0(O) -	0/0
351	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	651.17	7.08	- -	-	-	0/0
352	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
353	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016	0(O) -	0/0
354	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G' - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24(O) 3(R)	0/0
355	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	241.09	12/2008 -	09/2014	69(O) -	0/0
356	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	252.46	06/2013 06/2013	12/2014	18(O) 18(R)	0/0
357	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	189.24	1.77	- -	-	-	0/0
358	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	603.22	1.31	- -	-	-	0/0
359	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240(O) -	0/0
360	Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareilly - [N22000270]NR,Uttar Pradesh	04/2013	654.00 -	654.00	-	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
361	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	270.00	280.64	02/2011 02/2011	03/2013	-	0/0
362	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	261.70	111.25	02/2006 -	-	-	0/0
363	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	863.23	725.50	- -	03/2012	-	0/0
364	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
365	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	832.00	355.51	- 05/2009	05/2009	-	0/0
366	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	580.90	03/1994 -	10/2013	235(O) -	0/0
367	Gadag-Wadi NL - [N22000299]SWR,Karnataka	04/2013	1,117.00 -	1,117.00	-	- -	-	-	0/0
368	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	415.67	13.43	- -	-	-	0/0
369	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	445.25	0.94	- -	-	-	0/0
370	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	130.62	12/2011 11/2013	11/2013	23(O) 0(R)	0/0
371	Grade Seperator at Dayabasti - [N22000269]NR,Delhi	04/1999	159.20 -	159.20	50.29	- -	-	-	0/0
372	Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh	04/2011	283.54 -	283.54	0.02	- -	-	-	0/0
373	Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	206.22	2.66	- -	-	-	0/0
374	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State	04/2011	1,176.09 3,845.60	3,845.60	1.71	02/2020 -	02/2020	0(O) -	0/0
375	HAIJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	528.65	191.64	- -	-	-	0/0
376	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	1,185.64	242.38	- 09/2009	-	-	0/0
377	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
378	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	412.91	717.04	- -	01/2013	-	0/0
379	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	149.24	- -	03/2014	-	0/0
380	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	178.39	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
381	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	2,135.00	101.17	- -	-	-	0/0
382	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State	04/2000	157.17 -	157.17	75.86	- -	-	-	0/0
383	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	213.01	-	- -	-	-	0/0
384	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	267.09	0.10	- -	-	-	0/0
385	Hansnabad-Hingalganj New BG line - [N22000218]ER,Multi State	04/2010	172.03 -	172.03	2.93	- -	-	-	0/0
386	Haridwar-Laksar - [N22000289]NR,Uttarakhand	04/2012	219.83 -	444.18	-	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
387	Himmatnagar - Udaipur Gauge Canvession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	829.74	35.38	03/2015 -	03/2015	0(O) -	0/0
388	Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana	04/2013	400.00 -	400.00	-	- -	-	-	0/0
389	Hospet-Hubli-Londa-Vascodagama DL - [N22000297]SWR,Karnataka	04/2010	2,127.00 -	2,127.00	47.34	- -	-	-	0/0
390	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	157.94	37.90	- -	-	-	0/0
391	Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State	04/2011	166.89 -	166.89	-	- -	-	-	0/0
392	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP,Andhra Pradesh	04/2012	632.68 -	816.55	0.44	04/2012 -	-	-	0/0
393	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	847.75	836.10	06/2007 -	06/2007	-	0/0
394	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	1,043.56	716.15	03/2012 08/2012	-	-	0/0
395	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	693.39	477.36	03/2012 03/2012	12/2012	-	0/0
396	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,655.40	03/2011 03/2014	03/2017	72(O) 36(R)	0/0
397	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	653.47	248.21	03/2014 -	03/2014	0(O) -	0/0
398	Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State	04/2008	165.65 -	165.65	131.83	- -	-	-	0/0
399	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar	04/2009	470.00 -	470.00	34.32	- -	-	-	0/0
400	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	333.50	319.60	03/2012 03/2012	03/2013	-	0/0
401	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	1,708.41	1,481.00	- -	03/2013	-	0/0
402	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	643.00	-	- -	-	-	0/0
403	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	744.71	511.57	- -	03/2014	- -	1/1
404	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	775.36	755.54	- -	10/2012	-	0/0
405	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.39	12/2010 12/2010	03/2015	51(O) 51(R)	0/0
406	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	162.87	124.50	- -	-	-	0/0
407	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	257.89	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
408	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	265.42	- -	03/2014	- -	0/0
409	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	- -	0/0
410	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	768.87	496.29	- 03/2010	03/2010	-	0/0
411	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	2,957.21	1,618.13	07/2005 -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
412	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	418.17	171.00	- -	-	-	0/0
413	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	341.41	289.96	03/2012 03/2013	03/2013	-	0/0
414	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	1,045.20	9.41	- -	-	-	0/0
415	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	302.23	357.12	- -	12/2012	-	0/0
416	Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State	04/2008	2,050.00 -	2,050.00	92.95	- -	-	-	0/0
417	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER,Multi State	04/2001	923.52 -	923.52	232.54	- -	-	-	0/0
418	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER,Multi State	04/2010	174.56 -	174.56	46.21	- -	-	-	0/0
419	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	279.70	1.64	- -	-	-	0/0
420	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	126.12	12/2012 -	03/2015	27(O) -	0/0
421	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State	04/2010	423.66 -	423.66	136.58	03/2017 -	03/2017	0(O) -	0/0
422	Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State	04/2012	1,054.35 -	1,054.35	0.35	- -	-	-	0/0
423	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	287.99	421.25	01/1999 -	12/2013	179(O) -	0/0
424	Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh	04/2013	723.00 -	723.00	-	- -	-	-	0/0
425	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	252.96	1.57	- -	-	-	0/0
426	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
427	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	346.15	6.69	- -	-	-	0/0
428	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	1,630.97	396.70	05/2008 03/2011	-	-	0/0
429	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	229.64	03/2002 -	10/2013	139(O) -	0/0
430	Lakshmikantapur-Namkhana subsequently MM for Namkh - [N22000216]ER,Multi State	04/1999	406.99 -	406.99	137.78	- -	-	-	0/0
431	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244]ER,Multi State	04/2009	257.42 -	257.42	33.39	03/2014 -	03/2014	0(O) -	0/0
432	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam	04/2012	246.07 -	246.07	0.11	- -	-	-	0/0
433	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,677.32	03/2009 -	12/2014	69(O) -	0/0
434	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	480.00	0.61	07/2008 -	07/2008	-	0/0
435	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	472.00	179.39	- -	02/2013	-	0/0
436	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	900.05	730.72	12/2011 12/2011	03/2013	-	0/0
437	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	791.59	0.76	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
438	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	477.88	442.21	03/2012 03/2013	03/2013	-	0/0
439	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	1,383.45	359.56	- -	-	-	0/0
440	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,301.02	03/2014 03/2016	12/2016	33(O) 9(R)	0/0
441	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	645.00	248.11	- -	03/2012	-	0/0
442	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	260.72	10.87	- -	-	-	0/0
443	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State	04/2011	601.43 -	800.00	0.14	- -	-	-	0/0
444	Magrahat-Diamond Harbour with MM Sangrampur-Krishna - [N22000243]ER,Multi State	04/2009	493.96 -	493.96	115.49	- -	-	-	0/0
445	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	258.20	0.14	- -	03/2016	-	0/0
446	Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
447	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	965.16	557.76	- -	-	-	0/0
448	Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh	04/2012	289.79 -	289.79	-	- -	-	-	0/0
449	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	439.88	0.70	- -	-	-	0/0
450	Monigram- Nimita - [N22000301]ER,Multi State	04/2012	250.93 -	250.93	-	- -	-	-	0/0
451	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	211.00	4.41	- -	-	-	0/0
452	Mudkhed-Parbhani - [N22000283](SCR),Maharashtra	04/2011	390.60 -	390.60	0.68	- -	-	-	0/0
453	Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka	04/2007	179.65 -	645.00	167.20	- -	-	-	0/0
454	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	165.82	0.25	- -	-	-	0/0
455	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
456	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	228.05	0.64	- -	-	-	0/0
457	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	883.00	667.01	02/2009 -	03/2012	-	0/0
458	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	1,036.78	357.94	07/2012 -	-	-	0/0
459	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	532.87	42.20	- -	-	-	0/0
460	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	143.25	- -	03/2015	-	0/0
461	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,480.03	12/2008 -	03/2015	75(O) -	0/0
462	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	169.82	32.10	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
463	Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh	04/2011	1,313.48 -	1,313.48	0.51	- -	-	-	0/0
464	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	620.57	-	- -	-	-	0/0
465	New Alipur to Akra, MM for Budge Budge-Pujali NL, - [N22000240]ER,Multi State	04/2010	494.54 -	494.54	31.92	- -	-	-	0/0
466	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.34	- -	03/2015	- -	0/0
467	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	242.22	37.95	- -	-	-	0/0
468	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	4,083.02	2.79	- -	-	-	0/0
469	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	247.75	148.41	- -	03/2014	- -	0/0
470	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	238.83	98.33	- -	-	-	0/0
471	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	221.42	21.80	- -	-	-	0/0
472	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
473	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	209.77	22.93	- -	03/2015	- -	0/0
474	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	283.55	0.40	- -	03/2015	- -	0/0
475	New Jalpaiguri-Siliguri-New Bongaigaon including B - [N22000209]NEFR,Multi State	04/1999	523.17 -	1,393.44	1,032.99	- -	-	-	0/0
476	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24(O) -	0/0
477	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02 -	2,619.02	332.96	03/2016 -	03/2016	0(O) -	0/0
478	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	2,069.60	25.21	03/2014 -	03/2014	0(O) -	0/0
479	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98 -	3,951.98	187.23	03/2016 -	03/2016	0(O) -	0/0
480	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	52.60	03/2016 -	06/2016	3(O) -	0/0
481	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	1,117.11	459.49	03/2008 06/2008	-	-	0/0
482	PANVEL PEN DOUBLING - [N22000255]CR,Multi State	04/2006	191.00 -	191.00	196.89	- -	01/2014	- -	0/0
483	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,880.08	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
484	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	627.20	- -	02/2014	- -	0/0
485	PEN ROHA DOUBLING - [N22000254]CR,Multi State	04/2007	203.00 -	203.00	156.83	- -	03/2014	- -	0/0
486	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
487	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	293.74	139.31	12/2010 12/2010	12/2010	-	0/0
488	Pirpainti-Bhagalpur - [N22000222]ER,Multi State	04/2011	261.38 -	261.38	14.55	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
489	Pirpainti-Jasidih - [N22000219]ER,Multi State	04/2013	915.98 -	915.98	-	- -	-	-	0/0
490	Plassey-Jiaganj Doubling - [N22000220]ER,Multi State	04/2011	248.07 -	248.07	9.83	03/2015 -	03/2015	0(O) -	0/0
491	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State	04/2011	299.60 -	299.60	1.09	03/2017 -	03/2017	0(O) -	0/0
492	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	323.00	-	- -	-	-	0/0
493	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	1,029.92	818.25	- -	03/2013	-	0/6
494	Qadian-Beas - [N22000295]NR,Punjab	04/2011	205.22 -	205.22	1.22	- -	-	-	0/0
495	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	289.93	264.93	12/2007 03/2010	-	-	0/0
496	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,174.03	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
497	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	285.59	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
498	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	1,225.90	227.86	- -	-	-	0/0
499	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.35	347.27	06/2004 -	12/2014	126(O) -	0/0
500	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,019.17	2,201.79	- -	03/2014	-	0/0
501	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	639.97	176.01	03/1998 08/2005	08/2005	-	0/0
502	Rajkot-Veraval,Wansjalila to Jatalsar with new MM f - [N22000143]WR,Gujarat	04/1994	320.66 -	320.66	460.14	- -	-	-	0/0
503	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	505.38	03/2013 -	03/2014	12(O) -	0/0
504	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	288.97	-	- -	-	-	0/0
505	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And - [N22000153]NWR,Rajasthan	04/2010	739.65 -	872.22	789.67	- -	-	-	0/0
506	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	2,082.75	11.26	- -	-	-	0/0
507	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	1,421.25	260.43	03/2012 -	-	-	0/0
508	Rayadurga-Tumkur NL - [N22000279]SWR,Multi State	04/2007	970.34 -	970.34	188.92	- -	-	-	0/0
509	Rohtak-Meham Hansi - [N22000272]NR,Haryana	04/2012	287.00 -	287.00	0.04	- -	-	-	0/0
510	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	714.10	2.42	- 12/2017	12/2017	- 0(R)	0/0
511	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
512	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	59.60	12/2015 -	03/2017	15(O) -	0/0
513	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	818.29	105.60	02/2015 -	02/2015	0(O) -	0/0
514	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	193.44	12.34	- -	-	-	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
515	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	325.00	230.97	- -	-	-	0/0
516	Sakri-Nirmali and Jhanjharpur-Laukahabazar and Sah - [N22000180]ECR,Bihar	04/2004	372.14 -	355.81	365.77	- -	-	-	0/0
517	Santoshpur-Remount Road via Garden Reach-Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	268.52	77.87	- -	-	-	0/0
518	Shimoga-Harihar NL - [N22000278]SWR,Karnataka	04/2011	562.74 -	562.74	0.06	- -	-	-	0/0
519	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	678.62	14.68	- -	-	-	0/0
520	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State	04/2000	297.47 -	297.47	51.70	- -	-	-	0/0
521	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	277.28	35.91	- -	-	-	0/0
522	Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State	04/2013	296.00 -	296.00	-	- -	-	-	0/0
523	Sriperumbudur-Guduvanchery with spur to Irungattukkottai-Ava - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	839.00	-	- -	-	-	0/0
524	Sultanganj-Katuria via Asarganj, Tarapur And Belha - [N22000217]ER,Multi State	04/2007	450.00 -	450.00	7.70	- -	-	-	0/0
525	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	516.23	420.70	03/2014 -	03/2014	0(O) -	0/0
526	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	810.78	128.44	- -	-	-	0/0
527	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	448.95	06/2005 07/2011	06/2016	132(O) 59(R)	0/0
528	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	1,188.91	640.12	- 12/2009	02/2012	-	0/0
529	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	582.83	175.75	- -	-	-	0/0
530	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	227.40	58.00	- -	-	-	0/0
531	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	800.00	549.98	- -	-	-	0/0
532	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	3,176.10	3,454.29	12/2006 08/2010	08/2010	-	0/0
533	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	171.02	113.17	06/2013 -	-	-	0/0
534	Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	365.17	1.43	- -	-	-	0/0
535	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.39 -	236.93	-	- -	-	-	0/0
536	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	167.73	49.10	03/2012 -	02/2013	-	0/0
537	Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka	04/2011	913.00 -	913.00	0.46	- -	-	-	0/0
538	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181(O) -	0/0
539	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	1,116.53	231.10	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
540	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	1,389.62	675.23	03/2014 -	03/2014	0(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
541	Unchahar-Amethi - [N22000294]NR,Uttar Pradesh	04/2012	380.00 -	380.00	0.35	- -	-	-	0/0
542	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	548.01	199.64	- 03/2010	-	-	0/0
543	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
544	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	685.17	14.31	- -	-	-	0/0
545	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	264.06	113.62	- -	04/2014	- -	0/0
546	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	1,604.00	18.11	- -	-	-	0/0
547	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	297.85	1.16	- -	-	-	0/0
548	White Field-Kolar NL - [N22000280]SWR,Karnataka	04/2011	341.05 -	348.85	0.18	- -	-	-	0/0
549	Yamunanagar-Chandigarh via Sadhaura Narayangarh - [N22000293]NR,Multi State	04/2013	876.00 -	876.00	-	- -	-	-	0/0
550	ansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur M - [N22000268]NR,Punjab	04/2009	396.04 -	396.04	76.07	- -	-	-	0/0
	Total		147,446.28 -	258,258.56	75,461.51				1/7
	<u>Road Transport And Highways</u>								
551	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	250.50	230.10	10/2014 -	10/2014	0(O) -	0/0
552	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	373.47	40.66	07/2014 -	07/2014	0(O) -	0/0
553	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	395.20	05/2013 -	03/2014	10(O) -	0/0
554	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54 -	511.54	642.20	11/2013 -	11/2013	0(O) -	0/0
555	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	624.00	314.70	04/2014 -	04/2014	0(O) -	0/0
556	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh	10/2011	1,565.00 -	1,565.00	691.40	10/2014 -	10/2014	0(O) -	0/0
557	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	356.40	-	07/2014 -	07/2014	0(O) -	0/0
558	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	291.36	98.48	01/2014 -	01/2014	0(O) -	0/0
559	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	226.00	189.10	02/2014 -	02/2014	0(O) -	0/0
560	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	564.60	02/2014 -	04/2014	2(O) -	0/0
561	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014	0(O) -	0/0
562	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	325.00	161.20	05/2014 -	05/2014	0(O) -	0/0
563	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat	03/2012	828.00 -	828.00	490.60	09/2014 -	09/2014	0(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
564	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,734.00	08/2014 -	07/2015	11(O) -	0/0
565	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,352.00	06/2013 -	12/2013	6(O) -	0/0
566	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.39	09/2013 -	07/2014	10(O) -	0/0
567	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	843.90	08/2013 -	12/2013	4(O) -	0/0
568	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.40	07/2013 -	12/2013	5(O) -	0/0
569	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	398.00	441.10	02/2014 -	02/2014	0(O) -	0/0
570	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,266.00	08/2013 -	12/2014	16(O) -	0/0
571	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,328.00	08/2013 -	12/2014	16(O) -	0/0
572	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	299.60	08/2013 -	12/2015	28(O) -	0/0
573	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	1,396.18	1,048.00	09/2014 -	09/2014	0(O) -	0/0
574	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	240.70	09/2007 -	03/2014	78(O) -	0/0
575	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	2,125.24	34.28	12/2015 -	12/2015	0(O) -	0/0
576	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,144.00	11/2012 -	12/2013	13(O) -	0/0
577	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.60	01/2009 -	12/2013	59(O) -	0/0
578	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	390.56	772.40	02/2012 -	06/2013	-	0/0
579	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	117(O) -	0/0
580	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	357.00	09/2013 -	12/2014	15(O) -	0/0
581	BARSAT-KRISHNANAGAR - [N24000229]NHAI,West Bengal	08/2012	867.00 -	867.00	-	02/2015 -	02/2015	0(O) -	0/0
582	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	2,388.00	1,388.00	06/2014 -	06/2014	0(O) -	0/0
583	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	567.90	-	10/2013	-	2/2
584	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9(O) -	0/0
585	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	509.40	08/2013 -	12/2013	4(O) -	0/0
586	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	289.00	06/2008 -	03/2014	69(O) -	0/0
587	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	252.60	06/2008 -	03/2014	69(O) -	0/0
588	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	239.90	06/2005 -	03/2014	105(O) -	0/0
589	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	297.90	04/2010 -	12/2014	56(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
590	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65(O) -	0/0
591	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	839.20	03/2013 -	12/2013	9(O) -	0/0
592	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	667.90	-	12/2013	-	0/1
593	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2013	7(O) -	0/0
594	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	446.20	10/2011 -	03/2014	29(O) -	0/0
595	Chilikaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	857.90	10/2011 -	06/2014	32(O) -	0/0
596	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.80	10/2008 -	06/2014	68(O) -	0/0
597	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015	0(O) -	0/0
598	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	660.30	05/2010 -	10/2013	41(O) -	0/0
599	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	582.90	07/2013 -	12/2013	5(O) -	0/0
600	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI, Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6(O) -	0/0
601	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	718.70	-	12/2013	-	1/1
602	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	253.90	06/2008 -	03/2014	69(O) -	0/0
603	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	207.70	05/2008 -	12/2013	67(O) -	0/0
604	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	305.20	09/2010 -	08/2014	47(O) -	0/0
605	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	318.00	08/2013 -	02/2015	18(O) -	0/0
606	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	1,573.00	17.23	09/2015 -	09/2015	0(O) -	0/0
607	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	475.50	09/2008 -	12/2013	63(O) -	0/0
608	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015	0(O) -	0/0
609	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	160.00	10/2013 -	11/2015	25(O) -	0/0
610	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30(O) -	0/0
611	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	144.30	09/2008 -	03/2014	66(O) -	0/0
612	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.46	02/2004 -	09/2013	115(O) -	0/0
613	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,287.00	08/2013 -	06/2014	10(O) -	0/0
614	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	276.20	04/2008 -	03/2014	71(O) -	0/0
615	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	217.60	04/2008 -	03/2014	71(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
616	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60(O) -	0/0
617	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,123.00	09/2012 -	12/2013	15(O) -	0/0
618	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26(O) -	0/0
619	HAPUR-GARH Mukteswar (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74(O) -	0/0
620	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	324.60	02/2009 03/2014	05/2014	63(O) 2(R)	0/0
621	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	158.70	07/2009 -	05/2014	58(O) -	0/0
622	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	70.00	09/2007 -	04/2014	79(O) -	0/0
623	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	281.10	10/2013 -	03/2014	5(O) -	0/0
624	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	110(O) -	0/0
625	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	204.82	08/2004 07/2010	10/2013	110(O) 39(R)	0/0
626	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	948.00	01/2013 -	10/2013	9(O) -	0/0
627	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,790.00	- -	10/2013	- -	3/3
628	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	532.70	05/2013 -	02/2014	9(O) -	0/0
629	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8(O) -	0/0
630	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	651.60	02/2013 -	12/2013	10(O) -	0/0
631	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11(O) -	0/0
632	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.40	09/2009 -	12/2013	51(O) -	0/0
633	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	536.00	518.00	01/2014 -	01/2014	0(O) -	0/0
634	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,975.00	12/2012 -	02/2014	14(O) -	0/0
635	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	280.40	10/2008 -	12/2013	62(O) -	0/0
636	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	295.00	10/2008 -	12/2013	62(O) -	0/0
637	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	702.16	498.90	07/2014 -	07/2014	0(O) -	0/0
638	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	938.40	- -	06/2014	- -	2/3
639	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	12/2013	19(O) -	0/0
640	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
641	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI, Madhya Pradesh	12/2003	263.17 -	263.17	235.20	09/2009 -	09/2014	60(O) -	0/0
642	LUCKNOW-RAIBAREILI - [N24000207]NHAI, Uttar Pradesh	07/1999	635.90 -	635.90	257.00	07/2012 -	07/2014	24(O) -	0/0
643	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, Assam	12/2003	155.04 -	280.13	125.00	11/2008 -	06/2014	67(O) -	0/0
644	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, Assam	12/2003	199.81 -	385.13	93.63	04/2009 -	12/2014	68(O) -	0/0
645	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, Assam	12/2003	167.64 -	167.64	72.60	11/2008 -	12/2014	73(O) -	0/0
646	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI, Assam	12/2003	200.00 -	200.00	169.00	04/2009 -	12/2014	68(O) -	0/0
647	MURADABAD-BAREILY - [N24000154]NHAI, Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,876.00	06/2013 -	03/2014	9(O) -	0/0
648	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, Multi State	09/2011	754.00 -	754.00	515.80	03/2013 -	03/2014	12(O) -	0/0
649	Muzafarpur - Sonbarsa - [N24000174]NHAI, Bihar	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	0(O) -	0/0
650	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI, Assam	12/2003	264.72 -	264.72	301.10	06/2008 -	03/2014	69(O) -	0/0
651	NAGPUR-KONDHALI, NH-6(NHAI) - [N24000055]NHAI, Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63(O) -	0/0
652	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI, Maharashtra	04/2012	484.19 -	484.19	282.80	10/2014 -	10/2014	0(O) -	0/0
653	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, Assam	12/2003	208.00 -	208.00	308.70	04/2008 -	05/2014	73(O) -	0/0
654	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, Assam	12/2003	225.00 -	225.00	266.10	06/2008 -	12/2013	66(O) -	0/0
655	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI, Assam	12/2003	200.00 -	200.00	288.30	06/2008 -	12/2013	66(O) -	0/0
656	NASHRI CHANANI - [N24000162]NHAI, Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11(O) -	0/0
657	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	288.40	06/2011 06/2011	10/2013	28(O) 28(R)	0/2
658	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI, Kerala	03/2005	557.00 -	557.00	1,129.00	02/2010 -	12/2014	58(O) -	0/0
659	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI, Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11(O) -	0/0
660	New 4 Lane elevated road from Chennai airport - [N24000139]NHAI, Tamil Nadu	09/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013	0(O) -	0/0
661	PANIKHOLI-RIMOLI - [N24000197]NHAI, Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13(O) -	0/0
662	PANIPAT-ROHTAK - [N24000151]NHAI, Haryana	04/2011	807.00 -	807.00	1,318.00	10/2014 -	10/2014	0(O) -	0/0
663	PANVEL-INDAPUR - [N24000216]NHAI, Multi State	12/2011	942.69 -	942.69	198.50	06/2014 -	06/2014	0(O) -	0/0
664	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI, Punjab	12/2003	284.00 -	359.00	327.60	05/2008 -	12/2013	67(O) -	0/0
665	PATNA-BAKTARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, Bihar	09/2011	574.00 -	574.00	655.30	03/2014 -	03/2014	0(O) -	0/0
666	PATNA-MUZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	625.90	02/2013 -	10/2013	8(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
667	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,325.00	07/2012 -	12/2013	17(O) -	0/0
668	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,201.00	03/2013 -	04/2014	13(O) -	0/0
669	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	835.00	388.20	01/2014 -	01/2014	0(O) -	0/0
670	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	12/2013	25(O) -	0/0
671	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17(O) -	0/0
672	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	973.60	07/2015 -	06/2016	11(O) -	0/0
673	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	338.40	10/2008 -	03/2014	65(O) -	0/0
674	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	1,479.00	227.90	06/2015 -	06/2015	0(O) -	0/0
675	REENGUS SIKAR - [N24000227]NHAI,Rajasthan	03/2012	333.51 -	333.51	236.80	09/2014 -	09/2014	0(O) -	0/0
676	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00 -	650.00	1,119.00	11/2013 -	11/2013	0(O) -	0/0
677	SALEM - U / UNDRUPET (BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2013	35(O) -	0/0
678	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	725.40	03/2013 -	12/2013	9(O) -	0/0
679	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	909.00	941.90	05/2014 -	05/2014	0(O) -	0/0
680	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	240.40	09/2007 -	03/2014	78(O) -	0/0
681	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	225.00	191.30	07/2008 -	03/2013	-	0/0
682	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	535.00	-	12/2013 -	12/2013	0(O) -	0/0
683	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013	0(O) -	0/0
684	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	1,535.00	1,218.00	05/2014 -	05/2014	0(O) -	0/0
685	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31(O) -	0/0
686	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014	0(O) -	0/0
687	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	03/2014	72(O) -	0/0
688	SUNAKHALA-GANJAM (GO) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	162.71	04/2004 -	11/2013	115(O) -	0/0
689	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,721.00	08/2011 -	12/2013	28(O) -	0/0
690	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	09/2014	63(O) -	0/0
691	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	860.70	07/2010 -	03/2014	44(O) -	0/0

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
692	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	567.00	1,166.00	11/2013 -	11/2013	0(O) -	0/0
693	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	571.00	-	10/2013 -	10/2013	0(O) -	0/0
694	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	119.10	05/2013 -	12/2013	7(O) -	0/0
695	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	680.00	-	- -	04/2013	-	2/2
696	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	2,848.00	921.30	03/2014 -	03/2014	0(O) -	0/0
697	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	193.10	198.60	03/2008 -	02/2008	-	0/0
698	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	54.59	11/2012 -	03/2014	16(O) -	0/0
699	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,Tamil Nadu	06/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015	0(O) -	0/0
700	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	672.60	07/2013 -	06/2014	11(O) -	0/0
701	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	1,047.00	202.40	06/2014 -	06/2014	0(O) -	0/0
	Total		104,964.22 -	106,902.84	83,933.30				10/14
	<u>Shipping And Ports</u>								
702	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	359.44	358.78	04/2011 11/2011	11/2011	-	0/0
703	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	220.49	98.31	01/2013 06/2013	06/2013	-	0/0
704	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
705	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	448.43	12/2012 11/2013	11/2013	11(O) 0(R)	0/0
706	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	277.03	294.87	12/2011 10/2012	10/2012	-	0/0
707	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014	0(O) -	0/0
708	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-1(O) 0(R)	0/0
709	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	974.80	12/2010 09/2012	12/2014	48(O) 27(R)	0/0
710	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
711	Construction of berthing and allied facilities off - [N25000037]PORT TRUST, Gujarat	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
712	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	1,571.60	5.75	10/2008 -	-	-	0/0
713	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
714	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 12/2013	12/2013	93(O) 0(R)	0/0
715	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
716	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
717	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
718	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	2,427.40	832.04	10/2008 11/2010	-	-	0/0
719	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	4,150.00	3,661.95	01/2012 09/2012	08/2013	-	0/0
720	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		15,617.12 -	17,902.42	8,652.15				0/1
	<u>Telecommunications</u>								
721	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59(O) -	0/0
722	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	247.00	75.89	02/2007 12/2010	-	-	0/0
723	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	229.41	67.21	02/2007 03/2012	02/2013	-	0/0
724	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	229.41	67.21	03/2012 02/2013	-	-	0/0
725	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38(O) 21(R)	0/0
726	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	176.00	86.11	10/2007 -	12/2013	74(O) -	0/0
727	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	84.39	06/2009 -	12/2013	54(O) -	0/0
728	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	373.94	227.58	12/2008 -	12/2012	-	0/0
729	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34(O) 9(R)	0/0
730	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	392.13	164.58	03/2009 -	01/2013	-	0/0
731	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	152.65	-	03/2010 -	-	-	0/0
732	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	952.88	-	03/2010 -	-	-	0/0
733	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	237.44	05/2011 -	12/2013	31(O) -	0/0
	Total		5,699.24 -	5,527.92	2,032.84				0/0
	<u>Urban Development</u>								
734	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3

Sector Wise Details

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
735	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
736	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	35,242.00	3,853.30	03/2016 -	03/2016	0(0) -	0/0
737	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	300.76	09/2014 -	05/2015	8(0) -	0/0
	Total		44,245.18 -	49,518.08	6,421.63				3/3
	<u>Water Resources</u>								
738	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		904,955.28	1,078,958.46	505,233.32				1063/3714

Sector wise current status of projects on the Flash Report

Urban Development


Current Status:

Number of Projects	4
Number of Projects On Schedule	1
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 1 project are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

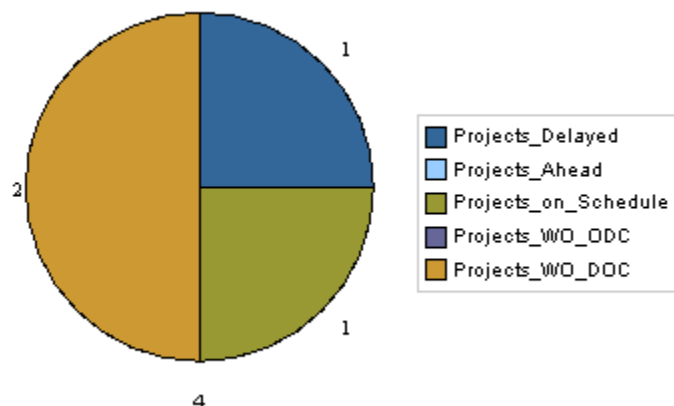

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 44245.18 crore but this was subsequently revised to Rs. 49518.08 crore implying a cost overrun of 11.9%. The expenditure incurred on these projects till September, 2013 is Rs. 6421.63 crore, which is 13% of the revised cost of the projects.

Figures are in Rs. Crore

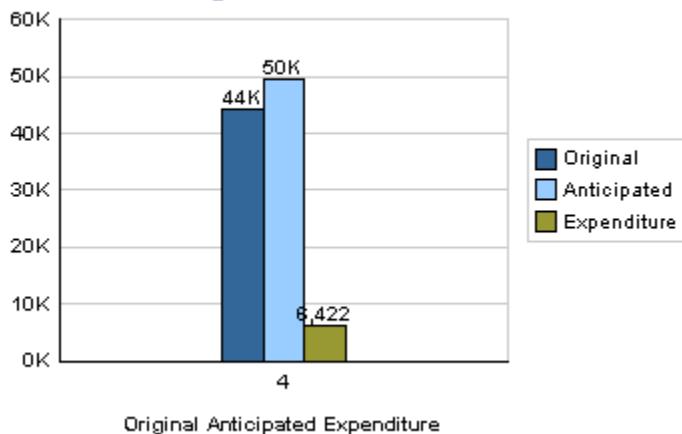

Sector wise current status of projects on the Flash Report

Telecommunications

Current Status:


Number of Projects **13**

Number of Projects Delayed **6**

Number of Projects Without Date Of Commissioning **7**

Brief Analysis


Project Status with respect to Original Schedule: Out of 13 projects, 6 projects are delayed .7 projects do not have fixed dates of commissioning.

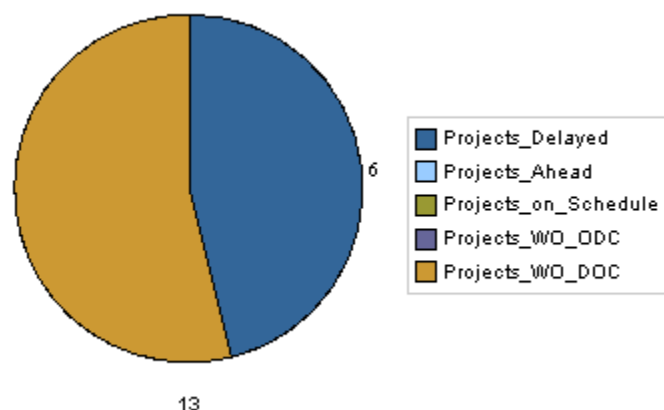

Investment Scenario

The Total Original cost of implementation of 13 projects when sanctioned, was of the order of Rs. 5699.24 crore but this was subsequently revised to Rs. 5527.92 crore implying a cost overrun of -3%. The expenditure incurred on these projects till September, 2013 is Rs. 2032.84 crore, which is 36.8% of the revised cost of the projects.

Figures are in Rs. Crore

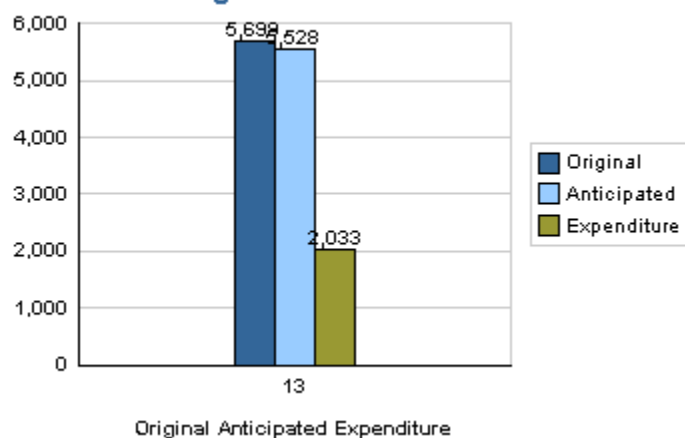

Sector wise current status of projects on the Flash Report


Shipping And Ports

Current Status:

Number of Projects	19
Number of Projects On Schedule	1
Number of Projects Delayed	4
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	13

Brief Analysis


Project Status with respect to Original Schedule: Out of 19 projects, 1 project are ahead of schedule, 1 project are on schedule and 4 projects are delayed .13 projects do not have fixed dates of commissioning.

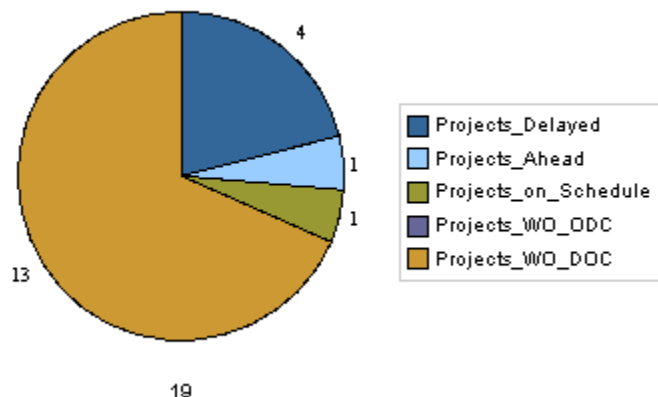

Investment Scenario

The Total Original cost of implementation of 19 projects when sanctioned, was of the order of Rs. 15617.12 crore but this was subsequently revised to Rs. 17902.42 crore implying a cost overrun of 14.6%. The expenditure incurred on these projects till September, 2013 is Rs. 8652.15 crore, which is 48.3% of the revised cost of the projects.

Figures are in Rs. Crore

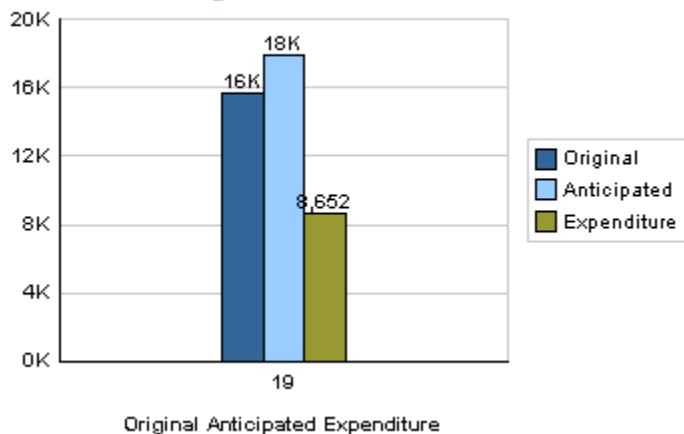

Sector wise current status of projects on the Flash Report

Road Transport And Highways


Current Status:

Number of Projects	151
Number of Projects On Schedule	41
Number of Projects Delayed	101

Number of Projects Without Original Date of Commissioning	5
Number of Projects Without Date Of Commissioning	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 151 projects, 41 projects are on schedule and 101 projects are delayed .4 projects do not have fixed dates of commissioning.5 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

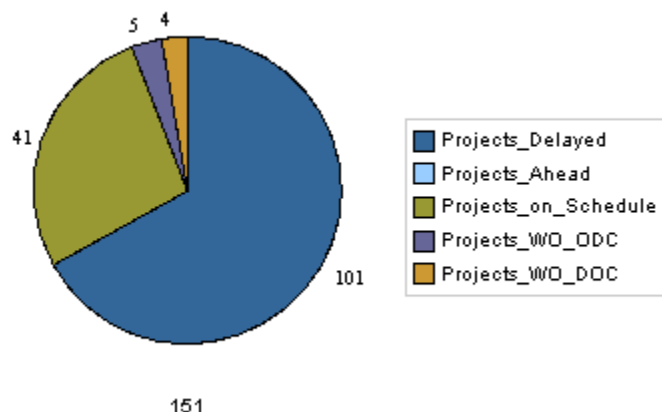

Investment Scenario

The Total Original cost of implementation of 151 projects when sanctioned, was of the order of Rs. 104964.22 crore but this was subsequently revised to Rs. 106902.84 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till September, 2013 is Rs. 83933.3 crore, which is 78.5% of the revised cost of the projects.

Figures are in Rs. Crore

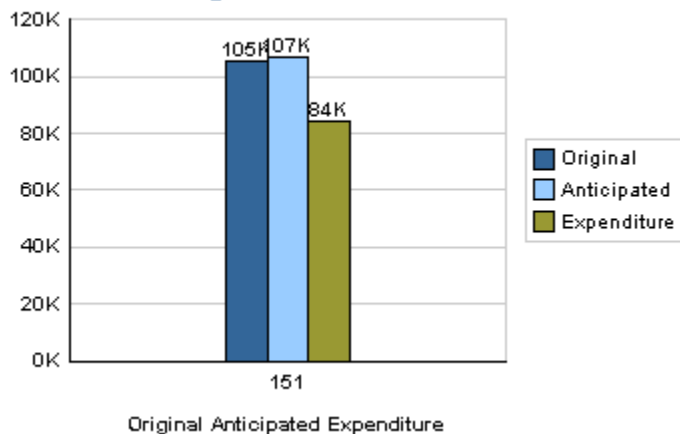

Sector wise current status of projects on the Flash Report

Railways


Current Status:

Number of Projects	283
Number of Projects On Schedule	16
Number of Projects Delayed	37

Number of Projects Without Original Date of Commissioning	20
Number of Projects Without Date Of Commissioning	210

Brief Analysis


Project Status with respect to Original Schedule: Out of 283 projects, 16 projects are on schedule and 37 projects are delayed .210 projects do not have fixed dates of commissioning.20 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

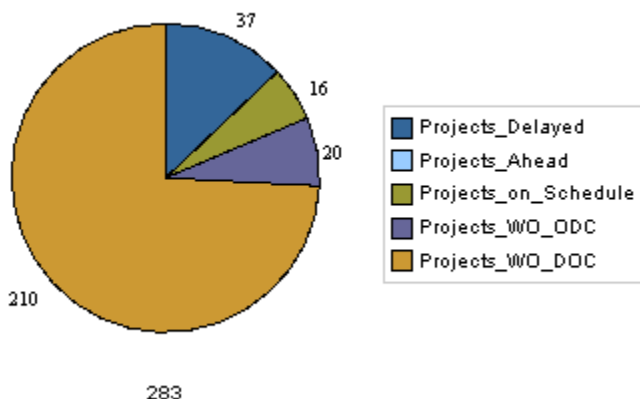

Investment Scenario

The Total Original cost of implementation of 283 projects when sanctioned, was of the order of Rs. 147446.28 crore but this was subsequently revised to Rs. 258258.56 crore implying a cost overrun of 75.2%. The expenditure incurred on these projects till September, 2013 is Rs. 75461.51 crore, which is 29.2% of the revised cost of the projects.

Figures are in Rs. Crore

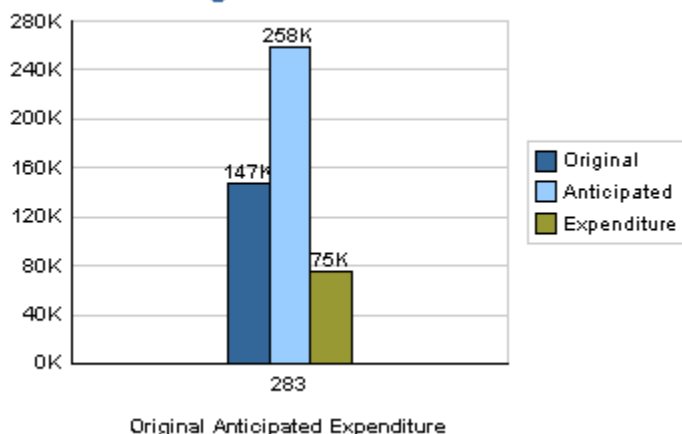

Sector wise current status of projects on the Flash Report


Power

Current Status:

Number of Projects	98
Number of Projects On Schedule	37
Number of Projects Delayed	52
Number of Projects Ahead	3
Number of Projects Without Date Of Commissioning	6

Brief Analysis


Project Status with respect to Original Schedule: Out of 98 projects, 3 projects are ahead of schedule, 37 projects are on schedule and 52 projects are delayed .6 projects do not have fixed dates of commissioning.

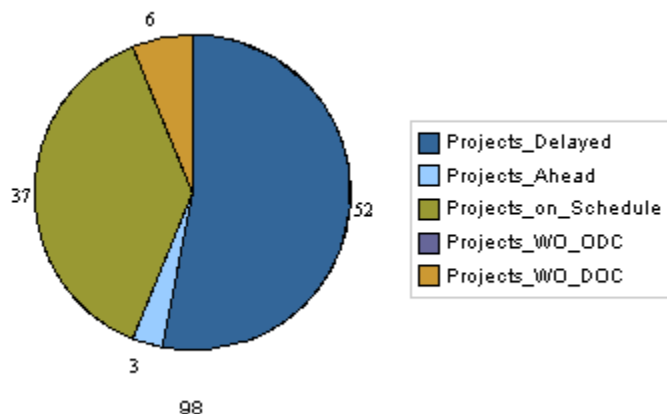

Investment Scenario

The Total Original cost of implementation of 98 projects when sanctioned, was of the order of Rs. 246982.72 crore but this was subsequently revised to Rs. 266241.78 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till September, 2013 is Rs. 126527.06 crore, which is 47.5% of the revised cost of the projects.

Figures are in Rs. Crore

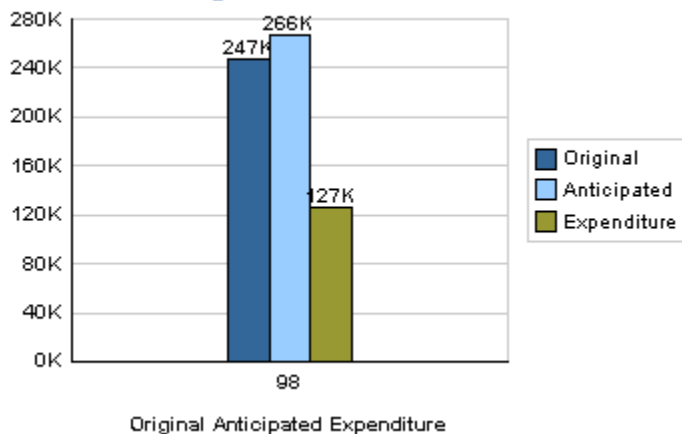

Sector wise current status of projects on the Flash Report


Petroleum

Current Status:

Number of Projects	83
Number of Projects On Schedule	21
Number of Projects Delayed	50
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	10

Brief Analysis


Project Status with respect to Original Schedule: Out of 83 projects, 1 project are ahead of schedule, 21 projects are on schedule and 50 projects are delayed .10 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

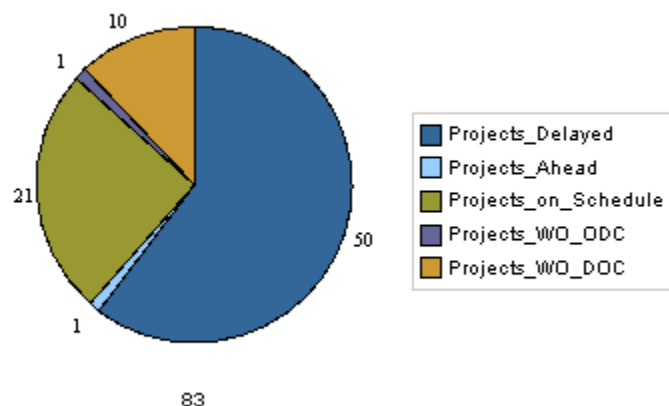

Investment Scenario

The Total Original cost of implementation of 83 projects when sanctioned, was of the order of Rs. 183767.28 crore but this was subsequently revised to Rs. 198154.01 crore implying a cost overrun of 7.8%. The expenditure incurred on these projects till September, 2013 is Rs. 96241.8 crore, which is 48.6% of the revised cost of the projects.

Figures are in Rs. Crore

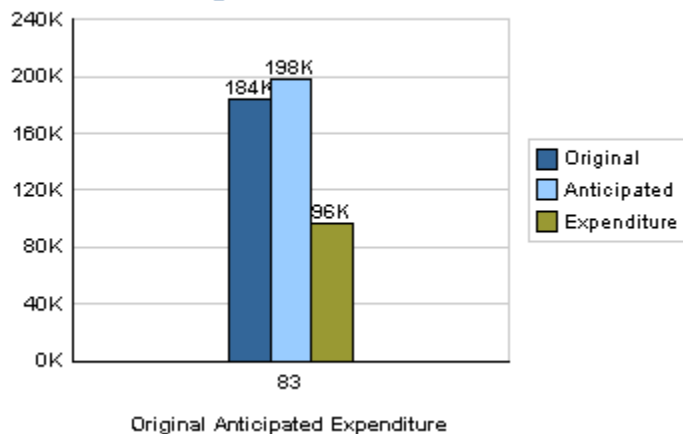

Sector wise current status of projects on the Flash Report

Steel


Current Status:

Number of Projects	18
Number of Projects On Schedule	3
Number of Projects Delayed	14

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are on schedule and 14 projects are delayed .1 project do not have fixed dates of commissioning.

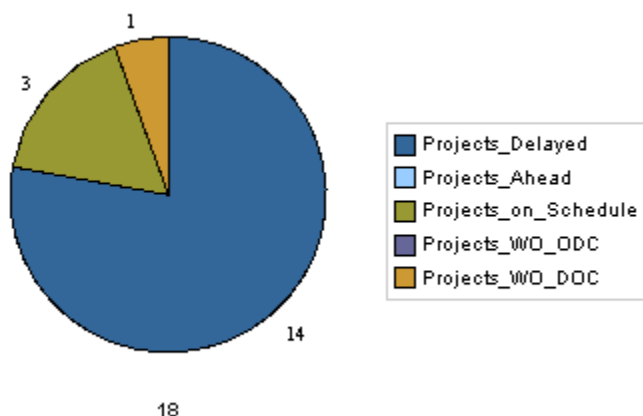

Investment Scenario

The Total Original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 65625.22 crore but this was subsequently revised to Rs. 71782.4 crore implying a cost overrun of 9.4%. The expenditure incurred on these projects till September, 2013 is Rs. 53801.46 crore, which is 75% of the revised cost of the projects.

Figures are in Rs. Crore

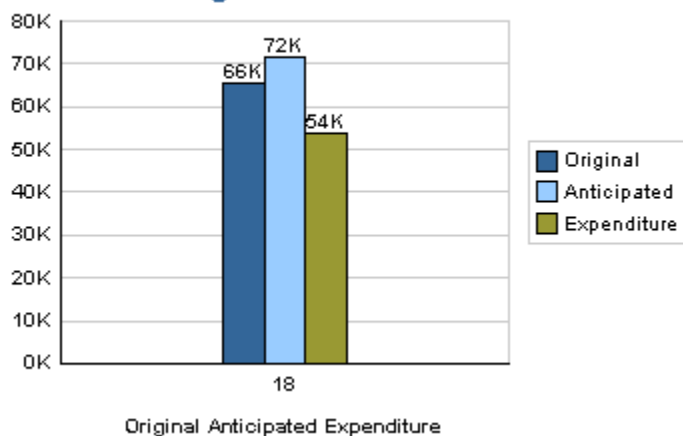

Sector wise current status of projects on the Flash Report

Coal


Current Status:

Number of Projects	55
Number of Projects On Schedule	23
Number of Projects Delayed	28

Number of Projects Without Date Of Commissioning 4

Brief Analysis


Project Status with respect to Original Schedule: Out of 55 projects, 23 projects are on schedule and 28 projects are delayed .4 projects do not have fixed dates of commissioning.

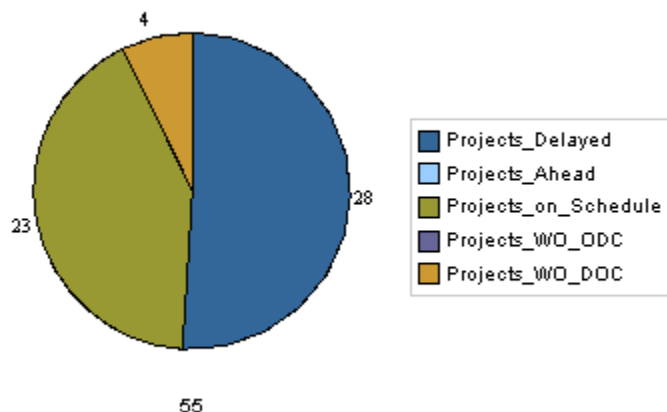

Investment Scenario

The Total Original cost of implementation of 55 projects when sanctioned, was of the order of Rs. 38127.05 crore but this was subsequently revised to Rs. 41212.5 crore implying a cost overrun of 8.1%. The expenditure incurred on these projects till September, 2013 is Rs. 15788.6 crore, which is 38.3% of the revised cost of the projects.

Figures are in Rs. Crore

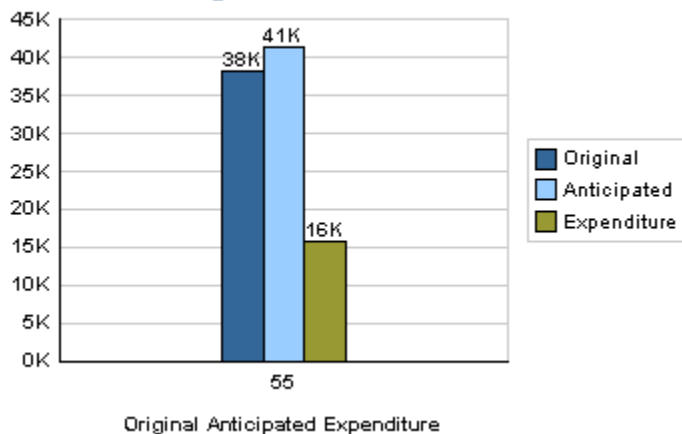

Sector wise current status of projects on the Flash Report

Civil Aviation


Current Status:

Number of Projects	8
Number of Projects On Schedule	2
Number of Projects Delayed	3

Number of Projects Without Date Of Commissioning	3
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 2 projects are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

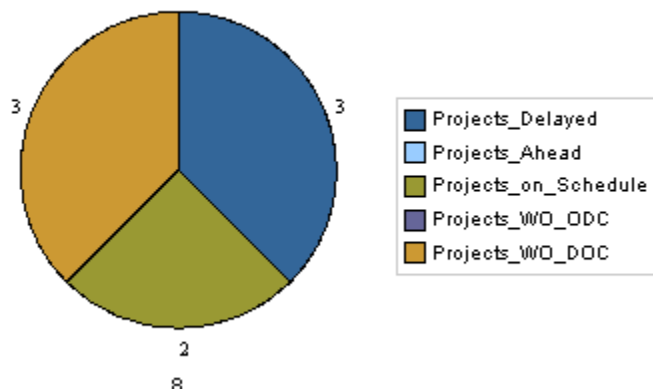

Investment Scenario

The Total Original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6624.95 crore implying a cost overrun of 9.8%. The expenditure incurred on these projects till September, 2013 is Rs. 5453.37 crore, which is 82.3% of the revised cost of the projects.

Figures are in Rs. Crore

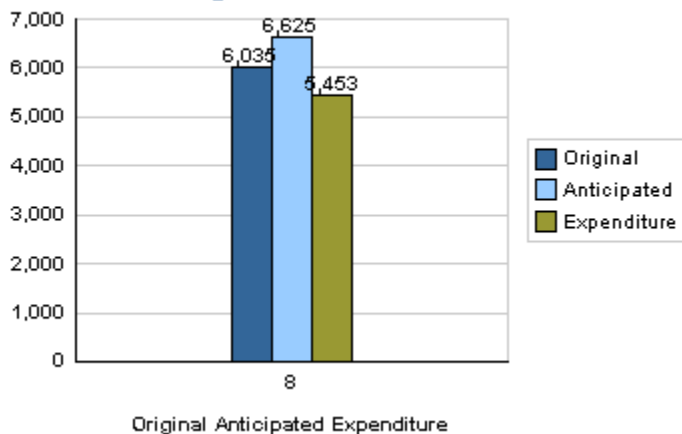

Sector wise current status of projects on the Flash Report


Atomic Energy

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis


Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

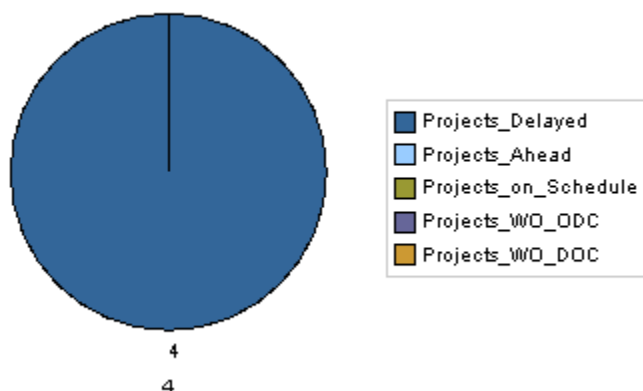

Investment Scenario

The Total Original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till September, 2013 is Rs. 26373.6 crore, which is 56.4% of the revised cost of the projects.

Figures are in Rs. Crore

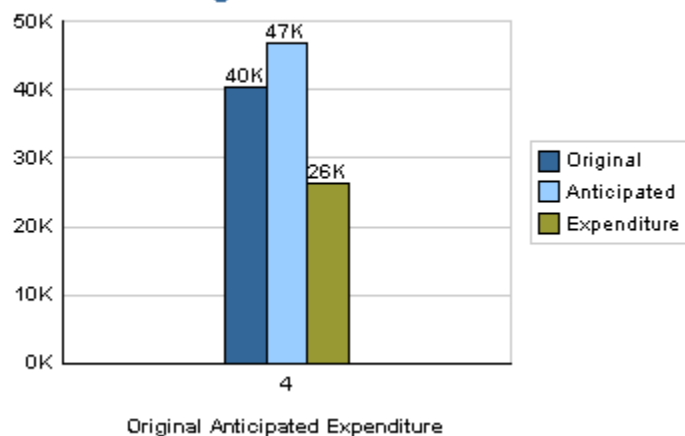

ANNEXURES

LIST OF CENTRAL SECTOR PROJECTS

SN	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	Andhra Pradesh	46	37404.55	45444.29	23595.41
2	Arunachal Pradesh	4	9512.22	17330.32	9855.35
3	Assam	41	24155.49	38429.73	25585.61
4	Bihar	46	32579.04	41019.11	28266.97
5	Chandigarh	1	452.00	452.00	145.42
6	Chhatisgarh	24	58278.32	59362.92	22523.78
7	Delhi	6	38669.29	38649.70	4338.77
8	Goa	1	335.61	335.61	244.70
9	Gujarat	33	38022.74	39317.22	14210.07
10	Haryana	9	4399.88	6082.46	7125.97
11	Himachal Pradesh	6	14402.45	20285.83	14824.62
12	Jammu and Kashmir	9	14305.70	33912.56	15603.26
13	Jharkhand	26	15873.15	20137.87	9917.65
14	Karnataka	37	53868.01	63795.47	26901.84
15	Kerala	10	21010.59	22835.37	6200.62
16	Madhya pradesh	21	31448.20	32674.58	9339.88
17	Maharashtra	56	95785.33	109499.29	50575.16
18	Manipur	1	727.56	4453.50	1655.40
19	Meghalaya	3	4845.02	4845.02	709.89
20	Mizoram	2	1532.97	3297.97	566.56
21	Multi State	173	181049.63	203896.01	82191.05
22	Nagaland	2	5124.00	6715.48	8.94
23	Odisha	31	56321.53	63614.31	41542.21
24	Punjab	6	2212.64	3154.41	3746.82
25	Rajasthan	25	25256.57	25682.57	10992.11
26	Sikkim	2	1648.94	3690.04	291.31
27	Tamil Nadu	41	53242.79	68268.93	44426.10
28	Tripura	5	2669.39	4021.10	2278.61
29	Uttar Pradesh	30	22605.71	27184.92	14750.92
30	Uttarakhand	6	7844.04	10199.28	2741.74
31	West Bengal	35	49371.92	60370.59	30076.58
TOTAL		738	904955.28	1078958.46	505233.32

List of Projects in which Expenditure is more than cost

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	Atomic Energy	09/2003	3492.00	0.00	4681.60
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	Civil Aviation	08/2008	1942.51	0.00	2474.30
3	ADRIYALA SHAFT PROJECT	Coal	12/2009	212.34	779.26	802.36
4	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY	Petroleum	04/2008	825.00	0.00	1469.11
5	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	Petroleum	07/2009	238.68	0.00	293.12
6	RESITMENT OF MARKETING INSTALATION AT VISAKH	Petroleum	01/2009	756.00	898.00	913.72
7	IOR GELEKI (ONGCL)	Petroleum	09/2001	390.09	1674.11	1727.24
8	IOR LAKWA - LAKHMANI (ONGCL)	Petroleum	09/2001	345.10	663.69	729.07
9	TRIPURA GAS BASED POWER PROJECT	Power	07/2009	421.01	0.00	645.71
10	SUBANSIRI LOWER H.E.P (NHPC)	Power	09/2003	6285.33	0.00	6362.61
11	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	Power	09/2005	1061.38	0.00	1387.84
12	NIMOO BAZGO HYDROELECTRIC PROJECT	Power	08/2006	611.01	0.00	877.64
13	URI H.E.P STAGE -II (NHPC)	Power	08/2005	1729.29	0.00	2053.70
14	PARBATI HEP (NHPC) II	Power	09/2002	3919.59	0.00	4058.55
15	BARH STPP(3X660MW) NTPC	Power	12/2003	8692.97	0.00	8704.00
16	KOLDAM HEP (NTPC)	Power	10/2002	4527.15	0.00	5134.00
17	RAMPUR HEP(412 MW)	Power	01/2007	2047.03	0.00	2763.64
18	PANVEL PEN DOUBLING	Railways	04/2006	191.00	0.00	196.89
19	Sakri-Hasanpur Road (NL)	Railways	04/1999	175.69	0.00	230.97
20	LANJHIGARH-JUNAGARH NL(ECOR)	Railways	04/1993	100.00	142.98	229.64
21	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	Railways	04/1996	114.01	332.92	442.21
22	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	Railways	04/1997	233.00	501.69	716.15
23	DANIAWAN-BIHARSARIF (NL), ECR	Railways	04/2001	104.79	0.00	106.18
24	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP)	Railways	03/2000	907.69	3156.32	3454.29
25	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	Railways	04/1986	158.77	580.83	580.90
26	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NARHARIAGUN, NEFR	Railways	09/1996	156.00	156.00	358.30
27	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project	Railways	04/1996	1676.31	1676.31	3677.32
28	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR	Railways	09/1997	1000.00	1500.00	2854.15
29	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	Railways	04/2000	733.00	733.00	1480.03
30	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	Railways	01/2004	915.70	915.70	2201.79
31	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	Railways	12/2006	170.00	170.00	412.10

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
32	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai	Railways	04/1999	523.17	0.00	1032.99
33	Construction of NL from Kumarghat-Agartala	Railways	04/1999	895.00	0.00	944.37
34	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	Railways	04/2003	727.56	727.53	1655.40
35	KATIHAR - JOGBANI (GC)(NEFR)	Railways	09/2001	100.00	492.98	741.39
36	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER)	Railways	04/1999	323.40	323.40	511.57
37	JIND-SONEPAT (NL),NR	Railways	01/2004	190.81	238.56	477.36
38	CHANDIGARH-LUDHIANA(NEW BG LINE),NR	Railways	07/1998	248.44	576.27	970.35
39	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR	Railways	03/2002	409.00	625.30	836.10
40	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	Railways	03/1995	2500.00	2500.00	8822.50
41	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC)	Railways	04/2010	739.65	0.00	789.67
42	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur	Railways	04/2013	456.00	0.00	557.76
43	RAICHUR-GUNTAKAL(DL)(SCR)	Railways	04/2003	136.62	0.00	264.93
44	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	Railways	04/2000	133.41	207.00	257.89
45	RAJATGARH-BARANG(LD),ECOR	Railways	04/1999	166.16	0.00	285.59
46	NANDYAL-YERRAGUNTLA(NL),SCR	Railways	03/1996	155.74	429.49	667.01
47	GADWAL - RAICHUR (NL), SCR	Railways	04/1998	92.63	228.09	280.64
48	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	124.43	495.68	627.20
49	RANCHI-LOHARDAGA(GC),SER	Railways	04/1997	194.07	194.07	347.27
50	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif	Railways	04/2007	247.00	0.00	520.43
51	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	Railways	09/2006	343.17	343.17	676.38
52	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	Railways	09/1995	100.00	100.00	549.98
53	Cuddalore-Salem via Vriddhachalam GC	Railways	04/1999	198.68	0.00	266.48
54	Chennai Beach-Tambaram-Chengalpattu Suburban GC	Railways	04/1999	271.24	0.00	458.54
55	KARUR-SALEM(NL),SR	Railways	02/1997	155.55	155.00	755.54
56	CALICUT-MANGALORE (DL) (SR)	Railways	02/1996	240.00	0.00	599.40
57	Kolar-Chickbalapur GC	Railways	04/2006	287.99	0.00	421.25
58	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR)	Railways	04/2007	482.00	482.70	505.38
59	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR)	Railways	04/1996	157.00	262.82	319.60
60	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR	Railways	02/1997	295.00	412.91	717.04
61	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	65.94	302.23	357.12
62	Rajkot-Veraval,Wansjalia to Jatalsar with new MM for Shapur-Saradiya And Somnath-Kodinar (GC)	Railways	04/1994	320.66	0.00	460.14

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
63	Armur to kadloor yellareddy	Road Transport And Highways	02/2010	390.56	0.00	772.40
64	DHARAMTUL TO SONAPUR (AS-19)	Road Transport And Highways	12/2003	200.00	0.00	253.90
65	BRAHMPUTRA BRIDGE,NH NO-31	Road Transport And Highways	12/2003	217.61	0.00	297.90
66	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15)	Road Transport And Highways	05/2009	572.30	0.00	857.90
67	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	Road Transport And Highways	12/2003	160.00	0.00	207.70
68	NALBARI TO BIJNI (AS-6)	Road Transport And Highways	12/2003	225.00	0.00	266.10
69	SONAPUR TO GUWAHTI (AS-3)	Road Transport And Highways	12/2003	245.00	0.00	491.20
70	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	Road Transport And Highways	12/2003	157.47	0.00	240.40
71	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C	Road Transport And Highways	12/2003	230.00	0.00	239.90
72	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	Road Transport And Highways	12/2003	280.00	0.00	324.60
73	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	Road Transport And Highways	12/2003	195.00	0.00	252.60
74	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	Road Transport And Highways	12/2003	237.80	0.00	289.00

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
75	NALBARI TO BIJNI (AS-8)	Road Transport And Highways	12/2003	200.00	0.00	288.30
76	GUWHATI TO NALBARI (AS-4)	Road Transport And Highways	12/2003	175.96	0.00	217.60
77	NAGAON TO DHARAMTUL (AS-2)	Road Transport And Highways	12/2003	264.72	0.00	301.10
78	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80	Road Transport And Highways	12/2003	166.27	0.00	198.60
79	DELHI/ HARYANA BORDER TO ROHTAK	Road Transport And Highways	04/2007	486.00	0.00	660.30
80	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km)	Road Transport And Highways	05/2009	1108.00	0.00	3466.00
81	PANIPAT-ROHTAK	Road Transport And Highways	04/2011	807.00	0.00	1318.00
82	ROHTAK-BAWAL	Road Transport And Highways	05/2011	650.00	0.00	1119.00
83	Gujarat/Maharashtra BorderSurat-Hazira Port Section	Road Transport And Highways	03/2010	1509.10	0.00	2123.00
84	4 LANNING OF AHMEDABAD TO GODHARA	Road Transport And Highways	12/2010	1008.50	0.00	1352.00
85	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	Road Transport And Highways	03/2011	785.50	0.00	843.90
86	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402	Road Transport And Highways	12/2003	240.00	0.00	295.00

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
87	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	Road Transport And Highways	12/2003	332.94	0.00	475.50
88	2 LANNING OF MOKAMA-MUNGER	Road Transport And Highways	05/2011	351.54	0.00	395.20
89	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	Road Transport And Highways	09/2011	574.00	0.00	655.30
90	4-LANNING OF CHAPRA-HAJIPUR	Road Transport And Highways	01/2011	575.00	0.00	714.40
91	2 LANNING OF MUZAFFARPUR - SONBARSA	Road Transport And Highways	05/2011	511.54	0.00	642.20
92	GUWAHATI TO NALBARI (AS-5)	Road Transport And Highways	12/2003	198.16	0.00	276.20
93	NALBARI T BIJNI (AS-7)	Road Transport And Highways	12/2003	208.00	0.00	308.70
94	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A	Road Transport And Highways	12/2003	284.00	0.00	327.60
95	AMRITSAR-PATHANKOT	Road Transport And Highways	05/2010	705.00	0.00	2144.00
96	GANJAM-ICCHAPURUM,NH-5(NHAI)	Road Transport And Highways	04/2000	263.27	0.00	276.46
97	BHUBANESWAR TO PURI	Road Transport And Highways	03/2011	500.29	0.00	509.40
98	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	Road Transport And Highways	11/2011	909.00	0.00	941.90

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	NAGPUR-KONDHALI,NH-6(NHAI)	Road Transport And Highways	03/2005	168.00	0.00	457.30
100	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	Road Transport And Highways	03/2005	940.00	0.00	1325.00
101	Pune-sholapur,pkg1	Road Transport And Highways	11/2009	1110.00	0.00	1802.00
102	Talegaon-amravati	Road Transport And Highways	11/2009	567.00	0.00	1166.00
103	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	Road Transport And Highways	12/2003	232.45	0.00	305.20
104	Gurgaon-Kotputli Km 42.70 to 54.4 Km	Road Transport And Highways	04/2009	1673.70	0.00	2839.00
105	Surat- Dahisar(Six Lane) Km 263 to Km 502	Road Transport And Highways	02/2009	1693.75	0.00	2721.00
106	4-laning of Faraka-Raiganj	Road Transport And Highways	02/2011	1078.84	0.00	1328.00
107	4-laning of Brahampore-Faraka	Road Transport And Highways	02/2011	998.79	0.00	1266.00
108	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24	Road Transport And Highways	03/2005	220.00	0.00	284.20
109	JHANSI TO LALITPUR, NH-25,26	Road Transport And Highways	12/2003	355.06	0.00	507.40
110	MURADABAD-BAREILY	Road Transport And Highways	04/2010	1267.00	0.00	1876.00

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
111	GHAZIABAD-ALIGARH NH-91	Road Transport And Highways	02/2011	1141.00	0.00	1287.00
112	Hazaribagh-Ranchi	Road Transport And Highways	08/2010	625.07	0.00	948.00
113	4-laning of Barhi-Hazaribagh	Road Transport And Highways	02/2012	398.00	0.00	441.10
114	AURANG-RAIPUR, NH-6, KM.232 TO KM.281	Road Transport And Highways	03/2005	190.00	0.00	264.60
115	THANJAUR-TRICHY,NH-67(NHAI)	Road Transport And Highways	03/2005	280.00	0.00	581.50
116	TRICHY - KORUR NH-67	Road Transport And Highways	03/2005	516.00	0.00	860.70
117	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68	Road Transport And Highways	03/2005	941.00	0.00	1901.00
118	Chennai-Tada(Six lane)	Road Transport And Highways	04/2009	353.37	0.00	446.20
119	KOTA BYPASS,RJ-4, NH-76 (NHAI)	Road Transport And Highways	12/2003	275.00	0.00	280.40
120	Kishangarh-Ajmer-Beawer	Road Transport And Highways	11/2009	795.00	0.00	1127.00
121	Jaipur-Tonk-Deoli	Road Transport And Highways	06/2010	792.06	0.00	1975.00
122	JAIPUR-REENGUS	Road Transport And Highways	08/2010	267.81	0.00	651.60

SN	PROJECT	SECTOR	DOA	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
123	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI)	Road Transport And Highways	12/2003	251.03	0.00	338.40
124	INDORE-DEWAS(NH-3)	Road Transport And Highways	11/2010	325.00	0.00	532.70
125	NH CONNECTIVITY TO ICTT VALLARPADA EU NH SH	Road Transport And Highways	03/2005	557.00	0.00	1129.00
126	Hungund-Surathkal and Mangalore-Knt/Kerala Border	Road Transport And Highways	09/2010	946.00	0.00	1790.00
127	KUNDUPUR-SURATHKAL & MANGLORE	Road Transport And Highways	09/2010	671.00	0.00	938.40
128	DEVIHALLI-HASSAN	Road Transport And Highways	12/2010	453.00	0.00	718.70
129	BELGAUM-DHARWAD(NH-4)	Road Transport And Highways	12/2010	480.00	0.00	567.90
130	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	Shipping And Ports	03/2007	245.67	298.17	371.18
131	Acquisition of Two nos. of 3060 DWT	Shipping And Ports	04/2009	277.03	280.00	294.87
132	EXPANSION OF IISCO STEEL PLANT	Steel	02/2008	14443.00	0.00	15038.24

List of Projects Ahead of Schedule w.r.t. Original Schedule

						(Sep,2013)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Power</u>						
1	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	76.61	06/2016 -	04/2015
	Total		1,508.74 -	1,508.74	76.61		
	<u>Petroleum</u>						
2	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149	8/2011	586.00	586.00	74.77	08/2015 -	07/2015
	Total		586.00 -	586.00	74.77		
	<u>Power</u>						
3	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129	2/2012	3,201.44 -	3,201.44	981.51	10/2014 -	09/2014
4	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	271.58	12/2014 -	11/2014
	Total		5,136.79 -	5,136.79	1,253.09		
	<u>Shipping And Ports</u>						
5	Acquistion of three(3) nos of 6500TEU Cellular container - [N25000052	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013
	Total		1,028.10 -	1,012.23	554.60		
	Grand Total		8,259.63	8,243.76	1,959.07		

List of projects without Original Date of Commissioning

(Sep,2013)									
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Antici pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>Petroleum</u>								
1	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	10,281.00	0.04	- -	04/2015	-	0/0
	Total		10,281.00 -	10,281.00	.04				0/0
	<u>Railways</u>								
2	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
3	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	406.40	358.30	- -	12/2013	-	0/0
4	PANVEL PEN DOUBLING - [N22000255]CR,Multi State	04/2006	191.00 -	191.00	196.89	- -	01/2014	-	0/0
5	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	925.30	627.20	- -	02/2014	-	0/0
6	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	410.08	233.81	- -	03/2014	-	0/0
7	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,Multi State	04/1999	323.40 323.40	744.71	511.57	- -	03/2014	-	0/1
8	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	1,995.25	265.42	- -	03/2014	-	0/0
9	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	3,019.17	2,201.79	- -	03/2014	-	0/0
10	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	230.03	149.24	- -	03/2014	-	0/0
11	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	247.75	148.41	- -	03/2014	-	0/0
12	PEN ROHA DOUBLING - [N22000254]CR,Multi State	04/2007	203.00 -	203.00	156.83	- -	03/2014	-	0/0
13	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	264.06	113.62	- -	04/2014	-	0/0
14	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	703.17	250.34	- -	03/2015	-	0/0
15	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	385.20	143.25	- -	03/2015	-	0/0
16	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	359.86	1.22	- -	03/2015	-	0/0
17	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77 -	209.77	22.93	- -	03/2015	-	0/0
18	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55 -	283.55	0.40	- -	03/2015	-	0/0
19	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12 -	312.12	30.77	- -	03/2015	-	0/0

(Sep,2013)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Antici pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
20	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20 -	258.20	0.14	- -	03/2016	-	0/0
21	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	714.10	2.42	- 12/2017	12/2017	0(R3)	0/0
	Total		5,786.86 -	12,448.65	5,609.46				0/1
	<u>Road Transport And Highways</u>								
22	Hungund-Surathkal and Mangalore-Knt/Kerala Border - [N24000138]NHAI,Karnataka	09/2010	946.00 -	946.00	1,790.00	- -	10/2013	-	3/3
23	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,Karnataka	12/2010	480.00 -	480.00	567.90	- -	10/2013	-	2/2
24	DEVIHALLI-HASSAN - [N24000152]NHAI,Karnataka	12/2010	453.00 -	453.00	718.70	- -	12/2013	-	1/1
25	CHITRADURGA-TUMKUR(NH-4) - [N24000157]NHAI,Karnataka	03/2011	839.00 -	839.00	667.90	- -	12/2013	-	0/1
26	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,Karnataka	09/2010	671.00 -	671.00	938.40	- -	06/2014	-	2/3
	Total		3,389.00 -	3,389.00	4,682.90				8/10
	Grand Total		19,456.86	26,118.65	10,292.40				8/11

List of projects without Date of Commissioning

					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Civil Aviation</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>Coal</u>				
4	KUSMUNDA EXPN.OCP(SECL)(10-15)MTY - [N06000008]SECL,Chhatisgarh	06/2008	1,188.31 -	03/2013 -	-
5	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,Andhra Pradesh	10/2006	249.03 -	03/2012 -	-
6	JALLARAM SHAFT PROJECT - [N06000025]SCCL,Andhra Pradesh	09/2007	467.78 -	03/2013 -	-
7	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,Andhra Pradesh	12/2009	418.97 -	03/2012 -	-
	Total		2,324.09 -		
	<u>Steel</u>				
8	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]RINL,Andhra Pradesh	07/2007	260.00 349.64	08/2010 08/2010	06/2013
	Total		260.00 -		
	<u>Petroleum</u>				
9	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066]HPCL,Tamil Nadu	01/2008	224.00 394.00	- -	03/2013
10	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013
11	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE- - [N16000070]GAIL,Multi State	07/2009	238.68 -	01/2012 -	07/2013
12	RESITEMENT OF MARKETING INSTALATION AT VISAKHAPATT - [N16000057]HPCL,Andhra Pradesh	01/2009	756.00 898.00	- -	08/2013
13	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,Andhra Pradesh	03/2009	3,597.00 2,730.00	09/2011 03/2012	08/2013
14	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,Multi State	08/2009	1,793.00 -	09/2012 -	-
15	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
16	BNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL, Multi State	12/2009	540.92 -	07/2012 07/2012	-
17	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJEC - [N16000129]GAIL, Multi State	06/2009	2,915.00 -	12/2012 -	-
18	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL, Tamil Nadu	05/2013	711.00 -	- -	-
	Total		12,512.49 -		
	<u>Power</u>				
19	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL, Tamil Nadu	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
20	MOUDA STTP (NTPC) - [N18000048]NTPC, Maharashtra	11/2008	5,459.28 -	08/2012 -	03/2013
21	VINDHYACHAL STTP STAGE-IV (NTPC) - [N18000072]NTPC, Madhya Pradesh	01/2009	5,915.00 -	10/2012 -	03/2013
22	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]PGCIL, Himachal Pradesh	07/2006	557.24 775.25	01/2010 -	07/2013
23	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL, Maharashtra	12/2007	477.69 -	09/2010 -	-
24	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL, Karnataka	03/2005	596.45 1,007.16	12/2007 12/2009	-
	Total		14,784.95 -		
	<u>Railways</u>				
25	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER, Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005
26	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD), NR - [220100258]NR, Multi State	03/2002	409.00 625.30	06/2007 -	06/2007
27	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR, Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008
28	GULBARGA-BIDAR, SCR(NL) - [220100254]SCR, Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009
29	KODERMA GIRIDH (NL), ECR - [220100306]ECR, Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010
30	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP, West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010
31	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER, West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010
32	AMRAVATI-NARKHER NL(CR) - [220100118]CR, Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011
33	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR, Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011
34	BARDHAMAN-KATWA (GC) - [N22000091]ER, West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011
35	CALICUT-MANGALORE (DL) (SR) - [220100151]SR, Multi State	02/1996	240.00 -	- -	02/2012
36	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
37	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012
38	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012
39	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012
40	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	03/2012
41	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012
42	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012
43	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012
44	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012
45	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012
46	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012
47	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013
48	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013
49	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013
50	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013
51	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013
52	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013
53	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013
54	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,Multi State	03/1998	280.00 842.35	- -	03/2013
55	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013
56	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013
57	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013
58	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013
59	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013
60	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-
61	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
62	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	- -	-
63	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-
64	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-
65	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-
66	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-
67	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-
68	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-
69	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-
70	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-
71	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-
72	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-
73	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-
74	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-
75	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	- -	-
76	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	- -	-
77	Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State	04/2007	1,640.04 -	- -	-
78	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	- -	-
79	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	- -	-
80	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	- -	-
81	Rajkot-Veraval,Wansjalai to Jatalsar with new MM f - [N22000143]WR,Gujarat	04/1994	320.66 -	- -	-
82	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	- -	-
83	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	- -	-
84	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	- -	-
85	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.39 -	- -	-
86	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
87	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	- -	-
88	Mavli Jn.-Bari Sadri, MM of Ajmer- Chitturgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	- -	-
89	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And - [N22000153]NWR,Rajasthan	04/2010	739.65 -	- -	-
90	Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	- -	-
91	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	- -	-
92	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	- -	-
93	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	- -	-
94	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	- -	-
95	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	- -	-
96	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	- -	-
97	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	06/2013 -	-
98	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	- -	-
99	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	- -	-
100	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	- -	-
101	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	- -	-
102	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	- -	-
103	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	- -	-
104	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	- -	-
105	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	- -	-
106	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	- -	-
107	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	- -	-
108	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	- -	-
109	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	- -	-
110	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	- -	-
111	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
112	Sakri-Nirmali and Jhanjharpur-Laukahabazar and Sah - [N22000180]ECR,Bihar	04/2004	372.14 -	- -	-
113	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar	04/2009	470.00 -	- -	-
114	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	- -	-
115	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	- -	-
116	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	- -	-
117	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	- -	-
118	Sriperumbudur-Guduvanchery with spur to Irungattukottai-Ava - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	- -	-
119	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	- -	-
120	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	- -	-
121	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	- -	-
122	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	- -	-
123	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	- -	-
124	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	- -	-
125	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	- -	-
126	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	- -	-
127	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	- -	-
128	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	- -	-
129	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	- -	-
130	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	- -	-
131	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	- -	-
132	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	- -	-
133	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	- -	-
134	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	- -	-
135	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	- -	-
136	New Jalpaiguri-Siliguri-New Bongaigaon including B - [N22000209]NEFR,Multi State	04/1999	523.17 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
137	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR, Assam	04/2012	246.07 -	- -	-
138	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP, West Bengal	04/2009	573.78 -	- -	-
139	Hyderabad/Secunderabad Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP, Andhra Pradesh	04/2012	632.68 -	04/2012 -	-
140	Madurai-Tuticorin via Aruppukottai - [N22000215]SR, Multi State	04/2011	601.43 -	- -	-
141	Lakshmikantapur-Namkhana subsequently MM for Namkh - [N22000216]ER, Multi State	04/1999	406.99 -	- -	-
142	Sultanganj-Katuria via Asarganj, Tarapur And Belha - [N22000217]ER, Multi State	04/2007	450.00 -	- -	-
143	Hansnabad-Hingalgarh New BG line - [N22000218]ER, Multi State	04/2010	172.03 -	- -	-
144	Pirpainti-Jasidih - [N22000219]ER, Multi State	04/2013	915.98 -	- -	-
145	Bandel-Boinchi 3rd line - [N22000221]ER, Multi State	04/2011	288.35 -	- -	-
146	Pirpainti-Bhagalpur - [N22000222]ER, Multi State	04/2011	261.38 -	- -	-
147	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER, Multi State	04/2000	157.17 -	- -	-
148	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER, Multi State	04/2001	923.52 -	- -	-
149	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER, Multi State	04/2005	595.91 -	- -	-
150	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER, Multi State	04/2010	174.56 -	- -	-
151	Sondalia-Champapukur doubling with new MM for Bira-Chakia NL - [N22000228]ER, Multi State	04/2010	277.28 -	- -	-
152	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER, Multi State	04/2010	296.44 -	- -	-
153	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER, Multi State	04/2010	157.94 -	- -	-
154	Wardha-Nanded Maharashtra - [N22000231]CR, Maharashtra	04/2008	697.00 -	- -	-
155	Kalyan-Kasara 3rd line - [N22000233]CR, Maharashtra	04/2011	277.70 -	- -	-
156	Bariarpur-Mananpur via Kharagpur, Lachimpur-Barahat - [N22000234]ER, Multi State	04/2007	450.55 -	- -	-
157	Tarakeshwar-Magra New BG line - [N22000235]ER, Multi State	04/2010	365.17 -	- -	-
158	Hansdih-Godda NL - [N22000236]ER, Multi State	04/2011	267.09 -	- -	-
159	Sainthia-Tarapith 3rd line - [N22000237]ER, Multi State	04/2011	193.44 -	- -	-
160	Boinchi-Shaktigarh 3rd line - [N22000238]ER, Multi State	04/2011	175.80 -	- -	-
161	New Alipur to Akra, MM for Budge Budge-Pujali NL, - [N22000240]ER, Multi State	04/2010	494.54 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
162	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State	04/2000	297.47 -	- -	-
163	Chandpara-Bangaon doubling with extension to Chandb - [N22000242]ER,Multi State	04/2003	337.96 -	- -	-
164	Magrahat-Diamond Harbour with MM Sangrampur-Krishna - [N22000243]ER,Multi State	04/2009	493.96 -	- -	-
165	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	- -	-
166	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	- -	-
167	Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	- -	-
168	Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State	04/2011	166.89 -	- -	-
169	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	- -	-
170	Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka	04/2011	913.00 -	- -	-
171	Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka	04/2007	179.65 -	- -	-
172	Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka	04/2010	377.93 -	- -	-
173	Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh	04/2013	1,112.00 -	- -	-
174	Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh	04/2013	723.00 -	- -	-
175	Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State	04/2012	1,054.35 -	- -	-
176	Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State	04/2008	184.26 -	- -	-
177	Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh	04/2012	923.23 -	- -	-
178	Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh	04/2011	283.54 -	- -	-
179	Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh	04/2012	289.79 -	- -	-
180	ansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur M - [N22000268]NR,Punjab	04/2009	396.04 -	- -	-
181	Grade Separator at Dayabasti - [N22000269]NR,Delhi	04/1999	159.20 -	- -	-
182	Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareli - [N22000270]NR,Uttar Pradesh	04/2013	654.00 -	- -	-
183	Rohtak-Meham Hansi - [N22000272]NR,Haryana	04/2012	287.00 -	- -	-
184	Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh	04/2008	1,046.88 -	- -	-
185	Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State	04/2007	336.91 -	- -	-
186	Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka	04/2013	558.00 -	- -	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
187	Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State	04/2013	296.00 -	- -	-
188	Shimoga-Harihar NL - [N22000278]SWR,Karnataka	04/2011	562.74 -	- -	-
189	Rayadurga-Tumkur NL - [N22000279]SWR,Multi State	04/2007	970.34 -	- -	-
190	White Field-Kolar NL - [N22000280]SWR,Karnataka	04/2011	341.05 -	- -	-
191	Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi	04/2012	295.68 -	- -	-
192	Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh	04/2013	829.00 -	- -	-
193	Mudkhed-Parbhani - [N22000283](SCR),Maharashtra	04/2011	390.60 -	- -	-
194	Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh	04/2012	153.00 -	- -	-
195	Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh	04/2011	1,313.48 -	- -	-
196	Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh	04/2010	337.49 -	- -	-
197	Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State	04/2008	2,050.00 -	- -	-
198	Haridwar-Laksar - [N22000289]NR,Uttarakhand	04/2012	219.83 -	- -	-
199	Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State	04/2010	338.54 -	- -	-
200	Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State	04/2008	165.65 -	- -	-
201	Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana	04/2013	400.00 -	- -	-
202	Yamunanagar-Chandigarh via Sadhaura Narayangarh - [N22000293]NR,Multi State	04/2013	876.00 -	- -	-
203	Unchahar-Amethi - [N22000294]NR,Uttar Pradesh	04/2012	380.00 -	- -	-
204	Qadian-Beas - [N22000295]NR,Punjab	04/2011	205.22 -	- -	-
205	Chandigarh-Baddi NL - [N22000296]NR,Multi State	04/2007	328.14 -	- -	-
206	Hospet-Hubli-Londa-Vascodegama DL - [N22000297]SWR,Karnataka	04/2010	2,127.00 -	- -	-
207	Gadag-Wadi NL - [N22000299]SWR,Karnataka	04/2013	1,117.00 -	- -	-
208	Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka	04/2013	327.25 -	- -	-
209	Monigram- Nimtita - [N22000301]ER,Multi State	04/2012	250.93 -	- -	-
210	Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal	04/2012	255.64 -	- -	-
211	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-
213	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-
214	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-
215	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-
216	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-
217	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-
218	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-
219	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-
220	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-
221	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-
222	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-
223	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-
224	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-
225	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-
226	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-
227	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-
228	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-
229	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-
230	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-
231	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-
232	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-
233	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-
234	Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State	04/2013	1,239.00 -	- -	-
	Total		95,164.79 -		
	Road Transport And Highways				

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
235	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008
236	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013
237	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,Karnataka	11/2010	680.00 -	- -	04/2013
238	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013
	Total		1,461.83 -		
	<u>Shipping And Ports</u>				
239	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,Odisha	12/2005	154.84 253.36	- 01/2009	12/2010
240	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011
241	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 11/2011	11/2011
242	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012
243	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012
244	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012
245	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012
246	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013
247	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013
248	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013
249	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013
250	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-
251	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	-
	Total		11,119.97 -		
	<u>Telecommunications</u>				
252	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012
253	GSM equipment of 799000Lines (2G) 101000 lines 3(G) - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013
254	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013
255	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
256	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-
257	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-
258	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 02/2013	-
	Total		2,533.01 -		
	<u>Urban Development</u>				
259	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,Karnataka	05/2006	6,395.00 -	06/2011 -	03/2013
260	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>Water Resources</u>				
261	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		151,589.72		

List of on schedule Projects w.r.t. Original Schedule

(Sep,2013)							
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070	2/2011	452.00 -	452.00	145.42	03/2015 -	03/2015
2	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	145.44		
	<u>Coal</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	161.60	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	45.02	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	72.34	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	51.42	03/2015 -	03/2015
8	Rajrappa RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016
9	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.14 -	430.14	58.90	03/2016 -	03/2016
11	KALYANIKHANI OPENCAST PROJECT - [N06000101	7/2012	417.33 -	417.33	0.09	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	52.65	03/2016 -	03/2016
14	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	Muraidih UG - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094	7/2011	447.06 -	447.06	14.03	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
19	AMRAPALI OC - [N06000103	2/2012	858.11 -	858.11	49.40	03/2020 -	03/2020
20	KARMA OCP (1.0MTY) - [N06000088	6/2009	162.46 -	162.46	40.81	03/2014 -	03/2014

(Sep,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	89.92	03/2016 -	03/2016
22	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
23	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.33	03/2016 -	03/2016
24	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	151.06	03/2017 -	03/2017
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	579.32	03/2016 03/2016	03/2016
	Total		11,169.15 -	10,797.81	1,683.93		
	<u>Petroleum</u>						
26	Wax Project - [N16000101	6/2010	576.60 -	576.60	306.39	12/2013 -	12/2013
27	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165	4/2010	270.00 -	270.00	-	12/2014 -	12/2014
28	Reconstruction of BPA and BPB Platforms - [N16000161	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
29	Integrated Development of Bassein Field - [N16000160	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
30	Pipeline Replacement Project, Ahmedabad - [N16000159	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
31	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	48.71	10/2014 -	10/2014
32	Mounded Bullet - [N16000154	12/2012	279.00 -	279.00	4.87	12/2014 -	12/2014
33	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	37.26	07/2015 -	07/2015
34	DBPL-II - [N16000147	6/2009	486.00 -	486.00	61.61	09/2013 -	09/2013
35	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
36	REWARI KANPUR PIPELINE PROJECT - [N16000145	2/2012	1,210.64 -	1,210.64	281.76	11/2015 -	11/2015
37	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	134.21	12/2014 -	12/2014
38	Butene-1 at Panipat - [N16000139	2/2012	190.00 -	190.00	80.85	03/2014 -	03/2014
39	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	515.24	05/2014 -	05/2014
40	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	99.87	12/2014 -	12/2014
41	Construction of three ETPs, Mehsana - [N16000135	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
42	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014
43	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	26.61	05/2014 -	05/2014

(Sep,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112	8/2010	8,140.00 -	8,140.00	5,177.12	02/2014 -	02/2014
45	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	1,278.32	05/2015 -	05/2015
46	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	289.05	03/2015 -	03/2015
	Total		33,182.93 -	32,651.61	8,361.98		
	<u>Power</u>						
47	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101	5/2011	1,961.87 -	1,961.87	1,131.45	05/2014 -	05/2014
48	Common System Associated with Coastal Energen Priv - [N18000103	9/2011	1,940.13 -	1,940.13	1,040.50	09/2014 -	09/2014
49	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	203.81	06/2014 -	06/2014
50	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112	11/2011	2,127.51 -	2,127.51	1,186.02	07/2014 -	07/2014
51	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114	12/2011	552.44 -	552.44	329.39	02/2014 -	02/2014
52	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	1,653.00	11/2016 -	11/2016
53	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	1,194.00	09/2016 -	09/2016
54	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	1,845.00	12/2016 -	12/2016
55	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	282.68	11/2014 -	11/2014
56	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	195.23	11/2014 -	11/2014
57	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	377.02	08/2014 -	08/2014
58	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126	3/2012	206.44 -	206.44	41.42	06/2014 -	06/2014
59	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	872.60	06/2015 -	06/2015
60	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
61	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145	6/2012	1,909.24 -	1,909.24	195.81	06/2015 -	06/2015
62	COMMON SYS. ASSOCIATED PART- B - [N18000144	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
63	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC - [N18000143	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
64	Lata-Tapovan HPP 3x57MW - [N18000142	7/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017
65	LARA STPP STAGE-I - [N18000140	11/2012	11,846.00 -	11,846.00	1,115.00	05/2017 -	05/2017
66	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014

(Sep,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
67	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
68	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	105.74	03/2015 -	03/2015
69	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	503.00	08/2015 -	08/2015
70	Transmission System associated with Mauda Stage-II - [N18000153	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
71	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
72	Gadarwara Super Thermal Power Project Stage-I - [N18000151	2/2013	11,638.55 -	11,638.55	687.00	09/2017 -	09/2017
73	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
74	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122	2/2012	1,927.16 -	1,927.16	444.72	10/2014 -	10/2014
75	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121	2/2012	324.33 -	324.33	19.57	08/2014 -	08/2014
76	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120	2/2012	1,310.85 -	1,310.85	464.56	02/2015 -	02/2015
77	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118	1/2012	259.28 -	259.28	111.93	01/2014 -	01/2014
78	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117	1/2012	1,422.85 -	1,422.85	432.96	01/2015 -	01/2015
79	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116	12/2011	1,746.65 -	1,746.65	174.49	08/2014 -	08/2014
80	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	144.01	08/2014 -	08/2014
81	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113	12/2011	2,422.66 -	2,422.66	520.74	08/2014 -	08/2014
82	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNA - [N18000111	8/2011	1,637.34 -	1,637.34	937.10	08/2014 -	08/2014
83	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107	8/2011	1,391.97 -	1,391.97	1,059.23	12/2013 -	12/2013
	Total		101,898.41 -	101,898.41	17,384.61		
	Railways						
84	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	105.60	02/2015 -	02/2015
85	New Work for Construction of Metro railway from NS - [N22000110	4/2010	3,951.98 -	3,951.98	187.23	03/2016 -	03/2016
86	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112	4/2008	829.74 -	829.74	35.38	03/2015 -	03/2015
87	Suratpura - Hanumangarh - Sriganaganagar Gauge Conversion - [N22000114	4/2008	516.23 -	516.23	420.70	03/2014 -	03/2014
88	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
89	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245	4/2010	423.66 -	423.66	136.58	03/2017 -	03/2017

(Sep,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
90	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244	4/2009	257.42 -	257.42	33.39	03/2014 -	03/2014
91	Princepghat-Majerhat Doubling of Circular Railway - [N22000239	4/2011	299.60 -	299.60	1.09	03/2017 -	03/2017
92	Plassey-Jiaganj Doubling - [N22000220	4/2011	248.07 -	248.07	9.83	03/2015 -	03/2015
93	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164	4/2010	309.44 -	388.67	42.55	12/2015 -	12/2015
94	Dholpur-Sirmuttra with extension to Gangapurcity A - [N22000158	4/2010	622.41 -	2,030.50	1.22	02/2019 -	02/2019
95	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	1.71	02/2020 -	02/2020
96	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	675.23	03/2014 -	03/2014
97	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113	4/2008	653.19 -	653.47	248.21	03/2014 -	03/2014
98	New Work for Construction of Metro railway - [N22000111	4/2010	2,619.02 -	2,619.02	332.96	03/2016 -	03/2016
99	New Work for Construction of Metro railway from Ba - [N22000109	4/2010	2,069.60 -	2,069.60	25.21	03/2014 -	03/2014
	Total		20,423.88 -	25,216.05	2,256.89		
	<u>Road Transport And Highways</u>						
100	New 4 Lane elevated road from chennai airport - [N24000139	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
101	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,318.00	10/2014 -	10/2014
102	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
103	Muzafarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
104	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	518.00	01/2014 -	01/2014
105	BARSAT-KRISHNANAGAR - [N24000229	8/2012	867.00 -	867.00	-	02/2015 -	02/2015
106	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
107	REENGUS SIKAR - [N24000227	3/2012	333.51 -	333.51	236.80	09/2014 -	09/2014
108	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226	10/2011	1,565.00 -	1,565.00	691.40	10/2014 -	10/2014
109	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225	3/2012	828.00 -	828.00	490.60	09/2014 -	09/2014
110	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
111	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	34.28	12/2015 -	12/2015
112	2 LANING WITH PS KANPUR KABRAI - [N24000221	1/2013	373.47 -	373.47	40.66	07/2014 -	07/2014

(Sep,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
113	2 LANING WITH PS AGRA ALIGARH - [N24000220	10/2012	250.50 -	250.50	230.10	10/2014 -	10/2014
114	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	17.23	09/2015 -	09/2015
115	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
116	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	198.50	06/2014 -	06/2014
117	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	227.90	06/2015 -	06/2015
118	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213	4/2012	624.00 -	624.00	314.70	04/2014 -	04/2014
119	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	441.10	02/2014 -	02/2014
120	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	161.20	05/2014 -	05/2014
121	SNG toBANL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
122	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	642.20	11/2013 -	11/2013
123	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
124	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	655.30	03/2014 -	03/2014
125	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183	11/2011	1,535.00 -	1,535.00	1,218.00	05/2014 -	05/2014
126	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	921.30	03/2014 -	03/2014
127	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	189.10	02/2014 -	02/2014
128	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
129	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	282.80	10/2014 -	10/2014
130	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	498.90	07/2014 -	07/2014
131	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	98.48	01/2014 -	01/2014
132	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,048.00	09/2014 -	09/2014
133	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	202.40	06/2014 -	06/2014
134	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,388.00	06/2014 -	06/2014
135	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	941.90	05/2014 -	05/2014
136	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	388.20	01/2014 -	01/2014
137	Tirupati - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013

(Sep,2013)

						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
138	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
139	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,119.00	11/2013 -	11/2013
140	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	1,166.00	11/2013 -	11/2013
	Total		38,794.74 -	38,794.74	16,885.28		
	<u>Shipping And Ports</u>						
141	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
	Total		966.46 -	994.82	363.20		
	<u>Steel</u>						
142	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078	7/2012	332.65 -	332.65	-	08/2014 -	08/2014
143	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	3.54	12/2014 -	12/2014
144	Coke Oven Battery-5 - [N12000080	3/2012	339.35 -	339.35	12.59	06/2015 -	06/2015
	Total		926.90 -	926.90	16.13		
	<u>Urban Development</u>						
145	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	3,853.30	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	3,853.30		
	Grand Total		243,274.07	247,191.94	50,950.76		

List of Delayed Projects w.r.t. Original and Revised Schedule

(Sep,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,485.00	12/2008 -	06/2014	66	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	3,088.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,119.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,373.60				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building(Goa) - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	244.70	05/2012 -	11/2013	18	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	06/2014	3	-
7	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.71	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	989.35	476.41				
	<u>Coal</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,783.98	06/2009 -	01/2014	55	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.30	03/2010 -	03/2014	48	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.85	03/2011 -	03/2014	36	-
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 -	741.62	374.23	03/2013 -	03/2014	12	-
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,689.91	03/2012 -	03/2014	24	-
13	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	115.88	03/2012 -	03/2014	24	-
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	802.36	03/2013 09/2012	10/2014	19	25
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,Madhya pradesh	10/2007	259.40 -	259.40	6.98	03/2012 -	03/2015	36	-
16	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.85	03/2013 -	03/2015	24	-
17	BALRAM OCP EXTENSION,MCL 8.00 Mty - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.85	03/2010 -	03/2015	60	-
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	116.91	03/2013 -	03/2015	24	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.67	03/2012 -	03/2015	36	-
20	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.33	03/2013 -	03/2015	24	-
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,422.40	03/2014 -	03/2016	24	-
22	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,271.75	03/2014 -	03/2016	24	-
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	27.60	07/2012 -	03/2016	44	-
24	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	267.52	03/2014 -	03/2016	24	-
25	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	91.60	12/2012 -	03/2016	39	-
26	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	19.29	03/2014 -	03/2016	24	-
27	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.23	03/2014 -	03/2016	24	-
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.96	03/2014 -	03/2016	24	-
30	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
31	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	138.21	03/2012 -	03/2016	48	-
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72	-
33	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
34	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	61.20	03/2012 -	03/2017	60	-
35	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	34.04	12/2015 -	02/2018	26	-
	Total		24,633.81 -	28,090.60	13,060.76				
	Steel								
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,554.63	10/2009 10/2012	10/2013	48	12
37	67.5 MW TG-5 AUX. STEAM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 343.58	343.58	280.63	02/2011 02/2011	10/2013	32	32
38	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	354.04	12/2011 03/2012	12/2013	24	21
39	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 216.68	216.68	152.61	10/2012 10/2012	12/2013	14	14
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	15,038.24	12/2011 -	12/2013	24	-
41	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	283.63	05/2012 05/2012	12/2013	19	19

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,779.97	12/2011 -	12/2013	24	-
43	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,933.09	03/2013 -	12/2013	9	-
44	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,Karnataka	04/2011	572.00 -	572.00	327.46	04/2013 12/2013	12/2013	8	0
45	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,Karnataka	02/2011	898.55 -	898.55	222.75	05/2013 03/2014	03/2014	10	0
46	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,841.57	12/2012 -	03/2014	15	-
47	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	95.71	10/2013 -	06/2014	8	-
48	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	10,590.79	03/2013 -	09/2014	18	-
49	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	74.38	11/2013 -	06/2015	19	-
	Total		64,438.32 -	70,505.86	53,529.50				
	<u>Petrochemicals</u>								
50	Assam gas Cracker project - [N16000106]BCPL,Assam	04/2006	5,460.61 8,920.00	8,920.00	4,510.51	04/2012 12/2013	12/2013	20	0
	Total		5,460.61 -	8,920.00	4,510.51				
	<u>Petroleum</u>								
51	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]ONGC,Assam	09/2001	345.10 663.69	750.00	729.07	03/2007 03/2014	09/2013	78	-6
52	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24	16
53	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013	5	-
54	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12	-
55	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,773.71	01/2012 -	10/2013	21	-
56	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.26	11/2012 -	10/2013	11	-
57	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	773.81	12/2011 -	11/2013	23	-
58	IOR GELEKI (ONGCL) - [160100216]ONGC,Assam	09/2001	390.09 1,674.11	1,674.11	1,727.24	03/2007 03/2017	12/2013	81	-39
59	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93	9
60	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	730.97	03/2010 03/2012	12/2013	45	21
61	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	263.46	03/2012 -	12/2013	21	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	673.33	01/2013 -	12/2013	11	-
63	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	745.49	07/2012 -	12/2013	17	-
64	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.72	09/2012 -	12/2013	15	-
65	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	234.31	03/2013 -	12/2013	9	-
66	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	238.10	04/2012 06/2013	12/2013	20	6
67	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20	-
68	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	722.53	10/2011 -	12/2013	26	-
69	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26	-
70	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	133.48	06/2012 -	12/2013	18	-
71	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	904.74	10/2011 -	01/2014	27	-
72	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
73	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
74	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
75	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
76	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	03/2014	18	-
77	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 -	03/2014	12	-
78	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	199.40	08/2012 -	03/2014	19	-
79	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	28.10	06/2012 -	03/2014	21	-
80	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	91.79	08/2013 -	03/2014	7	-
81	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	59.74	06/2012 -	03/2014	21	-
82	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,116.27	08/2010 03/2012	05/2014	45	26
83	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	23,278.00	11/2012 -	05/2014	18	-
84	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
85	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	289.87	05/2013 -	05/2014	12	-
86	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	14.71	03/2014 -	05/2014	2	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
87	Development of Cluster-7 Fields - [N16000104]ONGC,Multi State	03/2010	3,241.03 6,638.94	6,638.94	1,451.42	03/2013 11/2014	11/2014	20	0
88	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
89	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	445.86	09/2011 -	12/2014	39	-
90	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
91	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3	-
92	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
93	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35	-
94	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	957.44	01/2014 -	12/2015	23	-
95	Integrated Refinery Expansion Project - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	508.63	12/2015 -	05/2016	5	-
96	Construction of one Multipurpose Support Vessel (MSV) - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
97	Creation of Secondary Tank farm with dehydration facility and ETP at Madhuban - [N16000167]OIL,Multi State	08/2006	374.56 -	374.56	10.46	09/2012 -	10/2016	49	-
98	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24	-
99	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24	-
100	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	03/2017	23	-
	Total		127,204.86 -	143,219.59	81,524.13				
	<u>Power</u>								
101	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	2,053.70	11/2009 02/2013	10/2013	47	8
102	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	877.64	08/2010 01/2013	10/2013	38	9
103	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	159.08	11/2011 -	10/2013	23	-
104	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,512.00	10/2012 -	10/2013	12	-
105	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	154.44	06/2012 -	11/2013	17	-
106	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	134.45	01/2013 -	11/2013	10	-
107	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	385.26	11/2011 -	12/2013	25	-
108	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.62	02/2012 -	12/2013	22	-
109	765KV System for Central part of Northern Region Grid - Part-III - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	847.35	05/2012 -	12/2013	19	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
110	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	138.63	07/2013 -	12/2013	5	-
111	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	331.70	10/2013 -	12/2013	2	-
112	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,184.87	10/2010 01/2013	03/2014	41	14
113	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	885.68	10/2009 -	03/2014	53	-
114	RAMPUR HEP(412 MW) - [N18000024]SJVNL,Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,763.64	01/2012 -	03/2014	26	-
115	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,Multi State	08/2008	2,360.95 2,580.90	2,580.90	2,066.28	08/2012 -	03/2014	19	-
116	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,979.25	08/2012 -	03/2014	19	-
117	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	607.55	11/2012 -	03/2014	16	-
118	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,289.56	08/2013 -	03/2014	7	-
119	Northern region system strengthening scheme XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	327.34	07/2013 -	03/2014	8	-
120	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	785.24	12/2013 -	03/2014	3	-
121	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	645.71	07/2013 -	05/2014	10	-
122	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,248.80	03/2013 -	05/2014	14	-
123	Transmission system for phase-I generation projects in orissa-part B - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,720.10	12/2013 -	05/2014	5	-
124	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,906.96	03/2014 -	05/2014	2	-
125	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,539.61	10/2012 -	06/2014	20	-
126	Trans. System associated with PALLATANA GBPP & BPTS. - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,427.35	12/2012 -	06/2014	18	-
127	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	910.02	08/2012 -	06/2014	22	-
128	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	363.51	11/2011 -	07/2014	32	-
129	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,134.00	04/2009 -	09/2014	65	-
130	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 1,117.92	1,117.92	660.88	08/2013 08/2013	09/2014	13	13
131	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,354.00	08/2013 -	09/2014	13	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
132	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	182.18	11/2013 -	09/2014	10	-
133	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,387.84	09/2009 06/2013	11/2014	62	17
134	Supplementary transmission associated with vellur TPS - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	95.16	04/2013 -	12/2014	20	-
135	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	470.13	07/2006 -	02/2015	103	-
136	Transmission System of Vindhuchal -IV And Rihand -III Gen. Proj. - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,719.39	11/2012 -	03/2015	28	-
137	Northern region system strengthening scheme-XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	891.31	04/2013 -	03/2015	23	-
138	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	63.45	01/2013 -	03/2015	26	-
139	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	1,042.98	11/2013 -	03/2015	16	-
140	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	725.71	11/2012 -	03/2015	28	-
141	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	48.69	04/2015 -	05/2015	1	-
142	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,689.59	08/2013 -	06/2015	22	-
143	Transm System for development of Pooling stn. in NR part of West Bengal And Transfer of power from B - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	392.18	01/2015 -	12/2015	11	-
144	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	4,050.00	07/2011 -	06/2016	59	-
145	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,677.22	01/2016 01/2016	11/2016	10	10
146	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	518.78	07/2010 02/2016	02/2017	79	12
147	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,473.56	12/2009 05/2013	03/2017	87	46
148	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,704.00	12/2009 -	03/2017	87	-
149	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	3,846.30	1,899.00	03/2013 -	07/2017	52	-
150	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	364.22	07/2014 -	09/2017	38	-
151	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,362.61	09/2010 08/2014	03/2018	90	43
152	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	4,058.55	09/2009 07/2014	07/2018	106	48
	Total		123,653.83 -	141,352.78	96,477.77				
	<u>Railways</u>								
153	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	580.90	03/1994 -	10/2013	235	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
154	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	229.64	03/2002 -	10/2013	139	-
155	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	406.74	12/2009 03/2011	10/2013	46	31
156	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	611.03	130.62	12/2011 11/2013	11/2013	23	0
157	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER) - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	179.63	12/2012 -	12/2013	12	-
158	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	287.99	421.25	01/1999 -	12/2013	179	-
159	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
160	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	505.38	03/2013 -	03/2014	12	-
161	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	285.59	02/2009 02/2009	08/2014	66	66
162	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	257.89	03/2009 03/2009	08/2014	65	65
163	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	241.09	12/2008 -	09/2014	69	-
164	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	319.75	03/2004 12/2010	12/2014	129	48
165	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.35	347.27	06/2004 -	12/2014	126	-
166	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,174.03	03/2009 12/2012	12/2014	69	24
167	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	252.46	06/2013 06/2013	12/2014	18	18
168	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,677.32	03/2009 -	12/2014	69	-
169	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
170	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	178.39	03/2007 03/2007	03/2015	96	96
171	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.39	12/2010 12/2010	03/2015	51	51
172	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,480.03	12/2008 -	03/2015	75	-
173	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	126.12	12/2012 -	03/2015	27	-
174	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,151.00	944.37	03/2007 -	03/2015	96	-
175	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.19	2,854.15	04/2008 03/2014	12/2015	92	21
176	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,880.08	10/2007 12/2012	12/2015	98	36
177	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	-
178	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	489.13	03/2014 -	12/2015	21	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
179	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	41.85	03/2015 -	12/2015	9	-
180	TAMLUK DIGHA, LINE DOUBLING (SER) - [N22000097]SER, West Bengal	03/1984	293.97 1,025.39	1,074.47	448.95	06/2005 07/2011	06/2016	132	59
181	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbander (MTP) - [N22000108]RVNL, West Bengal	04/2010	2,397.72 -	2,397.72	52.60	03/2016 -	06/2016	3	-
182	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, West Bengal	03/1998	111.90 1,039.29	1,423.98	482.85	03/2005 12/2008	12/2016	141	96
183	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,301.02	03/2014 03/2016	12/2016	33	9
184	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR, Manipur	04/2003	727.56 727.53	4,453.50	1,655.40	03/2011 03/2014	03/2017	72	36
185	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR, Uttar Pradesh	04/2006	325.00 325.00	1,116.53	231.10	03/2010 03/2017	03/2017	84	0
186	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR, Mizoram	04/2008	619.34 -	2,384.34	96.43	04/2014 -	03/2017	35	-
187	SEVOK RANGPO, NEFR - [N22000102]NEFR, Sikkim	04/2008	1,339.48 -	3,380.58	59.60	12/2015 -	03/2017	15	-
188	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]NEFR, Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24	-
189	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
	Total		26,070.75 -	75,820.69	31,648.19				
	<u>Road Transport And Highways</u>								
190	GANJAM-ICCHAPURUM, NH-5(NHAI) - [N24000057]NHAI, Odisha	04/2000	263.27 -	263.27	276.46	02/2004 -	09/2013	115	-
191	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI, Karnataka	04/2000	241.00 -	196.65	204.82	08/2004 07/2010	10/2013	110	39
192	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI, Karnataka	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	110	-
193	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI, Karnataka	04/2000	196.50 363.00	196.50	288.40	06/2011 06/2011	10/2013	28	28
194	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, Haryana	04/2007	486.00 -	486.00	660.30	05/2010 -	10/2013	41	-
195	Pune-sholapur, pkg1 - [N24000127]NHAI, Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
196	Hazaribagh-Ranchi - [N24000141]NHAI, Jharkhand	08/2010	625.07 -	625.07	948.00	01/2013 -	10/2013	9	-
197	PATNA-MUZZAFFARPUR - [N24000165]NHAI, Bihar	08/2010	671.30 -	671.30	625.90	02/2013 -	10/2013	8	-
198	BHOPAL-SANCHI - [N24000192]NHAI, Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9	-
199	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI, Odisha	04/2000	225.00 -	241.53	162.71	04/2004 -	11/2013	115	-
200	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI, Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
201	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI, Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	117	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
202	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	327.60	05/2008 -	12/2013	67	-
203	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	295.00	10/2008 -	12/2013	62	-
204	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.60	01/2009 -	12/2013	59	-
205	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	475.50	09/2008 -	12/2013	63	-
206	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	280.40	10/2008 -	12/2013	62	-
207	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	288.30	06/2008 -	12/2013	66	-
208	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	266.10	06/2008 -	12/2013	66	-
209	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	207.70	05/2008 -	12/2013	67	-
210	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42	-
211	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.40	09/2009 -	12/2013	51	-
212	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2013	35	-
213	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,325.00	07/2012 -	12/2013	17	-
214	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
215	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,123.00	09/2012 -	12/2013	15	-
216	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	12/2013	19	-
217	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26	-
218	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,721.00	08/2011 -	12/2013	28	-
219	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	12/2013	25	-
220	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
221	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	839.20	03/2013 -	12/2013	9	-
222	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2013	7	-
223	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,144.00	11/2012 -	12/2013	13	-
224	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	582.90	07/2013 -	12/2013	5	-
225	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,352.00	06/2013 -	12/2013	6	-
226	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	843.90	08/2013 -	12/2013	4	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
227	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
228	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	119.10	05/2013 -	12/2013	7	-
229	SAMAIKHIALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	725.40	03/2013 -	12/2013	9	-
230	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.40	07/2013 -	12/2013	5	-
231	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	509.40	08/2013 -	12/2013	4	-
232	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	651.60	02/2013 -	12/2013	10	-
233	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,975.00	12/2012 -	02/2014	14	-
234	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	532.70	05/2013 -	02/2014	9	-
235	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	240.40	09/2007 -	03/2014	78	-
236	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	144.30	09/2008 -	03/2014	66	-
237	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	239.90	06/2005 -	03/2014	105	-
238	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	252.60	06/2008 -	03/2014	69	-
239	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	289.00	06/2008 -	03/2014	69	-
240	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	338.40	10/2008 -	03/2014	65	-
241	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	217.60	04/2008 -	03/2014	71	-
242	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	301.10	06/2008 -	03/2014	69	-
243	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	03/2014	72	-
244	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	276.20	04/2008 -	03/2014	71	-
245	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	253.90	06/2008 -	03/2014	69	-
246	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63	-
247	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	240.70	09/2007 -	03/2014	78	-
248	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	860.70	07/2010 -	03/2014	44	-
249	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	446.20	10/2011 -	03/2014	29	-
250	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	54.59	11/2012 -	03/2014	16	-
251	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,876.00	06/2013 -	03/2014	9	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
252	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	395.20	05/2013 -	03/2014	10	-
253	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	515.80	03/2013 -	03/2014	12	-
254	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	281.10	10/2013 -	03/2014	5	-
255	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	70.00	09/2007 -	04/2014	79	-
256	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,201.00	03/2013 -	04/2014	13	-
257	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	564.60	02/2014 -	04/2014	2	-
258	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	324.60	02/2009 03/2014	05/2014	63	2
259	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	308.70	04/2008 -	05/2014	73	-
260	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	158.70	07/2009 -	05/2014	58	-
261	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.80	10/2008 -	06/2014	68	-
262	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	125.00	11/2008 -	06/2014	67	-
263	Chikaluripet-Vijaywada 6 lane (km 355 to Km 434.15) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	857.90	10/2011 -	06/2014	32	-
264	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
265	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,287.00	08/2013 -	06/2014	10	-
266	Kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	672.60	07/2013 -	06/2014	11	-
267	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.39	09/2013 -	07/2014	10	-
268	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	257.00	07/2012 -	07/2014	24	-
269	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	305.20	09/2010 -	08/2014	47	-
270	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	09/2014	63	-
271	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	235.20	09/2009 -	09/2014	60	-
272	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	93.63	04/2009 -	12/2014	68	-
273	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	72.60	11/2008 -	12/2014	73	-
274	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	169.00	04/2009 -	12/2014	68	-
275	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	297.90	04/2010 -	12/2014	56	-
276	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
277	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,129.00	02/2010 -	12/2014	58	-
278	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-
279	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	357.00	09/2013 -	12/2014	15	-
280	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,328.00	08/2013 -	12/2014	16	-
281	4-laning of Brahmapore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,266.00	08/2013 -	12/2014	16	-
282	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	318.00	08/2013 -	02/2015	18	-
283	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
284	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65	-
285	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,734.00	08/2014 -	07/2015	11	-
286	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13	-
287	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	160.00	10/2013 -	11/2015	25	-
288	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	299.60	08/2013 -	12/2015	28	-
289	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
290	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	973.60	07/2015 -	06/2016	11	-
	Total		61,318.65 -	63,230.44	61,202.82				
	<u>Shipping And Ports</u>								
291	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers from M/S Jiangsu Eastern Heavy Industries - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	532.83	448.43	12/2012 11/2013	11/2013	11	0
292	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	600.00	139.80	03/2006 12/2013	12/2013	93	0
293	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
294	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	974.80	12/2010 09/2012	12/2014	48	27
	Total		2,502.59 -	3,104.70	1,669.75				
	<u>Telecommunications</u>								
295	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
296	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	176.00	86.11	10/2007 -	12/2013	74	-
297	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	84.39	06/2009 -	12/2013	54	-
298	Assam Telecom Circle, Phase-V.I., 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
299	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
300	Supply Installation testing and commissioning of Rural Wimax network Phase-II - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	237.44	05/2011 -	12/2013	31	-
	Total		3,166.23 -	2,950.50	1,430.37				
	Urban Development								
301	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	2,494.00	300.76	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	300.76				
	Grand Total		482,375.00	587,404.51	372,204.57				

List of ongoing projects having time and cost overrun w.r.t original schedule

(Sep,2013)								
					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	Range of T.O.R (in months)
1	2	3	4	5	6	7	8	9
	<u>Atomic Energy</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54- 54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2014	31.12	66- 66
	Total		16,663.00 -	22,947.00				
	<u>Coal</u>							
3	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	03/2013 -	10/2014	360.36	19- 19
4	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24- 24
5	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44- 44
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	01/2014	49.09	55- 55
7	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	03/2012 -	03/2014	33.36	24- 24
	Total		7,938.86 -	34,520.95				
	<u>Petrochemicals</u>							
8	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35	20- 20
	Total		5,460.61 -	43,440.95				
	<u>Petroleum</u>							
9	IOR, RUDRASAGAR (ONGCL) - [160100217]	09/2001	113.90 -	438.85	03/2006 -	12/2013	285.29	93- 93
10	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44	21- 21
11	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2013	41.85	18- 18
12	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29	12- 12
13	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	12/2013	12.16	20- 20
14	IOR LAKWA - LAKHMANI (ONGCL) - [160100215]	09/2001	345.10 -	750.00	03/2007 -	09/2013	117.33	78- 78
15	IOR GELEKI (ONGCL) - [160100216]	09/2001	390.09 -	1,674.11	03/2007 -	12/2013	329.16	81- 81

(Sep,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	Range of T.O.R (in months)
1	2	3	4	5	6	7	8	9
16	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46	94- 94
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	01/2014	54.46	27- 27
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	12/2013	67.62	26- 26
19	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	09/2013	121.45	5- 5
20	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76	23- 23
21	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71	63- 63
22	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50	63- 63
23	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20- 20
24	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40	45- 45
25	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27	46- 46
26	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	05/2014	9.85	18- 18
	Total		53,921.74 -	116,828.46				
	<u>Power</u>							
27	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08	10- 10
28	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76	13- 13
29	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006	08/2006	611.01 -	936.00	08/2010 -	10/2013	53.19	38- 38
30	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243	09/2005	1,061.38 -	1,501.75	09/2009 -	11/2014	41.49	62- 62
31	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77	79- 79
32	URI H.E.P STAGE -II (NHPC) - [180100251	08/2005	1,729.29 -	2,081.00	11/2009 -	10/2013	20.34	47- 47
33	KISHANGANGA HEP - [N18000031	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69	10- 10
34	PARBATI H.E.P. STAGE -III (NHPC) - [180100250	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85	41- 41
35	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32	19- 19
36	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	09/2017	50.31	38- 38

(Sep,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	Range of T.O.R (in months)
1	2	3	4	5	6	7	8	9
37	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82	87- 87
38	Tapovan-Vishnugad HEP (4x130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	07/2017	29.14	52- 52
39	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106- 106
40	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69	65- 65
41	SUBANSIRI LOWER H.E.P (NHPC) - [180100221	09/2003	6,285.33 -	10,667.00	09/2010 -	03/2018	69.71	90- 90
42	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87- 87
	Total		44,349.86 -	178,877.27				
	<u>Railways</u>							
43	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01	96- 96
44	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	10/2013	127.94	139- 139
45	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	12/2010 -	03/2015	941.79	51- 51
46	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	10/2013	300.67	46- 46
47	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55	141- 141
48	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	12/2008 -	09/2014	89.20	69- 69
49	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65- 65
50	Champajharan-Bimalgarh Doubling extension - [N22000162	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33	9- 9
51	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	03/1994 -	10/2013	265.83	235- 235
52	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66- 66
53	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03	24- 24
54	Ghutiasharif-Canning (ER) - [N22000117	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65	23- 23
55	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.35	06/2004 -	12/2014	207.29	126- 126
56	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50	132- 132
57	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84- 84
58	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58	129- 129

(Sep,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	Range of T.O.R (in months)
1	2	3	4	5	6	7	8	9
59	Ramanagram-Mysore doubling with electrification of Kengesii- Musore (SWR) - [N22000107	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15	12- 12
60	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240- 240
61	BHAIRABI SAIRONG, NL, NEFR - [N22000100	04/2008	619.34 -	2,384.34	04/2014 -	03/2017	284.98	35- 35
62	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98- 98
63	BHOPAL BINA 3D LINE DOUBLING - [N22000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69- 69
64	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,453.50	03/2011 -	03/2017	512.11	72- 72
65	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,350.00	12/2008 -	03/2015	220.60	75- 75
66	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	03/2014 -	12/2015	114.06	21- 21
67	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124	04/2006	850.00 -	2,441.48	03/2015 -	03/2017	187.23	24- 24
68	Construction of NL from Kumarghat-Agartala - [N22000194	04/1999	895.00 -	1,151.00	03/2007 -	03/2015	28.60	96- 96
69	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69- 69
70	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2015	399.62	92- 92
71	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38	15- 15
72	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127	04/1996	1,676.31 -	5,000.00	03/2009 -	12/2014	198.27	69- 69
73	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181- 181
74	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36	33- 33
	Total		22,453.88 -	251,085.98				
	<u>Road Transport And Highways</u>							
75	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	03/2014	30.10	66- 66
76	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68	67- 67
77	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	05/2014	85.58	58- 58
78	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75	68- 68
79	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2014	82.12	79- 79

(Sep,2013)

					Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overrun (%)	Range of T.O.R (in months)
1	2	3	4	5	6	7	8	9
80	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	04/2004 -	11/2013	7.35	115- 115
81	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29	65- 65
82	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	05/2008 -	12/2013	26.41	67- 67
83	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	03/2014	33.70	78- 78
84	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2013	106.50	25- 25
	Total		3,158.01 -	256,338.08				
	<u>Shipping And Ports</u>							
85	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035	10/2002	150.00 -	600.00	03/2006 -	12/2013	300.00	93- 93
86	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016	11/2007	1,228.00 -	1,460.00	12/2010 -	12/2014	18.89	48- 48
	Total		1,378.00 -	258,398.08				
	<u>Steel</u>							
87	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038	08/2007	108.00 -	216.68	10/2012 -	12/2013	100.63	14- 14
88	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068	07/2007	230.00 -	343.58	02/2011 -	10/2013	49.38	32- 32
89	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018	01/2007	295.89 -	607.17	12/2011 06/2010	12/2013	105.20	24- 24
90	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067	10/2005	8,692.00 -	12,291.00	10/2009 -	10/2013	41.41	48- 48
91	EXPANSION OF IISCO STEEL PLANT - [N12000051	02/2008	14,443.00 -	16,408.00	12/2011 -	12/2013	13.61	24- 24
	Total		23,768.89 -	288,264.51				
	<u>Telecommunications</u>							
92	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42	54- 54
93	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52	34- 34
	Total		1,065.85 -	289,353.83				
	Grand Total		180,158.70	1,740,055.11				

List of ongoing projects having cost overrun w.r.t. to original schedule

(Sep,2013)							
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>Atomic Energy</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	06/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>Civil Aviation</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,325.00	05/2011 -	03/2013	19.69
4	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
	Total		3,750.51 -	27,287.00			
	<u>Coal</u>						
5	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	01/2014	49.09
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
7	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	977.53	03/2013 -	10/2014	360.36
8	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,540.93	03/2012 -	03/2014	33.36
10	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
11	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		8,579.45 -	39,549.64			
	<u>Petrochemicals</u>						
12	Assam gas Cracker project - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	12/2013	63.35
	Total		5,460.61 -	48,469.64			
	<u>Petroleum</u>						

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
13	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	09/2001	345.10 -	750.00	03/2007 -	09/2013	117.33
14	IOR GELEKI (ONGCL) - [160100216	09/2001	390.09 -	1,674.11	03/2007 -	12/2013	329.16
15	IOR, RUDRASAGAR (ONGCL) - [160100217	09/2001	113.90 -	438.85	03/2006 -	12/2013	285.29
16	DEV OF G1 AND GS-15 (ONGCL) - [160100231	04/2003	429.82 -	2,735.65	04/2006 -	02/2014	536.46
17	DEVELOPMENT OF C-SERIES FIELDS - [N16000023	08/2006	3,195.16 -	3,690.37	12/2008 -	03/2014	15.50
18	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032	01/2007	2,323.40 -	2,920.82	09/2010 03/2012	12/2015	25.71
19	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	5,633.44	08/2010 03/2012	05/2014	73.40
20	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039	10/2007	5,713.03 -	8,813.41	05/2010 -	03/2014	54.27
21	RESITMENT OF MARKETING INSTALATION AT VISAKH - [N16000057	01/2009	756.00 -	898.00	- -	08/2013	18.78
22	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	32,710.00	11/2012 -	05/2014	9.85
23	CONSTRUCTION OF NEW TERMINAL AT ENNORE CHENNAI - [N16000066	01/2008	224.00 -	394.00	- -	03/2013	75.89
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I [N16000070	07/2009	238.68 -	312.00	01/2012 -	07/2013	30.72
25	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081	04/2008	825.00 -	1,827.00	04/2013 -	09/2013	121.45
26	ADDITIONAL DEV. OF D-1 FIELD - [N16000086	01/2010	2,163.64 -	2,331.62	06/2012 -	05/2014	7.76
27	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099	03/2009	234.78 234.78	317.64	09/2012 -	09/2013	35.29
28	Development of Cluster-7 Fields - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
29	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
30	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	12/2013	12.16
31	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	10/2014 -	10/2014	0.00
33	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	01/2014	54.46
34	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	12/2013	67.62
35	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	12/2013	41.85

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
36	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]	08/2008	126.18 -	159.54	06/2012 -	03/2014	26.44
	Total		58,175.86 -	127,137.62			
	<u>Power</u>						
37	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
38	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	6,414.56	04/2009 -	09/2014	41.69
39	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]	09/2003	6,285.33 -	10,667.00	09/2010 -	03/2018	69.71
40	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	5,139.00	12/2009 06/2016	03/2017	105.82
41	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
42	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]	09/2005	1,061.38 -	1,501.75	09/2009 -	11/2014	41.49
43	KAIGA 3 and 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
44	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]	10/2005	2,304.56 -	2,716.00	10/2010 -	03/2014	17.85
45	URI H.E.P STAGE -II (NHPC) - [180100251]	08/2005	1,729.29 -	2,081.00	11/2009 -	10/2013	20.34
46	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
47	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]	08/2006	611.01 -	936.00	08/2010 -	10/2013	53.19
48	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	02/2017	79.77
49	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	07/2017	29.14
50	TRANSMISSION SYSTEM ASSOCIATED WITH PARBATI-III HEP - [N18000018]	07/2006	557.24 -	775.25	01/2010 -	07/2013	39.12
51	KISHANGANGA HEP - [N18000031]	07/2007	2,238.67 -	3,642.00	01/2016 -	11/2016	62.69
52	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	09/2017	50.31
53	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,117.92	08/2013 -	09/2014	94.76
54	MOUDA STPP - [N18000048]	11/2008	5,459.28 -	6,010.89	08/2012 -	03/2013	10.10
55	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	03/2014	9.32
56	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	623.44	07/2013 -	05/2014	48.08

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		52,742.12 -	199,138.80			
	<u>Railways</u>						
57	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	580.83	03/1994 -	10/2013	265.83
58	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
59	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
60	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
61	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	120.90 175.30	725.00	06/1999 -	03/2011	499.67
62	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
63	New BG Rly line from Eklakhi-Balurghat including Gazole-Itahar(NL),NEFR - [220100135	04/1983	36.80 274.41	703.17	- -	03/2015	1,810.79
64	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148	04/1993	100.00 119.29	227.94	03/2002 -	10/2013	127.94
65	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
66	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
67	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.48	03/2004 -	12/2014	351.58
68	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168	04/1995	184.00 -	900.05	12/2011 12/2010	03/2013	389.16
69	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	353.08 -	2,820.00	- -	-	698.69
70	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183	02/1997	295.00 -	412.91	- -	01/2013	39.97
71	DAUSA-GANGAPUR CITY(NL),NWR - [220100184	02/1997	151.84 -	410.08	- -	03/2014	170.07
72	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
73	NANGALDAM-TALWARA(NL),NR - [220100188	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
74	KADUR-CHIKMAGALUR-SAKLESHPUR (NL),(SWR) - [220100190	04/1996	157.00 -	333.50	03/2012 -	03/2013	112.42
75	KARUR-SALEM(NL),SR - [220100191	02/1997	155.55 -	775.36	- -	10/2012	398.46
76	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
77	HUBLI-ANKOLA(NL),SWR - [220100193	04/1997	227.00 -	2,135.00	- -	-	840.53

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
78	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197	03/1997	395.00 598.98	1,708.41	- -	03/2013	332.51
79	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201	09/1997	1,000.00 -	4,996.19	04/2008 12/2011	12/2015	399.62
80	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	218.24 236.41	645.00	- -	03/2012	195.55
81	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	31.42 154.30	535.40	03/2007 03/2007	03/2015	1,604.01
82	KOTTUR-HARIHAR(NL),(SWR) - [220100212	04/1995	65.94 -	302.23	- -	12/2012	358.34
83	RANCHI-LOHARDAGA(GC),SER - [220100214	04/1997	194.07 -	596.35	06/2004 -	12/2014	207.29
84	MACHERLA-NALGONDA(NL)(SCR) - [220100220	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
85	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222	03/1999	491.19 -	2,957.21	07/2005 -	-	502.05
86	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	925.00 -	1,630.97	05/2008 -	-	76.32
87	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240	04/1997	233.00 335.77	1,043.56	03/2012 -	-	347.88
88	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241	07/1998	248.44 -	1,115.21	12/2012 -	04/2013	348.89
89	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243	04/1999	108.00 -	432.72	12/2009 -	10/2013	300.67
90	KATIHAR - JOGBANI (GC)(NEFR) - [220100247	09/2001	100.00 -	1,041.79	12/2010 -	03/2015	941.79
91	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	550.00 -	1,566.00	- -	-	184.73
92	GULBARGA-BIDAR,SCR(NL) - [220100254	02/1998	242.42 369.70	832.00	- 05/2009	05/2009	243.21
93	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR- NAUTANWA GC (NER) [220100255	03/2002	381.17 -	863.23	- -	03/2012	126.47
94	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256	04/1999	323.40 -	744.71	- -	03/2014	130.28
95	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	78.23 -	162.87	- -	-	108.19
96	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258	03/2002	409.00 408.76	847.75	06/2007 -	06/2007	107.27
97	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	100.00 -	800.00	- -	-	700.00
98	QUILON-TIRUNELVELI-TENKASI- VIRUDHUNAGAR(SR)(GC) [220100263	03/1998	280.00 -	1,029.92	- -	03/2013	267.83
99	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	330.00 -	1,045.20	- -	-	216.73
100	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,350.00	12/2008 -	03/2015	220.60

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
101	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara and Noapara-NSCB Airport(MTP) - [220100268	03/2000	907.69 -	3,176.10	12/2006 -	08/2010	249.91
102	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	03/2013	191.48
103	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	157.96 -	1,188.91	- 12/2009	02/2012	652.67
104	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	138.00 240.59	607.09	12/2012 12/2012	02/2013	339.92
105	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	901.62	- -	-	553.35
106	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	12/2016	1,172.55
107	JIND-SONEPAT (NL),NR - [220100280	01/2004	190.81 -	693.39	03/2012 -	12/2012	263.39
108	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	355.38 -	1,995.25	- -	03/2014	461.44
109	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
110	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
111	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	4,453.50	03/2011 -	03/2017	512.11
112	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	04/2003	324.66 -	528.65	- -	-	62.83
113	KOSI BRIDGE (NL), ECR - [220100304	04/2002	323.41 -	341.41	03/2012 -	03/2013	5.57
114	KODERMA GIRIDH (NL), ECR - [220100306	04/1996	371.36 -	768.87	- -	03/2010	107.04
115	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
116	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
117	DANIWAN-BIHARSARIF (NL), ECR - [220100311	04/2001	104.79 -	406.92	- -	-	288.32
118	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314	04/2001	727.13 727.13	1,225.90	- -	-	68.59
119	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2014	229.71
120	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	02/2013	116.33
121	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	129.70 -	245.39	12/2008 -	09/2014	89.20
122	RUPSA-BANGRIPOSI (GC)(SER) - [220100323	02/1996	57.94 -	639.97	03/1998 08/2005	08/2005	1,004.54
123	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
124	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
125	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [N220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
126	TALCHER-BIMALAGARH(NL)(ECOR) - [N220100328	04/2005	726.96 -	810.78	- -	-	11.53
127	RAICHUR-GUNTAKAL(DL)(SCR) - [N220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
128	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	114.01 283.95	477.88	03/2012 -	03/2013	319.16
129	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N220000032	04/2006	378.56 -	791.59	- -	-	109.11
130	GOELKERA-MANOHARPUR,(LD)(SER) - [N220000045	03/1997	186.92 -	261.70	02/2006 -	-	40.01
131	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N220000049	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
132	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS and PU - [N220000052	04/2003	98.74 -	337.30	- -	03/2012	241.60
133	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N220000053	03/2005	470.09 -	1,417.97	- -	03/2012	201.64
134	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N220000075	09/2006	324.90 -	385.54	03/2010 -	-	18.66
135	BHOPAL BINA 3D LINE DOUBLING - [N220000077	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
136	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI [N220000079	09/2007	404.19 -	1,383.45	- -	-	242.28
137	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N220000080	09/2006	343.17 -	914.98	- -	12/2012	166.63
138	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N220000082	12/2006	170.00 -	435.87	03/2011 -	03/2011	156.39
139	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR [N220000083	09/1996	156.00 -	406.40	- -	12/2013	160.51
140	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N220000084	09/2006	125.00 -	227.40	- -	-	81.92
141	TIDIVANAM-NAGARI (NL) - [N220000085	09/2006	456.00 -	582.83	- -	-	27.81
142	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N220000086	09/2006	200.00 -	385.20	- -	03/2015	92.60
143	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N220000087	09/2006	300.00 -	532.87	- -	-	77.62
144	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N220000088	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
145	BARDHAMAN-KATWA (GC) - [N220000091	04/2007	245.15 -	1,106.62	12/2010 -	03/2011	351.41
146	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N220000092	04/2008	5,300.00 -	6,220.15	03/2014 -	12/2016	17.36
147	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N220000094	02/2008	171.10 -	246.44	03/2012 -	03/2014	44.03

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
148	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.47	06/2005 -	06/2016	265.50
149	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	12/2015	114.06
150	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,384.34	04/2014 -	03/2017	284.98
151	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	- -	03/2015	27.20
152	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,380.58	12/2015 -	03/2017	152.38
153	Ramanagram-Mysore doubling with electrification of Kengesil-Musore (SWR) - [N22000107]	04/2007	482.00 -	482.70	03/2013 -	03/2014	0.15
154	Jaipur - Ringus - Churu and Sikar - Loharu Guage Conversion (NWR) - [N22000113]	04/2008	653.19 -	653.47	03/2014 -	03/2014	0.04
155	Dakshin-barasal-lakshmikantapur - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	02/2012	105.53
156	Ghutiasharif-Canning (ER) - [N22000117]	04/2009	189.97 -	611.03	12/2011 -	11/2013	221.65
157	Pandabeswar-Chinpai doubling (ER) - [N22000118]	04/2004	225.68 -	293.74	12/2010 -	12/2010	30.16
158	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
159	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]	04/2008	394.14 -	1,215.30	03/2013 -	03/2013	208.34
160	Bhuj-Naliya(GC) with extension from naliya to Vayor (WR) - [N22000123]	04/2008	318.24 -	485.65	03/2012 -	-	52.61
161	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]	04/2006	850.00 -	2,441.48	03/2015 -	03/2017	187.23
162	Bhavnagar-workshop facilities for 50 BG coaches POH per month (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
163	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]	04/1996	1,676.31 -	5,000.00	03/2009 -	12/2014	198.27
164	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]	03/2012	160.89 -	199.75	- -	-	24.15
165	Virangam-Samakhiali (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
166	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
167	Thiyat Hamira-Sanu - [N22000149]	04/2013	236.39 -	236.93	- -	-	0.23
168	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittisgarh-Udaipur - [N22000152]	04/2013	456.00 -	965.16	- -	-	111.66
169	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And Ratangarh-Degana GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
170	Ajmer-Bangurgram - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
171	Dholpur-Sirmuttra with extension to Gangapurcity And Mohari-Tantpur & Tanpur-Bansi Paharpur - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
172	Digha-Jaleswar including MM for Digha-Egra - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
173	Champajharan-Bimalgarh Doubling extension - [N22000162]	04/2010	149.90 -	177.38	03/2015 -	12/2015	18.33
174	Tamluk-Basulya-Sutahata Doubling - [N22000163]	04/2010	146.95 -	171.02	06/2013 -	-	16.38
175	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	12/2015	25.60
176	Sakri-Hasanpur Road (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
177	Chhapra-Muzaffarpur (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
178	Attipattu-Puttur - [N22000184]	04/2008	446.87 -	527.00	- -	-	17.93
179	Chennai-Cuddalore via Mamallapuram - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22
180	Cuddalore-Salem via Vriddhachalam GC - [N22000187]	04/1999	198.68 -	556.64	- -	-	180.17
181	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]	04/1999	271.24 -	520.00	- -	-	91.71
182	Villupuram-Dindigul with Electrification - [N22000189]	04/2008	822.39 -	1,280.83	- -	-	55.74
183	Kuruppanthara-Chingavanam - [N22000190]	04/2007	270.14 -	346.15	- -	-	28.14
184	New BG line from Dudhnoi-Mendipatar - [N22000192]	04/1999	175.43 -	247.75	- -	03/2014	41.22
185	Construction of NL from Kumarghat-Agartala - [N22000194]	04/1999	895.00 -	1,151.00	03/2007 -	03/2015	28.60
186	Erode-Palani - [N22000199]	04/2008	288.57 -	603.22	- -	-	109.04
187	Madurai-Bodinayakanur - [N22000201]	04/2008	164.41 -	260.72	- -	-	58.58
188	Chengalpattu-Villupuram doubling with new MM for Tambaram-Chengalpattu 3rd line GC alongwith electrif - [N22000202]	04/2007	247.00 -	951.24	- -	-	285.12
189	Chengannur-Chingavanam - [N22000203]	04/2006	191.72 -	222.95	- -	-	16.29
190	New Jalpaiguri-Siliguri-New Bongaigaon including Br. line And MM for Chalsa-Naxal& Rajabhatkhowa-Jai - [N22000209]	04/1999	523.17 -	1,393.44	- -	-	166.35
191	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Phase-II - [N22000213]	04/2012	632.68 -	816.55	04/2012 -	-	29.06
192	Madurai-Tuticorin via Aruppukottai - [N22000215]	04/2011	601.43 -	800.00	- -	-	33.02
193	Wardha-Nanded Maharashtra - [N22000231]	04/2008	697.00 -	1,604.00	- -	-	130.13
194	Kalyan-Kasara 3rd line - [N22000233]	04/2011	277.70 -	279.70	- -	-	0.72

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
195	3rd line between Bhusawal-Jalgaon - [N22000247	04/2011	182.06 -	184.06	- -	-	1.10
196	Munirabad (gingera) -Raichur NL - [N22000257	04/2007	179.65 -	645.00	- -	-	259.03
197	Akola-Khandwa GC Akola-Akot - [N22000263	04/2008	184.26 -	2,000.00	- -	-	985.42
198	Bhanupali-Bilaspur Beri NL - [N22000273	04/2008	1,046.88 -	2,966.99	- -	-	183.41
199	White Field-Kolar NL - [N22000280	04/2011	341.05 -	348.85	- -	-	2.29
200	Haridwar-Laksar - [N22000289	04/2012	219.83 -	444.18	- -	-	102.06
	Total		59,267.87 -	369,333.45			
	<u>Road Transport And Highways</u>						
201	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153	04/2000	225.00 -	241.53	04/2004 -	11/2013	7.35
202	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	03/2014	30.10
203	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 - [240106236	12/2003	166.27 -	193.10	03/2008 -	02/2008	16.14
204	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237	12/2003	284.00 -	359.00	05/2008 -	12/2013	26.41
205	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	12/2014	92.75
206	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	06/2014	80.68
207	HARANGAJO TO MAIBANG, km 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	04/2014	82.12
208	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	05/2014	85.58
209	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	07/2015	2.29
210	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	03/2014	33.70
211	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	12/2013	106.50
	Total		3,324.28 -	374,778.65			
	<u>Shipping And Ports</u>						
212	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
213	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
214	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	1,460.00	12/2010 -	12/2014	18.89
215	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	12/2013	300.00
216	Construction of berthing and allied facilities off Tekra near Tuna,Kandla Port Trust - [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
217	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
218	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN - [N25000048]	03/2009	3,500.00 -	4,150.00	01/2012 -	08/2013	18.57
219	Acquisition of two(2) Nos. of 317000 DWT very large crude carriers from M/S Jiangsu rongsheng heavy - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	02/2014	2.93
220	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		8,628.97 -	385,997.15			
	<u>Steel</u>						
221	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	10/2013	41.41
222	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	12/2013	105.20
223	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	08/2007	108.00 -	216.68	10/2012 -	12/2013	100.63
224	EXPANSION OF IISCO STEEL PLANT - [N12000051]	02/2008	14,443.00 -	16,408.00	12/2011 -	12/2013	13.61
225	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]	07/2007	230.00 -	343.58	02/2011 -	10/2013	49.38
226	330 TPH BOILER-6 AND AUXILIARY SYSTEM - [N12000069]	07/2007	260.00 -	349.64	08/2010 -	06/2013	34.48
	Total		24,028.89 -	416,213.22			
	<u>Telecommunications</u>						
227	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTTRANCHAL - [N26000058]	01/2009	149.15 -	158.72	06/2009 -	12/2013	6.42
228	GSM equipment of 799000Lines (2G) 101000 lines 3(G) JharkhandPhase V.1 Telecom Circle - [N26000088]	03/2008	328.13 -	392.13	03/2009 -	01/2013	19.50
229	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]	11/2009	916.70 -	930.60	11/2010 -	09/2013	1.52
	Total		1,393.98 -	417,694.67			
	<u>Urban Development</u>						

(Sep,2013)

					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
230	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
231	C/o office building for IDBI at bandra Kurla Complex,Mumbai - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	429,476.75			
	<u>Water Resources</u>						
232	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	430,663.75			
	Grand Total		249,067.62	3,288,687.34			

List of Projects without Milestones w.r.t. Original Schedule

				(Sep,2013)		
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>Civil Aviation</u>					
1	D/O KAMARAJ DOMESTIC TER-PH-II And EXP. ANNA INT. - [N04000038]AAI,Tamil Nadu	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012	0/0
2	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,West Bengal	08/2008	1,942.51 -	05/2011 -	03/2013	0/0
3	GAGAN PROJECT - [N04000065]AAI,Multi State	09/2008	626.00 -	06/2013 -	06/2013	0/0
4	Construction of New International Terminal Building - [N04000069]AAI,Goa	05/2010	335.61 -	05/2012 -	11/2013	0/0
5	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AI - [N04000072]AAI,Multi State	02/2010	344.28 -	03/2014 -	06/2014	0/0
6	C/o new Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	01/2011 04/2013	03/2015	0/0
7	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070]AAI,Chandigarh	02/2011	452.00 -	03/2015 -	03/2015	0/0
8	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,Multi State	10/2012	217.60 -	03/2015 -	03/2015	0/0
	Total		6,035.46 -			0/0
	<u>Coal</u>					
9	Muraidih UG - [N06000096]BCCL,Jharkhand	02/2011	339.88 -	04/2014 -	04/2014	0/0
10	Moonidih XV Seam UG - [N06000098]BCCL,Jharkhand	08/2011	1,230.27 -	04/2015 -	04/2015	0/0
	Total		1,570.15 -			0/0
	<u>Steel</u>					
11	Coke Oven Battery-5 - [N12000080]SAIL,West Bengal	03/2012	339.35 -	06/2015 -	06/2015	0/0
	Total		339.35 -			0/0
	<u>Petroleum</u>					
12	Capacity Augmentation of Kota Piyala Section of MMBPL Pipeli - [N16000153]BPCL,Rajasthan	04/2011	152.89 -	06/2013 -	06/2013	0/0
13	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	03/2010 03/2012	12/2013	0/0
14	Wax Project - [N16000101]NRL,Assam	06/2010	576.60 -	12/2013 -	12/2013	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
15	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	09/2012 -	12/2013	0/0
16	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLAN - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	04/2012 06/2013	12/2013	0/0
17	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	04/2012 -	12/2013	0/0
18	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	10/2011 -	12/2013	0/0
19	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	06/2012 -	12/2013	0/0
20	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	10/2011 -	01/2014	0/0
21	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	04/2006 06/2012	02/2014	0/0
22	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,Multi State	08/2010	8,140.00 -	02/2014 -	02/2014	0/0
23	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	12/2008 04/2013	03/2014	0/0
24	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	05/2010 03/2013	03/2014	0/0
25	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	07/2010 05/2012	03/2014	0/0
26	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	09/2012 -	03/2014	0/0
27	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	06/2012 -	03/2014	0/0
28	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	06/2012 -	05/2014	0/0
29	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,Multi State	11/2012	309.81 -	10/2014 -	10/2014	0/0
30	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	10/2010 -	12/2014	0/0
31	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	09/2011 -	12/2014	0/0
32	Replacement of CDU/VDU at Mumbai Refinery - [N16000142]BPCL,Maharashtra	01/1999	1,419.00 -	12/2014 -	12/2014	0/0
33	Mounded Bullet - [N16000154]CPCL,Tamil Nadu	12/2012	279.00 -	12/2014 -	12/2014	0/0
34	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165]OIL,Multi State	04/2010	270.00 -	12/2014 -	12/2014	0/0
35	Reconstruction of BPA and BPB Platforms - [N16000161]ONGC,Maharashtra	03/2013	1,138.50 -	04/2015 -	04/2015	0/0
36	Surat Paradip Pipeline Project - [N16000163]GAIL,Multi State	10/2012	10,281.00 -	- -	04/2015	0/0
37	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,Multi State	02/2011	913.00 -	07/2015 -	07/2015	0/0
38	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,Multi State	08/2011	586.00 -	08/2015 -	07/2015	0/0
39	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,Karnataka	11/2012	666.00 -	11/2015 -	11/2015	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
40	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	09/2010 03/2012	12/2015	0/0
41	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	01/2013 -	12/2015	0/0
42	Integrated Development of Bassein Field - [N16000160]ONGC,Maharashtra	12/2012	3,513.07 -	02/2016 -	02/2016	0/0
43	IREP - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	12/2015 -	05/2016	0/0
44	Construction of one Multipurpose Support Vessel - [N16000103]ONGC,Multi State	01/2010	723.64 -	03/2013 -	06/2016	0/0
45	CREATION OF SECONDARY TANK FARM WITH DEHYDRATION FACILITY - [N16000167]OIL,Multi State	08/2006	374.56 -	09/2012 -	10/2016	0/0
46	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	12/2014 -	12/2016	0/0
47	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	12/2014 -	12/2016	0/0
48	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	04/2015 -	03/2017	0/0
49	DE-BOTTLENECKING OF SMPL (Salaya-Mathura crude pip - [N16000089]IOCL,Maharashtra	12/2009	1,584.00 -	- -	-	0/0
50	Ennore-Trichy-Madurai LPG Pipeline - [N16000162]IOCL,Tamil Nadu	05/2013	711.00 -	- -	-	0/0
	Total		88,807.21 -			0/0
	<u>Power</u>					
51	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123]PGCIL,Multi State	03/2012	198.63 -	09/2014 -	09/2014	0/0
52	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139]PGCIL,Tamil Nadu	01/2013	182.80 -	10/2014 -	10/2014	0/0
53	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	09/2009 06/2013	11/2014	0/0
54	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,Multi State	09/2012	1,935.35 -	12/2014 -	11/2014	0/0
55	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC - [N18000143]PGCIL,Multi State	03/2013	514.20 -	06/2015 -	06/2015	0/0
56	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145]PGCIL,Andhra Pradesh	06/2012	1,909.24 -	06/2015 -	06/2015	0/0
57	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,Multi State	09/2013	680.69 -	03/2016 -	03/2016	0/0
58	Transmission System associated with Mauda Stage-II - [N18000153]PGCIL,Multi State	09/2013	1,575.30 -	05/2016 -	05/2016	0/0
	Total		8,057.59 -			0/0
	<u>Railways</u>					
59	RUPSA-BANGRIPOSI (GC)(SER) - [220100323]SER,Odisha	02/1996	57.94 604.04	03/1998 08/2005	08/2005	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
60	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,Multi State	03/2002	409.00 625.30	06/2007 -	06/2007	0/0
61	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,Andhra Pradesh	07/1998	125.00 363.26	07/2008 -	07/2008	0/0
62	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,Karnataka	02/1998	242.42 369.70	- 05/2009	05/2009	0/0
63	KODERMA GIRIDH (NL), ECR - [220100306]ECR,Jharkhand	04/1996	371.36 768.87	- 03/2010	03/2010	0/0
64	TOLLYGANJ-GARIA with extension to Dum Dum-Noapara - [220100268]MRTP,West Bengal	03/2000	907.69 3,156.32	12/2006 08/2010	08/2010	0/0
65	Pandabeswar-Chinpai doubling (ER) - [N22000118]ER,West Bengal	04/2004	225.68 293.74	12/2010 12/2010	12/2010	0/0
66	AMRAVATI-NARKHER NL(CR) - [220100118]CR,Maharashtra	06/1994	120.90 663.10	06/1999 03/2011	03/2011	0/0
67	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,Multi State	12/2006	170.00 170.00	03/2011 03/2011	03/2011	0/0
68	BARDHAMAN-KATWA (GC) - [N22000091]ER,West Bengal	04/2007	245.15 1,106.62	12/2010 03/2011	03/2011	0/0
69	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,Multi State	02/1996	240.00 -	- -	02/2012	0/0
70	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,West Bengal	04/2000	157.96 1,188.91	- 12/2009	02/2012	0/0
71	Dakshin-barasal-lakshmikantapur - [N22000116]ER,West Bengal	04/2009	259.51 533.38	12/2011 02/2012	02/2012	0/0
72	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,Andhra Pradesh	03/1996	155.74 429.49	02/2009 -	03/2012	0/0
73	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,Multi State	04/1997	218.24 377.32	- -	03/2012	0/0
74	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,Uttar Pradesh	03/2002	381.17 863.23	- -	03/2012	0/0
75	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC - [N22000052]WS&PU,Bihar	04/2003	98.74 224.51	- -	03/2012	0/0
76	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,Bihar	03/2005	470.09 1,417.97	- -	03/2012	0/0
77	KARUR-SALEM(NL),SR - [220100191]SR,Tamil Nadu	02/1997	155.55 155.00	- -	10/2012	0/0
78	KOTTUR-HARIHAR(NL),(SWR) - [220100212]SWR,Karnataka	04/1995	65.94 302.23	- -	12/2012	0/0
79	JIND-SONEPAT (NL),NR - [220100280]NR,Haryana	01/2004	190.81 238.56	03/2012 03/2012	12/2012	0/0
80	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,Tamil Nadu	09/2006	343.17 343.17	- -	12/2012	0/0
81	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,Karnataka	02/1997	295.00 412.91	- -	01/2013	0/0
82	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,Multi State	04/2000	138.00 607.09	12/2012 12/2012	02/2013	0/0
83	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,Bihar	04/2003	218.19 218.19	- -	02/2013	0/0
84	Tinpahar - Sahibganj (ER) - [N22000115]ER,Jharkhand	04/2008	167.73 167.73	03/2012 -	02/2013	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
85	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,Jharkhand	04/1995	184.00 900.05	12/2011 12/2011	03/2013	0/0
86	KADUR-CHIKMAGALUR-SAKLIESHPUR (NL),(SWR) - [220100190]SWR,Karnataka	04/1996	157.00 262.82	03/2012 03/2012	03/2013	0/0
87	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,Uttar Pradesh	03/1997	395.00 1,577.45	- -	03/2013	0/0
88	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,Multi State	04/1998	92.63 228.09	02/2011 02/2011	03/2013	0/0
89	KOSI BRIDGE (NL), ECR - [220100304]ECR,Bihar	04/2002	323.41 322.95	03/2012 03/2013	03/2013	0/0
90	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,Bihar	04/1996	114.01 332.92	03/2012 03/2013	03/2013	0/0
91	Ahmedabad-Himmatnagar-Udaipur (WR) - [N22000121]WR,Gujarat	04/2008	394.14 385.60	03/2013 -	03/2013	0/0
92	CHANDIGARH-LUDHIANA(NEW BG LINE),NR - [220100241]NR,Punjab	07/1998	248.44 576.27	12/2012 01/2013	04/2013	0/0
93	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	03/1994 -	10/2013	0/0
94	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	03/2002 -	10/2013	0/0
95	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	12/2009 03/2011	10/2013	0/0
96	Ghutiasharif-Canning (ER) - [N22000117]ER,West Bengal	04/2009	189.97 611.03	12/2011 11/2013	11/2013	0/0
97	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,Madhya pradesh	04/2005	383.79 -	- -	12/2013	0/0
98	CONSTRUCTION OF NEW LINE FROM HARMATI-ITANAGAR/NAR - [N22000083]NEFR,Arunachal Pradesh	09/1996	156.00 156.00	- -	12/2013	0/0
99	Bandel-Naihati new rail bridge in replacement of j - [N22000119]ER,West Bengal	04/1999	207.52 207.52	12/2012 -	12/2013	0/0
100	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	01/1999 -	12/2013	0/0
101	PANVEL PEN DOUBLING - [N22000255]CR,Multi State	04/2006	191.00 -	- -	01/2014	0/0
102	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,Andhra Pradesh	12/1994	124.43 495.68	- -	02/2014	0/0
103	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,Rajasthan	02/1997	151.84 410.08	- -	03/2014	0/0
104	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,Odisha	04/1994	355.38 470.21	- -	03/2014	0/0
105	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGER - [220100315]NEFR,Multi State	01/2004	915.70 915.70	- -	03/2014	0/0
106	HATHUA-BHATNI (N L) (NER) - [220100319]NER,Multi State	04/2005	230.03 230.03	- -	03/2014	0/0
107	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G' - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	03/2012 12/2013	03/2014	0/0
108	Ramanagram-Mysore doubling with electrification of - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	03/2013 -	03/2014	0/0
109	New Work for Construction of Metro railway from Ba - [N22000109]RVNL,West Bengal	04/2010	2,069.60 -	03/2014 -	03/2014	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
110	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113]NWR,Rajasthan	04/2008	653.19 653.19	03/2014 -	03/2014	0/0
111	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114]NWR,Rajasthan	04/2008	516.23 516.23	03/2014 -	03/2014	0/0
112	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122]WR,Gujarat	04/2008	1,389.62 -	03/2014 -	03/2014	0/0
113	New BG line from Dudhnoi-Mendipatar - [N22000192]NEFR,Multi State	04/1999	175.43 -	- -	03/2014	0/0
114	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244]ER,Multi State	04/2009	257.42 -	03/2014 -	03/2014	0/0
115	PEN ROHA DOUBLING - [N22000254]CR,Multi State	04/2007	203.00 -	- -	03/2014	0/0
116	Viramgam-Surendranagar (DL) - [N22000146]WR,Gujarat	04/2010	279.40 -	- -	04/2014	0/0
117	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	02/2009 02/2009	08/2014	0/0
118	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	03/2009 03/2009	08/2014	0/0
119	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	12/2008 -	09/2014	0/0
120	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	03/2004 12/2010	12/2014	0/0
121	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	06/2004 -	12/2014	0/0
122	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	03/2009 12/2012	12/2014	0/0
123	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	06/2013 06/2013	12/2014	0/0
124	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarg - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	03/2009 -	12/2014	0/0
125	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,Odisha	04/1998	183.23 -	02/2015 -	02/2015	0/0
126	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	03/1995 -	03/2015	0/0
127	New BG Rly line from Eklakhi-Balurghat including G - [220100135]NEFR,West Bengal	04/1983	36.80 274.41	- -	03/2015	0/0
128	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	03/2007 03/2007	03/2015	0/0
129	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	12/2010 12/2010	03/2015	0/0
130	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), - [220100266]NEFR,Multi State	04/2000	733.00 733.00	12/2008 -	03/2015	0/0
131	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL P - [N22000086]NEFR,Assam	09/2006	200.00 200.00	- -	03/2015	0/0
132	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,Bihar	04/2008	282.92 282.92	- -	03/2015	0/0
133	Himmatnagar - Udaipur Gauge Convession (NWR) - [N22000112]NWR,Rajasthan	04/2008	829.74 829.74	03/2015 -	03/2015	0/0
134	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	12/2012 -	03/2015	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
135	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00	03/2007	03/2015	0/0
136	New Coochbehar to Samuktala - [N22000197]NEFR,West Bengal	04/2011	209.77	-	03/2015	0/0
137	New Coochbehar-Gumanihat Patch Doubling project - [N22000198]NEFR,West Bengal	04/2012	283.55	-	03/2015	0/0
138	Ambari Falakata to New Maynaguri - [N22000210]NEFR,Assam	04/2011	312.12	-	03/2015	0/0
139	Plassey-Jiaganj Doubling - [N22000220]ER,Multi State	04/2011	248.07	03/2015	03/2015	0/0
140	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	04/2008 03/2014	12/2015	0/0
141	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	10/2007 12/2012	12/2015	0/0
142	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20	03/2010	12/2015	0/0
143	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	03/2014	12/2015	0/0
144	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90	03/2015	12/2015	0/0
145	Dangoaposi-Rajkharswan 3rd line Doubling - [N22000164]SER,Jharkhand	04/2010	309.44	12/2015	12/2015	0/0
146	New Work for Construction of Metro railway from NS - [N22000110]RVNL,West Bengal	04/2010	3,951.98	03/2016	03/2016	0/0
147	New Work for Construction of Metro railway - [N22000111]RVNL,West Bengal	04/2010	2,619.02	03/2016	03/2016	0/0
148	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP,West Bengal	03/2013	4,874.58	03/2016	03/2016	0/0
149	Manoharpur-Bondamunda 3rd line Doubling - [N22000165]SER,Jharkhand	04/2012	258.20	-	03/2016	0/0
150	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	06/2005 07/2011	06/2016	0/0
151	New Work for Construction of Metro railway from No - [N22000108]RVNL,West Bengal	04/2010	2,397.72	03/2016	06/2016	0/0
152	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,039.29	03/2005 12/2008	12/2016	0/0
153	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	03/2014 03/2016	12/2016	0/0
154	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	03/2011 03/2014	03/2017	0/0
155	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,Uttar Pradesh	04/2006	325.00 325.00	03/2010 03/2017	03/2017	0/0
156	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34	04/2014	03/2017	0/0
157	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48	12/2015	03/2017	0/0
158	New Line from Dimapur to Zubza(Kohima) national pr - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	03/2015	03/2017	0/0
159	Princepghat-Majerhat Doubling of Circular Railway - [N22000239]ER,Multi State	04/2011	299.60	03/2017	03/2017	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
160	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245]ER,Multi State	04/2010	423.66 -	03/2017 -	03/2017	0/0
161	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	11/2002 -	12/2017	0/0
162	Running of 12 car trains on Harbour Line - [N22000214]MRTP,Maharashtra	04/2012	714.10 -	- 12/2017	12/2017	0/0
163	Dholpur-Sirmuttra with extension to Gangapucity A - [N22000158]NCR,Multi State	04/2010	622.41 2,030.50	02/2019 -	02/2019	0/0
164	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148]NCR,Multi State	04/2011	1,176.09 3,845.60	02/2020 -	02/2020	0/0
165	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGD - [220100149]RVNL,Chhatisgarh	04/1995	304.00 -	12/2012 -	-	0/0
166	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,Multi State	02/1997	386.30 1,038.00	03/1998 -	-	0/0
167	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,Kerala	10/1998	550.00 517.70	- -	-	0/0
168	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,Odisha	04/1996	301.64 -	- 09/2009	-	0/0
169	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,Jharkhand	04/2002	459.91 418.17	- -	-	0/0
170	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,Andhra Pradesh	04/2003	136.62 -	12/2007 03/2010	-	0/0
171	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,Jharkhand	03/1997	186.92 -	02/2006 -	-	0/0
172	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,Andhra Pradesh	07/2006	743.00 -	03/2008 06/2008	-	0/0
173	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,Chhatisgarh	09/2006	324.90 -	03/2010 -	-	0/0
174	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,Uttar Pradesh	03/2013	307.00 -	- -	-	0/0
175	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,Multi State	03/2007	243.78 -	- -	-	0/0
176	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,Uttar Pradesh	03/2008	195.64 -	- -	-	0/0
177	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,Uttar Pradesh	03/2012	160.89 -	- -	-	0/0
178	CHHAPRA-BALLIA UP - [N22000134]NER,Multi State	03/2013	295.00 -	- -	-	0/0
179	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,Uttar Pradesh	03/2013	643.00 -	- -	-	0/0
180	Bangurgram-Guriya Patch doubling - [N22000137]NWR,Rajasthan	04/2012	246.08 -	- -	-	0/0
181	Chottaudepur-Dhar(NL) - [N22000138]WR,Multi State	04/2007	1,347.26 -	- -	-	0/0
182	Dahod-Indore via Sardarpur, Jhabua and Dhar (NL) - [N22000139]WR,Multi State	04/2007	1,640.04 -	- -	-	0/0
183	Ahmedabad-Botad (GC) - [N22000140]WR,Gujarat	04/2012	567.18 -	- -	-	0/0
184	Dhasa-Jetalsar (GC) - [N22000141]WR,Gujarat	04/2012	376.59 -	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
185	Miyagam-Karjan-Dabhoi-Samlaya (GC) - [N22000142]WR,Gujarat	04/2011	439.88 -	- -	-	0/0
186	Rajkot-Veraval,Wansjalai to Jataisar with new MM f - [N22000143]WR,Gujarat	04/1994	320.66 -	- -	-	0/0
187	Palanpur-Samakhayali (DL) - [N22000144]WR,Gujarat	04/2013	1,266.89 -	- -	-	0/0
188	Viramgam-Samakhiali (DL) - [N22000145]WR,Gujarat	04/2011	446.00 -	- -	-	0/0
189	Ratlam-Dungarpur via Banswara (NL) - [N22000147]NWR,Multi State	04/2012	2,082.75 -	- -	-	0/0
190	Thiyat Hamira-Sanu - [N22000149]NWR,Rajasthan	04/2013	236.39 -	- -	-	0/0
191	Ajmer-Kota (Nasirabad-Jaundri) - [N22000150]NWR,Rajasthan	04/2013	822.00 -	- -	-	0/0
192	Pushkar-Merta - [N22000151]NWR,Rajasthan	04/2013	323.00 -	- -	-	0/0
193	Mavli Jn.-Bari Sadri, MM of Ajmer- Chittsurgarh-Udaipur - [N22000152]NWR,Rajasthan	04/2013	456.00 -	- -	-	0/0
194	Ratangarh-Sardarsahar (MM of Sadulpur-Bikaner And - [N22000153]NWR,Rajasthan	04/2010	739.65 -	- -	-	0/0
195	Guriya-Marwar And Karjoda-Palanpur - [N22000154]NWR,Rajasthan	04/2011	239.73 -	- -	-	0/0
196	Ajmer-Bangurgram - [N22000155]NWR,Rajasthan	04/2011	213.39 -	- -	-	0/0
197	Rani-Marwar Jn. Patch doubling - [N22000156]NWR,Rajasthan	04/2012	288.97 -	- -	-	0/0
198	Alwar-Bandikui doubling - [N22000157]NWR,Rajasthan	04/2013	242.09 -	- -	-	0/0
199	Bowaichandi-Arambagh - [N22000159]SER,West Bengal	04/2010	267.37 -	- -	-	0/0
200	Digha-Jaleswar including MM for Digha-Egra - [N22000160]SWR,Multi State	04/2010	553.63 -	- -	-	0/0
201	Bhadutola-Jhargram via Lalgah (NL) - [N22000161]SER,West Bengal	04/2011	289.64 -	- -	-	0/0
202	Tamluk-Basulya-Sutahata Doubling - [N22000163]SER,West Bengal	04/2010	146.95 -	06/2013 -	-	0/0
203	Ara-Bhabhua Road (NL) - [N22000166]SER,Bihar	04/2008	490.80 -	- -	-	0/0
204	Nawada-Laxmipur (NL) - [N22000167]SER,Bihar	04/2008	620.57 -	- -	-	0/0
205	Gaya-Daltonganj via Rafiganj (NL) - [N22000168]ECOR,Bihar	04/2008	445.25 -	- -	-	0/0
206	Gaya-Chatra (NL) - [N22000169]ECOR,Multi State	04/2008	415.67 -	- -	-	0/0
207	Bihta-Aurangabad (NL) - [N22000170]ECOR,Bihar	04/2008	326.20 -	- -	-	0/0
208	Sakri-Hasanpur Road (NL) - [N22000171]ECOR,Bihar	04/1999	175.69 -	- -	-	0/0
209	Chhapra-Muzaffarpur (NL) - [N22000172]ECOR,Bihar	04/2006	285.07 -	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
210	Darbangha-Kusheshwarsthan (NL) - [N22000173]ECR,Bihar	04/2005	366.73 -	- -	-	0/0
211	Motihari-Sitamarhi (NL) - [N22000174]ECR,Bihar	04/2006	211.00 -	- -	-	0/0
212	Sitamarhi-Jaynagar-Nirmali via Sursand (NL) - [N22000175]ECR,Bihar	04/2008	678.62 -	- -	-	0/0
213	Muzaffarpur-Katra-Orai-Janakpur Road (NL) - [N22000176]ECR,Bihar	04/2008	228.05 -	- -	-	0/0
214	Araria-Supaul (NL) - [N22000177]ECR,Bihar	04/2008	304.41 -	- -	-	0/0
215	Kursela-Bihariganj (NL) - [N22000178]ECR,Bihar	04/2008	192.56 -	- -	-	0/0
216	Muzaffarpur-Darbangha (NL) - [N22000179]ECR,Bihar	04/2008	281.30 -	- -	-	0/0
217	Sakri-Nirmali and Jhanjharpur-Laukahabazar and Sah - [N22000180]ECR,Bihar	04/2004	372.14 -	- -	-	0/0
218	Jaynagar-Bijalpura including extension Bijalpura-Bardibas(Ne - [N22000181]ECR,Bihar	04/2009	470.00 -	- -	-	0/0
219	Hajipur-Ramdayalunagar Doubling - [N22000182]ECR,Bihar	04/2013	213.01 -	- -	-	0/0
220	New Bongaigaon-Rangia-Kamakghya Doubling - [N22000183]NEFR,Multi State	04/2013	1,798.00 -	- -	-	0/0
221	Attippattu-Puttur - [N22000184]SR,Tamil Nadu	04/2008	446.87 -	- -	-	0/0
222	Chennai-Cuddalore via Mamallapuram - [N22000185]SR,Multi State	04/2008	523.52 -	- -	-	0/0
223	Sriperumbudur-Guduvanchery with spur to Irungattukottai-Ava - [N22000186]SR,Tamil Nadu	04/2013	839.00 -	- -	-	0/0
224	Cuddalore-Salem via Vriddhachalam GC - [N22000187]SR,Tamil Nadu	04/1999	198.68 -	- -	-	0/0
225	Chennai Beach-Tambaram-Chengalpattu Suburban GC - [N22000188]SR,Tamil Nadu	04/1999	271.24 -	- -	-	0/0
226	Villupuram-Dindigul with Electrification - [N22000189]SR,Multi State	04/2008	822.39 -	- -	-	0/0
227	Kuruppanthara-Chingavanam - [N22000190]SR,Multi State	04/2007	270.14 -	- -	-	0/0
228	Kumbalam-Turavur - [N22000191]SR,Kerala	04/2011	252.96 -	- -	-	0/0
229	New BG line from Kaliyaganj to Buniadpur - [N22000193]NEFR,West Bengal	04/2010	221.42 -	- -	-	0/0
230	Agartala-Akhaura NL - [N22000195]NEFR,Tripura	04/2012	252.00 -	- -	-	0/0
231	Dimapur-Tizit NL - [N22000196]NEFR,Nagaland	04/2013	4,274.00 -	- -	-	0/0
232	Erode-Palani - [N22000199]SR,Tamil Nadu	04/2008	288.57 -	- -	-	0/0
233	Madurai-Bodinayakanur - [N22000201]SR,Tamil Nadu	04/2008	164.41 -	- -	-	0/0
234	Chengalpattu-Villupuram doubling with new MM for Tambaram-Ch - [N22000202]SR,Tamil Nadu	04/2007	247.00 -	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
235	Chengannur-Chingavanam - [N22000203]SR,Kerala	04/2006	191.72 -	- -	-	0/0
236	Ernakulam-Kumbalam - [N22000204]SR,Kerala	04/2010	189.24 -	- -	-	0/0
237	New BG line from Byrnihat to Shillong - [N22000205]NEFR,Meghalaya	04/2010	4,083.02 -	- -	-	0/0
238	New BG line from Balurghat to Hilly NFR - [N22000206]NEFR,Multi State	04/2010	242.22 -	- -	-	0/0
239	New BG line from Jagbani to Biratnagar - [N22000207]NEFR,Multi State	04/2010	241.52 -	- -	-	0/0
240	Murkongselek-Pasighat NL - [N22000208]NEFR,Multi State	04/2011	165.82 -	- -	-	0/0
241	New Jalpaiguri-Siliguri-New Bongaigaon including B - [N22000209]NEFR,Multi State	04/1999	523.17 -	- -	-	0/0
242	Lumding-Hojai Patch Doubling Project - [N22000211]NEFR,Assam	04/2012	246.07 -	- -	-	0/0
243	Circular Railway including Remount Road to Santoshpur - [N22000212]MRTP,West Bengal	04/2009	573.78 -	- -	-	0/0
244	Hyderabad/Secunderabd Multi Modal Transport System(MMTS) Pha - [N22000213]MRTP,Andhra Pradesh	04/2012	632.68 -	04/2012 -	-	0/0
245	Madurai-Tuticorin via Aruppukkottai - [N22000215]SR,Multi State	04/2011	601.43 -	- -	-	0/0
246	Lakshmikantapur-Namkhana subsequently MM for Namkh - [N22000216]ER,Multi State	04/1999	406.99 -	- -	-	0/0
247	Sultanganj-Katuria via Asarganj, Tarapur And Belha - [N22000217]ER,Multi State	04/2007	450.00 -	- -	-	0/0
248	Hansnabad-Hingalgaon New BG line - [N22000218]ER,Multi State	04/2010	172.03 -	- -	-	0/0
249	Pirpainti-Jasidih - [N22000219]ER,Multi State	04/2013	915.98 -	- -	-	0/0
250	Bandel-Boinchi 3rd line - [N22000221]ER,Multi State	04/2011	288.35 -	- -	-	0/0
251	Pirpainti-Bhagalpur - [N22000222]ER,Multi State	04/2011	261.38 -	- -	-	0/0
252	Habra-Chandpara, MM for Machalandpur-Swarupnagar NL - [N22000223]ER,Multi State	04/2000	157.17 -	- -	-	0/0
253	Kalinarayanpur-Krishnanagar doubling alongwith Krishnanagar - [N22000224]ER,Multi State	04/2001	923.52 -	- -	-	0/0
254	Chinpai-Sainthia doubling, MM for Pranti-Suri, Chowrigacha-S - [N22000225]ER,Multi State	04/2005	595.91 -	- -	-	0/0
255	Kalinarayanpur-Shantipur doubling with new MM for Ranaghat-D - [N22000227]ER,Multi State	04/2010	174.56 -	- -	-	0/0
256	Sondalia-Champapur doubling with new MM for Bira-Chakia NL - [N22000228]ER,Multi State	04/2010	277.28 -	- -	-	0/0
257	Dankuni-Chandanpur 4th line, 1st phase of Dankuni-Shaktigarh - [N22000229]ER,Multi State	04/2010	296.44 -	- -	-	0/0
258	Howrah Division- Platform shelter (40 C Category stations) - [N22000230]ER,Multi State	04/2010	157.94 -	- -	-	0/0
259	Wardha-Nanded Maharashtra - [N22000231]CR,Maharashtra	04/2008	697.00 -	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
260	Kalyan-Kasara 3rd line - [N22000233]CR,Maharashtra	04/2011	277.70 -	- -	-	0/0
261	Bariarpur-Mananpurvia Kharagpur, Lachimpur-Barahat - [N22000234]ER,Multi State	04/2007	450.55 -	- -	-	0/0
262	Tarakeshwar-Magra New BG line - [N22000235]ER,Multi State	04/2010	365.17 -	- -	-	0/0
263	Hansdiha-Godda NL - [N22000236]ER,Multi State	04/2011	267.09 -	- -	-	0/0
264	Sainthia-Tarapith 3rd line - [N22000237]ER,Multi State	04/2011	193.44 -	- -	-	0/0
265	Boinchi-Shaktigarh 3rd line - [N22000238]ER,Multi State	04/2011	175.80 -	- -	-	0/0
266	New Alipur to Akra, MM for Budge Budge-Pujali NL, - [N22000240]ER,Multi State	04/2010	494.54 -	- -	-	0/0
267	Sonarpur-Canning with new MM for Kalikapur-Minakhan via Ghat - [N22000241]ER,Multi State	04/2000	297.47 -	- -	-	0/0
268	Chandpara-Bangaon doubling with extension to Chandb - [N22000242]ER,Multi State	04/2003	337.96 -	- -	-	0/0
269	Magrahat-Diamond Harbour with MM Sangrampur-Krishna - [N22000243]ER,Multi State	04/2009	493.96 -	- -	-	0/0
270	Nabadwipdham-Patuli doubling - [N22000246]ER,Multi State	04/2010	169.82 -	- -	-	0/0
271	3rd line between Bhusawal-Jalgaon - [N22000247]CR,Maharashtra	04/2011	182.06 -	- -	-	0/0
272	Santoshpur-Remount Road via Garden Reach- Metiabruze - [N22000248]ER,Multi State	04/2010	268.52 -	- -	-	0/0
273	Howrah-Development of station including segregation of aariv - [N22000249]ER,Multi State	04/2011	166.89 -	- -	-	0/0
274	Wardha-Sewagram NGP 3rd line - [N22000250]CR,Maharashtra	04/2012	297.85 -	- -	-	0/0
275	Tumkur-Chitradurga-Davengere NL - [N22000256]SWR,Karnataka	04/2011	913.00 -	- -	-	0/0
276	Munirabad (gingera) -Raichur NL - [N22000257]SWR,Karnataka	04/2007	179.65 -	- -	-	0/0
277	Bagalkot-Kudachi NL - [N22000258]SWR,Karnataka	04/2010	377.93 -	- -	-	0/0
278	Manuguru-Ramagundam - [N22000259](SCR),Andhra Pradesh	04/2013	1,112.00 -	- -	-	0/0
279	Kondapalli-Kothagudem - [N22000260](SCR),Andhra Pradesh	04/2013	723.00 -	- -	-	0/0
280	Kazipet-Vijayawada 3rd line with Electrification - [N22000261](SCR),Multi State	04/2012	1,054.35 -	- -	-	0/0
281	Akola-Khandwa GC Akola-Akot - [N22000263](SCR),Multi State	04/2008	184.26 -	- -	-	0/0
282	Bhadrachalam-Kovvur - [N22000264](SCR),Andhra Pradesh	04/2012	923.23 -	- -	-	0/0
283	Gudur-Durgarajapatnam - [N22000265](SCR),Andhra Pradesh	04/2011	283.54 -	- -	-	0/0
284	Meerut-Muzafarnagar Patch DL - [N22000267]NR,Uttar Pradesh	04/2012	289.79 -	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
285	ansa-Bhatinda Ph-1 including MM for Rama Mandi(Raman)-Maur M - [N22000268]NR,Punjab	04/2009	396.04 -	- -	-	0/0
286	Grade Seperator at Dayabasti - [N22000269]NR,Delhi	04/1999	159.20 -	- -	-	0/0
287	Faizabad-Lalganj via Akbarganj, Maharajganj and Raebareli - [N22000270]NR,Uttar Pradesh	04/2013	654.00 -	- -	-	0/0
288	Rohtak-Meham Hansi - [N22000272]NR,Haryana	04/2012	287.00 -	- -	-	0/0
289	Bhanupali-Bilaspur Beri NL - [N22000273]NR,Himachal Pradesh	04/2008	1,046.88 -	- -	-	0/0
290	Deoband (Muzaffarnagar)- Roorkee NL - [N22000274]NR,Multi State	04/2007	336.91 -	- -	-	0/0
291	Chikballa-pur-Puttaparthi-Sri Satya Sai Nilayam NL - [N22000276]SWR,Karnataka	04/2013	558.00 -	- -	-	0/0
292	Srinivasa-pura-Madanapalli NL - [N22000277]SWR,Multi State	04/2013	296.00 -	- -	-	0/0
293	Shimoga-Harihar NL - [N22000278]SWR,Karnataka	04/2011	562.74 -	- -	-	0/0
294	Rayadurga-Tumkur NL - [N22000279]SWR,Multi State	04/2007	970.34 -	- -	-	0/0
295	White Field-Kolar NL - [N22000280]SWR,Karnataka	04/2011	341.05 -	- -	-	0/0
296	Anand Vihar-Tilak Bridge 3rd and 4th line - [N22000281]NR,Delhi	04/2012	295.68 -	- -	-	0/0
297	Cumbum-Proddatur - [N22000282](SCR),Andhra Pradesh	04/2013	829.00 -	- -	-	0/0
298	Mudkhed-Parbhani - [N22000283](SCR),Maharashtra	04/2011	390.60 -	- -	-	0/0
299	Akkannapet-Medak - [N22000285](SCR),Andhra Pradesh	04/2012	153.00 -	- -	-	0/0
300	Nadikude-Sri Kalahasti - [N22000286](SCR),Andhra Pradesh	04/2011	1,313.48 -	- -	-	0/0
301	Bhadrachalam Road-Sattupalli - [N22000287](SCR),Andhra Pradesh	04/2010	337.49 -	- -	-	0/0
302	Kadapa-Bangalore (NL), Kadapa-Pendlimarri Ph-I - [N22000288](SCR),Multi State	04/2008	2,050.00 -	- -	-	0/0
303	Haridwar-Laksar - [N22000289]NR,Uttarakhand	04/2012	219.83 -	- -	-	0/0
304	Ambala Cantt-Dhapper Ph-1 with new MM of Dhapper-Chandigarh - [N22000290]NR,Multi State	04/2010	338.54 -	- -	-	0/0
305	Jakhal-Mansa Doubling on SPR Section - [N22000291]NR,Multi State	04/2008	165.65 -	- -	-	0/0
306	Hissar-Sirsa via Agroha and Fatehabad - [N22000292]NR,Haryana	04/2013	400.00 -	- -	-	0/0
307	Yamunanagar-Chandigarh via Sadhaura Narayanganr - [N22000293]NR,Multi State	04/2013	876.00 -	- -	-	0/0
308	Unchahar-Amethi - [N22000294]NR,Uttar Pradesh	04/2012	380.00 -	- -	-	0/0
309	Qadian-Beas - [N22000295]NR,Punjab	04/2011	205.22 -	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
310	Chandigarh-Baddi NL - [N22000296]NR,Multi State	04/2007	328.14 -	- -	-	0/0
311	Hospet-Hubli-Londa-Vascodagama DL - [N22000297]SWR,Karnataka	04/2010	2,127.00 -	- -	-	0/0
312	Gadag-Wadi NL - [N22000299]SWR,Karnataka	04/2013	1,117.00 -	- -	-	0/0
313	Chikballa-pur-Gowribidanur NL - [N22000300]SWR,Karnataka	04/2013	327.25 -	- -	-	0/0
314	Monigram- Nimtita - [N22000301]ER,Multi State	04/2012	250.93 -	- -	-	0/0
315	Bazar Sau -Azimganj Jn. doubling - [N22000302]ER,West Bengal	04/2012	255.64 -	- -	-	0/0
316	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,Multi State	04/1990	155.66 356.87	- 03/2010	-	0/0
317	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,Maharashtra	02/1997	353.08 514.68	- -	-	0/0
318	NANGALDAM-TALWARA(NL),NR - [220100188]NR,Multi State	03/1981	37.68 450.00	07/2012 -	-	0/0
319	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,Karnataka	04/1997	227.00 997.58	- -	-	0/0
320	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,Jharkhand	03/1999	491.19 2,957.21	07/2005 -	-	0/0
321	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]NCR,Multi State	09/1998	925.00 -	05/2008 03/2011	-	0/0
322	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,Bihar	04/1997	233.00 501.69	03/2012 08/2012	-	0/0
323	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,Bihar	04/1997	78.23 162.87	- -	-	0/0
324	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,Tamil Nadu	09/1995	100.00 100.00	- -	-	0/0
325	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,Andhra Pradesh	12/2001	330.00 1,047.00	- -	-	0/0
326	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,Karnataka	02/1999	138.00 901.62	- -	-	0/0
327	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,Bihar	04/2003	324.66 528.65	- -	-	0/0
328	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,Bihar	04/2001	104.79 -	- -	-	0/0
329	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,Madhya pradesh	04/2001	727.13 727.13	- -	-	0/0
330	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,Odisha	04/2005	726.96 810.78	- -	-	0/0
331	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,Andhra Pradesh	04/2006	378.56 671.82	- -	-	0/0
332	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-A - [N22000079]SR,Tamil Nadu	09/2007	404.19 404.19	- -	-	0/0
333	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,Tamil Nadu	09/2006	125.00 125.00	- -	-	0/0
334	TIDIVANAM-NAGARI (NL) - [N22000085]SR,Tamil Nadu	09/2006	456.00 456.00	- -	-	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
335	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) - [N22000087]NEFR,Bihar	09/2006	300.00 300.00	- -	-	0/0
336	Ratlam-Mhow-Khandwa-Akola (GC) - [N22000120]WR,Madhya pradesh	04/2008	603.04 603.04	03/2012 -	-	0/0
337	Bhuj-Naliya(GC) with extension from naliya to Vayo - [N22000123]WR,Gujarat	04/2008	318.24 -	03/2012 -	-	0/0
338	Bhavnagar-workshop facilities for 50 BG coaches PO - [N22000125]WR,Gujarat	04/2006	117.36 196.95	03/2011 -	-	0/0
339	Delhi-Sohna-Nuh-Firozpur-Jhirka-Alwar - [N22000271]NR,Multi State	04/2013	1,239.00 -	- -	-	0/0
	Total		146,842.88 -			0/0
	<u>Road Transport And Highways</u>					
340	VIJAYAPUR TO PATHANKOT (NS-35/J&K) NH-1A KM.50 TO KM.80 - [240106236]NHAI,Jammu and Kashmir	12/2003	166.27 -	03/2008 -	02/2008	0/0
341	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,West Bengal	12/2003	225.00 -	07/2008 -	03/2013	0/0
342	Armur to kadloor yellareddy - [N24000143]NHAI,Andhra Pradesh	02/2010	390.56 -	02/2012 -	06/2013	0/0
343	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	02/2004 -	09/2013	0/0
344	New 4 Lane elevated road from chennai airport - [N24000139]NHAI,Tamil Nadu	09/2010	1,655.00 -	09/2013 -	09/2013	0/0
345	Haveri-Harihar (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	08/2004 07/2010	10/2013	0/0
346	Harihar-Chitradurga (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	08/2004 -	10/2013	0/0
347	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	05/2010 -	10/2013	0/0
348	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	05/2012 -	10/2013	0/0
349	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	01/2013 -	10/2013	0/0
350	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	02/2013 -	10/2013	0/0
351	Tirupati - Chennai - [N24000178]NHAI,Tamil Nadu	04/2011	571.00 -	10/2013 -	10/2013	0/0
352	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	01/2013 -	10/2013	0/0
353	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	04/2004 -	11/2013	0/0
354	Hapur-Garhmukteswar (Others) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	09/2007 -	11/2013	0/0
355	Balasore Bhadrak (Revived) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	02/2004 -	11/2013	0/0
356	Talegaon-amravati - [N24000140]NHAI,Maharashtra	11/2009	567.00 -	11/2013 -	11/2013	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
357	ROHTAK-BAWAL - [N24000169]NHAI,Haryana	05/2011	650.00	11/2013	11/2013	0/0
358	Muzafarpur - Sonbarsa - [N24000174]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
359	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,Bihar	05/2011	511.54	11/2013	11/2013	0/0
360	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00	05/2008	12/2013	0/0
361	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00	10/2008	12/2013	0/0
362	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00	01/2009	12/2013	0/0
363	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94	09/2008	12/2013	0/0
364	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00	10/2008	12/2013	0/0
365	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00	06/2008	12/2013	0/0
366	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00	06/2008	12/2013	0/0
367	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00	05/2008	12/2013	0/0
368	LAKHNAADON TO MP/MH BORDER,KM 596.75-653 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60	06/2010	12/2013	0/0
369	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06	09/2009	12/2013	0/0
370	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00	01/2011	12/2013	0/0
371	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00	07/2012	12/2013	0/0
372	Four Lanning from MP/Maharashtra Border to nagpur - [N24000124]NHAI,Maharashtra	04/2010	1,170.52	06/2011	12/2013	0/0
373	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10	09/2012	12/2013	0/0
374	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00	05/2012	12/2013	0/0
375	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70	10/2011	12/2013	0/0
376	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75	08/2011	12/2013	0/0
377	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00	11/2011	12/2013	0/0
378	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00	04/2013	12/2013	0/0
379	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00	03/2013	12/2013	0/0
380	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00	05/2013	12/2013	0/0
381	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00	11/2012	12/2013	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
382	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	07/2013 -	12/2013	0/0
383	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	06/2013 -	12/2013	0/0
384	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	08/2013 -	12/2013	0/0
385	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171]NHAI,Tamil Nadu	06/2011	535.00 -	12/2013 -	12/2013	0/0
386	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172]NHAI,Tamil Nadu	09/2011	1,250.00 -	12/2013 -	12/2013	0/0
387	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENN - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	06/2013 -	12/2013	0/0
388	Trichy Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	05/2013 -	12/2013	0/0
389	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	03/2013 -	12/2013	0/0
390	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	07/2013 -	12/2013	0/0
391	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	08/2013 -	12/2013	0/0
392	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	02/2013 -	12/2013	0/0
393	JORBAT - BARAPANI - [N24000180]NHAI,Meghalaya	01/2011	536.00 -	01/2014 -	01/2014	0/0
394	PUNE-SHOLAPUR,Pkg-II - [N24000193]NHAI,Maharashtra	09/2011	835.00 -	01/2014 -	01/2014	0/0
395	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,Uttar Pradesh	07/2012	291.36 -	01/2014 -	01/2014	0/0
396	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	12/2012 -	02/2014	0/0
397	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	05/2013 -	02/2014	0/0
398	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,Meghalaya	02/2011	226.00 -	02/2014 -	02/2014	0/0
399	4-laning of Barhi-Hazaribagh - [N24000191]NHAI,Jharkhand	02/2012	398.00 -	02/2014 -	02/2014	0/0
400	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	09/2007 -	03/2014	0/0
401	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	09/2008 -	03/2014	0/0
402	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	06/2005 -	03/2014	0/0
403	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	06/2008 -	03/2014	0/0
404	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(2)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	06/2008 -	03/2014	0/0
405	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	10/2008 -	03/2014	0/0
406	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	04/2008 -	03/2014	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
407	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	06/2008 -	03/2014	0/0
408	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	03/2008 -	03/2014	0/0
409	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	04/2008 -	03/2014	0/0
410	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	06/2008 -	03/2014	0/0
411	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	12/2008 -	03/2014	0/0
412	AGRA-BYPASS(NS-1/UP-1),KM 176.8-13.03 NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	09/2007 -	03/2014	0/0
413	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	07/2010 -	03/2014	0/0
414	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	10/2011 -	03/2014	0/0
415	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	11/2012 -	03/2014	0/0
416	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	06/2013 -	03/2014	0/0
417	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	05/2013 -	03/2014	0/0
418	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,Multi State	09/2011	2,848.00 -	03/2014 -	03/2014	0/0
419	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,Bihar	09/2011	574.00 -	03/2014 -	03/2014	0/0
420	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	03/2013 -	03/2014	0/0
421	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	10/2013 -	03/2014	0/0
422	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	09/2007 -	04/2014	0/0
423	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	03/2013 -	04/2014	0/0
424	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	02/2014 -	04/2014	0/0
425	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,Bihar	10/2011	375.09 -	04/2014 -	04/2014	0/0
426	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,Multi State	04/2012	624.00 -	04/2014 -	04/2014	0/0
427	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	02/2009 03/2014	05/2014	0/0
428	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	04/2008 -	05/2014	0/0
429	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	07/2009 -	05/2014	0/0
430	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183]NHAI,Andhra Pradesh	11/2011	1,535.00 -	05/2014 -	05/2014	0/0
431	2laning with PS Gopalganj-Chappra - [N24000190]NHAI,Bihar	12/2011	325.00 -	05/2014 -	05/2014	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
432	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI,Odisha	11/2011	909.00 -	05/2014 -	05/2014	0/0
433	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	10/2008 -	06/2014	0/0
434	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	11/2008 -	06/2014	0/0
435	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.1) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	10/2011 -	06/2014	0/0
436	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	07/2013 -	06/2014	0/0
437	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	08/2013 -	06/2014	0/0
438	kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	07/2013 -	06/2014	0/0
439	SNG toBANL - [N24000189]NHAI,Jammu and Kashmir	06/2011	1,100.70 -	06/2014 -	06/2014	0/0
440	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,Rajasthan	12/2011	2,388.00 -	06/2014 -	06/2014	0/0
441	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205]NHAI,Multi State	12/2011	1,047.00 -	06/2014 -	06/2014	0/0
442	PANVEL-INDAPUR - [N24000216]NHAI,Multi State	12/2011	942.69 -	06/2014 -	06/2014	0/0
443	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING - [N24000153]NHAI,Karnataka	03/2011	359.00 -	09/2013 -	07/2014	0/0
444	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	07/2012 -	07/2014	0/0
445	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,West Bengal	02/2012	702.16 -	07/2014 -	07/2014	0/0
446	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,Bihar	07/2012	356.40 -	07/2014 -	07/2014	0/0
447	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,Uttar Pradesh	01/2013	373.47 -	07/2014 -	07/2014	0/0
448	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE - [N24000108]NHAI,Multi State	12/2003	232.45 -	09/2010 -	08/2014	0/0
449	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	06/2009 -	09/2014	0/0
450	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	09/2009 -	09/2014	0/0
451	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,West Bengal	04/2012	1,396.18 -	09/2014 -	09/2014	0/0
452	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,Gujarat	03/2012	828.00 -	09/2014 -	09/2014	0/0
453	REENGUS SIKAR - [N24000227]NHAI,Rajasthan	03/2012	333.51 -	09/2014 -	09/2014	0/0
454	PANIPAT-ROHTAK - [N24000151]NHAI,Haryana	04/2011	807.00 -	10/2014 -	10/2014	0/0
455	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,Maharashtra	04/2012	484.19 -	10/2014 -	10/2014	0/0
456	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,Uttar Pradesh	10/2012	250.50 -	10/2014 -	10/2014	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
457	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,Madhya pradesh	10/2011	1,565.00 -	10/2014 -	10/2014	0/0
458	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	04/2009 -	12/2014	0/0
459	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	11/2008 -	12/2014	0/0
460	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	04/2009 -	12/2014	0/0
461	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	04/2010 -	12/2014	0/0
462	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	12/2009 -	12/2014	0/0
463	NH CONNECTIVITY TO ICTT VALLARPADAUE NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	02/2010 -	12/2014	0/0
464	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	01/2014 -	12/2014	0/0
465	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	09/2013 -	12/2014	0/0
466	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	08/2013 -	12/2014	0/0
467	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	08/2013 -	12/2014	0/0
468	Dindigul - Kumli - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	08/2013 -	02/2015	0/0
469	BARSAT-KRISHNANAGAR - [N24000229]NHAI,West Bengal	08/2012	867.00 -	02/2015 -	02/2015	0/0
470	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION - [N24000149]NHAI,Kerala	02/2010	617.00 -	08/2012 -	03/2015	0/0
471	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,Multi State	10/2012	1,928.22 -	04/2015 -	04/2015	0/0
472	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI,Multi State	12/2012	1,479.00 -	06/2015 -	06/2015	0/0
473	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	02/2010 -	07/2015	0/0
474	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	08/2014 -	07/2015	0/0
475	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,Multi State	02/2013	1,232.00 -	08/2015 -	08/2015	0/0
476	ETAWAH CHAKERI - [N24000219]NHAI,Uttar Pradesh	03/2013	1,573.00 -	09/2015 -	09/2015	0/0
477	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	09/2014 -	10/2015	0/0
478	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	10/2013 -	11/2015	0/0
479	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,Tamil Nadu	06/2013	1,287.95 -	11/2015 -	11/2015	0/0
480	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	08/2013 -	12/2015	0/0
481	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,Gujarat	01/2013	2,125.24 -	12/2015 -	12/2015	0/0

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
482	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	06/2015 -	05/2016	0/0
483	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	07/2015 -	06/2016	0/0
	Total		100,698.72 -			0/0
	<u>Shipping And Ports</u>					
484	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUS - [N25000059]RVNL,Kerala	03/2007	245.67 298.17	04/2009 11/2009	02/2011	0/0
485	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY - [N25000014]SHIPP.,Maharashtra	10/2007	359.44 -	04/2011 11/2011	11/2011	0/0
486	Modification & Strengthening of Existing Berth No. 1 to 6 - [N25000050]PORT TRUST,Gujarat	06/2010	277.00 -	03/2012 -	03/2012	0/0
487	Acquisition of Two nos. of 3060 DWT - [N25000043]SHIPP.,Maharashtra	04/2009	277.03 280.00	12/2011 10/2012	10/2012	0/0
488	Mechanization of coal handling facilities to 200 - [N25000049]PORT TRUST,Andhra Pradesh	02/2010	444.10 -	06/2010 -	11/2012	0/0
489	Construction of berthing and allied facilities off - [N25000037]PORT TRUST,Gujarat	04/2005	882.00 -	02/2011 -	12/2012	0/0
490	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,Gujarat	12/2005	702.00 -	03/2011 -	03/2013	0/0
491	Setting up of Single Point Mooring (SPM) and allie - [N25000060]PORT TRUST,Gujarat	02/2011	830.00 -	05/2013 -	05/2013	0/0
492	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,Multi State	07/2011	220.49 -	01/2013 06/2013	06/2013	0/0
493	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHU - [N25000048]PORT TRUST,Kerala	03/2009	3,500.00 4,150.00	01/2012 09/2012	08/2013	0/0
494	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051]SHIPP.,Maharashtra	08/2010	612.72 532.83	12/2012 11/2013	11/2013	0/0
495	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052]SHIPP.,Maharashtra	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013	0/0
496	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035]PORT TRUST,Tamil Nadu	10/2002	150.00 309.00	03/2006 12/2013	12/2013	0/0
497	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053]SHIPP.,Maharashtra	10/2010	966.46 -	02/2014 -	02/2014	0/0
498	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062]SHIPP.,Multi State	01/2012	511.87 -	03/2014 08/2014	08/2014	0/0
499	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TER - [N25000016]MUMBAI PORT TRU,Maharashtra	11/2007	1,228.00 1,460.00	12/2010 09/2012	12/2014	0/0
500	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,Tamil Nadu	06/2005	2,427.40 -	10/2008 11/2010	-	0/0
501	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL A - [N25000003]PORT TRUST,Maharashtra	10/2005	800.00 1,571.60	10/2008 -	-	0/0
	Total		15,462.28 -			0/0
	<u>Telecommunications</u>					

			(Sep,2013)			
				Date of Commissioning		
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
502	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) - [N26000041]BSNL,Punjab	02/2008	373.94 -	12/2008 -	12/2012	0/0
503	GSM equipment of 799000Lines (2G) 101000 lines 3(G - [N26000088]BSNL,Jharkhand	03/2008	328.13 -	03/2009 -	01/2013	0/0
504	CONVERGENT BILLING AND CRM-MTNL(DELHI) - [N26000011]MTNL,Delhi	12/2005	249.00 -	02/2007 03/2012	02/2013	0/0
505	GSM equipment of 1625000Lines (2G) 325000 lines 3(- [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	11/2010 12/2012	09/2013	0/0
506	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 992 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	10/2007 -	12/2013	0/0
507	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	06/2009 -	12/2013	0/0
508	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	01/2009 -	12/2013	0/0
509	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	10/2010 03/2012	12/2013	0/0
510	Supply Installation testing and commissioning of Rural Wimax - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	05/2011 -	12/2013	0/0
511	CONVERGENT BILLING AND CRM(MUMBAI) - [N26000016]MTNL,Maharashtra	01/2006	247.00 -	02/2007 12/2010	-	0/0
512	Implementation of FTTH, the state of the art access ,gpon eq - [N26000072]BSNL,Multi State	12/2007	952.88 -	03/2010 -	-	0/0
513	Implementation of FTTH, the state of the art Acces - [N26000073]BSNL,Multi State	12/2007	152.65 -	03/2010 -	-	0/0
514	DELHI CONVERGENT BILLING AND CRM PE-5834 - [N26000099]MTNL,Delhi	02/2006	229.41 -	03/2012 02/2013	-	0/0
	Total		5,699.24 -			0/0
	<u>Urban Development</u>					
515	FARIDABAD EXTENSION - [N28000057]DMRC,Delhi	09/2011	2,494.00 -	09/2014 -	05/2015	0/0
516	DELHI MRTS PHASE-III - [N28000056]DMRC,Delhi	09/2011	35,242.00 -	03/2016 -	03/2016	0/0
517	C/o office building for IDBI at bandra Kurla Compl - [N28000048]CPWD,Maharashtra	11/2006	114.18 173.08	04/2009 -	-	0/0
	Total		37,850.18 -			0/0
	<u>Water Resources</u>					
518	PAGLADIYA DAM PROJECT - [300100001]MoWR,Assam	01/2001	542.90 -	12/2007 -	12/2012	0/0
	Total		542.90 -			0/0
	Grand Total		411,905.96			0/0

List of Projects on schedule w.r.t. Latest Schedule

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Civil Aviation</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MO - [N04000070	2/2011	452.00 -	452.00	145.42	03/2015 -	03/2015
2	SUPPLY OF 56 Nos AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071	10/2012	217.60 -	217.60	0.02	03/2015 -	03/2015
	Total		669.60 -	669.60	145.44		
	<u>Coal</u>						
3	BLOCK-B OCP NCL (3.5 MTY) - [N06000009	6/2011	746.04 -	535.10	161.60	03/2015 -	03/2015
4	BINA EXTN. PROJ(6.0 Mtpa) - [N06000019	11/2006	168.97 -	168.97	45.02	03/2014 -	03/2014
5	GOPAL PRASAD OCP (15MTY) - [N06000042	2/2008	395.87 -	395.87	72.34	03/2015 -	03/2015
6	PELMA OCP(10.00MTY) - [N06000045	7/2008	448.32 -	448.32	-	03/2015 -	03/2015
7	RKP OCP PHASE-I - [N06000079	3/2010	209.78 -	209.78	51.42	03/2015 -	03/2015
8	Rajrappa RCE OCP (3.0 MTY) - [N06000087	12/2009	510.85 -	510.85	265.56	03/2016 -	03/2016
9	Kistaram OCP - [N06000089	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
10	RFR OF MANUGURU OC PROJECT - [N06000102	11/2012	430.14 -	430.14	58.90	03/2016 -	03/2016
11	KALYANIKHANI OPENCAST PROJECT - [N06000101	7/2012	417.33 -	417.33	0.09	07/2016 -	07/2016
12	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100	6/2012	365.01 -	365.01	-	06/2015 -	06/2015
13	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099	4/2012	258.56 -	258.56	52.65	03/2016 -	03/2016
14	Moonidih XV Seam UG - [N06000098	8/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2015
15	Muraidih UG - [N06000096	2/2011	339.88 -	339.88	-	04/2014 -	04/2014
16	JALAGAM VENGALA RAO OCP-II - [N06000094	7/2011	447.06 -	447.06	14.03	03/2015 -	03/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	7/2011	162.76 -	162.76	2.56	03/2015 -	03/2015
18	KHADIA EXPANSION OPENCAST PROJECT 4 TO 10 MTPA,6MT - [N06000091	6/2011	1,131.28 -	1,131.28	4.92	03/2018 -	03/2018
19	AMRAPALI OC - [N06000103	2/2012	858.11 -	858.11	49.40	03/2020 -	03/2020

(Sep,2013)

						Date of Commissioning	
SI.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
20	KARMA OCP (1.0MTY) - [N06000088	6/2009	162.46 -	162.46	40.81	03/2014 -	03/2014
21	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082	11/2009	150.59 -	198.59	89.92	03/2016 -	03/2016
22	Batura OCP (2.0 MTY) - [N06000049	9/2008	203.82 -	203.82	-	03/2015 -	03/2015
23	TALABIRA OCP - [N06000043	3/2008	447.72 -	447.72	44.33	03/2016 -	03/2016
24	BHUBANESWARI OCP, MCL (20.0 Mty) - [N06000034	12/2007	490.00 -	490.10	151.06	03/2017 -	03/2017
25	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010	12/2009	1,352.04 -	1,143.54	579.32	03/2016 03/2016	03/2016
	Total		11,169.15 -	10,797.81	1,683.93		
	<u>Petrochemicals</u>						
26	ASSAM GAS CRACKER PROJECT - [N16000106	4/2006	5,460.61 -	8,920.00	4,510.51	04/2012 12/2013	12/2013
	Total		5,460.61 -	8,920.00	4,510.51		
	<u>Petroleum</u>						
27	Wax Project - [N16000101	6/2010	576.60 -	576.60	306.39	12/2013 -	12/2013
28	Purchase of 2 Nos. of 2000 HP Drilling Rig - [N16000165	4/2010	270.00 -	270.00	-	12/2014 -	12/2014
29	Reconstruction of BPA and BPB Platforms - [N16000161	3/2013	1,138.50 -	1,138.50	-	04/2015 -	04/2015
30	Integrated Development of Bassein Field - [N16000160	12/2012	3,513.07 -	3,513.07	-	02/2016 -	02/2016
31	Pipeline Replacement Project, Ahmedabad - [N16000159	9/2011	202.25 -	160.16	-	07/2016 -	07/2016
32	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	309.82	48.71	10/2014 -	10/2014
33	Mounded Bullet - [N16000154	12/2012	279.00 -	279.00	4.87	12/2014 -	12/2014
34	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148	2/2011	913.00 -	913.00	37.26	07/2015 -	07/2015
35	DBPL-II - [N16000147	6/2009	486.00 -	486.00	61.61	09/2013 -	09/2013
36	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	16.56	11/2015 -	11/2015
37	REWARI KANPUR PIPELINE PROJECT - [N16000145	2/2012	1,210.64 -	1,210.64	281.76	11/2015 -	11/2015
38	Replacement of CDU/VDU at Mumbai Refinery - [N16000142	1/1999	1,419.00 -	1,419.00	134.21	12/2014 -	12/2014
39	Butene-1 at Panipat - [N16000139	2/2012	190.00 -	190.00	80.85	03/2014 -	03/2014

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
40	Pipeline Replacement Project-3 - [N16000137	4/2012	2,547.26 -	1,417.00	515.24	05/2014 -	05/2014
41	Development of Western Periphery of MH South Field - [N16000136	4/2012	600.17 -	600.17	99.87	12/2014 -	12/2014
42	Construction of three ETPs, Mehsana - [N16000135	3/2012	260.74 -	260.74	0.52	11/2014 -	11/2014
43	Construction of one ETP at GGS-NADA, Ankleshwar - [N16000134	10/2011	200.69 -	200.69	3.03	07/2014 -	07/2014
44	Development of C-26 Cluster Fields - [N16000133	3/2012	2,592.17 -	2,592.17	26.61	05/2014 -	05/2014
45	Heera and South Heera Redevelopment Ph-II - [N16000132	3/2012	5,608.40 -	5,608.40	1,278.32	05/2015 -	05/2015
46	Integrated Development of B-127 fields - [N16000131	12/2011	2,059.63 -	2,665.65	289.05	03/2015 -	03/2015
47	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112	8/2010	8,140.00 -	8,140.00	5,177.12	02/2014 -	02/2014
48	Development of Cluster-7 Fields - [N16000104	3/2010	3,241.03 -	6,638.94	1,451.42	03/2013 11/2014	11/2014
	Total		36,423.96 -	39,290.55	9,813.40		
	<u>Power</u>						
49	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA - [N18000101	5/2011	1,961.87 -	1,961.87	1,131.45	05/2014 -	05/2014
50	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109	10/2011	487.49 -	487.49	203.81	06/2014 -	06/2014
51	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNA - [N18000111	8/2011	1,637.34 -	1,637.34	937.10	08/2014 -	08/2014
52	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL P - [N18000107	8/2011	1,391.97 -	1,391.97	1,059.23	12/2013 -	12/2013
53	Common System Associated with Coastal Energen Priv - [N18000103	9/2011	1,940.13 -	1,940.13	1,040.50	09/2014 -	09/2014
54	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR - [N18000112	11/2011	2,127.51 -	2,127.51	1,186.02	07/2014 -	07/2014
55	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT - [N18000114	12/2011	552.44 -	552.44	329.39	02/2014 -	02/2014
56	SOLAPUR STPP - [N18000133	3/2012	9,395.18 -	9,395.18	1,653.00	11/2016 -	11/2016
57	MOUDA STPP STAGE 2 - [N18000132	3/2012	7,921.47 -	7,921.47	1,194.00	09/2016 -	09/2016
58	KUDGI STPP STAGE 1 - [N18000131	12/2011	15,166.19 -	15,166.19	1,845.00	12/2016 -	12/2016
59	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130	6/2012	1,263.26 -	1,263.26	282.68	11/2014 -	11/2014
60	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128	11/2011	723.63 -	723.63	195.23	11/2014 -	11/2014
61	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127	12/2011	901.77 -	901.77	377.02	08/2014 -	08/2014

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
62	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA - [N18000126	3/2012	206.44 -	206.44	41.42	06/2014 -	06/2014
63	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125	3/2012	9,569.76 -	9,569.76	872.60	06/2015 -	06/2015
64	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BA - [N18000124	3/2012	213.78 -	213.78	-	03/2014 -	03/2014
65	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & - [N18000145	6/2012	1,909.24 -	1,909.24	195.81	06/2015 -	06/2015
66	COMMON SYS. ASSOCIATED PART- B - [N18000144	3/2013	2,514.88 -	2,514.88	-	12/2015 -	12/2015
67	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC - [N18000143	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
68	Lata-Tapovan HPP 3x57MW - [N18000142	7/2012	1,527.00 -	1,527.00	113.03	08/2017 -	08/2017
69	LARA STPP STAGE-I - [N18000140	11/2012	11,846.00 -	11,846.00	1,115.00	05/2017 -	05/2017
70	COMMON TRANSMISSION SCHEME WITH ISSG - [N18000139	1/2013	182.80 -	182.80	3.60	10/2014 -	10/2014
71	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138	12/2012	156.04 -	156.04	-	10/2014 -	10/2014
72	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136	9/2012	803.34 -	803.34	105.74	03/2015 -	03/2015
73	VINDHYACHAL STPP STAGE-V - [N18000134	12/2011	3,180.40 -	3,180.40	503.00	08/2015 -	08/2015
74	Transmission System associated with Mauda Stage-II - [N18000153	9/2013	1,575.30 -	1,575.30	-	05/2016 -	05/2016
75	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152	9/2013	680.69 -	680.69	-	03/2016 -	03/2016
76	Gadarwara Super Thermal Power Project Stage-I - [N18000151	2/2013	11,638.55 -	11,638.55	687.00	09/2017 -	09/2017
77	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHER - [N18000123	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
78	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000122	2/2012	1,927.16 -	1,927.16	444.72	10/2014 -	10/2014
79	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART - [N18000121	2/2012	324.33 -	324.33	19.57	08/2014 -	08/2014
80	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP P - [N18000120	2/2012	1,310.85 -	1,310.85	464.56	02/2015 -	02/2015
81	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT - [N18000118	1/2012	259.28 -	259.28	111.93	01/2014 -	01/2014
82	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJEC - [N18000117	1/2012	1,422.85 -	1,422.85	432.96	01/2015 -	01/2015
83	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR - [N18000116	12/2011	1,746.65 -	1,746.65	174.49	08/2014 -	08/2014
84	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115	12/2011	297.33 -	297.33	144.01	08/2014 -	08/2014
85	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARK - [N18000113	12/2011	2,422.66 -	2,422.66	520.74	08/2014 -	08/2014

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		101,898.41 -	101,898.41	17,384.61		
	<u>Railways</u>						
86	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	4/1998	183.23 -	818.29	105.60	02/2015 -	02/2015
87	New Work for Construction of Metro railway from NS - [N22000110	4/2010	3,951.98 -	3,951.98	187.23	03/2016 -	03/2016
88	New Work for Construction of Metro railway from Ba - [N22000109	4/2010	2,069.60 -	2,069.60	25.21	03/2014 -	03/2014
89	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088	4/2006	325.00 -	1,116.53	231.10	03/2010 03/2017	03/2017
90	New Work for Construction of Metro railway - [N22000111	4/2010	2,619.02 -	2,619.02	332.96	03/2016 -	03/2016
91	Jaipur - Ringus - Churu and Sikar - Loharu Guage C - [N22000113	4/2008	653.19 -	653.47	248.21	03/2014 -	03/2014
92	Ghutiasharif-Canning (ER) - [N22000117	4/2009	189.97 -	611.03	130.62	12/2011 11/2013	11/2013
93	Katwa-Patuli doubling with new MM for Ahmedpur-Katwa GC - [N22000245	4/2010	423.66 -	423.66	136.58	03/2017 -	03/2017
94	Liluah-Dankuni 3rd line, MM for Dankuni-Jongalpara-Furfura S - [N22000244	4/2009	257.42 -	257.42	33.39	03/2014 -	03/2014
95	Princepghat-Majerhat Doubling of Circular Railway - [N22000239	4/2011	299.60 -	299.60	1.09	03/2017 -	03/2017
96	Plassey-Jiaganj Doubling - [N22000220	4/2011	248.07 -	248.07	9.83	03/2015 -	03/2015
97	Dangoaposi-Rajkharwan 3rd line Doubling - [N22000164	4/2010	309.44 -	388.67	42.55	12/2015 -	12/2015
98	Dholpur-Sirmuttra with extension to Gangapurcity A - [N22000158	4/2010	622.41 -	2,030.50	1.22	02/2019 -	02/2019
99	Gwalior-Seopurkala with extension to Kota (GC) - [N22000148	4/2011	1,176.09 -	3,845.60	1.71	02/2020 -	02/2020
100	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	4,874.58	-	03/2016 -	03/2016
101	Udhna-Jalgaon with electrification(doubling) (WR) - [N22000122	4/2008	1,389.62 -	1,389.62	675.23	03/2014 -	03/2014
102	Suratpura - Hanumangarh - Sriganganagar Guage Conv - [N22000114	4/2008	516.23 -	516.23	420.70	03/2014 -	03/2014
103	Himmatnagar - Udaipur Gauge Conversion (NWR) - [N22000112	4/2008	829.74 -	829.74	35.38	03/2015 -	03/2015
	Total		20,938.85 -	26,943.61	2,618.61		
	<u>Road Transport And Highways</u>						
104	New 4 Lane elevated road from chennai airport - [N24000139	9/2010	1,655.00 -	1,655.00	393.70	09/2013 -	09/2013
105	Talegaon-amravati - [N24000140	11/2009	567.00 -	567.00	1,166.00	11/2013 -	11/2013

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
106	PANIPAT-ROHTAK - [N24000151	4/2011	807.00 -	807.00	1,318.00	10/2014 -	10/2014
107	ROHTAK-BAWAL - [N24000169	5/2011	650.00 -	650.00	1,119.00	11/2013 -	11/2013
108	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM. - [N24000172	9/2011	1,250.00 -	1,250.00	16.15	12/2013 -	12/2013
109	Tirupati - Chennai - [N24000178	4/2011	571.00 -	571.00	-	10/2013 -	10/2013
110	BARSAT-KRISHNANAGAR - [N24000229	8/2012	867.00 -	867.00	-	02/2015 -	02/2015
111	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228	6/2013	1,287.95 -	1,287.95	-	11/2015 -	11/2015
112	REENGUS SIKAR - [N24000227	3/2012	333.51 -	333.51	236.80	09/2014 -	09/2014
113	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226	10/2011	1,565.00 -	1,565.00	691.40	10/2014 -	10/2014
114	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225	3/2012	828.00 -	828.00	490.60	09/2014 -	09/2014
115	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224	10/2012	1,928.22 -	1,928.22	302.60	04/2015 -	04/2015
116	AHMEDABAD TO VADODARA SECTION - [N24000222	1/2013	2,125.24 -	2,125.24	34.28	12/2015 -	12/2015
117	2 LANING WITH PS KANPUR KABRAI - [N24000221	1/2013	373.47 -	373.47	40.66	07/2014 -	07/2014
118	2 LANING WITH PS AGRA ALIGARH - [N24000220	10/2012	250.50 -	250.50	230.10	10/2014 -	10/2014
119	ETAWAH CHAKERI - [N24000219	3/2013	1,573.00 -	1,573.00	17.23	09/2015 -	09/2015
120	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218	2/2013	1,232.00 -	1,232.00	252.60	08/2015 -	08/2015
121	PANVEL-INDAPUR - [N24000216	12/2011	942.69 -	942.69	198.50	06/2014 -	06/2014
122	RANCHI-RARGA-JAMSETHPUR - [N24000215	12/2012	1,479.00 -	1,479.00	227.90	06/2015 -	06/2015
123	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213	4/2012	624.00 -	624.00	314.70	04/2014 -	04/2014
124	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211	7/2012	356.40 -	356.40	-	07/2014 -	07/2014
125	2laning with PS Gopalganj-Chappra - [N24000190	12/2011	325.00 -	325.00	161.20	05/2014 -	05/2014
126	SNG toBANL - [N24000189	6/2011	1,100.70 -	1,100.70	-	06/2014 -	06/2014
127	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188	5/2011	511.54 -	511.54	642.20	11/2013 -	11/2013
128	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	174.40	04/2014 -	04/2014
129	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	655.30	03/2014 -	03/2014

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
130	SIX LANNING OF NELLORE-CHILKALURIPET - [N24000183	11/2011	1,535.00 -	1,535.00	1,218.00	05/2014 -	05/2014
131	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	2,848.00	921.30	03/2014 -	03/2014
132	2-LANNING OF SHILONG BYPASS - [N24000181	2/2011	226.00 -	226.00	189.10	02/2014 -	02/2014
133	JORBAT - BARAPANI - [N24000180	1/2011	536.00 -	536.00	518.00	01/2014 -	01/2014
134	NAGPUR-WAINGANGA BRIDGE - [N24000210	4/2012	484.19 -	484.19	282.80	10/2014 -	10/2014
135	KRISHNANAGAR-BERHAMPUR - [N24000209	2/2012	702.16 -	702.16	498.90	07/2014 -	07/2014
136	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208	7/2012	291.36 -	291.36	98.48	01/2014 -	01/2014
137	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206	4/2012	1,396.18 -	1,396.18	1,048.00	09/2014 -	09/2014
138	six laning of Chandikhol-Jagatpur-Bhubaneswar - [N24000205	12/2011	1,047.00 -	1,047.00	202.40	06/2014 -	06/2014
139	BEAWAR-PALI-PINDWARA - [N24000199	12/2011	2,388.00 -	2,388.00	1,388.00	06/2014 -	06/2014
140	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196	11/2011	909.00 -	909.00	941.90	05/2014 -	05/2014
141	PUNE-SHOLAPUR,Pkg-II - [N24000193	9/2011	835.00 -	835.00	388.20	01/2014 -	01/2014
142	4-laning of Barhi-Hazaribagh - [N24000191	2/2012	398.00 -	398.00	441.10	02/2014 -	02/2014
143	Muzafarpur - Sonbarsa - [N24000174	5/2011	511.54 -	511.54	65.78	11/2013 -	11/2013
144	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO - [N24000171	6/2011	535.00 -	535.00	-	12/2013 -	12/2013
	Total		38,794.74 -	38,794.74	16,885.28		
	<u>Shipping And Ports</u>						
145	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHI - [N25000035	10/2002	150.00 -	600.00	139.80	03/2006 12/2013	12/2013
146	Acquisition of 4 nos of 82000 DWT kamsavmax Bulk carriers - [N25000051	8/2010	612.72 -	532.83	448.43	12/2012 11/2013	11/2013
147	Acquisition of three(3) nos of 6500TEU Cellular container - [N25000052	10/2010	1,028.10 -	1,012.23	554.60	12/2013 11/2013	11/2013
148	Acquisition of two(2) Nos. of 317000 DWT very large crude - [N25000053	10/2010	966.46 -	994.82	363.20	02/2014 -	02/2014
149	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPL - [N25000062	1/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014
	Total		3,269.15 -	3,651.75	1,612.75		
	<u>Steel</u>						

(Sep,2013)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
150	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072	4/2011	572.00 -	572.00	327.46	04/2013 12/2013	12/2013
151	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073	2/2011	898.55 -	898.55	222.75	05/2013 03/2014	03/2014
152	Cold repair of Coke Oven Battery-9 at BSP, Bhilai, chhattisga - [N12000078	7/2012	332.65 -	332.65	-	08/2014 -	08/2014
153	Rebuilding of Coke Oven Battery-3 at RSP, Rourkela, Oddisha - [N12000079	1/2012	254.90 -	254.90	3.54	12/2014 -	12/2014
154	Coke Oven Battery-5 - [N12000080	3/2012	339.35 -	339.35	12.59	06/2015 -	06/2015
	Total		2,397.45 -	2,397.45	566.34		
	<u>Urban Development</u>						
155	DELHI MRTS PHASE-III - [N28000056	9/2011	35,242.00 -	35,242.00	3,853.30	03/2016 -	03/2016
	Total		35,242.00 -	35,242.00	3,853.30		
	Grand Total		256,263.92	268,605.92	59,074.17		

List of Projects Ahead of Schedule w.r.t. Latest Schedule

(Sep,2013)							
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Petroleum</u>						
1	IOR LAKWA - LAKHMANI (ONGCL) - [160100215	9/2001	345.10 663.69	750.00	729.07	03/2007 03/2014	09/2013
2	IOR GELEKI (ONGCL) - [160100216	9/2001	390.09 1,674.11	1,674.11	1,727.24	03/2007 03/2017	12/2013
	Total		735.19 -	2,424.11	2,456.31		
	<u>Power</u>						
3	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144	9/2012	1,508.74 -	1,508.74	76.61	06/2016 -	04/2015
	Total		1,508.74 -	1,508.74	76.61		
	<u>Petroleum</u>						
4	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149	8/2011	586.00	586.00	74.77	08/2015 -	07/2015
	Total		586.00 -	586.00	74.77		
	<u>Power</u>						
5	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART- - [N18000129	2/2012	3,201.44 -	3,201.44	981.51	10/2014 -	09/2014
6	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137	9/2012	1,935.35 -	1,935.35	271.58	12/2014 -	11/2014
	Total		5,136.79 -	5,136.79	1,253.09		
	Grand Total		7,966.72	9,655.64	3,860.78		

List of Delayed Projects w.r.t. Latest Schedule

(Sep,2013)									
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>Atomic Energy</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,Tamil Nadu	12/2001	13,171.00 17,270.00	17,270.00	16,485.00	12/2008 -	06/2014	66	-
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,Tamil Nadu	09/2003	3,492.00 -	5,677.00	4,681.60	09/2010 -	03/2015	54	-
3	KAKRAPAR ATOMIC POWER PROJECT - 3 and 4 - [N02000010]NPCIL,Gujarat	10/2009	11,459.00 -	11,459.00	3,088.00	12/2015 -	11/2016	11	-
4	RAJASTHAN ATOMIC POWER PROJECT -7 and 8 (2X700 MW) - [N02000027]NPCIL,Rajasthan	10/2009	12,320.00 -	12,320.00	2,119.00	12/2016 -	03/2017	3	-
	Total		40,442.00 -	46,726.00	26,373.60				
	<u>Civil Aviation</u>								
5	Construction of New International Terminal Building(Goa) - [N04000069]AAI,Goa	05/2010	335.61 -	335.61	244.70	05/2012 -	11/2013	18	-
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,Multi State	02/2010	344.28 -	344.28	-	03/2014 -	06/2014	3	-
7	C/o New Airport at Pakyong(Sikkim) Airport - [N04000050]AAI,Sikkim	01/2009	309.46 -	309.46	231.71	01/2011 04/2013	03/2015	50	23
	Total		989.35 -	989.35	476.41				
	<u>Coal</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,Tamil Nadu	10/2004	2,030.78 3,027.59	3,027.59	2,783.98	06/2009 -	01/2014	55	-
9	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,Odisha	01/2005	302.96 -	302.96	115.30	03/2010 -	03/2014	48	-
10	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,Jharkhand	12/2007	471.66 341.63	341.63	108.85	03/2011 -	03/2014	36	-
11	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,Uttar Pradesh	06/2011	789.88 -	741.62	374.23	03/2013 -	03/2014	12	-
12	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,Tamil Nadu	05/2008	4,904.54 6,540.93	6,540.93	4,689.91	03/2012 -	03/2014	24	-
13	ANANTA OC EXPANSION PH-III (15.0 Mty) - [N06000067]MCL,Odisha	08/2008	207.28 -	207.28	115.88	03/2012 -	03/2014	24	-
14	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,Andhra Pradesh	12/2009	212.34 779.26	977.53	802.36	03/2013 09/2012	10/2014	19	25
15	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL, Madhya pradesh	10/2007	259.40 -	259.40	6.98	03/2012 -	03/2015	36	-
16	KANIHA OCP, MCL, (10.0 Mty) - [N06000035]MCL,Odisha	12/2007	457.77 -	457.77	112.85	03/2013 -	03/2015	24	-
17	BALRAM OCP EXTENSION,MCL 8.00 Mty - [N06000044]MCL,Odisha	12/2007	172.08 -	172.08	124.85	03/2010 -	03/2015	60	-
18	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,Odisha	11/2008	479.63 -	479.63	116.91	03/2013 -	03/2015	24	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
19	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,Andhra Pradesh	03/2010	181.19 -	181.19	34.67	03/2012 -	03/2015	36	-
20	Purnadih OCP (3.0 MTY) - [N06000085]CCL,Jharkhand	07/2008	210.98 -	210.98	89.33	03/2013 -	03/2015	24	-
21	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,Chhatisgarh	06/2010	2,675.67 -	2,675.67	1,422.40	03/2014 -	03/2016	24	-
22	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,Chhatisgarh	12/2009	1,943.66 -	1,943.66	1,271.75	03/2014 -	03/2016	24	-
23	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,Jharkhand	08/2008	469.78 -	706.40	27.60	07/2012 -	03/2016	44	-
24	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,Chhatisgarh	06/2008	462.35 -	462.35	267.52	03/2014 -	03/2016	24	-
25	KAKATIYA LONGWALL - [N06000048]SCCL,Andhra Pradesh	12/2008	453.63 -	453.63	91.60	12/2012 -	03/2016	39	-
26	RAJMAHAL OC EXP. - [N06000056]ECL,Jharkhand	09/2009	153.82 -	153.82	19.29	03/2014 -	03/2016	24	-
27	PENGANGA OC - [N06000066]WCL,Maharashtra	10/2008	339.77 -	339.77	1.23	03/2014 -	03/2016	24	-
28	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,Chhatisgarh	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	-
29	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,Chhatisgarh	12/2009	321.42 -	321.50	209.96	03/2014 -	03/2016	24	-
30	Churi Benti UG (0.81 MTY) - [N06000083]CCL,Jharkhand	08/2007	163.51 -	163.51	35.12	03/2011 -	03/2016	60	-
31	Tapin OCP (2.5 MTY) - [N06000086]CCL,Jharkhand	08/2008	264.68 -	264.68	138.21	03/2012 -	03/2016	48	-
32	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,West Bengal	11/2006	287.18 -	287.17	4.74	03/2011 -	03/2017	72	-
33	JAGANNATHPOR OC - [N06000075]SECL,Chhatisgarh	09/2008	152.43 -	152.43	-	03/2015 -	03/2017	24	-
34	North Urimari OCP (3.0 MTY) - [N06000084]CCL,Jharkhand	12/2007	179.87 -	179.87	61.20	03/2012 -	03/2017	60	-
35	NEYVELI NEW THERMAL POWER PROJECT(2x500 MW) - [N06000095]NLC,Tamil Nadu	06/2011	5,907.11 -	5,907.11	34.04	12/2015 -	02/2018	26	-
	Total		24,633.81 -	28,090.60	13,060.76				
	<u>Steel</u>								
36	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,Andhra Pradesh	10/2005	8,692.00 12,291.00	12,291.00	10,554.63	10/2009 10/2012	10/2013	48	12
37	67.5 MW TG-5 AUX. STEM EMERGENCY POWER REQUIREMENT EXP. UNIT - [N12000068]RINL,Andhra Pradesh	07/2007	230.00 343.58	343.58	280.63	02/2011 02/2011	10/2013	32	32
38	Bailadila Iron Ore Project Deposit- 11B (NMDC) - [N12000018]NMDC,Chhatisgarh	01/2007	295.89 607.17	607.17	354.04	12/2011 03/2012	12/2013	24	21
39	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,Andhra Pradesh	08/2007	108.00 216.68	216.68	152.61	10/2012 10/2012	12/2013	14	14
40	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL,West Bengal	02/2008	14,443.00 -	16,408.00	15,038.24	12/2011 -	12/2013	24	-
41	Augmentation of Iron Ore Storage in RMHP - [N12000053]RINL,Multi State	05/2008	480.00 -	450.00	283.63	05/2012 05/2012	12/2013	19	19

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
42	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,Jharkhand	01/2008	6,325.00 -	6,325.00	3,779.97	12/2011 -	12/2013	24	-
43	Expansion of Rourkela Steel Plant - [N12000056]SAIL,Odisha	09/2008	11,812.00 -	11,812.00	9,933.09	03/2013 -	12/2013	9	-
44	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,West Bengal	06/2009	2,875.00 -	2,875.00	1,841.57	12/2012 -	03/2014	15	-
45	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,Maharashtra	12/2011	187.33 -	187.33	95.71	10/2013 -	06/2014	8	-
46	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,Chhatisgarh	09/2008	17,265.00 -	17,265.00	10,590.79	03/2013 -	09/2014	18	-
47	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,Odisha	11/2011	254.55 -	254.55	74.38	11/2013 -	06/2015	19	-
	Total		62,967.77 -	69,035.31	52,979.29				
	<u>Petroleum</u>								
48	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY - [N16000069]HPCL,Maharashtra	03/2009	3,284.00 2,174.00	2,174.00	1,459.18	09/2011 05/2012	09/2013	24	16
49	HYDROCRACKER REVAMP AND SETTING UP A NEW CCR AT MUMBAI REFINERY - [N16000081]BPCL,Maharashtra	04/2008	825.00 -	1,827.00	1,469.11	04/2013 -	09/2013	5	-
50	Construction of six Effluent Treatment Plants (ETP), Ahmedabad And Ankleswar - [N16000099]ONGC,Gujarat	03/2009	234.78 234.78	317.64	96.88	09/2012 -	09/2013	12	-
51	MRPL Phase-III Expansion - [N16000114]Mangalore Refin,Karnataka	08/2008	12,412.00 -	12,160.26	10,773.71	01/2012 -	10/2013	21	-
52	Development of SB-14 field - [N16000116]ONGC,Multi State	01/2011	410.44 -	410.44	228.26	11/2012 -	10/2013	11	-
53	ADDITIONAL GAS PROCESSING UNITS AT URAN - [N16000064]ONGC,Maharashtra	10/2008	1,797.35 -	977.00	773.81	12/2011 -	11/2013	23	-
54	IOR, RUDRASAGAR (ONGCL) - [160100217]ONGC,Assam	09/2001	113.90 438.85	438.85	432.22	03/2006 03/2013	12/2013	93	9
55	OFFSHORE GRID INTERCONNECTIVITY PROJECT IN MUMBAI HIGH - [N16000031]ONGC,Maharashtra	01/2007	740.02 -	740.02	730.97	03/2010 03/2012	12/2013	45	21
56	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,Multi State	12/2009	463.32 -	330.47	263.46	03/2012 -	12/2013	21	-
57	Fluidized catalytic cracking unit(FCCU) revamp at Mathura Refinery - [N16000107]IOCL,Uttar Pradesh	07/2010	1,000.00 -	1,000.00	673.33	01/2013 -	12/2013	11	-
58	Polypropylene unit - [N16000113]Mangalore Refin,Karnataka	05/2009	1,803.78 -	1,803.78	745.49	07/2012 -	12/2013	17	-
59	Construction of 6 ETPs - [N16000117]ONGC,Gujarat	03/2009	302.26 -	240.95	98.72	09/2012 -	12/2013	15	-
60	Development of BHE and BH-35 Area. - [N16000118]ONGC,Multi State	08/2010	372.11 -	372.11	234.31	03/2013 -	12/2013	9	-
61	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,Maharashtra	08/2009	246.81 276.83	276.83	238.10	04/2012 06/2013	12/2013	20	6

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
62	SINGLE POINT MOORING FACILITY(SMP) PROJECT - [N16000152]Mangalore Refin,Karnataka	07/2010	1,043.57 -	957.10	655.84	04/2012 -	12/2013	20	-
63	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRL,Karnataka	01/2006	732.00 1,227.00	1,227.00	722.53	10/2011 -	12/2013	26	-
64	GAS TURBINE GENERATION SET - [N18000146]OIL,Assam	07/2009	216.88 -	216.88	160.99	10/2011 -	12/2013	26	-
65	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,Assam	08/2008	144.02 -	204.29	133.48	06/2012 -	12/2013	18	-
66	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRL,Andhra Pradesh	01/2006	672.00 1,038.00	1,038.00	904.74	10/2011 -	01/2014	27	-
67	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,Multi State	04/2003	429.82 2,735.65	2,735.65	2,184.00	04/2006 06/2012	02/2014	94	20
68	DEVELOPMENT OF C-SERIES FIELDS - [N16000023]ONGC,Maharashtra	08/2006	3,195.16 3,690.37	3,690.37	2,520.91	12/2008 04/2013	03/2014	63	11
69	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 - [N16000039]ONGC,Maharashtra	10/2007	5,713.03 8,813.41	8,813.41	7,204.61	05/2010 03/2013	03/2014	46	12
70	DEVELOPMENT OF B-46 CLUSTER FIELD - [N16000046]ONGC,Maharashtra	06/2007	1,436.21 1,456.96	1,436.21	1,100.32	07/2010 05/2012	03/2014	44	22
71	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II - [N16000060]ONGC,Maharashtra	01/2009	7,133.39 -	6,855.93	5,308.52	09/2012 -	03/2014	18	-
72	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,Assam	03/2009	2,465.15 -	2,378.86	1,496.19	03/2013 -	03/2014	12	-
73	Up-gradation of Konaban GGS and Pipeline Grid Project, Tripura - [N16000098]ONGC,Tripura	07/2008	288.04 288.04	253.66	199.40	08/2012 -	03/2014	19	-
74	102 MW WIND POWER PROJECT - [N16000119]ONGC,Rajasthan	07/2010	1,106.00 -	678.02	28.10	06/2012 -	03/2014	21	-
75	Construction of 23 Immediate Supply Vessels (ISV) - [N16000123]ONGC,Multi State	11/2010	331.20 -	269.10	91.79	08/2013 -	03/2014	7	-
76	CONSTRUCTION OF 2 FGS IN CHABUA & BAGHJAN - [N18000150]OIL,Assam	08/2008	126.18 -	159.54	59.74	06/2012 -	03/2014	21	-
77	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,Maharashtra	06/2007	3,248.78 5,633.44	5,633.44	5,116.27	08/2010 03/2012	05/2014	45	26
78	PARADIP REFINERY PROJECT - [N16000058]IOCL,Odisha	02/2009	29,777.00 -	32,710.00	23,278.00	11/2012 -	05/2014	18	-
79	ADDITIONAL DEV. OF D-1 FIELD - [N16000086]ONGC,Multi State	01/2010	2,163.64 2,331.62	2,331.62	1,557.08	06/2012 -	05/2014	23	-
80	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,Maharashtra	03/2011	861.79 -	761.68	289.87	05/2013 -	05/2014	12	-
81	IOR of B-173A Field - [N16000140]ONGC,Multi State	01/2012	352.49 -	352.49	14.71	03/2014 -	05/2014	2	-
82	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,Haryana	11/2007	281.07 -	281.07	4.42	10/2010 -	12/2014	50	-
83	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,Multi State	06/2007	736.65 -	736.65	445.86	09/2011 -	12/2014	39	-
84	CONSTRUCTION OF ONE ETP AND THREE ETPS CUM WATER INJECTION PLANTS(WIP) - [N16000127]ONGC,Assam	06/2010	202.94 -	202.94	2.00	01/2014 -	01/2015	12	-
85	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,Assam	09/2012	871.35 -	871.35	2.26	03/2015 -	06/2015	3	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
86	DEVELOPMENT OF B-22 CLUSTER FIELDS - [N16000032]ONGC,Maharashtra	01/2007	2,323.40 2,920.82	2,920.82	1,902.72	09/2010 03/2012	12/2015	63	45
87	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,Multi State	07/2009	7,596.18 -	7,596.18	13.30	01/2013 -	12/2015	35	-
88	Development of WO-16 Cluster Fields - [N16000105]ONGC,Multi State	06/2010	2,523.00 -	2,523.00	957.44	01/2014 -	12/2015	23	-
89	Integrated Refinery Expansion Project - [N16000143]BPCL,Kerala	01/1999	14,225.00 -	14,225.00	508.63	12/2015 -	05/2016	5	-
90	Construction of one Multipurpose Support Vessel (MSV) - [N16000103]ONGC,Multi State	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	-
91	Creation of Secondary Tank farm with dehydration facility and ETP at Madhuban - [N16000167]OIL,Multi State	08/2006	374.56 -	374.56	10.46	09/2012 -	10/2016	49	-
92	Ahmedabad Redevelopment - [N16000120]ONGC,Gujarat	11/2010	1,916.10 -	1,916.10	783.72	12/2014 -	12/2016	24	-
93	Ankleswar Redevelopment - [N16000122]ONGC,Gujarat	11/2010	2,189.63 -	2,189.63	1,039.14	12/2014 -	12/2016	24	-
94	Mehesana Redevelopment - [N16000121]ONGC,Gujarat	11/2010	3,823.00 -	3,823.00	701.81	04/2015 -	03/2017	23	-
	Total		123,228.64 -	134,156.54	77,616.40				
	<u>Power</u>								
95	URI H.E.P STAGE -II (NHPC) - [180100251]NHPC,Jammu and Kashmir	08/2005	1,729.29 -	2,081.00	2,053.70	11/2009 02/2013	10/2013	47	8
96	NIMOO BAZGO HYDROELECTRIC PROJECT - [N18000006]NHPC,Jammu and Kashmir	08/2006	611.01 -	936.00	877.64	08/2010 01/2013	10/2013	38	9
97	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,Multi State	02/2009	184.19 -	184.19	159.08	11/2011 -	10/2013	23	-
98	RIHAND STTP STAGE-III (2X500MW) - [N18000073]NTPC,Uttar Pradesh	01/2009	6,230.81 -	6,230.81	4,512.00	10/2012 -	10/2013	12	-
99	System Strengthening -XII of SR - [N18000085]PGCIL,Multi State	02/2010	232.34 -	232.34	154.44	06/2012 -	11/2013	17	-
100	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XX - [N18000088]PGCIL,Multi State	10/2010	182.68 -	182.68	134.45	01/2013 -	11/2013	10	-
101	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,Multi State	02/2009	509.66 -	509.66	385.26	11/2011 -	12/2013	25	-
102	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,Multi State	02/2009	410.29 -	410.29	266.62	02/2012 -	12/2013	22	-
103	765KV System for Central part of Northern Region Grid - Part-III - [N18000079]PGCIL,Multi State	11/2009	1,075.12 -	1,075.12	847.35	05/2012 -	12/2013	19	-
104	TRANSMISSION SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUB STATION AT KALA IN UT DNH - [N18000102]PGCIL,Maharashtra	07/2011	181.93 -	181.93	138.63	07/2013 -	12/2013	5	-
105	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED - [N18000106]PGCIL,Madhya pradesh	08/2011	425.51 -	425.51	331.70	10/2013 -	12/2013	2	-
106	PARBATI H.E.P. STAGE -III (NHPC) - [180100250]NHPC,Himachal Pradesh	10/2005	2,304.56 -	2,716.00	2,184.87	10/2010 01/2013	03/2014	41	14

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
107	EASTERN REGION STRENGTHENING SCHEME-I - [N18000004]PGCIL,Multi State	10/2006	975.96 -	975.96	885.68	10/2009 -	03/2014	53	-
108	RAMPUR HEP(412 MW) - [N18000024]SJVN, Himachal Pradesh	01/2007	2,047.03 -	2,047.03	2,763.64	01/2012 -	03/2014	26	-
109	SUPPLIMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,Multi State	08/2008	2,360.95 2,580.90	2,580.90	2,066.28	08/2012 -	03/2014	19	-
110	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,Multi State	08/2008	7,075.33 -	7,075.33	5,979.25	08/2012 -	03/2014	19	-
111	Northern Region Transmission Strengthening Scheme - [N18000083]PGCIL,Multi State	03/2010	965.58 -	965.58	607.55	11/2012 -	03/2014	16	-
112	Establishment of pooling stations at Rajgarh and raipur for IPP generation projects in chattisgarh - [N18000092]PGCIL,Chhatisgarh	12/2010	1,719.52 -	1,719.52	1,289.56	08/2013 -	03/2014	7	-
113	Northern region system strengthening scheme XVI - [N18000094]PGCIL,Multi State	07/2010	752.64 -	752.64	327.34	07/2013 -	03/2014	8	-
114	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,Multi State	09/2011	1,366.34 -	1,366.34	785.24	12/2013 -	03/2014	3	-
115	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,Tripura	07/2009	421.01 -	623.44	645.71	07/2013 -	05/2014	10	-
116	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,Odisha	09/2010	2,074.86 -	2,074.86	1,248.80	03/2013 -	05/2014	14	-
117	Transmission system for phase-I generation projects in orissa-part B - [N18000093]PGCIL,Odisha	12/2010	2,743.19 -	2,743.19	1,720.10	12/2013 -	05/2014	5	-
118	Transmission system for phase-I gen.proj.in orissa part-C - [N18000096]PGCIL,Multi State	03/2011	2,569.25 -	2,569.25	1,906.96	03/2014 -	05/2014	2	-
119	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,Multi State	10/2008	4,824.12 -	4,824.12	3,539.61	10/2012 -	06/2014	20	-
120	Trans. System associated with PALLATANA GBPP & BPTS. - [N18000080]PGCIL,Multi State	02/2010	2,144.00 -	2,144.00	1,427.35	12/2012 -	06/2014	18	-
121	System Strengthening in NR for SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,Multi State	12/2009	1,216.83 -	1,216.83	910.02	08/2012 -	06/2014	22	-
122	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XV - [N18000052]PGCIL,Multi State	02/2009	520.48 -	520.48	363.51	11/2011 -	07/2014	32	-
123	KOLDAM HEP (NTPC) - [180100211]NTPC,Himachal Pradesh	10/2002	4,527.15 -	6,414.56	5,134.00	04/2009 -	09/2014	65	-
124	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,Arunachal Pradesh	12/2008	573.99 1,117.92	1,117.92	660.88	08/2013 08/2013	09/2014	13	13
125	BARH STPP STAGE -II - [N18000047]NTPC,Bihar	02/2008	7,341.04 -	7,341.04	6,354.00	08/2013 -	09/2014	13	-
126	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,Jharkhand	10/2011	558.26 -	558.26	182.18	11/2013 -	09/2014	10	-
127	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,West Bengal	09/2005	1,061.38 -	1,501.75	1,387.84	09/2009 06/2013	11/2014	62	17
128	Supplementary transmission associated with vellur TPS - [N18000097]PGCIL,Multi State	08/2010	170.36 -	170.36	95.16	04/2013 -	12/2014	20	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
129	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,Mizoram	01/2011	913.63 -	913.63	470.13	07/2006 -	02/2015	103	-
130	Transmission System of Vindhuachal -IV And Rihand -III Gen. Proj. - [N18000076]PGCIL,Multi State	03/2010	4,672.99 -	4,672.99	2,719.39	11/2012 -	03/2015	28	-
131	Northern region system strengthening scheme-XXI - [N18000095]PGCIL,Multi State	08/2010	1,677.57 -	1,677.57	891.31	04/2013 -	03/2015	23	-
132	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-A - [N18000098]PGCIL,Multi State	05/2010	250.03 -	250.03	63.45	01/2013 -	03/2015	26	-
133	Transmission system for transfer of power from Gen.proj in sikkim to NR/WR part-B - [N18000099]PGCIL,Multi State	03/2011	1,585.12 -	1,585.12	1,042.98	11/2013 -	03/2015	16	-
134	EASTERN REGION TRANSMISSION SYSTEM-III - [N18000100]PGCIL,Multi State	07/2010	1,272.80 -	1,272.80	725.71	11/2012 -	03/2015	28	-
135	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,Multi State	09/2012	524.40 -	524.40	48.69	04/2015 -	05/2015	1	-
136	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,Multi State	02/2009	11,130.19 -	11,130.19	6,689.59	08/2013 -	06/2015	22	-
137	Transm System for development of Pooling stn. in NR part of West Bengal And Transfer of power from B - [N18000077]PGCIL,West Bengal	04/2010	4,404.57 -	4,404.57	392.18	01/2015 -	12/2015	11	-
138	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,Assam	01/2008	4,375.35 -	4,375.35	4,050.00	07/2011 -	06/2016	59	-
139	KISHANGANGA HEP - [N18000031]NHPC,Jammu and Kashmir	07/2007	2,238.67 3,642.04	3,642.00	2,677.22	01/2016 01/2016	11/2016	10	10
140	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,Uttar Pradesh	07/2006	1,657.00 2,978.86	2,978.86	518.78	07/2010 02/2016	02/2017	79	12
141	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,Arunachal Pradesh	12/2004	2,496.90 -	5,139.00	2,473.56	12/2009 05/2013	03/2017	87	46
142	BARH STPP(3X660MW) NTPC - [180100242]NTPC,Bihar	12/2003	8,692.97 -	8,693.00	8,704.00	12/2009 -	03/2017	87	-
143	Tapovan-Vishnugad HEP (4x130MW) - [N18000014]NTPC,Uttarakhand	11/2006	2,978.48 -	3,846.30	1,899.00	03/2013 -	07/2017	52	-
144	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,Uttarakhand	08/2008	2,491.58 -	3,745.08	364.22	07/2014 -	09/2017	38	-
145	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,Arunachal Pradesh	09/2003	6,285.33 -	10,667.00	6,362.61	09/2010 08/2014	03/2018	90	43
146	PARBATI HEP (NHPC) II - [180100210]NHPC,Himachal Pradesh	09/2002	3,919.59 -	5,366.00	4,058.55	09/2009 07/2014	07/2018	106	48
	Total		123,653.83 -	141,352.78	96,477.77				
	<u>Railways</u>								
147	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) - [220100007]NCR,Multi State	04/1986	158.77 580.83	580.83	580.90	03/1994 -	10/2013	235	-
148	LANJHIGARH-JUNAGARH NL(ECOR) - [220100148]ECOR,Odisha	04/1993	100.00 142.98	227.94	229.64	03/2002 -	10/2013	139	-
149	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,Uttar Pradesh	04/1999	108.00 427.21	432.72	406.74	12/2009 03/2011	10/2013	46	31

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
150	Bandel-Naihati new rail bridge in replacement of jubilee bridge no.8 (ER) - [N22000119]ER,West Bengal	04/1999	207.52 207.52	207.52	179.63	12/2012 -	12/2013	12	-
151	Kolar-Chickbalapur GC - [N22000275]SWR,Karnataka	04/2006	287.99 -	287.99	421.25	01/1999 -	12/2013	179	-
152	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,Uttar Pradesh	02/2008	171.10 224.89	246.44	141.55	03/2012 12/2013	03/2014	24	3
153	Ramanagram-Mysore doubling with electrification of Kengesli- Musore (SWR) - [N22000107]SWR,Karnataka	04/2007	482.00 482.70	482.70	505.38	03/2013 -	03/2014	12	-
154	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,Odisha	04/1999	166.16 -	288.00	285.59	02/2009 02/2009	08/2014	66	66
155	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,Odisha	04/2000	133.41 207.00	276.00	257.89	03/2009 03/2009	08/2014	65	65
156	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,Uttar Pradesh	09/2001	129.70 245.39	245.39	241.09	12/2008 -	09/2014	69	-
157	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,Maharashtra	03/1996	401.81 495.44	1,814.48	319.75	03/2004 12/2010	12/2014	129	48
158	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,Jharkhand	04/1997	194.07 194.07	596.35	347.27	06/2004 -	12/2014	126	-
159	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,Bihar	04/2002	921.00 2,363.00	2,363.00	1,174.03	03/2009 12/2012	12/2014	69	24
160	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,Tamil Nadu	04/2006	495.74 -	495.74	252.46	06/2013 06/2013	12/2014	18	18
161	Lumding-SILCHAR Jiribam, Badarpur-Baraigram Kumarghat national project - [N22000127]NEFR,Assam	04/1996	1,676.31 1,676.31	5,000.00	3,677.32	03/2009 -	12/2014	69	-
162	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,Multi State	03/1984	520.00 835.04	835.04	602.18	03/1995 -	03/2015	240	-
163	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,West Bengal	04/1974	31.42 393.46	535.40	178.39	03/2007 03/2007	03/2015	96	96
164	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,Bihar	09/2001	100.00 492.98	1,041.79	741.39	12/2010 12/2010	03/2015	51	51
165	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,Multi State	04/2000	733.00 733.00	2,350.00	1,480.03	12/2008 -	03/2015	75	-
166	Katakhal to Bhairabi - [N22000126]NEFR,Assam	04/1998	227.90 227.90	223.01	126.12	12/2012 -	03/2015	27	-
167	Construction of NL from Kumarghat-Agartala - [N22000194]NEFR,Tripura	04/1999	895.00 -	1,151.00	944.37	03/2007 -	03/2015	96	-
168	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,Assam	09/1997	1,000.00 1,500.00	4,996.19	2,854.15	04/2008 03/2014	12/2015	92	21
169	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,Bihar	04/2001	624.47 2,921.00	2,921.00	1,880.08	10/2007 12/2012	12/2015	98	36
170	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,Madhya pradesh	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	-
171	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,Tripura	04/2008	813.34 813.34	1,741.00	489.13	03/2014 -	12/2015	21	-
172	Champajharan-Bimalgarh Doubling extension - [N22000162]SER,Odisha	04/2010	149.90 -	177.38	41.85	03/2015 -	12/2015	9	-
173	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,West Bengal	03/1984	293.97 1,025.39	1,074.47	448.95	06/2005 07/2011	06/2016	132	59

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
174	New Work for Construction of Metro railway from Noapara-Barasai VIA Bimanbender (MTP) - [N22000108]RVNL,West Bengal	04/2010	2,397.72 -	2,397.72	52.60	03/2016 -	06/2016	3	-
175	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,West Bengal	03/1998	111.90 1,039.29	1,423.98	482.85	03/2005 12/2008	12/2016	141	96
176	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,Maharashtra	04/2008	5,300.00 5,300.00	6,220.15	1,301.02	03/2014 03/2016	12/2016	33	9
177	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,Manipur	04/2003	727.56 727.53	4,453.50	1,655.40	03/2011 03/2014	03/2017	72	36
178	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,Mizoram	04/2008	619.34 -	2,384.34	96.43	04/2014 -	03/2017	35	-
179	SEVOK RANGPO, NEFR - [N22000102]NEFR,Sikkim	04/2008	1,339.48 -	3,380.58	59.60	12/2015 -	03/2017	15	-
180	New Line from Dimapur to Zubza(Kohima) national project (NEFR) - [N22000124]NEFR,Nagaland	04/2006	850.00 850.00	2,441.48	8.94	03/2015 -	03/2017	24	-
181	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,Jammu and Kashmir	03/1995	2,500.00 2,500.00	20,000.00	8,822.50	11/2002 -	12/2017	181	-
	Total		25,555.78 -	74,093.13	31,286.47				
	<u>Road Transport And Highways</u>								
182	GANJAM-ICCHAPURUM,NH-5(NHAI) - [N24000057]NHAI,Odisha	04/2000	263.27 -	263.27	276.46	02/2004 -	09/2013	115	-
183	HAVERI-HARIHAR (GQ) KM.340-KM.284 (NH-4) - [240101132]NHAI,Karnataka	04/2000	241.00 -	196.65	204.82	08/2004 07/2010	10/2013	110	39
184	HARIHAR-CHITRADURGA (GQ) KM.284-KM.207 (NH-4) - [240101133]NHAI,Karnataka	04/2000	318.00 -	207.56	196.57	08/2004 -	10/2013	110	-
185	NEW MANGALORE PORT NH-17 AND 48 - [N24000040]NHAI,Karnataka	04/2000	196.50 363.00	196.50	288.40	06/2011 06/2011	10/2013	28	28
186	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,Haryana	04/2007	486.00 -	486.00	660.30	05/2010 -	10/2013	41	-
187	Pune-sholapur, pkg1 - [N24000127]NHAI,Maharashtra	11/2009	1,110.00 -	1,110.00	1,802.00	05/2012 -	10/2013	17	-
188	Hazaribagh-Ranchi - [N24000141]NHAI,Jharkhand	08/2010	625.07 -	625.07	948.00	01/2013 -	10/2013	9	-
189	PATNA-MUZZAFFARPUR - [N24000165]NHAI,Bihar	08/2010	671.30 -	671.30	625.90	02/2013 -	10/2013	8	-
190	BHOPAL-SANCHI - [N24000192]NHAI,Madhya pradesh	10/2011	209.00 -	209.00	34.38	01/2013 -	10/2013	9	-
191	SUNAKHALA-GANJAM (GQ) KM.338-KM.284 (NH-5) - [240101153]NHAI,Odisha	04/2000	225.00 -	241.53	162.71	04/2004 -	11/2013	115	-
192	HAPUR-GARHMUKTESWAR (OTHERS) KM.58-93, NH-24 - [240106205]NHAI,Uttar Pradesh	03/2005	220.00 -	220.00	284.20	09/2007 -	11/2013	74	-
193	BALASORE BHADRAK (REVIVED) KM 136.5 - 199.14 NH-5 - [N24000116]NHAI,Odisha	04/2000	228.70 -	228.70	194.51	02/2004 -	11/2013	117	-
194	PATHANKOT- BHOGPUR, KM.26-KM.70, NS-38 NH-1A - [240106237]NHAI,Punjab	12/2003	284.00 -	359.00	327.60	05/2008 -	12/2013	67	-
195	KOTWA TO DEWAPUR(10 LMNHP),NH-28 PHASE-II, KM.440 TO KM.402 - [240106243]NHAI,Bihar	12/2003	240.00 -	240.00	295.00	10/2008 -	12/2013	62	-
196	AURANG-RAIPUR, NH-6, KM.232 TO KM.281 - [240106260]NHAI,Chhatisgarh	03/2005	190.00 -	190.00	264.60	01/2009 -	12/2013	59	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
197	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,Bihar	12/2003	332.94 -	332.94	475.50	09/2008 -	12/2013	63	-
198	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,Rajasthan	12/2003	275.00 -	250.39	280.40	10/2008 -	12/2013	62	-
199	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,Assam	12/2003	200.00 -	200.00	288.30	06/2008 -	12/2013	66	-
200	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,Assam	12/2003	225.00 -	225.00	266.10	06/2008 -	12/2013	66	-
201	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,Assam	12/2003	160.00 -	160.00	207.70	05/2008 -	12/2013	67	-
202	LAKHNAADON TO MP/MH BORDER,KM 596.75-653.22 (NS-1/BOT/MP-2),NH7 - [N24000094]NHAI,Madhya pradesh	12/2003	407.60 -	407.60	186.50	06/2010 -	12/2013	42	-
203	JHANSI TO LALITPUR, NH-25,26 - [N24000096]NHAI,Uttar Pradesh	12/2003	355.06 -	355.06	507.40	09/2009 -	12/2013	51	-
204	SALEM - U / UNDRUPET(BOT -1/TN-06) NH -68 - [N24000102]NHAI,Tamil Nadu	03/2005	941.00 -	941.00	1,901.00	01/2011 -	12/2013	35	-
205	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI,Maharashtra	03/2005	940.00 -	940.00	1,325.00	07/2012 -	12/2013	17	-
206	Four Lanning from MP/Maharashtra Border to nagpur, Nagpur bypass - [N24000124]NHAI,Maharashtra	04/2010	1,170.52 -	1,170.52	4.41	06/2011 -	12/2013	30	-
207	Gujarat/Maharashtra BorderSurat-Hazira Port Section - [N24000125]NHAI,Gujarat	03/2010	1,509.10 -	1,509.10	2,123.00	09/2012 -	12/2013	15	-
208	Kishangarh-Ajmer-Beawer - [N24000128]NHAI,Rajasthan	11/2009	795.00 -	795.00	1,127.00	05/2012 -	12/2013	19	-
209	Gurgaon-Kotputli Km 42.70 to 54.4 Km - [N24000130]NHAI,Multi State	04/2009	1,673.70 -	1,673.70	2,839.00	10/2011 -	12/2013	26	-
210	Surat- Dahisar(Six Lane) Km 263 to Km 502 - [N24000131]NHAI,Multi State	02/2009	1,693.75 -	1,693.75	2,721.00	08/2011 -	12/2013	28	-
211	Panipat-Jalandhar 6 lane(Km 96 to 387.1 km) - [N24000133]NHAI,Haryana	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	12/2013	25	-
212	Indore-Jhabua-Gujrat/MP - [N24000136]NHAI,Madhya pradesh	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2013	8	-
213	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,Tamil Nadu	09/2010	852.00 -	852.00	839.20	03/2013 -	12/2013	9	-
214	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,Andhra Pradesh	11/2010	1,585.00 -	1,585.00	957.80	05/2013 -	12/2013	7	-
215	AMRITSAR-PATHANKOT - [N24000147]NHAI,Punjab	05/2010	705.00 -	705.00	2,144.00	11/2012 -	12/2013	13	-
216	DEOLI-KOTA - [N24000148]NHAI,Rajasthan	01/2011	593.00 -	593.00	582.90	07/2013 -	12/2013	5	-
217	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,Gujarat	12/2010	1,008.50 -	1,008.50	1,352.00	06/2013 -	12/2013	6	-
218	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,Gujarat	03/2011	785.50 -	785.50	843.90	08/2013 -	12/2013	4	-
219	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,Tamil Nadu	06/2011	600.00 -	600.00	75.85	06/2013 -	12/2013	6	-
220	Two laning of Trichy - Karaikudi and Trychi Bypass - [N24000176]NHAI,Tamil Nadu	05/2010	374.00 -	374.00	119.10	05/2013 -	12/2013	7	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
221	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI,Gujarat	09/2010	805.39 -	805.39	725.40	03/2013 -	12/2013	9	-
222	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,Bihar	01/2011	575.00 -	575.00	714.40	07/2013 -	12/2013	5	-
223	BHUBANESWAR TO PURI - [N24000195]NHAI,Odisha	03/2011	500.29 -	500.29	509.40	08/2013 -	12/2013	4	-
224	JAIPUR-REENGUS - [N24000198]NHAI,Rajasthan	08/2010	267.81 -	267.81	651.60	02/2013 -	12/2013	10	-
225	Jaipur-Tonk-Deoli - [N24000135]NHAI,Rajasthan	06/2010	792.06 -	792.06	1,975.00	12/2012 -	02/2014	14	-
226	INDORE-DEWAS(NH-3) - [N24000159]NHAI,Madhya pradesh	11/2010	325.00 -	325.00	532.70	05/2013 -	02/2014	9	-
227	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI,Assam	12/2003	157.47 -	154.57	240.40	09/2007 -	03/2014	78	-
228	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,Uttar Pradesh	12/2003	155.00 -	201.66	144.30	09/2008 -	03/2014	66	-
229	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,Assam	12/2003	230.00 -	230.00	239.90	06/2005 -	03/2014	105	-
230	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,Assam	12/2003	195.00 -	195.00	252.60	06/2008 -	03/2014	69	-
231	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,Assam	12/2003	237.80 -	237.80	289.00	06/2008 -	03/2014	69	-
232	RAJMARG CHORAHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,Madhya pradesh	12/2003	251.03 -	251.03	338.40	10/2008 -	03/2014	65	-
233	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,Assam	12/2003	175.96 -	175.96	217.60	04/2008 -	03/2014	71	-
234	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,Assam	12/2003	264.72 -	264.72	301.10	06/2008 -	03/2014	69	-
235	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,Assam	12/2003	245.00 -	245.00	491.20	03/2008 -	03/2014	72	-
236	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,Assam	12/2003	198.16 -	198.16	276.20	04/2008 -	03/2014	71	-
237	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,Assam	12/2003	200.00 -	200.00	253.90	06/2008 -	03/2014	69	-
238	NAGPUR-KONDHALI,NH-6(NHAI) - [N24000055]NHAI,Maharashtra	03/2005	168.00 -	168.00	457.30	12/2008 -	03/2014	63	-
239	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,Uttar Pradesh	12/2003	348.16 -	465.50	240.70	09/2007 -	03/2014	78	-
240	TRICHY - KORUR NH-67 - [N24000101]NHAI,Tamil Nadu	03/2005	516.00 -	516.00	860.70	07/2010 -	03/2014	44	-
241	Chennai-Tada(Six lane) - [N24000129]NHAI,Tamil Nadu	04/2009	353.37 -	353.37	446.20	10/2011 -	03/2014	29	-
242	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,Maharashtra	02/2011	193.45 -	193.45	54.59	11/2012 -	03/2014	16	-
243	MURADABAD-BAREILY - [N24000154]NHAI,Uttar Pradesh	04/2010	1,267.00 -	1,267.00	1,876.00	06/2013 -	03/2014	9	-
244	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,Bihar	05/2011	351.54 -	351.54	395.20	05/2013 -	03/2014	10	-
245	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,Multi State	09/2011	754.00 -	754.00	515.80	03/2013 -	03/2014	12	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
246	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,Uttarakhand	11/2011	478.00 -	478.00	281.10	10/2013 -	03/2014	5	-
247	HARANGAJO TO MAIBANG,km 164.08-190.587 NH-54 - [N24000061]NHAI,Assam	12/2003	212.00 -	386.10	70.00	09/2007 -	04/2014	79	-
248	PUNE-SATARA(NH-4) - [N24000156]NHAI,Maharashtra	10/2010	1,724.55 -	1,724.55	1,201.00	03/2013 -	04/2014	13	-
249	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,Bihar	05/2011	664.00 -	664.00	564.60	02/2014 -	04/2014	2	-
250	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,Assam	12/2003	280.00 -	280.00	324.60	02/2009 03/2014	05/2014	63	2
251	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,Assam	12/2003	208.00 -	208.00	308.70	04/2008 -	05/2014	73	-
252	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,Assam	12/2003	196.00 -	363.74	158.70	07/2009 -	05/2014	58	-
253	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,Bihar	12/2003	300.00 -	300.00	176.80	10/2008 -	06/2014	68	-
254	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,Assam	12/2003	155.04 -	280.13	125.00	11/2008 -	06/2014	67	-
255	Chilkaluripet-Vijaywada 6 lane (km 355 to Km 434.15) - [N24000132]NHAI,Andhra Pradesh	05/2009	572.30 -	572.30	857.90	10/2011 -	06/2014	32	-
256	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,Jammu and Kashmir	07/2010	1,813.76 -	1,813.76	-	07/2013 -	06/2014	11	-
257	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,Uttar Pradesh	02/2011	1,141.00 -	1,141.00	1,287.00	08/2013 -	06/2014	10	-
258	Kandla - Mundra port - [N24000175]NHAI,Gujarat	01/2011	953.88 -	953.88	672.60	07/2013 -	06/2014	11	-
259	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,Karnataka	03/2011	359.00 -	359.00	39.39	09/2013 -	07/2014	10	-
260	LUCKNOW-RAIBAREILI - [N24000207]NHAI,Uttar Pradesh	07/1999	635.90 -	635.90	257.00	07/2012 -	07/2014	24	-
261	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,Multi State	12/2003	232.45 -	232.45	305.20	09/2010 -	08/2014	47	-
262	THANJAUR-TRICHY,NH-67(NHAI) - [N24000056]NHAI,Tamil Nadu	03/2005	280.00 -	280.00	581.50	06/2009 -	09/2014	63	-
263	LAKHNADON TO MP/MH BORDER (NS-1/BOT/MP-2), NH-7 - [N24000095]NHAI,Madhya pradesh	12/2003	263.17 -	263.17	235.20	09/2009 -	09/2014	60	-
264	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,Assam	12/2003	199.81 -	385.13	93.63	04/2009 -	12/2014	68	-
265	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,Assam	12/2003	167.64 -	167.64	72.60	11/2008 -	12/2014	73	-
266	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,Assam	12/2003	200.00 -	200.00	169.00	04/2009 -	12/2014	68	-
267	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,Assam	12/2003	217.61 -	217.61	297.90	04/2010 -	12/2014	56	-
268	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,Multi State	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2014	60	-
269	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,Kerala	03/2005	557.00 -	557.00	1,129.00	02/2010 -	12/2014	58	-
270	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,Odisha	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2014	11	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
271	BAREILY-SITAPUR - [N24000200]NHAI,Uttar Pradesh	03/2011	1,046.00 -	1,046.00	357.00	09/2013 -	12/2014	15	-
272	4-laning of Faraka-Raiganj - [N24000202]NHAI,Multi State	02/2011	1,078.84 -	1,078.84	1,328.00	08/2013 -	12/2014	16	-
273	4-laning of Brahampore-Faraka - [N24000203]NHAI,Multi State	02/2011	998.79 -	998.79	1,266.00	08/2013 -	12/2014	16	-
274	2 laning of Dindigul - Perigulam Theni- kumili - [N24000177]NHAI,Tamil Nadu	09/2011	485.00 -	485.00	318.00	08/2013 -	02/2015	18	-
275	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,Kerala	02/2010	617.00 -	617.00	154.50	08/2012 -	03/2015	31	-
276	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,Rajasthan	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2015	65	-
277	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,Multi State	02/2011	2,498.76 -	2,498.76	1,734.00	08/2014 -	07/2015	11	-
278	PANIKHOLI-RIMOLI - [N24000197]NHAI,Odisha	03/2012	1,410.00 -	1,410.00	153.80	09/2014 -	10/2015	13	-
279	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,Kerala	04/2011	682.00 -	682.00	160.00	10/2013 -	11/2015	25	-
280	4-laning of Raiganj-Dalkola - [N24000204]NHAI,Multi State	02/2011	580.43 -	580.43	299.60	08/2013 -	12/2015	28	-
281	NASHRI CHANANI - [N24000162]NHAI,Jammu and Kashmir	06/2010	2,159.00 -	2,159.00	-	06/2015 -	05/2016	11	-
282	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,Jammu and Kashmir	07/2010	1,987.00 -	1,987.00	973.60	07/2015 -	06/2016	11	-
	Total		61,318.65 -	63,230.44	61,202.82				
	<u>Shipping And Ports</u>								
283	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU, Maharashtra	11/2007	1,228.00 1,460.00	1,460.00	974.80	12/2010 09/2012	12/2014	48	27
	Total		1,228.00 -	1,460.00	974.80				
	<u>Telecommunications</u>								
284	GSM equipment of 1625000Lines (2G) 325000 lines 3(G) MP Phase V.1 Telecom Circle - [N26000090]BSNL,Madhya pradesh	11/2009	916.70 -	930.60	828.80	11/2010 12/2012	09/2013	34	9
285	EXPANSION OF EXISTING 750K GSM NETWORK PE NO. 9920/05-06 - [N26000029]MTNL,Maharashtra	06/2006	231.38 -	176.00	86.11	10/2007 -	12/2013	74	-
286	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTRANCHAL - [N26000058]BSNL,Uttarakhand	01/2009	149.15 -	158.72	84.39	06/2009 -	12/2013	54	-
287	Assam Telecom Circle, Phase-V.I, 2G & 3G - [N26000062]BSNL,Assam	06/2007	336.81 -	336.81	164.18	01/2009 -	12/2013	59	-
288	ERP implementation in BSNL on Turnkey basis - [N26000096]BSNL,Multi State	10/2009	384.00 -	384.00	29.45	10/2010 03/2012	12/2013	38	21
289	Supply Installation testing and commissioning of Rural Wimax network Phase-II - [N26000100]BSNL,Multi State	07/2010	1,148.19 -	964.37	237.44	05/2011 -	12/2013	31	-

(Sep,2013)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	Total		3,166.23 -	2,950.50	1,430.37				
	<u>Urban Development</u>								
290	FARIDABAD EXTENSION - [N28000057]DMRC, Delhi	09/2011	2,494.00 -	2,494.00	300.76	09/2014 -	05/2015	8	-
	Total		2,494.00 -	2,494.00	300.76				
	Grand Total		469,678.06	564,578.65	362,179.45				
