

**346th FLASH REPORT
ON
CENTRAL SECTOR PROJECTS
(` 150 crore and above)
August 2014**



PORT TRUST - SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN



Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division
Sardar Patel Bhavan, Sansad Marg
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations

AAI	Airport Authority of India
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Generation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petrochemicals Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Copn.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Copn.
NCL	Northern coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corpn.
NGN	Next Generation Network
NLC	Neyveli Lignite Corpn.
NMDC	National Mineral Development Corpn.
NPC	Nuclear Power Corporation
NRL	Numaligarh Refinery Ltd.
OB	Over burden
OC	Opencast
OECE	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

Contents

Executive Summary in English	1 -9
Month wise list of completed projects Costing Rs. 150 Crore and Above During 2013-14	10-11
Summary of Projects	12-25
Trend and Graphical Analysis of Projects	26-38
Sector wise analysis of projects	39-39
List of All Ongoing Projects	40-73
Sector wise Graph	74-85
ANNEXURE	86-86
Central Sector Projects	87-87
List of Projects Having Expenditure More than cost	88-97
List of Projects Ahead of Schedule	98-98
List of Projects with out Original date of Commissioning	99-100
List of Projects with out date of Commissioning	101-113
List of On schedule Projects Original Schedule	114-119
List of Delayed Projects w.r.t Original Schedule	120-138
List of Projects Having Time and cost overrun w.r.t original	139-143
List of Projects Having cost overrun w.r.t original	144-154

कार्यकारी सारांश

1. अगस्त, 2014 की फ्लैश रिपोर्ट में `150 करोड़ और उससे अधिक लागत वाली केन्द्रीय क्षेत्र की 720 अवसंरचनात्मक परियोजनाओं की स्थिति दी गई है। अगस्त, 2014 के दौरान 3 परियोजनाओं (पेट्रोलियम में 2 परियोजनाएं तथा पोत परिवहन एवं पत्तन क्षेत्र में 1 परियोजना) के पूरा होने की सूचना दी गई है।

2. संदर्भाधीन माह के दौरान, 720 परियोजनाओं में से, 295 परियोजनाओं में मूल समय-सारणी की तुलना में विलंब हुआ तथा 42 परियोजनाओं के संबंध में पिछले माह में सूचित की गई समापन की तारीख की तुलना में अतिरिक्त विलंब की सूचना दी गई है। इन 42 परियोजनाओं में से, 17 परियोजनाएं `1000 करोड़ और अधिक लागत वाली बड़ी परियोजनाएं हैं।

क्र.सं.	क्षेत्र	निगरानी के तहत आने वाली परियोजनाएं	नवीनतम समय-सारणी की तुलना में विलंबित परियोजनाएं	रिपोर्ट वाले माह के दौरान अतिरिक्त विलंबित परियोजनाएं	अतिरिक्त विलंबित बड़ी परियोजनाएं
1.	रेलवे	288	32	7	2
2.	सड़क परिवहन एवं राजमार्ग	136	92	0	0
3.	विद्युत	101	64	12	8
4.	पेट्रोलियम	75	43	10	5
5.	कोयला	59	34	4	1
6.	इस्पात	20	16	6	1
7.	पोत परिवहन एवं पत्तन	18	3	1	0
8.	नागर विमानन	8	3	2	0
9.	शहरी विकास	5	1	0	0
10.	परमाणु ऊर्जा	4	4	0	0
11.	दूरसंचार	4	3	0	0
12.	पेट्रोरसायन	1	0	0	0
13.	जल संसाधन	1	0	0	0
कुल		720	295	42	17

3. 720 परियोजनाओं के कार्यान्वयन की कुल मूल लागत लगभग `9,27,317.65 करोड़ थी तथा उनके पूरा होने की अनुमानित लागत `11,04,729.32 करोड़ होने की संभावना है जो `1,77,411.67 करोड़ (मूल लागत का 19.10%) की समग्र लागत वृद्धि को दर्शाता है। अगस्त, 2014 तक इन परियोजनाओं पर किया गया व्यय `5,46,379.88 करोड़ है जो परियोजनाओं की अनुमानित लागत का 49.50% है। लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाएं नीचे दी गई हैं:-

लागतवृद्धि की अधिकतम प्रतिशतता वाली 5 परियोजनाओं की सूची (31.08.2014की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (`करोड़)		लागत-वृद्धि (% में)
				मूल	अनुमानित	
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	2651.54
2	गाजोले-ईटाहार सहित इकलाखी-बलूरघाट से नई बी जी रेलवे लाइन (एनएल), एनईएफआर	रेलवे	04/1983	36.80	703.18	1810.82
3	बांकुरा-दामोदर (जीसी) (एसईआर)	रेलवे	03/1998	111.90	1423.98	1172.55
4	अकोला-खण्डवा जीसी अकोला-अकोट	रेलवे	04/2008	184.26	2000.00	985.42
5	बंगलोर सत्यमंगलम (एनएल) (एसडब्ल्यूआर)	रेलवे	02/1999	138.00	1382.78	902.01

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीयसलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे।

4. वास्तविक अर्थ में अधिकतम लागतवृद्धि वाली 5 परियोजनाएं निम्नानुसार हैं:-

अधिकतम लागतवृद्धि वाली 5 परियोजनाओं की सूची(31.08.2014की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		
				मूल लागत	अनुमानित लागत	लागत-वृद्धि
1	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	20000.00	17500.00
2	कुसमुण्डा एक्सपे. (ओसीपी) (एसईसीएल) (15-50) एमटीवाई	कोयला	06/2008	1188.31	7612.33	6424.02
3	जिरीबाम से इंफाल (तुपुई) (एनएल) (एनईएफआर)	रेलवे	04/2003	727.56	5996.00	5268.44
4	बंगलौर मेट्रो रेल परियोजना	शहरी विकास	05/2006	6395.00	11609.00	5214.00
5	बाढ़ एसटीपीपी (3x660 मेवा.) एनटीपीसी	विद्युत	12/2003	8692.97	13737.00	5044.03

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक लागतवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

5. 720 परियोजनाओं में से,6 परियोजनाएं समय से पहले चल रही हैं,105 समय पर तथा 295 परियोजनाएं मूल समय-सारणी की तुलना में विलंबित हैं । तथापि, विलंबित परियोजनाओं की संख्यामें 274 तक की कमी हो जाती है यदि विलंब की गणना समापन की अद्यतन समय-सारणी के आधार पर की जाती है । इसके अलावा,19 परियोजनाएं किसी आरंभ संबंधी समय-सारणी/तारीख के बिना स्वीकृत की गई हैं तथा 295 परियोजनाओं के संबंध में न तो शुरू करने का वर्ष और न परियोजना के अनंतिम रूप से पूरा होने की अवधि सूचित की गई है । 295 विलंबित परियोजनाओं में से,63 परियोजनाओं में 1 से 12 माह तक का विलंब हुआ,66 परियोजनाओं में 13 से 24 महीने तक का विलंब हुआ,97 परियोजनाओं में 25 से 60 माह तक का विलंब हुआ तथा 69 परियोजनाओं में 61 माह और उससे अधिक का विलंब हुआ । अधिकतम विलंब वाली 5 परियोजनाएं नीचे दी गई हैं:-

अधिकतम समयवृद्धि वाली 5 परियोजनाओं की सूची (31.08.2014की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	शुरू करने की तारीख		समय-वृद्धि (महीने में)
				मूल	अनुमानित	
1	गुना-इटावावायाशिवपुरी-ग्वालियर-भिंड एनएल (एनसीआर)	रेलवे	04/1986	03/1994	10/2014	247
2	फ्रैंट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	03/1995	03/2015	240
3	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	11/2002	12/2017	181
4	बेलापुर-सीवूड-यूरान इलेक्ट्रीफाइड डबल लाईन (एमटीपी)	रेलवे	03/1996	03/2004	03/2016	144
5	रांची-लोहरदगा (जीसी) (एसईआर)	रेलवे	04/1997	06/2004	06/2015	132

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार और अधिक समयवृद्धि से बचने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

6. अप्रैल, 2014 में इस मंत्रालय के प्रबोधन पर 727 परियोजनाओं में से 235 परियोजनाओं के संबंध में लागतवृद्धि तथा 282 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है; जबकि अगस्त 2014 के दौरान 720 परियोजनाओं में से 212 परियोजनाओं के संबंध में लागतवृद्धि तथा 295 परियोजनाओं के संबंध में समयवृद्धि की सूचना दी गई है । अप्रैल 2014 की तुलना में लागतवृद्धि की सूचना देने वाली परियोजनाओं की संख्या 32% से घटकर 29% हो गई है जबकि समयवृद्धि की सूचना देने वाली परियोजनाओं की संख्या में वृद्धि 39%से 41%हो गई है (अनुबंध 6 (क) तथा 6(ख) ।

7. विभिन्न अन्य परियोजना कार्यान्वयन एजेंसियों द्वारा यथा सूचित समयवृद्धि के संक्षिप्त कारणों में भूमि अधिग्रहण में विलंब, वन संबंधी अनुमति में विलंब, उपस्करों की आपूर्ति में विलंब, निधि की कमी, भू वैज्ञानिक गतिविधियां, उपस्कर स्थापित करने में समस्या, भूखनन की स्थिति, सिविल कार्यों में धीमी प्रगति, श्रम की कमी, ठेकेदार द्वारा अपर्याप्त संसाधन जुटाना, माओवादी समस्याएं, न्यायालय मामले, संविदात्मक मुद्दे, आरओयू/आरओडब्ल्यू समस्याएं, कानून और व्यवस्था की स्थिति, आदि शामिल हैं।

8. मंत्रालय के ऑनलाइन कम्प्यूटरीकृत मॉनीटरिंग सिस्टम (ओसीएमएस) में विभिन्न अवसंरचना परियोजनाओं के पीईआरटी चार्टों से तैयार किए गए लक्ष्यों की निगरानी की परिकल्पना की गई है। परियोजना प्राधिकारियों से नियमित रूप से अनुरोध किया गया है कि वे बेहतर निगरानी को सुचारू बनाने के लिए प्रत्येक परियोजना के संबंध में उपलब्धियों की सूची की प्रविष्टि करें। तथापि, सभी परियोजना एजेंसियां उपलब्धियों की सूची प्रदान नहीं कर रही हैं। पहले शुरू की गई 5 परियोजनाएं जिनके लक्ष्य परियोजना एजेंसियों द्वारा प्रदान नहीं किए जा रहे हैं, नीचे दी गई हैं:-

बिना उपलब्धियों वाली पहली 5 परियोजनाओं की सूची (31.08.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (रु.करोड़)		संचयी व्यय (रु.करोड़)	शुरू करने की तारीख		उपलब्धि
				मूल	अनुमानित		मूल	अनुमानित	
1	हावड़ा-आमता-चंपादंगा एनएल (एससीआर)	रेलवे	04/1974	31.42	535.40	176.52	03/2007	03/2015	एन.आर.
2	नांगल बांध तलवारा (एनएल), एनआर	रेलवे	03/1981	37.68	1036.78	353.41	07/2012	एन.आर.	एन.आर.
3	इकलाखी-बलूरघाट से नई बी जी रेलवे लाइन	रेलवे	04/1983	36.80	703.17	247.74	एन.आर.	03/2015	एन.आर.
4	फ्रैंट आप्रेशन्स इन्फोर्मेशन सिस्टम (एफओआईएस)	रेलवे	03/1984	520.00	634.13	555.27	03/1995	03/2013	एन.आर.
5	तामलुक दीघा, लाइन का दोहरीकरण	रेलवे	03/1984	293.97	1074.47	433.89	06/2005	06/2016	एन.आर.

(एसईआर)								
---------	--	--	--	--	--	--	--	--

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार लक्ष्यों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

9. यह भीपाया गया है कि परियोजना एजेंसियां संशोधित लागत अनुमानों तथा अनेक परियोजनाओं को शुरू करने की समय-सारणी को सूचित नहीं कर रही हैं, जो संकेत देता है कि समय/लागतवृद्धि संबंधी आंकड़े कम बताए गए हैं । पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां संशोधित लागत अनुमानों की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं, नीचे दी गई हैं:-

बिना संशोधित लागत अनुमानों वाली पहली 5 परियोजनाओं की सूची (31.08.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना की लागत (₹ करोड़)		संचयी व्यय (₹ करोड़)
				मूल	संशोधित	
1	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	155.66	एन.आर.	200.42
2	शापुर-सरादिया और सोमनाथ-कोडिनार के लिए राजकोटवेरावल, वंशजालिया से जतलसर नए एमएम के साथ (जीसी)	रेलवे	04/1994	320.66	एन.आर.	462.18
3	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	124.43	495.68	688.63
4	उधमपुर-श्रीनगर-बारामूला (एनएल), एनआर	रेलवे	03/1995	2500.00	2500.00	8805.00
5	दल्ली-रजहारा रौघट (दल्ली-रजहारा जगदलपुर के भाग), एनएल, आरवीएनएल	रेलवे	04/1995	304.00	एन.आर.	138.39

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार संशोधित लागत अनुमानों को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

पहले शुरू की गई 5 परियोजनाएं जिनमें परियोजना एजेंसियां शुरू करने की संशोधित समय-सारणी की सूचना नहीं दे रही हैं/प्रदान नहीं करा रही हैं अथवा अद्यतन नहीं कर रही हैं, नीचे दी गई हैं:-

शुरू करने की संशोधित समय-सारणी के बिना पहली 5 परियोजनाओं की सूची (31.08.2014 की स्थिति के अनुसार)

क्र. सं.	परियोजना	क्षेत्र	अनुमोदन की तारीख	परियोजना को शुरू करने की तारीख		
				मूल	संशोधित	अनुमानित
1	नांगल बांध-तलवारा (एनएल), एनआर	रेलवे	03/1981	07/2012	एन.आर.	एन.आर.
2	विरमगम-भिल्डी (डब्ल्यूआर), जीसी	रेलवे	04/1990	एन.आर.	03/2010	एन.आर.
3	अमरावती-नरखेर एनएल (सीआर)	रेलवे	06/1994	06/1999	03/2011	03/2011
4	पेड़ापल्ली-करीमनगर-निजामाबाद एनएल (एससीआर)	रेलवे	12/1994	एन.आर.	एन.आर.	03/2012
5	कोटूर-हरीहर (एनएल), (एसडब्ल्यूआर)	रेलवे	04/1995	एन.आर.	एन.आर.	12/2012

एन.आर.: सूचित नहीं ।

टिप्पणी: परियोजना कार्यान्वयन एजेंसी के मुख्य कार्यकारी तथा संबंधित प्रशासनिक मंत्रालयों के सचिव और वित्तीय सलाहकार शुरू करने की संशोधित समय-सारणी को निश्चित करने के लिए इन परियोजनाओं की विशेष समीक्षा करेंगे ।

10. विलंब/अतिरिक्त विलंब का क्षेत्र-वार ब्यौरा निम्नानुसार है:-

- पोत परिवहन एवं पत्तन क्षेत्र में 18 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । माह के दौरान परियोजना 'मेसर्स जियांगसू राँगशेंग हैवी, भारतीय पत्तन निगम ने 317000 डीडब्ल्यूटी वेरी लार्ज क्रूड कैरियर के दो(2) सं. का अधिग्रहण करने में संविदात्मक मुद्दे के कारण 9 माह के अतिरिक्त विलंब की सूचना दी है ।
- नागर विमानन क्षेत्र में 8 परियोजनाओं में से 3 परियोजनाएं विलंबित हैं । माह के दौरान 2 परियोजनाओं के संबंध में 1 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है । परियोजना 'नए अंतर्राष्ट्रीय टर्मिनल बिल्डिंग (गोवा) का निर्माण, एएआई' में आधार की संरचनात्मक डिजाइन में परिवर्तन तथा श्रमिक की कमी के कारण 1 माह के अतिरिक्त विलंब

की सूचना प्राप्त हुई है; तथा परियोजना '10 हवाईअड्डों पर एयरपोर्ट ऑपरेशंस नियंत्रण केन्द्रों की स्थापना, एएआई' में उपस्करों की आपूर्ति में विलंब के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है ।

iii) **कोयला क्षेत्र** में, 59 परियोजनाओं में से 34 परियोजनाएं विलंबित हैं । माह के दौरान, 4 परियोजनाओं के संबंध में 5-72 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 बड़ी परियोजना है। परियोजना 'अदरियाला शॉफ्ट परियोजना, एससीसीएल' में उपस्करों की आपूर्ति में विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'ककटिया लोंगवाल, एससीसीएल' में लोंगवाल तकनीकी के लिए तकनीकी प्रदाता-सह ऑपरेटर (टीपीओ) के प्रवेश के कारण 12 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'जलगाम वेंगला राव ओसीपी-II, एससीसीएल' में वन संबंधी अनुमति में विलंब तथा भूमि अधिग्रहण के कारण 36 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'गोपाल प्रसाद ओसीपी (15 एमटीवाई), एमसीएल' में 72 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

iv) **इस्पात क्षेत्र** में 20 परियोजनाओं में से 16 परियोजनाएं विलंबित हैं । माह के दौरान, 6 परियोजनाओं के संबंध में 1-3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 1 मेगा परियोजना है । परियोजना 'कोक ओवन बैट्री सं. 4, चरण-II, आरआईएनएल' में स्थल पर भू-वैज्ञानिक स्थिति के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं '3 एमटी से 6.3 एमटी तक लिक्विड इस्पात क्षमता का विस्तार, आरआईएनएल' तथा 'आरएमएचपी में लौह अयस्क भंडारण का संवर्धन, आरआईएनएल' में सामग्रियों की आपूर्ति में विलंब के कारण क्रमशः 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बेलाडिला लौह अयस्क परियोजना डिपोजिट-11बी, एनएमडीसी' में नक्सलवादी समस्याओं के कारण 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजना '7.0 एमटीपीए कुमारस्वामी लौह अयस्क खान परियोजना, एनएमडीसी' तथा '1.2 एमटीपीए पेलेट संयंत्र परियोजना, दोनीमलाई, एनएमडीसी' में क्रमशः 2 तथा 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है) ।

v) **रेलवे क्षेत्र** में, 288 परियोजनाओं में से 32 परियोजनाएं विलंबित हैं । माह के दौरान, 7 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 2 मेगा परियोजनाएं हैं । परियोजना 'शिवपुरी-ग्वालियर-भिण्ड एनएल के माध्यम से गूना-इटावा, एनसीआर' में खंभों में दरार पड़ने के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है;

परियोजनाएं विद्युतीकरण सहित तम्बरम-चेन्नगलापट्टू तीसरी लाइन जीसी के लिए नए एमएम के साथ चेन्नगलापट्टू-विल्लुपुरम दोहरीकरण, एसआर तथा केनगेसी-मैसूर के विद्युतीकरण सहित रमनाग्राम-मैसूर दोहरीकरण, एसडब्ल्यूआर में भूमिअधिग्रहण में विलंब के कारण 3 तथा 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बारानगर से बराकपुर तथा दक्षिणेश्वर (एमटीपी) तक मेट्रो रेलवे के निर्माण हेतु नया कार्य, आरवीएनएल' में राज्य सरकार द्वारा यूटीलिटीज के स्थानान्तरण के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; तथा परियोजनाएं 'आनन्द नगर-नौटनवा जीसी के साथ गोन्डा-गोरखपुर लूप, एनईआर', 'ईटावा-मैनपुरी (एनएल), एनसीआर' तथा 'खुरजा-मेरठ-सहारनपुर तथा गाजियाबाद-मेरठ का विद्युतीकरण, आरई' (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

vi) **पेट्रोलियम क्षेत्र में,** 75 परियोजनाओं में से 43 परियोजनाएं विलंबित हैं। माह के दौरान 10 परियोजनाओं के संबंध में 1-24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 5 मेगा परियोजनाएं हैं। परियोजना 'विजयपुर तथा पाटा में पेट्रोरसायन कॉम्प्लेक्स-II, गेल' में ठेकेदार के साथ निधि की कमी के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'पारादीप रिफाइनरी परियोजना, आईओसीएल' तथा 'बीपीसीएल/एचपीसीएल से यूरान एलपीजी संयंत्र तक एलपीजी के हस्तांतरण हेतु पाईपलाइन, बीपीसीएल' में कानून तथा व्यवस्था की समस्याओं और ऑफशोर सेक्शन में पड़े हुए ऑप्टिकल फाइबर में अत्यधिक नुकसान के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'मधुबन में डिहाइड्रेशन सुविधा तथा इफ्लूएन्ट ट्रीटमेंट संयंत्र के साथ द्वितीयक टैंक फार्म, ऑयल' में नौहोलिया में भूमि संबंधी लड़ाई के कारण 3 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'वीकेपीएल नवीकरण तथा स्परलाइन लेईंग (भिलवाड़ा तथा चितौड़गढ़ के लिए), गेल' में स्थल पर भू-वैज्ञानिक स्थिति के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'केन्द्रीय गैस गैदरिंग स्टेशन तथा ऑफटेक बिन्दु, ऑयल' में राष्ट्रीय वन्य जीव बोर्ड (एनबीडब्ल्यूएल) से अनुमति प्राप्त करने में हुए विलंब के कारण 5 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'अहमदाबाद पुनर्विकास परियोजना' में भूमि अधिग्रहण में विलंब के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना '23 इमिडिएट आपूर्ति वेसल्स (आईएसवी) का निर्माण, ओएनजीसी' में सीमा शुल्क संबंधित मुद्दों के कारण 7 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'नहरकटिया-बरौनी कूड ऑयल ट्रंक पाइप लाइन के कूड ऑयल पम्प स्टेशनों का नवीनीकरण, ऑयल' में निविदा आमंत्रण के कारण 8 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'अंकलेश्वर पुनर्विकास परियोजना, ओएनजीसी' में कार्यों के आवंटन में परिवर्तन के कारण 24 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है।

vii) विद्युत क्षेत्र में, 101 परियोजनाओं में से 64 परियोजनाएं विलंबित हैं। माह के दौरान, 12 परियोजनाओं के संबंध में 1-15 माह तक के अतिरिक्त विलंब की सूचना प्राप्त हुई है, जिनमें से 8 मेगा परियोजनाएं हैं। परियोजनाएं 'डीवीसी तथा मैथून आरबीसी के साथ जुड़ी हुई सप्लीमेन्टरी ट्रान्समिशन, पीजीसीआईएल' तथा 'डीवीसी तथा मैथून आरबीसी के साथ 765 केवी पूर्लिंग स्टेशन तथा नेटवर्क, पीजीसीआईएल' में माओवादी समस्याओं के कारण प्रत्येक में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'एसआर ग्रिड की व्यवस्था का सुदृढीकरण XIII, पीजीसीआईएल' तथा 'उत्तरी क्षेत्र की व्यवस्था का सुदृढीकरण योजना-XXI, पीजीसीआईएल' में आरओयू/आरओडब्ल्यू समस्याओं के कारण क्रमशः 1 तथा 15 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'मगरवाड़ा में 400/220 केवी जीआईएस उपस्टेशन की स्थापना के लिए पारेषण प्रणाली, पीजीसीआईएल' में जीआईएस उपकरणों की जांच में विलंब के कारण 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'उड़ीसा भाग-बी में चरण-1 जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' तथा 'उड़ीसा भाग-सी में चरण-1 जनरेशन परियोजनाओं के लिए पारेषण प्रणाली, पीजीसीआईएल' में वन संबंधी अनुमति में विलंब के कारण प्रत्येक में 2 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'बाढ़-II टीपीएस के साथ इमिडिएट इवैक्युशन प्रणाली, पीजीसीआईएल' में नीची सतह वाले क्षेत्र में पानी भरने के कारण 4 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजनाएं 'छत्तीसगढ़ में आईपीपी परियोजनाओं के लिए रायपुर-वर्धा कॉरीडोर में व्यवस्था का सुदृढीकरण' तथा 'मुन्दरा अल्ट्रा मेगा विद्युत परियोजना के साथ जुड़ी हुई पारेषण प्रणाली, पीजीसीआईएल' में वन संबंधी अनुमति में विलंब के कारण 5 तथा 9 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'छत्तीसगढ़ में आईपीपी जनरेशन परियोजना के लिए चंपा तथा रायगढ़ में पूर्लिंग स्टेशनों की स्थापना, पीजीसीआईएल' में संविदात्मक मुद्दों के कारण 6 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है; परियोजना 'कृष्णपटनम यूएमपीपी-भाग सी 1 के साथ जुड़ी हुई पारेषण प्रणाली, पीजीसीआईएल' में 1 माह के अतिरिक्त विलंब की सूचना प्राप्त हुई है (तथापि, इन परियोजनाओं में विलंब के लिए परियोजना प्राधिकारियों द्वारा कोई विशेष कारण सूचित नहीं किया गया है)।

11. दिनांक 31.08.2014 की स्थिति के अनुसार, विभिन्न क्षेत्रों में `150 करोड़ तथा अधिक लागत वाली परियोजनाओं के संबंध में स्थिति रिपोर्ट में सूचित की गई है।
12. इसे सचिव, सांख्यिकी और कार्यक्रम कार्यान्वयन मंत्रालय का अनुमोदन प्राप्त है।

EXECUTIVE SUMMARY

1. The Flash Report for August 2014 contains information on the status of the 720 Central Sector Infrastructure Projects costing ₹150 crore and above. During August 2014, 3 projects (2 projects in Petroleum and 1 project in Shipping & Ports Sector) have reported completion.

2. During the reference month, out of 720 projects, 295 projects are delayed with respect to original schedule and 42 projects have reported additional delays vis-à-vis the date of completion reported in the previous month. Of these 42 projects, 17 are Mega Projects costing ₹1000 crore and above.

S. No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additionally delayed during the month under report	Additionally delayed Mega Projects
1.	RAILWAYS	288	32	7	2
2.	ROAD TRANSPORT AND HIGHWAYS	136	92	0	0
3.	POWER	101	64	12	8
4.	PETROLEUM	75	43	10	5
5.	COAL	59	34	4	1
6.	STEEL	20	16	6	1
7.	SHIPPING AND PORTS	18	3	1	0
8.	CIVIL AVIATION	8	3	2	0
9.	URBAN DEVELOPMENT	5	1	0	0
10.	ATOMIC ENERGY	4	4	0	0
11.	TELECOMMUNICATIONS	4	3	0	0
12.	PETROCHEMICALS	1	0	0	0
13.	WATER RESOURCES	1	0	0	0
Total		720	295	42	17

3. Total original cost of implementation of the 720 projects was ₹9,27,317.65 crore and their anticipated completion cost is likely to be ₹11,04,729.32 crore, which reflects overall cost overruns of ₹1,77,411.67 crore (19.10 % of original cost). The expenditure incurred on these projects till August 2014 is ₹5,46,379.88 crore, which is 49.50 % of the anticipated cost of the projects. The 5 projects with the maximum percentage cost overruns are as follows:-

LIST OF 5 PROJECTS HAVING MAXIMUM PERCENTAGE COST OVERRUNS(as on 31-08-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		COST OVERRUNS (in %)
				ORIGINAL	ANTICIPATED	
1	NANGALDAM-TALWARA(NL),NR	RAILWAYS	03/1981	37.68	1036.78	2651.54
2	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	RAILWAYS	04/1983	36.80	703.18	1810.82
3	BANKURA - DAMODAR (GC) (SER)	RAILWAYS	03/1998	111.90	1423.98	1172.55
4	AKOLA-KHANDWA GC AKOLA-AKOT	RAILWAYS	04/2008	184.26	2000.00	985.42
5	BANGLORE SATYAMANGALAM (NL)(SWR)	RAILWAYS	02/1999	138.00	1382.78	902.01

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

4. The 5 projects with maximum cost overruns in absolute terms are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM COST OVERRUNS(as on 31-08-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹; crore)		
				ORIGINAL	ANTICIPATED	COST OVERRUNS
1	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	2500.00	20000.00	17500.00
2	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	COAL	06/2008	1188.31	7612.33	6424.02
3	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	5996.00	5268.44
4	BANGALORE METRO RAIL PROJECT	URBAN DEVELOPMENT	05/2006	6395.00	11609.00	5214.00
5	BARH STPP(3X660MW) NTPC	POWER	12/2003	8692.97	13737.00	5044.03

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further cost overruns.

5. Out of the 720 projects, 6 projects are ahead of schedule, 105 are on schedule and 295 are delayed with respect to original schedule. However, the number of delayed projects decreases to 274 if delay is calculated on the basis of latest schedule of completion. Further, 19 projects have been sanctioned without any commissioning schedule/date and for 295 projects neither the year of commissioning nor the tentative gestation period has been reported. Out of 295 delayed projects, 63 projects have overall delay in the range of 1 to 12 months, 66 projects have delay in

the range of 13 to 24 months, 97 projects have delay in the range of 25 to 60 months and 69 projects have delay of 61 months and above. The 5 projects with the maximum delay are as below:-

LIST OF 5 PROJECTS HAVING MAXIMUM TIME OVERRUNS (as on 31-08-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		TIME OVERRUNS(in months)
				ORIGINAL	ANTICIPATED	
1	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR)	RAILWAYS	04/1986	03/1994	10/2014	247
2	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	RAILWAYS	03/1984	03/1995	03/2015	240
3	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAYS	03/1995	11/2002	12/2017	181
4	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	RAILWAYS	03/1996	03/2004	03/2016	144
5	RANCHI-LOHARDAGA(GC),SER	RAILWAYS	04/1997	06/2004	06/2015	132

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to avoid further time overruns.

6. In April 2014, out of 727 projects on the monitor of this Ministry, 235 projects reported cost overruns and 282 projects reported time overruns; while during August 2014, out of 720 projects, 212 projects reported cost overruns and 295 projects reported time overruns. In comparison to April 2014, number of projects reporting cost overruns has gone down from 32% to 29% whereas projects reporting time overruns have increased to 41% from 39% (Annexure 6 (a) & 6 (b)).

7. The brief reasons for time overruns as reported by various project implementing agencies are delay in land acquisition, delay in forest clearance, delay in supply of equipments, fund constraints, geological surprises, problems in equipment erection, geo-mining conditions,

slow progress in civil works, shortage of labour, inadequate mobilization by the contractor, maoist problems, court cases, contractual issues, ROU/ROW problems, law and order situation, etc.

8. The Online Computerized Monitoring System (OCMS) owned by this Ministry envisages monitoring of milestones drawn from the PERT Charts of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The earliest initiated 5 projects in which project agencies are not providing milestones are as follows:-

List of 5 Earliest Projects without Milestones(as on 31-08-2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	COST OF PROJECT (₹ ; crore)		CUMULATIVE EXPENDITURE (₹ ; crore)	DATE OF COMMISSIONING		MILESTONES
				ORIGINAL	ANTICIPATED		ORIGINAL	ANTICIPATED	
1	HOWRAH-AMTA-CHAMPADANGA NL (SER)	Railways	04/1974	31.42	535.40	176.52	03/2007	03/2015	N.R.
2	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	37.68	1036.78	353.41	07/2012	N.R.	N.R.
3	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT	Railways	04/1983	36.80	703.17	247.74	N.R.	03/2015	N.R.
4	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS)	Railways	03/1984	520.00	634.13	555.27	03/1995	03/2013	N.R.
5	TAMLUK DIGHA, LINE DOUBLING (SER)	Railways	03/1984	293.97	1074.47	433.89	06/2005	06/2016	N.R.

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up milestones.

9. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The earliest initiated 5 projects in which project agencies are not reporting/providing revised cost estimates are as follows:-

List of 5 Earliest Projects without Revised Cost Estimates (as on 31-08-2014)

S N	PROJECT	SECTOR	DATE OF APPROVA L	COST OF PROJECT (₹, crore)		CUMULATIVE EXPENDITURE (₹, crore)
				ORIGINAL	REVISED	
1	VIRAMGAM-BHILDI(WR),GC	RAILWAY S	04/1990	155.66	N.R.	200.42
2	RAJKOTVERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAY S	04/1994	320.66	N.R.	462.18
3	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	RAILWAY S	12/1994	124.43	495.68	688.63
4	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	RAILWAY S	03/1995	2500.00	2500.00	8805.00
5	DALLI-RAJHARA-RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL	RAILWAY S	04/1995	304.00	N.R.	138.39

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised cost estimates.

The earliest initiated 5 projects in which project agencies are not reporting/providing or updating revised commissioning schedules are as below:-

List of 5 Earliest Projects without Revised Commissioning Schedule(as on 31.08.2014)

SN	PROJECT	SECTOR	DATE OF APPROVAL	DATE OF COMMISSIONING		
				ORIGINAL	REVISED	ANTICIPATED
1	NANGALDAM-TALWARA(NL),NR	Railways	03/1981	07/2012	N.R.	N.R.
2	VIRAMGAM-BHILDI(WR),GC	Railways	04/1990	N.R.	03/2010	N.R.
3	AMRAVATI-NARKHER NL(CR)	Railways	06/1994	06/1999	03/2011	03/2011
4	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR)	Railways	12/1994	N.R.	N.R.	03/2012
5	KOTTUR-HARIHAR(NL),(SWR)	Railways	04/1995	N.R.	N.R.	12/2012

N.R.: Not Reported.

N.B.: The Chief Executive of the Project Implementing Agency and the Secretary and Financial Advisor of the concerned administrative Ministry may like to take a special review of these Projects in order to firm-up revised commissioning schedule.

10. The Sector-wise details of additional delays are as under:-

i) In the **Shipping & Ports Sector**, out of 18 projects, 3 projects are delayed. During the month project, namely 'Acquisition of Two(2) Nos. of 317000 DWT Very Large Crude Carriers from M/s Jiangsu Rongsheng Heavy Shipping Corporation of India' has reported additional delay of 9 months due to contractual issue.

ii) In the **Civil Aviation Sector**, out of 8 projects, 3 projects are delayed. During the month 2 projects has reported additional delays of 1 and 3 months. The project 'Construction of New International Terminal Building (Goa), AAI' has reported additional delay of 1 month due to change in structural design of foundation and shortage of labour; and the project 'Establishment of Airport Operations Control Centres at 10 Airports, AAI' has reported additional delay of 3 months due to delay in supply of equipments.

iii) In the **Coal Sector**, out of 59 projects, 34 projects are delayed. During the month, 4 projects have reported additional delay in the range of 5-72 months, out of which 1 is Mega project. The project 'Adriyala Shaft Project SCCL' has reported additional delay of 5 months due to delay in supply of equipments; the project 'Kakatiya Longwall, SCCL' has reported additional delay of 12 months due to induction of Technology Provider cum Operator (TPO) for longwall technology; the project 'Jalagam Vengala Rao OCP-II, SCCL' has reported additional delay of 36 months due to delay in forest clearance and land acquisition; and the project 'Gopal Prasad OCP (15MTY), MCL' has reported additional delay of 72 months (however, no specific reasons have been reported by the project implementing agency for the delay in this project).

iv) In the **Steel Sector**, out of 20 projects, 16 projects are delayed. During the month, 6 projects have reported additional delays in the range of 1-3 months, out of which 1 is Mega project. The project 'Coke Oven Battery No. 4 Phase-II, RINL' has reported additional delay of 1 month due to geological condition at site; the projects 'Expansion of Liquid Steel Capacity from 3MT to 6.3MT, RINL' and 'Augmentation of Iron ORE Storage in RMHP, RINL' have reported additional delays of 2 and 3 months respectively due to delay in supply of materials; the project 'Bailadila Iron ORE Project Deposit- 11B, NMDC' has reported additional delay of 2 months due to naxalites problems; and the project '7.0 MTPA Kumaraswamy Iron ORE Mine Project, NMDC' and '1.2 MTPA Pellet Plant Project, Donimalai, NMDC' have reported additional delays of 2 and 3 months respectively (however, no specific reasons have been reported by the project implementing

agency for the delay in these projects).

v) In the **Railway Sector**, out of 288 projects, 32 projects are delayed. During the month, 7 projects have reported additional delays in the range of 1-24 months, out of which 2 are Mega projects. The project 'Guna-Etawah VIA Shivpuri-Gwalior -Bhind NL, NCR' has reported additional delay of 1 month due to occurrence of cracks in piers; The projects 'Chengalpattu-Villupuram Doubling with New MM for Tambaram-Chengalpattu 3rd Line GC Alongwith Electrification, SR' and 'Ramanagram-Mysore Doubling with Electrification of Kengesii- Musore, SWR' have reported additional delays of 3 and 24 months due to delay in land acquisition; the project 'New Work for Construction of Metro Railway from Baranagar to Barrackpore and Dakshineswar (MTP), RVNL' has reported additional delay of 24 months due to shifting of utilities by state Government; and the projects 'Gonda-Gorakhpur Loop with Anand Nagar-Nautanwa GC, NER', 'Etawah-Mainpuri (NL), NCR' And 'Electrification of Khurja-Meerut-Saharanpur and Ghaziabad-Meerut, RE' (however, no specific reasons have been reported by the project implementing agencies for the delay in these projects).

vi) In the **Petroleum Sector**, out of 75 projects, 43 projects are delayed. During the month, 10 projects have reported additional delays in the range of 1-24 months, out of which 5 are Mega projects. The project 'Petrochemical Complex-II at Vijaypur and Pata, GAIL' has reported additional delay of 1 month due to fund constraint with the contractor; the project 'Paradip Refinery Project, IOCL' and 'Pipeline For Transfer of LPG from BPCL/HPCL to Uran LPG Plant, BPCL' have reported additional delays of 2 months each due to law and order problems and multiple damage in optical fiber cables laid in offshore section; the project 'Secondary Tank Farm with Dehydration Facility and Effluent Treatment Plant at Madhuban, OIL' has reported additional delay of 3 months due to land litigation at Naoholia; the project 'VKPL Upgradation and Laying of Spurline (to Bhilwara and Chittorgarh), GAIL' has reported additional delay of 4 months due to geological condition at site; the project 'Central Gas Gathering Station and Offtake Point, OIL' has reported additional delay of 5 months due to delay in getting permission of National Board of Wild Life (NBWL) the project 'Ahmedabad Redevelopment Project, has reported additional delay of 6 months due to delay in land acquisition; the project 'Construction of 23 Immediate Supply Vessels (ISV), ONGC' has reported additional delay of 7 months due to custom bond issues; the project 'Upgradation of Crude Oil Pump Stations of Naharkatiya-Barauni Crude Oil Trunk Pipeline, OIL' has reported additional delay of 8 months due to refloating of tender; and the project 'Ankleswar Redevelopment, ONGC' has reported additional delay of 24 months due to change in scope of works.

vii) In the Power Sector, out of 101 projects, 64 projects are delayed. During the month 12 projects have reported additional delays in the range of 1-15 months, out of which 8 are Mega projects. The projects 'Supplementary Transmission Associated with DVC and Maithon RBC, PGCIL' and '765 Kv Pooling Station And Network with DVC and Maithon RBC, PGCIL' have reported additional delays of 1 month each due to Maoist problems; the projects 'System Strengthening XIII of SR Grid, PGCIL' and 'Northern Region System Strengthening Scheme-XXI PGCIL' have reported additional delays of 1 and 15 months respectively due to ROU/ROW problems; the project 'Transmission System for Establishment of 400/220 KV GIS Substation at Magarwada, PGCIL' has reported additional delay of 1 month due to delay in testing of GIS equipments; the projects 'Transmission System for Phase-I Generation Projects in Orissa-Part B, PGCIL' and 'Transmission System for Phase-I Generation Project in Orissa Part-C, PGCIL' have reported additional delays of 2 months each due to delay in forest clearance; the project 'Immediate Evacuation System with Barh-II TPS, PGCIL' has reported additional delay of 4 months due to submergence in low lying; the projects 'System Strengthening in Raipur-Wardha Corridor for IPP Projects in Chhattisgarh, PGCIL' and 'Transmission System Associated with Mundra Ultra Mega Power Project, PGCIL' have reported additional delays of 5 and 9 months due to delay in forest clearance; the project 'Establishment of Pooling Stations at Champa and Raigarh for IPP Generation Project in Chhattisgarh, PGCIL' has reported additional delay of 6 months due to contractual issues; and the project 'Transmission System Associated with Krishnapatnam UMPP-Part C1, PGCIL' has reported additional delay of 1 month (however, no specific reasons have been reported by the project implementing agency for the delay in this project).


11. The status as on 31.08.2014 in respect of projects costing ₹150 crore and above in the various sectors is indicated in the Report.

12. This has the approval of Secretary, Ministry of Statistics and Programme Implementation.

EXECUTIVE SUMMARY

Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	288	7
2	ROAD TRANSPORT AND HIGHWAYS	136	0
3	POWER	101	12
4	PETROLEUM	75	10
5	COAL	59	4
6	STEEL	20	6
7	SHIPPING AND PORTS	18	1
8	CIVIL AVIATION	8	2
9	URBAN DEVELOPMENT	5	0
10	ATOMIC ENERGY	4	0
11	TELECOMMUNICATIONS	4	0
12	PETROCHEMICALS	1	0
13	WATER RESOURCES	1	0
	Total	720	42

Sectoral break up of on-going infrastructure projects.

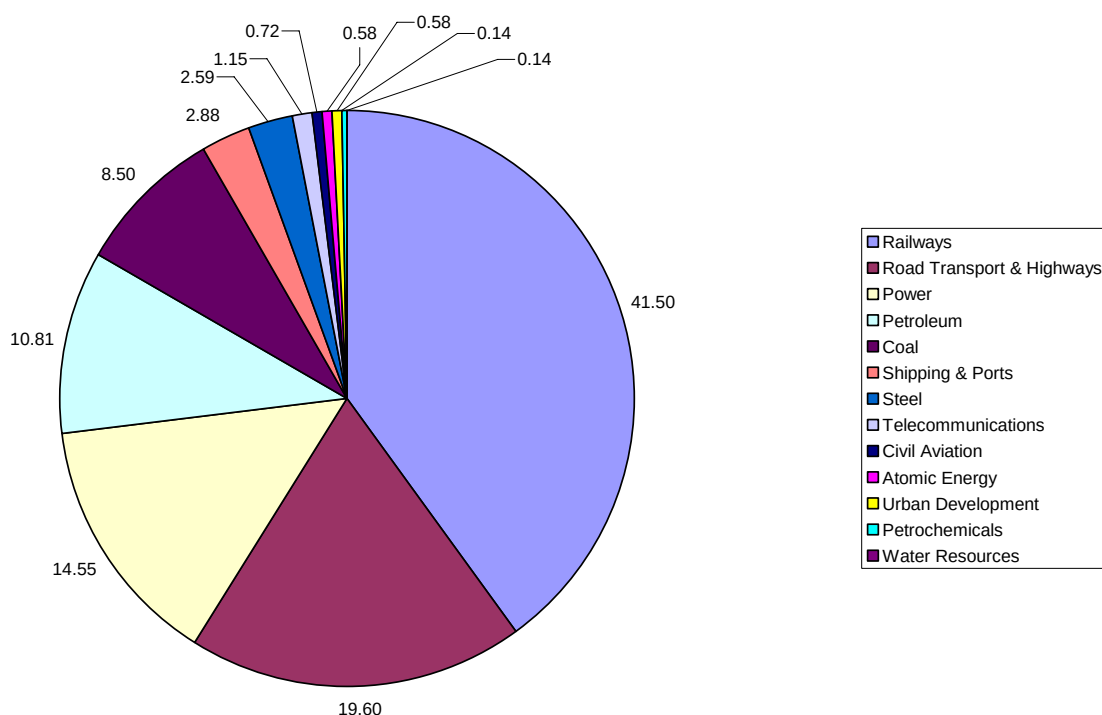

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2014			
	<u>COAL</u>			
1	BINA EXTN. PROJ(6.0 MTPA) (NORTHERN COAL FIELDS LIMITED) - [N06000019]	168.97	03/2014	67.53
	<u>POWER</u>			
2	PARBATI H.E.P. STAGE -III (NHPC) (NATIONAL HYDRO-ELECTRIC POWER CORPORATION) - [180100250]	2,304.56	10/2010	2349.46
	June,2014			
	<u>PETROLEUM</u>			
3	MUMBAI HIGH SOUTH REDEVELOPMENT PH-2 (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000039]	5,713.03	05/2010	3918.86
4	DEVELOPMENT OF B-46 CLUSTER FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000046]	1,436.21	07/2010	1165.53
5	MUMBAI HIGH NORTH DEVELOPMENT PHASE-II (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000060]	7,133.39	09/2012	2795.5
	<u>POWER</u>			
6	MOUDA STPP (NATIONAL THERMAL POWER CORPORATION) - [N18000048]	5,459.28	08/2012	4056
7	VINDHYACHAL STTP STAGE-IV (NATIONAL THERMAL POWER CORPORATION) - [N18000072]	5,915.00	10/2012	N.A.
8	RIHAND STTP STAGE-III (2X500MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000073]	6,230.81	10/2012	4357
	<u>RAILWAYS</u>			
9	CONSTRUCTION OF NEW LINE FROM HARMATI- ITANAGAR/NARHARIAGUN, NEFR (NORTH EAST FRONTIER RAILWAY) - [N22000083]	156.00	-	424.43
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	VIJAYAPUR TO PATHANKOT (NS-35/J AND K) NH-1A KM.50 TO KM.80 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [240106236]	166.27	03/2008	200.4
11	CHITRADURGA-TUMKUR(NH-4) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000157]	839.00	-	692.5
	July,2014			
	<u>STEEL</u>			
12	67.5 MW TG-5 AUX. S'TEM EMERGENCY POWER REQUIREMENT EXP. UNIT (RASTRIYA ISPAT NIGAM LIMITED) - [N12000068]	202.00	01/2010	294.84

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2014-2015

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
13	330 TPH BOILER-6 AND AUXILIARY SYSTEM (RASTRIYA ISPAT NIGAM LIMITED) - [N12000069]	260.00	12/2009	260.75
	<u>PETROLEUM</u>			
14	DEVELOPMENT OF C-SERIES FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000023]	3,195.16	12/2008	3886.15
15	DEVELOPMENT OF B-22 CLUSTER FIELDS (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000032]	2,323.40	09/2010	1916.1
16	DIESEL HYDROTREATOR PROJECT AT MUMBAI REFINERY (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000069]	3,284.00	09/2011	1916.3
17	ADDITIONAL DEV. OF D-1 FIELD (OIL & NATURAL GAS CORPORATION LIMITED) - [N16000086]	2,163.64	06/2012	2182.31
	<u>POWER</u>			
18	TRANSMISSION SYSTEM FOR CONNECTIVITY OF MB POWER LIMITED (POWER GRID CORPORATION OF INDIA LIMITED) - [N18000106]	425.51	10/2013	386.32
	<u>TELECOMMUNICATIONS</u>			
19	GSM EQUIPMENT OF 390K LINES(2G) AND 130K LINES(3G) PH-5.1 PUNJAB (BHARAT SANCHAR NIGAM LIMITED) - [N26000041]	373.94	12/2008	227.58
20	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK.PROCUREMENT OF GPON EQUIPMANT (BHARAT SANCHAR NIGAM LIMITED) - [N26000072]	952.88	03/2010	N.A.
21	IMPLEMENTATION OF FTTH, THE STATE OF THE ART ACCESS NETWORK,PROCUREMENT OF GEON EQUIPMENT (BHARAT SANCHAR NIGAM LIMITED) - [N26000073]	152.65	03/2010	N.A.
22	GSM EQUIPMENT OF 799000LINES (2G) 101000 LINES 3(G) JHARKHANDPHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000088]	328.13	03/2009	164.58
23	GSM EQUIPMENT OF 1625000LINES (2G) 325000 LINES 3(G) MP PHASE V.1 TELECOM CIRCLE (BHARAT SANCHAR NIGAM LIMITED) - [N26000090]	916.70	11/2010	828.48
	August,2014			
	<u>PETROLEUM</u>			
24	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I (GAS AUTHORITY OF INDIA LIMITED) - [N16000070]	238.68	01/2012	293.12
25	SINGLE POINT MOORING FACILITY(SMP) PROJECT (MANGALORE REFINERY AND PETROCHEMICALS LIMITED) - [N16000152]	1,043.57	04/2012	648.92
	<u>SHIPPING AND PORTS</u>			
26	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN (PORT TRUST) - [N25000048]	3,500.00	01/2012	3661.95


Summary of projects in the Flash Report for the month of August, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	720
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	2
Number of Projects in Current Month	720


Brief Analysis

Project Status with respect to Original Schedule: Out of 720 projects, 6 projects are ahead of schedule, 105 projects are on schedule and 295 projects are delayed. Of the balance, 295 projects do not have fixed dates of commissioning while 19 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

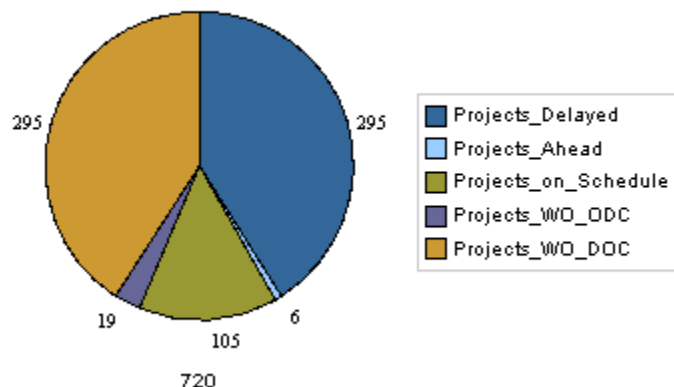

Investment Scenario

Total original cost of implementation of 720 projects when sanctioned, was of the order of Rs. 927317.65 crore but this was subsequently revised to Rs. 1104729.32 crore implying a cost overrun of 19.1%. The expenditure incurred on these projects till August, 2014 is Rs. 546379.88 crore, which is 49.5% of the revised cost of the projects.

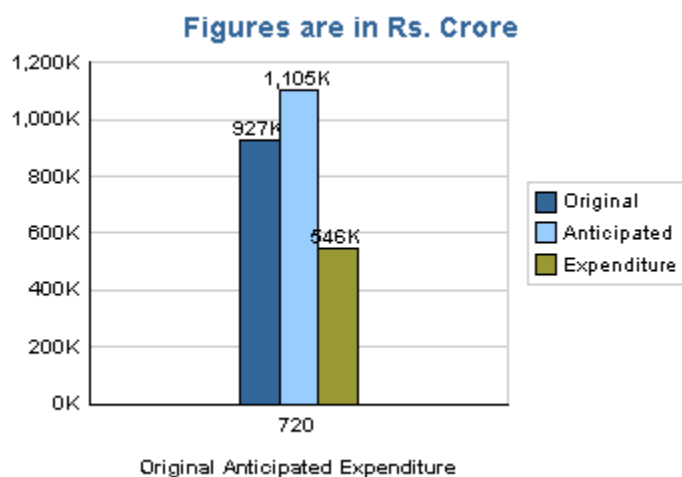

Projects Added / Completed / Dropped / Frozen

No of Projects in Previous Month	720
No of Projects Completed/Dropped/Frozen in Current Month	3
No of Projects elevated o the status of major project during the current month	1
No of Projects added in Current Month	2
No of Projects in Current Month	720

Project status							
Number of Projects							
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total	Delayed Projects (%)
Original (Date)	295	6	105	19	295	720	40.97
Latest Approved (Date)	274	13	119	19	295	720	38.06

Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	630	7,86,494.35	8,74,851.35	4,03,763.85	46.20	88,357.00	11.20
Project with Revision in Cost	90	1,88,476.42	2,29,877.97	1,42,616.03	62.00	41,401.55	22.00
Total	720	9,74,970.77	11,04,729.32	5,46,379.88	49.46	129758.55	13.31
Original Cost of All Projects							
Original Cost	720	9,27,317.65	11,04,729.32	5,46,379.88	49.50	1,77,411.67	19.10

Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	295	548,838.05	650,274.08	417,343.89	64.20	101,436.03	18.50
Latest Approved (RCE)	275	554,818.67	617,598.58	402,473.72	65.20	62,779.91	11.30

Additional Delayed Project cost							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% cost w.r.t anticipated cost	Rs crore	%
Latest Approved	42	90,715.61	103,264.42	77,948.26	75.50	12,548.81	13.80

Extent of cost overrun in projects with respect to original schedule(Sector Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	2	16,663.0	22,947.0	37.7
2	CIVIL AVIATION	8	6,035.5	6,926.8	14.8	3	4,086.1	4,977.5	21.8
3	COAL	59	41,532.1	51,354.2	23.6	8	9,767.8	20,187.6	106.7
4	STEEL	20	66,395.1	72,349.1	9.0	4	23,538.9	29,522.9	25.4
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	75	177,359.0	192,956.7	8.8	17	58,563.1	78,426.6	33.9
7	POWER	101	235,782.3	249,446.6	5.8	14	34,911.1	48,575.5	39.1
8	RAILWAYS	288	163,318.1	275,005.7	68.4	143	69,972.6	181,991.4	160.1
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.4	104,296.5	1.9	8	2,649.0	4,651.6	75.6
10	SHIPPING AND PORTS	18	12,117.1	14,450.6	19.3	8	5,129.0	7,766.7	51.4
11	TELECOMMUNICATIONS	4	2,018.2	1,843.9	-8.6	1	149.2	158.7	6.4
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	2	6,509.2	11,782.1	81.0
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		720	927,317.7	1,104,729.3	19.1	212	237,942.5	421,094.4	77.0

Extent of cost overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overrun			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	20	24,072.7	29,249.2	21.5	7	10,837.4	16,880.9	55.8
2	ARUNACHAL PRADESH	3	9,356.2	12,067.7	29.0	2	3,070.9	5,782.3	88.3
3	ASSAM	38	26,930.7	41,646.2	54.6	15	13,124.3	27,929.0	112.8
4	BIHAR	46	34,128.2	40,874.2	19.8	14	13,719.7	20,686.1	50.8
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	15.8
6	GUJARAT	31	37,705.2	38,531.3	2.2	6	2,786.3	3,932.7	41.1
7	HARYANA	9	4,540.9	6,690.9	47.3	3	1,633.6	3,783.5	131.6
8	HIMACHAL PRADESH	5	13,457.4	20,758.1	54.2	4	11,540.7	18,841.3	63.3
9	JAMMU AND KASHMIR	6	13,202.5	30,702.5	132.6	1	2,500.0	20,000.0	700.0
10	KARNATAKA	33	77,723.9	92,714.6	19.3	18	14,297.2	29,539.7	106.6
11	KERALA	11	19,110.7	23,264.4	21.7	5	16,205.4	20,359.2	25.6
12	MADHYA PRADESH	16	23,264.0	24,732.7	6.3	4	2,145.0	4,033.1	88.0
13	MAHARASHTRA	44	70,756.2	82,782.9	17.0	14	16,502.4	29,176.9	76.8
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	724.1
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	0	0.0	0.0	0.0
16	MIZORAM	2	988.1	3,307.1	234.7	2	988.1	3,307.1	234.7
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	187.8
18	ODISHA	36	62,065.4	70,718.5	13.9	11	32,706.7	41,359.7	26.5
19	PUNJAB	3	1,306.3	1,279.2	-2.1	0	0.0	0.0	0.0
20	RAJASTHAN	25	25,638.7	25,695.9	0.2	6	2,613.5	3,156.8	20.8
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	1,339.5	3,375.4	152.0
22	TAMIL NADU	40	54,818.7	71,711.4	30.8	21	31,836.2	48,728.9	53.1
23	TRIPURA	6	2,966.3	4,780.6	61.2	3	2,129.4	3,978.1	86.8
24	UTTAR PRADESH	25	14,024.7	16,666.2	18.8	8	2,768.5	5,458.2	97.2
25	WEST BENGAL	38	57,186.3	65,301.4	14.2	9	22,482.8	30,597.9	36.1
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	0.0
27	DELHI	4	41,531.3	41,531.3	0.0	0	0.0	0.0	0.0
28	CHHATISGARH	26	58,226.6	65,735.3	12.9	6	2,585.1	10,093.7	290.5
29	JHARKHAND	29	21,180.9	21,745.6	2.7	4	1,235.0	1,971.5	59.6
30	UTTARAKHAND	7	9,501.0	13,063.9	37.5	5	7,496.0	11,058.9	47.5
31	TELANGANA	21	9,410.3	12,179.1	29.4	5	1,473.0	4,241.8	188.0
32	MULTI STATE	186	201,091.3	224,912.1	11.8	35	18,012.9	43,990.5	144.2
Total		720	927,317.7	1,104,729.3	19.1	212	237,942.5	421,094.4	77.0

Extent of time overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	4	40,442.0	46,726.0	17 - 71
2	CIVIL AVIATION	8	6,035.5	6,926.8	14.8	3	989.4	1,042.3	10 - 71
3	COAL	59	41,532.1	51,354.2	23.6	34	28,134.6	38,376.3	24 - 120
4	STEEL	20	66,395.1	72,349.1	9.0	16	64,938.5	70,892.5	3 - 73
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	75	177,359.0	192,956.7	8.8	43	117,139.5	133,459.9	3 - 110
7	POWER	101	235,782.3	249,446.6	5.8	64	200,279.8	213,153.7	1 - 113
8	RAILWAYS	288	163,318.1	275,005.7	68.4	32	27,208.1	73,974.1	3 - 247
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.4	104,296.5	1.9	92	63,635.9	65,611.0	2 - 120
10	SHIPPING AND PORTS	18	12,117.1	14,450.6	19.3	3	2,706.3	3,664.9	5 - 51
11	TELECOMMUNICATIONS	4	2,018.2	1,843.9	-8.6	3	870.0	879.5	51 - 71
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		720	927,317.7	1,104,729.3	19.1	295	548,838.1	650,274.1	

Extent of time overrun in projects with respect to original schedule(State Wise)

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	20	24,072.7	29,249.2	21.5	7	13,735.3	17,809.0	11 - 73
2	ARUNACHAL PRADESH	3	9,356.2	12,067.7	29.0	3	9,356.2	12,067.7	25 - 99
3	ASSAM	38	26,930.7	41,646.2	54.6	30	18,889.4	27,049.7	8 - 120
4	BIHAR	46	34,128.2	40,874.2	19.8	11	21,521.1	25,259.7	4 - 98
5	GOA	1	335.6	388.5	15.8	1	335.6	388.5	28 - 28
6	GUJARAT	31	37,705.2	38,531.3	2.2	11	24,598.1	24,536.8	6 - 48
7	HARYANA	9	4,540.9	6,690.9	47.3	2	1,594.0	2,774.0	40 - 55
8	HIMACHAL PRADESH	5	13,457.4	20,758.1	54.2	3	10,493.8	15,874.3	30 - 106
9	JAMMU AND KASHMIR	6	13,202.5	30,702.5	132.6	6	13,202.5	30,702.5	6 - 181
10	KARNATAKA	33	77,723.9	92,714.6	19.3	8	32,425.5	33,061.4	15 - 48
11	KERALA	11	19,110.7	23,264.4	21.7	5	17,074.0	20,053.0	5 - 58
12	MADHYA PRADESH	16	23,264.0	24,732.7	6.3	8	14,759.0	14,871.8	6 - 74
13	MAHARASHTRA	44	70,756.2	82,782.9	17.0	17	37,339.3	44,104.0	3 - 144
14	MANIPUR	1	727.6	5,996.0	724.1	1	727.6	5,996.0	84 - 84
15	MEGHALAYA	3	4,845.0	4,845.0	0.0	1	536.0	536.0	11 - 11
16	MIZORAM	2	988.1	3,307.1	234.7	2	988.1	3,307.1	71 - 113
17	NAGALAND	2	5,124.0	6,720.6	31.2	1	850.0	2,446.6	60 - 60
18	ODISHA	36	62,065.4	70,718.5	13.9	22	53,577.0	58,654.4	3 - 84
19	PUNJAB	3	1,306.3	1,279.2	-2.1	1	705.0	705.0	21 - 21
20	RAJASTHAN	25	25,638.7	25,695.9	0.2	7	17,752.0	17,305.7	2 - 77
21	SIKKIM	2	1,648.9	3,684.9	123.5	1	309.5	309.5	71 - 71
22	TAMIL NADU	40	54,818.7	71,711.4	30.8	13	35,894.9	44,873.9	6 - 71
23	TRIPURA	6	2,966.3	4,780.6	61.2	4	2,417.4	4,231.8	16 - 108
24	UTTAR PRADESH	25	14,024.7	16,666.2	18.8	12	5,982.0	7,488.9	2 - 93
25	WEST BENGAL	38	57,186.3	65,301.4	14.2	11	29,900.9	31,917.8	3 - 96
26	CHANDIGARH	1	452.0	452.0	0.0	0	0.0	0.0	-
27	DELHI	4	41,531.3	41,531.3	0.0	1	2,494.0	2,494.0	8 - 8
28	CHHATISGARH	26	58,226.6	65,735.3	12.9	17	54,882.4	61,617.8	5 - 120
29	JHARKHAND	29	21,180.9	21,745.6	2.7	15	11,283.8	11,871.9	3 - 132
30	UTTARAKHAND	7	9,501.0	13,063.9	37.5	6	9,281.2	12,734.0	7 - 94
31	TELANGANA	21	9,410.3	12,179.1	29.4	6	2,345.9	3,545.8	24 - 48
32	MULTI STATE	186	201,091.3	224,912.1	11.8	62	103,586.7	111,685.7	1 - 247
Total		720	927,317.7	1,104,729.3	19.1	295	548,838.1	650,274.1	

Extent of time overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time overruns			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.0	46,726.0	15.5	3	36,950.0	41,049.0	17 - 71
2	CIVIL AVIATION	8	6,035.5	6,926.8	14.8	3	989.4	1,042.3	10 - 71
3	COAL	59	41,532.1	51,354.2	23.6	33	26,946.3	30,764.0	24 - 84
4	STEEL	20	66,395.1	72,349.1	9.0	16	64,938.5	70,892.5	3 - 73
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	0	0.0	0.0	-
6	PETROLEUM	75	177,359.0	192,956.7	8.8	39	110,018.1	122,968.4	3 - 110
7	POWER	101	235,782.3	249,446.6	5.8	63	197,782.9	208,499.7	1 - 113
8	RAILWAYS	288	163,318.1	275,005.7	68.4	31	26,883.1	72,857.5	3 - 247
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.4	104,296.5	1.9	82	61,683.5	63,533.5	2 - 120
10	SHIPPING AND PORTS	18	12,117.1	14,450.6	19.3	1	1,228.0	2,158.2	51 - 51
11	TELECOMMUNICATIONS	4	2,018.2	1,843.9	-8.6	2	486.0	495.5	63 - 71
12	URBAN DEVELOPMENT	5	73,993.3	79,266.2	7.1	1	2,494.0	2,494.0	8 - 8
13	WATER RESOURCES	1	542.9	1,187.0	118.6	0	0.0	0.0	-
Total		720	927,317.7	1,104,729.3	19.1	274	530,399.7	616,754.6	

Extent of cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with cost overruns			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	46,726.0	46,726.0	0.0	0	0.0	0.0	0.0
2	CIVIL AVIATION	8	6,242.5	6,926.8	11.0	2	2,278.1	2,962.5	30.0
3	COAL	59	51,328.6	51,354.2	0.0	4	1,431.8	1,716.6	19.9
4	STEEL	20	70,414.1	72,349.1	2.7	1	14,443.0	16,408.0	13.6
5	PETROCHEMICALS	1	5,460.6	8,920.0	63.4	1	5,460.6	8,920.0	63.4
6	PETROLEUM	75	190,540.3	192,956.7	1.3	6	36,948.9	42,512.4	15.1
7	POWER	101	236,169.1	249,446.6	5.6	8	23,866.0	37,143.5	55.6
8	RAILWAYS	288	175,278.7	275,005.7	56.9	136	72,322.9	172,381.0	138.3
9	ROAD TRANSPORT AND HIGHWAYS	136	102,859.7	104,296.5	1.4	8	2,992.3	4,651.6	55.5
10	SHIPPING AND PORTS	18	13,338.0	14,450.6	8.3	6	4,617.6	5,941.7	28.7
11	TELECOMMUNICATIONS	4	2,018.2	1,843.9	-8.6	1	149.2	158.7	6.4
12	URBAN DEVELOPMENT	5	74,052.2	79,266.2	7.0	1	6,395.0	11,609.0	81.5
13	WATER RESOURCES	1	542.9	1,187.0	118.6	1	542.9	1,187.0	118.6
Total		720	974,970.8	1,104,729.3	13.3	175	171,448.2	305,591.9	78.2

Extent of time & cost overrun in projects with respect to latest schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 71
2	CIVIL AVIATION	8	6,035.46	6,926.79	14.77	1	1,808.00	2,015.00	13- 13
3	COAL	59	41,532.08	51,354.22	23.65	3	8,123.63	17,242.66	31- 120
4	STEEL	20	66,395.10	72,349.06	8.97	3	9,095.89	13,114.85	39- 73
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	75	177,359.04	192,956.69	8.79	5	7,590.23	17,622.76	10- 110
7	POWER	101	235,782.29	249,446.64	5.80	2	2,078.01	3,973.71	16- 94
8	RAILWAYS	288	163,318.14	275,005.73	68.39	2	279.10	705.11	36- 60
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,296.49	1.93	3	580.65	705.74	59- 80
10	SHIPPING AND PORTS	18	12,117.12	14,450.58	19.26	4	1,900.70	3,408.41	10- 99
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	0	0.00	0.00	0- 0
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		720	927317.65	1104729.32	19.13	25	48119.21	81735.24	

Extent of time & cost overrun in projects with respect to original schedule

(All Cost/ Expenditure in Rs. crore)

						Projects with time & cost overruns			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	40,442.00	46,726.00	15.54	2	16,663.00	22,947.00	54- 71
2	CIVIL AVIATION	8	6,035.46	6,926.79	14.77	1	335.61	388.53	28- 28
3	COAL	59	41,532.08	51,354.22	23.65	6	9,127.17	19,498.95	24- 120
4	STEEL	20	66,395.10	72,349.06	8.97	4	23,538.89	29,522.85	36- 73
5	PETROCHEMICALS	1	5,460.61	8,920.00	63.35	0	0.00	0.00	0- 0
6	PETROLEUM	75	177,359.04	192,956.69	8.79	14	55,561.22	74,783.67	5- 110
7	POWER	101	235,782.29	249,446.64	5.80	11	32,166.65	44,495.60	16- 106
8	RAILWAYS	288	163,318.14	275,005.73	68.39	29	22,340.92	69,106.90	3- 247
9	ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	104,296.49	1.93	8	2,649.01	4,651.57	40- 93
10	SHIPPING AND PORTS	18	12,117.12	14,450.58	19.26	2	2,194.46	3,152.98	11- 51
11	TELECOMMUNICATIONS	4	2,018.15	1,843.90	-8.63	1	149.15	158.72	63- 63
12	URBAN DEVELOPMENT	5	73,993.32	79,266.22	7.13	0	0.00	0.00	0- 0
13	WATER RESOURCES	1	542.90	1,187.00	118.64	0	0.00	0.00	0- 0
Total		720	927317.65	1104729.32	19.13	78	164726.08	268706.77	

List of projects completed/dropped/Frozen during current month							(All Cost /Expenditure in Rs. crore)
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	KARANPUR MORADABAD-KASHIPUR-RUDRAPUR PIPELINE PROJECT PHASE-I	07/2009	238.68	01/2012	312.00	04/2013	293.12
2	SINGLE POINT MOORING FACILITY(SMP) PROJECT	07/2010	1,043.57	04/2012	957.10	12/2013	648.92
	<u>SHIPPING AND PORTS</u>						
3	SETTING UP OF LNG REGASIFICATION TERMINAL AT PUTHUVYPEEN COCHIN	03/2009	3,500.00	01/2012	4,150.00	08/2014	3,661.95

List of projects added					(All Cost in Rs. crore)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>STEEL</u>					
1	UPGRADATION OF BLAST FURNACE-1 AT RSP	6/2014	708.91	4/2016	708.91	4/2016
2	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT	4/2014	188.93	4/2015	188.93	4/2015

Milestones (Cumulative due & achieved)		
Total	3573	
Achieved up to month	1392	

List of projects reporting additional delays							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) AAI	335.61	388.53	05/2012	08/2014	09/2014	1
2	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS AAI	344.28	344.28	03/2014	10/2014	01/2015	3
	<u>COAL</u>						
3	ADRIYALA SHAFT PROJECT SCCL	212.34	1,228.39	03/2013	10/2014	03/2015	5
4	KAKATIYA LONGWALL SCCL	453.63	453.63	12/2012	03/2015	03/2016	12
5	JALAGAM VENGALA RAO OCP-II SCCL	447.06	447.06	03/2015	03/2015	03/2018	36
6	GOPAL PRASAD OCP (15MTY) MCL	395.87	395.87	03/2015	03/2015	03/2021	72
	<u>STEEL</u>						
7	COKE OVEN BATTERY NO. 4 PHASE-II RINL	108.00	216.68	09/2008	09/2014	10/2014	1
8	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) RINL	8,692.00	12,291.00	10/2009	10/2014	12/2014	2
9	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) NMDC	295.89	607.17	12/2011	01/2015	03/2015	2
10	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) NMDC	898.55	898.55	05/2013	01/2015	03/2015	2
11	AUGMENTATION OF IRON ORE STORAGE IN RMHP RINL	480.00	450.00	09/2009	12/2014	03/2015	3
12	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) NMDC	572.00	572.00	04/2013	12/2014	03/2015	3
	<u>PETROLEUM</u>						
13	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA GAIL	8,140.00	8,140.00	02/2014	09/2014	10/2014	1
14	PARADIP REFINERY PROJECT IOCL	29,777.00	34,555.00	11/2012	12/2014	02/2015	2
15	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT BPCL	246.81	276.83	04/2012	08/2014	10/2014	2


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
16	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN OIL	94.00	352.56	09/2012	12/2016	03/2017	3
17	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) GAIL	463.32	330.47	03/2012	03/2015	07/2015	4
18	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT OIL	144.02	204.29	06/2012	07/2014	12/2014	5
19	AHMEDABAD REDEVELOPMENT PROJECT ONGC	1,916.10	1,916.10	12/2014	06/2017	12/2017	6
20	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) ONGC	331.20	269.10	08/2013	10/2014	05/2015	7
21	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE OIL	871.35	1,200.00	03/2015	03/2015	11/2015	8
22	ANKLESWAR REDEVELOPMENT ONGC	2,189.63	2,189.63	12/2014	12/2016	12/2018	24
	<u>POWER</u>						
23	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC PGCIL	2,360.95	2,580.90	08/2012	09/2014	10/2014	1
24	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHON RBC PGCIL	7,075.33	7,075.33	08/2012	08/2014	09/2014	1
25	SYSTEM STRENGTHENING XIII OF SR GRID PGCIL	487.49	487.49	06/2014	11/2014	12/2014	1
26	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD PGCIL	259.28	259.28	01/2014	09/2014	10/2014	1
27	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 PGCIL	324.33	324.33	08/2014	08/2014	09/2014	1
28	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B PGCIL	2,743.19	2,743.19	12/2013	12/2014	02/2015	2
29	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C PGCIL	2,569.25	2,569.25	03/2014	12/2014	02/2015	2
30	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS PGCIL	901.77	901.77	08/2014	08/2014	12/2014	4
31	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH PGCIL	1,422.85	1,422.85	01/2015	01/2015	06/2015	5


List of projects reporting additional delays

Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
32	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH PGCIL	1,961.87	1,961.87	05/2014	09/2014	03/2015	6
33	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT PGCIL	4,824.12	4,824.12	10/2012	03/2015	12/2015	9
34	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI PGCIL	1,677.57	1,677.57	04/2013	12/2014	03/2016	15
	<u>RAILWAYS</u>						
35	GUNA-ETAWAH VIA SHIVPURI-GWALIOR - BHIND NL, (NCR) NCR	158.77	608.02	03/1994	09/2014	10/2014	1
36	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) NER	863.23	1,072.51	N.A.	02/2015	03/2015	1
37	ETAWAH-MAINPURI (NL),NCR NCR	120.00	245.39	12/2008	09/2014	12/2014	3
38	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	247.00	951.24	N.A.	12/2014	03/2015	3
39	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT RE	171.10	272.39	03/2012	10/2014	03/2015	5
40	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) SWR	482.00	874.57	03/2013	03/2014	03/2016	24
41	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) RVNL	2,298.42	2,298.42	03/2014	03/2014	03/2016	24
	<u>SHIPPING AND PORTS</u>						
42	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY SHIPP.	966.46	994.82	02/2014	04/2014	01/2015	9

Graphical Presentation of All Projects w.r.t. Original Schedule

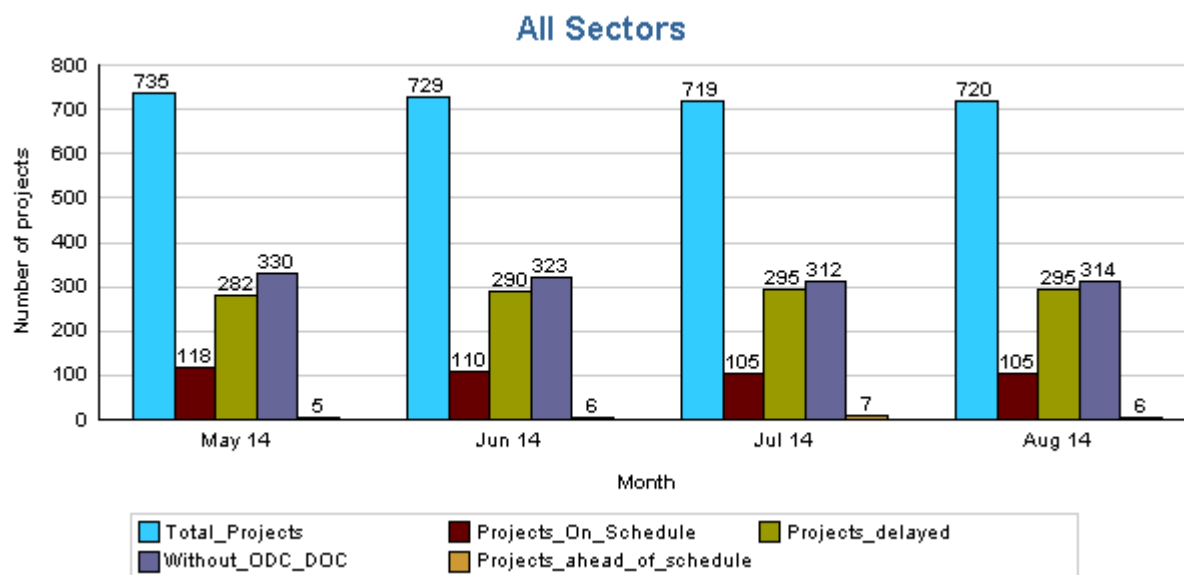

Break-up of 295 Delayed projects in August 2014

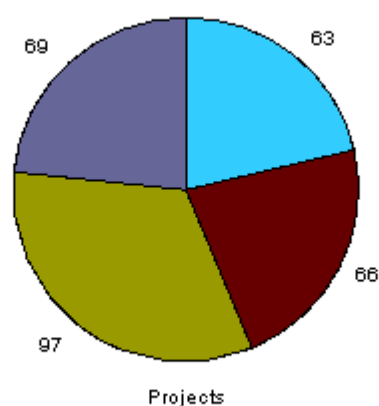


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of All Projects w.r.t. Revised Schedule

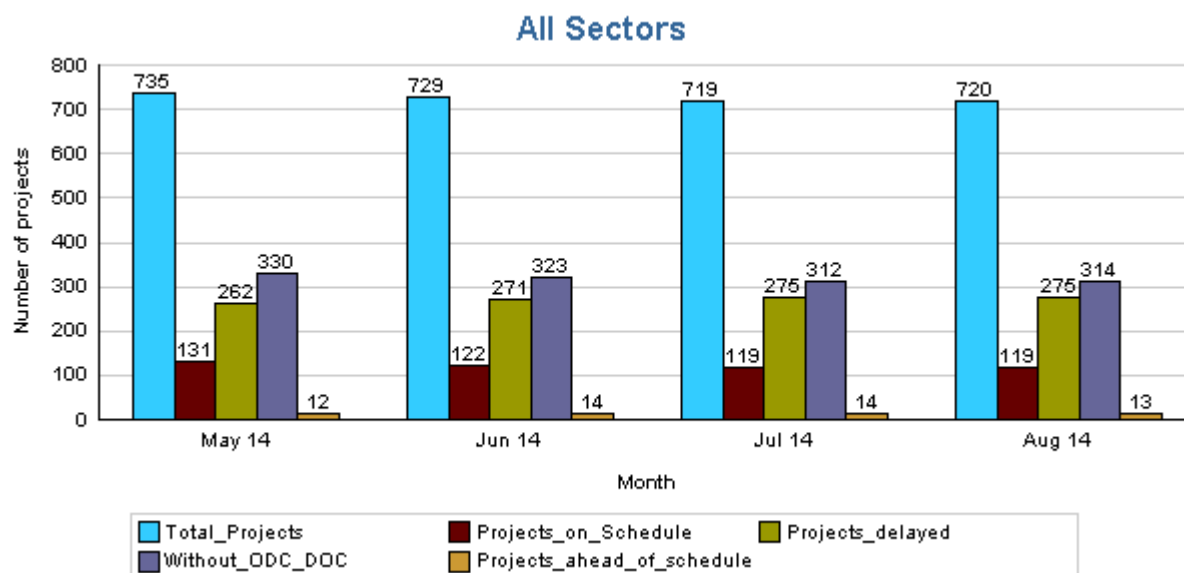


Break-up of 275 Delayed projects in August 2014

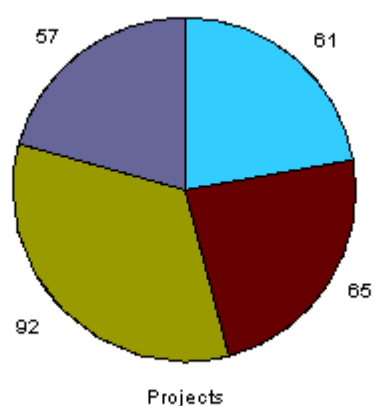


Delay in Months




Graphical Presentation of URBAN DEVELOPMENT Sector

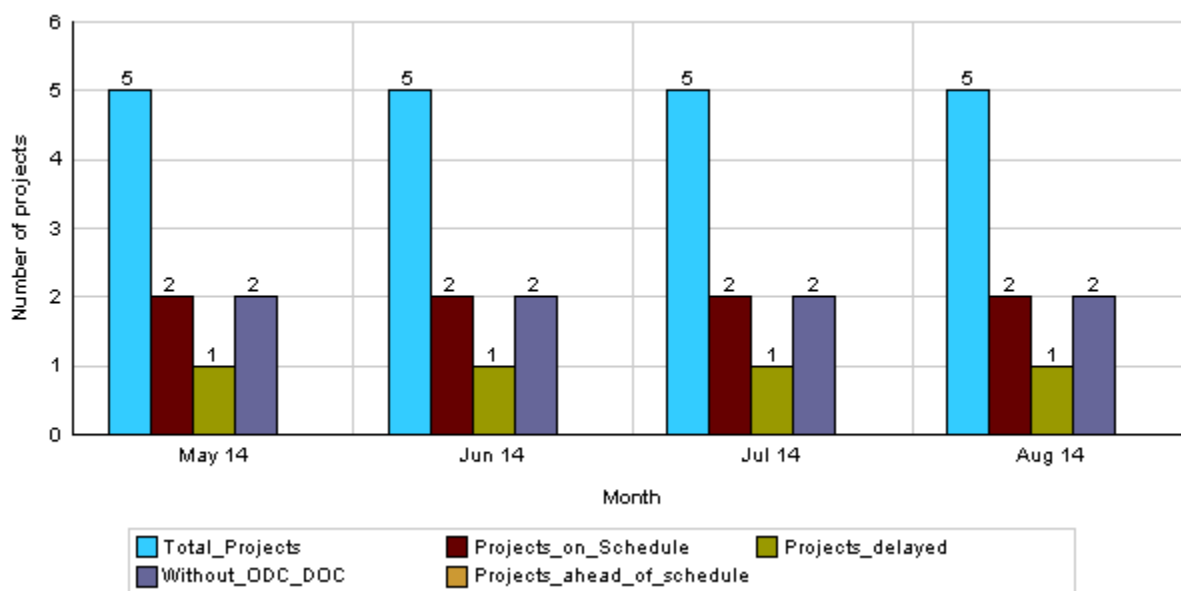


Break-up of 1 Delayed projects in August 2014



Graphical Presentation of TELECOMMUNICATIONS Sector

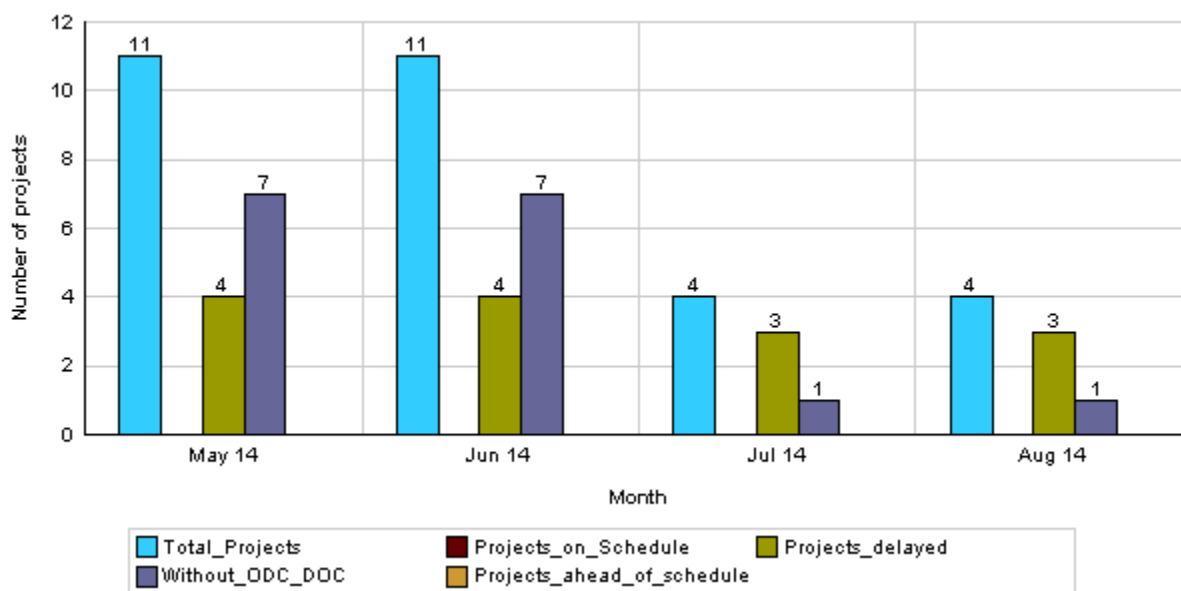


Break-up of 3 Delayed projects in August 2014

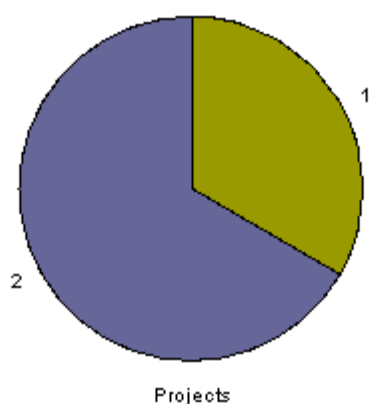


Delay in Months

1-12 13-24 25-60 MORE THAN 60

Graphical Presentation of SHIPPING AND PORTS Sector

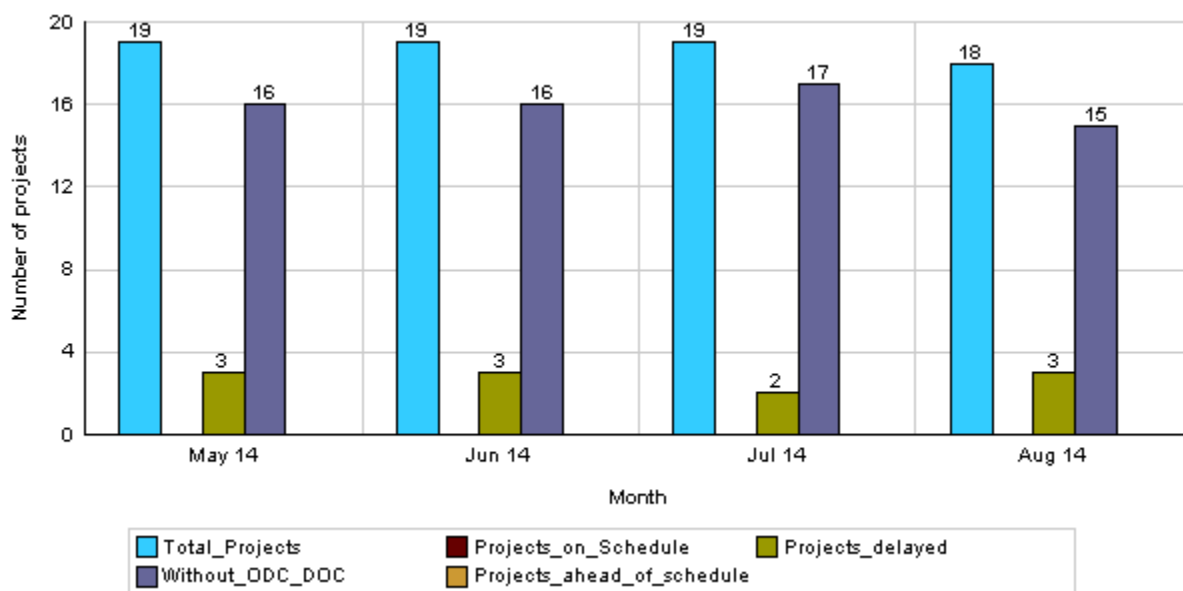


Break-up of 3 Delayed projects in August 2014

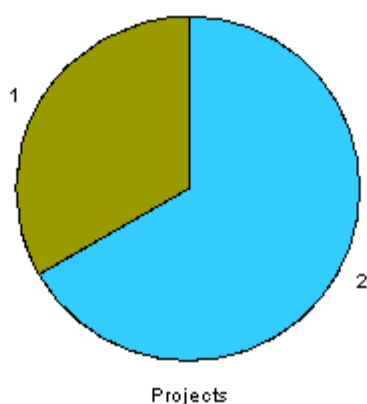


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

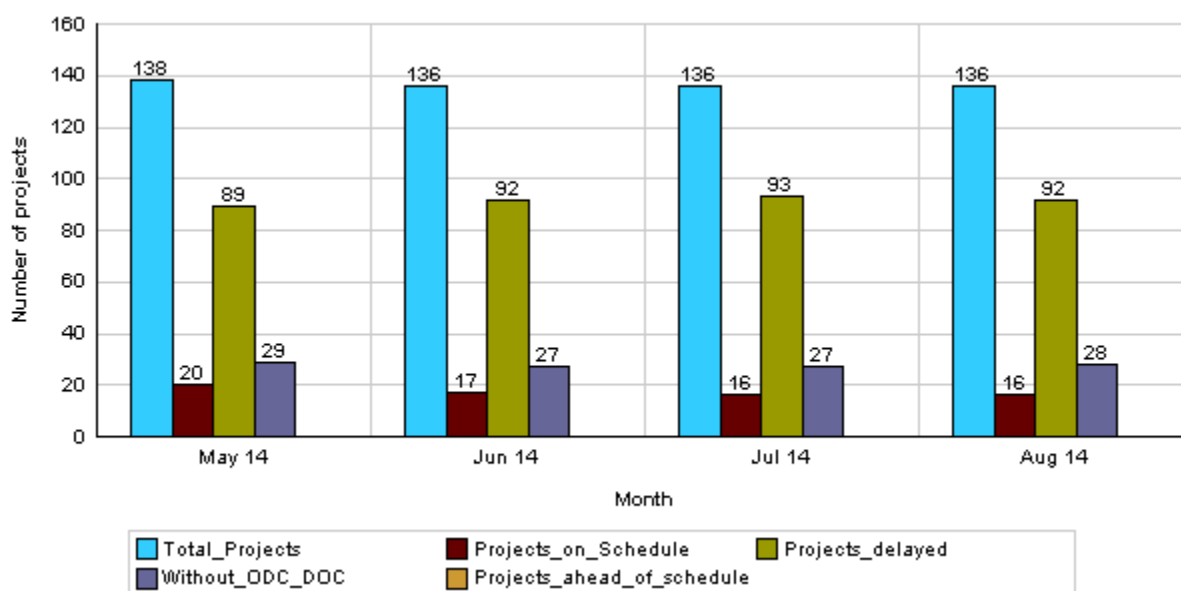


Break-up of 92 Delayed projects in August 2014

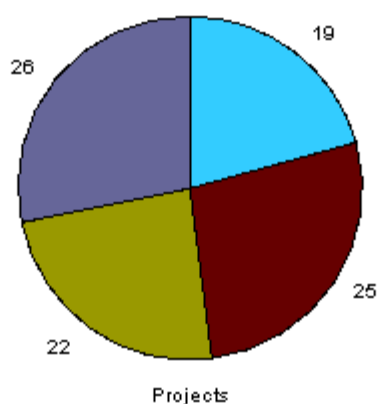


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

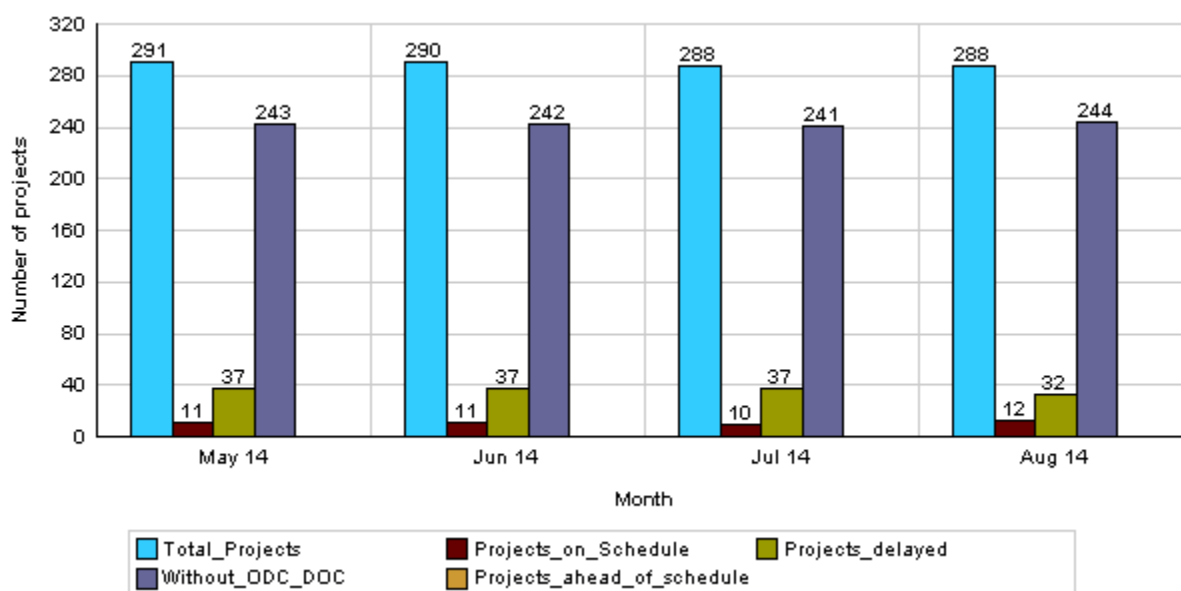


Break-up of 32 Delayed projects in August 2014

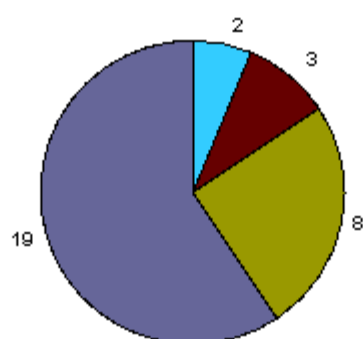


Projects

Delay in Months: 1-12 (Light Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Dark Blue)

Graphical Presentation of POWER Sector

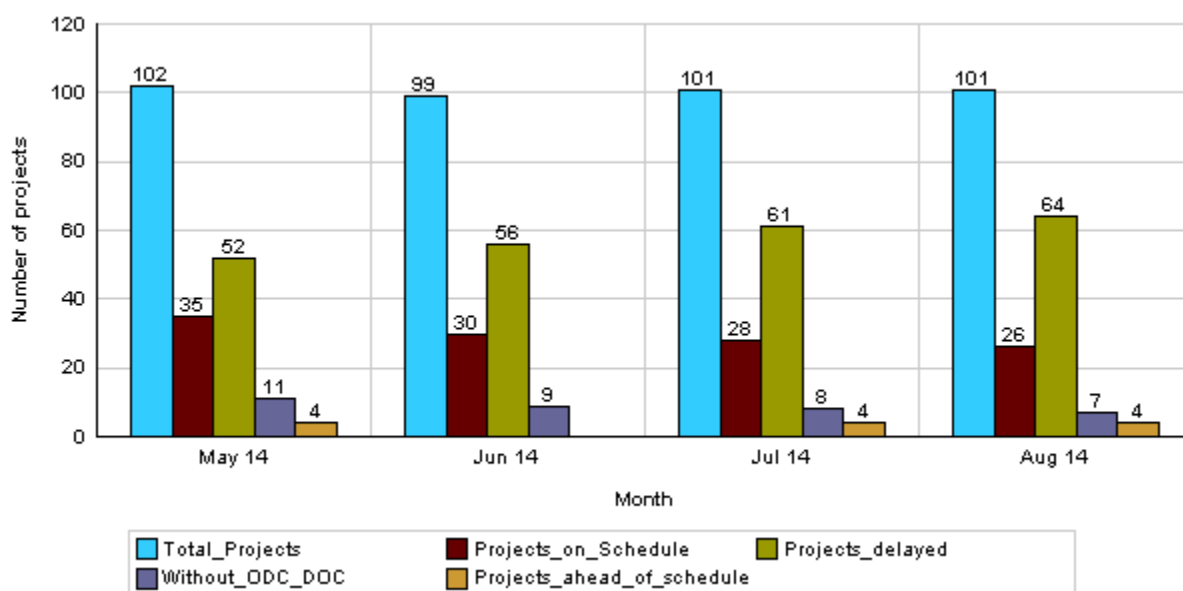


Break-up of 64 Delayed projects in August 2014

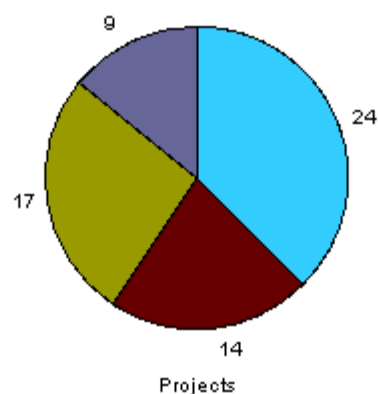


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of PETROLEUM Sector

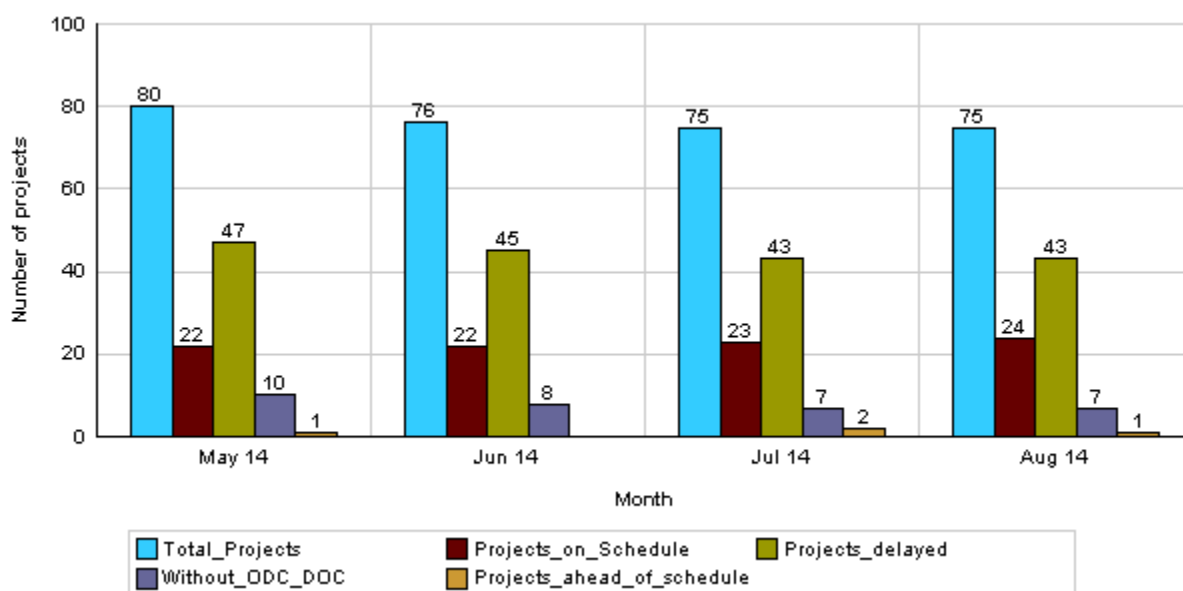


Break-up of 43 Delayed projects in August 2014

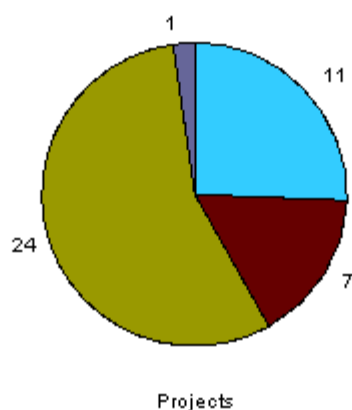


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	11	7	24	1

Graphical Presentation of STEEL Sector

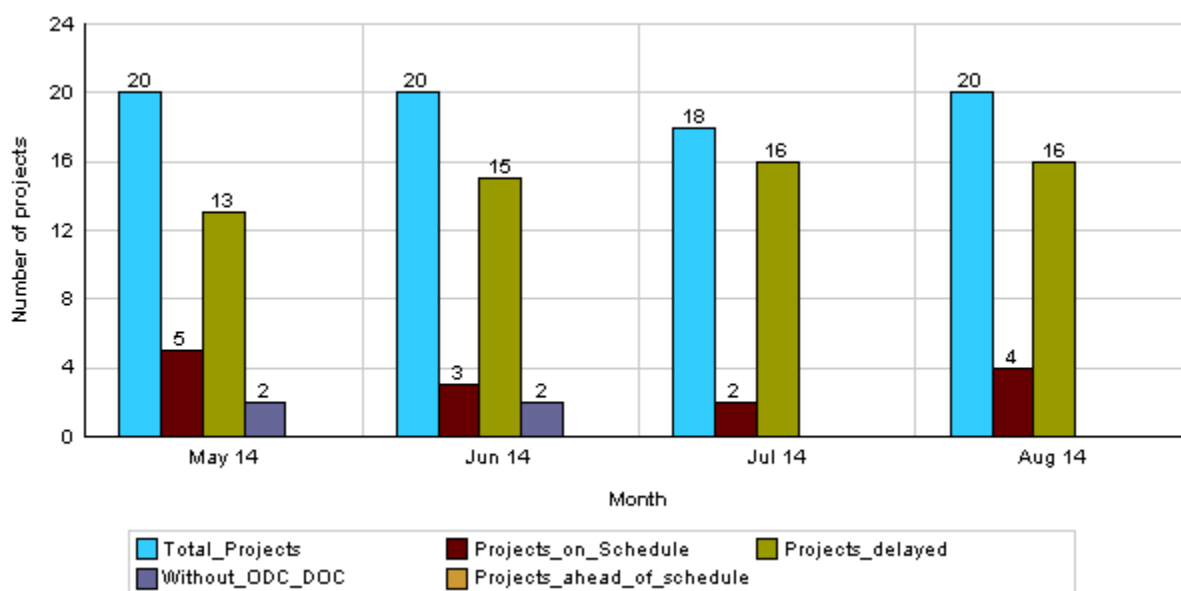


Break-up of 16 Delayed projects in August 2014

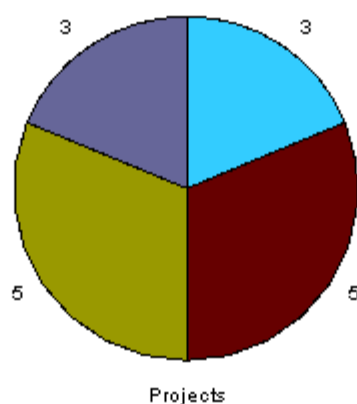


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of COAL Sector

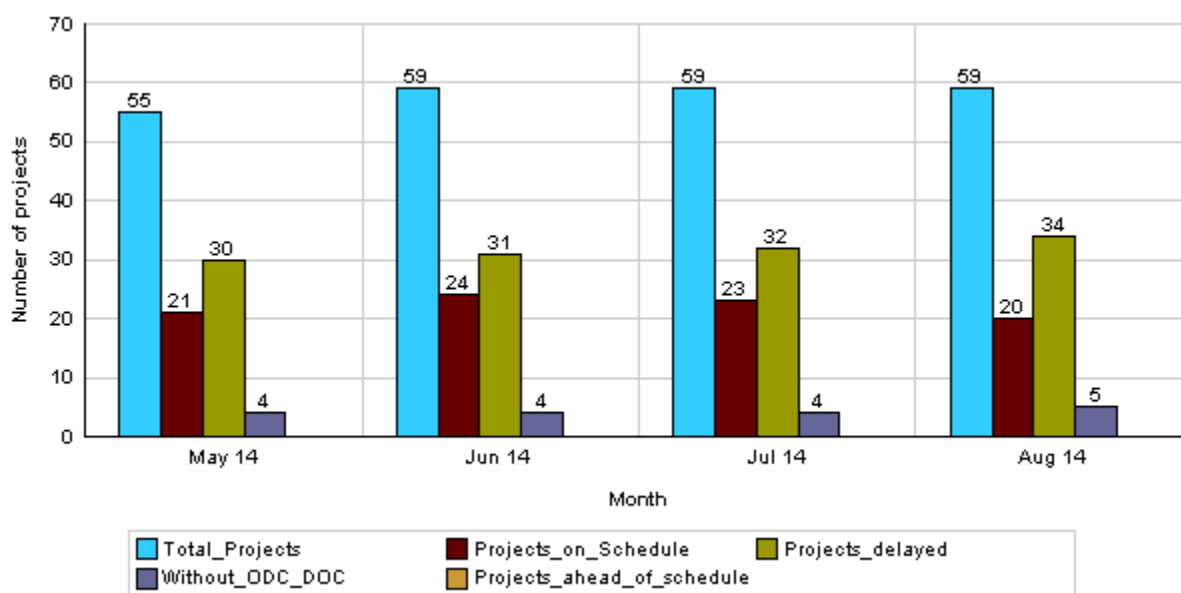


Break-up of 34 Delayed projects in August 2014

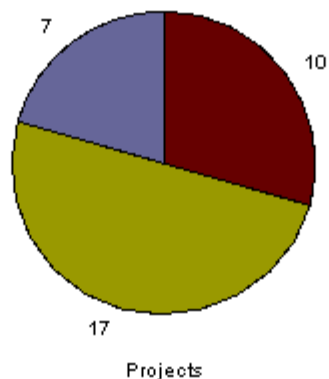


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

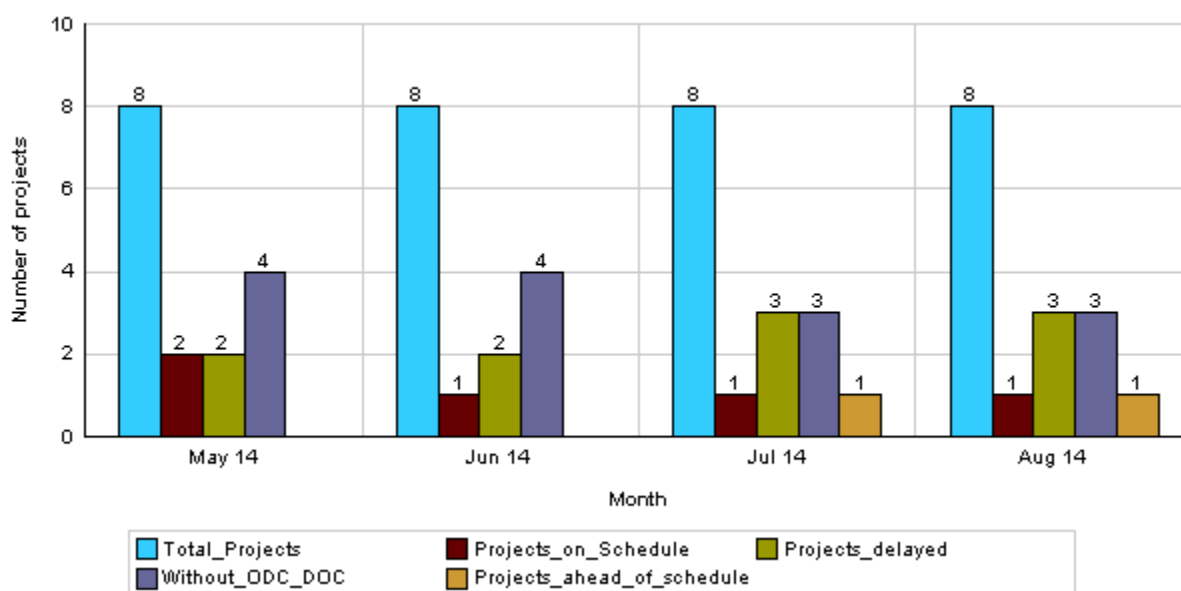


Break-up of 3 Delayed projects in August 2014

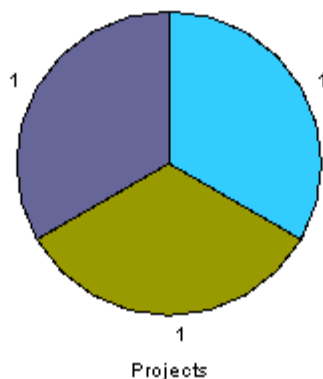


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of ATOMIC ENERGY Sector

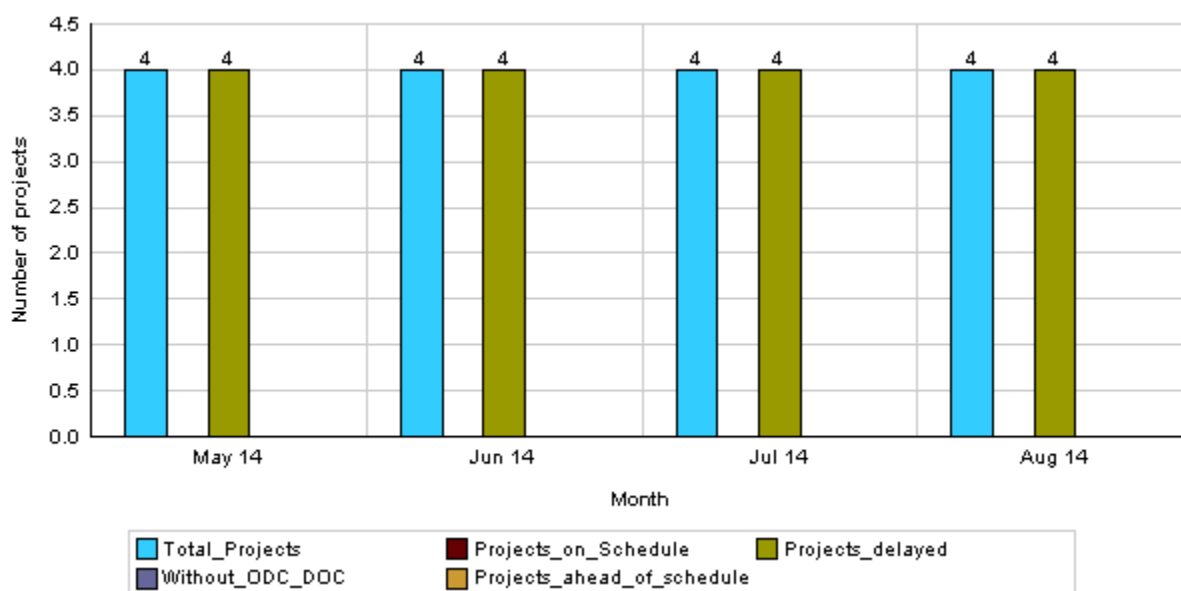

Break-up of 4 Delayed projects in August 2014

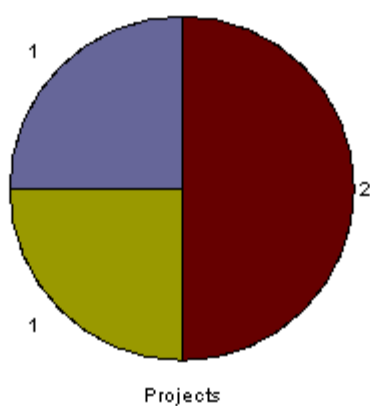

Delay in Months

Delay in Months	Count
1-12	1
13-24	2
25-60	1
MORE THAN 60	1

Sectorwise analysis of projects					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	40,442.00	46,726.00	46,726.00	30,894.17
CIVIL AVIATION	8	6,035.46	6,242.46	6,926.79	5,874.27
COAL	59	41,532.08	51,328.63	51,354.22	18,758.99
STEEL	20	66,395.10	70,414.06	72,349.06	61,178.76
PETROCHEMICALS	1	5,460.61	5,460.61	8,920.00	7,844.77
PETROLEUM	75	177,359.04	190,540.27	192,956.69	89,744.01
POWER	101	235,782.29	236,169.10	249,446.64	141,316.71
RAILWAYS	288	163,318.14	175,278.73	275,005.73	83,307.56
ROAD TRANSPORT AND HIGHWAYS	136	102,321.44	102,859.69	104,296.49	90,471.53
SHIPPING AND PORTS	18	12,117.12	13,337.95	14,450.58	4,745.00
TELECOMMUNICATIONS	4	2,018.15	2,018.15	1,843.90	556.35
URBAN DEVELOPMENT	5	73,993.32	74,052.22	79,266.22	11,652.27
WATER RESOURCES	1	542.90	542.90	1,187.00	35.49
Grand total	720	927,317.65	974,970.77	1,104,729.32	546,379.88

(All Cost/ Expenditure in Rs. Crore)

Sector Wise Details									
(August 2014)									
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Date of Commissioning		Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,277.00	12/2015 11/2016	10/2017	22(O) 11(R)	4/70
2	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	17,846.00	12/2008 10/2013	11/2014	71(O) 13(R)	40/102
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,564.17	09/2010 03/2015	03/2015	54(O) 0(R)	12/88
4	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,207.00	12/2016 03/2017	05/2018	17(O) 14(R)	4/69
	Total		40,442.00 -	46,726.00	30,894.17				60/329
	<u>CIVIL AVIATION</u>								
5	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]AAI,WEST BENGAL	08/2008	1,942.51 -	2,573.92	2,573.92	05/2011 -	03/2013	-	0/2
6	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.91	01/2011 04/2013	12/2016	71(O) 44(R)	0/0
7	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	283.54	05/2012 -	09/2014	28(O) -	0/0
8	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	2,015.00	1,939.20	01/2011 02/2012	02/2012	-	0/0
9	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]AAI,CHANDIGARH	02/2011	452.00 -	452.00	287.31	03/2015 -	02/2015	-1(O) -	0/0
10	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	19.61	03/2014 -	01/2015	10(O) -	0/0
11	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	626.00	492.74	06/2013 -	06/2013	-	0/0
12	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]AAI,MULTI STATE	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015	0(O) -	0/0
	Total		6,035.46 -	6,926.79	5,874.27				0/2
	<u>COAL</u>								
13	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	03/2015	24(O) 30(R)	21/22
14	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]SECL,CHHATISGARH	11/2009	150.59 -	198.59	94.83	03/2016 -	03/2016	0(O) -	2/7
15	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]NCL,MADHYA PRADESH	12/2009	1,352.04 1,143.54	1,143.54	664.21	03/2016 03/2016	03/2016	0(O) 0(R)	0/4

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	AMRAPALI OC(12MTY) - [N06000103]CCL,JHARKHAND	02/2012	858.11 -	858.11	95.94	03/2020 -	03/2020	0(O) -	0/3
17	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	167.94	03/2012 -	03/2017	60(O) -	4/5
18	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	100.76	03/2011 -	03/2017	72(O) -	0/2
19	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	142.24	03/2010 -	03/2017	84(O) -	3/4
20	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]SECL,CHHATISGARH	04/2012	258.56 -	258.56	60.25	03/2016 -	03/2016	0(O) -	0/6
21	BATURA OCP (2.0 MTY) - [N06000049]SECL,MADHYA PRADESH	09/2008	203.82 -	203.82	-	03/2015 -	03/2015	0(O) -	1/6
22	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]MCL,ODISHA	12/2007	490.00 -	490.10	182.71	03/2017 -	03/2017	0(O) -	3/11
23	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]NCL,MADHYA PRADESH	06/2011	746.04 -	535.10	264.36	03/2015 -	03/2015	0(O) -	0/3
24	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH	12/2013	610.33 -	610.33	-	03/2022 -	03/2022	0(O) -	0/7
25	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	272.77	03/2014 -	03/2016	24(O) -	2/9
26	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60(O) -	0/2
27	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,556.91	03/2014 -	03/2016	24(O) -	6/13
28	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,576.83	03/2014 -	03/2016	24(O) -	10/16
29	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72(O) -	1/12
30	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	118.50	03/2013 -	03/2017	48(O) -	2/7
31	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24(O) -	1/7
32	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36(O) -	4/31
33	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	467.78	12.31	03/2013 -	-	-	6/83
34	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72(O) -	0/1
35	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.81	12/2012 -	03/2016	39(O) -	11/44
36	KALYANIKHANI OPENCASE PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	417.33	2.16	07/2016 -	07/2016	0(O) -	3/39
37	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	120.62	03/2013 -	03/2017	48(O) -	3/9
38	KAPURIA UG(PSLW) - [N06000108]BCCL,JHARKHAND	08/2011	988.35 -	988.35	6.84	04/2017 -	04/2017	0(O) -	0/0
39	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	53.04	03/2014 -	03/2017	36(O) -	0/2
40	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24(O) -	1/7

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
41	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]NCL,UTTAR PRADESH	06/2011	1,131.28 -	1,131.28	30.30	03/2018 -	03/2018	0(O) -	0/4
42	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29 -	242.29	-	03/2015 -	03/2015	0(O) -	0/28
43	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	741.62	398.35	03/2013 -	03/2014	-	0/2
44	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.48	03/2010 -	03/2017	84(O) -	8/10
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	755.11	03/2013 03/2023	03/2023	120(O) 0(R)	0/16
46	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44(O) -	0/3
47	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	211.55	03/2014 -	03/2016	24(O) -	1/6
48	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.13	03/2012 -	03/2015	36(O) -	4/6
49	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2019	48(O) -	0/0
50	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	-	04/2014 -	04/2014	-	0/0
51	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	343.27	12/2015 -	04/2018	28(O) -	5/35
52	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36(O) -	0/2
53	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	6.84	03/2021 -	03/2021	0(O) -	0/0
54	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60(O) -	0/2
55	PELMA OCP(10.00MTY) - [N06000045]SECL,CHHATISGARH	07/2008	448.32 -	448.32	0.46	03/2015 -	03/2015	0(O) -	1/1
56	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.63	03/2014 -	03/2016	24(O) -	0/1
57	PURNADIDH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	144.07	03/2013 -	03/2015	24(O) -	0/3
58	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	41.46	03/2014 -	03/2016	24(O) -	0/0
59	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	223.19	03/2016 -	03/2016	0(O) -	0/2
60	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	226.56	03/2012 -	03/2016	48(O) -	24/27
61	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	162.76	2.48	03/2015 -	03/2015	0(O) -	4/29
62	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.14 -	430.14	68.08	03/2016 -	-	-	6/48
63	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]SCCL,TELANGANA	06/2012	365.01 -	365.01	6.56	06/2015 -	06/2015	0(O) -	3/51
64	RKP OCP PHASE-I - [N06000079]SCCL,TELANGANA	03/2010	209.78 -	209.78	67.29	03/2015 -	03/2015	0(O) -	8/31
65	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	249.03	72.23	03/2012 -	-	-	24/42

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
66	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL, WEST BENGAL	08/2012	1,055.05 -	1,055.05	31.24	03/2018 -	03/2018	0(O) -	0/0
67	TALABIRA OCP - [N06000043]MCL, ODISHA	03/2008	447.72 -	447.72	52.34	03/2016 -	03/2020	48(O) -	0/11
68	TAPIN OCP (2.5 MTY) - [N06000086]CCL, JHARKHAND	08/2008	264.68 -	264.68	142.19	03/2012 -	03/2016	48(O) -	0/2
69	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC, TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	3,017.28	06/2009 03/2013	10/2014	64(O) 19(R)	19/23
70	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC, TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,505.34	03/2012 05/2014	10/2014	31(O) 5(R)	25/39
71	WIND POWER PROJECT, KAZHUNEERKULAM, TAMILNADU - [N06000110]NLC, TAMIL NADU	04/2012	364.75 -	364.75	78.53	10/2014 -	10/2014	0(O) -	2/11
	Total		41,532.08 -	51,354.22	18,758.99				218/797
	<u>STEEL</u>								
72	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC, KARNATAKA	04/2011	572.00 -	572.00	402.05	04/2013 09/2014	03/2015	23(O) 6(R)	17/18
73	REBUILDING OF COB-7 AT BSL - [N12000083]SAIL, JHARKHAND	10/2013	245.67 -	245.67	18.01	05/2016 -	05/2016	0(O) -	0/3
74	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC, KARNATAKA	02/2011	898.55 -	898.55	333.54	05/2013 01/2015	03/2015	22(O) 2(R)	14/20
75	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL, MULTI STATE	07/2007	480.00 -	450.00	313.71	09/2009 05/2012	03/2015	66(O) 34(R)	1/1
76	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC, CHHATISGARH	01/2007	295.89 607.17	607.17	376.00	12/2011 01/2015	03/2015	39(O) 2(R)	16/20
77	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL, ANDHRA PRADESH	06/2006	108.00 216.68	216.68	162.45	09/2008 12/2013	10/2014	73(O) 10(R)	3/4
78	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL, CHHATISGARH	07/2012	332.65 -	332.65	120.75	08/2014 -	01/2015	5(O) -	3/4
79	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT - [N12000085]SAIL, CHHATISGARH	04/2014	188.93 -	188.93	-	04/2015 -	04/2015	0(O) -	0/3
80	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL, ODISHA	11/2011	254.55 -	254.55	113.57	11/2013 -	06/2015	19(O) -	2/4
81	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL, CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,243.14	03/2013 -	09/2015	30(O) -	29/35
82	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL, JHARKHAND	05/2010	6,325.00 -	6,325.00	4,831.60	12/2011 -	12/2014	36(O) -	18/24
83	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL, WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,298.40	12/2012 -	03/2015	27(O) -	14/20
84	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,226.60	12/2011 -	12/2014	36(O) -	23/29
85	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL, ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,934.43	10/2009 10/2012	12/2014	62(O) 26(R)	68/68
86	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL, ODISHA	08/2010	11,812.00 -	11,812.00	11,397.96	03/2013 -	03/2015	24(O) -	18/20

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
87	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	136.18	10/2013 -	08/2015	22(O) -	2/5
88	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	78.35	09/2014 -	01/2015	4(O) -	0/2
89	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]SAIL, WEST BENGAL	11/2012	313.05 -	313.05	115.87	06/2015 -	06/2015	0(O) -	2/3
90	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	74.37	12/2014 -	03/2015	3(O) -	0/2
91	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]SAIL,ODISHA	06/2014	708.91 -	708.91	1.78	04/2016 -	04/2016	0(O) -	0/2
	Total		66,395.10 -	72,349.06	61,178.76				230/287
	<u>PETROCHEMICALS</u>								
92	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	8,920.00	7,844.77	04/2012 -	-	-	22/29
	Total		5,460.61 -	8,920.00	7,844.77				22/29
	<u>PETROLEUM</u>								
93	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	10/2014	28(O) -	0/3
94	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]ONGC,MULTI STATE	03/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018	0(O) -	0/0
95	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC,GUJARAT	11/2010	1,916.10 -	1,916.10	1,160.14	12/2014 -	12/2017	36(O) -	0/0
96	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC,GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2018	48(O) -	0/0
97	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC,ASSAM	03/2009	2,465.15 -	2,378.86	1,711.73	03/2013 03/2015	03/2016	36(O) 12(R)	0/5
98	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]IOCL,MULTI STATE	08/2011	586.00 -	586.00	198.47	08/2015 -	08/2015	0(O) -	0/12
99	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL,ASSAM	08/2008	144.02 -	204.29	154.72	06/2012 09/2013	12/2014	30(O) 15(R)	0/0
100	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC,MULTI STATE	06/2007	736.65 -	736.65	452.59	09/2011 12/2013	12/2015	51(O) 24(R)	0/0
101	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC,MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21(O) -	0/5
102	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC,GUJARAT	03/2009	302.26 -	240.95	105.93	09/2012 -	03/2015	30(O) -	0/0
103	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC,MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39(O) -	0/0
104	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 -	761.68	609.20	05/2013 06/2014	03/2015	22(O) 9(R)	0/5
105	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL,MULTI STATE	06/2009	486.00 -	486.00	105.71	09/2013 -	02/2015	17(O) -	0/1

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
106	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	540.92	340.00	07/2012 07/2012	-	-	6/7
107	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	984.65	- -	08/2015	-	0/12
108	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC,MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 06/2012	06/2015	110(O) 36(R)	0/0
109	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC,MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,867.35	08/2010 03/2012	05/2015	57(O) 38(R)	0/10
110	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC,MAHARASHTRA	03/2012	2,592.17 -	2,592.17	304.81	05/2014 -	05/2015	12(O) -	0/9
111	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20(O) 0(R)	0/10
112	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]ONGC,MULTI STATE	04/2013	284.82 -	284.82	-	04/2015 -	04/2015	0(O) -	0/0
113	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]ONGC,MULTI STATE	04/2012	600.17 -	600.17	248.73	12/2014 -	12/2014	0(O) -	0/8
114	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC,MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23(O) -	0/9
115	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]ONGC,MULTI STATE	10/2013	429.06 -	429.06	-	10/2014 -	10/2014	0(O) -	0/0
116	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	2,730.00	3,128.58	09/2011 03/2012	07/2014	-	56/59
117	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]IOCL,WEST BENGAL	03/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017	0(O) -	0/0
118	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	711.00	3.26	- -	-	-	0/0
119	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	179.67	10/2011 06/2014	08/2014	34(O) 2(R)	0/9
120	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]ONGC,MAHARASHTRA	03/2012	5,608.40 -	5,608.40	2,805.04	05/2015 -	05/2015	0(O) -	0/17
121	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]IOCL,ASSAM	02/2014	163.88 -	163.88	3.34	07/2016 -	07/2016	0(O) -	0/0
122	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]ONGC,MAHARASHTRA	12/2011	2,059.63 2,665.65	2,665.65	597.89	03/2015 -	03/2015	0(O) -	0/12
123	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]ONGC,MAHARASHTRA	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016	0(O) -	0/0
124	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]ONGC,MULTI STATE	05/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016	0(O) -	0/0
125	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL,KERALA	01/1999	14,225.00 16,504.00	16,504.00	3,203.62	12/2015 -	05/2016	5(O) -	0/0
126	IOR OF B-173A FIELD - [N16000140]ONGC,MULTI STATE	01/2012	352.49 -	352.49	97.37	03/2014 -	04/2015	13(O) -	0/5
127	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL,MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35(O) -	0/0
128	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	281.07	6.18	10/2010 -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
129	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL,MULTI STATE	06/2009	2,915.00 -	2,300.00	1,408.97	12/2012 06/2015	06/2015	30(O) 0(R)	0/14
130	KOTA JOBNER PIPELINE PROJECT - [N16000170]BPCL,RAJASTHAN	04/2011	276.26 -	276.27	165.75	03/2015 -	03/2015	0(O) -	0/64
131	LPG MARKETING TERMINAL, PARADIP - [N16000174]IOCL,ODISHA	07/2009	158.91 -	158.91	107.81	03/2015 -	03/2015	0(O) -	0/0
132	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	12/2012	607.06 -	607.06	46.12	01/2016 -	01/2016	0(O) -	0/0
133	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]HPCL,KARNATAKA	11/2012	666.00 701.00	701.00	277.96	11/2015 -	11/2015	0(O) -	18/29
134	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	144.04	06/2014 -	12/2014	6(O) -	0/0
135	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC,GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32(O) -	0/0
136	MH NORTH REDEVELOPMENT PHASE III - [N16000188]ONGC,MAHARASHTRA	06/2014	5,706.47 -	5,706.47	-	05/2017 -	05/2017	0(O) -	0/0
137	MOUNDED BULLET PROJECT AT CPCL - [N16000154]CPCL,TAMIL NADU	12/2012	279.00 -	279.00	89.30	12/2014 -	12/2014	0(O) -	0/0
138	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 12,160.26	12,160.26	12,077.74	01/2012 -	09/2014	32(O) -	0/108
139	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	171.83	-	- -	-	-	0/0
140	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]IOCL,MULTI STATE	02/2011	913.00 -	913.00	312.22	07/2015 -	12/2015	5(O) -	0/0
141	PARADIP REFINERY PROJECT - [N16000058]IOCL,ODISHA	02/2009	29,777.00 -	34,555.00	26,669.53	11/2012 11/2013	02/2015	27(O) 15(R)	74/100
142	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]IOCL,MULTI STATE	08/2009	1,793.00 -	1,793.00	1,013.11	09/2012 -	12/2015	39(O) -	6/7
143	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,890.00	02/2014 -	10/2014	8(O) -	0/0
144	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	260.70	04/2012 -	10/2014	30(O) -	0/0
145	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]ONGC,GUJARAT	09/2011	202.25 -	160.16	34.66	07/2016 -	07/2016	0(O) -	0/5
146	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC,MULTI STATE	04/2012	2,547.26 -	1,417.00	1,304.46	05/2014 -	05/2015	12(O) -	0/5
147	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]IOCL,ODISHA	03/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017	0(O) -	0/0
148	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	1,004.06	07/2012 -	10/2014	27(O) -	0/31
149	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL,MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	02/2016	14(O) -	0/0
150	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]ONGC,MAHARASHTRA	03/2013	1,138.50 -	686.58	110.40	04/2015 -	04/2015	0(O) -	0/0
151	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL,MAHARASHTRA	01/1999	1,419.00 -	1,419.00	726.22	12/2014 -	03/2015	3(O) -	0/0
152	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]IOCL,BIHAR	04/2013	480.00 -	480.00	-	02/2016 -	02/2016	0(O) -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
153	RESID UPGRADATION PROJECT - [N16000184]CPCL,TAMIL NADU	02/2011	3,110.36 -	3,110.36	219.08	11/2015 -	11/2015	0(O) -	0/0
154	RESITEMENT OF BILASPUR AND BISRAPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]IOCL,CHHATISGARH	01/2011	232.00 -	232.00	89.79	09/2016 -	12/2015	-9(O) -	0/12
155	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]IOCL,JHARKHAND	04/2011	191.96 -	191.96	46.35	05/2015 -	12/2015	7(O) -	0/12
156	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]ONGC,MULTI STATE	03/2013	2,913.10 -	2,910.30	9.50	05/2016 -	05/2016	0(O) -	0/0
157	REWARI KANPUR PIPELINE PROJECT - [N16000145]HPCL,MULTI STATE	02/2012	1,210.64 -	1,210.64	660.01	11/2015 -	11/2015	0(O) -	14/25
158	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL,MULTI STATE	08/2006	94.00 352.56	352.56	10.60	09/2012 03/2017	03/2017	54(O) 0(R)	0/0
159	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]ISPRIL,KARNATAKA	01/2006	732.00 1,227.00	1,227.00	882.71	10/2011 -	10/2015	48(O) -	0/0
160	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]ISPRIL,KERALA	01/2006	993.00 1,693.00	1,693.00	1,275.74	01/2012 -	10/2015	45(O) -	0/0
161	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]ISPRIL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	984.98	10/2011 -	12/2014	38(O) -	0/0
162	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	- 04/2015	04/2015	- 0(R)	0/0
163	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC,TRIPURA	07/2008	288.04 288.04	253.66	216.68	08/2012 -	03/2015	31(O) -	0/5
164	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL,ASSAM	09/2012	871.35 -	1,200.00	50.75	03/2015 11/2015	11/2015	8(O) 0(R)	0/5
165	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL,MULTI STATE	11/2012	309.81 462.79	462.79	85.74	10/2014 -	10/2015	12(O) -	0/0
166	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL,MULTI STATE	12/2009	463.32 -	330.47	270.84	03/2012 -	07/2015	40(O) -	13/20
167	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	549.46	12/2013 05/2014	10/2014	10(O) 5(R)	65/69
	Total		177,359.04 -	192,956.69	89,744.01				252/709
	<u>POWER</u>								
168	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,380.46	08/2012 -	09/2014	25(O) -	0/11
169	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	260.88	- 03/2015	03/2015	- 0(R)	5/17
170	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]PGCIL,MULTI STATE	03/2014	155.57 -	155.57	-	03/2016 -	03/2016	0(O) -	0/0
171	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]PGCIL,MULTI STATE	12/2012	156.04 -	156.04	77.46	10/2014 -	10/2014	0(O) -	0/7

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
172	BARH STPP STAGE -II - [N18000047]NTPC,BIHAR	02/2008	7,341.04 -	7,341.04	7,849.00	08/2013 -	03/2015	19(O) -	15/20
173	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	10,223.00	12/2009 -	03/2017	87(O) -	23/46
174	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,680.00	07/2011 -	08/2016	61(O) -	8/34
175	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]PGCIL,MULTI STATE	03/2013	2,514.88 -	2,514.88	180.75	12/2015 -	12/2015	0(O) -	2/20
176	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL,TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,449.26	09/2014 -	03/2015	6(O) -	6/19
177	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]PGCIL,MULTI STATE	06/2012	1,909.24 -	1,909.24	598.23	06/2015 -	06/2015	0(O) -	0/0
178	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATTNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,449.25	08/2014 -	09/2014	1(O) -	6/19
179	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	206.44	43.97	06/2014 -	-	-	0/20
180	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]PGCIL,MULTI STATE	03/2013	514.20 -	514.20	-	06/2015 -	06/2015	0(O) -	0/7
181	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]PGCIL,TAMIL NADU	01/2013	182.80 -	182.80	65.23	10/2014 -	10/2014	0(O) -	2/14
182	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]PGCIL,MULTI STATE	02/2014	196.58 -	196.58	-	02/2016 -	02/2016	0(O) -	0/0
183	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	881.93	11/2012 -	12/2015	37(O) -	1/12
184	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	1,364.52	39.74	05/2016 -	04/2016	-1(O) -	0/20
185	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 -	522.29	-	11/2016 -	11/2016	0(O) -	0/0
186	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]PGCIL,MULTI STATE	03/2012	198.63 -	198.63	-	09/2014 -	09/2014	0(O) -	0/0
187	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL,CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,503.95	05/2014 -	03/2015	10(O) -	2/11
188	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,411.00	09/2017 -	03/2018	6(O) -	13/39
189	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL,BIHAR	12/2011	901.77 -	901.77	704.20	08/2014 -	12/2014	4(O) -	1/15

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
190	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]PGCIL,MULTI STATE	05/2014	303.07 -	303.07	-	07/2016 -	07/2016	0(O) -	0/0
191	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,432.05	12/2013 -	10/2014	10(O) -	2/8
192	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]PGCIL,MAHARASHTRA	10/2013	1,315.90 -	1,315.90	99.57	11/2016 -	03/2016	-8(O) -	0/17
193	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	1,007.16	946.61	12/2007 12/2009	-	-	1/10
194	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,179.32	12/2009 03/2017	03/2017	87(O) 0(R)	11/29
195	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	3,642.04 -	3,642.04	3,578.56	01/2016 -	11/2016	10(O) -	4/6
196	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,047.00	04/2009 -	05/2015	73(O) -	3/9
197	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	4,923.00	12/2016 -	03/2018	15(O) -	18/23
198	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	2,159.07	1,880.50	09/2008 -	03/2013	-	14/23
199	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,766.00	05/2017 -	03/2019	22(O) -	15/37
200	LATA-TOPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	140.00	08/2017 -	03/2018	7(O) -	0/9
201	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	2,968.00	09/2016 -	03/2018	18(O) -	20/23
202	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,060.80	08/2013 -	06/2015	22(O) -	0/17
203	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]PGCIL,MULTI STATE	02/2014	908.08 -	908.08	-	06/2016 -	06/2016	0(O) -	0/20
204	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL,MULTI STATE	07/2010	752.64 -	752.64	417.62	07/2013 -	03/2015	20(O) -	1/10
205	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	287.57	02/2012 -	03/2016	49(O) -	0/13
206	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	413.76	11/2011 -	03/2016	52(O) -	1/13
207	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]PGCIL,MULTI STATE	02/2014	539.82 -	539.82	-	06/2016 -	06/2016	0(O) -	0/20
208	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,070.12	04/2013 -	03/2016	35(O) -	0/11
209	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]PGCIL,MULTI STATE	11/2011	723.63 -	723.63	394.08	11/2014 -	11/2014	0(O) -	2/16
210	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]PGCIL,MULTI STATE	09/2013	680.69 -	680.69	49.29	03/2016 -	03/2016	0(O) -	0/17
211	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]PGCIL,MULTI STATE	09/2012	803.34 -	803.34	358.09	03/2015 -	03/2015	0(O) -	4/17
212	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	139.82	04/2015 -	05/2015	1(O) -	0/18

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
213	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	690.64	11/2012 -	03/2016	40(O) -	0/11
214	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,622.40	09/2009 -	07/2018	106(O) -	4/12
215	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	909.40	08/2013 -	09/2015	25(O) -	22/37
216	RAMPUR HEP(412 MW) - [N18000024]SJVN, HIMACHAL PRADESH	01/2007	2,047.03 -	3,288.28	3,261.56	03/2012 -	09/2014	30(O) -	19/28
217	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 2,998.00	9,395.18	2,998.00	11/2016 -	03/2018	16(O) -	16/19
218	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]PGCIL,MULTI STATE	05/2014	829.98 -	829.98	-	09/2016 -	09/2016	0(O) -	0/0
219	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]PGCIL,KARNATAKA	02/2014	167.40 -	167.40	-	12/2015 -	12/2015	0(O) -	0/7
220	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,925.96	09/2010 -	12/2018	99(O) -	0/0
221	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,136.01	08/2012 -	10/2014	26(O) -	1/6
222	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]PGCIL,MULTI STATE	09/2012	1,508.74 -	1,508.74	394.08	06/2016 -	12/2015	-6(O) -	0/19
223	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]PGCIL,MULTI STATE	08/2014	288.49 -	288.49	-	02/2017 -	02/2017	0(O) -	0/0
224	SYSTEM STRENGTHENING - XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	232.34	187.19	06/2012 -	-	-	0/3
225	SYSTEM STRENGTHENING - XIX IN SOUTHERN REGIONAL GRID - [N18000137]PGCIL,MULTI STATE	09/2012	1,935.35 -	1,935.35	798.98	12/2014 -	11/2014	-1(O) -	2/13
226	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	149.54	03/2014 -	10/2014	7(O) -	3/7
227	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	524.63	08/2014 -	05/2015	9(O) -	1/17
228	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,012.19	08/2012 -	12/2014	28(O) -	0/6
229	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	0.80	08/2014 -	08/2016	24(O) -	0/0
230	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]PGCIL,MAHARASHTRA	02/2012	1,310.85 -	1,310.85	841.33	02/2015 -	02/2015	0(O) -	1/8
231	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL,MULTI STATE	06/2012	1,263.26 -	1,263.26	786.18	11/2014 -	12/2014	1(O) -	0/15

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
232	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATTISGARH	01/2012	1,422.85 -	1,422.85	782.72	01/2015 -	06/2015	5(O) -	3/19
233	SYSTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	243.87	08/2014 -	10/2014	2(O) -	6/19
234	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	298.72	06/2014 -	12/2014	6(O) -	7/19
235	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,180.00	03/2013 -	03/2018	60(O) -	0/14
236	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,061.38	1,540.94	09/2009 -	03/2016	78(O) -	2/5
237	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	778.83	07/2010 02/2016	05/2018	94(O) 27(R)	4/15
238	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	169.32	01/2014 -	10/2014	9(O) -	3/16
239	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,194.96	08/2014 -	06/2015	10(O) -	2/19
240	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAND AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,746.81	10/2014 -	06/2015	8(O) -	2/17
241	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,963.78	10/2012 -	12/2015	38(O) -	0/11
242	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	184.19	161.72	11/2011 -	06/2014	-	0/4
243	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	400.47	-	05/2017 -	-	-	0/0
244	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,844.30	12/2012 -	06/2015	30(O) -	0/11
245	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]PGCIL,ANDHRA PRADESH	08/2014	188.75 -	188.75	-	02/2017 -	02/2017	0(O) -	0/0
246	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	5,151.37	-	04/2018 -	04/2018	0(O) -	0/0
247	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	627.95	01/2015 -	12/2015	11(O) -	6/21
248	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP-PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	324.33	194.46	08/2014 -	09/2014	1(O) -	9/20
249	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]PGCIL,GUJARAT	02/2014	378.71 -	378.71	11.10	10/2016 -	10/2016	0(O) -	0/20
250	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]PGCIL,MULTI STATE	02/2012	1,927.16 -	1,927.16	1,291.77	10/2014 -	10/2014	0(O) -	2/10

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
251	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]PGCIL,MULTI STATE	09/2013	1,575.30 -	1,575.30	94.20	05/2016 -	05/2016	0(O) -	0/18
252	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL,GUJARAT	12/2011	552.44 -	552.44	433.50	02/2014 -	12/2014	10(O) -	4/11
253	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL,MULTI STATE	09/2011	1,366.34 -	1,366.34	1,063.76	12/2013 -	02/2015	14(O) -	3/11
254	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL,JHARKHAND	10/2011	558.26 -	558.26	308.81	11/2013 -	03/2015	16(O) -	6/20
255	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,638.84	03/2013 -	11/2014	20(O) -	4/14
256	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL,MULTI STATE	03/2011	2,569.25 -	2,569.25	2,521.77	03/2014 -	02/2015	11(O) -	4/14
257	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL,ODISHA	12/2010	2,743.19 -	2,743.19	2,311.10	12/2013 -	02/2015	14(O) -	2/12
258	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	69.70	01/2013 -	06/2015	29(O) -	4/20
259	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NR/WR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,311.26	11/2013 -	06/2015	19(O) -	4/15
260	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL,MULTI STATE	03/2010	4,672.99 -	4,672.99	3,336.27	11/2012 -	03/2015	28(O) -	0/1
261	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL,CHHATISGARH	11/2011	2,127.51 -	2,127.51	1,923.03	07/2014 -	03/2015	8(O) -	3/14
262	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	811.41	07/2013 08/2014	11/2014	16(O) 3(R)	21/25
263	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 913.63	913.63	647.19	07/2006 01/2014	12/2015	113(O) 23(R)	2/13
264	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	-	04/2016 -	04/2016	0(O) -	0/0
265	VINDHYACHAL STPP STAGE-V - [N18000134]NTPC,MADHYA PRADESH	12/2011	3,180.40 -	3,180.40	1,190.00	08/2015 -	08/2015	0(O) -	19/19
266	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	495.58	07/2014 -	07/2018	48(O) -	1/1
267	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	494.49	09/2010 -	12/2014	51(O) -	0/7
268	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATISGARH	03/2012	9,569.76 -	9,569.76	2,445.59	06/2015 -	12/2015	6(O) -	2/21
	Total		235,782.29 -	249,446.64	141,316.71				374/1381

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>RAILWAYS</u>								
269	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.43	04/2012 -	03/2016	47(O) -	0/0
270	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	184.06	4.74	- -	-	-	0/0
271	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 -	1,741.00	697.37	03/2014 -	03/2017	36(O) -	0/0
272	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	252.00	-	- -	-	-	0/0
273	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	414.84	12/2009 03/2011	12/2014	60(O) 45(R)	0/0
274	AHMEDABAD-BOTAD (GC) - [N22000140]WR,GUJARAT	04/2012	567.18 -	567.18	2.67	- -	-	-	0/0
275	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	394.14 -	385.60	71.68	03/2013 -	-	-	0/0
276	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	2,820.00	322.91	- -	-	-	0/0
277	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	218.39	24.14	- -	-	-	0/0
278	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	822.00	-	- -	-	-	0/0
279	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	2,000.00	17.32	- -	-	-	0/0
280	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 -	485.00	417.14	03/2011 -	-	-	0/0
281	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	242.09	-	- -	-	-	0/0
282	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	338.54	118.39	- -	-	-	0/0
283	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	113.56	- -	03/2016	-	0/0
284	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	725.00	575.22	06/1999 -	-	-	0/0
285	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	295.68	0.81	- -	-	-	0/0
286	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	307.00	-	- -	-	-	0/0
287	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	1,566.00	138.10	- -	-	-	0/0
288	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	490.80	0.39	- -	-	-	0/0
289	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	304.41	0.19	- -	-	-	0/0
290	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	528.00	2.96	- -	-	-	0/0
291	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER,UTTAR PRADESH	03/2012	199.75 -	199.75	55.01	- -	-	-	0/0
292	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	986.30	60.47	- -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
293	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	288.35	8.71	- -	-	-	0/0
294	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	207.52	206.38	12/2012 -	-	-	0/0
295	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	1,382.78	0.76	- -	-	-	0/0
296	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	246.08	2.95	- -	-	-	0/0
297	BANKURA - DAMODAR (GC) (SER) - [220100277]SER, WEST BENGAL	03/1998	111.90 1,039.29	1,423.98	481.56	03/2005 12/2008	-	-	0/0
298	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,106.62	236.03	12/2010 -	-	-	0/0
299	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	450.55	12.83	- -	-	-	0/0
300	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	255.64	-	- -	-	-	0/0
301	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 -	1,814.10	392.88	03/2004 12/2010	03/2016	144(O) 63(R)	0/0
302	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	337.50	0.50	- -	-	-	0/0
303	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	923.23	0.36	- -	-	-	0/0
304	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	858.67 -	858.67	0.73	- -	-	-	0/0
305	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER, WEST BENGAL	04/2011	289.64 -	289.64	0.09	- -	-	-	0/0
306	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	191.67	04/2014 -	03/2020	71(O) -	0/0
307	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	2,966.99	40.79	- -	-	-	0/0
308	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	196.95	198.63	03/2011 -	-	-	0/0
309	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER,UTTAR PRADESH	03/2008	195.64 -	195.64	80.71	- -	-	-	0/0
310	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69(O) -	0/0
311	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 -	321.62	2.22	03/2012 -	-	-	0/0
312	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	326.20	1.68	- -	-	-	0/0
313	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	175.80	1.44	- -	-	-	0/0
314	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	267.37	34.08	- -	-	-	0/0
315	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,500.00 -	4,996.19	3,302.95	04/2008 12/2011	12/2016	104(O) 60(R)	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
316	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	579.37	599.40	- -	02/2012	-	0/0
317	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	59.57	03/2015 -	12/2016	21(O) -	0/0
318	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	328.14	0.17	- -	-	-	0/0
319	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	337.96	60.82	- -	-	-	0/0
320	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	582.03	- -	03/2015	- -	0/0
321	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	222.95	122.80	- -	-	-	0/0
322	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	520.00	462.28	- -	-	-	0/0
323	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,200.00	2.04	- -	-	-	0/0
324	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	494.92	3.62	- -	-	-	0/0
325	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	378.56	106.98	- -	-	-	0/0
326	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	1,417.97	1,011.09	- -	03/2012	-	0/0
327	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	585.93	194.91	- -	12/2013	-	0/0
328	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	243.78	27.33	- -	-	-	0/0
329	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	367.77	-	- -	-	-	0/0
330	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.43	-	- -	-	-	0/0
331	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	595.91	89.59	- -	-	-	0/0
332	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 -	1,347.26	156.55	- -	-	-	0/0
333	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	573.78	166.84	- -	-	-	0/0
334	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR, TRIPURA	04/1999	895.00 -	1,242.25	977.30	03/2007 -	03/2016	108(O) -	0/0
335	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	556.64	268.12	- -	-	-	0/0
336	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	829.00	-	- -	-	-	0/0
337	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 -	1,640.04	166.32	- -	-	-	0/0
338	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	533.38	112.92	12/2011 -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
339	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	968.60	-	12/2012 -	-	-	0/0
340	DANGOAPOLI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	388.67	92.56	12/2015 -	03/2016	3(O)	0/0
341	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	406.92	153.26	- -	-	-	0/0
342	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	296.44	4.00	- -	-	-	0/0
343	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	205.00	5.20	- -	-	-	0/0
344	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	410.08	252.70	- -	03/2014	-	0/0
345	DELANG-PURI DOUBLING - [N22000320]ECOR,ODISHA	03/2011	165.16 -	165.16	102.77	03/2015 -	03/2015	0(O)	0/0
346	DELHI-SOHNA-NUH-FIROZPUR-JHIRKA-ALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	1,239.00	-	- -	-	-	0/0
347	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	336.91	143.17	- -	-	-	0/0
348	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 240.59	607.09	556.20	12/2012 12/2012	-	-	0/0
349	DHASA-JETALSAR (GC) - [N22000141]JWR,GUJARAT	04/2012	376.59 -	376.59	2.67	- -	-	-	0/0
350	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	622.41 2,030.50	2,030.50	2.43	02/2019 -	02/2019	0(O)	0/0
351	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	651.17	7.22	- -	-	-	0/0
352	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	4,274.00	-	- -	-	-	0/0
353	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	797.92	- -	03/2015	-	0/0
354	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	4,874.58	400.00	03/2016 -	03/2016	0(O)	0/0
355	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36(O) 15(R)	0/0
356	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	189.24	1.52	- -	-	-	0/0
357	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	603.22	1.49	- -	-	-	0/0
358	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	232.11	12/2008 -	12/2014	72(O)	0/0
359	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP, TAMIL NADU	04/2006	495.74 -	495.74	275.58	06/2013 06/2013	-	-	0/0
360	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	654.00	-	- -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
361	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240(O) -	0/0
362	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	1,922.00	0.55	- -	-	-	0/0
363	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	270.00	305.66	02/2011 02/2011	-	-	0/0
364	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	415.67	13.98	- -	-	-	0/0
365	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	445.25	1.14	- -	-	-	0/0
366	GHUTIASARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	611.03	139.66	12/2011 11/2013	11/2013	-	0/0
367	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	280.00	146.24	02/2006 -	-	-	0/0
368	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	863.23 -	1,072.51	854.60	- -	03/2015	- -	0/0
369	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	1,038.00	590.26	03/1998 -	-	-	0/0
370	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	156.65	53.11	- -	-	-	0/0
371	GUDUR-DURGARAJAPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	283.54	0.16	- -	-	-	0/0
372	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	604.31	- 05/2009	02/2015	- 69(R)	0/0
373	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	593.82	03/1994 -	10/2014	247(O) -	0/0
374	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	206.22	13.68	- -	-	-	0/0
375	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	1,176.09 3,845.60	3,845.60	1.92	02/2020 -	02/2020	0(O) -	0/0
376	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	157.17	76.90	- -	-	-	0/0
377	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]JECR,BIHAR	04/2013	213.01 -	213.01	5.62	- -	-	-	0/0
378	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]JECR,BIHAR	04/2003	528.65 -	324.66	201.06	- -	-	-	0/0
379	HANSIDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	267.09	1.50	- -	-	-	0/0
380	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	172.03	5.86	- -	-	-	0/0
381	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	1,185.64	-	- 09/2009	-	-	0/0
382	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	329.97	0.50	- -	-	-	0/0
383	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	337.30	222.07	- -	03/2012	-	0/0
384	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	1,289.92	924.92	- -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
385	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	230.03	161.01	- -	-	-	0/0
386	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]NWR,RAJASTHAN	04/2008	829.74 -	829.74	72.09	03/2015 -	03/2015	0(O) -	0/0
387	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	400.00	-	- -	-	-	0/0
388	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	2,127.00	47.50	- -	-	-	0/0
389	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	157.94	42.18	- -	-	-	0/0
390	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	445.40	180.42	03/2007 03/2007	03/2015	96(O) 96(R)	0/0
391	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	0.02	- -	-	-	0/0
392	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	2,135.00	108.42	- -	-	-	0/0
393	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR,MULTI STATE	04/2007	313.24 -	313.24	192.00	01/1999 -	-	-	0/0
394	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	653.46	249.71	03/2014 -	03/2014	-	0/0
395	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	162.96	141.87	- -	-	-	0/0
396	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	847.75	838.77	06/2007 -	-	-	0/0
397	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	1,043.56	745.16	03/2012 -	-	-	0/0
398	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	470.00	14.00	- -	-	-	0/0
399	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR,ODISHA	03/2006	201.00 -	201.17	215.46	- -	-	-	0/0
400	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	740.00	583.47	03/2012 03/2012	12/2012	-	0/0
401	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.56	5,996.00	2,460.85	03/2011 03/2014	03/2018	84(O) 48(R)	0/0
402	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	185.74	- -	11/2014	- -	0/0
403	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	923.52	206.80	- -	-	-	0/0
404	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	174.56	57.93	- -	-	-	0/0
405	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	279.70	3.99	- -	-	-	0/0
406	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,604.36	- -	03/2015	- -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
407	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	643.00	-	- -	-	-	0/0
408	KAPTANGANJ-THAWE-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	744.71	552.56	- -	-	-	1/1
409	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	800.00	777.73	- -	10/2012	-	0/0
410	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 -	331.40	141.17	12/2012 -	03/2016	39(O) -	0/0
411	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	1,022.64	743.71	12/2010 -	-	-	0/0
412	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]ER,MULTI STATE	04/2010	423.66 -	423.66	206.48	03/2017 -	03/2017	0(O) -	0/0
413	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	1,054.35	0.97	- -	-	-	0/0
414	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	162.87	131.82	- -	-	-	0/0
415	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65(O) 65(R)	0/0
416	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	1,995.25	320.72	- -	-	-	0/0
417	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	826.57 -	826.57	53.09	- -	-	-	0/0
418	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 -	359.86	2.22	- -	-	-	0/0
419	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	768.87	556.12	- 03/2010	03/2010	-	0/0
420	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	2,957.21	1,840.48	07/2005 -	-	-	0/0
421	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	418.17	235.28	- -	-	-	0/0
422	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	723.00	-	- -	-	-	0/0
423	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	341.41	296.78	03/2012 -	-	-	0/0
424	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	1,045.20	0.03	- -	-	-	0/0
425	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	252.96	1.52	- -	-	-	0/0
426	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	192.56	0.38	- -	-	-	0/0
427	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	346.15	14.82	- -	-	-	0/0
428	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	406.99	141.55	- -	-	-	0/0
429	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	1,630.97	448.45	05/2008 -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
430	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	69.16	03/2014 -	03/2014	-	0/0
431	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	364.06	0.30	- -	-	-	0/0
432	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 -	5,185.44	4,365.70	03/2009 -	03/2016	84(O) -	0/0
433	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	480.00	2.76	07/2008 -	07/2008	-	0/0
434	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	450.00	14.62	- -	-	-	0/0
435	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	800.00	0.54	- -	-	-	0/0
436	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	493.96	120.60	- -	-	-	0/0
437	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	472.00	205.48	- -	-	-	0/0
438	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	900.05	843.26	12/2011 12/2010	-	-	0/0
439	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	791.59	1.74	- -	-	-	0/0
440	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.45	- -	03/2016	- -	0/0
441	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	369.00	106.73	- -	-	-	0/0
442	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	477.88	464.57	03/2012 -	-	-	0/0
443	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	1,112.00	-	- -	-	-	0/0
444	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	285.57 -	285.57	1.95	01/1999 -	-	-	0/0
445	MAVLI JN.-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	855.16	557.65	- -	-	-	0/0
446	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'I'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	1,383.45	437.30	- -	-	-	0/0
447	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	377.44	1.80	- -	-	-	0/0
448	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	439.88 -	439.88	0.78	- -	-	-	0/0
449	MM FROM BURAMARA-CHAKULIA - [N22000305]SER,MULTI STATE	04/2008	466.48 -	466.48	0.25	01/1999 -	-	-	0/0
450	MM FROM PANSKURA-GHATAL NL - [N22000309]SER,WEST BENGAL	04/2011	276.69 -	276.69	-	01/1999 -	-	-	0/0
451	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	250.93	0.11	- -	-	-	0/0
452	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	211.00	4.51	- -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
453	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	390.60	2.51	- -	-	-	0/0
454	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,791.64	03/2014 -	03/2019	60(O) -	0/0
455	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	289.60	- -	12/2014	-	0/0
456	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	1,350.91	285.47	- -	-	-	0/0
457	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	545.64	0.54	- -	-	-	0/0
458	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	281.30	0.58	- -	-	-	0/0
459	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	228.05	0.02	- -	-	-	0/0
460	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	169.82	24.33	- -	-	-	0/0
461	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	1,313.48	1.38	- -	-	-	0/0
462	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	883.00	719.34	02/2009 -	03/2012	-	0/0
463	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 -	1,036.78	401.23	07/2012 -	-	-	0/0
464	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	620.57	-	- -	-	-	0/0
465	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.54	31.20	- -	-	-	0/0
466	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 -	532.87	51.18	- -	-	-	0/0
467	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 -	430.33	202.06	- -	03/2017	-	0/0
468	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	242.22	38.14	- -	-	-	0/0
469	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	4,083.02	7.09	- -	-	-	0/0
470	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	247.75	234.48	- -	-	-	0/0
471	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	241.52	148.33	- -	-	-	0/0
472	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	221.42	21.13	- -	-	-	0/0
473	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR,WEST BENGAL	04/1983	36.80 274.41	703.18	256.24	- -	-	-	0/0
474	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	1,798.00	-	- -	-	-	0/0
475	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR,WEST BENGAL	04/2011	209.77 -	209.77	68.59	- -	03/2017	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
476	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	283.55	11.83	- -	03/2017	- -	0/0
477	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR, MULTI STATE	04/1999	523.17 -	1,418.21	1,039.99	- -	-	-	0/0
478	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR, NAGALAND	04/2006	850.00 -	2,446.57	9.43	03/2015 -	03/2020	60(O) -	0/0
479	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NEFR, MULTI STATE	04/2000	733.00 733.00	2,483.04	1,651.28	12/2008 -	03/2017	99(O) -	0/0
480	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	68.05	03/2014 -	03/2016	24(O) -	0/0
481	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51 -	2,913.51	470.69	03/2016 -	03/2016	0(O) -	0/0
482	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	118.54	03/2016 -	06/2016	3(O) -	0/0
483	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98 -	4,259.48	486.12	03/2016 -	03/2016	0(O) -	0/0
484	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL, ANDHRA PRADESH	07/2006	743.00 -	1,117.11	-	03/2008 06/2008	-	-	0/0
485	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	1,266.89	-	- -	-	-	0/0
486	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	293.74	139.64	12/2010 -	-	-	0/0
487	PANVEL PEN DOUBLING - [N22000255]CR, MULTI STATE	04/2006	96.16 -	260.16	230.82	- -	-	-	0/0
488	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR, BIHAR	04/2001	624.47 -	2,921.00	2,214.57	10/2007 12/2012	12/2015	98(O) 36(R)	0/0
489	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR, TELANGANA	12/1994	124.43 -	925.30	692.19	- -	02/2014	-	0/0
490	PEN ROHA DOUBLING - [N22000254]CR, MULTI STATE	04/2007	98.74 -	203.00	214.24	- -	03/2014	-	0/0
491	PIRPAINTI-BHAGALPUR - [N22000222]ER, MULTI STATE	04/2011	261.38 -	261.38	20.22	- -	-	-	0/0
492	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	915.98	0.09	- -	-	-	0/0
493	PLASSEY-JIAGANJ DOUBLING - [N22000220]ER, MULTI STATE	04/2011	248.07 -	248.07	23.13	03/2015 -	03/2015	0(O) -	0/0
494	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	299.60	1.10	03/2017 -	03/2017	0(O) -	0/0
495	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	323.00	-	- -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
496	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	205.22	1.54	- -	-	-	0/0
497	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR,TAMIL NADU	04/1999	460.94 -	1,030.00	804.20	01/1999 -	-	-	0/0
498	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	1,122.00	852.86	- -	03/2013	-	0/6
499	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	289.93	-	12/2007 03/2010	-	-	0/0
500	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,435.24	03/2009 12/2012	12/2014	69(O) 24(R)	0/0
501	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66(O) 66(R)	0/0
502	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 -	913.48	458.00	- -	-	-	0/0
503	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	598.36	03/2013 -	03/2016	36(O) -	0/0
504	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	1,225.90	243.00	- -	-	-	0/0
505	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	596.40	381.74	06/2004 -	06/2015	132(O) -	0/0
506	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 -	3,019.17	2,962.51	- -	03/2015	-	0/0
507	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	288.97	0.09	- -	-	-	0/0
508	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	872.22	789.79	- -	-	-	0/0
509	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	2,082.75	29.15	- -	-	-	0/0
510	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	603.04 -	1,421.25	416.26	03/2012 -	-	-	0/0
511	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	1,743.00	291.59	- -	-	-	0/0
512	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	755.54	2.95	- -	-	-	0/0
513	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	714.10	42.80	- -	03/2017	-	0/0
514	SAINTIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	193.44	27.19	- -	-	-	0/0
515	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	325.00	248.15	- -	-	-	0/0
516	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	355.81	353.04	- -	-	-	0/0
517	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	385.54	-	03/2010 -	-	-	0/0
518	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 -	155.81	14.00	- -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
519	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	679.27 -	1,111.99	26.36	- -	-	-	0/0
520	SANTOSH PUR-REMOUNT ROAD VIA GARDEN REACH- METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	268.52	78.81	- -	-	-	0/0
521	SEVOK RANGPO, NEFR - [N22000102]NEFR,SIKKIM	04/2008	1,339.48 -	3,375.42	85.19	12/2015 -	12/2015	0(O) -	0/0
522	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	832.47	0.58	- -	-	-	0/0
523	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	678.62	17.47	- -	-	-	0/0
524	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAK PUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	297.47	51.82	- -	-	-	0/0
525	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	277.28	63.20	- -	-	-	0/0
526	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	-	-	0/0
527	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	1,500.00	0.01	- -	-	-	0/0
528	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	183.23 -	818.29	128.11	02/2015 -	02/2015	0(O) -	0/0
529	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	450.00	7.67	- -	-	-	0/0
530	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	516.23	549.03	03/2014 -	-	-	0/0
531	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	810.78	136.68	- -	-	-	0/0
532	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	1,074.45	460.73	06/2005 07/2011	-	-	0/0
533	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.02	148.69	06/2013 -	12/2014	18(O) -	0/0
534	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	365.17	1.30	- -	-	-	0/0
535	TARAKESHWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER,WEST BENGAL	04/2000	1,188.91 -	1,188.91	682.60	- 12/2009	-	-	0/0
536	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	236.93	-	- -	-	-	0/0
537	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	820.00	195.66	- -	-	-	0/0
538	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	420.00	61.53	- -	-	-	0/0
539	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	167.73	100.64	03/2012 -	-	-	0/0
540	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	900.00	587.51	- -	-	-	0/0
541	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP,WEST BENGAL	03/2000	1,049.69 3,156.32	3,176.10	3,480.49	12/2006 -	-	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
542	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	0.18	- -	-	-	0/0
543	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	1,801.01	0.80	- -	-	-	0/0
544	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181(O) -	0/0
545	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR,GUJARAT	04/2008	1,389.62 -	1,389.62	901.82	03/2014 -	-	-	0/0
546	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	380.00	1.33	- -	-	-	0/0
547	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	324.86	03/2010 03/2017	03/2017	84(O) 0(R)	0/0
548	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	1,503.71	78.23	- -	-	-	0/0
549	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	1,280.83	0.84	- -	-	-	0/0
550	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	548.01	199.89	- 03/2010	-	-	0/0
551	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	446.00 -	685.17	135.22	- -	-	-	0/0
552	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR,GUJARAT	04/2010	279.40 -	279.40	213.87	- -	-	-	0/0
553	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	2,501.05	75.91	- -	-	-	0/0
554	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	297.85	6.26	- -	-	-	0/0
555	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	348.85	0.34	- -	-	-	0/0
556	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	876.00	-	- -	-	-	0/0
	Total		163,318.14 -	275,005.73	83,307.56				1/7
	ROAD TRANSPORT AND HIGHWAYS								
557	2 LANING OF DINDIGUL - PERIGULAM THENI-KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	360.50	08/2013 -	02/2015	18(O) -	0/0
558	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	511.54	65.78	11/2013 -	11/2013	-	0/0
559	2 LANING WITH PS AGRA ALIGARH - [N24000220]NHAI,UTTAR PRADESH	10/2012	250.50 -	250.50	361.30	10/2014 -	10/2014	0(O) -	0/0
560	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI,UTTAR PRADESH	01/2013	373.47 -	373.47	268.10	07/2014 -	09/2014	2(O) -	0/0
561	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI,BIHAR	05/2011	351.54 -	351.54	396.40	05/2013 -	05/2013	-	0/0
562	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	09/2014	10(O) -	0/0
563	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,MULTI STATE	04/2012	624.00 -	624.00	439.20	04/2014 -	09/2014	5(O) -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
564	2-LANING WITH PAVED SHOULDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]NHAI,MADHYA PRADESH	10/2011	1,565.00 -	1,565.00	1,502.00	10/2014 -	10/2014	0(O) -	0/0
565	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	356.40	58.28	07/2014 -	07/2014	-	0/0
566	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	137.80	01/2014 -	12/2015	23(O) -	0/0
567	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	226.00	282.30	02/2014 -	02/2014	-	0/0
568	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	664.00	758.30	02/2014 -	02/2014	-	0/0
569	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	405.40	04/2014 -	03/2015	11(O) -	0/0
570	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	325.00	171.00	05/2014 -	05/2014	-	0/0
571	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI,GUJARAT	03/2012	828.00 -	828.00	722.70	09/2014 -	03/2015	6(O) -	0/3
572	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	2,498.76	-	08/2014 -	08/2014	0(O) -	0/0
573	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI,GUJARAT	12/2010	1,008.50 -	1,008.50	1,380.00	06/2013 -	06/2013	-	0/3
574	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	12/2016	39(O) -	0/0
575	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI,GUJARAT	03/2011	785.50 -	785.50	938.20	08/2013 -	08/2013	-	0/3
576	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016	0(O) -	0/0
577	4-LANING OF BARIH-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	459.30	02/2014 -	09/2015	19(O) -	0/0
578	4-LANING OF BRAHAMPUR-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,560.00	08/2013 -	12/2014	16(O) -	0/0
579	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,757.00	08/2013 -	06/2015	22(O) -	0/0
580	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	365.20	08/2013 -	12/2015	28(O) -	0/0
581	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]NHAI,HARYANA	10/2013	283.25 -	283.25	210.10	10/2015 -	10/2015	0(O) -	0/0
582	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.90	07/2013 -	03/2015	20(O) -	0/0
583	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	1,396.18	1,760.00	09/2014 -	09/2014	0(O) -	0/0
584	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	295.10	09/2007 07/2011	06/2015	93(O) 47(R)	0/0
585	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI,GUJARAT	01/2013	2,125.24 -	2,125.24	129.90	12/2015 -	12/2015	0(O) -	0/3
586	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,190.00	11/2012 -	08/2014	21(O) -	0/0
587	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI,TELANGANA	02/2010	390.56 -	390.56	631.70	02/2012 -	06/2013	-	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
588	BAREILY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	384.20	09/2013 -	12/2015	27(O) -	0/0
589	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12(O) -	0/0
590	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,199.00	06/2014 -	08/2014	2(O) -	0/0
591	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI,KARNATAKA	12/2010	480.00 -	480.00	664.00	-	08/2014	-	2/2
592	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35(O) -	0/0
593	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19(O) -	0/0
594	BIJNI TO ASSAM /WB BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	310.70	06/2008 -	03/2015	81(O) -	0/0
595	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	267.10	06/2008 -	03/2015	81(O) -	0/0
596	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.50	06/2005 -	06/2015	120(O) -	0/0
597	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	217.61	258.40	04/2010 01/2016	03/2015	59(O) -10(R)	0/0
598	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2016	77(O) -	0/0
599	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	891.90	03/2013 -	12/2014	21(O) -	0/0
600	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38(O) -	0/0
601	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44(O) -	0/0
602	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19(O) -	0/0
603	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	300.00	176.80	10/2008 -	-	-	0/0
604	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 -	1,928.22	571.30	04/2015 -	04/2015	0(O) -	0/0
605	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	665.10	05/2010 -	12/2014	55(O) -	0/0
606	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	753.90	07/2013 -	08/2014	13(O) -	0/0
607	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	09/2014	15(O) -	0/0
608	DEVIHALLI-HASSAN - [N24000152]NHAI,KARNATAKA	12/2010	453.00 -	453.00	780.80	-	05/2013	-	1/1
609	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	283.20	06/2008 -	08/2014	74(O) -	0/0
610	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 01/2015	10/2014	77(O) -3(R)	0/0
611	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	316.80	09/2010 -	08/2014	47(O) -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
612	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	1,573.00	849.00	09/2015 -	09/2015	0(O) -	0/0
613	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	521.60	09/2008 -	12/2014	75(O) -	0/0
614	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	1,916.79	272.80	11/2016 -	11/2016	0(O) -	0/0
615	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]NHAI,MULTI STATE	02/2013	1,232.00 -	1,232.00	542.90	08/2015 -	08/2015	0(O) -	0/0
616	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	693.10	10/2013 -	11/2015	25(O) -	0/0
617	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI,UTTAR PRADESH	12/2003	155.00 -	201.66	189.20	09/2008 -	12/2014	75(O) -	0/0
618	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,144.00	08/2013 06/2014	09/2014	13(O) 3(R)	0/0
619	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,542.00	09/2012 -	12/2014	27(O) -	2/3
620	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI,ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	10/2014	78(O) -3(R)	0/0
621	GUWAHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
622	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72(O) -	0/0
623	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 361.00	280.00	359.00	02/2009 -	12/2014	70(O) -	0/0
624	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	239.60	07/2009 -	12/2014	65(O) -	0/0
625	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	125.20	09/2007 -	03/2015	90(O) -	0/0
626	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	316.80	10/2013 -	12/2015	26(O) -	0/0
627	HAZARIBAGH-RANCHI - [N24000141]NHAI,JHARKHAND	08/2010	625.07 -	625.07	995.90	01/2013 -	01/2013	-	0/0
628	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	946.00	737.50	- -	-	-	3/3
629	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	608.40	05/2013 -	12/2015	31(O) -	0/0
630	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20(O) -	0/0
631	JAIPUR-REENGUS - [N24000198]NHAI,RAJASTHAN	08/2010	267.81 -	267.81	697.30	02/2013 -	02/2013	-	0/0
632	JAIPUR-TONK-DEOLI - [N24000135]NHAI,RAJASTHAN	06/2010	792.06 -	792.06	1,982.00	12/2012 -	12/2012	-	0/0
633	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,153.00	07/2013 -	12/2014	17(O) -	0/0
634	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	664.90	01/2014 -	12/2014	11(O) -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
635	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	953.88	892.00	07/2013 -	11/2014	16(O) -	0/0
636	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	08/2014	27(O) -	0/0
637	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	284.90	10/2008 -	09/2014	71(O) -	0/0
638	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	706.50	07/2014 -	12/2015	17(O) -	0/0
639	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI,KARNATAKA	09/2010	671.00 -	671.00	1,190.00	- -	06/2015	- -	2/3
640	LUCKNOW-RAIBAREILI - [N24000207]NHAI,UTTAR PRADESH	07/1999	635.90 -	635.90	599.00	07/2012 -	09/2014	26(O) -	0/0
641	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	280.13	170.90	11/2008 12/2014	09/2014	70(O) -3(R)	0/0
642	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	145.80	04/2009 12/2014	03/2015	71(O) 3(R)	0/0
643	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 167.64	167.64	127.50	11/2008 12/2014	12/2014	73(O) 0(R)	0/0
644	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 200.00	200.00	204.80	04/2009 12/2014	12/2014	68(O) 0(R)	0/0
645	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,395.00	06/2013 -	03/2015	21(O) -	0/0
646	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	591.00	03/2013 -	12/2015	33(O) -	0/0
647	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	311.80	06/2008 -	08/2014	74(O) -	0/0
648	NAGPUR-WAINGANGA BRIDGE - [N24000210]NHAI,MAHARASHTRA	04/2012	484.19 -	484.19	285.20	10/2014 -	10/2014	0(O) -	0/0
649	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2015	12/2014	80(O) -1(R)	0/0
650	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 09/2014	09/2014	75(O) 0(R)	0/0
651	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	200.00	281.60	06/2008 -	-	-	0/0
652	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	567.40	06/2015 -	05/2016	11(O) -	0/0
653	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI,TAMIL NADU	09/2010	1,655.00 -	1,655.00	551.40	09/2013 -	09/2013	-	0/0
654	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,122.00	02/2010 -	12/2014	58(O) -	0/0
655	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35(O) -	0/0
656	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	779.30	09/2014 -	10/2015	13(O) -	0/0
657	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40(O) -	0/0
658	PANIPAT-ROHTAK - [N24000151]NHAI,HARYANA	04/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014	0(O) -	0/0
659	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.30	06/2014 -	12/2015	18(O) -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
660	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	574.00	948.60	03/2014 -	08/2014	5(O) -	0/0
661	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	12/2014	22(O) -	0/0
662	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	940.00	1,341.00	07/2012 -	07/2012	-	0/0
663	PUNE-SATARA(NH-4) - [N24000156]NHAI, MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,210.00	03/2013 -	12/2014	21(O) -	0/0
664	PUNE-SHOLAPUR, PKG-II - [N24000193]NHAI, MAHARASHTRA	09/2011	835.00 -	835.00	475.20	01/2014 -	08/2014	7(O) -	0/0
665	PUNE-SHOLAPUR, PKG1 - [N24000127]NHAI, MAHARASHTRA	11/2009	1,110.00 -	1,110.00	1,826.00	05/2012 -	03/2012	-	0/0
666	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,162.00	07/2015 -	06/2016	11(O) -	0/0
667	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI, MADHYA PRADESH	12/2003	251.03 -	251.03	383.70	10/2008 -	12/2014	74(O) -	0/0
668	RANCHI-RARGA-JAMSETHPUR - [N24000215]NHAI, MULTI STATE	12/2012	1,479.00 -	1,479.00	344.90	06/2015 -	06/2015	0(O) -	0/0
669	REENGUS SIKAR - [N24000227]NHAI, RAJASTHAN	03/2012	333.51 -	333.51	269.30	09/2014 -	09/2014	0(O) -	0/0
670	ROHTAK-BAWAL - [N24000169]NHAI, HARYANA	05/2011	650.00 -	650.00	1,162.00	11/2013 -	11/2013	-	0/0
671	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	831.60	03/2013 -	12/2014	21(O) -	0/0
672	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	963.90	05/2014 -	09/2014	4(O) -	0/0
673	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 - 157.47	154.57	265.00	09/2007 03/2014	12/2014	87(O) 9(R)	0/0
674	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI, WEST BENGAL	12/2003	225.00 -	225.00	191.00	07/2008 -	-	-	0/0
675	SIX LANNING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, MULTI STATE	12/2011	1,047.00 -	1,047.00	288.20	06/2014 -	12/2014	6(O) -	0/0
676	SIX LANNING OF HOSUR- KRISHNAGRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	09/2014	9(O) -	0/0
677	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,312.00	12/2013 -	09/2014	9(O) -	0/0
678	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,043.00	05/2014 -	05/2015	12(O) -	0/0
679	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI, KERALA	02/2010	617.00 -	617.00	156.20	08/2012 -	03/2016	43(O) -	0/0
680	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	09/2014	78(O) -4(R)	0/0
681	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	297.50	06/2014 -	12/2014	6(O) -	0/0
682	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40(O) -	2/2

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
683	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	567.00	1,376.00	11/2013 -	11/2013	-	0/0
684	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11(O) -	0/0
685	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	146.90	05/2013 -	12/2014	19(O) -	0/0
686	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	680.00	383.20	- -	07/2014	-	2/2
687	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,081.00	03/2014 -	12/2015	21(O) -	0/0
688	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	606.00	-	- -	-	-	0/0
689	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	65.80	11/2012 -	12/2014	25(O) -	0/0
690	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]NHAI,TAMIL NADU	06/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015	0(O) -	0/0
691	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	1,348.20	-	- -	-	-	0/0
692	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	1,123.17	-	- -	-	-	0/0
	Total		102,321.44 -	104,296.49	90,471.53				14/28
	<u>SHIPPING AND PORTS</u>								
693	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	359.44	211.30	04/2011 11/2011	11/2011	-	0/0
694	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	532.83	505.54	12/2012 11/2013	11/2013	-	0/0
695	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	220.49	47.32	01/2013 06/2013	06/2013	-	0/0
696	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5(O) 0(R)	0/0
697	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	277.03	81.40	12/2011 10/2012	10/2012	-	0/0
698	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 01/2015	01/2015	11(O) 0(R)	0/0
699	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	1,012.23	554.60	12/2013 11/2013	11/2013	-	0/0
700	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,016.95	12/2010 09/2012	03/2015	51(O) 30(R)	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
701	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	755.50	219.00	03/2011 -	03/2013	-	0/0
702	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	1,060.00	0.93	02/2011 -	12/2012	-	0/0
703	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	1,571.60	9.70	10/2008 -	-	-	0/0
704	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	253.36	221.58	- 01/2009	12/2010	-	0/1
705	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	600.00	139.80	03/2006 06/2014	06/2014	-	0/0
706	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	444.10	-	06/2010 -	11/2012	-	0/0
707	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	277.00	0.21	03/2012 -	03/2012	-	0/0
708	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	373.22	371.18	04/2009 11/2009	02/2011	-	0/0
709	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	2,427.40	831.23	10/2008 11/2010	-	-	0/0
710	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	621.53	-	05/2013 -	05/2013	-	0/0
	Total		12,117.12 -	14,450.58	4,745.00				0/1
	<u>TELECOMMUNICATIONS</u>								
711	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	189.58	01/2009 -	12/2014	71(O) -	0/0
712	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 01/2015	01/2015	51(O) 0(R)	0/0
713	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	86.05	06/2009 -	09/2014	63(O) -	0/0
714	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	964.37	251.27	05/2011 -	06/2014	-	0/0
	Total		2,018.15 -	1,843.90	556.35				0/0
	<u>URBAN DEVELOPMENT</u>								
715	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	11,609.00	2,267.57	06/2011 -	03/2013	-	3/3
716	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019	0(O) -	0/0

Sector Wise Details

(August 2014)

						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
717	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	173.08	-	04/2009 -	-	-	0/0
718	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016	0(O) -	0/0
719	FARIDABAD EXTENSION - [N28000057]DMRC,DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8(O) -	0/0
	Total		73,993.32 -	79,266.22	11,652.27				3/3
	<u>WATER RESOURCES</u>								
720	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	1,187.00	35.49	12/2007 -	12/2012	-	0/0
	Total		542.90 -	1,187.00	35.49				0/0
	Grand Total		927,317.65	1,104,729.32	546,379.88				1174/3573


Summary of projects in the Flash Report for the month of August, 2014

Project Implementation - Current Status:

Number of Projects in Previous Month	720
Number of Projects completed/dropped/frozen in Current Month	3
Number of Projects elevated to the status of Major project during the current month	1
Number of Projects Added in Current Month	2
Number of Projects in Current Month	720


Brief Analysis

Project Status with respect to Original Schedule: Out of 720 projects, 6 projects are ahead of schedule, 105 projects are on schedule and 295 projects are delayed. Of the balance, 295 projects do not have fixed dates of commissioning while 19 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

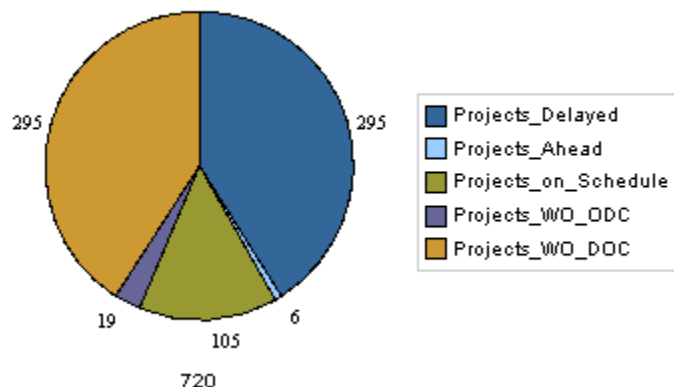

Investment Scenario

Total original cost of implementation of 720 projects when sanctioned, was of the order of Rs. 927317.65 crore but this was subsequently revised to Rs. 1104729.32 crore implying a cost overrun of 19.1%. The expenditure incurred on these projects till August, 2014 is Rs. 546379.88 crore, which is 49.5% of the revised cost of the projects.

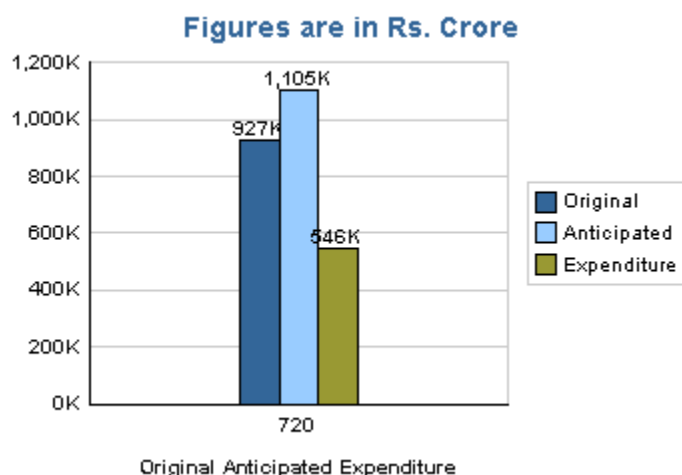

Sector wise current status of projects on the Flash Report

URBAN DEVELOPMENT


Current Status:

Number of Projects	5
Number of Projects On Schedule	2
Number of Projects Delayed	1

Number of Projects Without Date Of Commissioning	2
--	---

Brief Analysis


Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are on schedule and 1 project are delayed .2 projects do not have fixed dates of commissioning.

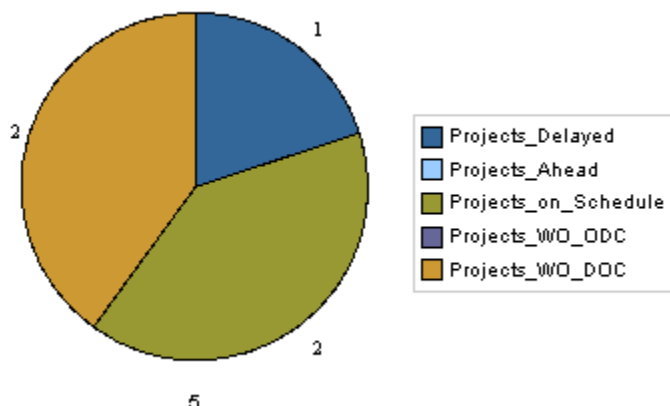

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 73993.32 crore but this was subsequently revised to Rs. 79266.22 crore implying a cost overrun of 7.1%. The expenditure incurred on these projects till August, 2014 is Rs. 11652.27 crore, which is 14.7% of the revised cost of the projects.

Figures are in Rs. Crore

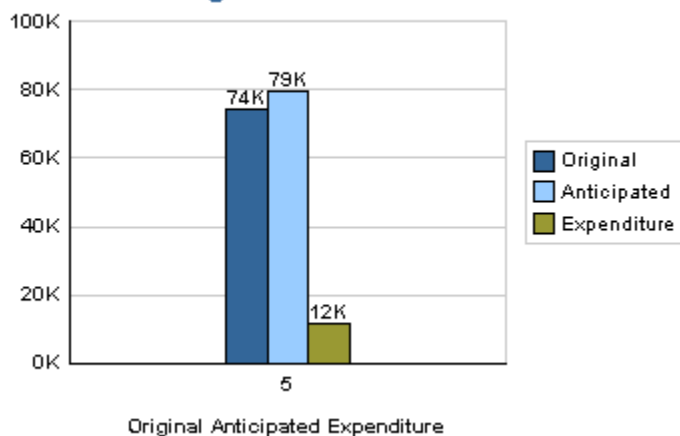

Sector wise current status of projects on the Flash Report


TELECOMMUNICATIONS

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed .1 project do not have fixed dates of commissioning.

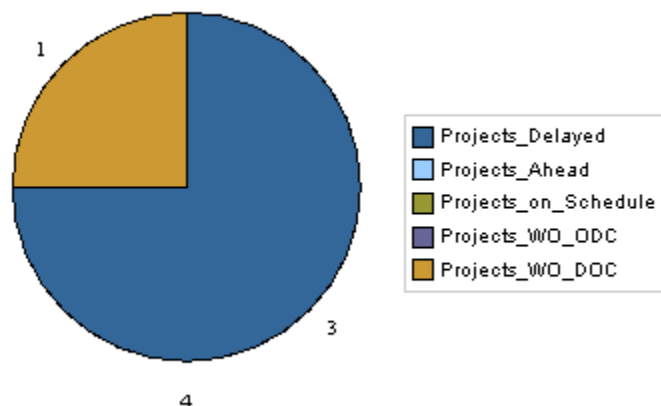

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 2018.15 crore but this was subsequently revised to Rs. 1843.9 crore implying a cost overrun of -8.6%. The expenditure incurred on these projects till August, 2014 is Rs. 556.35 crore, which is 30.2% of the revised cost of the projects.

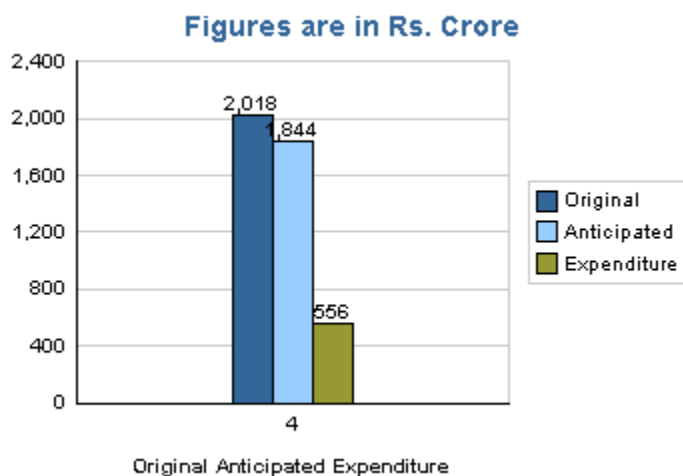

Sector wise current status of projects on the Flash Report

SHIPPING AND PORTS

Current Status:


Number of Projects **18**

Number of Projects Delayed **3**

Number of Projects Without Date Of Commissioning **15**

Brief Analysis


Project Status with respect to Original Schedule: Out of 18 projects, 3 projects are delayed .15 projects do not have fixed dates of commissioning.

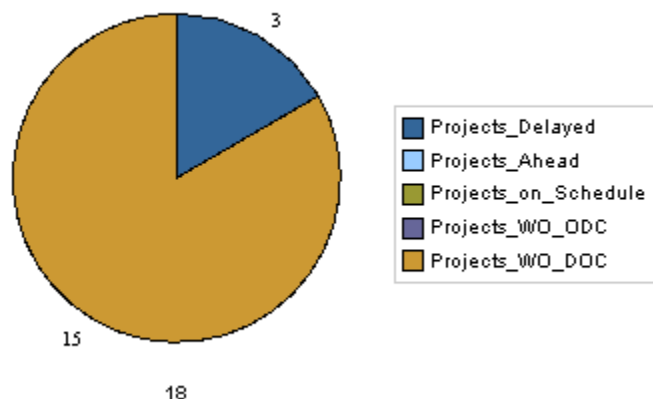

Investment Scenario

Total original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 12117.12 crore but this was subsequently revised to Rs. 14450.58 crore implying a cost overrun of 19.3%. The expenditure incurred on these projects till August, 2014 is Rs. 4745 crore, which is 32.8% of the revised cost of the projects.

Figures are in Rs. Crore

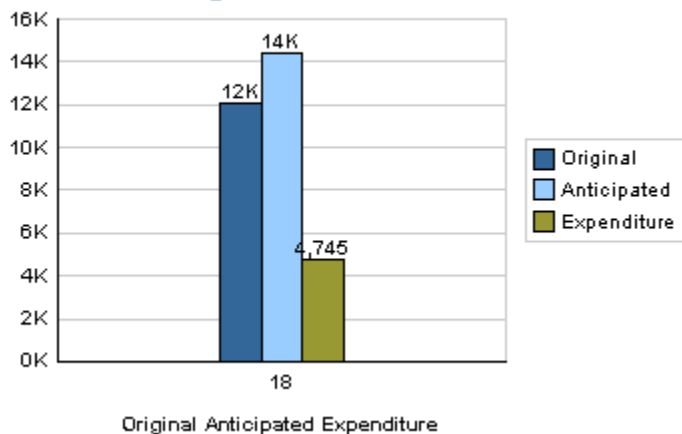

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHW


Current Status:

Number of Projects	136
Number of Projects On Schedule	16
Number of Projects Delayed	92

Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	26

Brief Analysis


Project Status with respect to Original Schedule: Out of 136 projects, 16 projects are on schedule and 92 projects are delayed .26 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

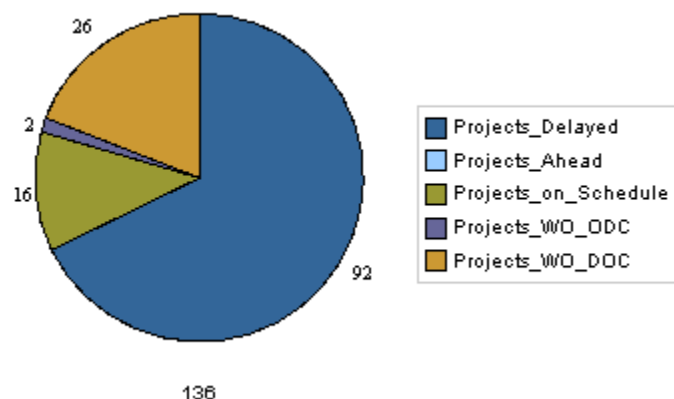

Investment Scenario

Total original cost of implementation of 136 projects when sanctioned, was of the order of Rs. 102321.44 crore but this was subsequently revised to Rs. 104296.49 crore implying a cost overrun of 1.9%. The expenditure incurred on these projects till August, 2014 is Rs. 90471.53 crore, which is 86.7% of the revised cost of the projects.

Figures are in Rs. Crore

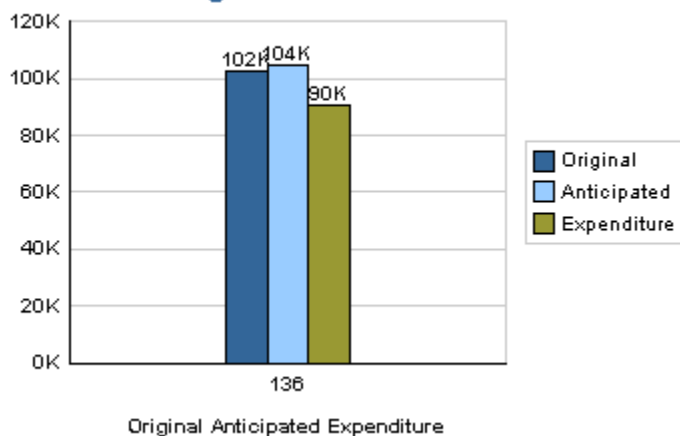

Sector wise current status of projects on the Flash Report

RAILWAYS


Current Status:

Number of Projects	288
Number of Projects On Schedule	12
Number of Projects Delayed	32

Number of Projects Without Original Date of Commissioning	14
Number of Projects Without Date Of Commissioning	230

Brief Analysis


Project Status with respect to Original Schedule: Out of 288 projects, 12 projects are on schedule and 32 projects are delayed .230 projects do not have fixed dates of commissioning.14 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

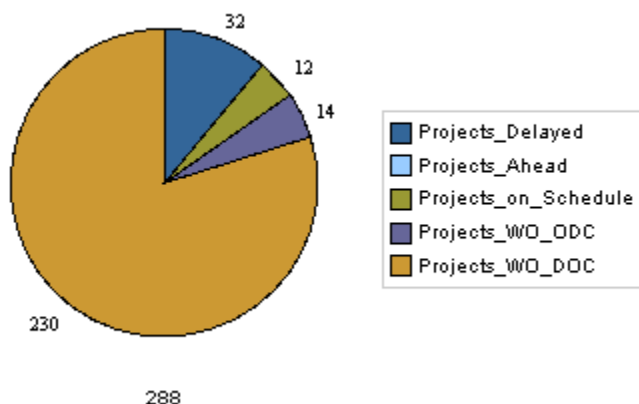

Investment Scenario

Total original cost of implementation of 288 projects when sanctioned, was of the order of Rs. 163318.14 crore but this was subsequently revised to Rs. 275005.73 crore implying a cost overrun of 68.4%. The expenditure incurred on these projects till August, 2014 is Rs. 83307.56 crore, which is 30.3% of the revised cost of the projects.

Figures are in Rs. Crore

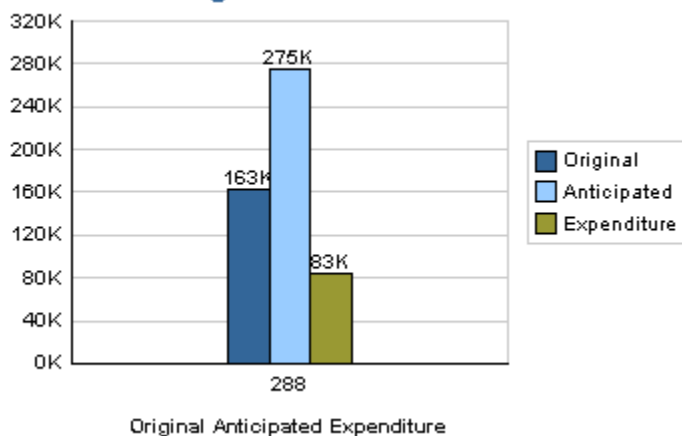

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	101
Number of Projects On Schedule	26
Number of Projects Delayed	64
Number of Projects Ahead	4
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	6


Brief Analysis

Project Status with respect to Original Schedule: Out of 101 projects, 4 projects are ahead of schedule, 26 projects are on schedule and 64 projects are delayed .6 projects do not have fixed dates of commissioning.1 project were sanctioned without any commissioning date but subsequently dates of completion were finalised.

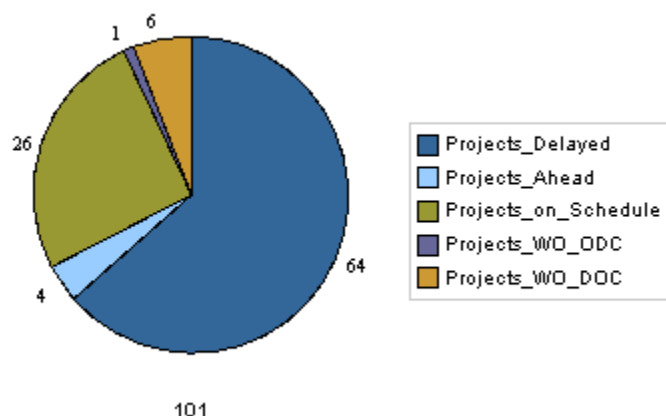

Investment Scenario

Total original cost of implementation of 101 projects when sanctioned, was of the order of Rs. 235782.29 crore but this was subsequently revised to Rs. 249446.64 crore implying a cost overrun of 5.8%. The expenditure incurred on these projects till August, 2014 is Rs. 141316.71 crore, which is 56.7% of the revised cost of the projects.

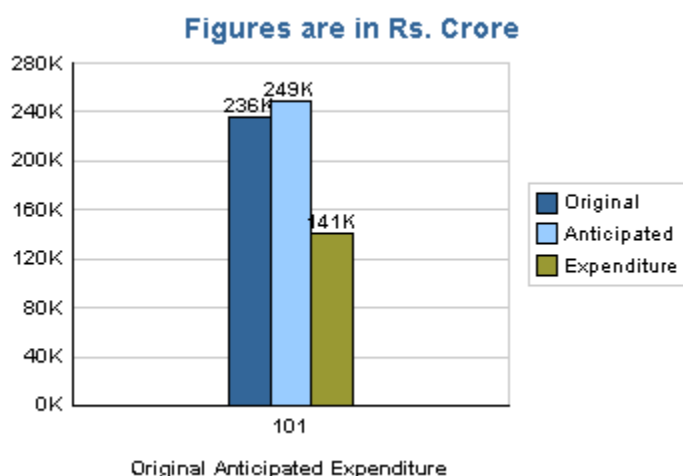

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	75
Number of Projects On Schedule	24
Number of Projects Delayed	43
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	5


Brief Analysis

Project Status with respect to Original Schedule: Out of 75 projects, 1 project are ahead of schedule, 24 projects are on schedule and 43 projects are delayed .5 projects do not have fixed dates of commissioning.2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

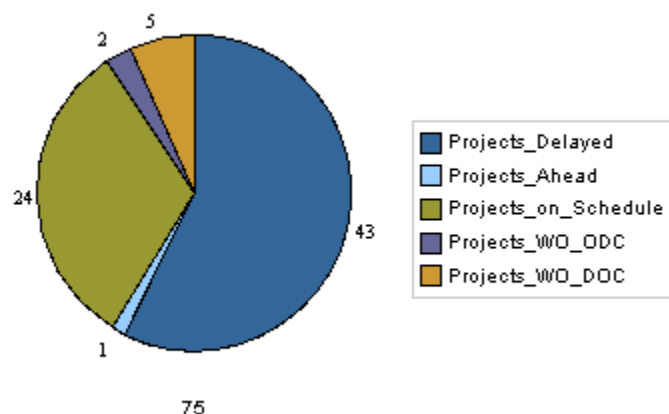

Investment Scenario

Total original cost of implementation of 75 projects when sanctioned, was of the order of Rs. 177359.04 crore but this was subsequently revised to Rs. 192956.69 crore implying a cost overrun of 8.8%. The expenditure incurred on these projects till August, 2014 is Rs. 89744.01 crore, which is 46.5% of the revised cost of the projects.

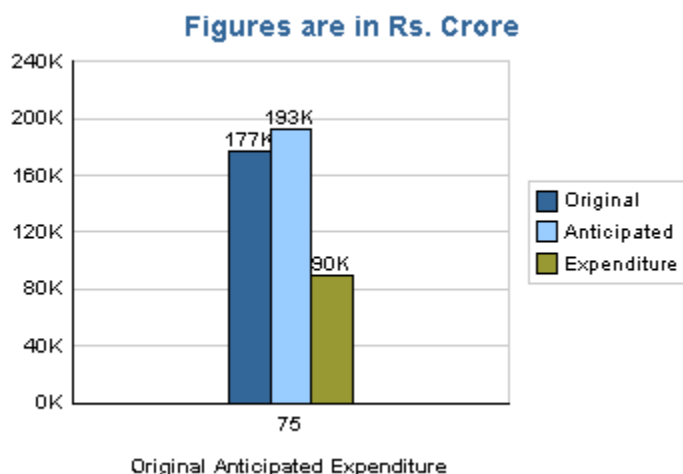

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	20
Number of Projects On Schedule	4
Number of Projects Delayed	16

Brief Analysis


Project Status with respect to Original Schedule: Out of 20 projects, 4 projects are on schedule and 16 projects are delayed.

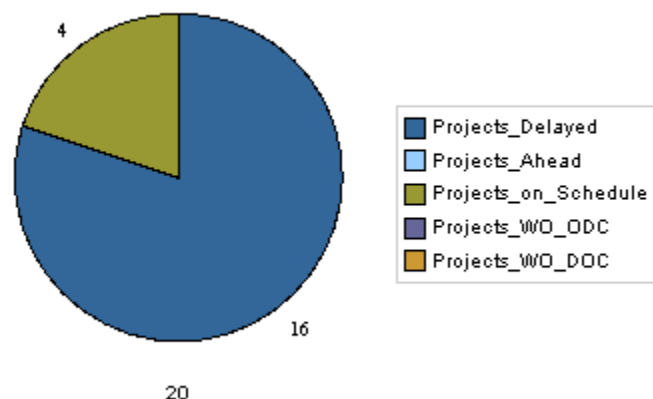

Investment Scenario

Total original cost of implementation of 20 projects when sanctioned, was of the order of Rs. 66395.1 crore but this was subsequently revised to Rs. 72349.06 crore implying a cost overrun of 9%. The expenditure incurred on these projects till August, 2014 is Rs. 61178.76 crore, which is 84.6% of the revised cost of the projects.

Figures are in Rs. Crore

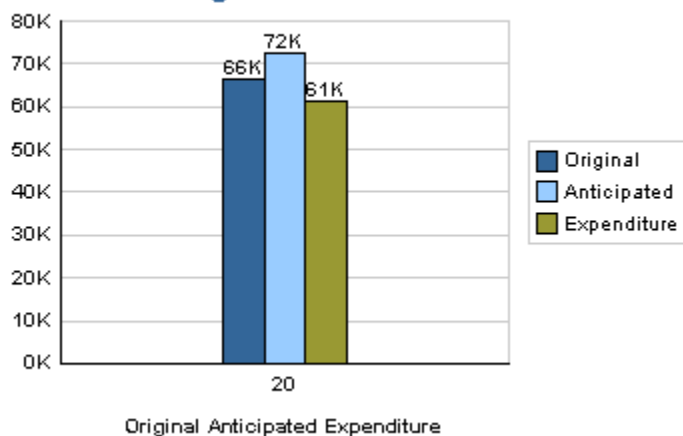

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	59
Number of Projects On Schedule	20
Number of Projects Delayed	34

Number of Projects Without Date Of Commissioning 5

Brief Analysis


Project Status with respect to Original Schedule: Out of 59 projects, 20 projects are on schedule and 34 projects are delayed .5 projects do not have fixed dates of commissioning.

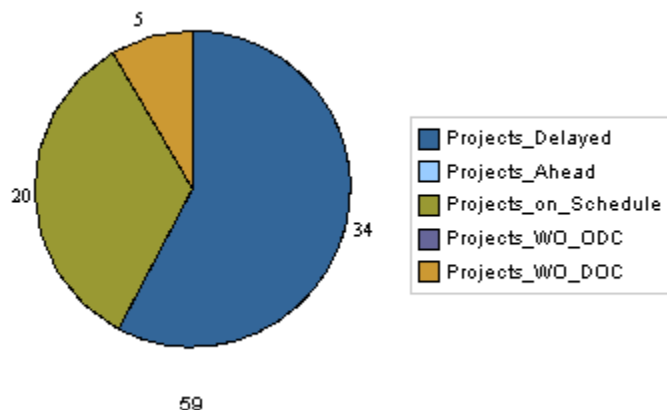

Investment Scenario

Total original cost of implementation of 59 projects when sanctioned, was of the order of Rs. 41532.08 crore but this was subsequently revised to Rs. 51354.22 crore implying a cost overrun of 23.6%. The expenditure incurred on these projects till August, 2014 is Rs. 18758.99 crore, which is 36.5% of the revised cost of the projects.

Figures are in Rs. Crore

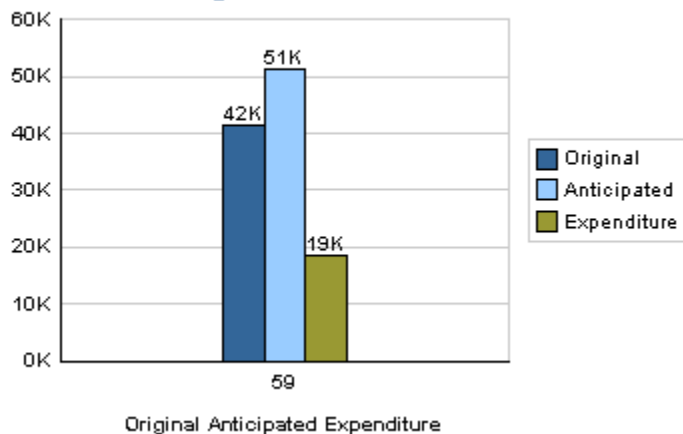

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	8
Number of Projects On Schedule	1
Number of Projects Delayed	3
Number of Projects Ahead	1
Number of Projects Without Date Of Commissioning	3

Brief Analysis


Project Status with respect to Original Schedule: Out of 8 projects, 1 project are ahead of schedule, 1 project are on schedule and 3 projects are delayed .3 projects do not have fixed dates of commissioning.

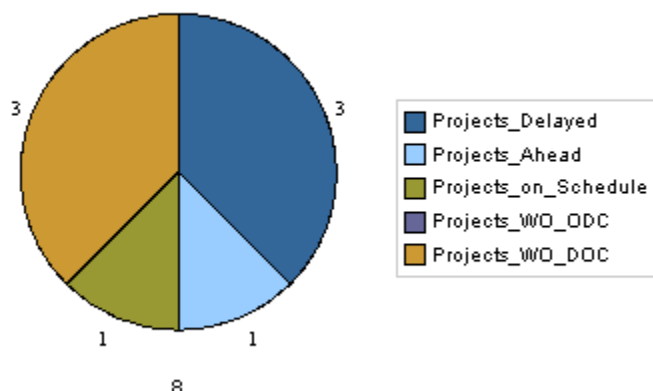

Investment Scenario

Total original cost of implementation of 8 projects when sanctioned, was of the order of Rs. 6035.46 crore but this was subsequently revised to Rs. 6926.79 crore implying a cost overrun of 14.8%. The expenditure incurred on these projects till August, 2014 is Rs. 5874.27 crore, which is 84.8% of the revised cost of the projects.

Figures are in Rs. Crore

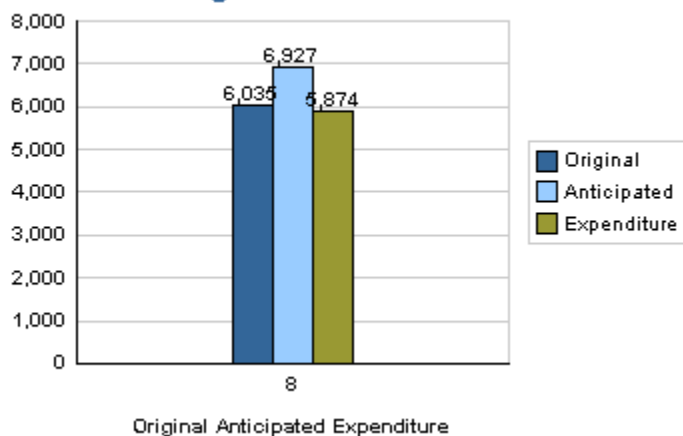

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4


Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed .

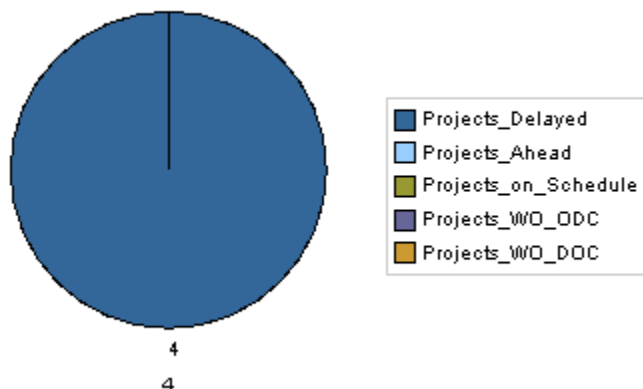

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 40442 crore but this was subsequently revised to Rs. 46726 crore implying a cost overrun of 15.5%. The expenditure incurred on these projects till August, 2014 is Rs. 30894.17 crore, which is 66.1% of the revised cost of the projects.

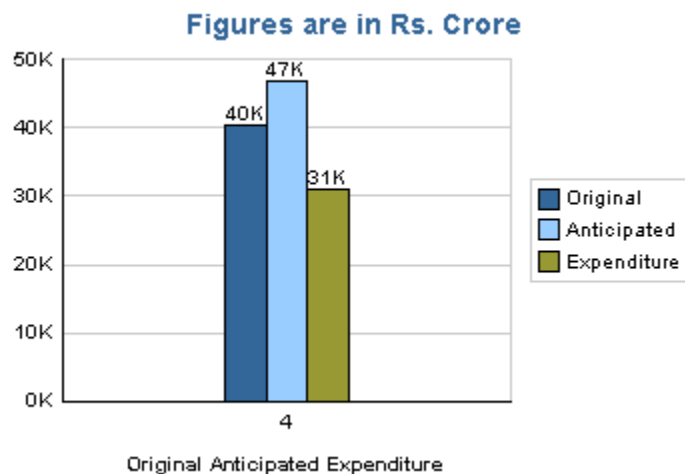

ANNEXURES

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	ANDHRA PRADESH	20	24,072.68	29,249.24	19,980.25
2	ARUNACHAL PRADESH	3	9,356.22	12,067.66	11,014.68
3	ASSAM	38	26,930.69	41,646.22	31,744.56
4	BIHAR	46	34,128.19	40,874.24	33,550.72
5	CHANDIGARH	1	452	452	287.31
6	CHHATISGARH	26	58,226.63	65,735.25	28,811
7	DELHI	4	41,531.33	41,531.33	9,438.62
8	GOA	1	335.61	388.53	283.54
9	GUJARAT	31	37,705.24	38,531.29	18,951.74
10	HARYANA	9	4,540.88	6,690.86	7,305.23
11	HIMACHAL PRADESH	5	13,457.44	20,758.06	14,244.55
12	JAMMU AND KASHMIR	6	13,202.5	30,702.5	15,563.46
13	JHARKHAND	29	21,180.88	21,745.59	11,813.17
14	KARNATAKA	33	77,723.87	92,714.56	29,544.84
15	KERALA	11	19,110.65	23,264.43	7,131.9
16	MADHYA PRADESH	16	23,264.01	24,732.7	7,211.84
17	MAHARASHTRA	44	70,756.24	82,782.92	32,410.82
18	MANIPUR	1	727.56	5,996	2,460.85
19	MEGHALAYA	3	4,845.02	4,845.02	954.29
20	MIZORAM	2	988.06	3,307.11	838.86
21	MULTI STATE	186	2,01,091.33	2,24,912.09	94,003.56
22	NAGALAND	2	5,124	6,720.57	9.43
23	ODISHA	36	62,065.42	70,718.47	47,449.29
24	PUNJAB	3	1,306.26	1,279.22	2,298.27
25	RAJASTHAN	25	25,638.72	25,695.94	13,784.08
26	SIKKIM	2	1,648.94	3,684.88	363.1
27	TAMIL NADU	40	54,818.67	71,711.37	47,854.37
28	TELANGANA	21	9,410.31	12,179.13	3,222.35
29	TRIPURA	6	2,966.26	4,780.63	2,963.64
30	UTTAR PRADESH	25	14,024.68	16,666.2	11,762.52
31	UTTARAKHAND	7	9,501.04	13,063.93	3,997.76
32	WEST BENGAL	38	57,186.32	65,301.38	35,129.28
TOTAL		720	9,27,317.65	11,04,729.32	5,46,379.88

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
1	KUDANKULAM APP (NPCIL)	ATOMIC ENERGY	12/2001	13,171	17270	17,846
2	PARBATI HEP (NHPC) II	POWER	09/2002	3,919.59	-	4,622.4
3	SUBANSIRI LOWER H.E.P (NHPC)	POWER	09/2003	6,285.33	-	6,925.96
4	KAMENG HYDROELECTRIC PROJECT (NEEPCO)	POWER	12/2004	2,496.9	-	3,179.32
5	BARH STPP(3X660MW) NTPC	POWER	12/2003	8,692.97	-	10,223
6	TEESTA LOW DAM HEP, STAGE-IV (NHPC)	POWER	09/2005	1,061.38	-	1,540.94
7	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL)	POWER	03/2005	596.45	-	946.61
8	VIRANGAM-BHILDI(WR), GC	RAILWAYS	04/1990	155.66	-	199.89
9	PEDAPALLI-KARIMNAGAR-NIZAMABAD(NL)(SCR)	RAILWAYS	12/1994	124.43	-	692.19
10	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	RAILWAYS	03/1995	2,500	2500	8,805
11	CALICUT-MANGALORE (DL) (SR)	RAILWAYS	02/1996	240	-	599.4
12	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL), SWR	RAILWAYS	02/1997	295	-	924.92
13	NANGALDAM-TALWARA(NL), NR	RAILWAYS	03/1981	37.68	-	401.23
14	KARUR-SALEM(NL), SR	RAILWAYS	02/1997	155.55	-	777.73

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
15	NANDYAL - YERRAGUNTLA(NL), SCR	RAILWAYS	03/1996	155.74	164.36	719.34
16	KANPUR-KASGANJ-MATHURA(GC), NER	RAILWAYS	03/1997	677.97	1062.36	1,604.36
17	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR	RAILWAYS	09/1997	1,500	-	3,302.95
18	MUNEERABAD-MAHABOBNAGAR(NL), SCR	RAILWAYS	04/1997	218.24	236.41	289.6
19	RANCHI-LOHARDAGA(GC), SER	RAILWAYS	04/1997	194.07	-	381.74
20	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	RAILWAYS	09/1998	247.66	-	448.45
21	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	RAILWAYS	04/1997	501.69	335.77	745.16
22	KATIHAR - JOGBANI (GC)(NEFR)	RAILWAYS	09/2001	492.98	-	743.71
23	GULBARGA-BIDAR, SCR(NL)	RAILWAYS	02/1998	242.42	369.7	604.31
24	JALANDHAR-PATHANKOT-JAMMU-TAWI(LD), NR	RAILWAYS	03/2002	625.3	408.76	838.77
25	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	RAILWAYS	09/1995	100	-	587.51
26	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC)	RAILWAYS	03/1998	280	-	852.86
27	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	RAILWAYS	04/2000	733	733	1,651.28
28	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	RAILWAYS	03/2000	1,049.69	3156.32	3,480.49

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
29	GADWAL - RAICHUR (NL), SCR	RAILWAYS	04/1998	92.63	-	305.66
30	JIND-SONEPAT (NL), NR	RAILWAYS	01/2004	238.56	-	583.47
31	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	RAILWAYS	04/2003	727.56	727.56	2,460.85
32	RAIL-CUM-ROAD BRIDGE AT MUNGERRA (NL), ECR	RAILWAYS	04/2002	921	-	1,435.24
33	PATNA GANGA BRIDGE (NL), ECR	RAILWAYS	04/2001	624.47	-	2,214.57
34	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR	RAILWAYS	01/2004	915.7	-	2,962.51
35	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275	ROAD TRANSPORT AND HIGHWAYS	12/2003	157.47	157.47	265
36	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06	ROAD TRANSPORT AND HIGHWAYS	12/2003	155	-	189.2
37	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31C	ROAD TRANSPORT AND HIGHWAYS	12/2003	230	-	243.5
38	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	200	204.8
39	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	195	-	267.1
40	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	237.8	-	310.7
41	FORBESGANJ TO SIMRAHI (NH-57)(NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	332.94	-	521.6
42	KOTA BYPASS, RJ-4, NH-76 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	275	-	284.9

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
43	RAJMARG CHORAHA TO LAKHNANDON, KM 297 TO KM 351, NH-26 (NHAI)	ROAD TRANSPORT AND HIGHWAYS	12/2003	251.03	-	383.7
44	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT	CIVIL AVIATION	08/2008	1,942.51	-	2,573.92
45	ADRIYALA SHAFT PROJECT	COAL	12/2009	212.34	1228.39	1,248.89
46	EXPANSION OF IISCO STEEL PLANT	STEEL	06/2008	14,443	-	16,226.6
47	DEVELOPMENT OF B-193 CLUSTER FIELDS	PETROLEUM	06/2007	3,248.78	5633.44	5,867.35
48	ASSAM GAS CRACKER PROJECT	PETROCHEMICALS	04/2006	5,460.61	-	7,844.77
49	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT	PETROLEUM	08/2009	246.81	-	260.7
50	RAMPUR HEP(412 MW)	POWER	01/2007	2,047.03	-	3,261.56
51	WESTERN REGION STRENGTHENING SCHEME-V	POWER	12/2007	477.69	-	494.49
52	BARH STPP STAGE -II	POWER	02/2008	7,341.04	-	7,849
53	TRIPURA GAS BASED POWER PROJECT	POWER	07/2009	421.01	623.44	811.41
54	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN	POWER	08/2011	1,391.97	-	1,432.05
55	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT	PETROLEUM	08/2008	144.02	-	154.72
56	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	RAILWAYS	04/1996	332.92	332.92	464.57

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
57	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	RAILWAYS	09/2007	404.19	-	437.3
58	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE	RAILWAYS	09/2006	343.17	-	797.92
59	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR	RAILWAYS	12/2006	170	-	417.14
60	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	RAILWAYS	09/2006	200	-	202.06
61	TAMLUK DIGHA, LINE DOUBLING (SER)	RAILWAYS	03/1984	293.97	-	460.73
62	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR)	RAILWAYS	04/2007	482	-	598.36
63	SURATPURA - HANUMANGARH - SRIGANGANAGAR GAUGE CONVERSION (NWR)	RAILWAYS	04/2008	516.23	-	549.03
64	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	RAILWAYS	04/2006	117.36	196.95	198.63
65	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT	RAILWAYS	04/1996	1,676.31	-	4,365.7
66	RAJKOT-VERAVAL, WANSJALIA TO JATASAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	RAILWAYS	04/1994	320.66	-	458
67	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	RAILWAYS	04/2013	456	-	557.65
68	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC)	RAILWAYS	04/2010	739.65	-	789.79
69	SAKRI-HASANPUR ROAD (NL)	RAILWAYS	04/1999	175.69	-	248.15
70	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	RAILWAYS	04/1999	198.68	-	268.12

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
71	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC	RAILWAYS	04/1999	271.24	-	462.28
72	NEW BG LINE FROM DUDHNOI-MENDIPATAR	RAILWAYS	04/1999	175.43	-	234.48
73	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA	RAILWAYS	04/1999	895	-	977.3
74	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	RAILWAYS	04/2007	247	-	582.03
75	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI	RAILWAYS	04/1999	523.17	-	1,039.99
76	PEN ROHA DOUBLING	RAILWAYS	04/2007	98.74	-	214.24
77	PANVEL PEN DOUBLING	RAILWAYS	04/2006	96.16	-	230.82
78	MUNIRABAD (GINGERA) -RAICHUR NL	RAILWAYS	04/2007	179.65	-	285.47
79	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI	RAILWAYS	04/1999	460.94	-	804.2
80	JHARSUGUDA-RENGALI DOUBLING	RAILWAYS	03/2006	201	-	215.46
81	NALBARI TO BIJNI (AS-8)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	281.6
82	GUWHATI TO NALBARI (AS-4)	ROAD TRANSPORT AND HIGHWAYS	12/2003	175.96	-	182.5
83	NAGAON TO DHARAMTUL (AS-2)	ROAD TRANSPORT AND HIGHWAYS	12/2003	264.72	-	311.8
84	SONAPUR TO GUWAHTI (AS-3)	ROAD TRANSPORT AND HIGHWAYS	12/2003	245	-	491.2

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
85	GUWAHATI TO NALBARI (AS-5)	ROAD TRANSPORT AND HIGHWAYS	12/2003	198.16	-	242.4
86	NALBARI TO BIJNI (AS-6)	ROAD TRANSPORT AND HIGHWAYS	12/2003	225	-	258.4
87	NALBARI T BIJNI (AS-7)	ROAD TRANSPORT AND HIGHWAYS	12/2003	208	230	290.6
88	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	ROAD TRANSPORT AND HIGHWAYS	12/2003	160	-	197.6
89	DHARAMTUL TO SONAPUR (AS-19)	ROAD TRANSPORT AND HIGHWAYS	12/2003	200	-	283.2
90	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH	ROAD TRANSPORT AND HIGHWAYS	03/2005	557	-	1,122
91	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3	ROAD TRANSPORT AND HIGHWAYS	12/2003	232.45	-	316.8
92	DELHI/ HARYANA BORDER TO ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2007	486	-	665.1
93	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III)	ROAD TRANSPORT AND HIGHWAYS	03/2005	940	-	1,341
94	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	ROAD TRANSPORT AND HIGHWAYS	03/2010	1,509.1	-	2,542
95	PUNE-SHOLAPUR, PKG1	ROAD TRANSPORT AND HIGHWAYS	11/2009	1,110	-	1,826
96	KISHANGARH-AJMER-BEAWER	ROAD TRANSPORT AND HIGHWAYS	11/2009	795	-	1,128
97	CHENNAI-TADA(SIX LANE)	ROAD TRANSPORT AND HIGHWAYS	04/2009	353.37	-	446.2
98	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	ROAD TRANSPORT AND HIGHWAYS	02/2009	1,693.75	-	2,762

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
99	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15)	ROAD TRANSPORT AND HIGHWAYS	05/2009	572.3	-	886.9
100	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	ROAD TRANSPORT AND HIGHWAYS	05/2009	1,108	-	3,466
101	JAIPUR-TONK-DEOLI	ROAD TRANSPORT AND HIGHWAYS	06/2010	792.06	-	1,982
102	TALEGAON-AMRAVATI	ROAD TRANSPORT AND HIGHWAYS	11/2009	567	-	1,376
103	HAZARIBAGH-RANCHI	ROAD TRANSPORT AND HIGHWAYS	08/2010	625.07	-	995.9
104	ARMUR TO KADLOOR YELLAREDDY	ROAD TRANSPORT AND HIGHWAYS	02/2010	390.56	-	631.7
105	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM	ROAD TRANSPORT AND HIGHWAYS	09/2010	852	-	891.9
106	KUNDUPUR-SURATHKAL & MANGLORE	ROAD TRANSPORT AND HIGHWAYS	09/2010	671	-	1,190
107	AMRITSAR-PATHANKOT	ROAD TRANSPORT AND HIGHWAYS	05/2010	705	-	2,190
108	DEOLI-KOTA	ROAD TRANSPORT AND HIGHWAYS	01/2011	593	-	753.9
109	PANIPAT-ROHTAK	ROAD TRANSPORT AND HIGHWAYS	04/2011	807	-	1,209.43
110	DEVIHALLI-HASSAN	ROAD TRANSPORT AND HIGHWAYS	12/2010	453	-	780.8
111	MURADABAD-BAREILY	ROAD TRANSPORT AND HIGHWAYS	04/2010	1,267	-	2,395
112	BELGAUM-DHARWAD(NH-4)	ROAD TRANSPORT AND HIGHWAYS	12/2010	480	-	664

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
113	INDORE-DEWAS(NH-3)	ROAD TRANSPORT AND HIGHWAYS	11/2010	325	-	608.4
114	2 LANNING OF MOKAMA-MUNGER	ROAD TRANSPORT AND HIGHWAYS	05/2011	351.54	-	396.4
115	4 LANNING OF AHMEDABAD TO GODHARA	ROAD TRANSPORT AND HIGHWAYS	12/2010	1,008.5	-	1,380
116	4 LANNING OF GODHARA TO GUJARAT/MP BORDER	ROAD TRANSPORT AND HIGHWAYS	03/2011	785.5	-	938.2
117	ROHTAK-BAWAL	ROAD TRANSPORT AND HIGHWAYS	05/2011	650	-	1,162
118	GHAZIABAD-ALIGARH NH-91	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,141	1141	2,144
119	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	ROAD TRANSPORT AND HIGHWAYS	09/2011	1,250	-	1,312
120	SAMAIKHIALI - GANDHIDHAM	ROAD TRANSPORT AND HIGHWAYS	09/2010	805.39	-	831.6
121	JORBAT - BARAPANI	ROAD TRANSPORT AND HIGHWAYS	01/2011	536	-	664.9
122	2-LANNING OF SHILONG BYPASS	ROAD TRANSPORT AND HIGHWAYS	02/2011	226	-	282.3
123	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	ROAD TRANSPORT AND HIGHWAYS	11/2011	1,535	-	2,043
124	2-LANNING WITH PS KHAGARIA-PURNEA	ROAD TRANSPORT AND HIGHWAYS	05/2011	664	-	758.3
125	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	ROAD TRANSPORT AND HIGHWAYS	09/2011	574	-	948.6
126	2-LANNING WITH PS MOTIHARI-RAXAUL	ROAD TRANSPORT AND HIGHWAYS	10/2011	375.09	-	405.4

LIST OF PROJECTS IN WHICH EXPENDITURE IS MORE THAN APPROVED COST

(All Cost /Expenditure in Rs. crore)

S.NO.	PROJECT	SECTOR	DATE OF APPROVAL	COST ORIGINAL	COST REVISED	EXPENDITURE CUMM
127	4-LANNING OF CHAPRA-HAJIPUR	ROAD TRANSPORT AND HIGHWAYS	01/2011	575	-	824.9
128	2 LANNING OF MUZAFFARPUR - SONBARSA	ROAD TRANSPORT AND HIGHWAYS	05/2011	511.54	-	1,179
129	4-LANING OF BARHI-HAZARIBAGH	ROAD TRANSPORT AND HIGHWAYS	02/2012	398	-	459.3
130	BHUBANESWAR TO PURI	ROAD TRANSPORT AND HIGHWAYS	03/2011	500.29	-	622.1
131	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER	ROAD TRANSPORT AND HIGHWAYS	11/2011	909	-	963.9
132	JAIPUR-REENGUS	ROAD TRANSPORT AND HIGHWAYS	08/2010	267.81	-	697.3
133	4-LANING OF FARAKA-RAIGANJ	ROAD TRANSPORT AND HIGHWAYS	02/2011	1,078.84	-	1,757
134	4-LANING OF BRAHAMPURE-FARAKA	ROAD TRANSPORT AND HIGHWAYS	02/2011	998.79	-	1,560
135	6-LANING OF DHANKUNI-KHARAGPUR SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2012	1,396.18	-	1,760
136	KRISHNANAGAR-BERHAMPUR	ROAD TRANSPORT AND HIGHWAYS	02/2012	702.16	-	706.5
137	FOUR LANNING OF WALAYAR-VADAKKANANCHERRY SECTION	ROAD TRANSPORT AND HIGHWAYS	04/2011	682	-	693.1
138	2 LANING WITH PS AGRA ALIGARH	ROAD TRANSPORT AND HIGHWAYS	10/2012	250.5	-	361.3
139	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST	SHIPPING AND PORTS	03/2007	245.67	298.17	371.18

Details of Projects Ahead of Schedule w.r.t. Original Schedule

						(August 2014)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	DEVELOPMENT OF CHANDIGARH INTERNATIONAL AIRPORT(MOHALI) PH - II - [N04000070]	2/2011	452.00 -	452.00	287.31	03/2015 -	02/2015
	Total		452.00 -	452.00	287.31		
	<u>POWER</u>						
2	SYSTEM STRENGTHENING - XVII IN SOUTHERN REGIONAL GRID - [N16000144]	9/2012	1,508.74 -	1,508.74	394.08	06/2016 -	12/2015
	Total		1,508.74 -	1,508.74	394.08		
	<u>PETROLEUM</u>						
3	RESITEMENT OF BILASPUR AND BISRAMPUR DEPOTS TO KORBA (CHATTISGARH) - [N16000186]	1/2011	232.00 -	232.00	89.79	09/2016 -	12/2015
	Total		232.00 -	232.00	89.79		
	<u>POWER</u>						
4	SYSTEM STRENGTHENING -XIX IN SOUTHERN REGIONAL GRID - [N18000137]	9/2012	1,935.35 -	1,935.35	798.98	12/2014 -	11/2014
5	INTER-REGIONAL SYSTEM STRENGTHENING SCHEME IN WR AND NR (PART-A) - [N18000154]	10/2013	1,315.90 -	1,315.90	99.57	11/2016 -	03/2016
6	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,364.52	39.74	05/2016 -	04/2016
	Total		4,615.77 -	4,615.77	938.29		
	Grand Total		6,808.51	6,808.51	1,709.47		

Details of Projects Without Original Date of Commissioning

(August 2014)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>PETROLEUM</u>								
1	SURAT PARADIP PIPELINE PROJECT - [N16000163]GAIL,MULTI STATE	10/2012	10,281.00 -	10,281.00	1.36	- 04/2015	04/2015	0(R3)	0/0
2	DE-BOTTLENECKING OF SMPL - [N16000089]IOCL,MAHARASHTRA	12/2009	1,584.00 -	1,584.00	984.65	- -	08/2015	-	0/12
	Total		11,865.00 -	11,865.00	986.01				0/12
	<u>POWER</u>								
3	AGARTALA GAS TURBINE PLANT COMBINED CYCLE EXTENSION PROJECT (51 MW) - [N18000156]NEEPCO,TRIPURA	07/2012	296.87 -	296.87	260.88	- 03/2015	03/2015	0(R3)	0/17
	Total		296.87 -	296.87	260.88				0/17
	<u>RAILWAYS</u>								
4	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,050.00 -	2,050.00	185.74	- -	11/2014	-	0/0
5	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	218.24 236.41	645.00	289.60	- -	12/2014	-	0/0
6	GULBARGA-BIDAR,SCR(NL) - [220100254]SCR,KARNATAKA	02/1998	242.42 369.70	844.00	604.31	- 05/2009	02/2015	69(R1)	0/0
7	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]NER,UTTAR PRADESH	03/1997	677.97 1,062.36	1,651.54	1,604.36	- -	03/2015	-	0/0
8	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) - [220100255]NER,UTTAR PRADESH	03/2002	863.23 -	1,072.51	854.60	- -	03/2015	-	0/0
9	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315]NEFR,ASSAM	01/2004	915.70 -	3,019.17	2,962.51	- -	03/2015	-	0/0
10	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]SR,TAMIL NADU	09/2006	343.17 -	914.98	797.92	- -	03/2015	-	0/0
11	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	247.00 -	951.24	582.03	- -	03/2015	-	0/0
12	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	258.20	1.45	- -	03/2016	-	0/0
13	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NEFR,ASSAM	04/2011	312.12 -	312.12	113.56	- -	03/2016	-	0/0
14	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NEFR,ASSAM	09/2006	200.00 -	430.33	202.06	- -	03/2017	-	0/0

(August 2014)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Antici Pated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	NEW COOCHBEHAR TO SAMUKTALA - [N22000197]NEFR, WEST BENGAL	04/2011	209.77 -	209.77	68.59	- -	03/2017	-	0/0
16	NEW COOCHBEHAR-GUMANIHAT PATCH DOUBLING PROJECT - [N22000198]NEFR, WEST BENGAL	04/2012	283.55 -	283.55	11.83	- -	03/2017	-	0/0
17	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	714.10	42.80	- -	03/2017	-	0/0
	Total		7,535.47 -	13,356.51	8,321.36				0/0
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
18	BELGAUM-DHARWAD(NH-4) - [N24000158]NHAI, KARNATAKA	12/2010	480.00 -	480.00	664.00	- -	08/2014	-	2/2
19	KUNDUPUR-SURATHKAL & MANGLORE - [N24000146]NHAI, KARNATAKA	09/2010	671.00 -	671.00	1,190.00	- -	06/2015	-	2/3
	Total		1,151.00 -	1,151.00	1,854.00				4/5
	Grand Total		20,848.34	26,669.38	11,422.25				4/34

Details of Projects Without Date of Commissioning

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>CIVIL AVIATION</u>				
1	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]AAI,TAMIL NADU	08/2008	1,808.00 2,015.00	01/2011 02/2012	02/2012
2	C/O INTEGRATED PASSENGER TER. BULD. NSCB AIRPORT - [N04000037]AAI, WEST BENGAL	08/2008	1,942.51 -	05/2011 -	03/2013
3	GAGAN PROJECT - [N04000065]AAI,MULTI STATE	09/2008	626.00 -	06/2013 -	06/2013
	Total		4,376.51 -		
	<u>COAL</u>				
4	KRISHNASHILA (NCL) (4MTY) - [N06000007]NCL,UTTAR PRADESH	06/2011	789.88 -	03/2013 -	03/2014
5	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	04/2014 -	04/2014
6	SHANTIKHANI LONGWALL PROJ-SCCL - [N06000017]SCCL,TELANGANA	10/2006	249.03 -	03/2012 -	-
7	JALLARAM SHAFT PROJECT - [N06000025]SCCL,TELANGANA	09/2007	467.78 -	03/2013 -	-
8	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.14 -	03/2016 -	-
	Total		2,276.71 -		
	<u>PETROCHEMICALS</u>				
9	ASSAM GAS CRACKER PROJECT - [N16000106]BCPL,ASSAM	04/2006	5,460.61 -	04/2012 -	-
	Total		5,460.61 -		
	<u>PETROLEUM</u>				
10	DIESEL HYDROTREATOR PROJECT AT VISAKH REFINERY - [N16000068]HPCL,ANDHRA PRADESH	03/2009	3,597.00 2,730.00	09/2011 03/2012	07/2014
11	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	- -	-
12	NEW MARKETING TERMINAL AT ENNORE - [N16000178]IOCL,TAMIL NADU	11/2006	171.83 -	- -	-
13	JHAJJAR HISSAR PIPE LINE PROJECT - [N16000051]GAIL,HARYANA	11/2007	281.07 -	10/2010 -	-
14	DBNPL SPURLINE (UTTRANCHAL AND PUNJAB) - [N16000094]GAIL,MULTI STATE	12/2009	540.92 -	07/2012 07/2012	-
	Total		5,301.82 -		
	<u>POWER</u>				

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
15	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258]PGCIL,TAMIL NADU	05/2005	1,779.29 2,159.07	09/2008 -	03/2013
16	TR. SYSTEM ASSOCIATED WITH RAMPUR HEP - [N18000063]PGCIL,MULTI STATE	02/2009	184.19 -	11/2011 -	06/2014
17	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246]PGCIL,KARNATAKA	03/2005	596.45 -	12/2007 12/2009	-
18	SYSTEM STRENGTHENING -XII OF SR - [N18000085]PGCIL,MULTI STATE	02/2010	232.34 -	06/2012 -	-
19	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN VEMAGIRI AREA OF ANDHRA PRADESH PART-A1 - [N18000126]PGCIL,ANDHRA PRADESH	03/2012	206.44 -	06/2014 -	-
20	TRANS. SYSTEM ASSOCIATED WITH LARA STPS-I (2X800) GEN. PROJECT OF NTPC - [N18000167]PGCIL,MULTI STATE	06/2014	400.47 -	05/2017 -	-
	Total		3,399.18 -		
	<u>RAILWAYS</u>				
21	MACHERLA-NALGONDA(NL)(SCR) - [220100220]SCR,TELANGANA	07/1998	125.00 -	07/2008 -	07/2008
22	KODERMA GIRIDH (NL), ECR - [220100306]ECR,JHARKHAND	04/1996	768.87 -	- 03/2010	03/2010
23	CALICUT-MANGALORE (DL) (SR) - [220100151]SR,MULTI STATE	02/1996	240.00 -	- -	02/2012
24	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	155.74 164.36	02/2009 -	03/2012
25	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]WS&PU,BIHAR	04/2003	98.74 224.51	- -	03/2012
26	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]WS&PU,BIHAR	03/2005	470.09 1,417.97	- -	03/2012
27	JIND-SONEPAT (NL),NR - [220100280]NR,HARYANA	01/2004	238.56 -	03/2012 03/2012	12/2012
28	GHUTIASHARIF-CANNING (ER) - [N22000117]ER,WEST BENGAL	04/2009	611.03 -	12/2011 11/2013	11/2013
29	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 -	- -	12/2013
30	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106]SCR,TELANGANA	12/1994	124.43 -	- -	02/2014
31	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2014
32	PEN ROHA DOUBLING - [N22000254]CR,MULTI STATE	04/2007	98.74 -	- -	03/2014
33	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA-JAGDALPUR),NL,RVNL - [220100149]RVNL,CHHATISGARH	04/1995	304.00 -	12/2012 -	-
34	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	301.64 -	- 09/2009	-
35	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329]RVNL,ANDHRA PRADESH	04/2003	136.62 -	12/2007 03/2010	-
36	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]RVNL,ANDHRA PRADESH	07/2006	743.00 -	03/2008 06/2008	-
37	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]RVNL,CHHATISGARH	09/2006	324.90 -	03/2010 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
38	VIRAMGAM-BHILDI(WR),GC - [220100062]WR,MULTI STATE	04/1990	155.66 -	- 03/2010	-
39	AMRAVATI-NARKHER NL(CR) - [220100118]CR,MAHARASHTRA	06/1994	663.01 663.01	06/1999 -	-
40	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NEFR, WEST BENGAL	04/1983	36.80 274.41	- -	-
41	MANDARHILL-DUMKA-RAMPURHAT (NL),ER - [220100168]ER,JHARKHAND	04/1995	900.05 -	12/2011 12/2010	-
42	AHMEDNAGAR-PARLI VAJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	514.68 -	- -	-
43	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR - [220100183]SWR,KARNATAKA	02/1997	295.00 -	- -	-
44	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08 -	- -	03/2014
45	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	386.30 1,038.00	03/1998 -	-
46	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	37.68 -	07/2012 -	-
47	KARUR-SALEM(NL),SR - [220100191]SR,TAMIL NADU	02/1997	155.55 -	- -	10/2012
48	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	227.00 997.58	- -	-
49	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]ECR,JHARKHAND	03/1999	2,957.21 -	07/2005 -	-
50	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	05/2008 -	-
51	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	501.69 335.77	03/2012 -	-
52	KATIHAR - JOGBANI (GC)(NEFR) - [220100247]NEFR,BIHAR	09/2001	492.98 -	12/2010 -	-
53	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	550.00 517.70	- -	-
54	KAPTANGANJ-THAWA-SIWAN-CHHAPRA GC (NER) - [220100256]NER,MULTI STATE	04/1999	744.71 -	- -	-
55	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 -	- -	-
56	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]NR,MULTI STATE	03/2002	625.30 408.76	06/2007 -	-
57	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	100.00 -	- -	-
58	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) - [220100263]SR,MULTI STATE	03/1998	280.00 -	- -	03/2013
59	KOTPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	330.00 -	- -	-
60	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 3,156.32	12/2006 -	-
61	GADWAL - RAICHUR (NL), SCR - [220100270]SCR,MULTI STATE	04/1998	92.63 -	02/2011 02/2011	-
62	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	- 12/2009	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 240.59	12/2012 12/2012	-
64	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	02/1999	138.00 -	- -	-
65	BANKURA - DAMODAR (GC) (SER) - [220100277]SER,WEST BENGAL	03/1998	111.90 1,039.29	03/2005 12/2008	-
66	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	470.21 -	- -	-
67	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 -	- -	-
68	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	322.95 -	03/2012 -	-
69	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 -	- -	-
70	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	- -	-
71	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]WCR,MADHYA PRADESH	04/2001	470.92 727.13	- -	-
72	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316]NER,BIHAR	04/2003	218.19 -	- -	-
73	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03 -	- -	-
74	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 -	- -	-
75	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	332.92 332.92	03/2012 -	-
76	EXT. OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTT,TAMIL NADU	04/2006	495.74 -	06/2013 06/2013	-
77	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	378.56 -	- -	-
78	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045]SER,JHARKHAND	03/1997	261.70 -	02/2006 -	-
79	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	404.19 -	- -	-
80	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]NEFR,MULTI STATE	12/2006	170.00 -	03/2011 -	-
81	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	125.00 -	- -	-
82	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	456.00 -	- -	-
83	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NEFR,BIHAR	09/2006	300.00 -	- -	-
84	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL	04/2007	1,106.62 -	12/2010 -	-
85	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]SER,WEST BENGAL	03/1984	293.97 -	06/2005 07/2011	-
86	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NEFR,BIHAR	04/2008	282.92 -	- -	-
87	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]NWR,RAJASTHAN	04/2008	653.19 653.19	03/2014 -	03/2014
88	SURATPURA - HANUMANGARH - SRIGANGANAGAR GUAGE CONVERSION (NWR) - [N22000114]NWR,RAJASTHAN	04/2008	516.23 -	03/2014 -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
89	TINPAHAR - SAHIBGANJ (ER) - [N22000115]ER,JHARKHAND	04/2008	167.73 -	03/2012 -	-
90	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]ER, WEST BENGAL	04/2009	259.51 -	12/2011 -	-
91	PANDABESWAR-CHINPAI DOUBLING (ER) - [N22000118]ER, WEST BENGAL	04/2004	293.74 -	12/2010 -	-
92	BANDEL-NAIHATI NEW RAIL BRIDGE IN REPLACEMENT OF JUBILEE BRIDGE NO.8 (ER) - [N22000119]ER, WEST BENGAL	04/1999	207.52 -	12/2012 -	-
93	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR, MADHYA PRADESH	04/2008	603.04 -	03/2012 -	-
94	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR, GUJARAT	04/2008	394.14 -	03/2013 -	-
95	UDHNA-JALGAON WITH ELECTRIFICATION(DOUBLING) (WR) - [N22000122]WR, GUJARAT	04/2008	1,389.62 -	03/2014 -	-
96	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR, GUJARAT	04/2008	318.24 -	03/2012 -	-
97	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR, GUJARAT	04/2006	117.36 196.95	03/2011 -	-
98	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
99	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER, MULTI STATE	03/2007	243.78 -	- -	-
100	BHOJIPUR TANAKPUR VIA PILIBHIT - [N22000132]NER, UTTAR PRADESH	03/2008	195.64 -	- -	-
101	AUNRIHAR MANDUADIH GAZIPUR VARANASI UP - [N22000133]NER, UTTAR PRADESH	03/2012	199.75 -	- -	-
102	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	- -	-
103	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
104	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	- -	-
105	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR, MULTI STATE	04/2007	1,347.26 -	- -	-
106	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR, MULTI STATE	04/2007	1,640.04 -	- -	-
107	AHMEDABAD-BOTAD (GC) - [N22000140]WR, GUJARAT	04/2012	567.18 -	- -	-
108	DHASA-JETALSAR (GC) - [N22000141]WR, GUJARAT	04/2012	376.59 -	- -	-
109	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR, GUJARAT	04/2011	439.88 -	- -	-
110	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR, GUJARAT	04/1994	320.66 -	- -	-
111	PALANPUR-SAMAKHAYALI (DL) - [N22000144]WR, GUJARAT	04/2013	1,266.89 -	- -	-
112	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR, GUJARAT	04/2011	446.00 -	- -	-
113	VIRAMGAM-SURENDRANAGAR (DL) - [N22000146]WR, GUJARAT	04/2010	279.40 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
114	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2012	2,082.75 -	- -	-
115	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	- -	-
116	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
117	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
118	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	456.00 -	- -	-
119	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]NWR,RAJASTHAN	04/2010	739.65 -	- -	-
120	GURIYA-MARWAR AND KARJODA-PALANPUR - [N22000154]NWR,RAJASTHAN	04/2011	239.73 -	- -	-
121	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	- -	-
122	RANI-MARWAR JN. PATCH DOUBLING - [N22000156]NWR,RAJASTHAN	04/2012	288.97 -	- -	-
123	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	- -	-
124	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	-
125	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	553.63 -	- -	-
126	BHADUTOLA-JHARGRAM VIA LALGARH (NL) - [N22000161]SER,WEST BENGAL	04/2011	289.64 -	- -	-
127	ARA-BHABHUA ROAD (NL) - [N22000166]SER,BIHAR	04/2008	490.80 -	- -	-
128	NAWADA-LAXMIPUR (NL) - [N22000167]SER,BIHAR	04/2008	620.57 -	- -	-
129	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECOR,BIHAR	04/2008	445.25 -	- -	-
130	GAYA-CHATRA (NL) - [N22000169]ECOR,MULTI STATE	04/2008	415.67 -	- -	-
131	BIHTA-AURANGABAD (NL) - [N22000170]ECOR,BIHAR	04/2008	326.20 -	- -	-
132	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECOR,BIHAR	04/1999	175.69 -	- -	-
133	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECOR,BIHAR	04/2006	285.07 -	- -	-
134	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	- -	-
135	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	- -	-
136	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	- -	-
137	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05 -	- -	-
138	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	304.41 -	- -	-
139	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
140	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	- -	-
141	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 -	- -	-
142	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	470.00 -	- -	-
143	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR	04/2013	213.01 -	- -	-
144	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NEFR,MULTI STATE	04/2013	1,798.00 -	- -	-
145	ATTIPPATTU-PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	446.87 -	- -	-
146	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	-
147	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
148	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	-
149	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188]SR,TAMIL NADU	04/1999	271.24 -	- -	-
150	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189]SR,MULTI STATE	04/2008	822.39 -	- -	-
151	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	-
152	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
153	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192]NEFR,MULTI STATE	04/1999	175.43 -	- -	-
154	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NEFR,WEST BENGAL	04/2010	221.42 -	- -	-
155	AGARTALA-AKHAURA NL - [N22000195]NEFR,TRIPURA	04/2012	252.00 -	- -	-
156	DIMAPUR-TIZIT NL - [N22000196]NEFR,NAGALAND	04/2013	4,274.00 -	- -	-
157	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
158	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- -	-
159	CHENGANNUR-CHINGAVANAM - [N22000203]SR,KERALA	04/2006	191.72 -	- -	-
160	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
161	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NEFR,MEGHALAYA	04/2010	4,083.02 -	- -	-
162	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NEFR,MULTI STATE	04/2010	242.22 -	- -	-
163	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NEFR,MULTI STATE	04/2010	241.52 -	- -	-
164	MURKONGSELEK-PASIGHAT NL - [N22000208]NEFR,MULTI STATE	04/2011	165.82 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
165	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209]NEFR,MULTI STATE	04/1999	523.17 -	- -	-
166	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211]NEFR,ASSAM	04/2012	246.07 -	- -	-
167	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	-
168	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	601.43 -	- -	-
169	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1999	406.99 -	- -	-
170	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	-
171	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	-
172	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	- -	-
173	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	-
174	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	-
175	HABRA-CHANDPARA, MM FOR MACHALANDPUR-SWARUPNAGAR NL - [N22000223]ER,MULTI STATE	04/2000	157.17 -	- -	-
176	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	- -	-
177	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.91 -	- -	-
178	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	-
179	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	- -	-
180	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	296.44 -	- -	-
181	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	- -	-
182	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	499.30 -	- -	-
183	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	277.70 -	- -	-
184	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	-
185	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	-
186	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	267.09 -	- -	-
187	SAINTHIA-TARAPITH 3RD LINE - [N22000237]ER,MULTI STATE	04/2011	193.44 -	- -	-

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
188	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	-
189	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	- -	-
190	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	-
191	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA & CHAND - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	-
192	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	493.96 -	- -	-
193	NABADWIPDHAM-PATULI DOUBLING - [N22000246]ER,MULTI STATE	04/2010	169.82 -	- -	-
194	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	182.06 -	- -	-
195	SANTOSHUPUR-REMOUNT ROAD VIA GARDEN REACH-METIABRUZE - [N22000248]ER,MULTI STATE	04/2010	268.52 -	- -	-
196	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	-
197	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	297.85 -	- -	-
198	PANVEL PEN DOUBLING - [N22000255]CR,MULTI STATE	04/2006	96.16 -	- -	-
199	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	913.00 -	- -	-
200	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257]SWR,KARNATAKA	04/2007	179.65 -	- -	-
201	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	377.93 -	- -	-
202	MANUGURU-RAMAGUNDAM - [N22000259]SCOR,TELANGANA	04/2013	1,112.00 -	- -	-
203	KONDAPALLI-PENUBALLI - [N22000260]SCOR,MULTI STATE	04/2013	723.00 -	- -	-
204	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCOR,MULTI STATE	04/2012	1,054.35 -	- -	-
205	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]SCOR,MULTI STATE	04/2008	184.26 -	- -	-
206	BHADRACHALAM-KOVVUR - [N22000264]SCOR,MULTI STATE	04/2012	923.23 -	- -	-
207	GUDUR-DURGARAJPATNAM - [N22000265]SCOR,ANDHRA PRADESH	04/2011	283.54 -	- -	-
208	MEERUT-MUZAFARNAGAR PATCH DL - [N22000267]NR,UTTAR PRADESH	04/2012	377.44 -	- -	-
209	MANSA-BHATINDA PH-1 INCLUDING MM FOR RAMA MANDI(RAMAN)-MAUR MANDI VIA TALWANDI SABOO NL - [N22000268]NR,PUNJAB	04/2009	396.04 -	- -	-
210	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	- -	-
211	FAIZABAD-LALGANJ VIA AKBARGANJ, MAHARAJGANJ AND RAEBARELI - [N22000270]NR,UTTAR PRADESH	04/2013	654.00 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
212	DELHI-SOHNALAHIRKALWAR - [N22000271]NR,MULTI STATE	04/2013	1,239.00 -	- -	-
213	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	- -	-
214	BHANUPALI-BILASPUR BERI NL - [N22000273]NR,HIMACHAL PRADESH	04/2008	1,046.88 -	- -	-
215	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	- -	-
216	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	-
217	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	-
218	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	562.74 -	- -	-
219	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	970.34 -	- -	-
220	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	341.05 -	- -	-
221	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	- -	-
222	CUMBUM-PRODDATUR - [N22000282]SCOR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
223	MUDKHED-PARBHANI - [N22000283]SCOR,MAHARASHTRA	04/2011	390.60 -	- -	-
224	NADIKUDE-SRI KALAHASTI - [N22000286]SCOR,ANDHRA PRADESH	04/2011	1,313.48 -	- -	-
225	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCOR,MULTI STATE	04/2010	337.49 -	- -	-
226	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
227	AMBALA CANTT-DHAPPER PH-1 WITH NEW MM OF DHAPPER-CHANDIGARH - [N22000290]NR,MULTI STATE	04/2010	338.54 -	- -	-
228	JAKHAL-MANSA DOUBLING ON SPR SECTION - [N22000291]NR,MULTI STATE	04/2008	162.96 -	- -	-
229	HISSAR-SIRSA VIA AGROHA AND FATEHABAD - [N22000292]NR,HARYANA	04/2013	400.00 -	- -	-
230	YAMUNANAGAR-CHANDIGARH VIA SADHAURA NARAYANGARH - [N22000293]NR,MULTI STATE	04/2013	876.00 -	- -	-
231	UNCHAHA-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	380.00 -	- -	-
232	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	- -	-
233	CHANDIGARH-BADDI NL - [N22000296]NR,MULTI STATE	04/2007	328.14 -	- -	-
234	HOSPET-HUBLI-LONDA-VASCO DAGAMA DL - [N22000297]SWR,KARNATAKA	04/2010	2,127.00 -	- -	-
235	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	-
236	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	1,117.00 -	- -	-
237	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	-

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
238	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	-
239	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	-
240	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]SR, TAMIL NADU	04/1999	460.94 -	01/1999 -	-
241	JAGGAYYAPET - MELLACHERUVU - [N22000304]SCR, MULTI STATE	04/2007	313.24 -	01/1999 -	-
242	MM FROM BURAMARA-CHAKULIA - [N22000305]SER, MULTI STATE	04/2008	466.48 -	01/1999 -	-
243	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	285.57 -	01/1999 -	-
244	MM FROM PANSKURA-GHATAL NL - [N22000309]SER, WEST BENGAL	04/2011	276.69 -	01/1999 -	-
245	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR(221 KM) - [N22000313]RVNL, ANDHRA PRADESH	03/2012	1,503.71 -	- -	-
246	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	679.27 -	- -	-
247	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR, ODISHA	03/2013	858.67 -	- -	-
248	JHARSUGUDA-RENGALI DOUBLING - [N22000317]ECOR, ODISHA	03/2006	201.00 -	- -	-
249	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR, CHHATISGARH	12/2012	826.57 -	- -	-
250	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 -	- -	-
	Total		111,547.08 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
251	PUNE-SHOLAPUR, PKG1 - [N24000127]NHAI, MAHARASHTRA	11/2009	1,110.00 -	05/2012 -	03/2012
252	PIMPALGAON-NASIK-GONDE, NH-3 (NHDP-PHASE-III) - [N24000123]NHAI, MAHARASHTRA	03/2005	940.00 -	07/2012 -	07/2012
253	JAIPUR-TONK-DEOLI - [N24000135]NHAI, RAJASTHAN	06/2010	792.06 -	12/2012 -	12/2012
254	HAZARIBAGH-RANCHI - [N24000141]NHAI, JHARKHAND	08/2010	625.07 -	01/2013 -	01/2013
255	JAIPUR-REENGUS - [N24000198]NHAI, RAJASTHAN	08/2010	267.81 -	02/2013 -	02/2013
256	DEVIHALLI-HASSAN - [N24000152]NHAI, KARNATAKA	12/2010	453.00 -	- -	05/2013
257	2 LANNING OF MOKAMA-MUNGER - [N24000166]NHAI, BIHAR	05/2011	351.54 -	05/2013 -	05/2013
258	ARMUR TO KADLOOR YELLAREDDY - [N24000143]NHAI, TELANGANA	02/2010	390.56 -	02/2012 -	06/2013
259	4 LANNING OF AHMEDABAD TO GODHARA - [N24000167]NHAI, GUJARAT	12/2010	1,008.50 -	06/2013 -	06/2013
260	4 LANNING OF GODHARA TO GUJARAT/MP BORDER - [N24000168]NHAI, GUJARAT	03/2011	785.50 -	08/2013 -	08/2013
261	NEW 4 LANE ELEVATED ROAD FROM CHENNAI AIRPORT-MADURAVOYAL NH NO.4 - [N24000139]NHAI, TAMIL NADU	09/2010	1,655.00 -	09/2013 -	09/2013

					Date of Commissioning (Month/Year)
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
262	TALEGAON-AMRAVATI - [N24000140]NHAI,MAHARASHTRA	11/2009	567.00 -	11/2013 -	11/2013
263	ROHTAK-BAWAL - [N24000169]NHAI,HARYANA	05/2011	650.00 -	11/2013 -	11/2013
264	2 LANING OF MUZAFFARPUR - SONBARSA - [N24000174]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	11/2013
265	2-LANNING OF SHILONG BYPASS - [N24000181]NHAI,MEGHALAYA	02/2011	226.00 -	02/2014 -	02/2014
266	2-LANNING WITH PS KHAGARIA-PURNEA - [N24000184]NHAI,BIHAR	05/2011	664.00 -	02/2014 -	02/2014
267	2LANING WITH PS GOPALGANJ-CHAPRA - [N24000190]NHAI,BIHAR	12/2011	325.00 -	05/2014 -	05/2014
268	UGRADATION OF HYDERABAD-BANGALORE SECTION - [N24000160]NHAI,KARNATAKA	11/2010	680.00 -	- -	07/2014
269	2-LANING WITH PAVED SHOULDER OF MUZAFFARPUR-BARAUNI - [N24000211]NHAI,BIHAR	07/2012	356.40 -	07/2014 -	07/2014
270	DEEWAPUR TO UP/BIHAR BORDER (LMNHP-9)-NH-28, KM.402-360.915 - [240106244]NHAI,BIHAR	12/2003	300.00 -	10/2008 -	-
271	SILIGURI TO ISLAMPUR (WB-7) - [N24000028]NHAI,WEST BENGAL	12/2003	225.00 -	07/2008 -	-
272	NALBARI TO BIJNI (AS-8) - [N24000035]NHAI,ASSAM	12/2003	200.00 -	06/2008 -	-
273	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	- -	-
274	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA	05/2013	1,348.20 -	- -	-
275	VIJAYAWADA MACHILIPATNAM OF NH-9 ON BOT(TOOL) UNDER NHDP-III - [N24000234]NHAI,ANDHRA PRADESH	09/2013	606.00 -	- -	-
276	YADGIRI-WARANGAL OF NH 202(NEW NH 163) UNDER NHDP-IV - [N24000235]NHAI,TELANGANA	04/2014	1,123.17 -	- -	-
	Total		17,107.35 -		
	<u>SHIPPING AND PORTS</u>				
277	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]PORT TRUST,ODISHA	12/2005	154.84 253.36	- 01/2009	12/2010
278	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST - [N25000059]RVNL,KERALA	03/2007	245.67 298.17	04/2009 11/2009	02/2011
279	ACQUISITION OF 4 NO. OF ANCHOR HANDLING CUM SUPPLY VESSELS - [N25000014]SHIPP.,MAHARASHTRA	10/2007	359.44 -	04/2011 11/2011	11/2011
280	MODIFICATION & STRENGTHENING OF EXISTING BERTH NO. 1 TO 6 - [N25000050]PORT TRUST,GUJARAT	06/2010	277.00 -	03/2012 -	03/2012
281	ACQUISITION OF TWO NOS. OF 3060 DWT - [N25000043]SHIPP.,MAHARASHTRA	04/2009	277.03 280.00	12/2011 10/2012	10/2012
282	MECHANIZATION OF COAL HANDLING FACILITIES TO 200000 DWT VESSELS ON DBFOT BASIS - [N25000049]PORT TRUST,ANDHRA PRADESH	02/2010	444.10 -	06/2010 -	11/2012
283	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST - [N25000037]PORT TRUST,GUJARAT	04/2005	882.00 -	02/2011 -	12/2012
284	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]PORT TRUST,GUJARAT	12/2005	702.00 -	03/2011 -	03/2013

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
285	SETTING UP OF SINGLE POINT MOORING (SPM) AND ALLIED FACILITIES OFF VEERA IN GULF OF KUTCH ON BOT BAS - [N25000060]PORT TRUST,GUJARAT	02/2011	830.00 -	05/2013 -	05/2013
286	ACQUISITION OF ONE (1) NOS. OF 3500 TEU CELLULAR CONTAINER - [N25000061]SHIPP.,MULTI STATE	07/2011	220.49 -	01/2013 06/2013	06/2013
287	ACQUISITION OF 4 NOS OF 82000 DWT KAMSAVMAX BULK CARRIERS FROM M/S JIANGSU EASTERN HEAVY INDUSTRIES - [N25000051]SHIPP.,MAHARASHTRA	08/2010	612.72 532.83	12/2012 11/2013	11/2013
288	ACQUISITION OF THREE(3) NOS OF 6500TEU CELLULAR CONTAINER VESSELS FROM M/S STX SHIPBUILDING CO. LTD. - [N25000052]SHIPP.,MAHARASHTRA	10/2010	1,028.10 1,012.23	12/2013 11/2013	11/2013
289	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]PORT TRUST,TAMIL NADU	10/2002	150.00 309.00	03/2006 06/2014	06/2014
290	SETHUSAMUDRAM SHIP CHANNEL PROJECT - [250100175]PORT TRUST,TAMIL NADU	06/2005	2,427.40 -	10/2008 11/2010	-
291	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL - [N25000003]PORT TRUST,MAHARASHTRA	10/2005	800.00 1,571.60	10/2008 -	-
	Total		9,410.79 -		
	<u>TELECOMMUNICATIONS</u>				
292	SUPPLY INSTALLATION TESTING AND COMMISSIONING OF RURAL WIMAX NETWORK PHASE-II - [N26000100]BSNL,MULTI STATE	07/2010	1,148.19 -	05/2011 -	06/2014
	Total		1,148.19 -		
	<u>URBAN DEVELOPMENT</u>				
293	BANGALORE METRO RAIL PROJECT - [N28000008]MRTP,KARNATAKA	05/2006	6,395.00 -	06/2011 -	03/2013
294	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048]CPWD,MAHARASHTRA	11/2006	114.18 173.08	04/2009 -	-
	Total		6,509.18 -		
	<u>WATER RESOURCES</u>				
295	PAGLADIYA DAM PROJECT - [300100001]MOWR,ASSAM	01/2001	542.90 -	12/2007 -	12/2012
	Total		542.90 -		
	Grand Total		167,080.32		

Details of On Schedule Projects w.r.t. Original Schedule

(August 2014)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
1	SUPPLY OF 56 NOS AIRFIELD FIRE TENDERS AT VARIOUS AIRPORTS - [N04000071]	10/2012	217.60 -	217.60	0.04	03/2015 -	03/2015
	Total		217.60 -	217.60	.04		
	<u>COAL</u>						
2	BLOCK-B OCP NCL (3.5 MTY) - [N06000009]	6/2011	746.04 -	535.10	264.36	03/2015 -	03/2015
3	AMLOHRI EPR (NCL) (6 MTY , INCR.) - [N06000010]	12/2009	1,352.04 -	1,143.54	664.21	03/2016 03/2016	03/2016
4	PELMA OCP(10.00MTY) - [N06000045]	7/2008	448.32 -	448.32	0.46	03/2015 -	03/2015
5	RKP OCP PHASE-I - [N06000079]	3/2010	209.78 -	209.78	67.29	03/2015 -	03/2015
6	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]	12/2009	510.85 -	510.85	223.19	03/2016 -	03/2016
7	KHADIA EXPANSION OPENCAST PROJECT(4 TO 10 MTPA,6MTPA INCREMENTAL) - [N06000091]	6/2011	1,131.28 -	1,131.28	30.30	03/2018 -	03/2018
8	BAROUD OC EXPANSION (RCE)- 3MTY - [N06000099]	4/2012	258.56 -	258.56	60.25	03/2016 -	03/2016
9	KALYANIKHANI OPENCAST PROJECT - [N06000101]	7/2012	417.33 -	417.33	2.16	07/2016 -	07/2016
10	WIND POWER PROJECT,KAZHUNEERKULAM,TAMILNADU - [N06000110]	4/2012	364.75 -	364.75	78.53	10/2014 -	10/2014
11	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]	8/2012	1,055.05 -	1,055.05	31.24	03/2018 -	03/2018
12	KAPURIA UG(PSLW) - [N06000108]	8/2011	988.35 -	988.35	6.84	04/2017 -	04/2017
13	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]	2/2014	555.52 -	555.52	6.84	03/2021 -	03/2021
14	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.33 -	610.33	-	03/2022 -	03/2022
15	AMRAPALI OC(12MTY) - [N06000103]	2/2012	858.11 -	858.11	95.94	03/2020 -	03/2020
16	RG OC -III EXTENSION (PHASE -II) PROJECT - [N06000100]	6/2012	365.01 -	365.01	6.56	06/2015 -	06/2015
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	162.76	2.48	03/2015 -	03/2015
18	KISTARAM OCP - [N06000089]	11/2010	242.29 -	242.29	-	03/2015 -	03/2015
19	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	94.83	03/2016 -	03/2016
20	BATURA OCP (2.0 MTY) - [N06000049]	9/2008	203.82 -	203.82	-	03/2015 -	03/2015

(August 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
21	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	182.71	03/2017 -	03/2017
	Total		11,120.78 -	10,749.44	1,818.19		
	<u>PETROLEUM</u>						
22	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131]	12/2011	2,059.63 -	2,665.65	597.89	03/2015 -	03/2015
23	REWARI KANPUR PIPELINE PROJECT - [N16000145]	2/2012	1,210.64 -	1,210.64	660.01	11/2015 -	11/2015
24	AUGMENTATION OF PARADIP HALDIA BARAUNI PIPELINE - [N16000149]	8/2011	586.00 -	586.00	198.47	08/2015 -	08/2015
25	PIPELINE REPLACEMENT PROJECT, AHMEDABAD - [N16000159]	9/2011	202.25 -	160.16	34.66	07/2016 -	07/2016
26	MH NORTH REDEVELOPMENT PHASE III - [N16000188]	6/2014	5,706.47 -	5,706.47	-	05/2017 -	05/2017
27	RESID UPGRADE PROJECT - [N16000184]	2/2011	3,110.36 -	3,110.36	219.08	11/2015 -	11/2015
28	ADDITIONAL DEVELOPMENT OF VASAI EAST FIELD - [N16000183]	3/2014	2,476.82 -	2,476.82	-	12/2018 -	12/2018
29	DEVELOPMENT PLAN FOR LOWER PAYS IN NBP-14 BLOCK OF NBP FIELD (D-1) - [N16000182]	10/2013	429.06 -	429.06	-	10/2014 -	10/2014
30	REVAMP OF UNMANNED PLATFORMS PH-II IN MH AND NH ASSETS - [N16000181]	3/2013	2,913.10 -	2,910.30	9.50	05/2016 -	05/2016
31	INSTALLATION OF DEMONSTRATION UNIT OF INDA DEPT AT GUWAHATI REFINERY - [N16000180]	2/2014	163.88 -	163.88	3.34	07/2016 -	07/2016
32	POLYPROPYLENE PLANT AT PARADIP REFINERY - [N16000179]	3/2014	3,150.00 -	3,150.00	92.49	09/2017 -	09/2017
33	REPLACEMENT OF COKE CHAMBERS IN COKER A AT BARAUNI REFINERY - [N16000177]	4/2013	480.00 -	480.00	-	02/2016 -	02/2016
34	DISTILLATE YIELD IMPROVEMENT PROJECT (COKER) AT HALDIA REFINERY - [N16000175]	3/2014	3,076.00 -	3,076.00	42.24	09/2017 -	09/2017
35	LPG MARKETING TERMINAL, PARADIP - [N16000174]	7/2009	158.91 -	158.91	107.81	03/2015 -	03/2015
36	DEVELOPMENT OF SHALLOW WATER WELLS IN EASTERN OFFSHORE - [N16000173]	4/2013	284.82 -	284.82	-	04/2015 -	04/2015
37	INTEGRATED DEVELOPMENT OF VASHISTA AND S-1 FIELDS - [N16000172]	5/2013	4,124.35 -	4,124.35	-	04/2016 -	04/2016
38	LPG TERMINAL AT KOCHI - [N16000171]	12/2012	607.06 -	607.06	46.12	01/2016 -	01/2016
39	KOTA JOBNER PIPELINE PROJECT - [N16000170]	4/2011	276.26 -	276.27	165.75	03/2015 -	03/2015
40	RECONSTRUCTION OF BPA AND BPB PLATFORMS - [N16000161]	3/2013	1,138.50 -	686.58	110.40	04/2015 -	04/2015
41	INTEGRATED DEVELOPMENT OF BASSEIN FIELD - [N16000160]	12/2012	3,513.07 -	3,513.07	0.27	02/2016 -	02/2016
42	MOUNDED BULLET PROJECT AT CPCL - [N16000154]	12/2012	279.00 -	279.00	89.30	12/2014 -	12/2014
43	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146]	11/2012	666.00 -	701.00	277.96	11/2015 -	11/2015

(August 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
44	DEVELOPMENT OF WESTERN PERIPHERY OF MH SOUTH FIELD - [N16000136]	4/2012	600.17 -	600.17	248.73	12/2014 -	12/2014
45	HEERA AND SOUTH HEERA REDEVELOPMENT PH-II - [N16000132]	3/2012	5,608.40 -	5,608.40	2,805.04	05/2015 -	05/2015
	Total		42,820.75 -	42,964.97	5,709.06		
	POWER						
46	SYSTEM STRENGTHENING IN WARDHA-AURANGABAD CORRIDOR FOR IPP PROJECTS IN CHATTISGARH - [N18000120]	2/2012	1,310.85 -	1,310.85	841.33	02/2015 -	02/2015
47	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXIV - [N18000128]	11/2011	723.63 -	723.63	394.08	11/2014 -	11/2014
48	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVI - [N18000136]	9/2012	803.34 -	803.34	358.09	03/2015 -	03/2015
49	COMMON TRANSMISSION SCHEME WITH ISSG PROJECTS IN NAGAPATTINAM/CUDDALOR OF TAMIL NADU - PART A1 - [N18000139]	1/2013	182.80 -	182.80	65.23	10/2014 -	10/2014
50	SUB-STATION EXT. WORKS ASSOCIATED WITH TRANS. SYSTEM REQUIRED FOR EVACUATION OF POWER FROM KUDGI TPS - [N18000161]	2/2014	167.40 -	167.40	-	12/2015 -	12/2015
51	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXXII - [N18000159]	2/2014	908.08 -	908.08	-	06/2016 -	06/2016
52	NORTHERN REGION SYSTEM STRENGTHENING SCHEME - XXX - [N18000158]	2/2014	539.82 -	539.82	-	06/2016 -	06/2016
53	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]	1/2014	374.63 -	374.63	-	04/2016 -	04/2016
54	TRANSMISSION SYSTEM ASSOCIATED WITH MAUDA STAGE-II - [N18000153]	9/2013	1,575.30 -	1,575.30	94.20	05/2016 -	05/2016
55	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXV - [N18000152]	9/2013	680.69 -	680.69	49.29	03/2016 -	03/2016
56	COMMON SYSTEM ASSOCIATED WITH EAST COAST ENERGY PVT. LTD. & NCC POWER PROJECTS LTD. LTOA GENERATION - [N18000145]	6/2012	1,909.24 -	1,909.24	598.23	06/2015 -	06/2015
57	COMMON SYS. ASSOCIATED WITH EAST COAST ENERGY PVT LTD AND NCC POWER PROJECTS LTD LTOA GEN PART- B - [N18000144]	3/2013	2,514.88 -	2,514.88	180.75	12/2015 -	12/2015
58	COMMON TR. SYS. ASSOCIATED WITH EAST COAST AND NCC POWER PROJECTS IN SRIKAKULAM AREA A.P. PART- C - [N18000143]	3/2013	514.20 -	514.20	-	06/2015 -	06/2015
59	EASTERN REGION STRENGTHENING SCHEME -IX - [N18000171]	2/2014	196.58 -	196.58	-	02/2016 -	02/2016
60	TRANS. SYSTEM FOR CONNECTIVITY FOR NCC POWER PROJECTS LTD. - [N18000170]	8/2014	188.75 -	188.75	-	02/2017 -	02/2017
61	SYSTEM STRENGTHENING - XX IN SOUTHERN REGIONAL GRID - [N18000169]	8/2014	288.49 -	288.49	-	02/2017 -	02/2017
62	TRANS.SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]	6/2014	5,151.37 -	5,151.37	-	04/2018 -	04/2018
63	TRANSMISSION SYSTEM ASSOCIATED WITH KAKRAPAR ATOMIC POWER PROJECT - 3&4 - [N18000166]	2/2014	378.71 -	378.71	11.10	10/2016 -	10/2016

(August 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
64	AUGMENTATION OF TRANSFORMERS IN NORTHERN REGION - PART B - [N18000165]	3/2014	155.57 -	155.57	-	03/2016 -	03/2016
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	522.29	-	11/2016 -	11/2016
66	INSTALLATION OF BUS RECTOR AND ICT IN WESTERN REGION - [N18000163]	5/2014	303.07 -	303.07	-	07/2016 -	07/2016
67	STATIC VAR COMPENSATORS (SVCS) IN NORTHERN REGION - [N18000162]	5/2014	829.98 -	829.98	-	09/2016 -	09/2016
68	AUGMENTION OF TRANSFORMERS IN NORTHERN REGION - PART A - [N18000138]	12/2012	156.04 -	156.04	77.46	10/2014 -	10/2014
69	VINDHYACHAL STPP STAGE-V - [N18000134]	12/2011	3,180.40 -	3,180.40	1,190.00	08/2015 -	08/2015
70	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NORTHERN REGION - [N18000123]	3/2012	198.63 -	198.63	-	09/2014 -	09/2014
71	TRANSMISSION SYSTEM ASSOCIATED WITH KRISHNAPATNAM UMPP-PART B - [N18000122]	2/2012	1,927.16 -	1,927.16	1,291.77	10/2014 -	10/2014
	Total		25,681.90 -	25,681.90	5,151.53		
	<u>RAILWAYS</u>						
72	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	4/1998	183.23 -	818.29	128.11	02/2015 -	02/2015
73	HIMMATNAGAR - UDAIPUR GAUGE CANVESSION (NWR) - [N22000112]	4/2008	829.74 -	829.74	72.09	03/2015 -	03/2015
74	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	1,176.09 -	3,845.60	1.92	02/2020 -	02/2020
75	PLASSEY-JIAGANJ DOUBLING - [N22000220]	4/2011	248.07 -	248.07	23.13	03/2015 -	03/2015
76	DELANG-PURI DOUBLING - [N22000320]	3/2011	165.16 -	165.16	102.77	03/2015 -	03/2015
77	KATWA-PATULI DOUBLING WITH NEW MM FOR AHMEDPUR-KATWA GC - [N22000245]	4/2010	423.66 -	423.66	206.48	03/2017 -	03/2017
78	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	4/2011	299.60 -	299.60	1.10	03/2017 -	03/2017
79	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	4/2010	622.41 -	2,030.50	2.43	02/2019 -	02/2019
80	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	3/2013	4,874.58 -	4,874.58	400.00	03/2016 -	03/2016
81	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	4/2010	2,913.51 -	2,913.51	470.69	03/2016 -	03/2016
82	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	3,375.42	85.19	12/2015 -	12/2015
83	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	4/2010	3,951.98 -	4,259.48	486.12	03/2016 -	03/2016
	Total		17,027.51 -	24,083.61	1,980.03		

(August 2014)

						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
84	PANIPAT-ROHTAK - [N24000151]	4/2011	807.00 -	807.00	1,209.43	10/2014 -	10/2014
85	4 LANING OF NAGPUR-BETUL - [N24000155]	2/2011	2,498.76 -	2,498.76	-	08/2014 -	08/2014
86	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]	4/2012	1,396.18 -	1,396.18	1,760.00	09/2014 -	09/2014
87	RANCHI-RARGA-JAMSETHPUR - [N24000215]	12/2012	1,479.00 -	1,479.00	344.90	06/2015 -	06/2015
88	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	849.00	09/2015 -	09/2015
89	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	129.90	12/2015 -	12/2015
90	2-LANING WITH PAVED SHOLDERS OF MULTAI CHHINDWARA SEONI SEC - [N24000226]	10/2011	1,565.00 -	1,565.00	1,502.00	10/2014 -	10/2014
91	WALAJAPET POONAMALEE KM 106.8 TO KM 13.8 - [N24000228]	6/2013	1,287.95 -	1,287.95	540.10	11/2015 -	11/2015
92	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,266.60	-	09/2016 -	09/2016
93	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]	11/2013	1,916.79 -	1,916.79	272.80	11/2016 -	11/2016
94	4-LANING OF ROHATAK JIND(LENGTH 45 KM) - [N24000231]	10/2013	283.25 -	283.25	210.10	10/2015 -	10/2015
95	REENGUS SIKAR - [N24000227]	3/2012	333.51 -	333.51	269.30	09/2014 -	09/2014
96	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]	10/2012	1,928.22 -	1,928.22	571.30	04/2015 -	04/2015
97	2 LANING WITH PS AGRA ALIGARH - [N24000220]	10/2012	250.50 -	250.50	361.30	10/2014 -	10/2014
98	FOUR LANING OF ORISSA CHATTISHGARH BORDER - [N24000218]	2/2013	1,232.00 -	1,232.00	542.90	08/2015 -	08/2015
99	NAGPUR-WAINGANGA BRIDGE - [N24000210]	4/2012	484.19 -	484.19	285.20	10/2014 -	10/2014
	Total		20,427.19 -	20,427.19	8,848.23		
	<u>STEEL</u>						
100	REBUILDING OF BATTERY BLOCK 5A AND RE-CONSTRUCTION OF BATTERY BLOCK 5B - [N12000080]	11/2012	313.05 -	313.05	115.87	06/2015 -	06/2015
101	REBUILDING OF COB-7 AT BSL - [N12000083]	10/2013	245.67 -	245.67	18.01	05/2016 -	05/2016
102	UPGRADATION OF BLAST FURNACE-1 AT RSP - [N12000084]	6/2014	708.91 -	708.91	1.78	04/2016 -	04/2016
103	DEVELOPMENT OF PERMANENT BARRACKS AT 21 LOCATIONS AT ROWGHAT DEPOSIT [N12000085]	4/2014	188.93 -	188.93	-	04/2015 -	04/2015
	Total		1,456.56 -	1,456.56	135.66		
	<u>URBAN DEVELOPMENT</u>						

(August 2014)							
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
104	DELHI MRTS PHASE-III - [N28000056]	9/2011	38,585.00 -	38,585.00	8,699.49	03/2016 -	03/2016
105	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	2/2014	26,405.14 -	26,405.14	-	02/2019 -	02/2019
	Total		64,990.14 -	64,990.14	8,699.49		
	Grand Total		183,742.43	190,571.41	32,342.23		

Details of Delayed Projects w.r.t. Original and Revised Schedule

All Cost/ Expenditure in Rs. Crore						(August 2014)			
						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
1	KUDANKULAM APP (NPCIL) - [020100040]NPCIL,TAMIL NADU	12/2001	13,171.00 17,270.00	17,270.00	17,846.00	12/2008 10/2013	11/2014	71	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI,TAMIL NADU	09/2003	3,492.00 5,677.00	5,677.00	4,564.17	09/2010 03/2015	03/2015	54	62.57
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00 -	11,459.00	5,277.00	12/2015 11/2016	10/2017	22	0
4	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00 -	12,320.00	3,207.00	12/2016 03/2017	05/2018	17	0
	Total		40,442.00 -	46,726.00	30,894.17				
	<u>CIVIL AVIATION</u>								
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]AAI,GOA	05/2010	335.61 335.61	388.53	283.54	05/2012 -	09/2014	28	15.77
6	ESTABLISHMENT OF AIRPORT OPERATIONS CONTROL CENTRES AT 10 AIRPORTS - [N04000072]AAI,MULTI STATE	02/2010	344.28 -	344.28	19.61	03/2014 -	01/2015	10	0
7	C/O NEW AIRPORT AT PAKYONG(SIKKIM) AIRPORT - [N04000050]AAI,SIKKIM	01/2009	309.46 -	309.46	277.91	01/2011 04/2013	12/2016	71	0
	Total		989.35 -	1,042.27	581.06				
	<u>COAL</u>								
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]NLC,TAMIL NADU	10/2004	2,030.78 3,027.59	3,027.59	3,017.28	06/2009 03/2013	10/2014	64	49.09
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]NLC,TAMIL NADU	05/2008	4,904.54 6,602.74	6,602.74	5,505.34	03/2012 05/2014	10/2014	31	34.63
10	ADRIYALA SHAFT PROJECT - [N06000016]SCCL,TELANGANA	12/2009	212.34 1,228.39	1,228.39	1,248.89	03/2013 09/2012	03/2015	24	478.5
11	NIGAH OC EXPANSION PROJECT 10 MTY TO 15 MTY, SINGRAULI - [N06000033]NCL,MADHYA PRADESH	10/2007	259.40 -	259.40	6.99	03/2012 -	03/2015	36	0
12	MANUGURU OC-II EXTENSION PHASE-II - [N06000080]SCCL,TELANGANA	03/2010	181.19 -	181.19	36.13	03/2012 -	03/2015	36	0
13	PURNADIH OCP (3.0 MTY) - [N06000085]CCL,JHARKHAND	07/2008	210.98 -	210.98	144.07	03/2013 -	03/2015	24	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
14	GEVRA EXPANSION OCP (SECL) (25-35) MTY - [060100093]SECL,CHHATISGARH	06/2010	2,675.67 -	2,675.67	1,576.83	03/2014 -	03/2016	24	0
15	DIPKA EXPANSION OCP (SECL) (20-25) MTY - [060100094]SECL,CHHATISGARH	12/2009	1,943.66 -	1,943.66	1,556.91	03/2014 -	03/2016	24	0
16	MAGADH OC 20 MTY (CCL) - [N06000015]CCL,JHARKHAND	08/2008	469.78 -	706.40	44.65	07/2012 -	03/2016	44	50.37
17	CHURCHA ROUG(1.35MTY) - [N06000046]SECL,CHHATISGARH	06/2008	462.35 -	462.35	272.77	03/2014 -	03/2016	24	0
18	KAKATIYA LONGWALL - [N06000048]SCCL,TELANGANA	12/2008	453.63 -	453.63	104.81	12/2012 -	03/2016	39	0
19	RAJMAHAL OC EXP. - [N06000056]ECL,JHARKHAND	09/2009	153.82 -	153.82	41.46	03/2014 -	03/2016	24	0
20	PENGANGA OC - [N06000066]WCL,MAHARASHTRA	10/2008	339.77 -	339.77	1.63	03/2014 -	03/2016	24	0
21	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	-	03/2014 -	03/2016	24	0
22	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	418.97	226.56	03/2012 -	03/2016	48	0
23	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.42 -	321.50	211.55	03/2014 -	03/2016	24	.02
24	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	35.52	03/2011 -	03/2016	60	0
25	TAPIN OCP (2.5 MTY) - [N06000086]CCL,JHARKHAND	08/2008	264.68 -	264.68	142.19	03/2012 -	03/2016	48	0
26	KULDA OCP (MAHANADI COALFIELDS LTD) - [060100092]MCL,ODISHA	01/2005	302.96 -	302.96	129.48	03/2010 -	03/2017	84	0
27	ASHOK EXPN.OCP -CCL (10 MTY) - [060100096]CCL,JHARKHAND	12/2007	471.66 341.63	341.63	100.76	03/2011 -	03/2017	72	-27.57
28	JHANJRA R-VI SEAM PSLW - [N06000020]ECL,WEST BENGAL	11/2006	287.18 -	287.17	44.70	03/2011 -	03/2017	72	0
29	KANIHA OCP, MCL, (10.0 MTY) - [N06000035]MCL,ODISHA	12/2007	457.77 -	457.77	120.62	03/2013 -	03/2017	48	0
30	BALRAM OCP EXTENSION,MCL 8.00 MTY - [N06000044]MCL,ODISHA	12/2007	172.08 -	172.08	142.24	03/2010 -	03/2017	84	0
31	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	207.28	167.94	03/2012 -	03/2017	60	0
32	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.63 -	479.63	118.50	03/2013 -	03/2017	48	0
33	JAGANNATHPOR OC - [N06000075]SECL,CHHATISGARH	09/2008	152.43 -	152.43	21.55	03/2015 -	03/2017	24	0
34	NORTH URIMARI OCP (3.0 MTY) - [N06000084]CCL,JHARKHAND	12/2007	179.87 -	179.87	60.93	03/2012 -	03/2017	60	0
35	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	53.04	03/2014 -	03/2017	36	0
36	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	447.06	29.03	03/2015 -	03/2018	36	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
37	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 -	5,907.11	343.27	12/2015 -	04/2018	28	0
38	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	-	04/2015 -	04/2019	48	0
39	TALABIRA OCP - [N06000043]MCL,ODISHA	03/2008	447.72 -	447.72	52.34	03/2016 -	03/2020	48	0
40	GOPAL PRASAD OCP (15MTY) - [N06000042]MCL,ODISHA	02/2008	395.87 -	395.87	76.74	03/2015 -	03/2021	72	0
41	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]SECL,CHHATISGARH	06/2008	1,188.31 7,612.33	7,612.33	755.11	03/2013 03/2023	03/2023	120	540.6
	Total		28,134.59 -	38,376.33	16,389.83				
	<u>STEEL</u>								
42	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]RINL,ANDHRA PRADESH	06/2006	108.00 216.68	216.68	162.45	09/2008 12/2013	10/2014	73	100.63
43	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]RINL,ANDHRA PRADESH	10/2005	8,692.00 12,291.00	12,291.00	10,934.43	10/2009 10/2012	12/2014	62	41.41
44	EXPANSION OF IISCO STEEL PLANT - [N12000051]SAIL, WEST BENGAL	06/2008	14,443.00 -	16,408.00	16,226.60	12/2011 -	12/2014	36	13.61
45	EXPANSION OF BOKARO STEEL PLANT - [N12000055]SAIL,JHARKHAND	05/2010	6,325.00 -	6,325.00	4,831.60	12/2011 -	12/2014	36	0
46	COLD REPAIR OF COKE OVEN BATTERY-9 AT BSP, BHILAI, CHHATISGARH - [N12000078]SAIL,CHHATISGARH	07/2012	332.65 -	332.65	120.75	08/2014 -	01/2015	5	0
47	INSTALLATION OF ADDITIONAL HEAT TREATMENT FACILITIES IN SPP AT RSP - [N12000082]SAIL,ODISHA	10/2012	160.48 -	160.48	78.35	09/2014 -	01/2015	4	0
48	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]NMDC,CHHATISGARH	01/2007	295.89 607.17	607.17	376.00	12/2011 01/2015	03/2015	39	105.2
49	AUGMENTATION OF IRON ORE STORAGE IN RMHP - [N12000053]RINL,MULTI STATE	07/2007	480.00 -	450.00	313.71	09/2009 05/2012	03/2015	66	-6.25
50	EXPANSION OF ROURKELA STEEL PLANT - [N12000056]SAIL,ODISHA	08/2010	11,812.00 -	11,812.00	11,397.96	03/2013 -	03/2015	24	0
51	1.2 MTPA PELLET PLANT PROJECT ,DONIMALAI (NMDC) - [N12000072]NMDC,KARNATAKA	04/2011	572.00 -	572.00	402.05	04/2013 09/2014	03/2015	23	0
52	7.0 MTPA KUMARASWAMY IRON ORE MINE PROJECT (NMDC) - [N12000073]NMDC,KARNATAKA	02/2011	898.55 -	898.55	333.54	05/2013 01/2015	03/2015	22	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
53	EXPANSION OF DURGAPUR STEEL PLANT - [N12000074]SAIL,WEST BENGAL	08/2010	2,875.00 -	2,875.00	2,298.40	12/2012 -	03/2015	27	0
54	REBUILDING OF COKE OVEN BATTERY-3 AT RSP, ROURKELA, ODDISHA - [N12000079]SAIL,ODISHA	06/2012	237.09 -	237.09	74.37	12/2014 -	03/2015	3	0
55	ENHANCEMENT OF PRODUCTION CAPACITY AT BOLANI IRON ORE MINES - [N12000075]SAIL,ODISHA	11/2011	254.55 -	254.55	113.57	11/2013 -	06/2015	19	0
56	INSTALLATION OF 45MVA SAF T WITH OTHER ASSOCIATED FACILITIES - [N12000076]SAIL,MAHARASHTRA	12/2011	187.33 -	187.33	136.18	10/2013 -	08/2015	22	0
57	EXPANSION OF BHILAI STEEL PLANT - [N12000057]SAIL,CHHATISGARH	08/2010	17,265.00 -	17,265.00	13,243.14	03/2013 -	09/2015	30	0
	Total		64,938.54 -	70,892.50	61,043.10				
	PETROLEUM								
58	GAS TURBINE GENERATION SET - [N18000146]OIL,ASSAM	07/2009	216.88 -	216.88	179.67	10/2011 06/2014	08/2014	34	0
59	MRPL PHASE-III EXPANSION - [N16000114]MANGALORE REFIN,KARNATAKA	08/2008	12,412.00 12,160.26	12,160.26	12,077.74	01/2012 -	09/2014	32	-2.03
60	WAX PROJECT - [N16000101]NRL,ASSAM	06/2010	576.60 676.05	676.05	549.46	12/2013 05/2014	10/2014	10	17.25
61	PETROCHEMICAL COMPLEX-II AT VIJAYPUR AND PATA - [N16000112]GAIL,MULTI STATE	08/2010	8,140.00 -	8,140.00	6,890.00	02/2014 -	10/2014	8	0
62	POLYPROPYLENE UNIT - [N16000113]MANGALORE REFIN,KARNATAKA	05/2009	1,803.78 -	1,803.78	1,004.06	07/2012 -	10/2014	27	0
63	102 MW WIND POWER PROJECT - [N16000119]ONGC,RAJASTHAN	07/2010	1,106.00 -	678.02	405.00	06/2012 -	10/2014	28	-38.7
64	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]BPCL,MAHARASHTRA	08/2009	246.81 -	276.83	260.70	04/2012 -	10/2014	30	12.16
65	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]ONGC,MULTI STATE	03/2010	3,241.03 6,638.94	6,638.94	2,192.69	03/2013 11/2014	11/2014	20	104.84
66	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]SPRL,ANDHRA PRADESH	01/2006	672.00 1,038.00	1,038.00	984.98	10/2011 -	12/2014	38	54.46
67	MARKETING TERMINAL AT PARADEEP - [N16000168]IOCL,ODISHA	07/2009	199.75 -	199.75	144.04	06/2014 -	12/2014	6	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
68	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]OIL, ASSAM	08/2008	144.02 -	204.29	154.72	06/2012 09/2013	12/2014	30	41.85
69	PARADIP REFINERY PROJECT - [N16000058]IOCL, ODISHA	02/2009	29,777.00 -	34,555.00	26,669.53	11/2012 11/2013	02/2015	27	16.05
70	DABHOL BANGALORE PIPELINE PROJECT PHASE-II - [N16000147]GAIL, MULTI STATE	06/2009	486.00 -	486.00	105.71	09/2013 -	02/2015	17	0
71	UP-GRADATION OF KONABAN GGS AND PIPELINE GRID PROJECT, TRIPURA - [N16000098]ONGC, TRIPURA	07/2008	288.04 288.04	253.66	216.68	08/2012 -	03/2015	31	-11.94
72	CONSTRUCTION OF 6 ETPS - [N16000117]ONGC, GUJARAT	03/2009	302.26 -	240.95	105.93	09/2012 -	03/2015	30	-20.28
73	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC, MAHARASHTRA	03/2011	861.79 -	761.68	609.20	05/2013 06/2014	03/2015	22	-11.62
74	REPLACEMENT OF CDU/VDU AT MUMBAI REFINERY - [N16000142]BPCL, MAHARASHTRA	01/1999	1,419.00 -	1,419.00	726.22	12/2014 -	03/2015	3	0
75	IOR OF B-173A FIELD - [N16000140]ONGC, MULTI STATE	01/2012	352.49 -	352.49	97.37	03/2014 -	04/2015	13	0
76	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]ONGC, MAHARASHTRA	06/2007	3,248.78 5,633.44	6,000.00	5,867.35	08/2010 03/2012	05/2015	57	84.68
77	CONSTRUCTION OF 23 IMMEDIATE SUPPLY VESSELS (ISV) - [N16000123]ONGC, MULTI STATE	11/2010	331.20 -	269.10	190.04	08/2013 -	05/2015	21	-18.75
78	DEVELOPMENT OF C-26 CLUSTER FIELDS - [N16000133]ONGC, MAHARASHTRA	03/2012	2,592.17 -	2,592.17	304.81	05/2014 -	05/2015	12	0
79	PIPELINE REPLACEMENT PROJECT-3 - [N16000137]ONGC, MULTI STATE	04/2012	2,547.26 -	1,417.00	1,304.46	05/2014 -	05/2015	12	-44.37
80	DEV OF G1 AND GS-15 (ONGCL) - [160100231]ONGC, MULTI STATE	04/2003	429.82 3,955.21	3,955.21	3,413.13	04/2006 06/2012	06/2015	110	820.2
81	KOCHI-KOOTANAD BANGALORE MANGALORE PIPELINE PROJECT - [N16000129]GAIL, MULTI STATE	06/2009	2,915.00 -	2,300.00	1,408.97	12/2012 06/2015	06/2015	30	-21.1
82	VKPL UPGRADATION AND LAYING OF SPURLINE (TO BHILWARA AND CHITTORGARH) - [N16000093]GAIL, MULTI STATE	12/2009	463.32 -	330.47	270.84	03/2012 -	07/2015	40	-28.67
83	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]HPCL, MULTI STATE	11/2012	309.81 462.79	462.79	85.74	10/2014 -	10/2015	12	49.38
84	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]SPRL, KARNATAKA	01/2006	732.00 1,227.00	1,227.00	882.71	10/2011 -	10/2015	48	67.62
85	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]SPRL, KERALA	01/2006	993.00 1,693.00	1,693.00	1,275.74	01/2012 -	10/2015	45	70.49

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
86	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]OIL, ASSAM	09/2012	871.35 -	1,200.00	50.75	03/2015 11/2015	11/2015	8	37.72
87	JAGDISHPUR-HALDIA PIPELINE PROJECT PHASE-I - [N16000072]GAIL, MULTI STATE	07/2009	7,596.18 -	7,596.18	13.50	01/2013 -	12/2015	35	0
88	CONSTRUCTION OF 12 OFFSHORE SUPPLY VESSELS(OSV) - [N16000084]ONGC, MULTI STATE	06/2007	736.65 -	736.65	452.59	09/2011 12/2013	12/2015	51	0
89	PARADIP-RAIPUR- RANCHI PIPELINE - [N16000088]OCL, MULTI STATE	08/2009	1,793.00 -	1,793.00	1,013.11	09/2012 -	12/2015	39	0
90	DEVELOPMENT OF WO-16 CLUSTER FIELDS - [N16000105]ONGC, MULTI STATE	06/2010	2,523.00 -	2,523.00	1,013.04	01/2014 -	12/2015	23	0
91	PARADIP HALDIA DURGAPUR LPG PIPELINE - [N16000148]OCL, MULTI STATE	02/2011	913.00 -	913.00	312.22	07/2015 -	12/2015	5	0
92	RESITEMENT OF TATA NAGAR AND RACHI DEPOTS TO KHUNTI (JHARKHAND) - [N16000187]OCL, JHARKHAND	04/2011	191.96 -	191.96	46.35	05/2015 -	12/2015	7	0
93	PURCHASE OF 2 NOS. OF 2000 HP DRILLING RIG - [N16000165]OIL, MULTI STATE	04/2010	270.00 -	270.00	-	12/2014 -	02/2016	14	0
94	ASSAM RENEWAL PROJECT FOR GROUP A - [N16000061]ONGC, ASSAM	03/2009	2,465.15 -	2,378.86	1,711.73	03/2013 03/2015	03/2016	36	-3.5
95	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]BPCL, KERALA	01/1999	14,225.00 16,504.00	16,504.00	3,203.62	12/2015 -	05/2016	5	16.02
96	CONSTRUCTION OF ONE MULTIPURPOSE SUPPORT VESSEL (MSV) - [N16000103]ONGC, MULTI STATE	01/2010	723.64 -	723.64	-	03/2013 -	06/2016	39	0
97	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]OIL, MULTI STATE	08/2006	94.00 352.56	352.56	10.60	09/2012 03/2017	03/2017	54	275.06
98	AHMEDABAD REDEVELOPMENT PROJECT - [N16000120]ONGC, GUJARAT	11/2010	1,916.10 -	1,916.10	1,160.14	12/2014 -	12/2017	36	0
99	MEHESANA REDEVELOPMENT PROJECT - [N16000121]ONGC, GUJARAT	11/2010	3,823.00 -	3,823.00	1,076.57	04/2015 -	12/2017	32	0
100	ANKLESWAR REDEVELOPMENT - [N16000122]ONGC, GUJARAT	11/2010	2,189.63 -	2,189.63	1,039.42	12/2014 -	12/2018	48	0
	Total		117,139.47 -	133,459.90	79,481.13				

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
	<u>POWER</u>								
101	RAMPUR HEP(412 MW) - [N18000024]SJVNL,HIMACHAL PRADESH	01/2007	2,047.03 -	3,288.28	3,261.56	03/2012 -	09/2014	30	60.64
102	765 KV POOLING STATION AND NETWORK WITH DVC AND MAITHOB RBC - [N18000069]PGCIL,MULTI STATE	08/2008	7,075.33 -	7,075.33	6,380.46	08/2012 -	09/2014	25	0
103	COMMON SYSTEM ASSOCIATED WITH ISGS PROJECTS IN KRISHNAPATNAM OF ANDHRA PRADESH(PGCIL) - [N18000111]PGCIL,MULTI STATE	08/2011	1,637.34 -	1,637.34	1,449.25	08/2014 -	09/2014	1	0
104	TRANSMISSION SYS ASSOCIATED WITH KRISHNAPATNAM UMPP- PART C1 - [N18000121]PGCIL,MULTI STATE	02/2012	324.33 -	324.33	194.46	08/2014 -	09/2014	1	0
105	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]PGCIL,MULTI STATE	08/2008	2,360.95 2,580.90	2,580.90	2,136.01	08/2012 -	10/2014	26	9.32
106	INTEGRATION OF POOLING STATION IN CHATTISGARH WITH CENTRAL PART OF WR FOR IPP GENERATION PROJECTS IN - [N18000107]PGCIL,CHHATISGARH	08/2011	1,391.97 -	1,391.97	1,432.05	12/2013 -	10/2014	10	0
107	SYTEM STRENGTHENING OF SOUTHERN REGION - XIV - [N18000115]PGCIL,MULTI STATE	12/2011	297.33 -	297.33	243.87	08/2014 -	10/2014	2	0
108	TR SYSTEM FOR ESTABLISHMENT OF 400/220 KV GIS SUBSTATION AT MAGARWADA IN UT DD - [N18000118]PGCIL,GUJARAT	01/2012	259.28 -	259.28	169.32	01/2014 -	10/2014	9	0
109	SYSTEM STRENGTHENING COMMON FOR WR AND NR (LINE BAYS AND REACTOR PROVISION) - [N18000124]PGCIL,MADHYA PRADESH	03/2012	213.78 -	213.78	149.54	03/2014 -	10/2014	7	0
110	TRIPURA GAS BASED POWER PROJECT - [N18000071]NEEPCO,TRIPURA	07/2009	421.01 623.44	994.85	811.41	07/2013 08/2014	11/2014	16	136.3
111	TRANSMISSION SYSTEM FOR PHASE-I GEN PROJECT IN ORISSA - PART-A - [N18000087]PGCIL,ODISHA	09/2010	2,074.86 -	2,074.86	1,638.84	03/2013 -	11/2014	20	0
112	WESTERN REGION STRENGTHENING SCHEME-V - [N18000035]PGCIL,MAHARASHTRA	12/2007	477.69 -	477.69	494.49	09/2010 -	12/2014	51	0
113	SYSTEM STRENGTHENING IN NR FOR SASAN & MUNDRA (UMPP) - [N18000081]PGCIL,MULTI STATE	12/2009	1,216.83 -	1,216.83	1,012.19	08/2012 -	12/2014	28	0
114	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	487.49	298.72	06/2014 -	12/2014	6	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
115	TRANSMISSION SYSTEM FOR CONNECTIVITY OF ESSAR POWER GUJARAT LIMITED - [N18000114]PGCIL, GUJARAT	12/2011	552.44 -	552.44	433.50	02/2014 -	12/2014	10	0
116	IMMEDIATE EVACUATION SYSTEM WITH BARH-II TPS - [N18000127]PGCIL, BIHAR	12/2011	901.77 -	901.77	704.20	08/2014 -	12/2014	4	0
117	SYSTEM STRENGTHENING-XVIII IN SOUTHERN REGION GRID - [N18000130]PGCIL, MULTI STATE	06/2012	1,263.26 -	1,263.26	786.18	11/2014 -	12/2014	1	0
118	TRANSMISSION SYSTEM FOR PHASE-I GENERATION PROJECTS IN ORISSA-PART B - [N18000093]PGCIL, ODISHA	12/2010	2,743.19 -	2,743.19	2,311.10	12/2013 -	02/2015	14	0
119	TRANSMISSION SYSTEM FOR PHASE-I GEN.PROJ.IN ORISSA PART-C - [N18000096]PGCIL, MULTI STATE	03/2011	2,569.25 -	2,569.25	2,521.77	03/2014 -	02/2015	11	0
120	TRANSMISSION SYSTEM FOR IPP GENERATION PROJECTS IN MP AND CHATTISGARH - [N18000105]PGCIL, MULTI STATE	09/2011	1,366.34 -	1,366.34	1,063.76	12/2013 -	02/2015	14	0
121	BARH STPP STAGE -II - [N18000047]NTPC, BIHAR	02/2008	7,341.04 -	7,341.04	7,849.00	08/2013 -	03/2015	19	0
122	TRANSMISSION SYSTEM OF VINDHUACHAL -IV AND RIHAND -III GEN. PROJ. - [N18000076]PGCIL, MULTI STATE	03/2010	4,672.99 -	4,672.99	3,336.27	11/2012 -	03/2015	28	0
123	NORTHERN REGION SYSTEM STRENGTHENING SCHEME XVI - [N18000094]PGCIL, MULTI STATE	07/2010	752.64 -	752.64	417.62	07/2013 -	03/2015	20	0
124	ESTABLISHMENT OF POOLING STATIONS AT CHAMPA AND RAIGARH FOR IPP GENERATION PROJECT IN CHHATTISGARH - [N18000101]PGCIL, CHHATTISGARH	05/2011	1,961.87 -	1,961.87	1,503.95	05/2014 -	03/2015	10	0
125	COMMON SYSTEM ASSOCIATED WITH COASTAL ENERGEN PRIVATE LIMITED AND IND-BARATH POWER(MADRAS) LIMITED L - [N18000103]PGCIL, TAMIL NADU	09/2011	1,940.13 -	1,940.13	1,449.26	09/2014 -	03/2015	6	0
126	TRANSMISSION SYSTEM FOR PHASE-1 GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL-PART-A1 - [N18000104]PGCIL, JHARKHAND	10/2011	558.26 -	558.26	308.81	11/2013 -	03/2015	16	0
127	TRANSMISSION SYSTEM STRENGTHENING IN WESTERN PART OF WR FOR IPPS GENERATION PROJECTS IN CHATTISGARH - [N18000112]PGCIL, CHHATTISGARH	11/2011	2,127.51 -	2,127.51	1,923.03	07/2014 -	03/2015	8	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
128	KOLDAM HEP (NTPC) - [180100211]NTPC,HIMACHAL PRADESH	10/2002	4,527.15 7,220.00	7,220.00	6,047.00	04/2009 -	05/2015	73	59.48
129	SYSTEM STRENGTHENING IN NORTH/WEST PART OF WR FOR IPP PROJECTS IN CHATTISGARH - [N18000116]PGCIL,CHHATISGARH	12/2011	1,746.65 -	1,746.65	524.63	08/2014 -	05/2015	9	0
130	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXVIII - [N18000135]PGCIL,MULTI STATE	09/2012	524.40 -	524.40	139.82	04/2015 -	05/2015	1	0
131	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 -	11,130.19	9,060.80	08/2013 -	06/2015	22	0
132	TRANS. SYSTEM ASSOCIATED WITH PALLATANA GBPP and BPTS. - [N18000080]PGCIL,MULTI STATE	02/2010	2,144.00 -	2,144.00	1,844.30	12/2012 -	06/2015	30	0
133	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-A - [N18000098]PGCIL,MULTI STATE	05/2010	250.03 -	250.03	69.70	01/2013 -	06/2015	29	0
134	TRANSMISSION SYSTEM FOR TRANSFER OF POWER FROM GEN.PROJ IN SIKKIM TO NRWR PART-B - [N18000099]PGCIL,MULTI STATE	03/2011	1,585.12 -	1,585.12	1,311.26	11/2013 -	06/2015	19	0
135	TR SYSTEM FOR PHASE-I GENERATION PROJECTS IN JHARKHAND AND WEST BENGAL- PART-A2 - [N18000113]PGCIL,MULTI STATE	12/2011	2,422.66 -	2,422.66	1,194.96	08/2014 -	06/2015	10	0
136	SYSTEM STRENGTHENING IN RAIPUR-WARDHA CORRIDOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000117]PGCIL,CHHATISGARH	01/2012	1,422.85 -	1,422.85	782.72	01/2015 -	06/2015	5	0
137	TR. SYS. FOR PHASE-I PROJ. IN JHARKHAN AND WEST BENGAL PART-B - [N18000129]PGCIL,MULTI STATE	02/2012	3,201.44 -	3,201.44	1,746.81	10/2014 -	06/2015	8	0
138	PARE HYDRO ELECTRIC PROJECT - [N18000045]NEEPCO,ARUNACHAL PRADESH	12/2008	573.99 1,128.38	1,128.38	909.40	08/2013 -	09/2015	25	96.59
139	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	4,824.12	3,963.78	10/2012 -	12/2015	38	0
140	TRANSM SYSTEM FOR DEVELOPMENT OF POOLING STN. IN NR PART OF WEST BENGAL AND TRANSFER OF POWER FROM B - [N18000077]PGCIL,WEST BENGAL	04/2010	4,404.57 -	4,404.57	627.95	01/2015 -	12/2015	11	0
141	EASTERN REGION STRENGTHENING SCHEME-III - [N18000100]PGCIL,MULTI STATE	07/2010	1,272.80 -	1,272.80	881.93	11/2012 -	12/2015	37	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
142	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119]NEEPCO,MIZORAM	01/2011	368.72 913.63	913.63	647.19	07/2006 01/2014	12/2015	113	147.78
143	WR-NR HVDC INTERCONNECTOR FOR IPP PROJECTS IN CHHATTISGARH - [N18000125]PGCIL,CHHATTISGARH	03/2012	9,569.76 -	9,569.76	2,445.59	06/2015 -	12/2015	6	0
144	TEESTA LOW DAM HEP, STAGE-IV (NHPC) - [180100243]NHPC,WEST BENGAL	09/2005	1,061.38 -	1,061.38	1,540.94	09/2009 -	03/2016	78	0
145	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XVIII - [N18000053]PGCIL,MULTI STATE	02/2009	509.66 -	509.66	413.76	11/2011 -	03/2016	52	0
146	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XIX - [N18000056]PGCIL,MULTI STATE	02/2009	410.29 -	410.29	287.57	02/2012 -	03/2016	49	0
147	NORTHERN REGION TRANSMISSION STRENGTHENING SCHEME - [N18000083]PGCIL,MULTI STATE	03/2010	965.58 -	965.58	690.64	11/2012 -	03/2016	40	0
148	NORTHERN REGION SYSTEM STRENGTHENING SCHEME-XXI - [N18000095]PGCIL,MULTI STATE	08/2010	1,677.57 -	1,677.57	1,070.12	04/2013 -	03/2016	35	0
149	BONGAIGAON THERMAL POWER PROJECT - [N18000041]NTPC,ASSAM	01/2008	6,749.18 6,749.18	6,749.18	4,680.00	07/2011 -	08/2016	61	0
150	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXII - [N18000160]PGCIL,MULTI STATE	02/2014	243.53 -	243.53	0.80	08/2014 -	08/2016	24	0
151	KISHANGANGA HEP - [N18000031]NHPC,JAMMU AND KASHMIR	07/2007	3,642.04 -	3,642.04	3,578.56	01/2016 -	11/2016	10	0
152	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]NEEPCO,ARUNACHAL PRADESH	12/2004	2,496.90 -	4,653.95	3,179.32	12/2009 03/2017	03/2017	87	86.39
153	BARH STPP(3X660MW) NTPC - [180100242]NTPC,BIHAR	12/2003	8,692.97 -	8,693.00	10,223.00	12/2009 -	03/2017	87	0
154	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 3,846.30	3,846.30	2,180.00	03/2013 -	03/2018	60	29.14
155	KUDGI STPP STAGE 1 - [N18000131]NTPC,KARNATAKA	12/2011	15,166.19 -	15,166.19	4,923.00	12/2016 -	03/2018	15	0
156	MOUDA STPP STAGE 2 - [N18000132]NTPC,MAHARASHTRA	03/2012	7,921.47 -	7,921.47	2,968.00	09/2016 -	03/2018	18	0
157	SOLAPUR STPP - [N18000133]NTPC,MAHARASHTRA	03/2012	9,395.18 2,998.00	9,395.18	2,998.00	11/2016 -	03/2018	16	0
158	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	1,527.00	140.00	08/2017 -	03/2018	7	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
159	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I - [N18000151]NTPC,MADHYA PRADESH	02/2013	11,638.55 -	11,638.55	1,411.00	09/2017 -	03/2018	6	0
160	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCL,UTTARAKHAND	07/2006	1,657.00 2,978.86	2,978.86	778.83	07/2010 02/2016	05/2018	94	79.77
161	PARBATI HEP (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 -	5,366.00	4,622.40	09/2009 -	07/2018	106	36.9
162	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCL,UTTARAKHAND	08/2008	2,491.58 -	3,745.08	495.58	07/2014 -	07/2018	48	50.31
163	SUBANSIRI LOWER H.E.P (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 -	6,285.33	6,925.96	09/2010 -	12/2018	99	0
164	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) - [N18000140]NTPC,CHHATISGARH	11/2012	11,846.00 -	11,846.00	1,766.00	05/2017 -	03/2019	22	0
	Total		200,279.83 -	213,153.69	131,351.94				
	<u>RAILWAYS</u>								
165	RAJATGARH-BARANG(LD),ECOR - [220100286]RVNL,ODISHA	04/1999	166.16 -	288.00	-	02/2009 02/2009	08/2014	66	73.33
166	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	276.00	-	03/2009 03/2009	08/2014	65	106.88
167	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]NCR,MULTI STATE	04/1986	158.77 608.02	608.02	593.82	03/1994 -	10/2014	247	282.96
168	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]NCR,UTTAR PRADESH	04/1999	108.00 427.21	432.72	414.84	12/2009 03/2011	12/2014	60	300.67
169	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307]ECR,BIHAR	04/2002	921.00 -	2,363.00	1,435.24	03/2009 12/2012	12/2014	69	156.57
170	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	09/2001	120.00 245.39	245.39	232.11	12/2008 -	12/2014	72	104.49
171	TAMLUK-BASULYA-SUTAHATA DOUBLING - [N22000163]SER,WEST BENGAL	04/2010	171.02 -	171.02	148.69	06/2013 -	12/2014	18	0
172	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]FOIS,MULTI STATE	03/1984	520.00 835.04	835.04	646.73	03/1995 -	03/2015	240	60.58
173	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	445.40	180.42	03/2007 03/2007	03/2015	96	13.2
174	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 236.37	272.39	141.55	03/2012 12/2013	03/2015	36	59.2

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
175	RANCHI-LOHARDAGA(GC),SER - [220100214]SER,JHARKHAND	04/1997	194.07 -	596.40	381.74	06/2004 -	06/2015	132	207.31
176	PATNA GANGA BRIDGE (NL), ECR - [220100308]ECR,BIHAR	04/2001	624.47 -	2,921.00	2,214.57	10/2007 12/2012	12/2015	98	367.76
177	BHOPAL BINA 3D LINE DOUBLING - [N22000077]RVNL,MADHYA PRADESH	09/2007	687.20 -	800.00	-	03/2010 -	12/2015	69	16.41
178	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	401.81 -	1,814.10	392.88	03/2004 12/2010	03/2016	144	351.48
179	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]SWR,KARNATAKA	04/2007	482.00 -	874.57	598.36	03/2013 -	03/2016	36	81.45
180	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42 -	2,298.42	68.05	03/2014 -	03/2016	24	0
181	KATAKHAL TO BHAIRABI - [N22000126]NEFR,ASSAM	04/1998	227.90 -	331.40	141.17	12/2012 -	03/2016	39	45.41
182	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]NEFR,ASSAM	04/1996	1,676.31 -	5,185.44	4,365.70	03/2009 -	03/2016	84	209.34
183	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]SER,JHARKHAND	04/2010	309.44 -	388.67	92.56	12/2015 -	03/2016	3	25.6
184	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194]NEFR,TRIPURA	04/1999	895.00 -	1,242.25	977.30	03/2007 -	03/2016	108	38.8
185	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]MRTP,TELANGANA	04/2012	632.68 -	816.55	17.43	04/2012 -	03/2016	47	29.06
186	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]RVNL, WEST BENGAL	04/2010	2,397.72 -	2,397.72	118.54	03/2016 -	06/2016	3	0
187	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]NEFR,ASSAM	09/1997	1,500.00 -	4,996.19	3,302.95	04/2008 12/2011	12/2016	104	233.08
188	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	184.91	59.57	03/2015 -	12/2016	21	23.36
189	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NEFR,MULTI STATE	04/2000	733.00 733.00	2,483.04	1,651.28	12/2008 -	03/2017	99	238.75
190	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]NR,UTTAR PRADESH	04/2006	325.00 -	1,116.53	324.86	03/2010 03/2017	03/2017	84	243.55

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
191	AGARTALA SABROOM, NL, NEFR - [N22000099]NEFR,TRIPURA	04/2008	813.34 -	1,741.00	697.37	03/2014 -	03/2017	36	114.06
192	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 2,500.00	20,000.00	8,805.00	11/2002 -	12/2017	181	700
193	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NEFR,MANIPUR	04/2003	727.56 727.56	5,996.00	2,460.85	03/2011 03/2014	03/2018	84	724.12
194	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 6,213.84	7,012.84	1,791.64	03/2014 -	03/2019	60	32.32
195	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NEFR,MIZORAM	04/2008	619.34 -	2,393.48	191.67	04/2014 -	03/2020	71	286.46
196	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NEFR,NAGALAND	04/2006	850.00 -	2,446.57	9.43	03/2015 -	03/2020	60	187.83
	Total		27,208.08 -	73,974.06	32,456.32				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
197	NAGAON TO DHARAMTUL (AS-2) - [N24000042]NHAI,ASSAM	12/2003	264.72 -	264.72	311.80	06/2008 -	08/2014	74	0
198	DHARAMTUL TO SONAPUR (AS-19) - [N24000051]NHAI,ASSAM	12/2003	200.00 -	200.00	283.20	06/2008 -	08/2014	74	0
199	DHOLPUR - MORENA SECTION (INCLUDING CHAMBOL BRIDGE) NH-3 - [N24000108]NHAI,MULTI STATE	12/2003	232.45 -	232.45	316.80	09/2010 -	08/2014	47	0
200	KISHANGARH-AJMER-BEAWER - [N24000128]NHAI,RAJASTHAN	11/2009	795.00 -	795.00	1,128.00	05/2012 -	08/2014	27	0
201	AMRITSAR-PATHANKOT - [N24000147]NHAI,PUNJAB	05/2010	705.00 -	705.00	2,190.00	11/2012 -	08/2014	21	0
202	DEOLI-KOTA - [N24000148]NHAI,RAJASTHAN	01/2011	593.00 -	593.00	753.90	07/2013 -	08/2014	13	0
203	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	574.00	948.60	03/2014 -	08/2014	5	0
204	PUNE-SHOLAPUR,PKG-II - [N24000193]NHAI,MAHARASHTRA	09/2011	835.00 -	835.00	475.20	01/2014 -	08/2014	7	0
205	BEAWAR-PALI-PINDWARA - [N24000199]NHAI,RAJASTHAN	12/2011	2,388.00 -	2,388.00	2,199.00	06/2014 -	08/2014	2	0
206	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 241.28	280.13	170.90	11/2008 12/2014	09/2014	70	80.68
207	KOTA BYPASS,RJ-4, NH-76 (NHAI) - [240106297]NHAI,RAJASTHAN	12/2003	275.00 -	250.39	284.90	10/2008 -	09/2014	71	-8.95
208	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	245.00	491.20	03/2008 01/2015	09/2014	78	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
209	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI, ASSAM	12/2003	225.00 -	225.00	258.40	06/2008 09/2014	09/2014	75	0
210	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 1,141.00	1,141.00	2,144.00	08/2013 06/2014	09/2014	13	0
211	SIX LANNING OF HOSUR-KRISHNAGIRI NH-7 KM.33.130 TO KM.93.00 - [N24000171]NHAI, TAMIL NADU	06/2011	535.00 -	535.00	52.18	12/2013 -	09/2014	9	0
212	SIX LANNING OF KRISHNAGIRI-WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI, TAMIL NADU	09/2011	1,250.00 -	1,250.00	1,312.00	12/2013 -	09/2014	9	0
213	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI-ENNORE PORT CONNECTIVITY - [N24000173]NHAI, TAMIL NADU	06/2011	600.00 -	600.00	312.80	06/2013 -	09/2014	15	0
214	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	571.00	-	10/2013 -	09/2014	11	0
215	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	511.54	1,179.00	11/2013 -	09/2014	10	0
216	SAMBALPUR-BARGARH-CHHATISGARH/ORISSA BORDER - [N24000196]NHAI, ODISHA	11/2011	909.00 -	909.00	963.90	05/2014 -	09/2014	4	0
217	LUCKNOW-RAIBAREILI - [N24000207]NHAI, UTTAR PRADESH	07/1999	635.90 -	635.90	599.00	07/2012 -	09/2014	26	0
218	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI, MULTI STATE	04/2012	624.00 -	624.00	439.20	04/2014 -	09/2014	5	0
219	2 LANING WITH PS KANPUR KABRAI - [N24000221]NHAI, UTTAR PRADESH	01/2013	373.47 -	373.47	268.10	07/2014 -	09/2014	2	0
220	GUWAHATI TO NALBARI (AS-5) - [N24000046]NHAI, ASSAM	12/2003	198.16 -	198.16	242.40	04/2008 01/2015	10/2014	78	0
221	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]NHAI, ASSAM	12/2003	160.00 -	160.00	197.60	05/2008 01/2015	10/2014	77	0
222	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	953.88	892.00	07/2013 -	11/2014	16	0
223	SILCHAR-UDARBAND (PH.II) HN-54, KM.309 TO KM.275 - [240100207]NHAI, ASSAM	12/2003	157.47 157.47	154.57	265.00	09/2007 03/2014	12/2014	87	-1.84
224	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]NHAI, UTTAR PRADESH	12/2003	155.00 -	201.66	189.20	09/2008 -	12/2014	75	30.1
225	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 361.00	280.00	359.00	02/2009 -	12/2014	70	0
226	MAIBANG TO LUNDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 167.64	167.64	127.50	11/2008 12/2014	12/2014	73	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
227	MAIBANG TO LUNDING (AS-27), KM.40.000 TO KM.60.500 - [240106281]NHAI,ASSAM	12/2003	200.00 200.00	200.00	204.80	04/2009 12/2014	12/2014	68	0
228	FORBESGANJ TO SIMRAHI (NH-57)(NHAI) - [240106294]NHAI,BIHAR	12/2003	332.94 -	332.94	521.60	09/2008 -	12/2014	75	0
229	RAJMARG CHORHA TO LAKHNANDON,KM 297 TO KM 351, NH-26 (NHAI) - [240106304]NHAI,MADHYA PRADESH	12/2003	251.03 -	251.03	383.70	10/2008 -	12/2014	74	0
230	GUWHATI TO NALBARI (AS-4) - [N24000038]NHAI,ASSAM	12/2003	175.96 -	175.96	182.50	04/2008 01/2015	12/2014	80	0
231	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 230.00	208.00	290.60	04/2008 01/2015	12/2014	80	0
232	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 331.23	363.74	239.60	07/2009 -	12/2014	65	85.58
233	NH CONNECTIVITY TO ICTT VALLARPADA EU NH - SH - [N24000107]NHAI,KERALA	03/2005	557.00 -	557.00	1,122.00	02/2010 -	12/2014	58	0
234	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	486.00	665.10	05/2010 -	12/2014	55	0
235	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	1,509.10	2,542.00	09/2012 -	12/2014	27	0
236	CHENNAI-TADA(SIX LANE) - [N24000129]NHAI,TAMIL NADU	04/2009	353.37 -	353.37	446.20	10/2011 -	12/2014	38	0
237	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	1,693.75	2,762.00	08/2011 -	12/2014	40	0
238	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	1,175.00	138.70	04/2013 -	12/2014	20	0
239	CHENGAPALLI TO COIMBATORE BYPASS KM-102.035-144.740 KM - [N24000144]NHAI,TAMIL NADU	09/2010	852.00 -	852.00	891.90	03/2013 -	12/2014	21	0
240	CUDDAPAH-MYDUKUR-KURNOOL KM-167.750-356.502 KM - [N24000145]NHAI,ANDHRA PRADESH	11/2010	1,585.00 -	1,585.00	996.80	05/2013 -	12/2014	19	0
241	WADNER-DEVDHARI(NS-60/MH)(KM 94-123 KM) - [N24000150]NHAI,MAHARASHTRA	02/2011	193.45 -	193.45	65.80	11/2012 -	12/2014	25	0
242	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	1,210.00	03/2013 -	12/2014	21	0
243	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	1,813.76	1,153.00	07/2013 -	12/2014	17	0
244	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	671.30	630.90	02/2013 -	12/2014	22	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
245	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	374.00	146.90	05/2013 -	12/2014	19	0
246	SAMAIKHALI - GANDHIDHAM - [N24000179]NHAI, GUJARAT	09/2010	805.39 -	805.39	831.60	03/2013 -	12/2014	21	0
247	JORBAT - BARAPANI - [N24000180]NHAI,MEGHALAYA	01/2011	536.00 -	536.00	664.90	01/2014 -	12/2014	11	0
248	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	1,100.70	297.50	06/2014 -	12/2014	6	0
249	4-LANING OF BRAHMAPORE-FARAKA - [N24000203]NHAI,MULTI STATE	02/2011	998.79 -	998.79	1,560.00	08/2013 -	12/2014	16	0
250	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,MULTI STATE	12/2011	1,047.00 -	1,047.00	288.20	06/2014 -	12/2014	6	0
251	2 LANING OF DINDIGUL - PERIGULAM THENI- KUMILI - [N24000177]NHAI,TAMIL NADU	09/2011	485.00 -	485.00	360.50	08/2013 -	02/2015	18	0
252	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	385.13	145.80	04/2009 12/2014	03/2015	71	92.75
253	BIJNI TO ASSAM WB BORDER (NH-31.C)(1)(NHAI) - [240106290]NHAI,ASSAM	12/2003	195.00 -	195.00	267.10	06/2008 -	03/2015	81	0
254	BIJNI TO ASSAM /WB.BORDER (NH-31.C)(NHAI) - [240106293]NHAI,ASSAM	12/2003	237.80 -	237.80	310.70	06/2008 -	03/2015	81	0
255	HARANGAJO TO MAIBANG,KM 164.08-190.587 NH-54 - [N24000061]NHAI,ASSAM	12/2003	212.00 333.83	386.10	125.20	09/2007 -	03/2015	90	82.12
256	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 309.56	217.61	258.40	04/2010 01/2016	03/2015	59	0
257	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 -	2,288.00	3,466.00	11/2011 -	03/2015	40	106.5
258	MURADABAD-BAREILY - [N24000154]NHAI,UTTAR PRADESH	04/2010	1,267.00 -	1,267.00	2,395.00	06/2013 -	03/2015	21	0
259	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	375.09	405.40	04/2014 -	03/2015	11	0
260	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR	01/2011	575.00 -	575.00	824.90	07/2013 -	03/2015	20	0
261	BHUBANESWAR TO PURI - [N24000195]NHAI,ODISHA	03/2011	500.29 -	500.29	622.10	08/2013 -	03/2015	19	0
262	4 LANING OF JETPUR SOMNATH SECTION OF NH 8D LENGTH KM 127.6 - [N24000225]NHAI, GUJARAT	03/2012	828.00 -	828.00	722.70	09/2014 -	03/2015	6	0
263	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	1,535.00	2,043.00	05/2014 -	05/2015	12	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
264	BIJNI TO ASSAM/WB BORDER PH.II, KM.30.00 TO 0.00, NH-31 C - [240106226]NHAI,ASSAM	12/2003	230.00 -	230.00	243.50	06/2005 -	06/2015	120	0
265	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]NHAI,UTTAR PRADESH	12/2003	348.16 -	465.50	295.10	09/2007 07/2011	06/2015	93	33.7
266	CHILKALURIPET-VIJAYWADA 6 LANE (KM 355 TO KM 434.15) - [N24000132]NHAI,ANDHRA PRADESH	05/2009	572.30 -	572.30	886.90	10/2011 -	06/2015	44	0
267	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,MULTI STATE	02/2011	1,078.84 -	1,078.84	1,757.00	08/2013 -	06/2015	22	0
268	4-LANING OF BARHI-HAZARIBAGH - [N24000191]NHAI,JHARKHAND	02/2012	398.00 -	398.00	459.30	02/2014 -	09/2015	19	0
269	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	1,410.00	779.30	09/2014 -	10/2015	13	0
270	FOUR LANNING OF WALAYAR-VADAKKANCHERRY SECTION - [N24000214]NHAI,KERALA	04/2011	682.00 -	682.00	693.10	10/2013 -	11/2015	25	0
271	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	604.00	495.40	12/2009 -	12/2015	72	0
272	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	325.00	608.40	05/2013 -	12/2015	31	0
273	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	2,848.00	1,081.00	03/2014 -	12/2015	21	0
274	BHOPAL-SANCHI - [N24000192]NHAI,MADHYA PRADESH	10/2011	209.00 -	209.00	38.77	01/2013 -	12/2015	35	0
275	BAREILLY-SITAPUR (NH-24) - [N24000200]NHAI,UTTAR PRADESH	03/2011	1,046.00 -	1,046.00	384.20	09/2013 -	12/2015	27	0
276	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	754.00	591.00	03/2013 -	12/2015	33	0
277	4-LANING OF RAIGANJ-DALKOLA - [N24000204]NHAI,MULTI STATE	02/2011	580.43 -	580.43	365.20	08/2013 -	12/2015	28	0
278	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	291.36	137.80	01/2014 -	12/2015	23	0
279	KRISHNANAGAR-BERHAMPUR - [N24000209]NHAI,WEST BENGAL	02/2012	702.16 -	702.16	706.50	07/2014 -	12/2015	17	0
280	HARIDWAR-DEHRADUN (APPROVED LENGTH 69) - [N24000212]NHAI,UTTARAKHAND	11/2011	478.00 -	478.00	316.80	10/2013 -	12/2015	26	0
281	PANVEL-INDAPUR - [N24000216]NHAI,MULTI STATE	12/2011	942.69 -	942.69	286.30	06/2014 -	12/2015	18	0
282	BARSAT-KRISHNANAGAR - [N24000229]NHAI,WEST BENGAL	08/2012	867.00 -	867.00	598.60	02/2015 -	02/2016	12	0
283	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION(KM 240-270KM) - [N24000149]NHAI,KERALA	02/2010	617.00 -	617.00	156.20	08/2012 -	03/2016	43	0

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
284	NASHRI CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	06/2010	2,159.00 -	2,159.00	567.40	06/2015 -	05/2016	11	0
285	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	1,987.00	1,162.00	07/2015 -	06/2016	11	0
286	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]NHAI,RAJASTHAN	12/2003	275.00 -	281.31	180.10	02/2010 -	07/2016	77	2.29
287	4 LANNING OF BELGUM-KHANPUR SECTION AND 2 LANING OF KHANPUR-KNT/GOA BORDER - [N24000153]NHAI,KARNATAKA	03/2011	359.00 -	359.00	39.49	09/2013 -	12/2016	39	0
288	NIROLI-ROXY-RAJAMUNDA - [N24000194]NHAI,ODISHA	07/2011	586.00 -	586.00	237.60	01/2014 -	12/2016	35	0
	Total		63,635.90 -	65,610.95	62,604.84				
	<u>SHIPPING AND PORTS</u>								
289	ACQUISITION OF SIX (6) NOS. OF ANCHOR HANDLING TUG CUM SUPPLY - [N25000062]SHIPP.,MULTI STATE	01/2012	511.87 -	511.87	106.72	03/2014 08/2014	08/2014	5	0
290	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]SHIPP.,MAHARASHTRA	10/2010	966.46 -	994.82	427.54	02/2014 01/2015	01/2015	11	2.93
291	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]MUMBAI PORT TRU,MAHARASHTRA	11/2007	1,228.00 1,460.00	2,158.16	1,016.95	12/2010 09/2012	03/2015	51	75.75
	Total		2,706.33 -	3,664.85	1,551.21				
	<u>TELECOMMUNICATIONS</u>								
292	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL - [N26000058]BSNL,UTTARAKHAND	01/2009	149.15 -	158.72	86.05	06/2009 -	09/2014	63	6.42
293	ASSAM TELECOM CIRCLE, PHASE-V.I, 2G & 3G - [N26000062]BSNL,ASSAM	06/2007	336.81 -	336.81	189.58	01/2009 -	12/2014	71	0
294	ERP IMPLEMENTATION IN BSNL ON TURNKEY BASIS - [N26000096]BSNL,MULTI STATE	10/2009	384.00 -	384.00	29.45	10/2010 01/2015	01/2015	51	0
	Total		869.96 -	879.53	305.08				
	<u>URBAN DEVELOPMENT</u>								

All Cost/ Expenditure in Rs. Crore (August 2014)

						Date of Commissioning (Month/Year)			
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)
1	2	3	4	5	6	7	8	9	10
295	FARIDABAD EXTENSION - [N28000057]DMRC, DELHI	09/2011	2,494.00 -	2,494.00	685.21	09/2014 -	05/2015	8	0
	Total		2,494.00 -	2,494.00	685.21				
	Grand Total		548,838.05	650,274.08	417,343.89				

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2014)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57	54
2	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	11/2014	31.12	71
	Total		16,663.00 -	22,947.00				
	<u>CIVIL AVIATION</u>							
3	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	09/2014	15.77	28
	Total		335.61 -	23,335.53				
	<u>COAL</u>							
4	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50	24
5	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02	24
6	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37	44
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60	120
8	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	10/2014	49.09	64
9	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	10/2014	34.63	31
	Total		9,127.17 -	42,834.48				
	<u>PETROLEUM</u>							
10	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167]	08/2006	94.00 -	352.56	09/2012 -	03/2017	275.06	54
11	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149]	08/2008	144.02 -	204.29	06/2012 -	12/2014	41.85	30
12	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138]	08/2009	246.81 -	276.83	04/2012 -	10/2014	12.16	30
13	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155]	11/2012	309.81 -	462.79	10/2014 -	10/2015	49.38	12
14	DEV OF G1 AND GS-15 (ONGCL) - [160100231]	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20	110

(August 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
15	WAX PROJECT - [N16000101]	06/2010	576.60 -	676.05	12/2013 -	10/2014	17.25	10
16	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156]	01/2006	672.00 -	1,038.00	10/2011 -	12/2014	54.46	38
17	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157]	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62	48
18	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148]	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72	8
19	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169]	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49	45
20	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104]	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84	20
21	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033]	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68	57
22	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143]	01/1999	14,225.00 -	16,504.00	12/2015 -	05/2016	16.02	5
23	PARADIP REFINERY PROJECT - [N16000058]	02/2009	29,777.00 -	34,555.00	11/2012 -	02/2015	16.05	27
	Total		55,561.22 -	117,618.15				
	<u>POWER</u>							
24	TRIPURA GAS BASED POWER PROJECT - [N18000071]	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30	16
25	PARE HYDRO ELECTRIC PROJECT - [N18000045]	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59	25
26	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77	94
27	RAMPUR HEP(412 MW) - [N18000024]	01/2007	2,047.03 -	3,288.28	03/2012 -	09/2014	60.64	30
28	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC - [N18000065]	08/2008	2,360.95 -	2,580.90	08/2012 -	10/2014	9.32	26
29	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31	48
30	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239]	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39	87
31	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2018	29.14	60
32	PARBATI HEP (NHPC) II - [180100210]	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90	106
33	KOLDAM HEP (NTPC) - [180100211]	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48	73
34	BARH STPP(3X660MW) NTPC - [180100242]	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00	87

(August 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		32,166.65 -	162,113.75				
	<u>RAILWAYS</u>							
35	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67	60
36	ETAWAH-MAINPURI (NL),NCR - [220100318]	09/2001	120.00 -	245.39	12/2008 -	12/2014	104.49	72
37	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88	65
38	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36	21
39	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007]	04/1986	158.77 274.56	608.02	03/1994 -	10/2014	282.96	247
40	RAJATGARH-BARANG(LD),ECOR - [220100286]	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33	66
41	ELECTRIFICATION OF KHURJA-MEERUT- SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20	36
42	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31	132
43	KATAKHAL TO BHAIRABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41	39
44	DANGOAPSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60	3
45	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55	84
46	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20	96
47	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48	144
48	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45	36
49	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009]	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58	240
50	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2020	286.46	71
51	PATNA GANGA BRIDGE (NL), ECR - [220100308]	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76	98
52	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06	47
53	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41	69
54	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	727.56 -	5,996.00	03/2011 -	03/2018	724.12	84

(August 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
55	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [N220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75	99
56	AGARTALA SABROOM, NL, NEFR - [N22000099	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06	36
57	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	850.00 -	2,446.57	03/2015 -	03/2020	187.83	60
58	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80	108
59	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57	69
60	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES, NEFR - [220100201	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	12/2016	233.08	104
61	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2016	209.34	84
62	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00	181
63	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32	60
	Total		22,340.92 -	231,220.65				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
64	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10	75
65	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68	70
66	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58	65
67	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75	71
68	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12	90
69	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29	77
70	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70	93
71	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50	40
	Total		2,649.01 -	235,872.22				
	<u>SHIPPING AND PORTS</u>							
72	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053	10/2010	966.46 -	994.82	02/2014 -	01/2015	2.93	11

(August 2014)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
73	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	03/2015	75.75	51
	Total		2,194.46 -	239,025.20				
	<u>STEEL</u>							
74	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	10/2014	100.63	73
75	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	03/2015	105.20	39
76	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	12/2014	41.41	62
77	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	12/2014	13.61	36
	Total		23,538.89 -	268,548.05				
	<u>TELECOMMUNICATIONS</u>							
78	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTANCHAL [N26000058]	01/2009	149.15 -	158.72	06/2009 -	09/2014	6.42	63
	Total		149.15 -	268,706.77				
	Grand Total		164,726.08	1,612,221.80				

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2014)							
					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
1	KUDANKULAM APP (NPCIL) - [020100040]	12/2001	13,171.00 -	17,270.00	12/2008 -	11/2014	31.12
2	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	5,677.00	09/2010 -	03/2015	62.57
	Total		16,663.00 -	22,947.00			
	<u>CIVIL AVIATION</u>						
3	C/O INTEGRATED PASSENGER TER. BULD. NSCBI AIRPORT - [N04000037]	08/2008	1,942.51 -	2,573.92	05/2011 -	03/2013	32.50
4	D/O KAMARAJ DOMESTIC TER-PH-II AND EXP. ANNA INT. TER BLDG(K1) - [N04000038]	08/2008	1,808.00 -	2,015.00	01/2011 -	02/2012	11.45
5	CONSTRUCTION OF NEW INTERNATIONAL TERMINAL BUILDING(GOA) - [N04000069]	05/2010	335.61 -	388.53	05/2012 -	09/2014	15.77
	Total		4,086.12 -	27,924.45			
	<u>COAL</u>						
6	TPS-II EXPANSION (1470MW TO 1970MW) (NLC) - [060100087]	10/2004	2,030.78 -	3,027.59	06/2009 -	10/2014	49.09
7	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	06/2008	1,188.31 -	7,612.33	03/2013 -	03/2023	540.60
8	MAGADH OC 20 MTY (CCL) - [N06000015]	08/2008	469.78 -	706.40	07/2012 -	03/2016	50.37
9	ADRIYALA SHAFT PROJECT - [N06000016]	12/2009	212.34 -	1,228.39	03/2013 -	03/2015	478.50
10	BHUBANESWARI OCP, MCL (20.0 MTY) - [N06000034]	12/2007	490.00 -	490.10	03/2017 -	03/2017	0.02
11	TUTICORIN THERMAL POWER PROJECT- 2X500 MW - [N06000047]	05/2008	4,904.54 -	6,602.74	03/2012 -	10/2014	34.63
12	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]	12/2009	321.42 -	321.50	03/2014 -	03/2016	0.02
13	AMLAI OC EXPANSION SECTOR B (1.50 MTY) - [N06000082]	11/2009	150.59 -	198.59	03/2016 -	03/2016	31.87
	Total		9,767.76 -	48,112.09			
	<u>PETROCHEMICALS</u>						
14	ASSAM GAS CRACKER PROJECT - [N16000106]	04/2006	5,460.61 -	8,920.00	04/2012 -	-	63.35
	Total		5,460.61 -	57,032.09			

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	<u>PETROLEUM</u>						
15	DEV OF G1 AND GS-15 (ONGCL) - [N160100231	04/2003	429.82 -	3,955.21	04/2006 -	06/2015	820.20
16	DEVELOPMENT OF B-193 CLUSTER FIELDS - [N16000033	06/2007	3,248.78 -	6,000.00	08/2010 03/2012	05/2015	84.68
17	PARADIP REFINERY PROJECT - [N16000058	02/2009	29,777.00 -	34,555.00	11/2012 -	02/2015	16.05
18	WAX PROJECT - [N16000101	06/2010	576.60 -	676.05	12/2013 -	10/2014	17.25
19	DEVELOPMENT OF CLUSTER-7 FIELDS - [N16000104	03/2010	3,241.03 -	6,638.94	03/2013 -	11/2014	104.84
20	INTEGRATED DEVELOPMENT OF B-127 FIELDS - [N16000131	12/2011	2,059.63 -	2,665.65	03/2015 -	03/2015	29.42
21	PIPELINE FOR TRANSFER OF LPG FROM BPCR/HPCR TO URAN LPG PLANT - [N16000138	08/2009	246.81 -	276.83	04/2012 -	10/2014	12.16
22	INTEGRATED REFINERY EXPANSION PROJECT - [N16000143	01/1999	14,225.00 -	16,504.00	12/2015 -	05/2016	16.02
23	MANGALORE HASSAN MYSORE SOLUR LPG PIPELINE (MHMSLPL) - [N16000146	11/2012	666.00 -	701.00	11/2015 -	11/2015	5.26
24	URAN CHAKAN/SHIKRAPUR LPG PIPELINE - [N16000155	11/2012	309.81 -	462.79	10/2014 -	10/2015	49.38
25	STRATEGIC CRUDE OIL STORAGE PROJECT AT VIZAG - [N16000156	01/2006	672.00 -	1,038.00	10/2011 -	12/2014	54.46
26	STRATEGIC CRUDE OIL STORAGE PROJECT AT MANGALORE - [N16000157	01/2006	732.00 -	1,227.00	10/2011 -	10/2015	67.62
27	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN - [N16000167	08/2006	94.00 -	352.56	09/2012 -	03/2017	275.06
28	STRATEGIC CRUDE OIL STORAGE PROJECT AT PADUR - [N16000169	01/2006	993.00 -	1,693.00	01/2012 -	10/2015	70.49
29	KOTA JOBNER PIPELINE PROJECT - [N16000170	04/2011	276.26 -	276.27	03/2015 -	03/2015	0.00
30	UPGRADATION OF CRUDE OIL PUMP STATIONS OF NAHARKATIYA-BARAUNI CRUDE OIL TRUNK PIPELINE - [N18000148	09/2012	871.35 -	1,200.00	03/2015 -	11/2015	37.72
31	CENTRAL GAS GATHERING STATION AND OFFTAKE POINT - [N18000149	08/2008	144.02 -	204.29	06/2012 -	12/2014	41.85
	Total		58,563.11 -	135,458.68			
	<u>POWER</u>						
32	PARBATI HEP (NHPC) II - [180100210	09/2002	3,919.59 -	5,366.00	09/2009 -	07/2018	36.90
33	KOLDAM HEP (NTPC) - [180100211	10/2002	4,527.15 -	7,220.00	04/2009 -	05/2015	59.48
34	KAMENG HYDROELECTRIC PROJECT (NEEPCO) - [180100239	12/2004	2,496.90 -	4,653.95	12/2009 06/2016	03/2017	86.39

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
35	BARH STPP(3X660MW) NTPC - [180100242	12/2003	8,692.97 -	8,693.00	12/2009 -	03/2017	0.00
36	KAIGA 3 AND 4 TRANSMISSION SYSTEM (PGCIL) - [180100246	03/2005	596.45 -	1,007.16	12/2007 -	-	68.86
37	KUNADANKULAM APP TRANS SYSTEM (PGCIL) - [180100258	05/2005	1,779.29 -	2,159.07	09/2008 -	03/2013	21.34
38	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010	07/2006	1,657.00 -	2,978.86	07/2010 -	05/2018	79.77
39	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014	11/2006	2,978.48 -	3,846.30	03/2013 -	03/2018	29.14
40	RAMPUR HEP(412 MW) - [N18000024	01/2007	2,047.03 -	3,288.28	03/2012 -	09/2014	60.64
41	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042	08/2008	2,491.58 -	3,745.08	07/2014 -	07/2018	50.31
42	PARE HYDRO ELECTRIC PROJECT - [N18000045	12/2008	573.99 -	1,128.38	08/2013 -	09/2015	96.59
43	SUPPLEMENTARY TRANSMISSION ASSOCIATED WITH DVC AND MAITHON RBC [N18000065	08/2008	2,360.95 -	2,580.90	08/2012 -	10/2014	9.32
44	TRIPURA GAS BASED POWER PROJECT - [N18000071	07/2009	421.01 -	994.85	07/2013 -	11/2014	136.30
45	TUIRIAL HYDRO ELECTRIC PROJECT (60MW) - [N18000119	01/2011	368.72 -	913.63	07/2006 02/2015	12/2015	147.78
	Total		34,911.11 -	184,034.14			
	<u>RAILWAYS</u>						
46	GUNA-ETAWAH VIA SHIVPURI-GWALIOR -BHIND NL, (NCR) - [220100007	04/1986	158.77 274.56	608.02	03/1994 -	10/2014	282.96
47	FREIGHT OPERATIONS INFORMATION SYSTEM (FOIS) - [220100009	03/1984	520.00 422.79	835.04	03/1995 -	03/2015	60.58
48	VIRAMGAM-BHILDI(WR),GC - [220100062	04/1990	155.66 -	548.01	- 03/2010	-	252.06
49	PEDAPALLI-KARIMNAGAR-NIZAMABAD NL(SCR) - [220100106	12/1994	124.43 -	925.30	- -	02/2014	643.63
50	AMRAVATI-NARKHER NL(CR) - [220100118	06/1994	663.01 175.30	725.00	06/1999 -	-	9.35
51	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133	03/1995	2,500.00 -	20,000.00	11/2002 -	12/2017	700.00
52	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135	04/1983	36.80 274.41	703.18	- -	-	1,810.82
53	DALLI-RAJHARA - RAOGHAT(PART OF DALLI-RAJHARA- JAGDALPUR),NL,RVNL - [220100149	04/1995	304.00 -	968.60	12/2012 -	-	218.62
54	CALICUT-MANGALORE (DL) (SR) - [220100151	02/1996	240.00 -	579.37	- -	02/2012	141.40
55	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	401.81 -	1,814.10	03/2004 -	03/2016	351.48
56	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181	02/1997	514.68 -	2,820.00	- -	-	447.91

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
57	HASSAN-BANGALORE VIA SHRAVANA-BELGOLA(NL),SWR [220100183]	02/1997	295.00 -	1,289.92	- -	-	337.26
58	GONDIA-JABALPUR(GC),(SECR) - [220100186]	02/1997	386.30 -	1,038.00	03/1998 -	-	168.70
59	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	37.68 -	1,036.78	07/2012 -	-	2,651.54
60	KARUR-SALEM(NL),SR - [220100191]	02/1997	155.55 -	800.00	- -	-	414.30
61	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	155.74 164.36	883.00	02/2009 -	03/2012	466.97
62	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	227.00 -	2,135.00	- -	-	840.53
63	KANPUR-KASGANJ-MATHURA(GC),NER - [220100197]	03/1997	677.97 1,062.36	1,651.54	- -	03/2015	143.60
64	BPUTRA BRIDGE AT BOGIBIL AND LINK LINES,NEFR - [220100201]	09/1997	1,500.00 -	4,996.19	04/2008 12/2011	12/2016	233.08
65	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	218.24 236.41	645.00	- -	12/2014	195.55
66	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	445.40	03/2007 03/2007	03/2015	13.20
67	RANCHI-LOHARDAGA(GC),SER - [220100214]	04/1997	194.07 -	596.40	06/2004 -	06/2015	207.31
68	MACHERLA-NALGONDA(NL)(SCR) - [220100220]	07/1998	125.00 -	480.00	07/2008 -	07/2008	284.00
69	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 -	1,630.97	05/2008 -	-	558.55
70	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	501.69 335.77	1,043.56	03/2012 -	-	108.01
71	AGRA-ETAWAH VIA FATEHABAD AND BAH (NL) NCR - [220100243]	04/1999	108.00 -	432.72	12/2009 -	12/2014	300.67
72	KATI HAR - JOGBANI (GC)(NEFR) - [220100247]	09/2001	492.98 -	1,022.64	12/2010 -	-	107.44
73	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	550.00 -	1,566.00	- -	-	184.73
74	GULBARGA-BIDAR,SCR(NL) - [220100254]	02/1998	242.42 369.70	844.00	- 05/2009	02/2015	248.16
75	GONDA-GORAKHPUR LOOP WITH ANAND NAGAR-NAUTANWA GC (NER) [220100255]	03/2002	863.23 -	1,072.51	- -	03/2015	24.24
76	JALANDHAR-PATHANKOT-JAMMU-TAWI (LD),NR - [220100258]	03/2002	625.30 408.76	847.75	06/2007 -	-	35.57
77	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	100.00 -	900.00	- -	-	800.00
78	QUILON-TIRUNELVELI-TENKASI-VIRUDHUNAGAR(SR)(GC) [220100263]	03/1998	280.00 -	1,122.00	- -	-	300.71
79	KOTLIPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	330.00 -	1,045.20	- -	-	216.73

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
80	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	04/2000	733.00 -	2,483.04	12/2008 -	03/2017	238.75
81	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	03/2000	1,049.69 -	3,176.10	12/2006 -	-	202.58
82	GADWAL - RAICHUR (NL), SCR - [220100270	04/1998	92.63 -	270.00	02/2011 -	-	191.48
83	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274	02/1999	138.00 -	1,382.78	- -	-	902.01
84	BANKURA - DAMODAR (GC) (SER) - [220100277	03/1998	111.90 -	1,423.98	03/2005 12/2008	-	1,172.55
85	JIND-SONEPAT (NL),NR - [220100280	01/2004	238.56 -	740.00	03/2012 -	12/2012	210.19
86	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	470.21 -	1,995.25	- -	-	324.33
87	HARIDASPUR-PARADEEP(NL) - [220100285	04/1996	301.64 -	1,185.64	- 09/2009	-	293.06
88	RAJATGARH-BARANG(LD),ECOR - [220100286	04/1999	166.16 -	288.00	02/2009 02/2009	08/2014	73.33
89	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	04/2003	727.56 -	5,996.00	03/2011 -	03/2018	724.12
90	KOSI BRIDGE (NL), ECR - [220100304	04/2002	322.95 -	341.41	03/2012 -	-	5.72
91	RAIL-CUM-ROAD BRIDGE AT MUNGER (NL), ECR - [220100307	04/2002	921.00 -	2,363.00	03/2009 -	12/2014	156.57
92	PATNA GANGA BRIDGE (NL), ECR - [220100308	04/2001	624.47 -	2,921.00	10/2007 -	12/2015	367.76
93	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	470.92 727.13	1,225.90	- -	-	160.32
94	RANGIA-MURKONGSELEK, (GC) ALONG WITH LINKED FINGERS NEFR - [220100315	01/2004	915.70 -	3,019.17	- -	03/2015	229.71
95	MAHARAJGANJ-MASRAKH (NL) - NER - [220100316	04/2003	218.19 -	472.00	- -	-	116.33
96	ETAWAH-MAINPURI (NL),NCR - [220100318	09/2001	120.00 -	245.39	12/2008 -	12/2014	104.49
97	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	585.93	- -	12/2013	52.67
98	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325	04/1998	183.23 -	818.29	02/2015 -	02/2015	346.59
99	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327	04/2000	133.41 207.00	276.00	03/2009 03/2009	08/2014	106.88
100	RAICHUR-GUNTAKAL(DL)(SCR) - [220100329	04/2003	136.62 -	289.93	12/2007 03/2010	-	112.22
101	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	332.92 283.95	477.88	03/2012 -	-	43.54
102	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032	04/2006	378.56 -	791.59	- -	-	109.11
103	GOELKERA-MANOHARPUR,(LD)(SER) - [N22000045	03/1997	261.70 -	280.00	02/2006 -	-	6.99

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
104	OBULAVARIPALLE-KRISHNAPATNAM(RVNL) - [N22000049]	07/2006	743.00 -	1,117.11	03/2008 06/2008	-	50.35
105	HARNOUT -SET.UP OF W/S TO UND. POH OF UP TO50 COAC. WS AND PU - [N22000052]	04/2003	98.74 -	337.30	-	03/2012	241.60
106	CHHAPRA-SETTING UP OF WHEEL MANUFACTURING PLANT - [N22000053]	03/2005	470.09 -	1,417.97	-	03/2012	201.64
107	SALKA ROAD -ANUPNAGAR LINE DOUBLING - [N22000075]	09/2006	324.90 -	385.54	03/2010 -	-	18.66
108	BHOPAL BINA 3D LINE DOUBLING - [N22000077]	09/2007	687.20 -	800.00	03/2010 -	12/2015	16.41
109	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]	09/2007	404.19 -	1,383.45	-	-	242.28
110	DINDIGUL-POLLACHI-PALGHAT-POLLACHI AND COIMBATORE - [N22000080]	09/2006	343.17 -	914.98	-	03/2015	166.63
111	ALUABARI ROAD SILIGURI JUNCTION VIA GALGALIA, NEFR - [N22000082]	12/2006	170.00 -	485.00	03/2011 -	-	185.29
112	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]	09/2006	125.00 -	420.00	-	-	236.00
113	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	456.00 -	820.00	-	-	79.82
114	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	200.00 -	430.33	-	03/2017	115.17
115	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	300.00 -	532.87	-	-	77.62
116	UTRATIA-ZAFRABAD, NR (LINE DOUBLING) - [N22000088]	04/2006	325.00 -	1,116.53	03/2010 -	03/2017	243.55
117	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]	04/2008	5,300.00 -	7,012.84	03/2014 -	03/2019	32.32
118	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	272.39	03/2012 -	03/2015	59.20
119	TAMLUK DIGHA,LINE DOUBLING (SER) - [N22000097]	03/1984	293.97 -	1,074.45	06/2005 -	-	265.50
120	AGARTALA SABROOM, NL, NEFR - [N22000099]	04/2008	813.34 -	1,741.00	03/2014 -	03/2017	114.06
121	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	619.34 -	2,393.48	04/2014 -	03/2020	286.46
122	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	282.92 -	359.86	-	-	27.20
123	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	3,375.42	12/2015 -	12/2015	151.99
124	RAMANAGRAM-MYSORE DOUBLING WITH ELECTRIFICATION OF KENGESII- MUSORE (SWR) - [N22000107]	04/2007	482.00 -	874.57	03/2013 -	03/2016	81.45
125	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2016	7.78
126	JAIPUR - RINGUS - CHURU AND SIKAR - LOHARU GUAGE CONVERSION (NWR) - [N22000113]	04/2008	653.19 -	653.46	03/2014 -	-	0.04

(August 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
127	DAKSHIN-BARASAL-LAKSHMIKANTAPUR - [N22000116]	04/2009	259.51 -	533.38	12/2011 -	-	105.53
128	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	603.04 -	1,421.25	03/2012 -	-	135.68
129	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24 -	321.62	03/2012 -	-	1.06
130	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	850.00 -	2,446.57	03/2015 -	03/2020	187.83
131	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]	04/2006	117.36 196.95	196.95	03/2011 -	-	67.82
132	KATAKHAL TO BHAIKABI - [N22000126]	04/1998	227.90 -	331.40	12/2012 -	03/2016	45.41
133	LUMDING-SILCHAR JIRIBAM, BADARPUR-BARAIGRAM KUMARGHAT NATIONAL PROJECT - [N22000127]	04/1996	1,676.31 -	5,185.44	03/2009 -	03/2016	209.34
134	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	494.92	- -	-	67.77
135	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 -	913.48	- -	-	184.87
136	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	446.00 -	685.17	- -	-	53.63
137	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	1,176.09 -	3,845.60	02/2020 -	02/2020	226.98
138	MAVLI JN.-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	456.00 -	855.16	- -	-	87.54
139	RATANGARH-SARDARSAHAR (MM OF SADULPUR-BIKANER AND RATANGARH-DEGANA GC) - [N22000153]	04/2010	739.65 -	872.22	- -	-	17.92
140	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	218.39	- -	-	2.34
141	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR & TANPUR-BANSI PAHARPUR - [N22000158]	04/2010	622.41 -	2,030.50	02/2019 -	02/2019	226.23
142	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	553.63 -	651.17	- -	-	17.62
143	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]	04/2010	149.90 -	184.91	03/2015 -	12/2016	23.36
144	DANGOAPOSI-RAJKHARSWAN 3RD LINE DOUBLING - [N22000164]	04/2010	309.44 -	388.67	12/2015 -	03/2016	25.60
145	SAKRI-HASANPUR ROAD (NL) - [N22000171]	04/1999	175.69 -	325.00	- -	-	84.98
146	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	285.07 -	378.56	- -	-	32.80
147	ATTIPPATTU-PUTTUR - [N22000184]	04/2008	446.87 -	528.00	- -	-	18.16
148	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,200.00	- -	-	129.22

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
149	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	1,500.00	- -	-	78.78
150	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	556.64	- -	-	180.17
151	CHENNAI BEACH-TAMBARAM-CHENGALPATTU SUBURBAN GC - [N22000188	04/1999	271.24 -	520.00	- -	-	91.71
152	VILLUPURAM-DINDIGUL WITH ELECTRIFICATION - [N22000189	04/2008	822.39 -	1,280.83	- -	-	55.74
153	KURUPPANTHARA-CHINGAVANAM - [N22000190	04/2007	270.14 -	346.15	- -	-	28.14
154	NEW BG LINE FROM DUDHNOI-MENDIPATAR - [N22000192	04/1999	175.43 -	247.75	- -	-	41.22
155	CONSTRUCTION OF NL FROM KUMARGHAT-AGARTALA - [N22000194	04/1999	895.00 -	1,242.25	03/2007 -	03/2016	38.80
156	ERODE-PALANI - [N22000199	04/2008	288.57 -	603.22	- -	-	109.04
157	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	450.00	- -	-	173.71
158	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	247.00 -	951.24	- -	03/2015	285.12
159	CHENGANNUR-CHINGAVANAM - [N22000203	04/2006	191.72 -	222.95	- -	-	16.29
160	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	165.82 -	545.64	- -	-	229.06
161	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON INCLUDING BR. LINE AND MM FOR CHALSA-NAXAL& RAJABHATKHOWA-JAI - [N22000209	04/1999	523.17 -	1,418.21	- -	-	171.08
162	LUMDING-HOJAI PATCH DOUBLING PROJECT - [N22000211	04/2012	246.07 -	364.06	- -	-	47.95
163	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213	04/2012	632.68 -	816.55	04/2012 -	03/2016	29.06
164	MADURAI-TUTICORIN VIA ARUPPUKKOTTAI - [N22000215	04/2011	601.43 -	800.00	- -	-	33.02
165	WARDHA-NANDED MAHARASHTRA - [N22000231	04/2008	499.30 -	2,501.05	- -	-	400.91
166	KALYAN-KASARA 3RD LINE - [N22000233	04/2011	277.70 -	279.70	- -	-	0.72
167	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247	04/2011	182.06 -	184.06	- -	-	1.10
168	PEN ROHA DOUBLING - [N22000254	04/2007	98.74 -	203.00	- -	03/2014	105.59
169	PANVEL PEN DOUBLING - [N22000255	04/2006	96.16 -	260.16	- -	-	170.55
170	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	913.00 -	1,801.01	- -	-	97.26
171	MUNIRABAD (GINGERA) -RAICHUR NL - [N22000257	04/2007	179.65 -	1,350.91	- -	-	651.97

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
172	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	377.93 -	986.30	- -	-	160.97
173	AKOLA-KHANDWA GC AKOLA-AKOT - [N22000263]	04/2008	184.26 -	2,000.00	- -	-	985.42
174	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	755.54	- -	-	163.25
175	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	1,046.88 -	2,966.99	- -	-	183.41
176	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]	04/2013	558.00 -	692.43	- -	-	24.09
177	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	-	57.65
178	SHIMOGA-HARIHAR NL - [N22000278]	04/2011	562.74 -	832.47	- -	-	47.93
179	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	970.34 -	1,743.00	- -	-	79.63
180	WHITE FIELD-KOLAR NL - [N22000280]	04/2011	341.05 -	348.85	- -	-	2.29
181	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	337.49 -	337.50	- -	-	0.00
182	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	329.97	- -	-	50.10
183	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	-	14.14
184	GADAG-WADI NL - [N22000299]	04/2013	1,117.00 -	1,922.00	- -	-	72.07
185	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]	04/2013	327.25 -	367.77	- -	-	12.38
186	QUILON-TIRUNELVELI - TRICHENDUR, TENKASI - [N22000303]	04/1999	460.94 -	1,030.00	01/1999 -	-	123.46
187	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	679.27 -	1,111.99	- -	-	63.70
188	JHARSUGUDA-RENGALI DOUBLING - [N22000317]	03/2006	201.00 -	201.17	- -	-	0.08
	Total		69,972.64 -	366,025.52			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
189	GANGA BRIDGE TO RAMDEVI CROSSING PH.II NH-25, KM.75-80.06 - [240106221]	12/2003	155.00 -	201.66	09/2008 -	12/2014	30.10
190	MAIBANG TO LUNDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	385.13	04/2009 -	03/2015	92.75
191	MAIBANG TO LUNDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	280.13	11/2008 -	09/2014	80.68
192	HARANGAJO TO MAIBANG, KM 164.08-190.587 NH-54 - [N24000061]	12/2003	212.00 -	386.10	09/2007 -	03/2015	82.12
193	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	363.74	07/2009 -	12/2014	85.58

(August 2014)

Date of Commissioning (Month/Year)							
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
194	CHAMBAL BRIDGE, NH-76 (RJ-5) - [N24000068]	12/2003	275.00 -	281.31	02/2010 -	07/2016	2.29
195	AGRA-BYPASS(NS-1/UP-1), NH-2,3 - [N24000098]	12/2003	348.16 -	465.50	09/2007 -	06/2015	33.70
196	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	03/2015	106.50
	Total		2,649.01 -	370,677.09			
	<u>SHIPPING AND PORTS</u>						
197	DEEPENING AND WIDENING OF MUMBAI HARBOUR CHANNEL AND JNPT CHANNEL [N25000003]	10/2005	800.00 -	1,571.60	10/2008 -	-	96.45
198	DEEPENING OF CHANNEL AT PARADIP PORT - [N25000004]	12/2005	154.84 -	253.36	- 01/2009	12/2010	63.63
199	CONST. & DEV. OF 2 OFFSHORE CONTAINER BERTHS & TERMINAL - [N25000016]	11/2007	1,228.00 -	2,158.16	12/2010 -	03/2015	75.75
200	ENNORE MANALI EXPRESS WAY,F/O SPECIAL PURPOSE VEHICLE (SPV) - [N25000035]	10/2002	150.00 -	600.00	03/2006 -	06/2014	300.00
201	CONSTRUCTION OF BERTHING AND ALLIED FACILITIES OFF TEKRA NEAR TUNA,KANDLA PORT TRUST [N25000037]	04/2005	882.00 -	1,060.00	02/2011 -	12/2012	20.18
202	CONSTRUCTION OF 13 & 14 CARGO BERTH AT KANDLA - [N25000039]	12/2005	702.00 -	755.50	03/2011 -	03/2013	7.62
203	ACQUISITION OF TWO(2) NOS. OF 317000 DWT VERY LARGE CRUDE CARRIERS FROM M/S JIANGSU RONGSHENG HEAVY - [N25000053]	10/2010	966.46 -	994.82	02/2014 -	01/2015	2.93
204	RAIL CONNECTIVITY TO ICTT AT VALLARPADAM AT COCHIN PORT TRUST [N25000059]	03/2007	245.67 -	373.22	04/2009 -	02/2011	51.92
	Total		5,128.97 -	378,443.75			
	<u>STEEL</u>						
205	EXPANSION OF LIQUID STEEL CAPACITY FROM 3MT TO 6.3MT (RINL) - [120100067]	10/2005	8,692.00 -	12,291.00	10/2009 -	12/2014	41.41
206	BAILADILA IRON ORE PROJECT DEPOSIT- 11B (NMDC) - [N12000018]	01/2007	295.89 -	607.17	12/2011 06/2010	03/2015	105.20
207	COKE OVEN BATTERY NO. 4 PHASE-II - [N12000038]	06/2006	108.00 -	216.68	09/2008 -	10/2014	100.63
208	EXPANSION OF IISCO STEEL PLANT - [N12000051]	06/2008	14,443.00 -	16,408.00	12/2011 -	12/2014	13.61
	Total		23,538.89 -	407,966.60			
	<u>TELECOMMUNICATIONS</u>						
209	GSM EQUIPMENT OF 283000 LINES (2G) AND 75000 LINES (3G) IN UTTARANCHAL [N26000058]	01/2009	149.15 -	158.72	06/2009 -	09/2014	6.42

(August 2014)

					Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8
	Total		149.15 -	408,125.32			
	<u>URBAN DEVELOPMENT</u>						
210	BANGALORE METRO RAIL PROJECT - [N28000008	05/2006	6,395.00 -	11,609.00	06/2011 -	03/2013	81.53
211	C/O OFFICE BUILDING FOR IDBI AT BANDRA KURLA COMPLEX,MUMBAI - [N28000048	11/2006	114.18 173.08	173.08	04/2009 -	-	51.59
	Total		6,509.18 -	419,907.40			
	<u>WATER RESOURCES</u>						
212	PAGLADIYA DAM PROJECT - [300100001	01/2001	542.90 -	1,187.00	12/2007 -	12/2012	118.64
	Total		542.90 -	421,094.40			
	Grand Total		237,942.45	3,247,748.53			
