

**430th FLASH REPORT ON
CENTRAL SECTOR PROJECTS
(Rs.150 crore and above)
August, 2021**



KUDANKULAM NUCLEAR POWER PROJECT UNIT-3



सत्यमेव जयते

Government of India
Ministry of Statistics and Programme Implementation
Infrastructure and Project Monitoring Division

Khurshid Lal Bhawan, Janpath
New Delhi-110001
Website: www.cspm.gov.in

Abbreviations used in the report

AAI	Airport Authority of India Ltd.
AERB	Atomic Energy Regulatory Board
AIBP	Accelerated Irrigation Benefit Programme
AIR	All India Radio
APW	Active Process Water
ATU	Atomic Treating Unit
BCM	Billion Cubic Meter
BHEL	Bharat Heavy Electricals Ltd.
BHPV	Bharat Heavy Plates & Vessel Ltd.
BLU	Boiler Light Up
BOLT	Build , Operate, Lease & Transfer
BPST	Bureau of Parliamentary Studies & Training
CCEA	Cabinet Committee on Economic Affairs
CCU	Catalytic Cracking Unit
CDS	Crude Distribution System
CDU	Crude Distillation Unit
CEA	Central Electricity Authority
CEC	Central Empowered Committee
CHP	Coal Handling Plant
CLW	Chittaranjan Locomotive Works
CMPDI	Central Mine Planning & Design Institute
COS	Committee of Secretaries
COR	Cost Overrun
CPP	Captive Power Plant
CRIS	Centre for Railway Information System
CRL	Cochin Refinery Ltd.
CSL	Cochin Shipyard Ltd.
CTU	Crude Topping Unit
DAE	Department of Atomic Energy
DB	Dumb Barges
DCME	Digital Circuit Multiplexing Equipment
DGMS	Director General Mines Safety
DHDS	Diesel Hydro Desulphurisation project
DOA	Date of Approval
DOC	Date of Commissioning
DOT	Department of Telecommunication
DVC	Damodar Valley Corporation
ECL	Eastern Coalfields Ltd.
EIL	Engineers India Ltd.
EMP	Environment Management Plan
EOT	Electrical Overhead Travelling crane
ESP	Electrostatic Precipitator
FCCU	Fluidised Catalytic Cracker Unit
ERP	Enterprise Resource Planning
FE	Foreign Exchange
FOIS	Freight Operation Information System
FPU	Feed Preparation Unit
GAIL	Gas Authority of India Ltd.
GC	Gauge Conversion
GDS	Gateway Digital Switch
GIS	Gas Insulated Station
GT	Gas Turbine
GTPP	Gas Turbine Power Plant
HCU	Hydro- cracker Unit
HEC	Heavy Engineering Corporation
HEMM	Heavy Equipment & Mining Machinery
HEP	Hydro Electric Project
HPCL	Hindustan Petroleum Corporation Ltd.
HRT	Head Race Tunnel
HSCL	Hindustan Steel Construction Ltd.
HVDC	High Voltage Direct Current
IAAI	International Airport Authority of India
ICT	Inter Connecting Transformer
IDC	Interest During construction
IFFCO	Indian Farmer Fertilizer Co-operative Ltd.
IMG	Inter Ministerial Group
IOC	Indian Oil Corporation Ltd.
IPCL	Indian Petrochemicals Ltd.
KV	Kilo Volts.
L&T	Larsen & Toubro

LEP	Life Extension Program
LOI	Letter of Intent
LPG	Liquified Petroleum Gas
LSTK	Lump sum Turnkey contract
MAMC	Minning & Allied Machinery Corporation.
MFL	Madras Fertilizer Ltd.
MGCL	Madras Gas Cracker Complex
MIS	Management Information System
MMSCMD	Million Metric Standard Cubic Meter day
MMT	Million Metric Tonnes
MOE&F	Ministry of Environment & Forest
MT	Metric Tonnes
MTY	Metric Tonne per year
MU	Million Unit
MW	Mega Watts
NAC	New Anticipated Cost
NALCO	National Aluminium Company
NBCC	National Building Construction Corporation.
NCL	Northern Coalfields Ltd
NEC	North East Council
NEEPCO	North-Eastern Electric Power Corporation Ltd.
NFL	National Fertilizer Ltd.
NH	National Highway
NHPC	National Hydro-Electric Power Corporation
NIRE	National Institute of Renewable Energy
NIT	Notice Inviting Tender
NJPC	Nathpa Jhakri Power Corporation Ltd.
NGN	Next Generation Network
NLC	Neyveli Lignite Corporation Ltd.
NMDC	National Mineral Development Corporation Ltd.
NPC	Nuclear Power Corporation Ltd.
NRL	Numaligarh Refinery Ltd.
OB	Over Burden
OC	Opencast
OECF	Overseas Economic Co-operation Fund
ONGC	Oil & Natural Gas Commission
OPGC	Orissa Power Generation Corporation
P & M	Plant & Machinery
PERT	Project Evaluation & Review Technique
PSTN	Public Switched Telephone Network
PHT	Primary Heat Transport
PIB	Public Investment Board
PSLW	Powered Support Longwall
QRC	Quick Roll Changer
RAPP	Rajasthan Atomic Power Plant
RCE	Revised Cost Estimates
RCF	Railway Coach Factory
ROB	Road Over Bridge
ROH	Regular Overhauling
RTU	Remote Terminal Unit
SAIL	Steel Authority of India Ltd.
SCI	Shipping Corporation of India Ltd.
SDH	Synchronous Digital Hierarchy
SG	Steam Generator
SP	Self Propelled
ST	Steam Turbine
STPS	Super Thermal Power Station
SUR	Sulphur Recovery Unit
SWSU	Sour Water Stripping Unit
TBM	Tunnel Boring Machine
TG	Turbo Generator
TPA	Tonnes Per Annum
TPS	Thermal Power Station
TOR	Time Overrun
TPY	Tonnes per year
UG	Under Ground
ULDCS	Unified Load Despatch & Communication Scheme
VDU	Vacuum Distillation Unit
WHRB	Waste Heat Recovery Boiler
WO_DOC	With out Date of Commissioning
WO_ODC	With out original Date of Commissioning

EXECUTIVE SUMMARY


1. The Flash Report for August 2021 contains information on the status of the 1718 Central Sector Infrastructure Projects costing ₹150 crore and above.

2. During the reference month, out of 1718 projects, 33 projects are added and 83 projects are completed. 560 projects are delayed with respect to their original schedules and 86 projects have reported additional delays vis-à-vis their date of completion reported in the previous month. Of these 86 projects, 34 are Mega Projects costing ₹1000 crore and above. The sectorwise break up is tabulated below:

(All the figures are in number)

S.No.	Sector	Projects on monitor	Delayed Projects w.r.t original schedule	Additional delayed during the month under report
1	ROAD TRANSPORT AND HIGHWAYS	878	148	30
2	RAILWAYS	312	145	12
3	PETROLEUM	148	81	10
4	COAL	108	59	5
5	POWER	76	42	16
6	WATER RESOURCES	47	8	0
7	URBAN DEVELOPMENT	30	16	5
8	HEALTH AND FAMILY WELFARE	29	10	3
9	DEPARTMENT OF HIGHER EDUCATION	26	8	1
10	CIVIL AVIATION	18	16	3
11	STEEL	9	6	0
12	HOME AFFAIRS	7	4	1
13	MINES	5	2	0
14	ATOMIC ENERGY	4	4	0
15	FERTILISERS	4	2	0
16	RURAL DEVELOPMENT	4	3	0
17	TELECOMMUNICATIONS	3	3	0
18	FINANCE	2	0	0
19	HEAVY INDUSTRY	2	0	0
20	DPIIT	2	1	0
21	SHIPPING AND PORTS	1	0	0
22	DEFENCE PRODUCTION	1	1	0
23	COMMERCE	1	0	0
24	DONER	1	1	0
		1718	560	86

3. Total original cost of implementation of the 1718 projects was ₹21,99,181.52 crore and their anticipated completion cost is likely to be ₹26,36,710.50 crore, which reflects overall cost overruns of ₹4,37,528.98 crore (19.90% of original cost). The expenditure incurred on these projects till August 2021 is ₹12,52,298.40 crore, which is 47.49% of the anticipated cost of the projects. The information can be viewed graphically as:

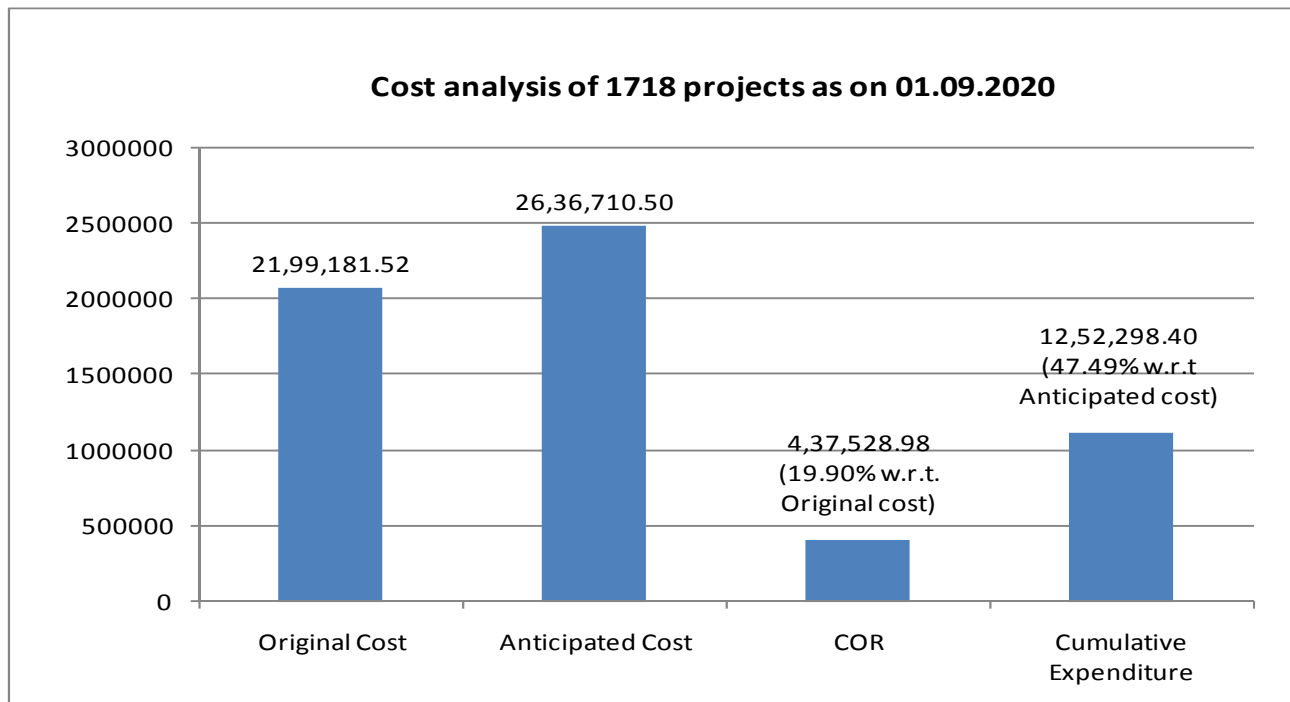


4. The sector-wise list of projects (maximum five in numbers) having maximum percentage of cost overruns and having maximum cost overruns in absolute term are at **Table A** and **Table B** respectively.

5. Out of the 1718 projects, 12 projects are ahead of schedule, 275 are on schedule, 560 are delayed, 470 projects reported cost overrun and 214 projects reported both time and cost overrun with respect to their original project implementation schedules. However, the number of delayed projects decreases to 373 if delay is calculated on the basis of latest schedule of completion. Further, for 871 projects neither the year of commissioning nor the tentative gestation period has been reported.


Status of projects (as on 01.09.2021)

(All the figures corresponds to number of project)

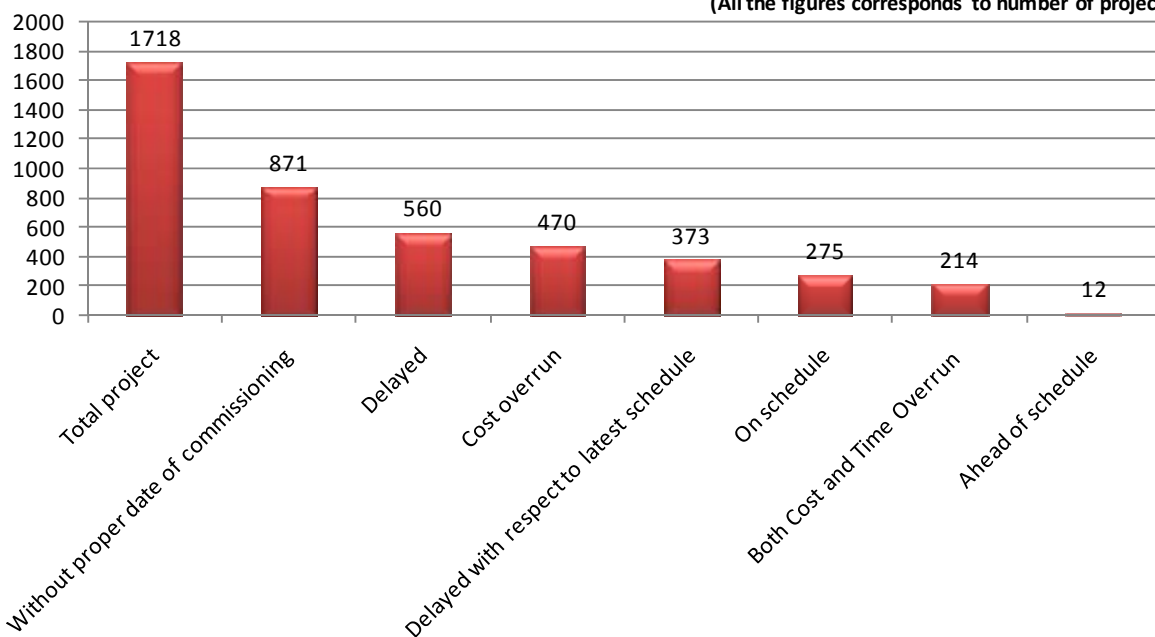


6. Out of 560 delayed projects, 96 (17.14%) projects have overall delay in the range of 1 to 12 months, 128 (22.86%) projects have delay in the range of 13 to 24 months, 210 (37.50%) projects have delay in the range of 25 to 60 months and 126 (22.50%) projects have delay of 61 months and above. The above information can be viewed graphically as shown below:

Break-up of 560 Delayed projects in August 2021

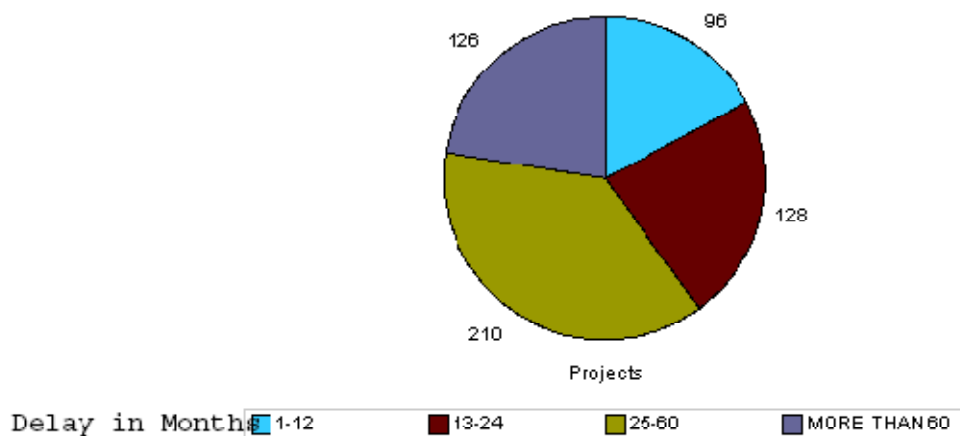

7. The status of online reporting of projects can be viewed month wise as:

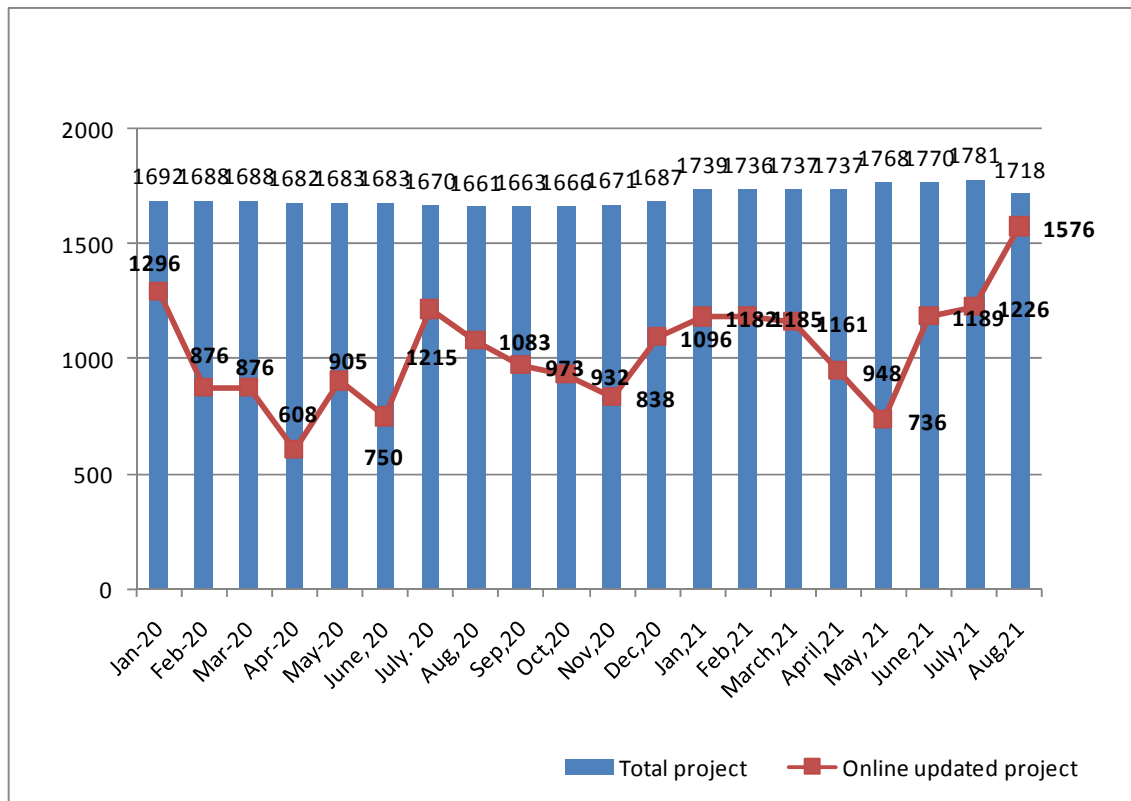

The average time overrun in these 560 delayed projects is 46.94 months. The sector wise list of projects (maximum five in numbers) having maximum time overruns (TOR) are at **Table-C**.

8. The brief reasons for time overruns as reported by various project implementing agencies are:

- Delay in land acquisition,
- Delay in obtaining forest/environment clearances,
- Lack of infrastructure support & linkages,
- Delay in tie-up of project financing,
- Delay in finalization of detailed engineering, change in scope,
- Delay in tendering,
- Delay in ordering & equipment supply,
- Law & order problems,
- Geological surprises,
- Pre-commissioning teething troubles and contractual issues.
- Contractual issues
- Inadequate manpower
- Delay in technical approval
- Encroachment
- State wise lockdown due to COVID 19

9. The Online Computerized Monitoring System (OCMS) of this Ministry envisages monitoring of milestones of the various infrastructure projects. The project authorities have been regularly requested to enter the list of milestones for each project, to facilitate better monitoring. However, not all the project agencies are reporting/providing the list of milestones. The sector wise list of earliest projects (maximum five in numbers) without milestones are at **Table-D**.

10. It has also been observed that project agencies are not reporting revised cost estimates and commissioning schedules for many projects, which suggests that time/cost overrun figures are under-reported. The sector wise list of earliest (oldest) projects (maximum five in numbers) without revised cost estimates are at **Table-E**.

11. The sector wise list of earliest projects (maximum five in numbers) without revised commissioning schedule are at **Table-F**.

12. Based on the above information, the concerned administrative Ministry may like to review the projects in order to avoid further cost overrun, time overruns, to firm-up milestones in case of milestone is not available, to firm-up revised cost estimates and revised commissioning schedule if the same has been not revised and lapsed.

13. This has the approval of Competent Authority, Ministry of Statistics and Programme Implementation.

Table- A

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Percentage of Cost Overruns
(as on 01-09-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (%)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	95.88
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	44.69
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	38.63
CIVIL AVIATION					
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	69.63
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	7.88
COAL					
7	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	201.44
8	BHANEGAON OC	02/2015	187.94	409.68	117.98
9	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	349.28	114.60
10	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	93.35
11	AMALGAMATED GONDEGAON GHATROHAN OC	02/2016	198.68	325.18	63.67
DEPARTMENT OF HIGHER EDUCATION					
12	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES	03/2021	127.26	188.88	48.42
13	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	29.31
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	10.22
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	1.85
16	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	0.57
DPIIT					
17	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9.80
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	8.49
HEALTH AND FAMILY WELFARE					
19	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	655.58	58.31
20	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	22.29
21	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	156.56	190.34	21.58
22	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	07/2016	152.95	177.92	16.33
23	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	15.92
HEAVY INDUSTRY					
24	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3727.30	116.96
HOME AFFAIRS					
25	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	132.80
26	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	64.04

27	NSG AT KOLKATA	10/2014	162.88	238.00	46.12
28	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF	06/2019	277.35	290.33	4.68
PETROLEUM					
29	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.34	132.23
30	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	117.11
31	LPG TERMINAL AT KOCHI	10/2015	607.06	1236.00	103.60
32	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	102.71
33	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	66.09
POWER					
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	218.08
35	TEHRI PUMPED STORAGE PLANT(1000MW)	07/2006	1657.00	4825.60	191.23
36	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	152.52
37	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	145.16
38	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	126.58
RAILWAYS					
39	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	3230.57
40	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	04/2011	120.70	2172.16	1699.64
41	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	1017.96
42	BIHTA-AURANGABAD (NL)	04/2008	326.20	2995.01	818.15
43	RAMGANJMUUNDI-BHOPAL (NL),WCR	04/2001	424.60	2909.99	585.35
ROAD TRANSPORT AND HIGHWAYS					
44	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	217.96	884.00	305.58
45	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	655.17	234.27
46	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	167.64	435.78	159.95
47	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	04/2013	151.59	369.92	144.03
48	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	612.58	118.78
RURAL DEVELOPMENT					
49	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	3.96
50	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	2.23
STEEL					
51	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	41.32
52	FORGED WHEEL PLANT	04/2014	1682.85	2100.00	24.79
TELECOMMUNICATIONS					
53	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	84.97
URBAN DEVELOPMENT					
54	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	44.39
55	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	25.89
56	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	20.00
57	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	18.69
58	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	16.25
WATER RESOURCES					
59	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	447.22
60	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	76.68
61	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	62.63
62	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	213.62	261.12	22.24
63	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	17.91

Table - B**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Cost Overruns (COR)****(as on 01-09-2021)**

SN	PROJECT	DOA	COST ORIGINAL (Rs. crore)	COST ANTICIPATED (Rs. crore)	COR (Rs.crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	16580.00	5121.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	17079.00	4759.00
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	3492.00	6840.00	3348.00
CIVIL AVIATION					
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	417.23	707.73	290.50
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	07/2018	346.27	480.33	134.06
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	1142.00	1232.00	90.00
COAL					
7	RANIGANJ MASTER PLAN	08/2009	2661.73	5146.48	2484.75
8	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	5907.11	7980.79	2073.68
9	JAGANNATHPOR OCP(3.00MTY)	09/2008	152.43	459.49	307.06
10	MAGADH EXPANSION OC(51 MTY)	08/2008	6964.33	7254.37	290.04
11	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	703.39	223.86
DEPARTMENT OF HIGHER EDUCATION					
12	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	141.94
13	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES	03/2021	127.26	188.88	61.62
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	02/2019	186.00	205.00	19.00
15	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	549.31	559.47	10.16
16	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	496.18	498.99	2.81
DPIIT					
17	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	1233.21
18	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	405.00
HEALTH AND FAMILY WELFARE					
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	03/2019	1577.00	1828.00	251.00
20	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	655.58	241.47
21	AIIMS BILASPUR	04/2018	1351.00	1471.00	120.00
22	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	585.00	79.42
23	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	250.00	45.56
HEAVY INDUSTRY					
24	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	04/2011	1718.00	3727.30	2009.30
HOME AFFAIRS					
25	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	1219.21	2000.00	780.79

26	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	151.74
27	NSG AT KOLKATA	10/2014	162.88	238.00	75.12
28	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF	06/2019	277.35	290.33	12.98
	PETROLEUM				
29	VISAKH REFINERY MODERNISATION PROJECT	07/2016	20928.00	26264.00	5336.00
30	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	2915.00	5909.00	2994.00
31	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	05/2016	4497.00	6025.00	1528.00
32	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	01/2015	1823.00	3027.90	1204.90
33	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	861.79	2001.34	1139.55
	POWER				
34	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	13707.10
35	BARH STPP(3X660MW) NTPC	02/2005	8692.97	21312.11	12619.14
36	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	3919.59	9897.59	5978.00
37	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	5353.00	10566.00	5213.00
38	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	4754.42	9129.32	4374.90
	RAILWAYS				
39	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	16592.00	51101.00	34509.00
40	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	2500.00	27949.00	25449.00
41	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	11589.00	28181.00	16592.00
42	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	09/1998	247.66	8248.50	8000.84
43	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	04/2003	4454.17	12264.15	7809.98
	ROAD TRANSPORT AND HIGHWAYS				
44	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	03/2016	1587.49	2982.00	1394.51
45	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	05/2009	1108.00	2288.00	1180.00
46	4 LANING FROM PHAGWARA TO RUPNAGAR	08/2016	1169.61	2280.00	1110.39
47	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	03/2018	1532.62	2499.00	966.38
48	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	1083.00	1827.15	744.15
	RURAL DEVELOPMENT				
49	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	149.73	155.66	5.93
50	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	202.61	207.12	4.51
	STEEL				
51	NMDC INTEGRATED STEEL PLANT	01/2010	15525.00	21940.00	6415.00
52	FORGED WHEEL PLANT	04/2014	1682.85	2100.00	417.15
	TELECOMMUNICATIONS				
53	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	11330.00
	URBAN DEVELOPMENT				
54	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	10270.00
55	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	26405.14	30695.12	4289.98
56	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	14600.00	18380.00	3780.00
57	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	10773.00	12787.00	2014.00
58	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	1036.35
	WATER RESOURCES				
59	POLAVARAM IRRIGATION PROJECT	02/2009	10151.04	55548.87	45397.83
60	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	173.13
61	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	254.13	413.29	159.16
62	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	370.40	430.49	60.09

63	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	50.14
----	---	---------	--------	--------	-------

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further cost overruns.

Table -C

**Sector-wise List of Projects (Maximum Five in Numbers) Having Maximum Time Overruns (TOR)
(as on 01-09-2021)**

SN	PROJECT	DOA	DOC ORIGINAL	DOC ANTICIPATED	TOR (IN MONTHS)
ATOMIC ENERGY					
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	09/2003	09/2010	10/2022	145
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016	03/2023	75
3	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	02/2022	74
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	03/2013	11/2020	11/2023	36
CIVIL AVIATION					
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	09/2018	06/2022	45
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	01/2016	03/2020	07/2022	28
7	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	08/2017	02/2020	05/2022	27
8	CCS INTERNATIONAL AIRPORT , LUCKNOW	06/2018	09/2021	12/2023	27
9	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	07/2018	09/2020	09/2022	24
COAL					
10	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	03/2010	03/2029	228
11	MAGADH EXPANSION OC(51 MTY)	08/2008	07/2012	03/2028	188
12	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	03/2013	03/2028	180
13	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	03/2017	03/2031	168
14	KARTALI (EAST) OCP (2.50 MTY)	07/2008	03/2014	03/2026	144
DEFENCE PRODUCTION					
15	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	02/2020	12/2021	22
DEPARTMENT OF HIGHER EDUCATION					
16	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	02/2016	06/2017	03/2022	57
17	PERMANENT CAMPUS FOR IIM BODH GAYA	09/2018	09/2020	11/2022	26
18	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	01/2018	05/2020	03/2022	22
19	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	07/2019	03/2021	06/2022	15
20	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	07/2019	03/2022	09/2022	6
DONER					
21	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	04/2014	09/2017	08/2021	47
DPIIT					
22	INDIA INTERNATIONAL CONVENTION AND	11/2017	12/2019	05/2022	29

	EXPO CENTRE				
	FERTILISERS				
23	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	01/2018	11/2019	10/2021	23
24	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	04/2018	04/2020	10/2021	18
	HEALTH AND FAMILY WELFARE				
25	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	11/2013	09/2021	94
26	NEIGRIHMS SHILLONG MEGHALYA	10/2016	05/2018	03/2022	46
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	08/2017	03/2019	09/2021	30
28	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	09/2017	03/2020	12/2021	21
29	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	03/2018	09/2020	04/2022	19
	HOME AFFAIRS				
30	NSG AT KOLKATA	10/2014	04/2018	12/2021	44
31	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019	03/2022	29
32	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI	05/2019	01/2022	06/2022	5
33	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF	06/2019	07/2022	10/2022	3
	MINES				
34	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	04/2021	03/2023	23
35	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	04/2021	12/2022	20
	PETROLEUM				
36	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	06/2009	12/2012	02/2022	110
37	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	03/2011	05/2013	02/2022	105
38	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	02/2017	08/2022	66
39	LPG TERMINAL AT KOCHI	10/2015	10/2017	03/2022	53
40	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	04/2018	05/2022	49
	POWER				
41	PARBATI HEP (4X200 MW) (NHPC) II	09/2002	09/2009	03/2023	162
42	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	09/2010	08/2023	155
43	BARH STPP(3X660MW) NTPC	02/2005	10/2011	07/2023	141
44	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	08/2008	06/2013	06/2024	132
45	BRBCL-NABINAGAR TPP- JV (4X250 MW)	01/2007	07/2012	10/2021	111
	RAILWAYS				
46	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	04/1998	03/2003	03/2030	324
47	MUNEERABAD-MAHABOBNAGAR(NL),SCR	04/1997	03/2000	03/2023	276
48	BANGLORE - SATYAMANGALAM (NL)(SWR)	04/1996	03/2002	03/2024	264
49	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	03/1995	11/2002	12/2022	241
50	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	04/2010	03/2005	03/2025	240
	ROAD TRANSPORT AND HIGHWAYS				
51	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	08/2010	10/2010	12/2021	134

52	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	08/2010	10/2010	12/2021	134
53	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	03/2011	12/2021	129
54	4-LANING OF BRAHAMPORE-FARAKA	02/2011	08/2013	06/2023	118
55	VARANASI-AURANGABAD KM.786 TO KM.978.40	09/2011	03/2014	12/2022	105
RURAL DEVELOPMENT					
56	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	03/2007	12/2015	02/2022	74
57	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016	09/2022	69
58	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016	03/2022	63
STEEL					
59	NMDC INTEGRATED STEEL PLANT	01/2010	05/2015	01/2022	80
60	NEW SINTER PLANT AT BOKARO STEEL PLANT	03/2015	10/2017	11/2022	61
61	COKE OVEN BATTERY-5	12/2011	12/2017	07/2022	55
62	FORGED WHEEL PLANT	04/2014	09/2018	09/2021	36
63	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	06/2019	10/2021	28
TELECOMMUNICATIONS					
64	NETWORK FOR SPECTRUM	03/2012	07/2015	03/2022	80
65	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	03/2018	12/2021	45
66	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	06/2021	11/2021	5
URBAN DEVELOPMENT					
67	BANGALORE METRO RAIL PROJECT PHASE-2	02/2014	02/2019	03/2025	73
68	DELHI MRTS PHASE-III	09/2011	03/2016	08/2021	65
69	AHMEDABAD METRO RAIL PROJECT PHASE 1	11/2014	12/2018	08/2022	44
70	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	03/2020	03/2023	36
71	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	06/2015	04/2019	02/2022	34
WATER RESOURCES					
72	POLAVARAM IRRIGATION PROJECT	02/2009	03/2020	04/2022	25
73	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	03/2017	12/2019	12/2021	24
74	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	05/2016	12/2021	12/2022	12
75	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	03/2019	07/2021	06/2022	11
76	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	05/2016	02/2022	12/2022	10

N.B.: The concerned administrative Ministry may like to review these Projects in order to avoid further time overruns.

Table – D

**Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Milestones
(as on 01-09-2021)**

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST ANTICIPATED (Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)	ORIGINAL DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
CIVIL AVIATION							
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	303.80	12 303.80	180.24	04/2020	03/2022

	COAL						
2	BARSINGSAR THERMAL POWER STATION EXTENSION	03/2015	2112.60	2112.60	93.05	09/2020	N.A.
3	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	513.63	513.63	175.30	12/2019	N.A.
4	BITHNOK LIGNITE THERMAL POWER STATION	03/2015	2196.30	2196.30	143.95	09/2020	N.A.
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	522.45	522.45	9.88	09/2019	N.A.
6	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	243.00	334.27	24.70	04/2018	06/2022
	COMMERCE						
7	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	302.64	302.64	30.00	10/2020	N.A.
	DEPARTMENT OF HIGHER EDUCATION						
8	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	484.32	626.26	0.00	09/2014	N.A.
9	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	171.72	171.72	53.94	03/2020	N.A.
10	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	01/2018	676.00	676.00	0.00	04/2023	04/2023
11	STUDY IN INDIA	03/2018	150.00	150.00	0.00	04/2018	N.A.
12	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	08/2018	418.00	418.00	110.00	03/2019	N.A.
	DPIIT						
13	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	12579.09	13812.30	9346.57	09/2019	07/2021
14	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	4773.00	5178.00	2744.03	12/2019	05/2022
	HEALTH AND FAMILY WELFARE						
15	LGBRIMH-TEZPUR, ASSAM	07/2012	175.57	175.57	163.37	12/2014	03/2018
16	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	655.58	561.94	11/2013	09/2021
17	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	07/2016	703.00	557.48	513.24	06/2020	10/2021
18	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	07/2016	785.00	715.06	574.62	04/2020	10/2021
19	CNCI KOLKATA WEST BENGAL	08/2016	244.00	248.00	224.92	09/2018	05/2019
	HEAVY INDUSTRY						
20	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	1554.00	900.00	815.00	09/2019	N.A.
	HOME AFFAIRS						
21	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	114.26	266.00	0.00	12/2013	N.A.
22	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI	05/2019	199.31	199.31	27.86	01/2022	06/2022
23	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF	06/2019	277.35	290.33	27.25	07/2022	10/2022
24	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E.	01/2020	166.98	13 166.98	0.00	10/2023	10/2023

	TYPE-						
25	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96	01/2020	166.98	166.98	0.29	05/2022	05/2022
	PETROLEUM						
26	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	678.00	1472.00	19.44	02/2017	08/2022
27	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	711.00	711.00	11.12	06/2020	N.A.
28	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	1112.00	1507.24	769.00	06/2019	02/2022
29	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	05/2016	261.00	261.00	176.30	01/2021	10/2021
30	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	05/2016	212.00	212.00	164.11	01/2021	09/2021
	POWER						
31	LOKTAK D/S HEP(NHPC)	12/1999	578.62	1311.05	155.41	06/2006	N.A.
32	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	09/2003	6285.33	19992.43	14059.55	09/2010	08/2023
33	PAKRI BARWADIH COAL MINING PROJECT	10/2004	4237.96	4552.00	3785.00	10/2017	N.A.
34	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	01/2014	374.63	374.63	252.99	04/2016	12/2021
35	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	8112.12	8112.12	2022.77	04/2020	07/2025
	RAILWAYS						
36	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	393.46	1026.00	182.49	03/2007	N.A.
37	NANGALDAM-TALWARA(NL),NR	03/1981	450.00	2200.00	0.00	07/2012	03/2024
38	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	297.32	614.00	275.06	03/2019	N.A.
39	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	04/1987	406.99	545.70	149.31	03/2006	03/2025
40	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	546.71	547.77	07/2014	N.A.
	ROAD TRANSPORT AND HIGHWAYS						
41	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	319.68	369.77	301.91	N.A.	N.A.
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	675.00	675.00	364.81	N.A.	N.A.
43	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	360.84	489.84	04/2010	07/2019
44	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	167.98	270.97	05/2008	06/2019
45	GWALIOR-JHANSI, NH-75	12/2003	604.00	364.59	332.18	12/2009	09/2020
	STEEL						
46	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	542.24	542.24	56.59	12/2023	12/2023
	TELECOMMUNICATIONS						

47	NETWORK FOR SPECTRUM	03/2012	13334.00	24664.00	17845.00	07/2015	03/2022
48	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	03/2020	431.16	422.87	0.00	06/2021	11/2021
URBAN DEVELOPMENT							
49	KOCHI METRO RAIL PROJECT	07/2012	5181.79	6218.14	6059.17	07/2017	N.A.
50	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	07/2013	23136.00	33406.00	18788.65	03/2020	03/2023
51	NAGPUR METRO RAIL	08/2014	8680.00	8680.00	8260.83	03/2018	12/2019
52	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	6928.00	6928.00	6928.00	03/2019	N.A.
53	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	1128.00	1128.00	28.50	03/2022	06/2023
WATER RESOURCES							
54	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	279.91	330.05	244.84	12/2019	01/2021
55	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	274.76	274.76	217.98	12/2019	N.A.
56	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	398.90	284.90	03/2020	03/2021
57	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	272.32	272.32	248.86	04/2020	03/2021
58	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	268.63	317.85	01/2021	N.A.

N.A.: Not Available.

FLASH REPORT

Table-E

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Cost Estimates (as on 01-09-2021)

SN	PROJECTS	DATE OF APPROVAL	COST ORIGINAL (Rs. Crore)	COST REVISED(Rs. Crore)	CUMULATIVE EXPENDITURE (Rs. Crore)
ATOMIC ENERGY					
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	11459.00	0.00	17041.00
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12320.00	0.00	13528.00
COAL					
3	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	479.53	0.00	703.39
4	RCE OF INDARAM OCP(1.20 MTPA)	07/2011	162.76	0.00	283.01
HEALTH AND FAMILY WELFARE					
5	LHMC NEW DELHI-RE-DEVELOPMENT	02/2013	414.11	0.00	561.94
6	AIIMS - MOTHER AND CHILD BLOCK	12/2013	204.44	0.00	249.24
7	AIIMS - OPD(NEW)	08/2014	293.65	0.00	299.76
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	505.58	0.00	586.96
9	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	168.90	0.00	169.51
PETROLEUM					
10	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	423.00	0.00	440.03
11	PIPELINE REPLACEMENT PROJECT (PRP-VI)	05/2019	763.92	0.00	791.46
POWER					

12	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	487.49	0.00	590.30
13	NAITWAR MORI HEP	10/2017	648.33	0.00	657.62
RAILWAYS					
14	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	332.15	0.00	547.77
15	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	02/1991	551.51	724.70	773.12
16	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	04/1991	329.39	0.00	1219.42
17	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	09/1995	303.98	0.00	704.89
18	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	02/1996	268.87	0.00	920.84
ROAD TRANSPORT AND HIGHWAYS					
19	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	280.00	0.00	612.58
20	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	160.00	0.00	270.97
21	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	217.61	0.00	489.84
22	NALBARI T BIJNI (AS-7)	12/2003	208.00	0.00	370.56
23	HARANGAJO TO MAIBANG, NH-54	12/2003	196.00	0.00	655.17
STEEL					
24	FORGED WHEEL PLANT	04/2014	1682.85	0.00	1704.90
URBAN DEVELOPMENT					
25	DELHI MRTS PHASE-III	09/2011	38585.00	0.00	39332.34
26	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	4264.00	0.00	4683.08
27	KOCHI METRO RAIL PROJECT	07/2012	5181.79	0.00	6059.17
WATER RESOURCES					
28	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	225.77	0.00	284.90
29	SAIDPUR SEWER NETWORK PATNA	04/2015	268.63	0.00	317.85

N.B.: The concerned administrative Ministry may like to review these Projects in order to firm-up revised cost estimates.

Table-F

Sector-wise List of Earliest (oldest) Projects (Maximum Five in Numbers) Without Revised Commissioning Schedule (as on 01-09-2021)

SN	SECTOR/ PROJECT	DATE OF APPROVAL	ORIGINAL DATE OF COMMISSIONING	REVISED DATE OF COMMISSIONING	ANTICIPATED DATE OF COMMISSIONING
COAL					
1	ANANTA OC EXPANSION PH-III (15.0 MTY)	08/2008	03/2012	N.A.	03/2021
2	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	06/2011	12/2015	N.A.	02/2021
3	PATHERDIH NLW WASHERY	10/2012	04/2014	N.A.	04/2020
4	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	03/2015	09/2019	N.A.	N.A.
5	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	03/2015	12/2019	N.A.	N.A.
COMMERCE					
6	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI	06/2018	10/2020	N.A.	N.A.
DEPARTMENT OF HIGHER EDUCATION					
7	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	01/2010	10/2012	N.A.	N.A.
8	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	09/2012	03/2016	N.A.	N.A.
9	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014 ¹⁶	N.A.	N.A.

10	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	09/2013	09/2014	N.A.	N.A.
11	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	07/2019	N.A.	N.A.
DPIIT					
12	DELHI MUMBAI INDUSTRIAL CORRIDOR	09/2011	09/2019	01/2014	07/2021
FERTILISERS					
13	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	01/2018	11/2019	05/2021	04/2021
14	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	01/2018	11/2019	05/2021	04/2021
FINANCE					
15	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019	N.A.	07/2021
HEALTH AND FAMILY WELFARE					
16	LGBRIMH-TEZPUR, ASSAM	07/2012	12/2014	N.A.	03/2018
17	AIIMS - MOTHER AND CHILD BLOCK	12/2013	05/2017	N.A.	03/2021
18	AIIMS - OPD(NEW)	08/2014	05/2017	N.A.	01/2020
19	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	09/2014	03/2018	N.A.	09/2019
20	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	05/2017	N.A.	07/2019
HEAVY INDUSTRY					
21	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	04/2011	09/2011	03/2021	03/2021
22	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	08/2016	09/2019	N.A.	N.A.
HOME AFFAIRS					
23	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013	N.A.	N.A.
MINES					
24	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020	N.A.	02/2021
25	UTKAL D AND E COAL BLOCK	05/2016	01/2020	N.A.	N.A.
PETROLEUM					
26	ENNORE-TRICHY-MADURAI LPG PIPELINE	05/2013	06/2020	N.A.	N.A.
27	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	06/2016	08/2019	06/2021	05/2021
28	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	02/2017	05/2021	05/2021	05/2021
29	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	08/2017	04/2021	03/2021	03/2021
30	BS-VI PROJECTS	09/2017	12/2019	N.A.	N.A.
POWER					
31	LOKTAK D/S HEP(NHPC)	12/1999	06/2006	N.A.	N.A.
32	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017	N.A.	N.A.
33	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012	N.A.	N.A.
34	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	06/2014	N.A.	N.A.
35	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	07/2012	08/2017	N.A.	N.A.
RAILWAYS					
36	HOWRAH-AMTA-CHAMPADANGA NL (SER)	04/1974	03/2007	03/2007	N.A.

37	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	04/1983	03/2019	N.A.	N.A.
38	MUZAFFARPUR-SITAMARHI NEW LINE	01/1991	07/2014	N.A.	N.A.
39	NANDYAL-YERRAGUNTALA(NL),SCR	03/1996	02/2009	N.A.	N.A.
40	HARIDASPUR-PARADEEP(NL)	04/1996	12/2017	N.A.	N.A.
ROAD TRANSPORT AND HIGHWAYS					
41	FOUR LANING OF BHOJPUR TO BUXAR	01/1991	N.A.	N.A.	N.A.
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	01/1991	N.A.	N.A.	N.A.
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	01/1991	N.A.	N.A.	N.A.
44	SONAPUR TO GUWAHTI (AS-3)	12/2003	03/2008	N.A.	08/2020
45	NALBARI T BIJNI (AS-7)	12/2003	04/2008	N.A.	02/2021
URBAN DEVELOPMENT					
46	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	07/2021	N.A.	N.A.
47	CHENNAI METRO RAIL LTD (PHASE 1)	02/2009	12/2015	N.A.	N.A.
48	REDEVELOPMENT OF EAST KIDWAI NAGAR	06/2012	11/2019	N.A.	N.A.
49	KOCHI METRO RAIL PROJECT	07/2012	07/2017	09/2020	N.A.
50	NAGPUR METRO RAIL	08/2014	03/2018	N.A.	12/2019
51	LUCKNOW METRO RAIL CORPORATION LTD	01/2016	03/2019	N.A.	N.A.
WATER RESOURCES					
52	IRRIGATION WORK OF BAGMATI	10/2005	03/2015	N.A.	N.A.
53	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	02/2011	12/2019	N.A.	01/2021
54	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	02/2014	12/2019	05/2021	N.A.
55	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	03/2020	N.A.	03/2021
56	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	04/2020	N.A.	03/2021

N.A.: Not Available.

TABLE-1

EXECUTIVE SUMMARY COSTING Rs. 150 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	ROAD TRANSPORT AND HIGHWAYS	878	30
2	RAILWAYS	312	12
3	PETROLEUM	148	10
4	COAL	108	5
5	POWER	76	16
6	WATER RESOURCES	47	0
7	URBAN DEVELOPMENT	30	5
8	HEALTH AND FAMILY WELFARE	29	3
9	DEPARTMENT OF HIGHER EDUCATION	26	1
10	CIVIL AVIATION	18	3
11	STEEL	9	0
12	HOME AFFAIRS	7	1
13	MINES	5	0
14	ATOMIC ENERGY	4	0
15	FERTILISERS	4	0
16	RURAL DEVELOPMENT	4	0
17	TELECOMMUNICATIONS	3	0
18	FINANCE	2	0
19	HEAVY INDUSTRY	2	0
20	DPIIT	2	0
21	SHIPPING AND PORTS	1	0
22	DEFENCE PRODUCTION	1	0
23	COMMERCE	1	0
24	DONER	1	0
	Total	1718	86

TABLE-2

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	May,2021			
	<u>PETROLEUM</u>			
1	MMPL PIPELINE REROUTING PROJECT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000261]	449.58	12/2019	396.13
2	PUNE POL STORAGE DEPOT (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000313]	282.64	08/2020	194.26
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
3	4-LANNING OF PUNJAB HARYANA BORDER-JIND SECTION OF NH-71 FROM KM 238.695 TO KM 307.00 ON DBFOT TOLL (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000664]	639.79	03/2020	597.77
4	REHABILITATION AND UPGRADATION OF NH67 FROM KM 424.650 TO 487.693 OF GOOTY-TADIPATRI SECTION TO TWO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000930]	378.24	01/2018	315.42
5	REHABILITATION & UPGRADATION OF NH-67 FROM KM 641.000 TO KM 695.000 (DORNALA T JUNCTION TO ATMAKUR S (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001183]	251.55	02/2015	7.74
	June,2021			
	<u>PETROLEUM</u>			
6	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
7	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	<u>WATER RESOURCES</u>			
8	SEWAGE TREATMENT PLANT AT JAGJEETPUR AND SARAI (Uttarakhand Pey Jal Nigam) - [N30000003]	273.37	08/2019	84.55
9	SAIDPUR STP AND ADJOINING NETWORK FOR PATNA BIHAR (Bihar Urban Infrastructure Development Corporation Ltd) - [N300000038]	184.93	04/2020	163.36
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
10	REHABILITATION AND UPGRADATION OF NH-111 FROM KM. 82.500 TO 163.400 (KATHGHORA TO SHIVNAGAR SECTION EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000287]	485.44	12/2015	447.13

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
11	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM. 37.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000617]	198.00	10/2016	184.62
12	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 127.500 TO 178.944 DARRIGHAT TO BANARI SECTION (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001220]	491.52	09/2016	474.76
	August,2021			
	<u>PETROLEUM</u>			
13	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN (OIL INDIA LIMITED) - [N16000167]	352.56	03/2017	455.00
14	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
15	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000312]	255.00	11/2020	275.68
	<u>POWER</u>			
16	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
17	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
18	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
19	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
20	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
21	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
22	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
23	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000273]	587.44	09/2020	463.48
24	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP (NATIONAL THERMAL POWER CORPORATION) - [N18000274]	349.00	11/2020	313.00
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
25	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDAPAR BRIDGE EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000251]	297.00	04/2018	290.64
26	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000276]	156.26	-	141.35

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
27	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000294]	269.22	01/2015	33.24
28	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000295]	257.09	01/2015	14.18
29	REHABILITATION AND UPGRADING TO 2 LNES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000297]	376.52	04/2014	171.16
30	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000298]	383.40	03/2015	244.68
31	TWO LANING OF GOBOK - SIJON NALLAH (CORRECSPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000311]	207.03	05/2012	308.09
32	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON-EPC MO EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000317]	157.18	07/2015	148.24
33	CONSTRUCTION OF PAVED SHOULDERS INCULDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000318]	154.14	08/2015	142.06
34	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000333]	621.43	06/2018	387.22
35	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000371]	445.89	03/2017	464.05
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000376]	219.40	01/2018	0.10
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000379]	218.63	10/2017	29.27
38	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000385]	766.36	-	685.36
39	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000388]	497.05	05/2017	754.27
40	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000389]	847.02	-	795.00
41	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000397]	322.00	03/2018	56.41

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
42	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG ITEM RATE(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000402]	358.22	10/2016	339.86
43	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000414]	229.41	05/2018	6.65
44	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA-PITRI JUNCTION) IN TH EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000417]	342.05	01/2017	258.91
45	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000467]	511.00	10/2013	2,323.04
46	NH 79 CHITTORGARH NEEMUCH MP BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING BOT (TOLL)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000470]	511.00	10/2013	492.00
47	FOUR LANING OF CHANDIGARH - KHARAR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000503]	447.29	12/2017	346.39
48	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000523]	159.39	11/2017	210.29
49	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA EPC(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000524]	892.17	-	648.44
50	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000537]	278.39	08/2014	22.18
51	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08
52	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEMETRIC IMPR (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000580]	206.80	07/2016	74.04
53	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000581]	288.24	11/2015	287.37
54	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000608]	248.97	05/2019	270.65
55	CONSTRUCTION OF FLYOVER/UNDERPASS FOR IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000625]	1,004.67	05/2019	577.21
56	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000640]	326.63	04/2018	249.26
57	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000641]	239.91	10/2017	147.25
58	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000644]	342.05	01/2017	258.91

Month wise List of Completed Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
59	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000646]	157.30	06/2018	97.29
60	FOUR LANING OF DELINKED STRETCH OF SEONI – MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000727]	960.24	-	738.74
61	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000871]	600.87	11/2017	682.36
62	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000873]	823.20	11/2017	807.99
63	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000878]	235.91	02/2018	176.23
64	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000879]	202.69	11/2019	148.21
65	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000884]	191.21	11/2019	127.13
66	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000895]	287.34	01/2019	194.85
67	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000905]	322.48	07/2020	291.93
68	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000906]	173.24	06/2020	56.66
69	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000908]	276.01	03/2019	187.39
70	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26. (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000911]	165.06	12/2016	92.59
71	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000936]	244.95	08/2018	136.22
72	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 ((MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000938]	297.12	07/2018	373.98
73	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000942]	208.50	11/2019	165.82
74	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000962]	178.23	09/2018	122.99
75	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000999]	230.34	10/2019	201.82

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
76	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001001]	199.98	08/2016	163.16
77	MAJALGAON TO KAIJ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001036]	413.99	07/2019	299.72
78	AKKALKOT TO DHUDHNI (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001120]	211.42	02/2019	131.85
79	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001131]	212.99	06/2020	156.72
80	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001139]	218.94	03/2020	120.69
81	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001143]	176.94	10/2018	141.11
82	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2- (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001147]	239.63	02/2019	212.53
83	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001148]	599.34	01/2020	492.15
84	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001153]	197.37	02/2014	89.36
85	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001155]	175.20	01/2017	142.48
86	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8 (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24001184]	269.69	09/2019	0.01
87	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001202]	388.83	12/2019	304.70
88	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001205]	209.10	10/2019	201.70
89	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001223]	179.89	03/2013	242.23
90	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001225]	169.26	01/2019	270.11
91	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001237]	162.72	09/2016	136.59
92	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/ (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001238]	307.70	01/2017	313.06
	URBAN DEVELOPMENT			

Month wise List of Completed Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
93	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000079]	884.30	12/2015	874.29
94	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000123]	218.72	11/2020	175.63
	<u>DEPARTMENT OF HIGHER EDUCATION</u>			
95	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB (CENTRAL PUBLIC WORKS DEPARTMENT) - [N28000102]	294.00	04/2019	289.13

FLASH REPORT

TABLE-3

Month wise List of Deleted Projects Costing Rs. 150 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	FOUR LANING FROM BISWANATH CHARIALI TO GOHPUR FROM KM 208 TO KM 264.10 OF NH-52 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000321]	829.00	01/2019	350.14
2	4 LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000430]	223.30	06/2018	111.16
3	FUNDED) CONSTRUCTION OF 2-LANE HUNLI-ANINI ROAD FROM KM 53.500 TO KM 92.500 IN THE STATE OF ARUNACH(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000618]	434.06	-	306.05
4	CONSTRUCTION OF 2-LANE OF HUNLI-ANINI ROAD FROM KM. 106.20 TO KM. 120 (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000676]	138.93	01/2017	124.76
5	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
6	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. (NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000681]	194.66	04/2017	117.61
7	CONSTRUCTION OF FOUR/ SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.683(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000689]	507.68	04/2017	129.13
8	CONSTRUCTION/UPGRADATION OF ALTERNATIVE HIGHWA TO GANGTOK IN SIKKIM VIA BAGRAKOT-CHUIKHIM-NIMBONG-KA(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000766]	318.42	11/2017	66.63
	August,2021			
9	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
10	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000274]	333.21	12/2015	256.11
11	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000296]	278.87	05/2014	0.00
12	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000302]	333.21	12/2015	256.11

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
13	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000307]	156.63	02/2012	0.00
14	TWO LANING OF LALPUL- MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000309]	305.49	03/2011	131.08
15	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
16	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000335]	159.12	11/2015	0.00
17	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000373]	305.49	03/2017	0.00
18	SATANA-BELA SECTION OF NH-75(4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000375]	320.48	08/2015	189.49
19	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000395]	257.80	-	12.38
20	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAFLONG JATINGA ROAD (L=7.46 KM.) BASKA BAR(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000396]	470.20	02/2011	569.40
21	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000398]	282.41	08/2016	327.21
22	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
23	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000407]	333.21	11/2015	256.11
24	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
25	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00
26	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000519]	478.35	-	516.69
27	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000530]	154.62	-	0.00
28	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000575]	665.50	07/2016	0.00

Month wise List of Deleted Projects Costing Rs. 150 crore and above during

2021-2022

Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
29	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000577]	369.77	06/2016	0.00
30	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000927]	293.64	08/2020	28.24
31	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001144]	445.89	03/2017	469.64
32	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001145]	164.54	08/2015	141.33
33	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001154]	367.44	01/2017	61.95
34	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001167]	165.67	01/2016	87.63
35	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001170]	471.16	08/2014	201.64
36	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24001230]	281.45	12/2020	112.70

TABLE-4

Projects Added / Completed / Dropped / Frozen Rs. 150 Crore and above

No of Projects in Previous Month	1781
No of Projects Completed/Dropped/Frozen in Current Month	112
No of Projects Elevated in Current Month	16
No of Projects added in Current Month	33
No of Projects in Current Month	1718

Project status Rs. 150 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	560 (32.60%)	12 (.70%)	275 (16.01%)	99 (5.76%)	772 (44.94%)	1718
Latest Approved (Date)	373 (21.71%)	19 (1.11%)	480 (27.94%)	74 (4.31%)	772 (44.94%)	1718

Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	1409	17,05,941.40	18,56,666.43	7,94,651.34	42.80	1,50,725.03	8.80
Project with Revision in Cost	309	7,63,229.74	7,80,044.07	4,57,647.06	58.70	16,814.33	2.20
Total	1,718	24,69,171.14	26,36,710.50	12,52,298.40	47.49	1,67,539.36	6.79
Original Cost of All Projects							
Original Cost	1,718	21,99,181.52	26,36,710.50	12,52,298.40	47.49	4,37,528.98	19.90

Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	560	9,42,586.32	12,32,995.82	6,99,753.08	56.80	2,90,409.50	30.81
Latest Approved (RCE)	373	7,13,746.99	7,99,235.36	4,47,220.05	56.00	85,488.37	11.98

Additional Delayed Project cost Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	86	2,05,470.84	2,18,411.44	1,35,589.95	62.10	12,940.60	6.30
Total	86	2,05,470.84	2,18,411.44	1,35,589.95	62.08	12,940.60	6.30

TABLE-5

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 150 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	18	13,348.06	13,862.62	3.85	3	1,905.50	2,420.06	27.00
3	COAL	108	1,48,672.06	1,54,186.72	3.71	22	38,833.49	45,248.40	16.52
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0.00
7	STEEL	9	25,452.51	32,284.66	26.84	2	17,207.85	24,040.00	39.70
8	PETROLEUM	148	3,36,760.67	3,43,338.97	1.95	28	58,421.67	76,792.19	31.44
9	POWER	76	2,29,308.93	2,91,506.86	27.12	29	1,12,524.61	1,76,835.90	57.15
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	1	1,718.00	3,727.30	116.96
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,784.86	3.35	12	5,589.39	6,443.65	15.28
12	RAILWAYS	312	4,62,095.03	7,04,966.85	52.56	219	2,40,281.10	4,94,845.91	105.94
13	ROAD TRANSPORT AND HIGHWAYS	878	5,29,993.60	5,46,560.65	3.13	120	87,014.84	1,09,020.49	25.29
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	1	13,334.00	24,664.00	84.97
16	URBAN DEVELOPMENT	30	2,81,283.00	3,03,630.26	7.94	8	97,923.03	1,20,349.49	22.90
17	WATER RESOURCES	47	26,322.76	71,923.93	173.24	9	12,606.87	58,532.15	364.29
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	26	10,910.66	11,104.02	1.77	5	1,843.07	2,078.60	12.78
21	HOME AFFAIRS	7	2,306.97	3,327.60	44.24	4	1,773.70	2,794.33	57.54

Extent of cost overrun in projects with respect to original cost (Sector Wise)						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	2.96
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
Total		1718	21,99,181.52	26,36,710.50	19.90	470	7,35,952.55	12,07,644.55	64.09

^ - Cost Overrun = Anticipated Cost minus Original Cost

FLASH REPORT

TABLE-6

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Antici pated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	74	1,24,241.29	1,72,051.82	38.48	15	46,946.11	1,03,678.64	120.85
2	ARUNACHAL PRADESH	41	22,951.00	37,016.20	61.28	6	9,255.14	23,320.34	151.97
3	ASSAM	53	49,175.61	53,790.59	9.38	17	8,013.42	12,853.01	60.39
4	BIHAR	103	1,24,613.06	1,61,188.44	29.35	36	55,279.68	93,610.38	69.34
5	GOA	10	5,332.77	5,343.26	0.20	2	529.17	539.66	1.98
6	GUJARAT	61	1,07,586.79	1,18,636.40	10.27	18	34,707.66	46,736.36	34.66
7	HARYANA	39	62,518.91	64,850.78	3.73	7	3,823.83	6,288.07	64.44
8	HIMACHAL PRADESH	19	21,918.19	31,802.62	45.10	3	8,237.58	18,122.01	119.99
9	JAMMU AND KASHMIR	26	45,784.09	71,711.34	56.63	3	6,236.00	32,296.00	417.90
10	KARNATAKA	56	70,450.03	82,675.13	17.35	20	46,700.32	59,259.15	26.89
11	KERALA	23	34,828.89	39,970.99	14.76	12	18,147.21	23,289.33	28.34
12	MADHYA PRADESH	76	67,158.93	76,531.18	13.96	17	14,110.50	24,478.41	73.48
13	MAHARASHTRA	239	2,03,714.25	2,25,925.96	10.90	37	63,040.14	90,528.34	43.60
14	MANIPUR	19	9,640.91	18,089.68	87.63	2	5,032.79	13,575.20	169.74
15	MEGHALAYA	13	5,269.68	8,588.18	62.97	2	1,390.78	4,709.28	238.61
16	MIZORAM	23	11,751.40	15,700.10	33.60	5	3,593.57	7,542.27	109.88
17	NAGALAND	36	16,462.29	21,094.41	28.14	3	3,035.84	7,667.96	152.58
18	ODISHA	80	1,15,673.21	1,20,106.58	3.83	19	17,958.65	26,630.02	48.29
19	PUNJAB	21	11,288.85	12,858.74	13.91	6	4,559.90	6,549.20	43.63
20	RAJASTHAN	54	51,369.15	59,216.94	15.28	12	18,745.78	26,641.89	42.12
21	SIKKIM	21	7,778.98	15,698.13	101.80	5	2,227.62	10,146.77	355.50
22	TAMIL NADU	70	1,23,008.14	1,42,839.68	16.12	23	39,766.24	61,349.00	54.27
23	TRIPURA	21	5,174.00	5,395.32	4.28	4	1,119.64	1,340.96	19.77
24	UTTAR PRADESH	119	1,53,485.51	1,57,906.11	2.88	31	38,440.22	45,680.61	18.84
25	WEST BENGAL	72	63,906.08	82,743.75	29.48	30	29,474.39	48,653.92	65.07
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	44.38
27	DELHI	33	89,350.41	90,970.21	1.81	11	12,251.98	14,604.98	19.21
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	0.00
29	CHHATISGARH	46	78,872.08	89,155.66	13.04	11	27,653.71	38,056.64	37.62
30	JHARKHAND	41	68,724.52	73,429.78	6.85	14	30,065.79	36,327.05	20.83
31	UTTARAKHAND	32	35,922.92	50,877.81	41.63	11	27,061.50	42,042.89	55.36
32	TELANGANA	49	37,249.74	40,283.18	8.14	10	15,929.81	19,457.47	22.15
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	38.72
34	MULTI STATE	130	3,68,262.98	4,84,139.25	31.47	75	1,41,616.28	2,60,242.68	83.77
Total		1718	21,99,181.52	26,36,710.50	19.90	470	7,35,952.55	12,07,644.55	64.09

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-7

Extent of time overrun in projects with respect to original schedule Rs. 150 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	18	13,348.06	13,862.62	3.85	16	12,382.65	12,897.21	4 - 45
3	COAL	108	1,48,672.06	1,54,186.72	3.71	59	76,414.36	79,515.85	12 - 228
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	4	1,101.28	1,101.28	0.00	2	642.64	642.64	18 - 23
6	MINES	5	7,078.62	7,075.17	-0.05	2	6,023.00	6,023.00	20 - 23
7	STEEL	9	25,452.51	32,284.66	26.84	6	21,626.09	28,458.24	11 - 80
8	PETROLEUM	148	3,36,760.67	3,43,338.97	1.95	81	1,42,945.11	1,50,114.24	2 - 110
9	POWER	76	2,29,308.93	2,91,506.86	27.12	42	1,66,780.39	2,23,457.09	4 - 162
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,784.86	3.35	10	5,452.54	5,471.35	9 - 94
12	RAILWAYS	312	4,62,095.03	7,04,966.85	52.56	145	1,94,023.99	3,21,095.00	2 - 324
13	ROAD TRANSPORT AND HIGHWAYS	878	5,29,993.60	5,46,560.65	3.13	148	76,444.06	77,862.28	8 - 134
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	3	14,013.36	25,335.07	5 - 80
16	URBAN DEVELOPMENT	30	2,81,283.00	3,03,630.26	7.94	16	1,34,730.10	1,51,244.55	8 - 73
17	WATER RESOURCES	47	26,322.76	71,923.93	173.24	8	11,797.25	57,131.86	4 - 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	1	246.31	210.00	22 - 22
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	26	10,910.66	11,104.02	1.77	8	4,633.56	4,594.20	3 - 57
21	HOME AFFAIRS	7	2,306.97	3,327.60	44.24	4	1,858.75	2,727.64	3 - 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	3	527.83	538.27	63 - 74
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
24	DONER	1	151.33	151.33	0.00	1	151.33	151.33	47 - 47
Total		1718	21,99,181.52	26,36,710.50	19.90	560	9,42,586.32	12,32,995.82	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-8

Extent of time overrun in projects with respect to original schedule(State Wise)						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,24,241.29	1,72,051.82	38.48	31	87,104.21	1,32,475.32	4 - 180
2	ARUNACHAL PRADESH	41	22,951.00	37,016.20	61.28	5	7,166.23	21,044.67	59 - 155
3	ASSAM	53	49,175.61	53,790.59	9.38	20	11,294.28	13,941.30	12 - 74
4	BIHAR	103	1,24,613.06	1,61,188.44	29.35	20	37,522.17	63,524.19	4 - 141
5	GOA	10	5,332.77	5,343.26	0.20	0	0.00	0.00	-
6	GUJARAT	61	1,07,586.79	1,18,636.40	10.27	15	31,799.51	42,151.74	3 - 139
7	HARYANA	39	62,518.91	64,850.78	3.73	11	9,225.92	9,400.64	5 - 29
8	HIMACHAL PRADESH	19	21,918.19	31,802.62	45.10	4	8,016.52	14,114.52	9 - 162
9	JAMMU AND KASHMIR	26	45,784.09	71,711.34	56.63	2	10,612.12	36,061.12	63 - 241
10	KARNATAKA	56	70,450.03	82,675.13	17.35	17	40,871.18	46,917.08	2 - 264
11	KERALA	23	34,828.89	39,970.99	14.76	6	7,614.89	9,296.74	6 - 53
12	MADHYA PRADESH	76	67,158.93	76,531.18	13.96	42	31,314.19	38,395.19	8 - 64
13	MAHARASHTRA	239	2,03,714.25	2,25,925.96	10.90	45	73,495.11	95,721.81	3 - 216
14	MANIPUR	19	9,640.91	18,089.68	87.63	2	4,971.74	12,688.08	36 - 153
15	MEGHALAYA	13	5,269.68	8,588.18	62.97	3	821.60	821.60	34 - 47
16	MIZORAM	23	11,751.40	15,700.10	33.60	13	7,757.62	11,706.32	43 - 134
17	NAGALAND	36	16,462.29	21,094.41	28.14	18	6,991.88	11,576.36	9 - 132
18	ODISHA	80	1,15,673.21	1,20,106.58	3.83	31	56,912.81	60,212.19	3 - 228
19	PUNJAB	21	11,288.85	12,858.74	13.91	6	3,709.37	3,523.41	5 - 108
20	RAJASTHAN	54	51,369.15	59,216.94	15.28	12	21,883.77	27,188.01	3 - 75
21	SIKKIM	21	7,778.98	15,698.13	101.80	2	1,629.53	8,890.05	49 - 96
22	TAMIL NADU	70	1,23,008.14	1,42,839.68	16.12	30	70,396.09	79,942.63	3 - 198
23	TRIPURA	21	5,174.00	5,395.32	4.28	5	1,269.36	1,452.17	14 - 74
24	UTTAR PRADESH	119	1,53,485.51	1,57,906.11	2.88	33	78,871.75	79,620.63	2 - 68
25	WEST BENGAL	72	63,906.08	82,743.75	29.48	30	33,938.03	41,033.92	4 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	7	2,230.29	2,520.99	23 - 54
27	DELHI	33	89,350.41	90,970.21	1.81	18	52,320.98	53,701.69	3 - 94
28	PONDICHERRY	1	195.00	195.00	0.00	1	195.00	195.00	19 - 19
29	CHHATISGARH	46	78,872.08	89,155.66	13.04	23	33,673.34	43,371.32	18 - 144
30	JHARKHAND	41	68,724.52	73,429.78	6.85	19	54,061.45	54,051.85	12 - 188
31	UTTARAKHAND	32	35,922.92	50,877.81	41.63	14	25,305.74	36,642.78	3 - 132
32	TELANGANA	49	37,249.74	40,283.18	8.14	15	17,878.52	18,758.66	6 - 168
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	15 - 15
34	MULTI STATE	130	3,68,262.98	4,84,139.25	31.47	59	1,11,384.85	1,61,573.51	5 - 276
Total		1718	21,99,181.52	26,36,710.50	19.90	560	9,42,586.32	12,32,995.82	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-9

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 150 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	3	63,628.00	73,508.00	36 - 75
2	CIVIL AVIATION	18	14,240.97	13,862.62	-2.66	12	11,339.25	10,960.90	4 - 27
3	COAL	108	1,51,274.98	1,54,186.72	1.92	43	40,626.97	43,537.90	0 - 168
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	-
5	FERTILISERS	4	1,101.28	1,101.28	0.00	1	215.92	215.92	23 - 23
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	-
7	STEEL	9	31,867.51	32,284.66	1.31	2	1,296.88	1,296.88	28 - 61
8	PETROLEUM	148	3,53,716.42	3,43,338.97	-2.93	36	25,059.76	23,921.08	-3 - 44
9	POWER	76	2,89,863.95	2,91,506.86	0.57	22	1,33,025.74	1,32,986.58	11 - 132
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	-
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,784.86	3.35	9	4,577.54	4,723.55	9 - 94
12	RAILWAYS	312	5,65,966.06	7,04,966.85	24.56	110	1,84,090.14	2,55,798.72	0 - 324
13	ROAD TRANSPORT AND HIGHWAYS	878	5,37,496.73	5,46,560.65	1.69	102	59,197.70	58,909.57	0 - 118
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	3	25,335.07	25,335.07	5 - 80
16	URBAN DEVELOPMENT	30	2,89,853.18	3,03,630.26	4.75	7	1,01,202.22	1,03,216.22	8 - 73
17	WATER RESOURCES	47	71,815.10	71,923.93	0.15	8	57,131.86	57,131.86	4 - 25
18	DEFENCE PRODUCTION	1	210.00	210.00	0.00	1	210.00	210.00	22 - 22
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	-
20	DEPARTMENT OF HIGHER EDUCATION	26	10,923.48	11,104.02	1.65	8	4,633.38	4,594.20	3 - 57
21	HOME AFFAIRS	7	2,546.83	3,327.60	30.66	2	1,418.52	2,199.31	5 - 29
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	3	606.71	538.27	63 - 74
23	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	-
24	DONER	1	151.33	151.33	0.00	1	151.33	151.33	47 - 47
Total		1718	24,69,171.14	26,36,710.50	6.79	373	7,13,746.99	7,99,235.36	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-10

Extent of cost overrun in projects with respect to latest cost						Rs.	150	Crore and above	
(All Cost/ Expenditure in Rs. crore)						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	41.55
2	CIVIL AVIATION	18	14,240.97	13,862.62	-2.66	2	1,488.27	1,712.33	15.06
3	COAL	108	1,51,274.98	1,54,186.72	1.92	8	22,093.43	25,131.51	13.75
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0.00
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0.00
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0.00
7	STEEL	9	31,867.51	32,284.66	1.31	1	1,682.85	2,100.00	24.79
8	PETROLEUM	148	3,53,716.42	3,43,338.97	-2.93	4	5,553.52	6,811.34	22.65
9	POWER	76	2,89,863.95	2,91,506.86	0.57	12	32,885.29	36,641.56	11.42
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	0.00
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,784.86	3.35	12	5,589.39	6,443.65	15.28
12	RAILWAYS	312	5,65,966.06	7,04,966.85	24.56	196	2,07,391.13	3,60,289.33	73.72
13	ROAD TRANSPORT AND HIGHWAYS	878	5,37,496.73	5,46,560.65	1.69	145	95,967.17	1,14,030.43	18.82
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	0	0.00	0.00	0.00
16	URBAN DEVELOPMENT	30	2,89,853.18	3,03,630.26	4.75	4	43,354.79	57,131.87	31.78
17	WATER RESOURCES	47	71,815.10	71,923.93	0.15	4	1,393.47	1,736.93	24.65
18	DEFENCE PRODUCTION	1	210.00	210.00	0.00	0	0.00	0.00	0.00
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0.00
20	DEPARTMENT OF HIGHER EDUCATION	26	10,923.48	11,104.02	1.65	5	1,855.89	2,078.60	12.00
21	HOME AFFAIRS	7	2,546.83	3,327.60	30.66	1	1,219.21	2,000.00	64.04
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0.00
23	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0.00
Total		1718	24,69,171.14	26,36,710.50	6.79	398	4,61,605.50	6,68,756.85	44.88

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-11

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	74- 75
2	CIVIL AVIATION	18	14,240.97	13,862.62	-2.66	2	1,488.27	1,712.33	15- 24
3	COAL	108	1,51,274.98	1,54,186.72	1.92	6	4,567.14	7,604.41	36- 132
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,971.07	7,075.17	-11.24	0	0.00	0.00	0- 0
7	STEEL	9	31,867.51	32,284.66	1.31	0	0.00	0.00	0- 0
8	PETROLEUM	148	3,53,716.42	3,43,338.97	-2.93	0	0.00	0.00	0- 0
9	POWER	76	2,89,863.95	2,91,506.86	0.57	2	17,866.58	19,383.42	15- 54
10	HEAVY INDUSTRY	2	5,281.30	4,627.30	-12.38	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,784.86	3.35	2	1,765.11	2,126.58	9- 94
12	RAILWAYS	312	5,65,966.06	7,04,966.85	24.56	75	1,07,317.35	1,84,668.05	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	878	5,37,496.73	5,46,560.65	1.69	7	5,259.56	6,006.60	20- 105
14	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	25,335.07	25,335.07	0.00	0	0.00	0.00	0- 0
16	URBAN DEVELOPMENT	30	2,89,853.18	3,03,630.26	4.75	1	10,773.00	12,787.00	44- 44
17	WATER RESOURCES	47	71,815.10	71,923.93	0.15	0	0.00	0.00	0- 0
18	DEFENCE PRODUCTION	1	210.00	210.00	0.00	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	26	10,923.48	11,104.02	1.65	1	496.00	498.99	57- 57
21	HOME AFFAIRS	7	2,546.83	3,327.60	30.66	1	1,219.21	2,000.00	29- 29
22	RURAL DEVELOPMENT	4	968.31	899.87	-7.07	0	0.00	0.00	0- 0
23	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	0- 0
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
Total		1718	24,69,171.14	26,36,710.50	6.79	99	1,74,531.22	2,70,446.38	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-12

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 150 Crore and above						(All Cost/ Expenditure in Rs. crore)			
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	18	13,348.06	13,862.62	3.85	3	1,905.50	2,420.06	15- 45
3	COAL	108	1,48,672.06	1,54,186.72	3.71	17	31,207.71	35,209.45	12- 188
4	FINANCE	2	557.77	557.73	-0.01	0	0.00	0.00	0- 0
5	FERTILISERS	4	1,101.28	1,101.28	0.00	0	0.00	0.00	0- 0
6	MINES	5	7,078.62	7,075.17	-0.05	0	0.00	0.00	0- 0
7	STEEL	9	25,452.51	32,284.66	26.84	2	17,207.85	24,040.00	36- 80
8	PETROLEUM	148	3,36,760.67	3,43,338.97	1.95	24	56,299.71	74,077.05	6- 110
9	POWER	76	2,29,308.93	2,91,506.86	27.12	18	94,597.17	1,53,347.22	6- 162
10	HEAVY INDUSTRY	2	3,272.00	4,627.30	41.42	0	0.00	0.00	0- 0
11	HEALTH AND FAMILY WELFARE	29	15,273.26	15,784.86	3.35	2	1,765.11	2,126.58	9- 94
12	RAILWAYS	312	4,62,095.03	7,04,966.85	52.56	108	1,38,600.99	2,71,385.55	3- 324
13	ROAD TRANSPORT AND HIGHWAYS	878	5,29,993.60	5,46,560.65	3.13	23	10,966.02	13,389.68	20- 134
14	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
15	TELECOMMUNICATIONS	3	14,013.36	25,335.07	80.79	1	13,334.00	24,664.00	80- 80
16	URBAN DEVELOPMENT	30	2,81,283.00	3,03,630.26	7.94	4	60,511.47	77,105.12	34- 73
17	WATER RESOURCES	47	26,322.76	71,923.93	173.24	2	10,349.47	55,773.56	4- 25
18	DEFENCE PRODUCTION	1	246.31	210.00	-14.74	0	0.00	0.00	0- 0
19	COMMERCE	1	302.64	302.64	0.00	0	0.00	0.00	0- 0
20	DEPARTMENT OF HIGHER EDUCATION	26	10,910.66	11,104.02	1.77	1	496.18	498.99	57- 57
21	HOME AFFAIRS	7	2,306.97	3,327.60	44.24	3	1,659.44	2,528.33	3- 44
22	RURAL DEVELOPMENT	4	889.43	899.87	1.17	2	352.34	362.78	63- 74
23	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
24	DONER	1	151.33	151.33	0.00	0	0.00	0.00	0- 0
Total		1718	21,99,181.52	26,36,710.50	19.90	214	4,71,296.96	7,82,605.37	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-13

List of projects completed/dropped/Frozen during current month							
Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
1	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE-1B FOR IIT ROPAR, PUNJAB	08/2016	294.00	04/2019	350.69	08/2021	289.13
	<u>PETROLEUM</u>						
2	SECONDARY TANK FARM WITH DEHYDRATION FACILITY AND EFFLUENT TREATMENT PLANT AT MADHUBAN	07/2011	352.56	03/2017	490.24	N.A.	455.00
3	MUMBAI REFINERY EXPANSION PROJECT	09/2015	4,199.00	03/2020	5,060.00	08/2021	4,808.22
4	CONSTRUCTION OF A NEW POL DEPOT AT VILLAGE DATA IN HISAR DISTRICT IN HARYANA	11/2017	255.00	11/2020	300.00	06/2021	275.68
	<u>POWER</u>						
5	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	03/2013	11,638.55	01/2018	15,105.22	N.A.	13,657.43
6	TANDA TPP STAGE-II (2X660 MW)	09/2014	9,188.98	07/2019	9,842.02	N.A.	7,391.78
7	MOUDA STPP STAGE 2	03/2012	7,921.47	09/2016	7,921.47	N.A.	5,302.00
8	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11,846.00	10/2017	12,739.82	N.A.	13,766.78
9	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture	04/2012	9,750.89	02/2017	12,176.28	N.A.	11,130.00
10	DARLIPALLI STPP STAGE-I (2X800 MW)	02/2014	12,532.44	12/2018	13,140.91	07/2021	12,084.99
11	85 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	03/2019	349.00	11/2020	349.00	N.A.	313.00
12	140 MW BILHAUR SOLAR PV PROJECT BILHAUR UP	12/2018	587.44	09/2020	587.44	N.A.	463.48
13	KHARGONE STPP STAGE I (1320 MW)	03/2015	9,870.51	01/2020	11,148.86	N.A.	10,019.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
14	FOUR LANING OF 5.122 KM OF NH9 (NEW NH 65) FROM KM 269.900 (DESIGN CH0.0) TO KM 275-622(DESIGN C	07/2015	333.21	12/2015	333.21	N.A.	256.11
15	CONSTRUCTION OF HIGH LEVEL BRIDGE ACROSS INDRAVATI RIVER ON NH-63 (ERSTWHILE NH-16) AND CONSTRUCTION ITEM RATE	12/2011	156.26	N.A.	247.95	N.A.	141.35
16	WIDENING AND STRENGTHENING OF NH-65 TO FOUR LANES WITH PAVED SHOULDERS FROM EXISTING KM 267+500 TO K EPC	10/2014	269.22	01/2015	269.22	N.A.	33.24

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
				Original		Now anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
17	WIDENING AND STRENGTHENING OF NH-65 TO TWO LANES WITH PAVED SHOULDERS FROM EXISTING EPC	10/2014	257.09	01/2015	257.09	N.A.	14.18
18	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS EPC	10/2013	278.87	05/2014	278.87	N.A.	0.00
19	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING O ITEM RATE	01/1991	376.52	04/2014	376.52	N.A.	171.16
20	WIDENING AND STRENGTHENING OF NH-15 TO TWO LANES WITH PAVED SHOULDER FROM EXISTING KM 173/0 TO KM 24 EPC	02/2015	383.40	03/2015	383.40	N.A.	244.68
21	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0)	07/2015	333.21	12/2015	333.21	N.A.	256.11
22	TWO LANING OF KHONSA - TISSA - LONGDING (NH-52B) (42.50 KM) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRA ITEM RATE	12/2011	156.63	02/2012	276.00	N.A.	0.00
23	TWO LANING OF LALPUL - MANMAO- CHANGLANG ROAD (NH-52B) IN ARUNACHAL PRADESH UNDER ARUNACHAL PRADESH P ITEM RATE	11/2010	305.49	03/2011	305.49	N.A.	131.08
24	TWO LANING OF GOBOK - SIJON NALLAH (CORRESPONDING TO EXISTING CH: 27.00 TO KM75.00) IN ARUNACHAL PR ITEM RATE	03/2012	207.03	05/2012	389.45	08/2021	308.09
25	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK-PFUTSERO ROA ITEM RATE	12/2010	1,296.00	02/2011	1,296.00	N.A.	782.76
26	REHABILITATION AND UPGRADATION OF NH 226 E FROM 0-1 - 66-20 TO 2 LANE WITH PAVED SHOULDERS ON EPC MO EPC	03/2015	157.18	07/2015	162.00	N.A.	148.24
27	CONSTRUCTION OF PAVED SHOULDERS INCLUDING STRENGTHENING OF EXISTING CARRIAGEWAY FROM KM 0-0-51-0 I- EPC	11/2015	154.14	08/2015	154.14	N.A.	142.06
28	CONSTRUCTION OF 2-LANE ROAD FROM KM 33 TO KM 65.00 OF AKAJAN-LIKABALI-BAME ROAD IN ARUNACHAL PRADESH EPC	07/2015	197.16	10/2018	197.16	N.A.	91.25
29	6 LANING OF AGRA - ETAWAH BYPASS PPP (BOT)	07/2015	1,657.20	01/2019	1,657.20	N.A.	0.00
30	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) PPP (BOT)	07/2015	2,288.18	05/2019	2,288.18	N.A.	487.81
31	REHABILITATION AND UP-GRADATION OF NH-149 FROM KM 0.00 TO KM 68.280	07/2014	342.05	01/2017	342.05	N.A.	258.91

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		DOA	Original		Now anticipated		Final Expenditure
Sl.No	Project		Cost	DOC	Cost	DOC	
	(PALLAHARA-PITRI JUNCTION) IN TH EPC						
32	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF NABARANGPUR-KOK	01/1991	229.41	05/2018	229.41	N.A.	6.65
33	FOUR LANING OF 5.122 KM OF NH 9 (NEW NH 65) FROM KM 269/900 (DESIGN CH. 0/0) TO KM 275/022 (DESIGN C EPC	10/2015	333.21	11/2015	353.89	N.A.	256.11
34	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG ITEM RATE	01/1991	358.22	10/2016	377.64	N.A.	339.86
35	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP BOT (TOLL)	11/2011	954.43	09/2015	1,191.51	10/2021	235.61
36	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF ANISABAD-AURANG ITEM RATE	01/1991	282.41	08/2016	322.01	N.A.	327.21
37	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BANKUARA- PURUL	01/1991	322.00	03/2018	322.00	N.A.	56.41
38	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PAVED SHOULDER OF MUDKI-JAWAHAR SINGH WALA SECTION OF	03/2018	173.24	06/2020	173.24	08/2021	56.66
39	REHABILITATION AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER OF ABOHAR-SITOGUNNO-DABWALI ROAD OF NH	03/2018	322.48	07/2020	322.48	08/2021	291.93
40	REHABILITATION AND UP-GRADATION TO 2LPS 81 TO 175	09/2016	287.34	01/2019	287.34	N.A.	194.85
41	2 LANING OF BAMEETHA TO SATNA SECTION OF NH-75 FROM KM. 57+400 TO KM. 155+000 IN THE STATE OF MP	03/2018	191.21	11/2019	191.21	N.A.	127.13
42	UPGRADATION OF NH-31C WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 10	03/2017	202.69	11/2019	202.69	N.A.	148.21
43	REHABILITATION AND UPGRADATION OF INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2 LANE PAVED SHOULDER RIGID	11/2017	235.91	02/2018	235.91	02/2021	176.23
44	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-48 INVOLVING NH-717, NH-31, NH-31C, NH-317A O	08/2014	823.20	11/2017	937.76	08/2021	807.99
45	PROPOSED DEVELOPMENT FOR ROAD CORRIDOR COMPONENT OF AH-02 INVOLVING NH-327B, NH-31C, NH-31 NH-10 O	08/2014	600.87	11/2017	720.97	08/2021	682.36

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
46	WIDENING AND STRENGTHENING OF EXISTING SL IL DL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER FROM KM	02/2015	239.91	10/2017	160.00	N.A.	147.25
47	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR FROM KM 400.878 TO KM 450.000 OF NH-76E TO 2-	10/2016	239.63	02/2019	239.63	N.A.	212.53
48	WIDENING AND STRENGTHENING OF NH-730A FROM KM 0.00 TO KM 50.675 IN THE STATE OF UTTAR PRADESH	05/2013	164.54	08/2015	164.54	01/2021	141.33
49	REHABILITATION AND UPGRADATION OF NH-233 FROM KM 65.870 TO KM 122.270 IN THE STATE OF UTTAR PRADESH	10/2013	445.89	03/2017	653.29	N.A.	469.64
50	REHABILITATION AND UPGRADATION OF PILIBHIT TO PURANPUR SECTION FROM KM 0.00 TO KM 38.00 OF NH-730 TO	10/2016	176.94	10/2018	176.94	N.A.	141.11
51	REHABILITATION AND UPGRADATION OF MAU-JASRA FROM KM 326.000 TO KM 379.555 OF NH-76 TO 2-LANE WITH PA	10/2016	218.94	03/2020	218.94	N.A.	120.69
52	REHABILITATION AND UPGRADATION OF BALRAMPUR-TULSIPUR FROM KM 323.745 TO KM 351.000 OF NH-730 TO 2-L	03/2018	212.99	06/2020	212.99	N.A.	156.72
53	AKKALKOT TO DHUDHNI	04/2016	211.42	02/2019	211.42	08/2021	131.85
54	MAJALGAON TO KAIJ	01/2017	413.99	07/2019	413.99	08/2021	299.72
55	WANDS OF EXISTING SINGLE LANE TO DOUBLE LANE CARRIAGEWAY IN KM 0 TO 40 OF NH-104 IN BIHAR UNDER EPC	05/2014	199.98	08/2016	199.98	N.A.	163.16
56	CONSTRUCTION OF FLYOVER FROM KM 604/252 TO 607/060 (MARTHANDAM JUNCTION) AND FROM KM 630/116 TO 631/	05/2016	307.70	01/2017	307.70	N.A.	313.06
57	WIDENING TO 4 LANE / 4 LANE WITH PAVED SHOULDERS WITH STRENGTHENING OF EXISTING CARRIAGEWAY IN KM 0/	01/2016	162.72	09/2016	162.72	N.A.	136.59
58	IMPROVEMENT AND UP-GRADATION OF EXISTING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 KM	11/2018	281.45	12/2020	281.45	03/2022	112.70
59	WIDENING OF SL TO 2 L KM. 287.0 TO 292.0 322.0 TO 342.0 AND KM 352.0 TO 400.0 OF NH16 INCLUDING 1	12/2010	169.26	01/2019	299.00	N.A.	270.11
60	WIDENING OF SL TO 2 L KM. 107-184.80 SUKUMA TO KONTA ON NH 221	03/2010	179.89	03/2013	271.00	N.A.	242.23
61	R AND U FROM KM 385.00 TO KM 420.000 TO 2- LANE WITH PS (EXCLUDING ROB AND ITS APPROACHES AT KM.404	12/2016	209.10	10/2019	209.10	N.A.	201.70
62	REHABILITATION AND UPGRADATION OF BARAICH -SHRAWAST FROM KM 248.400 TO KM 310.000 OF NH-730 TO 2-LA	03/2016	388.83	12/2019	388.83	N.A.	304.70

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
				Original		Now anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
63	IMPROVEMENT OF JUNCTION AT DHAULA KUAN ON NH-8	07/2017	269.69	09/2019	269.69	N.A.	0.01
64	REHABILITATION AND UP GRADATION OF CHITRADURGA TO SHIMOGA SECTION OF NH-13 FROM KM.422.000 TO KM.	01/2014	471.16	08/2014	471.16	N.A.	201.64
65	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.106.00 TO 153.00 OF NH-218 (218-KNT-2014-15-776)	03/2015	165.67	01/2016	165.67	N.A.	87.63
66	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.125.626 TO 155 OF NH -167 HAGARI JADECHERLA SECT	08/2016	175.20	01/2017	175.20	N.A.	142.48
67	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 54.37 TO 101.400 OF NH-50 UNDER EPC MODE IN THE STAT	08/2016	367.44	01/2017	367.44	N.A.	61.95
68	CONSTRUCTION OF SILCHAR BYPASS ON NH-53 IN ASSAM	11/2010	197.37	02/2014	197.37	01/2020	89.36
69	REHABILITATION AND UPGRADATION OF PRATAPGARH-ALLAHABAD BYPASS ROAD AND JUNCTION SECTION OF NH-96 F	03/2016	599.34	01/2020	599.34	N.A.	492.15
70	WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO 40.00 ON EPC MODE ON NH 2C	11/2016	230.34	10/2019	230.34	N.A.	201.82
71	REHABILITATION AND UP-GRADATION TO 2 LANE WITH PS 131 TO 189 OF NH-86	09/2016	178.23	09/2018	178.23	N.A.	122.99
72	REHABILITATION AND UPGRADATION OF HARPALPUR -SUGIRA FROM KM 89.600 TO KM 133.520 OF NH-76 TO 2-LANE	03/2016	208.50	11/2019	208.50	N.A.	165.82
73	REHABILITATION AND UPGRADATION OF NEW NH-544DD (OLD SH-30) FROM DESIGN CHAINAGE KM 0.000 TO 56.000 (	03/2018	297.12	07/2018	294.12	N.A.	373.98
74	REHABILITATION AND UPGRADATION OF NH-42 FROM 76/000 TO KM 102/130 (DESIGN CH. 76/000 TO 99.971 EXCLU	03/2018	244.95	08/2018	244.95	N.A.	136.22
75	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	03/2018	293.64	08/2020	293.64	N.A.	28.24
76	WIDENING TO 2LPS FROM 181/0 TO 239/28 (BHAWANIPATNA TO KOKSARA) OF NH-26.	03/2016	165.06	12/2016	165.06	N.A.	92.59
77	CONSTN. OF 4 LANING IN KM.69.00 TO 100.00 DESIGN RD 94.600 TO 125.920 PACKAGE IV (EPC)	01/2017	276.01	03/2019	276.01	08/2021	187.39
78	WIDENING AND STRENGTHENING OF EXISTING SINGLE INTERMEDIATE LANE CARRIAGEWAY TO 2 LANE CARRIAGE WAY W	01/2015	326.63	04/2018	326.63	N.A.	249.26
79	CONSTRUCTION OF FLYOVER/UNDERPASS FOR	09/2016	1,004.67	05/2019	813.45	N.A.	577.21

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		DOA	Original		Now anticipated		Final Expenditure
Sl.No	Project		Cost	DOC	Cost	DOC	
	IMPROVEMENT OF EXISTING JUNCTIONS AT IFFCO CHOWK AT KM. 28.211						
80	CONSTRUCTION OF FOUR LANING OF UP/HARYANA NH-73	08/2016	248.97	05/2019	248.97	N.A.	270.65
81	CONSTRUCTION OF BHAGALPUR BYPASS FROM KM 124/175 TO 140/200 OF NH-80 UNDER EPC MODE	08/2015	288.24	11/2015	288.24	N.A.	287.37
82	STRENGTHENING AND WIDENING WORK OF EXISTING 2-LANE TO TWO LANE WITH PAVED SHOULDER AND GEOMETRIC IMPR	03/2015	206.80	07/2016	206.80	N.A.	74.04
83	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P	02/2016	369.77	06/2016	369.77	N.A.	0.00
84	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING	02/2014	665.50	07/2016	665.50	N.A.	0.00
85	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	02/2016	997.15	03/2019	1,115.95	N.A.	975.08
86	FOUR LANING OF DELINKED STRETCH OF SEONI - MP/MH BORDER OF NH-7 (LENGTH 28.70 KM) FROM KM 624.480 TO	01/2018	960.24	N.A.	960.24	N.A.	738.74
87	WIDENING OF EXISTING IL DL TO 2-LANE WITH 1.5 M WIDE PAVED SHOULDER FROM KM 0.0 TO KM 45.750 (BOLANG	06/2016	157.30	06/2018	157.30	N.A.	97.29
88	REHABILITATION AND UPGRADATION OF NH-149 FROM KM 0.00 TO KM 68.280 (PALLAHARA TO PITRI JUNCTION) IN	07/2014	342.05	01/2017	342.00	N.A.	258.91
89	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDERS CONFIGURATION AND STRENGTHENING OF ANISH	10/2013	278.39	08/2014	278.39	N.A.	22.18
90	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF SITAMARHIKM 40 EPC	01/1991	154.62	N.A.	154.62	N.A.	0.00
91	WIDENING STG.OF EXISTING TWO-LANE CARRIAGEWAY TO FOUR LANES WITH PAVED SIDE SHOULDERS OF HARIKE-ZIRA EPC	06/2015	892.17	N.A.	892.17	08/2021	648.44
92	WIDENING TO 2 LANE AND IMPROVEMENT FROM KM 100/700 TO 186/700 OF VIJAYWADA RANCI ROUTE IN ODISHA EPC	12/2011	159.39	11/2017	159.39	N.A.	210.29
93	REHABILITATION AND UPGRADING TO 2 LANES-2 LANE WITH PAVED SHOULDERS CONFIGURATION OF	01/1991	478.35	N.A.	478.35	N.A.	516.69
94	FOUR LANING OF CHANDIGARH - KHARAR	10/2015	447.29	12/2017	558.25	N.A.	346.39
95	NH 79 CHITTORGARH NEEMUCH MP	09/2012	511.00	10/2013	511.00	N.A.	492.00

List of projects completed/dropped/Frozen during current month							
(All Cost/ Expenditure in Rs. crore)							
		Original		Now anticipated			
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	BORDER FOUR LANING AND NH 113 NIMBAHERA PRATAPGARH TWO LANING BOT (TOLL)						
96	NH 79 OF CHITTORGARH NEEMUCH MP BORDER KM 183 000 TO KM 221 400 BY FOUR LANING WITH PAVED SHOULDER A BOT (TOLL)	09/2012	511.00	10/2013	511.00	N.A.	2,323.04
97	2 LANING OF OF LUMDING-DIPHU- MANJA ROAD (L=54.37 KM.) HAF LONG JATINGA ROAD (L=7.46 KM.) BASKA BAR ITEM RATE	11/2010	470.20	02/2011	630.36	03/2020	569.40
98	BAMITHA-SATANA (2L+PS) OF NH-75 IN MP BOT (TOLL)	08/2015	257.80	N.A.	257.00	N.A.	12.38
99	4-LANING OF LAMBRA-SHAHKOT SECTION OF NH-71 FROM KM 12.00 TO 44.600 EPC	11/2015	847.02	N.A.	847.02	N.A.	795.00
100	INDO-NEPAL BORDER TO RUDHAULI SECTION OF NH-233 IN UTTAR PRADESH KM 0/0 TO 65/870 EPC	11/2013	497.05	05/2017	881.05	N.A.	754.27
101	DEVELOPMENT TO FOUR LANE WITH PAVED SHOULDERS OF SHAHKOT-MOGA SECTION OF NH-71 (NEW NH-52) FROM EXIS EPC	12/2015	766.36	N.A.	766.36	08/2021	685.36
102	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BHOJPUR-CHHATAB EPC	01/1991	218.63	10/2017	218.63	N.A.	29.27
103	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF "MADHUGIRI-MULB EPC	01/1991	219.40	01/2018	219.40	N.A.	0.10
104	SATANA-BELA SECTION OF NH-75(4L) IN MP BOT (TOLL)	01/2012	320.48	08/2015	320.48	N.A.	189.49
105	2-LANING OF LALPUL-MANMAO-CHANGLANG ROAD(NH-52B) (NEW NH NO.215)FROM KM 0.00 TO KM 68.30IN THE STATE ITEM RATE	11/2010	305.49	03/2017	305.49	N.A.	0.00
106	RUDHAULI TO GHAGRA BRIDGE SECTION OF NH-233 IN UTTAR PRADESH KM 65/870 TO 122/270 EPC	10/2013	445.89	03/2017	653.29	N.A.	464.05
107	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.56.00 TO 106.00 OF NH-218 BIJAPU EPC	03/2015	159.12	11/2015	159.12	N.A.	0.00
108	RANCHI-RARGA-JAMSETHPUR PPP (ANNUITY)	12/2012	1,479.00	06/2015	1,479.00	N.A.	740.26
109	FOUR LANNING OF NH-4A(NH-748) FROM KM 118 TO 125 INCL.FOUR LANE KHNDEAPAR BRIDGE EPC	03/2015	297.00	04/2018	297.00	N.A.	290.64

List of projects completed/dropped/Frozen during current month							
Rs. 150 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
110	WIDENING TO 4 LANE WITH PAVED SHOULDER WITH CC PAVEMENT FROM KM 256/550 TO KM 289/500 ON KOTA-DARAH EPC	12/2015	621.43	06/2018	621.43	N.A.	387.22
	URBAN DEVELOPMENT						
111	CONSTRUCTION OF ADDITIONAL COMPLEX FOR THE SUPREME COURT OF INDIA AT LAND ADJOINING PRAGATI MAIDAN	07/2012	884.30	12/2015	884.30	12/2020	874.29
112	CONSTRUCTION OF 76 NOS MS FLATS FOR HONORABLE MPS OF LOK SABHA AT DR BD MARG NEW DELHI	07/2017	218.72	11/2020	218.72	08/2021	175.63

FLASH REPORT

TABLE-14

List of projects added Rs. 150 Crore and above					(August 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>COAL</u>					
1	KHADIA EXPANSION OCP	6/2021	491.67	3/2025	491.67	3/2025
	<u>HOME AFFAIRS</u>					
2	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI	5/2019	199.31	1/2022	199.31	6/2022
	<u>PETROLEUM</u>					
3	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	176.00	8/2027	176.00	8/2027
4	CGD PROJECT AT REWA DISTRICT	10/2018	177.00	2/2027	177.00	2/2027
5	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	613.00	12/2029	613.00	12/2029
6	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	2,998.00	3/2030	2,998.00	3/2030
7	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	2,880.00	8/2027	2,880.00	8/2027
8	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	439.00	2/2028	439.00	2/2028
9	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	6/2019	347.00	2/2028	347.00	2/2028
10	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	303.00	2/2028	303.00	2/2028
11	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	169.00	12/2029	169.00	12/2029
12	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2,996.00	2/2028	2,996.00	2/2028
13	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	163.00	12/2029	163.00	12/2029
14	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS	6/2019	988.00	12/2029	988.00	12/2029
15	CGD PROJECT AT SALEM DISTRICT	10/2018	1,304.00	3/2030	1,304.00	3/2030
	<u>POWER</u>					
16	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA & RADHANPUR) EPC	5/2021	674.92	9/2022	674.92	9/2022
	<u>ROAD TRANSPORT AND HIGHWAYS</u>					

List of projects added Rs. 150 Crore and above					(August 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
17	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH EPC	2/2021	588.09	3/2024	588.09	3/2024
18	BALANCE WORK OF 2-LANING OF LONGDING-TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH EPC	1/2020	358.26	2/2024	358.26	2/2024
19	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC EPC	6/2020	437.60	8/2021	437.60	8/2021
20	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC EPC	6/2020	496.47	8/2021	496.47	8/2021
21	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA EPC	8/2020	272.98	4/2021	272.98	4/2021
22	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA EPC	3/2019	423.15	12/2019	423.15	12/2019
23	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT EPC	1/2017	264.34	9/2017	264.34	9/2017
24	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT EPC	8/2020	222.61	3/2021	222.61	3/2023
25	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR EPC	6/2020	221.40	5/2021	221.40	12/2022
26	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION EPC	3/2020	207.79	3/2021	207.79	4/2022
27	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 EPC	8/2020	349.20	4/2021	349.20	4/2021
28	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. EPC	8/2020	242.80	3/2021	242.80	3/2021
29	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A EPC	3/2021	182.55	9/2021	182.55	9/2021
30	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 EPC	2/2019	731.89	11/2019	731.89	11/2019
31	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 EPC	2/2019	362.46	11/2019	362.46	11/2019
32	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 EPC	2/2019	594.75	11/2019	594.75	11/2019
33	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING	8/2020	302.62	2/2021	302.62	2/2021

List of projects added Rs. 150 Crore and above					(August 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	STRENGTHENING CARRIAGEWAY FROM KM 8 EPC					

FLASH REPORT

TABLE-15

Milestones (Cumulative due & achieved)	Rs. 150 Crore and above
Total	5885
Achieved up to month	2860

TABLE-16

List of projects reporting additional delayed Rs. 150 Crore and above							(August 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA AAI	458.00	458.00	03/2020	04/2022	07/2022	3
2	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT AAI	177.10	177.10	02/2020	12/2021	05/2022	5
3	CCS INTERNATIONAL AIRPORT , LUCKNOW AAI	1,383.00	1,383.00	09/2021	09/2022	12/2023	15
	<u>COAL</u>						
4	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW NLC	17,237.00	17,237.80	11/2021	07/2022	11/2022	4
5	MOONIDIH XV SEAM UG BCCL	1,230.27	1,230.27	04/2015	03/2022	02/2023	11
6	GARJANBAHAL OCP MCL	1,375.38	1,375.38	03/2021	03/2024	09/2025	18
7	HINGULA OC-II EXP. PH-III (15 MTY) MCL	479.53	703.39	03/2013	03/2022	03/2024	24
8	RECAST EPR AMRAPALI OC CCL	4,983.58	4,983.58	03/2020	03/2024	03/2028	48
	<u>PETROLEUM</u>						
9	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	08/2021	09/2021	1
10	RE-LIQUIFIED NATURAL GAS CPCL	421.00	305.00	08/2020	09/2021	10/2021	1
11	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY IOCL	315.00	315.00	12/2021	08/2021	09/2021	1
12	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI IOCL EPC	1,398.00	1,398.00	12/2023	08/2023	09/2023	1
13	RESITEMENT OF RAICHUR DEPOT TO GULBARGA BPCL	206.26	206.26	03/2021	08/2021	10/2021	2
14	PIPELINE NETWORK PROJECT GELEKI, ASSAM ONGC	249.85	303.75	05/2020	08/2021	11/2021	3
15	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY IOCL	255.40	255.40	08/2020	11/2021	03/2022	4

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (August 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
16	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY IOCL	1,019.00	1,019.00	01/2023	01/2023	05/2023	4
17	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY IOCL	206.63	340.76	02/2020	08/2021	07/2022	11
18	CITY GAS DISTRIBUTION IN WEST BENGAL HPCL EPC	5,830.20	5,830.20	03/2031	08/2029	08/2031	24
	<u>POWER</u>						
19	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	08/2021	09/2021	1
20	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) PGCIL	235.53	235.53	06/2019	10/2021	11/2021	1
21	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	1,931.39	02/2020	08/2021	09/2021	1
22	DURGAPUR PP-III (2X20 MW) - NSPCL NTPC	529.68	633.80	11/2018	11/2021	12/2021	1
23	DEVIKOT SOLAR 90MW NTPC EPC	501.29	501.29	09/2021	01/2022	02/2022	1
24	DEVIKOT SOLAR 150MW NTPC EPC	798.24	798.24	09/2021	01/2022	02/2022	1
25	EASTERN REGION STRENGTHENING SCHEME-XII PGCIL	522.29	546.36	11/2016	10/2021	12/2021	2
26	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	10/2021	12/2021	2
27	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	12/2021	02/2022	2
28	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY PGCIL Central Sector Projects	186.17	219.66	07/2019	08/2021	10/2021	2
29	EASTERN REGION STRENGTHENING SCHEME XX PGCIL	358.83	358.83	05/2020	08/2021	10/2021	2
30	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	2,311.89	12/2018	09/2021	11/2021	2
31	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,997.70	11/2020	07/2022	10/2022	3
32	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES PGCIL	5,111.33	6,700.00	12/2018	12/2021	03/2022	3

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (August 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
33	PATRATU STPP-I (3X800MW) NTPC	18,668.00	17,112.00	03/2023	09/2024	02/2025	5
34	NOKHRA NTPC EPC	1,722.14	1,722.14	09/2021	01/2022	01/2023	12
	<u>HEALTH AND FAMILY WELFARE</u>						
35	LHMC NEW DELHI-RE-DEVELOPMENT HSCC	414.11	655.58	11/2013	07/2021	09/2021	2
36	NEIGRIHMS SHILLONG MEGHALYA HSCC	363.99	363.99	05/2018	12/2021	03/2022	3
37	GERIATRICS BLOCK- AIIMS DELHI HSCC	156.56	190.34	N.A.	08/2021	11/2021	3
	<u>RAILWAYS</u>						
38	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING SER	258.20	358.68	12/2018	07/2021	08/2021	1
39	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM- CHENGALPATTU 3RD LINE GC ALONG WITH ELECTRIFICATION	931.98	1,121.00	N.A.	07/2021	08/2021	1
40	MANSI-PURNIA (EXTENSION OF MANSI- SAHARSA) GAN ECR	477.88	751.55	03/2012	07/2021	09/2021	2
41	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) NFR	602.27	2,144.78	12/2021	07/2021	09/2021	2
42	NEW BG LINE FROM JAGBANI TO BIRATNAGAR NFR	241.52	373.87	N.A.	12/2021	03/2022	3
43	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I IRCON	3,055.00	3,055.15	09/2018	03/2022	06/2022	3
44	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP MRTP	495.74	734.01	06/2013	12/2021	07/2022	7
45	RAMGANJMUHDI-BHOPAL (NL),WCR WCR	424.60	2,909.99	03/2021	03/2023	03/2024	12
46	VIRAMGAM-SAMAKHIALI (DL) WR	1,037.15	1,383.69	03/2021	12/2021	12/2022	12
47	MUZAFFARPUR SAGALI DOUBLING 100.60 KM ECR	731.64	1,185.73	03/2021	06/2022	03/2024	21
48	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING NCR	4,329.53	4,329.53	03/2023	03/2023	06/2025	27
49	BAGALKOT-KUDACHI NL SWR	986.30	1,530.09	03/2016	12/2023	12/2026	36

List of projects reporting additional delayed Rs. 150 Crore and above (August 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
50	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 MoRTH EPC	957.54	957.54	02/2020	08/2021	09/2021	1
51	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS NHAI	364.56	392.00	N.A.	07/2021	08/2021	1
52	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS MoRTH	166.21	173.41	08/2018	08/2021	09/2021	1
53	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A MoRTH	373.82	373.82	09/2019	08/2021	09/2021	1
54	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS MoRTH	296.50	296.50	09/2020	07/2021	08/2021	1
55	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION MoRTH	335.32	335.32	06/2017	09/2021	10/2021	1
56	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION MoRTH	423.79	423.79	01/2018	09/2021	10/2021	1
57	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 MoRTH EPC	628.45	628.45	01/2020	07/2021	09/2021	2
58	FOUR LANING OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	06/2021	08/2021	2
59	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 MoRTH	306.59	306.59	N.A.	07/2021	09/2021	2
60	REHABILITATION AND UPGRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI-KAWARDHA SECTION. MoRTH EPC	291.05	291.05	N.A.	07/2021	10/2021	3
61	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA MoRTH	536.65	536.65	12/2019	09/2021	12/2021	3
62	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V MoRTH	476.20	544.00	09/2016	09/2021	12/2021	3
63	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION MoRTH	624.98	731.50	10/2016	09/2021	12/2021	3
64	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K MoRTH	196.23	196.00	11/2020	08/2022	11/2022	3
65	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. MoRTH	205.05	205.05	03/2017	08/2021	12/2021	4

List of projects reporting additional delayed Rs. 150 Crore and above (August 2021)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
66	2L+PS OF THIKRI ANJAD SECTION OF NH-347B MoRTH	249.05	249.05	07/2018	08/2021	12/2021	4
67	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS MoRTH	809.16	809.16	07/2018	07/2021	11/2021	4
68	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM MoRTH	877.79	877.79	06/2019	08/2021	12/2021	4
69	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A MoRTH EPC	390.51	390.51	N.A.	07/2021	12/2021	5
70	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	08/2021	01/2022	5
71	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	1,928.22	04/2015	06/2021	12/2021	6
72	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- NHAI	1,031.95	1,031.95	N.A.	09/2021	03/2022	6
73	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS MoRTH	214.69	214.69	03/2018	09/2021	06/2022	9
74	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 MoRTH	497.14	572.66	08/2016	09/2021	06/2022	9
75	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O NHIDCL EPC	294.17	294.17	01/2016	04/2021	03/2022	11
76	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM NHIDCL	284.09	284.09	04/2017	03/2021	03/2022	12
77	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM NHIDCL EPC	454.89	454.89	05/2018	12/2020	03/2022	15
78	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI MoRTH	452.94	435.61	07/2016	09/2021	12/2022	15
79	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. NHIDCL	387.00	387.00	09/2018	09/2020	03/2022	18
	<u>URBAN DEVELOPMENT</u>						
80	DELHI MRTS PHASE-III DMRC	38,585.00	38,585.00	03/2016	07/2021	08/2021	1
81	KANPUR METRO RAIL PROJECT LMRCL Public Private (SPV)	11,076.48	11,076.48	03/2024	03/2024	03/2025	12
82	AGRA METRO RAIL PROJECT LMRCL Public Private (SPV)	8,379.62	8,379.62	03/2024	03/2024	05/2025	14

<u>List of projects reporting additional delayed</u> Rs. 150 Crore and above (August 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
83	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I CPWD	1,128.00	1,128.00	03/2022	03/2022	06/2023	15
84	REDEVELOPMENT OF GPRA AT MOHAMMADPUR CPWD	422.00	422.00	03/2021	07/2021	06/2023	23
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
85	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA CPWD	496.18	498.99	06/2017	10/2021	03/2022	5
	<u>HOME AFFAIRS</u>						
86	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF CPWD EPC	277.35	290.33	07/2022	07/2022	10/2022	3

FLASH REPORT

TABLE-17

Sector wise analysis of projects Rs. 150 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	704,68.00	80,348.00	61,584.57
CIVIL AVIATION	18	13,348.06	142,40.97	13,862.62	4,502.25
COAL	108	1,48,672.06	1,512,74.98	1,54,186.72	52,127.02
FINANCE	2	557.77	5,57.77	557.73	369.06
FERTILISERS	4	1,101.28	11,01.28	1,101.28	865.59
MINES	5	7,078.62	79,71.07	7,075.17	1,371.05
STEEL	9	25,452.51	318,67.51	32,284.66	23,985.05
PETROLEUM	148	3,36,760.67	3,537,16.42	3,43,338.97	1,18,737.04
POWER	76	2,29,308.93	2,898,63.95	2,91,506.86	1,88,096.10
HEAVY INDUSTRY	2	3,272.00	52,81.30	4,627.30	4,332.10
HEALTH AND FAMILY WELFARE	29	15,273.26	152,73.26	15,784.86	8,502.12
RAILWAYS	312	4,62,095.03	5,659,66.06	7,04,966.85	2,54,962.86
ROAD TRANSPORT AND HIGHWAYS	878	5,29,993.60	5,374,96.73	5,46,560.65	3,22,468.99
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,901.76
TELECOMMUNICATIONS	3	14,013.36	253,35.07	25,335.07	17,990.26
URBAN DEVELOPMENT	30	2,81,283.00	2,898,53.18	3,03,630.26	1,51,127.79
WATER RESOURCES	47	26,322.76	718,15.10	71,923.93	22,885.65
DEFENCE PRODUCTION	1	246.31	2,10.00	210.00	136.16
COMMERCE	1	302.64	3,02.64	302.64	30.00
DEPARTMENT OF HIGHER EDUCATION	26	10,910.66	109,23.48	11,104.02	2,426.77
HOME AFFAIRS	7	2,306.97	25,46.83	3,327.60	1,183.80
RURAL DEVELOPMENT	4	889.43	9,68.31	899.87	472.48
DPIIT	2	17,352.09	173,52.09	18,990.30	12,090.60
DONER	1	151.33	1,51.33	151.33	149.33
Grand total	1718	21,99,181.52	24,69,171.14	26,36,710.50	12,52,298.40

TABLE-18

State-Wise Position of Central Sector Projects costing Rs. 150 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	74	1,24,241.29	1,72,051.82	38.48	6	39,547.65	93,840.76	24 - 180
2	ARUNACHAL PRADESH	41	22,951.00	37,016.20	61.28	4	6,882.14	20,760.58	59 - 155
3	ASSAM	53	49,175.61	53,790.59	9.38	7	5,692.32	8,493.29	12 - 60
4	BIHAR	103	1,24,613.06	1,61,188.44	29.35	10	30,865.91	56,867.93	36 - 141
5	GOA	10	5,332.77	5,343.26	0.20	0	0.00	0.00	-
6	GUJARAT	61	1,07,586.79	1,18,636.40	10.27	10	27,755.34	38,235.35	3 - 139
7	HARYANA	39	62,518.91	64,850.78	3.73	2	493.05	667.77	16 - 29
8	HIMACHAL PRADESH	19	21,918.19	31,802.62	45.10	2	5,270.59	11,368.59	9 - 162
9	JAMMU AND KASHMIR	26	45,784.09	71,711.34	56.63	1	2,500.00	27,949.00	241 - 241
10	KARNATAKA	56	70,450.03	82,675.13	17.35	7	31,734.94	38,114.57	20 - 264
11	KERALA	23	34,828.89	39,970.99	14.76	3	6,307.35	7,989.20	32 - 53
12	MADHYA PRADESH	76	67,158.93	76,531.18	13.96	11	10,727.89	18,422.25	12 - 48
13	MAHARASHTRA	239	2,03,714.25	2,25,925.96	10.90	20	44,683.78	67,054.09	8 - 216
14	MANIPUR	19	9,640.91	18,089.68	87.63	1	4,454.17	12,264.15	153 - 153
15	MEGHALAYA	13	5,269.68	8,588.18	62.97	0	0.00	0.00	-
16	MIZORAM	23	11,751.40	15,700.10	33.60	5	3,593.57	7,542.27	87 - 134
17	NAGALAND	36	16,462.29	21,094.41	28.14	1	2,326.52	6,911.00	132 - 132
18	ODISHA	80	1,15,673.21	1,20,106.58	3.83	13	14,838.17	22,375.55	6 - 204
19	PUNJAB	21	11,288.85	12,858.74	13.91	1	754.54	756.27	30 - 30
20	RAJASTHAN	54	51,369.15	59,216.94	15.28	4	14,044.26	19,348.73	18 - 75
21	SIKKIM	21	7,778.98	15,698.13	101.80	1	1,339.48	8,600.00	96 - 96
22	TAMIL NADU	70	1,23,008.14	1,42,839.68	16.12	9	11,406.45	22,446.67	27 - 198
23	TRIPURA	21	5,174.00	5,395.32	4.28	3	921.97	1,104.78	24 - 74
24	UTTAR PRADESH	119	1,53,485.51	1,57,906.11	2.88	7	22,336.71	24,117.81	12 - 68
25	WEST BENGAL	72	63,906.08	82,743.75	29.48	14	16,068.31	23,184.80	4 - 324
26	A & N ISLANDS	9	2,888.63	3,159.99	9.39	2	655.03	945.73	23 - 45
27	DELHI	33	89,350.41	90,970.21	1.81	5	6,881.00	8,340.91	3 - 94
28	PONDICHERRY	1	195.00	195.00	0.00	0	0.00	0.00	-
29	CHHATISGARH	46	78,872.08	89,155.66	13.04	9	25,751.75	35,569.08	18 - 84
30	JHARKHAND	41	68,724.52	73,429.78	6.85	5	22,180.34	23,726.74	12 - 188
31	UTTARAKHAND	32	35,922.92	50,877.81	41.63	4	21,012.91	32,349.95	3 - 132
32	TELANGANA	49	37,249.74	40,283.18	8.14	7	12,777.27	14,151.63	9 - 132
33	LADAKH	8	2,633.23	2,767.29	5.09	1	346.27	480.33	15 - 15
34	MULTI STATE	130	3,68,262.98	4,84,139.25	31.47	39	77,147.28	1,28,625.59	9 - 276
Total		1718	21,99,181.52	26,36,710.50	19.90	214	4,71,296.96	7,82,605.37	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-19

EXECUTIVE SUMMARY COSTING Rs. 1000 Crore and above			
Sl.No.	Sector	Projects on Monitor	Projects Additionally Delayed
1	RAILWAYS	156	8
2	ROAD TRANSPORT AND HIGHWAYS	152	4
3	PETROLEUM	60	4
4	POWER	42	9
5	COAL	31	4
6	URBAN DEVELOPMENT	23	4
7	CIVIL AVIATION	5	1
8	STEEL	5	0
9	ATOMIC ENERGY	4	0
10	HEALTH AND FAMILY WELFARE	4	0
11	DPIIT	2	0
12	MINES	1	0
13	HEAVY INDUSTRY	1	0
14	SHIPPING AND PORTS	1	0
15	TELECOMMUNICATIONS	1	0
16	WATER RESOURCES	1	0
17	HOME AFFAIRS	1	0
	Total	490	34

FLASH REPORT

TABLE-20

Month wise List of Completed Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of commissioning	Cumulative Expenditure (Rs. crore)
	June,2021			
	<u>PETROLEUM</u>			
1	MOTOR SPIRIT BLOCK PROJECT (MSBP) TO PRODUCE BSVI MS AT KOCHI REFINERY (BHARAT PETROLEUM CORPORATION LIMITED) - [N16000263]	3,313.00	02/2020	2,977.00
	<u>POWER</u>			
2	KAMENG HYDROELECTRIC PROJECT (NEEPCO) (NORTH EAST ELECTRIC POWER CORPORATION) - [180100239]	2,496.90	12/2009	8,231.56
	August,2021			
	<u>PETROLEUM</u>			
3	MUMBAI REFINERY EXPANSION PROJECT (HINDUSTAN PETROLEUM CORPORATION LIMITED) - [N16000281]	4,199.00	03/2020	4,808.22
	<u>POWER</u>			
4	MOUDA STPP STAGE 2 (NATIONAL THERMAL POWER CORPORATION) - [N18000132]	7,921.47	09/2016	5,302.00
5	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000140]	11,846.00	10/2017	13,766.78
6	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I (NATIONAL THERMAL POWER CORPORATION) - [N18000151]	11,638.55	01/2018	13,657.43
7	TANDA TPP STAGE-II (2X660 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000175]	9,188.98	07/2019	7,391.78
8	DARLIPALLI STPP STAGE-I (2X800 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000176]	12,532.44	12/2018	12,084.99
9	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture(NATIONAL THERMAL POWER CORPORATION) - [N18000193]	9,750.89	02/2017	11,130.00
10	KHARGONE STPP STAGE I (1320 MW) (NATIONAL THERMAL POWER CORPORATION) - [N18000205]	9,870.51	01/2020	10,019.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
11	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000548]	997.15	03/2019	975.08

TABLE-21

Month wise List of Deleted Projects Costing Rs. 1000 crore and above during				
2021-2022				
Sl. No	Project Name	Original Cost (Rs. crore)	Original Date of Commissioning	Cumulative Expenditure (Rs. crore)
	July,2021			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>			
1	CONSTRUCTION OF MEKA ROING HUNLI FROM EXISTING KM16 OF ROING HUNLI ROAD TO KM 21.500 OF HUNLI AN(NATIONAL HIGHWAYS AND INFRASTRUCTURE DEVELOPMENT CORPORATION Ltd.) - [N24000677]	1,253.10	03/2017	204.77
	August,2021			
2	RANCHI-RARGA-JAMSETHPUR (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000215]	1,479.00	06/2015	740.26
3	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK- PFUTSERO ROA(MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000315]	1,296.00	02/2011	782.76
4	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP (MINISTRY OF ROAD TRANSPORT AND HIGHWAYS (STATE PWDs)) - [N24000401]	954.43	09/2015	235.61
5	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000425]	2,288.18	05/2019	487.81
6	6 LANING OF AGRA - ETAWAH BYPASS (NATIONAL HIGHWAYS AUTHORITY OF INDIA) - [N24000452]	1,657.20	01/2019	0.00

TABLE-22

Projects Added / Completed / Dropped / Frozen Rs. 1000 Crore and above

No of Projects in Previous Month	499
No of Projects Completed/Dropped/Frozen in Current Month	14
No of Projects Elevated in Current Month	1
No of Projects added in Current Month	4
No of Projects in Current Month	490

Project status Rs. 1000 Crore and above						
Number of Projects						
With Respect To	Delayed	Ahead	On schedule	Without ODC but DOC available	Without D.O.C	Total
Original (Date)	212 (43.27%)	9 (1.84%)	64 (13.06%)	27 (5.51%)	178 (36.33%)	490
Latest Approved (Date)	136 (27.76%)	12 (2.45%)	145 (29.59%)	19 (3.88%)	178 (36.33%)	490

Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Project with No Revision in Cost	381	12,75,491.83	14,16,677.19	5,91,127.33	41.70	1,41,185.36	11.10
Project with Revision in Cost	109	6,82,279.16	6,98,805.70	4,09,218.15	58.60	16,526.54	2.40
Total	490	19,57,770.99	21,15,482.89	10,00,345.48	47.29	1,57,711.90	8.06
Original Cost of All Projects							
Original Cost	490	16,93,780.41	21,15,482.89	10,00,345.48	47.29	4,21,702.48	24.90

Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
Cost overrun							
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Original (OCE)	212	7,94,206.49	10,80,727.03	6,18,575.31	57.20	2,86,520.54	36.08
Latest Approved (RCE)	136	6,10,712.41	6,97,302.47	3,94,751.25	56.60	86,590.06	14.18

Additional Delayed Project cost Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
						Cost overrun	
With Respect to	No. of Projects	Sanctioned Cost	Anticipated Cost	Expenditure Cost	% Expenditure cost w.r.t anticipated cost	Rs crore	%
Latest Approved	34	1,84,872.14	1,96,052.44	1,20,213.67	61.30	11,180.30	6.00
Total	34	1,84,872.14	1,96,052.44	1,20,213.67	61.32	11,180.30	6.05

TABLE-23

Extent of cost overrun in projects with respect to original cost (Sector Wise) Rs. 1000 Crore and above									
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	48.51
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	7.88
3	COAL	31	1,15,520.67	1,20,369.94	4.20	4	32,770.17	37,619.44	14.80
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0.00
5	STEEL	5	24,006.86	30,839.01	28.46	2	17,207.85	24,040.00	39.70
6	PETROLEUM	60	3,01,532.96	3,07,677.30	2.04	15	53,911.61	71,328.85	32.31
7	POWER	42	2,13,886.71	2,75,086.32	28.61	20	1,08,221.40	1,71,494.36	58.47
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	1	1,718.00	3,727.30	116.96
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
10	RAILWAYS	156	3,90,765.14	6,24,898.32	59.92	122	2,05,464.63	4,40,881.81	114.58
11	ROAD TRANSPORT AND HIGHWAYS	152	2,33,854.51	2,45,961.09	5.18	42	56,601.05	70,739.38	24.98
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	84.97
14	URBAN DEVELOPMENT	23	2,78,636.14	3,00,963.73	8.01	7	97,725.70	1,20,132.49	22.93
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	447.22
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		490	16,93,780.41	21,15,482.89	24.90	224	6,47,017.75	10,86,196.80	67.88

^ - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-24

Extent of cost overrun in projects with respect to original cost (State Wise) Rs.							1000	Crore and above	
(All Cost/ Expenditure in Rs. crore)									
						Projects with cost overrun^			
Sl.No	State	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Cost overrun (%)
1	ANDHRA PRADESH	23	1,03,670.37	1,51,341.40	45.98	10	45,532.51	1,02,125.54	124.29
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	2	8,264.33	22,029.33	166.56
3	ASSAM	8	33,271.03	35,800.76	7.60	4	4,630.48	7,160.21	54.63
4	BIHAR	29	91,524.56	1,25,836.81	37.49	16	46,877.81	81,825.56	74.55
5	GUJARAT	23	87,132.33	97,455.51	11.85	10	31,206.03	42,188.26	35.19
6	HARYANA	13	51,125.78	52,305.78	2.31	1	1,108.00	2,288.00	106.50
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	8,237.58	18,122.01	119.99
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	3	6,236.00	32,296.00	417.90
9	KARNATAKA	18	54,648.17	66,415.89	21.53	12	43,122.74	54,890.46	27.29
10	KERALA	10	29,165.92	33,917.04	16.29	8	16,604.02	21,355.14	28.61
11	MADHYA PRADESH	20	39,277.37	47,992.47	22.19	9	11,154.92	20,387.07	82.76
12	MAHARASHTRA	45	1,24,625.66	1,49,758.19	20.17	19	55,363.97	81,203.43	46.67
13	MANIPUR	2	5,032.79	13,575.20	169.74	2	5,032.79	13,575.20	169.74
14	MEGHALAYA	1	906.46	4,083.02	350.44	1	906.46	4,083.02	350.44
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	130.69
16	NAGALAND	2	6,600.52	11,185.00	69.46	1	2,326.52	6,911.00	197.05
17	ODISHA	36	91,606.34	99,463.99	8.58	11	15,603.93	23,461.58	50.36
18	PUNJAB	4	5,049.00	6,182.38	22.45	2	2,557.95	3,868.29	51.23
19	RAJASTHAN	15	32,394.98	39,028.50	20.48	4	15,533.72	22,167.24	42.70
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	542.04
21	TAMIL NADU	28	1,03,421.30	1,22,011.29	17.98	13	36,726.73	55,711.72	51.69
22	UTTAR PRADESH	44	1,19,109.19	1,23,839.81	3.97	13	31,802.29	37,474.04	17.83
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	14	25,352.53	43,152.57	70.21
24	DELHI	9	80,186.38	81,749.70	1.95	3	10,256.21	11,898.73	16.01
25	CHHATISGARH	17	66,005.94	75,749.95	14.76	7	25,902.96	35,748.99	38.01
26	JHARKHAND	15	61,033.49	65,171.82	6.78	6	27,885.12	33,579.45	20.42
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	5	24,870.06	39,070.51	57.10
28	TELANGANA	6	19,991.02	22,099.10	10.55	3	12,977.58	15,453.54	19.08
29	MULTI STATE	62	3,39,965.59	4,50,548.72	32.53	40	1,27,211.56	2,40,048.46	88.70
Total		490	16,93,780.41	21,15,482.89	24.90	224	6,47,017.75	10,86,196.80	67.88

[^] - Cost Overrun = Anticipated Cost minus Original Cost

TABLE-25

Extent of time overrun in projects with respect to original schedule Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Original Cost	Anticipated Cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	4	67,120.00	80,348.00	36 - 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	5	7,613.90	7,703.90	4 - 27
3	COAL	31	1,15,520.67	1,20,369.94	4.20	16	59,676.23	62,451.82	12 - 228
4	MINES	1	5,540.00	5,540.00	0.00	1	5,540.00	5,540.00	20 - 20
5	STEEL	5	24,006.86	30,839.01	28.46	4	21,099.86	27,932.01	36 - 80
6	PETROLEUM	60	3,01,532.96	3,07,677.30	2.04	29	1,22,503.04	1,29,324.61	4 - 110
7	POWER	42	2,13,886.71	2,75,086.32	28.61	27	1,60,217.95	2,16,433.41	4 - 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	156	3,90,765.14	6,24,898.32	59.92	99	1,66,627.91	2,92,493.71	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	152	2,33,854.51	2,45,961.09	5.18	13	20,896.11	21,059.68	15 - 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	23	2,78,636.14	3,00,963.73	8.01	9	1,32,083.24	1,48,578.02	12 - 73
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29 - 29
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29 - 29
Total		490	16,93,780.41	21,15,482.89	24.90	212	7,94,206.49	10,80,727.03	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-26

<u>Extent of time overrun in projects with respect to original schedule(State Wise)</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	23	1,03,670.37	1,51,341.40	45.98	9	78,917.36	1,24,288.47	24 - 180
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	35,800.76	7.60	4	4,630.48	7,160.21	12 - 48
4	BIHAR	29	91,524.56	1,25,836.81	37.49	10	33,252.42	58,706.95	14 - 141
5	GUJARAT	23	87,132.33	97,455.51	11.85	8	28,375.60	38,291.84	3 - 74
6	HARYANA	13	51,125.78	52,305.78	2.31	3	6,046.66	6,046.66	7 - 29
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	3	7,756.52	13,854.52	9 - 162
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	2	10,612.12	36,061.12	63 - 241
9	KARNATAKA	18	54,648.17	66,415.89	21.53	6	34,583.00	40,637.64	26 - 264
10	KERALA	10	29,165.92	33,917.04	16.29	3	6,307.35	7,989.20	32 - 53
11	MADHYA PRADESH	20	39,277.37	47,992.47	22.19	12	18,383.83	25,424.45	12 - 48
12	MAHARASHTRA	45	1,24,625.66	1,49,758.19	20.17	17	61,074.52	82,573.72	7 - 216
13	MANIPUR	2	5,032.79	13,575.20	169.74	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	120 - 120
16	NAGALAND	2	6,600.52	11,185.00	69.46	1	2,326.52	6,911.00	132 - 132
17	ODISHA	36	91,606.34	99,463.99	8.58	20	46,784.99	53,851.88	5 - 228
18	PUNJAB	4	5,049.00	6,182.38	22.45	1	1,069.59	1,069.59	22 - 22
19	RAJASTHAN	15	32,394.98	39,028.50	20.48	4	17,374.02	22,133.02	4 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	28	1,03,421.30	1,22,011.29	17.98	13	59,759.13	69,451.46	3 - 145
22	UTTAR PRADESH	44	1,19,109.19	1,23,839.81	3.97	17	72,880.51	73,846.66	5 - 48
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	14	28,463.62	35,177.64	4 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	6	48,279.73	49,386.32	15 - 65
25	CHHATISGARH	17	66,005.94	75,749.95	14.76	7	27,278.34	36,436.75	18 - 80
26	JHARKHAND	15	61,033.49	65,171.82	6.78	8	50,765.98	50,522.86	13 - 188
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	4	21,748.36	32,785.84	3 - 132
28	TELANGANA	6	19,991.02	22,099.10	10.55	3	13,183.42	13,214.26	23 - 168
29	MULTI STATE	62	3,39,965.59	4,50,548.72	32.53	33	99,879.97	1,48,526.94	9 - 276
Total		490	16,93,780.41	21,15,482.89	24.90	212	7,94,206.49	10,80,727.03	

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-27

<u>Extent of time overrun in projects with respect to latest schedule</u>						Rs. 1000 Crore and above			
(All Cost/ Expenditure in Rs. crore)						Projects with time overruns\$			
Sl.No	Sector	No. of Projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	3	63,628.00	73,508.00	36 - 75
2	CIVIL AVIATION	5	8,168.90	7,703.90	-5.69	5	8,168.90	7,703.90	4 - 27
3	COAL	31	1,17,884.39	1,20,369.94	2.11	10	27,992.87	30,477.62	0 - 168
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	-
5	STEEL	5	30,421.86	30,839.01	1.37	1	1,034.01	1,034.01	61 - 61
6	PETROLEUM	60	3,17,603.47	3,07,677.30	-3.13	6	13,761.10	12,879.70	4 - 37
7	POWER	42	2,74,280.05	2,75,086.32	0.29	15	1,30,539.17	1,30,500.01	11 - 132
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	-
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9 - 9
10	RAILWAYS	156	4,92,859.42	6,24,898.32	26.79	74	1,62,645.23	2,35,177.74	3 - 324
11	ROAD TRANSPORT AND HIGHWAYS	152	2,39,157.07	2,45,961.09	2.85	12	19,522.83	19,686.40	15 - 105
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	-
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	1	24,664.00	24,664.00	80 - 80
14	URBAN DEVELOPMENT	23	2,87,186.65	3,00,963.73	4.80	6	1,00,637.22	1,02,651.22	12 - 73
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	1	55,548.87	55,548.87	25 - 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29 - 29
17	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	-
Total		490	19,57,770.99	21,15,482.89	8.06	136	6,10,712.41	6,97,302.47	

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-28

<u>Extent of cost overrun in projects with respect to latest cost</u>						Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)			
						Projects with cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Cost overrun (%)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	41.55
2	CIVIL AVIATION	5	8,168.90	7,703.90	-5.69	1	1,142.00	1,232.00	7.88
3	COAL	31	1,17,884.39	1,20,369.94	2.11	2	19,898.73	22,384.28	12.49
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0.00
5	STEEL	5	30,421.86	30,839.01	1.37	1	1,682.85	2,100.00	24.79
6	PETROLEUM	60	3,17,603.47	3,07,677.30	-3.13	3	5,130.52	6,309.34	22.98
7	POWER	42	2,74,280.05	2,75,086.32	0.29	6	29,820.22	32,699.84	9.66
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	0.00
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	2	2,928.00	3,299.00	12.67
10	RAILWAYS	156	4,92,859.42	6,24,898.32	26.79	105	1,74,144.97	3,09,643.87	77.81
11	ROAD TRANSPORT AND HIGHWAYS	152	2,39,157.07	2,45,961.09	2.85	40	55,271.66	66,369.65	20.08
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0.00
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	0	0.00	0.00	0.00
14	URBAN DEVELOPMENT	23	2,87,186.65	3,00,963.73	4.80	4	43,354.79	57,131.87	31.78
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0.00
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	64.04
17	DPIIT	2	17,352.09	18,990.30	9.44	2	17,352.09	18,990.30	9.44
Total		490	19,57,770.99	21,15,482.89	8.06	169	3,75,724.04	5,55,819.15	47.93

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

TABLE-29

Extent of time & cost overrun in projects with respect to latest schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Latest Approved Cost	Anticipated Cost	Cost Overrun (%)	No.	Latest Approved Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	70,468.00	80,348.00	14.02	2	23,779.00	33,659.00	74- 75
2	CIVIL AVIATION	5	8,168.90	7,703.90	-5.69	1	1,142.00	1,232.00	24- 24
3	COAL	31	1,17,884.39	1,20,369.94	2.11	1	2,661.73	5,146.48	60- 60
4	MINES	1	6,435.90	5,540.00	-13.92	0	0.00	0.00	0- 0
5	STEEL	5	30,421.86	30,839.01	1.37	0	0.00	0.00	0- 0
6	PETROLEUM	60	3,17,603.47	3,07,677.30	-3.13	0	0.00	0.00	0- 0
7	POWER	42	2,74,280.05	2,75,086.32	0.29	2	17,866.58	19,383.42	15- 54
8	HEAVY INDUSTRY	1	3,727.30	3,727.30	0.00	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	156	4,92,859.42	6,24,898.32	26.79	54	97,883.99	1,71,551.49	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	152	2,39,157.07	2,45,961.09	2.85	1	2,848.00	3,379.45	105- 105
12	SHIPPING AND PORTS	1	4,633.81	4,633.81	0.00	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	24,664.00	24,664.00	0.00	0	0.00	0.00	0- 0
14	URBAN DEVELOPMENT	23	2,87,186.65	3,00,963.73	4.80	1	10,773.00	12,787.00	44- 44
15	WATER RESOURCES	1	55,548.87	55,548.87	0.00	0	0.00	0.00	0- 0
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29- 29
17	DPIIT	2	17,352.09	18,990.30	9.44	0	0.00	0.00	0- 0
Total		490	19,57,770.99	21,15,482.89	8.06	64	1,59,524.51	2,50,609.84	

^ - Cost Overrun = Anticipated Cost minus Revised/Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Revised/Original Date of Commissioning

TABLE-30

Extent of time & cost overrun in projects with respect to original schedule&cost Rs. 1000 Crore and above (All Cost/ Expenditure in Rs. crore)									
						Projects with time\$ & cost overruns^			
Sl.No.	Sector	No. of projects	Original Cost	Anticipated Cost	Cost Overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ATOMIC ENERGY	4	67,120.00	80,348.00	19.71	3	27,271.00	40,499.00	74- 145
2	CIVIL AVIATION	5	7,613.90	7,703.90	1.18	1	1,142.00	1,232.00	24- 24
3	COAL	31	1,15,520.67	1,20,369.94	4.20	3	26,863.06	29,638.65	12- 188
4	MINES	1	5,540.00	5,540.00	0.00	0	0.00	0.00	0- 0
5	STEEL	5	24,006.86	30,839.01	28.46	2	17,207.85	24,040.00	36- 80
6	PETROLEUM	60	3,01,532.96	3,07,677.30	2.04	14	53,088.34	70,191.06	8- 110
7	POWER	42	2,13,886.71	2,75,086.32	28.61	14	92,710.70	1,50,999.51	15- 162
8	HEAVY INDUSTRY	1	1,718.00	3,727.30	116.96	0	0.00	0.00	0- 0
9	HEALTH AND FAMILY WELFARE	4	6,160.00	6,531.00	6.02	1	1,351.00	1,471.00	9- 9
10	RAILWAYS	156	3,90,765.14	6,24,898.32	59.92	76	1,23,390.95	2,50,391.74	3- 324
11	ROAD TRANSPORT AND HIGHWAYS	152	2,33,854.51	2,45,961.09	5.18	1	2,848.00	3,379.45	105- 105
12	SHIPPING AND PORTS	1	5,369.18	4,633.81	-13.70	0	0.00	0.00	0- 0
13	TELECOMMUNICATIONS	1	13,334.00	24,664.00	84.97	1	13,334.00	24,664.00	80- 80
14	URBAN DEVELOPMENT	23	2,78,636.14	3,00,963.73	8.01	3	60,314.14	76,888.12	36- 73
15	WATER RESOURCES	1	10,151.04	55,548.87	447.22	1	10,151.04	55,548.87	25- 25
16	HOME AFFAIRS	1	1,219.21	2,000.00	64.04	1	1,219.21	2,000.00	29- 29
17	DPIIT	2	17,352.09	18,990.30	9.44	1	4,773.00	5,178.00	29- 29
Total		490	16,93,780.41	21,15,482.89	24.90	122	4,35,664.29	7,36,121.40	

^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

TABLE-31

<u>List of projects completed/dropped/Frozen during current month</u>							
Rs. 1000 Crore and above							
(All Cost/ Expenditure in Rs. crore)							
			Original		Now anticipated		
Sl.No	Project	DOA	Cost	DOC	Cost	DOC	Final Expenditure
	<u>PETROLEUM</u>						
1	MUMBAI REFINERY EXPANSION PROJECT	09/2015	4,199.00	03/2020	5,060.00	08/2021	4,808.22
	<u>POWER</u>						
2	GADARWARA SUPER THERMAL POWER PROJECT STAGE-I	03/2013	11,638.55	01/2018	15,105.22	N.A.	13,657.43
3	TANDA TPP STAGE-II (2X660 MW)	09/2014	9,188.98	07/2019	9,842.02	N.A.	7,391.78
4	DARLIPALLI STPP STAGE-I (2X800 MW)	02/2014	12,532.44	12/2018	13,140.91	07/2021	12,084.99
5	MOUDA STPP STAGE 2	03/2012	7,921.47	09/2016	7,921.47	N.A.	5,302.00
6	LARA SUPER THERMAL POWER PROJECT STAGE-I (2 X 800 MW)	12/2012	11,846.00	10/2017	12,739.82	N.A.	13,766.78
7	MUNPL-MEJA TPP - JV (2X660 MW) Joint Venture	04/2012	9,750.89	02/2017	12,176.28	N.A.	11,130.00
8	KHARGONE STPP STAGE I (1320 MW)	03/2015	9,870.51	01/2020	11,148.86	N.A.	10,019.31
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
9	WIDENING OF 2(TWO) LANING OF LONGLENG-CHANTONGYA ROAD, MON-TAMLU-MERANGKONG ROAD, PHEK-PFUTSERO ROA ITEM RATE	12/2010	1,296.00	02/2011	1,296.00	N.A.	782.76
10	RANCHI-RARGA-JAMSETHPUR PPP (ANNUITY)	12/2012	1,479.00	06/2015	1,479.00	N.A.	740.26
11	SIDHI TO SINGRAULI SECTION OF NH-75E (4L) IN MP BOT (TOLL)	11/2011	954.43	09/2015	1,191.51	10/2021	235.61
12	4-LANNING OF MAHULIA BAHARAGORA-JH/WB BORDER SECTION	02/2016	997.15	03/2019	1,115.95	N.A.	975.08
13	4 LANING OF AMRAVATI - CHIKHLI (PKG-I) PPP (BOT)	07/2015	2,288.18	05/2019	2,288.18	N.A.	487.81
14	6 LANING OF AGRA - ETAWAH BYPASS PPP (BOT)	07/2015	1,657.20	01/2019	1,657.20	N.A.	0.00

TABLE-32

List of projects added Rs. 1000 Crore and above					(August 2021)	
			Original		Anticipated	
Sl.No	Project	DOA	Cost	DOC	Cost	DOC
	<u>PETROLEUM</u>					
1	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	2,998.00	3/2030	2,998.00	3/2030
2	CGD PROJECT AT SALEM DISTRICT	10/2018	1,304.00	3/2030	1,304.00	3/2030
3	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	2,880.00	8/2027	2,880.00	8/2027
4	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2,996.00	2/2028	2,996.00	2/2028

FLASH REPORT

TABLE-33

Milestones (Cumulative due & achieved)	Rs. 1000	Crore and above
Total	2600	
Achieved up to month	1577	

TABLE-34

List of projects reporting additional delayed Rs. 1000 Crore and above							(August 2021)
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
	<u>CIVIL AVIATION</u>						
1	CCS INTERNATIONAL AIRPORT , LUCKNOW AAI	1,383.00	1,383.00	09/2021	09/2022	12/2023	15
	<u>COAL</u>						
2	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW NLC	17,237.00	17,237.80	11/2021	07/2022	11/2022	4
3	MOONIDIH XV SEAM UG BCCL	1,230.27	1,230.27	04/2015	03/2022	02/2023	11
4	GARJANBAHAL OCP MCL	1,375.38	1,375.38	03/2021	03/2024	09/2025	18
5	RECAST EPR AMRAPALI OC CCL	4,983.58	4,983.58	03/2020	03/2024	03/2028	48
	<u>PETROLEUM</u>						
6	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY BPCL	4,588.29	5,245.96	08/2018	08/2021	09/2021	1
7	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI IOCL EPC	1,398.00	1,398.00	12/2023	08/2023	09/2023	1
8	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY IOCL	1,019.00	1,019.00	01/2023	01/2023	05/2023	4
9	CITY GAS DISTRIBUTION IN WEST BENGAL HPCL EPC	5,830.20	5,830.20	03/2031	08/2029	08/2031	24
	<u>POWER</u>						
10	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P PGCIL	14,733.37	14,733.37	11/2019	08/2021	09/2021	1
11	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN PGCIL Central Sector Projects	1,931.39	1,931.39	02/2020	08/2021	09/2021	1
12	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) PGCIL	1,394.52	1,394.52	05/2017	10/2021	12/2021	2
13	NPGCPL-NABINAGAR STPP - JV (3X660 MW) NTPC Joint Venture	12,964.60	17,304.00	05/2018	12/2021	02/2022	2
14	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL NTPC	1,885.13	2,311.89	12/2018	09/2021	11/2021	2

List of projects reporting additional delayed Rs. 1000 Crore and above (August 2021)							
Sl. No	Project name	Cost (Rs.crore)		DOC reported			Delay (in months)
		Original	Anticipated	Original	Last month	This month	
15	TELANGANA SUPER THERMAL POWER PROJECT PHASE I NTPC	10,598.98	10,997.70	11/2020	07/2022	10/2022	3
16	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES PGCIL	5,111.33	6,700.00	12/2018	12/2021	03/2022	3
17	PATRATU STPP-I (3X800MW) NTPC	18,668.00	17,112.00	03/2023	09/2024	02/2025	5
18	NOKHRA NTPC EPC	1,722.14	1,722.14	09/2021	01/2022	01/2023	12
	<u>RAILWAYS</u>						
19	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF SR	931.98	1,121.00	N.A.	07/2021	08/2021	1
20	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) NFR	602.27	2,144.78	12/2021	07/2021	09/2021	2
21	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I IRCON	3,055.00	3,055.15	09/2018	03/2022	06/2022	3
22	RAMGANJMUNDI-BHOPAL (NL),WCR WCR	424.60	2,909.99	03/2021	03/2023	03/2024	12
23	VIRAMGAM-SAMAKHIALI (DL) WR	1,037.15	1,383.69	03/2021	12/2021	12/2022	12
24	MUZAFFARPUR SAGALI DOUBLING 100.60 KM ECR	731.64	1,185.73	03/2021	06/2022	03/2024	21
25	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING NCR	4,329.53	4,329.53	03/2023	03/2023	06/2025	27
26	BAGALKOT-KUDACHI NL SWR	986.30	1,530.09	03/2016	12/2023	12/2026	36
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
27	FOUR LANE OF YADGIRI - WARANGAL NHAI	1,423.96	1,056.08	11/2018	06/2021	08/2021	2
28	FOUR LANE OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU NHAI	1,166.26	1,296.93	N.A.	08/2021	01/2022	5
29	DELHI AGRA APPROVED LENGTH 180.0 KM NHAI PPP (BOT)	1,928.22	1,928.22	04/2015	06/2021	12/2021	6
30	6-LANE OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- NHAI	1,031.95	1,031.95	N.A.	09/2021	03/2022	6
	<u>URBAN DEVELOPMENT</u>						

<u>List of projects reporting additional delayed</u> Rs. 1000 Crore and above (August 2021)							
		Cost (Rs.crore)		DOC reported			
Sl. No	Project name	Original	Anticipated	Original	Last month	This month	Delay (in months)
31	DELHI MRTS PHASE-III DMRC	38,585.00	38,585.00	03/2016	07/2021	08/2021	1
32	KANPUR METRO RAIL PROJECT LMRCL Public Private (SPV)	11,076.48	11,076.48	03/2024	03/2024	03/2025	12
33	AGRA METRO RAIL PROJECT LMRCL Public Private (SPV)	8,379.62	8,379.62	03/2024	03/2024	05/2025	14
34	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I CPWD	1,128.00	1,128.00	03/2022	03/2022	06/2023	15

FLASH REPORT

TABLE-35

<u>Sector wise analysis of projects</u> Rs. 1000 Crore and above					
		Cost (Rs. crore)			
Sector	Number of projects	Original	Latest	Anticipated	Cumulative Expenditure
ATOMIC ENERGY	4	67,120.00	704,68.00	80,348.00	61,584.57
CIVIL AVIATION	5	7,613.90	81,68.90	7,703.90	2,095.84
COAL	31	1,15,520.67	1,178,84.39	1,20,369.94	41,798.23
MINES	1	5,540.00	64,35.90	5,540.00	788.26
STEEL	5	24,006.86	304,21.86	30,839.01	23,438.15
PETROLEUM	60	3,01,532.96	3,176,03.47	3,07,677.30	1,02,752.65
POWER	42	2,13,886.71	2,742,80.05	2,75,086.32	1,79,115.89
HEAVY INDUSTRY	1	1,718.00	37,27.30	3,727.30	3,517.10
HEALTH AND FAMILY WELFARE	4	6,160.00	61,60.00	6,531.00	1,094.65
RAILWAYS	156	3,90,765.14	4,928,59.42	6,24,898.32	2,17,989.34
ROAD TRANSPORT AND HIGHWAYS	152	2,33,854.51	2,391,57.07	2,45,961.09	1,65,821.34
SHIPPING AND PORTS	1	5,369.18	46,33.81	4,633.81	1,901.76
TELECOMMUNICATIONS	1	13,334.00	246,64.00	24,664.00	17,845.00
URBAN DEVELOPMENT	23	2,78,636.14	2,871,86.65	3,00,963.73	1,49,620.04
WATER RESOURCES	1	10,151.04	555,48.87	55,548.87	17,935.78
HOME AFFAIRS	1	1,219.21	12,19.21	2,000.00	956.28
DPIIT	2	17,352.09	173,52.09	18,990.30	12,090.60
Grand total	490	16,93,780.41	19,57,770.99	21,15,482.89	10,00,345.48


TABLE-36

State-Wise Position of Central Sector Projects costing Rs. 1000 Crore and above showing Both Time and Cost Overruns (All Cost/ Expenditure in Rs. crore)									
						Projects with time overruns\$			
Sl.No	State	No. of Projects	Original Cost	Anticipated cost	Cost overrun (%)	No.	Original Cost	Anticipated Cost	Range of T.O.R (in months)
1	ANDHRA PRADESH	23	1,03,670.37	1,51,341.40	45.98	6	39,547.65	93,840.76	24 - 180
2	ARUNACHAL PRADESH	3	9,982.92	23,747.92	137.89	1	6,285.33	19,992.43	155 - 155
3	ASSAM	8	33,271.03	35,800.76	7.60	4	4,630.48	7,160.21	12 - 48
4	BIHAR	29	91,524.56	1,25,836.81	37.49	7	29,343.85	54,798.38	36 - 141
5	GUJARAT	23	87,132.33	97,455.51	11.85	6	25,968.21	35,884.45	3 - 74
6	HARYANA	13	51,125.78	52,305.78	2.31	0	0.00	0.00	-
7	HIMACHAL PRADESH	8	17,307.75	27,192.18	57.11	2	5,270.59	11,368.59	9 - 162
8	JAMMU AND KASHMIR	15	42,035.66	67,962.91	61.68	1	2,500.00	27,949.00	241 - 241
9	KARNATAKA	18	54,648.17	66,415.89	21.53	4	29,931.16	35,985.80	36 - 264
10	KERALA	10	29,165.92	33,917.04	16.29	3	6,307.35	7,989.20	32 - 53
11	MADHYA PRADESH	20	39,277.37	47,992.47	22.19	7	9,716.13	17,273.80	12 - 48
12	MAHARASHTRA	45	1,24,625.66	1,49,758.19	20.17	11	40,968.11	62,556.06	8 - 216
13	MANIPUR	2	5,032.79	13,575.20	169.74	1	4,454.17	12,264.15	153 - 153
14	MEGHALAYA	1	906.46	4,083.02	350.44	0	0.00	0.00	-
15	MIZORAM	1	2,393.47	5,521.45	130.69	1	2,393.47	5,521.45	120 - 120
16	NAGALAND	2	6,600.52	11,185.00	69.46	1	2,326.52	6,911.00	132 - 132
17	ODISHA	36	91,606.34	99,463.99	8.58	9	13,130.22	20,197.11	21 - 204
18	PUNJAB	4	5,049.00	6,182.38	22.45	0	0.00	0.00	-
19	RAJASTHAN	15	32,394.98	39,028.50	20.48	1	12,320.00	17,079.00	75 - 75
20	SIKKIM	1	1,339.48	8,600.00	542.04	1	1,339.48	8,600.00	96 - 96
21	TAMIL NADU	28	1,03,421.30	1,22,011.29	17.98	6	10,455.67	20,543.00	27 - 145
22	UTTAR PRADESH	44	1,19,109.19	1,23,839.81	3.97	5	21,973.71	23,562.80	12 - 39
23	WEST BENGAL	25	47,280.10	65,048.81	37.58	6	14,041.95	20,771.30	60 - 324
24	DELHI	9	80,186.38	81,749.70	1.95	2	5,992.21	7,178.00	29 - 29
25	CHHATISGARH	17	66,005.94	75,749.95	14.76	5	24,001.00	33,261.43	18 - 80
26	JHARKHAND	15	61,033.49	65,171.82	6.78	2	21,330.91	22,643.79	54 - 188
27	UTTARAKHAND	7	27,696.84	41,897.29	51.27	3	20,364.58	31,402.06	3 - 132
28	TELANGANA	6	19,991.02	22,099.10	10.55	1	10,598.98	10,997.70	23 - 23
29	MULTI STATE	62	3,39,965.59	4,50,548.72	32.53	26	70,472.56	1,20,389.93	9 - 276
Total		490	16,93,780.41	21,15,482.89	24.90	122	4,35,664.29	7,36,121.40	


^ - Cost Overrun = Anticipated Cost minus Original Cost

\$- Time overrun = Anticipated Date of Commissioning minus Original Date of Commissioning

Graphical Presentation of All Projects w.r.t. Original Schedule

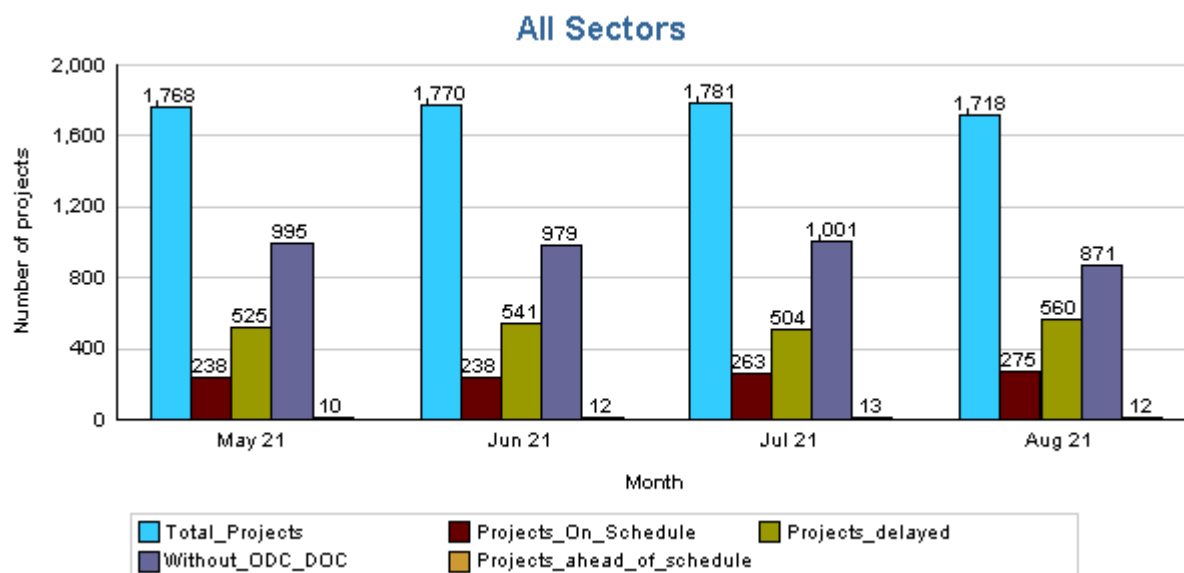

Break-up of 560 Delayed projects in August 2021

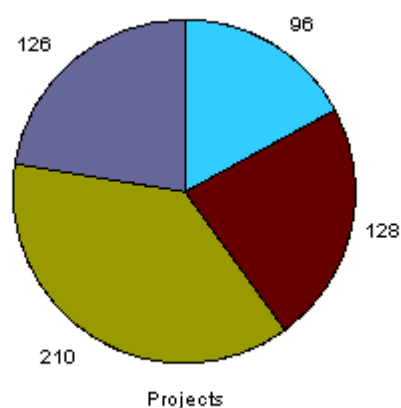


Delay in Months


Legend:

- 1-12 (Light Blue)
- 13-24 (Dark Red)
- 25-60 (Olive Green)
- MORE THAN 60 (Purple)

Graphical Presentation of RURAL DEVELOPMENT Sector

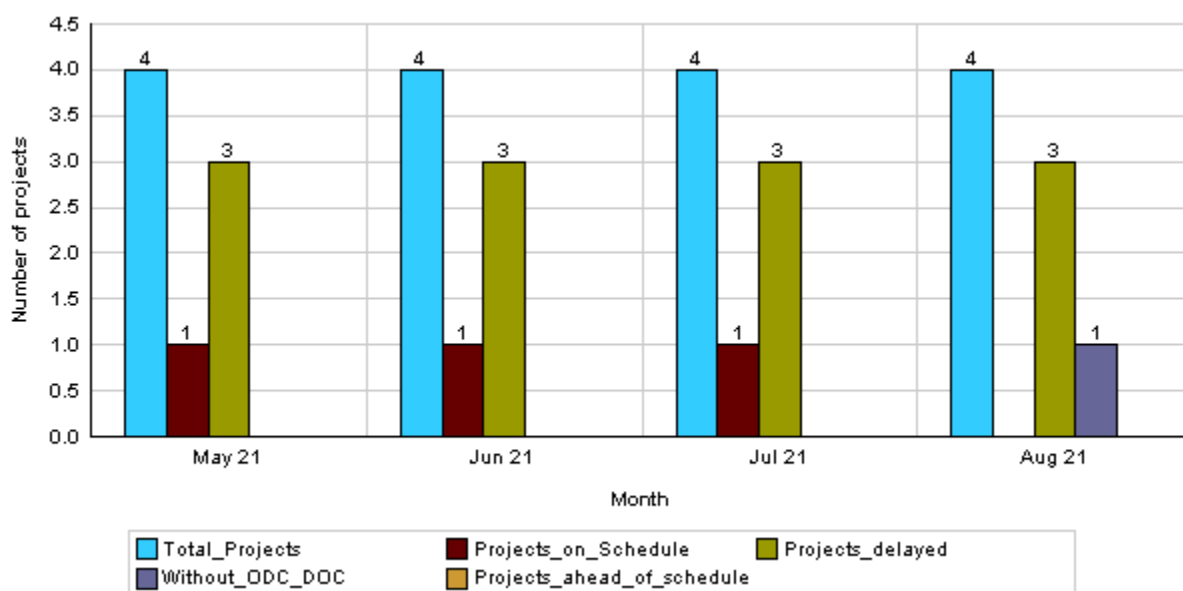


Break-up of 3 Delayed projects in August 2021

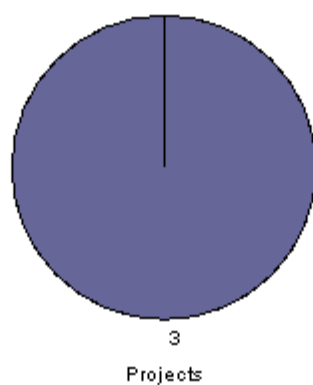


Delay in Months

1-12	13-24	25-60	MORE THAN 60

Graphical Presentation of HOME AFFAIRS Sector

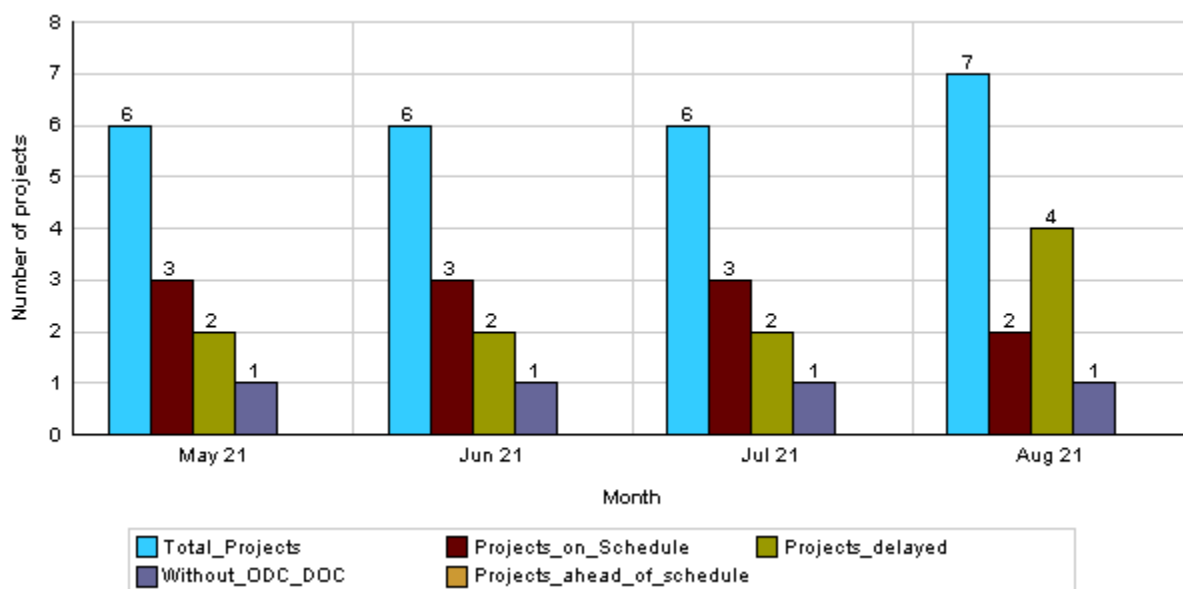


Break-up of 4 Delayed projects in August 2021

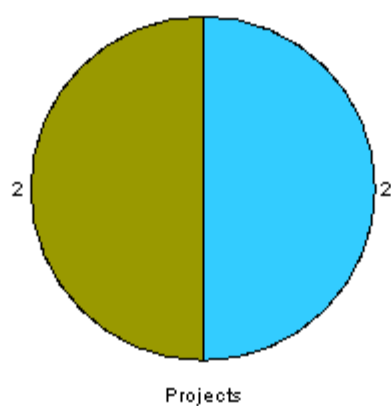


Delay in Months

1-12
 13-24
 25-60
 MORE THAN 60

Graphical Presentation of DEPARTMENT OF HIGHER EDUCATION Sector

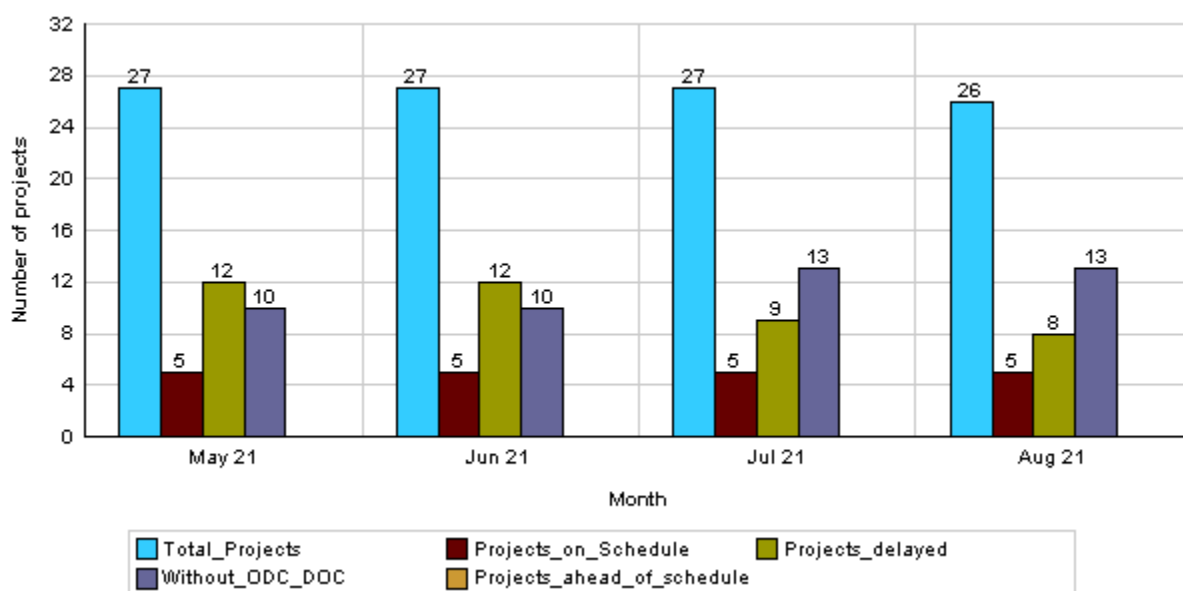


Break-up of 8 Delayed projects in August 2021

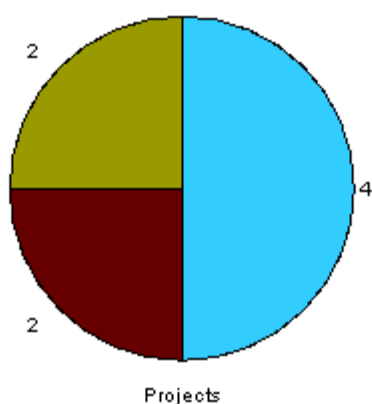


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of WATER RESOURCES Sector

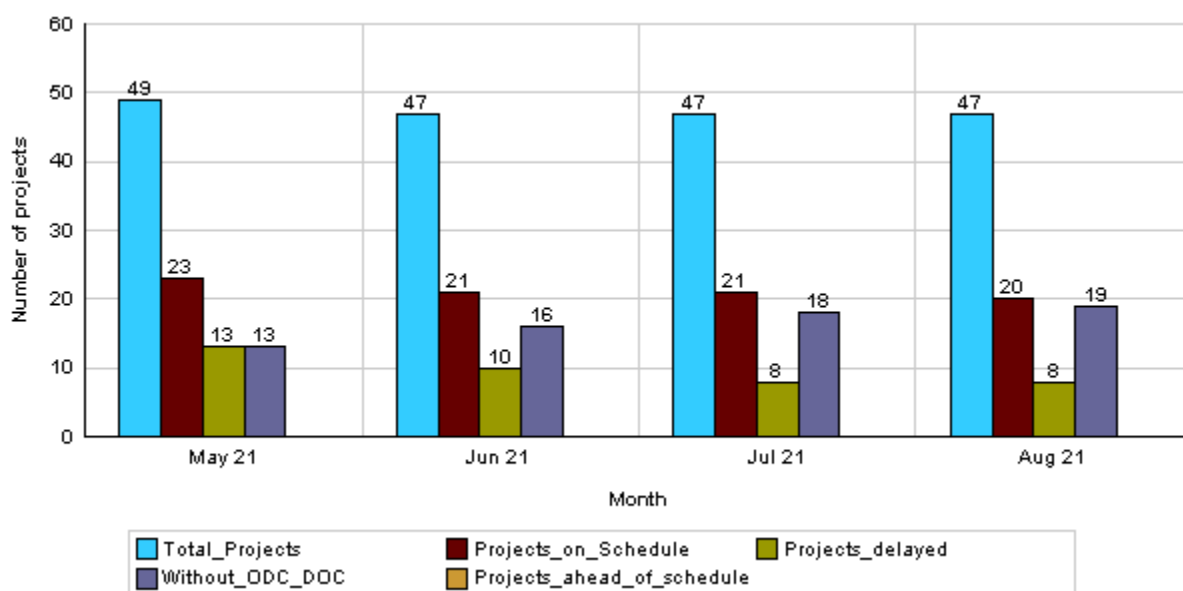


Break-up of 8 Delayed projects in August 2021

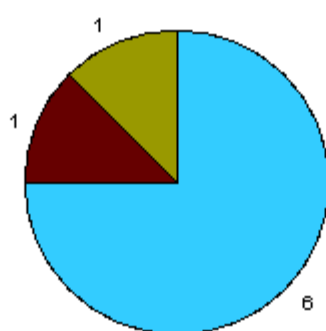


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of URBAN DEVELOPMENT Sector

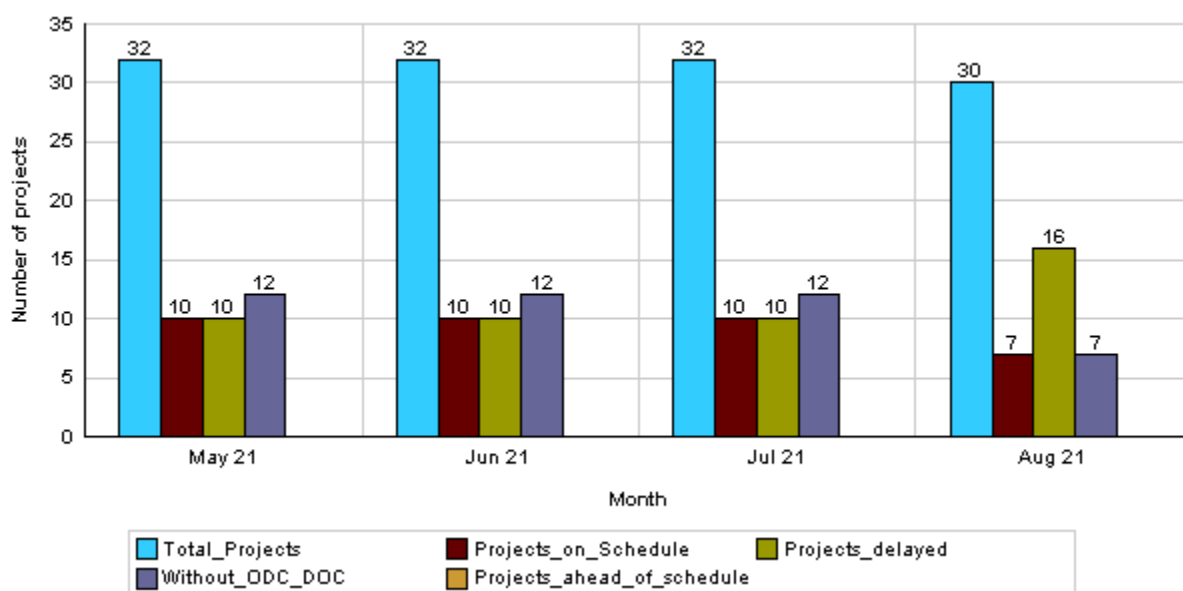


Break-up of 16 Delayed projects in August 2021

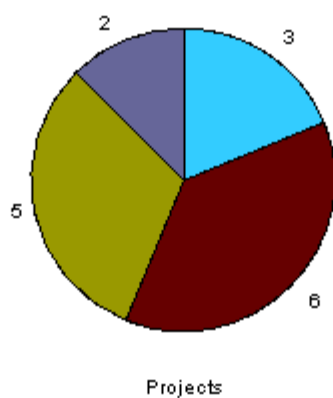


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of TELECOMMUNICATIONS Sector

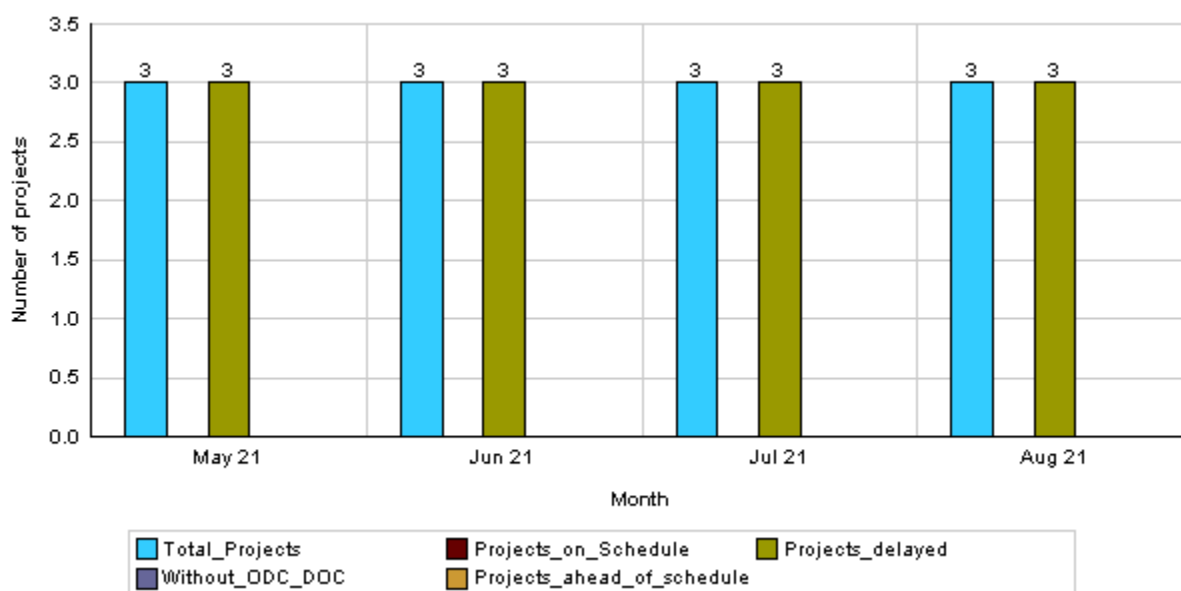

Break-up of 3 Delayed projects in August 2021

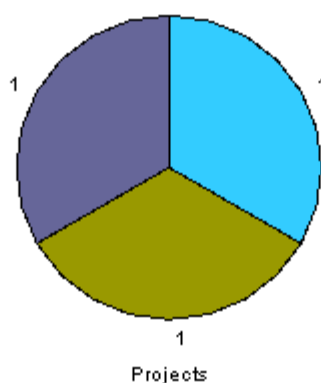


Delay in Months


Legend:

- 1-12 (Blue)
- 13-24 (Dark Red)
- 25-60 (Olive)
- MORE THAN 60 (Dark Blue)

Graphical Presentation of ROAD TRANSPORT AND HIGHWAYS Sector

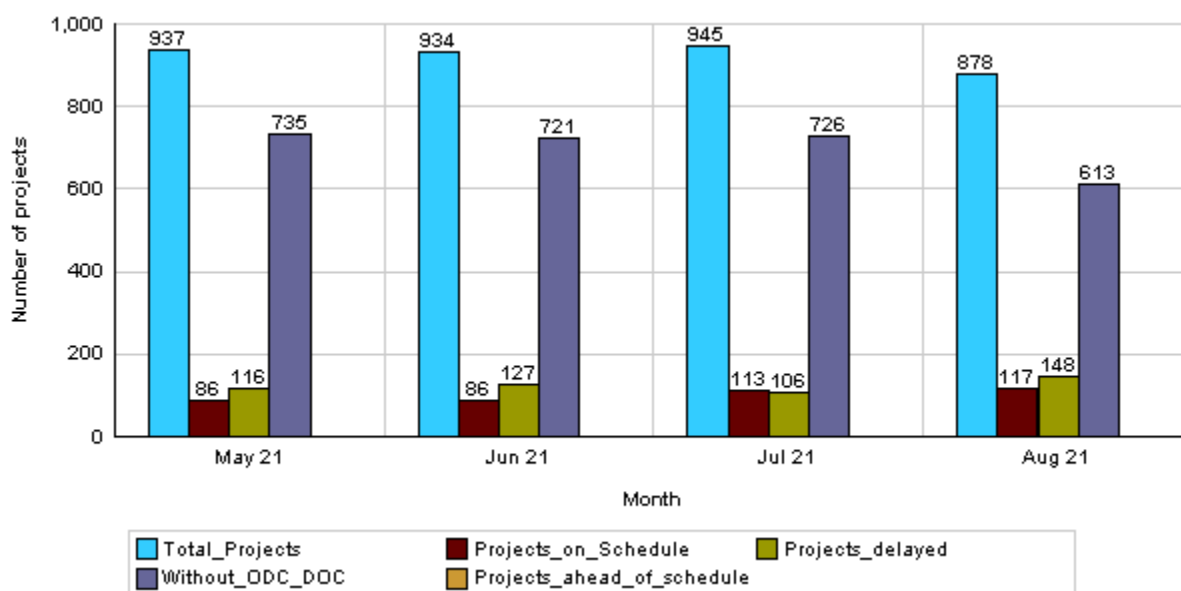


Break-up of 148 Delayed projects in August 2021

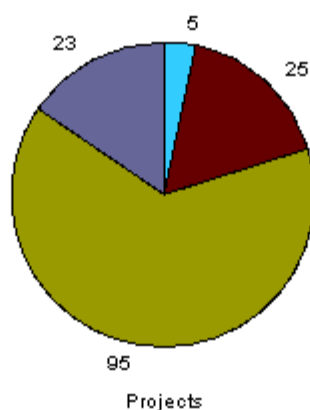


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of RAILWAYS Sector

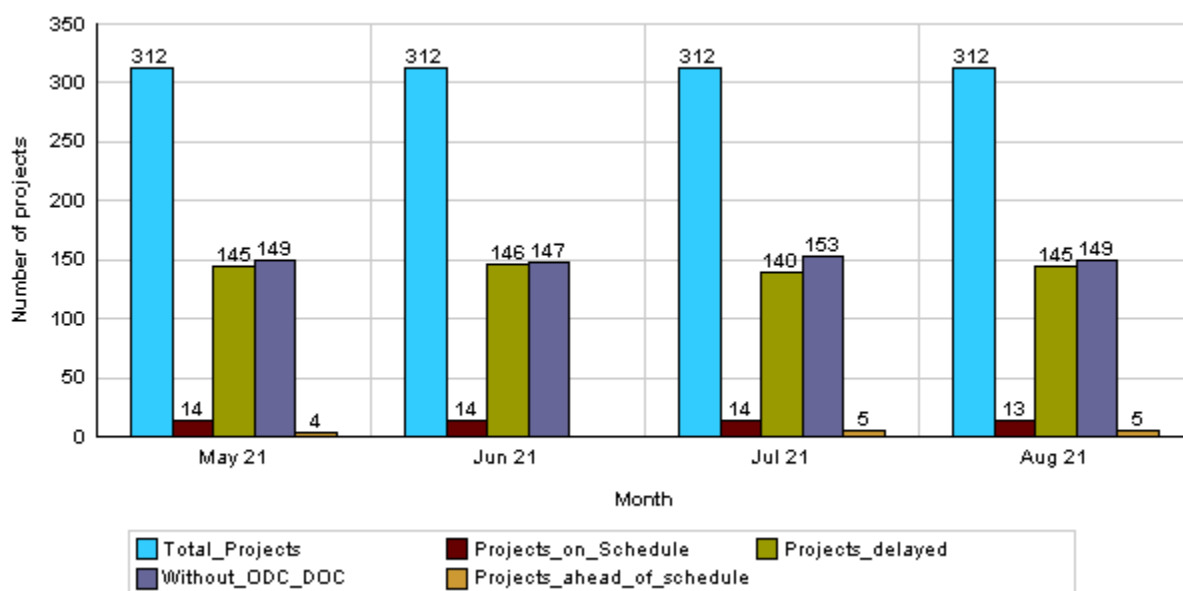


Break-up of 145 Delayed projects in August 2021

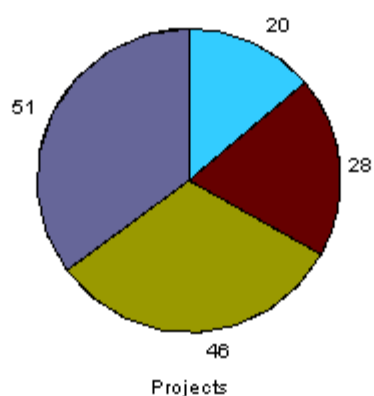


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of HEALTH AND FAMILY WELFARE Sector

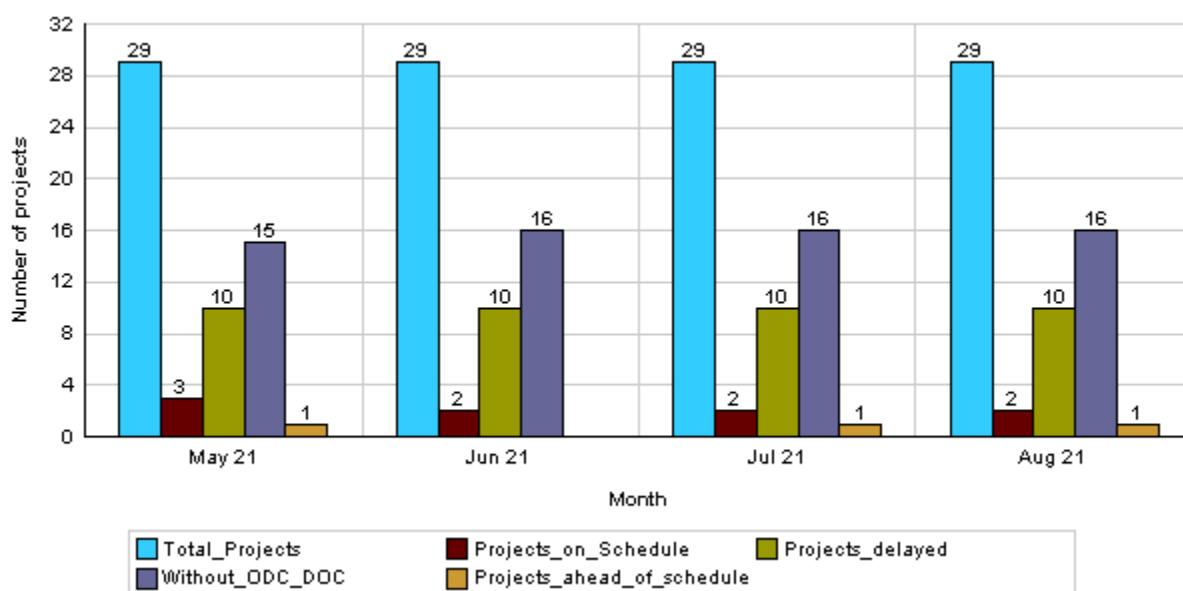


Break-up of 10 Delayed projects in August 2021

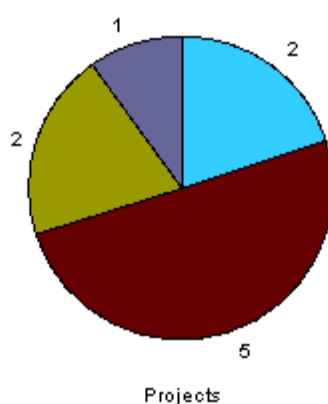


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of POWER Sector

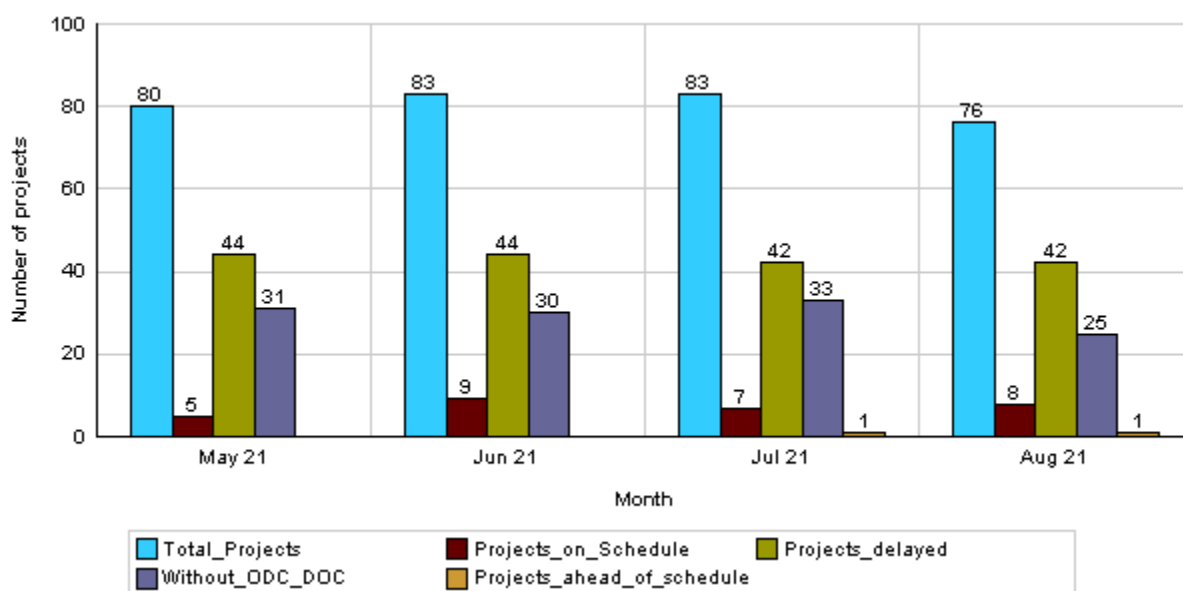


Break-up of 42 Delayed projects in August 2021

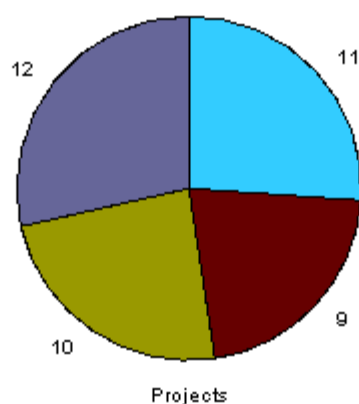


Delay in Months

1-12	13-24	25-60	MORE THAN 60
------	-------	-------	--------------

Graphical Presentation of PETROLEUM Sector

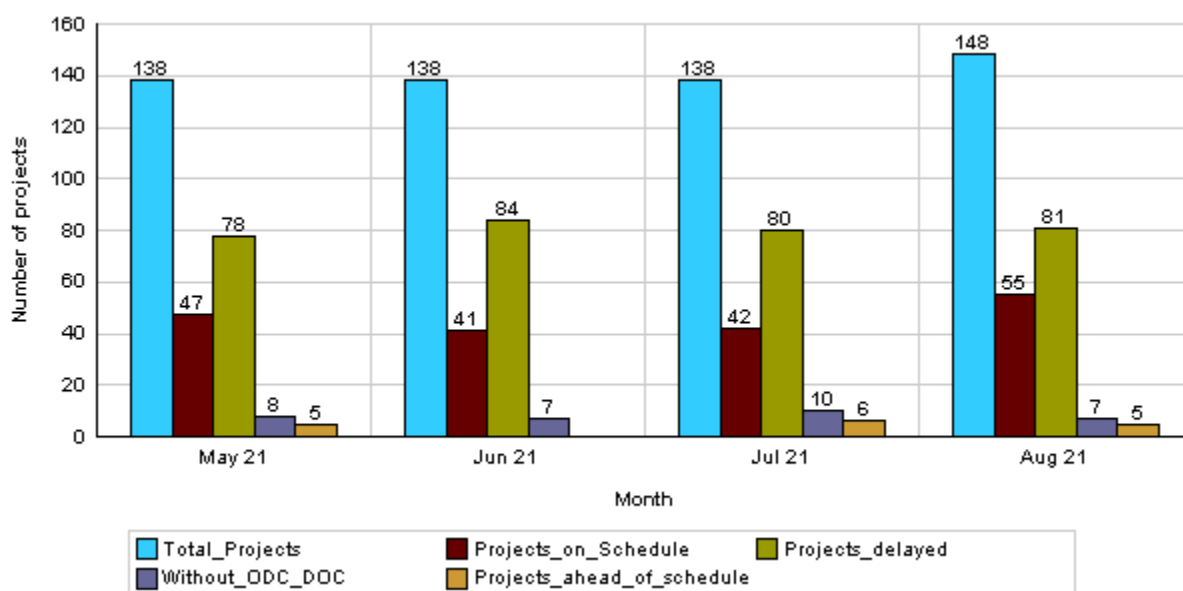


Break-up of 81 Delayed projects in August 2021

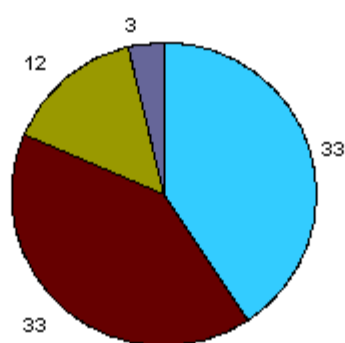


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
	33	33	12	3

Graphical Presentation of STEEL Sector

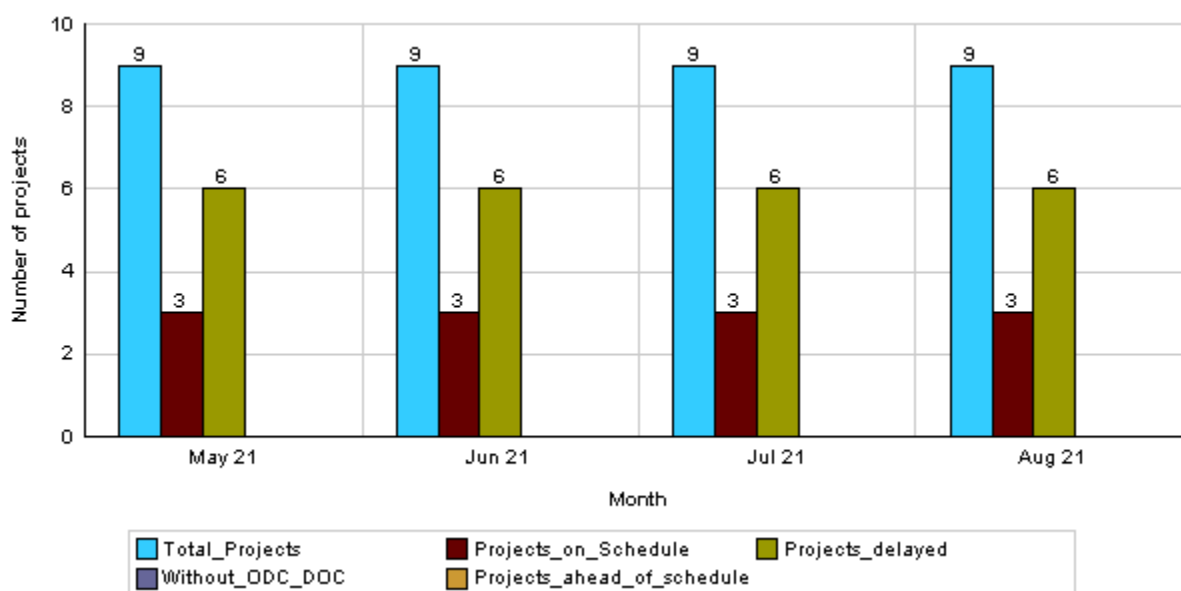


Break-up of 6 Delayed projects in August 2021

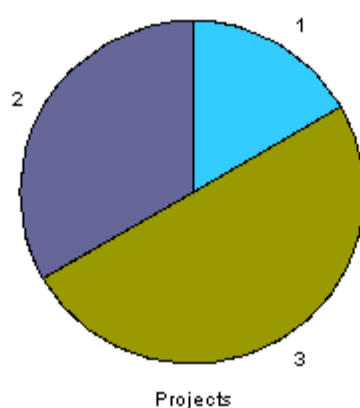


Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	1	0	3	2

Graphical Presentation of MINES Sector

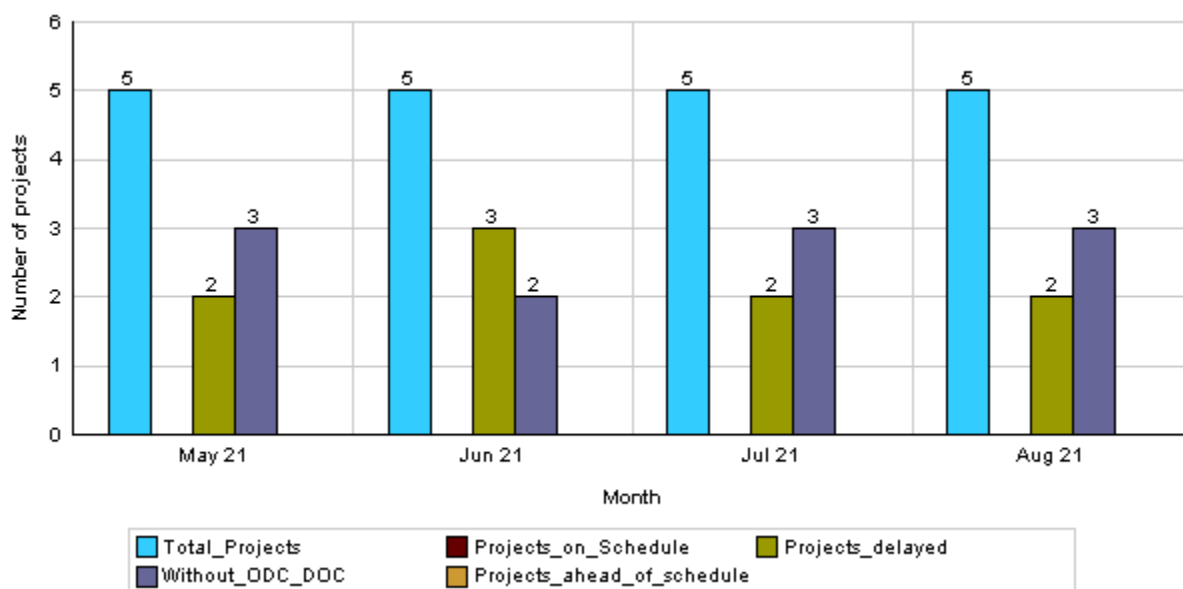


Break-up of 2 Delayed projects in August 2021

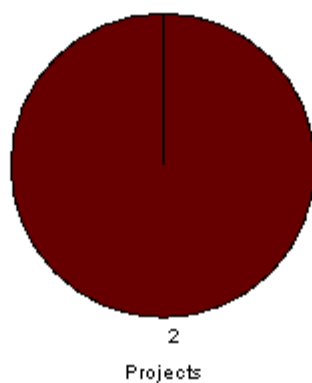


Delay in Months

Delay in Months	Number of Projects
1-12	1
13-24	1
25-60	0
MORE THAN 60	0

Graphical Presentation of FERTILISERS Sector

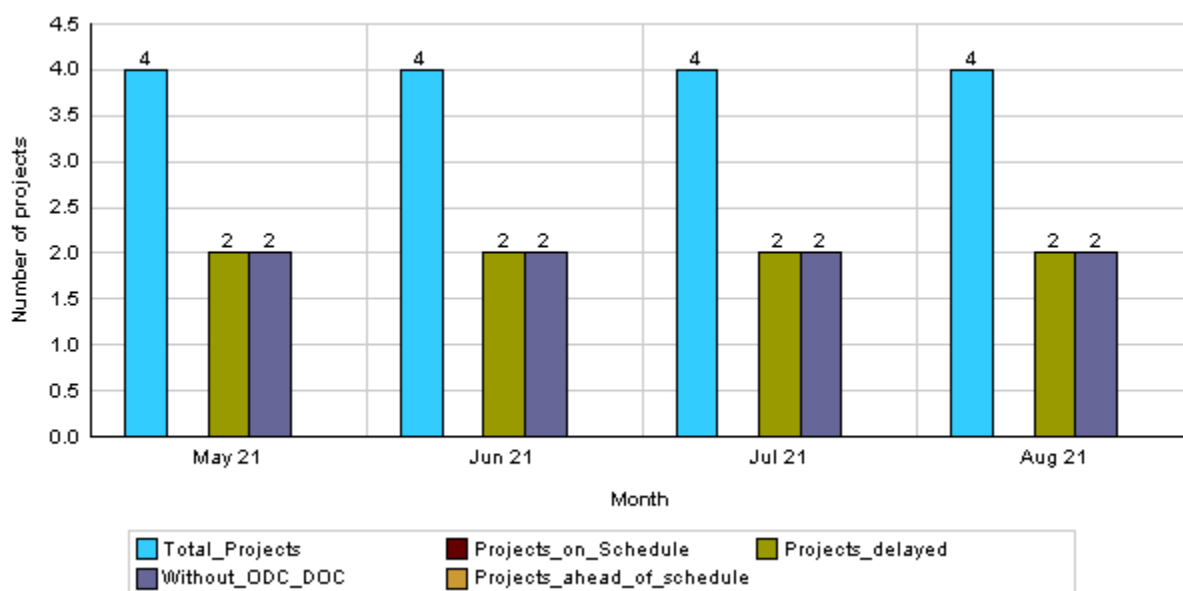


Break-up of 2 Delayed projects in August 2021

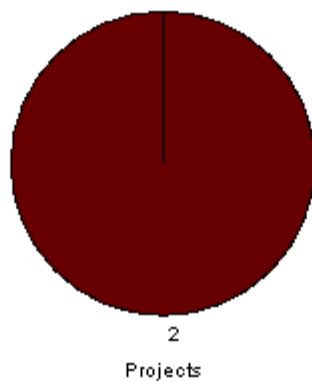


Delay in Months

Delay in Months	Number of Projects
1-12	1
13-24	1
25-60	0
MORE THAN 60	0

Graphical Presentation of COAL Sector

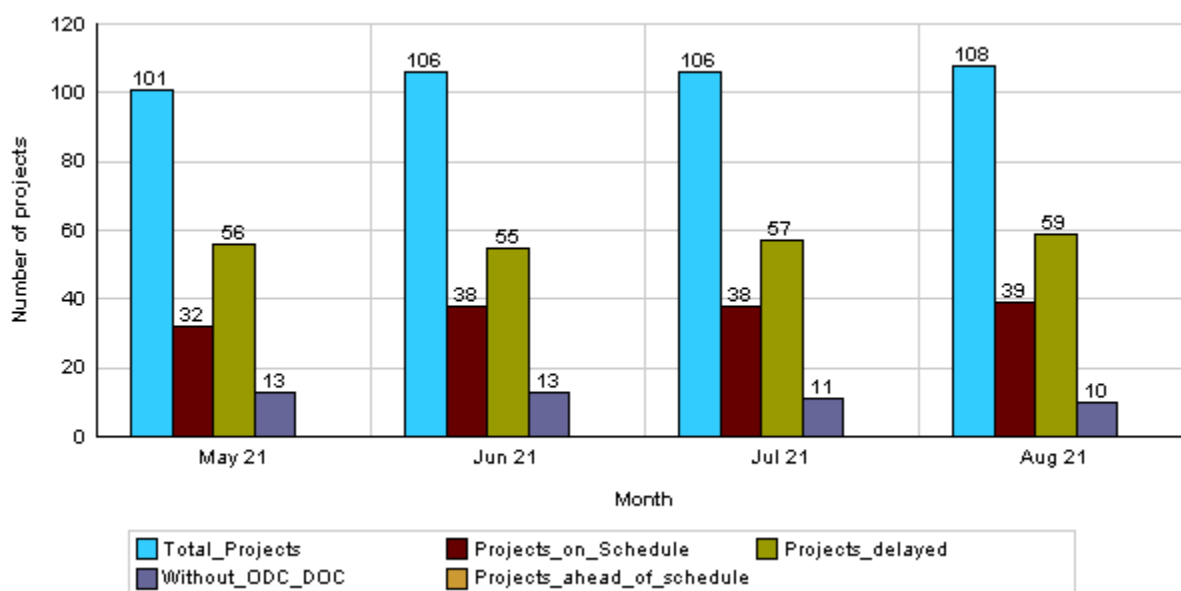


Break-up of 59 Delayed projects in August 2021

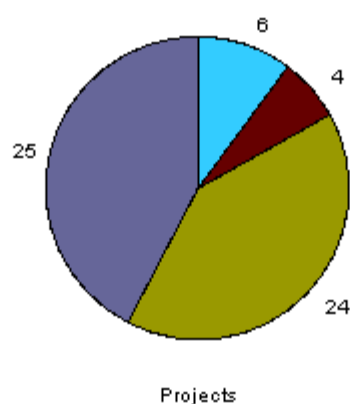


Delay in Months ■ 1-12 ■ 13-24 ■ 25-60 ■ MORE THAN 60

Graphical Presentation of CIVIL AVIATION Sector

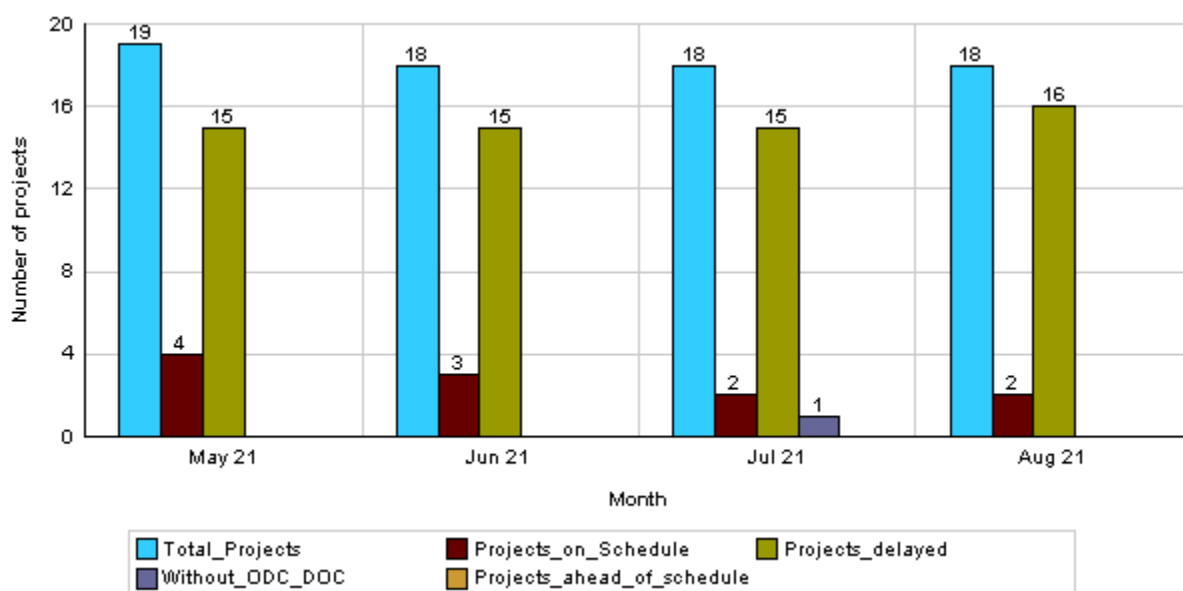


Break-up of 16 Delayed projects in August 2021

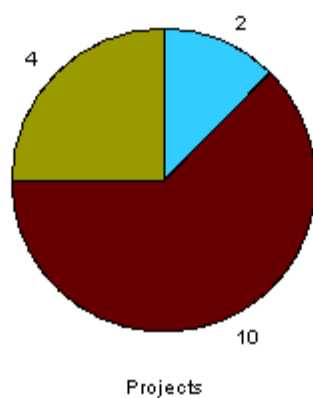


Delay in Months: 1-12 (Blue), 13-24 (Dark Red), 25-60 (Olive Green), MORE THAN 60 (Purple)

Graphical Presentation of ATOMIC ENERGY Sector

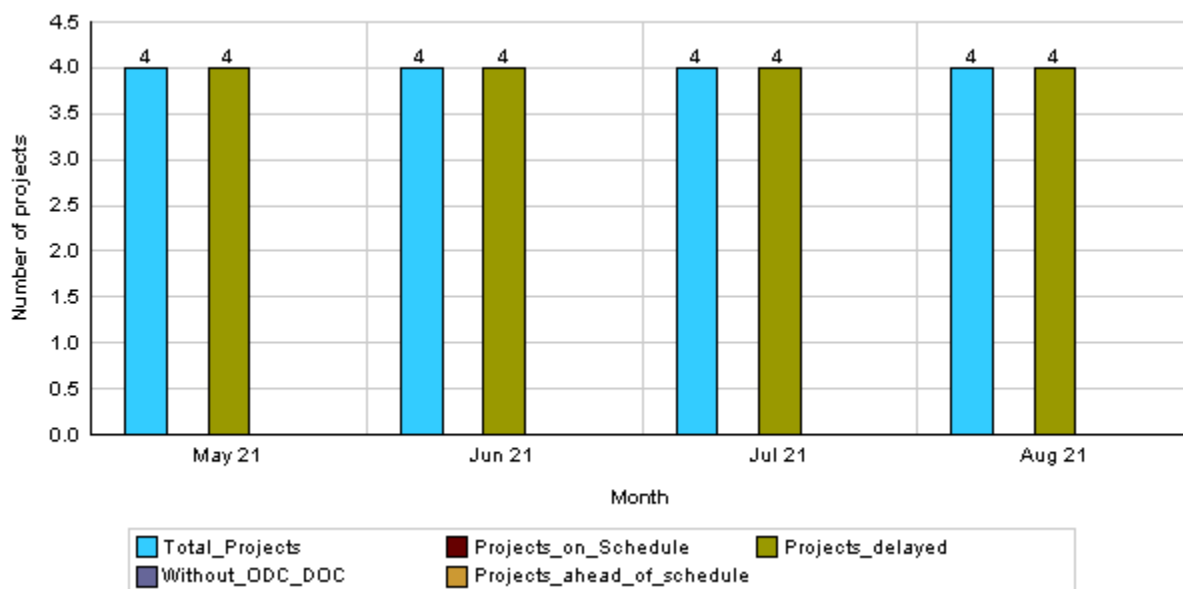

Break-up of 4 Delayed projects in August 2021

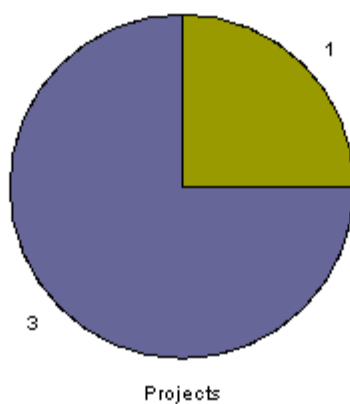

Delay in Months

Delay in Months	1-12	13-24	25-60	MORE THAN 60
1-12	0	0	0	0
13-24	0	0	0	0
25-60	0	0	1	0
MORE THAN 60	0	0	0	3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	ATOMIC ENERGY								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT ,	10/2009	11,459.00	16,580.00	17,041.00	12/2015	02/2022	74(O)	62/70
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN ,	10/2009	12,320.00	17,079.00	13,528.00	12/2016	03/2023	75(O)	52/68
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI 500 MWE) - [020100044]BHAVNI,TAMIL NADU ,	09/2003	3,492.00	6,840.00	5,986.57	09/2010	10/2022	145(O)	83/87
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU , Central Sector Projects	03/2013	39,849.00	39,849.00	25,029.00	11/2020	11/2023	36(O)	28/76
	Total		67,120.00	80,348.00	61,584.57				225/301
	CIVIL AVIATION								
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI,A & N ISLANDS ,	10/2013	417.23	707.73	456.88	09/2018	06/2022	45(O)	0/6
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH ,	08/2017	177.10	177.10	98.00	02/2020	05/2022	27(O)	1/4
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]AAI,ANDHRA PRADESH ,	04/2020	611.80	611.80	33.70	03/2023	03/2023	0(O)	3/14
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM ,	12/2016	1,142.00	1,232.00	371.33	03/2021	03/2023	24(O)	0/1
9	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES PHASE I AND II - [N04000082]AAI,BIHAR ,	05/2018	1,216.90	1,216.90	211.80	10/2022	12/2023	14(O)	0/3
10	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA BCAS AAIB AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI ,	11/2016	303.80	303.80	180.24	04/2020	03/2022	23(O)	0/0
11	C/O NEW GREENFIELD AIRPORT AT HISSAR RAJKOT GUJARAT - [N04000088]AAI,GUJARAT ,	01/2018	1,405.00	1,405.00	334.66	08/2022	12/2022	4(O)	1/15
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH ,	07/2018	346.27	480.33	105.53	09/2021	12/2022	15(O)	2/4
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH ,	06/2016	412.24	412.24	204.49	06/2021	12/2022	18(O)	0/1
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING RECONSTRUCTION OF OLD TERMINAL BUILDING MODIFICAT - [N04000079]AAI,MAHARASHTRA ,	03/2017	475.39	475.39	162.78	04/2021	08/2022	16(O)	3/10
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II CHENNAI - [N04000074]AAI,TAMIL NADU ,	06/2018	2,467.00	2,467.00	689.52	02/2022	12/2023	22(O)	0/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU ,	08/2018	951.28 -	951.28	437.28	10/2021 -	10/2022	12(O) -	2/13
17	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU ,	06/2019	380.87 -	380.87	12.79	03/2022 12/2023	12/2023	21(O) 0	2/14
18	CO CIVIL AVIATION REASEARCH ORG. (PH-II) AT BEGUMPET AIRPORT HYDRABAD - [N04000086]AAI,TELANGANA ,	05/2020	353.61 -	353.61	67.32	05/2022 -	05/2022	0(O) -	0/4
19	CCS INTERNATIONAL AIRPORT LUCKNOW - [N04000077]AAI,UTTAR PRADESH ,	06/2018	1,383.00 1,938.00	1,383.00	488.53	09/2021 -	12/2023	27(O) -	0/2
20	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT DEHRADUN - [N04000085]AAI,UTTARAKHAND ,	07/2018	456.86 -	456.86	306.08	09/2020 -	09/2022	24(O) -	0/1
21	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI,WEST BENGAL ,	01/2016	458.00 -	458.00	149.44	03/2020 07/2022	07/2022	28(O) 3	0/2
22	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT KOLKATA - [N04000081]AAI,WEST BENGAL ,	01/2019	389.71 -	389.71	191.88	11/2021 01/2023	01/2023	14(O) 0	0/2
	Total		13,348.06 -	13,862.62	4,502.25				14/108
	COAL								
23	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH ,	06/2010	11,816.40 -	11,816.40	4,583.09	03/2023 03/2016	03/2023	0(O) 0	15/21
24	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N060000008]SECL,CHHATISGARH ,	08/2013	7,612.33 -	7,612.33	2,960.03	03/2023 -	03/2023	0(O) -	13/22
25	PELMA OCP(15.00MTY) - [N06000045]SECL,CHHATISGARH ,	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023	0(O) -	1/12
26	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH ,	09/2008	152.43 459.49	459.49	198.78	03/2015 03/2020	03/2022	84(O) 0	9/11
27	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH ,	07/2008	178.44 -	178.44	11.37	03/2014 -	03/2026	144(O) -	3/9
28	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH ,	12/2009	321.50 -	321.50	210.73	03/2014 -	03/2023	108(O) -	5/6
29	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]SECL,CHHATISGARH ,	12/2013	610.63 -	610.63	159.50	03/2022 -	03/2022	0(O) -	4/11
30	AMERA OC RCE - [N06000123]SECL,CHHATISGARH ,	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60(O) -	1/7
31	AMGAON OPENCAST PROJECT RCE - [N06000135]SECL,CHHATISGARH ,	07/2015	316.10 -	316.10	145.17	03/2020 -	03/2023	36(O) -	3/6
32	DURGAPUR OPENCAST PROJECT - [N06000136]SECL,CHHATISGARH ,	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36(O) -	2/12
33	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH ,	10/2015	1,875.32 -	1,875.32	.00	03/2024 -	03/2027	36(O) -	2/6
34	VIJAY WEST OPENCAST PROJECT - [N06000158]SECL,CHHATISGARH ,	05/2017	976.95 -	976.95	76.12	03/2026 -	03/2026	0(O) -	2/2
35	MAHAMAYA OPENCAST PROJECT - [N06000164]SECL,CHHATISGARH ,	05/2018	410.26 -	410.26	40.10	03/2026 -	03/2026	0(O) -	2/4
36	JHIRIA WEST OPENCAST PROJECT - [N06000166]SECL,CHHATISGARH ,	11/2018	389.97 -	389.97	.00	03/2026 -	03/2026	0(O) -	3/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
37	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL,CHHATISGARH ,	08/2020	2,309.80 -	2,309.80	284.31	03/2029 -	03/2029	0(O) -	0/0
38	JAMPALI OCP RCE - [N06000198]SECL,CHHATISGARH ,	05/2020	278.64 -	278.64	183.90	03/2024 -	03/2024	0(O) -	0/0
39	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]SECL,CHHATISGARH ,	12/2020	2,310.12 -	2,310.12	.00	03/2029 -	03/2029	0(O) -	0/0
40	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL,CHHATISGARH ,	12/2020	5,241.40 -	5,241.40	1,960.09	03/2029 -	03/2029	0(O) -	0/0
41	MAGADH EXPANSION OC(51 MTY) - [N06000015]JCLL,JHARKHAND ,	08/2008	6,964.33 7,254.37	7,254.37	729.50	07/2012 03/2028	03/2028	188(O) 0	7/7
42	CHURI BENTI UG (0.81 MTY) - [N06000083]JCLL,JHARKHAND ,	08/2007	163.51 -	163.51	124.64	03/2011 -	03/2022	132(O) -	7/7
43	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]JCLL,JHARKHAND ,	12/2009	510.85 -	510.85	497.88	03/2016 -	03/2022	72(O) -	7/7
44	KARMA OCP (1.0MTY) - [N06000088]JCLL,JHARKHAND ,	06/2009	162.46 -	162.46	89.27	03/2014 -	03/2022	96(O) -	7/7
45	MURAI DIH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND ,	02/2011	339.88 -	339.88	61.16	04/2014 -	04/2023	108(O) -	4/7
46	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND ,	08/2011	1,230.27 -	1,230.27	493.13	04/2015 -	02/2023	94(O) -	2/6
47	RECAST EPR AMRAPALI OC - [N06000103]JCLL,JHARKHAND ,	02/2012	4,983.58 4,983.58	4,983.58	258.81	03/2020 03/2028	03/2028	96(O) 48	8/8
48	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND ,	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2022	12(O) -	0/2
49	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND ,	08/2010	289.45 -	289.45	285.43	05/2014 -	10/2021	89(O) -	0/8
50	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND ,	10/2012	269.82 -	269.82	211.94	04/2014 -	04/2020	-	0/10
51	HURA - C OC (3 MTY) - [N06000143]ECLL,JHARKHAND ,	10/2015	359.69 -	359.69	249.15	03/2022 -	03/2022	0(O) -	4/22
52	CHITRA EAST (RCE) OCP - [N06000169]ECLL,JHARKHAND ,	08/2018	513.98 -	513.98	134.97	03/2024 -	03/2024	0(O) -	0/17
53	NORTH URIMARI EXPANSION OCP - [N06000182]JCLL,JHARKHAND ,	03/2019	1,553.06 -	1,553.06	337.20	03/2023 -	03/2023	0(O) -	2/2
54	TETARIAKHAR EXPANSION OCP - [N06000186]JCLL,JHARKHAND , Central Sector Projects	11/2019	243.52 -	243.52	37.16	03/2023 -	03/2023	0(O) -	1/1
55	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND ,	07/2013	1,795.01 -	1,795.01	36.52	08/2022 -	09/2023	13(O) -	5/11
56	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND ,	10/2015	243.00 334.27	334.27	24.70	04/2018 -	06/2022	50(O) -	0/0
57	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH ,	02/2015	481.60 -	481.60	.00	03/2023 -	03/2027	48(O) -	3/10
58	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH ,	12/2014	357.80 -	357.80	100.65	03/2021 04/2024	04/2024	37(O) 0	4/10
59	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH ,	12/2014	371.04 -	371.04	66.44	03/2021 -	03/2024	36(O) -	5/9
60	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH ,	07/2015	231.92 -	231.92	1.78	03/2022 -	03/2025	36(O) -	1/10
61	AMADAND OPENCASE EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH ,	03/2016	869.44 -	869.44	126.15	03/2021 -	03/2022	12(O) -	4/6
62	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH ,	07/2016	281.25 -	281.25	18.24	03/2022 03/2026	03/2026	48(O) 0	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
63	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH , Central Sector Projects	05/2017	1,783.09 -	1,783.09	738.88	03/2021 -	03/2022	12(O) -	3/9
64	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH ,	11/2017	1,255.17 -	1,255.17	230.12	03/2022 -	03/2023	12(O) -	3/9
65	SEMARIA OPENCAST PROJECT - [N06000176]NCL,MADHYA PRADESH ,	05/2019	396.58 -	396.58	.00	03/2026 -	03/2026	0(O) -	1/5
66	VISHNUPURI UG TO OC MINE - [N06000178]WCL,MADHYA PRADESH ,	07/2018	195.57 -	195.57	2.94	03/2025 -	03/2025	0(O) -	0/7
67	GANDHIGRAM UG MINE - [N06000183]WCL,MADHYA PRADESH ,	08/2019	414.16 -	414.16	1.00	03/2026 -	03/2026	0(O) -	1/7
68	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]NCL,MADHYA PRADESH ,	07/2019	998.71 -	998.71	.00	03/2023 -	03/2023	0(O) -	1/7
69	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]NCL,MADHYA PRADESH ,	11/2020	1,729.68 -	1,729.68	.00	03/2025 -	03/2025	0(O) -	0/8
70	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]MEGA,MADHYA PRADESH ,	03/2021	496.28 -	496.28	.00	03/2028 -	03/2028	0(O) -	0/0
71	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA ,	11/2014	1,184.33 -	1,184.33	392.88	03/2020 03/2027	03/2027	84(O) 0	5/13
72	BHANEKAON OC - [N06000121]WCL,MAHARASHTRA ,	02/2015	187.94 409.68	409.68	86.90	03/2023 -	03/2023	0(O) -	7/11
73	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA ,	05/2015	295.56 299.67	299.67	164.36	03/2019 03/2022	03/2022	36(O) 54	10/13
74	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA ,	06/2015	205.49 -	205.49	138.58	03/2020 09/2021	09/2021	18(O) 0	8/10
75	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA ,	06/2015	483.69 499.00	499.00	253.70	03/2021 -	03/2021	-	4/6
76	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]WCL,MAHARASHTRA ,	08/2015	727.28 745.03	745.03	390.11	03/2025 -	03/2025	0(O) -	9/13
77	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA ,	08/2015	288.90 333.43	333.43	145.08	03/2023 -	03/2024	12(O) -	3/10
78	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA ,	11/2015	313.34 -	313.34	149.32	03/2021 03/2024	03/2024	36(O) 0	5/6
79	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA ,	11/2015	851.60 826.80	826.80	233.76	03/2020 03/2026	03/2026	72(O) 0	2/6
80	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA ,	02/2016	198.68 325.18	325.18	272.90	03/2019 -	03/2022	36(O) -	6/9
81	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA ,	02/2016	304.52 327.41	327.41	160.84	03/2019 -	03/2022	36(O) -	6/8
82	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA ,	03/2017	362.73 402.90	402.90	336.00	03/2020 09/2022	09/2022	30(O) 0	0/1
83	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA ,	11/2018	318.14 -	318.14	217.47	03/2021 09/2022	09/2022	18(O) 0	0/4
84	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA ,	11/2018	252.71 -	252.71	102.41	03/2021 -	09/2022	18(O) -	0/3
85	GHONSA EXPANSION DEEP OC - [N06000205]WCL,MAHARASHTRA ,	03/2021	241.72 -	241.72	57.00	03/2028 -	03/2028	0(O) -	0/7
86	SASTI EXPANSION OC - [N06000206]WCL,MAHARASHTRA ,	08/2020	371.59 -	371.59	52.55	03/2026 -	03/2026	0(O) -	0/7
87	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]WCL,MULTI STATE ,	08/2016	319.76 404.45	404.45	246.02	03/2022 -	03/2022	0(O) -	0/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
88	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE ,	09/2016	289.29 -	289.30	36.10	03/2022 03/2025	03/2025	36(O) 0	2/12
89	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE ,	02/2017	328.00 -	328.00	296.56	03/2021 -	09/2023	30(O) -	4/6
90	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]NCL,MULTI STATE ,	08/2020	836.42 -	836.42	60.07	03/2024 -	03/2024	0(O) -	0/6
91	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA ,	12/2007	3,145.45 -	3,145.45	589.39	03/2017 -	03/2031	168(O) -	11/12
92	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL,ODISHA ,	12/2007	8,416.19 8,416.19	8,416.19	918.79	03/2013 03/2028	03/2028	180(O) 0	8/10
93	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL,ODISHA ,	12/2007	3,504.21 3,504.21	3,504.21	589.67	03/2010 03/2029	03/2029	228(O) 0	3/5
94	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA ,	08/2008	207.28 -	207.28	204.49	03/2012 -	03/2021	-	5/7
95	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA ,	11/2008	479.53 -	703.39	703.39	03/2013 -	03/2024	132(O) -	6/9
96	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA ,	05/2014	479.15 -	479.15	226.00	03/2019 -	03/2024	60(O) -	3/9
97	SIARMAL OCP (40.00MTY) - [N06000113]MCL,ODISHA ,	05/2014	3,756.36 -	3,756.36	2,180.34	03/2026	03/2026	0(O) -	9/15
98	GARJANBAHAL OCP - [N06000117]MCL,ODISHA ,	11/2014	1,375.38 -	1,375.38	581.31	03/2021 -	09/2025	54(O) -	9/10
99	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]MCL,ODISHA ,	05/2018	2,434.75 -	2,434.75	499.88	03/2027 -	03/2027	0(O) -	3/12
100	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]MCL,ODISHA ,	11/2018	2,838.87 -	2,838.87	1,271.62	03/2029 -	03/2029	0(O) -	1/9
101	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA , Central Sector Projects	07/2017	2,401.07 -	2,401.07	802.61	07/2020 -	04/2020	-	18/22
102	NAINI COAL MINE - [N06000203]SCCL,ODISHA ,	03/2020	494.30 -	494.30	73.09	03/2024 -	03/2024	0(O) -	0/7
103	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN , Central Sector Projects	03/2015	522.45 -	522.45	9.88	09/2019 -	-	-	0/0
104	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN , Central Sector Projects	03/2015	513.63 -	513.63	175.30	12/2019 -	-	-	0/0
105	BARSINGAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,112.60 -	2,112.60	93.05	09/2020 -	-	-	0/0
106	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN , Central Sector Projects	03/2015	2,196.30 -	2,196.30	143.95	09/2020 -	-	-	0/0
107	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU ,	06/2011	5,907.11 7,980.79	7,980.79	7,407.39	12/2015 -	02/2021	-	35/35
108	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC,TAMIL NADU ,	04/2013	1,458.17 709.06	709.06	492.01	06/2015 03/2025	03/2025	117(O) 0	5/7
109	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA ,	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132(O) -	1/2
110	KISTARAM OCP - [N06000089]SCCL,TELANGANA ,	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84(O) -	4/5
111	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA ,	07/2011	162.76 -	349.28	283.01	03/2015 -	03/2022	84(O) -	13/29
112	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA ,	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	96(O) -	10/13

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
113	KALYANIKHANI OPENCAST PROJECT - [N06000101]SCCL,TELANGANA ,	07/2012	417.33 -	384.32	134.71	07/2016 -	03/2022	68(O) -	26/28
114	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA ,	11/2012	430.45 -	415.37	213.44	03/2016 -	09/2021	66(O) -	38/39
115	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]SCCL,TELANGANA ,	05/2015	397.09 -	442.42	111.66	03/2019 -	03/2022	36(O) -	17/18
116	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA ,	03/2017	413.84 -	413.84	200.14	03/2019 -	03/2022	36(O) -	6/11
117	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL,TELANGANA ,	11/2016	272.73 -	272.73	153.75	-	03/2022	-	2/6
118	GODAVARIKHANI COAL MINE - [N06000202]SCCL,TELANGANA ,	07/2019	438.98 -	438.98	73.60	03/2023 -	03/2023	0(O) -	0/11
119	VENKATESH KHANI COAL MINE - [N06000204]SCCL,TELANGANA ,	10/2020	484.51 -	484.51	23.39	03/2023 -	03/2023	0(O) -	0/8
120	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC,UTTAR PRADESH ,	07/2016	17,237.00 -	17,237.80	12,346.08	11/2021 11/2022	11/2022	12(O) 4	15/48
121	KHADIA EXPANSION OCP - [N06000208]NCL,UTTAR PRADESH ,	06/2021	491.67 -	491.67	.00	03/2025 -	03/2025	0(O) -	0/0
122	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL,WEST BENGAL ,	11/2015	1,210.12 -	1,210.12	49.04	03/2022 03/2029	03/2029	84(O) 0	9/13
123	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL ,	08/2012	1,055.05 -	1,055.05	689.34	03/2018 -	10/2021	43(O) -	12/16
124	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL ,	08/2009	2,661.73 -	5,146.48	622.13	08/2019 -	08/2024	60(O) -	1/19
125	SIDULI MINE (OC AND UG) - [N06000165]ECL,WEST BENGAL ,	05/2018	535.18 -	535.18	1.53	03/2026 -	03/2026	0(O) -	4/22
126	NAKRAKONDA KUMARDIH B OCP - [N06000170]ECL,WEST BENGAL ,	08/2018	502.68 -	502.68	15.70	03/2029 -	03/2029	0(O) -	1/22
127	TILABONI UG MINE - [N06000172]ECL,WEST BENGAL ,	02/2019	916.62 -	916.62	1.17	03/2027 -	03/2027	0(O) -	1/27
128	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]ECL,WEST BENGAL ,	07/2019	826.42 -	826.42	.19	03/2027 -	03/2027	0(O) -	0/22
129	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL,WEST BENGAL ,	04/2020	483.65 -	483.65	4.39	03/2025 -	03/2025	0(O) -	0/0
130	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL ,	12/2015	304.13 341.22	341.22	64.19	03/2017 -	03/2022	60(O) -	0/0
	Total		1,48,672.06 -	1,54,186.72	52,127.02				492/1039
	<u>FINANCE</u>								
131	C/O OF 152 NOS TYPE-II 304 NOS TYPE-III 76 NOS TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU ,	12/2015	209.00 -	208.96	205.75	10/2019 -	07/2021	-	1/6
132	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]CPWD,TAMIL NADU ,	11/2017	348.77 -	348.77	163.31	11/2021 -	11/2021	0(O) -	2/8
	Total		557.77 -	557.73	369.06				3/14
	<u>FERTILISERS</u>								

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
133	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA ,	01/2018	215.92 -	215.92	172.01	11/2019 06/2021	10/2021	23(O) 0	0/2
134	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA ,	04/2018	426.72 -	426.72	295.13	04/2020 10/2021	10/2021	18(O) 0	12/14
135	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB ,	01/2018	218.83 -	218.83	194.44	11/2019 05/2021	04/2021	-	1/2
136	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB ,	01/2018	239.81 -	239.81	204.01	11/2019 05/2021	04/2021	-	1/2
	Total		1,101.28 -	1,101.28	865.59				14/20
	<u>MINES</u>								
137	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA ,	12/2014	5,540.00 6,435.90	5,540.00	788.26	04/2021 12/2022	12/2022	20(O) 0	4/4
138	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA ,	05/2016	534.00 -	534.00	349.66	01/2020 -	-	-	3/3
139	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA , Central Sector Projects	12/2015	355.00 -	355.00	95.45	11/2020 -	02/2021	-	3/3
140	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA , Central Sector Projects	11/2017	483.00 483.00	483.00	2.68	04/2021 03/2023	03/2023	23(O) 0	2/2
141	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU ,	09/2017	166.62 163.17	163.17	135.00	06/2019 12/2021	12/2020	-	1/1
	Total		7,078.62 -	7,075.17	1,371.05				13/13
	<u>STEEL</u>								
142	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH ,	12/2011	2,858.00 -	2,858.00	1,995.82	12/2017 07/2022	07/2022	55(O) 0	5/6
143	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH ,	01/2010	15,525.00 21,940.00	21,940.00	18,779.12	05/2015 01/2022	01/2022	80(O) 0	71/86
144	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL,CHHATISGARH ,	11/2020	542.24 -	542.24	56.59	12/2023 -	12/2023	0(O) -	0/0
145	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]NMDC,CHHATISGARH , Central Sector Projects	11/2015	2,907.00 -	2,907.00	408.71	06/2023 -	06/2023	0(O) -	1/8
146	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND ,	03/2015	1,034.01 -	1,034.01	549.60	10/2017 12/2021	11/2022	61(O) 0	0/2
147	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND ,	11/2016	262.87 -	262.87	199.74	06/2019 08/2021	10/2021	28(O) 0	1/1
148	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]SAIL,ODISHA ,	11/2020	377.18 -	377.18	37.11	05/2023 -	05/2023	0(O) -	0/1
149	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH ,	04/2014	1,682.85 -	2,100.00	1,704.90	09/2018 09/2021	09/2021	36(O) 0	5/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
150	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL,WEST BENGAL ,	12/2018	263.36 -	263.36	253.46	09/2020 09/2021	08/2021	11(O) -1	4/4
	Total		25,452.51 -	32,284.66	23,985.05				87/113
	<u>PETROLEUM</u>								
151	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL,ANDHRA PRADESH ,	07/2016	20,928.00 26,264.00	26,264.00	16,008.48	07/2020 07/2022	07/2022	24(O) 0	95/111
152	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH ,	03/2016	34,012.00 -	25,090.00	13,580.92	06/2020 06/2022	06/2022	24(O) 0	15/20
153	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL AP - [N16000302]IOCL,ANDHRA PRADESH ,	08/2017	384.58 -	384.58	269.55	04/2021 03/2021	03/2021	-	0/0
154	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH ,	08/2018	466.00 -	466.00	280.16	04/2021 12/2021	12/2021	8(O) 0	0/0
155	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH ,	04/2018	355.00 -	355.00	120.72	04/2022 -	02/2023	10(O) -	0/0
156	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH ,	10/2018	316.20 -	316.20	116.20	10/2021 03/2022	03/2022	5(O) 0	0/0
157	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH ,	07/2017	580.20 -	580.20	207.44	02/2021 -	03/2023	25(O) -	0/16
158	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH ,	09/2019	196.26 -	196.26	92.83	07/2020 -	09/2021	14(O) -	1/5
159	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH ,	07/2019	167.00 -	167.00	9.93	07/2022 -	07/2022	0(O) -	0/0
160	RUF PITCH LOADING GANTRY - [N16000406]HPCL,ANDHRA PRADESH , EPC	10/2020	332.61 -	332.61	.01	11/2022 -	11/2022	0(O) -	0/0
161	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH , EPC	10/2020	303.40 -	303.40	211.10	03/2021 -	08/2021	5(O) -	0/0
162	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL,ANDHRA PRADESH , EPC	10/2020	210.94 -	210.94	121.18	08/2021 -	08/2021	0(O) -	0/0
163	CGD PROJECT AT SRIKAKULAM VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH ,	06/2019	2,880.00 -	2,880.00	.00	08/2027 -	08/2027	0(O) -	0/0
164	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) CACHAR ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM ,	06/2016	423.00 -	502.00	440.03	08/2019 06/2021	05/2021	-	10/13
165	PIPELINE NETWORK PROJECT GELEKI ASSAM - [N16000278]ONGC,ASSAM ,	07/2016	249.85 303.75	303.75	205.92	05/2020 08/2021	11/2021	18(O) 3	4/5
166	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM ,	01/2018	543.91 652.10	638.60	383.44	02/2020 -	12/2021	22(O) -	1/14
167	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM ,	08/2018	557.00 -	557.00	537.30	02/2020 06/2021	09/2021	19(O) 0	5/5
168	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS MADHUBAN - [N16000356]OIL,ASSAM ,	06/2016	224.75 222.21	198.00	178.00	08/2020 09/2021	09/2021	13(O) 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
169	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM ,	01/2019	12,366.00 -	12,366.00	567.38	10/2024 -	10/2024	0(O) -	0/0
170	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM ,	01/2019	10,228.00 -	10,228.00	285.27	10/2024 -	10/2024	0(O) -	0/0
171	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR ,	05/2018	206.50 -	206.50	147.35	03/2021 09/2021	09/2021	6(O) 0	21/26
172	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR ,	12/2017	199.36 -	199.36	48.78	10/2020 08/2022	08/2022	22(O) 0	2/2
173	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]GAIL,BIHAR ,	10/2017	359.25 -	359.25	165.40	10/2022 -	10/2022	0(O) -	10/10
174	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR ,	07/2018	189.00 -	189.00	166.08	01/2021 06/2021	11/2021	10(O) 0	6/8
175	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI BIHAR - [N16000344]IOCL,BIHAR ,	04/2018	522.00 -	522.00	373.16	03/2021 12/2021	12/2021	9(O) 0	0/0
176	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]IOCL,BIHAR ,	01/2020	14,810.00 -	14,810.00	1,303.20	04/2023 -	04/2023	0(O) -	2/2
177	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR ,	06/2020	403.00 -	403.00	89.57	08/2022 -	08/2022	0(O) -	0/0
178	CGD PROJECT AT AURANGABAD KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR ,	10/2018	176.00 -	176.00	.00	08/2027 -	08/2027	0(O) -	0/0
179	CGD PROJECT AT ARARIA PURNIA KATIAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR ,	06/2019	988.00 -	988.00	.00	12/2029 -	12/2029	0(O) -	0/0
180	CGD PROJECT AT ARWAL JEHANABAD BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR ,	06/2019	439.00 -	439.00	.00	02/2028 -	02/2028	0(O) -	0/0
181	CGD PROJECT AT KHAGARIA SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR ,	06/2019	163.00 -	163.00	.00	12/2029 -	12/2029	0(O) -	0/0
182	CGD PROJECT AT LAKHISARAI MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR ,	06/2019	347.00 -	347.00	.00	02/2028 -	02/2028	0(O) -	0/0
183	CGD PROJECT AT MUZAFFARPUR VAISHALI SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR ,	06/2019	2,996.00 -	2,996.00	.00	02/2028 -	02/2028	0(O) -	0/0
184	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]HPCL,CHHATISGARH , EPC	03/2021	456.00 -	456.00	12.89	03/2024 -	03/2024	0(O) -	2/64
185	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT ,	04/2016	327.78 -	200.00	195.40	04/2018 -	12/2021	44(O) -	19/20
186	REDEVELOPMENT OF SANTHAL FIELD - [N16000279]ONGC,GUJARAT ,	02/2017	1,162.56 -	970.30	901.28	03/2026 -	03/2026	0(O) -	7/10
187	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL,GUJARAT ,	10/2017	906.00 -	906.00	327.90	02/2020 10/2021	10/2021	20(O) 0	7/8
188	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA GUJARAT - [N16000336]IOCL,GUJARAT ,	03/2018	588.20 730.20	730.20	128.08	- 05/2023	05/2023	- 0	11/17
189	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT ,	09/2018	225.54 247.90	247.90	41.34	02/2021 -	08/2022	18(O) -	6/8
190	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT , Central Sector Projects	10/2019	403.00 -	403.00	145.34	12/2021 -	04/2022	4(O) -	9/11
191	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]IOCL,GUJARAT ,	11/2019	5,251.00 -	5,251.00	421.90	05/2023 -	05/2023	0(O) -	5/11

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
192	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT ,	06/2020	1,378.00 -	1,378.00	159.37	12/2022 -	12/2022	0(O) -	0/0
193	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT ,	02/2020	444.87 -	444.87	103.78	08/2022 -	08/2022	0(O) -	0/0
194	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT , Central Sector Projects	09/2020	18,936.00 -	18,936.00	763.62	09/2024 -	08/2024	-1(O) -	0/0
195	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT ,	10/2020	1,614.00 -	1,614.00	.21	08/2023 -	08/2023	0(O) -	0/0
196	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA ,	04/2018	206.63 340.76	340.76	131.80	02/2020 08/2021	07/2022	29(O) 11	6/7
197	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA ,	08/2018	1,636.00 -	1,636.00	862.17	08/2020 04/2022	04/2022	20(O) 0	6/7
198	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA ,	01/2019	909.00 -	909.00	416.23	01/2021 03/2022	03/2022	14(O) 0	2/6
199	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA ,	10/2018	598.00 -	598.00	391.04	02/2020 02/2022	02/2022	24(O) 0	4/5
200	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA ,	08/2018	286.42 327.01	327.01	215.40	08/2020 05/2021	12/2021	16(O) 0	14/16
201	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV PANIPAT - [N16000363]IOCL,HARYANA ,	12/2018	278.60 -	278.60	63.96	06/2021 07/2022	07/2022	13(O) 0	1/3
202	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA ,	06/2019	2,281.94 -	2,281.94	539.26	12/2022 07/2023	07/2023	7(O) 0	0/0
203	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL,HARYANA ,	08/2019	1,255.00 -	1,255.00	255.22	10/2021 -	10/2021	0(O) -	0/0
204	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA ,	09/2019	164.69 -	164.69	15.02	07/2021 03/2022	03/2022	8(O) 0	0/0
205	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL,HARYANA , EPC	09/2018	520.00 -	520.00	144.71	09/2026 02/2027	02/2027	5(O) 0	0/52
206	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]IOCL,HARYANA ,	02/2021	34,627.00 -	34,627.00	445.30	09/2024 -	09/2024	0(O) -	0/0
207	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]ONGC,JHARKHAND ,	12/2015	823.27 1,137.79	1,137.79	709.24	03/2023 03/2022	03/2022	-12(O) 0	6/10
208	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND ,	06/2017	161.50 -	161.50	102.16	06/2020 -	09/2021	15(O) -	5/12
209	CITY GAS DISTRIBUTION (CGD) NETWORK RANCHI - [N16000329]GAIL,JHARKHAND ,	10/2017	226.45 -	226.45	124.00	10/2022 -	10/2022	0(O) -	19/19
210	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL,JHARKHAND ,	11/2018	248.55 -	248.55	126.45	06/2022 -	06/2022	0(O) -	0/0
211	CITY GAS DISTRIBUTION JAMSHEDPUR - [N16000389]GAIL,JHARKHAND ,	10/2017	221.45 -	221.45	99.53	10/2022 -	10/2022	0(O) -	9/9
212	CGD PROJECT AT BOKARO HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND ,	10/2018	613.00 -	613.00	.00	12/2029 -	12/2029	0(O) -	0/0
213	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA ,	09/2016	1,810.00 1,810.00	1,810.00	1,728.12	12/2019 04/2021	02/2022	26(O) 0	9/12

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
214	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA , Central Sector Projects	11/2017	581.00 637.00	637.00	519.50	03/2020 11/2020	11/2021	20(O) 0	2/3
215	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA ,	10/2018	206.26 -	206.26	149.39	03/2021 -	10/2021	7(O) -	0/15
216	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]HPCL,KARNATAKA ,	06/2019	2,166.38 -	2,166.38	1,199.32	06/2022 -	06/2022	0(O) -	12/18
217	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]HPCL,KARNATAKA ,	12/2018	854.00 -	854.00	161.21	12/2022 -	12/2022	0(O) -	14/19
218	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]HPCL,KARNATAKA ,	06/2018	380.00 -	380.00	263.70	11/2021 -	11/2021	0(O) -	13/19
219	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA ,	06/2020	200.00 -	200.00	2.54	06/2023 08/2023	08/2023	2(O) 0	1/6
220	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA ,	10/2015	607.06 -	1,236.00	437.75	10/2017 03/2022	03/2022	53(O) 0	44/52
221	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA ,	11/2014	4,588.29 5,245.96	5,245.96	5,184.50	08/2018 11/2019	09/2021	37(O) 1	0/20
222	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA ,	12/2015	1,112.00 1,507.24	1,507.24	769.00	06/2019 -	02/2022	32(O) -	0/0
223	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL,KERALA ,	09/2018	11,130.00 -	11,130.00	422.60	03/2023 -	03/2023	0(O) -	0/0
224	PROVISION OF 2ND SPUR FOR TWL GANTRY TWD FACILITY FOR MS AND HSD ADDITIONAL TANKS FOR MS HSD AND - [N16000304]IOCL,MADHYA PRADESH ,	08/2017	236.00 319.61	319.61	195.28	06/2020 09/2021	09/2021	15(O) 0	0/0
225	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH ,	10/2018	177.00 -	177.00	.00	02/2027 -	02/2027	0(O) -	0/0
226	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA ,	03/2011	861.79 1,846.46	2,001.34	1,568.64	05/2013 02/2022	02/2022	105(O) 0	5/8
227	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA , Central Sector Projects	12/2015	3,190.69 3,375.90	3,375.90	2,876.04	04/2018 05/2022	05/2022	49(O) 0	13/15
228	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]IOCL,MAHARASHTRA ,	05/2016	1,945.00 -	1,945.00	1,529.03	02/2022 -	02/2022	0(O) -	5/5
229	ADDITIONAL FACILITIES AT MANMAD FOR COVERION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA ,	05/2016	212.00 -	212.00	164.11	01/2021 -	09/2021	8(O) -	0/0
230	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA ,	05/2016	348.00 437.00	437.00	162.73	01/2021 -	08/2022	19(O) -	0/0
231	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI - [N16000276]IOCL,MAHARASHTRA ,	05/2016	261.00 -	261.00	176.30	01/2021 -	10/2021	9(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
232	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA ,	02/2017	4,006.83 4,475.92	3,596.00	3,517.17	05/2021 05/2021	05/2021	-	14/15
233	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD) MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA ,	06/2017	249.26 -	249.26	162.09	06/2020 -	09/2021	15(O) -	4/12
234	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3 D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA ,	02/2019	2,292.46 -	2,203.71	1,995.31	05/2021 12/2021	12/2021	7(O) 0	4/6
235	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA ,	04/2019	3,228.80 3,976.67	3,976.67	1,307.63	03/2022 05/2023	05/2023	14(O) 0	4/6
236	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA ,	05/2019	3,660.71 3,740.05	3,740.05	2,997.59	05/2021 01/2022	01/2022	8(O) 0	4/6
237	HEERA REDEVELOPMENT - PHASE III - [N16000360]ONGC,MAHARASHTRA ,	06/2019	2,494.68 -	2,354.72	1,603.69	03/2022 -	03/2022	0(O) -	4/6
238	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA ,	05/2019	763.92 -	733.86	791.46	12/2020 12/2021	12/2021	12(O) 0	4/5
239	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA ,	07/2020	640.00 -	640.00	346.57	12/2021 -	03/2022	3(O) -	0/0
240	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL,MAHARASHTRA ,	08/2020	697.00 -	697.00	195.24	03/2023 -	03/2023	0(O) -	0/0
241	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE ,	01/2015	1,823.00 3,027.90	3,027.90	2,117.81	03/2021 12/2021	12/2021	9(O) 0	5/5
242	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE ,	01/2015	2,321.00 3,338.00	3,338.00	2,996.28	12/2020 03/2022	03/2022	15(O) 0	5/5
243	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE ,	01/2015	690.00 -	690.00	587.17	07/2018 05/2021	10/2021	39(O) 0	27/36
244	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE ,	05/2016	406.00 -	406.00	269.65	10/2020 -	03/2022	17(O) -	6/12
245	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE ,	09/2016	571.66 -	571.66	479.91	12/2019 -	08/2021	20(O) -	6/22
246	LAYING OF VIJAIIPUR-AURAIYA PIPELINE SECTION OF VIJAIIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE ,	07/2015	2,881.40 -	2,000.00	1,622.70	12/2020 -	10/2021	10(O) -	21/24
247	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE ,	03/2017	2,433.00 -	2,433.00	2,147.10	12/2020 12/2021	12/2021	12(O) 0	21/24
248	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE ,	03/2017	3,437.00 3,048.00	3,048.00	2,009.10	12/2020 12/2021	12/2021	12(O) 0	21/24
249	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE , Central Sector Projects	06/2009	2,915.00 5,909.00	5,909.00	3,786.80	12/2012 02/2022	02/2022	110(O) 0	26/42
250	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL,MULTI STATE ,	09/2017	2,677.00 -	3,072.00	2,443.16	06/2021 08/2022	07/2022	13(O) -1	18/26
251	BARAUNI-GUWAHATI PIPELINE - [N16000334]GAIL,MULTI STATE ,	06/2018	3,308.00 3,060.00	3,060.00	2,312.50	12/2021 -	12/2021	0(O) -	17/20

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
252	BARMER PALANPUR PIPELINE - [N16000384]HPCL,MULTI STATE , Central Sector Projects	11/2019	776.00 -	776.00	307.06	11/2022 -	11/2022	0(O) -	12/20
253	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]GAIL,MULTI STATE ,	09/2019	2,658.34 -	2,658.34	340.70	07/2022 -	07/2022	0(O) -	10/14
254	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]GAIL,MULTI STATE ,	03/2020	1,030.65 -	1,030.65	335.00	11/2022 -	11/2022	0(O) -	9/12
255	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]GAIL,MULTI STATE ,	06/2020	7,844.25 -	7,844.25	1,504.40	05/2023 -	05/2023	0(O) -	11/29
256	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE ,	06/2019	169.00 -	169.00	.00	12/2029 -	12/2029	0(O) -	0/0
257	CGD PROJECT AT SHEIKHPURA JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE ,	06/2019	303.00 -	303.00	.00	02/2028 -	02/2028	0(O) -	0/0
258	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA ,	03/2017	1,933.00 -	1,933.00	1,456.60	12/2020 12/2021	12/2021	12(O) 0	20/24
259	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA , Central Sector Projects	12/2016	161.59 -	161.59	53.22	12/2019 03/2022	03/2022	27(O) 0	18/26
260	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]GAIL,ODISHA , Central Sector Projects	07/2017	243.53 -	243.53	132.46	07/2022 -	07/2022	0(O) -	10/10
261	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA ,	08/2017	315.00 -	315.00	225.95	12/2021 08/2021	09/2021	-3(O) 1	3/3
262	CITY GAS DISTRIBUTION (CGD) NETWORK CUTTACK - [N16000328]GAIL,ODISHA ,	07/2017	182.20 -	182.20	85.28	07/2022 -	07/2022	0(O) -	9/9
263	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]IOCL,ODISHA ,	04/2018	5,654.00 -	5,654.00	3,161.40	10/2021 -	10/2021	0(O) -	7/10
264	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA ,	10/2018	1,297.50 -	1,297.50	795.89	10/2021 -	03/2022	5(O) -	1/1
265	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA ,	11/2018	462.30 -	462.30	87.24	09/2021 06/2022	06/2022	9(O) 0	1/5
266	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA ,	05/2019	3,361.00 -	3,361.00	1,977.07	08/2021 09/2022	09/2022	13(O) 0	7/11
267	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA ,	06/2019	371.00 427.00	427.00	25.79	09/2022 03/2023	03/2023	6(O) 0	1/8
268	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]BPCL,ODISHA ,	08/2019	1,607.00 -	1,607.00	263.13	08/2022 -	08/2022	0(O) -	0/21
269	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA , Central Sector Projects	01/2020	202.16 -	202.16	16.19	07/2022 -	07/2022	0(O) -	0/0
270	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA , Central Sector Projects	07/2020	13,805.00 -	13,805.00	295.70	01/2024 -	01/2024	0(O) -	0/0
271	SECOND GENERATION ETHANOL BIOREFINERY PROJECT BATHINDA PUNJAB - [N16000402]HPCL,PUNJAB ,	05/2020	1,421.46 -	1,244.50	101.45	02/2023 -	02/2023	0(O) -	11/22
272	LPG BP PROJECT JODHPUR - [N16000318]IOCL,RAJASTHAN ,	03/2018	229.80 -	229.80	85.09	- 05/2022	05/2022	- 0	17/26

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
273	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU ,	05/2013	711.00 -	711.00	11.12	06/2020 -	-	-	0/0
274	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL,TAMIL NADU ,	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66(O) 0	0/0
275	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU ,	11/2015	650.82 -	624.35	453.71	03/2019 09/2021	09/2021	30(O) 0	4/5
276	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU ,	05/2016	4,497.00 6,025.00	6,025.00	3,897.13	12/2018 02/2022	02/2022	38(O) 0	5/5
277	AUGMENTATION OF CTMPL - [N16000286]IOCL,TAMIL NADU , Central Sector Projects	12/2016	228.00 -	228.00	150.39	11/2021 -	11/2021	0(O) -	5/5
278	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU ,	09/2017	1,858.00 -	1,858.00	1,528.75	12/2019 -	-	-	0/0
279	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU ,	08/2017	421.00 -	305.00	272.50	08/2020 -	10/2021	14(O) -	0/0
280	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR TAMIL NADU - [N16000305]IOCL,TAMIL NADU ,	12/2017	466.43 -	466.43	235.77	10/2020 01/2022	01/2022	15(O) 0	0/0
281	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT CHENNAI - [N16000403]IOCL,TAMIL NADU ,	10/2020	921.00 -	921.00	5.26	09/2023 02/2024	12/2023	3(O) 0	0/0
282	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU , EPC	10/2020	1,398.00 -	1,398.00	88.76	12/2023 -	09/2023	-3(O) -	0/0
283	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU ,	10/2018	2,998.00 -	2,998.00	.00	03/2030 -	03/2030	0(O) -	0/0
284	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU ,	10/2018	1,304.00 -	1,304.00	.00	03/2030 -	03/2030	0(O) -	0/0
285	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA ,	12/2018	611.00 -	611.00	89.82	04/2022 -	08/2023	16(O) -	0/0
286	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]GAIL,UTTAR PRADESH , Central Sector Projects	04/2017	287.49 345.15	345.15	231.37	04/2022 -	04/2022	0(O) -	44/53
287	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH ,	08/2017	318.80 -	318.80	162.87	08/2021 -	11/2022	15(O) -	0/0
288	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH ,	08/2017	255.40 -	255.40	90.08	08/2020 03/2022	03/2022	19(O) 4	1/1
289	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]IOCL,UTTAR PRADESH ,	03/2018	676.00 -	676.00	464.35	08/2022 -	08/2022	0(O) -	3/3
290	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]BPCL,UTTAR PRADESH ,	12/2017	1,524.06 -	1,524.06	905.06	12/2021 -	12/2021	0(O) -	0/21
291	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL,UTTAR PRADESH ,	03/2019	3,450.20 -	3,450.20	276.62	03/2029 08/2029	08/2029	5(O) 0	0/64
292	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH ,	08/2018	217.92 217.92	217.92	96.60	04/2021 -	03/2022	11(O) -	12/14

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
293	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND , Central Sector Projects	02/2017	160.10 -	160.10	102.85	02/2020 06/2021	10/2021	20(O) 0	19/26
294	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL, WEST BENGAL ,	03/2017	1,740.00 -	1,740.00	912.00	12/2020 12/2021	12/2021	12(O) 0	13/24
295	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL ,	04/2017	163.02 207.36	207.36	122.11	04/2020 10/2021	10/2021	18(O) 0	19/26
296	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]IOCL, WEST BENGAL ,	03/2018	3,712.00 -	3,696.00	2,213.96	09/2022 -	03/2022	-6(O) -	3/3
297	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL , EPC	03/2019	5,830.20 -	5,830.20	120.62	03/2031 08/2031	08/2031	5(O) 24	0/50
298	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL, WEST BENGAL ,	06/2020	1,019.00 -	1,019.00	85.59	01/2023 -	05/2023	4(O) -	0/0
	Total		3,36,760.67 -	3,43,338.97	1,18,737.04				914/1571
	POWER								
299	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC, ARUNACHAL PRADESH ,	09/2003	6,285.33 19,992.43	19,992.43	14,059.55	09/2010 08/2023	08/2023	155(O) 0	0/0
300	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR ,	02/2005	8,692.97 21,312.11	21,312.11	19,169.37	10/2011 07/2023	07/2023	141(O) 0	33/48
301	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC, BIHAR ,	01/2007	5,353.00 10,566.00	10,566.00	8,917.95	07/2012 06/2020	10/2021	111(O) 0	22/25
302	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC, BIHAR , Joint Venture	01/2013	12,964.60 17,304.00	17,304.00	16,096.71	05/2018 -	02/2022	45(O) -	43/45
303	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]SJVN, BIHAR ,	03/2019	10,439.09 10,439.09	10,439.09	2,725.87	01/2024 -	01/2024	0(O) -	16/27
304	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC, CHHATISGARH ,	09/2015	3,004.00 -	3,004.00	1,307.03	11/2019 -	-	-	0/0
305	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL, DELHI ,	03/2015	1,394.52 -	1,394.52	554.29	05/2017 12/2021	12/2021	55(O) 2	4/9
306	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD, DELHI ,	10/2017	271.90 -	271.90	90.99	11/2019 -	-	-	0/0
307	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL, GUJARAT , Central Sector Projects	05/2017	175.64 -	175.64	115.43	09/2018 -	-	-	0/0
308	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL, GUJARAT ,	12/2017	193.14 -	193.14	108.80	06/2019 -	-	-	0/0
309	KAWAS SOLAR 56 MW - [N18000283]NTPC, GUJARAT , EPC	08/2020	261.80 -	261.80	63.92	10/2021 01/2022	10/2021	0(O) 0	0/0
310	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC, GUJARAT , EPC	01/2021	842.27 -	842.27	92.08	07/2022 -	06/2022	-1(O) -	0/0
311	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI MESANKA & RADHANPUR) - [N18000296]NTPC, GUJARAT , EPC	05/2021	674.92 -	674.92	.00	09/2022 -	09/2022	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
312	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH ,	09/2002	3,919.59 9,897.59	9,897.59	9,164.35	09/2009 03/2023	03/2023	162(O) 0	5/5
313	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH ,	11/2020	1,810.56 -	1,810.56	486.06	01/2026 -	01/2026	0(O) -	0/0
314	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN,HIMACHAL PRADESH ,	10/2020	687.97 -	687.97	155.02	11/2025 -	11/2025	0(O) -	0/0
315	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR ,	10/2014	8,112.12 -	8,112.12	2,022.77	04/2020 -	07/2025	63(O) -	0/0
316	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR ,	03/2019	4,287.59 -	4,287.59	582.89	- 08/2024	08/2024	- 0	0/0
317	NORTH KARANPURA STPP (3X660 MW) - [N18000177]JNTPC,JHARKHAND ,	02/2014	14,366.58 -	15,389.42	12,083.75	06/2019 10/2022	12/2023	54(O) 0	29/32
318	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]JNTPC,JHARKHAND ,	10/2004	4,237.96 4,238.00	4,552.00	3,785.00	10/2017 -	-	-	0/0
319	PATRATU STPP-I (3X800MW) - [N18000275]JNTPC,JHARKHAND ,	11/2017	18,668.00 -	17,112.00	4,073.68	03/2023 -	02/2025	23(O) -	3/13
320	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA , Central Sector Projects	05/2017	445.89 -	675.73	372.58	02/2019 -	-	-	0/0
321	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA , EPC	09/2019	403.62 -	403.62	100.92	06/2021 12/2021	12/2021	6(O) 0	0/0
322	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH , Central Sector Projects	01/2017	2,104.21 -	1,587.16	592.99	09/2020 08/2022	08/2022	23(O) 0	12/16
323	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR ,	12/1999	578.62 1,311.05	1,311.05	155.41	06/2006 -	-	-	0/0
324	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE ,	10/2008	4,824.12 -	5,071.94	4,612.66	10/2012 -	-	-	8/11
325	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE ,	02/2009	11,130.19 14,719.10	14,719.10	12,953.79	08/2013 11/2022	08/2022	108(O) 0	23/26
326	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE ,	10/2011	487.49 -	639.46	590.30	06/2014 -	-	-	10/12
327	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE ,	10/2013	1,364.52 -	1,891.41	1,290.03	04/2016 -	-	-	12/12
328	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE ,	01/2014	374.63 -	374.63	252.99	04/2016 12/2017	12/2021	68(O) 0	0/0
329	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE ,	05/2014	522.29 546.36	546.36	480.43	11/2016 12/2021	12/2021	61(O) 2	10/12
330	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE ,	06/2014	5,151.37 -	5,151.37	3,269.93	03/2018 -	-	-	9/12
331	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE ,	01/2015	871.62 -	902.49	628.13	10/2017 -	-	-	5/5
332	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE ,	01/2015	203.28 -	260.03	200.16	07/2017 -	-	-	3/5
333	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE ,	03/2015	197.40 -	197.40	90.28	03/2018 -	12/2021	45(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
334	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE ,	03/2016	808.63 -	808.63	678.82	01/2018 07/2021	06/2021	-	0/0
335	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE ,	05/2016	3,519.59 -	3,519.59	2,562.41	05/2019 -	-	-	0/0
336	HVDC BIPOLE LINK BETWEEN WR (RAIGARH CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE ,	05/2016	14,733.37 -	14,733.37	11,641.93	11/2019 07/2021	09/2021	22(O) 1	0/0
337	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE ,	03/2017	283.72 -	283.72	196.10	11/2019 -	-	-	0/0
338	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE ,	10/2016	408.46 -	516.12	369.27	01/2019 -	-	-	0/0
339	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE ,	10/2016	608.24 -	608.24	425.04	04/2019 -	-	-	0/0
340	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/ - [N18000242]PGCIL,MULTI STATE ,	02/2017	322.30 -	322.30	204.09	02/2019 09/2021	02/2022	36(O) 1	0/0
341	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE ,	02/2017	235.53 -	235.53	155.39	06/2019 11/2021	11/2021	29(O) 1	0/0
342	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE ,	03/2017	379.95 -	379.95	235.59	12/2019 09/2021	12/2021	24(O) 0	0/0
343	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH CHATTISGARH) AND SOUTHERN REGION (PUGALAR TM) NOR - [N18000247]PGCIL,MULTI STATE ,	02/2017	5,070.13 -	5,070.13	4,138.57	04/2020 09/2021	06/2021	-	0/0
344	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE ,	12/2014	4,754.42 9,129.32	9,129.32	2,480.78	12/2018 03/2024	03/2024	63(O) 0	0/0
345	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE ,	12/2014	5,111.33 6,700.00	6,700.00	3,068.24	12/2018 12/2021	03/2022	39(O) 3	0/0
346	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE , Central Sector Projects	12/2015	3,654.00 -	3,654.00	3,508.04	04/2019 -	-	-	0/0
347	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE , Central Sector Projects	03/2017	3,500.00 3,500.00	3,994.00	3,029.93	07/2020 12/2020	10/2021	15(O) 0	0/0
348	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE , Central Sector Projects	08/2017	1,931.39 -	1,931.39	1,783.23	02/2020 09/2021	09/2021	19(O) 1	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
349	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE ,	09/2017	198.49 -	198.49	132.15	09/2019 -	-	-	0/0
350	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE ,	11/2017	358.83 -	358.83	259.50	05/2020 08/2021	10/2021	17(O) 2	0/0
351	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA ,	05/2016	1,885.13 2,311.89	2,311.89	1,892.27	12/2018 -	11/2021	35(O) -	0/0
352	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN , EPC	01/2020	1,522.71 -	1,522.71	894.14	09/2021 10/2022	01/2022	4(O) 0	0/0
353	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN , EPC	03/2020	1,782.00 -	1,782.00	527.71	09/2021 07/2022	09/2022	12(O) -1	0/0
354	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN , EPC	12/2019	702.28 -	702.28	529.41	03/2021 11/2021	11/2021	8(O) 0	0/0
355	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN , EPC	03/2020	1,749.31 -	1,749.31	1,125.51	09/2021 02/2022	02/2022	5(O) 0	0/0
356	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN , EPC	01/2021	382.22 -	382.22	.00	03/2022 -	03/2022	0(O) -	0/0
357	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN , EPC	01/2021	1,221.73 -	1,221.73	137.36	07/2022 -	07/2022	0(O) -	0/0
358	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN , EPC	02/2021	599.99 -	559.98	60.85	07/2022 -	07/2022	0(O) -	0/0
359	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU , Central Sector Projects	05/2017	186.17 219.66	219.66	158.03	07/2019 07/2021	10/2021	27(O) 2	0/0
360	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU , EPC	03/2020	1,316.22 -	1,316.22	650.94	09/2021 02/2022	02/2022	5(O) 0	0/0
361	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA ,	01/2016	10,598.98 10,997.70	10,997.70	8,740.94	11/2020 07/2022	10/2022	23(O) 3	27/30
362	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA , EPC	06/2019	401.90 -	401.90	153.54	04/2021 10/2021	10/2021	6(O) 0	0/0
363	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH ,	03/2019	11,089.42 -	11,089.42	2,347.19	09/2023 -	08/2024	11(O) -	1/11
364	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH , EPC	03/2020	501.29 -	501.29	343.39	09/2021 02/2022	02/2022	5(O) 1	0/0
365	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH , EPC	01/2020	798.24 -	798.24	273.17	09/2021 02/2022	02/2022	5(O) 1	0/0
366	NOKHRA - [N18000282]NTPC,UTTAR PRADESH , EPC	03/2020	1,722.14 -	1,722.14	340.93	09/2021 07/2022	01/2023	16(O) 12	0/0
367	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND ,	07/2006	1,657.00 4,825.60	4,825.60	4,170.24	02/2016 -	06/2023	88(O) -	26/30
368	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND ,	11/2006	2,978.48 5,867.38	5,867.38	5,045.40	03/2013 12/2021	-	-	8/15
369	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND ,	08/2008	2,491.58 3,860.35	3,860.35	2,271.34	06/2013 11/2018	06/2024	132(O) 0	11/17
370	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND ,	07/2012	1,527.00 -	1,801.07	149.93	08/2017 -	-	-	0/15
371	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND ,	10/2017	648.33 -	947.89	657.62	12/2021 06/2022	06/2022	6(O) 0	11/32
372	RAMMAM-III HEP (3X40 MW) - [N18000178]NTPC,WEST BENGAL ,	09/2014	1,381.84 -	1,381.54	704.78	09/2019 12/2024	12/2024	63(O) 0	6/10

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
373	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL ,	04/2016	454.11 -	454.11	344.89	04/2018 03/2021	06/2021	-	0/0
374	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL ,	12/2016	529.68 633.80	633.80	461.33	11/2018 -	12/2021	37(O) -	0/0
	Total		2,29,308.93 -	2,91,506.86	1,88,096.10				337/475
	<u>HEAVY INDUSTRY</u>								
375	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI , Central Sector Projects	08/2016	1,554.00 -	900.00	815.00	09/2019 -	-	-	0/0
376	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATIP) - [N20000001]NATIS,MULTI STATE ,	04/2011	1,718.00 3,727.30	3,727.30	3,517.10	09/2011 03/2021	03/2021	-	24/25
	Total		3,272.00 -	4,627.30	4,332.10				24/25
	<u>HEALTH AND FAMILY WELFARE</u>								
377	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS- MNAGLAGIRI GUNTUR ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH , Central Sector Projects	08/2017	272.19 -	272.54	268.55	03/2019 -	03/2021	-	0/0
378	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH , Central Sector Projects	03/2018	601.02 -	601.02	453.44	- -	09/2021	- -	0/0
379	LGBRIMH-TEZPUR ASSAM - [N21000007]HSCC,ASSAM ,	07/2012	175.57 -	175.57	163.37	12/2014 -	03/2018	-	0/0
380	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI ASSAM - [N21000027]HITES,ASSAM ,	05/2017	875.00 -	747.80	387.54	05/2021 09/2022	09/2022	16(O) 0	0/0
381	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI ,	02/2013	414.11 -	655.58	561.94	11/2013 -	09/2021	94(O) -	0/0
382	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI ,	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021	-	2/2
383	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI ,	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	-	5/5
384	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI ,	12/2017	156.56 -	190.34	156.14	- -	11/2021	- -	0/0
385	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA , Central Sector Projects	01/2018	249.01 -	249.07	231.05	- -	01/2021	-	0/0
386	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA ,	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	-	2/2
387	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH ,	04/2018	1,351.00 -	1,471.00	814.67	09/2021 -	06/2022	9(O) -	2/4
388	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH ,	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11(O) -	0/0
389	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR ,	03/2019	1,404.00 -	1,404.00	279.98	09/2023 -	09/2023	0(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
390	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR ,	03/2019	1,577.00 -	1,828.00	.00	09/2025 -	09/2025	0(O) -	0/0
391	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR ,	03/2019	1,828.00 -	1,828.00	.00	09/2025 -	05/2024	-16(O) -	0/0
392	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST) - [N28000112]CPWD,KERALA ,	09/2017	150.29 -	150.29	52.74	03/2020 -	12/2021	21(O) -	2/7
393	RESIDENTIAL COMPLEX AND OPD BLOCK AIIMS NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA , Central Sector Projects	08/2017	274.19 -	274.19	259.46	03/2019 -	01/2021	-	0/0
394	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA , Central Sector Projects	03/2018	582.99 -	582.99	522.60	-	09/2021	-	0/0
395	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA ,	10/2016	363.99 -	363.99	246.43	05/2018 -	03/2022	46(O) -	0/0
396	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY ,	03/2018	195.00 -	195.00	16.41	09/2020	04/2022	19(O) -	0/33
397	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB ,	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	-	1/1
398	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA PUNJAB - [N21000026]HITES,PUNJAB ,	07/2016	703.00 -	557.48	513.24	06/2020 -	10/2021	16(O) -	0/0
399	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA ,	10/2016	209.84 -	209.84	154.21	03/2020 -	05/2021	-	1/5
400	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH , Central Sector Projects	03/2018	268.84 -	268.84	243.92	-	03/2021	-	0/0
401	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH ,	07/2016	785.00 -	715.06	574.62	04/2020 -	10/2021	18(O) -	0/0
402	CONSTRUCTION OF HOSPITAL BLOCK IIT KHARAGPUR - [N21000010]HSCC,WEST BENGAL ,	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	-	3/3
403	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL ,	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	-	0/0
404	RESIDENTIALCOMPLEX AND OPD BLOCK AIIMS KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL , Central Sector Projects	08/2017	355.15 -	355.15	313.77	03/2019 -	09/2021	30(O) -	0/0
405	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC,WEST BENGAL ,	04/2018	651.99 -	651.99	568.10	-	09/2021	-	0/0
	Total		15,273.26 -	15,784.86	8,502.12				18/62
	<u>RAILWAYS</u>								
406	NANDYAL-YERRAGUNTLA(NL) SCR - [220100192]SCR,ANDHRA PRADESH ,	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	-	0/0
407	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH ,	12/2001	1,045.20 -	2,120.16	1,009.94	03/2009 -	03/2024	180(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
408	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH ,	04/2011	761.37 -	761.37	.52	-	-	-	0/0
409	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH ,	04/2013	829.00 -	829.00	.94	-	-	-	1/1
410	NADIKUDE-SRI KALAHASTI - [N22000286]SCR, ANDHRA PRADESH ,	04/2011	2,288.70 -	2,643.25	1,277.06	03/2021	03/2024	36(O)	0/1
411	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL, ANDHRA PRADESH ,	03/2012	1,503.71 -	3,377.00	2,152.52	03/2020	03/2022	24(O)	0/0
412	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH ,	04/2015	3,873.07 -	3,873.07	.38	-	-	-	0/0
413	GUNTUR-GUNTAKAL - [N22000368]SCR, ANDHRA PRADESH ,	04/2016	3,631.00 -	3,887.48	1,239.48	03/2022	03/2024	24(O)	0/0
414	VIJAYAWADA-GUDUR - [N22000369]RVNL, ANDHRA PRADESH ,	04/2015	3,246.26 -	3,548.68	1,568.77	12/2023	12/2023	0(O)	0/0
415	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR, ANDHRA PRADESH ,	04/2015	2,499.71 -	2,499.71	727.14	03/2022 03/2024	03/2024	24(O) 0	0/0
416	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH ,	01/2013	387.70 -	487.13	434.63	03/2018	-	-	0/0
417	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH ,	08/2016	234.50 -	235.00	14.14	03/2019	-	-	0/0
418	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT) NEFR - [N22000086]NFR, ASSAM ,	09/2006	385.20 -	1,105.00	858.45	03/2019	03/2023	48(O)	0/0
419	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM ,	04/2011	314.00 486.96	800.00	832.55	03/2019	06/2021	-	0/0
420	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM ,	04/2015	2,232.32 -	2,950.00	1,758.52	03/2022	03/2023	12(O)	0/0
421	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM ,	04/2015	870.96 -	1,873.21	1,397.73	03/2021	03/2022	12(O)	0/0
422	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC) ECR - [220100240]ECR, BIHAR ,	04/1997	324.73 898.53	1,070.00	1,076.60	03/2012 11/2022	11/2022	128(O) 0	0/0
423	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR ,	04/1997	162.87 614.45	614.45	352.16	-	12/2023	-	0/0
424	HAJIPUR-SUGAULI VIA VAISHALI (NL) ECR - [220100303]ECR, BIHAR ,	04/2003	528.65 2,066.78	2,066.78	1,581.82	- 03/2023	03/2023	- 0	0/0
425	KOSI BRIDGE (NL) ECR - [220100304]ECR, BIHAR ,	04/2002	499.41 516.02	516.02	458.36	03/2020	-	-	0/0
426	DANIAWAN-BIHARSARIF (NL) ECR - [220100311]ECR, BIHAR ,	04/2001	406.92 -	339.00	200.00	-	-	-	0/0
427	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR, BIHAR ,	04/1996	477.88 751.55	751.55	714.87	03/2012 09/2021	09/2021	114(O) 2	0/0
428	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG) NEFR - [N22000087]NFR, BIHAR ,	09/2006	532.87 2,132.03	2,145.00	1,014.54	03/2019	03/2024	60(O)	0/0
429	KISHANGANJ JALALGARH NL NEFR - [N22000101]NFR, BIHAR ,	04/2008	333.76 -	360.00	6.74	-	-	-	0/0
430	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR ,	04/2008	633.87 -	633.87	.40	-	-	-	0/0
431	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR ,	04/2008	620.57 -	620.57	.31	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
432	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR ,	04/2008	445.25 -	445.25	1.15	-	-	-	0/0
433	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR ,	04/2008	326.20 -	2,995.01	2.04	-	03/2024	-	0/0
434	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR ,	04/1999	325.00 735.20	735.20	388.33	-	03/2021	-	0/0
435	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR ,	04/2006	378.56 -	1,858.75	386.36	-	03/2023	-	0/0
436	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR ,	04/2005	205.00 -	205.00	5.21	-	-	-	0/0
437	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR ,	04/2006	211.00 -	1,006.00	24.16	-	-	-	0/0
438	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR ,	04/2008	678.62 -	678.62	17.20	-	-	-	0/0
439	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR ,	04/2008	228.05 -	228.05	1.53	-	03/2024	-	0/0
440	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR ,	04/2008	1,605.17 -	1,605.17	61.37	-	03/2023	0	0/0
441	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR ,	04/2008	192.56 -	192.56	.39	-	-	-	0/0
442	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR ,	04/2008	281.30 -	281.30	.60	-	-	-	0/0
443	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR ,	04/2004	372.14 1,470.50	1,470.50	1,377.83	-	03/2023	-	0/0
444	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR ,	04/2009	548.00 -	819.01	538.55	03/2020 03/2023	03/2023	36(O) 0	0/0
445	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR,BIHAR ,	04/2013	213.01 -	495.00	497.30	-	10/2019	-	0/1
446	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR ,	05/2015	380.00 -	519.33	294.63	-	03/2025	-	0/0
447	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR ,	12/2015	1,200.20 1,200.20	1,200.20	970.88	03/2020	03/2023	36(O) -	0/1
448	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR ,	12/2015	1,491.47 -	1,491.47	543.60	03/2020 03/2023	03/2023	36(O) 0	1/1
449	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR ,	01/1991	332.15 -	546.71	547.77	07/2014	-	-	0/0
450	SAGALI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR ,	04/2016	744.04 -	1,215.54	488.59	03/2021 03/2024	03/2024	36(O) 0	0/0
451	MUZAFFARPUR SAGALI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR ,	04/2016	731.64 -	1,185.73	269.99	03/2021 03/2024	03/2024	36(O) 21	0/0
452	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR ,	04/1998	180.82 -	726.31	546.29	-	08/2020	-	0/0
453	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA DANIYAWAN-BIHARSHARIF - [N22000476]ECR,BIHAR ,	04/1991	329.39 -	1,483.14	1,219.42	-	03/2022	-	0/0
454	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH ,	12/2012	1,160.00 1,160.83	1,160.83	988.59	03/2020 03/2023	03/2023	36(O) 0	1/1

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
455	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH ,	03/2007	1,402.02 -	1,300.00	1,152.05	03/2020 -	12/2021	21(O) -	0/0
456	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH ,	05/2014	207.00 -	207.00	153.83	03/2018 -	-	-	0/0
457	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH ,	04/2008	872.00 1,226.51	1,226.51	1,153.59	12/2019 10/2020	10/2020	-	0/0
458	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH ,	04/2015	1,973.00 2,135.34	2,135.34	648.00	03/2021 12/2023	12/2023	33(O) 0	0/1
459	GEVRA ROAD PENDRA ROAD - [N22000488]JRCON,CHHATISGARH ,	02/2014	2,288.00 -	4,970.11	962.98	03/2022 -	09/2023	18(O) -	0/1
460	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]JRCON,CHHATISGARH ,	04/2013	3,055.00 -	3,055.15	2,666.33	09/2018 -	06/2022	45(O) -	0/1
461	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH ,	02/2016	393.98 -	393.98	339.31	03/2020 -	-	-	1/2
462	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI ,	04/1999	156.65 -	359.00	111.51	- -	03/2024	- -	0/0
463	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI ,	04/2012	295.68 -	419.00	160.58	- -	09/2023	-	0/0
464	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT ,	04/2008	829.74 1,246.59	1,886.76	1,875.42	03/2020 03/2024	03/2024	48(O) 0	0/0
465	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT ,	04/2008	318.24 321.62	321.62	126.36	03/2012 10/2023	10/2023	139(O) 0	0/0
466	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT ,	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	-	0/0
467	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT ,	04/2012	975.62 -	1,500.00	1,261.64	12/2021 -	12/2021	0(O) -	0/0
468	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT ,	04/2012	644.38 -	872.65	611.25	03/2021 -	-	-	0/0
469	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT ,	04/2011	844.10 844.10	844.10	251.82	- 03/2024	03/2024	- 0	0/0
470	RAJKOT-VERAVAL WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT ,	04/1994	320.66 858.96	1,378.11	555.49	03/2019 03/2023	03/2023	48(O) 0	0/0
471	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT ,	04/2013	1,548.66 -	1,868.89	1,462.02	12/2021 -	03/2022	3(O) -	0/0
472	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT ,	04/2011	1,037.15 1,125.53	1,383.69	1,199.84	03/2021 12/2022	12/2022	21(O) 12	0/0
473	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT ,	04/2015	1,002.39 1,002.39	1,002.39	730.07	03/2021 12/2022	12/2022	21(O) 0	0/0
474	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT ,	10/2013	343.00 -	343.00	222.83	03/2019 -	-	-	0/0
475	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT ,	03/2017	243.60 -	243.60	.00	- -	-	-	0/0
476	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT ,	03/2012	248.26 -	248.26	.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
477	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT ,	03/2012	153.83 -	153.83	.00	- -	-	-	0/0
478	BHILDI-VIRANGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT ,	02/1991	551.51 724.70	890.76	773.12	03/2019 10/2021	10/2021	31(O) 0	0/0
479	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT ,	04/2017	691.84 811.60	890.62	812.08	03/2020 09/2021	09/2021	18(O) 0	0/0
480	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA ,	04/2012	287.00 -	893.45	717.17	12/2011 -	06/2021	-	0/0
481	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA ,	12/2015	346.32 -	346.32	320.28	03/2019 -	-	-	0/0
482	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH ,	04/2008	2,966.99 -	6,753.42	547.68	12/2026 -	12/2025	-12(O) -	0/0
483	UDHAMPUR-SRINAGAR-BARAMULLA (NL) NR - [220100133]NR,JAMMU AND KASHMIR ,	03/1995	2,500.00 27,949.00	27,949.00	25,191.80	11/2002 -	12/2022	241(O) -	0/0
484	KODERMA-RANCHI VIA BARKAKANA (NL) ECR - [220100222]ECR,JHARKHAND ,	03/1999	1,033.07 3,020.95	3,620.00	3,614.37	- 03/2022	03/2022	- 0	0/0
485	KODERMA-TILAIYA (NL) ECR - [220100305]ECR,JHARKHAND ,	04/2002	459.91 1,625.87	1,625.87	890.81	- 03/2023	03/2023	- 0	0/0
486	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND ,	04/2012	258.20 -	358.68	316.37	12/2018 -	08/2021	32(O) -	0/0
487	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND ,	04/2012	148.77 -	377.00	203.03	12/2016 -	08/2020	-	0/0
488	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND ,	03/2016	1,724.20 -	1,724.20	896.81	03/2021 -	12/2023	33(O) -	0/0
489	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND ,	03/2015	348.23 -	390.00	366.22	03/2021 -	03/2022	12(O) -	0/0
490	HUBLI-ANKOLA(NL) SWR - [220100193]SWR,KARNATAKA ,	04/1997	2,315.00 103.74	5,174.30	157.01	- -	12/2024	-	0/0
491	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA ,	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	264(O) -	0/0
492	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA ,	04/2011	1,801.01 -	2,161.36	76.42	- -	12/2023	-	0/0
493	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA ,	04/2010	986.30 -	1,530.09	311.40	03/2016 -	12/2026	129(O) -	1/1
494	CHIKBALLA-PUR-PUTTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA ,	04/2013	558.00 -	692.00	.00	- -	12/2023	-	0/0
495	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA ,	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96(O) -	0/0
496	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA ,	04/2011	348.85 -	348.85	.36	- -	12/2025	-	0/0
497	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]RVNL,KARNATAKA ,	04/2010	2,127.00 -	3,000.00	1,921.53	03/2023 -	12/2022	-3(O) -	0/1
498	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA ,	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
499	GADAG-WADI NL - [N22000299]SWR,KARNATAKA ,	04/2013	2,841.84 -	2,841.84	362.40	12/2018 -	06/2025	78(O) -	0/0
500	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA ,	04/2013	327.25 -	327.25	.00	- -	12/2023	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
501	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA ,	04/2012	279.54 -	279.54	36.82	03/2016 -	12/2023	93(O) -	0/0
502	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA ,	03/2015	1,156.94 -	1,800.59	1,128.98	03/2020 -	03/2023	36(O) -	1/5
503	ARSIKERE-TUMKUR - [N22000332]SWR,KARNATAKA ,	03/2015	578.00 -	760.00	639.39	03/2020 11/2021	11/2021	20(O) 0	1/2
504	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA ,	03/1996	644.78 889.00	731.77	465.72	03/2017 -	03/2025	96(O) -	0/0
505	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA ,	10/1998	1,566.00 -	2,815.62	.00	- -	-	-	0/0
506	KUMBALAM-TURAVUR - [N22000191]SR,KERALA ,	04/2011	252.96 -	369.55	.00	- -	-	-	0/0
507	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA ,	04/2010	189.24 -	275.21	.00	- -	-	-	0/0
508	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA ,	02/2015	1,431.90 -	1,431.90	.00	- -	-	-	0/0
509	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA ,	02/2015	1,000.00 -	1,246.00	.00	- -	-	-	0/0
510	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA ,	02/2012	550.00 -	550.00	.00	03/2016 -	-	-	0/0
511	RAMGANJIMUNDI-BHOPAL (NL) WCR - [220100314]WCR,MADHYA PRADESH ,	04/2001	424.60 -	2,909.99	1,282.25	03/2021 03/2024	03/2024	36(O) 12	4/15
512	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH ,	04/2005	383.79 1,413.76	1,511.50	1,430.54	- 08/2020	08/2020	-	0/0
513	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH ,	04/2008	3,503.69 5,839.02	6,171.08	2,301.98	03/2022 03/2024	03/2024	24(O) 0	0/0
514	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH ,	12/2015	1,763.93 -	2,470.00	1,244.18	03/2020 -	03/2024	48(O) -	1/1
515	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH ,	04/2011	1,485.85 -	1,835.83	1,270.60	12/2020 -	12/2021	12(O) -	0/0
516	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH ,	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12(O) -	0/10
517	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH ,	08/2016	582.13 1,247.64	1,247.64	415.54	03/2022 -	03/2023	12(O) -	1/1
518	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH ,	12/2015	174.00 -	174.00	172.08	03/2019 -	-	-	0/0
519	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH ,	04/2010	585.93 1,268.32	1,268.32	1,058.10	02/2019 12/2021	12/2021	34(O) 0	0/1
520	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH ,	04/2015	1,370.00 -	1,370.94	.00	12/2021 -	12/2023	24(O) -	0/0
521	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH ,	04/2016	700.00 603.69	603.69	314.13	06/2020 03/2023	03/2023	33(O) 0	0/0
522	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA ,	03/1996	495.44 -	2,980.41	1,821.99	03/2004 -	03/2022	216(O) -	0/0
523	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]CR,MAHARASHTRA ,	02/1997	2,271.50 -	4,794.60	2,831.83	03/2021 -	03/2023	24(O) -	0/0
524	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA ,	04/2008	5,300.00 -	918.53	284.75	03/2014 -	-	-	0/0
525	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA ,	04/2012	714.10 -	714.10	65.20	04/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
526	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA ,	04/2008	3,168.29 -	3,445.48	1,401.51	03/2023 -	03/2023	0(O) -	0/0
527	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA ,	04/2011	792.89 -	910.93	352.67	03/2021 -	03/2023	24(O) -	0/0
528	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA ,	04/2011	184.06 -	325.00	324.93	03/2019 -	-	-	0/0
529	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA ,	04/2012	540.02 -	540.02	352.20	03/2022 -	03/2024	24(O) -	0/0
530	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA ,	02/2016	9,968.00 -	9,968.00	.00	03/2024 -	03/2024	0(O) -	0/0
531	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA ,	02/2016	2,425.00 -	5,341.68	.00	03/2024 -	03/2024	0(O) -	0/0
532	VAIBHAVWADI - KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA ,	02/2016	2,750.00 -	3,438.51	.00	03/2024 -	-	-	0/0
533	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA ,	02/2015	1,272.19 -	1,283.49	479.21	03/2022 -	03/2023	12(O) -	0/0
534	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA ,	02/2015	2,449.91 -	2,449.91	433.66	03/2023 -	03/2024	12(O) -	0/0
535	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA ,	02/2015	3,627.47 3,627.00	3,627.47	1,557.30	03/2024 -	03/2023	-12(O) -	0/0
536	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA ,	02/2016	1,876.00 -	2,081.27	565.94	03/2023 -	03/2023	0(O) -	0/0
537	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA ,	02/2016	1,035.16 -	1,035.16	292.56	03/2022 -	03/2024	24(O) -	0/0
538	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA ,	02/2016	637.95 -	637.95	199.88	03/2023 -	03/2024	12(O) -	0/0
539	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA ,	03/2009	713.48 -	2,725.00	2,249.00	03/2020 -	12/2021	21(O) -	0/0
540	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA ,	04/2015	723.78 -	723.78	.19	12/2025 -	03/2025	-9(O) -	0/0
541	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA ,	09/2016	1,908.51 3,176.60	3,176.60	1,334.01	03/2023 12/2023	12/2023	9(O) 0	0/1
542	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA ,	10/2013	305.00 -	305.00	269.73	03/2019 -	-	-	0/0
543	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA ,	03/2010	265.88 -	265.88	.00	-	-	-	0/0
544	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA ,	03/2012	217.38 -	217.38	.00	-	-	-	0/0
545	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA ,	06/2018	229.00 1,096.00	1,096.00	40.47	12/2021 12/2024	12/2024	36(O) 0	0/1
546	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR ,	04/2003	4,454.17 -	12,264.15	11,303.51	03/2011 -	12/2023	153(O) -	0/0
547	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA ,	04/2010	906.46 1,202.33	4,083.02	264.34	03/2021 -	-	-	0/0
548	BHAIRABI SAIRONG NL NEFR - [N22000100]NFR,MIZORAM ,	04/2008	2,393.47 5,021.45	5,521.45	4,169.01	03/2014 -	03/2024	120(O) -	0/0
549	GONDIA-JABALPUR(GC) (SECR) - [220100186]SECR,MULTI STATE ,	02/1997	511.86 1,756.00	2,005.25	1,849.61	04/2020 03/2021	03/2021	-	0/1

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
550	NANGALDAM-TALWARA(NL) NR - [220100188]NFR,MULTI STATE ,	03/1981	450.00 -	2,200.00	.00	07/2012 -	03/2024	140(O) -	0/0
551	MUNEERABAD-MAHABOONAGAR(NL) SCR - [220100205]SCR,MULTI STATE ,	04/1997	1,723.00 1.00	3,421.35	1,989.23	03/2000 -	03/2023	276(O) -	0/0
552	LALITPUR-SATNA-REWA-SINGRULI NL (NCR) - [220100232]WCR,MULTI STATE ,	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202(O) -	0/9
553	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL) NEFR - [220100266]NFR,MULTI STATE ,	04/2000	1,180.19 2,531.34	4,541.38	3,825.94	12/2008 -	09/2021	153(O) -	0/0
554	DEOGHAR - SULTANGANJ (INL) ER - [220100273]ER,MULTI STATE ,	04/2000	607.09 -	1,425.44	638.19	02/2013 -	03/2024	133(O) -	0/0
555	HATHUA-BHATNI (NL) (NER) - [220100319]NER,MULTI STATE ,	04/2005	230.03 -	230.03	277.14	12/2022 -	12/2022	0(O) -	0/0
556	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE ,	03/2007	243.78 -	895.00	114.63	12/2021 -	12/2021	0(O) -	0/0
557	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE ,	03/2013	295.00 -	580.00	521.43	01/2019 -	02/2022	37(O) -	0/0
558	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE ,	04/2007	1,347.26 1,524.68	1,524.68	974.69	03/2022 03/2023	03/2023	12(O) 0	0/0
559	DAHOD-INDORE VIA SARDARPUR JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE ,	04/2007	1,640.04 1,873.10	1,873.10	869.58	03/2022 03/2023	03/2023	12(O) 0	0/0
560	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE ,	04/2011	2,082.75 -	4,262.36	186.14 -	- -	-	-	0/1
561	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE ,	04/2011	2,912.96 -	3,845.60	303.16	03/2022 12/2024	12/2024	33(O) 0	0/3
562	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE ,	04/2010	2,030.50 -	2,030.50	.00	- -	-	-	0/0
563	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE ,	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120(O) -	0/0
564	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE ,	04/2008	415.67 -	549.75	15.58	- -	-	-	0/0
565	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE ,	04/2013	1,798.00 2,042.51	2,042.51	219.14	03/2019 -	12/2023	57(O) -	0/0
566	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE ,	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	-	0/0
567	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE ,	04/2007	270.14 -	457.08	.00	- -	12/2021	-	0/0
568	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE ,	04/2010	242.22 -	471.00	76.57	03/2020 -	-	-	0/0
569	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE ,	04/2010	241.52 -	373.87	333.46	- 12/2021	03/2022	- 3	0/0
570	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE ,	04/2011	414.84 -	750.00	156.80	03/2020 -	-	-	0/0
571	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE ,	04/1999	819.23 -	1,871.00	1,082.01	- -	-	-	0/0
572	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE ,	04/2011	120.70 -	2,172.16	273.27	03/2019 -	12/2027	105(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
573	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE ,	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228(O) -	0/0
574	SULTANGANJ-KATURIA VIA ASARGANJ TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE ,	04/2007	450.00 -	1,261.34	.00	- -	03/2025	- -	0/0
575	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE ,	04/2010	172.03 -	260.10	11.77	- -	03/2025	- -	0/0
576	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE ,	04/2013	915.98 -	2,137.81	409.74	03/2022 -	03/2025	36(O) -	0/0
577	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE ,	04/2011	288.35 -	502.48	508.72	- -	03/2021	-	0/0
578	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE ,	04/2011	261.38 -	565.00	552.51	- -	05/2019	-	0/0
579	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE ,	04/2001	923.52 -	995.10	614.44	03/2016 -	03/2025	108(O) -	0/0
580	CHINPAI-SAINTHIA DOUBLING MM FOR PRANTI-SURI CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE ,	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96(O) -	0/0
581	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE ,	04/2010	174.56 -	174.56	71.43	- -	03/2025	- -	0/0
582	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE ,	04/2010	277.28 -	266.32	197.54	03/2016 -	03/2025	108(O) -	0/0
583	DANKUNI-CHANDANPUR 4TH LINE 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE ,	04/2010	365.17 -	439.30	454.56	03/2017 -	03/2025	96(O) -	0/0
584	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE ,	04/2010	157.94 -	157.94	51.74	11/2018 -	03/2021	-	0/0
585	BARIARPIUR-MANANPURVIA KHARAGPUER LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE ,	04/2007	450.55 -	250.55	20.11	- -	03/2025	- -	0/0
586	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE ,	04/2010	365.17 -	527.54	1.76	- -	03/2025	- -	0/0
587	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE ,	04/2011	542.18 -	663.13	544.63	03/2020 -	03/2021	-	0/0
588	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE ,	04/2011	175.80 -	495.10	299.53	- -	03/2022	- -	0/0
589	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE ,	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108(O) -	0/0
590	NEW ALIPUR TO AKRA MM FOR BUDGE BUDGE-PUJALI NL PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE ,	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240(O) -	0/0
591	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE ,	04/2000	297.47 -	298.22	36.13	- -	03/2025	- -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
592	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE ,	04/2003	337.96 -	336.96	40.65	- -	03/2025	- -	0/0
593	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE ,	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	157(O) -	0/0
594	LILUAH-DANKUNI 3RD LINE MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE ,	04/2009	257.42 -	257.42	108.87	03/2014 -	03/2025	132(O) -	0/0
595	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE ,	04/2011	166.89 -	166.89	.02	- -	03/2025	- -	0/0
596	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE ,	04/2012	1,856.95 -	1,952.68	684.12	03/2023 -	03/2024	12(O) -	0/0
597	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE ,	04/2007	336.91 -	791.39	574.59	- -	03/2023	- -	0/0
598	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE ,	04/2013	296.00 -	466.65	.00	- -	12/2023	- -	0/0
599	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE ,	04/2007	2,062.30 -	2,432.50	1,126.08	- -	12/2025	- -	2/2
600	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE ,	04/2010	704.31 -	927.94	656.85	03/2020 -	11/2021	20(O) -	1/1
601	KADAPA-BANGALORE (NL) KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE ,	04/2008	2,132.77 -	3,037.95	348.32	03/2014 -	03/2027	156(O) -	1/1
602	MONIGRAM- NIMITTA - [N22000301]ER,MULTI STATE ,	04/2012	250.93 -	310.70	377.47	- -	03/2024	- -	0/0
603	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE ,	05/2015	600.00 -	701.81	261.79	03/2020 -	10/2022	31(O) -	0/0
604	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE ,	05/2015	860.43 -	1,147.00	945.81	03/2020 -	09/2021	18(O) -	0/0
605	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE ,	03/2015	1,614.59 1,877.81	1,878.00	1,457.95	03/2019 -	03/2024	60(O) -	0/0
606	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE ,	05/2015	678.54 678.54	929.86	863.90	03/2019 12/2021	12/2021	33(O) 0	0/38
607	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE , Central Sector Projects	10/2006	11,589.00 30,357.00	28,181.00	.00	- -	-	-	0/0
608	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE ,	04/2015	2,063.03 -	2,063.03	1,530.08	03/2021 -	03/2024	36(O) -	0/0
609	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE ,	04/2015	636.38 -	636.38	.00	- -	-	-	0/0
610	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE ,	12/2015	1,08,000.00 -	1,08,000.00	14,605.32	12/2023 -	12/2023	0(O) -	0/0
611	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE ,	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	-	0/0
612	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE ,	04/2007	328.14 -	1,540.13	242.31	03/2023 -	03/2023	0(O) -	0/0
613	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE ,	03/2002	625.00 -	859.00	852.73	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
614	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND ,	04/2006	2,326.52 -	6,911.00	1,300.10	03/2015 -	03/2026	132(O) -	0/0
615	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND ,	04/2013	4,274.00 -	4,274.00	.00	03/2020 -	-	-	0/0
616	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA ,	04/1994	2,923.13 3,791.66	3,791.66	1,602.15	03/2009 03/2026	03/2026	204(O) 0	0/0
617	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA ,	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	-	0/0
618	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA ,	04/1998	1,202.70 -	2,440.53	1,066.19	02/2015 -	06/2022	88(O) -	0/0
619	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA ,	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	-	1/1
620	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA ,	04/2005	810.78 1,928.07	1,928.07	895.94	06/2021 03/2025	03/2025	45(O) 0	0/0
621	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA ,	04/2010	149.90 -	230.00	54.46	03/2015 -	-	-	0/0
622	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA ,	03/2011	1,111.99 -	1,539.28	1,186.14	02/2019 -	12/2021	34(O) -	0/0
623	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA ,	03/2013	843.04 843.04	843.04	248.28	10/2020 03/2024	03/2024	41(O) 0	0/0
624	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA ,	03/2012	155.81 238.03	238.03	222.65	03/2020 -	03/2022	24(O) -	0/0
625	JAGADALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA ,	04/2015	1,547.38 1,547.38	1,547.38	678.19	03/2022 03/2023	03/2023	12(O) 0	0/0
626	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA ,	04/2015	2,361.74 -	2,361.74	450.42	03/2022 -	03/2026	48(O) -	0/0
627	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA ,	04/2015	701.61 -	810.02	192.59	11/2018 03/2024	03/2024	64(O) 0	0/0
628	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA ,	04/2015	1,172.92 1,172.92	1,172.92	653.15	12/2018 03/2024	03/2024	63(O) 0	0/0
629	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA ,	11/2015	969.83 -	1,312.96	1,018.29	03/2020 -	02/2022	23(O) -	0/0
630	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA ,	01/1991	2,335.67 -	3,327.72	794.54	12/2024 -	12/2026	24(O) -	0/0
631	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA ,	03/2006	948.04 -	2,009.00	1,532.13	03/2020 -	12/2021	21(O) -	0/0
632	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA ,	03/2009	942.95 -	1,536.00	1,054.76	03/2019 -	06/2022	39(O) -	0/0
633	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]JRCON,ODISHA ,	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48(O) -	0/0
634	QADIAN-BEAS - [N22000295]NR,PUNJAB ,	04/2011	205.22 -	841.90	1.73	- -	03/2024	- -	0/0
635	MANSA-BHATINDA (PHASE-I) INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB ,	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108(O) -	0/0
636	DAUSA-GANGAPUR CITY(NL) NWR - [220100184]NWR,RAJASTHAN ,	02/1997	410.08 -	860.41	745.83	02/2019 -	06/2022	40(O) -	0/0
637	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN ,	04/2012	246.08 -	395.00	366.38	12/2019 -	03/2021	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
638	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN ,	04/2013	236.93 -	350.45	287.39	10/2018 -	01/2020	-	0/0
639	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN ,	04/2013	822.00 -	821.64	.00	-	-	-	0/1
640	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN ,	04/2013	323.00 -	322.98	.00	-	-	-	0/0
641	MAVLI JUNCTION-BARI SADRI MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN ,	04/2013	420.18 -	480.00	371.38	03/2020 -	09/2021	18(O)	0/0
642	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN ,	04/2011	213.39 -	375.00	361.04	11/2019 -	03/2021	-	0/0
643	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN ,	04/2013	242.09 -	525.00	473.86	02/2019 -	02/2020	-	0/0
644	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN ,	05/2015	873.71 -	2,215.27	4.60	-	-	-	0/0
645	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN ,	01/2011	493.17 -	493.17	464.53	03/2018 -	-	-	0/0
646	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN ,	08/2018	808.85 -	808.85	275.78	08/2022	11/2022	3(O)	0/0
647	SEVOK RANGPO NEFR - [N22000102]NFR,SIKKIM ,	04/2008	1,339.48 4,084.69	8,600.00	1,656.02	12/2015 12/2023	12/2023	96(O) 0	0/0
648	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU ,	09/1995	303.98 -	1,720.00	704.89	03/2020 -	03/2025	60(O)	0/0
649	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS MTP - [N22000028]MRTP,TAMIL NADU ,	04/2006	495.74 -	734.01	472.27	06/2013 07/2022	07/2022	109(O) 7	1/4
650	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU ,	09/2007	724.69 -	2,950.00	1,644.43	02/2019 -	03/2025	73(O)	0/0
651	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU ,	09/2006	227.40 -	227.40	65.02	-	-	-	0/0
652	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU ,	09/2006	582.83 -	3,150.00	239.49	-	12/2025	-	0/0
653	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU ,	04/2008	151.84 -	527.37	2.59	02/2019 -	-	-	0/0
654	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU ,	04/2013	839.00 -	839.01	.63	-	-	-	0/0
655	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU ,	04/1999	198.68 -	559.95	273.32	-	03/2024	-	0/0
656	ERODE-PALANI - [N22000199]SR,TAMIL NADU ,	04/2008	288.57 -	603.23	1.63	-	-	-	0/0
657	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU ,	04/2008	164.41 -	608.13	389.96	- 12/2021	12/2021	- 0	0/0
658	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU ,	04/2007	931.98 -	1,121.00	969.72	- 08/2021	08/2021	- 1	0/0
659	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU ,	10/2013	187.26 -	327.00	275.03	04/2014 -	-	-	0/0
660	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU ,	02/1996	268.87 -	950.00	920.84	03/2005 -	09/2021	198(O)	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
661	ATTIPATTU - KORUKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU ,	02/1999	257.00 257.00	154.46	153.84	03/2018 -	-	-	0/0
662	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU ,	02/2017	1,567.00 -	1,567.00	.00	03/2024 -	03/2026	24(O) -	0/0
663	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU ,	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3(O) -	0/0
664	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU ,	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27(O) -	0/0
665	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA ,	04/2006	1,160.48 -	1,160.48	631.65	03/2010 -	03/2024	168(O) -	1/1
666	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA ,	04/2012	632.68 -	950.00	741.79	03/2016 -	12/2021	69(O) -	0/0
667	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA ,	04/2013	1,112.00 -	2,911.84	.92	- -	-	-	1/1
668	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA ,	03/2015	636.38 -	636.38	613.12	03/2021 -	-	-	3/3
669	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA ,	04/2015	773.94 -	850.00	618.69	12/2024 -	12/2024	0(O) -	0/0
670	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA ,	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9(O) -	0/0
671	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA ,	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24(O) -	2/3
672	ETAWAH-MAINPURI (NL) NCR - [220100318]NCR,UTTAR PRADESH ,	04/1997	120.00 -	346.00	345.51	12/2008 -	-	-	0/0
673	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH ,	02/2008	171.10 -	275.08	141.55	03/2012 -	-	-	0/0
674	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH ,	03/2013	307.00 -	1,409.09	.00	- -	-	-	0/0
675	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH ,	03/2013	643.00 -	644.00	.00	- -	-	-	0/0
676	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH ,	04/2012	1,229.00 -	489.64	105.51	- -	03/2023	- -	0/0
677	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH ,	04/2014	182.92 -	197.73	.00	- -	-	-	0/0
678	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH ,	03/2015	1,295.42 -	1,758.00	1,143.78	03/2022 -	03/2022	0(O) -	0/0
679	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH ,	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	-	4/6
680	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH ,	04/2015	943.60 -	1,000.00	544.48	03/2022 -	12/2024	33(O) -	0/0
681	LUCKNOW- PILIBHIT VIA SITAPUR LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH ,	04/2011	927.01 -	1,400.00	1,233.65	03/2019 -	06/2022	39(O) -	0/0
682	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH ,	04/2015	1,765.92 -	1,765.92	746.29	03/2023 -	12/2024	21(O) -	0/0
683	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH ,	03/2012	1,183.25 -	1,825.00	1,266.69	12/2020 -	12/2022	24(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
684	RAMNA - SINGRAULI DOUBLING - [N22000417]JECR,UTTAR PRADESH ,	08/2015	2,436.21 -	2,436.21	1,283.84	03/2020 -	03/2024	48(O) -	0/0
685	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]JECR,UTTAR PRADESH ,	08/2015	528.57 -	528.57	223.40	03/2019 -	03/2022	36(O) -	0/0
686	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH ,	04/2016	213.00 -	213.35	53.51	04/2016 -	12/2021	68(O) -	0/0
687	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH ,	04/2016	1,900.00 -	1,277.06	.00	01/2022 -	03/2025	38(O) -	0/0
688	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH ,	04/2017	150.00 -	341.66	.00	04/2017 -	10/2022	66(O) -	0/0
689	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH ,	04/2017	1,343.00 -	1,476.15	.00	01/2018 -	-	-	0/0
690	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH ,	04/2017	622.50 427.00	590.00	508.15	04/2017 -	03/2021	-	0/0
691	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH ,	04/2017	276.90 -	276.90	.00	04/2017 -	04/2022	60(O) -	0/0
692	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH ,	04/2016	602.50 -	714.34	88.04	-	12/2023	-	0/0
693	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH ,	04/2016	600.00 -	366.71	254.12	01/2022 -	03/2022	2(O) -	0/0
694	SHAHGANJ-BHATNI-PHEPHNA-INDARA MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH ,	04/2016	1,177.96 -	1,028.95	176.68	12/2019 -	04/2021	-	0/0
695	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH ,	03/2018	4,329.53 -	4,329.53	63.56	03/2023 -	06/2025	27(O) -	0/0
696	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH ,	09/2016	2,001.00 -	2,001.00	948.08	03/2021 12/2022	12/2022	21(O) 0	1/6
697	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH ,	06/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023	0(O) -	0/0
698	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND ,	04/2003	142.45 -	228.40	.15	-	-	-	0/0
699	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND ,	04/2012	219.83 -	346.63	204.53	-	-	-	0/0
700	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND ,	04/2011	16,216.00 -	22,716.11	2,045.67	12/2024 -	03/2025	3(O) -	0/0
701	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL) NEFR - [220100135]NFR,WEST BENGAL ,	04/1983	297.32 200.34	614.00	275.06	03/2019 -	-	-	0/0
702	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL ,	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	-	0/0
703	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRT,WEST BENGAL ,	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	-	0/0
704	TARAKESWAR - BISHNUPUR NEW BG LINE (NL) ER - [220100272]ER,WEST BENGAL ,	04/2000	1,188.91 -	1,619.48	906.00	03/2019 12/2009	03/2025	72(O) 0	0/0
705	BARDHAMAN-KATWA (GC) - [N22000091]ER,WEST BENGAL ,	04/2007	1,106.62 -	1,091.59	1,001.66	12/2010 -	03/2025	171(O) -	7/7
706	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL,WEST BENGAL ,	04/2010	2,397.72 -	2,397.72	197.20	03/2016 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
707	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL ,	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141(O) -	0/0
708	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL ,	04/2010	3,951.98 -	4,259.48	2,453.42	03/2016 -	03/2025	108(O) -	0/0
709	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL ,	04/2010	2,913.51 -	4,639.00	888.31	03/2016 -	03/2025	108(O) -	0/0
710	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL ,	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	-	0/0
711	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL ,	04/2010	267.37 -	620.00	40.99	-	03/2025	-	0/0
712	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL ,	04/2010	221.42 -	380.00	38.20	-	-	-	0/0
713	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL ,	04/2009	573.78 -	268.52	.03	-	03/2025	-	0/0
714	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL ,	04/2012	255.64 -	272.20	283.69	-	03/2022	-	0/0
715	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL ,	04/2016	602.27 -	2,144.78	977.32	12/2021 -	09/2021	-3(O) -	0/0
716	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL ,	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324(O) -	0/0
717	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL ,	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	-	0/0
	Total		4,62,095.03 -	7,04,966.85	2,54,962.86				38/139
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
718	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM A.P. - [N28000133]CPWD, ANDHRA PRADESH ,	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	-	3/7
719	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD, ANDHRA PRADESH ,	02/2019	655.34 -	655.34	125.17	06/2020 -	-	-	0/110
720	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE YERPEDU MANDAL CHITTOOR DISTRICT - [N42000007]CPWD, ANDHRA PRADESH ,	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4(O) -	0/0
721	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR ,	02/2016	496.18 496.00	498.99	288.03	06/2017 -	03/2022	57(O) -	2/6
722	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD, BIHAR ,	09/2018	375.00 -	375.00	48.46	09/2020 -	11/2022	26(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
723	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA DURG CHHATTISGARH STAGE I PHASE I. - [N28000141]CPWD,CHHATISGARH ,	03/2020	808.62 -	808.62	57.42	07/2022 -	07/2022	0(O) -	0/0
724	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM GOA. - [N42000002]CPWD,GOA ,	05/2019	303.90 -	303.90	31.80	03/2020 -	-	-	1/8
725	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH ,	11/2012	270.83 -	270.83	226.16	11/2014 -	-	-	2/8
726	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH ,	09/2018	392.51 -	392.51	38.44	06/2022 -	06/2022	0(O) -	0/0
727	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR ,	03/2019	329.00 -	329.00	.00	07/2022 -	07/2022	0(O) -	0/0
728	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR ,	01/2018	676.00 -	676.00	.00	04/2023 -	04/2023	0(O) -	0/0
729	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND ,	09/2012	171.86 -	171.86	111.29	03/2016 -	-	-	1/6
730	DEVELOPMENT OF PERMANENT CAMPUS OF IIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES - [N44000001]CPWD,JHARKHAND , PPP BOT (Hybrid Annuity)	03/2021	127.26 -	188.88	12.73	10/2023 -	10/2023	0(O) -	0/0
731	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA , EPC	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6(O) -	0/0
732	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA ,	01/2010	165.23 -	165.23	118.52	10/2012 -	-	-	1/8
733	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE KANJIKODE WEST DISTRICT PALAKKA - [N28000140]CPWD,KERALA , Central Sector Projects	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15(O) -	0/0
734	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY POWAI MUMBAI - [N28000117]CPWD,MAHARASHTRA ,	01/2018	223.37 -	223.37	61.35	07/2020 -	-	-	4/14
735	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA ,	09/2013	484.32 -	626.26	.00	09/2014 -	-	-	0/0
736	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE ,	03/2018	150.00 -	150.00	.00	04/2018 -	-	-	0/0
737	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE ,	08/2018	418.00 -	418.00	110.00	03/2019 -	-	-	0/0
738	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD,ODISHA ,	01/2019	790.79 -	790.79	213.06	03/2022 -	06/2022	3(O) -	0/5
739	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR PUNJAB - [N28000120]CPWD,PUNJAB ,	01/2018	430.00 -	387.83	218.29	05/2020 -	03/2022	22(O) -	3/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
740	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR PUNJAB. - [N28000142]CPWD,PUNJAB ,	10/2019	348.24 -	348.24	23.28	05/2022 -	10/2022	5(O) -	1/7
741	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN ,	12/2016	549.31 -	559.47	458.38	07/2019 -	-	-	3/6
742	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH ,	11/2017	171.72 -	171.72	53.94	03/2020 -	-	-	0/0
743	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL , EPC	03/2020	193.83 -	193.83	.45	06/2020 -	-	-	0/0
	Total		10,910.66 -	11,104.02	2,426.77				21/190
	HOME AFFAIRS								
744	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI ,	10/2013	1,219.21 -	2,000.00	956.28	10/2019 -	03/2022	29(O) -	1/7
745	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]CPWD,DELHI , EPC	06/2019	277.35 290.33	290.33	27.25	07/2022 10/2022	10/2022	3(O) 3	0/0
746	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]CPWD,HARYANA , EPC	01/2020	166.98 167.00	166.98	.00	10/2023 -	10/2023	0(O) -	0/0
747	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS 96 - [N45000001]CPWD,HARYANA ,	01/2020	166.98 -	166.98	.29	05/2022 -	05/2022	0(O) -	0/0
748	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD,UTTAR PRADESH ,	05/2019	199.31 -	199.31	27.86	01/2022 -	06/2022	5(O) -	0/0
749	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND ,	12/2008	114.26 266.00	266.00	.00	12/2013 -	-	-	0/0
750	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL , Central Sector Projects	10/2014	162.88 238.00	238.00	172.12	04/2018 12/2021	12/2021	44(O) 0	5/6
	Total		2,306.97 -	3,327.60	1,183.80				6/13
	RURAL DEVELOPMENT								
751	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI ,	11/2018	361.60 -	361.60	12.44	07/2021 -	-	-	0/2
752	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA ,	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2022	74(O) -	0/1
753	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA ,	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2022	63(O) -	2/5

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
754	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA ,	10/2011	175.49 206.71	175.49	124.87	12/2016 -	09/2022	69(O) -	0/4
	Total		889.43 -	899.87	472.48				2/12
	<u>DPIIT</u>								
755	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI ,	11/2017	4,773.00 -	5,178.00	2,744.03	12/2019 05/2022	05/2022	29(O) 0	0/0
756	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE ,	09/2011	12,579.09 -	13,812.30	9,346.57	09/2019 01/2014	07/2021	-	0/0
	Total		17,352.09 -	18,990.30	12,090.60				0/0
	<u>DONER</u>								
757	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE SHILONG IN MEGALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA ,	04/2014	151.33 -	151.33	149.33	09/2017 -	08/2021	47(O) -	12/15
	Total		151.33 -	151.33	149.33				12/15
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
758	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS ,	03/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022	39(O) 0	1/4
759	2 LANE WITH HARD SHOLDER REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS ,	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51(O) 0	2/4
760	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS ,	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	54(O) 0	3/4
761	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS ,	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41(O) -	1/4
762	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS ,	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41(O) 0	2/4
763	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS ,	11/2017	237.80 237.80	238.00	148.90	11/2019 10/2021	10/2021	23(O) 5	0/0
764	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS ,	11/2017	257.34 -	238.00	.00	11/2019 03/2021	03/2021	-	0/0
765	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS ,	02/2017	401.00 401.00	401.00	220.93	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
766	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH , PPP (BOT)	04/2011	571.00 -	571.00	582.53	10/2013 -	-	-	0/0
767	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2011	1,535.00 -	1,535.00	3,279.25	05/2014 -	-	-	0/0
768	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH , EPC	01/2014	195.45 -	195.45	.00	11/2014 -	-	-	0/4
769	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH , EPC	03/2015	271.45 -	271.45	243.29	10/2015 06/2021	-	-	3/4
770	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHILIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI,ANDHRA PRADESH ,	01/2016	1,134.97 -	1,134.97	.00	11/2018 -	-	-	0/0
771	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH ,	09/2014	1,684.00 -	1,684.00	.00	02/2017 -	-	-	0/0
772	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	1,187.10	962.95	03/2020 -	-	-	0/0
773	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH ,	12/2017	328.67 -	328.67	266.63	-	-	-	0/0
774	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH ,	12/2017	1,323.15 -	1,323.15	.00	-	-	-	0/0
775	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH ,	12/2017	357.00 -	357.00	.00	-	-	-	0/0
776	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH ,	02/2018	1,959.00 -	1,959.00	1,308.42	-	10/2021	-	0/0
777	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH ,	03/2018	1,532.62 -	2,499.00	880.34	03/2021 10/2021	04/2021	-	2/4
778	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH ,	03/2018	1,550.98 -	1,550.98	1,620.21	-	09/2021	-	0/0
779	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH ,	03/2018	565.09 -	565.09	651.47	-	02/2021	-	0/0
780	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH ,	03/2018	314.43 -	314.43	85.61	-	03/2022	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
781	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH ,	03/2018	557.30 -	557.30	433.20	- -	-	-	0/0
782	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH ,	10/2015	333.21 -	353.43	333.09	12/2015 -	-	-	3/3
783	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH ,	09/2016	372.68 309.37	372.68	244.96	02/2017 07/2021	-	-	3/4
784	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH ,	11/2016	290.15 -	290.15	136.41	05/2017 08/2021	08/2021	51(O) 0	2/4
785	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH ,	01/2017	319.28 -	319.28	188.42	08/2017 12/2021	12/2021	52(O) 0	3/4
786	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH ,	02/2017	429.43 373.05	429.43	319.71	11/2017 01/2022	-	-	3/4
787	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH ,	03/2018	228.32 202.83	228.32	135.54	08/2018 12/2021	12/2021	40(O) 0	3/4
788	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH ,	03/2018	289.67 274.73	289.67	206.00	08/2018 11/2021	11/2021	39(O) 0	3/4
789	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH ,	03/2018	504.19 556.13	504.19	465.26	11/2018 07/2021	-	-	3/4
790	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH ,	03/2016	995.09 995.00	995.09	560.85	05/2016 09/2021	09/2021	64(O) 0	3/4
791	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH ,	01/2018	418.03 381.75	418.03	323.62	08/2018 08/2021	08/2021	36(O) 0	3/4
792	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH ,	08/2016	350.61 -	350.61	324.60	01/2017 12/2021	12/2021	59(O) 0	3/4
793	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH ,	01/2016	386.09 316.06	386.09	214.31	05/2016 07/2021	-	-	3/4
794	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH ,	01/2016	348.95 -	348.95	225.76	08/2016 12/2021	07/2021	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
795	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH ,	03/2016	444.84 -	444.84	345.48	09/2016 08/2021	08/2021	59(O) 0	3/4
796	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH ,	11/2016	376.25 -	376.25	310.33	08/2017 12/2021	12/2021	52(O) 0	3/4
797	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH,ANDHRA PRADESH ,	01/2017	263.45 381.75	263.45	116.24	09/2017 05/2022	05/2022	56(O) 0	1/4
798	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH,ANDHRA PRADESH ,	01/2017	576.48 596.38	576.48	369.63	01/2018 04/2022	04/2022	51(O) 0	2/4
799	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH , EPC	09/2018	597.67 -	597.67	189.54	01/2020 -	-	-	0/0
800	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH , EPC	09/2018	617.41 -	617.41	526.54	02/2019 -	-	-	0/0
801	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH , PPP (BOT)	11/2019	1,226.88 -	1,226.88	146.49	02/2021 -	-	-	0/0
802	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	1,601.10 -	1,601.10	10.51	02/2021 -	-	-	0/0
803	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH , EPC	03/2020	207.79 -	207.79	.00	03/2021 -	04/2022	13(O) -	0/4
804	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH , EPC	06/2020	221.40 -	221.40	.00	05/2021 -	12/2022	19(O) -	0/0
805	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH , EPC	08/2020	222.61 -	222.61	.00	03/2021 -	03/2023	24(O) -	0/0
806	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH , EPC	03/2015	394.00 522.86	522.86	410.63	06/2018 -	03/2021	-	3/3
807	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH ,	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	- 0	3/4
808	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH ,	03/2017	284.09 284.09	284.09	157.65	04/2017 03/2021	03/2022	59(O) 12	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
809	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH ,	02/2017	195.23 -	252.79	133.92	04/2017 -	03/2022	59(O) -	2/4
810	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH ,	02/2017	203.36 -	263.31	145.13	04/2017 -	03/2022	59(O) -	2/4
811	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH ,	02/2017	180.57 -	180.57	60.86	04/2017 -	02/2021	-	1/4
812	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH ,	02/2017	167.28 -	167.28	22.06	04/2017 -	08/2020	-	1/4
813	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH ,	01/2017	198.22 -	252.05	144.26	04/2017 -	03/2022	59(O) -	3/4
814	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH ,	03/2018	392.60 -	392.60	.00	-	-	-	0/0
815	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH ,	12/2016	200.44 -	200.44	125.91	- 08/2021	12/2021	0	3/4
816	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH ,	03/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022	- 0	2/4
817	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH ,	09/2016	568.92 -	568.92	310.07	- 11/2021	03/2022	- 0	0/0
818	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH ,	12/2016	188.78 -	188.78	104.07	- 03/2021	03/2022	- 0	3/4
819	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH ,	02/2017	175.06 -	175.06	87.32	- 04/2022	04/2022	- 0	3/4
820	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH ,	02/2017	176.12 -	176.12	73.92	- 04/2022	04/2022	- 0	2/4
821	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH ,	10/2015	210.50 -	210.50	145.07	- -	10/2021	- -	4/4
822	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH ,	03/2015	172.75 -	172.75	134.38	- -	03/2021	- -	4/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
823	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH ,	01/2017	256.66 -	256.66	16.42	- -	03/2021	-	1/4
824	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH ,	09/2011	1,979.00 -	2,036.90	1,242.64	- 03/2020	-	-	0/0
825	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH ,	11/2016	243.89 -	243.89	210.90	- -	09/2020	-	0/0
826	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]NHIDCL,ARUNACHAL PRADESH , EPC	08/2020	301.06 -	301.06	23.41	04/2022 -	04/2022	0(O) -	0/4
827	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]NHIDCL,ARUNACHAL PRADESH , EPC	09/2020	353.90 -	353.90	18.03	05/2022 -	05/2022	0(O) -	0/4
828	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	403.68 -	403.68	63.69	02/2020 -	-	-	0/0
829	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	342.55 -	342.55	144.45	02/2020 -	-	-	0/0
830	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	421.48 -	421.48	50.14	11/2020 -	-	-	0/0
831	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	543.05 -	543.05	119.81	11/2020 -	-	-	0/0
832	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	486.70 -	486.70	75.26	10/2020 -	-	-	0/0
833	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	560.39 -	560.39	148.75	02/2020 -	-	-	0/0
834	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	347.78 -	347.78	93.70	09/2020 -	-	-	0/0
835	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	394.27 -	394.27	15.49	10/2020 -	-	-	0/0
836	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH , EPC	03/2019	450.65 -	450.65	37.16	11/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
837	TADADEGE - HENKAR - [N24001315]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	550.45 -	550.45	13.03	03/2023 -	03/2023	0(O) -	0/4
838	LADDA - BASAI - [N24001316]NHIDCL,ARUNACHAL PRADESH , EPC	02/2021	445.96 -	445.96	.00	04/2023 -	04/2023	0(O) -	0/4
839	DOGINALA - GAU - [N24001320]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	242.30 -	242.30	.00	09/2022 -	09/2022	0(O) -	0/4
840	DEMBUEN - BRUNI - [N24001321]NHIDCL,ARUNACHAL PRADESH , EPC	12/2020	606.63 -	606.63	.00	03/2023 -	03/2023	0(O) -	0/4
841	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]MoRTH,ARUNACHAL PRADESH , EPC	02/2021	588.09 -	588.09	.00	03/2024 -	03/2024	0(O) -	0/0
842	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]MoRTH,ARUNACHAL PRADESH , EPC	01/2020	358.26 -	358.26	.00	02/2024 -	02/2024	0(O) -	0/0
843	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH,ARUNACHAL PRADESH , EPC	06/2020	437.60 -	437.60	.00	08/2021 -	08/2021	0(O) -	0/0
844	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH,ARUNACHAL PRADESH , EPC	06/2020	496.47 -	496.47	.00	08/2021 -	08/2021	0(O) -	0/0
845	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH , EPC	03/2021	182.55 -	182.55	.00	09/2021 -	09/2021	0(O) -	0/0
846	HARANGAJO TO MAIBANG (AS-23) KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM ,	12/2003	280.00 -	612.58	612.58	02/2009 -	-	-	0/0
847	MAIBANG TO LUMDING (AS-25) KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM ,	12/2003	199.81 -	340.14	.00	04/2009 -	-	-	0/0
848	MAIBANG TO LUMDING (AS-26) KM.60.500 TO KM.83.400 NH-54 - [240106279]NHAI,ASSAM ,	12/2003	167.64 -	435.78	.00	11/2008 -	-	-	0/0
849	MAIBANG TO LUMDING (AS-24) KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM ,	12/2003	155.04 -	255.23	.00	11/2008 -	-	-	0/0
850	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM ,	12/2003	245.00 -	174.34	240.36	03/2008 -	08/2020	-	0/0
851	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM ,	12/2003	225.00 -	225.00	390.72	06/2008 -	09/2019	-	0/0
852	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM ,	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021	-	0/0
853	DHARAMTUL TO SONAPUR KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM ,	12/2003	160.00 -	167.98	270.97	05/2008 -	06/2019	-	0/0
854	HARANGAJO TO MAIBANG NH-54 - [N24000062]NHAI,ASSAM ,	12/2003	196.00 -	655.17	655.17	07/2009 -	-	-	0/0
855	BRAHMPUTRA BRIDGE NH NO-31 - [N24000063]NHAI,ASSAM ,	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	-	0/0
856	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM , EPC	05/2015	454.89 -	454.89	328.55	05/2018 -	03/2022	46(O) -	3/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
857	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM , EPC	06/2015	437.39 -	437.39	105.09	06/2018 -	12/2021	42(O) -	1/4
858	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM , EPC	06/2015	463.49 -	463.49	159.34	06/2018 -	12/2021	42(O) -	2/4
859	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM , EPC	03/2015	168.39 -	168.39	145.72	11/2018 -	11/2021	36(O) -	4/4
860	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM , EPC	10/2014	588.95 -	588.95	494.25	11/2018 -	02/2022	39(O) -	3/4
861	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM , EPC	11/2010	268.08 -	390.73	318.85	05/2017 05/2022	05/2022	60(O) 0	0/0
862	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM , EPC	01/1991	520.01 -	520.01	189.59	- -	12/2021	- -	2/4
863	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. -[N24000438]NHIDCL,ASSAM , EPC	12/2015	289.99 -	289.99	87.90	12/2018 -	12/2021	36(O) -	1/4
864	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM / KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM , EPC	01/2016	294.17 -	294.17	215.45	01/2016 -	03/2022	74(O) -	2/4
865	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM , EPC	01/2016	252.00 -	252.00	136.88	01/2016 -	03/2022	74(O) -	2/4
866	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM ,	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74(O) -	2/3
867	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM ,	10/2017	818.00 -	818.00	287.52	- -	03/2023	- -	1/4
868	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0 KM 54/0 TO KM 61/0 KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH,ASSAM ,	09/2018	160.00 -	160.00	116.26	09/2021 -	09/2021	0(O) -	0/0
869	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM ,	03/2017	1,049.51 -	1,049.51	143.02	- -	12/2021	- -	2/4
870	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM ,	03/2020	166.94 -	166.94	28.02	12/2020 12/2022	12/2022	24(O) 0	0/0
871	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]NHIDCL,ASSAM , EPC	03/2020	220.20 -	220.20	28.18	12/2022 -	12/2022	0(O) -	1/4
872	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]NHIDCL,ASSAM , EPC	08/2020	208.84 -	208.84	24.01	04/2022 -	04/2022	0(O) -	1/4
873	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]NHIDCL,ASSAM , EPC	08/2020	278.46 -	278.46	27.76	03/2022 -	03/2022	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
874	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]NHIDCL,ASSAM , EPC	03/2020	216.49 -	216.49	26.88	03/2022 -	03/2022	0(O) -	1/4
875	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]NHIDCL,ASSAM , EPC	11/2020	4,997.04 -	4,997.04	10.45	09/2028 -	09/2028	0(O) -	0/4
876	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328]NHIDCL,ASSAM , EPC	12/2020	804.00 -	804.00	3.23	08/2023 -	08/2023	0(O) -	0/4
877	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]NHIDCL,ASSAM , EPC	03/2020	261.13 -	261.13	23.56	06/2022 -	06/2022	0(O) -	0/4
878	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]NHIDCL,ASSAM , EPC	03/2020	217.50 -	217.50	34.17	06/2022 -	06/2022	0(O) -	0/4
879	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]NHIDCL,ASSAM , EPC	09/2019	761.54 -	761.54	86.48	05/2023 -	05/2023	0(O) -	1/4
880	DABOKA KATHKATI PACKAGE-2 - [N24001364]NHIDCL,ASSAM , EPC	03/2021	335.88 -	335.88	.00	01/2024 -	01/2024	0(O) -	0/0
881	DABOKA KATHKATI PACKAGE-4 - [N24001365]NHIDCL,ASSAM , EPC	02/2021	260.07 -	260.07	.00	12/2023 -	12/2023	0(O) -	0/0
882	DABOKA KATHKATI PACKAGE-5 - [N24001366]NHIDCL,ASSAM , EPC	03/2021	288.85 -	288.85	.00	01/2023 -	01/2023	0(O) -	0/0
883	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM , EPC	03/2021	636.42 -	636.42	.00	12/2022 -	12/2022	0(O) -	0/0
884	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]NHIDCL,ASSAM , EPC	03/2021	286.72 -	286.72	.00	01/2024 -	01/2024	0(O) -	0/0
885	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR , PPP (ANNUITY)	08/2010	671.30 -	671.30	.00	02/2013 -	-	-	3/4
886	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR , PPP (BOT)	09/2011	574.00 -	574.00	768.92	03/2014 -	-	-	0/0
887	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR ,	10/2011	375.09 -	375.09	494.33	04/2014 -	-	-	0/0
888	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI,BIHAR , PPP (ANNUITY)	01/2011	575.00 -	575.00	501.83	07/2013 12/2021	-	-	2/3
889	2 LANNING OF MUZZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR , PPP (ANNUITY)	05/2011	511.54 -	591.00	578.00	11/2013 -	-	-	0/0
890	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR , EPC	01/1991	675.00 780.77	675.00	364.81	- -	-	-	0/0
891	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR ,	08/2015	556.07 -	556.07	.00	-	-	-	0/0
892	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR ,	12/2015	1,041.10 -	1,041.10	377.35	04/2019 -	-	-	0/0
893	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR ,	08/2015	814.04 -	825.17	764.04	- -	10/2021	-	2/4
894	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR ,	08/2015	322.09 247.00	322.09	.00	04/2018 -	-	-	0/0
895	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI,BIHAR ,	01/1991	642.41 -	681.67	489.12	- -	-	-	1/4
896	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI,BIHAR ,	12/2015	1,167.45 -	1,182.94	267.10	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
897	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI,BIHAR ,	08/2015	399.54 -	297.27	259.67	04/2019 -	-	-	4/4
898	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI,BIHAR ,	08/2015	854.80 -	1,038.56	1,021.63	-	-	-	3/4
899	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI,BIHAR ,	08/2015	516.13 -	649.27	643.77	04/2018 -	-	-	4/4
900	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR , EPC	01/1991	319.68 -	369.77	301.91	-	-	-	0/0
901	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR ,	11/2013	683.83 683.82	560.70	691.29	07/2016 -	-	-	0/0
902	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR ,	02/2016	178.85 -	152.62	139.92	05/2016 -	-	-	0/0
903	ENGINEERING PROCUREMENT AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR ,	02/2016	553.30 -	478.35	524.35	05/2016 -	-	-	0/0
904	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR ,	01/2014	1,408.85 2,138.16	925.87	1,177.56	10/2016 -	-	-	0/0
905	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ - [N24000590]NHAI,BIHAR ,	05/2015	581.84 -	581.84	.00	05/2017 -	-	-	0/0
906	REHABILITATION OF 4-LANE 5.575 KM LONG 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR ,	08/2016	1,742.01 -	1,742.01	1,337.46	12/2016 -	-	-	0/0
907	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR ,	03/2017	672.89 -	736.01	74.96	03/2020 -	-	-	0/0
908	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR ,	03/2017	235.48 -	227.77	11.00	03/2020 -	05/2021	-	0/0
909	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR , Central Sector Projects	08/2017	950.64 -	950.64	308.25	08/2017 -	02/2022	54(O) -	0/0
910	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR ,	12/2017	2,598.00 1,962.50	1,962.50	235.00	- 01/2021	-	-	0/0
911	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR ,	01/2018	573.70 -	573.70	76.84	-	-	-	0/0
912	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR ,	01/2018	895.39 -	895.39	.00	-	-	-	0/0
913	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR ,	03/2018	496.20 -	537.17	58.32	-	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
914	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR ,	09/2018	1,478.40 -	1,478.40	27.02	- -	-	-	0/0
915	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR ,	03/2018	153.24 -	153.24	82.98	- -	-	-	0/0
916	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR ,	02/2019	2,926.42 -	2,926.42	211.88	- -	-	-	0/0
917	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR , EPC	10/2013	649.90 -	649.90	44.00	12/2020 -	-	-	0/0
918	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR , EPC	10/2013	446.97 -	446.97	.00	11/2020 -	-	-	0/0
919	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR , EPC	10/2013	464.09 -	464.09	.00	11/2020 -	-	-	0/0
920	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR , EPC	10/2019	1,101.99 -	1,101.99	181.13	02/2020 -	-	-	0/0
921	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH , EPC	12/2015	291.05 -	291.05	231.36	- 10/2021	10/2021	- 3	0/0
922	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH ,	12/2015	596.67 -	596.67	439.27	05/2018 -	-	-	0/0
923	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI,CHHATISGARH ,	12/2015	509.13 -	509.13	412.66	04/2018 -	-	-	0/0
924	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH ,	03/2018	1,029.96 -	1,261.05	333.72	- -	03/2021	-	0/0
925	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH ,	01/2016	497.14 572.66	572.66	278.09	08/2016 06/2022	06/2022	70(O) 9	0/0
926	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH ,	11/2015	335.32 -	335.32	275.33	06/2017 10/2021	10/2021	52(O) 1	0/0
927	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH ,	01/2016	476.20 543.73	544.00	400.49	09/2016 12/2021	12/2021	63(O) 3	0/0
928	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH ,	01/2016	624.98 731.50	731.50	460.02	10/2016 12/2021	12/2021	62(O) 3	0/0
929	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH ,	03/2016	452.94 435.61	435.61	107.15	07/2016 12/2022	12/2022	77(O) 15	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
930	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH ,	03/2017	423.79 -	423.79	289.08	01/2018 10/2021	10/2021	45(O) 1	0/0
931	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH ,	12/2014	496.02 -	496.02	240.54	03/2015 03/2022	03/2022	84(O) 0	0/0
932	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH ,	11/2017	188.80 -	188.80	87.05	05/2019 09/2021	09/2021	28(O) 0	0/0
933	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH ,	12/2014	379.16 -	379.16	313.04	11/2017 09/2021	09/2021	46(O) 0	0/0
934	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA ,	03/2015	298.33 -	298.33	325.55	- -	-	-	0/4
935	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA , EPC	03/2015	184.05 -	184.05	118.37	- -	-	-	2/4
936	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI MANGALORE SE - [N24000259]MoRTH,GOA , EPC	03/2015	280.16 -	290.59	244.36	- -	-	-	3/4
937	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA , EPC	10/2015	936.40 -	936.40	520.09	- -	-	-	0/0
938	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA , EPC	12/2015	773.98 -	773.98	394.63	- -	-	-	0/0
939	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA , EPC	12/2015	819.95 -	819.95	362.15	- -	-	-	0/0
940	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA ,	03/2017	634.32 -	634.32	292.34	05/2020 -	-	-	1/4
941	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA ,	03/2017	852.67 -	852.67	190.09	12/2019 -	-	-	1/4
942	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT , PPP (BOT)	03/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-	-	2/3
943	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT , PPP (BOT)	01/2011	953.88 -	953.88	.00	07/2013 -	-	-	0/0
944	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT , PPP (BOT)	01/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-	-	3/3
945	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT ,	03/2014	503.16 -	503.16	.00	08/2016 -	-	-	0/0
946	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT ,	05/2016	998.18 -	998.18	732.85	- -	-	-	2/2
947	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT ,	05/2016	834.64 -	834.64	203.40	- -	-	-	1/1
948	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE- IV) IN THE ST - [N24000569]NHAI, GUJARAT ,	05/2016	723.64 -	723.64	504.95	- -	-	-	2/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
949	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT ,	05/2016	763.08 -	763.08	398.51	- -	-	-	2/2
950	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT ,	05/2016	425.60 -	425.60	.00	- -	-	-	0/0
951	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT ,	05/2016	364.56 -	392.00	353.42	- -	08/2021	-	0/0
952	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT ,	07/2016	829.97 -	829.97	190.21	- -	-	-	0/0
953	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT ,	12/2016	417.19 -	417.19	199.86	- -	-	-	0/3
954	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT ,	01/2017	1,251.11 1,361.00	1,361.00	441.78	- -	-	-	0/0
955	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT ,	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	-	3/3
956	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT , Central Sector Projects	10/2017	232.49 -	232.49	.00	10/2017 -	-	-	0/0
957	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM,494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT ,	02/2018	1,052.21 -	1,449.00	342.39	- -	01/2021	-	0/0
958	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT ,	03/2018	2,702.05 -	2,043.00	1,888.51	- -	06/2021	-	0/0
959	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT ,	03/2018	1,437.64 -	1,437.64	564.11	- -	07/2021	-	0/0
960	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT ,	03/2018	1,161.39 -	1,161.39	.00	- -	-	-	0/0
961	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT , EPC	12/2017	867.97 -	867.97	577.48	11/2018 -	-	-	2/4
962	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT , EPC	03/2018	464.07 -	464.07	313.82	11/2018 -	-	-	4/4
963	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT , EPC	10/2018	400.76 -	400.76	166.41	05/2019 -	-	-	2/4
964	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT , EPC	08/2017	962.43 -	962.43	282.94	03/2018 -	-	-	1/4
965	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT ,	03/2018	351.00 -	351.00	154.34	06/2021 -	06/2021	-	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
966	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA , PPP (BOT)	04/2007	486.00 -	486.00	470.01	05/2010 -	-	-	0/0
967	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA , PPP (BOT)	05/2009	1,108.00 3,485.00	2,288.00	3,450.00	11/2011 -	-	-	0/0
968	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA ,	12/2015	602.95 -	507.70	.00	06/2016 -	-	-	0/0
969	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA ,	01/2016	574.28 -	537.16	.00	07/2018 -	-	-	0/0
970	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA , PPP (BOT)	07/2015	2,128.72 -	2,128.72	1,577.44	04/2019 -	09/2021	29(O) -	0/0
971	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA ,	03/2018	1,484.30 -	1,484.30	262.70	- 06/2021	12/2020	-	0/0
972	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA ,	03/2018	275.12 -	275.12	170.81	- -	-	-	0/0
973	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA ,	03/2018	307.79 -	307.79	197.30	- -	-	-	0/0
974	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA ,	03/2018	634.70 -	931.21	143.54	- -	-	-	0/0
975	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA ,	03/2018	795.50 906.65	922.64	353.55	- -	-	-	0/0
976	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA ,	03/2018	198.05 -	198.05	130.78	- -	-	-	0/0
977	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA ,	03/2018	181.78 -	181.78	129.84	- -	-	-	0/0
978	REDESIGNING REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA ,	03/2018	551.58 -	551.58	305.46	- -	-	-	0/0
979	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA ,	01/2017	247.25 -	247.25	179.30	03/2019 -	-	-	0/0
980	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA ,	01/2019	1,051.91 -	1,051.91	807.68	- -	-	-	0/0
981	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA ,	01/2019	1,120.06 -	1,120.06	831.50	- -	-	-	0/0
982	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA ,	01/2019	1,137.42 -	1,137.42	903.95	- -	-	-	0/0
983	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA ,	01/2019	1,033.19 -	1,033.19	876.52	- -	-	-	0/0
984	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA ,	01/2019	1,243.45 -	1,243.45	958.21	- -	-	-	0/0
985	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA ,	01/2019	889.36 -	889.36	637.39	- -	-	-	0/0
986	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA ,	01/2019	1,018.79 -	1,018.79	703.08	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
987	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA ,	01/2019	996.65 -	996.65	947.82	- -	-	-	0/0
988	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH , PPP (BOT)	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-	-	0/0
989	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI,HIMACHAL PRADESH ,	09/2015	934.46 -	934.46	1,298.21	03/2018 -	-	-	0/0
990	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI,HIMACHAL PRADESH ,	02/2016	273.20 -	273.20	668.42	02/2019 -	-	-	0/0
991	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH ,	08/2016	1,583.18 -	1,583.18	.00	- -	-	-	0/0
992	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH ,	09/2016	1,273.71 -	1,273.71	826.42	- -	-	-	0/0
993	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH ,	10/2016	447.75 -	447.75	1,324.11	- -	-	-	0/0
994	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P. - [N24000692]NHAI,HIMACHAL PRADESH ,	06/2017	2,485.93 -	2,485.93	983.69	06/2020 -	09/2021	15(O)	0/0
995	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050 ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH ,	03/2018	478.74 -	478.74	714.50	- -	-	-	0/0
996	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH , EPC	08/2020	272.98 -	272.98	8.75	04/2021 -	04/2021	-	0/0
997	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH , EPC	08/2020	242.80 -	242.80	7.55	03/2021 -	03/2021	-	0/0
998	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH , EPC	08/2020	349.20 -	349.20	.00	04/2021 -	04/2021	-	0/0
999	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,987.00 -	1,987.00	3,113.72	07/2015 -	09/2020	-	0/0
1000	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	-	0/0
1001	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	07/2010	1,813.76 -	1,813.76	2,652.71	07/2013 -	-	-	0/0
1002	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR , PPP (ANNUITY)	06/2011	1,100.70 -	1,100.70	2,932.90	06/2014 -	10/2020	-	0/0
1003	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR ,	12/2015	2,168.66 -	2,168.66	1,108.16	06/2019 -	-	-	0/0
1004	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR ,	12/2015	2,136.97 -	2,136.97	1,719.20	12/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1005	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR ,	12/2017	1,471.75 1,339.00	1,339.00	928.92	- -	01/2021	-	2/3
1006	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR ,	03/2018	404.17 -	404.17	203.27	08/2018 -	-	-	2/4
1007	WIDENING AND UPGADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR ,	03/2018	216.00 -	216.00	96.79	11/2018 -	-	-	1/4
1008	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR ,	03/2018	253.44 -	253.44	72.23	07/2019 -	-	-	0/4
1009	CONSTRUCTION OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]NHIDCL,JAMMU AND KASHMIR ,	12/2019	2,680.42 -	2,680.42	794.41	12/2023 -	12/2023	0(O) -	1/4
1010	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG B-I-D - [N24001256]NHIDCL,JAMMU AND KASHMIR , EPC	08/2020	6,808.69 -	6,808.69	176.00	09/2026 -	09/2026	0(O) -	0/6
1011	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	228.39 -	228.39	9.72	04/2022 -	04/2022	0(O) -	1/4
1012	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]NHIDCL,JAMMU AND KASHMIR , EPC	07/2020	210.79 -	210.79	10.84	04/2022 -	04/2022	0(O) -	1/4
1013	KHELLANI-KHANABAL PKG-1 - [N24001323]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	486.45 -	486.45	14.16	09/2022 -	09/2022	0(O) -	0/4
1014	KHELLANI-KHANABAL PKG-6 - [N24001324]NHIDCL,JAMMU AND KASHMIR , EPC	02/2021	285.28 -	285.28	.33	09/2022 -	09/2022	0(O) -	0/4
1015	KHELLANI-KHANABAL PKG-3 - [N24001341]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	398.51 -	398.51	.00	12/2022 -	12/2022	0(O) -	0/0
1016	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]NHIDCL,JAMMU AND KASHMIR , EPC	03/2021	260.40 -	260.40	.00	12/2022 -	12/2022	0(O) -	0/0
1017	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND ,	07/2016	458.03 -	486.00	406.73	- -	-	-	0/0
1018	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND ,	08/2016	323.72 -	336.60	316.60	08/2018 -	-	-	0/0
1019	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND ,	01/2018	273.46 -	276.17	99.20	- -	-	-	0/0
1020	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND ,	01/2018	1,155.16 -	1,155.16	474.16	- -	-	-	0/0
1021	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND ,	03/2018	1,005.08 1,073.10	1,005.08	.00	- 03/2021	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1022	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]MoRTH,JHARKHAND ,	12/2016	196.00 -	196.00	100.31	09/2021 -	09/2021	0(O) -	0/4
1023	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA ,	09/2010	946.00 -	946.00	818.53	06/2018 -	-	-	3/3
1024	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA , EPC	03/2015	165.67 -	165.67	116.49	11/2015 -	-	-	0/0
1025	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA , PPP (BOT)	05/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020	-	0/0
1026	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA , PPP (BOT)	03/2015	1,388.00 -	1,388.00	1,311.00	08/2018 -	-	-	0/0
1027	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA ,	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36(O) -	0/0
1028	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA ,	03/2016	870.00 -	870.00	36.30	03/2019 -	11/2020	-	0/0
1029	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA ,	08/2016	1,664.20 -	1,664.20	1,110.25	04/2020 -	12/2020	-	0/0
1030	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA ,	08/2016	1,167.42 -	870.00	334.82	03/2019 01/2021	09/2022	42(O) 0	0/0
1031	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA ,	09/2016	950.69 1,918.36	1,108.00	1,462.10	08/2019 -	-	-	0/0
1032	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA ,	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	-	0/0
1033	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA ,	03/2017	993.16 -	1,434.00	1,310.52	03/2020 -	-	-	0/0
1034	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA ,	02/2018	486.78 -	486.78	171.98	- -	-	-	0/0
1035	SIX-LANING OF BANGALORE – NIDAGATTA SECTION KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA ,	02/2018	1,995.34 -	2,400.00	3,368.89	- -	11/2021	- -	0/0
1036	SIX LANING OF NIDAGATTA-MYSORE SECTION KM 74.20 TO KM 135.304 OF NH-275 IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA ,	02/2018	2,177.80 -	2,450.00	2,425.12	- -	-	-	0/0
1037	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156]MoRTH,KARNATAKA ,	01/2017	166.67 -	166.67	184.91	09/2017 -	-	-	0/0
1038	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA ,	08/2016	175.50 -	175.50	162.58	02/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1039	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA ,	03/2018	159.97 -	159.97	38.24	06/2019 -	-	-	0/0
1040	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA ,	01/2018	159.70 -	159.70	112.10	07/2018 -	-	-	0/0
1041	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA ,	09/2017	191.60 -	191.60	110.74	10/2018 -	-	-	0/0
1042	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- [N24001161]MoRTH,KARNATAKA ,	12/2017	297.30 -	318.28	168.33	01/2019 -	-	-	0/0
1043	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA ,	03/2018	325.86 -	386.41	341.72	10/2018 -	-	-	0/0
1044	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA ,	08/2016	329.01 -	329.01	238.10	02/2017 -	-	-	0/0
1045	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA ,	10/2016	396.96 -	396.96	276.73	03/2017 -	-	-	0/0
1046	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA ,	11/2016	314.90 -	314.90	208.97	03/2017 -	-	-	0/0
1047	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA ,	03/2015	159.12 -	159.12	.00	01/2016 -	-	-	0/0
1048	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA ,	05/2018	171.60 -	171.60	74.83	05/2018 -	-	-	0/0
1049	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA ,	01/2017	291.49 -	291.49	219.48	08/2017 -	-	-	0/0
1050	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA ,	02/2017	157.32 188.00	157.32	.28	05/2019 -	-	-	0/0
1051	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA , EPC	01/2017	264.34 -	264.34	.00	09/2017 -	09/2017	-	0/0
1052	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA , EPC	03/2019	423.15 -	423.15	157.00	12/2019 -	12/2019	-	0/0
1053	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA , PPP (BOT)	02/2010	617.00 -	617.00	.00	08/2012 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1054	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA , EPC	01/2014	255.75 348.00	348.43	314.12	09/2017 -	-	-	0/0
1055	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA ,	06/2015	845.24 -	941.00	881.72	- 01/2020	01/2020	-	0/0
1056	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA ,	04/2016	804.97 -	804.97	561.12	06/2018 -	-	-	0/0
1057	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA , Central Sector Projects	09/2017	1,124.11 -	1,232.76	628.26	09/2017 -	-	-	0/0
1058	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA ,	02/2018	1,424.77 -	1,853.42	14.19	- -	-	-	0/0
1059	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA , EPC	02/2017	294.28 -	294.26	126.74	08/2017 -	-	-	0/0
1060	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA , EPC	02/2017	380.76 -	380.76	238.42	09/2017 -	-	-	0/0
1061	KARGIL-ZANSKR PACKAGE-5 - [N24001330]NHIDCL,LADAKH , EPC	08/2020	169.79 -	169.79	19.50	12/2023 -	12/2023	0(O) -	0/4
1062	KARGIL-ZANSKR PACKAGE-1 - [N24001343]NHIDCL,LADAKH , EPC	03/2021	384.23 -	384.23	.00	01/2023 -	01/2023	0(O) -	0/0
1063	KARGIL-ZANSKR PACKAGE-2 - [N24001344]NHIDCL,LADAKH , EPC	03/2021	404.89 -	404.89	.00	01/2023 -	01/2023	0(O) -	0/0
1064	KARGIL-ZANSKR PACKAGE-3 - [N24001345]NHIDCL,LADAKH , EPC	08/2020	381.01 -	381.01	.00	01/2023 -	01/2023	0(O) -	0/0
1065	KARGIL-ZANSKR PACKAGE-6 - [N24001346]NHIDCL,LADAKH , EPC	01/2021	239.81 -	239.81	23.77	05/2024 -	05/2024	0(O) -	0/0
1066	KARGIL-ZANSKR PACKAGE-7 - [N24001347]NHIDCL,LADAKH , EPC	01/2021	308.86 -	308.86	9.46	06/2024 -	06/2024	0(O) -	0/0
1067	KARGIL-ZANSKR PACKAGE-8 - [N24001348]NHIDCL,LADAKH , EPC	03/2021	398.37 -	398.37	.00	01/2023 -	01/2023	0(O) -	0/0
1068	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH , PPP (BOT)	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-	-	4/4
1069	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH , PPP (BOT)	11/2010	325.00 -	475.00	469.54	05/2013 -	-	-	3/3
1070	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH , EPC	06/2015	390.51 -	390.51	271.94	- 03/2021	12/2021	- 5	0/0
1071	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH , BOT (TOLL)	01/2012	410.72 -	410.72	392.42	04/2015 -	-	-	0/0
1072	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH ,	03/2015	795.76 -	686.13	669.94	- -	-	-	0/0
1073	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH ,	03/2015	794.30 -	691.38	669.35	- -	-	-	0/0
1074	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH , EPC	11/2015	628.45 -	628.45	445.35	01/2020 06/2021	09/2021	20(O) 2	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1075	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH , EPC	12/2015	957.54 -	957.54	765.48	02/2020 04/2021	09/2021	19(O) 1	0/0
1076	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH ,	03/2015	928.83 -	928.83	867.83	-	-	-	0/0
1077	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH , PPP (BOT)	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	-	0/0
1078	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH ,	06/2015	1,012.90 -	1,012.90	226.10	03/2016 -	-	-	0/0
1079	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI,MADHYA PRADESH ,	03/2015	810.22 -	810.22	742.47	-	-	-	0/0
1080	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH , EPC	03/2015	511.83 -	511.83	387.81	08/2017 06/2021	12/2022	64(O) 0	0/0
1081	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH ,	08/2016	227.49 -	227.49	.00	01/2019 -	-	-	4/4
1082	FOUR LANNING BALANCE WORK FOR BHOPAL - BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH , Central Sector Projects	10/2017	639.97 -	639.97	484.15	10/2017 -	-	-	3/4
1083	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	374.40 -	204.65	313.11	09/2017 -	-	-	3/4
1084	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH , Central Sector Projects	09/2017	990.61 -	990.61	664.13	09/2017 -	-	-	3/4
1085	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH ,	12/2017	950.27 -	950.27	266.64	-	08/2021	-	3/4
1086	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH ,	01/2018	770.73 -	770.73	409.98	-	-	-	0/0
1087	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH ,	03/2018	162.56 -	162.56	137.02	03/2018 10/2021	10/2021	43(O) 0	0/0
1088	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH ,	03/2018	166.21 -	173.41	154.26	08/2018 08/2021	09/2021	37(O) 1	0/0
1089	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH ,	02/2018	169.63 -	169.63	52.44	03/2018 04/2021	04/2022	49(O) 0	0/0
1090	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH ,	11/2017	184.62 -	184.62	125.42	02/2018 09/2021	09/2021	43(O) 0	0/0
1091	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH ,	01/2017	205.05 -	205.05	126.89	03/2017 06/2021	12/2021	57(O) 4	0/0
1092	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH ,	03/2018	214.69 -	214.69	78.48	03/2018 09/2021	06/2022	51(O) 9	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1093	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH ,	03/2018	217.22 -	226.88	173.03	08/2018 09/2021	09/2021	37(O) 0	0/0
1094	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH ,	03/2018	233.04 -	233.04	165.60	03/2018 10/2021	10/2021	43(O) 0	0/0
1095	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH ,	11/2017	249.05 -	249.05	198.83	07/2018 08/2021	12/2021	41(O) 4	0/0
1096	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH ,	11/2017	254.17 -	254.17	175.37	02/2018 03/2022	03/2022	49(O) 0	0/0
1097	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH ,	02/2018	279.44 -	279.44	203.95	03/2018 11/2021	11/2021	44(O) 0	0/0
1098	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH ,	01/2017	373.82 -	373.82	232.63	09/2019 06/2021	09/2021	24(O) 1	0/0
1099	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH ,	01/2016	809.16 -	809.16	615.21	07/2018 05/2021	11/2021	40(O) 4	0/0
1100	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193.0 TO KM - [N24000899]MoRTH,MADHYA PRADESH ,	03/2016	877.79 -	877.79	741.88	06/2019 04/2021	12/2021	30(O) 4	0/0
1101	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH ,	01/2017	359.00 359.00	359.00	315.85	06/2019 -	-	-	0/4
1102	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH ,	11/2017	392.33 428.55	428.55	379.29	03/2018 06/2021	10/2021	43(O) 0	0/0
1103	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH ,	01/2019	264.50 -	264.50	106.37	03/2021 11/2021	11/2021	8(O) 0	0/0
1104	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH ,	10/2019	743.88 -	743.89	407.00	- -	12/2021	- -	1/3
1105	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH ,	12/2017	656.98 -	840.00	223.00	- -	11/2022	- -	1/4
1106	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH ,	12/2017	1,094.97 -	1,094.97	737.00	- -	02/2022	- -	2/4
1107	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH ,	12/2017	217.96 -	884.00	443.00	- -	10/2022	- -	2/4
1108	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH ,	02/2019	990.97 -	990.97	690.00	12/2019 -	12/2021	24(O) -	2/3
1109	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH ,	02/2019	847.00 -	847.00	498.00	03/2020 -	04/2022	25(O) -	2/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1110	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH ,	03/2019	1,047.00 -	1,047.00	486.00	05/2020 -	05/2022	24(O) -	2/3
1111	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH ,	02/2019	996.27 -	996.27	560.00	03/2020 -	-	-	2/3
1112	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH , PPP BOT (Hybrid Annuity)	11/2019	716.00 -	716.00	.00	07/2021 -	07/2021	-	0/0
1113	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA , PPP (BOT)	10/2010	1,724.55 -	1,724.55	2,615.35	03/2013 -	09/2021	102(O) -	0/0
1114	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI,MAHARASHTRA , PPP (BOT)	05/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-	-	2/2
1115	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA , EPC	03/2015	168.30 -	168.30	106.56	- -	-	-	0/4
1116	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA , EPC	08/2014	187.79 -	187.79	82.95	07/2016 -	-	-	0/12
1117	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA , EPC	01/2014	446.77 -	446.77	303.72	- -	-	-	3/4
1118	WIDENING NH-848 FROM KM 16.000 TO 34.000 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA , EPC	10/2015	289.60 -	289.60	160.70	- -	-	-	0/0
1119	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA , EPC	01/2015	225.81 -	225.81	107.34	- -	-	-	0/0
1120	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA ,	09/2015	414.51 -	414.00	409.16	05/2018 11/2020	11/2020	-	1/1
1121	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA ,	10/2015	531.13 -	744.73	685.76	05/2018 03/2022	03/2022	46(O) 0	0/0
1122	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA , EPC	07/2015	1,885.74 -	1,885.74	1,636.02	05/2019 -	-	-	0/0
1123	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA ,	10/2015	593.26 716.78	716.78	617.58	05/2018 03/2022	03/2022	46(O) 0	0/1
1124	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB SERVICE ROADS FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA ,	12/2015	649.50 -	649.50	233.12	03/2019 12/2021	06/2022	39(O) 0	0/0
1125	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA ,	08/2015	505.00 -	504.00	415.26	05/2018 04/2019	06/2021	-	0/1
1126	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA , PPP (BOT)	01/2015	972.50 -	972.50	1,492.00	07/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1127	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA , PPP (BOT)	06/2014	923.04 -	923.04	866.79	11/2016 -	-	-	0/0
1128	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI,MAHARASHTRA , PPP (BOT)	07/2015	1,871.34 -	1,871.34	.00	01/2018 -	-	-	0/0
1129	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI,MAHARASHTRA ,	04/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-	-	0/0
1130	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI,MAHARASHTRA ,	03/2016	197.69 -	197.69	.00	07/2018 -	-	-	0/0
1131	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA ,	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29(O) -	0/0
1132	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA ,	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29(O) -	0/0
1133	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MORTH,MAHARASHTRA ,	03/2016	1,142.62 -	1,142.62	978.04	-	-	-	0/0
1134	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MORTH,MAHARASHTRA ,	03/2016	1,101.58 -	1,101.58	334.55	-	-	-	0/0
1135	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA ,	11/2016	1,071.61 -	1,048.10	1,091.93	-	07/2021	-	3/4
1136	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA ,	11/2016	1,064.88 -	1,021.00	409.21	-	07/2021	-	2/4
1137	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA ,	11/2016	400.25 -	400.25	140.57	03/2019 -	-	-	0/0
1138	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA ,	11/2016	446.17 -	446.17	112.52	03/2019 -	-	-	0/0
1139	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA ,	11/2016	290.73 -	315.00	246.70	-	-	-	0/0
1140	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA ,	01/2017	244.90 -	244.90	251.87	05/2019 -	-	-	0/0
1141	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA ,	02/2017	904.16 911.07	904.16	.00	02/2020 03/2021	-	-	0/0
1142	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA ,	03/2017	247.02 -	157.49	31.97	03/2020 -	-	-	0/0
1143	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA ,	03/2017	744.64 -	982.00	.00	03/2020 -	-	-	0/0
1144	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA ,	03/2017	1,030.44 -	1,065.51	.00	03/2020 -	-	-	0/3

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1145	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA ,	03/2017	988.34 -	1,043.28	.00	03/2020 -	-	-	3/3
1146	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA ,	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	-	0/0
1147	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA ,	03/2017	296.19 -	254.00	254.85	03/2020 -	-	-	0/0
1148	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA ,	03/2017	1,098.06 -	1,160.64	.00	03/2020 -	-	-	0/3
1149	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA ,	12/2017	404.94 495.24	448.18	462.99	- 05/2021	08/2021	- 0	0/0
1150	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA ,	01/2018	607.00 -	607.00	510.71	- -	08/2021	- -	0/1
1151	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA ,	01/2018	621.00 -	621.00	595.00	- -	-	-	2/3
1152	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA , EPC	03/2018	291.53 -	291.53	197.49	- -	02/2022	- -	0/0
1153	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA , EPC	03/2018	289.21 -	289.21	224.45	- -	01/2022	- -	0/0
1154	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA ,	03/2018	1,162.92 -	1,162.92	60.06	- -	07/2021	-	0/0
1155	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA ,	03/2018	642.13 -	807.00	691.19	- -	-	-	0/0
1156	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA ,	02/2016	545.64 -	545.64	177.20	07/2019 -	-	-	0/4
1157	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA ,	01/2017	313.95 -	313.95	68.33	06/2019 -	-	-	0/4
1158	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA ,	01/2017	245.77 246.00	245.77	202.72	06/2019 -	-	-	0/4
1159	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA ,	02/2017	203.21 203.00	203.21	150.09	05/2019 -	-	-	0/0
1160	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA ,	02/2017	373.10 373.00	373.10	314.20	05/2019 -	-	-	0/4
1161	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA ,	02/2017	322.48 322.00	322.48	230.03	05/2019 -	-	-	0/4
1162	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA ,	02/2017	548.03 548.00	548.03	387.91	06/2019 -	-	-	0/4
1163	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA ,	01/2017	391.06 391.00	391.06	235.49	06/2019 -	-	-	0/0
1164	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA ,	01/2017	385.87 386.00	385.87	258.29	06/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1165	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA ,	01/2017	341.16 341.00	341.16	228.07	06/2019 -	-	-	0/0
1166	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA ,	01/2017	471.61 472.00	471.61	321.02	06/2019 -	-	-	0/0
1167	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA ,	01/2017	228.89 229.00	228.89	154.69	06/2019 -	-	-	3/4
1168	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA ,	01/2017	392.83 393.00	392.83	273.42	06/2019 -	-	-	0/0
1169	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA ,	01/2017	463.62 664.00	463.62	258.30	06/2019 -	-	-	0/4
1170	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA ,	01/2017	396.91 397.00	396.91	280.56	06/2019 -	-	-	3/4
1171	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA ,	01/2017	363.82 364.00	363.82	39.43	09/2019 -	-	-	1/4
1172	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA ,	01/2017	376.72 377.00	376.72	261.86	06/2019 -	-	-	0/4
1173	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA ,	01/2017	457.52 -	457.52	352.94	07/2019 -	-	-	2/4
1174	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA ,	01/2017	355.17 -	355.17	269.58	07/2019 -	-	-	3/4
1175	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA ,	01/2017	376.19 -	376.19	70.16	05/2019 -	-	-	1/4
1176	SHAHUPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA ,	01/2018	150.79 -	150.79	59.88	12/2019 -	-	-	1/4
1177	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA ,	01/2018	170.00 -	170.00	118.19	12/2019 -	-	-	0/4
1178	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA ,	01/2017	422.38 -	422.38	224.47	08/2019 -	-	-	2/4
1179	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA ,	01/2017	595.77 -	595.77	286.10	08/2019 -	-	-	2/4
1180	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA ,	01/2017	228.54 -	228.54	159.32	08/2019 -	-	-	2/4
1181	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA ,	01/2017	409.62 410.00	409.62	227.76	05/2019 -	-	-	0/4
1182	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA ,	01/2017	486.19 -	486.19	303.24	07/2019 -	-	-	2/4
1183	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA ,	01/2017	420.57 -	420.57	261.37	07/2019 -	-	-	2/4
1184	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA ,	01/2018	418.36 -	418.36	263.13	12/2019 -	-	-	0/4
1185	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA ,	01/2017	554.78 -	554.78	292.74	07/2019 -	-	-	2/4
1186	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA ,	07/2018	237.40 -	237.40	9.66	05/2020 -	-	-	0/4
1187	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA ,	01/2017	356.66 -	356.66	122.34	- -	-	-	0/4
1188	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA ,	01/2017	461.96 -	461.96	303.98	11/2019 -	-	-	2/4
1189	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA ,	01/2017	211.34 -	211.34	128.55	07/2019 -	-	-	2/4
1190	SALAIKHURD TO TIRODA - [N24001042]MoRTH,MAHARASHTRA ,	01/2018	415.25 415.25	415.25	262.66	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above. (All Cost/ Expenditure in Rs. Crore)

						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1191	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA ,	01/2018	420.63 421.00	420.63	155.97	05/2020 -	-	-	0/4
1192	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA ,	01/2017	467.78 -	467.78	210.81	06/2019 -	-	-	0/4
1193	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA ,	01/2018	307.54 308.00	307.54	200.06	11/2019 -	-	-	0/4
1194	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA ,	01/2017	210.81 -	210.81	210.81	07/2019 -	-	-	0/4
1195	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA ,	01/2018	259.55 260.00	259.55	204.49	11/2019 -	-	-	0/0
1196	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA ,	01/2017	232.77 -	232.77	151.60	07/2019 -	-	-	0/0
1197	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA ,	01/2018	344.85 245.00	344.85	210.84	12/2019 -	-	-	0/4
1198	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA ,	03/2018	304.58 305.00	304.58	120.71	12/2019 -	-	-	0/4
1199	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA ,	02/2018	274.50 275.00	274.50	143.39	12/2019 -	-	-	0/4
1200	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA ,	01/2018	257.38 257.00	257.38	147.24	12/2019 -	-	-	0/4
1201	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA ,	01/2017	537.81 538.00	537.81	173.98	06/2019 -	-	-	0/4
1202	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA ,	01/2017	195.64 196.00	195.64	116.30	11/2019 -	-	-	0/4
1203	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA ,	02/2017	416.99 -	416.99	223.81	07/2019 -	-	-	0/4
1204	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA ,	02/2017	422.02 422.00	422.02	297.76	07/2019 -	-	-	0/0
1205	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA ,	02/2017	407.19 407.00	407.19	175.93	06/2019 -	-	-	0/4
1206	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA ,	03/2018	276.95 277.00	276.95	253.47	12/2019 -	-	-	0/4
1207	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA ,	03/2018	181.08 -	181.08	97.86	12/2019 -	-	-	0/4
1208	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA ,	03/2018	227.19 227.00	227.19	134.75	12/2019 -	-	-	0/4
1209	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA ,	03/2018	189.46 189.00	189.46	107.85	12/2019 -	-	-	0/4
1210	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA ,	03/2018	336.21 336.00	336.21	208.61	12/2019 -	-	-	0/4
1211	WADIGODRI TO DHANGRIPIPRI - [N24001063]MoRTH,MAHARASHTRA ,	03/2018	194.23 194.00	194.23	106.45	02/2020 -	-	-	0/4
1212	DHANGRIPIPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA ,	03/2018	217.14 217.00	217.14	134.90	02/2020 -	-	-	0/4
1213	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA ,	03/2018	238.19 238.00	238.19	154.05	12/2019 -	-	-	0/4
1214	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA ,	03/2018	336.47 336.00	336.47	185.03	12/2019 -	-	-	0/4
1215	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA ,	03/2018	272.04 272.00	272.04	218.03	12/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1216	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA ,	03/2018	165.51 -	165.51	133.93	12/2019 -	-	-	1/4
1217	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA ,	12/2017	456.93 457.00	456.93	155.00	09/2019 -	-	-	1/4
1218	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA ,	03/2018	182.63 -	182.63	137.99	12/2019 -	-	-	2/4
1219	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA ,	07/2018	299.92 300.00	299.92	164.11	08/2020 -	-	-	0/4
1220	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA ,	03/2018	181.30 -	181.30	137.37	12/2019 -	-	-	0/4
1221	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA ,	09/2018	301.38 301.00	301.38	144.50	08/2020 -	-	-	0/0
1222	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA ,	03/2018	249.29 -	249.29	155.48	12/2019 -	-	-	0/0
1223	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA ,	09/2017	344.25 344.00	344.25	139.00	08/2020 -	-	-	0/4
1224	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA ,	03/2018	219.91 -	219.91	123.76	12/2019 -	-	-	0/0
1225	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA ,	01/2018	225.25 225.00	225.25	199.34	12/2019 -	-	-	2/4
1226	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA ,	03/2018	228.31 -	228.31	73.45	12/2019 -	-	-	0/0
1227	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA ,	12/2017	426.06 426.00	426.06	190.63	06/2020 -	-	-	1/4
1228	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA ,	03/2018	256.15 -	256.15	174.63	12/2019 -	-	-	0/0
1229	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA ,	03/2018	294.87 295.00	294.87	120.82	12/2019 -	-	-	1/4
1230	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA ,	03/2018	223.46 -	223.46	52.22	12/2019 -	-	-	0/0
1231	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA ,	03/2018	393.10 393.00	393.10	224.68	12/2019 -	-	-	2/4
1232	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA ,	01/2017	244.93 -	244.93	159.96	05/2020 -	-	-	0/4
1233	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA ,	09/2017	417.90 418.00	417.90	217.12	06/2019 -	-	-	0/4
1234	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA ,	01/2017	178.26 -	178.26	159.96	07/2019 -	-	-	0/4
1235	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA ,	03/2018	222.13 222.00	222.13	156.87	11/2019 -	-	-	0/4
1236	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA ,	03/2018	177.84 177.00	177.84	110.20	12/2019 -	-	-	0/0
1237	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA ,	02/2018	303.24 303.00	303.24	193.15	12/2019 -	-	-	0/4
1238	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA ,	01/2017	509.18 -	509.18	228.82	07/2019 -	-	-	0/4
1239	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA ,	03/2016	536.65 356.00	536.65	550.22	12/2019 12/2021	12/2021	24(O) 3	0/0
1240	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA ,	01/2017	653.46 -	653.46	258.53	07/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1241	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA ,	12/2017	309.94 310.00	309.94	186.03	12/2019 -	-	-	0/0
1242	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA ,	12/2017	244.04 244.00	244.04	161.70	03/2019 -	-	-	0/0
1243	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA ,	01/2017	388.44 -	388.44	199.61	- -	-	-	0/0
1244	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA ,	01/2018	264.41 264.00	264.41	173.14	03/2019 -	-	-	0/0
1245	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA ,	07/2018	404.33 404.00	404.33	22.40	05/2020 -	-	-	0/4
1246	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA ,	01/2018	216.90 217.00	216.90	144.43	12/2019 -	-	-	1/4
1247	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA ,	01/2017	488.60 -	488.60	224.72	07/2019 -	-	-	0/4
1248	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA ,	01/2017	955.40 -	955.40	459.15	08/2019 -	-	-	0/4
1249	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA ,	01/2017	307.63 -	307.63	190.69	07/2019 -	-	-	0/4
1250	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA ,	07/2017	218.38 -	218.38	170.80	07/2019 -	-	-	0/4
1251	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA ,	01/2017	250.46 -	250.46	174.16	07/2019 -	-	-	0/4
1252	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA ,	10/2016	322.55 -	322.55	189.60	06/2019 -	-	-	2/4
1253	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA ,	11/2016	467.70 -	467.70	164.90	03/2019 -	-	-	0/4
1254	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA ,	03/2018	301.39 302.00	301.39	78.99	03/2018 -	-	-	0/4
1255	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA ,	07/2018	381.08 302.00	381.08	9.66	05/2020 -	-	-	0/4
1256	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA ,	03/2018	206.97 207.00	206.97	142.46	12/2019 -	-	-	0/4
1257	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA ,	03/2018	243.45 244.00	243.45	154.68	12/2019 -	-	-	0/4
1258	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA ,	09/2017	241.69 242.00	241.69	166.84	04/2020 -	-	-	1/4
1259	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA ,	04/2016	281.78 282.00	281.78	281.73	04/2019 -	-	-	0/4
1260	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA ,	07/2016	406.54 407.00	406.54	172.47	09/2019 -	-	-	2/4
1261	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA ,	07/2016	289.11 290.00	289.11	101.90	09/2018 -	-	-	0/4
1262	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA ,	01/2017	1,202.52 1,203.00	1,202.52	973.05	12/2019 -	-	-	1/4
1263	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA ,	01/2017	1,598.47 1,560.00	1,598.47	1,020.24	11/2019 -	-	-	1/4
1264	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA ,	12/2016	484.15 -	484.15	321.93	06/2019 -	-	-	2/4
1265	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA ,	12/2016	162.34 -	162.34	48.40	07/2019 -	-	-	1/4
1266	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA ,	01/2017	362.96 -	362.96	148.22	06/2019 -	-	-	0/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1267	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA ,	09/2016	269.05 -	269.05	222.40	07/2019 -	-	-	0/4
1268	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA ,	12/2015	289.60 -	289.60	210.10	11/2018 -	-	-	0/4
1269	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA ,	03/2017	341.80 -	341.80	134.43	06/2019 -	-	-	0/4
1270	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA ,	02/2017	381.77 -	381.77	177.79	06/2019 -	-	-	0/4
1271	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA ,	02/2017	456.32 -	456.32	330.00	06/2019 -	-	-	0/4
1272	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA ,	02/2017	337.46 -	337.46	231.00	06/2019 -	-	-	0/4
1273	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA ,	02/2017	456.45 -	456.45	285.49	06/2019 -	-	-	0/4
1274	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA ,	02/2017	406.51 -	406.51	290.64	06/2019 -	-	-	0/0
1275	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA ,	02/2017	295.09 -	295.99	169.64	07/2019 -	-	-	0/4
1276	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA ,	09/2017	743.21 743.00	743.21	290.00	06/2021 -	-	-	1/4
1277	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA ,	04/2016	983.14 983.00	983.14	709.06	12/2019 -	-	-	1/4
1278	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA ,	03/2016	1,230.02 1,230.00	1,230.02	631.68	11/2019 -	-	-	1/4
1279	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA ,	02/2016	1,244.75 1,245.00	1,244.75	840.10	02/2019 -	-	-	0/0
1280	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA ,	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-	-	2/4
1281	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA ,	09/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-	-	3/5
1282	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA ,	02/2017	205.72 206.00	205.72	71.12	06/2019 -	-	-	1/4
1283	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA ,	02/2018	355.99 -	355.99	238.22	12/2019 -	-	-	0/0
1284	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA ,	02/2018	313.58 -	313.58	164.00	04/2020 -	-	-	0/4
1285	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA , EPC	02/2019	731.89 -	731.89	.00	11/2019 -	11/2019	-	0/0
1286	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA , EPC	02/2019	362.46 -	362.46	.00	11/2019 -	11/2019	-	0/0
1287	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA , EPC	02/2019	594.75 -	594.75	.00	11/2019 -	11/2019	-	0/0
1288	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR ,	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	36(O) -	4/4
1289	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR ,	10/2016	235.31 -	235.31	195.72	11/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1290	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]NHIDCL, MANIPUR , EPC	03/2019	471.00 -	471.00	116.31	07/2022 -	07/2022	0(O) -	2/4
1291	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]NHIDCL, MANIPUR , EPC	03/2020	292.24 -	292.24	29.70	06/2022 -	06/2022	0(O) -	1/4
1292	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]NHIDCL, MANIPUR , EPC	06/2020	365.53 -	365.53	32.49	08/2022 -	08/2022	0(O) -	1/4
1293	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]NHIDCL, MANIPUR , EPC	03/2020	167.95 -	167.95	27.29	06/2022 -	06/2022	0(O) -	1/4
1294	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273]NHIDCL, MANIPUR , EPC	07/2020	177.76 -	177.76	23.02	08/2022 -	08/2022	0(O) -	1/4
1295	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274]NHIDCL, MANIPUR , EPC	08/2020	379.39 -	379.39	2.29	04/2022 -	04/2022	0(O) -	0/4
1296	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]NHIDCL, MANIPUR , EPC	08/2020	268.98 -	268.98	.00	04/2022 -	04/2022	0(O) -	0/4
1297	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]NHIDCL, MANIPUR , EPC	08/2020	228.97 -	228.97	.00	04/2022 -	04/2022	0(O) -	0/4
1298	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]NHIDCL, MANIPUR , EPC	03/2020	167.95 -	167.95	40.95	06/2022 -	06/2022	0(O) -	1/4
1299	MARIAM - PEREN PKG-1A - [N24001349]NHIDCL, MANIPUR , EPC	02/2021	226.32 -	226.32	.00	12/2022 -	12/2022	0(O) -	0/0
1300	MARIAM - PEREN (PKG 1B) - [N24001350]NHIDCL, MANIPUR , EPC	02/2021	188.36 -	188.36	.00	12/2022 -	12/2022	0(O) -	0/0
1301	MARIAM - PEREN PKG-2B - [N24001351]NHIDCL, MANIPUR , EPC	02/2021	232.26 -	232.26	.00	12/2022 -	12/2022	0(O) -	0/0
1302	IMPHAL - MOREH PACKAGE- 3 - [N24001352]NHIDCL, MANIPUR , EPC	03/2021	259.31 -	259.31	.00	12/2022 -	12/2022	0(O) -	0/0
1303	IMPHAL - KHONGSANG PKG-2 - [N24001353]NHIDCL, MANIPUR , EPC	03/2021	195.14 -	195.14	.00	12/2022 -	12/2022	0(O) -	0/0
1304	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL, MANIPUR , EPC	03/2021	234.08 -	234.08	.00	12/2022 -	12/2022	0(O) -	0/0
1305	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA ,	12/2015	479.20 -	479.20	712.89	05/2018 -	-	-	0/0
1306	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL, MEGHALAYA ,	04/2017	553.51 -	553.51	127.99	- 09/2021	09/2021	- 0	2/4
1307	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL, MEGHALAYA ,	03/2019	306.28 -	306.28	117.91	05/2019 -	03/2022	34(O) -	2/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1308	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]NHIDCL,MEGHALAYA , EPC	11/2020	351.12 -	351.12	40.99	12/2023 -	12/2023	0(O) -	0/4
1309	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]NHIDCL,MEGHALAYA , EPC	11/2020	525.68 -	525.68	27.54	12/2023 -	12/2023	0(O) -	0/4
1310	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]NHIDCL,MEGHALAYA , EPC	11/2020	445.51 -	445.51	12.93	12/2023 -	12/2023	0(O) -	0/4
1311	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]NHIDCL,MEGHALAYA , EPC	11/2020	284.21 -	284.21	2.63	12/2023 -	12/2023	0(O) -	0/4
1312	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]NHIDCL,MEGHALAYA , EPC	10/2020	157.86 -	157.86	17.63	04/2022 -	04/2022	0(O) -	0/4
1313	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]NHIDCL,MEGHALAYA , EPC	03/2021	260.21 -	260.21	.00	12/2022 -	12/2022	0(O) -	0/0
1314	WIDENING TO 2 LANE RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM , ITEM RATE	11/2010	624.41 -	992.67	890.74	03/2011 12/2021	12/2021	129(O) 0	0/0
1315	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM , ITEM RATE	08/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021	134(O) 0	0/0
1316	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM , ITEM RATE	08/2010	195.04 -	377.99	368.39	10/2010 12/2021	12/2021	134(O) 0	0/0
1317	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM ,	04/2017	519.09 -	519.09	71.38	09/2019 -	04/2023	43(O) -	1/4
1318	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM ,	04/2017	640.07 -	640.07	93.50	09/2019 06/2023	07/2023	46(O) 0	1/4
1319	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM ,	04/2017	642.96 -	642.96	71.41	09/2019 04/2023	06/2023	45(O) 0	1/4
1320	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM ,	04/2017	473.18 -	473.18	108.59	09/2019 04/2023	04/2023	43(O) 0	1/4
1321	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM ,	04/2017	537.82 -	537.82	121.93	09/2019 06/2023	04/2023	43(O) 0	1/4
1322	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM ,	04/2017	518.53 -	518.53	118.95	09/2019 04/2023	06/2023	45(O) 0	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1323	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM ,	04/2017	404.29 -	404.29	33.67	09/2019 03/2024	04/2024	55(O) 0	0/4
1324	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM ,	04/2017	428.11 -	428.11	71.30	09/2019 09/2023	09/2023	48(O) 0	1/4
1325	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM ,	08/2010	186.96 -	322.24	304.71	09/2014 12/2021	12/2021	87(O) 0	0/0
1326	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]NHIDCL,MIZORAM , EPC	09/2020	275.02 -	275.02	22.39	10/2022 -	10/2022	0(O) -	1/4
1327	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]NHIDCL,MIZORAM , EPC	03/2020	206.88 -	206.88	21.58	07/2022 -	07/2022	0(O) -	1/4
1328	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]NHIDCL,MIZORAM , EPC	03/2020	216.49 -	216.49	33.63	07/2022 -	07/2022	0(O) -	1/4
1329	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]NHIDCL,MIZORAM , EPC	03/2020	292.24 -	292.24	37.79	07/2022 -	07/2022	0(O) -	0/4
1330	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]NHIDCL,MIZORAM , EPC	03/2020	281.78 -	281.78	73.31	07/2022 -	07/2022	0(O) -	2/4
1331	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]NHIDCL,MIZORAM , EPC	03/2021	374.39 -	374.39	.00	12/2022 -	12/2022	0(O) -	0/0
1332	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]NHIDCL,MIZORAM , EPC	03/2021	233.25 -	233.25	.00	12/2022 -	12/2022	0(O) -	0/0
1333	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]NHIDCL,MIZORAM , EPC	03/2021	674.71 -	674.71	.00	06/2023 -	06/2023	0(O) -	0/0
1334	TLABUNG - LUNGLEI PKG-A - [N24001358]NHIDCL,MIZORAM , EPC	03/2021	698.44 -	698.44	.00	12/2022 -	12/2022	0(O) -	0/0
1335	TLABUNG - LUNGLEI PKG-B - [N24001359]NHIDCL,MIZORAM , EPC	03/2021	740.58 -	740.58	.00	01/2023 -	01/2023	0(O) -	0/0
1336	GWALIOR-JHANSI NH-75 - [N24000089]NHAI,MULTI STATE , PPP (ANNUITY)	12/2003	604.00 -	364.59	332.18	12/2009 09/2020	09/2020	-	0/0
1337	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE , PPP (BOT)	02/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-	-	2/2
1338	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE , PPP (ANNUITY)	02/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-	-	0/0
1339	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE , PPP (BOT)	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105(O) -	0/0
1340	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE , PPP (BOT)	09/2011	754.00 -	754.00	1,364.18	03/2013 -	-	-	0/0
1341	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE , PPP (BOT)	10/2012	1,928.22 1,928.22	1,928.22	1,876.06	04/2015 01/2021	12/2021	80(O) 6	3/4
1342	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE ,	09/2016	1,244.10 -	1,244.10	1,663.00	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1343	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE ,	03/2018	1,294.47 -	1,296.00	.00	- -	-	-	0/0
1344	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE ,	03/2018	998.70 -	962.00	.00	- -	-	-	0/0
1345	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND ,	03/2016	373.07 -	387.00	325.21	08/2016 -	05/2021	-	3/4
1346	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND ,	03/2016	396.52 -	396.52	298.94	08/2016 -	05/2021	-	3/4
1347	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND ,	03/2016	429.52 -	429.52	238.28	08/2016 -	02/2021	-	3/4
1348	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND ,	02/2017	387.00 -	387.00	309.45	09/2018 -	03/2022	42(O) -	2/4
1349	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND ,	03/2018	500.09 -	500.09	107.72	09/2018 -	11/2022	50(O) -	1/4
1350	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND ,	03/2018	339.57 -	339.57	161.84	09/2018 -	07/2022	46(O) -	2/4
1351	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL,NAGALAND ,	03/2018	239.30 -	239.30	112.70	09/2018 -	05/2022	44(O) -	2/4
1352	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND ,	03/2018	285.68 -	285.68	82.34	09/2018 -	09/2022	48(O) -	0/4
1353	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND ,	03/2018	315.03 -	315.03	101.42	09/2018 -	12/2021	39(O) -	0/4
1354	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND ,	03/2018	240.64 -	240.64	112.90	09/2018 -	12/2021	39(O) -	0/4
1355	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND ,	03/2018	237.72 -	237.72	120.12	09/2018 -	11/2021	38(O) -	1/2
1356	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND ,	03/2018	251.97 -	251.97	146.10	09/2018 -	11/2021	38(O) -	2/2
1357	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND ,	03/2018	282.98 -	282.98	153.26	09/2018 -	11/2021	38(O) -	0/2

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1358	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND ,	03/2018	215.12 -	215.12	107.31	09/2018 -	11/2021	38(O) -	1/4
1359	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND ,	03/2018	215.79 -	215.79	70.57	09/2018 -	12/2021	39(O) -	1/4
1360	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND ,	03/2018	272.89 -	272.89	59.98	09/2018 -	10/2022	49(O) -	0/4
1361	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND ,	03/2018	323.98 -	323.98	50.13	09/2018 -	11/2022	50(O) -	0/4
1362	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND ,	10/2016	167.62 -	167.62	104.39	12/2020 09/2021	09/2021	9(O) 0	0/0
1363	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND ,	10/2016	172.63 -	172.63	129.65	12/2020 09/2021	09/2021	9(O) 0	0/0
1364	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND ,	11/2016	336.25 369.96	369.96	322.13	09/2019 -	-	-	0/0
1365	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND ,	03/2017	217.35 -	217.35	97.62	11/2020 08/2021	08/2021	9(O) 0	0/0
1366	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND ,	03/2019	237.51 -	237.51	75.42	12/2022 -	12/2022	0(O) -	0/0
1367	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]NHIDCL,NAGALAND , EPC	09/2020	277.44 -	277.44	26.41	10/2022 -	10/2022	0(O) -	0/4
1368	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257]NHIDCL,NAGALAND , EPC	08/2020	159.85 -	159.85	2.80	10/2022 -	10/2022	0(O) -	0/4
1369	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES - [N24001258]NHIDCL,NAGALAND , EPC	08/2020	202.36 -	202.36	.00	04/2022 -	04/2022	0(O) -	0/4
1370	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]NHIDCL,NAGALAND , EPC	09/2020	315.63 -	315.63	7.28	04/2022 -	04/2022	0(O) -	0/4
1371	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]NHIDCL,NAGALAND , EPC	09/2020	257.15 -	257.15	40.94	04/2022 -	04/2022	0(O) -	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1372	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]NHIDCL,NAGALAND , EPC	03/2020	320.97 -	320.97	31.88	06/2022 -	06/2022	0(O) -	1/4
1373	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]NHIDCL,NAGALAND , EPC	03/2020	355.79 -	355.79	55.79	06/2022 -	06/2022	0(O) -	1/4
1374	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]NHIDCL,NAGALAND , EPC	03/2020	361.53 -	361.53	23.62	06/2022 -	06/2022	0(O) -	1/4
1375	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]NHIDCL,NAGALAND , EPC	03/2020	330.78 -	330.78	40.40	12/2021 -	12/2021	0(O) -	1/4
1376	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]NHIDCL,NAGALAND , EPC	03/2020	278.95 -	278.95	68.48	06/2022 -	06/2022	0(O) -	2/4
1377	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287]NHIDCL,NAGALAND , EPC	04/2020	330.80 -	330.80	30.14	12/2021 -	12/2021	0(O) -	1/4
1378	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288]NHIDCL,NAGALAND , EPC	08/2020	232.29 -	232.29	4.98	04/2022 -	04/2022	0(O) -	0/4
1379	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA , PPP (BOT)	03/2012	1,410.00 -	1,410.00	11.20	09/2014 -	-	-	0/0
1380	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA , PPP (BOT)	12/2011	1,047.00 -	1,047.00	1,873.47	06/2014 -	-	-	0/0
1381	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA ,	07/2015	1,282.94 -	1,282.94	720.08	-	-	-	0/0
1382	FOUR LANING WITH PS TALEBANI -SMBALPUR - [N24000485]NHAI,ODISHA ,	12/2015	752.28 -	752.28	272.74	-	03/2022	-	0/1
1383	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA , EPC	12/2011	191.08 -	191.08	182.41	08/2015 -	-	-	0/0
1384	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI,ODISHA ,	02/2016	1,069.65 -	1,069.65	836.93	-	-	-	0/0
1385	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA ,	09/2016	2,510.04 -	2,510.04	633.26	08/2019 -	-	-	0/0
1386	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA ,	10/2016	1,008.96 -	1,008.96	1,125.65	-	-	-	0/0
1387	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA ,	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	-	0/0
1388	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA ,	08/2013	171.96 172.00	172.00	100.67	06/2016 -	-	-	0/0
1389	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA ,	03/2017	1,288.07 -	1,420.00	1,021.47	03/2020 -	-	-	0/0
1390	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA , Central Sector Projects	07/2017	476.56 -	476.56	189.84	07/2017 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1391	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA ,	12/2017	686.65 -	686.65	290.00	- -	-	-	0/0
1392	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA ,	12/2017	417.51 -	417.51	213.88	- -	-	-	0/0
1393	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA ,	01/2018	953.09 -	953.09	438.00	- -	03/2022	-	0/0
1394	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA ,	01/2018	668.86 -	668.86	372.00	- -	-	-	0/0
1395	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA ,	01/2018	633.68 -	633.68	118.00	- -	-	-	0/1
1396	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA ,	01/2018	614.48 -	614.48	277.00	- -	08/2021	-	0/0
1397	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA ,	01/2018	564.66 -	564.66	341.88	- -	08/2021	-	0/1
1398	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA ,	01/2018	686.65 -	686.65	254.00	- -	-	-	0/0
1399	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA ,	01/2018	1,522.00 -	1,522.00	512.80	- -	-	-	0/0
1400	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA ,	01/2018	999.00 -	999.00	178.00	- -	-	-	0/0
1401	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA ,	01/2018	503.88 -	503.88	100.21	- -	-	-	0/0
1402	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA , EPC	03/2018	806.11 -	806.11	320.00	- -	-	-	0/0
1403	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MoRTH,ODISHA ,	08/2016	287.70 -	287.70	208.32	02/2017 -	-	-	0/0
1404	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA ,	09/2016	295.67 -	295.67	201.80	02/2017 -	-	-	0/0
1405	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA ,	12/2016	223.50 -	223.50	134.34	08/2018 -	-	-	0/0
1406	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA ,	12/2016	206.88 -	206.88	123.55	04/2018 -	-	-	0/0
1407	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA ,	03/2018	214.23 -	214.23	108.98	08/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1408	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA ,	03/2018	199.16 -	199.16	122.77	08/2018 -	-	-	0/0
1409	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB , EPC	11/2015	889.24 -	904.82	766.98	- -	-	-	0/0
1410	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB ,	09/2014	479.00 -	479.00	456.80	- -	03/2022	-	0/0
1411	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB ,	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	-	0/0
1412	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB ,	08/2016	1,169.61 - 1,367.00	2,280.00	1,367.00	- -	-	-	0/0
1413	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB ,	03/2017	754.54 -	756.27	430.26	03/2020 -	09/2022	30(O) -	0/0
1414	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB ,	02/2018	261.76 -	207.00	201.67	- -	07/2021	-	0/0
1415	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB , EPC	03/2018	199.90 -	199.90	124.52	- -	-	-	0/0
1416	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB , EPC	03/2018	196.05 -	196.05	143.03	- -	-	-	0/0
1417	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB ,	03/2018	293.10 -	293.10	166.39	08/2020 -	-	-	0/0
1418	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB ,	10/2017	1,069.59 -	1,069.59	728.55	10/2019 -	08/2021	22(O) -	0/0
1419	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB ,	03/2018	170.57 -	170.57	65.41	11/2020 -	-	-	0/0
1420	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB ,	03/2018	293.64 -	293.64	259.00	08/2020 -	-	-	0/0
1421	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN ,	09/2014	425.19 -	425.19	276.40	09/2016 -	-	-	0/0
1422	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI,RAJASTHAN ,	10/2015	597.00 -	597.00	.00	10/2017 -	-	-	3/4
1423	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN , PPP (BOT)	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020	-	0/0
1424	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN , PPP (BOT)	08/2014	822.90 -	822.90	844.08	04/2018 -	09/2021	41(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1425	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN , PPP (BOT)	02/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-	-	0/0
1426	TWO LANNING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN ,	08/2015	275.90 -	275.90	289.13	-	-	-	0/0
1427	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAUR - [N24000586]NHAI, RAJASTHAN , PPP (BOT)	06/2016	637.18 -	637.18	550.35	06/2019 -	09/2019	-	0/0
1428	FOUR LANNING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN , PPP (BOT)	06/2016	763.23 -	763.23	191.80	06/2019 -	-	-	1/1
1429	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN ,	06/2016	649.00 -	649.00	646.79	06/2019 -	-	-	0/0
1430	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI, RAJASTHAN ,	07/2016	688.70 -	688.70	870.48	-	-	-	0/0
1431	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A (NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI, RAJASTHAN ,	07/2016	331.46 -	331.46	267.94	10/2018 -	-	-	0/0
1432	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI, RAJASTHAN ,	09/2016	1,239.82 -	1,727.66	1,691.00	-	-	-	4/4
1433	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI, RAJASTHAN ,	09/2016	1,100.19 -	1,145.31	1,355.00	-	-	-	0/0
1434	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI, RAJASTHAN ,	12/2016	1,031.95 -	1,031.95	.00	-	03/2022	-	0/0
1435	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI, RAJASTHAN ,	04/2017	894.00 -	929.32	810.00	04/2020 -	12/2021	20(O)	0/0
1436	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI, RAJASTHAN , Central Sector Projects	10/2017	964.17 -	964.17	904.00	10/2017 -	-	-	0/0
1437	FOUR LANNING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI, RAJASTHAN ,	12/2017	1,308.73 -	1,308.73	330.46	-	-	-	0/0
1438	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN ,	02/2018	1,103.88 -	1,103.88	696.24	-	-	-	0/0
1439	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN ,	02/2018	741.86 -	741.86	225.92	-	-	-	0/0
1440	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI, RAJASTHAN ,	03/2018	874.25 - 866.55	866.55	862.73	- 08/2021	08/2021	- 0	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1441	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN ,	03/2018	1,158.35 -	1,158.35	496.04	- -	-	-	0/0
1442	WIDENING STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN ,	11/2017	187.82 -	187.82	131.74	04/2018 -	-	-	3/4
1443	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN ,	11/2017	163.95 -	163.95	116.47	04/2018 -	07/2020	-	4/4
1444	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN ,	02/2018	370.30 -	370.30	316.21	06/2018 -	-	-	3/4
1445	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN ,	02/2018	341.79 -	341.79	241.14	05/2018 -	-	-	3/4
1446	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN ,	03/2019	178.13 -	178.13	158.26	- -	-	-	4/4
1447	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]MoRTH,RAJASTHAN ,	03/2020	370.36 -	370.36	178.51	08/2022 -	08/2022	0(O) -	0/4
1448	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGAU SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN ,	03/2020	255.23 -	255.23	42.41	08/2020 -	08/2022	24(O) -	0/4
1449	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN ,	08/2020	196.23 -	196.00	28.61	11/2020 -	11/2022	24(O) -	1/4
1450	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM ,	04/2013	151.59 369.92	369.92	343.48	08/2013 06/2021	-	-	0/0
1451	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM , ITEM RATE	04/2013	166.27 359.90	359.90	302.35	08/2013 06/2021	-	-	0/0
1452	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM , ITEM RATE	01/2013	182.28 369.58	369.58	340.16	02/2013 06/2021	-	-	0/0
1453	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM , Central Sector Projects	04/2017	388.00 -	447.37	271.35	10/2017 -	-	-	3/4
1454	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM ,	03/2017	375.80 -	375.80	64.34	- -	-	-	2/4
1455	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM ,	11/2017	290.05 -	290.05	119.27	11/2017 -	12/2021	49(O) -	2/4
1456	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM ,	03/2018	264.84 -	264.84	63.83	06/2018 -	-	-	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1457	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]NHIDCL,SIKKIM , EPC	03/2019	402.94 -	402.94	44.89	04/2022 -	04/2022	0(O) -	1/4
1458	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]NHIDCL,SIKKIM , EPC	08/2020	295.97 -	295.97	19.19	04/2023 -	04/2023	0(O) -	0/4
1459	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]NHIDCL,SIKKIM , EPC	03/2020	242.97 -	242.97	32.98	06/2022 -	06/2022	0(O) -	0/4
1460	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]NHIDCL,SIKKIM , EPC	08/2020	311.00 -	311.00	17.38	04/2023 -	04/2023	0(O) -	0/4
1461	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]NHIDCL,SIKKIM , EPC	07/2020	345.38 -	345.38	74.52	04/2023 -	04/2023	0(O) -	0/4
1462	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]NHIDCL,SIKKIM , EPC	09/2020	183.31 -	183.31	.00	05/2022 -	05/2022	0(O) -	0/4
1463	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]NHIDCL,SIKKIM , EPC	09/2020	262.84 -	262.84	.00	05/2023 -	05/2023	0(O) -	0/4
1464	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]NHIDCL,SIKKIM , EPC	08/2020	292.80 -	292.80	2.53	05/2022 -	05/2022	0(O) -	0/4
1465	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM 27.200 (END OF RO - [N24001336]NHIDCL,SIKKIM , EPC	08/2020	230.45 -	230.45	1.29	04/2023 -	04/2023	0(O) -	0/4
1466	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]NHIDCL,SIKKIM , EPC	10/2020	493.42 -	493.42	.00	11/2023 -	11/2023	0(O) -	0/4
1467	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]NHIDCL,SIKKIM , EPC	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023	0(O) -	0/4
1468	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]NHIDCL,SIKKIM , EPC	01/2021	332.20 -	332.20	.00	09/2023 -	09/2023	0(O) -	0/0
1469	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]NHIDCL,SIKKIM , EPC	12/2020	410.60 -	410.60	.00	02/2024 -	02/2024	0(O) -	0/0
1470	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU , PPP (BOT)	09/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-	-	0/0
1471	DEVELOPMENT OF ADEQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU ,	06/2011	600.00 -	600.00	4.62	06/2013 -	09/2021	99(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1472	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU , PPP (ANNUITY)	05/2010	374.00 -	166.90	69.96	05/2013 -	08/2021	99(O) -	0/0
1473	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU , PPP (ANNUITY)	04/2012	624.00 -	624.00	108.46	04/2014 -	01/2022	93(O) -	0/0
1474	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU , EPC	03/2015	258.97 273.27	268.92	229.77	08/2015 -	-	-	0/4
1475	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU ,	05/2015	1,387.11 -	1,387.11	980.46	11/2017 -	-	-	0/0
1476	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU ,	06/2015	563.92 -	563.92	.00	12/2017 -	-	-	0/0
1477	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU ,	07/2014	401.11 -	401.11	273.89	01/2017 -	-	-	0/0
1478	TRICHY - KARUR - [N24000528]NHAI,TAMIL NADU , PPP (BOT)	03/2007	516.00 -	516.00	886.96	07/2008 -	-	-	0/0
1479	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU ,	02/2016	707.82 -	707.82	428.72	08/2018 -	01/2022	41(O) -	0/0
1480	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU ,	02/2016	641.17 -	641.17	395.10	07/2018 -	12/2021	41(O) -	0/0
1481	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU ,	03/2017	848.45 -	848.45	235.72	03/2020 -	12/2021	21(O) -	0/0
1482	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU , Central Sector Projects	03/2016	641.17 -	641.17	395.10	07/2016 -	12/2021	65(O) -	0/0
1483	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU , Central Sector Projects	08/2017	1,176.37 -	1,176.37	614.68	08/2017 -	07/2022	59(O) -	0/0
1484	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU , Central Sector Projects	09/2017	244.27 -	244.27	178.41	09/2017 -	-	-	0/0
1485	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU , Central Sector Projects	09/2017	1,227.87 -	1,227.87	644.68	09/2017 -	07/2022	58(O) -	0/0
1486	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU ,	12/2017	379.90 -	379.90	231.42	-	03/2021	-	0/0
1487	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU ,	02/2018	1,166.26 -	1,296.93	346.17	-	01/2022	-	0/0
1488	FOUR LANING OF CHETTIKULAM TO NATHAM SECTION OF NH-785 FROM CHETTIKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU , EPC	03/2018	505.35 -	505.35	255.05	-	12/2022	-	0/0
1489	FOUR LANING OF MADURAI- CHETTIKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTIKULAM (7/300) - [N24000827]NHAI,TAMIL NADU , EPC	03/2018	628.71 -	628.71	358.35	-	03/2022	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1490	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU ,	03/2018	633.55 -	482.04	.00	- -	-	-	0/0
1491	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU ,	03/2018	1,016.92 -	1,071.00	299.56	- -	01/2022	-	0/0
1492	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU ,	03/2018	2,065.96 -	2,169.00	.00	- -	-	-	0/0
1493	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU ,	03/2019	297.55 -	297.55	156.11	11/2019 -	-	-	3/4
1494	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU ,	03/2018	240.38 204.73	240.38	107.69	06/2019 -	-	-	3/4
1495	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU , EPC	07/2020	3,426.00 -	3,426.00	.00	12/2021 -	12/2021	0(0) -	0/0
1496	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU , EPC	08/2020	302.62 -	302.62	11.50	02/2021 -	02/2021	-	0/4
1497	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA , PPP (BOT)	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	-	0/0
1498	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA , EPC	01/2014	270.00 -	270.00	.00	03/2016 -	-	-	1/4
1499	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA , EPC	03/2015	153.21 -	153.21	100.95	01/2017 -	-	-	0/0
1500	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA ,	12/2015	1,423.96 -	1,056.08	995.39	11/2018 -	08/2021	33(0) -	0/0
1501	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA ,	03/2017	4,429.00 -	4,429.00	.00	03/2017 -	-	-	0/0
1502	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA ,	03/2018	802.65 -	802.65	436.81	- -	-	-	0/0
1503	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA ,	03/2018	950.63 -	950.63	608.25	- -	-	-	0/0
1504	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA ,	03/2018	857.62 -	857.62	291.66	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1505	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI, TELANGANA ,	03/2018	828.29 -	828.29	.00	- -	-	-	0/0
1506	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH, TELANGANA ,	10/2016	298.32 -	298.32	120.90	02/2019 -	-	-	0/0
1507	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH, TELANGANA ,	10/2016	248.83 -	248.83	124.12	03/2019 -	-	-	0/0
1508	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037 OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH, TELANGANA ,	01/2017	244.54 -	244.54	164.60	05/2019 -	-	-	0/0
1509	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH - [N24000983]MoRTH, TELANGANA ,	01/2017	196.52 -	196.52	115.81	10/2019 -	-	-	0/0
1510	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI - [N24000984]MoRTH, TELANGANA ,	01/2017	283.00 -	283.00	229.21	12/2019 -	-	-	0/0
1511	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA- RAVULAPALLY SECT - [N24000985]MoRTH, TELANGANA ,	01/2017	359.27 -	359.27	299.11	05/2019 -	-	-	0/0
1512	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY- MALLEPALLY SECTION - [N24000986]MoRTH, TELANGANA ,	01/2017	300.00 -	300.00	201.76	05/2019 -	-	-	0/0
1513	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH- SAMSHABAD SECTION) OF HYDERABAD- SAMSHABAD SECTION OF NH - [N24000987]MoRTH, TELANGANA ,	01/2018	283.15 -	283.15	130.89	05/2020 -	-	-	0/0
1514	WIDENING AND STRENGTHENING OF EXISTING 2- LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH, TELANGANA ,	01/2018	230.03 -	230.03	209.06	12/2019 -	-	-	0/0
1515	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH, TELANGANA ,	02/2018	206.13 -	206.13	171.69	06/2020 -	-	-	0/0
1516	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH, TELANGANA ,	02/2018	294.13 -	294.13	141.10	11/2019 -	-	-	0/0
1517	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH, TELANGANA ,	02/2018	220.28 -	220.28	137.20	11/2019 -	-	-	0/0
1518	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH, TELANGANA ,	02/2018	426.52 -	426.52	391.52	04/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1519	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA ,	03/2018	322.81 -	322.81	177.32	09/2020 -	-	-	0/0
1520	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA ,	03/2018	626.76 -	626.76	201.15	07/2020 -	-	-	0/0
1521	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA ,	01/2017	605.08 -	605.08	403.26	10/2019 -	-	-	0/0
1522	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA ,	03/2018	192.67 -	192.67	158.92	07/2019 -	-	-	0/0
1523	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA ,	01/2019	193.19 -	193.19	88.25	- -	-	-	0/0
1524	2 LANING WITH PAVED SHOULDER OF AGARTALA- UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA , EPC	10/2014	369.00 -	369.00	352.63	03/2018 -	-	-	3/4
1525	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA ,	10/2016	171.90 -	171.90	142.81	08/2020 -	10/2021	14(O)	0/0
1526	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]NHIDCL,TRIPURA , EPC	03/2020	247.76 -	247.76	29.13	01/2022 -	01/2022	0(O)	1/4
1527	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]NHIDCL,TRIPURA , EPC	06/2020	347.36 -	347.36	64.89	01/2022 -	01/2022	0(O)	1/4
1528	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT- KAILASHAHAR SECTION - [N24001263]NHIDCL,TRIPURA , EPC	06/2020	277.50 -	277.50	15.01	01/2022 -	01/2022	0(O)	0/4
1529	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]NHIDCL,TRIPURA , EPC	03/2020	154.51 -	154.51	12.08	07/2022 -	07/2022	0(O)	1/4
1530	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]NHIDCL,TRIPURA , EPC	03/2020	178.43 -	178.43	6.87	07/2022 -	07/2022	0(O)	1/4
1531	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA , EPC	01/2017	197.67 -	236.18	21.65	12/2022 -	12/2022	0(O)	0/0
1532	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308]NHIDCL,TRIPURA , EPC	11/2020	332.14 -	332.14	.00	07/2022 -	07/2022	0(O)	0/4
1533	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309]NHIDCL,TRIPURA , EPC	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022	0(O)	0/4
1534	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]NHIDCL,TRIPURA , EPC	11/2020	280.91 -	280.91	59.20	07/2022 -	07/2022	0(O)	1/4
1535	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311]NHIDCL,TRIPURA , EPC	11/2020	206.78 -	206.78	3.42	07/2022 -	07/2022	0(O)	1/4

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1536	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]NHIDCL,TRIPURA , EPC	06/2020	201.99 -	201.99	14.98	01/2022 -	01/2022	0(O) -	0/4
1537	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]NHIDCL,TRIPURA , EPC	09/2020	173.17 -	173.17	.00	04/2022 -	04/2022	0(O) -	0/4
1538	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]NHIDCL,TRIPURA , EPC	06/2020	257.96 -	257.96	95.22	01/2022 -	01/2022	0(O) -	2/4
1539	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]NHIDCL,TRIPURA , EPC	03/2020	165.54 -	165.54	.00	07/2022 -	07/2022	0(O) -	0/4
1540	MANU-SIMLUNG (PKG 4) - [N24001363]NHIDCL,TRIPURA , EPC	03/2021	354.79 -	354.79	.00	12/2022 -	12/2022	0(O) -	0/0
1541	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH , PPP (BOT)	02/2011	1,141.00 -	1,141.00	1,715.00	08/2013 -	-	-	0/0
1542	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH , PPP (BOT)	07/2012	291.36 -	469.31	459.07	01/2014 -	-	-	0/0
1543	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH , PPP (BOT)	03/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-	-	0/0
1544	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MORTH,UTTAR PRADESH , EPC	01/2014	282.41 -	282.41	155.53	03/2016 -	-	-	0/0
1545	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH ,	05/2015	261.09 -	261.09	240.96	05/2017 -	-	-	0/0
1546	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH ,	04/2014	351.34 -	417.68	433.68	01/2016 -	-	-	0/0
1547	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH ,	09/2015	368.73 -	368.73	242.67	09/2016 -	-	-	0/0
1548	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI,UTTAR PRADESH ,	04/2014	495.78 -	627.93	633.24	01/2016 -	-	-	0/0
1549	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH ,	12/2015	611.65 -	611.65	728.24	06/2016 -	-	-	0/0
1550	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH ,	01/2016	815.28 -	815.28	520.89	06/2018 -	-	-	0/0
1551	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH ,	01/2016	1,027.53 -	1,027.53	601.13	06/2018 -	-	-	0/0
1552	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH ,	06/2016	667.00 -	667.00	464.05	07/2018 -	-	-	0/0
1553	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH ,	12/2015	667.00 -	667.00	549.07	06/2018 -	-	-	0/0
1554	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MORTH,UTTAR PRADESH , EPC	05/2013	164.54 -	164.54	128.54	08/2015 -	-	-	0/0
1555	MEERUT-BULANDSHAHR - [N24000539]NHAI,UTTAR PRADESH ,	01/2016	683.24 -	987.94	.00	-	-	-	0/2
1556	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI,UTTAR PRADESH ,	01/2016	1,081.57 -	1,057.60	480.25	06/2019 -	-	-	0/0
1557	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI,UTTAR PRADESH ,	03/2016	676.73 -	676.73	.00	04/2019 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1558	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI,UTTAR PRADESH ,	03/2016	1,404.50 -	1,404.50	2,977.58	- -	-	-	0/0
1559	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH ,	03/2016	1,396.74 -	1,396.74	227.26	- -	-	-	0/0
1560	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH ,	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	-	0/0
1561	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM 204.300 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH ,	03/2016	899.00 -	899.00	450.47	04/2019 -	-	-	0/0
1562	4-LANNING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH ,	03/2016	1,668.00 -	1,668.00	946.08	- -	-	-	0/0
1563	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH ,	03/2016	1,408.00 -	1,408.00	442.70	- -	-	-	0/0
1564	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH ,	03/2016	1,737.00 -	1,737.00	1,159.07	- -	-	-	0/0
1565	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH ,	08/2016	2,016.00 -	2,016.00	1,996.00	04/2019 -	-	-	0/0
1566	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH ,	12/2016	534.55 -	531.00	433.62	- -	-	-	0/0
1567	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH ,	01/2017	450.68 -	450.68	397.62	- -	-	-	0/0
1568	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH ,	03/2017	1,373.28 -	1,373.28	1,285.22	03/2020 12/2021	12/2021	21(O) 0	3/4
1569	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH ,	03/2017	1,184.71 -	1,310.00	1,286.42	03/2020 -	-	-	3/4
1570	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH ,	03/2017	1,989.00 -	1,989.00	521.56	03/2020 -	-	-	0/0
1571	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH ,	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	-	0/0
1572	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH ,	12/2017	1,232.21 -	1,087.00	562.94	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1573	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH ,	12/2017	207.00 -	207.00	.00	- -	-	-	0/0
1574	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH ,	12/2017	305.00 -	305.00	.00	- -	-	-	0/0
1575	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH ,	01/2018	450.77 -	450.77	.00	- -	-	-	0/0
1576	FOR REHABILITATION AND UPGRADE FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH ,	02/2018	670.50 -	670.50	75.10	- -	-	-	0/0
1577	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH ,	03/2018	809.07 -	809.07	751.07	- -	-	-	0/0
1578	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH ,	03/2018	925.40 -	1,197.00	1,176.70	- -	-	-	0/0
1579	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH ,	03/2018	1,117.84 -	1,117.84	.00	- -	12/2021	-	0/0
1580	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH ,	03/2018	2,140.93 -	2,140.93	1,315.69	- -	-	-	0/0
1581	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH ,	03/2018	1,120.57 -	1,332.00	1,441.15	- -	-	-	0/0
1582	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH ,	03/2018	1,025.80 -	677.07	222.94	- -	-	-	0/0
1583	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH ,	03/2018	1,115.28 -	770.04	332.69	- -	-	-	0/0
1584	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD - [N24000806]NHAI,UTTAR PRADESH ,	02/2018	972.77 -	972.77	494.71	- -	-	-	0/0
1585	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH ,	11/2016	326.99 327.00	326.99	122.02	- -	12/2021	-	0/0
1586	REHABILITATION AND UPGRADE OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH ,	11/2016	215.16 215.00	215.16	145.76	09/2019 -	10/2019	-	0/0
1587	REHABILITATION AND UPGRADE OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH ,	03/2016	240.30 240.00	240.30	210.10	01/2020 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1588	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH ,	03/2016	249.50 -	249.50	228.82	05/2019 -	05/2021	-	0/0
1589	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14 - [N24001185]NHAI,UTTAR PRADESH , PPP BOT (Hybrid Annuity)	11/2017	2,159.00 -	2,159.00	1,602.06	01/2019 -	-	-	0/0
1590	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH ,	10/2016	218.90 -	218.90	145.28	03/2020 -	-	-	0/0
1591	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH ,	07/2016	208.88 -	208.88	175.79	10/2019 -	-	-	0/0
1592	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH ,	03/2018	263.89 -	242.05	189.09	04/2020 -	12/2021	20(O) -	0/0
1593	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH ,	03/2018	185.18 -	185.18	124.59	02/2020 -	-	-	0/0
1594	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH ,	03/2018	288.30 -	288.30	160.68	08/2020 -	12/2021	16(O) -	0/0
1595	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH ,	03/2016	296.50 -	296.50	237.08	09/2020 -	08/2021	11(O) -	0/0
1596	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH ,	03/2018	306.59 -	306.59	168.16	-	09/2021	-	0/0
1597	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH ,	11/2018	281.45 -	281.45	.00	-	-	-	0/0
1598	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH , EPC	10/2020	724.60 720.81	724.60	.00	03/2023 -	03/2023	0(O) -	0/0
1599	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND ,	11/2011	478.51 -	478.00	315.11	10/2013 -	-	-	0/0
1600	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND ,	03/2016	720.00 -	720.00	206.32	-	-	-	0/0
1601	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND ,	03/2016	1,443.00 -	1,443.00	1,246.85	-	-	-	0/0
1602	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND ,	11/2012	605.84 -	722.46	722.46	07/2018 -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1603	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND ,	03/2018	274.31 -	274.31	208.47	05/2018 -	03/2022	46(O) -	3/4
1604	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND ,	03/2018	403.36 -	403.36	330.75	06/2018 -	03/2022	45(O) -	3/4
1605	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND ,	03/2018	417.24 -	417.24	325.44	05/2018 -	03/2022	46(O) -	3/4
1606	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND ,	12/2017	257.34 -	257.34	214.90	12/2019 07/2021	07/2021	-	0/0
1607	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND ,	12/2017	200.34 -	200.34	185.44	12/2019 07/2021	07/2021	-	0/0
1608	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND ,	12/2017	248.22 -	248.22	234.12	12/2019 08/2021	08/2021	20(O) 0	0/0
1609	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND ,	06/2017	282.08 -	282.08	201.79	06/2019 12/2021	12/2021	30(O) 0	0/0
1610	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND ,	11/2017	232.81 -	232.81	171.22	11/2019 07/2021	07/2021	-	0/0
1611	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND ,	11/2017	283.51 -	283.51	246.37	11/2019 05/2021	05/2021	-	0/0
1612	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND ,	11/2017	266.52 -	266.52	.00	11/2019 11/2019	11/2019	-	0/0
1613	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND ,	02/2018	418.88 -	418.88	287.56	02/2020 09/2021	09/2021	19(O) 0	0/0
1614	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND ,	02/2018	293.68 -	293.68	179.19	- 10/2021	10/2021	- 0	0/0
1615	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND ,	05/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021	19(O) 0	0/0
1616	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND ,	03/2018	460.73 -	461.00	116.25	- -	-	-	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1617	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL, UTTARAKHAND ,	03/2018	1,383.78 -	1,383.78	387.45	07/2018 -	07/2022	48(O) -	2/5
1618	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH, UTTARAKHAND ,	08/2016	234.88 -	208.89	.00	12/2017 12/2019	12/2019	-	0/0
1619	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI, WEST BENGAL , PPP (BOT)	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	08/2021	96(O) -	3/4
1620	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI, WEST BENGAL , PPP (BOT)	02/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023	118(O) -	3/4
1621	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL , PPP (BOT)	04/2012	1,396.18 -	1,396.18	1,396.18	09/2014 -	-	-	0/0
1622	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL ,	10/2015	361.15 363.93	363.93	277.34	- -	-	-	0/0
1623	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL ,	12/2015	1,083.00 2,587.75	1,827.15	989.55	06/2018 -	-	-	0/0
1624	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL , PPP (BOT)	04/2014	1,665.00 -	2,360.65	4,495.94	- -	-	-	0/0
1625	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK HALDIA - [N24000553]NHAI, WEST BENGAL ,	03/2016	229.37 -	229.37	.00	11/2018 -	-	-	0/0
1626	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI, WEST BENGAL ,	09/2016	767.03 -	767.03	696.60	08/2018 -	-	-	0/0
1627	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL ,	03/2018	1,261.98 2,145.96	1,952.20	97.16	- -	-	-	0/0
1628	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL ,	03/2016	271.17 291.20	291.20	120.14	11/2018 01/2021	03/2022	40(O) 0	0/0
1629	REHABILITATION AND UPGRADE TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH, WEST BENGAL ,	01/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021	25(O) 0	0/0
1630	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH, WEST BENGAL ,	02/2018	426.18 426.18	426.18	254.29	09/2020 01/2022	01/2022	16(O) 0	0/0
1631	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL ,	02/2018	218.70 218.70	218.70	104.19	11/2020 04/2021	06/2021	-	0/0
1632	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE BAGDO - [N24000883]MoRTH, WEST BENGAL ,	03/2018	254.30 254.30	254.30	116.66	10/2020 03/2021	06/2021	-	0/0
1633	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH, WEST BENGAL ,	03/2016	160.27 213.97	213.97	26.72	08/2019 -	11/2022	39(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1634	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH, WEST BENGAL ,	06/2016	236.78 263.26	263.26	72.02	08/2019 08/2022	08/2022	36(O) 0	0/0
1635	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL ,	04/2014	279.70 398.52	398.52	331.86	08/2017 -	02/2020	-	0/0
	Total		5,29,993.60 -	5,46,560.65	3,22,468.99				442/1391
	<u>SHIPPING AND PORTS</u>								
1636	JAL MARG VIKAS PROJECT - [N25000072]IWAI, MULTI STATE ,	01/2018	5,369.18 4,633.81	4,633.81	1,901.76	03/2023 -	03/2023	0(O) -	1/7
	Total		5,369.18 -	4,633.81	1,901.76				1/7
	<u>TELECOMMUNICATIONS</u>								
16367	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE (NICF) AT GHIT - [N28000115]CPWD, DELHI ,	10/2014	248.20 -	248.20	145.26	03/2018 -	12/2021	45(O) -	3/5
1638	NETWORK FOR SPECTRUM - [N26000101]DOT, MULTI STATE ,	03/2012	13,334.00 24,664.00	24,664.00	17,845.00	07/2015 05/2020	03/2022	80(O) 0	0/0
1639	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL, MULTI STATE , Central Sector Projects	03/2020	431.16 422.87	422.87	.00	06/2021 -	11/2021	5(O) -	0/0
	Total		14,013.36 -	25,335.07	17,990.26				3/5
	<u>URBAN DEVELOPMENT</u>								
1640	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAIL, BIHAR ,	02/2019	13,365.77 13,925.50	13,925.50	258.94	06/2024 -	06/2024	0(O) -	0/0
1641	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE VI-5 SHOPS COMMUNI - [N28000149]CPWD, CHHATISGARH ,	05/2019	299.97 299.97	299.97	15.87	09/2020 01/2023	01/2023	28(O) 0	0/0
1642	DELHI MRTS PHASE-III - [N28000056]DMRC, DELHI ,	09/2011	38,585.00 -	38,585.00	39,332.34	03/2016 -	08/2021	65(O) -	1/1
1643	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC, DELHI ,	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	-	3/7
1644	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG NEW DELHI - [N28000087]CPWD, DELHI ,	06/2015	197.33 217.00	217.00	142.78	04/2019 02/2022	02/2022	34(O) 0	1/2
1645	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC, DELHI ,	07/2016	2,694.00 -	2,694.00	817.02	- -	12/2022	-	0/9
1646	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS MINTO ROAD NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD, DELHI ,	11/2017	238.56 238.56	238.56	205.72	05/2020 10/2021	10/2021	17(O) 0	2/2
1647	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD, DELHI ,	10/2016	422.00 422.00	422.00	80.75	03/2021 06/2023	06/2023	27(O) 23	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1648	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI ,	10/2016	392.00 392.00	392.00	141.85	08/2020 06/2022	06/2022	22(O) 0	1/5
1649	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI ,	10/2016	1,180.00 1,100.80	1,100.80	35.70	07/2021 06/2023	06/2023	23(O) 0	0/6
1650	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI ,	10/2016	1,128.00 1,128.00	1,128.00	28.50	03/2022 -	06/2023	15(O) -	0/0
1651	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]DMRC,DELHI ,	07/2019	24,948.65 -	24,948.65	2,269.98	03/2025 -	03/2025	0(O) -	0/1
1652	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI ,	05/2017	565.00 -	565.00	468.78	12/2020 -	08/2021	8(O) -	0/1
1653	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI ,	02/2020	532.00 532.00	532.00	452.00	11/2020 09/2021	09/2021	10(O) 0	4/5
1654	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT ,	11/2014	10,773.00 -	12,787.00	9,144.21	12/2018 -	08/2022	44(O) -	0/1
1655	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]MEGA,GUJARAT ,	03/2019	5,384.17 -	5,384.17	193.79	03/2024 -	03/2024	0(O) -	0/1
1656	SURAT METRO RAIL PROJECT - [N28000138]MEGA,GUJARAT ,	03/2019	12,020.32 -	12,020.32	177.50	03/2024 -	03/2024	0(O) -	0/1
1657	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRC,KARNATAKA ,	02/2014	26,405.14 30,695.12	30,695.12	18,226.61	02/2019 -	03/2025	73(O) -	138/249
1658	KOCHI METRO RAIL PROJECT - [N28000081]KMRC,KERALA ,	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 09/2020	-	-	0/0
1659	BHOPAL METRO RAIL - [N28000124]MPMRC,MADHYA PRADESH ,	11/2018	6,941.40 -	6,941.40	228.95	02/2023 -	02/2023	0(O) -	0/0
1660	INDORE METRO RAIL - [N28000125]MPMRC,MADHYA PRADESH ,	11/2018	7,500.80 -	7,500.80	138.49	02/2023 -	02/2023	0(O) -	0/0
1661	NAGPUR METRO RAIL - [N28000085]NMRC,MAHARASHTRA ,	08/2014	8,680.00 -	8,680.00	8,260.83	03/2018 -	12/2019	-	0/0
1662	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRC,MAHARASHTRA ,	07/2013	23,136.00 -	33,406.00	18,788.65	03/2020 03/2023	03/2023	36(O) 0	0/0
1663	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA ,	12/2016	11,420.00 11,420.00	11,420.00	6,845.77	11/2021 12/2022	12/2022	13(O) 0	0/0
1664	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE ,	03/2019	30,274.00 -	30,274.00	4,567.75	06/2025 -	06/2025	0(O) -	0/0
1665	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU ,	02/2009	14,600.00 18,380.00	18,380.00	17,619.68	12/2015 -	-	-	24/24
1666	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU ,	06/2016	3,770.00 -	3,770.00	2,959.83	03/2018 -	-	-	8/21
1667	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH ,	01/2016	6,928.00 6,928.00	6,928.00	6,928.00	03/2019 -	-	-	0/0
1668	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	11,076.48 -	11,076.48	1,690.78	03/2024 -	03/2025	12(O) -	0/0
1669	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH , Public Private (SPV)	05/2019	8,379.62 -	8,379.62	364.47	03/2024 -	05/2025	14(O) -	0/0
	Total		2,81,283.00 -	3,03,630.26	1,51,127.79				182/336

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>WATER RESOURCES</u>								
1670	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH , National Project	02/2009	10,151.04 55,548.87	55,548.87	17,935.78	03/2020 11/2021	04/2022	25(O) 0	0/19
1671	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR ,	10/2005	956.00 -	721.37	712.37	03/2015 -	-	-	5/7
1672	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR ,	03/2018	230.06 -	230.06	82.04	07/2021 -	07/2021	-	0/0
1673	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR ,	10/2017	254.13 -	413.29	.05	09/2020 -	-	-	0/0
1674	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR ,	11/2018	236.15 -	236.15	58.03	12/2020 06/2021	-	-	0/0
1675	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR ,	03/2018	305.19 -	305.19	24.12	08/2021 -	12/2021	4(O) -	0/0
1676	SEWER NETWORKS SPS AND STP MUNGER - [N30000036]BUIDCO,BIHAR ,	03/2018	294.02 -	294.02	.00	10/2021 -	10/2021	0(O) -	0/0
1677	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR ,	12/2014	225.77 -	398.90	284.90	03/2020 -	03/2021	-	0/0
1678	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR ,	04/2015	268.63 -	268.63	317.85	01/2021 -	-	-	0/0
1679	SEWERAGE SCHEME AT PAHARI ZONE V - PATNA - [N30000040]BUIDCO,BIHAR ,	05/2017	356.37 -	356.37	125.02	04/2021 -	04/2021	-	0/0
1680	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR ,	05/2017	184.86 -	184.86	168.85	05/2021 -	05/2021	-	0/0
1681	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR ,	05/2017	191.62 -	191.62	62.80	11/2020 03/2021	-	-	0/0
1682	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR ,	03/2017	277.42 -	277.42	194.56	05/2021 -	05/2021	-	0/0
1683	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR ,	08/2017	578.89 -	578.89	42.75	06/2022 -	06/2022	0(O) -	0/0
1684	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE PATNA - [N30000051]BUIDCO,BIHAR ,	08/2017	824.00 -	824.00	42.75	06/2022 -	06/2022	0(O) -	0/0
1685	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI ,	03/2017	665.78 -	665.78	211.73	12/2022 -	12/2022	0(O) -	0/0
1686	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI ,	05/2016	211.79 -	211.79	101.28	12/2021 -	12/2022	12(O) -	0/0
1687	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI ,	05/2016	239.11 -	239.11	138.16	02/2022 -	12/2022	10(O) -	0/0
1688	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI ,	12/2018	515.07 -	515.07	336.27	01/2021 -	06/2021	-	0/0
1689	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI ,	05/2017	344.81 -	344.81	.00	05/2020 -	-	-	0/0
1690	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB,MAHARASHTRA ,	03/2017	233.57 -	233.57	148.83	12/2019 -	12/2021	24(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1691	INTERCEPTION DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH ,	05/2017	767.59 -	767.59	112.27	09/2021 -	09/2021	0(O) -	0/0
1692	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH ,	03/2018	904.00 -	904.00	148.55	09/2021 -	09/2021	0(O) -	0/0
1693	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]UPJalNigam,UTTAR PRADESH ,	10/2017	213.62 261.12	261.12	.00	03/2022 -	03/2022	0(O) -	0/0
1694	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH ,	10/2016	370.40 430.49	430.49	396.14	08/2020 03/2021	-	-	0/0
1695	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH ,	03/2018	967.23 -	967.23	51.66	09/2021 -	09/2021	0(O) -	0/0
1696	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH ,	02/2017	161.31 -	161.31	91.38	11/2019 -	03/2021	-	0/0
1697	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH ,	03/2019	271.39 -	271.39	.00	08/2021 -	08/2021	0(O) -	0/0
1698	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH ,	12/2017	460.45 -	460.45	248.16	12/2020 -	05/2021	-	0/0
1699	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH ,	02/2011	279.91 330.05	330.05	244.84	12/2019 -	01/2021	-	0/0
1700	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH ,	01/2019	231.79 -	234.03	.00	12/2021 -	12/2021	0(O) -	0/0
1701	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH ,	01/2019	206.05 -	206.05	53.62	10/2021 -	10/2021	0(O) -	0/0
1702	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH ,	02/2019	681.78 -	690.71	.00	06/2022 -	06/2022	0(O) -	0/0
1703	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH ,	03/2019	298.12 213.91	213.91	.00	07/2021 -	06/2022	11(O) -	0/0
1704	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND ,	03/2017	158.00 -	158.00	84.05	11/2019 03/2021	-	-	0/0
1705	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL ,	01/2019	384.96 -	384.96	.00	04/2022 -	04/2022	0(O) -	0/0
1706	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]KMDA, WEST BENGAL ,	03/2019	287.53 -	287.53	.00	04/2022 -	04/2022	0(O) -	0/0
1707	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL ,	12/2018	234.31 -	234.31	.00	04/2022 -	04/2022	0(O) -	0/0
1708	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL ,	05/2018	198.43 224.69	224.69	.00	02/2022 -	06/2022	4(O) -	0/0

Detail of ongoing Projects Costing Rs 150 Crore and above.						(All Cost/ Expenditure in Rs. Crore)			
						Date of Commissioning		(August 2021)	
Sl.No	Project	Date of Approval	Original / Revised Cost	Anticipated Cost	Cumulative Expenditure Cost	Original / Revised	Anticipated	Delay w.r.t. Original/ Revised (in months)	Miles tones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
1709	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL ,	03/2018	165.16 -	165.16	.00	06/2022 -	06/2022	0(O) -	0/0
1710	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL ,	08/2017	307.12 -	307.12	.00	09/2022 -	09/2022	0(O) -	0/0
1711	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL ,	05/2018	160.00 154.73	154.73	.00	02/2022 -	10/2022	8(O) -	0/0
1712	INTERCEPTION DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL ,	08/2017	185.22 -	185.22	.00	12/2021 -	12/2021	0(O) -	0/0
1713	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL ,	02/2014	274.76 -	274.76	217.98	12/2019 05/2021	-	-	0/0
1714	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL ,	12/2014	272.32 -	272.32	248.86	04/2020 -	03/2021	-	0/0
1715	INTERCEPTION DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL ,	01/2018	172.10 -	172.10	.00	12/2021 -	12/2021	0(O) -	0/0
1716	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL ,	10/2017	164.93 -	164.93	.00	12/2021 -	12/2021	0(O) -	0/0
	Total		26,322.76 -	71,923.93	22,885.65				5/26
	DEFENCE PRODUCTION								
1718	RESIDENTIAL QUARTERS FOR HAL BANGLORE - [N28000103]CPWD, KARNATAKA ,	12/2016	246.31 210.00	210.00	136.16	02/2020 10/2021	12/2021	22(O) 0	7/10
	Total		246.31 -	210.00	136.16				7/10
	COMMERCE								
1718	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI NEW DELHI - [N40000003]NBCC, DELHI ,	06/2018	302.64 302.64	302.64	30.00	10/2020 -	-	-	0/0
	Total		302.64 -	302.64	30.00				0/0
	Grand Total		21,99,181.5 2	26,36,710.5 0	12,52,298.40				2860/5885

FLASH REPORT


Summary of projects in the Flash Report for the month of August, 2021

Project Implementation - Current Status:

Number of Projects in Previous Month	1781
Number of Projects completed/dropped/frozen in Current Month	112
Number of Projects elevated to the status of Major project during the current month	16
Number of Projects Added in Current Month	33
Number of Projects in Current Month	1718

Brief Analysis

Project Status with respect to Original Schedule: Out of 1718 projects, 12 projects are ahead of schedule, 275 projects are on schedule 560 projects are delayed. 772 projects do not have fixed dates of commissioning. 99 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

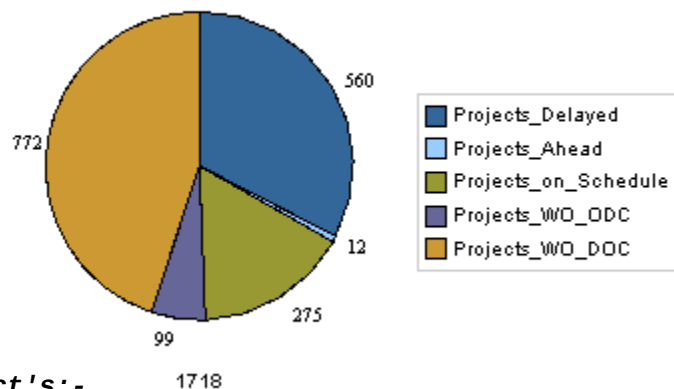


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 1718 projects when sanctioned, was of the order of Rs. 2199181.52 crore but this was subsequently revised to Rs. 2636710.5 crore implying a cost overrun of 19.9%. The expenditure incurred on these projects till August, 2021 is Rs. 1252298.4 crore, which is 47.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

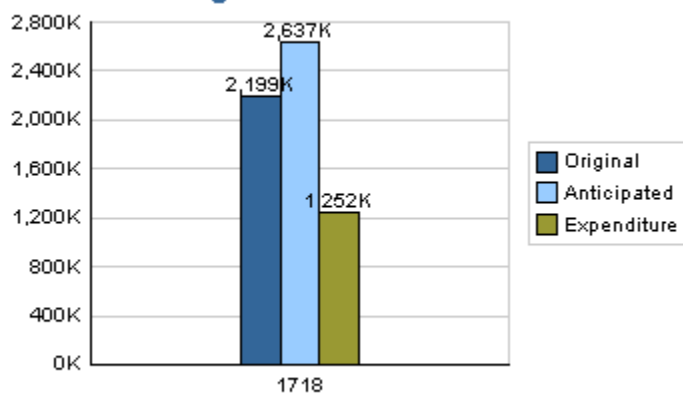

Sector wise current status of projects on the Flash Report


RURAL DEVELOPMENT

Current Status:

Number of Projects	4
Number of Projects Delayed	3
Number of Projects Without Date Of Commissioning	1

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 3 projects are delayed. 1 project does not have fixed dates of commissioning.

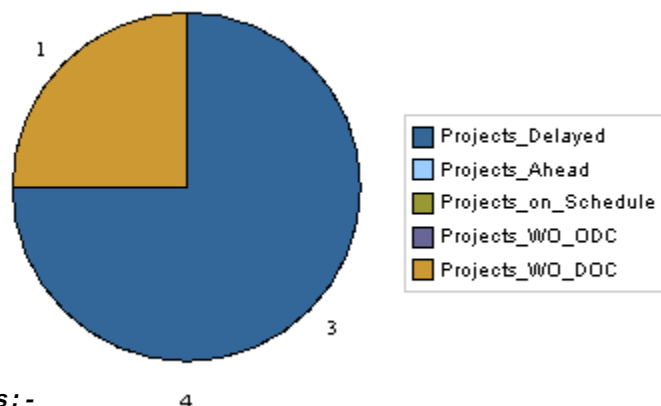


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 889.43 crore but this was subsequently anticipated to Rs. 899.87 crore implying a cost overrun of 1.2%. The expenditure incurred on these projects till August, 2021 is Rs. 472.48 crore, which is 52.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

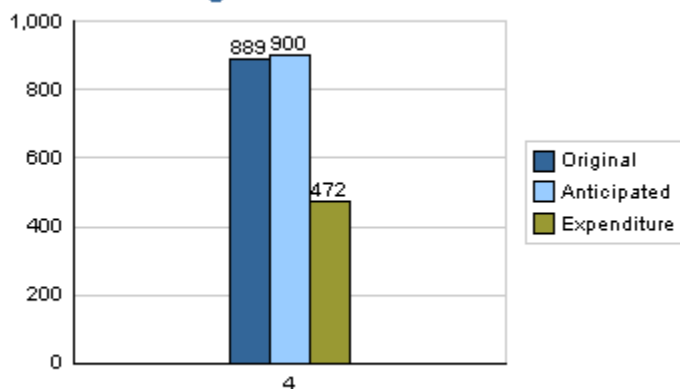

Sector wise current status of projects on the Flash Report

HOME AFFAIRS


Current Status:

Number of Projects	7
Number of Projects On Schedule	2
Number of Projects Delayed	4

Number of Projects Without Date Of Commissioning	1
--	---

Brief Analysis

Project Status with respect to Original Schedule: Out of 7 projects, 2 projects are on schedule 4 projects are delayed. 1 project does not have fixed dates of commissioning.

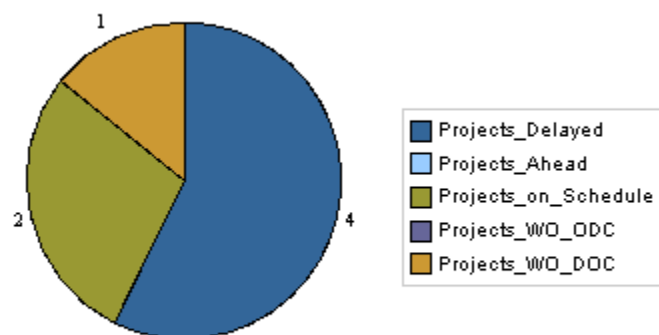


Total No Of Project's:-

7

Investment Scenario

Total original cost of implementation of 7 projects when sanctioned, was of the order of Rs. 2306.97 crore but this was subsequently anticipated to Rs. 3327.6 crore implying a cost overrun of 44.2%. The expenditure incurred on these projects till August, 2021 is Rs. 1183.8 crore, which is 35.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

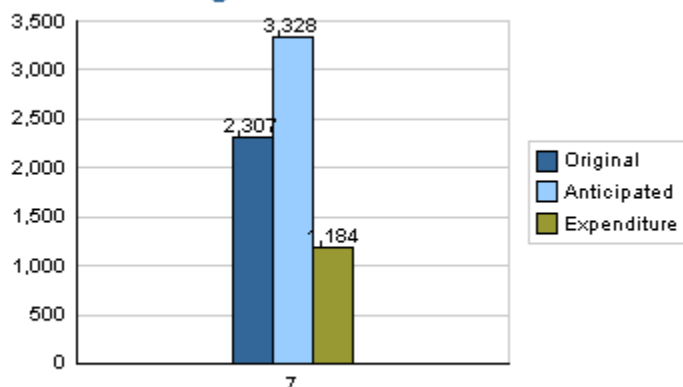

Sector wise current status of projects on the Flash Report

DEPARTMENT OF HIGHER EDUCATION


Current Status:

Number of Projects	26
Number of Projects On Schedule	5
Number of Projects Delayed	8

Number of Projects Without Date Of Commissioning 13

Brief Analysis

Project Status with respect to Original Schedule: Out of 26 projects, 5 projects are on schedule 8 projects are delayed. 13 projects do not have fixed dates of commissioning.

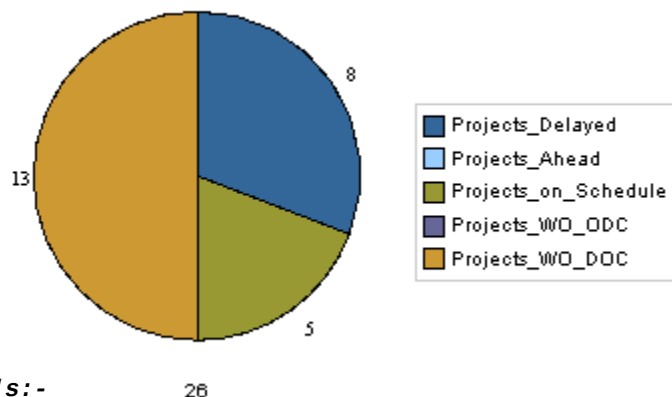


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 26 projects when sanctioned, was of the order of Rs. 10910.66 crore but this was subsequently anticipated to Rs. 11104.02 crore implying a cost overrun of 1.8%. The expenditure incurred on these projects till August, 2021 is Rs. 2426.77 crore, which is 21.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

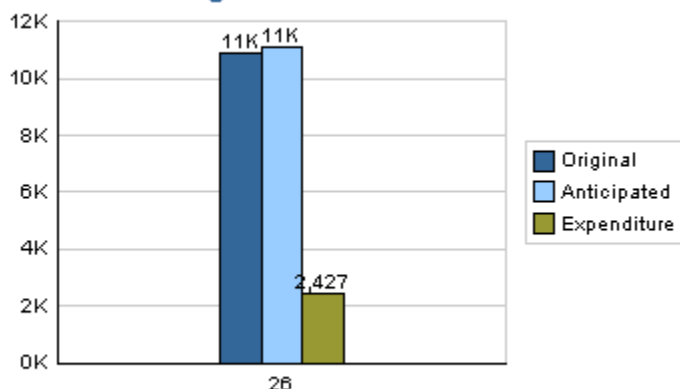

Sector wise current status of projects on the Flash Report

WATER RESOURCES


Current Status:

Number of Projects	47
Number of Projects On Schedule	20
Number of Projects Delayed	8

Number of Projects Without Date Of Commissioning 19

Brief Analysis

Project Status with respect to Original Schedule: Out of 47 projects, 20 projects are on schedule 8 projects are delayed. 19 projects do not have fixed dates of commissioning.

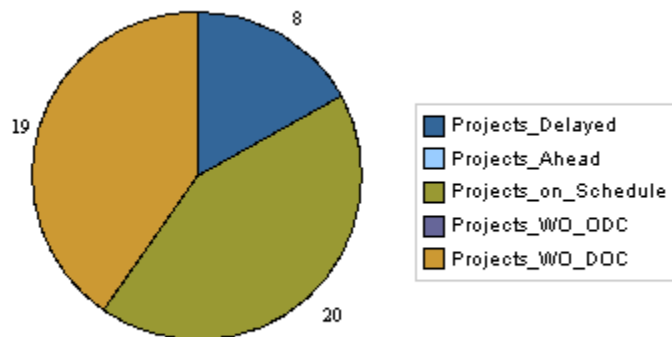


Total No Of Project's:-

47

Investment Scenario

Total original cost of implementation of 47 projects when sanctioned, was of the order of Rs. 26322.76 crore but this was subsequently anticipated to Rs. 71923.93 crore implying a cost overrun of 173.2%. The expenditure incurred on these projects till August, 2021 is Rs. 22885.65 crore, which is 31.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

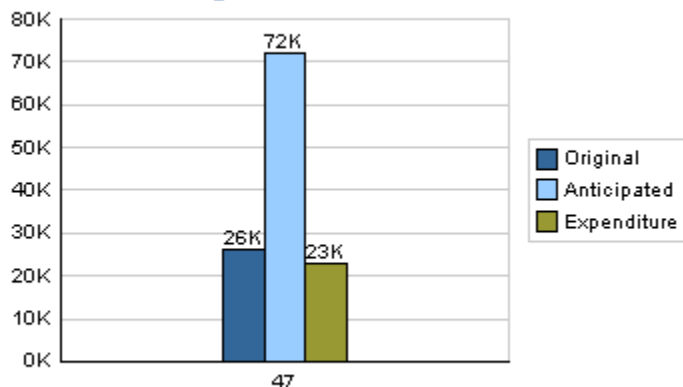

Sector wise current status of projects on the Flash Report


URBAN DEVELOPMENT

Current Status:

Number of Projects	30
Number of Projects On Schedule	7
Number of Projects Delayed	16
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 30 projects, 7 projects are on schedule 16 projects are delayed. 6 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

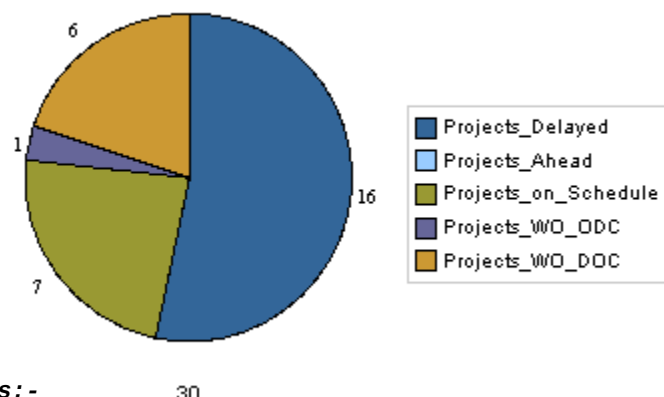


Total No Of Project's:-

30

Investment Scenario

Total original cost of implementation of 30 projects when sanctioned, was of the order of Rs. 281283 crore but this was subsequently anticipated to Rs. 303630.26 crore implying a cost overrun of 7.9%. The expenditure incurred on these projects till August, 2021 is Rs. 151127.79 crore, which is 49.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

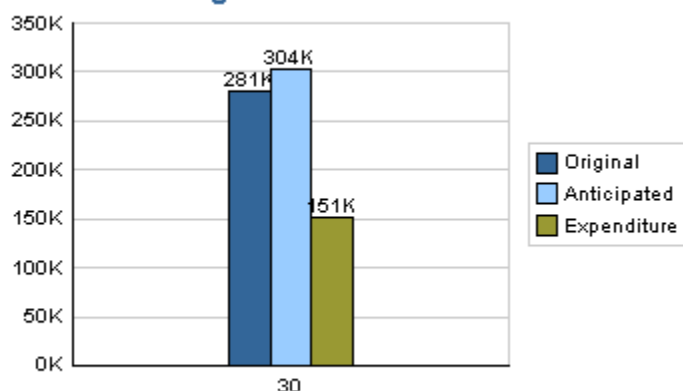


Sector wise current status of projects on the Flash Report

TELECOMMUNICATIONS

Current Status:Number of Projects **3**Number of Projects Delayed **3****Brief Analysis**

Project Status with respect to Original Schedule: Out of 3 projects, 3 projects are delayed.

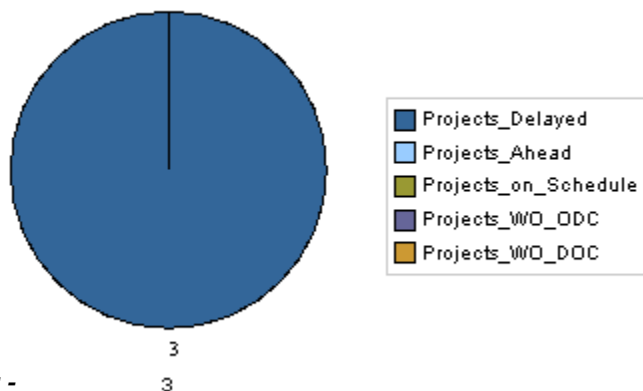


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 3 projects when sanctioned, was of the order of Rs. 14013.36 crore but this was subsequently anticipated to Rs. 25335.07 crore implying a cost overrun of 80.8%. The expenditure incurred on these projects till August, 2021 is Rs. 17990.26 crore, which is 71% of the anticipated cost of the projects.

Figures are in Rs. Crore

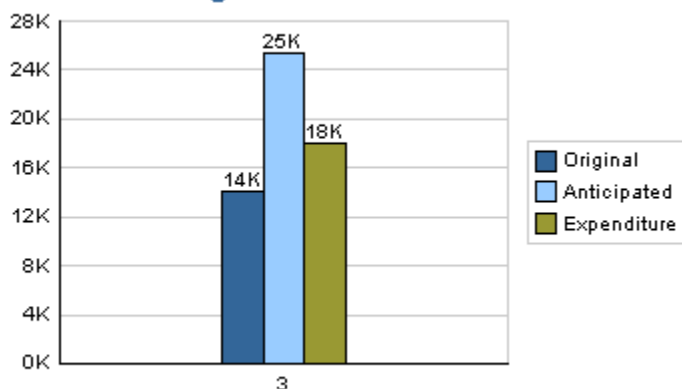

Sector wise current status of projects on the Flash Report

ROAD TRANSPORT AND HIGHWAYS


Current Status:

Number of Projects	878
Number of Projects On Schedule	117
Number of Projects Delayed	148

Number of Projects Without Original Date of Commissioning	44
Number of Projects Without Date Of Commissioning	569

Brief Analysis

Project Status with respect to Original Schedule: Out of 878 projects, 117 projects are on schedule 148 projects are delayed. 569 projects do not have fixed dates of commissioning. 44 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

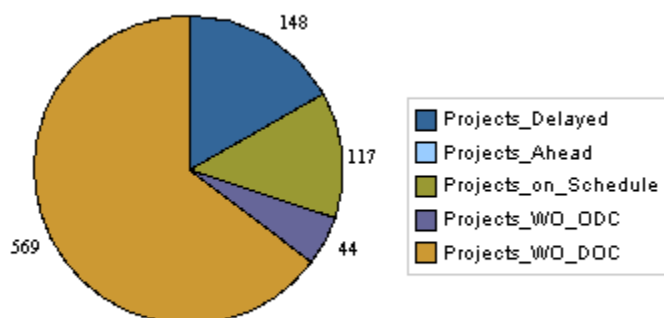


Total No Of Project's:-

878

Investment Scenario

Total original cost of implementation of 878 projects when sanctioned, was of the order of Rs. 529993.6 crore but this was subsequently anticipated to Rs. 546560.65 crore implying a cost overrun of 3.1%. The expenditure incurred on these projects till August, 2021 is Rs. 322468.99 crore, which is 59% of the anticipated cost of the projects.

Figures are in Rs. Crore

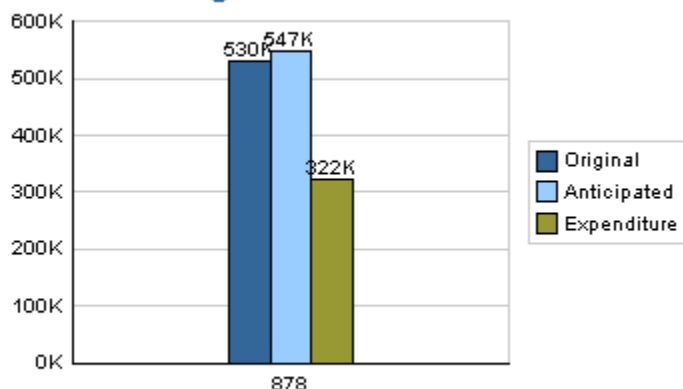

Sector wise current status of projects on the Flash Report


RAILWAYS

Current Status:

Number of Projects	312
Number of Projects On Schedule	13
Number of Projects Delayed	145
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	46
Number of Projects Without Date Of Commissioning	103

Brief Analysis

Project Status with respect to Original Schedule: Out of 312 projects, 5 projects are ahead of schedule, 13 projects are on schedule 145 projects are delayed. 103 projects do not have fixed dates of commissioning. 46 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

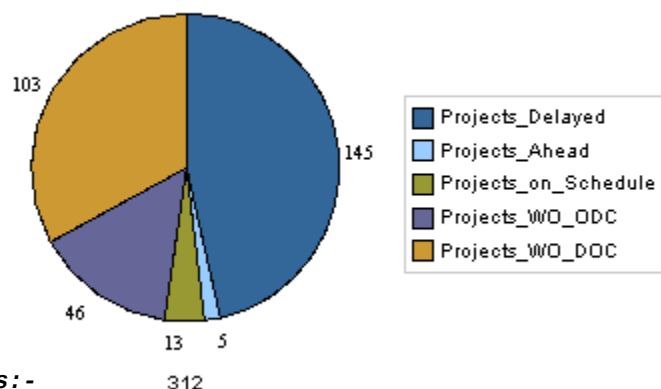


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 312 projects when sanctioned, was of the order of Rs. 462095.03 crore but this was subsequently anticipated to Rs. 704966.85 crore implying a cost overrun of 52.6%. The expenditure incurred on these projects till August, 2021 is Rs. 254962.86 crore, which is 36.2% of the anticipated cost of the projects.

Figures are in Rs. Crore

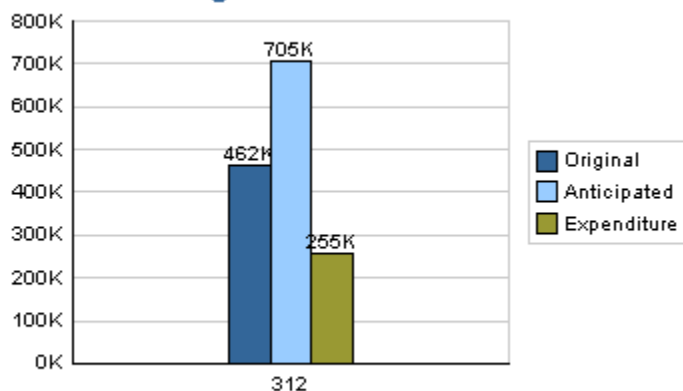

Sector wise current status of projects on the Flash Report


HEALTH AND FAMILY WELFARE

Current Status:

Number of Projects	29
Number of Projects On Schedule	2
Number of Projects Delayed	10
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	4
Number of Projects Without Date Of Commissioning	12

Brief Analysis

Project Status with respect to Original Schedule: Out of 29 projects, 1 project is ahead of schedule, 2 projects are on schedule 10 projects are delayed. 12 projects do not have fixed dates of commissioning. 4 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

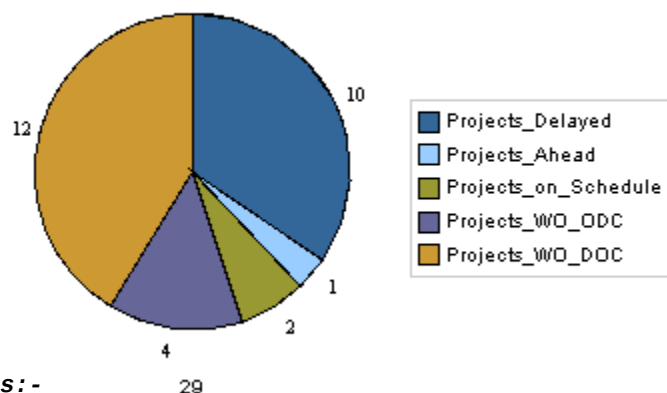


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 29 projects when sanctioned, was of the order of Rs. 15273.26 crore but this was subsequently anticipated to Rs. 15784.86 crore implying a cost overrun of 3.3%. The expenditure incurred on these projects till August, 2021 is Rs. 8502.12 crore, which is 53.9% of the anticipated cost of the projects.

Figures are in Rs. Crore

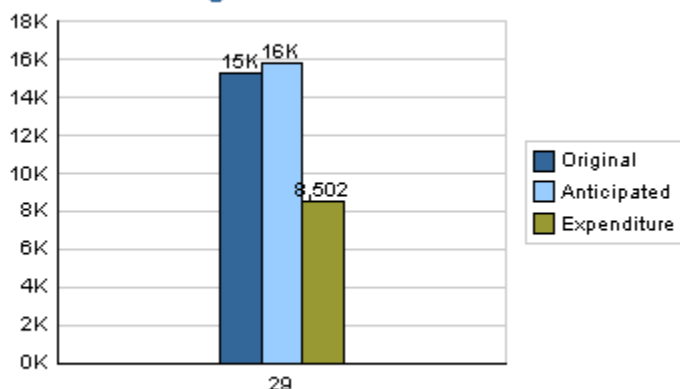

Sector wise current status of projects on the Flash Report


POWER

Current Status:

Number of Projects	76
Number of Projects On Schedule	8
Number of Projects Delayed	42
Number of Projects Ahead	1
Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	24

Brief Analysis

Project Status with respect to Original Schedule: Out of 76 projects, 1 project is ahead of schedule, 8 projects are on schedule 42 projects are delayed. 24 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

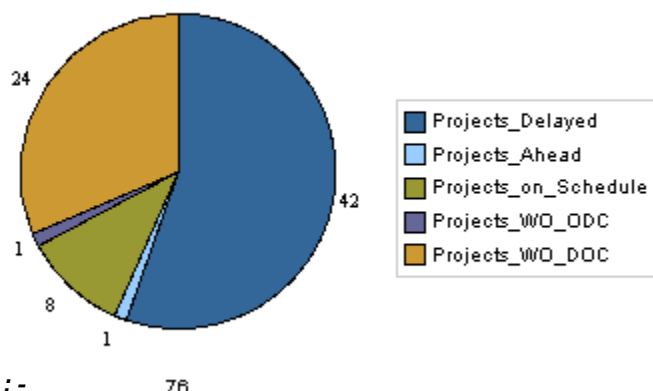


Total No Of Project's:-

76

Investment Scenario

Total original cost of implementation of 76 projects when sanctioned, was of the order of Rs. 229308.93 crore but this was subsequently anticipated to Rs. 291506.86 crore implying a cost overrun of 27.1%. The expenditure incurred on these projects till August, 2021 is Rs. 188096.1 crore, which is 64.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

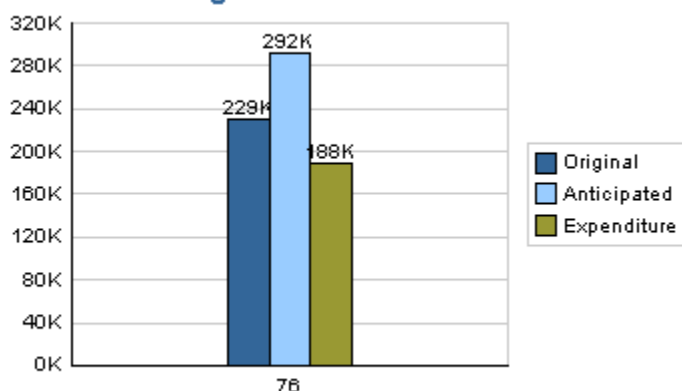

Sector wise current status of projects on the Flash Report


PETROLEUM

Current Status:

Number of Projects	148
Number of Projects On Schedule	55
Number of Projects Delayed	81
Number of Projects Ahead	5
Number of Projects Without Original Date of Commissioning	2
Number of Projects Without Date Of Commissioning	5

Brief Analysis

Project Status with respect to Original Schedule: Out of 148 projects, 5 projects are ahead of schedule, 55 projects are on schedule 81 projects are delayed. 5 projects do not have fixed dates of commissioning. 2 projects were sanctioned without any commissioning date but subsequently dates of completion were finalised.

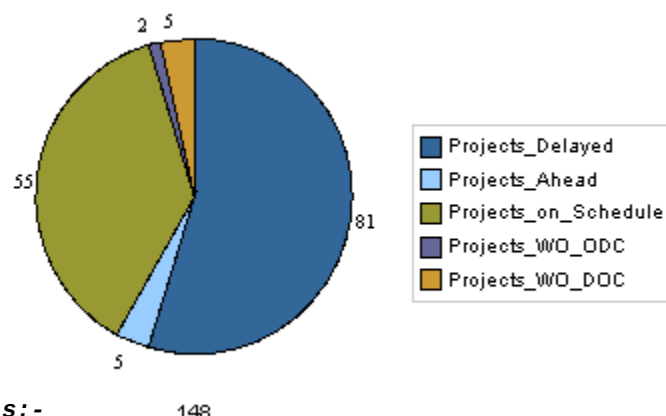


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 148 projects when sanctioned, was of the order of Rs. 336760.67 crore but this was subsequently anticipated to Rs. 343338.97 crore implying a cost overrun of 2%. The expenditure incurred on these projects till August, 2021 is Rs. 118737.04 crore, which is 34.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

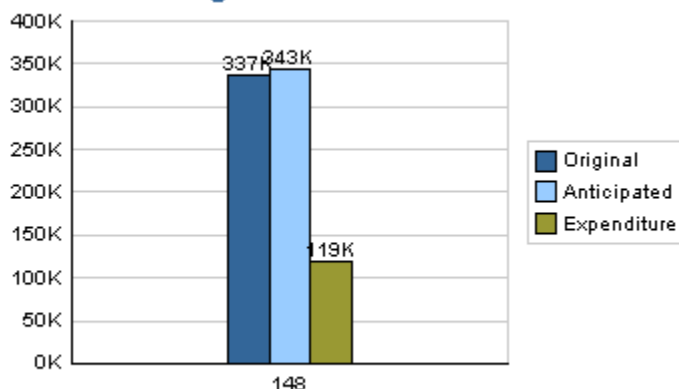

Sector wise current status of projects on the Flash Report


STEEL

Current Status:

Number of Projects	9
Number of Projects On Schedule	3
Number of Projects Delayed	6

Brief Analysis

Project Status with respect to Original Schedule: Out of 9 projects, 3 projects are on schedule 6 projects are delayed.

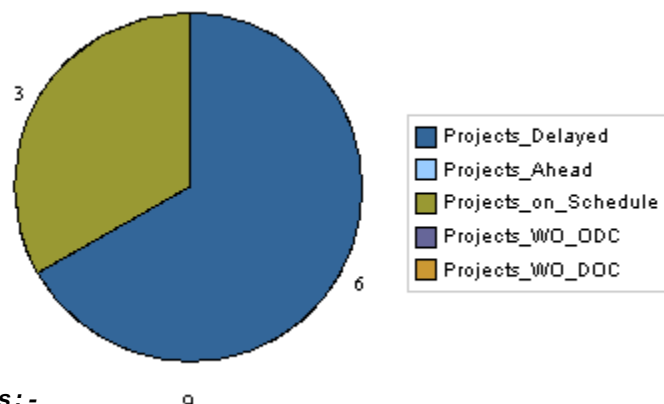


Total No Of Project's:-

9

Investment Scenario

Total original cost of implementation of 9 projects when sanctioned, was of the order of Rs. 25452.51 crore but this was subsequently anticipated to Rs. 32284.66 crore implying a cost overrun of 26.8%. The expenditure incurred on these projects till August, 2021 is Rs. 23985.05 crore, which is 74.3% of the anticipated cost of the projects.

Figures are in Rs. Crore

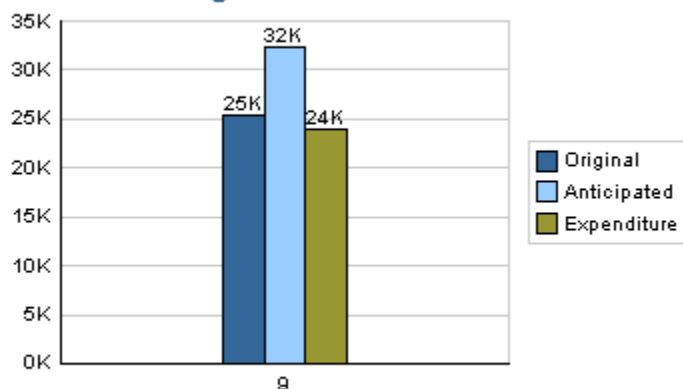

Sector wise current status of projects on the Flash Report


MINES

Current Status:

Number of Projects	5
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	3

Brief Analysis

Project Status with respect to Original Schedule: Out of 5 projects, 2 projects are delayed. 3 projects do not have fixed dates of commissioning.

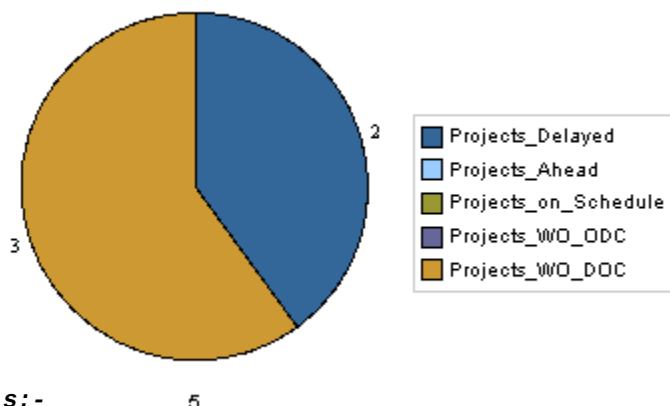


Total No Of Project's:-

5

Investment Scenario

Total original cost of implementation of 5 projects when sanctioned, was of the order of Rs. 7078.62 crore but this was subsequently anticipated to Rs. 7075.17 crore. The expenditure incurred on these projects till August, 2021 is Rs. 1371.05 crore, which is 19.4% of the anticipated cost of the projects.

Figures are in Rs. Crore

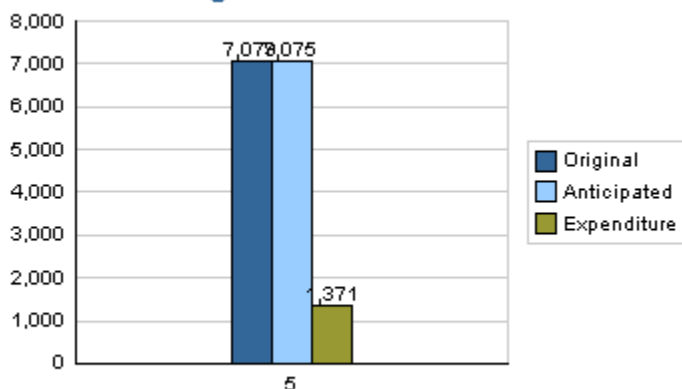

Sector wise current status of projects on the Flash Report


FERTILISERS

Current Status:

Number of Projects	4
Number of Projects Delayed	2
Number of Projects Without Date Of Commissioning	2

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 2 projects are delayed. 2 projects do not have fixed dates of commissioning.

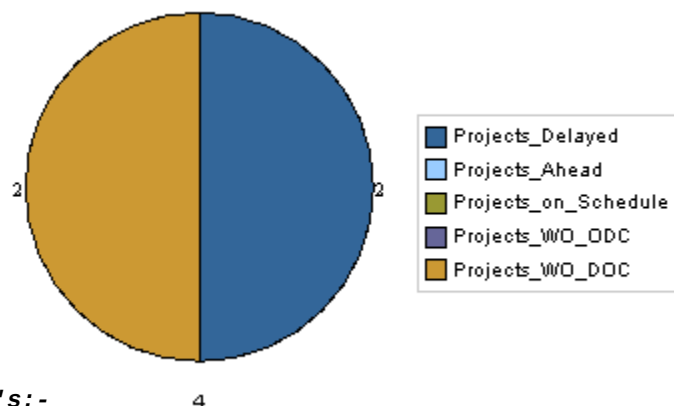


Total No Of Project's:-

4

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 1101.28 crore but this was subsequently anticipated to Rs. 1101.28 crore. The expenditure incurred on these projects till August, 2021 is Rs. 865.59 crore, which is 78.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

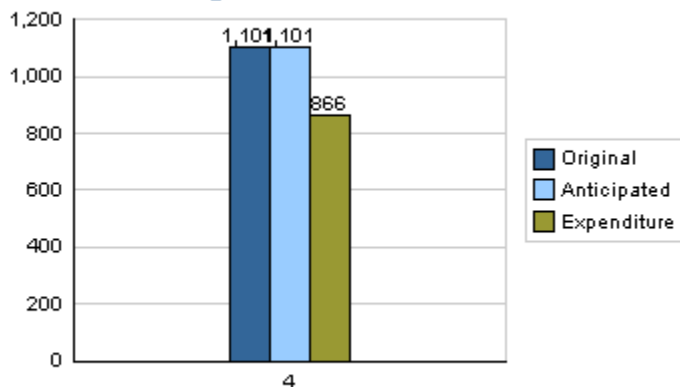

Sector wise current status of projects on the Flash Report

COAL


Current Status:

Number of Projects	108
Number of Projects On Schedule	39
Number of Projects Delayed	59

Number of Projects Without Original Date of Commissioning	1
Number of Projects Without Date Of Commissioning	9

Brief Analysis

Project Status with respect to Original Schedule: Out of 108 projects, 39 projects are on schedule 59 projects are delayed. 9 projects do not have fixed dates of commissioning. 1 project was sanctioned without any commissioning date but subsequently dates of completion was finalised.

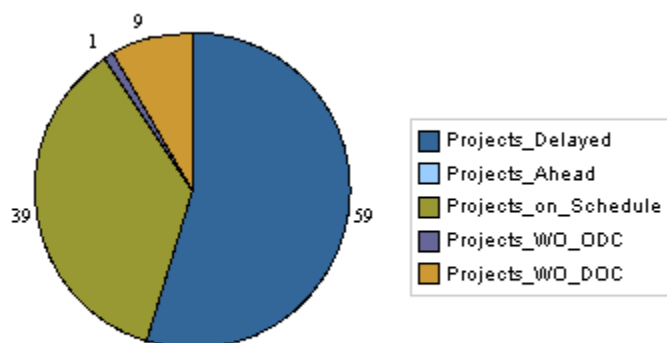


Total No Of Project's:-

108

Investment Scenario

Total original cost of implementation of 108 projects when sanctioned, was of the order of Rs. 148672.06 crore but this was subsequently anticipated to Rs. 154186.72 crore implying a cost overrun of 3.7%. The expenditure incurred on these projects till August, 2021 is Rs. 52127.02 crore, which is 33.8% of the anticipated cost of the projects.

Figures are in Rs. Crore

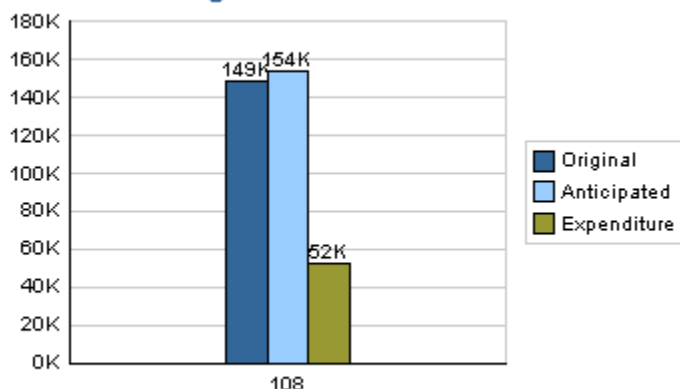

Sector wise current status of projects on the Flash Report


CIVIL AVIATION

Current Status:

Number of Projects	18
Number of Projects On Schedule	2
Number of Projects Delayed	16

Brief Analysis

Project Status with respect to Original Schedule: Out of 18 projects, 2 projects are on schedule 16 projects are delayed.

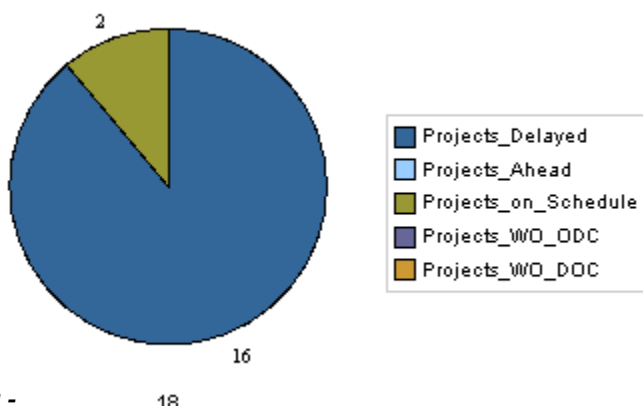


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 18 projects when sanctioned, was of the order of Rs. 13348.06 crore but this was subsequently anticipated to Rs. 13862.62 crore implying a cost overrun of 3.9%. The expenditure incurred on these projects till August, 2021 is Rs. 4502.25 crore, which is 32.5% of the anticipated cost of the projects.

Figures are in Rs. Crore

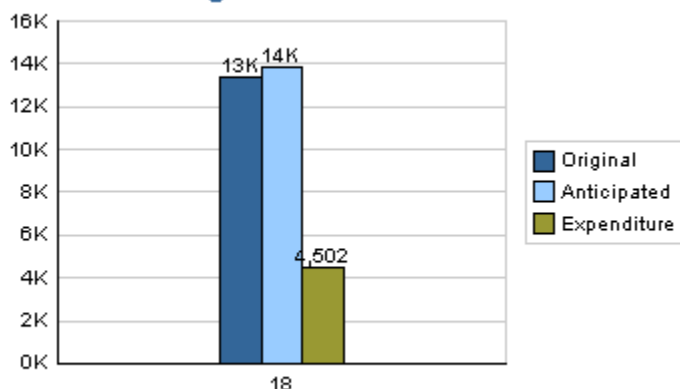

Sector wise current status of projects on the Flash Report


ATOMIC ENERGY

Current Status:

Number of Projects	4
Number of Projects Delayed	4

Brief Analysis

Project Status with respect to Original Schedule: Out of 4 projects, 4 projects are delayed.

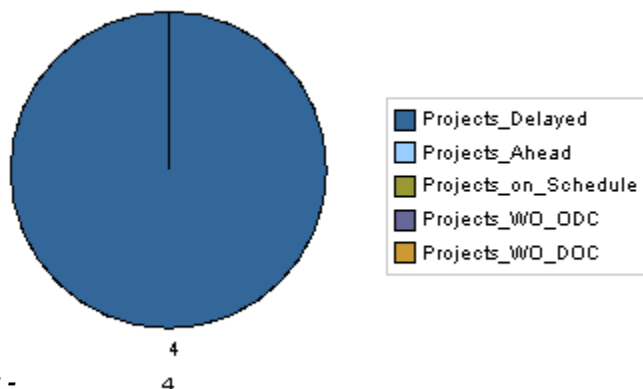


Total No Of Project's:-

Investment Scenario

Total original cost of implementation of 4 projects when sanctioned, was of the order of Rs. 67120 crore but this was subsequently anticipated to Rs. 80348 crore implying a cost overrun of 19.7%. The expenditure incurred on these projects till August, 2021 is Rs. 61584.57 crore, which is 76.6% of the anticipated cost of the projects.

Figures are in Rs. Crore

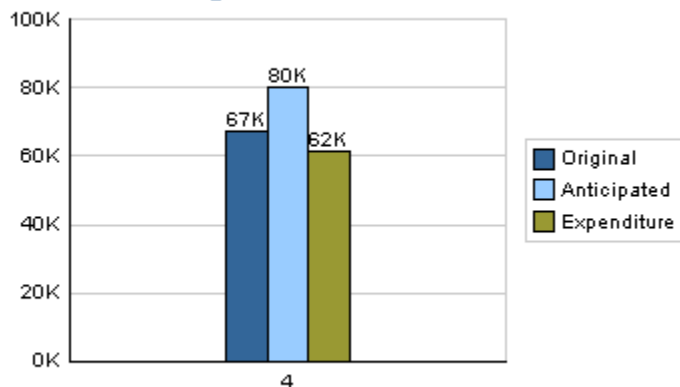

ANNEXURE

Annexure - I

STATUS OF CENTRAL SECTOR PROJECTS COSTING Rs.150 CRORE AND ABOVE (AUGUST 2021)

(All Cost /Expenditure in Rs. crore)

S.NO	STATE	NO OF PROJECTS	COST ORIGINAL	COST ANTICIPATED	CUMULATIVE EXPENDITURE
1	A & N ISLANDS	9	2,888.63	3,159.99	1,381.49
2	ANDHRA PRADESH	74	1,24,241.29	1,72,051.82	77,506.76
3	ARUNACHAL PRADESH	41	22,951	37,016.2	19,112.02
4	ASSAM	53	49,175.61	53,790.59	14,834.01
5	BIHAR	103	1,24,613.06	1,61,188.44	77,730.19
6	CHHATISGARH	46	78,872.08	89,155.66	43,453.18
7	DELHI	33	89,350.41	90,970.21	56,540.89
8	GOA	10	5,332.77	5,343.26	2,710.43
9	GUJARAT	61	1,07,586.79	1,18,636.4	57,936.93
10	HARYANA	39	62,518.91	64,850.78	19,313.7
11	HIMACHAL PRADESH	19	21,918.19	31,802.62	19,250.33
12	JAMMU AND KASHMIR	26	45,784.09	71,711.34	46,669.72
13	JHARKHAND	41	68,724.52	73,429.78	33,239.11
14	KARNATAKA	56	70,450.03	82,675.13	45,579.87
15	KERALA	23	34,828.89	39,970.99	15,968.24
16	LADAKH	8	2,633.23	2,767.29	158.26
17	MADHYA PRADESH	76	67,158.93	76,531.18	31,589.85
18	MAHARASHTRA	239	2,03,714.25	2,25,925.96	1,23,226.32
19	MANIPUR	19	9,640.91	18,089.68	12,359.62
20	MEGHALAYA	13	5,269.68	8,588.18	1,720.61
21	MIZORAM	23	11,751.4	15,700.1	6,935.51
22	MULTI STATE	130	3,68,262.98	4,84,139.25	2,01,623.03
23	NAGALAND	36	16,462.29	21,094.41	4,920.3
24	ODISHA	80	1,15,673.21	1,20,106.58	46,038.46
25	PONDICHERRY	1	195	195	16.41
26	PUNJAB	21	11,288.85	12,858.74	7,118.93
27	RAJASTHAN	54	51,369.15	59,216.94	37,524.08
28	SIKKIM	21	7,778.98	15,698.13	3,355.78
29	TAMIL NADU	70	1,23,008.14	1,42,839.68	85,267.73
30	TELANGANA	49	37,249.74	40,283.18	20,996.36
31	TRIPURA	21	5,174	5,395.32	1,485.93
32	UTTAR PRADESH	119	1,53,485.51	1,57,906.11	75,052.06
33	UTTARAKHAND	32	35,922.92	50,877.81	20,726.78
34	WEST BENGAL	72	63,906.08	82,743.75	40,955.51
TOTAL		1,718	21,99,181.52	26,36,710.5	12,52,298.4

List of Projects in which Expenditure is More than Approved Cost

Annexure - II

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	17,041.00	12/2015 -	02/2022
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,528.00	12/2016 -	03/2023
	Total		23,779.00 -	33,659.00	30,569.00		
	<u>COAL</u>						
	<u>Mahanadi Coal Fields Limited</u>						
3	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	703.39	703.39	03/2013 -	03/2024
	<u>Singareni Colliers Company Limited</u>						
4	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	7/2011	162.76 -	349.28	283.01	03/2015 -	03/2022
	Total		642.29 -	1,052.67	986.40		
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Hospital Services Consultancy Corporation Ltd</u>						
5	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	2/2013	414.11 -	655.58	561.94	11/2013 -	09/2021
6	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021
7	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019
8	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	9/2014	505.58 -	585.00	586.96	03/2018 -	09/2019
9	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	7/2016	152.95 -	177.92	164.17	02/2018 -	03/2021
10	AIIMS - OPD(NEW) - [N21000009]	8/2014	293.65 -	325.00	299.76	05/2017 -	01/2020
	Total		1,739.63 -	2,184.70	2,031.58		
	<u>PETROLEUM</u>						
	<u>Indian Oil Corporation Limited</u>						
11	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	6/2016	423.00 -	502.00	440.03	08/2019 06/2021	05/2021
	<u>Oil & Natural Gas Corporation Limited</u>						
12	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]	5/2019	763.92 -	733.86	791.46	12/2020 12/2021	12/2021

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		1,186.92 -	1,235.86	1,231.49		
	<u>POWER</u>						
	<u>Power Grid Corporation Of India Limited</u>						
13	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-
	<u>Satluj Jal Vidyut Nigam Limited</u>						
14	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	657.62	12/2021 06/2022	06/2022
	Total		1,135.82 -	1,587.35	1,247.92		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
15	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	4/2011	184.06 -	325.00	324.93	03/2019 -	-
16	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	2/1997	2,271.50 -	4,794.60	2,831.83	03/2021 -	03/2023
	<u>Container Corporation Of India</u>						
17	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	1/2013	387.70 -	487.13	434.63	03/2018 -	-
	<u>East Central Railways</u>						
18	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	3/1999	1,033.07 -	3,620.00	3,614.37	- 03/2022	03/2022
19	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240]	4/1997	324.73 -	1,070.00	1,076.60	03/2012 11/2022	11/2022
20	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	4/1991	329.39 -	1,483.14	1,219.42	- 03/2022	03/2022
21	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]	4/1998	180.82 -	726.31	546.29	- 08/2020	08/2020
22	GARHWA ROAD-RAMNA - [N22000465]	3/2015	348.23 -	390.00	366.22	03/2021 -	03/2022
23	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	1/1991	332.15 -	546.71	547.77	07/2014 -	-
24	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	4/2013	213.01 -	495.00	497.30	- 10/2019	10/2019
25	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	4/2006	378.56 -	1,858.75	386.36	- -	03/2023
26	HAJIPUR - BACHAWARA - [N22000334]	5/2015	678.54 -	929.86	863.90	03/2019 12/2021	12/2021
	<u>East Coast Railway</u>						
27	SAMBALPUR-TALCHER DOUBLING - [N22000315]	3/2011	1,111.99 -	1,539.28	1,186.14	02/2019 -	12/2021
	<u>Eastern Railways</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
28	DEOGHAR - SULTANGANJ (INL), ER - [220100273	4/2000	607.09 -	1,425.44	638.19	02/2013 -	03/2024
29	HANSDIHA-GODDA NL - [N22000236	4/2011	542.18 -	663.13	544.63	03/2020 -	03/2021
30	MONIGRAM- NIMTITA - [N22000301	4/2012	250.93 -	310.70	377.47	- -	03/2024
31	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	4/2011	175.80 -	495.10	299.53	- -	03/2022
32	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	4/2010	365.17 -	439.30	454.56	03/2017 -	03/2025
33	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	4/2012	255.64 -	272.20	283.69	- -	03/2022
34	PIRPAINTI-BHAGALPUR - [N22000222	4/2011	261.38 -	565.00	552.51	- -	05/2019
35	BANDEL-BOINCHI 3RD LINE - [N22000221	4/2011	288.35 -	502.48	508.72	- -	03/2021
<u>Metropolitan Rapid Transport Projects</u>							
36	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268	3/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-
37	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135	3/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-
38	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	3/1996	495.44 -	2,980.41	1,821.99	03/2004 -	03/2022
<u>North Central Railway</u>							
39	ETAWAH-MAINPURI (NL),NCR - [220100318	4/1997	120.00 -	346.00	345.51	12/2008 -	-
<u>North East Frontier Railway</u>							
40	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266	4/2000	1,180.19 -	4,541.38	3,825.94	12/2008 -	09/2021
41	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499	2/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-
42	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	4/2016	602.27 -	2,144.78	977.32	12/2021 -	09/2021
43	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	4/2011	314.00 -	800.00	832.55	03/2019 -	06/2021
44	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288	4/2003	4,454.17 -	12,264.15	11,303.51	03/2011 -	12/2023
45	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	4/2010	241.52 -	373.87	333.46	- 12/2021	03/2022
46	DIGARU-HOJAI (102 KM) - [N22000389	4/2015	870.96 -	1,873.21	1,397.73	03/2021 -	03/2022
47	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	4/1999	819.23 -	1,871.00	1,082.01	- -	-
48	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	9/2006	385.20 -	1,105.00	858.45	03/2019 -	03/2023

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North Eastern Railway</u>						
49	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
50	CHHAPRA-BALLIA UP - [N22000134]	3/2013	295.00 -	580.00	521.43	01/2019 -	02/2022
	<u>North Western Railway</u>						
51	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	2/1997	410.08 -	860.41	745.83	02/2019 -	06/2022
52	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	4/2012	246.08 -	395.00	366.38	12/2019 -	03/2021
53	THIYAT HAMIRA-SANU - [N22000149]	4/2013	236.93 -	350.45	287.39	10/2018 -	01/2020
54	ALWAR-BANDIKUI DOUBLING - [N22000157]	4/2013	242.09 -	525.00	473.86	02/2019 -	02/2020
55	AJMER-BANGURGRAM - [N22000155]	4/2011	213.39 -	375.00	361.04	11/2019 -	03/2021
	<u>Northern Railway</u>						
56	ROHTAK-MEHAM HANSI - [N22000272]	4/2012	287.00 -	893.45	717.17	12/2011 -	06/2021
57	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	4/2007	336.91 -	791.39	574.59	- -	03/2023
58	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	3/2002	625.00 -	859.00	852.73	03/2016 -	-
	<u>Rail Vikas Nigam Ltd.</u>						
59	HARIDASPUR-PARADEEP(NL) - [220100285]	4/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-
60	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	4/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-
61	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	3/2012	1,183.25 -	1,825.00	1,266.69	12/2020 -	12/2022
62	BANASGANI- JAKHPURA - DOUBLING - [N22000412]	3/2009	942.95 -	1,536.00	1,054.76	03/2019 -	06/2022
63	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	3/2006	948.04 -	2,009.00	1,532.13	03/2020 -	12/2021
64	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	3/2009	713.48 -	2,725.00	2,249.00	03/2020 -	12/2021
65	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	4/2011	927.01 -	1,400.00	1,233.65	03/2019 -	06/2022
66	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	4/2012	632.68 -	950.00	741.79	03/2016 -	12/2021
67	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,261.64	12/2021 -	12/2021
68	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	3/2012	1,503.71 -	3,377.00	2,152.52	03/2020 -	03/2022
	<u>South Central Railway</u>						
69	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	3/1996	164.36 -	1,050.00	999.64	02/2009 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
70	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205 <u>South East Central Railway</u>	4/1997	1,723.00 1.00	3,421.35	1,989.23	03/2000 -	03/2023
71	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	4/2005	383.79 -	1,511.50	1,430.54	- 08/2020	08/2020
72	GONDIA-JABALPUR(GC),(SECR) - [220100186 <u>South Eastern Railway</u>	2/1997	511.86 -	2,005.25	1,849.61	04/2020 03/2021	03/2021
73	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	4/2012	148.77 -	377.00	203.03	12/2016 -	08/2020
74	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	4/2012	258.20 -	358.68	316.37	12/2018 -	08/2021
75	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395 <u>South Western Railway</u>	11/2015	969.83 -	1,312.96	1,018.29	03/2020 -	02/2022
76	YELAHANKA-PENUKONDA - [N22000328	5/2015	860.43 -	1,147.00	945.81	03/2020	09/2021
77	ARSIKERE-TUMKUR - [N22000332 <u>Southern Railway</u>	3/2015	578.00 -	760.00	639.39	03/2020 11/2021	11/2021
78	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'- AGASTIYAMPALLI - [N22000079	9/2007	724.69 -	2,950.00	1,644.43	02/2019 -	03/2025
79	MADURAI-BODINAYAKKANUR - [N22000201	4/2008	164.41 -	608.13	389.96	- 12/2021	12/2021
80	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	4/2011	120.70 -	2,172.16	273.27	03/2019 -	12/2027
81	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	2/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022
82	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	2/1996	268.87 -	950.00	920.84	03/2005 -	09/2021
83	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	327.00	275.03	04/2014 -	-
84	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	4/2007	931.98 -	1,121.00	969.72	- 08/2021	08/2021
85	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	4/1999	198.68 -	559.95	273.32	- -	03/2024
86	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262 <u>West Central Railway</u>	9/1995	303.98 -	1,720.00	704.89	03/2020 -	03/2025
87	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314	4/2001	424.60 -	2,909.99	1,282.25	03/2021 03/2024	03/2024
88	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232 <u>Western Railway</u>	9/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025
89	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	4/2006	117.36 196.95	202.35	809.40	03/2011 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
90	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	4/2008	829.74 -	1,886.76	1,875.42	03/2020 03/2024	03/2024
91	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	4/2011	1,037.15 -	1,383.69	1,199.84	03/2021 12/2022	12/2022
92	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494	4/2017	691.84 -	890.62	812.08	03/2020 09/2021	09/2021
93	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	2/1991	551.51 -	890.76	773.12	03/2019 10/2021	10/2021
	Total		51,735.11 -	1,28,032.27	95,054.06		
	ROAD TRANSPORT AND HIGHWAYS						
	Ministry Of Road Transport And Highways (State Pwds)						
94	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	890.74	03/2011 12/2021	12/2021
95	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021
96	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIKAALA TO RENGAPALI ODISHA - [N24001091	3/2016	536.65 356.00	536.65	550.22	12/2019 12/2021	12/2021
97	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	8/2010	186.96 -	322.24	304.71	09/2014 12/2021	12/2021
98	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	3/2018	325.86 -	386.41	341.72	10/2018 -	-
99	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA - [N24001156	1/2017	166.67 -	166.67	184.91	09/2017 -	-
100	KALMATH TO ZARAP - [N24001137	9/2016	1,338.13 1,338.00	1,338.13	1,346.39	03/2020 -	-
101	TALGAON TO KALMATH - [N24001136	10/2016	904.70 905.00	904.70	969.90	03/2020 -	-
102	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	8/2010	195.04 -	377.99	368.39	10/2010 12/2021	12/2021
103	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574	11/2013	683.83 -	560.70	691.29	07/2016 -	-
104	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	318.85	05/2017 05/2022	05/2022
105	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257	3/2015	298.33 -	298.33	325.55	- -	-
	National Highways Authority Of India						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
106	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [N240106277	12/2003	280.00 -	612.58	612.58	02/2009 -	-
107	INDORE-DEWAS(NH-3) - [N24000159	11/2010	325.00 -	475.00	469.54	05/2013 -	-
108	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021
109	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232	11/2013	1,916.79 -	1,916.79	1,960.92	11/2016 -	-
110	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	443.00	- -	10/2022
111	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	3/2018	642.13 -	807.00	691.19	- -	-
112	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852	3/2018	478.74 -	478.74	714.50	- -	-
113	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810	3/2018	565.09 -	565.09	651.47	- -	02/2021
114	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809	3/2018	1,550.98 -	1,550.98	1,620.21	- -	09/2021
115	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	3/2018	1,120.57 -	1,332.00	1,441.15	- -	-
116	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	3/2018	925.40 -	1,197.00	1,176.70	- -	-
117	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	2/2018	2,177.80 -	2,450.00	2,425.12	- -	-
118	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	2/2018	1,995.34 -	2,400.00	3,368.89	- -	11/2021
119	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	3/2017	831.58 -	1,177.00	912.41	03/2020 -	-
120	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	3/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-
121	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	3/2017	1,184.71 -	1,310.00	1,286.42	03/2020 -	-
122	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650	1/2017	244.90 -	244.90	251.87	05/2019 -	-
123	4 LANING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 -	722.46	722.46	07/2018 -	-
124	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634	10/2016	447.75 -	447.75	1,324.11	- -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
125	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]	10/2016	1,008.96 -	1,008.96	1,125.65	- -	-
126	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]	11/2016	1,071.61 -	1,048.10	1,091.93	- 10/2021	07/2021
127	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]	9/2016	1,244.10 -	1,244.10	1,663.00	- -	-
128	SIX LANE OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O) - [N24000675]	3/2017	993.16 -	1,434.00	1,310.52	03/2020 -	-
129	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	9/2016	1,100.19 -	1,145.31	1,355.00	- -	-
130	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	9/2016	1,239.82 -	1,727.66	1,691.00	- -	-
131	4/2 LANNING WITH PS DAUSA-LALSOT-KAUNHUN SECTION OF NH-11A - [N24000591]	7/2016	688.70 -	688.70	870.48	- -	-
132	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]	3/2016	1,404.50 -	1,404.50	2,977.58	- -	-
133	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]	2/2016	273.20 -	273.20	668.42	02/2019 -	-
134	TRICHY - KARUR - [N24000528]	3/2007	516.00 -	516.00	886.96	07/2008 -	-
135	TWO LANE WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	8/2015	516.13 -	649.27	643.77	04/2018 -	-
136	NASHRI- CHANANI - [N24000162]	5/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-
137	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]	7/2010	1,987.00 -	1,987.00	3,113.72	07/2015 -	09/2020
138	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]	2/2009	1,693.75 -	1,693.75	2,848.49	08/2011 -	-
139	INDORE-JHABUA-GUJRAT/MP - [N24000136]	10/2010	1,175.00 -	1,175.00	1,509.96	04/2013 -	-
140	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]	3/2010	1,509.10 -	1,509.10	3,684.44	09/2012 -	-
141	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	4/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-
142	NALBARI TO BIJNI (AS-6) - [N24000047]	12/2003	225.00 -	225.00	390.72	06/2008 -	09/2019
143	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019
144	PUNE-SATARA(NH-4) - [N24000156]	10/2010	1,724.55 -	1,724.55	2,615.35	03/2013 -	09/2021
145	AHMEDABAD TO VADODARA SECTION - [N24000222]	1/2013	2,125.24 -	2,125.24	4,669.71	12/2015 -	-
146	ETAWAH CHAKERI - [N24000219]	3/2013	1,573.00 -	1,573.00	2,093.25	09/2015 -	-

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
147	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	7/2012	291.36 -	469.31	459.07	01/2014 -	-
148	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]	12/2011	1,047.00 -	1,047.00	1,873.47	06/2014 -	-
149	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]	2/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023
150	4-LANING OF FARAKA-RAIGANJ - [N24000202]	2/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	08/2021
151	MUZAFFARNAGAR-HARIDWAR - [N24000201]	9/2011	754.00 -	754.00	1,364.18	03/2013 -	-
152	SRINAGAR TO BANIHAL - [N24000189]	6/2011	1,100.70 -	1,100.70	2,932.90	06/2014 -	10/2020
153	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	5/2011	511.54 -	591.00	578.00	11/2013 -	-
154	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	8/2015	854.80 -	1,038.56	1,021.63	-	-
155	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]	8/2015	275.90 -	275.90	289.13	-	-
156	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]	12/2015	479.20 -	479.20	712.89	05/2018	-
157	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	4/2014	1,665.00 -	2,360.65	4,495.94	-	-
158	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]	4/2010	1,170.52 -	1,170.52	2,051.36	06/2012 -	-
159	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	5/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-
160	FOUR LANING OF PARWANOO -SOLAN - [N24000479]	9/2015	934.46 -	934.46	1,298.21	03/2018 -	-
161	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]	2/2008	1,673.70 -	1,673.70	3,326.93	10/2011 -	-
162	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]	5/2014	1,655.01 -	1,655.01	1,867.51	08/2016 -	12/2020
163	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]	12/2015	611.65 -	611.65	728.24	06/2016 -	-
164	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH- 47 - [N24000459]	6/2015	845.24 -	941.00	881.72	- 01/2020	01/2020
165	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]	1/2015	972.50 -	972.50	1,492.00	07/2017 -	-
166	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]	8/2014	822.90 -	822.90	844.08	04/2018 -	09/2021
167	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	685.76	05/2018 03/2022	03/2022
168	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER- FATEHPUR-SALA - [N24000426]	11/2012	530.07 -	530.07	556.02	08/2016 -	06/2020

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
169	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367	4/2014	495.78 -	627.93	633.24	01/2016 -	-
170	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360	4/2014	351.34 -	417.68	433.68	01/2016 -	-
171	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186	10/2011	375.09 -	375.09	494.33	04/2014 -	-
172	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185	9/2011	574.00 -	574.00	768.92	03/2014 -	-
173	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183	11/2011	1,535.00 -	1,535.00	3,279.25	05/2014 -	-
174	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	9/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022
175	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178	4/2011	571.00 -	571.00	582.53	10/2013 -	-
176	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172	9/2011	1,250.00 -	1,250.00	1,342.23	12/2013 -	-
177	GHAZIABAD-ALIGARH NH-91 - [N24000170	2/2011	1,141.00 -	1,141.00	1,715.00	08/2013	-
178	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163	7/2010	1,813.76 -	1,813.76	2,652.71	07/2013	-
179	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	270.97	05/2008 -	06/2019
180	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230	5/2013	1,348.20 -	1,348.20	1,792.90	02/2014 -	-
181	4 LANING OF NAGPUR-BETUL - [N24000155	2/2011	2,498.76 -	2,498.76	2,531.46	08/2014 -	-
182	HARANGAJO TO MAIBANG, NH-54 - [N24000062	12/2003	196.00 -	655.17	655.17	07/2009 -	-
	Total		84,235.38 -	93,634.99	1,24,659.86		
	<u>STEEL</u>						
	<u>Raastriya Ispat Nigam Limited</u>						
183	FORGED WHEEL PLANT - [N12000116	4/2014	1,682.85 -	2,100.00	1,704.90	09/2018 09/2021	09/2021
	Total		1,682.85 -	2,100.00	1,704.90		
	<u>URBAN DEVELOPMENT</u>						
	<u>Delhi Metro Rail Corporation</u>						
184	DELHI MRTS PHASE-III - [N28000056	9/2011	38,585.00 -	38,585.00	39,332.34	03/2016 -	08/2021
	<u>Kochi Metro Rail Corporation Ltd</u>						
185	KOCHI METRO RAIL PROJECT - [N28000081	7/2012	5,181.79 -	6,218.14	6,059.17	07/2017 09/2020	-
	<u>National Building Construcion Corporation Ltd</u>						

List of Projects in which Expenditure is More than Approved Cost

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
186	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080	6/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-
	Total		48,030.79 -	49,523.87	50,074.59		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
187	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037	12/2014	225.77 -	398.90	284.90	03/2020 -	03/2021
188	SAIDPUR SEWER NETWORK PATNA - [N30000039	4/2015	268.63 -	268.63	317.85	01/2021 -	-
	Total		494.40 -	667.53	602.75		
	Grand Total		2,14,662.19	3,13,678.24	3,08,162.55		

FLASH REPORT

Details of Projects Ahead of Schedule w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
1	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	-	09/2025	05/2024
	Total		1,828.00	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
2	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00	3,072.00	2,443.16	06/2021 08/2022	07/2022
	<u>Indian Oil Corporation Limited</u>						
3	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	2,213.96	09/2022	03/2022
4	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00	1,398.00	88.76	12/2023	09/2023
5	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00	921.00	5.26	09/2023 02/2024	12/2023
6	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00	18,936.00	763.62	09/2024	08/2024
	Total		27,644.00	28,023.00	5,514.76		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
7	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80	261.80	63.92	10/2021 01/2022	10/2021
8	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71	1,522.71	894.14	09/2021 10/2022	01/2022
9	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]	1/2021	842.27	842.27	92.08	07/2022	06/2022
	<u>Power Grid Corporation Of India Limited</u>						
10	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 14,719.10	14,719.10	12,953.79	08/2013 11/2022	08/2022
	Total		13,756.97	17,345.88	14,003.93		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
11	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,557.30	03/2024	03/2023

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>North East Frontier Railway</u>						
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	4/2016	602.27 -	2,144.78	977.32	12/2021 -	09/2021
	<u>Rail Vikas Nigam Ltd.</u>						
13	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	547.68	12/2026 -	12/2025
14	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	1,921.53	03/2023 -	12/2022
15	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	.19	12/2025 -	03/2025
	Total		10,047.51 -	16,249.45	5,004.02		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
16	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]	1/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
17	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	121.93	09/2019 06/2023	04/2023
18	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]	3/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022
	Total		2,653.27 -	2,653.27	913.32		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
19	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	253.46	09/2020 09/2021	08/2021
	Total		263.36 -	263.36	253.46		
	Grand Total		56,193.11	66,362.96	25,689.49		

Details of On Schedule Projects w.r.t. Original Schedule

Annexure - IV

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
1	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD - [N04000086]	5/2020	353.61 -	353.61	67.32	05/2022 -	05/2022
2	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT - [N04000091]	4/2020	611.80 -	611.80	33.70	03/2023 -	03/2023
	Total		965.41 -	965.41	101.02		
	<u>COAL</u>						
	<u>Ahmedabad Metro Rail</u>						
3	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2023 -	03/2028
	<u>Central Coal Fields Limited</u>						
4	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	337.20	03/2023 -	03/2023
5	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	37.16	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						
6	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	1.17	03/2027 -	03/2027
7	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	4.39	03/2025 -	03/2025
8	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	15.70	03/2029 -	03/2029
9	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18 -	535.18	1.53	03/2026 -	03/2026
10	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	134.97	03/2024 -	03/2024
11	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	0.19	03/2027 -	03/2027
12	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	249.15	03/2022 -	03/2022
	<u>Mahanadi Coal Fields Limited</u>						
13	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,271.62	03/2029 -	03/2029
14	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	499.88	03/2027 -	03/2027
15	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,180.34	03/2026 -	03/2026
	<u>Northern Coal Fields Limited</u>						
16	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
17	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
18	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
19	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
20	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
<u>Singareni Colliers Company Limited</u>							
21	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	23.39	03/2023 -	03/2023
22	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	73.60	03/2023 -	03/2023
23	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	73.09	03/2024 -	03/2024
<u>South-Eastern Coal Fields Limited</u>							
24	KJSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,960.03	03/2023 -	03/2023
25	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	40.10	03/2026 -	03/2026
26	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023
27	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,960.09	03/2029 -	03/2029
28	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
29	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]	6/2010	11,816.40 -	11,816.40	4,583.09	03/2023 03/2016	03/2023
30	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	159.50	03/2022 -	03/2022
31	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
32	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	76.12	03/2026 -	03/2026
33	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	284.31	03/2029 -	03/2029
34	JAMPALI OCP RCE - [N06000198]	5/2020	278.64 -	278.64	183.90	03/2024 -	03/2024
<u>Western Coal Fields Limited</u>							
35	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
36	BHANEGAON OC - [N06000121]	2/2015	187.94 -	409.68	86.90	03/2023 -	03/2023
37	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	246.02	03/2022 -	03/2022
38	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	1.00	03/2026 -	03/2026
39	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
40	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
41	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	390.11	03/2025 -	03/2025
	Total		57,371.02 -	57,695.20	16,056.19		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>						
	<u>Central Public Works Department</u>						
42	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	38.44	06/2022 -	06/2022
43	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
44	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMENITIES - [N44000001]	3/2021	127.26 -	188.88	12.73	10/2023 -	10/2023
45	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
46	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
	Total		2,333.39 -	2,395.01	108.59		
	<u>FINANCE</u>						
47	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	163.31	11/2021 -	11/2021
	Total		348.77 -	348.77	163.31		
	<u>HEALTH AND FAMILY WELFARE</u>						
48	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	279.98	09/2023 -	09/2023
49	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	Total		2,981.00 -	3,232.00	279.98		
	<u>HOME AFFAIRS</u>						
50	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	0.29	05/2022 -	05/2022
51	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		333.96 -	333.96	.29		
	<u>PETROLEUM</u>						

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Bharat Petroleum Corporation Limited</u>						
52	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]	11/2018	248.55 -	248.55	126.45	06/2022 -	06/2022
53	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	195.24	03/2023 -	03/2023
54	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	422.60	03/2023 -	03/2023
55	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL - [N16000365]	12/2017	1,524.06 -	1,524.06	905.06	12/2021 -	12/2021
56	2ND GENERATION LIGNOCELLULOSE BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) [N16000374]	8/2019	1,607.00 -	1,607.00	263.13	08/2022 -	08/2022
	<u>Gas Authority Of India Limited</u>						
57	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	124.00	10/2022 -	10/2022
58	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,312.50	12/2021 -	12/2021
59	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	335.00	11/2022 -	11/2022
60	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	85.28	07/2022 -	07/2022
61	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	165.40	10/2022 -	10/2022
62	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,504.40	05/2023 -	05/2023
63	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	231.37	04/2022 -	04/2022
64	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR - [N16000289]	7/2017	243.53 -	243.53	132.46	07/2022 -	07/2022
65	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	340.70	07/2022 -	07/2022
66	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	99.53	10/2022 -	10/2022
	<u>Hindustan Petroleum Corporation Limited</u>						
67	SETTING UP OF PHASE II FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	263.70	11/2021 -	11/2021
68	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB - [N16000402]	5/2020	1,421.46 -	1,244.50	101.45	02/2023 -	02/2023
69	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	0.01	11/2022 -	11/2022
70	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	307.06	11/2022 -	11/2022
71	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	121.18	08/2021 -	08/2021
72	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	12.89	03/2024 -	03/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
73	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE - [N16000369]	12/2018	854.00 -	854.00	161.21	12/2022 -	12/2022
74	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,199.32	06/2022 -	06/2022
	<u>Indian Oil Corporation Limited</u>						
75	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	3,161.40	10/2021 -	10/2021
76	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	-	03/2030 -	03/2030
77	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]	6/2019	2,880.00 -	2,880.00	-	08/2027 -	08/2027
78	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]	2/2021	34,627.00 -	34,627.00	445.30	09/2024 -	09/2024
79	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]	6/2019	2,996.00 -	2,996.00	-	02/2028 -	02/2028
80	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]	6/2019	163.00 -	163.00	-	12/2029 -	12/2029
81	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	-	03/2030 -	03/2030
82	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]	10/2018	613.00 -	613.00	-	12/2029 -	12/2029
83	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]	10/2018	176.00 -	176.00	-	08/2027 -	08/2027
84	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTA - [N16000386]	1/2020	14,810.00 -	14,810.00	1,303.20	04/2023 -	04/2023
85	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]	6/2019	303.00 -	303.00	-	02/2028 -	02/2028
86	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	255.22	10/2021 -	10/2021
87	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	-	02/2027 -	02/2027
88	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	295.70	01/2024 -	01/2024
89	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	150.39	11/2021 -	11/2021
90	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	16.19	07/2022 -	07/2022
91	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]	6/2019	347.00 -	347.00	-	02/2028 -	02/2028
92	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]	10/2020	1,614.00 -	1,614.00	0.21	08/2023 -	08/2023
93	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	421.90	05/2023 -	05/2023
94	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	-	12/2029 -	12/2029
95	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]	6/2019	988.00 -	988.00	-	12/2029 -	12/2029

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
96	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400	6/2020	1,378.00 -	1,378.00	159.37	12/2022 -	12/2022
97	LPG BP PROJECT CHITTOOR - [N16000381	7/2019	167.00 -	167.00	9.93	07/2022 -	07/2022
98	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249	5/2016	1,945.00 -	1,945.00	1,529.03	02/2022 -	02/2022
99	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399	6/2020	403.00 -	403.00	89.57	08/2022 -	08/2022
100	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422	6/2019	439.00 -	439.00	-	02/2028 -	02/2028
101	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333	3/2018	676.00 -	676.00	464.35	08/2022 -	08/2022
	<u>Numaligarh Refinery Limited</u>						
102	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379	1/2019	12,366.00 -	12,366.00	567.38	10/2024 -	10/2024
103	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394	1/2019	10,228.00 -	10,228.00	285.27	10/2024 -	10/2024
	<u>Oil & Natural Gas Corporation Limited</u>						
104	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	970.30	901.28	03/2026 -	03/2026
105	REDEVELOPMENT OF NANDASAN FIELD - [N16000404	2/2020	444.87 -	444.87	103.78	08/2022 -	08/2022
106	HEERA REDEVELOPMENT - PHASE III - [N16000360	6/2019	2,494.68 -	2,354.72	1,603.69	03/2022 -	03/2022
	Total		1,60,429.88 -	1,59,730.36	21,173.10		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
107	CHHATTARGARH 150 MW - [N18000294	2/2021	599.99 -	559.98	60.85	07/2022 -	07/2022
108	KAWAS SOLAR 56 MW - [N18000283	8/2020	261.80 -	261.80	63.92	10/2021 01/2022	10/2021
109	BHENSARA 320 MW - [N18000293	1/2021	1,221.73 -	1,221.73	137.36	07/2022 -	07/2022
110	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA & RADHANPUR) - [N18000296	5/2021	674.92 -	674.92	-	09/2022 -	09/2022
111	ANTA SOLAR 90 MW - [N18000292	1/2021	382.22 -	382.22	-	03/2022 -	03/2022
	<u>Satluj Jal Vidyut Nigam Limited</u>						
112	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194	3/2019	10,439.09 -	10,439.09	2,725.87	01/2024 -	01/2024
113	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291	10/2020	687.97 -	687.97	155.02	11/2025 -	11/2025
114	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279	11/2020	1,810.56 -	1,810.56	486.06	01/2026 -	01/2026

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
	Total		16,078.28	16,038.27	3,629.08		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
115	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]	2/2016	9,968.00	9,968.00	-	03/2024	03/2024
116	DAUND - MANMAD (236 KM) - [N22000360]	2/2016	1,876.00	2,081.27	565.94	03/2023	03/2023
117	PUNE-NASIK (265 KM) - [N22000354]	2/2016	2,425.00	5,341.68	-	03/2024	03/2024
118	WARDHA-NANDED MAHARASHTRA - [N22000231]	4/2008	3,168.29	3,445.48	1,401.51	03/2023	03/2023
	<u>North Eastern Railway</u>						
119	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78	895.00	114.63	12/2021	12/2021
120	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03	230.03	277.14	12/2022	12/2022
121	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42	1,758.00	1,143.78	03/2022	03/2022
	<u>Northern Railway</u>						
122	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14	1,540.13	242.31	03/2023	03/2023
	<u>National High Speed Rail Corporation Limited</u>						
123	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00	1,08,000.00	14,605.32	12/2023	12/2023
	<u>Rail Vikas Nigam Ltd.</u>						
124	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76	3,677.76	446.65	12/2023	12/2023
125	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94	850.00	618.69	12/2024	12/2024
126	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26	3,548.68	1,568.77	12/2023	12/2023
127	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62	1,500.00	1,261.64	12/2021	12/2021
	Total		1,36,208.24	1,42,836.03	22,246.38		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
128	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00	160.00	116.26	09/2021	09/2021
129	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]	3/2019	237.51	237.51	75.42	12/2022	12/2022
130	NAGPUR-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240]	3/2020	370.36	370.36	178.51	08/2022	08/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
131	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	100.31	09/2021 -	09/2021
132	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]	6/2020	437.60 -	437.60	-	08/2021 -	08/2021
133	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001373]	1/2020	358.26 -	358.26	-	02/2024 -	02/2024
134	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]	6/2020	496.47 -	496.47	-	08/2021 -	08/2021
135	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	1/2017	197.67 -	236.18	21.65	12/2022 -	12/2022
136	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]	3/2021	182.55 -	182.55	-	09/2021 -	09/2021
137	BALANCE WORK 2-LANING OF LALPUL MANMAO-CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372]	2/2021	588.09 -	588.09	-	03/2024 -	03/2024
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
138	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	794.41	12/2023 -	12/2023
139	LADDA - BASAI - [N24001316]	2/2021	445.96 -	445.96	-	04/2023 -	04/2023
140	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	12.93	12/2023 -	12/2023
141	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24 -	292.24	37.79	07/2022 -	07/2022
142	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	-	12/2022 -	12/2022
143	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322]	9/2020	183.31 -	183.31	-	05/2022 -	05/2022
144	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53 -	361.53	23.62	06/2022 -	06/2022
145	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]	3/2019	402.94 -	402.94	44.89	04/2022 -	04/2022
146	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
147	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	19.19	04/2023 -	04/2023
148	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
149	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	-	12/2022 -	12/2022
150	RANIKOR-MAHESKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]	10/2020	157.86 -	157.86	17.63	04/2022 -	04/2022
151	KHELLANI-KHANABAL PKG-6 - [N24001324]	2/2021	285.28 -	285.28	0.33	09/2022 -	09/2022
152	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325]	9/2020	262.84 -	262.84	-	05/2023 -	05/2023
153	TAMENGLONG - MAHUR PKG-3 - [N24001354]	3/2021	234.08 -	234.08	-	12/2022 -	12/2022
154	DOGINALA - GAU - [N24001320]	12/2020	242.30 -	242.30	-	09/2022 -	09/2022
155	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) - [N24001312]	3/2020	167.95 -	167.95	40.95	06/2022 -	06/2022
156	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]	3/2020	261.13 -	261.13	23.56	06/2022 -	06/2022
157	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256]	8/2020	6,808.69 -	6,808.69	176.00	09/2026 -	09/2026
158	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
159	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
160	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
161	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
162	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]	6/2020	257.96 -	257.96	95.22	01/2022 -	01/2022
163	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	-	01/2024 -	01/2024
164	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]	3/2020	247.76 -	247.76	29.13	01/2022 -	01/2022
165	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327]	8/2020	292.80 -	292.80	2.53	05/2022 -	05/2022
166	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329]	3/2020	165.54 -	165.54	-	07/2022 -	07/2022
167	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]	7/2020	345.38 -	345.38	74.52	04/2023 -	04/2023
168	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272]	3/2020	167.95 -	167.95	27.29	06/2022 -	06/2022
169	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270]	3/2020	292.24 -	292.24	29.70	06/2022 -	06/2022
170	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
171	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	-	12/2022 -	12/2022
172	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	18.03	05/2022 -	05/2022
173	DABOKA KATHKATI PACKAGE-5 - [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
174	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
175	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	27.54	12/2023 -	12/2023
176	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271]	6/2020	365.53 -	365.53	32.49	08/2022 -	08/2022
177	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	21.58	07/2022 -	07/2022
178	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]	8/2020	311.00 -	311.00	17.38	04/2023 -	04/2023
179	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	-	01/2023 -	01/2023
180	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	40.94	04/2022 -	04/2022
181	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254]	3/2020	242.97 -	242.97	32.98	06/2022 -	06/2022
182	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310]	11/2020	280.91 -	280.91	59.20	07/2022 -	07/2022
183	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
184	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268]	3/2019	471.00 -	471.00	116.31	07/2022 -	07/2022
185	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255]	9/2020	277.44 -	277.44	26.41	10/2022 -	10/2022
186	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]	3/2020	220.20 -	220.20	28.18	12/2022 -	12/2022
187	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	31.88	06/2022 -	06/2022
188	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]	6/2020	201.99 -	201.99	14.98	01/2022 -	01/2022
189	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326]	11/2020	4,997.04 -	4,997.04	10.45	09/2028 -	09/2028
190	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286]	3/2020	278.95 -	278.95	68.48	06/2022 -	06/2022
191	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285]	3/2020	330.78 -	330.78	40.40	12/2021 -	12/2021

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
192	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]	3/2020	154.51 -	154.51	12.08	07/2022 -	07/2022
193	DEMBUEN - BRUNI - [N24001321]	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
194	KHELLANI-KHANABAL PKG-1 - [N24001323]	3/2021	486.45 -	486.45	14.16	09/2022 -	09/2022
195	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	-	01/2023 -	01/2023
196	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	-	06/2023 -	06/2023
197	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	55.79	06/2022 -	06/2022
198	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]	3/2020	216.49 -	216.49	33.63	07/2022 -	07/2022
199	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269]	3/2020	216.49 -	216.49	26.88	03/2022 -	03/2022
200	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	-	12/2022 -	12/2022
201	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]	3/2021	636.42 -	636.42	-	12/2022 -	12/2022
202	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]	3/2020	281.78 -	281.78	73.31	07/2022 -	07/2022
203	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	-	12/2022 -	12/2022
204	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	-	01/2023 -	01/2023
205	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	6.87	07/2022 -	07/2022
206	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	9.72	04/2022 -	04/2022
207	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]	9/2020	173.17 -	173.17	-	04/2022 -	04/2022
208	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	24.01	04/2022 -	04/2022
209	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275]	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
210	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	-	12/2022 -	12/2022
211	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	-	01/2023 -	01/2023
212	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	23.41	04/2022 -	04/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
213	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333	9/2019	761.54 -	761.54	86.48	05/2023 -	05/2023
214	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288	8/2020	232.29 -	232.29	4.98	04/2022 -	04/2022
215	TLABUNG - LUNGLEI PKG-A - [N24001358	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
216	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277	9/2020	275.02 -	275.02	22.39	10/2022 -	10/2022
217	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266	7/2020	210.79 -	210.79	10.84	04/2022 -	04/2022
218	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311	11/2020	206.78 -	206.78	3.42	07/2022 -	07/2022
219	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328	12/2020	804.00 -	804.00	3.23	08/2023 -	08/2023
220	DABOKA KATHKATI PACKAGE-4 - [N24001365	2/2021	260.07 -	260.07	-	12/2023 -	12/2023
221	KARGIL-ZANSKR PACKAGE-6 - [N24001346	1/2021	239.81 -	239.81	23.77	05/2024 -	05/2024
222	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336	8/2020	230.45 -	230.45	1.29	04/2023 -	04/2023
223	TLABUNG - LUNGLEI PKG-B - [N24001359	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
224	IMPHAL – MOREH PACKAGE- 3 - [N24001352	3/2021	259.31 -	259.31	-	12/2022 -	12/2022
225	KHELLANI-KHANABAL PKG-3 - [N24001341	3/2021	398.51 -	398.51	-	12/2022 -	12/2022
226	KARGIL-ZANSKR PACKAGE-5 - [N24001330	8/2020	169.79 -	169.79	19.50	12/2023 -	12/2023
227	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273	7/2020	177.76 -	177.76	23.02	08/2022 -	08/2022
228	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249	6/2020	347.36 -	347.36	64.89	01/2022 -	01/2022
229	MARIAM - PEREN PKG-1A - [N24001349	2/2021	226.32 -	226.32	-	12/2022 -	12/2022
230	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274	8/2020	379.39 -	379.39	2.29	04/2022 -	04/2022
231	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313	11/2020	351.12 -	351.12	40.99	12/2023 -	12/2023
232	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287	4/2020	330.80 -	330.80	30.14	12/2021 -	12/2021
233	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	2.80	10/2022 -	10/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
234	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259	9/2020	315.63 -	315.63	7.28	04/2022 -	04/2022
235	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250	8/2020	278.46 -	278.46	27.76	03/2022 -	03/2022
236	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263	6/2020	277.50 -	277.50	15.01	01/2022 -	01/2022
237	KARGIL-ZANSKR PACKAGE-7 - [N24001347	1/2021	308.86 -	308.86	9.46	06/2024 -	06/2024
238	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335	11/2020	284.21 -	284.21	2.63	12/2023 -	12/2023
239	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
240	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
241	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309	11/2020	159.13 -	159.13	7.72	06/2022	06/2022
242	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308	11/2020	332.14 -	332.14	-	07/2022 -	07/2022
	<u>National Highways Authority Of India</u>						
243	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
244	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
	Total		54,550.23 -	54,588.74	3,268.22		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
245	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,901.76	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,901.76		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
246	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124	11/2015	2,907.00 -	2,907.00	408.71	06/2023 -	06/2023
	<u>Steel Authority Of India Limited (Sail)</u>						
247	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123	11/2020	542.24 -	542.24	56.59	12/2023 -	12/2023

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
248	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122	11/2020	377.18 -	377.18	37.11	05/2023 -	05/2023
	Total		3,826.42 -	3,826.42	502.41		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
249	SURAT METRO RAIL PROJECT - [N28000138	3/2019	12,020.32 -	12,020.32	177.50	03/2024 -	03/2024
250	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137	3/2019	5,384.17 -	5,384.17	193.79	03/2024 -	03/2024
	<u>Delhi Metro Rail Corporation</u>						
251	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135	7/2019	24,948.65 -	24,948.65	2,269.98	03/2025 -	03/2025
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
252	BHOPAL METRO RAIL - [N28000124	11/2018	6,941.40 -	6,941.40	228.95	02/2023	02/2023
253	INDORE METRO RAIL - [N28000125	11/2018	7,500.80 -	7,500.80	138.49	02/2023	02/2023
	<u>National Capital Region Transport Corp</u>						
254	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134	3/2019	30,274.00 -	30,274.00	4,567.75	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
255	PATNA METRO RAIL CORPORATION LIMITED - [N28000148	2/2019	13,365.77 -	13,925.50	258.94	06/2024 -	06/2024
	Total		1,00,435.11 -	1,00,994.84	7,835.40		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
256	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051	8/2017	824.00 -	824.00	42.75	06/2022 -	06/2022
257	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050	8/2017	578.89 -	578.89	42.75	06/2022 -	06/2022
258	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
	<u>Delhi Jal Board</u>						
259	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014	3/2017	665.78 -	665.78	211.73	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
260	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
261	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029	1/2019	384.96 -	384.96	-	04/2022 -	04/2022

Details of On Schedule Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning (Month/Year)	
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated
1	2	3	4	5	6	7	8
262	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
263	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
264	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
265	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
266	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
267	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022
	<u>Uttar Pradesh Jal Nigam</u>						
268	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
269	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
270	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
271	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	148.55	09/2021 -	09/2021
272	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	53.62	10/2021 -	10/2021
273	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
274	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	112.27	09/2021 -	09/2021
275	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	51.66	09/2021 -	09/2021
	Total		8,507.47 -	8,566.14	663.33		
	Grand Total		5,49,738.36	5,56,184.96	77,929.06		

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

Annexure - V

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Bhavini Limited</u>							
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00 -	6,840.00	5,986.57	09/2010 -	10/2022	95.88
	<u>Nuclear Power Corporation Of India Limited</u>							
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 -	16,580.00	17,041.00	12/2015 -	02/2022	44.69
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 -	17,079.00	13,528.00	12/2016 -	03/2023	38.63
	Total		27,271.00 -	40,499.00	36,555.57			
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR [N04000073]	10/2013	417.23 -	707.73	456.88	09/2018 -	06/2022	69.63
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 -	480.33	105.53	09/2021 -	12/2022	38.72
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 -	1,232.00	371.33	03/2021 -	03/2023	7.88
	Total		1,905.50 -	2,420.06	933.74			
	<u>COAL</u>							
	<u>Bharat Coking Coal Limited</u>							
7	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00 -	334.27	24.70	04/2018 -	06/2022	37.56
8	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13 -	341.22	64.19	03/2017 -	03/2022	12.20
	<u>Central Coal Fields Limited</u>							
9	MAGADH EXPANSION OC(51 MTY) - [N06000015]	08/2008	6,964.33 6,964.33	7,254.37	729.50	07/2012 03/2028	03/2028	4.16
	<u>Eastern Coal Fields Limited</u>							
10	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 -	5,146.48	622.13	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>							
11	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 -	703.39	703.39	03/2013 -	03/2024	46.68

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Neyveli Lignite Corporation</u>							
12	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]	06/2011	5,907.11 -	7,980.79	7,407.39	12/2015 -	02/2021	35.10
13	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 -	17,237.80	12,346.08	11/2021 -	11/2022	.00
	<u>Singareni Colliers Company Limited</u>							
14	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	16.86
15	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 -	442.42	111.66	03/2019 -	03/2022	11.42
16	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	5.85
17	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 -	349.28	283.01	03/2015 -	03/2022	114.60
	<u>South-Eastern Coal Fields Limited</u>							
18	JAGANNATHPORA OCP(3.00MTY) - [N06000075]	09/2008	152.43 -	459.49	198.78	03/2015 -	03/2022	201.44
	<u>Western Coal Fields Limited</u>							
19	BHANEGAON OC - [N06000121]	02/2015	187.94 -	409.68	86.90	03/2023 -	03/2023	117.98
20	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56 -	299.67	164.36	03/2019 -	03/2022	1.39
21	AMALGAMATED PAUNI-II III OC MINE - [N06000131]	06/2015	483.69 -	499.00	253.70	03/2021 -	03/2021	3.17
22	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	08/2015	727.28 -	745.03	390.11	03/2025 -	03/2025	2.44
23	ADASA UG TO OC - [N06000133]	08/2015	288.90 -	333.43	145.08	03/2023 -	03/2024	15.41
24	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68 -	325.18	272.90	03/2019 -	03/2022	63.67
25	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52 -	327.41	160.84	03/2019 -	03/2022	7.52
26	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	08/2016	319.76 -	404.45	246.02	03/2022 -	03/2022	26.49
27	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	36.10	03/2022 -	03/2025	.00
28	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73 -	402.90	336.00	03/2020 -	09/2022	11.07
	Total		38,833.49 -	45,248.40	25,077.95			
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Central Public Works Department</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
29	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	288.03	06/2017 -	03/2022	.57
30	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	458.38	07/2019 -	-	1.85
31	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	130.63	09/2020 -	-	10.22
32	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES - [N44000001]	03/2021	127.26 -	188.88	12.73	10/2023 -	10/2023	48.42
<u>Rail India Technical And Economic Service</u>								
33	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	-	09/2014 -	-	29.31
	Total		1,843.07 -	2,078.60	889.77			
<u>DPIIT</u>								
<u>Delhi Mumbai Industrial Corridor</u>								
34	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	9,346.57	09/2019 -	07/2021	9.80
<u>India International Convention And Expo Centre</u>								
35	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,744.03	12/2019 -	05/2022	8.49
	Total		17,352.09 -	18,990.30	12,090.60			
<u>HEALTH AND FAMILY WELFARE</u>								
<u>Central Public Works Department</u>								
36	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025	15.92
<u>Hospital Services Consultancy Corporation Ltd</u>								
37	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	655.58	561.94	11/2013 -	09/2021	58.31
38	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	249.24	05/2017 -	03/2021	22.29
39	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	299.76	05/2017 -	01/2020	10.68
40	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 -	191.20	169.51	05/2017 -	07/2019	13.20
41	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 -	585.00	586.96	03/2018 -	09/2019	15.71

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
42	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	164.17	02/2018 -	03/2021	16.33
43	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	224.92	09/2018 -	05/2019	1.64
44	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	268.55	03/2019 -	03/2021	.13
45	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	156.14	-	11/2021	21.58
46	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	231.05	-	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>							
47	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	814.67	09/2021 -	06/2022	8.88
	Total		5,589.39 -	6,443.65	3,726.91			
	<u>HEAVY INDUSTRY</u>							
	<u>Natrip Implementation Society</u>							
48	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]	04/2011	1,718.00 -	3,727.30	3,517.10	09/2011 -	03/2021	116.96
	Total		1,718.00 -	3,727.30	3,517.10			
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
49	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	956.28	10/2019 -	03/2022	64.04
50	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]	12/2008	114.26 266.00	266.00	-	12/2013 -	-	132.80
51	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	172.12	04/2018 -	12/2021	46.12
52	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]	06/2019	277.35 -	290.33	27.25	07/2022 -	10/2022	4.68
	Total		1,773.70 -	2,794.33	1,155.65			
	<u>PETROLEUM</u>							
	<u>Bharat Petroleum Corporation Limited</u>							
53	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]	11/2014	4,588.29 -	5,245.96	5,184.50	08/2018 -	09/2021	14.33

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
54	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11
55	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]	12/2015	1,112.00 -	1,507.24	769.00	06/2019 -	02/2022	35.54
	<u>Gas Authority Of India Limited</u>							
56	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]	06/2009	2,915.00 2,915.00	5,909.00	3,786.80	12/2012 -	02/2022	102.71
57	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	04/2017	287.49 -	345.15	231.37	04/2022 -	04/2022	20.06
58	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI- [N16000349]	09/2018	225.54 -	247.90	41.34	02/2021 -	08/2022	9.91
59	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]	08/2018	286.42 -	327.01	215.40	08/2020 -	12/2021	14.17
	<u>Hindustan Petroleum Corporation Limited</u>							
60	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]	07/2016	20,928.00 -	26,264.00	16,008.48	07/2020 -	07/2022	25.50
61	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	2,443.16	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>							
62	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	437.75	10/2017 -	03/2022	103.60
63	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	01/2015	1,823.00 -	3,027.90	2,117.81	03/2021 -	12/2021	66.09
64	PARADIP HYDERABAD PIPELINE - [N16000194]	01/2015	2,321.00 -	3,338.00	2,996.28	12/2020 -	03/2022	43.82
65	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	440.03	08/2019 -	05/2021	18.68
66	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	05/2016	4,497.00 -	6,025.00	3,897.13	12/2018 -	02/2022	33.98
67	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]	05/2016	348.00 -	437.00	162.73	01/2021 -	08/2022	25.57
68	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	04/2017	163.02 -	207.36	122.11	04/2020 -	10/2021	27.20
69	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304]	08/2017	236.00 -	319.61	195.28	06/2020 -	09/2021	35.43
70	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]	04/2018	206.63 -	340.76	131.80	02/2020 -	07/2022	64.91

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
71	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTA TO 2.5 MMTA AT KANDLA, GUJARAT [N16000336]	03/2018	588.20 -	730.20	128.08	- -	05/2023	24.14
72	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	06/2019	371.00 -	427.00	25.79	09/2022 -	03/2023	15.09
	<u>Mangalore Refinery And Petrochemicals Limited</u>							
73	SEA WATER DESALINATION PLANT - [N16000319]	11/2017	581.00 -	637.00	519.50	03/2020 -	11/2021	9.64
	<u>Oil & Natural Gas Corporation Limited</u>							
74	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128]	03/2011	861.79 -	2,001.34	1,568.64	05/2013 -	02/2022	132.23
75	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS [N16000213]	12/2015	3,190.69 -	3,375.90	2,876.04	04/2018 -	05/2022	5.80
76	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	709.24	03/2023 -	03/2022	38.20
77	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]	07/2016	249.85 250.00	303.75	205.92	05/2020 -	11/2021	21.57
78	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]	04/2019	3,228.80 -	3,976.67	1,307.63	03/2022 -	05/2023	23.16
79	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]	05/2019	3,660.71 -	3,740.05	2,997.59	05/2021 -	01/2022	2.17
	<u>Oil India Limited</u>							
80	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	383.44	02/2020 -	12/2021	17.41
	Total		58,421.67 -	76,792.19	49,922.28			
	<u>POWER</u>							
	<u>National Hydro-Electric Power Corporation</u>							
81	LOKTAK D/S HEP(NHPC) - [180100078]	12/1999	578.62 -	1,311.05	155.41	06/2006 -	-	126.58
82	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]	09/2002	3,919.59 -	9,897.59	9,164.35	09/2009 -	03/2023	152.52
83	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]	09/2003	6,285.33 -	19,992.43	14,059.55	09/2010 -	08/2023	218.08
	<u>National Thermal Power Corporation</u>							
84	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]	11/2006	2,978.48 -	5,867.38	5,045.40	03/2013 -	-	96.99
85	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	12,083.75	06/2019 -	12/2023	7.12
86	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,917.95	07/2012 -	10/2021	97.38

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
87	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	16,096.71	05/2018 -	02/2022	33.47
88	BARH STPP(3X660MW) NTPC - [180100242]	02/2005	8,692.97 -	21,312.11	19,169.37	10/2011 -	07/2023	145.16
89	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]	07/2012	1,527.00 -	1,801.07	149.93	08/2017 -	-	17.95
90	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,997.70	8,740.94	11/2020 -	10/2022	3.76
91	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	3,785.00	10/2017 -	-	7.41
92	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 -	2,311.89	1,892.27	12/2018 -	11/2021	22.64
93	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277] Power Grid Corporation Of India Limited	12/2016	529.68 -	633.80	461.33	11/2018 -	12/2021	19.66
94	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 -	5,071.94	4,612.66	10/2012 -	-	5.14
95	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,953.79	08/2013 -	08/2022	32.24
96	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 -	1,891.41	1,290.03	04/2016 -	-	38.61
97	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	480.43	11/2016 -	12/2021	4.61
98	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	01/2015	871.62 -	902.49	628.13	10/2017 -	-	3.54
99	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 -	260.03	200.16	07/2017 -	-	27.92
100	SYTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 -	639.46	590.30	06/2014 -	-	31.17
101	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 -	516.12	369.27	01/2019 -	-	26.36
102	COMPREHENSIVE SCHEME FOR THE STRENGHTENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,480.78	12/2018 -	03/2024	92.02
103	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	3,068.24	12/2018 -	03/2022	31.08
104	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,029.93	07/2020 -	10/2021	14.11
105	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	158.03	07/2019 -	10/2021	17.99
106	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	05/2017	445.89 -	675.73	372.58	02/2019 -	-	51.55

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>Satluj Jal Vidyut Nigam Limited</u>							
107	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	657.62	12/2021 -	06/2022	46.20
	<u>Thdc India Limited</u>							
108	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]	08/2008	2,491.58 -	3,860.35	2,271.34	06/2013 -	06/2024	54.94
109	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,170.24	02/2016 -	06/2023	191.23
	Total		1,12,524.61 -	1,76,835.90	137,055.49			
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
110	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	1,401.51	03/2023 -	03/2023	8.75
111	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	910.93	352.67	03/2021 -	03/2023	14.89
112	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 -	325.00	324.93	03/2019 -	-	76.57
113	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	2,831.83	03/2021 -	03/2023	111.08
114	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	-	03/2024 -	03/2024	120.28
115	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	-	03/2024 -	-	25.04
116	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	479.21	03/2022 -	03/2023	.89
117	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 -	2,081.27	565.94	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>							
118	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	434.63	03/2018 -	-	25.65
119	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	14.14	03/2019 -	-	.21
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>							
120	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]	10/2006	11,589.00 30,357.00	28,181.00	-	- -	-	143.17
121	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]	11/2007	16,592.00 51,101.00	51,101.00	22,485.00	03/2020 -	-	207.99
	<u>East Central Railways</u>							
122	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,620.00	3,614.37	- -	03/2022	250.41
123	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]	04/2003	528.65 -	2,066.78	1,581.82	- -	03/2023	290.95

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
124	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	04/1996	477.88 283.95	751.55	714.87	03/2012 -	09/2021	57.27
125	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	04/1997	324.73 -	1,070.00	1,076.60	03/2012 -	11/2022	229.50
126	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257	04/1997	162.87 -	614.45	352.16	- -	12/2023	277.26
127	KOSI BRIDGE (NL), ECR - [220100304	04/2002	499.41 -	516.02	458.36	03/2020 -	-	3.33
128	SAMASTIPUR-DARBANGHA - [N22000329	05/2015	380.00 -	519.33	294.63	- -	03/2025	36.67
129	HAJIPUR - BACHAWARA - [N22000334	05/2015	678.54 -	929.86	863.90	03/2019 -	12/2021	37.04
130	KODERMA-TILAIYA (NL), ECR - [220100305	04/2002	459.91 -	1,625.87	890.81	- -	03/2023	253.52
131	GAYA-CHATRA (NL) - [N22000169	04/2008	415.67 -	549.75	15.58	- -	-	32.26
132	BIHTA-AURANGABAD (NL) - [N22000170	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	818.15
133	SAKRI-HASANPUR ROAD (NL) - [N22000171	04/1999	325.00 -	735.20	388.33	- -	03/2021	126.22
134	CHHAPRA-MUZAFFARPUR (NL) - [N22000172	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	391.01
135	MOTIHARI-SITAMARHI (NL) - [N22000174	04/2006	211.00 -	1,006.00	24.16	- -	-	376.78
136	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180	04/2004	372.14 -	1,470.50	1,377.83	- -	03/2023	295.15
137	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 -	819.01	538.55	03/2020 -	03/2023	49.45
138	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 -	495.00	497.30	- -	10/2019	132.38
139	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15 -	546.71	547.77	07/2014 -	-	64.60
140	GARHWA ROAD-RAMNA - [N22000465	03/2015	348.23 -	390.00	366.22	03/2021 -	03/2022	11.99
141	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 -	1,215.54	488.59	03/2021 -	03/2024	63.37
142	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 -	1,185.73	269.99	03/2021 -	03/2024	62.06
143	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	04/1998	180.82 -	726.31	546.29	- -	08/2020	301.68
144	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 -	1,483.14	1,219.42	- -	03/2022	350.27
	East Coast Railway							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
145	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	895.94	06/2021 -	03/2025	137.80
146	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,602.15	03/2009 -	03/2026	29.71
147	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 -	1,539.28	1,186.14	02/2019 -	12/2021	38.43
148	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00 -	1,160.83	988.59	03/2020 -	03/2023	.07
149	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319	03/2012	155.81 -	238.03	222.65	03/2020 -	03/2022	52.77
150	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 -	810.02	192.59	11/2018 -	03/2024	15.45
<u>Eastern Railways</u>								
151	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	906.00	03/2019 12/2009	03/2025	36.22
152	DEOGHAR - SULTANGANJ (NL), ER - [220100273	04/2000	607.09 -	1,425.44	638.19	02/2013 -	03/2024	134.80
153	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	454.56	03/2017 -	03/2025	20.30
154	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 -	527.54	1.76	-	03/2025	44.46
155	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 -	663.13	544.63	03/2020 -	03/2021	22.31
156	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238	04/2011	175.80 -	495.10	299.53	-	03/2022	181.63
157	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02
158	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	.01
159	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241	04/2000	297.47 -	298.22	36.13	-	03/2025	.25
160	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	36.15
161	MONIGRAM- NIMITTA - [N22000301	04/2012	250.93 -	310.70	377.47	-	03/2024	23.82
162	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302	04/2012	255.64 -	272.20	283.69	-	03/2022	6.48
163	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	34.08
164	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217	04/2007	450.00 -	1,261.34	-	-	03/2025	180.30

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
165	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	11.77	- -	03/2025	51.19
166	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	409.74	03/2022 -	03/2025	133.39
167	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	508.72	- -	03/2021	74.26
168	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	552.51	- -	05/2019	116.16
169	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	614.44	03/2016 -	03/2025	7.75
170	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225] <u>Indian Railway Construction Company Limited</u>	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	29.20
171	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	962.98	03/2022 -	09/2023	117.23
172	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 -	3,055.15	2,666.33	09/2018 -	06/2022	.00
	<u>Metropolitan Rapid Transport Projects</u>							
173	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM- NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	3,837.57	12/2006 -	-	224.37
174	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	1,821.99	03/2004 -	03/2022	501.57
175	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 -	734.01	472.27	06/2013 -	07/2022	48.06
176	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 -	8,574.97	5,892.72	03/2016 -	-	75.91
	<u>North Central Railway</u>							
177	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	345.51	12/2008 -	-	188.33
178	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	303.16	03/2022 -	12/2024	32.02
179	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	330.00	03/2020 -	-	1.69
	<u>North East Frontier Railway</u>							
180	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 -	614.00	275.06	03/2019 -	-	106.51
181	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	4,169.01	03/2014 -	03/2024	130.69
182	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,825.94	12/2008 -	09/2021	284.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
183	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [N20100288	04/2003	4,454.17 -	12,264.15	11,303.51	03/2011 -	12/2023	175.34
184	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086	09/2006	385.20 -	1,105.00	858.45	03/2019 -	03/2023	186.86
185	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087	09/2006	532.87 -	2,145.00	1,014.54	03/2019 -	03/2024	302.54
186	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124	04/2006	2,326.52 -	6,911.00	1,300.10	03/2015 -	03/2026	197.05
187	KISHANGANJ JALALGARH, NL, NEFR - [N22000101	04/2008	333.76 -	360.00	6.74	- -	-	7.86
188	SEVOK RANGPO, NEFR - [N22000102	04/2008	1,339.48 -	8,600.00	1,656.02	12/2015 -	12/2023	542.04
189	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183	04/2013	1,798.00 -	2,042.51	219.14	03/2019 -	12/2023	13.60
190	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193	04/2010	221.42 -	380.00	38.20	- -	-	71.62
191	AGARTALA-AKHAURA NL - [N22000195	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26
192	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205	04/2010	906.46 -	4,083.02	264.34	03/2021 -	-	350.44
193	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206	04/2010	242.22 -	471.00	76.57	03/2020 -	-	94.45
194	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207	04/2010	241.52 -	373.87	333.46	- -	03/2022	54.80
195	MURKONGSELEK-PASIGHAT NL - [N22000208	04/2011	414.84 -	750.00	156.80	03/2020 -	-	80.79
196	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209	04/1999	819.23 -	1,871.00	1,082.01	- -	-	128.39
197	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210	04/2011	314.00 -	800.00	832.55	03/2019 -	06/2021	154.78
198	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388	04/2015	2,232.32 -	2,950.00	1,758.52	03/2022 -	03/2023	32.15
199	DIGARU-HOJAI (102 KM) - [N22000389	04/2015	870.96 -	1,873.21	1,397.73	03/2021 -	03/2022	115.07
200	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390	04/2016	602.27 -	2,144.78	977.32	12/2021 -	09/2021	256.12
201	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499	02/1999	380.60 -	1,090.60	1,089.12	04/2010 -	-	186.55
	<u>North Eastern Railway</u>							
202	KICHHA-KHATIMA (NL) - NER - [N20100317	04/2003	142.45 -	228.40	0.15	- -	-	60.34

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
203	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	- -	- -	8.10
204	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	-	- -	- -	358.99
205	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 -	895.00	114.63	12/2021 -	12/2021 -	267.13
206	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	580.00	521.43	01/2019 -	02/2022 -	96.61
207	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	- -	- -	.16
208	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,758.00	1,143.78	03/2022 -	03/2022 -	35.71
209	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	53.51	04/2016 -	12/2021 -	.16
210	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	-	04/2017 -	10/2022 -	127.77
211	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	-	01/2018 -	- -	9.91
212	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	88.04	- -	12/2023 -	18.56
	<u>North Western Railway</u>							
213	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	745.83	02/2019 -	06/2022 -	109.82
214	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	261.79	03/2020 -	10/2022 -	16.97
215	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 -	2,215.27	4.60	- -	- -	153.55
216	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	366.38	12/2019 -	03/2021 -	60.52
217	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	186.14	- -	- -	104.65
218	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	287.39	10/2018 -	01/2020 -	47.91
219	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]	04/2013	420.18 -	480.00	371.38	03/2020 -	09/2021 -	14.24
220	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	361.04	11/2019 -	03/2021 -	75.73
221	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	473.86	02/2019 -	02/2020 -	116.86
	<u>Northern Railway</u>							
222	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	111.51	- -	03/2024 -	129.17
223	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	717.17	12/2011 -	06/2021 -	211.31

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
224	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	574.59	- -	03/2023	134.90
225	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	160.58	- -	09/2023	41.71
226	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	204.53	- -	-	57.68
227	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	1.73	- -	03/2024	310.24
228	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	-	07/2012 -	03/2024	388.89
229	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	25,191.80	11/2002 -	12/2022	1,017.96
230	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	242.31	03/2023 -	03/2023	369.35
231	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	852.73	03/2016 -	-	37.44
	<u>Rail Vikas Nigam Ltd.</u>							
232	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	1,883.44	12/2017 -	-	55.57
233	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	1,066.19	02/2015 -	06/2022	102.92
234	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	388.21	03/2009 03/2009	-	196.83
235	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	888.31	03/2016 -	03/2025	59.22
236	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	547.68	12/2026 -	12/2025	127.62
237	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	1,921.53	03/2023 -	12/2022	41.04
238	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	2,453.42	03/2016 -	03/2025	7.78
239	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	18.95
240	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	2,152.52	03/2020 -	03/2022	124.58
241	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	1,261.64	12/2021 -	12/2021	53.75
242	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	611.25	03/2021 -	-	35.42
243	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	1,462.02	12/2021 -	03/2022	20.68
244	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	741.79	03/2016 -	12/2021	50.15

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
245	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	1,568.77	12/2023 -	12/2023	9.32
246	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	544.48	03/2022 -	12/2024	5.98
247	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	618.69	12/2024 -	12/2024	9.83
248	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	1,233.65	03/2019 -	06/2022	51.02
249	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	2,045.67	12/2024 -	03/2025	40.08
250	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	2,249.00	03/2020 -	12/2021	281.93
251	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	794.54	12/2024 -	12/2026	42.47
252	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	1,532.13	03/2020 -	12/2021	111.91
253	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	1,054.76	03/2019 -	06/2022	62.89
254	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 -	1,825.00	1,266.69	12/2020 -	12/2022	54.24
255	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	1,270.60	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>							
256	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 -	275.08	141.55	03/2012 -	-	60.77
	<u>South Central Railway</u>							
257	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 -	2,120.16	1,009.94	03/2009 -	03/2024	102.85
258	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 -	2,911.84	0.92	- -	-	161.86
259	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95 -	1,952.68	684.12	03/2023 -	03/2024	5.16
260	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,277.06	03/2021 -	03/2024	15.49
261	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 -	927.94	656.85	03/2020 -	11/2021	31.75
262	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	348.32	03/2014 -	03/2027	42.44
263	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 -	1,050.00	999.64	02/2009 -	-	538.84
264	MUNEERABAD-MAHABOONNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00	3,421.35	1,989.23	03/2000 -	03/2023	98.57
265	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,239.48	03/2022 -	03/2024	7.06

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
266	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	275.34
	<u>South East Central Railway</u>							
267	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,511.50	1,430.54	- -	08/2020	293.84
268	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	2,005.25	1,849.61	04/2020 -	03/2021	291.76
269	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420	09/2016	1,908.51 -	3,176.60	1,334.01	03/2023 -	12/2023	66.44
270	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438	04/2010	585.93 -	1,268.32	1,058.10	02/2019 -	12/2021	116.46
271	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	378.60
272	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483	04/2008	872.00 -	1,226.51	1,153.59	12/2019 -	10/2020	40.65
273	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484	04/2015	1,973.00 -	2,135.34	648.00	03/2021 -	12/2023	8.23
274	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	-	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>							
275	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30	1,026.00	182.49	03/2007 03/2007	-	160.76
276	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	203.03	12/2016 -	08/2020	153.41
277	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 -	620.00	40.99	- -	03/2025	131.89
278	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99
279	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 -	230.00	54.46	03/2015 -	-	53.44
280	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	358.68	316.37	12/2018 -	08/2021	38.92
281	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 -	1,312.96	1,018.29	03/2020 -	02/2022	35.38
282	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>							
283	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	1,801.01 -	2,161.36	76.42	- -	12/2023	20.01
284	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 -	1,530.09	311.40	03/2016 -	12/2026	55.13
285	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 -	692.00	-	- -	12/2023	24.01

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
286	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	-	-	12/2023	57.65
287	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	1,126.08	-	12/2025	17.95
288	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	0.34	-	12/2023	14.14
289	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	157.01	-	12/2024	123.51
290	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,960.00	7.35	03/2002	03/2024	41.74
291	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,800.59	1,128.98	03/2020	03/2023	55.63
292	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	945.81	03/2020	09/2021	33.31
293	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	639.39	03/2020	11/2021	31.49
294	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,457.95	03/2019	03/2024	16.31
295	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	731.77	465.72	03/2017	03/2025	13.49
	<u>Southern Railway</u>							
296	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079]	09/2007	724.69 -	2,950.00	1,644.43	02/2019	03/2025	307.07
297	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 -	3,150.00	239.49	-	12/2025	440.47
298	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 -	1,720.00	704.89	03/2020	03/2025	465.83
299	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 -	2,815.62	-	-	-	79.80
300	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	2.59	02/2019	-	247.32
301	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 -	1,205.00	2.28	-	03/2024	130.17
302	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 -	839.01	0.63	-	-	.00
303	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 -	559.95	273.32	-	03/2024	181.84
304	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	-	-	12/2021	69.20
305	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	-	-	-	46.09
306	ERODE-PALANI - [N22000199]	04/2008	288.57 -	603.23	1.63	-	-	109.04
307	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 -	608.13	389.96	-	12/2021	269.89

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
308	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	1,121.00	969.72	- -	08/2021	20.28
309	ERNAKULAM-KUMBALAM - [N22000204	04/2010	189.24 -	275.21	-	- -	-	45.43
310	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,172.16	273.27	03/2019 -	12/2027	1,699.64
311	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373	10/2013	187.26 -	327.00	275.03	04/2014 -	-	74.62
312	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400	02/2015	1,000.00 -	1,246.00	-	- -	-	24.60
313	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	920.84	03/2005 -	09/2021	253.33
314	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	102.11
<u>West Central Railway</u>								
315	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	1,282.25	03/2021 -	03/2024	585.35
316	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	3,230.57
317	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,763.93 -	2,470.00	1,244.18	03/2020 -	03/2024	40.03
318	KATNI GRADE SEPARATOR/BYE PASS - [N22000416	08/2016	582.13 -	1,247.64	415.54	03/2022 -	03/2023	114.32
<u>Western Railway</u>								
319	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	6,171.08	2,301.98	03/2022 -	03/2024	76.13
320	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	809.40	03/2011 -	-	72.42
321	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123	04/2008	318.24 -	321.62	126.36	03/2012 -	10/2023	1.06
322	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,886.76	1,875.42	03/2020 -	03/2024	127.39
323	CHOTTAUPEPUR-DHAR(NL) - [N22000138	04/2007	1,347.26 -	1,524.68	974.69	03/2022 -	03/2023	13.17
324	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139	04/2007	1,640.04 -	1,873.10	869.58	03/2022 -	03/2023	14.21
325	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	555.49	03/2019 -	03/2023	329.77
326	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	1,037.15 -	1,383.69	1,199.84	03/2021 -	12/2022	33.41
327	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	02/1991	551.51 -	890.76	773.12	03/2019 -	10/2021	61.51

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
328	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494]	04/2017	691.84 -	890.62	812.08	03/2020 -	09/2021	28.73
	Total		2,40,281.10 -	4,94,845.91	215,450.86			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
329	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 -	992.67	890.74	03/2011 -	12/2021	58.98
330	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 -	327.92	323.23	10/2010 -	12/2021	69.30
331	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]	04/2013	151.59 -	369.92	343.48	08/2013 -	-	144.03
332	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]	04/2013	166.27 -	359.90	302.35	08/2013 -	-	116.46
333	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]	01/2013	182.28 -	369.58	340.16	02/2013 -	-	102.75
334	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]	03/2015	258.97 -	268.92	229.77	08/2015 -	-	3.84
335	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 -	290.59	244.36	- -	-	3.72
336	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00	348.43	314.12	09/2017 -	-	36.24
337	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	318.85	05/2017 -	05/2022	45.75
338	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]	11/2015	889.24 -	904.82	766.98	- -	-	1.75
339	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]	08/2010	195.04 -	377.99	368.39	10/2010 -	12/2021	93.80
340	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]	01/1991	319.68 -	369.77	301.91	- -	-	15.67
341	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]	03/2014	191.50 192.00	192.00	183.94	05/2016 -	-	.26

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
342	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]	08/2013	171.96 172.00	172.00	100.67	06/2016 -	-	.02
343	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]	03/2018	460.73 -	461.00	116.25	- -	-	.06
344	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]	11/2017	237.80 -	238.00	148.90	11/2019 -	10/2021	.08
345	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]	03/2018	166.21 -	173.41	154.26	08/2018 -	09/2021	4.33
346	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]	03/2016	271.17 291.20	291.20	120.14	11/2018 -	03/2022	7.39
347	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND) - [N24000885]	03/2016	160.27 -	213.97	26.72	08/2019 -	11/2022	33.51
348	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]	06/2016	236.78 -	263.26	72.02	08/2019 -	08/2022	11.18
349	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]	04/2014	279.70 398.22	398.52	331.86	08/2017 -	02/2020	42.48
350	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]	03/2018	217.22 -	226.88	173.03	08/2018 -	09/2021	4.45
351	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928]	10/2015	333.21 -	353.43	333.09	12/2015 -	-	6.07
352	BHOKAR TO SANSAM - [N24001128]	02/2017	295.09 -	295.99	169.64	07/2019 -	-	.31
353	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]	11/2017	392.33 -	428.55	379.29	03/2018 -	10/2021	9.23
354	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]	12/2017	297.30 -	318.28	168.33	01/2019 -	-	7.06
355	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 -	386.41	341.72	10/2018 -	-	18.58
356	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]	11/2016	336.25 -	369.96	322.13	09/2019 -	-	10.03
357	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	304.71	09/2014 -	12/2021	72.36
358	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	1,242.64	- -	-	2.93

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
359	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	01/2016	497.14 -	572.66	278.09	08/2016 -	06/2022	15.19
360	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00	544.00	400.49	09/2016 -	12/2021	14.24
361	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	01/2016	624.98 -	731.50	460.02	10/2016 -	12/2021	17.04
362	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	21.65	12/2022 -	12/2022	19.48
National Highways And Infrastructure Development Corporation Ltd.								
363	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]	03/2015	394.00 -	522.86	410.63	06/2018 -	03/2021	32.71
364	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	133.92	04/2017 -	03/2022	29.48
365	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 -	263.31	145.13	04/2017 -	03/2022	29.48
366	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	325.21	08/2016 -	05/2021	3.73
367	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 -	252.05	144.26	04/2017 -	03/2022	27.16
368	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 -	447.37	271.35	10/2017 -	-	15.30
National Highways Authority Of India								
369	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	612.58	612.58	02/2009 -	-	118.78
370	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	-	04/2009 -	-	70.23
371	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 -	435.78	-	11/2008 -	-	159.95
372	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 -	255.23	-	11/2008 -	-	64.62
373	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 -	167.98	270.97	05/2008 -	06/2019	4.99
374	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	655.17	07/2009 -	-	234.27
375	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]	05/2009	1,108.00 -	2,288.00	3,450.00	11/2011 -	-	106.50
376	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	469.54	05/2013 -	-	46.15

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
377	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	489.84	04/2010 -	07/2019	65.82
378	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 -	230.00	370.56	04/2008 -	02/2021	10.58
379	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 -	1,544.00	1,446.45	09/2016 -	-	21.90
380	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 -	2,519.00	4,758.92	06/2015 -	-	16.67
381	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66
382	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	578.00	11/2013 -	-	15.53
383	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	459.07	01/2014 -	-	61.08
384	2-LANING WITH PAVED SHOULDERS OF RAEBARELI-BANDA SECTION OF NH-232 [N24000360]	04/2014	351.34 -	417.68	433.68	01/2016 -	-	18.88
385	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 -	627.93	633.24	01/2016 -	-	26.66
386	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 -	744.73	685.76	05/2018 -	03/2022	40.22
387	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]	10/2015	361.15 -	363.93	277.34	- -	-	.77
388	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 [N24000441]	10/2015	593.26 -	716.78	617.58	05/2018 -	03/2022	20.82
389	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 -	941.00	881.72	- -	01/2020	11.33
390	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) [N24000463]	12/2015	1,083.00 -	1,827.15	989.55	06/2018 -	-	68.71
391	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 -	825.17	764.04	- -	10/2021	1.37
392	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 -	1,601.77	1,393.40	11/2015 -	-	51.83
393	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	489.12	- -	-	6.11
394	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 -	1,182.94	267.10	- -	-	1.33
395	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 -	2,360.65	4,495.94	- -	-	41.78
396	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 -	1,038.56	1,021.63	- -	-	21.50
397	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 -	649.27	643.77	04/2018 -	-	25.80

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
398	MEERUT-BULANDSHAHAHAR - [N24000539]	01/2016	683.24 -	987.94	-	-	-	44.60
399	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 -	2,982.00	276.87	04/2019 -	-	87.84
400	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	353.42	-	08/2021	7.53
401	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 -	486.00	406.73	-	-	6.11
402	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 -	1,588.29	798.71	09/2019 -	-	14.40
403	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61 -	2,280.00	1,367.00	-	-	94.94
404	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	316.60	08/2018 -	-	3.98
405	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82 -	1,727.66	1,691.00	-	-	39.35
406	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]	09/2016	950.69 -	1,108.00	1,462.10	08/2019 -	-	16.55
407	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]	09/2016	1,100.19 -	1,145.31	1,355.00	-	-	4.10
408	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	246.70	-	-	8.35
409	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]	11/2012	605.84 -	722.46	722.46	07/2018 -	-	19.25
410	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]	01/2017	1,251.11 -	1,361.00	441.78	-	-	8.78
411	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]	03/2017	1,184.71 -	1,310.00	1,286.42	03/2020 -	-	10.58
412	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]	03/2017	744.64 -	982.00	-	03/2020 -	-	31.88
413	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]	03/2017	1,030.44 -	1,065.51	-	03/2020 -	-	3.40
414	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]	03/2017	988.34 -	1,043.28	-	03/2020 -	-	5.56
415	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]	03/2017	1,059.73 -	1,071.00	18.75	03/2017 -	-	1.06
416	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]	03/2017	1,098.06 -	1,160.64	-	03/2020 -	-	5.70

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
417	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	430.26	03/2020 -	09/2022	.23
418	TWO-LANING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	74.96	03/2020 -	-	9.38
419	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	962.95	03/2020 -	-	13.97
420	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	1,021.47	03/2020 -	-	10.24
421	6-LANING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 -	2,447.00	2,118.76	03/2020 -	-	18.50
422	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	912.41	03/2020 -	-	41.54
423	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	1,310.52	03/2020 -	-	44.39
424	SIX-LANING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	12/2021	3.95
425	4-LANING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 -	1,993.81	1,116.85	06/2020 -	-	1.78
426	4-LANING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	628.26	09/2017 -	-	9.67
427	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713	12/2017	404.94 -	448.18	462.99	-	08/2021	10.68
428	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 -	276.17	99.20	-	-	.99
429	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 -	1,853.42	14.19	-	-	30.09
430	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	346.17	-	01/2022	11.20
431	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 -	2,400.00	3,368.89	-	11/2021	20.28
432	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 -	2,450.00	2,425.12	-	-	12.50
433	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790	03/2018	1,261.98 -	1,952.20	97.16	-	-	54.69

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
434	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	1,176.70	- -	-	29.35
435	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	1,441.15	- -	-	18.87
436	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	342.39	- -	01/2021	37.71
437	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 -	2,499.00	880.34	03/2021 -	04/2021	63.05
438	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 -	537.17	58.32	- -	-	8.26
439	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	333.72	- -	03/2021	22.44
440	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	299.56	- -	01/2022	5.32
441	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 -	2,169.00	-	- -	-	4.99
442	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	-	- -	-	.12
443	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	143.54	- -	-	46.72
444	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	922.64	353.55	- -	-	15.98
445	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	691.19	- -	-	25.68
446	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	407.00	- -	12/2021	.00
447	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	223.00	- -	11/2022	27.86
448	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	443.00	- -	10/2022	305.58
	Total		87,014.84 -	1,09,020.49	76,296.01			

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
	<u>RURAL DEVELOPMENT</u>							
	<u>Hindustan Steelwork Construction Limited</u>							
449	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2022	2.23
450	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2022	3.96
	Total		352.34 -	362.78	335.17			
	<u>STEEL</u>							
	<u>National Mineral Development Corporation (Nmdc)</u>							
451	NMDC INTEGRATED STEEL PLANT - [N12000086]	01/2010	15,525.00 -	21,940.00	18,779.12	05/2015 -	01/2022	41.32
	<u>Raistriva Ispat Nigam Limited</u>							
452	FORGED WHEEL PLANT - [N12000116]	04/2014	1,682.85 -	2,100.00	1,704.90	09/2018 -	09/2021	24.79
	Total		17,207.85 -	24,040.00	20,484.02			
	<u>TELECOMMUNICATIONS</u>							
	<u>Department Of Telecommunication</u>							
453	NETWORK FOR SPECTRUM - [N26000101]	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	03/2022	84.97
	Total		13,334.00 -	24,664.00	17,845.00			
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							
454	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 -	12,787.00	9,144.21	12/2018 -	08/2022	18.69
	<u>Bangalore Metro Rail Corporation Limited</u>							
455	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]	02/2014	26,405.14 -	30,695.12	18,226.61	02/2019 -	03/2025	16.25
	<u>Central Public Works Department</u>							
456	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	06/2015	197.33 -	217.00	142.78	04/2019 -	02/2022	9.97
	<u>Chennai Metro Rail Ltd</u>							
457	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]	02/2009	14,600.00 -	18,380.00	17,619.68	12/2015 -	-	25.89
	<u>Kochi Metro Rail Corporation Ltd</u>							

Details of Ongoing Projects having Cost Overruns w.r.t. to Original Schedule

(August 2021)								
						Date of Commissioning (Month/Year)		
S.No	Project	Date of Approval (Month/Year)	Original / Revised Cost(Rs crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original/ Revised	Anticipated	Cost Overruns (%)
1	2	3	4	5	6	7	8	9
458	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 -	6,218.14	6,059.17	07/2017 -	-	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>							
459	MUMBAI METRO RAIL LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 -	33,406.00	18,788.65	03/2020 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>							
460	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 -	4,720.73	4,683.08	11/2019 -	-	10.71
	<u>Patna Metro Rail Corporation</u>							
461	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	02/2019	13,365.77 -	13,925.50	258.94	06/2024 -	06/2024	4.19
	Total		97,923.03 -	1,20,349.49	74,923.12			
	WATER RESOURCES							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
462	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 -	413.29	0.05	09/2020 -	-	62.63
463	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 -	398.90	284.90	03/2020 -	03/2021	76.68
	<u>Kolkata Metropolitan Development Authority</u>							
464	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23
	<u>Polavaram Project Authority</u>							
465	POLAVARAM IRRIGATION PROJECT - [N30000002]	02/2009	10,151.04 -	55,548.87	17,935.78	03/2020 -	04/2022	447.22
	<u>Uttar Pradesh Jal Nigam</u>							
466	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022	22.24
467	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]	10/2016	370.40 -	430.49	396.14	08/2020 -	-	16.22
468	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]	02/2011	279.91 -	330.05	244.84	12/2019 -	01/2021	17.91
469	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 -	234.03	-	12/2021 -	12/2021	.97
470	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 -	690.71	-	06/2022 -	06/2022	1.31
	Total		12,606.87 -	58,532.15	18,861.71			
	Grand Total		7,35,952.55	12,07,644.55	695,120.95			

FLASH REPORT

Details of Delayed Projects w.r.t. Original Schedule

Annexure - VI

Costing Rs. 150 Crore and above (August 2021)										
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Date of Commissioning (Month/Year)		Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
						Original / Revised	Anticipated			
1	2	3	4	5	6	7	8	9	10	11
	<u>ATOMIC ENERGY</u>									
	<u>Bhavini Limited</u>									
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]BHAVNI, TAMIL NADU	09/2003	3,492.00 6,840.00	6,840.00	5,986.57	09/2010 10/2022	10/2022	145	95.88	
	<u>Nuclear Power Corporation Of India Limited</u>									
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL, GUJARAT	10/2009	11,459.00 -	16,580.00	17,041.00	12/2015 -	02/2022	74	44.69	
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL, RAJASTHAN	10/2009	12,320.00 -	17,079.00	13,528.00	12/2016	03/2023	75	38.63	
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL, TAMIL NADU	03/2013	39,849.00 -	39,849.00	25,029.00	11/2020 -	11/2023	36	0	
	Total		67,120.00 -	80,348.00	61,584.57					
	<u>CIVIL AVIATION</u>									
	<u>Airport Authority Of India Limited</u>									
5	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPORT - [N04000076]AAI, DELHI	11/2016	303.80 351.21	303.80	180.24	04/2020 -	03/2022	23	0	NIL
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI, ANDHRA PRADESH	08/2017	177.10 -	177.10	98.00	02/2020 06/2021	05/2022	27	0	1. A portion of the site measuring 3.42 acres is fouling in the Runway extension and Basic Strip due to which the work will be further delay 2. High mast transmission towers in the approach path of Runway 08 to be shifted by APTRANSCO (Govt. of AP undertaking) for final commissioning of the Project and this part of the work is yet to physically start. However work order is placed by State Government and agency mobilizing Men, materials & Machinery for the work.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
7	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]AAI, A & N ISLANDS	10/2013	417.23 707.73	707.73	456.88	09/2018 06/2022	06/2022	45	69.63	NIL
8	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]AAI, WEST BENGAL	01/2016	458.00 -	458.00	149.44	03/2020 07/2022	07/2022	28	0	NIL
9	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICATION - [N04000079]AAI, MAHARASHTRA	03/2017	475.39 -	475.39	162.78	04/2021 -	08/2022	16	0	NIL
10	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI, UTTARAKHAND	07/2018	456.86 -	456.86	306.08	09/2020 -	09/2022	24	0	NIL
11	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI, TAMIL NADU	08/2018	951.28 -	951.28	437.28	10/2021 -	10/2022	12	0	NIL
12	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI, LADAKH	07/2018	346.27 -	480.33	105.53	09/2021 -	12/2022	15	38.72	NIL
13	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI, MADHYA PRADESH	06/2016	412.24 -	412.24	204.49	06/2021 -	12/2022	18	0	Diversion of Road Crossing the runway is pending with state Govt. (Amount Deposited by AAI)
14	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI, GUJARAT	01/2018	1,405.00 -	1,405.00	334.66	08/2022 -	12/2022	4	0	1) Doshaliguna & Lomakotadi Village road diversion. 2) Resolving land swapping of Doshaliguna village. 3) Removal of structures of Lomakotadi village coming inside operational area. 4) Relocation of Juna Hirasar village 5) Relocation of wind mills. 6) Land swapping for N.H. expansion & flyover construction.
15	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]AAI, WEST BENGAL	01/2019	389.71 -	389.71	191.88	11/2021 01/2023	01/2023	14	0	2

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
16	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00 -	1,232.00	371.33	03/2021 03/2022	03/2023	24	7.88	Transportation strike from 1st week of November 2020, to end of the month at CEMENT Plant in Govt, of Assam & Meghalaya.
17	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00 -	2,467.00	689.52	02/2022 -	12/2023	22	0	NIL
18	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00 1,938.00	1,383.00	488.53	09/2021 -	12/2023	27	0	
19	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90 -	1,216.90	211.80	10/2022 -	12/2023	14	0	AUGUMENTATION OF STORM WATER DRAINAGE SYSTEM FOR CONNECTING NEW STORM WATER SYSTEM OF AIRPORT WITH ENLARGED CAPACITY.
20	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]AAI,TAMIL NADU	06/2019	380.87 -	380.87	12.79	03/2022 12/2023	12/2023	21	0	NIL
	Total		12,382.65 -	12,897.21	4,401.23					
	<u>COAL</u>									
	<u>Bharat Coking Coal Limited</u>									
21	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45 -	289.45	285.43	05/2014 -	10/2021	89	0	
22	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52 -	555.52	5.87	03/2021 -	03/2022	12	0	
23	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	341.22	64.19	03/2017 -	03/2022	60	12.2	
24	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00 334.27	334.27	24.70	04/2018 -	06/2022	50	37.56	
25	MOONIDIH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27 -	1,230.27	493.13	04/2015 -	02/2023	94	0	
26	MURAIIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88 -	339.88	61.16	04/2014 -	04/2023	108	0	
	<u>Central Coal Fields Limited</u>									
27	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51 -	163.51	124.64	03/2011 -	03/2022	132	0	
28	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85 -	510.85	497.88	03/2016 -	03/2022	72	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
29	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46 -	162.46	89.27	03/2014 -	03/2022	96	0	
30	MAGADH EXPANSION OC(51 MTY) - [N06000015]CCL,JHARKHAND	08/2008	6,964.33 7,254.37	7,254.37	729.50	07/2012 03/2028	03/2028	188	4.16	
31	RECAST EPR AMRAPALI OC - [N06000103]CCL,JHARKHAND	02/2012	4,983.58 4,983.58	4,983.58	258.81	03/2020 03/2028	03/2028	96	0	
	<u>Eastern Coal Fields Limited</u>									
32	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05 -	1,055.05	689.34	03/2018 -	10/2021	43	0	1. Rehabilitation of PAFs: Progress of R&R activity delayed due to disputes among villagers for selection of rehab. site and resistance by villagers in shifting. 2.Expediting the work of tree felling for hand over of 32.65 Ha forest land.

FLASH REPORT

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2021)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
33	RANIGANJ MASTER PLAN - [N06000163]ECL, WEST BENGAL	08/2009	2,661.73	5,146.48	622.13	08/2019	08/2024	60	93.35	i). Publication of final figure of Demographic survey report for Non-ECL houses by ADDA. ii). Publication of valuation of immovable properties for LTH households by ADDA to assess the financial implications for payment of cash compensation to affected beneficiaries. iii). Identification and finalization of balance 33.69 Ha land in non-coal bearing areas for construction of remaining flats in connection with implementation of this rehabilitation project. iv). As per resolution of review meeting taken by Sec(coal), CMPDI, RI-1 has identified land areas both in non-coal bearing and deep-seated coal bearing measures and report was sent to ADDA for utilization in rehabilitation purpose. WB Govt. is examining the status of encumbrance free land areas. Communication in this regard is yet to be received from State authority. v). Furthermore, CMPDI has examined the stability status of 192.74 acres Govt. vested land out of the list submitted by CEO, ADDA. The report was communicated to ADDA to check the encumbrance free status of land areas. Out of this 192.74 acres, ADDA has accepted only 37.23 acres encumbrance free land areas belong to mouza Mahatadih for rehabilitation purpose. The examination of encumbrance free status of balance 155.51 acres vested land areas is under way by concerned Deptt. of WB Govt. However, no updated status on the matter has yet been received from ADDA. vi). Shifting of affected families (on the basis of priority list to be prepared as per vulnerability of

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
34	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]ECL, WEST BENGAL	11/2015	1,210.12 -	1,210.12	49.04	03/2022 03/2029	03/2029	84	0	
	<u>Mahanadi Coal Fields Limited</u>									
35	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL, ODISHA	11/2008	479.53 -	703.39	703.39	03/2013 -	03/2024	132	46.68	
36	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL, ODISHA	05/2014	479.15 -	479.15	226.00	03/2019 -	03/2024	60	0	
37	GARJANBAHAL OCP - [N06000117]MCL, ODISHA	11/2014	1,375.38 -	1,375.38	581.31	03/2021 -	09/2025	54	0	
38	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]MCL, ODISHA	12/2007	8,416.19 8,416.19	8,416.19	918.79	03/2013 03/2028	03/2028	180	0	
39	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]MCL, ODISHA	12/2007	3,504.21 3,504.21	3,504.21	589.67	03/2010 03/2029	03/2029	228	0	
40	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL, ODISHA	12/2007	3,145.45 -	3,145.45	589.39	03/2017 -	03/2031	168	0	
	<u>Neyveli Lignite Corporation</u>									
41	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]NLC, UTTAR PRADESH	07/2016	17,237.00 -	17,237.80	12,346.08	11/2021 11/2022	11/2022	12	0	PPA
42	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC, JHARKHAND	07/2013	1,795.01 -	1,795.01	36.52	08/2022 -	09/2023	13	0	
43	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]NLC, TAMIL NADU	04/2013	1,458.17 709.06	709.06	492.01	06/2015 03/2025	03/2025	117	-51.37	
	<u>Northern Coal Fields Limited</u>									
44	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL, MADHYA PRADESH	05/2017	1,783.09 -	1,783.09	738.88	03/2021 -	03/2022	12	0	
45	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL, MADHYA PRADESH	11/2017	1,255.17 -	1,255.17	230.12	03/2022 -	03/2023	12	0	
	<u>Singareni Colliers Company Limited</u>									
46	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL, TELANGANA	11/2012	430.45 -	415.37	213.44	03/2016 -	09/2021	66	-3.5	
47	KISTARAM OCP - [N06000089]SCCL, TELANGANA	11/2010	242.29 -	164.04	143.08	03/2015 -	03/2022	84	-32.3	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
48	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	283.01	03/2015 -	03/2022	84	114.6	
49	KALYANIKHANI OPENCAS T PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	134.71	07/2016 -	03/2022	68	-7.91	
50	KAKATIYAKHANI OPENCAS T-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	111.66	03/2019 -	03/2022	36	11.42	
51	KAKATIYAKHANI OPENCAS T III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	200.14	03/2019 -	03/2022	36	0	
52	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	16.86	
53	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	96	5.85	
	South-Eastern Coal Fields Limited									
54	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	198.78	03/2015 03/2020	03/2022	84	201.44	
55	AMADAND OPENCAS T EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	126.15	03/2021 -	03/2022	12	0	
56	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	210.73	03/2014 -	03/2023	108	0	
57	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	0	
58	AMGAON OPENCAS T PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	145.17	03/2020 -	03/2023	36	0	
59	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	66.44	03/2021 -	03/2024	36	0	
60	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]SECL,MADHYA PRADESH	12/2014	357.80 -	357.80	100.65	03/2021 04/2024	04/2024	37	0	
61	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	231.92	1.78	03/2022 -	03/2025	36	0	
62	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	11.37	03/2014 -	03/2026	144	0	
63	DURGAPUR OPENCAS T PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
64	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2027	48	0	
65	MADANNAGAR OPENCAST PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	0	
	<u>Western Coal Fields Limited</u>									
66	SINGHORI OC MINE - [N06000130]WCL,MAHARASHTRA	06/2015	205.49 -	205.49	138.58	03/2020 09/2021	09/2021	18	0	
67	NEW MAJRI UG TO OC - [N06000128]WCL,MAHARASHTRA	05/2015	295.56 299.67	299.67	164.36	03/2019 03/2022	03/2022	36	1.39	
68	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 325.18	325.18	272.90	03/2019 -	03/2022	36	63.67	
69	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 327.41	327.41	160.84	03/2019 -	03/2022	36	7.52	
70	KOLAR PIMPRI EXTENSION OC - [N06000160]WCL,MAHARASHTRA	03/2017	362.73 402.90	402.90	336.00	03/2020 09/2022	09/2022	30	11.07	
71	UKNI DEEP OC - [N06000179]WCL,MAHARASHTRA	11/2018	318.14 -	318.14	217.47	03/2021 09/2022	09/2022	18	0	
72	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	102.41	03/2021 -	09/2022	18	0	
73	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	296.56	03/2021 -	09/2023	30	0	
74	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	145.08	03/2023 -	03/2024	12	15.41	
75	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) - [N06000141]WCL,MAHARASHTRA	11/2015	313.34 -	313.34	149.32	03/2021 03/2024	03/2024	36	0	
76	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]WCL,MULTI STATE	09/2016	289.29 -	289.30	36.10	03/2022 03/2025	03/2025	36	0	
77	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]WCL,MAHARASHTRA	11/2015	851.60 826.80	826.80	233.76	03/2020 03/2026	03/2026	72	-2.91	
78	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]WCL,MADHYA PRADESH	07/2016	281.25 -	281.25	18.24	03/2022 03/2026	03/2026	48	0	
79	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]WCL,MAHARASHTRA	11/2014	1,184.33 -	1,184.33	392.88	03/2020 03/2027	03/2027	84	0	
	Total		76,414.36 -	79,515.85	26,614.77					
	<u>FERTILISERS</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	<u>National Fertiliser Limited</u>									
80	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92	215.92	172.01	11/2019 06/2021	10/2021	23	0	
	<u>Rashtriya Chemical & Fertiliser Limited</u>									
81	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]RCF,MAHARASHTRA	04/2018	426.72	426.72	295.13	04/2020 10/2021	10/2021	18	0	
	Total		642.64	642.64	467.14					
	<u>MINES</u>									
	<u>National Aluminum Company Limited (Nalco)</u>									
82	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]NALCO,ODISHA	12/2014	5,540.00 6,435.90	5,540.00	788.26	04/2021 12/2022	12/2022	20	0	
83	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]NALCO,ODISHA	11/2017	483.00 483.00	483.00	2.68	04/2021 03/2023	03/2023	23	0	
	Total		6,023.00	6,023.00	790.94					
	<u>STEEL</u>									
	<u>National Mineral Development Corporation (Nmdc)</u>									
84	NMDC INTEGRATED STEEL PLANT - [N12000086]NMDC,CHHATISGARH	01/2010	15,525.00 21,940.00	21,940.00	18,779.12	05/2015 01/2022	01/2022	80	41.32	
	<u>Raastriya Ispat Nigam Limited</u>									
85	FORGED WHEEL PLANT - [N12000116]RINL,UTTAR PRADESH	04/2014	1,682.85	2,100.00	1,704.90	09/2018 09/2021	09/2021	36	24.79	No
86	COKE OVEN BATTERY-5 - [N12000117]RINL,ANDHRA PRADESH	12/2011	2,858.00	2,858.00	1,995.82	12/2017 07/2022	07/2022	55	0	No
	<u>Steel Authority Of India Limited (Sail)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
87	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]SAIL, WEST BENGAL	12/2018	263.36 -	263.36	253.46	09/2020 09/2021	08/2021	11	0	
88	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL, JHARKHAND	11/2016	262.87 -	262.87	199.74	06/2019 08/2021	10/2021	28	0	
89	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL, JHARKHAND	03/2015	1,034.01 -	1,034.01	549.60	10/2017 12/2021	11/2022	61	0	
	Total		21,626.09 -	28,458.24	23,482.64					
	PETROLEUM									
	<u>Bharat Petroleum Corporation Limited</u>									
90	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT (PDPP) AT KOCHI REFINERY - [N16000227]BPCL, KERALA	11/2014	4,588.29 5,245.96	5,245.96	5,184.50	08/2018 11/2019	09/2021	37	14.33	
91	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL, KARNATAKA	10/2018	206.26 -	206.26	149.39	03/2021 -	10/2021	7	0	
92	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	1,507.24	769.00	06/2019 -	02/2022	32	35.54	
93	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	640.00	346.57	12/2021 -	03/2022	3	0	
94	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	1,472.00	19.44	02/2017 08/2022	08/2022	66	117.11	
95	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL, ANDHRA PRADESH	07/2017	580.20 -	580.20	207.44	02/2021 -	03/2023	25	0	
	<u>Chennai Petroleum Corporation Limited</u>									
96	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	305.00	272.50	08/2020 -	10/2021	14	-27.55	
	<u>Gas Authority Of India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
97	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,622.70	12/2020 -	10/2021	10	-30.59	
98	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	195.40	04/2018 -	12/2021	44	-38.98	
99	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]GAIL,ODISHA	03/2017	1,933.00 -	1,933.00	1,456.60	12/2020 12/2021	12/2021	12	0	
100	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]GAIL,MULTI STATE	03/2017	2,433.00 -	2,433.00	2,147.10	12/2020 12/2021	12/2021	12	0	
101	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]GAIL,MULTI STATE	03/2017	3,437.00 3,048.00	3,048.00	2,009.10	12/2020 12/2021	12/2021	12	-11.32	
102	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]GAIL,WEST BENGAL	03/2017	1,740.00 -	1,740.00	912.00	12/2020 12/2021	12/2021	12	0	
103	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	215.40	08/2020 05/2021	12/2021	16	14.17	
104	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285]GAIL,MULTI STATE	06/2009	2,915.00 5,909.00	5,909.00	3,786.80	12/2012 02/2022	02/2022	110	102.71	
105	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 217.92	217.92	96.60	04/2021 -	03/2022	11	0	
106	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	41.34	02/2021 -	08/2022	18	9.91	
	<u>Hindustan Petroleum Corporation Limited</u>									
107	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	303.40	211.10	03/2021 -	08/2021	5	0	
108	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26 -	249.26	162.09	06/2020 -	09/2021	15	0	
109	120 TMTA NEW LPG PLANT AT BARHI JHARKHAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50 -	161.50	102.16	06/2020 -	09/2021	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
110	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL, ANDHRA PRADESH	09/2019	196.26 -	196.26	92.83	07/2020 -	09/2021	14	0	
111	VISAKH REFINERY MODERNISATION PROJECT - [N16000235]HPCL, ANDHRA PRADESH	07/2016	20,928.00 26,264.00	26,264.00	16,008.48	07/2020 07/2022	07/2022	24	25.5	
112	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]HPCL, MULTI STATE	09/2017	2,677.00 -	3,072.00	2,443.16	06/2021 08/2022	07/2022	13	14.76	
113	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]HPCL, HARYANA	09/2018	520.00 -	520.00	144.71	09/2026 02/2027	02/2027	5	0	
114	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]HPCL, UTTAR PRADESH	03/2019	3,450.20 -	3,450.20	276.62	03/2029 08/2029	08/2029	5	0	
115	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]HPCL, WEST BENGAL	03/2019	5,830.20 -	5,830.20	120.62	03/2031 08/2031	08/2031	5	0	1. Laying of Gas pipeline along across NH-2 Application made by company in August 2020 for laying of Gas pipeline along across NH-2 for 22 km in Hooghly District to National Highway Authority of India. Permission awaited from PD PIU Durgapur NHAI Complex, Durgapur, WB. Assistance is sought for expediting the issue of demand note permissions to lay the CGD pipeline along across NH-2
	<u>Indian Oil Corporation Limited</u>									
116	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	212.00	164.11	01/2021 -	09/2021	8	0	
117	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 319.61	319.61	195.28	06/2020 09/2021	09/2021	15	35.43	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
118	LPG BP PROJECT MOTIHARI - [N16000317]IOCL,BIHAR	05/2018	206.50 -	206.50	147.35	03/2021 09/2021	09/2021	6	0	
119	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00 -	557.00	537.30	02/2020 06/2021	09/2021	19	0	
120	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00 -	690.00	587.17	07/2018 05/2021	10/2021	39	0	
121	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00 -	261.00	176.30	01/2021 -	10/2021	9	0	
122	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10 -	160.10	102.85	02/2020 06/2021	10/2021	20	0	
123	KHARAGPUR LPG BOTTLING PLANT - [N16000300]IOCL, WEST BENGAL	04/2017	163.02 207.36	207.36	122.11	04/2020 10/2021	10/2021	18	27.2	
124	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]IOCL, GUJARAT	10/2017	906.00 -	906.00	327.90	02/2020 10/2021	10/2021	20	0	
125	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00 -	189.00	166.08	01/2021 06/2021	11/2021	10	0	
126	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]IOCL,MULTI STATE	01/2015	1,823.00 3,027.90	3,027.90	2,117.81	03/2021 12/2021	12/2021	9	66.09	
127	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL,ANDHRA PRADESH	08/2018	466.00 -	466.00	280.16	04/2021 12/2021	12/2021	8	0	
128	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL,BIHAR	04/2018	522.00 -	522.00	373.16	03/2021 12/2021	12/2021	9	0	
129	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL,TAMIL NADU	12/2017	466.43 -	466.43	235.77	10/2020 01/2022	01/2022	15	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
130	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]IOCL,TAMIL NADU	05/2016	4,497.00 6,025.00	6,025.00	3,897.13	12/2018 02/2022	02/2022	38	33.98	
131	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]IOCL,HARYANA	10/2018	598.00 -	598.00	391.04	02/2020 02/2022	02/2022	24	0	
132	LPG TERMINAL AT KOCHI - [N16000171]IOCL,KERALA	10/2015	607.06 -	1,236.00	437.75	10/2017 03/2022	03/2022	53	103.6	
133	PARADIP HYDERABAD PIPELINE - [N16000194]IOCL,MULTI STATE	01/2015	2,321.00 3,338.00	3,338.00	2,996.28	12/2020 03/2022	03/2022	15	43.82	
134	LPG BP PROJECT KHORDHA - [N16000283]IOCL,ODISHA	12/2016	161.59 -	161.59	53.22	12/2019 03/2022	03/2022	27	0	
135	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]IOCL,UTTAR PRADESH	08/2017	255.40 -	255.40	90.08	08/2020 03/2022	03/2022	19	0	
136	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50 -	1,297.50	795.89	10/2021 -	03/2022	5	0	
137	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	316.20	116.20	10/2021 03/2022	03/2022	5	0	
138	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]IOCL,HARYANA	01/2019	909.00 -	909.00	416.23	01/2021 03/2022	03/2022	14	0	
139	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	164.69	15.02	07/2021 03/2022	03/2022	8	0	
140	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]IOCL,HARYANA	08/2018	1,636.00 -	1,636.00	862.17	08/2020 04/2022	04/2022	20	0	
141	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT	10/2019	403.00 -	403.00	145.34	12/2021 -	04/2022	4	0	
142	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]IOCL,ODISHA	11/2018	462.30 -	462.30	87.24	09/2021 06/2022	06/2022	9	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
143	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 340.76	340.76	131.80	02/2020 08/2021	07/2022	29	64.91	
144	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]IOCL,HARYANA	12/2018	278.60 -	278.60	63.96	06/2021 07/2022	07/2022	13	0	
145	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	162.73	01/2021 -	08/2022	19	25.57	
146	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]IOCL,BIHAR	12/2017	199.36 -	199.36	48.78	10/2020 08/2022	08/2022	22	0	
147	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]IOCL,ODISHA	05/2019	3,361.00 -	3,361.00	1,977.07	08/2021 09/2022	09/2022	13	0	
148	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	318.80	162.87	08/2021 -	11/2022	15	0	
149	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	355.00	120.72	04/2022 -	02/2023	10	0	
150	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]IOCL,ODISHA	06/2019	371.00 427.00	427.00	25.79	09/2022 03/2023	03/2023	6	15.09	
151	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	1,019.00	85.59	01/2023 -	05/2023	4	0	
152	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	2,281.94	539.26	12/2022 07/2023	07/2023	7	0	
153	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	611.00	89.82	04/2022 -	08/2023	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
154	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	921.00	5.26	09/2023 02/2024	12/2023	3	0	
	<u>Mangalore Refinery And Petrochemicals Limited</u>									
155	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	519.50	03/2020 11/2020	11/2021	20	9.64	
156	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,728.12	12/2019 04/2021	02/2022	26	0	
157	DEVANGONTHI MARKETING TERMINAL - [N16000401]MANGALORE REFIN,KARNATAKA	06/2020	200.00 -	200.00	2.54	06/2023 08/2023	08/2023	2	0	
	<u>Oil & Natural Gas Corporation Limited</u>									
158	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241]ONGC,TAMIL NADU	11/2015	650.82 -	624.35	453.71	03/2019 09/2021	09/2021	30	-4.07	
159	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	205.92	05/2020 08/2021	11/2021	18	21.57	
160	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357]ONGC,MAHARASHTRA	02/2019	2,292.46 -	2,203.71	1,995.31	05/2021 12/2021	12/2021	7	-3.87	
161	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370]ONGC,MAHARASHTRA	05/2019	763.92 -	733.86	791.46	12/2020 12/2021	12/2021	12	-3.93	
162	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359]ONGC,MAHARASHTRA	05/2019	3,660.71 3,740.05	3,740.05	2,997.59	05/2021 01/2022	01/2022	8	2.17	
163	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]ONGC,MAHARASHTRA	03/2011	861.79 1,846.46	2,001.34	1,568.64	05/2013 02/2022	02/2022	105	132.23	
164	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213]ONGC,MAHARASHTRA	12/2015	3,190.69 3,375.90	3,375.90	2,876.04	04/2018 05/2022	05/2022	49	5.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
165	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247]ONGC,ANDHRA PRADESH	03/2016	34,012.00 -	25,090.00	13,580.92	06/2020 06/2022	06/2022	24	-26.23	
166	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358]ONGC,MAHARASHTRA	04/2019	3,228.80 3,976.67	3,976.67	1,307.63	03/2022 05/2023	05/2023	14	23.16	
	<u>Oil India Limited</u>									
167	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	479.91	12/2019 -	08/2021	20	0	
168	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBANI - [N16000356]OIL,ASSAM	06/2016	224.75 222.21	198.00	178.00	08/2020 09/2021	09/2021	13	-11.9	
169	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 652.10	638.60	383.44	02/2020 -	12/2021	22	17.41	
170	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	269.65	10/2020 -	03/2022	17	0	
	Total		1,42,945.11 -	1,50,114.24	87,582.62					
	<u>POWER</u>									
	<u>Chenab Valley Power Projects [P] Limited</u>									
171	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	2,022.77	04/2020 -	07/2025	63	0	
	<u>National Hydro-Electric Power Corporation</u>									
172	PARBATI HEP (4X200 MW) (NHPC) II - [180100210]NHPC,HIMACHAL PRADESH	09/2002	3,919.59 9,897.59	9,897.59	9,164.35	09/2009 03/2023	03/2023	162	152.52	
173	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	19,992.43	14,059.55	09/2010 08/2023	08/2023	155	218.08	
	<u>National Thermal Power Corporation</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
174	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,917.95	07/2012 06/2020	10/2021	111	97.38	Support of State Govt. required for early resolution of acquisition / possession of 42.4355 Acres of critical land balance due to court cases, wrong payments in awarded land and ownership disputes in following areas: Main Plant: 21.372 acres Make-Up water corridor: 0.190 acres Ash Dyke:14.8135 acres Township:6.05 acres De-notification of 17.69 Acres GMM land for Raiyatikaran is critical as construction of Overflow Lagoon of Ash Dyke is held up. The proposal for de-notification is with Revenue Dept. GOB, since 05.02.2020. Report sent by Dist Authorities on 15.12.20.
175	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	401.90	153.54	04/2021 10/2021	10/2021	6	0	
176	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 2,311.89	2,311.89	1,892.27	12/2018 -	11/2021	35	22.64	
177	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	702.28	529.41	03/2021 11/2021	11/2021	8	0	
178	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	633.80	461.33	11/2018 -	12/2021	37	19.66	
179	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	403.62	100.92	06/2021 12/2021	12/2021	6	0	
180	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	1,522.71	894.14	09/2021 10/2022	01/2022	4	0	
181	NPGCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	16,096.71	05/2018 -	02/2022	45	33.47	
182	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	501.29	343.39	09/2021 02/2022	02/2022	5	0	
183	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24 -	798.24	273.17	09/2021 02/2022	02/2022	5	0	
184	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	1,749.31	1,125.51	09/2021 02/2022	02/2022	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
185	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC, TAMIL NADU	03/2020	1,316.22 -	1,316.22	650.94	09/2021 02/2022	02/2022	5	0	
186	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC, RAJASTHAN	03/2020	1,782.00 -	1,782.00	527.71	09/2021 07/2022	09/2022	12	0	
187	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC, TELANGANA	01/2016	10,598.98 10,997.70	10,997.70	8,740.94	11/2020 07/2022	10/2022	23	3.76	
188	NOKHRA - [N18000282]NTPC, UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	340.93	09/2021 07/2022	01/2023	16	0	

FLASH REPORT

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above										(August 2021)
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
189	BARH STPP(3X660MW) NTPC - [180100242]NTPC, BIHAR	02/2005	8,692.97 21,312.11	21,312.11	19,169.37	10/2011 07/2023	07/2023	141	145.16	•Support required for early completion of Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur rail route, which is critical to ease transportation of coal for Barh Project. Readiness of railway line Hazaribagh-Koderma-Tilaiya-Rajgir-Bakhtiyarpur route (250km) is critical to ease transportation of coal for Barh Project. NTPC has funded Rs 664 Crores to Railways for development of following works in envisaged Coal transportation route. •Construction of Karnauti-Bakhtiyarpur flyover. •Construction of Manpur Flyover (ROR) •Electrification of Manpur-Tilaiya-Bakhtiyarpur section. (Charging from Tilaiya sub-station balance) Bakhtiyarpur ROR line: Acquisition of 12.241 Acres supplementary land is under process. Land award has been done. Payment to landowner is in progress. However, few Raiyats are unwilling to accept the compensation as the award has been issued based on reduced circle rate. State Govt support required to Railways for acquisition / possession of said Land. Support of Ministry of Railways is required for timely completion of above works.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
190	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58	15,389.42	12,083.75	06/2019 10/2022	12/2023	54	7.12	Support of State Govt of Jharkhand is required for following: 1.Maintaining Law & order and resolution of following issue: Agitation by villagers for compensation on already awarded land. Raiyats had stopped site works completely w.e.f. 23.02.2021 for demand of additional compensation for already acquired land, which continued till 30.03.2021. Work was started but the workforce strength is still very low, due to fear of another agitation. 2.Acquisition / transfer/ possession of balance land for Ash Dyke and Reservoir. 3.Acquisition of Land by CCL for external CHP. 4.Early completion of Road Widening and strengthening of SH-7 from Hazaribagh to Bijupara. It is being done on deposit basis by RCD. The road diversion in project area needs to be completed on priority. 5.Repair of damaged bridge over Garhi River is critical for transportation of material for project. 6.Forest clearance in ATS lines.
191	RAMMAM-III HEPP (3X40 MW) - [N18000178]NTPC,WEST BENGAL	09/2014	1,381.84	1,381.54	704.78	09/2019 12/2024	12/2024	63	-02	•All inputs as regards to signing of PPA provided to West Bengal Electricity Corporation Limited. WBSECL to take board approval for further submission of proposal to WBSERC. State Govt is not ready to finalize power evacuation line in absence of PPA. •Shifting of balance Homesteads from Project area. (11Nos + 01 School).

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
192	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,073.68	03/2023 -	02/2025	23	-8.34	Support requested for resolving inter-ministerial issues. 1.Revision of the Banhardih Coal Mine development milestone schedules and funding arrangement. 2.Readiness of Start-up power and ATS matching with commissioning schedule of the project Expedition Award of construction of power evacuation and start up power line is required. 3.Transfer of balance land.
	Power Grid Corporation Of India Limited									
193	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	11,641.93	11/2019 07/2021	09/2021	22	0	
194	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	1,931.39	1,783.23	02/2020 09/2021	09/2021	19	0	
195	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,029.93	07/2020 12/2020	10/2021	15	14.11	
196	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	158.03	07/2019 07/2021	10/2021	27	17.99	
197	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	259.50	05/2020 08/2021	10/2021	17	0	
198	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	235.53	155.39	06/2019 11/2021	11/2021	29	0	
199	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	252.99	04/2016 12/2017	12/2021	68	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
200	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]PGCIL,MULTI STATE	05/2014	522.29 546.36	546.36	480.43	11/2016 12/2021	12/2021	61	4.61	
201	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.28	03/2018 -	12/2021	45	0	
202	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]PGCIL,DELHI	03/2015	1,394.52 -	1,394.52	554.29	05/2017 12/2021	12/2021	55	0	
203	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	235.59	12/2019 09/2021	12/2021	24	0	
204	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	204.09	02/2019 09/2021	02/2022	36	0	
205	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	3,068.24	12/2018 12/2021	03/2022	39	31.08	
206	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]PGCIL,MULTI STATE	02/2009	11,130.19 14,719.10	14,719.10	12,953.79	08/2013 11/2022	08/2022	108	32.24	
207	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	9,129.32	2,480.78	12/2018 03/2024	03/2024	63	92.02	
	<u>Satluj Jal Vidyut Nigam Limited</u>									
208	NAITWAR MORI HEP - [N18000265]SJVN,UTTARAKHAND	10/2017	648.33 -	947.89	657.62	12/2021 06/2022	06/2022	6	46.2	1. Stay imposed by Hon'ble High Court of Uttarakhand on all construction activities within 200 m of the river. 2. Agitation by locals in project area. 3. Delay due to Covid-19 pandemic. 4. Geological challenges. 5. Change in Design and scope of work.
	<u>Thdc India Limited</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
209	AMELIA COAL MINE - [N18000252]THDCIL,MADHYA PRADESH	01/2017	2,104.21	1,587.16	592.99	09/2020 08/2022	08/2022	23	-24.57	1. Te nancy/Private land (337.35 Ha): 12 out of 53 cases involving about 400 land losers pending in Court of Collector, Singrauli due to which distribution of Compensation is delayed. 3. Govt. land of Coal Block (178.13 Ha): Collector, Singrauli informed that permission under section 247 shall be accorded after grant of Mining Lease which is already submitted by THDCIL to Collector, Singrauli on 25.08.21.
210	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 4,825.60	4,825.60	4,170.24	02/2016	06/2023	88	191.23	Pending signing of Lease Deed with GoUK for existing 3 Ha. Land at Asena Quarry after permission of extension of mining lease received on 19.04.21 from GoUK and Allotment of additional 4.916 Ha. Land for mining at Asena Quarry by GoUK.
211	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	2,271.34	06/2013 11/2018	06/2024	132	54.94	Regular support on law & order issues is required from GoUK/ District Administration, Chamoli.
212	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42	11,089.42	2,347.19	09/2023	08/2024	11	0	- Continuous help of District administration is required for expeditious land acquisition. - Continuous help of District administration is required for expeditious shifting of Nagla residents to newly identified land.
	Total		1,66,780.39	2,23,457.09	1,49,714.98					
	HEALTH AND FAMILY WELFARE									
	Central Public Works Department									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
213	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29	150.29	52.74	03/2020	12/2021	21	0	
214	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00	195.00	16.41	09/2020	04/2022	19	0	
215	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00	260.00	25.38	06/2021	05/2022	11	0	
HLI Infra Tech Services Limited										
216	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00	715.06	574.62	04/2020	10/2021	18	-8.91	
217	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00	557.48	513.24	06/2020	10/2021	16	-20.7	
218	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00	747.80	387.54	05/2021 09/2022	09/2022	16	-14.54	
Hospital Services Consultancy Corporation Ltd										
219	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11	655.58	561.94	11/2013	09/2021	94	58.31	
220	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC,WEST BENGAL	08/2017	355.15	355.15	313.77	03/2019	09/2021	30	0	
221	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99	363.99	246.43	05/2018	03/2022	46	0	
National Building Construcion Corporation Ltd										
222	AIIMS BILASPUR - [N21000028]NBCC,HIMACHAL PRADESH	04/2018	1,351.00	1,471.00	814.67	09/2021	06/2022	9	8.88	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
	Total		5,452.54	5,471.35	3,506.74					
	<u>RAILWAYS</u>									
	<u>Central Railways</u>									
223	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50	4,794.60	2,831.83	03/2021	03/2023	24	111.08	
224	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89	910.93	352.67	03/2021	03/2023	24	14.89	
225	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19	1,283.49	479.21	03/2022	03/2023	12	.89	
226	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02	540.02	352.20	03/2022	03/2024	24	0	
227	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91	2,449.91	433.66	03/2023	03/2024	12	0	
228	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16	1,035.16	292.56	03/2022	03/2024	24	0	
229	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95	637.95	199.88	03/2023	03/2024	12	0	
	<u>East Central Railways</u>									
230	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88	751.55	714.87	03/2012	09/2021	114	57.27	
231	HAJIPUR - BACHAWARA - [N22000334]ECR,MULTI STATE	05/2015	678.54	929.86	863.90	03/2019	12/2021	33	37.04	
232	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57	528.57	223.40	03/2019	03/2022	36	0	Land acquisition
233	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23	390.00	366.22	03/2021	03/2022	12	11.99	
234	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73	1,070.00	1,076.60	03/2012	11/2022	128	229.5	
235	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00	819.01	538.55	03/2020	03/2023	36	49.45	land acquisition
236	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR,BIHAR	12/2015	1,200.20	1,200.20	970.88	03/2020	03/2023	36	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
237	RAMPUR DUMRA - TAL - RAJENDRAPUR DOUBLING INCLUDING GANGA BRIDGE - [N22000350]ECR,BIHAR	12/2015	1,491.47 -	1,491.47	543.60	03/2020 03/2023	03/2023	36	0	
238	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,283.84	03/2020 -	03/2024	48	0	
239	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	1,215.54	488.59	03/2021 03/2024	03/2024	36	63.37	
240	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	1,185.73	269.99	03/2021 03/2024	03/2024	36	62.06	
	<u>East Coast Railway</u>									
241	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	1,539.28	1,186.14	02/2019	12/2021	34	38.43	
242	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	238.03	222.65	03/2020	03/2022	24	52.77	
243	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]ECOR,CHHATISGARH	12/2012	1,160.00 1,160.83	1,160.83	988.59	03/2020 03/2023	03/2023	36	.07	
244	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	1,547.38	678.19	03/2022 03/2023	03/2023	12	0	
245	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	843.04	248.28	10/2020 03/2024	03/2024	41	0	
246	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	2,499.71	727.14	03/2022 03/2024	03/2024	24	0	
247	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	810.02	192.59	11/2018 03/2024	03/2024	64	15.45	
248	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	1,172.92	653.15	12/2018 03/2024	03/2024	63	0	
249	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	1,928.07	895.94	06/2021 03/2025	03/2025	45	137.8	
250	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	3,791.66	1,602.15	03/2009 03/2026	03/2026	204	29.71	
251	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	2,361.74	450.42	03/2022 -	03/2026	48	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
	<u>Eastern Railways</u>									
252	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	1,425.44	638.19	02/2013 -	03/2024	133	134.8	
253	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	906.00	03/2019 12/2009	03/2025	72	36.22	Land Acquisition – 1. Acquisition of land in stretch of 3.30 KM between Kamarpukur and Jairambati in Hooghly district is pending for possession to Railway. 2. Villagers of Vill - Bhabadighi, Hooghly District, are not allowing to work over a pond namely Bhabadighi between Goghat and Kamarpukur. 3. Tarakeswar to Dhaniakhali (19 Km) New line, Arambagh – Irphala (18.3 Km) New line, Irphala – Ghatal (11.2 Km) New line and Arambagh – Champadanga (23.30 Km) New line -- Work could not be started due to non - availability of land.
254	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	1,001.66	12/2010 -	03/2025	171	-1.36	Govt. of West Bengal to deposit Rs. 238.75 Cr. for their balance share of cost towards project Katwa-Bardhaman G.C.
255	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	34.08	Land is required for execution of the MM projects.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
256	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98	2,137.81	409.74	03/2022	03/2025	36	133.39	1. Jharkhand & Bihar Government to expedite land acquisition. Milestones may be set only after physical possession of land. 2. Jharkhand Govt. is to deposit Rs. 168.52 Crs. as share of expenditure incurred in this project upto Sept'2020.
257	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52	995.10	614.44	03/2016	03/2025	108	7.75	1 Krishnanagar City (Dhubulia) – Charatala (13.00KM) New line, Krishnanagar – Chapra (19.2 KM) New line Work could not be started due to non – availability of land. 2 Krishnanagar – Nabadwipghat (12.2 KM) Gauge Conversion— (Section Krishnanagar – Amghata) could not be commissioned due to 41 nos. of unauthorized crossings Amghata to Nabadwipghat work is dropped vide Bd's letter No. 2020/W- I/Compliance in Bd Mtg, dated 09.10.2020
258	CHINPAI- SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51	769.40	97.40	03/2017	03/2025	96	29.2	Suri – Prantik New Line (33.90 Km).- The land acquisition details for 250.627 Hectares, submitted to Govt. of West Bengal.
259	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28	266.32	197.54	03/2016	03/2025	108	-3.95	For Bira - Chakla (11.50) New line- The work will start after acquisition and handing over of land by State Government.

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
260	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	439.30	454.56	03/2017 -	03/2025	96	20.3	Baruipara – Furfura (12.30 km) New line - Work could not be started due to non-availability of land.
261	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240	.01	Budge Budge to Pujali (11.00 km) New Line, Pujali – Uluberia (Birshivpur) (10.25 Km) New Line and Pujali – Bakrahat (9.75 Km) New line-- Work could not be started due to non availability of land
262	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	157	36.15	Sangrampur – Krishanchandpur (25 Km) New Line, Diamond Harbour (Gurudasnagar) – Bahrahat (21 Km) New Line and Daimond Harbour (Gurudasnagar) - Kulpi (17.25 Km) New Line: Work could not be started due to non availability of land.
263	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	257.42	108.87	03/2014 -	03/2025	132	0	226.542 acres of land required to be acquired for the MM work.
264	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	12.02	
	<u>Indian Railway Construction Company Limited</u>									
265	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON,CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,666.33	09/2018 -	06/2022	45	0	Agitation by Land losers.
266	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON,CHHATISGARH	02/2014	2,288.00 -	4,970.11	962.98	03/2022 -	09/2023	18	117.23	
267	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-81.5	
	<u>Metropolitan Rapid Transport Projects</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
268	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	2,980.41	1,821.99	03/2004 -	03/2022	216	501.57	
269	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]MRTP,TAMIL NADU	04/2006	495.74 -	734.01	472.27	06/2013 07/2022	07/2022	109	48.06	
	<u>North Central Railway</u>									
270	JHANSI BINA DOUBLING - [N22000496]NCR,UTTAR PRADESH	09/2016	2,001.00 -	2,001.00	948.08	03/2021 12/2022	12/2022	21	0	
271	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]NCR,MULTI STATE	04/2011	2,912.96 -	3,845.60	303.16	03/2022 12/2024	12/2024	33	32.02	
272	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	63.56	03/2023 -	06/2025	27	0	
	<u>North East Frontier Railway</u>									
273	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,825.94	12/2008 -	09/2021	153	284.8	
274	AGARTALA-AKHAURA NL - [N22000195]NFR,TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	30.26	
275	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	1,873.21	1,397.73	03/2021 -	03/2022	12	115.07	
276	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	1,105.00	858.45	03/2019 -	03/2023	48	186.86	
277	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	2,950.00	1,758.52	03/2022 -	03/2023	12	32.15	
278	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	12,264.15	11,303.51	03/2011 -	12/2023	153	175.34	
279	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	8,600.00	1,656.02	12/2015 12/2023	12/2023	96	542.04	
280	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	219.14	03/2019 -	12/2023	57	13.6	
281	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	2,145.00	1,014.54	03/2019 -	03/2024	60	302.54	
282	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	4,169.01	03/2014 -	03/2024	120	130.69	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
283	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52	6,911.00	1,300.10	03/2015	03/2026	132	197.05	
	<u>North Eastern Railway</u>									
284	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00	213.35	53.51	04/2016	12/2021	68	.16	
285	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00	580.00	521.43	01/2019	02/2022	37	96.61	
286	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER,UTTAR PRADESH	04/2016	600.00	366.71	254.12	01/2022	03/2022	2	-38.88	
287	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90	276.90	-	04/2017	04/2022	60	0	
288	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00	341.66	-	04/2017	10/2022	66	127.77	
289	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00	1,277.06	-	01/2022	03/2025	38	-32.79	
	<u>North Western Railway</u>									
290	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18	480.00	371.38	03/2020	09/2021	18	14.24	
291	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08	860.41	745.83	02/2019	06/2022	40	109.82	
292	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00	701.81	261.79	03/2020	10/2022	31	16.97	
293	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85	808.85	275.78	08/2022	11/2022	3	0	
	<u>Northern Railway</u>									
294	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00	27,949.00	25,191.80	11/2002	12/2022	241	1017.96	
295	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00	2,200.00	-	07/2012	03/2024	140	388.89	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
296	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00	404.00	190.00	08/2016	08/2025	108	0	
	<u>Rail Vikas Nigam Ltd.</u>									
297	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68	950.00	741.79	03/2016	12/2021	69	50.15	
298	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48	2,725.00	2,249.00	03/2020	12/2021	21	281.93	
299	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04	2,009.00	1,532.13	03/2020	12/2021	21	111.91	
300	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02	1,300.00	1,152.05	03/2020	12/2021	21	-7.28	
301	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85	1,835.83	1,270.60	12/2020	12/2021	12	23.55	
302	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66	1,868.89	1,462.02	12/2021	03/2022	3	20.68	
303	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71	3,377.00	2,152.52	03/2020	03/2022	24	124.58	
304	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70	2,440.53	1,066.19	02/2015	06/2022	88	102.92	
305	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01	1,400.00	1,233.65	03/2019	06/2022	39	51.02	
306	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95	1,536.00	1,054.76	03/2019	06/2022	39	62.89	
307	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25	1,825.00	1,266.69	12/2020	12/2022	24	54.24	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
308	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60	1,000.00	544.48	03/2022	12/2024	33	5.98	
309	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92	1,765.92	746.29	03/2023	12/2024	21	0	
310	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL, WEST BENGAL	04/2010	3,951.98	4,259.48	2,453.42	03/2016	03/2025	108	7.78	
311	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL, WEST BENGAL	04/2010	2,913.51	4,639.00	888.31	03/2016	03/2025	108	59.22	
312	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL, UTTARAKHAND	04/2011	16,216.00	22,716.11	2,045.67	12/2024	03/2025	3	40.08	
313	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL, WEST BENGAL	04/2010	2,298.42	2,733.86	40.46	03/2014	12/2025	141	18.95	
314	VIZIANAGARAM - SAMABALPUR 3RD LINE - [N22000409]RVNL, ODISHA	01/1991	2,335.67	3,327.72	794.54	12/2024	12/2026	24	42.47	
	<u>South Central Railway</u>									
315	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR, MULTI STATE	04/2010	704.31	927.94	656.85	03/2020	11/2021	20	31.75	
316	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR, TELANGANA	04/2017	119.73	449.39	7.09	03/2022	12/2022	9	275.34	
317	MUNEERABAD-MAHABOBNAGAR(NL), SCR - [220100205]SCR, MULTI STATE	04/1997	1,723.00	3,421.35	1,989.23	03/2000	03/2023	276	98.57	
318	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR, ANDHRA PRADESH	12/2001	1,045.20	2,120.16	1,009.94	03/2009	03/2024	180	102.85	
319	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR, TELANGANA	04/2006	1,160.48	1,160.48	631.65	03/2010	03/2024	168	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
320	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	684.12	03/2023 -	03/2024	12	5.16	
321	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,277.06	03/2021 -	03/2024	36	15.49	
322	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,530.08	03/2021 -	03/2024	36	0	
323	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,239.48	03/2022 -	03/2024	24	7.06	
324	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	348.32	03/2014 -	03/2027	156	42.44	
<u>South East Central Railway</u>										
325	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT - [N22000438]SECR,MADHYA PRADESH	04/2010	585.93 1,268.32	1,268.32	1,058.10	02/2019 12/2021	12/2021	34	116.46	
326	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]SECR,MAHARASHTRA	09/2016	1,908.51 3,176.60	3,176.60	1,334.01	03/2023 12/2023	12/2023	9	66.44	
327	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]SECR,CHHATISGARH	04/2015	1,973.00 2,135.34	2,135.34	648.00	03/2021 12/2023	12/2023	33	8.23	
328	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	-	12/2021 -	12/2023	24	.07	
329	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]SECR,MAHARASHTRA	06/2018	229.00 1,096.00	1,096.00	40.47	12/2021 12/2024	12/2024	36	378.6	
<u>South Eastern Railway</u>										
330	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	358.68	316.37	12/2018 -	08/2021	32	38.92	
331	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.96	1,018.29	03/2020 -	02/2022	23	35.38	
332	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	896.81	03/2021 -	12/2023	33	0	
333	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	54.99	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
334	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER, WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	130.97	
	<u>South Western Railway</u>									
335	YELAHANKA-PENUKONDA - [N22000328]SWR, MULTI STATE	05/2015	860.43 -	1,147.00	945.81	03/2020 -	09/2021	18	33.31	
336	ARSIKERE-TUMKUR - [N22000332]SWR, KARNATAKA	03/2015	578.00 -	760.00	639.39	03/2020 11/2021	11/2021	20	31.49	
337	HUBLI- CHIKJAJUR - [N22000325]SWR, KARNATAKA	03/2015	1,156.94 -	1,800.59	1,128.98	03/2020 -	03/2023	36	55.63	
338	MARIKUPPAM - KUPPAM - [N22000308]SWR, KARNATAKA	04/2012	279.54 -	279.54	36.82	03/2016 -	12/2023	93	0	
339	BANGLORE - SATYAMANGALAM (NL) (SWR) - [220100274]SWR, KARNATAKA	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	264	41.74	
340	SHIMOGA-HARIHAR NL - [N22000278]SWR, KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	0	
341	HOTGI-KUDGI-GADAG - [N22000333]SWR, MULTI STATE	03/2015	1,614.59 1,877.81	1,878.00	1,457.95	03/2019 -	03/2024	60	16.31	
342	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR, KARNATAKA	03/1996	644.78 889.00	731.77	465.72	03/2017 -	03/2025	96	13.49	
343	GADAG-WADI NL - [N22000299]SWR, KARNATAKA	04/2013	2,841.84 -	2,841.84	362.40	12/2018 -	06/2025	78	0	
344	BAGALKOT-KUDACHI NL - [N22000258]SWR, KARNATAKA	04/2010	986.30 -	1,530.09	311.40	03/2016 -	12/2026	129	55.13	
	<u>Southern Railway</u>									
345	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR, TAMIL NADU	02/1996	268.87 -	950.00	920.84	03/2005 -	09/2021	198	253.33	
346	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR, TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-23.24	
347	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR, TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	102.11	
348	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR, TAMIL NADU	09/1995	303.98 -	1,720.00	704.89	03/2020 -	03/2025	60	465.83	
349	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR, TAMIL NADU	09/2007	724.69 -	2,950.00	1,644.43	02/2019 -	03/2025	73	307.07	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
350	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	0	
351	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	273.27	03/2019 -	12/2027	105	1699.64	
	<u>West Central Railway</u>									
352	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	0	
353	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	415.54	03/2022 -	03/2023	12	114.32	
354	RAMGANJ MUNDI-BHOPAL (NL), WCR - [220100314]WCR,MADHYA PRADESH	04/2001	424.60 -	2,909.99	1,282.25	03/2021 03/2024	03/2024	36	585.35	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
355	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93	2,470.00	1,244.18	03/2020	03/2024	48	40.03	Work is suffering badly on this Critical project due pending forest land clearance. The detail position is as under: ¿ Niwas Road to Deoragram: Forest land 46.067 Ha from Railway Km 1261 to 1301 under DFO Singrauli in isolated patches. Application has been uploaded on Sep'2018. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 2055 Nos. trees cutting have been submitted on 18.06.2020 and 21.07.2020. However, APCCF/Bhopal vide letter dated 31.07.2020 has sought clarifications from MOEF. MOEF vide letter dated 24.09.2020 has clarified that case need to be processed further in FCA. GM/WCR vide letter dated 09.10.2020 has requested Railway Board to intervene in this matter. A meeting was held in Collector Singrauli office on 12.12.20. This meeting was chaired by Hon'ble MP/ Sidhi Smt Riti Pathak. Collector Singrauli has been requested to expedite this proposal. ¿ Vijaysota to Beohari: Forest Land 66.69 Ha under DFO Shahdol from Rly Km 1162 to 1189 in isolated patches. Application has been uploaded in Feb'2019. As per letter of Principal Secretary MP State Forest deptt dated 4.6.20, approval under Forest act 1980 is not required for Railway land possessed before 1980. As per discussion with APCCF/ Bhopal, proposals for permission of 17454 Nos trees cutting have been submitted on 18.08.2020

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
356	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66	8,248.50	2,131.17	05/2008	03/2025	202	3230.57	
	<u>Western Railway</u>									
357	DABHOI-CHANDOD (17.07KM) - GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84 811.60	890.62	812.08	03/2020 09/2021	09/2021	18	28.73	
358	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51 724.70	890.76	773.12	03/2019 10/2021	10/2021	31	61.51	
359	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15 1,125.53	1,383.69	1,199.84	03/2021 12/2022	12/2022	21	33.41	
360	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39 1,002.39	1,002.39	730.07	03/2021 12/2022	12/2022	21	0	
361	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26 1,524.68	1,524.68	974.69	03/2022 03/2023	03/2023	12	13.17	
362	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04 1,873.10	1,873.10	869.58	03/2022 03/2023	03/2023	12	14.21	
363	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66 858.96	1,378.11	555.49	03/2019 03/2023	03/2023	48	329.77	
364	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00 603.69	603.69	314.13	06/2020 03/2023	03/2023	33	-13.76	
365	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24 321.62	321.62	126.36	03/2012 10/2023	10/2023	139	1.06	
366	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69 5,839.02	6,171.08	2,301.98	03/2022 03/2024	03/2024	24	76.13	
367	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74 1,246.59	1,886.76	1,875.42	03/2020 03/2024	03/2024	48	127.39	
	Total		1,94,023.99	3,21,095.00	1,52,587.39					
	<u>ROAD TRANSPORT AND HIGHWAYS</u>									
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
368	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH,UTTARAKHAND	12/2017	248.22 -	248.22	234.12	12/2019 08/2021	08/2021	20	0	
369	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	728.55	10/2019 -	08/2021	22	0	
370	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931]MoRTH,ANDHRA PRADESH	11/2016	290.15 -	290.15	136.41	05/2017 08/2021	08/2021	51	0	
371	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALAT JUNCTION) TO KM 420.800(P - [N24000963]MoRTH,ANDHRA PRADESH	01/2018	418.03 381.75	418.03	323.62	08/2018 08/2021	08/2021	36	0	
372	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]MoRTH,ANDHRA PRADESH	03/2016	444.84 -	444.84	345.48	09/2016 08/2021	08/2021	59	0	
373	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH,NAGALAND	03/2017	217.35 -	217.35	97.62	11/2020 08/2021	08/2021	9	0	
374	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	237.08	09/2020 -	08/2021	11	0	
375	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	445.35	01/2020 06/2021	09/2021	20	0	
376	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	765.48	02/2020 04/2021	09/2021	19	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
377	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH,UTTARAKHAND	02/2018	418.88 -	418.88	287.56	02/2020 09/2021	09/2021	19	0	
378	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	173.41	154.26	08/2018 08/2021	09/2021	37	4.33	
379	UPGRADATION OF PACHORE-SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH,MADHYA PRADESH	11/2017	184.62 -	184.62	125.42	02/2018 09/2021	09/2021	43	0	
380	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH,MADHYA PRADESH	03/2018	217.22 -	226.88	173.03	08/2018 09/2021	09/2021	37	4.45	
381	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	232.63	09/2019 06/2021	09/2021	24	0	
382	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940]MoRTH,ANDHRA PRADESH	03/2016	995.09 995.00	995.09	560.85	05/2016 09/2021	09/2021	64	0	
383	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH,NAGALAND	10/2016	167.62 -	167.62	104.39	12/2020 09/2021	09/2021	9	0	
384	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH,NAGALAND	10/2016	172.63 -	172.63	129.65	12/2020 09/2021	09/2021	9	0	
385	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	188.80	87.05	05/2019 09/2021	09/2021	28	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
386	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	379.16	313.04	11/2017 09/2021	09/2021	46	0	
387	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 237.80	238.00	148.90	11/2019 10/2021	10/2021	23	.08	
388	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	162.56	137.02	03/2018 10/2021	10/2021	43	0	
389	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021	25	0	
390	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	233.04	165.60	03/2018 10/2021	10/2021	43	0	
391	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	379.29	03/2018 06/2021	10/2021	43	9.23	
392	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	142.81	08/2020 -	10/2021	14	0	
393	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	335.32	275.33	06/2017 10/2021	10/2021	52	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
394	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTION - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	423.79	289.08	01/2018 10/2021	10/2021	45	0	
395	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	279.44	203.95	03/2018 11/2021	11/2021	44	0	
396	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	615.21	07/2018 05/2021	11/2021	40	0	
397	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937]MoRTH,ANDHRA PRADESH	03/2018	289.67 274.73	289.67	206.00	08/2018 11/2021	11/2021	39	0	
398	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	264.50	106.37	03/2021 11/2021	11/2021	8	0	
399	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	992.67	890.74	03/2011 12/2021	12/2021	129	58.98	
400	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021	134	69.3	
401	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	377.99	368.39	10/2010 12/2021	12/2021	134	93.8	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
402	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	282.08	201.79	06/2019 12/2021	12/2021	30	0	
403	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021	19	0	
404	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	126.89	03/2017 06/2021	12/2021	57	0	
405	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	198.83	07/2018 08/2021	12/2021	41	0	
406	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	741.88	06/2019 04/2021	12/2021	30	0	
407	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932]MoRTH,ANDHRA PRADESH	01/2017	319.28 -	319.28	188.42	08/2017 12/2021	12/2021	52	0	
408	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934]MoRTH,ANDHRA PRADESH	03/2018	228.32 202.83	228.32	135.54	08/2018 12/2021	12/2021	40	0	
409	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964]MoRTH,ANDHRA PRADESH	08/2016	350.61 -	350.61	324.60	01/2017 12/2021	12/2021	59	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
410	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]MoRTH,ANDHRA PRADESH	11/2016	376.25 -	376.25	310.33	08/2017 12/2021	12/2021	52	0	
411	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANI KALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	536.65	550.22	12/2019 12/2021	12/2021	24	0	
412	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	322.24	304.71	09/2014 12/2021	12/2021	87	72.36	
413	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	189.09	04/2020	12/2021	20	-8.28	
414	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	160.68	08/2020	12/2021	16	0	
415	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	544.00	400.49	09/2016 12/2021	12/2021	63	14.24	
416	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	731.50	460.02	10/2016 12/2021	12/2021	62	17.04	
417	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	426.18	254.29	09/2020 01/2022	01/2022	16	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
418	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH, WEST BENGAL	03/2016	271.17 291.20	291.20	120.14	11/2018 01/2021	03/2022	40	7.39	
419	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH, MADHYA PRADESH	11/2017	254.17 -	254.17	175.37	02/2018 03/2022	03/2022	49	0	
420	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH, CHHATISGARH	12/2014	496.02 -	496.02	240.54	03/2015 03/2022	03/2022	84	0	
421	REHABILITATION AND UPGRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH, MADHYA PRADESH	02/2018	169.63 -	169.63	52.44	03/2018 04/2021	04/2022	49	0	
422	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]MoRTH, ANDHRA PRADESH	01/2017	576.48 596.38	576.48	369.63	01/2018 04/2022	04/2022	51	0	
423	REHABILITATION AND UPGRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH, ANDHRA PRADESH	03/2020	207.79 -	207.79	-	03/2021 -	04/2022	13	0	
424	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH, ASSAM	11/2010	268.08 -	390.73	318.85	05/2017 05/2022	05/2022	60	45.75	
425	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]MoRTH, ANDHRA PRADESH	01/2017	263.45 381.75	263.45	116.24	09/2017 05/2022	05/2022	56	0	
426	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH, MADHYA PRADESH	03/2018	214.69 -	214.69	78.48	03/2018 09/2021	06/2022	51	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
427	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	572.66	278.09	08/2016 06/2022	06/2022	70	15.19	
428	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	263.26	72.02	08/2019 08/2022	08/2022	36	11.18	
429	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FROM - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	42.41	08/2020 -	08/2022	24	0	
430	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	26.72	08/2019 -	11/2022	39	33.51	
431	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	28.61	11/2020 -	11/2022	24	-12	
432	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	387.81	08/2017 06/2021	12/2022	64	0	
433	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	435.61	107.15	07/2016 12/2022	12/2022	77	-3.83	
434	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	166.94	28.02	12/2020 12/2022	12/2022	24	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
435	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	-	05/2021 -	12/2022	19	0	
436	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	-	03/2021 -	03/2023	24	0	
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
437	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	54	0	
438	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	36	-18.09	
439	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	168.39	145.72	11/2018 -	11/2021	36	0	
440	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	237.72	120.12	09/2018 -	11/2021	38	0	
441	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	251.97	146.10	09/2018 -	11/2021	38	0	
442	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	282.98	153.26	09/2018 -	11/2021	38	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
443	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	107.31	09/2018 -	11/2021	38	0	
444	4 LANING OF JORHAT TO JHANJHI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	105.09	06/2018 -	12/2021	42	0	
445	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL,ASSAM	06/2015	463.49 -	463.49	159.34	06/2018 -	12/2021	42	0	
446	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM. 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL,ASSAM	12/2015	289.99 -	289.99	87.90	12/2018 -	12/2021	36	0	
447	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL,NAGALAND	03/2018	315.03 -	315.03	101.42	09/2018 -	12/2021	39	0	
448	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL,NAGALAND	03/2018	240.64 -	240.64	112.90	09/2018 -	12/2021	39	0	
449	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL,NAGALAND	03/2018	215.79 -	215.79	70.57	09/2018 -	12/2021	39	0	
450	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL,SIKKIM	11/2017	290.05 -	290.05	119.27	11/2017 -	12/2021	49	0	
451	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744]NHIDCL,A & N ISLANDS	03/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022	39	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
452	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL,ASSAM	10/2014	588.95 -	588.95	494.25	11/2018 -	02/2022	39	0	
453	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL,ASSAM	05/2015	454.89 -	454.89	328.55	05/2018 -	03/2022	46	0	
454	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL,ASSAM	01/2016	294.17 -	294.17	215.45	01/2016 -	03/2022	74	0	
455	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL,ASSAM	01/2016	252.00 -	252.00	136.88	01/2016 -	03/2022	74	0	
456	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL,ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	157.65	04/2017 03/2021	03/2022	59	0	
457	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL,ARUNACHAL PRADESH	02/2017	195.23 -	252.79	133.92	04/2017 -	03/2022	59	29.48	
458	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL,ARUNACHAL PRADESH	02/2017	203.36 -	263.31	145.13	04/2017 -	03/2022	59	29.48	
459	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL,ARUNACHAL PRADESH	01/2017	198.22 -	252.05	144.26	04/2017 -	03/2022	59	27.16	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
460	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL,UTTARAKHAND	03/2018	274.31 -	274.31	208.47	05/2018 -	03/2022	46	0	
461	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL,UTTARAKHAND	03/2018	403.36 -	403.36	330.75	06/2018 -	03/2022	45	0	
462	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL,UTTARAKHAND	03/2018	417.24 -	417.24	325.44	05/2018 -	03/2022	46	0	
463	2 LANE WITH HARD SHOULDER, REHABILITATION AND UPGRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL,A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51	0	
464	REHABILITATION AND UPGRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL,A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41	0	
465	REHABILITATION AND UPGRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL,A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41	0	
466	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL,NAGALAND	02/2017	387.00 -	387.00	309.45	09/2018 -	03/2022	42	0	
467	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL,ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
468	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL, MEGHALAYA	03/2019	306.28 -	306.28	117.91	05/2019 -	03/2022	34	0	
469	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	112.70	09/2018 -	05/2022	44	0	
470	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL, NAGALAND	03/2018	339.57 -	339.57	161.84	09/2018 -	07/2022	46	0	
471	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL, UTTARAKHAND	03/2018	1,383.78 -	1,383.78	387.45	07/2018 -	07/2022	48	0	
472	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL, NAGALAND	03/2018	285.68 -	285.68	82.34	09/2018 -	09/2022	48	0	
473	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL, NAGALAND	03/2018	272.89 -	272.89	59.98	09/2018 -	10/2022	49	0	
474	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL, NAGALAND	03/2018	500.09 -	500.09	107.72	09/2018 -	11/2022	50	0	
475	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL, NAGALAND	03/2018	323.98 -	323.98	50.13	09/2018 -	11/2022	50	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
476	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	71.38	09/2019 -	04/2023	43	0	
477	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861]NHIDCL,MIZORAM	04/2017	473.18 -	473.18	108.59	09/2019 04/2023	04/2023	43	0	
478	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]NHIDCL,MIZORAM	04/2017	537.82 -	537.82	121.93	09/2019 06/2023	04/2023	43	0	
479	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	71.41	09/2019 04/2023	06/2023	45	0	
480	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	118.95	09/2019 04/2023	06/2023	45	0	
481	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	93.50	09/2019 06/2023	07/2023	46	0	
482	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865]NHIDCL,MIZORAM	04/2017	428.11 -	428.11	71.30	09/2019 09/2023	09/2023	48	0	
483	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	33.67	09/2019 03/2024	04/2024	55	0	
	<u>National Highways Authority Of India</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
484	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	69.96	05/2013 -	08/2021	99	-55.37	
485	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	08/2021	96	0	
486	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	995.39	11/2018 -	08/2021	33	-25.83	
487	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,615.35	03/2013 -	09/2021	102	0	
488	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	4.62	06/2013 -	09/2021	99	0	
489	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM.55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	09/2021	41	0	
490	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,577.44	04/2019 -	09/2021	29	0	
491	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	983.69	06/2020 -	09/2021	15	0	
492	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 1,928.22	1,928.22	1,876.06	04/2015 01/2021	12/2021	80	0	
493	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	395.10	07/2018 -	12/2021	41	0	
494	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29	0	
495	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29	0	
496	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	235.72	03/2020 -	12/2021	21	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
497	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653]NHAI,UTTAR PRADESH	03/2017	1,373.28 -	1,373.28	1,285.22	03/2020 12/2021	12/2021	21	0	
498	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	12/2021	20	3.95	
499	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI, TAMIL NADU	03/2016	641.17 -	641.17	395.10	07/2016 -	12/2021	65	0	
500	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	690.00	12/2019 -	12/2021	24	0	
501	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	108.46	04/2014 -	01/2022	93	0	
502	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	428.72	08/2018 -	01/2022	41	0	
503	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	308.25	08/2017 -	02/2022	54	0	
504	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	744.73	685.76	05/2018 03/2022	03/2022	46	40.22	
505	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441]NHAI,MAHARASHTRA	10/2015	593.26 716.78	716.78	617.58	05/2018 03/2022	03/2022	46	20.82	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
506	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36	0	
507	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	498.00	03/2020 -	04/2022	25	0	
508	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	486.00	05/2020 -	05/2022	24	0	
509	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	233.12	03/2019 12/2021	06/2022	39	0	
510	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	614.68	08/2017 -	07/2022	59	0	
511	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	644.68	09/2017 -	07/2022	58	0	
512	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	334.82	03/2019 01/2021	09/2022	42	-25.48	
513	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	430.26	03/2020 -	09/2022	30	.23	
514	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	18.66	
515	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023	118	0	
	Total		76,444.06 -	77,862.28	51,153.29					
	TELECOMMUNICATIONS									
	Bharat Sanchar Nigam Limited									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
516	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	422.87	-	06/2021 -	11/2021	5	-1.92	
	<u>Central Public Works Department</u>									
517	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2014	248.20 -	248.20	145.26	03/2018 -	12/2021	45	0	
	<u>Department Of Telecommunication</u>									
518	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	17,845.00	07/2015 05/2020	03/2022	80	84.97	
	Total		14,013.36 -	25,335.07	17,990.26					
	<u>URBAN DEVELOPMENT</u>									
	<u>Ahmedabad Metro Rail</u>									
519	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	9,144.21	12/2018 -	08/2022	44	18.69	NA
	<u>Bangalore Metro Rail Corporation Limited</u>									
520	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRL,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	18,226.61	02/2019 -	03/2025	73	16.25	
	<u>Central Public Works Department</u>									
521	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]CPWD,DELHI	02/2020	532.00 532.00	532.00	452.00	11/2020 09/2021	09/2021	10	0	
522	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]CPWD,DELHI	11/2017	238.56 238.56	238.56	205.72	05/2020 10/2021	10/2021	17	0	
523	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]CPWD,DELHI	06/2015	197.33 217.00	217.00	142.78	04/2019 02/2022	02/2022	34	9.97	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above (August 2021)										
						Date of Commissioning (Month/Year)				
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	Reasons for Delay (As Reported by Project Implementing Agencies)
1	2	3	4	5	6	7	8	9	10	11
524	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]CPWD,DELHI	10/2016	392.00 392.00	392.00	141.85	08/2020 06/2022	06/2022	22	0	
525	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 299.97	299.97	15.87	09/2020 01/2023	01/2023	28	0	
526	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 422.00	422.00	80.75	03/2021 06/2023	06/2023	27	0	
527	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]CPWD,DELHI	10/2016	1,180.00 1,100.80	1,100.80	35.70	07/2021 06/2023	06/2023	23	-6.71	
528	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	1,128.00	28.50	03/2022 -	06/2023	15	0	
	<u>Delhi Metro Rail Corporation</u>									
529	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,332.34	03/2016 -	08/2021	65	0	Delay in Tree cutting, R&R etc. All issues has been resolved now. All Corridors commissioned.
530	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	468.78	12/2020 -	08/2021	8	0	Time overrun due to lockdown. CMRS sanction the corridor on 13.07.2021. Corridor is scheduled to commissioned shortly.
	<u>Lucknow Metro Rail Corporation Limited</u>									
531	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	1,690.78	03/2024 -	03/2025	12	0	NO
532	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	364.47	03/2024 -	05/2025	14	0	NO
	<u>Maharashtra Metro Rail Corporation Ltd.</u>									
533	PUNE METRO RAIL PROJECT (PHASE I) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11,420.00	6,845.77	11/2021 12/2022	12/2022	13	0	•Delay in Land acquisition at Khadki •Delay in Slum R&R at Kamgar Putala & Rajiv Gandhi Nagar
	<u>Mumbai Metro Rail Corporation Ltd</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
534	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL, MAHARASHTRA	07/2013	23,136.00	33,406.00	18,788.65	03/2020 03/2023	03/2023	36	44.39	
	Total		1,34,730.10	1,51,244.55	95,964.78					
	<u>WATER RESOURCES</u>									
	<u>Brahmaputra Board</u>									
535	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPB, MAHARASHTRA	03/2017	233.57	233.57	148.83	12/2019	12/2021	24	0	
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>									
536	SEWER NETWORKS SPS AND STP HAJIPUR - [N300000035]BUIDCO, BIHAR	03/2018	305.19	305.19	24.12	08/2021	12/2021	4	0	
	<u>Delhi Jal Board</u>									
537	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N300000015]DJB, DELHI	05/2016	211.79	211.79	101.28	12/2021	12/2022	12	0	
538	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N300000016]DJB, DELHI	05/2016	239.11	239.11	138.16	02/2022	12/2022	10	0	
	<u>Kolkata Metropolitan Development Authority</u>									
539	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N300000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022	06/2022	4	13.23	
540	INTERCEPTION AND DIVERSION WITH STP AT HUGLY-CHINSURAH - [N300000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022	10/2022	8	-3.29	
	<u>Polavaram Project Authority</u>									
541	POLAVARAM IRRIGATION PROJECT - [N300000002]PPA, ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	17,935.78	03/2020 11/2021	04/2022	25	447.22	
	<u>Uttar Pradesh Jal Nigam</u>									

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
542	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UP JalNigam, UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-28.25	
	Total		11,797.25 -	57,131.86	18,348.17					
	<u>DEFENCE PRODUCTION</u>									
	<u>Central Public Works Department</u>									
543	RESIDENTIAL QUATERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 210.00	210.00	136.16	02/2020 10/2021	12/2021	22	-14.74	
	Total		246.31 -	210.00	136.16					
	<u>DEPARTMENT OF HIGHER EDUCATION</u>									
544	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	498.99	288.03	06/2017 -	03/2022	57	.57	
545	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD, PUNJAB	01/2018	430.00 -	387.83	218.29	05/2020 -	03/2022	22	-9.81	
546	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD, ODISHA	01/2019	790.79 -	790.79	213.06	03/2022 -	06/2022	3	0	
547	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD, KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	0	
548	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD, KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	0	
549	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD, PUNJAB	10/2019	348.24 -	348.24	23.28	05/2022 -	10/2022	5	0	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
550	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 -	375.00	48.46	09/2020 -	11/2022	26	0	
551	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	0	
	Total		4,633.56 -	4,594.20	890.49					
	<u>HOME AFFAIRS</u>									
552	NSG AT KOLKATA - [N28000104]CPWD,WEST BENGAL	10/2014	162.88 238.00	238.00	172.12	04/2018 12/2021	12/2021	44	46.12	
553	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD,DELHI	10/2013	1,219.21 -	2,000.00	956.28	10/2019	03/2022	29	64.04	
554	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD,UTTAR PRADESH	05/2019	199.31 -	199.31	27.86	01/2022 -	06/2022	5	0	
555	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAJ - [N45000002]CPWD,DELHI	06/2019	277.35 290.33	290.33	27.25	07/2022 10/2022	10/2022	3	4.68	
	Total		1,858.75 -	2,727.64	1,183.51					
	<u>RURAL DEVELOPMENT</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
556	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2022	74	3.96	
557	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2022	63	2.23	

Details of Delayed Projects w.r.t. Original Schedule

Costing Rs. 150 Crore and above						(August 2021)				
						Date of Commissioning (Month/Year)				Reasons for Delay (As Reported by Project Implementing Agencies)
S.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Time Overrun (Months)	Cost Overrun (%)	
1	2	3	4	5	6	7	8	9	10	11
558	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	09/2022	69	0	
	Total		527.83 -	538.27	460.04					
	<u>DPIIT</u>									
	<u>India International Convention And Expo Centre</u>									
559	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	5,178.00	2,744.03	12/2019 05/2022	05/2022	29	8.49	
	Total		4,773.00 -	5,178.00	2,744.03					
	<u>DONER</u>									
	<u>Hindustan Steelwork Construction Limited</u>									
560	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	149.33	09/2017 -	08/2021	47	0	Non-receipt of payment from client since Jan'20 till date and stalling of works due to imposition of complete lockdown from the month of May'21 in the state of Meghalaya.
	Total		151.33 -	151.33	149.33					
	Grand Total		9,42,586.32	12,32,995.82	6,99,753.08					

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

Annexure - VII

(August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>ATOMIC ENERGY</u>								
	<u>Bhavini Limited</u>								
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [020100044]	09/2003	3,492.00	6,840.00	5,986.57	09/2010	10/2022	95.88	145
	<u>Nuclear Power Corporation Of India Limited</u>								
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00	16,580.00	17,041.00	12/2015	02/2022	44.69	74
3	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) [N02000027]	10/2009	12,320.00	17,079.00	13,528.00	12/2016	03/2023	38.63	75
	Total		27,271.00	40,499.00	36,555.57				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27	480.33	105.53	09/2021	12/2022	38.72	15
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23	707.73	456.88	09/2018	06/2022	69.63	45
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]	12/2016	1,142.00	1,232.00	371.33	03/2021	03/2023	7.88	24
	Total		1,905.50	2,420.06	933.74				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
7	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]	10/2015	243.00	334.27	24.70	04/2018	06/2022	37.56	50
8	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]	12/2015	304.13	341.22	64.19	03/2017	03/2022	12.20	60
	<u>Central Coal Fields Limited</u>								
9	MAGADH EXPANSION OC(51 MTY) - [N06000015]	08/2008	6,964.33	7,254.37	729.50	07/2012	03/2028	4.16	188
	<u>Eastern Coal Fields Limited</u>								
10	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73	5,146.48	622.13	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>								
11	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53	703.39	703.39	03/2013	03/2024	46.68	132

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Neyveli Lignite Corporation</u>								
12	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW [N06000152]	07/2016	17,237.00	17,237.80	12,346.08	11/2021	11/2022	.00	12
	<u>Singareni Colliers Company Limited</u>								
13	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76	349.28	283.01	03/2015	03/2022	114.60	84
14	KAKATIYAKHANI OPENCAST-2 PROJECT - [N06000129]	05/2015	397.09	442.42	111.66	03/2019	03/2022	11.42	36
15	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06	473.22	79.04	03/2015	03/2023	5.85	96
16	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97	489.62	416.07	03/2012	03/2023	16.86	132
	<u>South-Eastern Coal Fields Limited</u>								
17	JAGANNATHPOR OCP(3.00MTY) - [N06000075]	09/2008	152.43	459.49	198.78	03/2015	03/2022	201.44	84
	<u>Western Coal Fields Limited</u>								
18	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29	289.30	36.10	03/2022	03/2025	.00	36
19	NEW MAJRI UG TO OC - [N06000128]	05/2015	295.56	299.67	164.36	03/2019	03/2022	1.39	36
20	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]	02/2016	198.68	325.18	272.90	03/2019	03/2022	63.67	36
21	BHATADI EXPANSION OC MINE - [N06000150]	02/2016	304.52	327.41	160.84	03/2019	03/2022	7.52	36
22	ADASA UG TO OC - [N06000133]	08/2015	288.90	333.43	145.08	03/2023	03/2024	15.41	12
23	KOLAR PIMPRI EXTENSION OC - [N06000160]	03/2017	362.73	402.90	336.00	03/2020	09/2022	11.07	30
	Total		31,207.71	35,209.45	16,693.83				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
	<u>Central Public Works Department</u>								
24	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18	498.99	288.03	06/2017	03/2022	.57	57
	Total		496.18	498.99	288.03				
	<u>DPIIT</u>								
	<u>India International Convention And Expo Centre</u>								
25	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE [N40000002]	11/2017	4,773.00	5,178.00	2,744.03	12/2019	05/2022	8.49	29

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		4,773.00 -	5,178.00	2,744.03				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
26	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003	02/2013	414.11 -	655.58	561.94	11/2013 -	09/2021	58.31	94
	<u>National Building Construcion Corporation Ltd</u>								
27	AIIMS BILASPUR - [N21000028	04/2018	1,351.00 -	1,471.00	814.67	09/2021 -	06/2022	8.88	9
	Total		1,765.11 -	2,126.58	1,376.61				
	<u>HOME AFFAIRS</u>								
	<u>Central Public Works Department</u>								
28	NSG AT KOLKATA - [N28000104	10/2014	162.88 -	238.00	172.12	04/2018 -	12/2021	46.12	44
29	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAF - [N45000002	06/2019	277.35 -	290.33	27.25	07/2022 -	10/2022	4.68	3
30	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 -	2,000.00	956.28	10/2019 -	03/2022	64.04	29
	Total		1,659.44 -	2,528.33	1,155.65				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
31	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234	11/2012	678.00 -	1,472.00	19.44	02/2017 -	08/2022	117.11	66
32	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314	12/2015	1,112.00 -	1,507.24	769.00	06/2019 -	02/2022	35.54	32
33	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227	11/2014	4,588.29 -	5,245.96	5,184.50	08/2018 -	09/2021	14.33	37
	<u>Gas Authority Of India Limited</u>								
34	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349	09/2018	225.54 -	247.90	41.34	02/2021 -	08/2022	9.91	18
35	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355	08/2018	286.42 -	327.01	215.40	08/2020 -	12/2021	14.17	16
36	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II - [N16000285	06/2009	2,915.00 2,915.00	5,909.00	3,786.80	12/2012 -	02/2022	102.71	110
	<u>Hindustan Petroleum Corporation Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
37	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00	3,072.00	2,443.16	06/2021	07/2022	14.76	13
38	VISAKH REFINERY MODERNISATION PROJECT - [N16000235	07/2016	20,928.00	26,264.00	16,008.48	07/2020	07/2022	25.50	24
	<u>Indian Oil Corporation Limited</u>								
39	KHARAGPUR LPG BOTTLING PLANT - [N16000300	04/2017	163.02	207.36	122.11	04/2020	10/2021	27.20	18
40	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND - [N16000304	08/2017	236.00	319.61	195.28	06/2020	09/2021	35.43	15
41	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321	04/2018	206.63	340.76	131.80	02/2020	07/2022	64.91	29
42	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368	06/2019	371.00	427.00	25.79	09/2022	03/2023	15.09	6
43	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268	05/2016	348.00	437.00	162.73	01/2021	08/2022	25.57	19
44	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06	1,236.00	437.75	10/2017	03/2022	103.60	53
45	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193	01/2015	1,823.00	3,027.90	2,117.81	03/2021	12/2021	66.09	9
46	PARADIP HYDERABAD PIPELINE - [N16000194	01/2015	2,321.00	3,338.00	2,996.28	12/2020	03/2022	43.82	15
47	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253	05/2016	4,497.00	6,025.00	3,897.13	12/2018	02/2022	33.98	38
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
48	SEA WATER DESALINATION PLANT - [N16000319	11/2017	581.00	637.00	519.50	03/2020	11/2021	9.64	20
	<u>Oil & Natural Gas Corporation Limited</u>								
49	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278	07/2016	249.85	303.75	205.92	05/2020	11/2021	21.57	18
50	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128	03/2011	861.79	2,001.34	1,568.64	05/2013	02/2022	132.23	105
51	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69	3,375.90	2,876.04	04/2018	05/2022	5.80	49
52	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	05/2019	3,660.71	3,740.05	2,997.59	05/2021	01/2022	2.17	8
53	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	04/2019	3,228.80	3,976.67	1,307.63	03/2022	05/2023	23.16	14
	<u>Oil India Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
54	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]	01/2018	543.91 -	638.60	383.44	02/2020 -	12/2021	17.41	22
	Total		56,299.71 -	74,077.05	48,413.56				
	<u>POWER</u>								
	<u>National Hydro-Electric Power Corporation</u>								
55	PARBATI HEP (4X200 MW) (NHPC) II - [N180100210]	09/2002	3,919.59 -	9,897.59	9,164.35	09/2009 -	03/2023	152.52	162
56	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [N180100221]	09/2003	6,285.33 -	19,992.43	14,059.55	09/2010 -	08/2023	218.08	155
	<u>National Thermal Power Corporation</u>								
57	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]	12/2016	529.68 -	633.80	461.33	11/2018 -	12/2021	19.66	37
58	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]	05/2016	1,885.13 -	2,311.89	1,892.27	12/2018 -	11/2021	22.64	35
59	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]	01/2007	5,353.00 -	10,566.00	8,917.95	07/2012 -	10/2021	97.38	111
60	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]	01/2016	10,598.98 -	10,997.70	8,740.94	11/2020 -	10/2022	3.76	23
61	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58 -	15,389.42	12,083.75	06/2019 -	12/2023	7.12	54
62	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]	01/2013	12,964.60 -	17,304.00	16,096.71	05/2018 -	02/2022	33.47	45
63	BARH STPP(3X660MW) NTPC - [N180100242]	02/2005	8,692.97 -	21,312.11	19,169.37	10/2011 -	07/2023	145.16	141
	<u>Power Grid Corporation Of India Limited</u>								
64	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]	05/2017	186.17 -	219.66	158.03	07/2019 -	10/2021	17.99	27
65	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	05/2014	522.29 -	546.36	480.43	11/2016 -	12/2021	4.61	61
66	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	3,029.93	07/2020 -	10/2021	14.11	15
67	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]	12/2014	5,111.33 -	6,700.00	3,068.24	12/2018 -	03/2022	31.08	39
68	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,480.78	12/2018 -	03/2024	92.02	63
69	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	02/2009	11,130.19 -	14,719.10	12,953.79	08/2013 -	08/2022	32.24	108
	<u>Satluj Jal Vidyut Nigam Limited</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
70	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	657.62	12/2021 -	06/2022	46.20	6
	<u>Thdc India Limited</u>								
71	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT [N18000042]	08/2008	2,491.58 -	3,860.35	2,271.34	06/2013 -	06/2024	54.94	132
72	TEHRI PUMPED STORAGE PLANT(1000MW) - [N18000010]	07/2006	1,657.00 -	4,825.60	4,170.24	02/2016 -	06/2023	191.23	88
	Total		94,597.17 -	1,53,347.22	119,856.62				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
73	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 -	910.93	352.67	03/2021	03/2023	14.89	24
74	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 -	1,283.49	479.21	03/2022 -	03/2023	.89	12
75	AHMEDNAGAR-PARLI VAJINATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	2,831.83	03/2021 -	03/2023	111.08	24
	<u>East Central Railways</u>								
76	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 -	390.00	366.22	03/2021 -	03/2022	11.99	12
77	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]	04/1996	477.88 283.95	751.55	714.87	03/2012 -	09/2021	57.27	114
78	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	538.55	03/2020 -	03/2023	49.45	36
79	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	863.90	03/2019 -	12/2021	37.04	33
80	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,070.00	1,076.60	03/2012 -	11/2022	229.50	128
81	MUZAFFARPUR SAGAU LI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	269.99	03/2021 -	03/2024	62.06	36
82	SAGAU LI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	488.59	03/2021 -	03/2024	63.37	36
	<u>East Coast Railway</u>								
83	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]	03/2012	155.81 -	238.03	222.65	03/2020 -	03/2022	52.77	24
84	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	192.59	11/2018 -	03/2024	15.45	64
85	KIRANDUL - JAGDALPUR DOUBLING - [N22000318]	12/2012	1,160.00 -	1,160.83	988.59	03/2020 -	03/2023	.07	36
86	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	1,186.14	02/2019 -	12/2021	38.43	34

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
87	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	04/2005	810.78 -	1,928.07	895.94	06/2021 -	03/2025	137.80	45
88	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284	04/1994	2,923.13 -	3,791.66	1,602.15	03/2009 -	03/2026	29.71	204
	<u>Eastern Railways</u>								
89	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	12.02	108
90	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 -	439.30	454.56	03/2017 -	03/2025	20.30	96
91	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	.01	240
92	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	34.08	228
93	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	36.15	157
94	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	29.20	96
95	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224	04/2001	923.52 -	995.10	614.44	03/2016 -	03/2025	7.75	108
96	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 -	1,425.44	638.19	02/2013 -	03/2024	134.80	133
97	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 -	1,619.48	906.00	03/2019 12/2009	03/2025	36.22	72
98	PIRPAINTI-JASIDIH - [N22000219	04/2013	915.98 -	2,137.81	409.74	03/2022 -	03/2025	133.39	36
	<u>Indian Railway Construction Company Limited</u>								
99	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489	04/2013	3,055.00 -	3,055.15	2,666.33	09/2018 -	06/2022	.00	45
100	GEVRA ROAD PENDRA ROAD - [N22000488	02/2014	2,288.00 -	4,970.11	962.98	03/2022 -	09/2023	117.23	18
	<u>Metropolitan Rapid Transport Projects</u>								
101	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028	04/2006	495.74 -	734.01	472.27	06/2013 -	07/2022	48.06	109
102	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164	03/1996	495.44 -	2,980.41	1,821.99	03/2004 -	03/2022	501.57	216
	<u>North Central Railway</u>								
103	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148	04/2011	2,912.96 -	3,845.60	303.16	03/2022 -	12/2024	32.02	33
	<u>North East Frontier Railway</u>								

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
104	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	30.26	24
105	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR [N22000086]	09/2006	385.20 -	1,105.00	858.45	03/2019 -	03/2023	186.86	48
106	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	1,397.73	03/2021 -	03/2022	115.07	12
107	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING [N22000183]	04/2013	1,798.00 -	2,042.51	219.14	03/2019 -	12/2023	13.60	57
108	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 -	2,145.00	1,014.54	03/2019 -	03/2024	302.54	60
109	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	1,758.52	03/2022	03/2023	32.15	12
110	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	3,825.94	12/2008 -	09/2021	284.80	153
111	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	4,169.01	03/2014 -	03/2024	130.69	120
112	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 -	6,911.00	1,300.10	03/2015 -	03/2026	197.05	132
113	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	1,656.02	12/2015 -	12/2023	542.04	96
114	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	11,303.51	03/2011 -	12/2023	175.34	153
<u>North Eastern Railway</u>									
115	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	53.51	04/2016 -	12/2021	.16	68
116	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	127.77	66
117	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	580.00	521.43	01/2019 -	02/2022	96.61	37
<u>North Western Railway</u>									
118	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	480.00	371.38	03/2020 -	09/2021	14.24	18
119	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	261.79	03/2020 -	10/2022	16.97	31
120	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	745.83	02/2019 -	06/2022	109.82	40
<u>Northern Railway</u>									
121	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	-	07/2012 -	03/2024	388.89	140
122	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]	03/1995	2,500.00 -	27,949.00	25,191.80	11/2002 -	12/2022	1,017.96	241
<u>Rail Vikas Nigam Ltd.</u>									

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
123	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68	950.00	741.79	03/2016	12/2021	50.15	69
124	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60	1,000.00	544.48	03/2022	12/2024	5.98	33
125	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01	1,400.00	1,233.65	03/2019	06/2022	51.02	39
126	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95	1,536.00	1,054.76	03/2019	06/2022	62.89	39
127	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25	1,825.00	1,266.69	12/2020	12/2022	54.24	24
128	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85	1,835.83	1,270.60	12/2020	12/2021	23.55	12
129	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66	1,868.89	1,462.02	12/2021	03/2022	20.68	3
130	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04	2,009.00	1,532.13	03/2020	12/2021	111.91	21
131	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70	2,440.53	1,066.19	02/2015	06/2022	102.92	88
132	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48	2,725.00	2,249.00	03/2020	12/2021	281.93	21
133	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42	2,733.86	40.46	03/2014	12/2025	18.95	141
134	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67	3,327.72	794.54	12/2024	12/2026	42.47	24
135	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71	3,377.00	2,152.52	03/2020	03/2022	124.58	24
136	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98	4,259.48	2,453.42	03/2016	03/2025	7.78	108
137	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51	4,639.00	888.31	03/2016	03/2025	59.22	108
138	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00	22,716.11	2,045.67	12/2024	03/2025	40.08	3
	<u>South Central Railway</u>								
139	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]	04/2017	119.73 185.00	449.39	7.09	03/2022	12/2022	275.34	9
140	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31	927.94	656.85	03/2020	11/2021	31.75	20
141	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]	04/2012	1,856.95	1,952.68	684.12	03/2023	03/2024	5.16	12

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
142	KOTLPALLI-NARASAPUR (NL) (SCR) - [N220100265]	12/2001	1,045.20 -	2,120.16	1,009.94	03/2009 -	03/2024	102.85	180
143	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 -	2,643.25	1,277.06	03/2021 -	03/2024	15.49	36
144	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 -	3,037.95	348.32	03/2014 -	03/2027	42.44	156
145	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [N220100205]	04/1997	1,723.00 1.00	3,421.35	1,989.23	03/2000 -	03/2023	98.57	276
146	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 -	3,887.48	1,239.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>								
147	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	06/2018	229.00 -	1,096.00	40.47	12/2021 -	12/2024	378.60	36
148	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	04/2010	585.93 -	1,268.32	1,058.10	02/2019 -	12/2021	116.46	34
149	ANUPPUR-KATNI - [N22000485]	04/2015	1,370.00 -	1,370.94	-	12/2021 -	12/2023	.07	24
150	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	04/2015	1,973.00 -	2,135.34	648.00	03/2021 -	12/2023	8.23	33
151	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	09/2016	1,908.51 -	3,176.60	1,334.01	03/2023 -	12/2023	66.44	9
	<u>South Eastern Railway</u>								
152	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]	04/2012	258.20 -	358.68	316.37	12/2018 -	08/2021	38.92	32
153	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	54.99	120
154	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	1,018.29	03/2020 -	02/2022	35.38	23
155	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>								
156	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]	03/1996	644.78 -	731.77	465.72	03/2017 -	03/2025	13.49	96
157	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	639.39	03/2020 -	11/2021	31.49	20
158	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	945.81	03/2020 -	09/2021	33.31	18
159	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	311.40	03/2016 -	12/2026	55.13	129
160	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,800.59	1,128.98	03/2020 -	03/2023	55.63	36
161	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	1,457.95	03/2019 -	03/2024	16.31	60
162	BANGLORE - SATYAMANGALAM (NL)(SWR) - [N220100274]	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	41.74	264

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>Southern Railway</u>								
163	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87	950.00	920.84	03/2005	09/2021	253.33	198
164	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00	1,536.00	1,233.08	03/2020	06/2022	102.11	27
165	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98	1,720.00	704.89	03/2020	03/2025	465.83	60
166	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70	2,172.16	273.27	03/2019	12/2027	1,699.64	105
167	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]	09/2007	724.69	2,950.00	1,644.43	02/2019	03/2025	307.07	73
	<u>West Central Railway</u>								
168	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]	08/2016	582.13	1,247.64	415.54	03/2022	03/2023	114.32	12
169	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93	2,470.00	1,244.18	03/2020	03/2024	40.03	48
170	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60	2,909.99	1,282.25	03/2021	03/2024	585.35	36
171	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66	8,248.50	2,131.17	05/2008	03/2025	3,230.57	202
	<u>Western Railway</u>								
172	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	04/2008	318.24	321.62	126.36	03/2012	10/2023	1.06	139
173	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]	04/2017	691.84	890.62	812.08	03/2020	09/2021	28.73	18
174	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51	890.76	773.12	03/2019	10/2021	61.51	31
175	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66	1,378.11	555.49	03/2019	03/2023	329.77	48
176	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15	1,383.69	1,199.84	03/2021	12/2022	33.41	21
177	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	04/2007	1,347.26	1,524.68	974.69	03/2022	03/2023	13.17	12
178	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	04/2007	1,640.04	1,873.10	869.58	03/2022	03/2023	14.21	12
179	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74	1,886.76	1,875.42	03/2020	03/2024	127.39	48
180	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69	6,171.08	2,301.98	03/2022	03/2024	76.13	24

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		1,38,600.99	2,71,385.55	134,800.21				
	ROAD TRANSPORT AND HIGHWAYS								
	Ministry Of Road Transport And Highways (State Pwds)								
181	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21	173.41	154.26	08/2018	09/2021	4.33	37
182	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885	03/2016	160.27	213.97	26.72	08/2019	11/2022	33.51	39
183	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22	226.88	173.03	08/2018	09/2021	4.45	37
184	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80	238.00	148.90	11/2019	10/2021	.08	23
185	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	06/2016	236.78	263.26	72.02	08/2019	08/2022	11.18	36
186	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874	03/2016	271.17 291.20	291.20	120.14	11/2018	03/2022	7.39	40
187	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96	322.24	304.71	09/2014	12/2021	72.36	87
188	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69	327.92	323.23	10/2010	12/2021	69.30	134
189	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04	377.99	368.39	10/2010	12/2021	93.80	134
190	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08	390.73	318.85	05/2017	05/2022	45.75	60
191	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151	11/2017	392.33	428.55	379.29	03/2018	10/2021	9.23	43
192	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	400.49	09/2016	12/2021	14.24	63
193	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217	01/2016	497.14	572.66	278.09	08/2016	06/2022	15.19	70
194	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221	01/2016	624.98	731.50	460.02	10/2016	12/2021	17.04	62
195	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41	992.67	890.74	03/2011	12/2021	58.98	129

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
196	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	144.26	04/2017 -	03/2022	27.16	59
197	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	133.92	04/2017 -	03/2022	29.48	59
198	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	145.13	04/2017 -	03/2022	29.48	59
	<u>National Highways Authority Of India</u>								
199	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	716.78	617.58	05/2018 -	03/2022	20.82	46
200	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	685.76	05/2018 -	03/2022	40.22	46
201	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	430.26	03/2020 -	09/2022	.23	30
202	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV [N24000691	04/2017	894.00 -	929.32	810.00	04/2020 -	12/2021	3.95	20
203	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	18.66	105
	Total		10,966.02 -	13,389.68	10,765.24				
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
204	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2022	3.96	74
205	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2022	2.23	63
	Total		352.34 -	362.78	335.17				
	<u>STEEL</u>								
	<u>National Mineral Development Corporation (Nmhc)</u>								
206	NMDC INTEGRATED STEEL PLANT - [N12000086	01/2010	15,525.00 -	21,940.00	18,779.12	05/2015 -	01/2022	41.32	80
	<u>Rastriya Ispat Nigam Limited</u>								
207	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85 -	2,100.00	1,704.90	09/2018 -	09/2021	24.79	36

Details of Ongoing Projects having Time and Cost Overruns w.r.t Original Schedule

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4		5	6	7	8	9
	Total		17,207.85 -	24,040.00	20,484.02				
	<u>TELECOMMUNICATIONS</u>								
	<u>Department Of Telecommunication</u>								
208	NETWORK FOR SPECTRUM - [N26000101	03/2012	13,334.00 -	24,664.00	17,845.00	07/2015 -	03/2022	84.97	80
	Total		13,334.00 -	24,664.00	17,845.00				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
209	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122	11/2014	10,773.00 -	12,787.00	9,144.21	12/2018 -	08/2022	18.69	44
	<u>Bangalore Metro Rail Corporation Limited</u>								
210	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058	02/2014	26,405.14 -	30,695.12	18,226.61	02/2019 -	03/2025	16.25	73
	<u>Central Public Works Department</u>								
211	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087	06/2015	197.33 -	217.00	142.78	04/2019 -	02/2022	9.97	34
	<u>Mumbai Metro Rail Corporation Ltd</u>								
212	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086	07/2013	23,136.00 -	33,406.00	18,788.65	03/2020 -	03/2023	44.39	36
	Total		60,511.47 -	77,105.12	46,302.25				
	<u>WATER RESOURCES</u>								
	<u>Kolkata Metropolitan Development Authority</u>								
213	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032	05/2018	198.43 -	224.69	-	02/2022 -	06/2022	13.23	4
	<u>Polavaram Project Authority</u>								
214	POLAVARAM IRRIGATION PROJECT - [N30000002	02/2009	10,151.04 -	55,548.87	17,935.78	03/2020 -	04/2022	447.22	25
	Total		10,349.47 -	55,773.56	17,935.78				
	Grand Total		4,71,296.96	7,82,605.37	476,485.31				

Details of Projects Without Date of Commissioning

Annexure - VIII

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Mahanadi Coal Fields Limited</u>				
2	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	03/2021
	<u>Neyveli Lignite Corporation</u>				
3	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 - 7,980.79	12/2015 -	02/2021
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Western Coal Fields Limited</u>				
9	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA	06/2015	483.69 499.00	03/2021 -	03/2021
	Total		14,613.95 -		
	<u>FINANCE</u>				
	<u>Central Public Works Department</u>				
10	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
	Total		209.00 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
11	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	11/2019 05/2021	04/2021
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 05/2021	04/2021
	Total		458.64 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
13	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 12/2021	12/2020
14	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	11/2020 -	02/2021
15	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		1,055.62 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
16	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	-
	<u>Indian Oil Corporation Limited</u>				
17	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021
18	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR), CACHAR, ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	08/2019 06/2021	05/2021
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
20	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,475.92	05/2021 05/2021	05/2021
	Total		7,383.41 -		
	<u>POWER</u>				
	<u>Central Public Works Department</u>				
21	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	-
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	03/2013 12/2021	-
24	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
25	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
26	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
27	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021
28	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	06/2021
29	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021
30	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	10/2012 -	-
31	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
32	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	04/2016 -	-
33	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
34	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	10/2017 -	-
35	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
36	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
37	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
38	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	-
39	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-
40	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
41	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	-
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	-
43	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	-
44	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	-
	Total		41,320.40 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
45	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI <u>Natrip Implementation Society</u>	08/2016	1,554.00 3,727.30	09/2019 -	-
46	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 03/2021	03/2021
	Total		3,272.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Central Public Works Department</u>				
47	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA <u>Hospital Services Consultancy Corporation Ltd</u>	10/2016	209.84 -	03/2020 -	05/2021
48	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
49	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
50	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
51	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
52	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
53	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
54	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021
55	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	03/2021
56	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	03/2021
57	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021
58	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021
	Total		3,019.16 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
59	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-
60	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
61	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI, RAJASTHAN	01/2011	493.17 -	03/2018 -	-
62	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI, MAHARASHTRA	10/2013	305.00 -	03/2019 -	-
63	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
64	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
65	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	-
66	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
67	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
68	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
69	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
70	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
<u>East Central Railways</u>					
71	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- 10/2019	10/2019
72	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR	04/1998	180.82 -	- 08/2020	08/2020
73	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 735.20	- -	03/2021
74	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 516.02	03/2020 -	-
75	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
76	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-
77	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
78	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR, BIHAR	04/2008	445.25 -	- -	-
79	GAYA-CHATRA (NL) - [N22000169]ECR, MULTI STATE	04/2008	415.67 -	- -	-
80	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
81	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
82	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
83	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
84	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
85	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>Eastern Railways</u>				
86	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
87	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
88	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
89	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
91	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT (MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
92	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
93	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
94	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
95	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
96	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-
97	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR,UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
	<u>North East Frontier Railway</u>				
98	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	06/2021
99	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR (NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
100	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
101	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
102	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
103	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
104	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
105	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
106	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-
107	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR, MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
108	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER, UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021
109	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER, UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
110	KICHHA-KHATIMA (NL) - NER - [220100317]NER, UTTARAKHAND	04/2003	142.45 -	- -	-
111	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER, UTTAR PRADESH	03/2013	307.00 -	- -	-
112	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER, UTTAR PRADESH	03/2013	643.00 -	- -	-
113	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER, UTTAR PRADESH	04/2014	182.92 -	- -	-
114	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER, UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
115	THIYAT HAMIRA-SANU - [N22000149]NWR, RAJASTHAN	04/2013	236.93 -	10/2018 -	01/2020
116	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR, RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
117	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR, RAJASTHAN	04/2012	246.08 -	12/2019 -	03/2021
118	AJMER-BANGURGRAM - [N22000155]NWR, RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021
119	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR, MULTI STATE	04/2011	2,082.75 -	- -	-
120	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR, RAJASTHAN	04/2013	822.00 -	- -	-
121	PUSHKAR-MERTA - [N22000151]NWR, RAJASTHAN	04/2013	323.00 -	- -	-
122	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR, RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
123	ROHTAK-MEHAM HANSI - [N22000272]NR, HARYANA	04/2012	287.00 -	12/2011 -	06/2021
124	HARIDWAR-LAKSAR - [N22000289]NR, UTTARAKHAND	04/2012	219.83 -	- -	-
125	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR, MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
126	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES, MULTI STATE	04/2015	636.38 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above

(August 2021)

				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
127	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES, TELANGANA	03/2015	636.38 -	03/2021 -	-
128	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES, CHHATISGARH	02/2016	393.98 -	03/2020 -	-
	<u>Rail Vikas Nigam Ltd.</u>				
129	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL, ODISHA	04/1996	1,185.64 -	12/2017 -	-
130	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL, ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
131	DHASA-JETALSAR (GC) - [N22000141]RVNL, GUJARAT	04/2012	644.38 -	03/2021 -	-
	<u>Railway Electrification</u>				
132	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE, UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
133	NANDYAL-YERRAGUNTLA(NL), SCR - [220100192]SCR, ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
134	MANUGURU-RAMAGUNDAM - [N22000259]SCR, TELANGANA	04/2013	1,112.00 -	- -	-
135	GUDUR-DURGARA JAPATNAM - [N22000265]SCR, ANDHRA PRADESH	04/2011	761.37 -	- -	-
136	CUMBUM-PRODDATUR - [N22000282]SCR, ANDHRA PRADESH	04/2013	829.00 -	- -	-
137	DUVVADA-VIJAYAWADA - [N22000366]SCR, ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
138	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR, MADHYA PRADESH	04/2005	383.79 1,413.76	- 08/2020	08/2020
139	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR, CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2020	10/2020
140	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR, MULTI STATE	02/1997	511.86 1,756.00	04/2020 03/2021	03/2021
	<u>South Eastern Railway</u>				
141	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER, JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER, WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
143	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER, ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
144	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR, KERALA	10/1998	1,566.00 -	- -	-
145	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR, TAMIL NADU	09/2006	227.40 -	- -	-
146	ATTIPPATTU PUTTUR - [N22000184]SR, TAMIL NADU	04/2008	151.84 -	02/2019 -	-
147	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR, TAMIL NADU	04/2013	839.00 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
148	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
149	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-
150	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
151	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	-
152	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
153	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
154	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
155	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
<u>Western Railway</u>					
156	BHAVNAGAR WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
157	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
158	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
159	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
160	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
161	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		97,634.83 -		
<u>ROAD TRANSPORT AND HIGHWAYS</u>					
<u>Central Public Works Department</u>					
162	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
<u>Ministry Of Road Transport And Highways (State Pwds)</u>					
163	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	02/2021
164	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	03/2021
165	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	04/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
166	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	04/2021
167	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	09/2017
168	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	12/2019
169	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
170	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 11/2019	11/2019
171	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2019	12/2019
172	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH, WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020
173	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
174	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020
175	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 03/2021	03/2021
176	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021
177	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	05/2021
178	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021
179	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH, WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021
180	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021
181	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021
182	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021
183	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 12/2021	07/2021
185	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
186	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
187	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
188	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
189	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
190	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
191	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
192	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
193	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
194	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
195	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
196	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADESH - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
197	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 369.92	08/2013 06/2021	-
198	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.90	08/2013 06/2021	-
199	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.58	02/2013 06/2021	-
200	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 273.27	08/2015 -	-
201	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
202	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
203	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-
205	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-
206	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
207	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-
208	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
209	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-
210	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-
211	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-
215	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-
216	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-
217	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-
218	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-
219	REHABILATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-
220	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
221	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-
222	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-
223	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-
224	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
225	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	-
226	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
227	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
228	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
229	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
230	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
231	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
232	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
233	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
234	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPIR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
235	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
236	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
237	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 07/2021	-
238	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 01/2022	-
239	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 556.13	11/2018 07/2021	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
240	REHABILITATION AND UPGADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
241	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
242	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552-EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-
243	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
244	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
245	REHABILITATION AND UPGADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 07/2021	-
246	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
247	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
248	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
249	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
250	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
251	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
252	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
253	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
254	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
255	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
256	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
257	REHABILITATION AND UPGADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
258	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
259	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-
260	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
261	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
262	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
263	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
264	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
265	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
266	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
267	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
268	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
269	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
270	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
271	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
272	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
273	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
274	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
275	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
276	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
277	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
278	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
279	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
280	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
281	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
282	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-
283	AMDIT TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
284	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
285	NAGAJ TO VAJJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
286	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
287	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
288	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
289	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
290	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
291	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
292	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
293	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
294	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
295	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
296	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
297	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
298	KAIJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
299	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
300	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
301	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
302	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
303	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
304	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
305	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
306	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
307	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-
308	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
309	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
310	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
311	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
312	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
313	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
314	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
315	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
316	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
317	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
318	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
319	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
320	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
321	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
322	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
323	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
324	WADIGODRI TO DHANGRIIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
325	DHANGRIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
326	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
327	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
328	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
329	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
330	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
331	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
332	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-
333	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
334	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
335	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
336	OSMANNAGAR TO KUNDAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
337	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
338	KUNDAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
339	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
340	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
341	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
342	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
343	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
344	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
345	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
346	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
347	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
348	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
349	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
350	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
351	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
352	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
353	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
354	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
355	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
356	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
357	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-
358	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
359	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
360	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
361	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
362	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
363	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
364	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
365	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
366	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
367	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
368	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
369	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
370	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
371	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
372	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
373	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	-
374	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
375	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
376	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
377	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
378	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
379	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
380	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
381	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
382	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-
383	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
384	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
385	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
386	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
387	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
388	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	06/2021 -	-
389	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
390	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
391	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
392	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
393	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
394	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
395	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	-
396	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
397	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
398	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
399	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
400	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
401	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
402	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
403	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-
404	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
405	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
406	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
407	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
408	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
409	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
410	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
411	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-
412	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	-
413	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-
414	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
415	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
416	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	-
417	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	-
418	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	-
419	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
420	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 204.73	06/2019 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
421	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-
422	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
423	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
424	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
425	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
426	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
427	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
428	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
429	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
430	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
431	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
432	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
433	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	08/2020
434	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
435	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	02/2021
436	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 522.86	06/2018 -	03/2021
437	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	03/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
438	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	03/2021
439	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
440	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
441	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
442	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
443	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
444	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
445	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
446	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
447	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
<u>National Highways Authority Of India</u>					
448	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2021
449	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	07/2021
450	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 -	11/2019 -	11/2019
451	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 -	11/2019 -	11/2019
452	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 -	11/2019 -	11/2019
453	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
454	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
455	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
456	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
457	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI, KERALA	06/2015	845.24 -	- 01/2020	01/2020
458	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI, RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020
459	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI, ASSAM	12/2003	245.00 -	03/2008 -	08/2020
460	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI, MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020
461	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI, JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
462	SRINAGAR TO BANIHAL - [N24000189]NHAI, JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
463	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI, MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
464	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI, KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
465	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI, KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
466	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI, KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
467	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI, HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
468	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI, JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
469	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI, GUJARAT	02/2018	1,052.21 -	- -	01/2021
470	NALBARI T BIJNI (AS-7) - [N24000048]NHAI, ASSAM	12/2003	208.00 -	04/2008 -	02/2021
471	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI, ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
472	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI, TAMIL NADU	12/2017	379.90 -	- -	03/2021
473	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI, CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
474	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI, ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 10/2021	04/2021
475	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI, BIHAR	03/2017	235.48 -	03/2020 -	05/2021
476	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI, MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	06/2021

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
477	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI, MAHARASHTRA	11/2016	1,071.61 -	- 10/2021	07/2021
478	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI, MAHARASHTRA	11/2016	1,064.88 -	- 01/2022	07/2021
479	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI, PUNJAB	02/2018	261.76 -	- -	07/2021
480	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI, GUJARAT	03/2018	1,437.64 -	- -	07/2021
481	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI, MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021
482	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI, ASSAM	12/2003	280.00 -	02/2009 -	-
483	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI, ASSAM	12/2003	199.81 -	04/2009 -	-
484	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI, ASSAM	12/2003	167.64 -	11/2008 -	-
485	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI, ASSAM	12/2003	155.04 -	11/2008 -	-
486	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI, ASSAM	12/2003	196.00 -	07/2009 -	-
487	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI, HARYANA	04/2007	486.00 -	05/2010 -	-
488	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI, GUJARAT	03/2010	1,509.10 -	09/2012 -	-
489	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI, MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
490	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI, HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-
491	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI, MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
492	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI, KARNATAKA	09/2010	946.00 -	06/2018 -	-
493	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI, KERALA	02/2010	617.00 -	08/2012 -	-
494	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI, MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
495	INDORE-DEWAS(NH-3) - [N24000159]NHAI, MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
496	NASHRI- CHANANI - [N24000162]NHAI, JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
497	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI, JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
498	PATNA-MUZZAFFARPUR - [N24000165]NHAI, BIHAR	08/2010	671.30 -	02/2013 -	-
499	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI, UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
500	KANDLA - MUNDRA PORT - [N24000175]NHAI, GUJARAT	01/2011	953.88 -	07/2013 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
501	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI, ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
502	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI, ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
503	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI, BIHAR	09/2011	574.00 -	03/2014 -	-
504	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-
505	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 12/2021	-
506	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-
507	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	-
508	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	-
509	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
510	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
511	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
512	ETAWAH CHAKERI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
513	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
514	WIDENING OF KHEDE-SINAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
515	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
516	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-
517	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	-
518	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
519	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-
520	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
521	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
522	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
523	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
524	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
525	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
526	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
527	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-
528	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 363.93	- -	-
529	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI, MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
530	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI, HARYANA	12/2015	602.95 -	06/2016 -	-
531	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI, HARYANA	01/2016	574.28 -	07/2018 -	-
532	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI, MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
533	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI, MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
534	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI, UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
535	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM - 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-
536	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI, MADHYA PRADESH	03/2015	795.76 -	- -	-
537	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI, MADHYA PRADESH	03/2015	794.30 -	- -	-
538	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI, JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
539	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI, BIHAR	08/2015	556.07 -	- -	-
540	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI, RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
541	FOUR LANING OF PARWANOO - SOLAN - [N24000479]NHAI, HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
542	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI, BIHAR	12/2015	1,041.10 -	04/2019 -	-
543	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI, JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
544	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI, MADHYA PRADESH	03/2015	928.83 -	- -	-
545	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI, KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
546	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI, UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
547	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI, UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
548	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI, MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
549	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI, CHHATISGARH	12/2015	596.67 -	05/2018 -	-
550	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI, MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
551	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI, UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
552	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI, UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-
553	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 247.00	04/2018 -	-
554	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
555	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-
556	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
557	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
558	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
559	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
560	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
561	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
562	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	-
563	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
564	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
565	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
566	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
567	MEERUT-BULANDSHAHAH - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
568	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
569	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
570	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
571	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
572	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
573	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
574	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI,UTTAR PRADESH	03/2016	1,396.74 -	- -	-
575	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-
576	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
577	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
578	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
579	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-
580	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-
581	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-
582	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	-
583	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI, UTTAR PRADESH	03/2016	1,737.00 -	- -	-
584	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI, KERALA	04/2016	804.97 -	06/2018 -	-
585	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI, GUJARAT	05/2016	998.18 -	- -	-
586	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI, GUJARAT	05/2016	834.64 -	- -	-
587	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI, GUJARAT	05/2016	723.64 -	- -	-
588	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI, GUJARAT	05/2016	763.08 -	- -	-
589	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI, GUJARAT	05/2016	425.60 -	- -	-
590	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI, RAJASTHAN	06/2016	763.23 -	06/2019 -	-
591	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI, RAJASTHAN	06/2016	649.00 -	06/2019 -	-
592	BALANCE WORK OF 4 LANING OF GORAKHPUR -GOPALGANJ - [N24000590]NHAI, BIHAR	05/2015	581.84 -	05/2017 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
593	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
594	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
595	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-
596	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
597	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
598	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
599	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	-
600	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
601	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
602	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
603	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
604	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-
605	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
606	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
607	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-
608	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
609	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
610	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
611	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
612	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
613	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
614	REHABILITATION AND UPGRADE TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI, ODISHA	10/2016	1,008.96 -	- -	-
615	FOUR LANE OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
616	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
617	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
618	4 LANE OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
619	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
620	SIX LANE FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 - 1,361.00	- -	-
621	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
622	FOUR LANE OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 - 911.07	02/2020 - 03/2021	-
623	FOUR LANE OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
624	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
625	4-LANE OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
626	4-LANE OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
627	4-LANE OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
628	4-LANE OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
629	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
630	4-LANE OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
631	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANE OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
632	TWO-LANE WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
633	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
634	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-
635	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
636	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
637	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
638	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	-
639	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
640	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
641	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
642	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
643	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
644	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
645	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
646	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
647	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
648	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
649	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-
650	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
651	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
652	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
653	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
654	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
655	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-
656	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
657	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
658	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
659	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
660	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
661	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
662	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
663	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
664	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
665	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
666	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
667	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
668	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
669	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
670	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
671	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
672	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
673	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
674	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
675	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI, WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-
676	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-
677	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
678	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-
679	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
680	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
681	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
682	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
683	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
684	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-
685	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
686	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
687	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
688	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
689	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-
690	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
691	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-
692	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
693	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
694	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-
695	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
696	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
697	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
698	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
699	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-
700	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
701	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- -	-
702	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
703	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
704	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
705	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
706	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
707	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
708	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
709	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
710	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-
711	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
712	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
713	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-
714	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
715	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
716	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
717	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
718	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
719	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
720	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
721	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
722	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
723	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
724	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
725	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
726	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
727	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
728	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
729	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
730	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
	Total		3,69,005.38 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
731	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 18,380.00	12/2015 -	-
732	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-
	<u>Kochi Metro Rail Corporation Ltd</u>				
733	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
734	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
735	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019
	<u>National Building Construcion Corporation Ltd</u>				
736	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		43,423.79 -		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
737	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021
738	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021
739	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021
740	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021
741	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021
742	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
743	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	-
744	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-
745	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Delhi Jal Board</u>				
746	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021
747	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
748	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
749	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021
750	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	-
	<u>Uttar Pradesh Jal Nigam</u>				
751	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
752	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021
753	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021
754	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	-
	<u>Uttarakhand Pey Jal Nigam</u>				
755	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-
	Total		6,018.04 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
756	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 302.64	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Central Public Works Department</u>				
757	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
758	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	-
759	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
760	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	-
761	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	07/2020 -	-

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
762	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	-
763	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
764	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
765	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
766	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				
767	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
768	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
769	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		3,943.71 -		
	<u>HOME AFFAIRS</u>				
	<u>Central Public Works Department</u>				
770	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
	Total		114.26 -		
	<u>RURAL DEVELOPMENT</u>				
771	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI	11/2018	361.60 -	07/2021 -	-
	Total		361.60 -		
	<u>DPIIT</u>				
	<u>Delhi Mumbai Industrial Corridor</u>				
772	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021
	Total		12,579.09 -		

Details of Projects Without Date of Commissioning

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning (Month/Year)	
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	Grand Total		6,04,715.52		

FLASH REPORT

Details of Projects Without Original Date of Commissioning

Annexure - IX

Costing Rs. 150 Crore and above (August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>COAL</u>								
	<u>Singareni Colliers Company Limited</u>								
1	SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA	11/2016	272.73	272.73	153.75	-	03/2022	-	2/6
	Total		272.73	272.73	153.75				2/6
	<u>PETROLEUM</u>								
	<u>Indian Oil Corporation Limited</u>								
2	LPG BP PROJECT JODHPUR - [N16000318]IOCL, RAJASTHAN	03/2018	229.80	229.80	85.09	-	05/2022	0(R3)	17/26
3	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]IOCL, GUJARAT	03/2018	588.20	730.20	128.08	-	05/2023	0(R3)	12/17
	Total		818.00	960.00	213.17				29/43
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
4	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL, JAMMU AND KASHMIR	03/2019	4,287.59	4,287.59	582.89	-	08/2024	0(R3)	0/0
	Total		4,287.59	4,287.59	582.89				0/0
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Hospital Services Consultancy Corporation Ltd</u>								
5	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02	601.02	453.44	-	09/2021	-	0/0
6	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99	582.99	522.60	-	09/2021	-	0/0
7	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99	651.99	568.10	-	09/2021	-	0/0
8	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI	12/2017	156.56	190.34	156.14	-	11/2021	-	0/0
	Total		1,992.56	2,026.34	1,700.28				0/0
	<u>RAILWAYS</u>								
	<u>East Central Railways</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
9	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222] ECR, JHARKHAND	03/1999	1,033.07 3,020.95	3,620.00	3,614.37	- 03/2022	03/2022	0(R3)	0/0
10	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476] ECR, BIHAR	04/1991	329.39 -	1,483.14	1,219.42	- 03/2022	03/2022	0(R3)	0/0
11	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303] ECR, BIHAR	04/2003	528.65 2,066.78	2,066.78	1,581.82	- 03/2023	03/2023	0(R3)	0/0
12	KODERMA-TILAIYA (NL), ECR - [220100305] ECR, JHARKHAND	04/2002	459.91 1,625.87	1,625.87	890.81	- 03/2023	03/2023	0(R3)	0/0
13	CHHAPRA-MUZAFFARPUR (NL) - [N22000172] ECR, BIHAR	04/2006	378.56 -	1,858.75	386.36	- -	03/2023	-	0/0
14	ARARIA-SUPAUL (NL) - [N22000177] ECR, BIHAR	04/2008	1,605.17 -	1,605.17	61.37	- 03/2023	03/2023	0(R3)	0/0
15	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180] ECR, BIHAR	04/2004	372.14 1,470.50	1,470.50	1,377.83	- -	03/2023	-	0/0
16	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257] ECR, BIHAR	04/1997	162.87 614.45	614.45	352.16	- -	12/2023	-	0/0
17	BIHTA-AURANGABAD (NL) - [N22000170] ECR, BIHAR	04/2008	326.20 -	2,995.01	2.04	- -	03/2024	-	0/0
18	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176] ECR, BIHAR	04/2008	228.05 -	228.05	1.53	- -	03/2024	-	0/0
19	SAMASTIPUR-DARBANGHA - [N22000329] ECR, BIHAR	05/2015	380.00 -	519.33	294.63	- -	03/2025	-	0/0
	<u>Eastern Railways</u>								
20	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238] ER, MULTI STATE	04/2011	175.80 -	495.10	299.53	- -	03/2022	-	0/0
21	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302] ER, WEST BENGAL	04/2012	255.64 -	272.20	283.69	- -	03/2022	-	0/0
22	MONIGRAM- NIMTITA - [N22000301] ER, MULTI STATE	04/2012	250.93 -	310.70	377.47	- -	03/2024	-	0/0
23	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217] ER, MULTI STATE	04/2007	450.00 -	1,261.34	-	- -	03/2025	-	0/0
24	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218] ER, MULTI STATE	04/2010	172.03 -	260.10	11.77	- -	03/2025	-	0/0
25	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227] ER, MULTI STATE	04/2010	174.56 -	174.56	71.43	- -	03/2025	-	0/0
26	BARIARPIUR-MANANPUR VIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234] ER, MULTI STATE	04/2007	450.55 -	250.55	20.11	- -	03/2025	-	0/0
27	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235] ER, MULTI STATE	04/2010	365.17 -	527.54	1.76	- -	03/2025	-	0/0
28	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241] ER, MULTI STATE	04/2000	297.47 -	298.22	36.13	- -	03/2025	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
29	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	336.96	40.65	- -	03/2025	-	0/0
30	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	166.89	.02	- -	03/2025	-	0/0
	<u>Metropolitan Rapid Transport Projects</u>								
31	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	268.52	.03	- -	03/2025	-	0/0
	<u>North East Frontier Railway</u>								
32	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	373.87	333.46	- 12/2021	03/2022	3(R3)	0/0
	<u>North Eastern Railway</u>								
33	BURHWAL - GONDA - 3RD RUNNING LINE - [N22000468]NER,UTTAR PRADESH	04/2016	602.50 -	714.34	88.04	- -	12/2023	-	0/0
	<u>Northern Railway</u>								
34	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91 -	791.39	574.59	- -	03/2023	-	0/0
35	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00 -	489.64	105.51	- -	03/2023	-	0/0
36	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68 -	419.00	160.58	- -	09/2023	-	0/0
37	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65 -	359.00	111.51	- -	03/2024	-	0/0
38	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22 -	841.90	1.73	- -	03/2024	-	0/0
	<u>South Eastern Railway</u>								
39	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37 -	620.00	40.99	- -	03/2025	-	0/0
	<u>South Western Railway</u>								
40	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	2,161.36	76.42	- -	12/2023	-	0/0
41	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	692.00	-	- -	12/2023	-	0/0
42	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	466.65	-	- -	12/2023	-	0/0
43	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	167.50	.34	- -	12/2023	-	0/0
44	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	327.25	-	- -	12/2023	-	0/0
45	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 103.74	5,174.30	157.01	- -	12/2024	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
46	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30 -	2,432.50	1,126.08	- -	12/2025	-	2/2
47	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	348.85	.36	- -	12/2025	-	0/0
	<u>Southern Railway</u>								
48	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	1,121.00	969.72	- 08/2021	08/2021	0(R3)	0/0
49	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	457.08	-	- -	12/2021	-	0/0
50	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	608.13	389.96	- 12/2021	12/2021	0(R3)	0/0
51	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	1,205.00	2.28	- -	03/2024	-	0/0
52	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	559.95	273.32	- -	03/2024	-	0/0
53	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	3,150.00	239.49	- -	12/2025	-	0/0
	<u>Western Railway</u>								
54	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	844.10	251.82	- 03/2024	03/2024	0(R3)	0/0
	Total		24,180.46 -	47,034.54	15,828.14				2/2
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
55	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59 -	306.59	168.16	- -	09/2021	-	0/0
56	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	291.05	231.36	- 10/2021	10/2021	0(R3)	0/0
57	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	293.68	179.19	- 10/2021	10/2021	0(R3)	0/0
58	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	271.94	- 03/2021	12/2021	9(R3)	0/0
59	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	326.99	122.02	- -	12/2021	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>								
60	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771]NHIDCL,MEGHALAYA	04/2017	553.51 -	553.51	127.99	- 09/2021	09/2021	0(R3)	2/4
61	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50 -	210.50	145.07	- -	10/2021	-	4/4
62	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01 -	520.01	189.59	- -	12/2021	-	2/4
63	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL,ARUNACHAL PRADESH	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	11(R3)	3/4
64	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL,ARUNACHAL PRADESH	12/2016	200.44 -	200.44	125.91	- 08/2021	12/2021	4(R3)	3/4
65	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	1,049.51	143.02	- -	12/2021	-	2/4
66	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]NHIDCL,ARUNACHAL PRADESH	03/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022	-3(R3)	2/4
67	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	568.92	310.07	- 11/2021	03/2022	4(R3)	0/0
68	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL,ARUNACHAL PRADESH	12/2016	188.78 -	188.78	104.07	- 03/2021	03/2022	12(R3)	3/4
69	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]NHIDCL,ARUNACHAL PRADESH	02/2017	175.06 -	175.06	87.32	- 04/2022	04/2022	0(R3)	3/4
70	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]NHIDCL,ARUNACHAL PRADESH	02/2017	176.12 -	176.12	73.92	- 04/2022	04/2022	0(R3)	2/4
71	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM	10/2017	818.00 -	818.00	287.52	- -	03/2023	-	1/4
	<u>National Highways Authority Of India</u>								

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above

(August 2021)

						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
72	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	266.64	- -	08/2021	-	3/4
73	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	341.88	- -	08/2021	-	0/1
74	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	353.42	- -	08/2021	-	0/0
75	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.24	448.18	462.99	- 05/2021	08/2021	3(R3)	0/0
76	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	510.71	- -	08/2021	-	0/1
77	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	277.00	- -	08/2021	-	0/0
78	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25 866.55	866.55	862.73	- 08/2021	08/2021	0(R3)	0/0
79	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,620.21	- -	09/2021	-	0/0
80	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	764.04	- -	10/2021	-	2/4
81	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,308.42	- -	10/2021	-	0/0
82	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,368.89	- -	11/2021	-	0/0
83	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
84	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	407.00	- -	12/2021	-	0/3
85	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	- -	01/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
86	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92	1,071.00	299.56	-	01/2022	-	0/0
87	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21	289.21	224.45	-	01/2022	-	0/0
88	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53	291.53	197.49	-	02/2022	-	0/0
89	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97	1,094.97	737.00	-	02/2022	-	2/4
90	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00	479.00	456.80	-	03/2022	-	0/0
91	FOUR LANING WITH PS.TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28	752.28	272.74	-	03/2022	-	0/1
92	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95	1,031.95	-	-	03/2022	-	0/0
93	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09	953.09	438.00	-	03/2022	-	0/0
94	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43	314.43	85.61	-	03/2022	-	0/0
95	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71	628.71	358.35	-	03/2022	-	0/0
96	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96	884.00	443.00	-	10/2022	-	2/4
97	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98	840.00	223.00	-	11/2022	-	1/4
98	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35	505.35	255.05	-	12/2022	-	0/0

Details of Projects Without Original Date of Commissioning

Costing Rs. 150 Crore and above (August 2021)									
						Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
	Total		29,993.93	31,506.52	18,172.64				37/70
			-						
	<u>URBAN DEVELOPMENT</u>								
	<u>National Building Construcion Corporation Ltd</u>								
99	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI	07/2016	2,694.00	2,694.00	817.02	-	12/2022	-	0/9
	Total		2,694.00	2,694.00	817.02				0/9
			-						
	Grand Total		64,239.27	88,781.72	37,467.89				70/130

FLASH REPORT

Details of Projects Without Milestones w.r.t. Original Schedule

Annexure - X

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
	<u>CIVIL AVIATION</u>					
	<u>Airport Authority Of India Limited</u>					
1	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80 351.21	04/2020 -	03/2022	0/0
	<u>COAL</u>					
	<u>Ahmedabad Metro Rail</u>					
2	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]MEGA,MADHYA PRADESH	03/2021	496.28 -	03/2028 -	03/2028	0/0
	<u>Bharat Coking Coal Limited</u>					
3	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL, WEST BENGAL	12/2015	304.13 341.22	03/2017 -	03/2022	0/0
4	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL, JHARKHAND	10/2015	243.00 334.27	04/2018 -	06/2022	0/0
	<u>Eastern Coal Fields Limited</u>					
5	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]ECL, WEST BENGAL	04/2020	483.65 -	03/2025 -	03/2025	0/0
	<u>Neyveli Lignite Corporation</u>					
6	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC, RAJASTHAN	03/2015	522.45 -	09/2019 -	-	0/0
7	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC, RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-	0/0
8	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC, RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-	0/0
9	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC, RAJASTHAN	03/2015	513.63 -	12/2019 -	-	0/0
	<u>Northern Coal Fields Limited</u>					
10	KHADIA EXPANSION OCP - [N06000208]NCL, UTTAR PRADESH	06/2021	491.67 -	03/2025 -	03/2025	0/0
	<u>South-Eastern Coal Fields Limited</u>					
11	JAMPALI OCP RCE - [N06000198]SECL, CHHATISGARH	05/2020	278.64 -	03/2024 -	03/2024	0/0
12	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]SECL, CHHATISGARH	08/2020	2,309.80 -	03/2029 -	03/2029	0/0
13	PORDA CHINTAPANI OCP (10 MTY) - [N06000199]SECL, CHHATISGARH	12/2020	2,310.12 -	03/2029 -	03/2029	0/0
14	DIPKA OC EXPANSION 40 MTY - [N06000200]SECL, CHHATISGARH	12/2020	5,241.40 -	03/2029 -	03/2029	0/0
	<u>STEEL</u>					
	<u>Steel Authority Of India Limited (Sail)</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
15	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]SAIL, CHHATISGARH	11/2020	542.24 -	12/2023 -	12/2023	0/0
	<u>PETROLEUM</u>					
	<u>Bharat Petroleum Corporation Limited</u>					
16	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL, KERALA	12/2015	1,112.00 1,507.24	06/2019 -	02/2022	0/0
17	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL, MAHARASHTRA	07/2020	640.00 -	12/2021 -	03/2022	0/0
18	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. - [N16000373]BPCL, JHARKHAND	11/2018	248.55 -	06/2022 -	06/2022	0/0
19	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]BPCL, TAMIL NADU	11/2012	678.00 1,472.00	02/2017 08/2022	08/2022	0/0
20	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]BPCL, KERALA	09/2018	11,130.00	03/2023	03/2023	0/0
21	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]BPCL, MAHARASHTRA	08/2020	697.00 -	03/2023 -	03/2023	0/0
	<u>Chennai Petroleum Corporation Limited</u>					
22	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL, TAMIL NADU	08/2017	421.00 -	08/2020 -	10/2021	0/0
23	BS-VI PROJECTS - [N16000295]CPCL, TAMIL NADU	09/2017	1,858.00 -	12/2019 -	-	0/0
	<u>Hindustan Petroleum Corporation Limited</u>					
24	220 KV GRID SUPPLY - [N16000407]HPCL, ANDHRA PRADESH	10/2020	303.40 -	03/2021 -	08/2021	0/0
25	SULPHUR FORMING UNIT IN SRU - [N16000408]HPCL, ANDHRA PRADESH	10/2020	210.94 -	08/2021 -	08/2021	0/0
26	RUF PITCH LOADING GANTRY - [N16000406]HPCL, ANDHRA PRADESH	10/2020	332.61 -	11/2022 -	11/2022	0/0
	<u>Indian Oil Corporation Limited</u>					
27	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL, ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021	0/0
28	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL, MAHARASHTRA	05/2016	212.00 -	01/2021 -	09/2021	0/0
29	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]IOCL, MADHYA PRADESH	08/2017	236.00 319.61	06/2020 09/2021	09/2021	0/0
30	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL, MAHARASHTRA	05/2016	261.00 -	01/2021 -	10/2021	0/0
31	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]IOCL, HARYANA	08/2019	1,255.00 -	10/2021 -	10/2021	0/0
32	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]IOCL, ANDHRA PRADESH	08/2018	466.00 -	04/2021 12/2021	12/2021	0/0
33	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]IOCL, BIHAR	04/2018	522.00 -	03/2021 12/2021	12/2021	0/0
34	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU - [N16000305]IOCL, TAMIL NADU	12/2017	466.43 -	10/2020 01/2022	01/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
35	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]IOCL,ANDHRA PRADESH	10/2018	316.20 -	10/2021 03/2022	03/2022	0/0
36	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]IOCL,HARYANA	09/2019	164.69 -	07/2021 03/2022	03/2022	0/0
37	LPG BP PROJECT CHITTOOR - [N16000381]IOCL,ANDHRA PRADESH	07/2019	167.00 -	07/2022 -	07/2022	0/0
38	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]IOCL,ODISHA	01/2020	202.16 -	07/2022 -	07/2022	0/0
39	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	01/2021 -	08/2022	0/0
40	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]IOCL,BIHAR	06/2020	403.00 -	08/2022 -	08/2022	0/0
41	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80 -	08/2021 -	11/2022	0/0
42	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]IOCL,GUJARAT	06/2020	1,378.00	12/2022 -	12/2022	0/0
43	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00 -	04/2022 -	02/2023	0/0
44	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00 -	01/2023 -	05/2023	0/0
45	R and D CAMPUS II AT FARIDABAD - [N16000375]IOCL,HARYANA	06/2019	2,281.94 -	12/2022 07/2023	07/2023	0/0
46	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00 -	04/2022 -	08/2023	0/0
47	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM - [N16000411]IOCL,GUJARAT	10/2020	1,614.00 -	08/2023 -	08/2023	0/0
48	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]IOCL,TAMIL NADU	10/2020	1,398.00 -	12/2023 -	09/2023	0/0
49	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]IOCL,TAMIL NADU	10/2020	921.00 -	09/2023 02/2024	12/2023	0/0
50	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]IOCL,ODISHA	07/2020	13,805.00 -	01/2024 -	01/2024	0/0
51	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]IOCL,GUJARAT	09/2020	18,936.00 -	09/2024 -	08/2024	0/0
52	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA - [N16000412]IOCL,HARYANA	02/2021	34,627.00 -	09/2024 -	09/2024	0/0
53	CGD PROJECT AT REWA DISTRICT - [N16000417]IOCL,MADHYA PRADESH	10/2018	177.00 -	02/2027 -	02/2027	0/0
54	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS - [N16000415]IOCL,BIHAR	10/2018	176.00 -	08/2027 -	08/2027	0/0
55	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS - [N16000420]IOCL,ANDHRA PRADESH	06/2019	2,880.00 -	08/2027 -	08/2027	0/0
56	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS - [N16000422]IOCL,BIHAR	06/2019	439.00 -	02/2028 -	02/2028	0/0
57	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS - [N16000424]IOCL,BIHAR	06/2019	347.00 -	02/2028 -	02/2028	0/0
58	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS - [N16000425]IOCL,BIHAR	06/2019	2,996.00 -	02/2028 -	02/2028	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
59	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS - [N16000427]IOCL,MULTI STATE	06/2019	303.00 -	02/2028 -	02/2028	0/0
60	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS - [N16000416]IOCL,JHARKHAND	10/2018	613.00 -	12/2029 -	12/2029	0/0
61	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS - [N16000421]IOCL,BIHAR	06/2019	988.00 -	12/2029 -	12/2029	0/0
62	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA - [N16000423]IOCL,BIHAR	06/2019	163.00 -	12/2029 -	12/2029	0/0
63	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]IOCL,MULTI STATE	06/2019	169.00 -	12/2029 -	12/2029	0/0
64	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]IOCL,TAMIL NADU	10/2018	2,998.00 -	03/2030 -	03/2030	0/0
65	CGD PROJECT AT SALEM DISTRICT - [N16000419]IOCL,TAMIL NADU	10/2018	1,304.00 -	03/2030 -	03/2030	0/0
66	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-	0/0
<u>Numaligarh Refinery Limited</u>						
67	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY - [N16000379]NRL,ASSAM	01/2019	12,366.00 -	10/2024 -	10/2024	0/0
68	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]NRL,ASSAM	01/2019	10,228.00 -	10/2024 -	10/2024	0/0
<u>Oil & Natural Gas Corporation Limited</u>						
69	REDEVELOPMENT OF NANDASAN FIELD - [N16000404]ONGC,GUJARAT	02/2020	444.87 -	08/2022 -	08/2022	0/0
<u>Oil India Limited</u>						
70	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN - [N16000356]OIL,ASSAM	06/2016	224.75 222.21	08/2020 09/2021	09/2021	0/0
<u>POWER</u>						
<u>Central Public Works Department</u>						
71	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	-	0/0
<u>Chenab Valley Power Projects [P] Limited</u>						
72	KIRU HYDRO ELECTRIC PROJECT - [N18000278]CVPPPL,JAMMU AND KASHMIR	03/2019	4,287.59 -	- 08/2024	08/2024	0/0
73	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	04/2020 -	07/2025	0/0
<u>National Hydro-Electric Power Corporation</u>						
74	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221]NHPC,ARUNACHAL PRADESH	09/2003	6,285.33 19,992.43	09/2010 08/2023	08/2023	0/0
75	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-	0/0
<u>National Thermal Power Corporation</u>						
76	KAWAS SOLAR 56 MW - [N18000283]NTPC,GUJARAT	08/2020	261.80 -	10/2021 01/2022	10/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
77	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]NTPC,TELANGANA	06/2019	401.90 -	04/2021 10/2021	10/2021	0/0
78	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 2,311.89	12/2018 -	11/2021	0/0
79	JETSAR SOLAR 160 MW - [N18000287]NTPC,RAJASTHAN	12/2019	702.28 -	03/2021 11/2021	11/2021	0/0
80	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	11/2018 -	12/2021	0/0
81	KAYAMKULAM SOLAR 70 MW - [N18000288]NTPC,KERALA	09/2019	403.62 -	06/2021 12/2021	12/2021	0/0
82	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]NTPC,RAJASTHAN	01/2020	1,522.71 -	09/2021 10/2022	01/2022	0/0
83	DEVIKOT SOLAR 90MW - [N18000280]NTPC,UTTAR PRADESH	03/2020	501.29 -	09/2021 02/2022	02/2022	0/0
84	DEVIKOT SOLAR 150MW - [N18000281]NTPC,UTTAR PRADESH	01/2020	798.24	09/2021 02/2022	02/2022	0/0
85	FATEHGARH SOLAR 296MW - [N18000289]NTPC,RAJASTHAN	03/2020	1,749.31 -	09/2021 02/2022	02/2022	0/0
86	ETTAYAPURAM SOLAR 230MW - [N18000290]NTPC,TAMIL NADU	03/2020	1,316.22 -	09/2021 02/2022	02/2022	0/0
87	ANTA SOLAR 90 MW - [N18000292]NTPC,RAJASTHAN	01/2021	382.22 -	03/2022 -	03/2022	0/0
88	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]NTPC,GUJARAT	01/2021	842.27 -	07/2022 -	06/2022	0/0
89	BHENSARA 320 MW - [N18000293]NTPC,RAJASTHAN	01/2021	1,221.73 -	07/2022 -	07/2022	0/0
90	CHHATTARGARH 150 MW - [N18000294]NTPC,RAJASTHAN	02/2021	599.99 -	07/2022 -	07/2022	0/0
91	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	09/2021 07/2022	09/2022	0/0
92	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA & RADHANPUR) - [N18000296]NTPC,GUJARAT	05/2021	674.92 -	09/2022 -	09/2022	0/0
93	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	09/2021 07/2022	01/2023	0/0
94	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-	0/0
95	TALAIPELLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-	0/0
Power Grid Corporation Of India Limited						
96	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021	0/0
97	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	06/2021	0/0
98	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021	0/0
99	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	11/2019 07/2021	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
100	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]PGCIL,MULTI STATE	08/2017	1,931.39 -	02/2020 09/2021	09/2021	0/0
101	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	07/2020 12/2020	10/2021	0/0
102	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	07/2019 07/2021	10/2021	0/0
103	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	05/2020 08/2021	10/2021	0/0
104	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]PGCIL,MULTI STATE	02/2017	235.53 -	06/2019 11/2021	11/2021	0/0
105	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	04/2016 12/2017	12/2021	0/0
106	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	03/2018 -	12/2021	0/0
107	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95	12/2019 09/2021	12/2021	0/0
108	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	02/2019 09/2021	02/2022	0/0
109	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	12/2018 12/2021	03/2022	0/0
110	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]PGCIL,MULTI STATE	12/2014	4,754.42 9,129.32	12/2018 03/2024	03/2024	0/0
111	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-	0/0
112	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-	0/0
113	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	-	0/0
114	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-	0/0
115	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-	0/0
116	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	-	0/0
117	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	-	0/0
118	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	-	0/0
119	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPG AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	-	0/0
	<u>Satluj Jal Vidyut Nigam Limited</u>					
120	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]SJVN,HIMACHAL PRADESH	10/2020	687.97 -	11/2025 -	11/2025	0/0
121	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]SJVN,HIMACHAL PRADESH	11/2020	1,810.56 -	01/2026 -	01/2026	0/0
	<u>HEAVY INDUSTRY</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
	<u>Bharat Heavy Electricals Limited</u>					
122	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N2000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-	0/0
	<u>HEALTH AND FAMILY WELFARE</u>					
	<u>Central Public Works Department</u>					
123	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	06/2021 -	05/2022	0/0
124	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]CPWD,JAMMU AND KASHMIR	03/2019	1,404.00 -	09/2023 -	09/2023	0/0
125	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]CPWD,JAMMU AND KASHMIR	03/2019	1,828.00 -	09/2025 -	05/2024	0/0
126	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]CPWD,JAMMU AND KASHMIR	03/2019	1,577.00 -	09/2025 -	09/2025	0/0
	<u>Hill Infra Tech Services Limited</u>					
127	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	04/2020 -	10/2021	0/0
128	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	06/2020 -	10/2021	0/0
129	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]HITES,ASSAM	05/2017	875.00 -	05/2021 09/2022	09/2022	0/0
	<u>Hospital Services Consultancy Corporation Ltd</u>					
130	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018	0/0
131	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC, WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019	0/0
132	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021	0/0
133	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021	0/0
134	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021	0/0
135	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021	0/0
136	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	11/2013 -	09/2021	0/0
137	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	03/2019 -	09/2021	0/0
138	HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC,ANDHRA PRADESH	03/2018	601.02 -	- -	09/2021	0/0
139	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC,MAHARASHTRA	03/2018	582.99 -	- -	09/2021	0/0
140	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	- -	09/2021	0/0
141	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC,DELHI	12/2017	156.56 -	- -	11/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
142	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC,MEGHALAYA	10/2016	363.99 -	05/2018 -	03/2022	0/0
	<u>RAILWAYS</u>					
	<u>Central Railways</u>					
143	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR,MAHARASHTRA	02/1997	2,271.50 -	03/2021 -	03/2023	0/0
144	WARDHA-NANDED MAHARASHTRA - [N22000231]CR,MAHARASHTRA	04/2008	3,168.29 -	03/2023 -	03/2023	0/0
145	KALYAN-KASARA 3RD LINE - [N22000233]CR,MAHARASHTRA	04/2011	792.89 -	03/2021 -	03/2023	0/0
146	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR,MAHARASHTRA	02/2015	1,272.19 -	03/2022 -	03/2023	0/0
147	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]CR,MAHARASHTRA	02/2015	3,627.47 - 3,627.00	03/2024 -	03/2023	0/0
148	DAUND - MANMAD (236 KM) - [N22000360]CR,MAHARASHTRA	02/2016	1,876.00 -	03/2023 -	03/2023	0/0
149	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR,MAHARASHTRA	04/2012	540.02 -	03/2022 -	03/2024	0/0
150	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353]CR,MAHARASHTRA	02/2016	9,968.00 -	03/2024 -	03/2024	0/0
151	PUNE-NASIK (265 KM) - [N22000354]CR,MAHARASHTRA	02/2016	2,425.00 -	03/2024 -	03/2024	0/0
152	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR,MAHARASHTRA	02/2015	2,449.91 -	03/2023 -	03/2024	0/0
153	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR,MAHARASHTRA	02/2016	1,035.16 -	03/2022 -	03/2024	0/0
154	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR,MAHARASHTRA	02/2016	637.95 -	03/2023 -	03/2024	0/0
155	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-	0/0
156	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-	0/0
	<u>Container Corporation Of India</u>					
157	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-	0/0
158	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	-	0/0
159	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI,ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-	0/0
160	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI,CHHATISGARH	05/2014	207.00 -	03/2018 -	-	0/0
161	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI,HARYANA	12/2015	346.32 -	03/2019 -	-	0/0
162	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI,MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
163	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI,GUJARAT	10/2013	343.00	03/2019	-	0/0
164	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI,ANDHRA PRADESH	08/2016	234.50	03/2019	-	0/0
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>					
165	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC,MULTI STATE	10/2006	11,589.00 30,357.00	- -	-	0/0
166	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC,MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-	0/0
	<u>East Central Railways</u>					
167	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR,BIHAR	04/1998	180.82	- 08/2020	08/2020	0/0
168	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR,BIHAR	04/1999	325.00 735.20	- -	03/2021	0/0
169	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002]ECR,BIHAR	04/1996	477.88 751.55	03/2012 09/2021	09/2021	0/0
170	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]ECR,JHARKHAND	03/1999	1,033.07 3,020.95	- 03/2022	03/2022	0/0
171	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR,UTTAR PRADESH	08/2015	528.57	03/2019	03/2022	0/0
172	GARHWA ROAD-RAMNA - [N22000465]ECR,JHARKHAND	03/2015	348.23	03/2021	03/2022	0/0
173	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]ECR,BIHAR	04/1991	329.39	- 03/2022	03/2022	0/0
174	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]ECR,BIHAR	04/1997	324.73 898.53	03/2012 11/2022	11/2022	0/0
175	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303]ECR,BIHAR	04/2003	528.65 2,066.78	- 03/2023	03/2023	0/0
176	KODERMA-TILAIYA (NL), ECR - [220100305]ECR,JHARKHAND	04/2002	459.91 1,625.87	- 03/2023	03/2023	0/0
177	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR,BIHAR	04/2006	378.56	-	03/2023	0/0
178	ARARIA-SUPAUL (NL) - [N22000177]ECR,BIHAR	04/2008	1,605.17	- 03/2023	03/2023	0/0
179	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR,BIHAR	04/2004	372.14 1,470.50	- -	03/2023	0/0
180	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]ECR,BIHAR	04/2009	548.00	03/2020 03/2023	03/2023	0/0
181	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR,BIHAR	04/1997	162.87 614.45	- -	12/2023	0/0
182	BIHTA-AURANGABAD (NL) - [N22000170]ECR,BIHAR	04/2008	326.20	-	03/2024	0/0
183	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR,BIHAR	04/2008	228.05	-	03/2024	0/0
184	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR,UTTAR PRADESH	08/2015	2,436.21	03/2020	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
185	SAGauli VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]ECR,BIHAR	04/2016	744.04 -	03/2021 03/2024	03/2024	0/0
186	MUZAFFARPUR SAGauli DOUBLING 100.60 KM - [N22000473]ECR,BIHAR	04/2016	731.64 -	03/2021 03/2024	03/2024	0/0
187	SAMASTIPUR-DARBANGHA - [N22000329]ECR,BIHAR	05/2015	380.00 -	-	03/2025	0/0
188	KOSI BRIDGE (NL), ECR - [220100304]ECR,BIHAR	04/2002	499.41 516.02	03/2020 -	-	0/0
189	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR,BIHAR	04/2001	406.92 -	-	-	0/0
190	ARA-BHABHUA ROAD (NL) - [N22000166]ECR,BIHAR	04/2008	633.87 -	-	-	0/0
191	NAWADA-LAXMIPUR (NL) - [N22000167]ECR,BIHAR	04/2008	620.57 -	-	-	0/0
192	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR,BIHAR	04/2008	445.25 -	-	-	0/0
193	GAYA-CHATRA (NL) - [N22000169]ECR,MULTI STATE	04/2008	415.67 -	-	-	0/0
194	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR,BIHAR	04/2005	205.00 -	-	-	0/0
195	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR,BIHAR	04/2006	211.00 -	-	-	0/0
196	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR,BIHAR	04/2008	678.62 -	-	-	0/0
197	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR,BIHAR	04/2008	192.56 -	-	-	0/0
198	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR,BIHAR	04/2008	281.30 -	-	-	0/0
199	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR,BIHAR	01/1991	332.15 -	07/2014 -	-	0/0
	<u>East Coast Railway</u>					
200	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR,ODISHA	03/2011	1,111.99 -	02/2019 -	12/2021	0/0
201	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR,ODISHA	03/2012	155.81 238.03	03/2020 -	03/2022	0/0
202	JAGDALPUR-KORAPUT DOUBLING - [N22000376]ECOR,ODISHA	04/2015	1,547.38 1,547.38	03/2022 03/2023	03/2023	0/0
203	BHADRAK - NERGUNDI 3RD LINE - [N22000316]ECOR,ODISHA	03/2013	843.04 843.04	10/2020 03/2024	03/2024	0/0
204	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]ECOR,ANDHRA PRADESH	04/2015	2,499.71 -	03/2022 03/2024	03/2024	0/0
205	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]ECOR,ODISHA	04/2015	701.61 -	11/2018 03/2024	03/2024	0/0
206	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]ECOR,ODISHA	04/2015	1,172.92 1,172.92	12/2018 03/2024	03/2024	0/0
207	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328]ECOR,ODISHA	04/2005	810.78 1,928.07	06/2021 03/2025	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
208	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]ECOR,ODISHA	04/1994	2,923.13 3,791.66	03/2009 03/2026	03/2026	0/0
209	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR,ODISHA	04/2015	2,361.74 -	03/2022 -	03/2026	0/0
	<u>Eastern Railways</u>					
210	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019	0/0
211	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021	0/0
212	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021	0/0
213	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021	0/0
214	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER,MULTI STATE	04/2011	175.80 -	- -	03/2022	0/0
215	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	- -	03/2022	0/0
216	DEOGHAR - SULTANGANJ (NL), ER - [220100273]ER,MULTI STATE	04/2000	607.09 -	02/2013 -	03/2024	0/0
217	MONIGRAM- NIMTITA - [N22000301]ER,MULTI STATE	04/2012	250.93 -	- -	03/2024	0/0
218	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	03/2019 12/2009	03/2025	0/0
219	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER,MULTI STATE	04/1987	406.99 -	03/2006 -	03/2025	0/0
220	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00 -	- -	03/2025	0/0
221	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03 -	- -	03/2025	0/0
222	PIRPAINTI-JASIDIH - [N22000219]ER,MULTI STATE	04/2013	915.98 -	03/2022 -	03/2025	0/0
223	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER,MULTI STATE	04/2001	923.52 -	03/2016 -	03/2025	0/0
224	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER,MULTI STATE	04/2005	595.51 -	03/2017 -	03/2025	0/0
225	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56 -	- -	03/2025	0/0
226	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER,MULTI STATE	04/2010	277.28 -	03/2016 -	03/2025	0/0
227	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]ER,MULTI STATE	04/2010	365.17 -	03/2017 -	03/2025	0/0
228	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55 -	- -	03/2025	0/0
229	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17 -	- -	03/2025	0/0
230	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER,MULTI STATE	04/2010	494.54 -	03/2005 -	03/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
231	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47 -	- -	03/2025	0/0
232	CHANDPARA-BANGAON DOUBLING WITH EXTENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96 -	- -	03/2025	0/0
233	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER,MULTI STATE	04/2009	499.96 -	02/2012 -	03/2025	0/0
234	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER,MULTI STATE	04/2009	257.42 -	03/2014 -	03/2025	0/0
235	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGREGATION OF ARRIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89 -	- -	03/2025	0/0
236	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER,MULTI STATE	04/2011	299.60 -	03/2017 -	03/2026	0/0
	<u>Indian Railway Construction Company Limited</u>					
237	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON,ODISHA	04/2016	5,200.00 -	03/2020 -	03/2024	0/0
	<u>Kolkata Metro Rail Corporation Limited</u>					
238	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -		0/0
	<u>Metropolitan Rapid Transport Projects</u>					
239	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP,MAHARASHTRA	03/1996	495.44 -	03/2004 -	03/2022	0/0
240	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78 -	- -	03/2025	0/0
241	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-	0/0
242	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP,MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-	0/0
243	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-	0/0
244	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP,MAHARASHTRA	04/2012	714.10 -	04/2016 -	-	0/0
	<u>North Central Railway</u>					
245	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR,UTTAR PRADESH	03/2018	4,329.53 -	03/2023 -	06/2025	0/0
246	ETAWAH-MAINPURI (NL),NCR - [220100318]NCR,UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-	0/0
247	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR,MULTI STATE	04/2010	2,030.50 -	- -	-	0/0
	<u>North East Frontier Railway</u>					
248	AMBAR FALAKATA TO NEW MAYNAGURI - [N22000210]NFR,ASSAM	04/2011	314.00 486.96	03/2019 -	06/2021	0/0
249	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]NFR,MULTI STATE	04/2000	1,180.19 2,531.34	12/2008 -	09/2021	0/0
250	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]NFR, WEST BENGAL	04/2016	602.27 -	12/2021 -	09/2021	0/0
251	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR,MULTI STATE	04/2010	241.52 -	- 12/2021	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
252	DIGARU-HOJAI (102 KM) - [N22000389]NFR,ASSAM	04/2015	870.96 -	03/2021 -	03/2022	0/0
253	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR,ASSAM	09/2006	385.20 -	03/2019 -	03/2023	0/0
254	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR,ASSAM	04/2015	2,232.32 -	03/2022 -	03/2023	0/0
255	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR,MANIPUR	04/2003	4,454.17 -	03/2011 -	12/2023	0/0
256	SEVOK RANGPO, NEFR - [N22000102]NFR,SIKKIM	04/2008	1,339.48 4,084.69	12/2015 12/2023	12/2023	0/0
257	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR,MULTI STATE	04/2013	1,798.00 2,042.51	03/2019 -	12/2023	0/0
258	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR,BIHAR	09/2006	532.87 2,132.03	03/2019 -	03/2024	0/0
259	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR,MIZORAM	04/2008	2,393.47 5,021.45	03/2014 -	03/2024	0/0
260	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR,NAGALAND	04/2006	2,326.52 -	03/2015 -	03/2026	0/0
261	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]NFR,WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-	0/0
262	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR,WEST BENGAL	04/2010	221.42 -	- -	-	0/0
263	DIMAPUR-TIZIT NL - [N22000196]NFR,NAGALAND	04/2013	4,274.00 -	03/2020 -	-	0/0
264	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]NFR,MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-	0/0
265	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR,MULTI STATE	04/2010	242.22 -	03/2020 -	-	0/0
266	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR,MULTI STATE	04/1999	819.23 -	- -	-	0/0
267	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR,WEST BENGAL	02/1999	380.60 -	04/2010 -	-	0/0
268	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR,BIHAR	04/2008	333.76 -	- -	-	0/0
269	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-	0/0
<u>North Eastern Railway</u>						
270	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021	0/0
271	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021	0/0
272	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]NER,MULTI STATE	03/2007	243.78 -	12/2021 -	12/2021	0/0
273	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER,UTTAR PRADESH	04/2016	213.00 -	04/2016 -	12/2021	0/0
274	CHHAPRA-BALLIA UP - [N22000134]NER,MULTI STATE	03/2013	295.00 -	01/2019 -	02/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
275	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]NER,UTTAR PRADESH	03/2015	1,295.42	03/2022	03/2022	0/0
276	AUNRIHAR - JAUNPUR PATCH DOUBLING . - [N22000469]NER,UTTAR PRADESH	04/2016	600.00	01/2022	03/2022	0/0
277	ETAH - KASGANJ - NEW LINE - [N22000462]NER,UTTAR PRADESH	04/2017	276.90	04/2017	04/2022	0/0
278	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER,UTTAR PRADESH	04/2017	150.00	04/2017	10/2022	0/0
279	HATHUA-BHATNI (N L) (NER) - [220100319]NER,MULTI STATE	04/2005	230.03	12/2022	12/2022	0/0
280	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50	-	12/2023	0/0
281	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER,UTTAR PRADESH	04/2016	1,900.00	01/2022	03/2025	0/0
282	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45	-	-	0/0
283	ANANDNAGAR GHUGHALI VIA MAHARAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00	-	-	0/0
284	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00	-	-	0/0
285	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92	-	-	0/0
286	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00	01/2018	-	0/0
	<u>North Western Railway</u>					
287	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93	10/2018	01/2020	0/0
288	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09	02/2019	02/2020	0/0
289	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08	12/2019	03/2021	0/0
290	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39	11/2019	03/2021	0/0
291	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR - [N22000152]NWR,RAJASTHAN	04/2013	420.18	03/2020	09/2021	0/0
292	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]NWR,RAJASTHAN	02/1997	410.08	02/2019	06/2022	0/0
293	PHULERA - DIGANA DOUBLING - [N22000326]NWR,MULTI STATE	05/2015	600.00	03/2020	10/2022	0/0
294	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR,RAJASTHAN	08/2018	808.85	08/2022	11/2022	0/0
295	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00	-	-	0/0
296	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUT KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71	-	-	0/0
	<u>Northern Railway</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
297	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00	12/2011	06/2021	0/0
298	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR - [220100133]NR,JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	11/2002	12/2022	0/0
299	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	-	03/2023	0/0
300	UNCHAHAH-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00	-	03/2023	0/0
301	CHANDIGARH-BADDI - [N22000467]NR,MULTI STATE	04/2007	328.14	03/2023	03/2023	0/0
302	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	-	09/2023	0/0
303	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00	07/2012	03/2024	0/0
304	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65	-	03/2024	0/0
305	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	-	03/2024	0/0
306	MANSABHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00	08/2016	08/2025	0/0
307	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83	-	-	0/0
308	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00	03/2016	-	0/0
	<u>National High Speed Rail Corporation Limited</u>					
309	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]NHSRCL,MULTI STATE	12/2015	1,08,000.00	12/2023	12/2023	0/0
	<u>Rail India Technical And Economic Service</u>					
310	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38	-	-	0/0
	<u>Rail Vikas Nigam Ltd.</u>					
311	AHMEDABAD-BOTAD (GC) - [N22000140]RVNL,GUJARAT	04/2012	975.62	12/2021	12/2021	0/0
312	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68	03/2016	12/2021	0/0
313	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48	03/2020	12/2021	0/0
314	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04	03/2020	12/2021	0/0
315	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02	03/2020	12/2021	0/0
316	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85	12/2020	12/2021	0/0
317	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66	12/2021	03/2022	0/0
318	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71	03/2020	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
319	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70	02/2015	06/2022	0/0
320	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01	03/2019	06/2022	0/0
321	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95	03/2019	06/2022	0/0
322	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25	12/2020	12/2022	0/0
323	VIJAYAWADA-GUDUR - [N22000369]RVNL,ANDHRA PRADESH	04/2015	3,246.26	12/2023	12/2023	0/0
324	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]RVNL,UTTAR PRADESH	06/2016	3,677.76	12/2023	12/2023	0/0
325	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60	03/2022	12/2024	0/0
326	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]RVNL,TELANGANA	04/2015	773.94	12/2024	12/2024	0/0
327	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92	03/2023	12/2024	0/0
328	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98	03/2016	03/2025	0/0
329	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51	03/2016	03/2025	0/0
330	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00	12/2024	03/2025	0/0
331	DIGHI PORT NEW LINE - [N22000408]RVNL,MAHARASHTRA	04/2015	723.78	12/2025	03/2025	0/0
332	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42	03/2014	12/2025	0/0
333	BHANUPALI-BILASPUR BERI NL - [N22000273]RVNL,HIMACHAL PRADESH	04/2008	2,966.99	12/2026	12/2025	0/0
334	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67	12/2024	12/2026	0/0
335	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64	12/2017	-	0/0
336	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38	03/2021	-	0/0
	<u>Railway Electrification</u>					
337	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10	03/2012	-	0/0
	<u>South Central Railway</u>					
338	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	03/2022	12/2022	0/0
339	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	03/2000	03/2023	0/0
340	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20	03/2009	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
341	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	03/2023 -	03/2024	0/0
342	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	03/2021 -	03/2024	0/0
343	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	03/2022 -	03/2024	0/0
344	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-	0/0
345	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-	0/0
346	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-	0/0
<u>South East Central Railway</u>						
347	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,413.76	- 08/2020	08/2020	0/0
348	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2020	10/2020	0/0
349	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	12/2021 -	12/2023	0/0
<u>South Eastern Railway</u>						
350	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020	0/0
351	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	12/2018 -	08/2021	0/0
352	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	03/2020 -	02/2022	0/0
353	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	03/2021 -	12/2023	0/0
354	BOWAICHANDI-ARAMBAGH - [N22000159]SER,WEST BENGAL	04/2010	267.37 -	- -	03/2025	0/0
355	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	03/2015 -	03/2025	0/0
356	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	03/2003 -	03/2030	0/0
357	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-	0/0
358	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-	0/0
<u>South Western Railway</u>						
359	YELAHANKA-PENKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	03/2020 -	09/2021	0/0
360	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR,KARNATAKA	04/2011	1,801.01 -	- -	12/2023	0/0
361	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00 -	- -	12/2023	0/0
362	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00 -	- -	12/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
363	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75 -	- -	12/2023	0/0
364	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25 -	- -	12/2023	0/0
365	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	03/2016 -	12/2023	0/0
366	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	03/2002 -	03/2024	0/0
367	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	03/2016 -	03/2024	0/0
368	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	03/2019 -	03/2024	0/0
369	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00 103.74	- -	12/2024	0/0
370	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	03/2017 -	03/2025	0/0
371	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	12/2018 -	06/2025	0/0
372	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85 -	- -	12/2025	0/0
	<u>Southern Railway</u>					
373	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]SR,TAMIL NADU	04/2007	931.98 -	- 08/2021	08/2021	0/0
374	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	03/2005 -	09/2021	0/0
375	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14 -	- -	12/2021	0/0
376	MADURAI-BODINAYAKKANUR - [N22000201]SR,TAMIL NADU	04/2008	164.41 -	- 12/2021	12/2021	0/0
377	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	03/2022 -	06/2022	0/0
378	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	03/2020 -	06/2022	0/0
379	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52 -	- -	03/2024	0/0
380	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68 -	- -	03/2024	0/0
381	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	03/2020 -	03/2025	0/0
382	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	02/2019 -	03/2025	0/0
383	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83 -	- -	12/2025	0/0
384	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	03/2024 -	03/2026	0/0
385	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	03/2019 -	12/2027	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
386	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00	-	-	0/0
387	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40	-	-	0/0
388	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84	02/2019	-	0/0
389	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00	-	-	0/0
390	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96	-	-	0/0
391	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57	-	-	0/0
392	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24	-	-	0/0
393	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26	04/2014	-	0/0
394	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90	-	-	0/0
395	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00	-	-	0/0
396	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00	03/2016	-	0/0
397	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00	03/2018	-	0/0
	<u>Western Railway</u>					
398	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494]WR,GUJARAT	04/2017	691.84	03/2020	09/2021	0/0
399	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]WR,GUJARAT	02/1991	551.51	03/2019	10/2021	0/0
400	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]WR,GUJARAT	04/2011	1,037.15	03/2021	12/2022	0/0
401	SURENDRA NAGAR RAJKOT - [N22000392]WR,GUJARAT	04/2015	1,002.39	03/2021	12/2022	0/0
402	CHOTTAUDEPUR-DHAR(NL) - [N22000138]WR,MULTI STATE	04/2007	1,347.26	03/2022	03/2023	0/0
403	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]WR,MULTI STATE	04/2007	1,640.04	03/2022	03/2023	0/0
404	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]WR,GUJARAT	04/1994	320.66	03/2019	03/2023	0/0
405	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]WR,MADHYA PRADESH	04/2016	700.00	06/2020	03/2023	0/0
406	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]WR,GUJARAT	04/2008	318.24	03/2012	10/2023	0/0
407	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]WR,MADHYA PRADESH	04/2008	3,503.69	03/2022	03/2024	0/0
408	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]WR,GUJARAT	04/2008	829.74	03/2020	03/2024	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
409	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]WR,GUJARAT	04/2011	844.10 844.10	- 03/2024	03/2024	0/0
410	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-	0/0
411	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-	0/0
412	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-	0/0
413	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-	0/0
414	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-	0/0
415	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-	0/0
ROAD TRANSPORT AND HIGHWAYS						
Ministry Of Road Transport And Highways (State Pwds)						
416	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	03/2021	0/0
417	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	04/2021	0/0
418	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	04/2021	0/0
419	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	09/2017	0/0
420	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	12/2019	0/0
421	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019	0/0
422	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 11/2019	11/2019	0/0
423	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2019	12/2019	0/0
424	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020	0/0
425	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	- -	09/2020	0/0
426	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 03/2021	03/2021	0/0
427	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021	0/0
428	REHABILITATION AND UPGRADATION OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	05/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
429	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH, WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021	0/0
430	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO) - [N24000883]MoRTH, WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021	0/0
431	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH, UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021	0/0
432	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH, UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021	0/0
433	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2-LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH, UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021	0/0
434	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774]MoRTH, UTTARAKHAND	12/2017	248.22 -	12/2019 08/2021	08/2021	0/0
435	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH, PUNJAB	10/2017	1,069.59 -	10/2019 -	08/2021	0/0
436	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]MoRTH, NAGALAND	03/2017	217.35 -	11/2020 08/2021	08/2021	0/0
437	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH, UTTAR PRADESH	03/2016	296.50 -	09/2020 -	08/2021	0/0
438	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]MoRTH, ARUNACHAL PRADESH	06/2020	437.60 -	08/2021 -	08/2021	0/0
439	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]MoRTH, ARUNACHAL PRADESH	06/2020	496.47 -	08/2021 -	08/2021	0/0
440	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH, MADHYA PRADESH	11/2015	628.45 -	01/2020 06/2021	09/2021	0/0
441	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH, MADHYA PRADESH	12/2015	957.54 -	02/2020 04/2021	09/2021	0/0
442	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779]MoRTH, UTTARAKHAND	02/2018	418.88 -	02/2020 09/2021	09/2021	0/0
443	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH, MADHYA PRADESH	03/2018	166.21 -	08/2018 08/2021	09/2021	0/0
444	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881]MoRTH, MADHYA PRADESH	11/2017	184.62 -	02/2018 09/2021	09/2021	0/0
445	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890]MoRTH, MADHYA PRADESH	03/2018	217.22 -	08/2018 09/2021	09/2021	0/0
446	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH, MADHYA PRADESH	01/2017	373.82 -	09/2019 06/2021	09/2021	0/0
447	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]MoRTH, ASSAM	09/2018	160.00 -	09/2021 -	09/2021	0/0
448	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]MoRTH, NAGALAND	10/2016	167.62 -	12/2020 09/2021	09/2021	0/0
449	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]MoRTH, NAGALAND	10/2016	172.63 -	12/2020 09/2021	09/2021	0/0
450	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH, UTTAR PRADESH	03/2018	306.59 -	- -	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
451	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]MoRTH,CHHATISGARH	11/2017	188.80 -	05/2019 09/2021	09/2021	0/0
452	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]MoRTH,CHHATISGARH	12/2014	379.16 -	11/2017 09/2021	09/2021	0/0
453	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]MoRTH,ARUNACHAL PRADESH	03/2021	182.55 -	09/2021 -	09/2021	0/0
454	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]MoRTH,CHHATISGARH	12/2015	291.05 -	- 10/2021	10/2021	0/0
455	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780]MoRTH,UTTARAKHAND	02/2018	293.68 -	- 10/2021	10/2021	0/0
456	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820]MoRTH,A & N ISLANDS	11/2017	237.80 237.80	11/2019 10/2021	10/2021	0/0
457	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870]MoRTH,MADHYA PRADESH	03/2018	162.56 -	03/2018 10/2021	10/2021	0/0
458	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]MoRTH,WEST BENGAL	01/2017	396.86 396.86	09/2019 11/2021	10/2021	0/0
459	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891]MoRTH,MADHYA PRADESH	03/2018	233.04 -	03/2018 10/2021	10/2021	0/0
460	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	03/2018 06/2021	10/2021	0/0
461	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	08/2020 -	10/2021	0/0
462	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]MoRTH,CHHATISGARH	11/2015	335.32 -	06/2017 10/2021	10/2021	0/0
463	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]MoRTH,CHHATISGARH	03/2017	423.79 -	01/2018 10/2021	10/2021	0/0
464	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894]MoRTH,MADHYA PRADESH	02/2018	279.44 -	03/2018 11/2021	11/2021	0/0
465	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	07/2018 05/2021	11/2021	0/0
466	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]MoRTH,MADHYA PRADESH	01/2019	264.50 -	03/2021 11/2021	11/2021	0/0
467	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]MoRTH,MIZORAM	11/2010	624.41 -	03/2011 12/2021	12/2021	0/0
468	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]MoRTH,MIZORAM	08/2010	193.69 -	10/2010 12/2021	12/2021	0/0
469	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	- 03/2021	12/2021	0/0
470	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415]MoRTH,MIZORAM	08/2010	195.04 -	10/2010 12/2021	12/2021	0/0
471	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775]MoRTH,UTTARAKHAND	06/2017	282.08 -	06/2019 12/2021	12/2021	0/0
472	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781]MoRTH,UTTARAKHAND	05/2018	248.00 -	05/2020 12/2021	12/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
473	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99 327.00	- -	12/2021	0/0
474	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	03/2017 06/2021	12/2021	0/0
475	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	07/2018 08/2021	12/2021	0/0
476	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	06/2019 04/2021	12/2021	0/0
477	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]MoRTH,MAHARASHTRA	03/2016	536.65 356.00	12/2019 12/2021	12/2021	0/0
478	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]MoRTH,MIZORAM	08/2010	186.96 -	09/2014 12/2021	12/2021	0/0
479	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	04/2020 -	12/2021	0/0
480	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J) - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	08/2020 -	12/2021	0/0
481	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]MoRTH,CHHATISGARH	01/2016	476.20 543.73	09/2016 12/2021	12/2021	0/0
482	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]MoRTH,CHHATISGARH	01/2016	624.98 731.50	10/2016 12/2021	12/2021	0/0
483	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880]MoRTH,WEST BENGAL	02/2018	426.18 426.18	09/2020 01/2022	01/2022	0/0
484	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	11/2018 01/2021	03/2022	0/0
485	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893]MoRTH,MADHYA PRADESH	11/2017	254.17 -	02/2018 03/2022	03/2022	0/0
486	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]MoRTH,CHHATISGARH	12/2014	496.02 -	03/2015 03/2022	03/2022	0/0
487	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	03/2018 04/2021	04/2022	0/0
488	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]MoRTH,ASSAM	11/2010	268.08 -	05/2017 05/2022	05/2022	0/0
489	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	03/2018 09/2021	06/2022	0/0
490	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]MoRTH,CHHATISGARH	01/2016	497.14 572.66	08/2016 06/2022	06/2022	0/0
491	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887]MoRTH,WEST BENGAL	06/2016	236.78 263.26	08/2019 08/2022	08/2022	0/0
492	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	08/2019 -	11/2022	0/0
493	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	08/2017 06/2021	12/2022	0/0
494	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- - [N24001180]MoRTH,NAGALAND	03/2019	237.51 -	12/2022 -	12/2022	0/0
495	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]MoRTH,CHHATISGARH	03/2016	452.94 435.61	07/2016 12/2022	12/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
496	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243]MoRTH,ASSAM	03/2020	166.94 -	12/2020 12/2022	12/2022	0/0
497	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]MoRTH,TRIPURA	01/2017	197.67 -	12/2022 -	12/2022	0/0
498	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	05/2021 -	12/2022	0/0
499	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	03/2021 -	03/2023	0/0
500	BALANCE WORK OF 2-LANING OF LONGDING- TISSA- KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACHAL - [N24001373]MoRTH,ARUNACHAL PRADESH	01/2020	358.26 -	02/2024 -	02/2024	0/0
501	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACHAL - [N24001372]MoRTH,ARUNACHAL PRADESH	02/2021	588.09 -	03/2024 -	03/2024	0/0
502	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-	0/0
503	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-	0/0
504	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-	0/0
505	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 369.92	08/2013 06/2021	-	0/0
506	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.90	08/2013 06/2021	-	0/0
507	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.58	02/2013 06/2021	-	0/0
508	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-	0/0
509	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-	0/0
510	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-	0/0
511	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH,BIHAR	01/1991	675.00 780.77	- -	-	0/0
512	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH,PUNJAB	11/2015	889.24 -	- -	-	0/0
513	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH,MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-	0/0
514	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH,GOA	10/2015	936.40 -	- -	-	0/0
515	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH,UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-	0/0
516	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH,GOA	12/2015	773.98 -	- -	-	0/0
517	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH,GOA	12/2015	819.95 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
518	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH,ODISHA	12/2011	191.08 -	08/2015 -	-	0/0
519	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH,BIHAR	01/1991	319.68 -	- -	-	0/0
520	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH,BIHAR	11/2013	683.83 683.82	07/2016 -	-	0/0
521	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH,BIHAR	02/2016	178.85 -	05/2016 -	-	0/0
522	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH,BIHAR	02/2016	553.30 -	05/2016 -	-	0/0
523	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH,BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-	0/0
524	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH,MAHARASHTRA	03/2016	1,142.62 -	- -	-	0/0
525	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH,MAHARASHTRA	03/2016	1,101.58 -	- -	-	0/0
526	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH,BIHAR	08/2016	1,742.01 -	12/2016 -	-	0/0
527	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH,ODISHA	03/2014	191.50 192.00	05/2016 -	-	0/0
528	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH,ODISHA	08/2013	171.96 172.00	06/2016 -	-	0/0
529	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH,UTTARAKHAND	03/2018	460.73 -	- -	-	0/0
530	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH,HARYANA	01/2017	247.25 -	03/2019 -	-	0/0
531	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-	0/0
532	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	-	0/0
533	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA. - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-	0/0
534	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-	0/0
535	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-	0/0
536	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-	0/0
537	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-	0/0
538	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-	0/0
539	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-	0/0
540	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-	0/0
541	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
542	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-	0/0
543	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-	0/0
544	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-	0/0
545	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-	0/0
546	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNAGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-	0/0
547	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-	0/0
548	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-	0/0
549	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-	0/0
550	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-	0/0
551	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-	0/0
552	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-	0/0
553	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-	0/0
554	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-	0/0
555	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-	0/0
556	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-	0/0
557	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-	0/0
558	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	-	-	0/0
559	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	-	-	0/0
560	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-	0/0
561	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-	0/0
562	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-	0/0
563	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-	0/0
564	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-	0/0
565	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
566	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-	0/0
567	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-	0/0
568	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-	0/0
569	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-	0/0
570	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-	0/0
571	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-	0/0
572	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-	0/0
573	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-	0/0
574	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-	0/0
575	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-	0/0
576	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-	0/0
577	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-	0/0
578	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-	0/0
579	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-	0/0
580	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-	0/0
581	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-	0/0
582	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	-	0/0
583	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-	0/0
584	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-	0/0
585	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-	0/0
586	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-	0/0
587	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-	0/0
588	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-	0/0
589	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
590	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-	0/0
591	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-	0/0
592	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-	0/0
593	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-	0/0
594	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-	0/0
595	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-	0/0
596	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-	0/0
597	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-	0/0
598	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260 - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	-	0/0
599	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-	0/0
600	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-	0/0
601	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	-	0/0
602	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	-	0/0
603	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	-	0/0
604	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-	0/0
605	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-	0/0
606	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-	0/0
607	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-	0/0
608	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-	0/0
609	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-	0/0
610	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-	0/0
611	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-	0/0
612	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-	0/0
613	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
614	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-	0/0
615	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-	0/0
616	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-	0/0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>					
617	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL,ARUNACHAL PRADESH	09/2016	568.92 -	- 11/2021	03/2022	0/0
618	KHELLANI-KHANABAL PKG-3 - [N24001341]NHIDCL,JAMMU AND KASHMIR	03/2021	398.51 -	12/2022 -	12/2022	0/0
619	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]NHIDCL,JAMMU AND KASHMIR	03/2021	260.40 -	12/2022 -	12/2022	0/0
620	MARIAM - PEREN PKG-1A - [N24001349]NHIDCL,MANIPUR	02/2021	226.32 -	12/2022 -	12/2022	0/0
621	MARIAM - PEREN (PKG 1B) - [N24001350]NHIDCL,MANIPUR	02/2021	188.36 -	12/2022 -	12/2022	0/0
622	MARIAM - PEREN PKG-2B - [N24001351]NHIDCL,MANIPUR	02/2021	232.26 -	12/2022 -	12/2022	0/0
623	IMPHAL – MOREH PACKAGE- 3 - [N24001352]NHIDCL,MANIPUR	03/2021	259.31 -	12/2022 -	12/2022	0/0
624	IMPHAL - KHONGSANG PKG-2 - [N24001353]NHIDCL,MANIPUR	03/2021	195.14 -	12/2022 -	12/2022	0/0
625	TAMENGLONG - MAHUR PKG-3 - [N24001354]NHIDCL,MANIPUR	03/2021	234.08 -	12/2022 -	12/2022	0/0
626	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]NHIDCL,MIZORAM	03/2021	374.39 -	12/2022 -	12/2022	0/0
627	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]NHIDCL,MIZORAM	03/2021	233.25 -	12/2022 -	12/2022	0/0
628	TLABUNG - LUNGLEI PKG-A - [N24001358]NHIDCL,MIZORAM	03/2021	698.44 -	12/2022 -	12/2022	0/0
629	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]NHIDCL,MEGHALAYA	03/2021	260.21 -	12/2022 -	12/2022	0/0
630	MANU-SIMLUNG (PKG 4) - [N24001363]NHIDCL,TRIPURA	03/2021	354.79 -	12/2022 -	12/2022	0/0
631	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]NHIDCL,ASSAM	03/2021	636.42 -	12/2022 -	12/2022	0/0
632	KARGIL-ZANSKR PACKAGE-1 - [N24001343]NHIDCL,LADAKH	03/2021	384.23 -	01/2023 -	01/2023	0/0
633	KARGIL-ZANSKR PACKAGE-2 - [N24001344]NHIDCL,LADAKH	03/2021	404.89 -	01/2023 -	01/2023	0/0
634	KARGIL-ZANSKR PACKAGE-3 - [N24001345]NHIDCL,LADAKH	08/2020	381.01 -	01/2023 -	01/2023	0/0
635	KARGIL-ZANSKR PACKAGE-8 - [N24001348]NHIDCL,LADAKH	03/2021	398.37 -	01/2023 -	01/2023	0/0
636	TLABUNG - LUNGLEI PKG-B - [N24001359]NHIDCL,MIZORAM	03/2021	740.58 -	01/2023 -	01/2023	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
637	DABOKA KATHKATI PACKAGE-5 - [N24001366]NHIDCL,ASSAM	03/2021	288.85	01/2023	01/2023	0/0
638	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]NHIDCL,MIZORAM	03/2021	674.71	06/2023	06/2023	0/0
639	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]NHIDCL,SIKKIM	01/2021	332.20	09/2023	09/2023	0/0
640	DABOKA KATHKATI PACKAGE-4 - [N24001365]NHIDCL,ASSAM	02/2021	260.07	12/2023	12/2023	0/0
641	DABOKA KATHKATI PACKAGE-2 - [N24001364]NHIDCL,ASSAM	03/2021	335.88	01/2024	01/2024	0/0
642	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]NHIDCL,ASSAM	03/2021	286.72	01/2024	01/2024	0/0
643	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]NHIDCL,SIKKIM	12/2020	410.60	02/2024	02/2024	0/0
644	KARGIL-ZANSKR PACKAGE-6 - [N24001346]NHIDCL,LADAKH	01/2021	239.81	05/2024	05/2024	0/0
645	KARGIL-ZANSKR PACKAGE-7 - [N24001347]NHIDCL,LADAKH	01/2021	308.86	06/2024	06/2024	0/0
National Highways Authority Of India						
646	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05	-	06/2021	0/0
647	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00	07/2021	07/2021	0/0
648	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89	11/2019	11/2019	0/0
649	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46	11/2019	11/2019	0/0
650	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75	11/2019	11/2019	0/0
651	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00	05/2008	06/2019	0/0
652	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61	04/2010	07/2019	0/0
653	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00	06/2008	09/2019	0/0
654	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18	06/2019	09/2019	0/0
655	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24	01/2020	01/2020	0/0
656	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07	08/2016	06/2020	0/0
657	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00	03/2008	08/2020	0/0
658	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00	12/2009	09/2020	0/0
659	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00	07/2015	09/2020	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
660	SRINAGAR TO BANIHAL - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70	06/2014	10/2020	0/0
661	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00	03/2019	11/2020	0/0
662	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01	08/2016	12/2020	0/0
663	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20	04/2020	12/2020	0/0
664	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30	06/2021	12/2020	0/0
665	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21	-	01/2021	0/0
666	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00	04/2008	02/2021	0/0
667	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09	-	02/2021	0/0
668	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90	-	03/2021	0/0
669	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96	-	03/2021	0/0
670	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48	03/2020	05/2021	0/0
671	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76	-	07/2021	0/0
672	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64	-	07/2021	0/0
673	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92	-	07/2021	0/0
674	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00	05/2013	08/2021	0/0
675	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96	11/2018	08/2021	0/0
676	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56	-	08/2021	0/0
677	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94	05/2021	08/2021	0/0
678	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48	-	08/2021	0/0
679	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838]NHAI,RAJASTHAN	03/2018	874.25	08/2021	08/2021	0/0
680	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55	03/2013	09/2021	0/0
681	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00	06/2013	09/2021	0/0
682	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90	04/2018	09/2021	0/0
683	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72	04/2019	09/2021	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
684	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	06/2020 -	09/2021	0/0
685	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	- -	09/2021	0/0
686	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	- -	10/2021	0/0
687	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	- -	11/2021	0/0
688	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	07/2018 -	12/2021	0/0
689	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	07/2019 -	12/2021	0/0
690	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	07/2019 -	12/2021	0/0
691	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250 (DESIGN CHAINAGE KM 0.000 TO KM 65 - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	03/2020 -	12/2021	0/0
692	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	04/2020 -	12/2021	0/0
693	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	07/2016 -	12/2021	0/0
694	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	- -	12/2021	0/0
695	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302]NHAI,TAMIL NADU	07/2020	3,426.00 -	12/2021 -	12/2021	0/0
696	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	04/2014 -	01/2022	0/0
697	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	08/2018 -	01/2022	0/0
698	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	- -	01/2022	0/0
699	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92 -	- -	01/2022	0/0
700	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21 -	- -	01/2022	0/0
701	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	08/2017 -	02/2022	0/0
702	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53 -	- -	02/2022	0/0
703	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]NHAI,MAHARASHTRA	10/2015	531.13 -	05/2018 03/2022	03/2022	0/0
704	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00 -	- -	03/2022	0/0
705	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	03/2019 -	03/2022	0/0
706	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE- - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95 -	- -	03/2022	0/0
707	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09 -	- -	03/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
1	2	3	4	5	6	7
708	CONSTRUCTION OF SIX LANE OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43 -	- -	03/2022	0/0
709	FOUR LANE OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71 -	- -	03/2022	0/0
710	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	03/2019 12/2021	06/2022	0/0
711	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	08/2017 -	07/2022	0/0
712	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	09/2017 -	07/2022	0/0
713	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	03/2019 01/2021	09/2022	0/0
714	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	03/2020 -	09/2022	0/0
715	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	03/2014 -	12/2022	0/0
716	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35 -	- -	12/2022	0/0
717	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]NHAI,UTTAR PRADESH	10/2020	724.60 720.81	03/2023 -	03/2023	0/0
718	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-	0/0
719	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-	0/0
720	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-	0/0
721	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-	0/0
722	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-	0/0
723	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-	0/0
724	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-	0/0
725	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-	0/0
726	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-	0/0
727	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-	0/0
728	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-	0/0
729	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-	0/0
730	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-	0/0
731	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
732	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-	0/0
733	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-	0/0
734	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI,BIHAR	10/2011	375.09 -	04/2014 -	-	0/0
735	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI,BIHAR	05/2011	511.54 -	11/2013 -	-	0/0
736	PANIKHOLI-RIMOLI - [N24000197]NHAI,ODISHA	03/2012	1,410.00 -	09/2014 -	-	0/0
737	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI,MULTI STATE	09/2011	754.00 -	03/2013 -	-	0/0
738	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI,ODISHA	12/2011	1,047.00 -	06/2014 -	-	0/0
739	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI,WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-	0/0
740	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI,UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-	0/0
741	ETAWAH CHAKERI - [N24000219]NHAI,UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-	0/0
742	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - [N24000232]NHAI,HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-	0/0
743	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI,TELANGANA	04/2014	1,266.60 -	09/2016 -	-	0/0
744	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI,RAJASTHAN	09/2014	425.19 -	09/2016 -	-	0/0
745	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI,TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-	0/0
746	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI,TAMIL NADU	06/2015	563.92 -	12/2017 -	-	0/0
747	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI,UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-	0/0
748	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI,TAMIL NADU	07/2014	401.11 -	01/2017 -	-	0/0
749	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI,UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-	0/0
750	VADODARA-SURAT SECTION - [N24000361]NHAI,GUJARAT	03/2014	503.16 -	08/2016 -	-	0/0
751	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI,UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-	0/0
752	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI,UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-	0/0
753	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI,ODISHA	07/2015	1,282.94 -	- -	-	0/0
754	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI,WEST BENGAL	10/2015	361.15 363.93	- -	-	0/0
755	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
756	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-	0/0
757	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-	0/0
758	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-	0/0
759	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-	0/0
760	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-	0/0
761	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI, WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-	0/0
762	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-	0/0
763	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-	0/0
764	FOUR LANING OF RAMBAN - BANIHAI SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-	0/0
765	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-	0/0
766	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-	0/0
767	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-	0/0
768	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-	0/0
769	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-	0/0
770	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-	0/0
771	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-	0/0
772	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-	0/0
773	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-	0/0
774	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-	0/0
775	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-	0/0
776	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-	0/0
777	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-	0/0
778	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-	0/0
779	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI,BIHAR	08/2015	322.09 247.00	04/2018 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
780	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-	0/0
781	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-	0/0
782	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-	0/0
783	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-	0/0
784	FOUR LANING FROM MP/MAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-	0/0
785	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-	0/0
786	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44 - [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-	0/0
787	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-	0/0
788	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-	0/0
789	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-	0/0
790	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR-HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-	0/0
791	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-	0/0
792	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-	0/0
793	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-	0/0
794	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-	0/0
795	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-	0/0
796	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-	0/0
797	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI, UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-	0/0
798	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-	0/0
799	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI, UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-	0/0
800	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI, UTTARAKHAND	03/2016	720.00 -	- -	-	0/0
801	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF NH-73) TO KM 17.900 - [N24000562]NHAI, UTTARAKHAND	03/2016	1,443.00 -	- -	-	0/0
802	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI, UTTAR PRADESH	03/2016	1,668.00 -	- -	-	0/0
803	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI, UTTAR PRADESH	03/2016	1,408.00 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
804	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-	0/0
805	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	-	0/0
806	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-	0/0
807	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000 TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-	0/0
808	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-	0/0
809	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-	0/0
810	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-	0/0
811	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-	0/0
812	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS- WEST BENGAL BORDER SECTION OF NH - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-	0/0
813	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-	0/0
814	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-	0/0
815	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	-	0/0
816	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-	0/0
817	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-	0/0
818	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-	0/0
819	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-	0/0
820	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-	0/0
821	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-	0/0
822	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-	0/0
823	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-	0/0
824	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-	0/0
825	4-LANNING OF KODEBAD-DHARTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-	0/0
826	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-	0/0
827	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
828	REHABILITATION AND UPGRADATION TO FOUR LANE OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-	0/0
829	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-	0/0
830	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-	0/0
831	4 LANNING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-	0/0
832	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-	0/0
833	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 1,361.00	- -	-	0/0
834	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-	0/0
835	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-	0/0
836	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-	0/0
837	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-	0/0
838	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-	0/0
839	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-	0/0
840	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-	0/0
841	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-	0/0
842	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-	0/0
843	REHABILITATION AND UPGRADATION BY 4-LANNING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-	0/0
844	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-	0/0
845	SIX LANNING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-	0/0
846	SIX LANNING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-	0/0
847	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-	0/0
848	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-	0/0
849	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-	0/0
850	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-	0/0
851	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
852	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJI WAL (KM 283.500 OF NH 65 NAGPUR ROAD) SECTION - [N24000711]NHAI, RAJASTHAN	12/2017	1,308.73 -	- -	-	0/0
853	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI, UTTAR PRADESH	12/2017	1,232.21 -	- -	-	0/0
854	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI, BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-	0/0
855	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI, ODISHA	12/2017	686.65 -	- -	-	0/0
856	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI, ODISHA	12/2017	417.51 -	- -	-	0/0
857	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI, ANDHRA PRADESH	12/2017	328.67 -	- -	-	0/0
858	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTING - [N24000719]NHAI, ANDHRA PRADESH	12/2017	1,323.15 -	- -	-	0/0
859	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE OF - [N24000720]NHAI, ANDHRA PRADESH	12/2017	357.00 -	- -	-	0/0
860	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARPUR - [N24000721]NHAI, UTTAR PRADESH	12/2017	207.00 -	- -	-	0/0
861	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI, UTTAR PRADESH	12/2017	305.00 -	- -	-	0/0
862	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI, BIHAR	01/2018	573.70 -	- -	-	0/0
863	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI, BIHAR	01/2018	895.39 -	- -	-	0/0
864	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI, JHARKHAND	01/2018	273.46 -	- -	-	0/0
865	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI, JHARKHAND	01/2018	1,155.16 -	- -	-	0/0
866	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI, MADHYA PRADESH	01/2018	770.73 -	- -	-	0/0
867	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI, ODISHA	01/2018	668.86 -	- -	-	0/0
868	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI, ODISHA	01/2018	686.65 -	- -	-	0/0
869	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI, ODISHA	01/2018	1,522.00 -	- -	-	0/0
870	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI, ODISHA	01/2018	999.00 -	- -	-	0/0
871	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI, ODISHA	01/2018	503.88 -	- -	-	0/0
872	VARANASI RING ROAD PKG - I - [N24000740]NHAI, UTTAR PRADESH	01/2018	450.77 -	- -	-	0/0
873	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI, TELANGANA	03/2017	4,429.00 -	03/2017 -	-	0/0
874	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI, KARNATAKA	02/2018	486.78 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
875	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-	0/0
876	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-	0/0
877	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-	0/0
878	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-	0/0
879	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-	0/0
880	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-	0/0
881	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI,RAJASTHAN	02/2018	1,103.88 -	- -	-	0/0
882	CONSTRUCTION/ UP-GRADATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI,RAJASTHAN	02/2018	741.86 -	- -	-	0/0
883	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-	0/0
884	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-	0/0
885	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-	0/0
886	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-	0/0
887	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI,TELANGANA	03/2018	802.65 -	- -	-	0/0
888	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-	0/0
889	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-	0/0
890	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-	0/0
891	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-	0/0
892	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI,TELANGANA	03/2018	950.63 -	- -	-	0/0
893	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI,TELANGANA	03/2018	857.62 -	- -	-	0/0
894	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHTRA - [N24000825]NHAI,TELANGANA	03/2018	828.29 -	- -	-	0/0
895	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-	0/0
896	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-	0/0
897	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-	0/0
898	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
899	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI, GUJARAT	03/2018	1,161.39 -	- -	-	0/0
900	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI, HARYANA	03/2018	275.12 -	- -	-	0/0
901	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING - [N24000837]NHAI, HARYANA	03/2018	307.79 -	- -	-	0/0
902	SIX LANE AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI, HARYANA	03/2018	634.70 -	- -	-	0/0
903	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI, RAJASTHAN	03/2018	1,158.35 -	- -	-	0/0
904	SIX LANE AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI, HARYANA	03/2018	795.50 906.65	- -	-	0/0
905	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI, PUNJAB	03/2018	199.90 -	- -	-	0/0
906	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI, PUNJAB	03/2018	196.05 -	- -	-	0/0
907	SIX LANE OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI, ODISHA	03/2018	806.11 -	- -	-	0/0
908	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI, HARYANA	03/2018	198.05 -	- -	-	0/0
909	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI, HARYANA	03/2018	181.78 -	- -	-	0/0
910	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI, HARYANA	03/2018	551.58 -	- -	-	0/0
911	FOUR LANE OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI, HIMACHAL PRADESH	03/2018	478.74 -	- -	-	0/0
912	FOUR LANE OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI, MAHARASHTRA	03/2018	642.13 -	- -	-	0/0
913	4-LANE OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI, JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-	0/0
914	SIX LANE OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI, UTTAR PRADESH	11/2017	2,159.00 -	01/2019	-	0/0
915	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI, HARYANA	01/2019	1,051.91 -	- -	-	0/0
916	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI, HARYANA	01/2019	1,120.06 -	- -	-	0/0
917	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI, HARYANA	01/2019	1,137.42 -	- -	-	0/0
918	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI, HARYANA	01/2019	1,033.19 -	- -	-	0/0
919	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI, HARYANA	01/2019	1,243.45 -	- -	-	0/0
920	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI, HARYANA	01/2019	889.36 -	- -	-	0/0
921	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI, HARYANA	01/2019	1,018.79 -	- -	-	0/0
922	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI, HARYANA	01/2019	996.65 -	- -	-	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
923	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-	0/0
924	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-	0/0
925	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-	0/0
926	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-	0/0
927	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-	0/0
928	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-	0/0
929	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-	0/0
930	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-	0/0
931	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-	0/0
932	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-	0/0
	<u>TELECOMMUNICATIONS</u>					
	<u>Bharat Sanchar Nigam Limited</u>					
933	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	06/2021 -	11/2021	0/0
	<u>Department Of Telecommunication</u>					
934	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	07/2015 05/2020	03/2022	0/0
	<u>URBAN DEVELOPMENT</u>					
	<u>Central Public Works Department</u>					
935	CONSTRUCTION729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]CPWD,CHHATISGARH	05/2019	299.97 299.97	09/2020 01/2023	01/2023	0/0
936	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]CPWD,DELHI	10/2016	422.00 422.00	03/2021 06/2023	06/2023	0/0
937	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	03/2022 -	06/2023	0/0
	<u>Kochi Metro Rail Corporation Ltd</u>					
938	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	-	0/0
	<u>Lucknow Metro Rail Corporation Limited</u>					
939	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	03/2024 -	03/2025	0/0
940	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	03/2024 -	05/2025	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
SI.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
941	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-	0/0
	<u>Maharashtra Metro Rail Corporation Ltd.</u>					
942	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]MMRC,MAHARASHTRA	12/2016	11,420.00 11,420.00	11/2021 12/2022	12/2022	0/0
	<u>Mumbai Metro Rail Corporation Ltd</u>					
943	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]MMRCL,MAHARASHTRA	07/2013	23,136.00 -	03/2020 03/2023	03/2023	0/0
	<u>Madhya Pradesh Metro Rail Co Limited</u>					
944	BHOPAL METRO RAIL - [N28000124]MPMRCL,MADHYA PRADESH	11/2018	6,941.40 -	02/2023 -	02/2023	0/0
945	INDORE METRO RAIL - [N28000125]MPMRCL,MADHYA PRADESH	11/2018	7,500.80 -	02/2023 -	02/2023	0/0
	<u>Nagpur Metro Rail Corporation Ltd</u>					
946	NAGPUR METRO RAIL - [N28000085]NMRCL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019	0/0
	<u>National Capital Region Transport Corp</u>					
947	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]NCRTC,MULTI STATE	03/2019	30,274.00 -	06/2025 -	06/2025	0/0
	<u>Patna Metro Rail Corporation</u>					
948	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]PATNA METRO RAI,BIHAR	02/2019	13,365.77 13,925.50	06/2024 -	06/2024	0/0
	<u>WATER RESOURCES</u>					
	<u>Brahmaputra Board</u>					
949	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	12/2019 -	12/2021	0/0
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>					
950	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021	0/0
951	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021	0/0
952	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021	0/0
953	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021	0/0
954	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021	0/0
955	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]BUIDCO,BIHAR	03/2018	294.02 -	10/2021 -	10/2021	0/0
956	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	08/2021 -	12/2021	0/0
957	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]BUIDCO,BIHAR	08/2017	578.89 -	06/2022 -	06/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
958	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]BUIDCO,BIHAR	08/2017	824.00 -	06/2022 -	06/2022	0/0
959	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-	0/0
960	I AND D AND STP AT CHAPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	-	0/0
961	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-	0/0
962	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-	0/0
	<u>Delhi Jal Board</u>					
963	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021	0/0
964	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]DJB,DELHI	03/2017	665.78 -	12/2022 -	12/2022	0/0
965	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	12/2021 -	12/2022	0/0
966	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	02/2022 -	12/2022	0/0
967	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -		0/0
	<u>Kolkata Metropolitan Development Authority</u>					
968	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA, WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021	0/0
969	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]KMDA, WEST BENGAL	08/2017	185.22 -	12/2021 -	12/2021	0/0
970	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI - [N30000048]KMDA, WEST BENGAL	01/2018	172.10 -	12/2021 -	12/2021	0/0
971	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]KMDA, WEST BENGAL	10/2017	164.93 -	12/2021 -	12/2021	0/0
972	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]KMDA, WEST BENGAL	01/2019	384.96 -	04/2022 -	04/2022	0/0
973	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPUR - [N30000030]KMDA, WEST BENGAL	03/2019	287.53 -	04/2022 -	04/2022	0/0
974	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]KMDA, WEST BENGAL	12/2018	234.31 -	04/2022 -	04/2022	0/0
975	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	02/2022 -	06/2022	0/0
976	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]KMDA, WEST BENGAL	03/2018	165.16 -	06/2022 -	06/2022	0/0
977	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]KMDA, WEST BENGAL	08/2017	307.12 -	09/2022 -	09/2022	0/0
978	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	02/2022 -	10/2022	0/0
979	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA, WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	-	0/0
	<u>Uttar Pradesh Jal Nigam</u>					

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
980	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021	0/0
981	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021	0/0
982	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021	0/0
983	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]UPJalNigam,UTTAR PRADESH	03/2019	271.39 -	08/2021 -	08/2021	0/0
984	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]UPJalNigam,UTTAR PRADESH	05/2017	767.59 -	09/2021 -	09/2021	0/0
985	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]UPJalNigam,UTTAR PRADESH	03/2018	904.00 -	09/2021 -	09/2021	0/0
986	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]UPJalNigam,UTTAR PRADESH	03/2018	967.23 -	09/2021 -	09/2021	0/0
987	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]UPJalNigam,UTTAR PRADESH	01/2019	206.05 -	10/2021 -	10/2021	0/0
988	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]UPJalNigam,UTTAR PRADESH	01/2019	231.79 -	12/2021 -	12/2021	0/0
989	FARRUKHABAD I AND D AND STP WORKS - HAM - [N30000008]UPJalNigam,UTTAR PRADESH	10/2017	213.62 261.12	03/2022 -	03/2022	0/0
990	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]UPJalNigam,UTTAR PRADESH	02/2019	681.78 -	06/2022 -	06/2022	0/0
991	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	07/2021 -	06/2022	0/0
992	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	-	0/0
	<u>Uttarakhand Pey Jal Nigam</u>					
993	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-	0/0
	<u>COMMERCE</u>					
	<u>National Building Construcion Corporation Ltd</u>					
994	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 302.64	10/2020 -	-	0/0
	<u>DEPARTMENT OF HIGHER EDUCATION</u>					
	<u>Central Public Works Department</u>					
995	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA - [N28000140]CPWD,KERALA	07/2019	753.63 -	03/2021 -	06/2022	0/0
996	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]CPWD,HIMACHAL PRADESH	09/2018	392.51 -	06/2022 -	06/2022	0/0
997	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]CPWD,JAMMU AND KASHMIR	03/2019	329.00 -	07/2022 -	07/2022	0/0
998	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]CPWD,CHHATTISGARH	03/2020	808.62 -	07/2022 -	07/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Date of Commissioning (Month/Year)		Milestones Achieved/ Total
				Original / Revised	Anticipated	
1	2	3	4	5	6	7
999	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD,KARNATAKA	07/2019	851.00 851.00	03/2022 -	09/2022	0/0
1000	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD,BIHAR	09/2018	375.00 -	09/2020 -	11/2022	0/0
1001	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD,ANDHRA PRADESH	09/2019	588.72 -	09/2022 -	01/2023	0/0
1002	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]CPWD,JAMMU AND KASHMIR	01/2018	676.00 -	04/2023 -	04/2023	0/0
1003	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMENITIES - [N44000001]CPWD,JHARKHAND	03/2021	127.26 -	10/2023 -	10/2023	0/0
1004	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	-	0/0
1005	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-	0/0
	<u>EdCIL(India) Limited</u>					
1006	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-	0/0
	<u>Indian Institute Of Technology, Kharagpur</u>					
1007	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-	0/0
	<u>Rail India Technical And Economic Service</u>					
1008	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-	0/0
	<u>HOME AFFAIRS</u>					
	<u>Central Public Works Department</u>					
1009	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE-C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]CPWD,HARYANA	01/2020	166.98 -	05/2022 -	05/2022	0/0
1010	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI - [N45000003]CPWD,UTTAR PRADESH	05/2019	199.31 -	01/2022 -	06/2022	0/0
1011	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF - [N45000002]CPWD,DELHI	06/2019	277.35 290.33	07/2022 10/2022	10/2022	0/0
1012	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE - - [N28000147]CPWD,HARYANA	01/2020	166.98 167.00	10/2023 -	10/2023	0/0
1013	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-	0/0
	<u>DPIIT</u>					
	<u>Delhi Mumbai Industrial Corridor</u>					
1014	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021	0/0
	<u>India International Convention And Expo Centre</u>					
1015	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]IICC,DELHI	11/2017	4,773.00 -	12/2019 05/2022	05/2022	0/0

Details of Projects Without Milestones w.r.t. Original Schedule

Costing Rs. 150 Crore and Above (August 2021)						
				Date of Commissioning (Month/Year)		
Sl.No	Project	Date of Approval (Month/Year)	Original/ Revised Cost (Rs. crore)	Original / Revised	Anticipated	Milestones Achieved/ Total
1	2	3	4	5	6	7
	Total		12,20,113.49 -			0/0
	Grand Total		12,20,113.49			0/0

FLASH REPORT

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Central Public Works Department</u>							
1	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES - PPP BOT (Hybrid Annuity) - [N44000001]	03/2021	127.26	188.88	10/2023	10/2023	48.42	0
	Total		127.26	188.88				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>National Highways Authority Of India</u>							
2	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS (ANNUITY) - [N24000176]	05/2010	374.00	166.90	05/2013	08/2021	-55.37	99
3	GWALIOR-JHANSI, NH-75 - PPP (ANNUITY) - [N24000089]	12/2003	604.00	364.59	12/2009	09/2020	-39.64	129
4	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - PPP (BOT) - [N24000208]	07/2012	291.36	469.31	01/2014	-	61.08	0
5	INDORE-DEWAS(NH-3) - PPP (BOT) - [N24000159]	11/2010	325.00	475.00	05/2013	-	46.15	0
6	DELHI/ HARYANA BORDER TO ROHTAK - PPP (BOT) - [N24000122]	04/2007	486.00	486.00	05/2010	-	.00	0
7	TRICHY - KARUR - PPP (BOT) - [N24000528]	03/2007	516.00	516.00	07/2008	-	.00	0
8	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - PPP (BOT) - [N24000426]	11/2012	530.07	530.07	08/2016	06/2020	.00	46
9	TIRUPATI - TIRUTHANI - CHENNAI - PPP (BOT) - [N24000178]	04/2011	571.00	571.00	10/2013	-	.00	0
10	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - PPP (BOT) - [N24000185]	09/2011	574.00	574.00	03/2014	-	.00	0
11	4-LANNING OF CHAPRA-HAJIPUR - PPP (ANNUITY) - [N24000187]	01/2011	575.00	575.00	07/2013	-	.00	0
12	2 LANNING OF MUZAFFARPUR - SONBARSA - PPP (ANNUITY) - [N24000188]	05/2011	511.54	591.00	11/2013	-	15.53	0
13	SIX LANNING OF VADAKKANANCHERRY THRISSURESECTION KM 240 270KM - PPP (BOT) - [N24000149]	02/2010	617.00	617.00	08/2012	-	.00	0
14	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM) - PPP (ANNUITY) - [N24000213]	04/2012	624.00	624.00	04/2014	01/2022	.00	93

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above (August 2021)								
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
15	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU PPP (BOT) - [N24000586]	06/2016	637.18	637.18	06/2019	09/2019	.00	3
16	PATNA-MUZZAFFARPUR - PPP (ANNUITY) - [N24000165]	08/2010	671.30	671.30	02/2013	-	.00	0
17	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - PPP BOT (Hybrid Annuity) - [N24001340]	11/2019	716.00	716.00	07/2021	-	.00	0
18	MUZZAFFARNAGAR-HARIDWAR - PPP (BOT) - [N24000201]	09/2011	754.00	754.00	03/2013	-	.00	0
19	FOUR LANING OF MAHUA TO KAGAVADAR OF NH- 8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - PPP (BOT) - [N24000587]	06/2016	763.23	763.23	06/2019	-	.00	0
20	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - PPP (BOT) - [N24000445]	08/2014	822.90	822.90	04/2018	09/2021	.00	41
21	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION PPP (BOT) - [N24000454]	06/2014	923.04	923.04	11/2016	-	.00	0
22	KANDLA - MUNDRA PORT - PPP (BOT) - [N24000175]	01/2011	953.88	953.88	07/2013	-	.00	0
23	4 LANING OF SOLAPUR YEDISHI SECTION OF NH- 211 - PPP (BOT) - [N24000453]	01/2015	972.50	972.50	07/2017	-	.00	0
24	4-LANING OF BRAHMAPORE-FARAKA - PPP (BOT) - [N24000203]	02/2011	998.79	998.79	08/2013	06/2023	.00	118
25	SIX LANING OF CHANDIKHOL-JAGATPUR- BHUBANESWAR PPP (BOT) - [N24000205]	12/2011	1,047.00	1,047.00	06/2014	-	.00	0
26	4-LANING OF FARAKA-RAIGANJ - PPP (BOT) - [N24000202]	02/2011	1,078.84	1,078.84	08/2013	08/2021	.00	96
27	SRINAGAR TO BANIHAL - PPP (ANNUITY) - [N24000189]	06/2011	1,100.70	1,100.70	06/2014	10/2020	.00	76
28	GHAZIABAD-ALIGARH NH-91 - PPP (BOT) - [N24000170]	02/2011	1,141.00	1,141.00	08/2013	-	.00	0
29	INDORE-JHABUA-GUJRAT/MP - PPP (BOT) - [N24000136]	10/2010	1,175.00	1,175.00	04/2013	-	.00	0
30	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - PPP (BOT) - [N24001300]	11/2019	1,226.88	1,226.88	02/2021	-	.00	0
31	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - PPP (BOT) - [N24000172]	09/2011	1,250.00	1,250.00	12/2013	-	.00	0
32	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 PPP (BOT) - [N24000230]	05/2013	1,348.20	1,348.20	02/2014	-	.00	0
33	FOUR LANING OF HOSPET - CHITRADURGA - PPP (BOT) - [N24000490]	03/2015	1,388.00	1,388.00	08/2018	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
34	6-LANING OF DHANKUNI-KHARAGPUR SECTION - PPP (BOT) - [N24000206]	04/2012	1,396.18	1,396.18	09/2014	-	.00	0
35	PANIKHOLI-RIMOLI - PPP (BOT) - [N24000197]	03/2012	1,410.00	1,410.00	09/2014	-	.00	0
36	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - PPP (BOT) - [N24000125]	03/2010	1,509.10	1,509.10	09/2012	-	.00	0
37	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - PPP (BOT) - [N24000183]	11/2011	1,535.00	1,535.00	05/2014	-	.00	0
38	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - PPP (BOT) - [N24000233]	04/2014	1,266.60	1,544.00	09/2016	-	21.90	0
39	ETAWAH CHAKERI - PPP (BOT) - [N24000219]	03/2013	1,573.00	1,573.00	09/2015	-	.00	0
40	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - PPP BOT (Hybrid Annuity) - [N24001301]	11/2019	1,601.10	1,601.10	02/2021	-	.00	0
41	FOUR LANING OF GWALIOR-SHIVPURI - PPP (BOT) - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
42	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - PPP (BOT) - [N24000462]	05/2014	1,655.01	1,655.01	08/2016	12/2020	.00	52
43	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - PPP (BOT) - [N24000477]	02/2008	1,673.70	1,673.70	10/2011	-	.00	0
44	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - PPP (BOT) - [N24000131]	02/2009	1,693.75	1,693.75	08/2011	-	.00	0
45	PUNE-SATARA(NH-4) - PPP (BOT) - [N24000156]	10/2010	1,724.55	1,724.55	03/2013	09/2021	.00	102
46	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - PPP (ANNUITY) - [N24000163]	07/2010	1,813.76	1,813.76	07/2013	-	.00	0
47	FOUR LANING OF AURANGABAD - YEDISHI - PPP (BOT) - [N24000508]	07/2015	1,871.34	1,871.34	01/2018	-	.00	0
48	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO186.50 KM) - PPP (BOT) - [N24000232]	11/2013	1,916.79	1,916.79	11/2016	-	.00	0
49	DELHI AGRA APPROVED LENGTH 180.0 KM - PPP (BOT) - [N24000224]	10/2012	1,928.22	1,928.22	04/2015	12/2021	.00	80
50	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00 - PPP (ANNUITY) - [N24000161]	07/2010	1,987.00	1,987.00	07/2015	09/2020	.00	62
51	AHMEDABAD TO VADODARA SECTION - PPP (BOT) - [N24000222]	01/2013	2,125.24	2,125.24	12/2015	-	.00	0
52	8 LANING OF MUKARBA CHOWK TO PANIPAT - PPP (BOT) - [N24000449]	07/2015	2,128.72	2,128.72	04/2019	09/2021	.00	29
53	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - PPP BOT (Hybrid Annuity) - [N24001185]	11/2017	2,159.00	2,159.00	01/2019	-	.00	0

Details of Ongoing Projects Under -Public Private Partnership Mode

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
54	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - PPP (BOT) - [N24000133]	05/2009	1,108.00 -	2,288.00	11/2011 -	-	106.50	0
55	SIX-LANING OF BARWA ADDA-PANAGARH - PPP (BOT) - [N24000515]	04/2014	1,665.00 -	2,360.65	-	-	41.78	0
56	4 LANING OF NAGPUR-BETUL - PPP (ANNUITY) - [N24000155]	02/2011	2,498.76 -	2,498.76	08/2014 -	-	.00	0
57	NASHRI- CHANANI - PPP (ANNUITY) - [N24000162]	05/2011	2,159.00 -	2,519.00	06/2015 -	-	16.67	0
58	VARANASI-AURANGABAD KM.786 TO KM.978.40 - PPP (BOT) - [N24000182]	09/2011	2,848.00 -	3,379.45	03/2014 -	12/2022	18.66	105
	Total		69,869.23 -	73,421.40				
	Grand Total		69,996.49	73,610.28				

FLASH REPORT

List of Projects Ahead of Schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
1	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR - [N28000150]	3/2019	1,828.00	1,828.00	-	09/2025	05/2024
	Total		1,828.00	1,828.00	.00		
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
2	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	9/2017	2,677.00	3,072.00	2,443.16	06/2021 08/2022	07/2022
	<u>Indian Oil Corporation Limited</u>						
3	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL - [N16000332]	3/2018	3,712.00	3,696.00	2,213.96	09/2022	03/2022
4	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI - [N16000405]	10/2020	1,398.00	1,398.00	88.76	12/2023	09/2023
5	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI - [N16000403]	10/2020	921.00	921.00	5.26	09/2023 02/2024	12/2023
6	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY - [N16000409]	9/2020	18,936.00	18,936.00	763.62	09/2024	08/2024
	Total		27,644.00	28,023.00	5,514.76		
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
7	KAWAS SOLAR 56 MW - [N18000283]	8/2020	261.80	261.80	63.92	10/2021 01/2022	10/2021
8	SAMBHU KI BHURJ SOLAR 250 MW - [N18000285]	1/2020	1,522.71	1,522.71	894.14	09/2021 10/2022	01/2022
9	GUJARAT 200 MW (GUVNL TENDER) - [N18000295]	1/2021	842.27	842.27	92.08	07/2022	06/2022
	<u>Power Grid Corporation Of India Limited</u>						
10	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT - [N18000066]	2/2009	11,130.19 14,719.10	14,719.10	12,953.79	08/2013 11/2022	08/2022
	Total		13,756.97	17,345.88	14,003.93		
	<u>RAILWAYS</u>						

Costing Rs. 150 Crore and above

(August 2021)

						Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Central Railways</u>						
11	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	2/2015	3,627.47	3,627.47	1,557.30	03/2024 -	03/2023
	<u>North East Frontier Railway</u>						
12	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	4/2016	602.27 -	2,144.78	977.32	12/2021 -	09/2021
	<u>Rail Vikas Nigam Ltd.</u>						
13	BHANUPALI-BILASPUR BERI NL - [N22000273]	4/2008	2,966.99	6,753.42	547.68	12/2026 -	12/2025
14	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	4/2010	2,127.00	3,000.00	1,921.53	03/2023 -	12/2022
15	DIGHI PORT NEW LINE - [N22000408]	4/2015	723.78	723.78	0.19	12/2025 -	03/2025
	Total		10,047.51 -	16,249.45	5,004.02		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
16	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN - [N24000876]	1/2017	396.86 396.86	396.86	271.47	09/2019 11/2021	10/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
17	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000862]	4/2017	537.82 -	537.82	121.93	09/2019 06/2023	04/2023
18	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF - [N24000946]	3/2017	1,718.59 -	1,718.59	519.92	- 06/2022	03/2022
	Total		2,653.27 -	2,653.27	913.32		
	<u>STEEL</u>						
	<u>Steel Authority Of India Limited (Sail)</u>						
19	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E - [N12000121]	12/2018	263.36 -	263.36	253.46	09/2020 09/2021	08/2021
	Total		263.36 -	263.36	253.46		
	Grand Total		56,193.11	66,362.96	25,689.49		

List of Projects on schedule w.r.t. Latest Schedule

Annexure - XII

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Bhavini Limited</u>						
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE) - [N020100044]	9/2003	3,492.00 -	6,840.00	5,986.57	09/2010 10/2022	10/2022
	Total		3,492.00 -	6,840.00	5,986.57		
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
2	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR - [N04000073]	10/2013	417.23 -	707.73	456.88	09/2018 06/2022	06/2022
3	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA - [N04000081]	1/2019	389.71 -	389.71	191.88	11/2021 01/2023	01/2023
4	DEVELOPMENT OF TUTICORIN AIRPORT - [N04000090]	6/2019	380.87 -	380.87	12.79	03/2022 12/2023	12/2023
5	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD [N04000086]	5/2020	353.61 -	353.61	67.32	05/2022 -	05/2022
6	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCB AIRPORT KOLKATA - [N04000080]	1/2016	458.00 -	458.00	149.44	03/2020 07/2022	07/2022
7	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT [N04000091]	4/2020	611.80 -	611.80	33.70	03/2023 -	03/2023
	Total		2,611.22 -	2,901.72	912.01		
	<u>COAL</u>						
	<u>Ahmedabad Metro Rail</u>						
8	BATURA WEST OC PROJECT (0.80 MTY) - [N06000207]	3/2021	496.28 -	496.28	-	03/2028 -	03/2028
	<u>Central Coal Fields Limited</u>						
9	MAGADH EXPANSION OC(51 MTY) - [N06000015]	8/2008	6,964.33 6,964.33	7,254.37	729.50	07/2012 03/2028	03/2028
10	TETARIAKHAR EXPANSION OCP - [N06000186]	11/2019	243.52 -	243.52	37.16	03/2023 -	03/2023
11	RECAST EPR AMRAPALI OC - [N06000103]	2/2012	4,983.58 4,983.58	4,983.58	258.81	03/2020 03/2028	03/2028
12	NORTH URIMARI EXPANSION OCP - [N06000182]	3/2019	1,553.06 -	1,553.06	337.20	03/2023 -	03/2023
	<u>Eastern Coal Fields Limited</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
13	EXPANSION PR OF JHANJRA UG(5.00 MTY) - [N06000020]	11/2015	1,210.12 -	1,210.12	49.04	03/2022 03/2029	03/2029
14	PARASEA- BELBAID REORGANISATION UG MINE - [N06000185]	7/2019	826.42 -	826.42	.19	03/2027 -	03/2027
15	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT - [N06000191]	4/2020	483.65 -	483.65	4.39	03/2025 -	03/2025
16	CHITRA EAST (RCE) OCP - [N06000169]	8/2018	513.98 -	513.98	134.97	03/2024 -	03/2024
17	TILABONI UG MINE - [N06000172]	2/2019	916.62 -	916.62	1.17	03/2027 -	03/2027
18	NAKRAKONDA KUMARDIH B OCP - [N06000170]	8/2018	502.68 -	502.68	15.70	03/2029 -	03/2029
19	SIDULI MINE (OC AND UG) - [N06000165]	5/2018	535.18	535.18	1.53	03/2026	03/2026
20	HURA - C OC (3 MTY) - [N06000143]	10/2015	359.69 -	359.69	249.15	03/2022	03/2022
Mahanadi Coal Fields Limited							
21	SIARMAL OCP (40.00MTY) - [N06000113]	5/2014	3,756.36 -	3,756.36	2,180.34	03/2026 -	03/2026
22	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY) - [N06000035]	12/2007	8,416.19 8,416.19	8,416.19	918.79	03/2013 03/2028	03/2028
23	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY) - [N06000044]	12/2007	3,504.21 3,504.21	3,504.21	589.67	03/2010 03/2029	03/2029
24	REORGANISATION OF BHARATPUR OCP EXPANSION - [N06000171]	11/2018	2,838.87 -	2,838.87	1,271.62	03/2029 -	03/2029
25	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP - [N06000167]	5/2018	2,434.75 -	2,434.75	499.88	03/2027 -	03/2027
Neyveli Lignite Corporation							
26	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA) - [N06000138]	4/2013	1,458.17 -	709.06	492.01	06/2015 03/2025	03/2025
27	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	7/2016	17,237.00 -	17,237.80	12,346.08	11/2021 11/2022	11/2022
Northern Coal Fields Limited							
28	SEMARIA OPENCAST PROJECT - [N06000176]	5/2019	396.58 -	396.58	-	03/2026 -	03/2026
29	BINA KAKRI AMALGAMATION OCP 14 MTPA - [N06000192]	8/2020	836.42 -	836.42	60.07	03/2024 -	03/2024
30	BLOCK-B EXPANSION OPENCAST PROJECT - [N06000184]	7/2019	998.71 -	998.71	-	03/2023 -	03/2023
31	NIGAH EXPANSION OCP (15 TO 25 MTPA) - [N06000196]	11/2020	1,729.68 -	1,729.68	-	03/2025 -	03/2025
32	KHADIA EXPANSION OCP - [N06000208]	6/2021	491.67 -	491.67	-	03/2025 -	03/2025
Singareni Colliers Company Limited							
33	GODAVARIKHANI COAL MINE - [N06000202]	7/2019	438.98 -	438.98	73.60	03/2023 -	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
34	VENKATESH KHANI COAL MINE - [N06000204]	10/2020	484.51 -	484.51	23.39	03/2023 -	03/2023
35	NAINI COAL MINE - [N06000203]	3/2020	494.30 -	494.30	73.09	03/2024 -	03/2024
	<u>South-Eastern Coal Fields Limited</u>						
36	PELMA OCP(15.00MTY) - [N06000045]	11/2014	1,624.59 -	1,624.59	9.08	03/2023 -	03/2023
37	VIJAY WEST OPENCAST PROJECT - [N06000158]	5/2017	976.95 -	976.95	76.12	03/2026 -	03/2026
38	JHIRIA WEST OPENCAST PROJECT - [N06000166]	11/2018	389.97 -	389.97	-	03/2026 -	03/2026
39	MAHAMAYA OPENCAST PROJECT - [N06000164]	5/2018	410.26 -	410.26	40.10	03/2026 -	03/2026
40	JAMPAL OCP RCE - [N06000198]	5/2020	278.64 -	278.64	183.90	03/2024 -	03/2024
41	DIPKA OC EXPANSION 40 MTY - [N06000200]	12/2020	5,241.40 -	5,241.40	1,960.09	03/2029 -	03/2029
42	PORDA CHIMTAPANI OCP (10 MTY) - [N06000199]	12/2020	2,310.12 -	2,310.12	-	03/2029 -	03/2029
43	BAROUD OC EXPANSION (3-10 MTY) - [N06000197]	8/2020	2,309.80 -	2,309.80	284.31	03/2029 -	03/2029
44	RAJNAGAR OCP RPR (1.70 MTY) - [N06000124]	12/2014	357.80 -	357.80	100.65	03/2021 04/2024	04/2024
45	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY - [N06000008]	8/2013	7,612.33 -	7,612.33	2,960.03	03/2023 -	03/2023
46	CHHAL OC SEAM -III (6.00 MTY) - [N06000104]	12/2013	610.63 -	610.63	159.50	03/2022 -	03/2022
	<u>Western Coal Fields Limited</u>						
47	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY) [N06000141]	11/2015	313.34 -	313.34	149.32	03/2021 03/2024	03/2024
48	SASTI EXPANSION OC - [N06000206]	8/2020	371.59 -	371.59	52.55	03/2026 -	03/2026
49	GHONSA EXPANSION DEEP OC - [N06000205]	3/2021	241.72 -	241.72	57.00	03/2028 -	03/2028
50	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	9/2016	289.29 -	289.30	36.10	03/2022 03/2025	03/2025
51	NILJAI EXPANSION (DEEP) OC (3.5 MTY) - [N06000154]	8/2016	319.76 -	404.45	246.02	03/2022 -	03/2022
52	RPR FOR JAMUNIA UG (0.90 MTY) - [N06000153]	7/2016	281.25 -	281.25	18.24	03/2022 03/2026	03/2026
53	AMALGAMATED YEKONA-I YEKONA-II - [N06000132]	8/2015	727.28 -	745.03	390.11	03/2025 -	03/2025
54	SINGHORI OC MINE - [N06000130]	6/2015	205.49 -	205.49	138.58	03/2020 09/2021	09/2021
55	NEW MAJRI UG TO OC - [N06000128]	5/2015	295.56 -	299.67	164.36	03/2019 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
56	BHANEAGAN OC - [N06000121]	2/2015	187.94 -	409.68	86.90	03/2023 -	03/2023
57	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY) - [N06000118]	11/2014	1,184.33 -	1,184.33	392.88	03/2020 03/2027	03/2027
58	GANDHIGRAM UG MINE - [N06000183]	8/2019	414.16 -	414.16	1.00	03/2026 -	03/2026
59	UKNI DEEP OC - [N06000179]	11/2018	318.14 -	318.14	217.47	03/2021 09/2022	09/2022
60	VISHNUPURI UG TO OC MINE - [N06000178]	7/2018	195.57 -	195.57	2.94	03/2025 -	03/2025
61	KOLAR PIMPRI EXTENSION OC - [N06000160]	3/2017	362.73 -	402.90	336.00	03/2020 09/2022	09/2022
62	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY) - [N06000142]	11/2015	851.60 -	826.80	233.76	03/2020 03/2026	03/2026
	Total		93,787.75 -	93,673.15	28,644.36		
DEPARTMENT OF HIGHER EDUCATION							
Central Public Works Department							
63	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1) - [N28000130]	3/2019	329.00 -	329.00	-	07/2022 -	07/2022
64	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C) - [N28000131]	1/2018	676.00 -	676.00	-	04/2023 -	04/2023
65	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR - [N42000008]	9/2018	392.51 -	392.51	38.44	06/2022 -	06/2022
66	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMENITIES - [N44000001]	3/2021	127.26 -	188.88	12.73	10/2023 -	10/2023
67	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I. - [N28000141]	3/2020	808.62 -	808.62	57.42	07/2022 -	07/2022
	Total		2,333.39 -	2,395.01	108.59		
DPIIT							
India International Convention And Expo Centre							
68	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	2,744.03	12/2019 05/2022	05/2022
	Total		4,773.00 -	5,178.00	2,744.03		
FERTILISERS							
Rashtriya Chemical & Fertiliser Limited							

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
69	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY - [N08000018]	4/2018	426.72 -	426.72	295.13	04/2020 10/2021	10/2021
	Total		426.72 -	426.72	295.13		
	<u>FINANCE</u>						
	<u>Central Public Works Department</u>						
70	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI - [N28000109]	11/2017	348.77 -	348.77	163.31	11/2021 -	11/2021
	Total		348.77 -	348.77	163.31		
	<u>HEALTH AND FAMILY WELFARE</u>						
71	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR - [N21000029]	3/2019	1,404.00 -	1,404.00	279.98	09/2023 -	09/2023
72	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	3/2019	1,577.00 -	1,828.00	-	09/2025 -	09/2025
	<u>HII Infra Tech Services Limited</u>						
73	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM - [N21000027]	5/2017	875.00 -	747.80	387.54	05/2021 09/2022	09/2022
	Total		3,856.00 -	3,979.80	667.52		
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
74	NSG AT KOLKATA - [N28000104]	10/2014	162.88 -	238.00	172.12	04/2018 12/2021	12/2021
75	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQ RAF - [N45000002]	6/2019	277.35 -	290.33	27.25	07/2022 10/2022	10/2022
76	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96 - [N45000001]	1/2020	166.98 -	166.98	.29	05/2022 -	05/2022
77	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE- - [N28000147]	1/2020	166.98 167.00	166.98	-	10/2023 -	10/2023
	Total		774.19 -	862.29	199.66		
	<u>MINES</u>						
	<u>National Aluminum Company Limited (Nalco)</u>						

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
78	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT - [N10000010]	12/2014	5,540.00 -	5,540.00	788.26	04/2021 12/2022	12/2022
79	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN - [N10000013]	11/2017	483.00 -	483.00	2.68	04/2021 03/2023	03/2023
	Total		6,023.00 -	6,023.00	790.94		
	<u>PETROLEUM</u>						
	<u>Bharat Petroleum Corporation Limited</u>						
80	IRUGUR-DEVANGONTHI POL PIPELINE - [N16000234]	11/2012	678.00 -	1,472.00	19.44	02/2017 08/2022	08/2022
81	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R - [N16000410]	8/2020	697.00 -	697.00	195.24	03/2023	03/2023
82	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC - [N16000346]	9/2018	11,130.00 -	11,130.00	422.60	03/2023	03/2023
83	2ND GENERATION LIGNOCELLULOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA) - [N16000374]	8/2019	1,607.00 -	1,607.00	263.13	08/2022 -	08/2022
84	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO. [N16000373]	11/2018	248.55 -	248.55	126.45	06/2022 -	06/2022
85	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL [N16000365]	12/2017	1,524.06 -	1,524.06	905.06	12/2021 -	12/2021
	<u>Gas Authority Of India Limited</u>						
86	DHAMRA-ANGUL PIPELINE PROJECT - [N16000272]	3/2017	1,933.00 -	1,933.00	1,456.60	12/2020 12/2021	12/2021
87	BOKARO-ANGUL PIPELINE PROJECT - [N16000274]	3/2017	3,437.00 -	3,048.00	2,009.10	12/2020 12/2021	12/2021
88	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II [N16000285]	6/2009	2,915.00 2,915.00	5,909.00	3,786.80	12/2012 02/2022	02/2022
89	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT - [N16000398]	6/2020	7,844.25 -	7,844.25	1,504.40	05/2023 -	05/2023
90	DHAMRA HALDIA PIPELINE PROJECT - [N16000391]	3/2020	1,030.65 -	1,030.65	335.00	11/2022 -	11/2022
91	CITY GAS DISTRIBUTION, JAMSHEDPUR - [N16000389]	10/2017	221.45 -	221.45	99.53	10/2022 -	10/2022
92	SRIKAKULAM ANGUL PIPELINE PROJECT - [N16000388]	9/2019	2,658.34 -	2,658.34	340.70	07/2022 -	07/2022
93	BARAUNI-GUWAHATI PIPELINE - [N16000334]	6/2018	3,308.00 -	3,060.00	2,312.50	12/2021 -	12/2021
94	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI - [N16000329]	10/2017	226.45 -	226.45	124.00	10/2022 -	10/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
95	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK - [N16000328]	7/2017	182.20 -	182.20	85.28	07/2022 -	07/2022
96	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA - [N16000327]	10/2017	359.25 -	359.25	165.40	10/2022 -	10/2022
97	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR [N16000289]	7/2017	243.53 -	243.53	132.46	07/2022 -	07/2022
98	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI - [N16000288]	4/2017	287.49 -	345.15	231.37	04/2022 -	04/2022
99	DURGAPUR-HALDIA PIPELINE PROJECT - [N16000275]	3/2017	1,740.00 -	1,740.00	912.00	12/2020 12/2021	12/2021
100	DOBHI-DURGAPUR PIPELINE PROJECT - [N16000273]	3/2017	2,433.00 -	2,433.00	2,147.10	12/2020 12/2021	12/2021
<u>Hindustan Petroleum Corporation Limited</u>							
101	VISAKH REFINERY MODERNISATION PROJECT [N16000235]	7/2016	20,928.00 -	26,264.00	16,008.48	07/2020 07/2022	07/2022
102	HASSAN CHERLAPALLI LPG PIPELINE - [N16000367]	6/2019	2,166.38 -	2,166.38	1,199.32	06/2022 -	06/2022
103	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE [N16000369]	12/2018	854.00 -	854.00	161.21	12/2022 -	12/2022
104	BARMER PALANPUR PIPELINE - [N16000384]	11/2019	776.00 -	776.00	307.06	11/2022 -	11/2022
105	CITY GAS DISTRIBUTION IN UP AND UK - [N16000387]	3/2019	3,450.20 -	3,450.20	276.62	03/2029 08/2029	08/2029
106	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB [N16000402]	5/2020	1,421.46 -	1,244.50	101.45	02/2023 -	02/2023
107	SULPHUR FORMING UNIT IN SRU - [N16000408]	10/2020	210.94 -	210.94	121.18	08/2021 -	08/2021
108	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT - [N16000413]	3/2021	456.00 -	456.00	12.89	03/2024 -	03/2024
109	RUF PITCH LOADING GANTRY - [N16000406]	10/2020	332.61 -	332.61	.01	11/2022 -	11/2022
110	CITY GAS DISTRIBUTION IN WEST BENGAL - [N16000392]	3/2019	5,830.20 -	5,830.20	120.62	03/2031 08/2031	08/2031
111	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS - [N16000385]	9/2018	520.00 -	520.00	144.71	09/2026 02/2027	02/2027
112	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU - [N16000380]	6/2018	380.00 -	380.00	263.70	11/2021 -	11/2021
<u>Indian Oil Corporation Limited</u>							
113	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	437.75	10/2017 03/2022	03/2022
114	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR - [N16000193]	1/2015	1,823.00 -	3,027.90	2,117.81	03/2021 12/2021	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
115	PARADIP HYDERABAD PIPELINE - [N16000194]	1/2015	2,321.00 -	3,338.00	2,996.28	12/2020 03/2022	03/2022
116	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT - [N16000340]	8/2018	1,636.00 -	1,636.00	862.17	08/2020 04/2022	04/2022
117	ETHYLENE GLYCOL PROJECT AT PARADIP - [N16000338]	4/2018	5,654.00 -	5,654.00	3,161.40	10/2021 -	10/2021
118	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT - [N16000336]	3/2018	588.20 -	730.20	128.08	- 05/2023	05/2023
119	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A - [N16000333]	3/2018	676.00 -	676.00	464.35	08/2022 -	08/2022
120	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000326]	10/2017	906.00 -	906.00	327.90	02/2020 10/2021	10/2021
121	DEVELOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY - [N16000324]	12/2017	199.36 -	199.36	48.78	10/2020 08/2022	08/2022
122	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY - [N16000323]	8/2017	255.40 -	255.40	90.08	08/2020 03/2022	03/2022
123	LPG BP PROJECT JODHPUR - [N16000318]	3/2018	229.80 -	229.80	85.09	- 05/2022	05/2022
124	LPG BP PROJECT MOTIHARI - [N16000317]	5/2018	206.50 -	206.50	147.35	03/2021 09/2021	09/2021
125	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU [N16000305]	12/2017	466.43 -	466.43	235.77	10/2020 01/2022	01/2022
126	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS [N16000415]	10/2018	176.00 -	176.00	-	08/2027 -	08/2027
127	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTPA - [N16000412]	2/2021	34,627.00 -	34,627.00	445.30	09/2024 -	09/2024
128	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM [N16000411]	10/2020	1,614.00 -	1,614.00	.21	08/2023 -	08/2023
129	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END - [N16000400]	6/2020	1,378.00 -	1,378.00	159.37	12/2022 -	12/2022
130	MUZAFFARPUR-MOTIHARI LPG PIPELINE - [N16000399]	6/2020	403.00 -	403.00	89.57	08/2022 -	08/2022
131	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY - [N16000396]	7/2020	13,805.00 -	13,805.00	295.70	01/2024 -	01/2024
132	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY - [N16000395]	1/2020	202.16 -	202.16	16.19	07/2022 -	07/2022
133	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA - [N16000386]	1/2020	14,810.00 -	14,810.00	1,303.20	04/2023 -	04/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
134	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY - [N16000368]	6/2019	371.00 -	427.00	25.79	09/2022 03/2023	03/2023
135	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS [N16000427]	6/2019	303.00 -	303.00	-	02/2028 -	02/2028
136	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS - [N16000426]	6/2019	169.00 -	169.00	-	12/2029 -	12/2029
137	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS [N16000425]	6/2019	2,996.00 -	2,996.00	-	02/2028 -	02/2028
138	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS [N16000424]	6/2019	347.00 -	347.00	-	02/2028 -	02/2028
139	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA [N16000423]	6/2019	163.00 -	163.00	-	12/2029 -	12/2029
140	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS [N16000422]	6/2019	439.00 -	439.00	-	02/2028 -	02/2028
141	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS [N16000421]	6/2019	988.00 -	988.00	-	12/2029 -	12/2029
142	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS [N16000420]	6/2019	2,880.00 -	2,880.00	-	08/2027 -	08/2027
143	CGD PROJECT AT SALEM DISTRICT - [N16000419]	10/2018	1,304.00 -	1,304.00	-	03/2030 -	03/2030
144	CGD PROJECT AT COIMBATORE DISTRICT - [N16000418]	10/2018	2,998.00 -	2,998.00	-	03/2030 -	03/2030
145	CGD PROJECT AT REWA DISTRICT - [N16000417]	10/2018	177.00 -	177.00	-	02/2027 -	02/2027
146	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS [N16000416]	10/2018	613.00 -	613.00	-	12/2029 -	12/2029
147	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT - [N16000363]	12/2018	278.60 -	278.60	63.96	06/2021 07/2022	07/2022
148	Fuel Quality Upgradation Project at Paradip Refinery - [N16000362]	5/2019	3,361.00 -	3,361.00	1,977.07	08/2021 09/2022	09/2022
149	ADDITIONAL STORAGE TANKS AT PARADIP - [N16000361]	11/2018	462.30 -	462.30	87.24	09/2021 06/2022	06/2022
150	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY - [N16000353]	10/2018	598.00 -	598.00	391.04	02/2020 02/2022	02/2022
151	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY - [N16000352]	1/2019	909.00 -	909.00	416.23	01/2021 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
152	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP - [N16000350]	10/2018	316.20 -	316.20	116.20	10/2021 03/2022	03/2022
153	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR - [N16000344]	4/2018	522.00 -	522.00	373.16	03/2021 12/2021	12/2021
154	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH - [N16000342]	8/2018	466.00 -	466.00	280.16	04/2021 12/2021	12/2021
155	COMPRESSED BIO GAS PLANT AT GORAKHPUR - [N16000383]	9/2019	164.69 -	164.69	15.02	07/2021 03/2022	03/2022
156	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY - [N16000382]	11/2019	5,251.00 -	5,251.00	421.90	05/2023 -	05/2023
157	LPG BP PROJECT CHITTOOR - [N16000381]	7/2019	167.00 -	167.00	9.93	07/2022 -	07/2022
158	PX-PTA REVAMP AT PANIPAT REFINERY - [N16000376]	8/2019	1,255.00 -	1,255.00	255.22	10/2021 -	10/2021
159	R and D CAMPUS II AT FARIDABAD - [N16000375]	6/2019	2,281.94 -	2,281.94	539.26	12/2022 07/2023	07/2023
160	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS, HSD AND - [N16000304]	8/2017	236.00 -	319.61	195.28	06/2020 09/2021	09/2021
161	KHARAGPUR LPG BOTTLING PLANT - [N16000300]	4/2017	163.02 -	207.36	122.11	04/2020 10/2021	10/2021
162	AUGMENTATION OF CTMPL - [N16000286]	12/2016	228.00 -	228.00	150.39	11/2021 -	11/2021
163	LPG BP PROJECT KHORDHA - [N16000283]	12/2016	161.59 -	161.59	53.22	12/2019 03/2022	03/2022
164	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE - [N16000253]	5/2016	4,497.00 -	6,025.00	3,897.13	12/2018 02/2022	02/2022
165	KOYALI AHMEDNAGAR SOLAPUR PIPELINE - [N16000249]	5/2016	1,945.00 -	1,945.00	1,529.03	02/2022 -	02/2022
Mangalore Refinery And Petrochemicals Limited							
166	DEVANGONTHI MARKETING TERMINAL - [N16000401]	6/2020	200.00 -	200.00	2.54	06/2023 08/2023	08/2023
Numaligarh Refinery Limited							
167	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTA REFINARY - [N16000379]	1/2019	12,366.00 -	12,366.00	567.38	10/2024 -	10/2024
168	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES - [N16000394]	1/2019	10,228.00 -	10,228.00	285.27	10/2024 -	10/2024
Oil & Natural Gas Corporation Limited							
169	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	3/2011	861.79 -	2,001.34	1,568.64	05/2013 02/2022	02/2022
170	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK - [N16000239]	12/2015	823.27 -	1,137.79	709.24	03/2023 03/2022	03/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
171	REDEVELOPMENT OF NANDASAN FIELD - [N16000404	2/2020	444.87 -	444.87	103.78	08/2022 -	08/2022
172	PIPELINE REPLACEMENT PROJECT (PRP-VI) - [N16000370	5/2019	763.92 -	733.86	791.46	12/2020 12/2021	12/2021
173	HEERA REDEVELOPMENT - PHASE III - [N16000360	6/2019	2,494.68 -	2,354.72	1,603.69	03/2022 -	03/2022
174	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV - [N16000359	5/2019	3,660.71 -	3,740.05	2,997.59	05/2021 01/2022	01/2022
175	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV - [N16000358	4/2019	3,228.80 -	3,976.67	1,307.63	03/2022 05/2023	05/2023
176	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION - [N16000357	2/2019	2,292.46 -	2,203.71	1,995.31	05/2021 12/2021	12/2021
177	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS - [N16000213	12/2015	3,190.69 -	3,375.90	2,876.04	04/2018 05/2022	05/2022
178	REDEVELOPMENT OF SANTHAL FIELD - [N16000279	2/2017	1,162.56 -	970.30	901.28	03/2026 -	03/2026
179	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002 - [N16000241	11/2015	650.82 -	624.35	453.71	03/2019 09/2021	09/2021
180	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT - [N16000247	3/2016	34,012.00 -	25,090.00	13,580.92	06/2020 06/2022	06/2022
	<u>Oil India Limited</u>						
181	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN [N16000356	6/2016	224.75 -	198.00	178.00	08/2020 09/2021	09/2021
	Total		2,78,230.58 -	2,84,343.31	90,545.58		
	<u>POWER</u>						
	<u>Chenab Valley Power Projects [P] Limited</u>						
182	KIRU HYDRO ELECTRIC PROJECT - [N18000278	3/2019	4,287.59 -	4,287.59	582.89	- 08/2024	08/2024
	<u>National Hydro-Electric Power Corporation</u>						
183	PARBATI HEP (4X200 MW) (NHPC) II - [180100210	9/2002	3,919.59 -	9,897.59	9,164.35	09/2009 03/2023	03/2023
184	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC) - [180100221	9/2003	6,285.33 -	19,992.43	14,059.55	09/2010 08/2023	08/2023
	<u>National Thermal Power Corporation</u>						
185	RAMMAM-III HEPP (3X40 MW) - [N18000178	9/2014	1,381.84 -	1,381.54	704.78	09/2019 12/2024	12/2024
186	BARH STPP(3X660MW) NTPC - [180100242	2/2005	8,692.97 -	21,312.11	19,169.37	10/2011 07/2023	07/2023
187	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA & RADHANPUR) [N18000296	5/2021	674.92 -	674.92	-	09/2022 -	09/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
188	CHHATTARGARH 150 MW - [N18000294]	2/2021	599.99 -	559.98	60.85	07/2022 -	07/2022
189	BHENSARA 320 MW - [N18000293]	1/2021	1,221.73 -	1,221.73	137.36	07/2022 -	07/2022
190	ANTA SOLAR 90 MW - [N18000292]	1/2021	382.22 -	382.22	-	03/2022 -	03/2022
191	ETTAYAPURAM SOLAR 230MW - [N18000290]	3/2020	1,316.22 -	1,316.22	650.94	09/2021 02/2022	02/2022
192	FATEHGARH SOLAR 296MW - [N18000289]	3/2020	1,749.31 -	1,749.31	1,125.51	09/2021 02/2022	02/2022
193	KAYAMKULAM SOLAR 70 MW - [N18000288]	9/2019	403.62 -	403.62	100.92	06/2021 12/2021	12/2021
194	JETSAR SOLAR 160 MW - [N18000287]	12/2019	702.28 -	702.28	529.41	03/2021 11/2021	11/2021
195	RAMAGUNDAM FLOATING SOLAR 100 MW - [N18000284]	6/2019	401.90 -	401.90	153.54	04/2021 10/2021	10/2021
196	DEVIKOT SOLAR 150MW - [N18000281]	1/2020	798.24 -	798.24	273.17	09/2021 02/2022	02/2022
197	DEVIKOT SOLAR 90MW - [N18000280]	3/2020	501.29 -	501.29	343.39	09/2021 02/2022	02/2022
	<u>Power Grid Corporation Of India Limited</u>						
198	EASTERN REGION STRENGTHENING SCHEME-XII - [N18000164]	5/2014	522.29 -	546.36	480.43	11/2016 12/2021	12/2021
199	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A) - [N18000188]	3/2015	1,394.52 -	1,394.52	554.29	05/2017 12/2021	12/2021
200	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN - [N18000264]	8/2017	1,931.39 -	1,931.39	1,783.23	02/2020 09/2021	09/2021
201	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P - [N18000249]	12/2014	4,754.42 -	9,129.32	2,480.78	12/2018 03/2024	03/2024
202	EASTERN REGION STRENGTHENING SCHEME XVII(PART B) - [N18000244]	2/2017	235.53 -	235.53	155.39	06/2019 11/2021	11/2021
	<u>Satluj Jal Vidyut Nigam Limited</u>						
203	BUXAR THERMAL POWER PLANT (1320 MW) - [N18000194]	3/2019	10,439.09 -	10,439.09	2,725.87	01/2024 -	01/2024
204	DHAULASIDH HYDROELECTRIC PROJECT (66 MW) - [N18000291]	10/2020	687.97 -	687.97	155.02	11/2025 -	11/2025
205	LUHRI HYDROELECTRIC PROJECT (STAGE1) - [N18000279]	11/2020	1,810.56 -	1,810.56	486.06	01/2026 -	01/2026
206	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 -	947.89	657.62	12/2021 06/2022	06/2022
	<u>Thdc India Limited</u>						
207	AMELIA COAL MINE - [N18000252]	1/2017	2,104.21 -	1,587.16	592.99	09/2020 08/2022	08/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	Total		57,847.35	94,292.76	57,127.71		
	<u>RAILWAYS</u>						
	<u>Central Railways</u>						
208	WARDHA-NANDED MAHARASHTRA - [N22000231	4/2008	3,168.29	3,445.48	1,401.51	03/2023	03/2023
209	DAUND - MANMAD (236 KM) - [N22000360	2/2016	1,876.00	2,081.27	565.94	03/2023	03/2023
210	INDORE - MANMAD VIA MALEGAON (368 KM) - [N22000353	2/2016	9,968.00	9,968.00	-	03/2024	03/2024
211	PUNE-NASIK (265 KM) - [N22000354	2/2016	2,425.00	5,341.68	-	03/2024	03/2024
	<u>East Central Railways</u>						
212	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222	3/1999	1,033.07	3,620.00	3,614.37	03/2022	03/2022
213	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE [N22000350	12/2015	1,491.47	1,491.47	543.60	03/2020 03/2023	03/2023
214	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC [N22000181	4/2009	548.00	819.01	538.55	03/2020 03/2023	03/2023
215	ARARIA-SUPAUL (NL) - [N22000177	4/2008	1,605.17	1,605.17	61.37	- 03/2023	03/2023
216	KODERMA-TILAIYA (NL), ECR - [220100305	4/2002	459.91	1,625.87	890.81	- 03/2023	03/2023
217	HAJIPUR - BACHAWARA - [N22000334	5/2015	678.54	929.86	863.90	03/2019 12/2021	12/2021
218	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR - [220100303	4/2003	528.65	2,066.78	1,581.82	- 03/2023	03/2023
219	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR - [220100240	4/1997	324.73	1,070.00	1,076.60	03/2012 11/2022	11/2022
220	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR - [N22000002	4/1996	477.88 283.95	751.55	714.87	03/2012 09/2021	09/2021
221	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476	4/1991	329.39	1,483.14	1,219.42	- 03/2022	03/2022
222	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473	4/2016	731.64	1,185.73	269.99	03/2021 03/2024	03/2024
223	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	4/2016	744.04	1,215.54	488.59	03/2021 03/2024	03/2024
	<u>East Coast Railway</u>						
224	TALCHER-BIMALAGARH(NL)(ECOR) - [220100328	4/2005	810.78	1,928.07	895.94	06/2021 03/2025	03/2025
225	KIRANDUL - JAGDALPUR DOUBLING - [N22000318	12/2012	1,160.00	1,160.83	988.59	03/2020 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
226	BHADRAK - NERGUNDI 3RD LINE - [N22000316]	3/2013	843.04 -	843.04	248.28	10/2020 03/2024	03/2024
227	KHURDA ROAD-BOLANGIR(NL)ECOR - [220100284]	4/1994	2,923.13 -	3,791.66	1,602.15	03/2009 03/2026	03/2026
228	KOTTAVALSA - KORAPUT DOUBLING - [N22000377]	4/2015	2,499.71 -	2,499.71	727.14	03/2022 03/2024	03/2024
229	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE. - [N22000381]	4/2015	1,172.92 -	1,172.92	653.15	12/2018 03/2024	03/2024
230	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	4/2015	701.61 -	810.02	192.59	11/2018 03/2024	03/2024
231	JAGADALPUR-KORAPUT DOUBLING - [N22000376]	4/2015	1,547.38 -	1,547.38	678.19	03/2022 03/2023	03/2023
<u>Metropolitan Rapid Transport Projects</u>							
232	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	4/2006	495.74 -	734.01	472.27	06/2013 07/2022	07/2022
<u>North Central Railway</u>							
233	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	4/2011	2,912.96 -	3,845.60	303.16	03/2022 12/2024	12/2024
234	JHANSI BINA DOUBLING - [N22000496]	9/2016	2,001.00 -	2,001.00	948.08	03/2021 12/2022	12/2022
<u>North East Frontier Railway</u>							
235	SEVOK RANGPO, NEFR - [N22000102]	4/2008	1,339.48 -	8,600.00	1,656.02	12/2015 12/2023	12/2023
<u>North Eastern Railway</u>							
236	HATHUA-BHATNI (N L) (NER) - [220100319]	4/2005	230.03 -	230.03	277.14	12/2022 -	12/2022
237	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	3/2015	1,295.42 -	1,758.00	1,143.78	03/2022 -	03/2022
238	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	3/2007	243.78 -	895.00	114.63	12/2021 -	12/2021
<u>Northern Railway</u>							
239	CHANDIGARH-BADDI - [N22000467]	4/2007	328.14 -	1,540.13	242.31	03/2023 -	03/2023
<u>National High Speed Rail Corporation Limited</u>							
240	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT - [N22000463]	12/2015	1,08,000.00 -	1,08,000.00	14,605.32	12/2023 -	12/2023
<u>Rail Vikas Nigam Ltd.</u>							
241	AHMEDABAD-BOTAD (GC) - [N22000140]	4/2012	975.62 -	1,500.00	1,261.64	12/2021 -	12/2021
242	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	4/2015	773.94 -	850.00	618.69	12/2024 -	12/2024
243	VIJAYAWADA-GUDUR - [N22000369]	4/2015	3,246.26 -	3,548.68	1,568.77	12/2023 -	12/2023
244	MATHURA-JHANSI-3RD LINE (273.80 KM) - [N22000501]	6/2016	3,677.76 -	3,677.76	446.65	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
	<u>South East Central Railway</u>						
245	RAJNANDGAON - NAGPUR - 3RD LINE (SECR) - [N22000420]	9/2016	1,908.51 -	3,176.60	1,334.01	03/2023 12/2023	12/2023
246	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT [N22000438]	4/2010	585.93 -	1,268.32	1,058.10	02/2019 12/2021	12/2021
247	JHARSUGUDA-BILASPUR 4TH LINE - [N22000484]	4/2015	1,973.00 -	2,135.34	648.00	03/2021 12/2023	12/2023
248	WADSA-GADHCHIROLI NEW LINE (52.36 KM) - [N22000480]	6/2018	229.00 -	1,096.00	40.47	12/2021 12/2024	12/2024
	<u>South Western Railway</u>						
249	ARSIKERE-TUMKUR - [N22000332]	3/2015	578.00 -	760.00	639.39	03/2020 11/2021	11/2021
	<u>Southern Railway</u>						
250	MADURAI-BODINAYAKKANUR + [N22000201]	4/2008	164.41 -	608.13	389.96	- 12/2021	12/2021
251	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	4/2007	931.98 -	1,121.00	969.72	- 08/2021	08/2021
	<u>West Central Railway</u>						
252	RAMGANJMUNDI-BHOPAL (NL),WCR - [220100314]	4/2001	424.60 -	2,909.99	1,282.25	03/2021 03/2024	03/2024
	<u>Western Railway</u>						
253	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	4/2008	3,503.69 -	6,171.08	2,301.98	03/2022 03/2024	03/2024
254	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	4/2008	829.74 -	1,886.76	1,875.42	03/2020 03/2024	03/2024
255	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR) - [N22000123]	4/2008	318.24 -	321.62	126.36	03/2012 10/2023	10/2023
256	CHOTTAUDEPUR-DHAR(NL) - [N22000138]	4/2007	1,347.26 -	1,524.68	974.69	03/2022 03/2023	03/2023
257	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494]	4/2017	691.84 -	890.62	812.08	03/2020 09/2021	09/2021
258	INDORE-DEWAS-UJJAIN (80 KMS) - [N22000493]	4/2016	700.00 -	603.69	314.13	06/2020 03/2023	03/2023
259	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	2/1991	551.51 -	890.76	773.12	03/2019 10/2021	10/2021
260	SURENDRA NAGAR RAJKOT - [N22000392]	4/2015	1,002.39 -	1,002.39	730.07	03/2021 12/2022	12/2022
261	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	4/2011	1,037.15 -	1,383.69	1,199.84	03/2021 12/2022	12/2022
262	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH- KODINAR (GC) - [N22000143]	4/1994	320.66 -	1,378.11	555.49	03/2019 03/2023	03/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
263	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC) - [N22000142]	4/2011	844.10 -	844.10	251.82	- 03/2024	03/2024
264	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL) - [N22000139]	4/2007	1,640.04 -	1,873.10	869.58	03/2022 03/2023	03/2023
	Total		1,83,150.53 -	2,21,480.37	60,622.31		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
265	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION. - [N24000281]	12/2015	291.05 -	291.05	231.36	- 10/2021	10/2021
266	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 -	390.73	318.85	05/2017 05/2022	05/2022
267	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) [N24000415]	8/2010	195.04 -	377.99	368.39	10/2010 12/2021	12/2021
268	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION - [N24001221]	1/2016	624.98 -	731.50	460.02	10/2016 12/2021	12/2021
269	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	1/2016	476.20 544.00	544.00	400.49	09/2016 12/2021	12/2021
270	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION - [N24001218]	11/2015	335.32 -	335.32	275.33	06/2017 10/2021	10/2021
271	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180 - [N24001217]	1/2016	497.14 -	572.66	278.09	08/2016 06/2022	06/2022
272	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I - [N24001216]	12/2016	196.00 -	196.00	100.31	09/2021 -	09/2021
273	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD - [N24001198]	1/2019	264.50 -	264.50	106.37	03/2021 11/2021	11/2021
274	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	8/2010	186.96 -	322.24	304.71	09/2014 12/2021	12/2021
275	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH- [N24001180]	3/2019	237.51 -	237.51	75.42	12/2022 -	12/2022
276	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN - [N24001179]	3/2017	217.35 -	217.35	97.62	11/2020 08/2021	08/2021
277	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331 - [N24001229]	12/2014	379.16 -	379.16	313.04	11/2017 09/2021	09/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
278	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A - [N24001228]	11/2017	188.80 -	188.80	87.05	05/2019 09/2021	09/2021
279	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION - [N24001226]	12/2014	496.02 -	496.02	240.54	03/2015 03/2022	03/2022
280	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO - [N24001224]	3/2017	423.79 -	423.79	289.08	01/2018 10/2021	10/2021
281	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI - [N24001222]	3/2016	452.94 -	435.61	107.15	07/2016 12/2022	12/2022
282	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001176]	10/2016	172.63 -	172.63	129.65	12/2020 09/2021	09/2021
283	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER - [N24001175]	10/2016	167.62 -	167.62	104.39	12/2020 09/2021	09/2021
284	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN - [N24001152]	9/2018	160.00 -	160.00	116.26	09/2021 -	09/2021
285	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	3/2016	536.65 356.00	536.65	550.22	12/2019 12/2021	12/2021
286	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH - [N24000970]	1/2017	576.48 -	576.48	369.63	01/2018 04/2022	04/2022
287	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216 - [N24000969]	1/2017	263.45 -	263.45	116.24	09/2017 05/2022	05/2022
288	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2 - [N24000968]	11/2016	376.25 -	376.25	310.33	08/2017 12/2021	12/2021
289	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216 - [N24000967]	3/2016	444.84 -	444.84	345.48	09/2016 08/2021	08/2021
290	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A - [N24001376]	3/2021	182.55 -	182.55	-	09/2021 -	09/2021
291	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC - [N24001375]	6/2020	496.47 -	496.47	-	08/2021 -	08/2021
292	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC - [N24001374]	6/2020	437.60 -	437.60	-	08/2021 -	08/2021
293	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC - [N24001373]	1/2020	358.26 -	358.26	-	02/2024 -	02/2024

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
294	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH - [N24001372	2/2021	588.09 -	588.09	-	03/2024 -	03/2024
295	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	1/2017	197.67 -	236.18	21.65	12/2022 -	12/2022
296	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W - [N24001243	3/2020	166.94 -	166.94	28.02	12/2020 12/2022	12/2022
297	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89 - [N24001240	3/2020	370.36 -	370.36	178.51	08/2022 -	08/2022
298	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	148.90	11/2019 10/2021	10/2021
299	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN - [N24000781	5/2018	248.00 -	248.00	109.23	05/2020 12/2021	12/2021
300	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K - [N24000780	2/2018	293.68 -	293.68	179.19	- 10/2021	10/2021
301	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR - [N24000779	2/2018	418.88 -	418.88	287.56	02/2020 09/2021	09/2021
302	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000775	6/2017	282.08 -	282.08	201.79	06/2019 12/2021	12/2021
303	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00 - [N24000774	12/2017	248.22 -	248.22	234.12	12/2019 08/2021	08/2021
304	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	8/2010	193.69 -	327.92	323.23	10/2010 12/2021	12/2021
305	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	890.74	03/2011 12/2021	12/2021
306	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216)(KAKINAD - [N24000964	8/2016	350.61 -	350.61	324.60	01/2017 12/2021	12/2021
307	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	1/2018	418.03 -	418.03	323.62	08/2018 08/2021	08/2021
308	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	3/2016	995.09 995.00	995.09	560.85	05/2016 09/2021	09/2021
309	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	3/2018	289.67 290.00	289.67	206.00	08/2018 11/2021	11/2021
310	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	3/2018	228.32 -	228.32	135.54	08/2018 12/2021	12/2021

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
311	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD - [N24000932	1/2017	319.28 -	319.28	188.42	08/2017 12/2021	12/2021
312	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69 - [N24000931	11/2016	290.15 -	290.15	136.41	05/2017 08/2021	08/2021
313	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS - [N24000894	2/2018	279.44 -	279.44	203.95	03/2018 11/2021	11/2021
314	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS - [N24000893	11/2017	254.17 -	254.17	175.37	02/2018 03/2022	03/2022
315	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS - [N24000891	3/2018	233.04 -	233.04	165.60	03/2018 10/2021	10/2021
316	UPGRADATION OF PORSABHIND ROAD TO 2L + PS - [N24000890	3/2018	217.22 -	226.88	173.03	08/2018 09/2021	09/2021
317	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N - [N24000887	6/2016	236.78 -	263.26	72.02	08/2019 08/2022	08/2022
318	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS - [N24000881	11/2017	184.62 -	184.62	125.42	02/2018 09/2021	09/2021
319	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19. - [N24000880	2/2018	426.18 -	426.18	254.29	09/2020 01/2022	01/2022
320	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS - [N24000870	3/2018	162.56 -	162.56	137.02	03/2018 10/2021	10/2021
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
321	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (- [N24000744	3/2015	262.97 -	262.97	63.74	10/2018 01/2022	01/2022
322	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T - [N24000771	4/2017	553.51 -	553.51	127.99	- 09/2021	09/2021
323	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM32.0 TO KM43.454 [DES - [N24001258	8/2020	202.36 -	202.36	-	04/2022 -	04/2022
324	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG - [N24001257	8/2020	159.85 -	159.85	2.80	10/2022 -	10/2022
325	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D - [N24001255	9/2020	277.44 -	277.44	26.41	10/2022 -	10/2022
326	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM LONG BI-D - [N24001256	8/2020	6,808.69 -	6,808.69	176.00	09/2026 -	09/2026
327	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00 - [N24001254	3/2020	242.97 -	242.97	32.98	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
328	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA - [N24001253]	12/2019	2,680.42 -	2,680.42	794.41	12/2023 -	12/2023
329	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600 - [N24001252]	8/2020	295.97 -	295.97	19.19	04/2023 -	04/2023
330	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N - [N24001251]	3/2019	402.94 -	402.94	44.89	04/2022 -	04/2022
331	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923 - [N24001250]	8/2020	278.46 -	278.46	27.76	03/2022 -	03/2022
332	2-LANING FROM MANU-SIMLUNG (PKG III) - [N24001249]	6/2020	347.36 -	347.36	64.89	01/2022 -	01/2022
333	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800 - [N24001248]	8/2020	208.84 -	208.84	24.01	04/2022 -	04/2022
334	2-LANING FROM MANU-SIMLUNG (PKG I) - [N24001247]	3/2020	247.76 -	247.76	29.13	01/2022 -	01/2022
335	4-LANING OF HAPACHARA - TULUNGIA SECTION - [N24001246]	3/2020	220.20 -	220.20	28.18	12/2022 -	12/2022
336	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO - [N24001245]	9/2020	353.90 -	353.90	18.03	05/2022 -	05/2022
337	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68. - [N24001244]	8/2020	301.06 -	301.06	23.41	04/2022 -	04/2022
338	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1 - [N24000973]	2/2017	176.12 -	176.12	73.92	- 04/2022	04/2022
339	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0 - [N24000972]	2/2017	175.06 -	175.06	87.32	- 04/2022	04/2022
340	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID - [N24001267]	3/2020	178.43 -	178.43	6.87	07/2022 -	07/2022
341	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K - [N24001266]	7/2020	210.79 -	210.79	10.84	04/2022 -	04/2022
342	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE - [N24001265]	3/2020	154.51 -	154.51	12.08	07/2022 -	07/2022
343	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL - [N24001264]	7/2020	228.39 -	228.39	9.72	04/2022 -	04/2022
344	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION - [N24001263]	6/2020	277.50 -	277.50	15.01	01/2022 -	01/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
345	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001262]	7/2020	345.38 -	345.38	74.52	04/2023 -	04/2023
346	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV - [N24001261]	8/2020	311.00 -	311.00	17.38	04/2023 -	04/2023
347	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T - [N24001260]	9/2020	257.15 -	257.15	40.94	04/2022 -	04/2022
348	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM - [N24001259]	9/2020	315.63 -	315.63	7.28	04/2022 -	04/2022
349	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III) - [N24001284]	3/2020	361.53 -	361.53	23.62	06/2022 -	06/2022
350	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV) - [N24001283]	3/2020	281.78 -	281.78	73.31	07/2022 -	07/2022
351	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II) - [N24001282]	3/2020	355.79 -	355.79	55.79	06/2022 -	06/2022
352	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III) - [N24001281]	3/2020	292.24 -	292.24	37.79	07/2022 -	07/2022
353	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I) - [N24001280]	3/2020	320.97 -	320.97	31.88	06/2022 -	06/2022
354	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II) - [N24001279]	3/2020	216.49 -	216.49	33.63	07/2022 -	07/2022
355	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I) - [N24001278]	3/2020	206.88 -	206.88	21.58	07/2022 -	07/2022
356	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54 - [N24001277]	9/2020	275.02 -	275.02	22.39	10/2022 -	10/2022
357	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI - [N24001276]	8/2020	228.97 -	228.97	-	04/2022 -	04/2022
358	DOGINALA - GAU - [N24001320]	12/2020	242.30 -	242.30	-	09/2022 -	09/2022
359	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08 - [N24001319]	6/2020	257.96 -	257.96	95.22	01/2022 -	01/2022
360	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3 - [N24001318]	9/2020	173.17 -	173.17	-	04/2022 -	04/2022
361	2-LANING FROM JOLAIBARI - BELONIA - [N24001317]	6/2020	201.99 -	201.99	14.98	01/2022 -	01/2022
362	LADDA - BASAI - [N24001316]	2/2021	445.96 -	445.96	-	04/2023 -	04/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
363	TADADEGE - HENKAR - [N24001315]	2/2021	550.45 -	550.45	13.03	03/2023 -	03/2023
364	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL - [N24001314]	11/2020	525.68 -	525.68	27.54	12/2023 -	12/2023
365	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (- [N24001313]	11/2020	351.12 -	351.12	40.99	12/2023 -	12/2023
366	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES) [N24001312]	3/2020	167.95 -	167.95	40.95	06/2022 -	06/2022
367	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7 - [N24001368]	3/2021	286.72 -	286.72	-	01/2024 -	01/2024
368	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5 - [N24001367]	3/2021	636.42 -	636.42	-	12/2022 -	12/2022
369	DABOKA KATHKATI PACKAGE-5 [N24001366]	3/2021	288.85 -	288.85	-	01/2023 -	01/2023
370	DABOKA KATHKATI PACKAGE-4 - [N24001365]	2/2021	260.07 -	260.07	-	12/2023 -	12/2023
371	DABOKA KATHKATI PACKAGE-2 - [N24001364]	3/2021	335.88 -	335.88	-	01/2024 -	01/2024
372	MANU-SIMLUNG (PKG 4) - [N24001363]	3/2021	354.79 -	354.79	-	12/2022 -	12/2022
373	RISHI BORDER- ROLEP- MENLA PKG- 3B - [N24001362]	12/2020	410.60 -	410.60	-	02/2024 -	02/2024
374	RISHI BORDER- ROLEP- MENLA PKG- 2A - [N24001361]	1/2021	332.20 -	332.20	-	09/2023 -	09/2023
375	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3 - [N24001360]	3/2021	260.21 -	260.21	-	12/2022 -	12/2022
376	TLABUNG - LUNGLEI PKG-B - [N24001359]	3/2021	740.58 -	740.58	-	01/2023 -	01/2023
377	TLABUNG - LUNGLEI PKG-A - [N24001358]	3/2021	698.44 -	698.44	-	12/2022 -	12/2022
378	DULTE- KWALKULH - CHAMPAI PKG.3 - [N24001357]	3/2021	674.71 -	674.71	-	06/2023 -	06/2023
379	DULTE- KWALKULH - CHAMPAI PKG.2 - [N24001356]	3/2021	233.25 -	233.25	-	12/2022 -	12/2022
380	DULTE- KWALKULH - CHAMPAI PKG.1 - [N24001355]	3/2021	374.39 -	374.39	-	12/2022 -	12/2022
381	TAMENGLONG - MAHUR PKG-3 - [N24001354]	3/2021	234.08 -	234.08	-	12/2022 -	12/2022
382	IMPHAL - KHONGSANG PKG-2 - [N24001353]	3/2021	195.14 -	195.14	-	12/2022 -	12/2022
383	IMPHAL – MOREH PACKAGE- 3 - [N24001352]	3/2021	259.31 -	259.31	-	12/2022 -	12/2022
384	MARIAM - PEREN PKG-2B - [N24001351]	2/2021	232.26 -	232.26	-	12/2022 -	12/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
385	MARIAM - PEREN (PKG 1B) - [N24001350]	2/2021	188.36 -	188.36	-	12/2022 -	12/2022
386	MARIAM - PEREN PKG-1A - [N24001349]	2/2021	226.32 -	226.32	-	12/2022 -	12/2022
387	KARGIL-ZANSKR PACKAGE-8 - [N24001348]	3/2021	398.37 -	398.37	-	01/2023 -	01/2023
388	KARGIL-ZANSKR PACKAGE-7 - [N24001347]	1/2021	308.86 -	308.86	9.46	06/2024 -	06/2024
389	KARGIL-ZANSKR PACKAGE-6 - [N24001346]	1/2021	239.81 -	239.81	23.77	05/2024 -	05/2024
390	KARGIL-ZANSKR PACKAGE-3 - [N24001345]	8/2020	381.01 -	381.01	-	01/2023 -	01/2023
391	KARGIL-ZANSKR PACKAGE-2 - [N24001344]	3/2021	404.89 -	404.89	-	01/2023	01/2023
392	KARGIL-ZANSKR PACKAGE-1 - [N24001343]	3/2021	384.23 -	384.23	-	01/2023	01/2023
393	DONIPAWA TO ASHAJIPORA BYPASS PKG-7 - [N24001342]	3/2021	260.40 -	260.40	-	12/2022 -	12/2022
394	KHELLANI-KHANABAL PKG-3 - [N24001341]	3/2021	398.51 -	398.51	-	12/2022 -	12/2022
395	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA) - [N24001339]	10/2020	157.86 -	157.86	17.63	04/2022 -	04/2022
396	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0 - [N24001338]	10/2020	816.79 -	816.79	2.20	12/2023 -	12/2023
397	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT - [N24001337]	10/2020	493.42 -	493.42	-	11/2023 -	11/2023
398	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO - [N24001336]	8/2020	230.45 -	230.45	1.29	04/2023 -	04/2023
399	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B - [N24001335]	11/2020	284.21 -	284.21	2.63	12/2023 -	12/2023
400	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL - [N24001334]	11/2020	445.51 -	445.51	12.93	12/2023 -	12/2023
401	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350 - [N24001333]	9/2019	761.54 -	761.54	86.48	05/2023 -	05/2023
402	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II) - [N24001332]	3/2020	217.50 -	217.50	34.17	06/2022 -	06/2022
403	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I) - [N24001331]	3/2020	261.13 -	261.13	23.56	06/2022 -	06/2022
404	KARGIL-ZANSKR PACKAGE-5 - [N24001330]	8/2020	169.79 -	169.79	19.50	12/2023 -	12/2023

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
405	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1 - [N24001329	3/2020	165.54 -	165.54	-	07/2022 -	07/2022
406	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD - [N24001328	12/2020	804.00 -	804.00	3.23	08/2023 -	08/2023
407	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM - [N24001327	8/2020	292.80 -	292.80	2.53	05/2022 -	05/2022
408	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD - [N24001326	11/2020	4,997.04 -	4,997.04	10.45	09/2028 -	09/2028
409	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT) - [N24001325	9/2020	262.84 -	262.84	-	05/2023 -	05/2023
410	KHELLANI-KHANABAL PKG-6 - [N24001324	2/2021	285.28 -	285.28	.33	09/2022 -	09/2022
411	KHELLANI-KHANABAL PKG-1 - [N24001323	3/2021	486.45 -	486.45	14.16	09/2022 -	09/2022
412	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L - [N24001322	9/2020	183.31 -	183.31	-	05/2022 -	05/2022
413	DEMBUEN - BRUNI - [N24001321	12/2020	606.63 -	606.63	-	03/2023 -	03/2023
414	KAILASHAHAR TO KHOWAI PKG-2 - [N24001311	11/2020	206.78 -	206.78	3.42	07/2022 -	07/2022
415	KAILASHAHAR TO KHOWAI PKG-3 - [N24001310	11/2020	280.91 -	280.91	59.20	07/2022 -	07/2022
416	KAILASHAHAR TO KHOWAI PKG-4 - [N24001309	11/2020	159.13 -	159.13	7.72	06/2022 -	06/2022
417	KAILASHAHAR TO KHOWAI PKG-5 - [N24001308	11/2020	332.14 -	332.14	-	07/2022 -	07/2022
418	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D - [N24001288	8/2020	232.29 -	232.29	4.98	04/2022 -	04/2022
419	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V) - [N24001287	4/2020	330.80 -	330.80	30.14	12/2021 -	12/2021
420	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV) - [N24001285	3/2020	330.78 -	330.78	40.40	12/2021 -	12/2021
421	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I) - [N24001286	3/2020	278.95 -	278.95	68.48	06/2022 -	06/2022
422	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO - [N24001275	8/2020	268.98 -	268.98	-	04/2022 -	04/2022
423	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI - [N24001274	8/2020	379.39 -	379.39	2.29	04/2022 -	04/2022
424	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B) - [N24001273	7/2020	177.76 -	177.76	23.02	08/2022 -	08/2022
425	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A) - [N24001272	3/2020	167.95 -	167.95	27.29	06/2022 -	06/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
426	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B) - [N24001271	6/2020	365.53 -	365.53	32.49	08/2022 -	08/2022
427	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A) - [N24001270	3/2020	292.24 -	292.24	29.70	06/2022 -	06/2022
428	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB) - [N24001269	3/2020	216.49 -	216.49	26.88	03/2022 -	03/2022
429	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137 - [N24001268	3/2019	471.00 -	471.00	116.31	07/2022 -	07/2022
430	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000865	4/2017	428.11 -	428.11	71.30	09/2019 09/2023	09/2023
431	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000861 <u>National Highways Authority Of India</u>	4/2017	473.18 -	473.18	108.59	09/2019 04/2023	04/2023
432	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	685.76	05/2018 03/2022	03/2022
433	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE -DANTOUR-JA - [N24000838	3/2018	874.25 -	866.55	862.73	- 08/2021	08/2021
434	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 -	724.60	-	03/2023 -	03/2023
435	PREPATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURA - [N24001302	7/2020	3,426.00 -	3,426.00	-	12/2021 -	12/2021
436	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2 - [N24000441	10/2015	593.26 -	716.78	617.58	05/2018 03/2022	03/2022
437	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2 - [N24000653	3/2017	1,373.28 -	1,373.28	1,285.22	03/2020 12/2021	12/2021
	Total		75,425.21 -	77,005.36	18,641.32		
	<u>SHIPPING AND PORTS</u>						
	<u>Inland Waterways Authority Of India</u>						
438	JAL MARG VIKAS PROJECT - [N25000072	1/2018	5,369.18 -	4,633.81	1,901.76	03/2023 -	03/2023
	Total		5,369.18 -	4,633.81	1,901.76		
	<u>STEEL</u>						
	<u>National Mineral Development Corporation (Nmhc)</u>						
439	NMDC INTEGRATED STEEL PLANT - [N12000086	1/2010	15,525.00 -	21,940.00	18,779.12	05/2015 01/2022	01/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Antici Pated
1	2	3	4	5	6	7	8
440	NMDC SLURRY PIPE LINE PROJECT - PHASE-1 - [N12000124]	11/2015	2,907.00 -	2,907.00	408.71	06/2023 -	06/2023
	<u>Rastriya Ispat Nigam Limited</u>						
441	FORGED WHEEL PLANT - [N12000116]	4/2014	1,682.85 -	2,100.00	1,704.90	09/2018 09/2021	09/2021
442	COKE OVEN BATTERY-5 - [N12000117]	12/2011	2,858.00 -	2,858.00	1,995.82	12/2017 07/2022	07/2022
	<u>Steel Authority Of India Limited (Sail)</u>						
443	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY - [N12000122]	11/2020	377.18 -	377.18	37.11	05/2023 -	05/2023
444	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP - [N12000123]	11/2020	542.24 -	542.24	56.59	12/2023 -	12/2023
	Total		23,892.27 -	30,724.42	22,982.25		
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						
445	AHMEDABAD METRO RAIL PROJECT PHASE II - [N28000137]	3/2019	5,384.17 -	5,384.17	193.79	03/2024 -	03/2024
446	SURAT METRO RAIL PROJECT - [N28000138]	3/2019	12,020.32 -	12,020.32	177.50	03/2024 -	03/2024
	<u>Central Public Works Department</u>						
447	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI - [N28000087]	6/2015	197.33 -	217.00	142.78	04/2019 02/2022	02/2022
448	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III- 364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI - [N28000149]	5/2019	299.97 -	299.97	15.87	09/2020 01/2023	01/2023
449	C/O STEEL STRUCTURE BUILDINGS USING PRE- ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG - [N28000143]	2/2020	532.00 -	532.00	452.00	11/2020 09/2021	09/2021
450	REDEVELOPMENT OF GPRA AT MOHAMMADPUR - [N28000110]	10/2016	422.00 -	422.00	80.75	03/2021 06/2023	06/2023
451	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N - [N28000114]	10/2016	392.00 -	392.00	141.85	08/2020 06/2022	06/2022
452	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I - [N28000128]	10/2016	1,180.00 -	1,100.80	35.70	07/2021 06/2023	06/2023
453	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B - [N28000106]	11/2017	238.56 -	238.56	205.72	05/2020 10/2021	10/2021
	<u>Delhi Metro Rail Corporation</u>						
454	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS - [N28000135]	7/2019	24,948.65 -	24,948.65	2,269.98	03/2025 -	03/2025

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
	<u>Maharastra Metro Rail Corporation Ltd.</u>						
455	PUNE METRO RAIL PROJECT (PHASE 1) - [N28000121]	12/2016	11,420.00 -	11,420.00	6,845.77	11/2021 12/2022	12/2022
	<u>Mumbai Metro Rail Corporation Ltd</u>						
456	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	7/2013	23,136.00 -	33,406.00	18,788.65	03/2020 03/2023	03/2023
	<u>Madhya Pradesh Metro Rail Co Limited</u>						
457	BHOPAL METRO RAIL - [N28000124]	11/2018	6,941.40 -	6,941.40	228.95	02/2023 -	02/2023
458	INDORE METRO RAIL - [N28000125]	11/2018	7,500.80 -	7,500.80	138.49	02/2023 -	02/2023
	<u>National Capital Region Transport Corp</u>						
459	DELHI GHAZIABAD MEERUT RRTS CORRIDOR - [N28000134]	3/2019	30,274.00 -	30,274.00	4,567.75	06/2025 -	06/2025
	<u>Patna Metro Rail Corporation</u>						
460	PATNA METRO RAIL CORPORATION LIMITED - [N28000148]	2/2019	13,365.77 -	13,925.50	258.94	06/2024 -	06/2024
	Total		1,38,252.97 -	1,49,023.17	34,544.49		
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
461	SEWER NETWORKS, SPS AND STP, MUNGER - [N30000036]	3/2018	294.02 -	294.02	-	10/2021 -	10/2021
462	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA - [N30000050]	8/2017	578.89 -	578.89	42.75	06/2022 -	06/2022
463	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA - [N30000051]	8/2017	824.00 -	824.00	42.75	06/2022 -	06/2022
	<u>Delhi Jal Board</u>						
464	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L - [N30000014]	3/2017	665.78 -	665.78	211.73	12/2022 -	12/2022
	<u>Kolkata Metropolitan Development Authority</u>						
465	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS - [N30000029]	1/2019	384.96 -	384.96	-	04/2022 -	04/2022
466	INTERCEPTION AND DIVERSION WITH STP AT BALLY - [N30000049]	10/2017	164.93 -	164.93	-	12/2021 -	12/2021
467	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI [N30000048]	1/2018	172.10 -	172.10	-	12/2021 -	12/2021
468	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL - [N30000030]	3/2019	287.53 -	287.53	-	04/2022 -	04/2022

List of Projects on schedule w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)	
						Date of Commissioning	
Sl.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original /Revised	Anticipated
1	2	3	4	5	6	7	8
469	I AND D AND STP WORKS AT BURDWAN WEST BENGAL - [N30000031]	12/2018	234.31 -	234.31	-	04/2022 -	04/2022
470	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS - [N30000033]	3/2018	165.16 -	165.16	-	06/2022 -	06/2022
471	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH - [N30000045]	8/2017	185.22 -	185.22	-	12/2021 -	12/2021
472	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA - [N30000034]	8/2017	307.12 -	307.12	-	09/2022 -	09/2022
	<u>Uttar Pradesh Jal Nigam</u>						
473	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA - [N30000006]	5/2017	767.59 -	767.59	112.27	09/2021 -	09/2021
474	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS - [N30000007]	3/2018	904.00 -	904.00	148.55	09/2021 -	09/2021
475	FARRUKHABAD I AND D AND STP WORKS HAM - [N30000008]	10/2017	213.62 -	261.12	-	03/2022 -	03/2022
476	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	2/2019	681.78 -	690.71	-	06/2022 -	06/2022
477	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH - [N30000022]	1/2019	206.05 -	206.05	53.62	10/2021 -	10/2021
478	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	1/2019	231.79 -	234.03	-	12/2021 -	12/2021
479	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS - [N30000010]	3/2018	967.23 -	967.23	51.66	09/2021 -	09/2021
480	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH - [N30000013]	3/2019	271.39 -	271.39	-	08/2021 -	08/2021
	Total		8,507.47 -	8,566.14	663.33		
	Grand Total		8,89,101.60	9,92,697.80	3,27,540.87		

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Annexure - XIII

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	<u>ATOMIC ENERGY</u>						
	<u>Nuclear Power Corporation Of India Limited</u>						
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]	10/2009	11,459.00 - 11,459.00	16,580.00	12/2015 -	02/2022	44.69
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]	10/2009	12,320.00 - 12,320.00	17,079.00	12/2016 -	03/2023	38.63
	Total		23,779.00 - 23,779.00	33,659.00			
	<u>CIVIL AVIATION</u>						
	<u>Airport Authority Of India Limited</u>						
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]	07/2018	346.27 - 346.27	480.33	09/2021 -	12/2022	38.72
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI [N04000083]	12/2016	1,142.00 - 1,142.00	1,232.00	03/2021 -	03/2023	7.88
	Total		1,488.27 - 1,488.27	1,712.33			
	<u>COAL</u>						
	<u>Eastern Coal Fields Limited</u>						
5	RANIGANJ MASTER PLAN - [N06000163]	08/2009	2,661.73 - 2,661.73	5,146.48	08/2019 -	08/2024	93.35
	<u>Mahanadi Coal Fields Limited</u>						
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]	11/2008	479.53 - 479.53	703.39	03/2013 -	03/2024	46.68
	<u>Neyveli Lignite Corporation</u>						
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152]	07/2016	17,237.00 - 17,237.00	17,237.80	11/2021 -	11/2022	.00
	<u>Singareni Colliers Company Limited</u>						
8	RAMAGUNDAM OC-II EXTENSION - [N06000078]	12/2009	418.97 - 418.97	489.62	03/2012 -	03/2023	16.86

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
9	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129]	05/2015	397.09 - 397.09	442.42	03/2019 -	03/2022	11.42
10	JALAGAM VENGALA RAO OCP-II - [N06000094]	07/2011	447.06 - 447.06	473.22	03/2015 -	03/2023	5.85
11	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]	07/2011	162.76 - 162.76	349.28	03/2015 -	03/2022	114.60
<u>Western Coal Fields Limited</u>							
12	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 - 289.29	289.30	03/2022 -	03/2025	.00
Total			22,093.43 .00 22,093.43	25,131.51			
<u>DEPARTMENT OF HIGHER EDUCATION</u>							
<u>Central Public Works Department</u>							
13	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00 496.00	498.99	06/2017 -	03/2022	.60
14	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 - 549.31	559.47	07/2019 -	-	1.85
15	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00 199.00	205.00	09/2020 -	-	3.02
16	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMENITIES - [N44000001]	03/2021	127.26 - 127.26	188.88	10/2023 -	10/2023	48.42
<u>Rail India Technical And Economic Service</u>							
17	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 - 484.32	626.26	09/2014 -	-	29.31
Total			1,843.07 695.00 1,855.89	2,078.60			
<u>DPIIT</u>							
<u>Delhi Mumbai Industrial Corridor</u>							
18	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 - 12,579.09	13,812.30	09/2019 -	07/2021	9.80
<u>India International Convention And Expo Centre</u>							

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
19	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 - 4,773.00	5,178.00	12/2019 -	05/2022	8.49
	Total		17,352.09 .00 17,352.09	18,990.30			
	<u>HEALTH AND FAMILY WELFARE</u>						
	<u>Central Public Works Department</u>						
20	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 - 1,577.00	1,828.00	09/2025 -	09/2025	15.92
	<u>Hospital Services Consultancy Corporation Ltd</u>						
21	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 - 414.11	655.58	11/2013 -	09/2021	58.31
22	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 - 204.44	250.00	05/2017 -	03/2021	22.29
23	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 - 293.65	325.00	05/2017 -	01/2020	10.68
24	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]	12/2014	168.90 - 168.90	191.20	05/2017 -	07/2019	13.20
25	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]	09/2014	505.58 - 505.58	585.00	03/2018 -	09/2019	15.71
26	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 - 152.95	177.92	02/2018 -	03/2021	16.33
27	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 - 244.00	248.00	09/2018 -	05/2019	1.64
28	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 - 272.19	272.54	03/2019 -	03/2021	.13
29	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 - 156.56	190.34	- -	11/2021	21.58
30	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 - 249.01	249.07	- -	01/2021	.02
	<u>National Building Construcion Corporation Ltd</u>						
31	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 - 1,351.00	1,471.00	09/2021 -	06/2022	8.88

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
	Total		5,589.39 .00 5,589.39	6,443.65			
	<u>HOME AFFAIRS</u>						
	<u>Central Public Works Department</u>						
32	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071	10/2013	1,219.21 - 1,219.21	2,000.00	10/2019 -	03/2022	64.04
	Total		1,219.21 .00 1,219.21	2,000.00			
	<u>PETROLEUM</u>						
	<u>Hindustan Petroleum Corporation Limited</u>						
33	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296	09/2017	2,677.00 - 2,677.00	3,072.00	06/2021 -	07/2022	14.76
	<u>Indian Oil Corporation Limited</u>						
34	LPG TERMINAL AT KOCHI - [N16000171	10/2015	607.06 - 607.06	1,236.00	10/2017 -	03/2022	103.60
35	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236	06/2016	423.00 - 423.00	502.00	08/2019 -	05/2021	18.68
	<u>Oil & Natural Gas Corporation Limited</u>						
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) [N16000128	03/2011	861.79 - 1,846.46	2,001.34	05/2013 -	02/2022	132.23
	Total		4,568.85 .00 5,553.52	6,811.34			
	<u>POWER</u>						
	<u>National Thermal Power Corporation</u>						
37	NORTH KARANPURA STPP (3X660 MW) - [N18000177	02/2014	14,366.58 - 14,366.58	15,389.42	06/2019 -	12/2023	7.12
38	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142	07/2012	1,527.00 - 1,527.00	1,801.07	08/2017 -	-	17.95
39	PAKRI BARWADIH COAL MINING PROJECT - [N18000225	10/2004	4,237.96 4,238.00 4,238.00	4,552.00	10/2017 -	-	7.41
	<u>Power Grid Corporation Of India Limited</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
40	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]	10/2008	4,824.12 - 4,824.12	5,071.94	10/2012 -	-	5.14
41	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52 - 1,364.52	1,891.41	04/2016 -	-	38.61
42	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]	01/2015	871.62 - 871.62	902.49	10/2017 -	-	3.54
43	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28 - 203.28	260.03	07/2017 -	-	27.92
44	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49 - 487.49	639.46	06/2014 -	-	31.17
45	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46 - 408.46	516.12	01/2019 -	-	26.36
46	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00 3,500.00	3,994.00	07/2020 -	10/2021	14.11
47	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	05/2017	445.89 - 445.89	675.73	02/2019 -	-	51.55
<u>SatluJ Jal Vidyut Nigam Limited</u>							
48	NAITWAR MORI HEP - [N18000265]	10/2017	648.33 - 648.33	947.89	12/2021 -	06/2022	46.20
Total							
			32,885.25 7,738.00 32,885.29	36,641.56			
<u>RAILWAYS</u>							
<u>Central Railways</u>							
49	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 - 3,168.29	3,445.48	03/2023 -	03/2023	8.75
50	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89 - 792.89	910.93	03/2021 -	03/2023	14.89
51	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06 - 184.06	325.00	03/2019 -	-	76.57
52	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 - 2,271.50	4,794.60	03/2021 -	03/2023	111.08

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
53	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 - 2,425.00	5,341.68	03/2024 -	03/2024	120.28
54	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 - 2,750.00	3,438.51	03/2024 -	-	25.04
55	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19 - 1,272.19	1,283.49	03/2022 -	03/2023	.89
56	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00 3,627.00	3,627.47	03/2024 -	03/2023	.01
57	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00 - 1,876.00	2,081.27	03/2023 -	03/2023	10.94
	<u>Container Corporation Of India</u>						
58	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 - 387.70	487.13	03/2018 -	-	25.65
59	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 - 234.50	235.00	03/2019 -	-	.21
	<u>East Central Railways</u>						
60	KODERMA-RANCHI VIA BARKAKANA (NL),ECR - [220100222]	03/1999	1,033.07 - 3,020.95	3,620.00	- -	03/2022	250.41
61	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR - [220100240]	04/1997	324.73 - 898.53	1,070.00	03/2012 -	11/2022	229.50
62	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 - 380.00	519.33	- -	03/2025	36.67
63	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 - 678.54	929.86	03/2019 -	12/2021	37.04
64	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 - 415.67	549.75	- -	-	32.26
65	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 - 326.20	2,995.01	- -	03/2024	818.15
66	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 - 378.56	1,858.75	- -	03/2023	391.01
67	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 - 211.00	1,006.00	- -	-	376.78

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
68	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181	04/2009	548.00 - 548.00	819.01	03/2020 -	03/2023	49.45
69	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182	04/2013	213.01 - 213.01	495.00	- -	10/2019	132.38
70	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374	01/1991	332.15 - 332.15	546.71	07/2014 -	-	64.60
71	GARHWA ROAD-RAMNA - [N22000465	03/2015	348.23 - 348.23	390.00	03/2021 -	03/2022	11.99
72	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472	04/2016	744.04 - 744.04	1,215.54	03/2021 -	03/2024	63.37
73	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473	04/2016	731.64 - 731.64	1,185.73	03/2021 -	03/2024	62.06
74	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475	04/1998	180.82 - 180.82	726.31	- -	08/2020	301.68
75	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIYAWAN-BIHARSHARIF, - [N22000476	04/1991	329.39 - 329.39	1,483.14	- -	03/2022	350.27
<u>East Coast Railway</u>							
76	SAMBALPUR-TALCHER DOUBLING - [N22000315	03/2011	1,111.99 - 1,111.99	1,539.28	02/2019 -	12/2021	38.43
77	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380	04/2015	701.61 - 701.61	810.02	11/2018 -	03/2024	15.45
<u>Eastern Railways</u>							
78	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272	04/2000	1,188.91 - 1,188.91	1,619.48	03/2019 12/2009	03/2025	36.22
79	DEOGHAR - SULTANGANJ (INL), ER - [220100273	04/2000	607.09 - 607.09	1,425.44	02/2013 -	03/2024	134.80
80	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229	04/2010	365.17 - 365.17	439.30	03/2017 -	03/2025	20.30
81	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235	04/2010	365.17 - 365.17	527.54	- -	03/2025	44.46
82	HANSDIHA-GODDA NL - [N22000236	04/2011	542.18 - 542.18	663.13	03/2020 -	03/2021	22.31

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
83	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 - 175.80	495.10	- -	03/2022	181.63
84	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]	04/2011	299.60 - 299.60	335.62	03/2017 -	03/2026	12.02
85	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 - 494.54	494.59	03/2005 -	03/2025	.01
86	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]	04/2000	297.47 - 297.47	298.22	- -	03/2025	.25
87	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 - 499.96	680.68	02/2012 -	03/2025	36.15
88	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 - 250.93	310.70	- -	03/2024	23.82
89	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 - 255.64	272.20	- -	03/2022	6.48
90	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 - 406.99	545.70	03/2006 -	03/2025	34.08
91	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]	04/2007	450.00 - 450.00	1,261.34	- -	03/2025	180.30
92	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 - 172.03	260.10	- -	03/2025	51.19
93	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 - 915.98	2,137.81	03/2022 -	03/2025	133.39
94	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 - 288.35	502.48	- -	03/2021	74.26
95	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 - 261.38	565.00	- -	05/2019	116.16
96	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 - 923.52	995.10	03/2016 -	03/2025	7.75
97	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL [N22000225]	04/2005	595.51 - 595.51	769.40	03/2017 -	03/2025	29.20
Indian Railway Construction Company Limited							
98	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 - 2,288.00	4,970.11	03/2022 -	09/2023	117.23

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
99	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]	04/2013	3,055.00 - 3,055.00	3,055.15	09/2018 -	06/2022	.00
	<u>Metropolitan Rapid Transport Projects</u>						
100	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 - 1,049.69	3,404.92	12/2006 -	-	224.37
101	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 - 495.44	2,980.41	03/2004 -	03/2022	501.57
102	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP - [N22000028]	04/2006	495.74 - 495.74	734.01	06/2013 -	07/2022	48.06
103	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]	03/2013	4,874.58 - 4,874.58	8,574.97	03/2016 -	-	75.91
	<u>North Central Railway</u>						
104	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 - 120.00	346.00	12/2008 -	-	188.33
105	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 - 2,912.96	3,845.60	03/2022 -	12/2024	32.02
106	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00 668.00	680.00	03/2020 -	-	1.80
	<u>North East Frontier Railway</u>						
107	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR [220100135]	04/1983	297.32 - 200.34	614.00	03/2019 -	-	106.51
108	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 - 5,021.45	5,521.45	03/2014 -	03/2024	130.69
109	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 - 2,531.34	4,541.38	12/2008 -	09/2021	284.80
110	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 - 4,454.17	12,264.15	03/2011 -	12/2023	175.34
111	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 - 385.20	1,105.00	03/2019 -	03/2023	186.86
112	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR [N22000087]	09/2006	532.87 - 2,132.03	2,145.00	03/2019 -	03/2024	302.54
113	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) [N22000124]	04/2006	2,326.52 - 2,326.52	6,911.00	03/2015 -	03/2026	197.05

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
114	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 - 333.76	360.00	- -	-	7.86
115	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 - 4,084.69	8,600.00	12/2015 -	12/2023	542.04
116	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 - 221.42	380.00	- -	-	71.62
117	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 - 569.63	742.00	03/2020 -	03/2022	30.26
118	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 - 1,202.33	4,083.02	03/2021 -	-	350.44
119	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 - 242.22	471.00	03/2020 -	-	94.45
120	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 - 241.52	373.87	- -	03/2022	54.80
121	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 - 414.84	750.00	03/2020 -	-	80.79
122	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 - 819.23	1,871.00	- -	-	128.39
123	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 - 486.96	800.00	03/2019 -	06/2021	154.78
124	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 - 2,232.32	2,950.00	03/2022 -	03/2023	32.15
125	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 - 870.96	1,873.21	03/2021 -	03/2022	115.07
126	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) [N22000390]	04/2016	602.27 - 602.27	2,144.78	12/2021 -	09/2021	256.12
127	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN - [N22000499]	02/1999	380.60 - 380.60	1,090.60	04/2010 -	-	186.55
<u>North Eastern Railway</u>							
128	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 - 142.45	228.40	- -	-	60.34
129	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 - 182.92	197.73	- -	-	8.10

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
130	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 - 307.00	1,409.09	- -	-	358.99
131	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP - [N22000131]	03/2007	243.78 - 243.78	895.00	12/2021 -	12/2021	267.13
132	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 - 295.00	580.00	01/2019 -	02/2022	96.61
133	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 - 643.00	644.00	- -	-	.16
134	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 - 1,295.42	1,758.00	03/2022 -	03/2022	35.71
135	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 - 213.00	213.35	04/2016 -	12/2021	.16
136	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 - 150.00	341.66	04/2017 -	10/2022	127.77
137	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 - 1,343.00	1,476.15	01/2018 -	-	9.91
138	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]	04/2017	622.50 427.00 427.00	590.00	04/2017 -	03/2021	38.17
139	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 - 602.50	714.34	- -	12/2023	18.56
<u>North Western Railway</u>							
140	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 - 410.08	860.41	02/2019 -	06/2022	109.82
141	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 - 600.00	701.81	03/2020 -	10/2022	16.97
142	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]	05/2015	873.71 - 873.71	2,215.27	- -	-	153.55
143	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 - 246.08	395.00	12/2019 -	03/2021	60.52
144	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 - 2,082.75	4,262.36	- -	-	104.65
145	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 - 236.93	350.45	10/2018 -	01/2020	47.91

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
146	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTURGARH-UDAIPUR [N22000152]	04/2013	420.18 - 420.18	480.00	03/2020 -	09/2021	14.24
147	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 - 213.39	375.00	11/2019 -	03/2021	75.73
148	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 - 242.09	525.00	02/2019 -	02/2020	116.86
	<u>Northern Railway</u>						
149	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 - 156.65	359.00	- -	03/2024	129.17
150	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 - 287.00	893.45	12/2011 -	06/2021	211.31
151	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 - 336.91	791.39	- -	03/2023	134.90
152	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 - 295.68	419.00	- -	09/2023	41.71
153	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 - 219.83	346.63	- -	-	57.68
154	QADIAN-BEAS - [N22000295]	04/2011	205.22 - 205.22	841.90	- -	03/2024	310.24
155	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 - 450.00	2,200.00	07/2012 -	03/2024	388.89
156	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 - 328.14	1,540.13	03/2023 -	03/2023	369.35
157	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 - 625.00	859.00	03/2016 -	-	37.44
	<u>Rail Vikas Nigam Ltd.</u>						
158	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 - 1,185.64	1,844.47	12/2017 -	-	55.57
159	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 - 1,202.70	2,440.53	02/2015 -	06/2022	102.92
160	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00 207.00	396.00	03/2009 03/2009	-	91.30

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
161	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22
162	BHANUPALI-BILASPUR BERI NL - [N22000273]	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62
163	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04
164	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78
165	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95
166	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58
167	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75
168	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	-	35.42
169	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68
170	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15
171	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32
172	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98
173	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83
174	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02
175	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08
176	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	12/2021	281.93

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
177	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 - 2,335.67	3,327.72	12/2024 -	12/2026	42.47
178	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 - 948.04	2,009.00	03/2020 -	12/2021	111.91
179	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 - 942.95	1,536.00	03/2019 -	06/2022	62.89
180	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]	03/2012	1,183.25 - 1,183.25	1,825.00	12/2020 -	12/2022	54.24
181	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 - 1,485.85	1,835.83	12/2020 -	12/2021	23.55
	<u>Railway Electrification</u>						
182	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]	02/2008	171.10 - 171.10	275.08	03/2012 -	-	60.77
	<u>South Central Railway</u>						
183	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]	12/2001	1,045.20 - 1,045.20	2,120.16	03/2009 -	03/2024	102.85
184	MANUGURU-RAMAGUNDAM - [N22000259]	04/2013	1,112.00 - 1,112.00	2,911.84	- -	-	161.86
185	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261]	04/2012	1,856.95 - 1,856.95	1,952.68	03/2023 -	03/2024	5.16
186	NADIKUDE-SRI KALAHASTI - [N22000286]	04/2011	2,288.70 - 2,288.70	2,643.25	03/2021 -	03/2024	15.49
187	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]	04/2010	704.31 - 704.31	927.94	03/2020 -	11/2021	31.75
188	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]	04/2008	2,132.77 - 2,132.77	3,037.95	03/2014 -	03/2027	42.44
189	NANDYAL-YERRAGUNTALA(NL),SCR - [220100192]	03/1996	164.36 - 164.36	1,050.00	02/2009 -	-	538.84
190	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]	04/1997	1,723.00 1.00 1.00	3,421.35	03/2000 -	03/2023	3,42,035.00
191	GUNTUR-GUNTAKAL - [N22000368]	04/2016	3,631.00 - 3,631.00	3,887.48	03/2022 -	03/2024	7.06

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
192	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00 185.00	449.39	03/2022 -	12/2022	142.91
	<u>South East Central Railway</u>						
193	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 - 1,413.76	1,511.50	- -	08/2020	293.84
194	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 - 1,756.00	2,005.25	04/2020 -	03/2021	291.76
195	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 - 1,370.00	1,370.94	12/2021 -	12/2023	.07
	<u>South Eastern Railway</u>						
196	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208	04/1974	393.46 154.30 154.30	1,026.00	03/2007 03/2007	-	564.94
197	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 - 148.77	377.00	12/2016 -	08/2020	153.41
198	BOWAICHANDI-ARAMBAGH - [N22000159	04/2010	267.37 - 267.37	620.00	- -	03/2025	131.89
199	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160	04/2010	651.00 - 651.00	1,009.00	03/2015 -	03/2025	54.99
200	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162	04/2010	149.90 - 149.90	230.00	03/2015 -	-	53.44
201	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 - 258.20	358.68	12/2018 -	08/2021	38.92
202	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395	11/2015	969.83 - 969.83	1,312.96	03/2020 -	02/2022	35.38
203	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402	04/1998	1,027.40 - 1,027.40	2,373.00	03/2003 -	03/2030	130.97
	<u>South Western Railway</u>						
204	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256	04/2011	1,801.01 - 1,801.01	2,161.36	- -	12/2023	20.01
205	BAGALKOT-KUDACHI NL - [N22000258	04/2010	986.30 - 986.30	1,530.09	03/2016 -	12/2026	55.13
206	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276	04/2013	558.00 - 558.00	692.00	- -	12/2023	24.01

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
207	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 - 296.00	466.65	- -	12/2023	57.65
208	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 - 2,062.30	2,432.50	- -	12/2025	17.95
209	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 - 146.75	167.50	- -	12/2023	14.14
210	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 - 103.74	5,174.30	- -	12/2024	123.51
211	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 - 1,382.78	1,960.00	03/2002 -	03/2024	41.74
212	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 - 1,156.94	1,800.59	03/2020 -	03/2023	55.63
213	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 - 860.43	1,147.00	03/2020 -	09/2021	33.31
214	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 - 578.00	760.00	03/2020 -	11/2021	31.49
215	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 - 1,877.81	1,878.00	03/2019 -	03/2024	16.31
<u>Southern Railway</u>							
216	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND'-AGASTIYAMPALLI [N22000079]	09/2007	724.69 - 724.69	2,950.00	02/2019 -	03/2025	307.07
217	TIDIVANAM-NAGARI (NL) - [N22000085]	09/2006	582.83 - 582.83	3,150.00	- -	12/2025	440.47
218	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]	09/1995	303.98 - 303.98	1,720.00	03/2020 -	03/2025	465.83
219	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]	10/1998	1,566.00 - 1,566.00	2,815.62	- -	-	79.80
220	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 - 151.84	527.37	02/2019 -	-	247.32
221	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]	04/2008	523.52 - 523.52	1,205.00	- -	03/2024	130.17
222	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]	04/2013	839.00 - 839.00	839.01	- -	-	.00

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
223	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]	04/1999	198.68 - 198.68	559.95	- -	03/2024	181.84
224	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 - 270.14	457.08	- -	12/2021	69.20
225	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 - 252.96	369.55	- -	-	46.09
226	ERODE-PALANI - [N22000199]	04/2008	288.57 - 288.57	603.23	- -	-	109.04
227	MADURAI-BODINAYAKKANUR - [N22000201]	04/2008	164.41 - 164.41	608.13	- -	12/2021	269.89
228	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202]	04/2007	931.98 - 931.98	1,121.00	- -	08/2021	20.28
229	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 - 189.24	275.21	- -	-	45.43
230	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]	04/2011	120.70 - 120.70	2,172.16	03/2019 -	12/2027	1,699.64
231	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM [N22000373]	10/2013	187.26 - 187.26	327.00	04/2014 -	-	74.62
232	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]	02/2015	1,000.00 - 1,000.00	1,246.00	- -	-	24.60
233	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]	02/1996	268.87 - 268.87	950.00	03/2005 -	09/2021	253.33
234	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]	02/2015	760.00 - 760.00	1,536.00	03/2020 -	06/2022	102.11
<u>West Central Railway</u>							
235	RAMGANJMUUNDI-BHOPAL (NL),WCR - [220100314]	04/2001	424.60 - 424.60	2,909.99	03/2021 -	03/2024	585.35
236	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]	09/1998	247.66 - 247.66	8,248.50	05/2008 -	03/2025	3,230.57
237	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]	12/2015	1,763.93 - 1,763.93	2,470.00	03/2020 -	03/2024	40.03
<u>Western Railway</u>							

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
238	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120]	04/2008	3,503.69 - 5,839.02	6,171.08	03/2022 -	03/2024	76.13
239	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) [N22000125]	04/2006	117.36 196.95 196.95	202.35	03/2011 -	-	2.74
240	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121]	04/2008	829.74 - 1,246.59	1,886.76	03/2020 -	03/2024	127.39
241	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143]	04/1994	320.66 - 858.96	1,378.11	03/2019 -	03/2023	329.77
242	VIRAMGAM-SAMAKHIALI (DL) - [N22000145]	04/2011	1,037.15 - 1,125.53	1,383.69	03/2021 -	12/2022	33.41
243	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487]	02/1991	551.51 - 724.70	890.76	03/2019 -	10/2021	61.51
244	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM [N22000494]	04/2017	691.84 - 811.60	890.62	03/2020 -	09/2021	28.73
	Total		1,94,075.60 5,466.25 2,07,391.13	3,60,289.33			
	<u>ROAD TRANSPORT AND HIGHWAYS</u>						
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>						
245	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306]	11/2010	624.41 - 624.41	992.67	03/2011 -	12/2021	58.98
246	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308]	08/2010	193.69 - 193.69	327.92	10/2010 -	12/2021	69.30
247	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]	03/2015	280.16 - 280.16	290.59	- -	-	3.72
248	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]	01/2014	255.75 348.00 348.00	348.43	09/2017 -	-	.12
249	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392]	11/2010	268.08 - 268.08	390.73	05/2017 -	05/2022	45.75
250	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 [N24000391]	11/2015	889.24 - 889.24	904.82	- -	-	1.75
251	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) [N24000415]	08/2010	195.04 - 195.04	377.99	10/2010 -	12/2021	93.80

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
252	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 - 319.68	369.77	- -	-	15.67
253	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 - 460.73	461.00	- -	-	.06
254	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 - 237.80	238.00	11/2019 -	10/2021	.08
255	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 - 166.21	173.41	08/2018 -	09/2021	4.33
256	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 - 217.22	226.88	08/2018 -	09/2021	4.45
257	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DSIGN CH0.0) TO KM 275/622(DSIGN CH 5.12 - [N24000928	10/2015	333.21 - 333.21	353.43	12/2015 -	-	6.07
258	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929	09/2016	372.68 - 309.37	372.68	02/2017 -	-	.00
259	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	02/2017	429.43 - 373.05	429.43	11/2017 -	-	.00
260	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	03/2018	228.32 - 202.83	228.32	08/2018 -	12/2021	.00
261	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	03/2018	289.67 290.00 274.73	289.67	08/2018 -	11/2021	-.11
262	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00 995.00	995.09	05/2016 -	09/2021	.01
263	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	01/2018	418.03 - 381.75	418.03	08/2018 -	08/2021	.00
264	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965	01/2016	386.09 - 316.06	386.09	05/2016 -	-	.00
265	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00 203.00	203.21	05/2019 -	-	.10
266	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00 373.00	373.10	05/2019 -	-	.03
267	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00 322.00	322.48	05/2019 -	-	.15

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
268	CHIKALI TO KHAMGAON - [N24001012]	02/2017	548.03 548.00 548.00	548.03	06/2019 -	-	.01
269	DIGRAS DARWAH KARANJA - [N24001013]	01/2017	391.06 391.00 391.00	391.06	06/2019 -	-	.02
270	MORSHI TO ACHALPUR - [N24001015]	01/2017	341.16 341.00 341.00	341.16	06/2019 -	-	.05
271	KARAD TO VITA - [N24001049]	01/2018	344.85 245.00 245.00	344.85	12/2019 -	-	40.76
272	SANGOLA TO JATH - [N24001052]	01/2018	257.38 257.00 257.00	257.38	12/2019 -	-	.15
273	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]	02/2017	422.02 422.00 422.00	422.02	07/2019 -	-	.00
274	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]	02/2017	407.19 407.00 407.00	407.19	06/2019 -	-	.05
275	PALPHATA TO PHULAMBARI - [N24001060]	03/2018	227.19 227.00 227.00	227.19	12/2019 -	-	.08
276	CHIKALI TO DHAD - [N24001061]	03/2018	189.46 189.00 189.00	189.46	12/2019 -	-	.24
277	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]	03/2018	336.21 336.00 336.00	336.21	12/2019 -	-	.06
278	WADIGODRI TO DHANGRIIMPRI - [N24001063]	03/2018	194.23 194.00 194.00	194.23	02/2020 -	-	.12
279	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]	03/2018	217.14 217.00 217.00	217.14	02/2020 -	-	.06
280	PARBHANI TO GANGKHED - [N24001065]	03/2018	238.19 238.00 238.00	238.19	12/2019 -	-	.08
281	LATUR TO PANGAON - [N24001066]	03/2018	336.47 336.00 336.00	336.47	12/2019 -	-	.14
282	OMREGA TO AUSA - [N24001067]	03/2018	272.04 272.00 272.00	272.04	12/2019 -	-	.01
283	KOTHARI TO DHANORA - [N24001073]	09/2018	301.38 301.00 301.00	301.38	08/2020 -	-	.13

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
284	OSMANNAGAR TO KUNDRAL - [N24001075]	09/2017	344.25 344.00 344.00	344.25	08/2020 -	-	.07
285	KUNDRAL TO WAZAR - [N24001077]	01/2018	225.25 225.00 225.00	225.25	12/2019 -	-	.11
286	ARDHAPUR TO HIMAYATNAGAR - [N24001079]	12/2017	426.06 426.00 426.00	426.06	06/2020 -	-	.01
287	CHIKLI TO TAKARKHED - [N24001083]	03/2018	393.10 393.00 393.00	393.10	12/2019 -	-	.03
288	MANGRUPHIR TO MAHAN - [N24001087]	03/2018	222.13 222.00 222.00	222.13	11/2019 -	-	.06
289	JALGAON TO NANDURA - [N24001088]	03/2018	177.84 177.00 177.00	177.84	12/2019 -	-	.47
290	MALEGAON TO RISOD - [N24001089]	02/2018	303.24 303.00 303.00	303.24	12/2019 -	-	.08
291	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091]	03/2016	536.65 356.00 356.00	536.65	12/2019 -	12/2021	50.74
292	NAIGAONBANDI TO MANGRULPIR - [N24001094]	12/2017	244.04 244.00 244.00	244.04	03/2019 -	-	.02
293	TALEGAON TO GONAPUR - [N24001096]	01/2018	264.41 264.00 264.00	264.41	03/2019 -	-	.16
294	SELDOH TO PANVAR - [N24001097]	07/2018	404.33 404.00 404.00	404.33	05/2020 -	-	.08
295	PANCHARAL TO MANDANGHAR - [N24001107]	07/2018	381.08 302.00 302.00	381.08	05/2020 -	-	26.19
296	VADPALE TO BHOGAN KHURD - [N24001115]	01/2017	1,598.47 1,560.00 1,560.00	1,598.47	11/2019 -	-	2.47
297	BHOKAR TO SARSAM - [N24001128]	02/2017	295.09 - 295.09	295.99	07/2019 -	-	.31
298	BHOGAN KHURD TO KASHEDI - [N24001132]	09/2017	743.21 743.00 743.00	743.21	06/2021 -	-	.03
299	PARSHURAM GHAT TO ARAWALI - [N24001133]	04/2016	983.14 983.00 983.00	983.14	12/2019 -	-	.01

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
300	KANTE TO WAKED - [N24001134]	03/2016	1,230.02 1,230.00 1,230.00	1,230.02	11/2019 -	-	.00
301	KALMATH TO ZARAP - [N24001137]	09/2016	1,338.13 1,338.00 1,338.00	1,338.13	03/2020 -	-	.01
302	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]	11/2016	215.16 215.00 215.00	215.16	09/2019 -	10/2019	.07
303	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]	03/2016	240.30 240.00 240.00	240.30	01/2020 -	-	.13
304	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH - [N24001161]	12/2017	297.30 -	318.28	01/2019 -	-	7.06
305	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]	03/2018	325.86 -	386.41	10/2018 -	-	18.58
306	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181]	08/2010	186.96 -	322.24	09/2014 -	12/2021	72.36
307	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]	09/2011	1,979.00 -	2,036.90	- -	-	2.93
308	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219]	01/2016	476.20 544.00 543.73	544.00	09/2016 -	12/2021	.00
309	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]	03/2018	240.38 -	240.38	06/2019 -	-	.00
310	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307]	01/2017	197.67 -	236.18	12/2022 -	12/2022	19.48
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>						
311	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]	02/2017	195.23 -	252.79	04/2017 -	03/2022	29.48
312	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]	02/2017	203.36 -	263.31	04/2017 -	03/2022	29.48
313	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73
314	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]	01/2017	198.22 -	252.05	04/2017 -	03/2022	27.16

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
315	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]	04/2017	388.00 - 388.00	447.37	10/2017 -	-	15.30
	<u>National Highways Authority Of India</u>						
316	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 - 280.00	612.58	02/2009 -	-	118.78
317	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 - 199.81	340.14	04/2009 -	-	70.23
318	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]	12/2003	167.64 - 167.64	435.78	11/2008 -	-	159.95
319	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]	12/2003	155.04 - 155.04	255.23	11/2008 -	-	64.62
320	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20) - [N24000049]	12/2003	160.00 - 160.00	167.98	05/2008 -	06/2019	4.99
321	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 - 196.00	655.17	07/2009 -	-	234.27
322	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 - 325.00	475.00	05/2013 -	-	46.15
323	BRAHMPUTRA BRIDGE, NH NO-31 - [N24000063]	12/2003	217.61 - 217.61	360.84	04/2010 -	07/2019	65.82
324	NALBARI T BIJNI (AS-7) - [N24000048]	12/2003	208.00 - 208.00	230.00	04/2008 -	02/2021	10.58
325	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]	04/2014	1,266.60 - 1,266.60	1,544.00	09/2016 -	-	21.90
326	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00 - 2,159.00	2,519.00	06/2015 -	-	16.67
327	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00 - 2,848.00	3,379.45	03/2014 -	12/2022	18.66
328	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 - 511.54	591.00	11/2013 -	-	15.53
329	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 - 291.36	469.31	01/2014 -	-	61.08
330	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]	04/2014	351.34 - 351.34	417.68	01/2016 -	-	18.88

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
331	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI - [N24000367]	04/2014	495.78 - 495.78	627.93	01/2016 -	-	26.66
332	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435]	10/2015	531.13 - 531.13	744.73	05/2018 -	03/2022	40.22
333	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]	06/2015	845.24 - 845.24	941.00	- -	01/2020	11.33
334	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]	08/2015	814.04 - 814.04	825.17	- -	10/2021	1.37
335	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00 - 1,055.00	1,601.77	11/2015 -	-	51.83
336	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 - 247.00	322.09	04/2018 -	-	.00
337	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 - 642.41	681.67	- -	-	6.11
338	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]	12/2015	1,167.45 - 1,167.45	1,182.94	- -	-	1.33
339	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00 - 1,665.00	2,360.65	- -	-	41.78
340	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]	08/2015	854.80 - 854.80	1,038.56	- -	-	21.50
341	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]	08/2015	516.13 - 516.13	649.27	04/2018 -	-	25.80
342	MEERUT-BULANDSHAHAH - [N24000539]	01/2016	683.24 - 683.24	987.94	- -	-	44.60
343	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49 - 1,587.49	2,982.00	04/2019 -	-	87.84
344	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 - 364.56	392.00	- -	08/2021	7.53
345	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]	07/2016	458.03 - 458.03	486.00	- -	-	6.11
346	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]	08/2016	1,388.34 - 1,388.34	1,588.29	09/2019 -	-	14.40

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
347	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601	08/2016	1,169.61 - 1,367.00	2,280.00	- -	-	94.94
348	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607	08/2016	323.72 - 323.72	336.60	08/2018 -	-	3.98
349	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621	09/2016	1,239.82 - 1,239.82	1,727.66	- -	-	39.35
350	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 - 1,100.19	1,145.31	- -	-	4.10
351	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM-509.550(DESIGN CHAINAGE - [N24000631	11/2016	290.73 - 290.73	315.00	- -	-	8.35
352	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638	11/2012	605.84 - 605.84	722.46	07/2018 -	-	19.25
353	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 - 1,184.71	1,310.00	03/2020 -	-	10.58
354	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 - 744.64	982.00	03/2020 -	-	31.88
355	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 - 1,030.44	1,065.51	03/2020 -	-	3.40
356	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 - 988.34	1,043.28	03/2020 -	-	5.56
357	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 - 1,059.73	1,071.00	03/2017 -	-	1.06
358	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 - 1,098.06	1,160.64	03/2020 -	-	5.70
359	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 - 754.54	756.27	03/2020 -	09/2022	.23
360	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 - 672.89	736.01	03/2020 -	-	9.38
361	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 - 1,041.62	1,187.10	03/2020 -	-	13.97
362	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 - 1,288.07	1,420.00	03/2020 -	-	10.24

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
363	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672	03/2017	2,064.99 - 2,064.99	2,447.00	03/2020 -	-	18.50
364	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 - 831.58	1,177.00	03/2020 -	-	41.54
365	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 - 993.16	1,434.00	03/2020 -	-	44.39
366	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 - 894.00	929.32	04/2020 -	12/2021	3.95
367	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693	06/2017	1,958.88 - 1,958.88	1,993.81	06/2020 -	-	1.78
368	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 - 1,124.11	1,232.76	09/2017 -	-	9.67
369	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725	01/2018	273.46 - 273.46	276.17	- -	-	.99
370	6-LANING OF KOZHICODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784	02/2018	1,424.77 - 1,424.77	1,853.42	- -	-	30.09
371	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 - 1,166.26	1,296.93	- -	01/2022	11.20
372	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787	02/2018	1,995.34 - 1,995.34	2,400.00	- -	11/2021	20.28
373	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789	02/2018	2,177.80 - 2,177.80	2,450.00	- -	-	12.50
374	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 - 925.40	1,197.00	- -	-	29.35
375	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 - 1,120.57	1,332.00	- -	-	18.87
376	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 - 1,052.21	1,449.00	- -	01/2021	37.71
377	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807	03/2018	1,532.62 - 1,532.62	2,499.00	03/2021 -	04/2021	63.05
378	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813	03/2018	496.20 - 496.20	537.17	- -	-	8.26

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
379	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 - 1,029.96	1,261.05	- -	03/2021	22.44
380	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 - 1,016.92	1,071.00	- -	01/2022	5.32
381	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830	03/2018	2,065.96 - 2,065.96	2,169.00	- -	-	4.99
382	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 - 1,294.47	1,296.00	- -	-	.12
383	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 - 634.70	931.21	- -	-	46.72
384	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 - 906.65	922.64	- -	-	15.98
385	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 - 642.13	807.00	- -	-	25.68
386	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 - 743.88	743.89	- -	12/2021	.00
387	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 - 656.98	840.00	- -	11/2022	27.86
388	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 - 217.96	884.00	- -	10/2022	305.58
389	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306	10/2020	724.60 - 720.81	724.60	03/2023 -	03/2023	.00
	Total		96,285.50 17,965.00 95,967.17	1,14,030.43			
	<u>STEEL</u>						
	<u>Rastriya Ispat Nigam Limited</u>						
390	FORGED WHEEL PLANT - [N12000116	04/2014	1,682.85 - 1,682.85	2,100.00	09/2018 -	09/2021	24.79
	Total		1,682.85 .00 1,682.85	2,100.00			
	<u>URBAN DEVELOPMENT</u>						
	<u>Ahmedabad Metro Rail</u>						

List of ongoing projects having cost overrun w.r.t. to Latest Approved Cost

Costing Rs. 150 Crore and above					(August 2021)		
					Date of Commissioning		
S.No	Project	Date of Approval	Original / Revised/ Latest Approved Cost(Rs crore)	Anticipated Cost (Rs.crore)	Original/ Revised	Anticipated	Cost Overrun (%)
1	2	3	4	5	6	7	8
391	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]	11/2014	10,773.00 - 10,773.00	12,787.00	12/2018 -	08/2022	18.69
	<u>Kochi Metro Rail Corporation Ltd</u>						
392	KOCHI METRO RAIL PROJECT - [N28000081]	07/2012	5,181.79 - 5,181.79	6,218.14	07/2017 -	-	20.00
	<u>Mumbai Metro Rail Corporation Ltd</u>						
393	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086]	07/2013	23,136.00 - 23,136.00	33,406.00	03/2020 -	03/2023	44.39
	<u>National Building Construcion Corporation Ltd</u>						
394	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]	06/2012	4,264.00 - 4,264.00	4,720.73	11/2019 -	-	10.71
	Total		43,354.79 - 43,354.79	57,131.87			
	<u>WATER RESOURCES</u>						
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>						
395	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]	10/2017	254.13 - 254.13	413.29	09/2020 -	-	62.63
396	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]	12/2014	225.77 - 225.77	398.90	03/2020 -	03/2021	76.68
	<u>Uttar Pradesh Jal Nigam</u>						
397	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021]	01/2019	231.79 - 231.79	234.03	12/2021 -	12/2021	.97
398	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024]	02/2019	681.78 - 681.78	690.71	06/2022 -	06/2022	1.31
	Total		1,393.47 - 1,393.47	1,736.93			
	Grand Total		4,47,610.77 31,864.25 4,61,605.50	6,68,756.85			

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	12320	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	11459	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492	145
4	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	NPCIL	03/2013	11/2020	11/2023	39849	36

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
5	DEVELOPMENT OF TUTICORIN AIRPORT	AAI	06/2019	03/2022	12/2023	380.87	21
6	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	AAI	08/2017	02/2020	05/2022	177.1	27
7	UPGRADATION OF JABALPUR AIRPORT	AAI	06/2016	06/2021	12/2022	412.24	18
8	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	AAI	12/2016	03/2021	03/2023	1142	24
9	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	AAI	01/2016	03/2020	07/2022	458	28
10	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	AAI	01/2019	11/2021	01/2023	389.71	14
11	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	AAI	05/2018	10/2022	12/2023	1216.9	14
12	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	AAI	07/2018	09/2020	09/2022	456.86	24
13	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	AAI	03/2017	04/2021	08/2022	475.39	16
14	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2022	417.23	45
15	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	AAI	06/2018	02/2022	12/2023	2467	22
16	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	AAI	08/2018	10/2021	10/2022	951.28	12
17	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	AAI	11/2016	04/2020	03/2022	303.8	23
18	CCS INTERNATIONAL AIRPORT , LUCKNOW	AAI	06/2018	09/2021	12/2023	1383	27
19	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2022	346.27	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
20	2.0 MTPA BHOJUDIH NLW WASHERY	BCCL	12/2015	03/2017	03/2022	304.13	60
21	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	60
22	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	NCL	11/2017	03/2022	03/2023	1255.17	12
23	JALAGAM VENGALA RAO OCP-II	SCCL	07/2011	03/2015	03/2023	447.06	96
24	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	84
25	KALYANIKHANI OPENCAST PROJECT	SCCL	07/2012	07/2016	03/2022	417.33	68
26	RFR OF MANUGURU OC PROJECT	SCCL	11/2012	03/2016	09/2021	430.45	66
27	RECAST EPR AMRAPALI OC	CCL	02/2012	03/2020	03/2028	4983.58	96
28	AMADAND OPENCAST EXPANSION PROJECT	SECL	03/2016	03/2021	03/2022	869.44	12
29	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	03/2022	198.68	36
30	BHATADI EXPANSION OC MINE	WCL	02/2016	03/2019	03/2022	304.52	36
31	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	NLC	07/2016	11/2021	11/2022	17237	12
32	DURGAPUR OPENCAST PROJECT	SECL	02/2015	03/2023	03/2026	916.24	36
33	RAJRAPPA RCE OCP (3.0 MTY)	CCL	12/2009	03/2016	03/2022	510.85	72
34	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	MCL	12/2007	03/2013	03/2028	8416.19	180
35	MANIKPUR OC EXPANSION (3.5 MTY)	SECL	12/2009	03/2014	03/2023	321.5	108
36	BHUBANESWARI EXPENSION OCP(40.0 MTY)	MCL	12/2007	03/2017	03/2031	3145.45	168
37	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	132
38	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	MCL	12/2007	03/2010	03/2029	3504.21	228
39	MURAIIDIH UG TURN-KEY PROJECT	BCCL	02/2011	04/2014	04/2023	339.88	108
40	MOONIDIH XV SEAM UG	BCCL	08/2011	04/2015	02/2023	1230.27	94
41	RPR FOR JAMUNIA UG (0.90 MTY)	WCL	07/2016	03/2022	03/2026	281.25	48
42	RECAST PR FOR DHANKASA UG (1.00 MTY)	WCL	09/2016	03/2022	03/2025	289.29	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
43	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	WCL	02/2017	03/2021	09/2023	328	30
44	KOLAR PIMPRI EXTENSION OC	WCL	03/2017	03/2020	09/2022	362.73	30
45	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	SCCL	03/2017	03/2019	03/2022	413.84	36
46	PATHERDIH 2.5 NLW COAL WASHERY	BCCL	10/2015	04/2018	06/2022	243	50
47	UKNI DEEP OC	WCL	11/2018	03/2021	09/2022	318.14	18
48	BELLORA-NAIGAON DEEP OC	WCL	11/2018	03/2021	09/2022	252.71	18
49	KANCHAN OC EXPANSION	SECL	12/2014	03/2021	03/2024	371.04	36
50	MADHUBAND NLW WASHERY	BCCL	08/2010	05/2014	10/2021	289.45	89
51	NEW MAJRI UG TO OC	WCL	05/2015	03/2019	03/2022	295.56	36
52	KAKATIYAKHANI OPENCAST-2 PROJECT	SCCL	05/2015	03/2019	03/2022	397.09	36
53	SINGHORI OC MINE	WCL	06/2015	03/2020	09/2021	205.49	18
54	ADASA UG TO OC	WCL	08/2015	03/2023	03/2024	288.9	12
55	BATURA HIGHWALL PROJECT	SECL	07/2015	03/2022	03/2025	231.92	36
56	AMGAON OPENCAST PROJECT RCE	SECL	07/2015	03/2020	03/2023	316.1	36
57	PACHWARA SOUTH COAL BLOCK	NLC	07/2013	08/2022	09/2023	1795.01	13
58	CHURI BENTI UG (0.81 MTY)	CCL	08/2007	03/2011	03/2022	163.51	132
59	KARMA OCP (1.0MTY)	CCL	06/2009	03/2014	03/2022	162.46	96
60	EXPANSION PR OF JHANJRA UG(5.00 MTY)	ECL	11/2015	03/2022	03/2029	1210.12	84
61	KISTARAM OCP	SCCL	11/2010	03/2015	03/2022	242.29	84
62	KARTALI (EAST) OCP (2.50 MTY)	SECL	07/2008	03/2014	03/2026	178.44	144
63	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	NLC	04/2013	06/2015	03/2025	1458.17	117
64	MADANNAGAR OPENCAST PROJECT	SECL	10/2015	03/2024	03/2027	1875.32	36
65	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	WCL	11/2015	03/2021	03/2024	313.34	36

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
66	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	WCL	11/2015	03/2020	03/2026	851.6	72
67	JAYANT EXPANSION OCP 10 TO 20 MTPA	NCL	05/2017	03/2021	03/2022	1783.09	12
68	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	84
69	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2028	6964.33	188
70	RAMAGUNDAM OC-II EXTENSION	SCCL	12/2009	03/2012	03/2023	418.97	132
71	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	BCCL	02/2014	03/2021	03/2022	555.52	12
72	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	ECL	08/2012	03/2018	10/2021	1055.05	43
73	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	MCL	05/2014	03/2019	03/2024	479.15	60
74	GARJANBAHAL OCP	MCL	11/2014	03/2021	09/2025	1375.38	54
75	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	WCL	11/2014	03/2020	03/2027	1184.33	84
76	AMRITDHARA OC PROJECT	SECL	02/2015	03/2023	03/2027	481.6	48
77	AMERA OC RCE	SECL	02/2015	03/2018	03/2023	335.97	60
78	RAJNAGAR OCP RPR (1.70 MTY)	SECL	12/2014	03/2021	04/2024	357.8	37

DEFENCE PRODUCTION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
79	RESIDENTIAL QUATERS FOR HAL, BANGLORE	CPWD	12/2016	02/2020	12/2021	246.31	22

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
80	PERMANENT CAMPUS FOR IIM BODH GAYA	CPWD	09/2018	09/2020	11/2022	375	26
81	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	CPWD	01/2018	05/2020	03/2022	430	22
82	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	CPWD	02/2016	06/2017	03/2022	496.18	57
83	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	CPWD	07/2019	03/2022	09/2022	851	6
84	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE 1A AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT PALAKKA	CPWD	07/2019	03/2021	06/2022	753.63	15

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

DONER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
85	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE, SHILONG IN MEGALAYA UNDER NLCPR	HSCL	04/2014	09/2017	08/2021	151.33	47

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
86	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	05/2022	4773	29

FERTILISERS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
87	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	RCF	04/2018	04/2020	10/2021	426.72	18
88	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	NFL	01/2018	11/2019	10/2021	215.92	23

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
89	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	CPWD	03/2018	09/2020	04/2022	195	19
90	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	HSCC	08/2017	03/2019	09/2021	355.15	30
91	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	09/2021	414.11	94
92	NEIGRIHMS SHILLONG MEGHALYA	HSCC	10/2016	05/2018	03/2022	363.99	46
93	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	CPWD	09/2017	03/2020	12/2021	150.29	21
94	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	HITES	07/2016	04/2020	10/2021	785	18
95	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	HITES	07/2016	06/2020	10/2021	703	16
96	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	HITES	05/2017	05/2021	09/2022	875	16
97	AIIMS BILASPUR	NBCC	04/2018	09/2021	06/2022	1351	9
98	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	CPWD	12/2018	06/2021	05/2022	260	11

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
99	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES (CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2022	1219.21	29
100	NSG AT KOLKATA	CPWD	10/2014	04/2018	12/2021	162.88	44

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

MINES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
101	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	NALCO	12/2014	04/2021	12/2022	5540	20
102	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	NALCO	11/2017	04/2021	03/2023	483	23

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
103	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	GAIL	08/2018	04/2021	03/2022	217.92	11
104	SWRO II WITH LLPH FACILITIES	HPCL	09/2019	07/2020	09/2021	196.26	14
105	R and D CAMPUS II AT FARIDABAD	IOCL	06/2019	12/2022	07/2023	2281.94	7
106	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	IOCL	06/2019	09/2022	03/2023	371	6
107	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	BPCL	07/2017	02/2021	03/2023	580.2	25
108	Fuel Quality Upgradation Project at Paradip Refinery	IOCL	05/2019	08/2021	09/2022	3361	13
109	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	IOCL	01/2019	01/2021	03/2022	909	14
110	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	IOCL	10/2018	02/2020	02/2022	598	24
111	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	GAIL	08/2018	08/2020	12/2021	286.42	16
112	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	OIL	06/2016	08/2020	09/2021	224.75	13
113	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	ONGC	02/2019	05/2021	12/2021	2292.46	7
114	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.8	14
115	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	ONGC	05/2019	05/2021	01/2022	3660.71	8
116	ADDITIONAL STORAGE TANKS AT PARADIP	IOCL	11/2018	09/2021	06/2022	462.3	9
117	INFRASTRUCTURE DEVELOPMENT TO FACILITATE IMPORT OF GRID POWER AT 220 KV, PANIPAT	IOCL	12/2018	06/2021	07/2022	278.6	13
118	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	IOCL	08/2017	08/2020	03/2022	255.4	19
119	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	IOCL	12/2017	10/2020	08/2022	199.36	22
120	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	IOCL	10/2017	02/2020	10/2021	906	20
121	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	OIL	01/2018	02/2020	12/2021	543.91	22
122	INSTALLATION OF 'INDJET' UNIT AT	IOCL	07/2018	01/2021	11/2021	189	10

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	BARAUNI REFINERY						
123	BS VI PROJECT AT GUWAHATI REFINERY	IOCL	08/2018	02/2020	09/2021	557	19
124	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	IOCL	08/2018	08/2020	04/2022	1636	20
125	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	IOCL	08/2018	04/2021	12/2021	466	8
126	REVAMPING OF FACILITIES AT VIZAG TERMINAL	IOCL	04/2018	04/2022	02/2023	355	10
127	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678	66
128	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	20928	24
129	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	ONGC	11/2015	03/2019	09/2021	650.82	30
130	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	ONGC	03/2016	06/2020	06/2022	34012	24
131	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497	38
132	BSVI UPGRADATION	MANGALORE REFI	09/2016	12/2019	02/2022	1810	26
133	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	OIL	05/2016	10/2020	03/2022	406	17
134	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	OIL	09/2016	12/2019	08/2021	571.66	20
135	DHAMRA-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1933	12
136	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	49
137	SITARGANJ LPG PROJECT	IOCL	02/2017	02/2020	10/2021	160.1	20
138	LPG BP PROJECT KHORDHA	IOCL	12/2016	12/2019	03/2022	161.59	27
139	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915	110
140	SEA WATER DESALINATION PLANT	MANGALORE REFI	11/2017	03/2020	11/2021	581	20
141	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	53
142	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	12/2021	1823	9
143	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321	15
144	PARADIP LPG IMPORT FACILITY	IOCL	01/2015	07/2018	10/2021	690	39

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
145	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	02/2022	861.79	105
146	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	09/2021	4588.29	37
147	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	GAIL	04/2016	04/2018	12/2021	327.78	44
148	DOBHI-DURGAPUR PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	2433	12
149	BOKARO-ANGUL PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	3437	12
150	DURGAPUR-HALDIA PIPELINE PROJECT	GAIL	03/2017	12/2020	12/2021	1740	12
151	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	10/2021	261	9
152	PIPELINE NETWORK PROJECT GELEKI, ASSAM	ONGC	07/2016	05/2020	11/2021	249.85	18
153	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677	13
154	KHARAGPUR LPG BOTTLING PLANT	IOCL	04/2017	04/2020	10/2021	163.02	18
155	RE-LIQUIFIED NATURAL GAS	CPCL	08/2017	08/2020	10/2021	421	14
156	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	09/2021	212	8
157	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	IOCL	05/2016	01/2021	08/2022	348	19
158	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	GAIL	07/2015	12/2020	10/2021	2881.4	10
159	REVAMPING OF EXISTING FACILITIES/AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	IOCL	08/2017	08/2021	11/2022	318.8	15
160	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	IOCL	08/2017	06/2020	09/2021	236	15
161	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	IOCL	12/2017	10/2020	01/2022	466.43	15
162	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112	32
163	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	HPCL	06/2017	06/2020	09/2021	249.26	15
164	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	HPCL	06/2017	06/2020	09/2021	161.5	15
165	LPG BP PROJECT MOTIHARI	IOCL	05/2018	03/2021	09/2021	206.5	6
166	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	29
167	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	IOCL	04/2018	03/2021	12/2021	522	9

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
168	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	BPCL	10/2018	03/2021	10/2021	206.26	7
169	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	GAIL	09/2018	02/2021	08/2022	225.54	18
170	GRASS ROOT TERMINAL AT MALKAPUR	IOCL	12/2018	04/2022	08/2023	611	16
171	PIPELINE REPLACEMENT PROJECT (PRP-VI)	ONGC	05/2019	12/2020	12/2021	763.92	12
172	COMPRESSED BIO GAS PLANT AT GORAKHPUR	IOCL	09/2019	07/2021	03/2022	164.69	8

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
173	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	12/2021	529.68	37
174	PATRATU STPP-I (3X800MW)	NTPC	11/2017	03/2023	02/2025	18668	23
175	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10/2022	10598.98	23
176	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P	PGCIL	05/2016	11/2019	09/2021	14733.37	22
177	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	PGCIL	02/2017	02/2019	02/2022	322.3	36
178	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	PGCIL	02/2017	06/2019	11/2021	235.53	29
179	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	PGCIL	03/2017	12/2019	12/2021	379.95	24
180	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	63
181	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	03/2022	5111.33	39
182	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	6
183	EASTERN REGION STRENGTHENING SCHEME XX	PGCIL	11/2017	05/2020	10/2021	358.83	17
184	AMELIA COAL MINE	THDCIL	01/2017	09/2020	08/2022	2104.21	23
185	JETSAR SOLAR 160 MW	NTPC	12/2019	03/2021	11/2021	702.28	8
186	KAYAMKULAM SOLAR 70 MW	NTPC	09/2019	06/2021	12/2021	403.62	6
187	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	02/2022	12964.6	45
188	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	162

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
189	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	155
190	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	11130.19	108
191	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	PGCIL	01/2014	04/2016	12/2021	374.63	68
192	EASTERN REGION STRENGTHENING SCHEME-XII	PGCIL	05/2014	11/2016	12/2021	522.29	61
193	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	CVPPPL	10/2014	04/2020	07/2025	8112.12	63
194	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	10/2021	3500	15
195	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	PGCIL	05/2017	07/2019	10/2021	186.17	27
196	HVDC BIPOLE LINK BETWEEN WR AND SR - NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	PGCIL	08/2017	02/2020	09/2021	1931.39	19
197	NOKHRA	NTPC	03/2020	09/2021	01/2023	1722.14	16
198	RAMAGUNDAM FLOATING SOLAR 100 MW	NTPC	06/2019	04/2021	10/2021	401.9	6
199	SAMBHU KI BHURJ-II SOLAR 300MW	NTPC	03/2020	09/2021	09/2022	1782	12
200	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	12/2023	14366.58	54
201	RAMMAM-III HEPP (3X40 MW)	NTPC	09/2014	09/2019	12/2024	1381.84	63
202	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	PGCIL	03/2015	03/2018	12/2021	197.4	45
203	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	PGCIL	03/2015	05/2017	12/2021	1394.52	55
204	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	10/2021	5353	111
205	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	06/2024	2491.58	132
206	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657	88
207	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	141
208	KHURJA SUPER THERMAL POWER PROJECT	THDCIL	03/2019	09/2023	08/2024	11089.42	11
209	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	11/2021	1885.13	35

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
210	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	NR	06/2009	08/2016	08/2025	404	108
211	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	09/2021	691.84	18
212	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288	18
213	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	SWR	03/1996	03/2017	03/2025	644.78	96
214	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973	33
215	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	36
216	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	39
217	MAU-GHAZIPUR-TARIGHAT NEW LINE	RVNL	04/2015	03/2023	12/2024	1765.92	21
218	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	21
219	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	24
220	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	21
221	RAIPUR - TITLAGARH - DOUBLING	RVNL	03/2007	03/2020	12/2021	1402.02	21
222	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	39
223	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	24
224	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	12
225	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798	57
226	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	24
227	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	69
228	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.7	105
229	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	228
230	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	36
231	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	ER	04/2001	03/2016	03/2025	923.52	108
232	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	96

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
233	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	CR	02/2015	03/2023	03/2024	2449.91	12
234	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.2	180
235	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	72
236	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	133
237	RAMGANJMUNDI-BHOPAL (NL), WCR	WCR	04/2001	03/2021	03/2024	424.6	36
238	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.7	88
239	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	45
240	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	73
241	BARDHAMAN-KATWA (GC)	ER	04/2007	12/2010	03/2025	1106.62	171
242	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2024	2393.47	120
243	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	09/2021	477.88	114
244	MANOHARABAD-KOTHPALLI NEW LINE(SCR)	SCR	04/2006	03/2010	03/2024	1160.48	168
245	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	108
246	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	24
247	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	ER	04/2010	03/2016	03/2025	277.28	108
248	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	ER	04/2010	03/2017	03/2025	365.17	96
249	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	24
250	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	ER	04/2011	03/2017	03/2026	299.6	108
251	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	ER	04/2010	03/2005	03/2025	494.54	240
252	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	157
253	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL	ER	04/2009	03/2014	03/2025	257.42	132
254	WARDHA-SEWAGRAM NGP 3RD LINE	CR	04/2012	03/2022	03/2024	540.02	24
255	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.3	129

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
256	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	SCR	04/2012	03/2023	03/2024	1856.95	12
257	SHIMOGA-HARIHAR NL	SWR	04/2011	03/2016	03/2024	832.47	96
258	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.7	36
259	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	11/2021	704.31	20
260	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	156
261	GADAG-WADI NL	SWR	04/2013	12/2018	06/2025	2841.84	78
262	MARIKUPPAM - KUPPAM	SWR	04/2012	03/2016	12/2023	279.54	93
263	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.5	24
264	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	03/2022	495.44	216
265	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	202
266	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	128
267	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR	NFR	04/2000	12/2008	09/2021	1180.19	153
268	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	204
269	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	153
270	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	M RTP	04/2006	06/2013	07/2022	495.74	109
271	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.2	48
272	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	60
273	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	132
274	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	96
275	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	40
276	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450	140
277	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500	241
278	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW	RVNL	04/2010	03/2016	03/2025	3951.98	108

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	GARIA VIA RAJARHAT (MTP)						
279	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	141
280	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723	276
281	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	264
282	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	03/2025	303.98	60
283	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	WR	04/2008	03/2012	10/2023	318.24	139
284	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	48
285	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	24
286	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	34
287	BHADRAK - NERGUNDI 3RD LINE	ECOR	03/2013	10/2020	03/2024	843.04	41
288	KIRANDUL - JAGDALPUR DOUBLING	ECOR	12/2012	03/2020	03/2023	1160	36
289	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	ECOR	03/2012	03/2020	03/2022	155.81	24
290	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	36
291	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600	31
292	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	09/2021	860.43	18
293	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	11/2021	578	20
294	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	60
295	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	12/2021	678.54	33
296	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295	37
297	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	12
298	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	12
299	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	48
300	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	21

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
301	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	33
302	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTURGARH-UDAIPUR	NWR	04/2013	03/2020	09/2021	420.18	18
303	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651	120
304	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	08/2021	258.2	32
305	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548	36
306	MANMAD - JALGAON - 3RD LINE (160 KM)	CR	02/2016	03/2022	03/2024	1035.16	24
307	WARDHA - NAGPUR - 4TH LINE (76 KM)	CR	02/2016	03/2023	03/2024	637.95	12
308	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631	24
309	JAGADALPUR-KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2023	1547.38	12
310	KOTTAVALSA - KORAPUT DOUBLING	ECOR	04/2015	03/2022	03/2024	2499.71	24
311	KORAPUT - SINGAPUR ROAD DOUBLING	ECOR	04/2015	03/2022	03/2026	2361.74	48
312	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	64
313	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE.	ECOR	04/2015	12/2018	03/2024	1172.92	63
314	KIUL - GAYA DOUBLING PROJECT	ECR	12/2015	03/2020	03/2023	1200.2	36
315	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	ECR	12/2015	03/2020	03/2023	1491.47	36
316	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	48
317	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	CR	02/2015	03/2022	03/2023	1272.19	12
318	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	12
319	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	12
320	SURENDRA NAGAR RAJKOT	WR	04/2015	03/2021	12/2022	1002.39	21
321	KAZIPET-BALHRSHA	SCR	04/2015	03/2021	03/2024	2063.03	36
322	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	02/2022	969.83	23
323	BONDAMUNDA RANCHI DOUBLING	SER	03/2016	03/2021	12/2023	1724.2	33

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
324	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	RVNL	04/2015	03/2022	12/2024	943.6	33
325	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.4	324
326	KATNI-BINA 3RD LINE (263 KM)	WCR	06/2016	03/2022	03/2023	2478.23	12
327	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	12
328	RAMNA - SINGRAULI DOUBLING	ECR	08/2015	03/2020	03/2024	2436.21	48
329	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	IRCON	04/2016	03/2020	03/2024	5200	48
330	KARAILA ROAD - SHAKTINAGAR DOUBLING	ECR	08/2015	03/2019	03/2022	528.57	36
331	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	9
332	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	9
333	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	198
334	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	SR	02/2017	03/2024	03/2026	1567	24
335	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760	27
336	INDARA - DOHRIGHAT GAUGE CONVERSION.	NER	04/2016	04/2016	12/2021	213	68
337	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	NER	04/2016	01/2022	03/2025	1900	38
338	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150	66
339	ETAH - KASGANJ - NEW LINE	NER	04/2017	04/2017	04/2022	276.9	60
340	GARHWA ROAD-RAMNA	ECR	03/2015	03/2021	03/2022	348.23	12
341	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	36
342	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	34
343	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229	36
344	ANUPPUR-KATNI	SECR	04/2015	12/2021	12/2023	1370	24
345	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	31
346	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	IRCON	04/2013	09/2018	06/2022	3055	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
347	INDORE-DEWAS-UJJAIN (80 KMS)	WR	04/2016	06/2020	03/2023	700	33
348	JHANSI BINA DOUBLING	NCR	09/2016	03/2021	12/2022	2001	21
349	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	NCR	03/2018	03/2023	06/2025	4329.53	27

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
350	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	MORTH	03/2020	12/2020	12/2022	166.94	24
351	REHABILITATION AND UPGRADEATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	MORTH	03/2016	06/2019	12/2021	877.79	30
352	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	NHIDCL	03/2019	05/2019	03/2022	306.28	34
353	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	MORTH	10/2017	10/2019	08/2021	1069.59	22
354	REHABILITATION AND UPGRADEATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	MORTH	11/2016	05/2017	08/2021	290.15	51
355	REHABILITATION AND UPGRADEATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	MORTH	01/2017	08/2017	12/2021	319.28	52
356	REHABILITATION AND UPGRADEATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	MORTH	03/2018	08/2018	12/2021	228.32	40
357	REHABILITATION AND UPGRADEATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	MORTH	03/2018	08/2018	11/2021	289.67	39
358	REHABILITATION AND UPGRADEATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 0	MORTH	03/2016	05/2016	09/2021	995.09	64
359	REHABILITATION AND UPGRADEATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	MORTH	01/2018	08/2018	08/2021	418.03	36
360	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MORTH	11/2010	03/2011	12/2021	624.41	129
361	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	12/2021	193.69	134
362	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	12/2021	195.04	134
363	FOUR LANNING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	NHAI	03/2016	07/2016	12/2021	641.17	65
364	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	NHAI	08/2017	08/2017	02/2022	950.64	54
365	FOUR LANNING OF CHOLOPURAM-THANJAVUR	NHAI	08/2017	08/2017	07/2022	1176.37	59
366	4-LANNING OF STHIYATHOPU-CHOLOPURAM	NHAI	09/2017	09/2017	07/2022	1227.87	58
367	FOUR LANNING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	NHIDCL	05/2015	05/2018	03/2022	454.89	46

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
368	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	NHIDCL	06/2015	06/2018	12/2021	437.39	42
369	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250(DESIGN KM 490.800 TO KM 5	NHIDCL	06/2015	06/2018	12/2021	463.49	42
370	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	NHIDCL	03/2015	11/2018	11/2021	168.39	36
371	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	NHIDCL	10/2014	11/2018	02/2022	588.95	39
372	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MoRTH	11/2010	05/2017	05/2022	268.08	60
373	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	NHIDCL	12/2015	12/2018	12/2021	289.99	36
374	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	MoRTH	11/2015	01/2020	09/2021	628.45	20
375	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	MoRTH	12/2015	02/2020	09/2021	957.54	19
376	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	MoRTH	03/2015	08/2017	12/2022	511.83	64
377	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) 0	NHIDCL	01/2016	01/2016	03/2022	294.17	74
378	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	NHIDCL	01/2016	01/2016	03/2022	252	74
379	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	MoRTH	03/2020	03/2021	04/2022	207.79	13
380	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	MoRTH	06/2020	05/2021	12/2022	221.4	19
381	REHABILITATION AND UPGRADEATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	MoRTH	08/2020	03/2021	03/2023	222.61	24
382	TWO LANING OF TRICHY - KARAIKUDI AND TRYCHI BYPASS	NHAI	05/2010	05/2013	08/2021	374	99
383	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	NHAI	04/2012	04/2014	01/2022	624	93
384	PUNE-SATARA(NH-4)	NHAI	10/2010	03/2013	09/2021	1724.55	102
385	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848	105
386	4-LANING OF FARAKA-RAIGANJ	NHAI	02/2011	08/2013	08/2021	1078.84	96
387	4-LANING OF BRAHAMPORE-FARAKA	NHAI	02/2011	08/2013	06/2023	998.79	118
388	DELHI AGRA APPROVED LENGTH 180.0 KM	NHAI	10/2012	04/2015	12/2021	1928.22	80
389	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	NHAI	08/2014	04/2018	09/2021	822.9	41
390	8 LANING OF MUKARBA CHOWK TO PANIPAT	NHAI	07/2015	04/2019	09/2021	2128.72	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
391	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	NHAI	06/2011	06/2013	09/2021	600	99
392	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	46
393	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	03/2022	593.26	46
394	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN	NHAI	12/2015	03/2019	06/2022	649.5	39
395	FOUR LANING OF YADGIRI - WARANGAL	NHAI	12/2015	11/2018	08/2021	1423.96	33
396	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	NHAI	03/2016	03/2019	03/2022	701.4	36
397	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	NHAI	02/2016	08/2018	01/2022	707.82	41
398	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	NHAI	02/2016	07/2018	12/2021	641.17	41
399	NAGPUR RING ROAD PACKAGE-1	NHAI	03/2016	07/2019	12/2021	546	29
400	NAGPUR RING ROAD PACKAGE-2	NHAI	03/2016	07/2019	12/2021	591.66	29
401	HOSPET-BELLARY-KARNATAKA AP BORDER	NHAI	08/2016	03/2019	09/2022	1167.42	42
402	FOUR LANNING OF VIKRAVANDI- SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	NHAI	03/2017	03/2020	12/2021	848.45	21
403	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	NHAI	03/2017	03/2020	12/2021	1373.28	21
404	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	NHAI	03/2017	03/2020	09/2022	754.54	30
405	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	NHIDCL	03/2017	04/2017	03/2022	284.09	59
406	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	NHIDCL	02/2017	04/2017	03/2022	195.23	59
407	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	NHIDCL	02/2017	04/2017	03/2022	203.36	59
408	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	NHIDCL	01/2017	04/2017	03/2022	198.22	59
409	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	NHAI	04/2017	04/2020	12/2021	894	20
410	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P	NHAI	06/2017	06/2020	09/2021	2485.93	15
411	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	NHIDCL	03/2018	05/2018	03/2022	274.31	46
412	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	NHIDCL	03/2018	06/2018	03/2022	403.36	45

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
413	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	NHIDCL	03/2018	05/2018	03/2022	417.24	46
414	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	NHIDCL	03/2015	10/2018	01/2022	262.97	39
415	2 LANE WITH HARD SHOULDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	NHIDCL	03/2017	12/2017	03/2022	409.85	51
416	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	NHIDCL	03/2015	04/2017	10/2021	277.17	54
417	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	NHIDCL	02/2018	10/2018	03/2022	391	41
418	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	NHIDCL	03/2018	10/2018	03/2022	234.27	41
419	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	NHIDCL	02/2017	09/2018	03/2022	387	42
420	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	NHIDCL	03/2018	09/2018	11/2022	500.09	50
421	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	07/2022	339.57	46
422	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	NHIDCL	03/2018	09/2018	05/2022	239.3	44
423	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	NHIDCL	03/2018	09/2018	09/2022	285.68	48
424	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	NHIDCL	03/2018	09/2018	12/2021	315.03	39
425	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO	NHIDCL	03/2018	09/2018	12/2021	240.64	39
426	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	NHIDCL	03/2018	09/2018	11/2021	237.72	38
427	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	NHIDCL	03/2018	09/2018	11/2021	251.97	38
428	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	NHIDCL	03/2018	09/2018	11/2021	282.98	38
429	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	NHIDCL	03/2018	09/2018	11/2021	215.12	38
430	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	NHIDCL	03/2018	09/2018	12/2021	215.79	39
431	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	NHIDCL	03/2018	09/2018	10/2022	272.89	49
432	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	NHIDCL	03/2018	09/2018	11/2022	323.98	50
433	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	NHIDCL	11/2017	11/2017	12/2021	290.05	49
434	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	MoRTH	12/2017	12/2019	08/2021	248.22	20
435	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2	MoRTH	06/2017	06/2019	12/2021	282.08	30

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S						
436	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	MORTH	02/2018	02/2020	09/2021	418.88	19
437	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	MORTH	05/2018	05/2020	12/2021	248	19
438	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	MORTH	03/2018	08/2018	09/2021	166.21	37
439	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	MORTH	03/2016	11/2018	03/2022	271.17	40
440	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	MORTH	02/2018	03/2018	04/2022	169.63	49
441	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	MORTH	01/2017	09/2019	10/2021	396.86	25
442	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	MORTH	02/2018	09/2020	01/2022	426.18	16
443	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	MORTH	11/2017	02/2018	09/2021	184.62	43
444	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	MORTH	03/2016	08/2019	11/2022	160.27	39
445	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	MORTH	06/2016	08/2019	08/2022	236.78	36
446	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	MORTH	01/2017	03/2017	12/2021	205.05	57
447	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	MORTH	11/2017	11/2019	10/2021	237.8	23
448	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	NHIDCL	03/2015	01/2016	03/2022	829	74
449	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	NHIDCL	03/2018	07/2018	07/2022	1383.78	48
450	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	519.09	43
451	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	07/2023	640.07	46
452	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	642.96	45
453	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	473.18	43
454	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2023	537.82	43
455	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	06/2023	518.53	45
456	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	NHIDCL	04/2017	09/2019	04/2024	404.29	55
457	WIDENING AND UP-GRADATION TO 2-LANE	NHIDCL	04/2017	09/2019	09/2023	428.11	48

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO						
458	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	NHIDCL	08/2017	10/2018	10/2021	517.57	36
459	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	MoRTH	03/2018	03/2018	10/2021	162.56	43
460	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	MoRTH	03/2018	03/2018	06/2022	214.69	51
461	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	MoRTH	03/2018	08/2018	09/2021	217.22	37
462	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	MoRTH	03/2018	03/2018	10/2021	233.04	43
463	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	MoRTH	11/2017	07/2018	12/2021	249.05	41
464	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	MoRTH	11/2017	02/2018	03/2022	254.17	49
465	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	MoRTH	02/2018	03/2018	11/2021	279.44	44
466	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	MoRTH	01/2017	09/2019	09/2021	373.82	24
467	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	MoRTH	01/2016	07/2018	11/2021	809.16	40
468	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH-214(NH216) (KAKINAD	MoRTH	08/2016	01/2017	12/2021	350.61	59
469	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	MoRTH	03/2016	09/2016	08/2021	444.84	59
470	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	MoRTH	11/2016	08/2017	12/2021	376.25	52
471	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	MoRTH	01/2017	09/2017	05/2022	263.45	56
472	REHABILITATION AND UPGRADATION OF REPALLE TO EEPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH	MoRTH	01/2017	01/2018	04/2022	576.48	51
473	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	MoRTH	03/2016	12/2019	12/2021	536.65	24
474	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	MoRTH	11/2017	03/2018	10/2021	392.33	43
475	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	MoRTH	03/2016	07/2016	12/2022	452.94	77
476	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	MoRTH	03/2017	01/2018	10/2021	423.79	45
477	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	MoRTH	12/2014	03/2015	03/2022	496.02	84
478	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	MoRTH	11/2017	05/2019	09/2021	188.8	28
479	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	MoRTH	12/2014	11/2017	09/2021	379.16	46

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
480	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION OF BEAWAR-ASIND SECTION (K)	MORTH	08/2020	11/2020	11/2022	196.23	24
481	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS-CONTROLLED EXPRESSWAY FROM BAWDI VILLAGE	NHAI	03/2019	05/2020	05/2022	1047	24
482	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	NHAI	02/2019	03/2020	04/2022	847	25
483	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	NHAI	02/2019	12/2019	12/2021	990.97	24
484	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	MORTH	10/2016	12/2020	09/2021	167.62	9
485	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	MORTH	10/2016	12/2020	09/2021	172.63	9
486	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	MORTH	10/2016	08/2020	10/2021	171.9	14
487	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	MORTH	03/2017	11/2020	08/2021	217.35	9
488	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	12/2021	186.96	87
489	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	MORTH	01/2019	03/2021	11/2021	264.5	8
490	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	MORTH	03/2018	04/2020	12/2021	263.89	20
491	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	MORTH	03/2018	08/2020	12/2021	288.3	16
492	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	MORTH	03/2016	09/2020	08/2021	296.5	11
493	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	MORTH	01/2016	08/2016	06/2022	497.14	70
494	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	MORTH	11/2015	06/2017	10/2021	335.32	52
495	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	MORTH	01/2016	09/2016	12/2021	476.2	63
496	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MORTH	01/2016	10/2016	12/2021	624.98	62
497	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO	MORTH	03/2020	08/2020	08/2022	255.23	24

RURAL DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
498	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE V	HSCL	03/2007	12/2015	02/2022	149.73	74
499	CONSTRUCTION AND MAINTENANCE OF RURAL ROAD UNDER PMGSY PHASE VI	HSCL	12/2007	12/2016	03/2022	202.61	63
500	CONSTRUCTION AND MAINTENANCE OF	HSCL	10/2011	12/2016	09/2022	175.49	69

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
	RURAL ROAD UNDER PMGSY PHASE VIII						

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
501	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	SAIL	12/2018	09/2020	08/2021	263.36	11
502	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	01/2022	15525	80
503	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	SAIL	11/2016	06/2019	10/2021	262.87	28
504	COKE OVEN BATTERY-5	RINL	12/2011	12/2017	07/2022	2858	55
505	FORGED WHEEL PLANT	RINL	04/2014	09/2018	09/2021	1682.85	36
506	NEW SINTER PLANT AT BOKARO STEEL PLANT	SAIL	03/2015	10/2017	11/2022	1034.01	61

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
507	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	CPWD	10/2014	03/2018	12/2021	248.2	45
508	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	13334	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
509	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	CPWD	05/2019	09/2020	01/2023	299.97	28
510	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	CPWD	10/2016	03/2022	06/2023	1128	15
511	KANPUR METRO RAIL PROJECT	LMRCL	05/2019	03/2024	03/2025	11076.48	12
512	AGRA METRO RAIL PROJECT	LMRCL	05/2019	03/2024	05/2025	8379.62	14
513	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	CPWD	06/2015	04/2019	02/2022	197.33	34
514	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	23136	36
515	DELHI MRTS PHASE-III	DMRC	09/2011	03/2016	08/2021	38585	65
516	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	CPWD	11/2017	05/2020	10/2021	238.56	17
517	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	CPWD	10/2016	03/2021	06/2023	422	27

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
518	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	CPWD	10/2016	08/2020	06/2022	392	22
519	PUNE METRO RAIL PROJECT (PHASE 1)	MMRC	12/2016	11/2021	12/2022	11420	13
520	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	10773	44
521	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	CPWD	10/2016	07/2021	06/2023	1180	23
522	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	03/2025	26405.14	73
523	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	DMRC	05/2017	12/2020	08/2021	565	8
524	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	CPWD	02/2020	11/2020	09/2021	532	10

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	TOR (Months)
525	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	KMDA	05/2018	02/2022	10/2022	160	8
526	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	10151.04	25
527	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	BPB	03/2017	12/2019	12/2021	233.57	24
528	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	UPJalNigam	03/2019	07/2021	06/2022	298.12	11
529	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	DJB	05/2016	02/2022	12/2022	239.11	10
530	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	DJB	05/2016	12/2021	12/2022	211.79	12

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
1	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	3492	6840	3348
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	11459	16580	5121
3	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	12320	17079	4759

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	417.23	707.73	290.5
5	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	346.27	480.33	134.06

COAL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
6	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	152.43	459.49	307.06
7	BHANEGAON OC	WCL	02/2015	03/2023	187.94	409.68	221.74
8	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	162.76	349.28	186.52
9	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	2661.73	5146.48	2484.75
10	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	198.68	325.18	126.5
11	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	NLC	06/2011	12/2015	5907.11	7980.79	2073.68
12	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	479.53	703.39	223.86
13	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	6964.33	7254.37	290.04

DEPARTMENT OF HIGHER EDUCATION

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
14	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	RITES	09/2013	09/2014	484.32	626.26	141.94

DPIIT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
15	DELHI MUMBAI INDUSTRIAL CORRIDOR	DMIC	09/2011	09/2019	12579.09	13812.3	1233.21
16	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	4773	5178	405

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN RS. 100 CRORE

(AUGUST 2021)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
17	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	414.11	655.58	241.47
18	AIIMS BILASPUR	NBCC	04/2018	09/2021	1351	1471	120
19	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	CPWD	03/2019	09/2025	1577	1828	251

HEAVY INDUSTRY

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
20	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIIP)	NATIS	04/2011	09/2011	1718	3727.3	2009.3

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
21	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	1219.21	2000	780.79
22	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	CPWD	12/2008	12/2013	114.26	266	151.74

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
23	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	607.06	1236	628.94
24	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	2321	3338	1017
25	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	861.79	2001.34	1139.55
26	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	1823	3027.9	1204.9
27	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	3190.69	3375.9	185.21
28	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	678	1472	794
29	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	ONGC	12/2015	03/2023	823.27	1137.79	314.52
30	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	3228.8	3976.67	747.87
31	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	IOCL	03/2018	N.A.	588.2	730.2	142
32	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	206.63	340.76	134.13
33	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	1112	1507.24	395.24
34	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	2677	3072	395

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
35	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	2915	5909	2994
36	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	4497	6025	1528
37	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	20928	26264	5336
38	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	BPCL	11/2014	08/2018	4588.29	5245.96	657.67

POWER

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
39	LOKTAK D/S HEP(NHPC)	NHPC	12/1999	06/2006	578.62	1311.05	732.43
40	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	PGCIL	10/2008	10/2012	4824.12	5071.94	247.82
41	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	3919.59	9897.59	5978
42	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	6285.33	19992.43	13707.1
43	TAPOVAN-VISHNUGAD HEP (4X130MW)	NTPC	11/2006	03/2013	2978.48	5867.38	2888.9
44	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	529.68	633.8	104.12
45	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	1885.13	2311.89	426.76
46	NAITWAR MORI HEP	SJVN	10/2017	12/2021	648.33	947.89	299.56
47	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	PGCIL	05/2017	02/2019	445.89	675.73	229.84
48	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	3500	3994	494
49	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10598.98	10997.7	398.72
50	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	NTPC	07/2012	08/2017	1527	1801.07	274.07
51	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	8692.97	21312.11	12619.14
52	SYTEM STRENGTHENING XIII OF SR GRID	PGCIL	10/2011	06/2014	487.49	639.46	151.97
53	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	1657	4825.6	3168.6
54	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	2491.58	3860.35	1368.77
55	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	12964.6	17304	4339.4
56	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	5353	10566	5213

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
57	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	14366.58	15389.42	1022.84
58	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	5111.33	6700	1588.67
59	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	4754.42	9129.32	4374.9
60	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	PGCIL	10/2016	01/2019	408.46	516.12	107.66
61	PAKRI BARWADIH COAL MINING PROJECT	NTPC	10/2004	10/2017	4237.96	4552	314.04
62	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	11130.19	14719.1	3588.91
63	EASTERN REGION STRENGTHENING SCHEME-V	PGCIL	10/2013	04/2016	1364.52	1891.41	526.89
RAILWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
64	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR	NFR	04/1983	03/2019	297.32	614	316.68
65	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	ECR	03/1999	N.A.	1033.07	3620	2586.93
66	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	1045.2	2120.16	1074.96
67	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	M RTP	03/2000	12/2006	1049.69	3404.92	2355.23
68	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	1188.91	1619.48	430.57
69	ETAWAH-MAINPURI (NL), NCR	NCR	04/1997	12/2008	120	346	226
70	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	ECR	04/2003	N.A.	528.65	2066.78	1538.13
71	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	2393.47	5521.45	3127.98
72	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	RE	02/2008	03/2012	171.1	275.08	103.98
73	TIDIVANAM-NAGARI (NL)	SR	09/2006	N.A.	582.83	3150	2567.17
74	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDII' -AGASTIYAMPALLI	SR	09/2007	02/2019	724.69	2950	2225.31
75	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	810.78	1928.07	1117.29
76	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	RVNL	04/2000	03/2009	133.41	396	262.59
77	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	1202.7	2440.53	1237.83

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
78	CHHINDWARA - NAGPUR (GC)(SECR)	SECR	04/2005	N.A.	383.79	1511.5	1127.71
79	ROHTAK-MEHAM HANSI	NR	04/2012	12/2011	287	893.45	606.45
80	GRADE SEPERATOR AT DAYABASTI	NR	04/1999	N.A.	156.65	359	202.35
81	MANUGURU-RAMAGUNDAM	SCR	04/2013	N.A.	1112	2911.84	1799.84
82	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	986.3	1530.09	543.79
83	TUMKUR-CHITRADURGA-DAVENGERE NL	SWR	04/2011	N.A.	1801.01	2161.36	360.35
84	3RD LINE BETWEEN BHUSAWAL-JALGAON	CR	04/2011	03/2019	184.06	325	140.94
85	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	499.96	680.68	180.72
86	BOINCHI-SHAKTIGARH 3RD LINE	ER	04/2011	N.A.	175.8	495.1	319.3
87	HANSDIHA-GODDA NL	ER	04/2011	03/2020	542.18	663.13	120.95
88	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	ECR	04/1997	N.A.	162.87	614.45	451.58
89	JAYANAGAR-DARBHANGA-NARKATIA GANJ (GC), ECR	ECR	04/1997	03/2012	324.73	1070	745.27
90	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	247.66	8248.5	8000.84
91	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	M RTP	03/1996	03/2004	495.44	2980.41	2484.97
92	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	2271.5	4794.6	2523.1
93	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	RVNL	04/2010	03/2023	2127	3000	873
94	QADIAN-BEAS	NR	04/2011	N.A.	205.22	841.9	636.68
95	HARIDWAR-LAKSAR	NR	04/2012	N.A.	219.83	346.63	126.8
96	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	2132.77	3037.95	905.18
97	HOWRAH-AMTA-CHAMPADANGA NL (SER)	SER	04/1974	03/2007	393.46	1026	632.54
98	GONDIA-JABALPUR(GC), (SECR)	SECR	02/1997	04/2020	511.86	2005.25	1493.39
99	MUNEERABAD-MAHABOONNAGAR(NL), SCR	SCR	04/1997	03/2000	1723	3421.35	1698.35
100	NANDYAL-YERRAGUNTLA(NL), SCR	SCR	03/1996	02/2009	164.36	1050	885.64

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
101	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	2298.42	2733.86	435.44
102	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	3951.98	4259.48	307.5
103	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	2500	27949	25449
104	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	450	2200	1750
105	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	410.08	860.41	450.33
106	ANGAMALI-SABARIMALA (N.L.)(SR)	SR	10/1998	N.A.	1566	2815.62	1249.62
107	KODERMA-TILAIYA (NL), ECR	ECR	04/2002	N.A.	459.91	1625.87	1165.96
108	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	678.54	929.86	251.32
109	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	1614.59	1878	263.41
110	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	578	760	182
111	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	NWR	05/2015	N.A.	873.71	2215.27	1341.56
112	SAMASTIPUR-DARBANGHA	ECR	05/2015	N.A.	380	519.33	139.33
113	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	860.43	1147	286.57
114	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	600	701.81	101.81
115	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	713.48	2725	2011.52
116	RISHIKESH - KARNAPRAYAG NEW LINE	RVNL	04/2011	12/2024	16216	22716.11	6500.11
117	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	927.01	1400	472.99
118	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	1027.4	2373	1345.6
119	TURAVUR-AMBALAPUZHA DOUBLING	SR	02/2015	N.A.	1000	1246	246
120	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	969.83	1312.96	343.13
121	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	NFR	04/2016	12/2021	602.27	2144.78	1542.51
122	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	870.96	1873.21	1002.25

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
123	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	2232.32	2950	717.68
124	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	701.61	810.02	108.41
125	MUZAFFARPUR-SITAMARHI NEW LINE	ECR	01/1991	07/2014	332.15	546.71	214.56
126	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	SR	10/2013	04/2014	187.26	327	139.74
127	VIJAYAWADA-GUDUR	RVNL	04/2015	12/2023	3246.26	3548.68	302.42
128	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	3631	3887.48	256.48
129	DAUND - MANMAD (236 KM)	CR	02/2016	03/2023	1876	2081.27	205.27
130	VAIBHAVWADI -KOLHAPUR (107 KM)	CR	02/2016	03/2024	2750	3438.51	688.51
131	PUNE-NASIK (265 KM)	CR	02/2016	03/2024	2425	5341.68	2916.68
132	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	1763.93	2470	706.07
133	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	NER	03/2015	03/2022	1295.42	1758	462.58
134	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	DFCC	10/2006	N.A.	11589	28181	16592
135	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	595.51	769.4	173.89
136	PIRPAINTI-BHAGALPUR	ER	04/2011	N.A.	261.38	565	303.62
137	BANDEL-BOINCHI 3RD LINE	ER	04/2011	N.A.	288.35	502.48	214.13
138	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	915.98	2137.81	1221.83
139	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	ER	04/2007	N.A.	450	1261.34	811.34
140	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	406.99	545.7	138.71
141	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	120.7	2172.16	2051.46
142	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	632.68	950	317.32
143	AMBARI FALAKATA TO NEW MAYNAGURI	NFR	04/2011	03/2019	314	800	486
144	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	NFR	04/1999	N.A.	819.23	1871	1051.77
145	MURKONGSELEK-PASIGHAT NL	NFR	04/2011	03/2020	414.84	750	335.16

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
146	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	NFR	04/2010	N.A.	241.52	373.87	132.35
147	NEW BG LINE FROM BALURGHAT TO HILLY NFR	NFR	04/2010	03/2020	242.22	471	228.78
148	NEW BG LINE FROM BYRNIHAT TO SHILLONG	NFR	04/2010	03/2021	906.46	4083.02	3176.56
149	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	SR	04/2007	N.A.	931.98	1121	189.02
150	MADURAI-BODINAYAKKANUR	SR	04/2008	N.A.	164.41	608.13	443.72
151	ERODE-PALANI	SR	04/2008	N.A.	288.57	603.23	314.66
152	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	569.63	742	172.37
153	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	NFR	04/2010	N.A.	221.42	380	158.58
154	KUMBALAM-TURAVUR	SR	04/2011	N.A.	252.96	369.55	116.59
155	KURUPPANTHARA-CHINGAVANAM	SR	04/2007	N.A.	270.14	457.08	186.94
156	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	SR	04/1999	N.A.	198.68	559.95	361.27
157	CHENNAI-CUDDALORE VIA MAMALLAPURAM	SR	04/2008	N.A.	523.52	1205	681.48
158	ATTIPPATTU PUTTUR	SR	04/2008	02/2019	151.84	527.37	375.53
159	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	1798	2042.51	244.51
160	HAJIPUR-RAMDAYALUNAGAR DOUBLING	ECR	04/2013	N.A.	213.01	495	281.99
161	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	548	819.01	271.01
162	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	ECR	04/2004	N.A.	372.14	1470.5	1098.36
163	MOTIHARI-SITAMARHI (NL)	ECR	04/2006	N.A.	211	1006	795
164	CHHAPRA-MUZAFFARPUR (NL)	ECR	04/2006	N.A.	378.56	1858.75	1480.19
165	SAKRI-HASANPUR ROAD (NL)	ECR	04/1999	N.A.	325	735.2	410.2
166	BIHTA-AURANGABAD (NL)	ECR	04/2008	N.A.	326.2	2995.01	2668.81
167	GAYA-CHATRA (NL)	ECR	04/2008	N.A.	415.67	549.75	134.08
168	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	258.2	358.68	100.48

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
169	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	651	1009	358
170	BOWAICHANDI-ARAMBAGH	SER	04/2010	N.A.	267.37	620	352.63
171	ALWAR-BANDIKUI DOUBLING	NWR	04/2013	02/2019	242.09	525	282.91
172	AJMER-BANGURGRAM	NWR	04/2011	11/2019	213.39	375	161.61
173	THIYAT HAMIRA-SANU	NWR	04/2013	10/2018	236.93	350.45	113.52
174	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	2912.96	3845.6	932.64
175	RATLAM-DUNGARPUR VIA BANSWARA (NL)	NWR	04/2011	N.A.	2082.75	4262.36	2179.61
176	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	1037.15	1383.69	346.54
177	PALANPUR-SAMAKHAYALI (DL)	RVNL	04/2013	12/2021	1548.66	1868.89	320.23
178	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	320.66	1378.11	1057.45
179	DHASA-JETALSAR (GC)	RVNL	04/2012	03/2021	644.38	872.65	228.27
180	AHMEDABAD-BOTAD (GC)	RVNL	04/2012	12/2021	975.62	1500	524.38
181	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	1640.04	1873.1	233.06
182	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	1347.26	1524.68	177.42
183	BANGURGRAM-GURIYA PATCH DOUBLING	NWR	04/2012	12/2019	246.08	395	148.92
184	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	M RTP	03/2013	03/2016	4874.58	8574.97	3700.39
185	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	295	580	285
186	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	NER	03/2007	12/2021	243.78	895	651.22
187	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	NER	03/2013	N.A.	307	1409.09	1102.09
188	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKAWA-JAIN	NFR	02/1999	04/2010	380.6	1090.6	710
189	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	691.84	890.62	198.78
190	JALANDHAR-PATHANKOT-JAMMU TAWI	NR	03/2002	03/2016	625	859	234
191	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	2288	4970.11	2682.11

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
192	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	551.51	890.76	339.25
193	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	1973	2135.34	162.34
194	CHAMPA-JHARSUGUDA 3RD LINE	SECR	04/2008	12/2019	872	1226.51	354.51
195	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	229	1096	867
196	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF,	ECR	04/1991	N.A.	329.39	1483.14	1153.75
197	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	ECR	04/1998	N.A.	180.82	726.31	545.49
198	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	731.64	1185.73	454.09
199	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	744.04	1215.54	471.5
200	BURHWAL - GONDA - 3RD RUNNING LINE.	NER	04/2016	N.A.	602.5	714.34	111.84
201	CHANDIGARH-BADDI	NR	04/2007	03/2023	328.14	1540.13	1211.99
202	WESTERN DEDICATED FREIGHT CORRIDOR	DFCC	11/2007	03/2020	16592	51101	34509
203	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	NER	04/2017	01/2018	1343	1476.15	133.15
204	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	150	341.66	191.66
205	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	760	1536	776
206	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	268.87	950	681.13
207	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	585.93	1268.32	682.39
208	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	119.73	449.39	329.66
209	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	1908.51	3176.6	1268.09
210	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	582.13	1247.64	665.51
211	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	1485.85	1835.83	349.98
212	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	1183.25	1825	641.75
213	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	942.95	1536	593.05
214	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	948.04	2009	1060.96

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
215	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	2335.67	3327.72	992.05
216	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	1156.94	1800.59	643.65
217	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	SER	04/2012	12/2016	148.77	377	228.23
218	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	1111.99	1539.28	427.29
219	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	1503.71	3377	1873.29
220	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	829.74	1886.76	1057.02
221	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	SR	09/1995	03/2020	303.98	1720	1416.02
222	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	1382.78	1960	577.22
223	HUBLI-ANKOLA(NL),SWR	SWR	04/1997	N.A.	2315	5174.3	2859.3
224	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	1339.48	8600	7260.52
225	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	2326.52	6911	4584.48
226	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	532.87	2145	1612.13
227	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	385.2	1105	719.8
228	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	495.74	734.01	238.27
229	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	4454.17	12264.15	7809.98
230	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	2923.13	3791.66	868.53
231	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	1180.19	4541.38	3361.19
232	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	704.31	927.94	223.63
233	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	2288.7	2643.25	354.55
234	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	NR	04/2012	N.A.	295.68	419	123.32
235	RAYADURGA-TUMKUR NL	SWR	04/2007	N.A.	2062.3	2432.5	370.2
236	SRINIVASA-PURA-MADANAPALLI NL	SWR	04/2013	N.A.	296	466.65	170.65
237	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	SWR	04/2013	N.A.	558	692	134

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
238	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	NR	04/2007	N.A.	336.91	791.39	454.48
239	BHANUPALI-BILASPUR BERI NL	RVNL	04/2008	12/2026	2966.99	6753.42	3786.43
240	TARAKESHWAR-MAGRA NEW BG LINE	ER	04/2010	N.A.	365.17	527.54	162.37
241	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	792.89	910.93	118.04
242	WARDHA-NANDED MAHARASHTRA	CR	04/2008	03/2023	3168.29	3445.48	277.19
243	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	3503.69	6171.08	2667.39
244	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	2913.51	4639	1725.49
245	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	477.88	751.55	273.67
246	RAMGANJMUHDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	424.6	2909.99	2485.39
247	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	607.09	1425.44	818.35
248	HARIDASPUR-PARADEEP(NL)	RVNL	04/1996	12/2017	1185.64	1844.47	658.83
ROAD TRANSPORT AND HIGHWAYS							
Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
249	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	NHAI	12/2003	02/2009	280	612.58	332.58
250	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	NHAI	05/2009	11/2011	1108	2288	1180
251	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	NHAI	12/2003	04/2009	199.81	340.14	140.33
252	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	624.41	992.67	368.26
253	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	MoRTH	04/2013	08/2013	151.59	369.92	218.33
254	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	MoRTH	01/2013	02/2013	182.28	369.58	187.3
255	INDORE-DEWAS(NH-3)	NHAI	11/2010	05/2013	325	475	150
256	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	624.98	731.5	106.52
257	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	NHAI	03/2018	N.A.	1029.96	1261.05	231.09
258	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	NHAI	03/2018	03/2021	1532.62	2499	966.38
259	SIX LANING OF SHAMLA JI TO MOTACHILODHA	NHAI	02/2018	N.A.	1052.21	1449	396.79

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
	FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF						
260	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	NHAI	03/2018	N.A.	1120.57	1332	211.43
261	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	NHAI	03/2018	N.A.	925.4	1197	271.6
262	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	NHAI	03/2018	N.A.	1261.98	1952.2	690.22
263	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	NHAI	02/2018	N.A.	2177.8	2450	272.2
264	SIX-LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	NHAI	02/2018	N.A.	1995.34	2400	404.66
265	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	NHAI	02/2018	N.A.	1166.26	1296.93	130.67
266	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	NHAI	02/2018	N.A.	1424.77	1853.42	428.65
267	4-LANNING OF THALSERRY -MAHE BYPASS	NHAI	09/2017	09/2017	1124.11	1232.76	108.65
268	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(0	NHAI	03/2017	03/2020	993.16	1434	440.84
269	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	NHAI	03/2017	03/2020	831.58	1177	345.42
270	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	NHAI	03/2017	03/2020	2064.99	2447	382.01
271	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	NHAI	03/2017	03/2020	1288.07	1420	131.93
272	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	NHAI	03/2017	03/2020	1041.62	1187.1	145.48
273	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV]	NHAI	03/2016	04/2019	1587.49	2982	1394.51
274	MEERUT-BULANDSHAHR	NHAI	01/2016	N.A.	683.24	987.94	304.7
275	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	NHAI	08/2015	04/2018	516.13	649.27	133.14
276	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	NHAI	08/2015	N.A.	854.8	1038.56	183.76
277	SIX-LANING OF BARWA ADDA-PANAGARH	NHAI	04/2014	N.A.	1665	2360.65	695.65
278	NASHRI- CHANANI	NHAI	05/2011	06/2015	2159	2519	360
279	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	NHAI	04/2014	09/2016	1266.6	1544	277.4
280	BRAHMPUTRA BRIDGE,NH NO-31	NHAI	12/2003	04/2010	217.61	360.84	143.23
281	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	NHIDCL	03/2015	06/2018	394	522.86	128.86

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
282	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	MORTH	04/2013	08/2013	166.27	359.9	193.63
283	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	10/2010	193.69	327.92	134.23
284	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	NHAI	12/2003	11/2008	167.64	435.78	268.14
285	HARANGAJO TO MAIBANG, NH-54	NHAI	12/2003	07/2009	196	655.17	459.17
286	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	NHAI	12/2003	11/2008	155.04	255.23	100.19
287	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	NHAI	12/2017	N.A.	217.96	884	666.04
288	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	NHAI	12/2017	N.A.	656.98	840	183.02
289	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MORTH	08/2010	09/2014	186.96	322.24	135.28
290	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	MORTH	04/2014	08/2017	279.7	398.52	118.82
291	FOUR LANNING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	NHAI	03/2018	N.A.	642.13	807	164.87
292	SIX LANNING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	NHAI	03/2018	N.A.	795.5	922.64	127.14
293	SIX LANNING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	NHAI	03/2018	N.A.	634.7	931.21	296.51
294	FOUR LANNING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N	NHAI	03/2018	N.A.	2065.96	2169	103.04
295	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	NHAI	03/2017	03/2020	744.64	982	237.36
296	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	NHAI	03/2017	03/2020	1184.71	1310	125.29
297	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	NHAI	01/2017	N.A.	1251.11	1361	109.89
298	4 LANNING OF KSHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20	NHAI	11/2012	07/2018	605.84	722.46	116.62
299	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	NHAI	09/2016	08/2019	950.69	1108	157.31
300	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	NHAI	09/2016	N.A.	1239.82	1727.66	487.84
301	4 LANNING FROM PHAGWARA TO RUPNAGAR	NHAI	08/2016	N.A.	1169.61	2280	1110.39
302	4/6 LANNING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	NHAI	08/2016	09/2019	1388.34	1588.29	199.95
303	FOUR LANNING OF GWALIOR-SHIVPURI	NHAI	05/2013	11/2015	1055	1601.77	546.77
304	4 LANNING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	NHAI	12/2015	06/2018	1083	1827.15	744.15

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
305	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	593.26	716.78	123.52
306	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	531.13	744.73	213.6
307	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MORTH	08/2010	10/2010	195.04	377.99	182.95
308	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MORTH	11/2010	05/2017	268.08	390.73	122.65
309	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBAIRELI	NHAI	04/2014	01/2016	495.78	627.93	132.15
310	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	NHAI	07/2012	01/2014	291.36	469.31	177.95
311	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	2848	3379.45	531.45

STEEL

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
312	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	15525	21940	6415
313	FORGED WHEEL PLANT	RINL	04/2014	09/2018	1682.85	2100	417.15

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
314	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	13334	24664	11330

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
315	BANGALORE METRO RAIL PROJECT PHASE-2	BMRL	02/2014	02/2019	26405.14	30695.12	4289.98
316	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	10773	12787	2014
317	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	23136	33406	10270
318	PATNA METRO RAIL CORPORATION LIMITED	PATNA METRO	02/2019	06/2024	13365.77	13925.5	559.73
319	CHENNAI METRO RAIL LTD (PHASE 1)	CMRL	02/2009	12/2015	14600	18380	3780
320	REDEVELOPMENT OF EAST KIDWAI NAGAR	NBCC	06/2012	11/2019	4264	4720.73	456.73
321	KOCHI METRO RAIL PROJECT	KMRCL	07/2012	07/2017	5181.79	6218.14	1036.35

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING COST OVERRUNS OF MORE THAN Rs. 100 CRORE

(AUGUST 2021)

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	Cost Original (Rs.crore)	Cost Anticipated (Rs.crore)	Cost Overrun (Rs.crore)
322	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	10151.04	55548.87	45397.83
323	I AND D AND STP WORKS FOR BHAGALPUR	BUIDCO	10/2017	09/2020	254.13	413.29	159.16
324	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	BUIDCO	12/2014	03/2020	225.77	398.9	173.13

FLASH REPORT

DOA -> Date of Approval

DOC -> date of Commissioning

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

ATOMIC ENERGY

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
1	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW)	NPCIL	10/2009	12/2016	03/2023	1,2320.00	1,7079.00	4759	75
2	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	NPCIL	10/2009	12/2015	02/2022	1,1459.00	1,6580.00	5121	74
3	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500 MWE)	BHAVNI	09/2003	09/2010	10/2022	3492.00	6840.00	3348	145

CIVIL AVIATION

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
4	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	AAI	07/2018	09/2021	12/2022	346.27	480.33	134.06	15
5	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	AAI	10/2013	09/2018	06/2022	417.23	707.73	290.5	45

COAL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
6	RANIGANJ MASTER PLAN	ECL	08/2009	08/2019	08/2024	2661.73	5146.48	2484.75	60
7	HINGULA OC-II EXP. PH-III (15 MTY)	MCL	11/2008	03/2013	03/2024	479.53	703.39	223.86	132
8	AMALGAMATED GONDEGAON GHATROHAN OC	WCL	02/2016	03/2019	03/2022	198.68	325.18	126.5	36
9	RCE OF INDARAM OCP(1.20 MTPA)	SCCL	07/2011	03/2015	03/2022	162.76	349.28	186.52	84
10	JAGANNATHPOR OCP(3.00MTY)	SECL	09/2008	03/2015	03/2022	152.43	459.49	307.06	84
11	MAGADH EXPANSION OC(51 MTY)	CCL	08/2008	07/2012	03/2028	6964.33	7254.37	290.04	188

DPIIT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
12	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	IICC	11/2017	12/2019	05/2022	4773.00	5178.00	405	29

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

HEALTH AND FAMILY WELFARE

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
13	AIIMS BILASPUR	NBCC	04/2018	09/2021	06/2022	1351.00	1471.00	120	9
14	LHMC NEW DELHI-RE-DEVELOPMENT	HSCC	02/2013	11/2013	09/2021	414.11	655.58	241.47	94

HOME AFFAIRS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
15	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	CPWD	10/2013	10/2019	03/2022	1219.21	2000.00	780.79	29

PETROLEUM

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
16	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	ONGC	04/2019	03/2022	05/2023	3228.80	3976.67	747.87	14
17	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	IOCL	04/2018	02/2020	07/2022	206.63	340.76	134.13	29
18	KOCHI SALEM LPG PIPELINE PROJECT	BPCL	12/2015	06/2019	02/2022	1112.00	1507.24	395.24	32
19	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	HPCL	09/2017	06/2021	07/2022	2677.00	3072.00	395	13
20	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	IOCL	05/2016	12/2018	02/2022	4497.00	6025.00	1528	38
21	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	ONGC	12/2015	04/2018	05/2022	3190.69	3375.90	185.21	49
22	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	GAIL	06/2009	12/2012	02/2022	2915.00	5909.00	2994	110
23	LPG TERMINAL AT KOCHI	IOCL	10/2015	10/2017	03/2022	607.06	1236.00	628.94	53
24	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	IOCL	01/2015	03/2021	12/2021	1823.00	3027.90	1204.9	9
25	PARADIP HYDERABAD PIPELINE	IOCL	01/2015	12/2020	03/2022	2321.00	3338.00	1017	15
26	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	ONGC	03/2011	05/2013	02/2022	861.79	2001.34	1139.55	105
27	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT	BPCL	11/2014	08/2018	09/2021	4588.29	5245.96	657.67	37

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

539

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
	KOCHI REFINERY								
28	IRUGUR-DEVANGONTHI POL PIPELINE	BPCL	11/2012	02/2017	08/2022	678.00	1472.00	794	66
29	VISAKH REFINERY MODERNISATION PROJECT	HPCL	07/2016	07/2020	07/2022	2,0928.00	2,6264.00	5336	24

POWER

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
30	DURGAPUR PP-III (2X20 MW) - NSPCL	NTPC	12/2016	11/2018	12/2021	529.68	633.80	104.12	37
31	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	NTPC	05/2016	12/2018	11/2021	1885.13	2311.89	426.76	35
32	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	NTPC	01/2016	11/2020	10/2022	1,0598.98	1,0997.70	398.72	23
33	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	THDCIL	08/2008	06/2013	06/2024	2491.58	3860.35	1368.77	132
34	EASTERN REGION STRENGTHENING SCHEME-XVIII	PGCIL	03/2017	07/2020	10/2021	3500.00	3994.00	494	15
35	NPGCL-NABINAGAR STPP - JV (3X660 MW)	NTPC	01/2013	05/2018	02/2022	1,2964.60	1,7304.00	4339.4	45
36	PARBATI HEP (4X200 MW) (NHPC) II	NHPC	09/2002	09/2009	03/2023	3919.59	9897.59	5978	162
37	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	NHPC	09/2003	09/2010	08/2023	6285.33	1,9992.43	13707.1	155
38	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	PGCIL	02/2009	08/2013	08/2022	1,1130.19	1,4719.10	3588.91	108
39	NORTH KARANPURA STPP (3X660 MW)	NTPC	02/2014	06/2019	12/2023	1,4366.58	1,5389.42	1022.84	54
40	BRBCL-NABINAGAR TPP- JV (4X250 MW)	NTPC	01/2007	07/2012	10/2021	5353.00	1,0566.00	5213	111
41	TEHRI PUMPED STORAGE PLANT(1000MW)	THDCIL	07/2006	02/2016	06/2023	1657.00	4825.60	3168.6	88
42	BARH STPP(3X660MW) NTPC	NTPC	02/2005	10/2011	07/2023	8692.97	2,1312.11	12619.1	141
43	NAITWAR MORI HEP	SJVN	10/2017	12/2021	06/2022	648.33	947.89	299.56	6

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

540

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
44	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	PGCIL	12/2014	12/2018	03/2022	5111.33	6700.00	1588.67	39
45	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	PGCIL	12/2014	12/2018	03/2024	4754.42	9129.32	4374.9	63

RAILWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
46	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	WR	04/2017	03/2020	09/2021	691.84	890.62	198.78	18
47	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	SECR	06/2018	12/2021	12/2024	229.00	1096.00	867	36
48	SAGALI VALMIKINAGAR DOUBLING 109.7 KM	ECR	04/2016	03/2021	03/2024	744.04	1215.54	471.5	36
49	ROURKELA JHARSUGUDA THIRD LINE 101 KM	SER	11/2015	03/2020	02/2022	969.83	1312.96	343.13	23
50	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	SER	04/1998	03/2003	03/2030	1027.40	2373.00	1345.6	324
51	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	RVNL	04/2011	03/2019	06/2022	927.01	1400.00	472.99	39
52	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL - ELECTRIFICATION (641.37 KM)	RVNL	03/2009	03/2020	12/2021	713.48	2725.00	2011.52	21
53	VIZIANAGARAM -SAMABALPUR 3RD LINE	RVNL	01/1991	12/2024	12/2026	2335.67	3327.72	992.05	24
54	SAMBALPUR - TITLAGARH - DOUBLING	RVNL	03/2006	03/2020	12/2021	948.04	2009.00	1060.96	21
55	BANASPANI- JAKHPURA - DOUBLING	RVNL	03/2009	03/2019	06/2022	942.95	1536.00	593.05	39
56	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	RVNL	03/2012	12/2020	12/2022	1183.25	1825.00	641.75	24
57	BINA - KOTA DOUBLING WITH RE	RVNL	04/2011	12/2020	12/2021	1485.85	1835.83	349.98	12
58	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR)	NFR	04/2006	03/2015	03/2026	2326.52	6911.00	4584.48	132
59	SEVOK RANGPO, NEFR	NFR	04/2008	12/2015	12/2023	1339.48	8600.00	7260.52	96

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

541

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
60	DAUSA-GANGAPUR CITY(NL), NWR	NWR	02/1997	02/2019	06/2022	410.08	860.41	450.33	40
61	NANGALDAM-TALWARA(NL), NR	NR	03/1981	07/2012	03/2024	450.00	2200.00	1750	140
62	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR	NR	03/1995	11/2002	12/2022	2500.00	2,7949.00	25449	241
63	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	RVNL	04/2010	03/2016	03/2025	3951.98	4259.48	307.5	108
64	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	RVNL	04/2010	03/2014	12/2025	2298.42	2733.86	435.44	141
65	MUNEERABAD-MAHABOBNAGAR(NL), SCR	SCR	04/1997	03/2000	03/2023	1723.00	3421.35	1698.35	276
66	VIRAMGAM-SAMAKHIALI (DL)	WR	04/2011	03/2021	12/2022	1037.15	1383.69	346.54	21
67	RATLAM-MHOW-KHANDWA-AKOLA (GC)	WR	04/2008	03/2022	03/2024	3503.69	6171.08	2667.39	24
68	KALYAN-KASARA 3RD LINE	CR	04/2011	03/2021	03/2023	792.89	910.93	118.04	24
69	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	ER	04/2009	02/2012	03/2025	499.96	680.68	180.72	157
70	BAGALKOT-KUDACHI NL	SWR	04/2010	03/2016	12/2026	986.30	1530.09	543.79	129
71	NADIKUDE-SRI KALAHASTI	SCR	04/2011	03/2021	03/2024	2288.70	2643.25	354.55	36
72	BHADRACHALAM ROAD-SATTUPALLI	SCR	04/2010	03/2020	11/2021	704.31	927.94	223.63	20
73	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	SCR	04/2008	03/2014	03/2027	2132.77	3037.95	905.18	156
74	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	CR	02/1997	03/2021	03/2023	2271.50	4794.60	2523.1	24
75	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	MRTP	03/1996	03/2004	03/2022	495.44	2980.41	2484.97	216
76	KOTLPALLI-NARASAPUR (NL) (SCR)	SCR	12/2001	03/2009	03/2024	1045.20	2120.16	1074.96	180

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

542

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
77	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	ER	04/2000	03/2019	03/2025	1188.91	1619.48	430.57	72
78	DEOGHAR - SULTANGANJ (INL), ER	ER	04/2000	02/2013	03/2024	607.09	1425.44	818.35	133
79	RAMGANJMUUNDI-BHOPAL (NL),WCR	WCR	04/2001	03/2021	03/2024	424.60	2909.99	2485.39	36
80	SUKINDA ROAD - ANGUL (NL)(ECOR)	RVNL	04/1998	02/2015	06/2022	1202.70	2440.53	1237.83	88
81	TALCHER-BIMALAGARH(NL)(ECOR)	ECOR	04/2005	06/2021	03/2025	810.78	1928.07	1117.29	45
82	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	SR	09/2007	02/2019	03/2025	724.69	2950.00	2225.31	73
83	BHAIRABI SAIRONG, NL, NEFR	NFR	04/2008	03/2014	03/2024	2393.47	5521.45	3127.98	120
84	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	ECR	04/1996	03/2012	09/2021	477.88	751.55	273.67	114
85	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	RVNL	04/2010	03/2016	03/2025	2913.51	4639.00	1725.49	108
86	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	WCR	09/1998	05/2008	03/2025	247.66	8248.50	8000.84	202
87	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR	ECR	04/1997	03/2012	11/2022	324.73	1070.00	745.27	128
88	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	NFR	04/2000	12/2008	09/2021	1180.19	4541.38	3361.19	153
89	KHURDA ROAD-BOLANGIR(NL)ECOR	ECOR	04/1994	03/2009	03/2026	2923.13	3791.66	868.53	204
90	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	NFR	04/2003	03/2011	12/2023	4454.17	1,2264.15	7809.98	153
91	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	MRTPT	04/2006	06/2013	07/2022	495.74	734.01	238.27	109
92	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	NFR	09/2006	03/2019	03/2023	385.20	1105.00	719.8	48
93	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	NFR	09/2006	03/2019	03/2024	532.87	2145.00	1612.13	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

543

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
94	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	NCR	04/2011	03/2022	12/2024	2912.96	3845.60	932.64	33
95	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	SER	04/2010	03/2015	03/2025	651.00	1009.00	358	120
96	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	SER	04/2012	12/2018	08/2021	258.20	358.68	100.48	32
97	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	ECR	04/2009	03/2020	03/2023	548.00	819.01	271.01	36
98	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	NFR	04/2013	03/2019	12/2023	1798.00	2042.51	244.51	57
99	AGARTALA-AKHAURA NL	NFR	04/2012	03/2020	03/2022	569.63	742.00	172.37	24
100	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	RVNL	04/2012	03/2016	12/2021	632.68	950.00	317.32	69
101	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	SR	04/2011	03/2019	12/2027	120.70	2172.16	2051.46	105
102	BANGLORE - SATYAMANGALAM (NL)(SWR)	SWR	04/1996	03/2002	03/2024	1382.78	1960.00	577.22	264
103	TIRUCHIRAPPALI-NAGORE-KARAIKKAL (SR) (GC)	SR	09/1995	03/2020	03/2025	303.98	1720.00	1416.02	60
104	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	WR	04/2008	03/2020	03/2024	829.74	1886.76	1057.02	48
105	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	RVNL	03/2012	03/2020	03/2022	1503.71	3377.00	1873.29	24
106	SAMBALPUR-TALCHER DOUBLING	ECOR	03/2011	02/2019	12/2021	1111.99	1539.28	427.29	34
107	HUBLI- CHIKJAJUR	SWR	03/2015	03/2020	03/2023	1156.94	1800.59	643.65	36
108	PHULERA - DIGANA DOUBLING	NWR	05/2015	03/2020	10/2022	600.00	701.81	101.81	31
109	YELAHANKA-PENUKONDA	SWR	05/2015	03/2020	09/2021	860.43	1147.00	286.57	18
110	ARSIKERE-TUMKUR	SWR	03/2015	03/2020	11/2021	578.00	760.00	182	20
111	HOTGI-KUDGI-GADAG	SWR	03/2015	03/2019	03/2024	1614.59	1878.00	263.41	60

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

544

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
112	HAJIPUR - BACHAWARA	ECR	05/2015	03/2019	12/2021	678.54	929.86	251.32	33
113	CHHAPRA-BALLIA UP	NER	03/2013	01/2019	02/2022	295.00	580.00	285	37
114	CHOTTAUDEPUR-DHAR(NL)	WR	04/2007	03/2022	03/2023	1347.26	1524.68	177.42	12
115	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	WR	04/2007	03/2022	03/2023	1640.04	1873.10	233.06	12
116	RAJKOT-VERAVAL, WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	WR	04/1994	03/2019	03/2023	320.66	1378.11	1057.45	48
117	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG	ER	04/1987	03/2006	03/2025	406.99	545.70	138.71	228
118	PIRPAINTI-JASIDIH	ER	04/2013	03/2022	03/2025	915.98	2137.81	1221.83	36
119	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	ER	04/2005	03/2017	03/2025	595.51	769.40	173.89	96
120	KATNI - SINGRAULI DOUBLING PROJECT	WCR	12/2015	03/2020	03/2024	1763.93	2470.00	706.07	48
121	GUNTUR-GUNTAKAL	SCR	04/2016	03/2022	03/2024	3631.00	3887.48	256.48	24
122	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	ECOR	04/2015	11/2018	03/2024	701.61	810.02	108.41	64
123	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	NFR	04/2015	03/2022	03/2023	2232.32	2950.00	717.68	12
124	DIGARU-HOJAI (102 KM)	NFR	04/2015	03/2021	03/2022	870.96	1873.21	1002.25	12
125	KATNI GRADE SEPARATOR/BYE PASS	WCR	08/2016	03/2022	03/2023	582.13	1247.64	665.51	12
126	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	SECR	09/2016	03/2023	12/2023	1908.51	3176.60	1268.09	9
127	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE-GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	SCR	04/2017	03/2022	12/2022	119.73	449.39	329.66	9
128	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	SECR	04/2010	02/2019	12/2021	585.93	1268.32	682.39	34

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

545

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
129	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	SR	02/1996	03/2005	09/2021	268.87	950.00	681.13	198
130	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	SR	02/2015	03/2020	06/2022	760.00	1536.00	776	27
131	NANPARA - NEPALGANJ GAUGE CONVERSION.	NER	04/2017	04/2017	10/2022	150.00	341.66	191.66	66
132	MUZAFFARPUR SAGALI DOUBLING 100.60 KM	ECR	04/2016	03/2021	03/2024	731.64	1185.73	454.09	36
133	JHARSUGUDA-BILASPUR 4TH LINE	SECR	04/2015	03/2021	12/2023	1973.00	2135.34	162.34	33
134	GEVRA ROAD PENDRA ROAD	IRCON	02/2014	03/2022	09/2023	2288.00	4970.11	2682.11	18
135	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	WR	02/1991	03/2019	10/2021	551.51	890.76	339.25	31

ROAD TRANSPORT AND HIGHWAYS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
136	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	MoRTH	01/2016	10/2016	12/2021	624.98	731.50	106.52	62
137	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	NHAI	10/2015	05/2018	03/2022	531.13	744.73	213.6	46
138	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	NHAI	10/2015	05/2018	03/2022	593.26	716.78	123.52	46
139	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	09/2014	12/2021	186.96	322.24	135.28	87
140	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	MoRTH	11/2010	05/2017	05/2022	268.08	390.73	122.65	60
141	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	MoRTH	11/2010	03/2011	12/2021	624.41	992.67	368.26	129
142	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	MoRTH	08/2010	10/2010	12/2021	193.69	327.92	134.23	134
143	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	MoRTH	08/2010	10/2010	12/2021	195.04	377.99	182.95	134
144	VARANASI-AURANGABAD KM.786 TO KM.978.40	NHAI	09/2011	03/2014	12/2022	2848.00	3379.45	531.45	105

DOA -> Date of Approval

COR -> Cost Overrun

DOC -> Date of Commissioning

546

TOR -> Time Overrun

DETAILS OF CENTRAL SECTOR PROJECTS SHOWING TIME OVERRUNS OF 6 MONTHS AND MORE AND COST OVERRUNS OF RS.100 CRORE AND ABOVE

(AUGUST 2021)

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)

STEEL

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
145	FORGED WHEEL PLANT	RINL	04/2014	09/2018	09/2021	1682.85	2100.00	417.15	36
146	NMDC INTEGRATED STEEL PLANT	NMDC	01/2010	05/2015	01/2022	1,5525.00	2,1940.00	6415	80

TELECOMMUNICATIONS

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
147	NETWORK FOR SPECTRUM	DOT	03/2012	07/2015	03/2022	1,3334.00	2,4664.00	11330	80

URBAN DEVELOPMENT

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
148	AHMEDABAD METRO RAIL PROJECT PHASE 1	MEGA	11/2014	12/2018	08/2022	1,0773.00	1,2787.00	2014	44
149	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	MMRCL	07/2013	03/2020	03/2023	2,3136.00	3,3406.00	10270	36
150	BANGALORE METRO RAIL PROJECT PHASE-2	BMRCL	02/2014	02/2019	03/2025	2,6405.14	3,0695.12	4289.98	73

WATER RESOURCES

Sn	Project	Agency	DOA	DOC Original	DOC Anticipated	Cost Original (Rs. crore)	Cost Anticipated (Rs. crore)	COR (Rs. crore)	TOR (Months)
151	POLAVARAM IRRIGATION PROJECT	PPA	02/2009	03/2020	04/2022	1,0151.04	5,5548.87	45397.8	25

DOA -> Date of Approval

DOC -> Date of Commissioning

TOR -> Time Overrun

COR -> Cost Overrun

Details of Ongoing Projects having Time and Cost Overruns w.r.t Latest Schedule

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	<u>ATOMIC ENERGY</u>							
	<u>Nuclear Power Corporation Of India Limited</u>							
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010	10/2009	11,459.00	16,580.00	12/2015	02/2022	44.69	74
2	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW) [N02000027	10/2009	12,320.00	17,079.00	12/2016	03/2023	38.63	75
	Total		23,779.00	33,659.00				
	<u>CIVIL AVIATION</u>							
	<u>Airport Authority Of India Limited</u>							
3	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078	07/2018	346.27	480.33	09/2021	12/2022	38.72	15
4	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083	12/2016	1,142.00	1,232.00	03/2021	03/2023	7.88	24
	Total		1,488.27	1,712.33				
	<u>COAL</u>							
	<u>Eastern Coal Fields Limited</u>							
5	RANIGANJ MASTER PLAN - [N06000163	08/2009	2,661.73	5,146.48	08/2019	08/2024	93.35	60
	<u>Mahanadi Coal Fields Limited</u>							
6	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068	11/2008	479.53	703.39	03/2013	03/2024	46.68	132
	<u>Neyveli Lignite Corporation</u>							
7	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW - [N06000152	07/2016	17,237.00	17,237.80	11/2021	11/2022	.00	12
	<u>Singareni Colliers Company Limited</u>							
8	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093	07/2011	162.76	349.28	03/2015	03/2022	114.60	84
9	KAKATIYAKHANI OPENCASE-2 PROJECT - [N06000129	05/2015	397.09	442.42	03/2019	03/2022	11.42	36
10	JALAGAM VENGALA RAO OCP-II - [N06000094	07/2011	447.06	473.22	03/2015	03/2023	5.85	96
11	RAMAGUNDAM OC-II EXTENSION - [N06000078	12/2009	418.97	489.62	03/2012	03/2023	16.86	132
	<u>Western Coal Fields Limited</u>							

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
12	RECAST PR FOR DHANKASA UG (1.00 MTY) - [N06000155]	09/2016	289.29 -	289.30	03/2022 -	03/2025	.00	36
	Total		22,093.43 -	25,131.51				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>							
	<u>Central Public Works Department</u>							
13	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES - [N44000001]	03/2021	127.26 -	188.88	10/2023 -	10/2023	48.42	0
14	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]	02/2019	186.00 199.00	205.00	09/2020 -	-	10.22	0
15	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]	02/2016	496.18 496.00	498.99	06/2017 -	03/2022	.57	57
16	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]	12/2016	549.31 -	559.47	07/2019 -	-	1.85	0
	<u>Rail India Technical And Economic Service</u>							
17	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]	09/2013	484.32 -	626.26	09/2014 -	-	29.31	0
	Total		1,843.07 -	2,078.60				
	<u>DPIIT</u>							
	<u>Delhi Mumbai Industrial Corridor</u>							
18	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]	09/2011	12,579.09 -	13,812.30	09/2019 -	07/2021	9.80	22
	<u>India International Convention And Expo Centre</u>							
19	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE - [N40000002]	11/2017	4,773.00 -	5,178.00	12/2019 -	05/2022	8.49	29
	Total		17,352.09 -	18,990.30				
	<u>HEALTH AND FAMILY WELFARE</u>							
	<u>Central Public Works Department</u>							
20	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR - [N21000030]	03/2019	1,577.00 -	1,828.00	09/2025 -	09/2025	15.92	0
	<u>Hospital Services Consultancy Corporation Ltd</u>							
21	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]	07/2016	152.95 -	177.92	02/2018 -	03/2021	16.33	37
22	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]	12/2017	156.56 -	190.34	- -	11/2021	21.58	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
23	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR [N21000010]	12/2014	168.90 -	191.20	05/2017 -	07/2019	13.20	26
24	CNCI KOLKATA WEST BENGAL - [N21000015]	08/2016	244.00 -	248.00	09/2018 -	05/2019	1.64	8
25	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]	01/2018	249.01 -	249.07	- -	01/2021	.02	0
26	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]	12/2013	204.44 -	250.00	05/2017 -	03/2021	22.29	46
27	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]	08/2017	272.19 -	272.54	03/2019 -	03/2021	.13	24
28	AIIMS - OPD(NEW) - [N21000009]	08/2014	293.65 -	325.00	05/2017 -	01/2020	10.68	32
29	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR [N21000011]	09/2014	505.58 -	585.00	03/2018 -	09/2019	15.71	18
30	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]	02/2013	414.11 -	655.58	11/2013 -	09/2021	58.31	94
	<u>National Building Construction Corporation Ltd</u>							
31	AIIMS BILASPUR - [N21000028]	04/2018	1,351.00 -	1,471.00	09/2021 -	06/2022	8.88	9
	Total		5,589.39 -	6,443.65				
	<u>HOME AFFAIRS</u>							
	<u>Central Public Works Department</u>							
32	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]	10/2013	1,219.21 -	2,000.00	10/2019 -	03/2022	64.04	29
	Total		1,219.21 -	2,000.00				
	<u>PETROLEUM</u>							
	<u>Hindustan Petroleum Corporation Limited</u>							
33	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST - [N16000296]	09/2017	2,677.00 -	3,072.00	06/2021 -	07/2022	14.76	13
	<u>Indian Oil Corporation Limited</u>							
34	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]	06/2016	423.00 -	502.00	08/2019 -	05/2021	18.68	21
35	LPG TERMINAL AT KOCHI - [N16000171]	10/2015	607.06 -	1,236.00	10/2017 -	03/2022	103.60	53
	<u>Oil & Natural Gas Corporation Limited</u>							
36	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS) - [N16000128]	03/2011	861.79 -	2,001.34	05/2013 -	02/2022	132.23	105

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
	Total		4,568.85	6,811.34				
	<u>POWER</u>							
	<u>National Thermal Power Corporation</u>							
37	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW [N18000142]	07/2012	1,527.00	1,801.07	08/2017	-	17.95	0
38	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]	10/2004	4,237.96 4,238.00	4,552.00	10/2017	-	7.41	0
39	NORTH KARANPURA STPP (3X660 MW) - [N18000177]	02/2014	14,366.58	15,389.42	06/2019	12/2023	7.12	54
	<u>Power Grid Corporation Of India Limited</u>							
40	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]	01/2015	203.28	260.03	07/2017	-	27.92	0
41	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]	10/2016	408.46	516.12	01/2019	-	26.36	0
42	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]	10/2011	487.49	639.46	06/2014	-	31.17	0
43	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]	05/2017	445.89	675.73	02/2019	-	51.55	0
44	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) [N18000181]	01/2015	871.62	902.49	10/2017	-	3.54	0
45	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]	10/2013	1,364.52	1,891.41	04/2016	-	38.61	0
46	EASTERN REGION STRENGTHENING SCHEME-XVIII - [N18000258]	03/2017	3,500.00 3,500.00	3,994.00	07/2020	10/2021	14.11	15
47	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT [N18000061]	10/2008	4,824.12	5,071.94	10/2012	-	5.14	0
	<u>Satluj Jal Vidyut Nigam Limited</u>							
48	NAITWAR MORI HEP - [N18000265]	10/2017	648.33	947.89	12/2021	06/2022	46.20	6
	Total		32,885.25	36,641.56				
	<u>RAILWAYS</u>							
	<u>Central Railways</u>							
49	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]	04/2011	184.06	325.00	03/2019	-	76.57	0
50	KALYAN-KASARA 3RD LINE - [N22000233]	04/2011	792.89	910.93	03/2021	03/2023	14.89	24
51	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]	02/2015	1,272.19	1,283.49	03/2022	03/2023	.89	12
52	DAUND - MANMAD (236 KM) - [N22000360]	02/2016	1,876.00	2,081.27	03/2023	03/2023	10.94	0

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
53	VAIBHAVWADI -KOLHAPUR (107 KM) - [N22000355]	02/2016	2,750.00 -	3,438.51	03/2024 -	-	25.04	0
54	WARDHA-NANDED MAHARASHTRA - [N22000231]	04/2008	3,168.29 -	3,445.48	03/2023 -	03/2023	8.75	0
55	PUNE-MIRAJ-LONDA (467 KM) - [N22000359]	02/2015	3,627.47 3,627.00	3,627.47	03/2024 -	03/2023	.00	-12
56	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]	02/1997	2,271.50 -	4,794.60	03/2021 -	03/2023	111.08	24
57	PUNE-NASIK (265 KM) - [N22000354]	02/2016	2,425.00 -	5,341.68	03/2024 -	03/2024	120.28	0
	<u>Container Corporation Of India</u>							
58	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]	08/2016	234.50 -	235.00	03/2019 -	-	.21	0
59	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]	01/2013	387.70 -	487.13	03/2018 -	-	25.65	0
	<u>East Central Railways</u>							
60	GARHWA ROAD-RAMNA - [N22000465]	03/2015	348.23 -	390.00	03/2021 -	03/2022	11.99	12
61	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]	04/2013	213.01 -	495.00	- -	10/2019	132.38	0
62	SAMASTIPUR-DARBANGHA - [N22000329]	05/2015	380.00 -	519.33	- -	03/2025	36.67	0
63	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]	01/1991	332.15 -	546.71	07/2014 -	-	64.60	0
64	GAYA-CHATRA (NL) - [N22000169]	04/2008	415.67 -	549.75	- -	-	32.26	0
65	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR [N22000475]	04/1998	180.82 -	726.31	- -	08/2020	301.68	0
66	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC - [N22000181]	04/2009	548.00 -	819.01	03/2020 -	03/2023	49.45	36
67	HAJIPUR - BACHAWARA - [N22000334]	05/2015	678.54 -	929.86	03/2019 -	12/2021	37.04	33
68	MOTIHARI-SITAMARHI (NL) - [N22000174]	04/2006	211.00 -	1,006.00	- -	-	376.78	0
69	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC), ECR [220100240]	04/1997	324.73 -	1,070.00	03/2012 -	11/2022	229.50	128
70	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM - [N22000473]	04/2016	731.64 -	1,185.73	03/2021 -	03/2024	62.06	36
71	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM - [N22000472]	04/2016	744.04 -	1,215.54	03/2021 -	03/2024	63.37	36
72	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIYAWAN-BIHARSHARIF, - [N22000476]	04/1991	329.39 -	1,483.14	- -	03/2022	350.27	0
73	CHHAPRA-MUZAFFARPUR (NL) - [N22000172]	04/2006	378.56 -	1,858.75	- -	03/2023	391.01	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
74	BIHTA-AURANGABAD (NL) - [N22000170]	04/2008	326.20 -	2,995.01	- -	03/2024	818.15	0
75	KODERMA-RANCHI VIA BARKAKANA (NL), ECR - [220100222]	03/1999	1,033.07 -	3,620.00	- -	03/2022	250.41	0
	<u>East Coast Railway</u>							
76	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE - [N22000380]	04/2015	701.61 -	810.02	11/2018 -	03/2024	15.45	64
77	SAMBALPUR-TALCHER DOUBLING - [N22000315]	03/2011	1,111.99 -	1,539.28	02/2019 -	12/2021	38.43	34
	<u>Eastern Railways</u>							
78	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]	04/2010	172.03 -	260.10	- -	03/2025	51.19	0
79	BAZAR SAU - AZIMGANJ JN. DOUBLING - [N22000302]	04/2012	255.64 -	272.20	- -	03/2022	6.48	0
80	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKAPUR NL - [N22000241]	04/2000	297.47 -	298.22	- -	03/2025	.25	0
81	MONIGRAM- NIMTITA - [N22000301]	04/2012	250.93 -	310.70	- -	03/2024	23.82	0
82	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY [N22000239]	04/2011	299.60 -	335.62	03/2017 -	03/2026	12.02	108
83	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL - [N22000229]	04/2010	365.17 -	439.30	03/2017 -	03/2025	20.30	96
84	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]	04/2010	494.54 -	494.59	03/2005 -	03/2025	.01	240
85	BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]	04/2011	175.80 -	495.10	- -	03/2022	181.63	0
86	BANDEL-BOINCHI 3RD LINE - [N22000221]	04/2011	288.35 -	502.48	- -	03/2021	74.26	0
87	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]	04/2010	365.17 -	527.54	- -	03/2025	44.46	0
88	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]	04/1987	406.99 -	545.70	03/2006 -	03/2025	34.08	228
89	PIRPAINTI-BHAGALPUR - [N22000222]	04/2011	261.38 -	565.00	- -	05/2019	116.16	0
90	HANSDIHA-GODDA NL - [N22000236]	04/2011	542.18 -	663.13	03/2020 -	03/2021	22.31	12
91	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]	04/2009	499.96 -	680.68	02/2012 -	03/2025	36.15	157
92	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]	04/2005	595.51 -	769.40	03/2017 -	03/2025	29.20	96
93	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]	04/2001	923.52 -	995.10	03/2016 -	03/2025	7.75	108

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
94	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR [N22000217]	04/2007	450.00 -	1,261.34	- -	03/2025	180.30	0
95	DEOGHAR - SULTANGANJ (INL), ER - [220100273]	04/2000	607.09 -	1,425.44	02/2013 -	03/2024	134.80	133
96	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]	04/2000	1,188.91 -	1,619.48	03/2019 12/2009	03/2025	36.22	72
97	PIRPAINTI-JASIDIH - [N22000219]	04/2013	915.98 -	2,137.81	03/2022 -	03/2025	133.39	36
<u>Indian Railway Construction Company Limited</u>								
98	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I [N22000489]	04/2013	3,055.00 -	3,055.15	09/2018 -	06/2022	.00	45
99	GEVRA ROAD PENDRA ROAD - [N22000488]	02/2014	2,288.00 -	4,970.11	03/2022 -	09/2023	117.23	18
<u>Metropolitan Rapid Transport Projects</u>								
100	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP [N22000028]	04/2006	495.74 -	734.01	06/2013 -	07/2022	48.06	109
101	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]	03/1996	495.44 -	2,980.41	03/2004 -	03/2022	501.57	216
102	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]	03/2000	1,049.69 -	3,404.92	12/2006 -	-	224.37	0
103	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE [N22000135]	03/2013	4,874.58 -	8,574.97	03/2016 -	-	75.91	0
<u>North Central Railway</u>								
104	ETAWAH-MAINPURI (NL),NCR - [220100318]	04/1997	120.00 -	346.00	12/2008 -	-	188.33	0
105	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]	04/2015	668.70 668.00	680.00	03/2020 -	-	1.69	0
106	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC) - [N22000148]	04/2011	2,912.96 -	3,845.60	03/2022 -	12/2024	32.02	33
<u>North East Frontier Railway</u>								
107	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]	04/2008	333.76 -	360.00	- -	-	7.86	0
108	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]	04/2010	241.52 -	373.87	- -	03/2022	54.80	0
109	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]	04/2010	221.42 -	380.00	- -	-	71.62	0
110	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]	04/2010	242.22 -	471.00	03/2020 -	-	94.45	0
111	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR - [220100135]	04/1983	297.32 -	614.00	03/2019 -	-	106.51	0
112	AGARTALA-AKHAURA NL - [N22000195]	04/2012	569.63 -	742.00	03/2020 -	03/2022	30.26	24
113	MURKONGSELEK-PASIGHAT NL - [N22000208]	04/2011	414.84 -	750.00	03/2020 -	-	80.79	0

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
114	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]	04/2011	314.00 -	800.00	03/2019 -	06/2021	154.78	27
115	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]	02/1999	380.60 -	1,090.60	04/2010 -	-	186.55	0
116	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]	09/2006	385.20 -	1,105.00	03/2019 -	03/2023	186.86	48
117	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]	04/1999	819.23 -	1,871.00	-	-	128.39	0
118	DIGARU-HOJAI (102 KM) - [N22000389]	04/2015	870.96 -	1,873.21	03/2021 -	03/2022	115.07	12
119	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM) - [N22000390]	04/2016	602.27 -	2,144.78	12/2021 -	09/2021	256.12	-3
120	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]	09/2006	532.87 -	2,145.00	03/2019 -	03/2024	302.54	60
121	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]	04/2015	2,232.32 -	2,950.00	03/2022 -	03/2023	32.15	12
122	NEW BG LINE FROM BYRNIHAT TO SHILLONG - [N22000205]	04/2010	906.46 -	4,083.02	03/2021 -	-	350.44	0
123	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR - [220100266]	04/2000	1,180.19 -	4,541.38	12/2008 -	09/2021	284.80	153
124	BHAIRABI SAIRONG, NL, NEFR - [N22000100]	04/2008	2,393.47 -	5,521.45	03/2014 -	03/2024	130.69	120
125	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]	04/2006	2,326.52 -	6,911.00	03/2015 -	03/2026	197.05	132
126	SEVOK RANGPO, NEFR - [N22000102]	04/2008	1,339.48 -	8,600.00	12/2015 -	12/2023	542.04	96
127	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]	04/2003	4,454.17 -	12,264.15	03/2011 -	12/2023	175.34	153
	<u>North Eastern Railway</u>							
128	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]	04/2014	182.92 -	197.73	-	-	8.10	0
129	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]	04/2016	213.00 -	213.35	04/2016 -	12/2021	.16	68
130	KICHHA-KHATIMA (NL) - NER - [220100317]	04/2003	142.45 -	228.40	-	-	60.34	0
131	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]	04/2017	150.00 -	341.66	04/2017 -	10/2022	127.77	66
132	CHHAPRA-BALLIA UP - [N22000134]	03/2013	295.00 -	580.00	01/2019 -	02/2022	96.61	37
133	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]	04/2017	622.50 427.00	590.00	04/2017 -	03/2021	-5.22	47
134	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]	03/2013	643.00 -	644.00	-	-	.16	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
135	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]	04/2016	602.50 -	714.34	- -	12/2023	18.56	0
136	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP [N22000131]	03/2007	243.78 -	895.00	12/2021 -	12/2021	267.13	0
137	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]	03/2013	307.00 -	1,409.09	- -	-	358.99	0
138	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]	04/2017	1,343.00 -	1,476.15	01/2018 -	-	9.91	0
139	ROSA-SITAPUR CANTT-BURHWAL DOUBLING - [N22000347]	03/2015	1,295.42 -	1,758.00	03/2022 -	03/2022	35.71	0
<u>North Western Railway</u>								
140	THIYAT HAMIRA-SANU - [N22000149]	04/2013	236.93 -	350.45	10/2018 -	01/2020	47.91	15
141	AJMER-BANGURGRAM - [N22000155]	04/2011	213.39 -	375.00	11/2019 -	03/2021	75.73	16
142	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]	04/2012	246.08 -	395.00	12/2019 -	03/2021	60.52	15
143	MAVLI JUNCTION-BARI SADRI, MM OF AJMER- CHITTSURGARH-UDAIPUR [N22000152]	04/2013	420.18 -	480.00	03/2020 -	09/2021	14.24	18
144	ALWAR-BANDIKUI DOUBLING - [N22000157]	04/2013	242.09 -	525.00	02/2019 -	02/2020	116.86	12
145	PHULERA - DIGANA DOUBLING - [N22000326]	05/2015	600.00 -	701.81	03/2020 -	10/2022	16.97	31
146	DAUSA-GANGAPUR CITY(NL),NWR - [220100184]	02/1997	410.08 -	860.41	02/2019 -	06/2022	109.82	40
147	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL [N22000330]	05/2015	873.71 -	2,215.27	- -	-	153.55	0
148	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]	04/2011	2,082.75 -	4,262.36	- -	-	104.65	0
<u>Northern Railway</u>								
149	HARIDWAR-LAKSAR - [N22000289]	04/2012	219.83 -	346.63	- -	-	57.68	0
150	GRADE SEPERATOR AT DAYABASTI - [N22000269]	04/1999	156.65 -	359.00	- -	03/2024	129.17	0
151	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]	04/2012	295.68 -	419.00	- -	09/2023	41.71	0
152	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL - [N22000274]	04/2007	336.91 -	791.39	- -	03/2023	134.90	0
153	QADIAN-BEAS - [N22000295]	04/2011	205.22 -	841.90	- -	03/2024	310.24	0
154	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]	03/2002	625.00 -	859.00	03/2016 -	-	37.44	0
155	ROHTAK-MEHAM HANSI - [N22000272]	04/2012	287.00 -	893.45	12/2011 -	06/2021	211.31	114
156	CHANDIGARH-BADDI - [N22000467]	04/2007	328.14 -	1,540.13	03/2023 -	03/2023	369.35	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
157	NANGALDAM-TALWARA(NL),NR - [220100188]	03/1981	450.00 -	2,200.00	07/2012 -	03/2024	388.89	140
	<u>Rail Vikas Nigam Ltd.</u>							
158	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]	04/2000	133.41 207.00	396.00	03/2009 03/2009	-	196.83	0
159	SECUNDERABAD-MAHABUBNAGAR DOUBLING - [N22000403]	04/2015	773.94 -	850.00	12/2024 -	12/2024	9.83	0
160	DHASA-JETALSAR (GC) - [N22000141]	04/2012	644.38 -	872.65	03/2021 -	-	35.42	0
161	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD [N22000213]	04/2012	632.68 -	950.00	03/2016 -	12/2021	50.15	69
162	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]	04/2015	943.60 -	1,000.00	03/2022 -	12/2024	5.98	33
163	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]	04/2011	927.01 -	1,400.00	03/2019 -	06/2022	51.02	39
164	AHMEDABAD-BOTAD (GC) - [N22000140]	04/2012	975.62 -	1,500.00	12/2021 -	12/2021	53.75	0
165	BANASPANI- JAKHPURA - DOUBLING - [N22000412]	03/2009	942.95 -	1,536.00	03/2019 -	06/2022	62.89	39
166	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION [N22000413]	03/2012	1,183.25 -	1,825.00	12/2020 -	12/2022	54.24	24
167	BINA - KOTA DOUBLING WITH RE - [N22000414]	04/2011	1,485.85 -	1,835.83	12/2020 -	12/2021	23.55	12
168	HARIDASPUR-PARADEEP(NL) - [220100285]	04/1996	1,185.64 -	1,844.47	12/2017 -	-	55.57	0
169	PALANPUR-SAMAKHAYALI (DL) - [N22000144]	04/2013	1,548.66 -	1,868.89	12/2021 -	03/2022	20.68	3
170	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]	03/2006	948.04 -	2,009.00	03/2020 -	12/2021	111.91	21
171	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]	04/1998	1,202.70 -	2,440.53	02/2015 -	06/2022	102.92	88
172	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]	03/2009	713.48 -	2,725.00	03/2020 -	12/2021	281.93	21
173	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]	04/2010	2,298.42 -	2,733.86	03/2014 -	12/2025	18.95	141
174	HOSPET-HUBLI-LONDA-VASCODAGAMA DL - [N22000297]	04/2010	2,127.00 -	3,000.00	03/2023 -	12/2022	41.04	-3
175	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]	01/1991	2,335.67 -	3,327.72	12/2024 -	12/2026	42.47	24
176	VIJAYWADA-GUDUGOLANU-BHIMAVARAM- NARSAPUR DL (221 KM) - [N22000313]	03/2012	1,503.71 -	3,377.00	03/2020 -	03/2022	124.58	24
177	VIJAYAWADA-GUDUR - [N22000369]	04/2015	3,246.26 -	3,548.68	12/2023 -	12/2023	9.32	0
178	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]	04/2010	3,951.98 -	4,259.48	03/2016 -	03/2025	7.78	108

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
179	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111	04/2010	2,913.51 -	4,639.00	03/2016 -	03/2025	59.22	108
180	BHANUPALI-BILASPUR BERI NL - [N22000273	04/2008	2,966.99 -	6,753.42	12/2026 -	12/2025	127.62	-12
181	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406	04/2011	16,216.00 -	22,716.11	12/2024 -	03/2025	40.08	3
	<u>Railway Electrification</u>							
182	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094	02/2008	171.10 -	275.08	03/2012 -	-	60.77	0
	<u>South Central Railway</u>							
183	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432	04/2017	119.73 185.00	449.39	03/2022 -	12/2022	275.34	9
184	BHADRACHALAM ROAD-SATTUPALLI - [N22000287	04/2010	704.31 -	927.94	03/2020 -	11/2021	31.75	20
185	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192	03/1996	164.36 -	1,050.00	02/2009 -	-	538.84	0
186	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION [N22000261	04/2012	1,856.95 -	1,952.68	03/2023 -	03/2024	5.16	12
187	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265	12/2001	1,045.20 -	2,120.16	03/2009 -	03/2024	102.85	180
188	NADIKUDE-SRI KALAHASTI - [N22000286	04/2011	2,288.70 -	2,643.25	03/2021 -	03/2024	15.49	36
189	MANUGURU-RAMAGUNDAM - [N22000259	04/2013	1,112.00 -	2,911.84	- -	-	161.86	0
190	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288	04/2008	2,132.77 -	3,037.95	03/2014 -	03/2027	42.44	156
191	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205	04/1997	1,723.00 1.00	3,421.35	03/2000 -	03/2023	98.57	276
192	GUNTUR-GUNTAKAL - [N22000368	04/2016	3,631.00 -	3,887.48	03/2022 -	03/2024	7.06	24
	<u>South East Central Railway</u>							
193	ANUPPUR-KATNI - [N22000485	04/2015	1,370.00 -	1,370.94	12/2021 -	12/2023	.07	24
194	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324	04/2005	383.79 -	1,511.50	- -	08/2020	293.84	0
195	GONDIA-JABALPUR(GC),(SECR) - [220100186	02/1997	511.86 -	2,005.25	04/2020 -	03/2021	291.76	11
	<u>South Eastern Railway</u>							
196	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION [N22000162	04/2010	149.90 -	230.00	03/2015 -	-	53.44	0
197	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165	04/2012	258.20 -	358.68	12/2018 -	08/2021	38.92	32
198	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323	04/2012	148.77 -	377.00	12/2016 -	08/2020	153.41	44

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
199	BOWAICHANDI-ARAMBAGH - [N22000159]	04/2010	267.37 -	620.00	- -	03/2025	131.89	0
200	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]	04/2010	651.00 -	1,009.00	03/2015 -	03/2025	54.99	120
201	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]	04/1974	393.46 154.30	1,026.00	03/2007 03/2007	-	160.76	0
202	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]	11/2015	969.83 -	1,312.96	03/2020 -	02/2022	35.38	23
203	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL [N22000402]	04/1998	1,027.40 -	2,373.00	03/2003 -	03/2030	130.97	324
	<u>South Western Railway</u>							
204	TORANAGALLU-RANJITPURA DL - [N22000298]	04/2011	146.75 -	167.50	- -	12/2023	14.14	0
205	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]	04/2013	296.00 -	466.65	- -	12/2023	57.65	0
206	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL [N22000276]	04/2013	558.00 -	692.00	- -	12/2023	24.01	0
207	ARSIKERE-TUMKUR - [N22000332]	03/2015	578.00 -	760.00	03/2020 -	11/2021	31.49	20
208	YELAHANKA-PENUKONDA - [N22000328]	05/2015	860.43 -	1,147.00	03/2020 -	09/2021	33.31	18
209	BAGALKOT-KUDACHI NL - [N22000258]	04/2010	986.30 -	1,530.09	03/2016 -	12/2026	55.13	129
210	HUBLI- CHIKJAJUR - [N22000325]	03/2015	1,156.94 -	1,800.59	03/2020 -	03/2023	55.63	36
211	HOTGI-KUDGI-GADAG - [N22000333]	03/2015	1,614.59 -	1,878.00	03/2019 -	03/2024	16.31	60
212	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]	04/1996	1,382.78 -	1,960.00	03/2002 -	03/2024	41.74	264
213	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]	04/2011	1,801.01 -	2,161.36	- -	12/2023	20.01	0
214	RAYADURGA-TUMKUR NL - [N22000279]	04/2007	2,062.30 -	2,432.50	- -	12/2025	17.95	0
215	HUBLI-ANKOLA(NL),SWR - [220100193]	04/1997	2,315.00 -	5,174.30	- -	12/2024	123.51	0
	<u>Southern Railway</u>							
216	ERNAKULAM-KUMBALAM - [N22000204]	04/2010	189.24 -	275.21	- -	-	45.43	0
217	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]	10/2013	187.26 -	327.00	04/2014 -	-	74.62	0
218	KUMBALAM-TURAVUR - [N22000191]	04/2011	252.96 -	369.55	- -	-	46.09	0
219	KURUPPANTHARA-CHINGAVANAM - [N22000190]	04/2007	270.14 -	457.08	- -	12/2021	69.20	0
220	ATTIPPATTU PUTTUR - [N22000184]	04/2008	151.84 -	527.37	02/2019 -	-	247.32	0

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
221	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187	04/1999	198.68 -	559.95	-	03/2024	181.84	0
222	ERODE-PALANI - [N22000199	04/2008	288.57 -	603.23	-	-	109.04	0
223	MADURAI-BODINAYAKKANUR - [N22000201	04/2008	164.41 -	608.13	-	12/2021	269.89	0
224	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186	04/2013	839.00 -	839.01	-	-	.00	0
225	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441	02/1996	268.87 -	950.00	03/2005	09/2021	253.33	198
226	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF - [N22000202	04/2007	931.98 -	1,121.00	-	08/2021	20.28	0
227	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185	04/2008	523.52	1,205.00	-	03/2024	130.17	0
228	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400	02/2015	1,000.00 -	1,246.00	-	-	24.60	0
229	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451	02/2015	760.00 -	1,536.00	03/2020	06/2022	102.11	27
230	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262	09/1995	303.98 -	1,720.00	03/2020	03/2025	465.83	60
231	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215	04/2011	120.70 -	2,172.16	03/2019	12/2027	1,699.64	105
232	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252	10/1998	1,566.00 -	2,815.62	-	-	79.80	0
233	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' - AGASTIYAMPALLI - [N22000079	09/2007	724.69 -	2,950.00	02/2019	03/2025	307.07	73
234	TIDIVANAM-NAGARI (NL) - [N22000085	09/2006	582.83 -	3,150.00	-	12/2025	440.47	0
<u>West Central Railway</u>								
235	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351	12/2015	1,763.93 -	2,470.00	03/2020	03/2024	40.03	48
236	RAMGANJMUHDI-BHOPAL (NL),WCR - [220100314	04/2001	424.60 -	2,909.99	03/2021	03/2024	585.35	36
237	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232	09/1998	247.66 -	8,248.50	05/2008	03/2025	3,230.57	202
<u>Western Railway</u>								
238	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125	04/2006	117.36 196.95	202.35	03/2011	-	72.42	0
239	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM - [N22000494	04/2017	691.84 -	890.62	03/2020	09/2021	28.73	18
240	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION - [N22000487	02/1991	551.51 -	890.76	03/2019	10/2021	61.51	31

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
241	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC) - [N22000143	04/1994	320.66 -	1,378.11	03/2019 -	03/2023	329.77	48
242	VIRAMGAM-SAMAKHIALI (DL) - [N22000145	04/2011	1,037.15 -	1,383.69	03/2021 -	12/2022	33.41	21
243	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR) - [N22000121	04/2008	829.74 -	1,886.76	03/2020 -	03/2024	127.39	48
244	RATLAM-MHOW-KHANDWA-AKOLA (GC) - [N22000120	04/2008	3,503.69 -	6,171.08	03/2022 -	03/2024	76.13	24
	Total		1,94,075.60 -	3,60,289.33				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>							
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>							
245	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872	03/2018	166.21 -	173.41	08/2018 -	09/2021	4.33	37
246	JALGAON TO NANDURA - [N24001088	03/2018	177.84 177.00	177.84	12/2019 -	-	.00	0
247	CHIKALI TO DHAD - [N24001061	03/2018	189.46 189.00	189.46	12/2019 -	-	.00	0
248	WADIGODRI TO DHANGRIIMPRI - [N24001063	03/2018	194.23 194.00	194.23	02/2020 -	-	.00	0
249	KHAMGAON TO SHEGAON - [N24001009	02/2017	203.21 203.00	203.21	05/2019 -	-	.00	0
250	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140	11/2016	215.16 215.00	215.16	09/2019 -	10/2019	.00	1
251	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064	03/2018	217.14 217.00	217.14	02/2020 -	-	.00	0
252	MANGRUPHIR TO MAHAN - [N24001087	03/2018	222.13 222.00	222.13	11/2019 -	-	.00	0
253	KUNDRAL TO WAZAR - [N24001077	01/2018	225.25 225.00	225.25	12/2019 -	-	.00	0
254	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS - [N24000890	03/2018	217.22 -	226.88	08/2018 -	09/2021	4.45	37
255	PALPHATA TO PHULAMBARI - [N24001060	03/2018	227.19 227.00	227.19	12/2019 -	-	.00	0
256	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3 - [N24000934	03/2018	228.32 -	228.32	08/2018 -	12/2021	.00	40
257	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K - [N24001307	01/2017	197.67 -	236.18	12/2022 -	12/2022	19.48	0
258	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00 - [N24000820	11/2017	237.80 -	238.00	11/2019 -	10/2021	.08	23
259	PARBHANI TO GANGKHED - [N24001065	03/2018	238.19 238.00	238.19	12/2019 -	-	.00	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
260	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141	03/2016	240.30 240.00	240.30	01/2020 -	-	.00	0
261	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239	03/2018	240.38 -	240.38	06/2019 -	-	.00	0
262	NAIGAONBANDI TO MANGRULPIR - [N24001094	12/2017	244.04 244.00	244.04	03/2019 -	-	.00	0
263	SANGOLA TO JATH - [N24001052	01/2018	257.38 257.00	257.38	12/2019 -	-	.00	0
264	TALEGAON TO GONAPUR - [N24001096	01/2018	264.41 264.00	264.41	03/2019 -	-	.00	0
265	OMREGA TO AUSA - [N24001067	03/2018	272.04 272.00	272.04	12/2019 -	-	.00	0
266	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG - [N24000937	03/2018	289.67 290.00	289.67	08/2018 -	11/2021	.00	39
267	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259	03/2015	280.16 -	290.59	-	-	3.72	0
268	BHOKAR TO SARSAM - [N24001128	02/2017	295.09 -	295.99	07/2019 -	-	.31	0
269	KOTHARI TO DHANORA - [N24001073	09/2018	301.38 301.00	301.38	08/2020 -	-	.00	0
270	MALEGAON TO RISOD - [N24001089	02/2018	303.24 303.00	303.24	12/2019 -	-	.00	0
271	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH- - [N24001161	12/2017	297.30 -	318.28	01/2019 -	-	7.06	0
272	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24001181	08/2010	186.96 -	322.24	09/2014 -	12/2021	72.36	87
273	MEHKAR TO CHIKALI - [N24001011	02/2017	322.48 322.00	322.48	05/2019 -	-	.00	0
274	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD - [N24000308	08/2010	193.69 -	327.92	10/2010 -	12/2021	69.30	134
275	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062	03/2018	336.21 336.00	336.21	12/2019 -	-	.00	0
276	LATUR TO PANGAON - [N24001066	03/2018	336.47 336.00	336.47	12/2019 -	-	.00	0
277	MORSHI TO ACHALPUR - [N24001015	01/2017	341.16 341.00	341.16	06/2019 -	-	.00	0
278	OSMANNAGAR TO KUNDRAI - [N24001075	09/2017	344.25 344.00	344.25	08/2020 -	-	.00	0
279	KARAD TO VITA - [N24001049	01/2018	344.85 245.00	344.85	12/2019 -	-	.00	0
280	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260	01/2014	255.75 348.00	348.43	09/2017 -	-	36.24	0

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
281	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH0.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928	10/2015	333.21 -	353.43	12/2015 -	-	6.07	0
282	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531	01/1991	319.68 -	369.77	- -	-	15.67	0
283	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929	09/2016	372.68 -	372.68	02/2017 -	-	.00	0
284	SHEGAON TO DEORI PHATA - [N24001010	02/2017	373.10 373.00	373.10	05/2019 -	-	.00	0
285	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI) - [N24000415	08/2010	195.04 -	377.99	10/2010 -	12/2021	93.80	134
286	PANCHARAL TO MANDANGHAR - [N24001107	07/2018	381.08 302.00	381.08	05/2020 -	-	.00	0
287	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965	01/2016	386.09 -	386.09	05/2016 -	-	.00	0
288	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162	03/2018	325.86 -	386.41	10/2018 -	-	18.58	0
289	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM - [N24000392	11/2010	268.08 -	390.73	05/2017 -	05/2022	45.75	60
290	DIGRAS DARWAH KARANJA - [N24001013	01/2017	391.06 391.00	391.06	06/2019 -	-	.00	0
291	CHIKLI TO TAKARKHED - [N24001083	03/2018	393.10 393.00	393.10	12/2019 -	-	.00	0
292	SELDOH TO PANVAR - [N24001097	07/2018	404.33 404.00	404.33	05/2020 -	-	.00	0
293	KARAD PATAN CHIPLUN GUHAGAR - [N24001057	02/2017	407.19 407.00	407.19	06/2019 -	-	.00	0
294	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P - [N24000963	01/2018	418.03 -	418.03	08/2018 -	08/2021	.00	36
295	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056	02/2017	422.02 422.00	422.02	07/2019 -	-	.00	0
296	ARDHAPUR TO HIMAYATNAGAR - [N24001079	12/2017	426.06 426.00	426.06	06/2020 -	-	.00	0
297	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933	02/2017	429.43 -	429.43	11/2017 -	-	.00	0
298	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782	03/2018	460.73 -	461.00	- -	-	.06	0
299	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA - [N24001091	03/2016	536.65 356.00	536.65	12/2019 -	12/2021	.00	24

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
300	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V - [N24001219	01/2016	476.20 544.00	544.00	09/2016 -	12/2021	14.24	63
301	CHIKALI TO KHAMGAON - [N24001012	02/2017	548.03 548.00	548.03	06/2019 -	-	.00	0
302	BHOGAN KHURD TO KASHEDI - [N24001132	09/2017	743.21 743.00	743.21	06/2021 -	-	.00	0
303	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391	11/2015	889.24 -	904.82	- -	-	1.75	0
304	PARSHURAM GHAT TO ARAWALI - [N24001133	04/2016	983.14 983.00	983.14	12/2019 -	-	.00	0
305	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN - [N24000306	11/2010	624.41 -	992.67	03/2011 -	12/2021	58.98	129
306	REHABILITATION AND UPGRADATION OF KARNATATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O - [N24000940	03/2016	995.09 995.00	995.09	05/2016 -	09/2021	.00	64
307	KANTE TO WAKED - [N24001134	03/2016	1,230.02 1,230.00	1,230.02	11/2019 -	-	.00	0
308	KALMATH TO ZARAP - [N24001137	09/2016	1,338.13 1,338.00	1,338.13	03/2020 -	-	.00	0
309	VADPALE TO BHOGAN KHURD - [N24001115	01/2017	1,598.47 1,560.00	1,598.47	11/2019 -	-	.00	0
310	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194	09/2011	1,979.00 -	2,036.90	- -	-	2.93	0
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>							
311	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690	01/2017	198.22 -	252.05	04/2017 -	03/2022	27.16	59
312	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679	02/2017	195.23 -	252.79	04/2017 -	03/2022	29.48	59
313	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680	02/2017	203.36 -	263.31	04/2017 -	03/2022	29.48	59
314	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686	03/2016	373.07 -	387.00	08/2016 -	05/2021	3.73	57
315	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695	04/2017	388.00 -	447.37	10/2017 -	-	15.30	0
	<u>National Highways Authority Of India</u>							
316	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049	12/2003	160.00 -	167.98	05/2008 -	06/2019	4.99	133
317	NALBARI T BIJNI (AS-7) - [N24000048	12/2003	208.00 -	230.00	04/2008 -	02/2021	10.58	154
318	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280	12/2003	155.04 -	255.23	11/2008 -	-	64.62	0

Costing Rs. 150 Crore and above					(August 2021)			
					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
319	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]	01/2018	273.46 -	276.17	- -	-	.99	0
320	SIX LANNING FROM EXISTING KM 494.410(DSIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DSIGN CHAINAGE - [N24000631]	11/2016	290.73 -	315.00	- -	-	8.35	0
321	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]	08/2015	322.09 -	322.09	04/2018 -	-	.00	0
322	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]	08/2016	323.72 -	336.60	08/2018 -	-	3.98	0
323	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]	12/2003	199.81 -	340.14	04/2009 -	-	70.23	0
324	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]	12/2003	217.61 -	360.84	04/2010 -	07/2019	65.82	111
325	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]	05/2016	364.56 -	392.00	- -	08/2021	7.53	0
326	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 [N24000360]	04/2014	351.34 -	417.68	01/2016 -	-	18.88	0
327	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 [240106279]	12/2003	167.64 -	435.78	11/2008 -	-	159.95	0
328	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]	07/2012	291.36 -	469.31	01/2014 -	-	61.08	0
329	INDORE-DEWAS(NH-3) - [N24000159]	11/2010	325.00 -	475.00	05/2013 -	-	46.15	0
330	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- [N24000594]	07/2016	458.03 -	486.00	- -	-	6.11	0
331	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]	03/2018	496.20 -	537.17	- -	-	8.26	0
332	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]	05/2011	511.54 -	591.00	11/2013 -	-	15.53	0
333	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]	12/2003	280.00 -	612.58	02/2009 -	-	118.78	0
334	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI [N24000367]	04/2014	495.78 -	627.93	01/2016 -	-	26.66	0
335	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR [N24000522]	08/2015	516.13 -	649.27	04/2018 -	-	25.80	0
336	HARANGAJO TO MAIBANG, NH-54 - [N24000062]	12/2003	196.00 -	655.17	07/2009 -	-	234.27	0
337	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]	01/1991	642.41 -	681.67	- -	-	6.11	0
338	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 [N24000638]	11/2012	605.84 -	722.46	07/2018 -	-	19.25	0
339	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN - [N24001306]	10/2020	724.60 -	724.60	03/2023 -	03/2023	.00	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
340	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665	03/2017	672.89 -	736.01	03/2020 -	-	9.38	0
341	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199	10/2019	743.88 -	743.89	- -	12/2021	.00	0
342	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (- [N24000435	10/2015	531.13 -	744.73	05/2018 -	03/2022	40.22	46
343	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662	03/2017	754.54 -	756.27	03/2020 -	09/2022	.23	30
344	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853	03/2018	642.13 -	807.00	- -	-	25.68	0
345	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482	08/2015	814.04 -	825.17	- -	10/2021	1.37	0
346	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212	12/2017	656.98 -	840.00	- -	11/2022	27.86	0
347	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214	12/2017	217.96 -	884.00	- -	10/2022	305.58	0
348	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841	03/2018	795.50 -	922.64	- -	-	15.98	0
349	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691	04/2017	894.00 -	929.32	04/2020 -	12/2021	3.95	20
350	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839	03/2018	634.70 -	931.21	- -	-	46.72	0
351	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459	06/2015	845.24 -	941.00	- -	01/2020	11.33	0
352	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656	03/2017	744.64 -	982.00	03/2020 -	-	31.88	0
353	MEERUT-BULANDSHAHR - [N24000539	01/2016	683.24 -	987.94	- -	-	44.60	0
354	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521	08/2015	854.80 -	1,038.56	- -	-	21.50	0
355	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658	03/2017	988.34 -	1,043.28	03/2020 -	-	5.56	0
356	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657	03/2017	1,030.44 -	1,065.51	03/2020 -	-	3.40	0
357	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659	03/2017	1,059.73 -	1,071.00	03/2017 -	-	1.06	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
358	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829	03/2018	1,016.92 -	1,071.00	- -	01/2022	5.32	0
359	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623	09/2016	1,100.19 -	1,145.31	- -	-	4.10	0
360	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661	03/2017	1,098.06 -	1,160.64	03/2020 -	-	5.70	0
361	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674	03/2017	831.58 -	1,177.00	03/2020 -	-	41.54	0
362	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507	12/2015	1,167.45 -	1,182.94	- -	-	1.33	0
363	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668	03/2017	1,041.62 -	1,187.10	03/2020 -	-	13.97	0
364	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793	03/2018	925.40 -	1,197.00	- -	-	29.35	0
365	4-LANNING OF THALSERRY -MAHE BYPASS - [N24000704	09/2017	1,124.11 -	1,232.76	09/2017 -	-	9.67	0
366	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814	03/2018	1,029.96 -	1,261.05	- -	03/2021	22.44	0
367	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831	03/2018	1,294.47 -	1,296.00	- -	-	.12	0
368	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785	02/2018	1,166.26 -	1,296.93	- -	01/2022	11.20	0
369	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654	03/2017	1,184.71 -	1,310.00	03/2020 -	-	10.58	0
370	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800	03/2018	1,120.57 -	1,332.00	- -	-	18.87	0
371	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM - [N24000671	03/2017	1,288.07 -	1,420.00	03/2020 -	-	10.24	0
372	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675	03/2017	993.16 -	1,434.00	03/2020 -	-	44.39	0
373	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801	02/2018	1,052.21 -	1,449.00	- -	01/2021	37.71	0
374	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233	04/2014	1,266.60 -	1,544.00	09/2016 -	-	21.90	0
375	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600	08/2016	1,388.34 -	1,588.29	09/2019 -	-	14.40	0

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
376	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]	05/2013	1,055.00	1,601.77	11/2015	-	51.83	0
377	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]	09/2016	1,239.82	1,727.66	-	-	39.35	0
378	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]	02/2018	1,424.77	1,853.42	-	-	30.09	0
379	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]	06/2017	1,958.88	1,993.81	06/2020	-	1.78	0
380	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]	03/2018	2,065.96	2,169.00	-	-	4.99	0
381	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]	08/2016	1,169.61	2,280.00	-	-	94.94	0
382	SIX LANING OF BARWA ADDA-PANAGARH - [N24000515]	04/2014	1,665.00	2,360.65	-	-	41.78	0
383	SIX LANING OF BANGALORE - NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]	02/2018	1,995.34	2,400.00	-	11/2021	20.28	0
384	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]	03/2017	2,064.99	2,447.00	03/2020	-	18.50	0
385	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]	02/2018	2,177.80	2,450.00	-	-	12.50	0
386	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]	03/2018	1,532.62	2,499.00	03/2021	04/2021	63.05	1
387	NASHRI- CHANANI - [N24000162]	05/2011	2,159.00	2,519.00	06/2015	-	16.67	0
388	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 208.300 KM [PACKAGE-IV] - [N24000551]	03/2016	1,587.49	2,982.00	04/2019	-	87.84	0
389	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]	09/2011	2,848.00	3,379.45	03/2014	12/2022	18.66	105
	Total		96,285.50	1,14,030.43				
	<u>STEEL</u>							
	<u>Rastrya Ispat Nigam Limited</u>							
390	FORGED WHEEL PLANT - [N12000116]	04/2014	1,682.85	2,100.00	09/2018	09/2021	24.79	36
	Total		1,682.85	2,100.00				
	<u>URBAN DEVELOPMENT</u>							
	<u>Ahmedabad Metro Rail</u>							

Costing Rs. 150 Crore and above

(August 2021)

					Date of Commissioning (Month/Year)			
Sl.No	Project	Date of Approval (Month/Year)	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs.crore)	Original / Revised	Anticipated	Cost Overruns (%)	T.O.R.s (in months)
1	2	3	4	5	6	7	8	9
391	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122 <u>Kochi Metro Rail Corporation Ltd</u>	11/2014	10,773.00 -	12,787.00	12/2018 -	08/2022	18.69	44
392	KOCHI METRO RAIL PROJECT - [N28000081 <u>Mumbai Metro Rail Corporation Ltd</u>	07/2012	5,181.79 -	6,218.14	07/2017 -	-	20.00	0
393	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ) - [N28000086 <u>National Building Construcion Corporation Ltd</u>	07/2013	23,136.00 -	33,406.00	03/2020 -	03/2023	44.39	36
394	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080 Total	06/2012	4,264.00 -	4,720.73	11/2019 -	-	10.71	0
			43,354.79 -	57,131.87				
	WATER RESOURCES							
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>							
395	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR [N30000037	12/2014	225.77 -	398.90	03/2020 -	03/2021	76.68	12
396	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027 <u>Uttar Pradesh Jal Nigam</u>	10/2017	254.13 -	413.29	09/2020 -	-	62.63	0
397	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH - [N30000021	01/2019	231.79 -	234.03	12/2021 -	12/2021	.97	0
398	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH - [N30000024	02/2019	681.78 -	690.71	06/2022 -	06/2022	1.31	0
	Total		1,393.47 -	1,736.93				
	Grand Total		4,47,610.77	6,68,756.85				

List of projects original without Date of Commissioning

Costing Rs.		150 Crore and above				(August 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
1	<u>COAL</u> <u>Singareni Colliers Company Limited</u> SRP OC-II EXPANSION PROJECT - [N06000173]SCCL, TELANGANA Total	11/2016	272.73 - 272.73 -	272.73 - 272.73 -	153.75 - 153.75 -	- - - -	03/2022 - - -	- - - -	2/6 - 2/6 -
2	<u>HEALTH AND FAMILY WELFARE</u> <u>Hospital Services Consultancy Corporation Ltd</u> HOSPITAL AND TEACHING- AIIMS GUNTUR - [N21000020]HSCC, ANDHRA PRADESH	03/2018	601.02 -	601.02 -	453.44 -	- -	09/2021 -	- -	0/0 -
3	HOSPITAL AND TEACHING- AIIMS NAGPUR - [N21000023]HSCC, MAHARASHTRA	03/2018	582.99 -	582.99 -	522.60 -	- -	09/2021 -	- -	0/0 -
4	HOSPITAL AND TEACHING- AIIMS KALYANI - [N21000024]HSCC, WEST BENGAL	04/2018	651.99 -	651.99 -	568.10 -	- -	09/2021 -	- -	0/0 -
5	GERIATRICS BLOCK- AIIMS DLEHI - [N21000019]HSCC, DELHI Total	12/2017	156.56 - 1,992.56 -	190.34 - 2,026.34 -	156.14 - 1,700.28 -	- - - -	11/2021 - - -	- - - -	0/0 - 0/0 -
6	<u>RAILWAYS</u> <u>East Central Railways</u> CHHAPRA-MUZAFFARPUR (NL) - [N22000172]ECR, BIHAR	04/2006	378.56 -	1,858.75 -	386.36 -	- -	03/2023 -	- -	0/0 -
7	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC) - [N22000180]ECR, BIHAR	04/2004	372.14 1,470.50	1,470.50 -	1,377.83 -	- -	03/2023 -	- -	0/0 -
8	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR) - [220100257]ECR, BIHAR	04/1997	162.87 614.45	614.45 -	352.16 -	- -	12/2023 -	- -	0/0 -
9	BIHTA-AURANGABAD (NL) - [N22000170]ECR, BIHAR	04/2008	326.20 -	2,995.01 -	2.04 -	- -	03/2024 -	- -	0/0 -
10	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL) - [N22000176]ECR, BIHAR	04/2008	228.05 -	228.05 -	1.53 -	- -	03/2024 -	- -	0/0 -
11	SAMASTIPUR-DARBANGHA - [N22000329]ECR, BIHAR	05/2015	380.00 -	519.33 -	294.63 -	- -	03/2025 -	- -	0/0 -
12	<u>Eastern Railways</u> BOINCHI-SHAKTIGARH 3RD LINE - [N22000238]ER, MULTI STATE	04/2011	175.80 -	495.10 -	299.53 -	- -	03/2022 -	- -	0/0 -
13	BAZAR SAU -AZIMGANJ JN. DOUBLING - [N22000302]ER, WEST BENGAL	04/2012	255.64 -	272.20 -	283.69 -	- -	03/2022 -	- -	0/0 -
14	MONIGRAM- NIMTITA - [N22000301]ER, MULTI STATE	04/2012	250.93 -	310.70 -	377.47 -	- -	03/2024 -	- -	0/0 -

Costing Rs.			150 Crore and above			(August 2021)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
15	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR - [N22000217]ER,MULTI STATE	04/2007	450.00	1,261.34	-	-	03/2025	-	0/0
16	HANSNABAD-HINGALGANJ NEW BG LINE - [N22000218]ER,MULTI STATE	04/2010	172.03	260.10	11.77	-	03/2025	-	0/0
17	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE - [N22000227]ER,MULTI STATE	04/2010	174.56	174.56	71.43	-	03/2025	-	0/0
18	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT - [N22000234]ER,MULTI STATE	04/2007	450.55	250.55	20.11	-	03/2025	-	0/0
19	TARAKESHWAR-MAGRA NEW BG LINE - [N22000235]ER,MULTI STATE	04/2010	365.17	527.54	1.76	-	03/2025	-	0/0
20	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL - [N22000241]ER,MULTI STATE	04/2000	297.47	298.22	36.13	-	03/2025	-	0/0
21	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA - [N22000242]ER,MULTI STATE	04/2003	337.96	336.96	40.65	-	03/2025	-	0/0
22	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES - [N22000249]ER,MULTI STATE	04/2011	166.89	166.89	.02	-	03/2025	-	0/0
Metropolitan Rapid Transport Projects									
23	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR - [N22000212]MRTP, WEST BENGAL	04/2009	573.78	268.52	.03	-	03/2025	-	0/0
North Eastern Railway									
24	BURHWAL - GONDA - 3RD RUNNING LINE. - [N22000468]NER,UTTAR PRADESH	04/2016	602.50	714.34	88.04	-	12/2023	-	0/0
Northern Railway									
25	DEOBAND (MUZAFFARNAGAR)-ROORKEE NL - [N22000274]NR,MULTI STATE	04/2007	336.91	791.39	574.59	-	03/2023	-	0/0
26	UNCHAHAR-AMETHI - [N22000294]NR,UTTAR PRADESH	04/2012	1,229.00	489.64	105.51	-	03/2023	-	0/0
27	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE - [N22000281]NR,DELHI	04/2012	295.68	419.00	160.58	-	09/2023	-	0/0
28	GRADE SEPERATOR AT DAYABASTI - [N22000269]NR,DELHI	04/1999	156.65	359.00	111.51	-	03/2024	-	0/0
29	QADIAN-BEAS - [N22000295]NR,PUNJAB	04/2011	205.22	841.90	1.73	-	03/2024	-	0/0
South Eastern Railway									
30	BOWAICHANDI-ARAMBAGH - [N22000159]SER, WEST BENGAL	04/2010	267.37	620.00	40.99	-	03/2025	-	0/0
South Western Railway									
31	TUMKUR-CHITRADURGA-DAVENGERE NL - [N22000256]SWR, KARNATAKA	04/2011	1,801.01	2,161.36	76.42	-	12/2023	-	0/0

Costing Rs. 150 Crore and above						(August 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
32	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL - [N22000276]SWR,KARNATAKA	04/2013	558.00	692.00	-	-	12/2023	-	0/0
33	SRINIVASA-PURA-MADANAPALLI NL - [N22000277]SWR,MULTI STATE	04/2013	296.00	466.65	-	-	12/2023	-	0/0
34	TORANAGALLU-RANJITPURA DL - [N22000298]SWR,KARNATAKA	04/2011	146.75	167.50	.34	-	12/2023	-	0/0
35	CHIKBALLA-PUR-GOWRIBIDANUR NL - [N22000300]SWR,KARNATAKA	04/2013	327.25	327.25	-	-	12/2023	-	0/0
36	HUBLI-ANKOLA(NL),SWR - [220100193]SWR,KARNATAKA	04/1997	2,315.00	5,174.30	157.01	-	12/2024	-	0/0
37	RAYADURGA-TUMKUR NL - [N22000279]SWR,MULTI STATE	04/2007	2,062.30	2,432.50	1,126.08	-	12/2025	-	2/2
38	WHITE FIELD-KOLAR NL - [N22000280]SWR,KARNATAKA	04/2011	348.85	348.85	.36	-	12/2025	-	0/0
<u>Southern Railway</u>									
39	KURUPPANTHARA-CHINGAVANAM - [N22000190]SR,MULTI STATE	04/2007	270.14	457.08	-	-	12/2021	-	0/0
40	CHENNAI-CUDDALORE VIA MAMALLAPURAM - [N22000185]SR,MULTI STATE	04/2008	523.52	1,205.00	2.28	-	03/2024	-	0/0
41	CUDDALORE-SALEM VIA VRIDDHACHALAM GC - [N22000187]SR,TAMIL NADU	04/1999	198.68	559.95	273.32	-	03/2024	-	0/0
42	TIDIVANAM-NAGARI (NL) - [N22000085]SR,TAMIL NADU	09/2006	582.83	3,150.00	239.49	-	12/2025	-	0/0
Total			18,042.26	33,686.48	6,515.39				2/2
<u>ROAD TRANSPORT AND HIGHWAYS</u>									
<u>Ministry Of Road Transport And Highways (State Pwds)</u>									
43	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230 - [N24001210]MoRTH,UTTAR PRADESH	03/2018	306.59	306.59	168.16	-	09/2021	-	0/0
44	R AND U OF KHUTAR -LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS - [N24000877]MoRTH,UTTAR PRADESH	11/2016	326.99	326.99	122.02	-	12/2021	-	0/0
<u>National Highways And Infrastructure Development Corporation Ltd.</u>									
45	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX - [N24000976]NHIDCL,ARUNACHAL PRADESH	10/2015	210.50	210.50	145.07	-	10/2021	-	4/4
46	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52 - [N24000431]NHIDCL,ASSAM	01/1991	520.01	520.01	189.59	-	12/2021	-	2/4

Costing Rs. 150 Crore and above						(August 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
47	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST - [N24001196]NHIDCL,ASSAM	03/2017	1,049.51 -	1,049.51	143.02	- -	12/2021	-	2/4
48	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE - [N24000902]NHIDCL,ASSAM <u>National Highways Authority Of India</u>	10/2017	818.00 -	818.00	287.52	- -	03/2023	-	1/4
49	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN - [N24000709]NHAI,MADHYA PRADESH	12/2017	950.27 -	950.27	266.64	- -	08/2021	-	3/4
50	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS - [N24000735]NHAI,ODISHA	01/2018	564.66 -	564.66	341.88	- -	08/2021	-	0/1
51	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS - [N24000572]NHAI,GUJARAT	05/2016	364.56 -	392.00	353.42	- -	08/2021	-	0/0
52	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104) - [N24000729]NHAI,MAHARASHTRA	01/2018	607.00 -	607.00	510.71	- -	08/2021	-	0/1
53	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG - [N24000734]NHAI,ODISHA	01/2018	614.48 -	614.48	277.00	- -	08/2021	-	0/0
54	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG - [N24000809]NHAI,ANDHRA PRADESH	03/2018	1,550.98 -	1,550.98	1,620.21	- -	09/2021	-	0/0
55	FOUR LANING OF KOILWAR TO BHOJPUR - [N24000482]NHAI,BIHAR	08/2015	814.04 -	825.17	764.04	- -	10/2021	-	2/4
56	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM - [N24000799]NHAI,ANDHRA PRADESH	02/2018	1,959.00 -	1,959.00	1,308.42	- -	10/2021	-	0/0
57	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT - [N24000787]NHAI,KARNATAKA	02/2018	1,995.34 -	2,400.00	3,368.89	- -	11/2021	-	0/0
58	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR RO - [N24000796]NHAI,UTTAR PRADESH	03/2018	1,117.84 -	1,117.84	-	- -	12/2021	-	0/0
59	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA - [N24001199]NHAI,MADHYA PRADESH	10/2019	743.88 -	743.89	407.00	- -	12/2021	-	0/3
60	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU - [N24000785]NHAI,TAMIL NADU	02/2018	1,166.26 -	1,296.93	346.17	- -	01/2022	-	0/0

Costing Rs. 150 Crore and above						(August 2021)			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. Original (in months)	Milestones Achieved/ Total
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
61	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS - [N24000829]NHAI,TAMIL NADU	03/2018	1,016.92	1,071.00	299.56	-	01/2022	-	0/0
62	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6) - [N24000849]NHAI,MAHARASHTRA	03/2018	289.21	289.21	224.45	-	01/2022	-	0/0
63	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6) - [N24000847]NHAI,MAHARASHTRA	03/2018	291.53	291.53	197.49	-	02/2022	-	0/0
64	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA - [N24001213]NHAI,MADHYA PRADESH	12/2017	1,094.97	1,094.97	737.00	-	02/2022	-	2/4
65	FOUR LANNING OF LUDHIYANA-TALWANDI SECTION - [N24000483]NHAI,PUNJAB	09/2014	479.00	479.00	456.80	-	03/2022	-	0/0
66	FOUR LANING WITH PS TALEBANI - SMBALPUR - [N24000485]NHAI,ODISHA	12/2015	752.28	752.28	272.74	-	03/2022	-	0/1
67	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE - [N24000636]NHAI,RAJASTHAN	12/2016	1,031.95	1,031.95	-	-	03/2022	-	0/0
68	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25 - [N24000731]NHAI,ODISHA	01/2018	953.09	953.09	438.00	-	03/2022	-	0/0
69	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1 - [N24000811]NHAI,ANDHRA PRADESH	03/2018	314.43	314.43	85.61	-	03/2022	-	0/0
70	FOUR LANING OF MADURAI-CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300) - [N24000827]NHAI,TAMIL NADU	03/2018	628.71	628.71	358.35	-	03/2022	-	0/0
71	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM - [N24001214]NHAI,MADHYA PRADESH	12/2017	217.96	884.00	443.00	-	10/2022	-	2/4
72	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V - [N24001212]NHAI,MADHYA PRADESH	12/2017	656.98	840.00	223.00	-	11/2022	-	1/4
73	FOUR LANINIG OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULUM (KM 7.300) TO NATHAM (KM. 3 - [N24000826]NHAI,TAMIL NADU	03/2018	505.35	505.35	255.05	-	12/2022	-	0/0
	Total		23,912.29	25,389.34	14,610.81				19/42

Costing Rs.		150	Crore and above			 (August 2021)			
						Date of Commissioning			
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. Original (in months)	Milestones Achieved/ Total
1	2	3	4	5	6	7	8	9	10
74	<u>URBAN DEVELOPMENT</u> <u>National Building Construcion Corporation Ltd</u>	07/2016							
	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR - [N28000105]NBCC,DELHI		2,694.00	2,694.00	817.02	-	12/2022	-	0/9
	Total		2,694.00	2,694.00	817.02				0/9
	Grand Total		46,913.84	64,068.89	23,797.25				23/59

FLASH REPORT

List of projects without Date of Commissioning

Costing Rs. 150 Crore and above					(August 2021)
					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>COAL</u>				
	<u>Bharat Coking Coal Limited</u>				
1	PATHERDIH NLW WASHERY - [N06000127]BCCL,JHARKHAND	10/2012	269.82 -	04/2014 -	04/2020
	<u>Mahanadi Coal Fields Limited</u>				
2	ANANTA OC EXPANSION PH-III (15.0 MTY) - [N06000067]MCL,ODISHA	08/2008	207.28 -	03/2012 -	03/2021
	<u>Neyveli Lignite Corporation</u>				
3	TALABIRA II AND III OCP - [N06000189]NLC,ODISHA	07/2017	2,401.07 -	07/2020 -	04/2020
4	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW) - [N06000095]NLC,TAMIL NADU	06/2011	5,907.11 7,980.79	12/2015 -	02/2021
5	HADLA LIGNITE MINE PROJECT(1.90 MTPA) - [N06000144]NLC,RAJASTHAN	03/2015	522.45 -	09/2019 -	-
6	BARSINGSAR THERMAL POWER STATION EXTENSION - [N06000187]NLC,RAJASTHAN	03/2015	2,112.60 -	09/2020 -	-
7	BITHNOK LIGNITE THERMAL POWER STATION - [N06000188]NLC,RAJASTHAN	03/2015	2,196.30 -	09/2020 -	-
8	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA) - [N06000145]NLC,RAJASTHAN	03/2015	513.63 -	12/2019 -	-
	<u>Western Coal Fields Limited</u>				
9	AMALGAMATED PAUNI-II III OC MINE - [N06000131]WCL,MAHARASHTRA	06/2015	483.69 499.00	03/2021 -	03/2021
	Total		14,613.95 -		
	<u>FINANCE</u>				
	<u>Central Public Works Department</u>				
10	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI - [N28000089]CPWD,TAMIL NADU	12/2015	209.00 -	10/2019 -	07/2021
	Total		209.00 -		
	<u>FERTILISERS</u>				
	<u>National Fertiliser Limited</u>				
11	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA - [N08000015]NFL,PUNJAB	01/2018	218.83 -	11/2019 05/2021	04/2021
12	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL - [N08000016]NFL,PUNJAB	01/2018	239.81 -	11/2019 05/2021	04/2021
	Total		458.64 -		

Costing Rs. 150 Crore and above

(August 2021)

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>MINES</u>				
	<u>National Aluminum Company Limited (Nalco)</u>				
13	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU - [N10000014]NALCO,TAMIL NADU	09/2017	166.62 163.17	06/2019 12/2021	12/2020
14	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND - [N10000012]NALCO,ODISHA	12/2015	355.00 -	11/2020 -	02/2021
15	UTKAL D AND E COAL BLOCK - [N10000011]NALCO,ODISHA	05/2016	534.00 -	01/2020 -	-
	Total		1,055.62 -		
	<u>PETROLEUM</u>				
	<u>Chennai Petroleum Corporation Limited</u>				
16	BS-VI PROJECTS - [N16000295]CPCL,TAMIL NADU	09/2017	1,858.00 -	12/2019 -	
	<u>Indian Oil Corporation Limited</u>				
17	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP - [N16000302]IOCL,ANDHRA PRADESH	08/2017	384.58 -	04/2021 03/2021	03/2021
18	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT - [N16000236]IOCL,ASSAM	06/2016	423.00 -	08/2019 06/2021	05/2021
19	ENNORE-TRICHY-MADURAI LPG PIPELINE - [N16000162]IOCL,TAMIL NADU	05/2013	711.00 -	06/2020 -	-
	<u>Oil & Natural Gas Corporation Limited</u>				
20	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA) - [N16000297]ONGC,MAHARASHTRA	02/2017	4,006.83 4,475.92	05/2021 05/2021	05/2021
	Total		7,383.41 -		
	<u>POWER</u>				
	<u>Central Public Works Department</u>				
21	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI - [N28000118]CPWD,DELHI	10/2017	271.90 -	11/2019 -	-
	<u>National Hydro-Electric Power Corporation</u>				
22	LOKTAK D/S HEP(NHPC) - [180100078]NHPC,MANIPUR	12/1999	578.62 1,311.05	06/2006 -	-
	<u>National Thermal Power Corporation</u>				
23	TAPOVAN-VISHNUGAD HEP (4X130MW) - [N18000014]NTPC,UTTARAKHAND	11/2006	2,978.48 5,867.38	03/2013 12/2021	-
24	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW - [N18000142]NTPC,UTTARAKHAND	07/2012	1,527.00 -	08/2017 -	-
25	PAKRI BARWADIH COAL MINING PROJECT - [N18000225]NTPC,JHARKHAND	10/2004	4,237.96 4,238.00	10/2017 -	-
26	TALAIPALLI COAL MINING PROJECT - [N18000266]NTPC,CHHATISGARH	09/2015	3,004.00 -	11/2019 -	-
	<u>Power Grid Corporation Of India Limited</u>				

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
27	TRANSMISSION SYSTEM STRENGTHENING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR - [N18000213]PGCIL,MULTI STATE	03/2016	808.63 -	01/2018 07/2021	06/2021
28	EASTERN REGION STRENGTHENING SCHEME-XV - [N18000214]PGCIL,WEST BENGAL	04/2016	454.11 -	04/2018 03/2021	06/2021
29	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR - [N18000247]PGCIL,MULTI STATE	02/2017	5,070.13 -	04/2020 09/2021	06/2021
30	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT - [N18000061]PGCIL,MULTI STATE	10/2008	4,824.12 -	10/2012 -	-
31	SYSTEM STRENGTHENING XIII OF SR GRID - [N18000109]PGCIL,MULTI STATE	10/2011	487.49 -	06/2014 -	-
32	EASTERN REGION STRENGTHENING SCHEME-V - [N18000155]PGCIL,MULTI STATE	10/2013	1,364.52 -	04/2016 -	-
33	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH - [N18000168]PGCIL,MULTI STATE	06/2014	5,151.37 -	03/2018 -	-
34	TRANSMISSION SYSTEM ASSOCIATED WITH TEHRI PUMP STORAGE PLANT (PSP) - [N18000181]PGCIL,MULTI STATE	01/2015	871.62 -	10/2017 -	-
35	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII - [N18000182]PGCIL,MULTI STATE	01/2015	203.28 -	07/2017 -	-
36	GREEN ENERGY CORRIDORS - INTER STATE TRANSMISSION SCHEME PART-D - [N18000218]PGCIL,MULTI STATE	05/2016	3,519.59 -	05/2019 -	-
37	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO - [N18000238]PGCIL,MULTI STATE	03/2017	283.72 -	11/2019 -	-
38	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II) - [N18000239]PGCIL,MULTI STATE	10/2016	408.46 -	01/2019 -	-
39	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000240]PGCIL,MULTI STATE	10/2016	608.24 -	04/2019 -	-
40	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI - [N18000257]PGCIL,MULTI STATE	12/2015	3,654.00 -	04/2019 -	-
41	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000261]PGCIL,GUJARAT	05/2017	175.64 -	09/2018 -	-
42	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B) - [N18000263]PGCIL,KARNATAKA	05/2017	445.89 -	02/2019 -	-
43	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION) - [N18000267]PGCIL,MULTI STATE	09/2017	198.49 -	09/2019 -	-
44	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT - [N18000269]PGCIL,GUJARAT	12/2017	193.14 -	06/2019 -	-
	Total		41,320.40 -		
	<u>HEAVY INDUSTRY</u>				
	<u>Bharat Heavy Electricals Limited</u>				
45	DEVELOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA - [N20000002]BHEL,DELHI	08/2016	1,554.00 -	09/2019 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Natrip Implementation Society</u>				
46	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP) - [N20000001]NATIS,MULTI STATE	04/2011	1,718.00 3,727.30	09/2011 03/2021	03/2021
	Total		3,272.00 -		
	<u>HEALTH AND FAMILY WELFARE</u>				
	<u>Central Public Works Department</u>				
47	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD - [N28000098]CPWD,TELANGANA	10/2016	209.84 -	03/2020 -	05/2021
	<u>Hospital Services Consultancy Corporation Ltd</u>				
48	LGBRIMH-TEZPUR, ASSAM - [N21000007]HSCC,ASSAM	07/2012	175.57 -	12/2014 -	03/2018
49	CNCI KOLKATA WEST BENGAL - [N21000015]HSCC,WEST BENGAL	08/2016	244.00 -	09/2018 -	05/2019
50	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR - [N21000010]HSCC,WEST BENGAL	12/2014	168.90 -	05/2017 -	07/2019
51	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR - [N21000011]HSCC,HARYANA	09/2014	505.58 -	03/2018 -	09/2019
52	AIIMS - OPD(NEW) - [N21000009]HSCC,DELHI	08/2014	293.65 -	05/2017 -	01/2020
53	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA - [N21000016]HSCC,MAHARASHTRA	08/2017	274.19 -	03/2019 -	01/2021
54	SUPER SPECIALITY BLOCK PMSSY GOA - [N21000022]HSCC,GOA	01/2018	249.01 -	- -	01/2021
55	AIIMS - MOTHER AND CHILD BLOCK - [N21000008]HSCC,DELHI	12/2013	204.44 -	05/2017 -	03/2021
56	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB - [N21000012]HSCC,PUNJAB	07/2016	152.95 -	02/2018 -	03/2021
57	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS-MNAGLAGIRI GUNTUR, ANDHRA PRADESH - [N21000017]HSCC,ANDHRA PRADESH	08/2017	272.19 -	03/2019 -	03/2021
58	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI - [N21000021]HSCC,UTTAR PRADESH	03/2018	268.84 -	- -	03/2021
	Total		3,019.16 -		
	<u>RAILWAYS</u>				
	<u>Central Railways</u>				
59	3RD LINE BETWEEN BHUSAWAL-JALGAON - [N22000247]CR,MAHARASHTRA	04/2011	184.06 -	03/2019 -	-
60	VAIBHAVWADI-KOLHAPUR (107 KM) - [N22000355]CR,MAHARASHTRA	02/2016	2,750.00 -	03/2024 -	-
	<u>Container Corporation Of India</u>				
61	MULTI MODAL LOGISTICS PARK AT KATHUWAS - [N22000421]CCOI,RAJASTHAN	01/2011	493.17 -	03/2018 -	-
62	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN - [N22000422]CCOI,MAHARASHTRA	10/2013	305.00 -	03/2019 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
63	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM - [N22000424]CCOI, ANDHRA PRADESH	01/2013	387.70 -	03/2018 -	-
64	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR - [N22000425]CCOI, CHHATISGARH	05/2014	207.00 -	03/2018 -	-
65	MULTI MODAL LOGISTICS PARK AT BARHI - [N22000426]CCOI, HARYANA	12/2015	346.32 -	03/2019 -	-
66	MULTI MODAL LOGISTICS PARK AT TIHI - [N22000427]CCOI, MADHYA PRADESH	12/2015	174.00 -	03/2019 -	-
67	MULTI MODAL LOGISTICS PARK AT VARNAMA - [N22000428]CCOI, GUJARAT	10/2013	343.00 -	03/2019 -	-
68	MULTI MODAL LOGISTICS PARK AT KAKINADA - [N22000431]CCOI, ANDHRA PRADESH	08/2016	234.50 -	03/2019 -	-
	<u>Dedicated Freight Corridor Corporation Of India Ltd</u>				
69	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT - [N22000346]DFCC, MULTI STATE	10/2006	11,589.00 30,357.00	- -	-
70	WESTERN DEDICATED FREIGHT CORRIDOR - [N22000464]DFCC, MULTI STATE	11/2007	16,592.00 51,101.00	03/2020 -	-
	<u>East Central Railways</u>				
71	HAJIPUR-RAMDAYALUNAGAR DOUBLING - [N22000182]ECR, BIHAR	04/2013	213.01 -	- 10/2019	10/2019
72	RAJGIR HISUA TALAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR - [N22000475]ECR, BIHAR	04/1998	180.82 -	- 08/2020	08/2020
73	SAKRI-HASANPUR ROAD (NL) - [N22000171]ECR, BIHAR	04/1999	325.00 735.20	- -	03/2021
74	KOSI BRIDGE (NL), ECR - [220100304]ECR, BIHAR	04/2002	499.41 516.02	03/2020 -	-
75	DANIAWAN-BIHARSARIF (NL), ECR - [220100311]ECR, BIHAR	04/2001	406.92 -	- -	-
76	ARA-BHABHUA ROAD (NL) - [N22000166]ECR, BIHAR	04/2008	633.87 -	- -	-
77	NAWADA-LAXMIPUR (NL) - [N22000167]ECR, BIHAR	04/2008	620.57 -	- -	-
78	GAYA-DALTONGANJ VIA RAFIGANJ (NL) - [N22000168]ECR, BIHAR	04/2008	445.25 -	- -	-
79	GAYA-CHATRA (NL) - [N22000169]ECR, MULTI STATE	04/2008	415.67 -	- -	-
80	DARBANGHA-KUSHESHWARSTHAN (NL) - [N22000173]ECR, BIHAR	04/2005	205.00 -	- -	-
81	MOTIHARI-SITAMARHI (NL) - [N22000174]ECR, BIHAR	04/2006	211.00 -	- -	-
82	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL) - [N22000175]ECR, BIHAR	04/2008	678.62 -	- -	-
83	KURSELA-BIHARIGANJ (NL) - [N22000178]ECR, BIHAR	04/2008	192.56 -	- -	-
84	MUZAFFARPUR-DARBANGHA (NL) - [N22000179]ECR, BIHAR	04/2008	281.30 -	- -	-
85	MUZAFFARPUR-SITAMARHI NEW LINE - [N22000374]ECR, BIHAR	01/1991	332.15 -	07/2014 -	-
	<u>Eastern Railways</u>				

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
86	PIRPAINTI-BHAGALPUR - [N22000222]ER,MULTI STATE	04/2011	261.38 -	- -	05/2019
87	BANDEL-BOINCHI 3RD LINE - [N22000221]ER,MULTI STATE	04/2011	288.35 -	- -	03/2021
88	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS) - [N22000230]ER,MULTI STATE	04/2010	157.94 -	11/2018 -	03/2021
89	HANSDIHA-GODDA NL - [N22000236]ER,MULTI STATE	04/2011	542.18 -	03/2020 -	03/2021
	<u>Kolkata Metro Rail Corporation Limited</u>				
90	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP) - [N22000108]KOMRCL, WEST BENGAL	04/2010	2,397.72 -	03/2016 -	-
	<u>Metropolitan Rapid Transport Projects</u>				
91	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP) - [220100268]MRTP, WEST BENGAL	03/2000	1,049.69 -	12/2006 -	-
92	MUMBAI URBAN TRANSPORT PROJECT PHASE-II - [N22000092]MRTP, MAHARASHTRA	04/2008	5,300.00 -	03/2014 -	-
93	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE - [N22000135]MRTP, WEST BENGAL	03/2013	4,874.58 -	03/2016 -	-
94	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE - [N22000214]MRTP, MAHARASHTRA	04/2012	714.10 -	04/2016 -	-
	<u>North Central Railway</u>				
95	ETAWAH-MAINPURI (NL), NCR - [220100318]NCR, UTTAR PRADESH	04/1997	120.00 -	12/2008 -	-
96	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPUR CITY AND MOHARI-TANPUR AND TANPUR-BANSI PAHARPUR - [N22000158]NCR, MULTI STATE	04/2010	2,030.50 -	- -	-
97	MATHURA-PLWAL 4TH LINE (80KM) - [N22000372]NCR, UTTAR PRADESH	04/2015	668.70 668.00	03/2020 -	-
	<u>North East Frontier Railway</u>				
98	AMBARI FALAKATA TO NEW MAYNAGURI - [N22000210]NFR, ASSAM	04/2011	314.00 486.96	03/2019 -	06/2021
99	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL), NEFR - [220100135]NFR, WEST BENGAL	04/1983	297.32 200.34	03/2019 -	-
100	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR - [N22000193]NFR, WEST BENGAL	04/2010	221.42 -	- -	-
101	DIMAPUR-TIZIT NL - [N22000196]NFR, NAGALAND	04/2013	4,274.00 -	03/2020 -	-
102	NEW BG LINE FROM BYRNihat TO SHILLONG - [N22000205]NFR, MEGHALAYA	04/2010	906.46 1,202.33	03/2021 -	-
103	NEW BG LINE FROM BALURGHAT TO HILLY NFR - [N22000206]NFR, MULTI STATE	04/2010	242.22 -	03/2020 -	-
104	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI - [N22000209]NFR, MULTI STATE	04/1999	819.23 -	- -	-
105	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHOWA-JAIN - [N22000499]NFR, WEST BENGAL	02/1999	380.60 -	04/2010 -	-
106	KISHANGANJ JALALGARH, NL, NEFR - [N22000101]NFR, BIHAR	04/2008	333.76 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
107	MURKONGSELEK-PASIGHAT NL - [N22000208]NFR,MULTI STATE	04/2011	414.84 -	03/2020 -	-
	<u>North Eastern Railway</u>				
108	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION - [N22000461]NER,UTTAR PRADESH	04/2017	622.50 427.00	04/2017 -	03/2021
109	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING. - [N22000470]NER,UTTAR PRADESH	04/2016	1,177.96 -	12/2019 -	04/2021
110	KICHHA-KHATIMA (NL) - NER - [220100317]NER,UTTARAKHAND	04/2003	142.45 -	- -	-
111	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP - [N22000130]NER,UTTAR PRADESH	03/2013	307.00 -	- -	-
112	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP - [N22000136]NER,UTTAR PRADESH	03/2013	643.00 -	- -	-
113	GHAZIPUR - AUNRIHAR (40 KM) - [N22000321]NER,UTTAR PRADESH	04/2014	182.92 -	- -	-
114	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE - [N22000460]NER,UTTAR PRADESH	04/2017	1,343.00 -	01/2018 -	-
	<u>North Western Railway</u>				
115	THIYAT HAMIRA-SANU - [N22000149]NWR,RAJASTHAN	04/2013	236.93 -	10/2018 -	01/2020
116	ALWAR-BANDIKUI DOUBLING - [N22000157]NWR,RAJASTHAN	04/2013	242.09 -	02/2019 -	02/2020
117	BANGURGRAM-GURIYA PATCH DOUBLING - [N22000137]NWR,RAJASTHAN	04/2012	246.08 -	12/2019 -	03/2021
118	AJMER-BANGURGRAM - [N22000155]NWR,RAJASTHAN	04/2011	213.39 -	11/2019 -	03/2021
119	RATLAM-DUNGARPUR VIA BANSWARA (NL) - [N22000147]NWR,MULTI STATE	04/2011	2,082.75 -	- -	-
120	AJMER-KOTA (NASIRABAD-JAUNDRI) - [N22000150]NWR,RAJASTHAN	04/2013	822.00 -	- -	-
121	PUSHKAR-MERTA - [N22000151]NWR,RAJASTHAN	04/2013	323.00 -	- -	-
122	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL - [N22000330]NWR,RAJASTHAN	05/2015	873.71 -	- -	-
	<u>Northern Railway</u>				
123	ROHTAK-MEHAM HANSI - [N22000272]NR,HARYANA	04/2012	287.00 -	12/2011 -	06/2021
124	HARIDWAR-LAKSAR - [N22000289]NR,UTTARAKHAND	04/2012	219.83 -	- -	-
125	JALANDHAR-PATHANKOT-JAMMU TAWI - [N22000492]NR,MULTI STATE	03/2002	625.00 -	03/2016 -	-
	<u>Rail India Technical And Economic Service</u>				
126	GOOTY-DHARMAVARAM-BANGLORE - [N22000370]RITES,MULTI STATE	04/2015	636.38 -	- -	-
127	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY - [N22000394]RITES,TELANGANA	03/2015	636.38 -	03/2021 -	-
128	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW - [N22000498]RITES,CHHATISGARH	02/2016	393.98 -	03/2020 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Rail Vikas Nigam Ltd.</u>				
129	HARIDASPUR-PARADEEP(NL) - [220100285]RVNL,ODISHA	04/1996	1,185.64 -	12/2017 -	-
130	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR) - [220100327]RVNL,ODISHA	04/2000	133.41 207.00	03/2009 03/2009	-
131	DHASA-JETALSAR (GC) - [N22000141]RVNL,GUJARAT	04/2012	644.38 -	03/2021 -	-
	<u>Railway Electrification</u>				
132	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT - [N22000094]RE,UTTAR PRADESH	02/2008	171.10 -	03/2012 -	-
	<u>South Central Railway</u>				
133	NANDYAL-YERRAGUNTLA(NL),SCR - [220100192]SCR,ANDHRA PRADESH	03/1996	164.36 -	02/2009 -	-
134	MANUGURU-RAMAGUNDAM - [N22000259]SCR,TELANGANA	04/2013	1,112.00 -	- -	-
135	GUDUR-DURGARA JAPATNAM - [N22000265]SCR,ANDHRA PRADESH	04/2011	761.37 -	- -	-
136	CUMBUM-PRODDATUR - [N22000282]SCR,ANDHRA PRADESH	04/2013	829.00 -	- -	-
137	DUVVADA-VIJAYAWADA - [N22000366]SCR,ANDHRA PRADESH	04/2015	3,873.07 -	- -	-
	<u>South East Central Railway</u>				
138	CHHINDWARA - NAGPUR (GC)(SECR) - [220100324]SECR,MADHYA PRADESH	04/2005	383.79 1,413.76	- 08/2020	08/2020
139	CHAMPA-JHARSUGUDA 3RD LINE - [N22000483]SECR,CHHATISGARH	04/2008	872.00 1,226.51	12/2019 10/2020	10/2020
140	GONDIA-JABALPUR(GC),(SECR) - [220100186]SECR,MULTI STATE	02/1997	511.86 1,756.00	04/2020 03/2021	03/2021
	<u>South Eastern Railway</u>				
141	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND - [N22000323]SER,JHARKHAND	04/2012	148.77 -	12/2016 -	08/2020
142	HOWRAH-AMTA-CHAMPADANGA NL (SER) - [220100208]SER,WEST BENGAL	04/1974	393.46 154.30	03/2007 03/2007	-
143	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION - [N22000162]SER,ODISHA	04/2010	149.90 -	03/2015 -	-
	<u>Southern Railway</u>				
144	ANGAMALI-SABARIMALA (N.L.)(SR) - [220100252]SR,KERALA	10/1998	1,566.00 -	- -	-
145	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL) - [N22000084]SR,TAMIL NADU	09/2006	227.40 -	- -	-
146	ATTIPPATTU PUTTUR - [N22000184]SR,TAMIL NADU	04/2008	151.84 -	02/2019 -	-
147	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKOTTAI-AVADI-SRIPERUMBUDUR - [N22000186]SR,TAMIL NADU	04/2013	839.00 -	- -	-
148	KUMBALAM-TURAVUR - [N22000191]SR,KERALA	04/2011	252.96 -	- -	-
149	ERODE-PALANI - [N22000199]SR,TAMIL NADU	04/2008	288.57 -	- -	-

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
150	ERNAKULAM-KUMBALAM - [N22000204]SR,KERALA	04/2010	189.24 -	- -	-
151	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM - [N22000373]SR,TAMIL NADU	10/2013	187.26 -	04/2014 -	-
152	TRIVANDRUM-KANYAKUMARI DOUBLING - [N22000399]SR,KERALA	02/2015	1,431.90 -	- -	-
153	TURAVUR-AMBALAPUZHA DOUBLING - [N22000400]SR,KERALA	02/2015	1,000.00 -	- -	-
154	PALAKKAD - SETTING UP OF RAIL COACH FACTORY - [N22000443]SR,KERALA	02/2012	550.00 -	03/2016 -	-
155	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING - [N22000444]SR,TAMIL NADU	02/1999	257.00 257.00	03/2018 -	-
	<u>Western Railway</u>				
156	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR) - [N22000125]WR,GUJARAT	04/2006	117.36 196.95	03/2011 -	-
157	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO - [N22000433]WR,GUJARAT	03/2017	243.60 -	- -	-
158	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM - [N22000434]WR,MAHARASHTRA	03/2010	265.88 -	- -	-
159	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A - [N22000435]WR,MAHARASHTRA	03/2012	217.38 -	- -	-
160	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON - [N22000436]WR,GUJARAT	03/2012	248.26 -	- -	-
161	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220 - [N22000437]WR,GUJARAT	03/2012	153.83 -	- -	-
	Total		97,634.83 -		
	<u>ROAD TRANSPORT AND HIGHWAYS</u>				
	<u>Central Public Works Department</u>				
162	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE - [N24001236]CPWD,TAMIL NADU	03/2019	297.55 -	11/2019 -	-
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>				
163	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8 - [N24001380]MoRTH,TAMIL NADU	08/2020	302.62 -	02/2021 -	02/2021
164	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50. - [N24001382]MoRTH,HIMACHAL PRADESH	08/2020	242.80 -	03/2021 -	03/2021
165	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA - [N24001381]MoRTH,HIMACHAL PRADESH	08/2020	272.98 -	04/2021 -	04/2021
166	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75 - [N24001383]MoRTH,HIMACHAL PRADESH	08/2020	349.20 -	04/2021 -	04/2021

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
167	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT - [N24001387]MoRTH,KARNATAKA	01/2017	264.34 -	09/2017 -	09/2017
168	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA - [N24001388]MoRTH,KARNATAKA	03/2019	423.15 -	12/2019 -	12/2019
169	REHABILITATION AND UPGRADE OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P - [N24001140]MoRTH,UTTAR PRADESH	11/2016	215.16 215.00	09/2019 -	10/2019
170	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000778]MoRTH,UTTARAKHAND	11/2017	266.52 -	11/2019 11/2019	11/2019
171	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER - [N24001130]MoRTH,UTTARAKHAND	08/2016	234.88 -	12/2017 12/2019	12/2019
172	REHABILITATION AND UPGRADE OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7 - [N24000889]MoRTH,WEST BENGAL	04/2014	279.70 398.52	08/2017 -	02/2020
173	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709 - [N24000957]MoRTH,RAJASTHAN	11/2017	163.95 -	04/2018 -	07/2020
174	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST - [N24001195]MoRTH,ARUNACHAL PRADESH	11/2016	243.89 -	-	09/2020
175	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000821]MoRTH,A & N ISLANDS	11/2017	257.34 -	11/2019 03/2021	03/2021
176	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION - [N24000777]MoRTH,UTTARAKHAND	11/2017	283.51 -	11/2019 05/2021	05/2021
177	REHABILITATION AND UPGRADE OF TULSIPUR -BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730 - [N24001146]MoRTH,UTTAR PRADESH	03/2016	249.50 -	05/2019 -	05/2021
178	UPGRADE OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4 - [N24000882]MoRTH,WEST BENGAL	02/2018	218.70 218.70	11/2020 04/2021	06/2021
179	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO - [N24000883]MoRTH,WEST BENGAL	03/2018	254.30 254.30	10/2020 03/2021	06/2021
180	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4 - [N24001197]MoRTH,GUJARAT	03/2018	351.00 -	06/2021 -	06/2021
181	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000772]MoRTH,UTTARAKHAND	12/2017	257.34 -	12/2019 07/2021	07/2021
182	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S - [N24000773]MoRTH,UTTARAKHAND	12/2017	200.34 -	12/2019 07/2021	07/2021
183	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG - [N24000776]MoRTH,UTTARAKHAND	11/2017	232.81 -	11/2019 07/2021	07/2021

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
184	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT - [N24000966]MoRTH,ANDHRA PRADESH	01/2016	348.95 -	08/2016 12/2021	07/2021
185	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT - [N24000245]MoRTH,TELANGANA	01/2014	270.00 -	03/2016 -	-
186	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM - [N24000248]MoRTH,TELANGANA	03/2015	153.21 -	01/2017 -	-
187	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16) - [N24000252]MoRTH,MAHARASHTRA	03/2015	168.30 -	- -	-
188	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO - [N24000253]MoRTH,MAHARASHTRA	08/2014	187.79 -	07/2016 -	-
189	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00 - [N24000254]MoRTH,MAHARASHTRA	01/2014	446.77 -	- -	-
190	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K - [N24000257]MoRTH,GOA	03/2015	298.33 -	- -	-
191	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD - [N24000258]MoRTH,GOA	03/2015	184.05 -	- -	-
192	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE - [N24000259]MoRTH,GOA	03/2015	280.16 -	- -	-
193	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1 - [N24000260]MoRTH,KERALA	01/2014	255.75 348.00	09/2017 -	-
194	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16 - [N24000275]MoRTH,MAHARASHTRA	10/2015	289.60 -	- -	-
195	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T - [N24000282]MoRTH,ANDHRA PRADESH	01/2014	195.45 -	11/2014 -	-
196	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES - [N24000301]MoRTH,ANDHRA PRADESH	03/2015	271.45 -	10/2015 06/2021	-
197	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM. - [N24000312]MoRTH,SIKKIM	04/2013	151.59 369.92	08/2013 06/2021	-
198	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM. - [N24000313]MoRTH,SIKKIM	04/2013	166.27 359.90	08/2013 06/2021	-
199	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM - [N24000314]MoRTH,SIKKIM	01/2013	182.28 369.58	02/2013 06/2021	-
200	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT - [N24000316]MoRTH,TAMIL NADU	03/2015	258.97 273.27	08/2015 -	-
201	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B - [N24000331]MoRTH,UTTAR PRADESH	01/2014	282.41 -	03/2016 -	-
202	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM - [N24000332]MoRTH,MAHARASHTRA	01/2015	225.81 -	- -	-
203	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP - [N24000334]MoRTH,KARNATAKA	03/2015	165.67 -	11/2015 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
204	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR - [N24000382]MoRTH, BIHAR	01/1991	675.00 780.77	- -	-
205	4-LANING OF MOGA - TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00 - [N24000391]MoRTH, PUNJAB	11/2015	889.24 -	- -	-
206	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP - [N24000412]MoRTH, MADHYA PRADESH	01/2012	410.72 -	04/2015 -	-
207	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE - [N24000444]MoRTH, GOA	10/2015	936.40 -	- -	-
208	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE - [N24000511]MoRTH, UTTAR PRADESH	05/2013	164.54 -	08/2015 -	-
209	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER - [N24000514]MoRTH, GOA	12/2015	773.98 -	- -	-
210	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR - [N24000516]MoRTH, GOA	12/2015	819.95 -	- -	-
211	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA - [N24000527]MoRTH, ODISHA	12/2011	191.08 -	08/2015 -	-
212	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104 - [N24000531]MoRTH, BIHAR	01/1991	319.68 -	- -	-
213	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000574]MoRTH, BIHAR	11/2013	683.83 683.82	07/2016 -	-
214	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000576]MoRTH, BIHAR	02/2016	178.85 -	05/2016 -	-
215	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 -LANE WITH P - [N24000578]MoRTH, BIHAR	02/2016	553.30 -	05/2016 -	-
216	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR - [N24000579]MoRTH, BIHAR	01/2014	1,408.85 2,138.16	10/2016 -	-
217	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE - [N24000584]MoRTH, MAHARASHTRA	03/2016	1,142.62 -	- -	-
218	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE - [N24000585]MoRTH, MAHARASHTRA	03/2016	1,101.58 -	- -	-
219	REHABILITATION OF 4-LANE 5.575 KM LONG, 4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM - [N24000610]MoRTH, BIHAR	08/2016	1,742.01 -	12/2016 -	-
220	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO - [N24000639]MoRTH, ODISHA	03/2014	191.50 192.00	05/2016 -	-
221	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR - [N24000645]MoRTH, ODISHA	08/2013	171.96 172.00	06/2016 -	-
222	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00 - [N24000782]MoRTH, UTTARAKHAND	03/2018	460.73 -	- -	-
223	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS - [N24000904]MoRTH, HARYANA	01/2017	247.25 -	03/2019 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
224	WIDENING AND PAVED SHOULDER OF TOHANA (IN HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA - [N24000907]MoRTH,PUNJAB	03/2018	293.10 -	08/2020 -	-
225	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000 - [N24000910]MoRTH,PUNJAB	03/2018	170.57 -	11/2020 -	-
226	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA - [N24000912]MoRTH,ODISHA	08/2016	287.70 -	02/2017 -	-
227	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA - [N24000913]MoRTH,ODISHA	09/2016	295.67 -	02/2017 -	-
228	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA - [N24000914]MoRTH,ODISHA	12/2016	223.50 -	08/2018 -	-
229	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA - [N24000915]MoRTH,ODISHA	12/2016	206.88 -	04/2018 -	-
230	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA - [N24000916]MoRTH,ODISHA	03/2018	214.23 -	08/2018 -	-
231	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA - [N24000917]MoRTH,ODISHA	03/2018	199.16 -	08/2018 -	-
232	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE - [N24000922]MoRTH,GUJARAT	12/2017	867.97 -	11/2018 -	-
233	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN - [N24000923]MoRTH,GUJARAT	03/2018	464.07 -	11/2018 -	-
234	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA - [N24000925]MoRTH,GUJARAT	10/2018	400.76 -	05/2019 -	-
235	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU - [N24000926]MoRTH,GUJARAT	08/2017	962.43 -	03/2018 -	-
236	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0) TO KM 275/622(DESIGN CH 5.12 - [N24000928]MoRTH,ANDHRA PRADESH	10/2015	333.21 -	12/2015 -	-
237	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU - [N24000929]MoRTH,ANDHRA PRADESH	09/2016	372.68 309.37	02/2017 07/2021	-
238	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V - [N24000933]MoRTH,ANDHRA PRADESH	02/2017	429.43 373.05	11/2017 01/2022	-
239	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA - [N24000939]MoRTH,ANDHRA PRADESH	03/2018	504.19 556.13	11/2018 07/2021	-
240	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES - [N24000941]MoRTH,PUNJAB	03/2018	293.64 -	08/2020 -	-
241	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND - [N24000943]MoRTH,BIHAR	09/2018	1,478.40 -	- -	-
242	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR - [N24000950]MoRTH,RAJASTHAN	11/2017	187.82 -	04/2018 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
243	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000958]MoRTH,RAJASTHAN	02/2018	370.30 -	06/2018 -	-
244	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM- - [N24000959]MoRTH,RAJASTHAN	02/2018	341.79 -	05/2018 -	-
245	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21 - [N24000965]MoRTH,ANDHRA PRADESH	01/2016	386.09 316.06	05/2016 07/2021	-
246	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON - [N24000980]MoRTH,TELANGANA	10/2016	298.32 -	02/2019 -	-
247	WIDEINING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ - [N24000981]MoRTH,TELANGANA	10/2016	248.83 -	03/2019 -	-
248	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE - [N24000982]MoRTH,TELANGANA	01/2017	244.54 -	05/2019 -	-
249	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON-THIRUMALAGIRI OF NH - [N24000983]MoRTH,TELANGANA	01/2017	196.52 -	10/2019 -	-
250	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA-KALWAKURTHY SECTI - [N24000984]MoRTH,TELANGANA	01/2017	283.00 -	12/2019 -	-
251	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-RAVULAPALLY SECT - [N24000985]MoRTH,TELANGANA	01/2017	359.27 -	05/2019 -	-
252	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION - [N24000986]MoRTH,TELANGANA	01/2017	300.00 -	05/2019 -	-
253	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH - [N24000987]MoRTH,TELANGANA	01/2018	283.15 -	05/2020 -	-
254	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4 - [N24000988]MoRTH,TELANGANA	01/2018	230.03 -	12/2019 -	-
255	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59 - [N24000989]MoRTH,TELANGANA	02/2018	206.13 -	06/2020 -	-
256	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT - [N24000990]MoRTH,TELANGANA	02/2018	294.13 -	11/2019 -	-
257	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS - [N24000991]MoRTH,TELANGANA	02/2018	220.28 -	11/2019 -	-
258	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN - [N24000992]MoRTH,TELANGANA	02/2018	426.52 -	04/2020 -	-
259	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC - [N24000993]MoRTH,TELANGANA	03/2018	322.81 -	09/2020 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
260	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES - [N24000994]MoRTH,TELANGANA	03/2018	626.76 -	07/2020 -	-
261	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR - [N24000996]MoRTH,TELANGANA	01/2017	605.08 -	10/2019 -	-
262	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL - MALLAMPALLY SECTION OF NH-365 - [N24000997]MoRTH,TELANGANA	03/2018	192.67 -	07/2019 -	-
263	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR - [N24000998]MoRTH,TELANGANA	01/2019	193.19 -	- -	-
264	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM 103.865 TO 142.050 (GAYA-GOH) OF NH - [N24001000]MoRTH,BIHAR	03/2018	153.24 -	- -	-
265	SARSAM TO KOTHARI - [N24001002]MoRTH,MAHARASHTRA	02/2016	545.64 -	07/2019 -	-
266	AKOLA TO AKOT - [N24001003]MoRTH,MAHARASHTRA	01/2017	313.95 -	06/2019 -	-
267	PATRADEVI TO KARASWADA 4L - [N24001004]MoRTH,GOA	03/2017	634.32 -	05/2020 -	-
268	KARASWADA TO BAMBOLIM - [N24001005]MoRTH,GOA	03/2017	852.67 -	12/2019 -	-
269	AKOT TO ANJANGAON - [N24001006]MoRTH,MAHARASHTRA	01/2017	245.77 246.00	06/2019 -	-
270	ANJANGAON TO MAH/MP BORDER - [N24001007]MoRTH,MADHYA PRADESH	01/2017	359.00 359.00	06/2019 -	-
271	AJANTHA TO BULDHANA - [N24001008]MoRTH,A & N ISLANDS	02/2017	401.00 401.00	07/2019 -	-
272	KHAMGAON TO SHEGAON - [N24001009]MoRTH,MAHARASHTRA	02/2017	203.21 203.00	05/2019 -	-
273	SHEGAON TO DEORI PHATA - [N24001010]MoRTH,MAHARASHTRA	02/2017	373.10 373.00	05/2019 -	-
274	MEHKAR TO CHIKALI - [N24001011]MoRTH,MAHARASHTRA	02/2017	322.48 322.00	05/2019 -	-
275	CHIKALI TO KHAMGAON - [N24001012]MoRTH,MAHARASHTRA	02/2017	548.03 548.00	06/2019 -	-
276	DIGRAS DARWAH KARANJA - [N24001013]MoRTH,MAHARASHTRA	01/2017	391.06 391.00	06/2019 -	-
277	NANDGAON TO MORSHI - [N24001014]MoRTH,MAHARASHTRA	01/2017	385.87 386.00	06/2019 -	-
278	MORSHI TO ACHALPUR - [N24001015]MoRTH,MAHARASHTRA	01/2017	341.16 341.00	06/2019 -	-
279	MORSHI TO MAH/MP BORDER - [N24001016]MoRTH,MAHARASHTRA	01/2017	471.61 472.00	06/2019 -	-
280	DAHEGAON TO KUHI - [N24001017]MoRTH,MAHARASHTRA	01/2017	228.89 229.00	06/2019 -	-
281	BHANDARA TO GHOTITOK - [N24001018]MoRTH,MAHARASHTRA	01/2017	392.83 393.00	06/2019 -	-
282	KATOL TO WARUD - [N24001019]MoRTH,MAHARASHTRA	01/2017	463.62 664.00	06/2019 -	-

Costing Rs. 150 Crore and above

(August 2021)

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
283	AMD TO SAONER - [N24001021]MoRTH,MAHARASHTRA	01/2017	396.91 397.00	06/2019 -	-
284	WADI TO ASOLA - [N24001022]MoRTH,MAHARASHTRA	01/2017	363.82 364.00	09/2019 -	-
285	NAGAJ TO VAJAPUR - [N24001023]MoRTH,MAHARASHTRA	01/2017	376.72 377.00	06/2019 -	-
286	MANGAON TO DIGHI PORT - [N24001024]MoRTH,MAHARASHTRA	01/2017	457.52 -	07/2019 -	-
287	INDAPUR TO AGARDANDA - [N24001025]MoRTH,MAHARASHTRA	01/2017	355.17 -	07/2019 -	-
288	WAKAN PALI KHOPOLI - [N24001026]MoRTH,MAHARASHTRA	01/2017	376.19 -	05/2019 -	-
289	SHAHPUR PATGAON SECTION I - [N24001027]MoRTH,MAHARASHTRA	01/2018	150.79 -	12/2019 -	-
290	PATGAON KHOPOLI SECTION I - [N24001028]MoRTH,MAHARASHTRA	01/2018	170.00 -	12/2019 -	-
291	AHMADPUR TO PIMPLA - [N24001029]MoRTH,MAHARASHTRA	01/2017	422.38 -	08/2019 -	-
292	PIMPLA TO MANJARSUMBHA - [N24001030]MoRTH,MAHARASHTRA	01/2017	595.77 -	08/2019 -	-
293	MANJUSUMBA TO CHUMBALI - [N24001031]MoRTH,MAHARASHTRA	01/2017	228.54 -	08/2019 -	-
294	DEORI TO AMGAON - [N24001032]MoRTH,MAHARASHTRA	01/2017	409.62 410.00	05/2019 -	-
295	MANTHA TALUKAS BORDER TO PARTUR - [N24001033]MoRTH,MAHARASHTRA	01/2017	486.19 -	07/2019 -	-
296	PARTUR TO MAJALGAON - [N24001034]MoRTH,MAHARASHTRA	01/2017	420.57 -	07/2019 -	-
297	MANSAR TO SALAIKHURD - [N24001035]MoRTH,MAHARASHTRA	01/2018	418.36 -	12/2019 -	-
298	KAJ TO KUSALAM - [N24001037]MoRTH,MAHARASHTRA	01/2017	554.78 -	07/2019 -	-
299	MAHAD TO RAIGAD FORT - [N24001038]MoRTH,MAHARASHTRA	07/2018	237.40 -	05/2020 -	-
300	JINTUR TO PARBHANI - [N24001039]MoRTH,MAHARASHTRA	01/2017	356.66 -	- -	-
301	JAHIRABAD TO LATUR - [N24001040]MoRTH,MAHARASHTRA	01/2017	461.96 -	11/2019 -	-
302	SHIROD SHAHPURER TO NANDED - [N24001041]MoRTH,MAHARASHTRA	01/2017	211.34 -	07/2019 -	-
303	SALAIKHURD TO TIRORA - [N24001042]MoRTH,MAHARASHTRA	01/2018	415.25 415.25	12/2019 -	-
304	NILAJPHATA TO BHANDARA - [N24001043]MoRTH,MAHARASHTRA	01/2018	420.63 421.00	05/2020 -	-
305	KALMAB TO RALEGAON - [N24001044]MoRTH,MAHARASHTRA	01/2017	467.78 -	06/2019 -	-
306	JALGAON TO BHADGAON - [N24001045]MoRTH,MAHARASHTRA	01/2018	307.54 308.00	11/2019 -	-
307	RALEGAON TO RAMTIRTH - [N24001046]MoRTH,MAHARASHTRA	01/2017	210.81 -	07/2019 -	-

Costing Rs. 150 Crore and above

(August 2021)

				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
308	BHADGAON TO CHALISGAON - [N24001047]MoRTH,MAHARASHTRA	01/2018	259.55 260.00	11/2019 -	-
309	MEHKAR TO AJISPUR - [N24001048]MoRTH,MAHARASHTRA	01/2017	232.77 -	07/2019 -	-
310	KARAD TO VITA - [N24001049]MoRTH,MAHARASHTRA	01/2018	344.85 245.00	12/2019 -	-
311	VITA TO NAGAJ - [N24001050]MoRTH,MAHARASHTRA	03/2018	304.58 305.00	12/2019 -	-
312	NALDURG TO AKKALKOT - [N24001051]MoRTH,MAHARASHTRA	02/2018	274.50 275.00	12/2019 -	-
313	SANGOLA TO JATH - [N24001052]MoRTH,MAHARASHTRA	01/2018	257.38 257.00	12/2019 -	-
314	KARAD TO TAGAON - [N24001053]MoRTH,MAHARASHTRA	01/2017	537.81 538.00	06/2019 -	-
315	TASGAON TO SHIRDHON - [N24001054]MoRTH,MAHARASHTRA	01/2017	195.64 196.00	11/2019 -	-
316	HELWAK TO KARAD - [N24001055]MoRTH,MAHARASHTRA	02/2017	416.99 -	07/2019 -	-
317	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI - [N24001056]MoRTH,MAHARASHTRA	02/2017	422.02 422.00	07/2019 -	-
318	KARAD PATAN CHIPLUN GUHAGAR - [N24001057]MoRTH,MAHARASHTRA	02/2017	407.19 407.00	06/2019 -	-
319	KARWANDI TO RAJURI - [N24001058]MoRTH,MAHARASHTRA	03/2018	276.95 277.00	12/2019 -	-
320	SHIVUR TO YEOLA - [N24001059]MoRTH,MAHARASHTRA	03/2018	181.08 -	12/2019 -	-
321	PALPHATA TO PHULAMBARI - [N24001060]MoRTH,MAHARASHTRA	03/2018	227.19 227.00	12/2019 -	-
322	CHIKALI TO DHAD - [N24001061]MoRTH,MAHARASHTRA	03/2018	189.46 189.00	12/2019 -	-
323	DHAD BHOKARDAN TO BHOKARDHAN SILLOD - [N24001062]MoRTH,MAHARASHTRA	03/2018	336.21 336.00	12/2019 -	-
324	WADIGODRI TO DHANGRIPIMPRI - [N24001063]MoRTH,MAHARASHTRA	03/2018	194.23 194.00	02/2020 -	-
325	DHANGRIPIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK - [N24001064]MoRTH,MAHARASHTRA	03/2018	217.14 217.00	02/2020 -	-
326	PARBHANI TO GANGKHED - [N24001065]MoRTH,MAHARASHTRA	03/2018	238.19 238.00	12/2019 -	-
327	LATUR TO PANGAON - [N24001066]MoRTH,MAHARASHTRA	03/2018	336.47 336.00	12/2019 -	-
328	OMREGA TO AUSA - [N24001067]MoRTH,MAHARASHTRA	03/2018	272.04 272.00	12/2019 -	-
329	WASHIM TO DASTAPUR - [N24001068]MoRTH,MAHARASHTRA	03/2018	165.51 -	12/2019 -	-
330	NANDED TO JALKOT - [N24001069]MoRTH,MAHARASHTRA	12/2017	456.93 457.00	09/2019 -	-
331	DASTAPUR TO KARANJA - [N24001070]MoRTH,MAHARASHTRA	03/2018	182.63 -	12/2019 -	-
332	JALKOT TO TOGRI - [N24001071]MoRTH,MAHARASHTRA	07/2018	299.92 300.00	08/2020 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
333	KHERDA TO NAGZARI - [N24001072]MoRTH,MAHARASHTRA	03/2018	181.30 -	12/2019 -	-
334	KOTHARI TO DHANORA - [N24001073]MoRTH,MAHARASHTRA	09/2018	301.38 301.00	08/2020 -	-
335	KHAMGAON TO DEULGAON SAKARSHA - [N24001074]MoRTH,MAHARASHTRA	03/2018	249.29 -	12/2019 -	-
336	OSMANNAGAR TO KUNDRAL - [N24001075]MoRTH,MAHARASHTRA	09/2017	344.25 344.00	08/2020 -	-
337	DEULGAON SAKARSHA TO MEHKAR - [N24001076]MoRTH,MAHARASHTRA	03/2018	219.91 -	12/2019 -	-
338	KUNDRAL TO WAZAR - [N24001077]MoRTH,MAHARASHTRA	01/2018	225.25 225.00	12/2019 -	-
339	PUNE TO MALE VILLAGE - [N24001078]MoRTH,MAHARASHTRA	03/2018	228.31 -	12/2019 -	-
340	ARDHAPUR TO HIMAYATNAGAR - [N24001079]MoRTH,MAHARASHTRA	12/2017	426.06 426.00	06/2020 -	-
341	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER - [N24001080]MoRTH,MAHARASHTRA	03/2018	256.15 -	12/2019 -	-
342	HIMAYATNAGAR TO PHULSAWANGI - [N24001081]MoRTH,MAHARASHTRA	03/2018	294.87 295.00	12/2019 -	-
343	PUNE RAIGARH DISTRICT BORDER TO MANGAON - [N24001082]MoRTH,MAHARASHTRA	03/2018	223.46 -	12/2019 -	-
344	CHIKLI TO TAKARKHED - [N24001083]MoRTH,MAHARASHTRA	03/2018	393.10 393.00	12/2019 -	-
345	PAHUR TO BODHWAD - [N24001084]MoRTH,MAHARASHTRA	01/2017	244.93 -	05/2020 -	-
346	TAKARKHED TO JALNA - [N24001085]MoRTH,MAHARASHTRA	09/2017	417.90 418.00	06/2019 -	-
347	BODHWAD TO STATE BORDER - [N24001086]MoRTH,MAHARASHTRA	01/2017	178.26 -	07/2019 -	-
348	MANGRUPHIR TO MAHAN - [N24001087]MoRTH,MAHARASHTRA	03/2018	222.13 222.00	11/2019 -	-
349	JALGAON TO NANDURA - [N24001088]MoRTH,MAHARASHTRA	03/2018	177.84 177.00	12/2019 -	-
350	MALEGAON TO RISOD - [N24001089]MoRTH,MAHARASHTRA	02/2018	303.24 303.00	12/2019 -	-
351	KOLDE TO KHETIYA - [N24001090]MoRTH,MAHARASHTRA	01/2017	509.18 -	07/2019 -	-
352	SATARA TO MHASWAD - [N24001092]MoRTH,MAHARASHTRA	01/2017	653.46 -	07/2019 -	-
353	ARNI TO NAIGAINBANDI - [N24001093]MoRTH,MAHARASHTRA	12/2017	309.94 310.00	12/2019 -	-
354	NAIGAONBANDI TO MANGRULPIR - [N24001094]MoRTH,MAHARASHTRA	12/2017	244.04 244.00	03/2019 -	-
355	SATARA MURVAD PILLOV PANDHARPUR - [N24001095]MoRTH,MAHARASHTRA	01/2017	388.44 -	- -	-
356	TALEGAON TO GONAPUR - [N24001096]MoRTH,MAHARASHTRA	01/2018	264.41 264.00	03/2019 -	-
357	SELDOH TO PANVAR - [N24001097]MoRTH,MAHARASHTRA	07/2018	404.33 404.00	05/2020 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
358	WARDHA TO HINGAGHAT - [N24001098]MoRTH,MAHARASHTRA	01/2018	216.90 217.00	12/2019 -	-
359	MHASWAD TO TEMBHURNI - [N24001099]MoRTH,MAHARASHTRA	01/2017	488.60 -	07/2019 -	-
360	AHMEDNAGAR TO BARAMATI - [N24001100]MoRTH,MAHARASHTRA	01/2017	955.40 -	08/2019 -	-
361	KURUDWADI TO PANDHARPUR - [N24001101]MoRTH,MAHARASHTRA	01/2017	307.63 -	07/2019 -	-
362	PANDHARPUR TO SANGOLA - [N24001102]MoRTH,MAHARASHTRA	07/2017	218.38 -	07/2019 -	-
363	SARAD VANI PIMPALGAON - [N24001103]MoRTH,MAHARASHTRA	01/2017	250.46 -	07/2019 -	-
364	MALEWADA TO CHIMUR - [N24001104]MoRTH,MAHARASHTRA	10/2016	322.55 -	06/2019 -	-
365	CHIMUR TO WARORA - [N24001105]MoRTH,MAHARASHTRA	11/2016	467.70 -	03/2019 -	-
366	PEN TO KHOPOLI - [N24001106]MoRTH,MAHARASHTRA	03/2018	301.39 302.00	03/2018 -	-
367	PANCHARAL TO MANDANGHAR - [N24001107]MoRTH,MAHARASHTRA	07/2018	381.08 302.00	05/2020 -	-
368	CHALISGAON TO NANDGAON - [N24001108]MoRTH,MAHARASHTRA	03/2018	206.97 207.00	12/2019 -	-
369	KUSUMBA TO MALEGAON - [N24001109]MoRTH,MAHARASHTRA	03/2018	243.45 244.00	12/2019 -	-
370	BAMNI TO NAVAEGAON - [N24001110]MoRTH,MAHARASHTRA	09/2017	241.69 242.00	04/2020 -	-
371	KOLHA TO NASRATPUR - [N24001111]MoRTH,MAHARASHTRA	04/2016	281.78 282.00	04/2019 -	-
372	NASRATPUR TO BARASGAON - [N24001112]MoRTH,MAHARASHTRA	07/2016	406.54 407.00	09/2019 -	-
373	BARASGAON TO RAHATEE - [N24001113]MoRTH,MAHARASHTRA	07/2016	289.11 290.00	09/2018 -	-
374	INDAPUR TO VADPALE - [N24001114]MoRTH,MAHARASHTRA	01/2017	1,202.52 1,203.00	12/2019 -	-
375	VADPALE TO BHOGAN KHURD - [N24001115]MoRTH,MAHARASHTRA	01/2017	1,598.47 1,560.00	11/2019 -	-
376	GADCHIROLI TO MUL - [N24001116]MoRTH,MAHARASHTRA	12/2016	484.15 -	06/2019 -	-
377	MUL TO CHANDRAPUR - [N24001117]MoRTH,MAHARASHTRA	12/2016	162.34 -	07/2019 -	-
378	SAKOLI TO BHANDARA - [N24001118]MoRTH,MAHARASHTRA	01/2017	362.96 -	06/2019 -	-
379	NAGBHID TO ARMORI - [N24001119]MoRTH,MAHARASHTRA	09/2016	269.05 -	07/2019 -	-
380	NASHIK TO PETH - [N24001121]MoRTH,MAHARASHTRA	12/2015	289.60 -	11/2018 -	-
381	PAITHAN TO SHIRUR - [N24001122]MoRTH,MAHARASHTRA	03/2017	341.80 -	06/2019 -	-
382	SHIRUR TO KHARDA - [N24001123]MoRTH,MAHARASHTRA	02/2017	381.77 -	06/2019 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
383	AURANGABAD TO SILLOD - [N24001124]MoRTH,MAHARASHTRA	02/2017	456.32 -	06/2019 -	-
384	SILLOD TO FARDAPUR - [N24001125]MoRTH,MAHARASHTRA	02/2017	337.46 -	06/2019 -	-
385	FARDAPUR TO JALGAON - [N24001126]MoRTH,MAHARASHTRA	02/2017	456.45 -	06/2019 -	-
386	KUMBHARI PHTA TO DEULGAON RAJA - [N24001127]MoRTH,MAHARASHTRA	02/2017	406.51 -	06/2019 -	-
387	BHOKAR TO SARSAM - [N24001128]MoRTH,MAHARASHTRA	02/2017	295.09 -	07/2019 -	-
388	BHOGAN KHURD TO KASHEDI - [N24001132]MoRTH,MAHARASHTRA	09/2017	743.21 743.00	06/2021 -	-
389	PARSHURAM GHAT TO ARAWALI - [N24001133]MoRTH,MAHARASHTRA	04/2016	983.14 983.00	12/2019 -	-
390	KANTE TO WAKED - [N24001134]MoRTH,MAHARASHTRA	03/2016	1,230.02 1,230.00	11/2019 -	-
391	WAKED TO TALEGAON - [N24001135]MoRTH,MAHARASHTRA	02/2016	1,244.75 1,245.00	02/2019 -	-
392	TALGAON TO KALMATH - [N24001136]MoRTH,MAHARASHTRA	10/2016	904.70 905.00	03/2020 -	-
393	KALMATH TO ZARAP - [N24001137]MoRTH,MAHARASHTRA	09/2016	1,338.13 1,338.00	03/2020 -	-
394	PARLI PIMPLA DAHIGUDA - [N24001138]MoRTH,MAHARASHTRA	02/2017	205.72 206.00	06/2019 -	-
395	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH - [N24001141]MoRTH,UTTAR PRADESH	03/2016	240.30 240.00	01/2020 -	-
396	RISOD TO HINGOLI - [N24001149]MoRTH,MAHARASHTRA	02/2018	355.99 -	12/2019 -	-
397	WARDHA TO ARVI - [N24001150]MoRTH,MAHARASHTRA	02/2018	313.58 -	04/2020 -	-
398	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS - PA - [N24001156]MoRTH,KARNATAKA	01/2017	166.67 -	09/2017 -	-
399	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH - [N24001157]MoRTH,KARNATAKA	08/2016	175.50 -	02/2017 -	-
400	RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2 - [N24001158]MoRTH,KARNATAKA	03/2018	159.97 -	06/2019 -	-
401	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION - [N24001159]MoRTH,KARNATAKA	01/2018	159.70 -	07/2018 -	-
402	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR - [N24001160]MoRTH,KARNATAKA	09/2017	191.60 -	10/2018 -	-
403	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH - [N24001161]MoRTH,KARNATAKA	12/2017	297.30 -	01/2019 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
404	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN - [N24001162]MoRTH,KARNATAKA	03/2018	325.86 -	10/2018 -	-
405	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001163]MoRTH,KARNATAKA	08/2016	329.01 -	02/2017 -	-
406	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN - [N24001164]MoRTH,KARNATAKA	10/2016	396.96 -	03/2017 -	-
407	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT - [N24001165]MoRTH,KARNATAKA	11/2016	314.90 -	03/2017 -	-
408	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775) - [N24001166]MoRTH,KARNATAKA	03/2015	159.12 -	01/2016 -	-
409	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT - [N24001168]MoRTH,KARNATAKA	05/2018	171.60 -	05/2018 -	-
410	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U - [N24001172]MoRTH,KARNATAKA	01/2017	291.49 -	08/2017 -	-
411	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI - JADERCELA SECTION - [N24001173]MoRTH,KARNATAKA	02/2017	157.32 188.00	05/2019 -	-
412	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260. - [N24001174]MoRTH,MANIPUR	10/2016	235.31 -	11/2020 -	-
413	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M - [N24001178]MoRTH,NAGALAND	11/2016	336.25 369.96	09/2019 -	-
414	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN. - [N24001200]MoRTH,RAJASTHAN	03/2019	178.13 -	- -	-
415	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00 - [N24001201]MoRTH,BIHAR	02/2019	2,926.42 -	- -	-
416	REHABILITATION AND UPGRADATION OF ALLAHABAD -MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT - [N24001203]MoRTH,UTTAR PRADESH	10/2016	218.90 -	03/2020 -	-
417	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO - [N24001204]MoRTH,UTTAR PRADESH	07/2016	208.88 -	10/2019 -	-
418	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF - [N24001207]MoRTH,UTTAR PRADESH	03/2018	185.18 -	02/2020 -	-
419	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T - [N24001211]MoRTH,UTTAR PRADESH	11/2018	281.45 -	- -	-
420	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM - [N24001239]MoRTH,TAMIL NADU	03/2018	240.38 204.73	06/2019 -	-
421	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1) - [N24001289]MoRTH,ARUNACHAL PRADESH	03/2019	403.68 -	02/2020 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
422	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2 - [N24001290]MoRTH,ARUNACHAL PRADESH	03/2019	342.55 -	02/2020 -	-
423	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE - [N24001291]MoRTH,ARUNACHAL PRADESH	03/2019	421.48 -	11/2020 -	-
424	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE - [N24001292]MoRTH,ARUNACHAL PRADESH	03/2019	543.05 -	11/2020 -	-
425	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE - [N24001293]MoRTH,ARUNACHAL PRADESH	03/2019	486.70 -	10/2020 -	-
426	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE - [N24001294]MoRTH,ARUNACHAL PRADESH	03/2019	560.39 -	02/2020 -	-
427	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE - [N24001295]MoRTH,ARUNACHAL PRADESH	03/2019	347.78 -	09/2020 -	-
428	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAGE - [N24001296]MoRTH,ARUNACHAL PRADESH	03/2019	394.27 -	10/2020 -	-
429	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE - [N24001297]MoRTH,ARUNACHAL PRADESH	03/2019	450.65 -	11/2020 -	-
430	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK - [N24001369]MoRTH,KERALA	02/2017	294.28 -	08/2017 -	-
431	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49) - [N24001370]MoRTH,KERALA	02/2017	380.76 -	09/2017 -	-
432	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU - [N24001194]MoRTH,ARUNACHAL PRADESH	09/2011	1,979.00 -	- 03/2020	-
	<u>National Highways And Infrastructure Development Corporation Ltd.</u>				
433	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI - [N24000685]NHIDCL,ARUNACHAL PRADESH	02/2017	167.28 -	04/2017 -	08/2020
434	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX - [N24000683]NHIDCL,ARUNACHAL PRADESH	02/2017	180.57 -	04/2017 -	02/2021
435	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00 - [N24000688]NHIDCL,NAGALAND	03/2016	429.52 -	08/2016 -	02/2021
436	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH - [N24000327]NHIDCL,ARUNACHAL PRADESH	03/2015	394.00 522.86	06/2018 -	03/2021
437	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN - [N24000978]NHIDCL,ARUNACHAL PRADESH	03/2015	172.75 -	- -	03/2021
438	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI - [N24000979]NHIDCL,ARUNACHAL PRADESH	01/2017	256.66 -	- -	03/2021

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
439	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1 - [N24000686]NHIDCL,NAGALAND	03/2016	373.07 -	08/2016 -	05/2021
440	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1 - [N24000687]NHIDCL,NAGALAND	03/2016	396.52 -	08/2016 -	05/2021
441	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S - [N24000328]NHIDCL,TRIPURA	10/2014	369.00 -	03/2018 -	-
442	RHENOK-RORATHANG-PAKYONG ON NH 717A - [N24000695]NHIDCL,SIKKIM	04/2017	388.00 -	10/2017 -	-
443	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00 - [N24000767]NHIDCL,SIKKIM	03/2017	375.80 -	- -	-
444	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM - [N24000769]NHIDCL,SIKKIM	03/2018	264.84 -	06/2018 -	-
445	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0 - [N24000866]NHIDCL,JAMMU AND KASHMIR	03/2018	404.17 -	08/2018 -	-
446	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM - [N24000867]NHIDCL,JAMMU AND KASHMIR	03/2018	216.00 -	11/2018 -	-
447	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA - [N24000868]NHIDCL,JAMMU AND KASHMIR	03/2018	253.44 -	07/2019 -	-
<u>National Highways Authority Of India</u>					
448	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S - [N24000815]NHAI,GUJARAT	03/2018	2,702.05 -	- -	06/2021
449	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE - [N24001340]NHAI,MADHYA PRADESH	11/2019	716.00 -	07/2021 -	07/2021
450	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001377]NHAI,MAHARASHTRA	02/2019	731.89 -	11/2019 -	11/2019
451	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001378]NHAI,MAHARASHTRA	02/2019	362.46 -	11/2019 -	11/2019
452	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965 - [N24001379]NHAI,MAHARASHTRA	02/2019	594.75 -	11/2019 -	11/2019
453	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20) - [N24000049]NHAI,ASSAM	12/2003	160.00 -	05/2008 -	06/2019
454	BRAHMPUTRA BRIDGE,NH NO-31 - [N24000063]NHAI,ASSAM	12/2003	217.61 -	04/2010 -	07/2019
455	NALBARI TO BIJNI (AS-6) - [N24000047]NHAI,ASSAM	12/2003	225.00 -	06/2008 -	09/2019
456	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGAU - [N24000586]NHAI,RAJASTHAN	06/2016	637.18 -	06/2019 -	09/2019
457	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47 - [N24000459]NHAI,KERALA	06/2015	845.24 -	- 01/2020	01/2020
458	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA - [N24000426]NHAI,RAJASTHAN	11/2012	530.07 -	08/2016 -	06/2020

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
459	SONAPUR TO GUWAHTI (AS-3) - [N24000044]NHAI,ASSAM	12/2003	245.00 -	03/2008 -	08/2020
460	GWALIOR-JHANSI, NH-75 - [N24000089]NHAI,MULTI STATE	12/2003	604.00 -	12/2009 09/2020	09/2020
461	QUAZIGUND-BANIHAI KM.220.00 TO KM.188.00 - [N24000161]NHAI,JAMMU AND KASHMIR	07/2010	1,987.00 -	07/2015 -	09/2020
462	SRINAGAR TO BANIHAI - [N24000189]NHAI,JAMMU AND KASHMIR	06/2011	1,100.70 -	06/2014 -	10/2020
463	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D - [N24000432]NHAI,MAHARASHTRA	09/2015	414.51 -	05/2018 11/2020	11/2020
464	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL - [N24000554]NHAI,KARNATAKA	03/2016	870.00 -	03/2019 -	11/2020
465	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION - [N24000462]NHAI,KARNATAKA	05/2014	1,655.01 -	08/2016 -	12/2020
466	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB - [N24000602]NHAI,KARNATAKA	08/2016	1,664.20 -	04/2020 -	12/2020
467	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P - [N24000835]NHAI,HARYANA	03/2018	1,484.30 -	- 06/2021	12/2020
468	CONSTRUCTION OF STAND ALONE RING ROAD/BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE - [N24000717]NHAI,JAMMU AND KASHMIR	12/2017	1,471.75 1,339.00	- -	01/2021
469	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF - [N24000801]NHAI,GUJARAT	02/2018	1,052.21 -	- -	01/2021
470	NALBARI T BIJNI (AS-7) - [N24000048]NHAI,ASSAM	12/2003	208.00 -	04/2008 -	02/2021
471	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS - [N24000810]NHAI,ANDHRA PRADESH	03/2018	565.09 -	- -	02/2021
472	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE - [N24000710]NHAI,TAMIL NADU	12/2017	379.90 -	- -	03/2021
473	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF - [N24000814]NHAI,CHHATISGARH	03/2018	1,029.96 -	- -	03/2021
474	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI-KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700) - [N24000807]NHAI,ANDHRA PRADESH	03/2018	1,532.62 -	03/2021 10/2021	04/2021
475	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE - [N24000666]NHAI,BIHAR	03/2017	235.48 -	03/2020 -	05/2021
476	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II - CONSTRUCTION OF NH-348 - PKG3 - [N24000451]NHAI,MAHARASHTRA	08/2015	505.00 -	05/2018 04/2019	06/2021
477	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700) - [N24000627]NHAI,MAHARASHTRA	11/2016	1,071.61 -	- 10/2021	07/2021
478	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00) - [N24000628]NHAI,MAHARASHTRA	11/2016	1,064.88 -	- 01/2022	07/2021
479	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROPUR IN THE STATE OF PUNJAB - [N24000791]NHAI,PUNJAB	02/2018	261.76 -	- -	07/2021

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
480	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S - [N24000833]NHAI,GUJARAT	03/2018	1,437.64 -	- -	07/2021
481	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF - [N24000851]NHAI,MAHARASHTRA	03/2018	1,162.92 -	- -	07/2021
482	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700 - [240106277]NHAI,ASSAM	12/2003	280.00 -	02/2009 -	-
483	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000 - [240106278]NHAI,ASSAM	12/2003	199.81 -	04/2009 -	-
484	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54 - [240106279]NHAI,ASSAM	12/2003	167.64 -	11/2008 -	-
485	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450 - [240106280]NHAI,ASSAM	12/2003	155.04 -	11/2008 -	-
486	HARANGAJO TO MAIBANG, NH-54 - [N24000062]NHAI,ASSAM	12/2003	196.00 -	07/2009 -	-
487	DELHI/ HARYANA BORDER TO ROHTAK - [N24000122]NHAI,HARYANA	04/2007	486.00 -	05/2010 -	-
488	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION - [N24000125]NHAI,GUJARAT	03/2010	1,509.10 -	09/2012 -	-
489	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502 - [N24000131]NHAI,MULTI STATE	02/2009	1,693.75 -	08/2011 -	-
490	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM) - [N24000133]NHAI,HARYANA	05/2009	1,108.00 3,485.00	11/2011 -	-
491	INDORE-JHABUA-GUJRAT/MP - [N24000136]NHAI,MADHYA PRADESH	10/2010	1,175.00 -	04/2013 -	-
492	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER - [N24000138]NHAI,KARNATAKA	09/2010	946.00 -	06/2018 -	-
493	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM - [N24000149]NHAI,KERALA	02/2010	617.00 -	08/2012 -	-
494	4 LANING OF NAGPUR-BETUL - [N24000155]NHAI,MULTI STATE	02/2011	2,498.76 -	08/2014 -	-
495	INDORE-DEWAS(NH-3) - [N24000159]NHAI,MADHYA PRADESH	11/2010	325.00 -	05/2013 -	-
496	NASHRI- CHANANI - [N24000162]NHAI,JAMMU AND KASHMIR	05/2011	2,159.00 -	06/2015 -	-
497	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00 - [N24000163]NHAI,JAMMU AND KASHMIR	07/2010	1,813.76 -	07/2013 -	-
498	PATNA-MUZZAFFARPUR - [N24000165]NHAI,BIHAR	08/2010	671.30 -	02/2013 -	-
499	GHAZIABAD-ALIGARH NH-91 - [N24000170]NHAI,UTTAR PRADESH	02/2011	1,141.00 -	08/2013 -	-
500	KANDLA - MUNDRA PORT - [N24000175]NHAI,GUJARAT	01/2011	953.88 -	07/2013 -	-
501	TIRUPATI - TIRUTHANI - CHENNAI - [N24000178]NHAI,ANDHRA PRADESH	04/2011	571.00 -	10/2013 -	-
502	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547 - [N24000183]NHAI,ANDHRA PRADESH	11/2011	1,535.00 -	05/2014 -	-
503	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95 - [N24000185]NHAI,BIHAR	09/2011	574.00 -	03/2014 -	-

Costing Rs. 150 Crore and above				(August 2021)	
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
504	2-LANNING WITH PS MOTIHARI-RAXAUL - [N24000186]NHAI, BIHAR	10/2011	375.09 -	04/2014 -	-
505	4-LANNING OF CHAPRA-HAJIPUR - [N24000187]NHAI, BIHAR	01/2011	575.00 -	07/2013 12/2021	-
506	2 LANNING OF MUZAFFARPUR - SONBARSA - [N24000188]NHAI, BIHAR	05/2011	511.54 -	11/2013 -	-
507	PANIKHOLI-RIMOLI - [N24000197]NHAI, ODISHA	03/2012	1,410.00 -	09/2014 -	-
508	MUZAFFARNAGAR-HARIDWAR - [N24000201]NHAI, MULTI STATE	09/2011	754.00 -	03/2013 -	-
509	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR - [N24000205]NHAI, ODISHA	12/2011	1,047.00 -	06/2014 -	-
510	6-LANING OF DHANKUNI-KHARAGPUR SECTION - [N24000206]NHAI, WEST BENGAL	04/2012	1,396.18 -	09/2014 -	-
511	2-LANING WITH PS RAIBAREILI TO ALLAHABAD - [N24000208]NHAI, UTTAR PRADESH	07/2012	291.36 -	01/2014 -	-
512	ETAWAH CHAKÉRI - [N24000219]NHAI, UTTAR PRADESH	03/2013	1,573.00 -	09/2015 -	-
513	AHMEDABAD TO VADODARA SECTION - [N24000222]NHAI, GUJARAT	01/2013	2,125.24 -	12/2015 -	-
514	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50 - [N24000230]NHAI, MAHARASHTRA	05/2013	1,348.20 -	02/2014 -	-
515	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM) - [N24000232]NHAI, HIMACHAL PRADESH	11/2013	1,916.79 -	11/2016 -	-
516	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9 - [N24000233]NHAI, TELANGANA	04/2014	1,266.60 -	09/2016 -	-
517	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR - [N24000344]NHAI, RAJASTHAN	09/2014	425.19 -	09/2016 -	-
518	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120 - [N24000349]NHAI, TAMIL NADU	05/2015	1,387.11 -	11/2017 -	-
519	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR - [N24000350]NHAI, TAMIL NADU	06/2015	563.92 -	12/2017 -	-
520	FOUR LANING OF VARANASI BYPASS - [N24000356]NHAI, UTTAR PRADESH	05/2015	261.09 -	05/2017 -	-
521	THIRUMAYAM - MANAMADURAI SECTION - [N24000359]NHAI, TAMIL NADU	07/2014	401.11 -	01/2017 -	-
522	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232 - [N24000360]NHAI, UTTAR PRADESH	04/2014	351.34 -	01/2016 -	-
523	VADODARA-SURAT SECTION - [N24000361]NHAI, GUJARAT	03/2014	503.16 -	08/2016 -	-
524	2 LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125 - [N24000362]NHAI, UTTAR PRADESH	09/2015	368.73 -	09/2016 -	-
525	2-LANING WITH PAVED SHOULDERS OF TANDA -RAEBARELI - [N24000367]NHAI, UTTAR PRADESH	04/2014	495.78 -	01/2016 -	-
526	2 LANING WITH PS OF GULABPURA - UNIARA - [N24000423]NHAI, RAJASTHAN	10/2015	597.00 -	10/2017 -	-
527	4 LANING OF BAHARAGORA - SINGHARA - [N24000427]NHAI, ODISHA	07/2015	1,282.94 -	- -	-
528	CONSTRUCTION OF ISLAMPUR BY PASS - [N24000437]NHAI, WEST BENGAL	10/2015	361.15 363.93	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
529	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3) - [N24000439]NHAI,MAHARASHTRA	07/2015	1,885.74 -	05/2019 -	-
530	4 LANING OF AMBALA - KAITHAL - PACKAGE -1 - [N24000443]NHAI,HARYANA	12/2015	602.95 -	06/2016 -	-
531	4 LANING OF AMBALA - KAITHAL - PACKAGE -2 - [N24000448]NHAI,HARYANA	01/2016	574.28 -	07/2018 -	-
532	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211 - [N24000453]NHAI,MAHARASHTRA	01/2015	972.50 -	07/2017 -	-
533	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION - [N24000454]NHAI,MAHARASHTRA	06/2014	923.04 -	11/2016 -	-
534	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I) - [N24000460]NHAI,UTTAR PRADESH	12/2015	611.65 -	06/2016 -	-
535	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785) - [N24000463]NHAI,WEST BENGAL	12/2015	1,083.00 2,587.75	06/2018 -	-
536	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II - [N24000468]NHAI,MADHYA PRADESH	03/2015	795.76 -	- -	-
537	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I - [N24000469]NHAI,MADHYA PRADESH	03/2015	794.30 -	- -	-
538	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A - [N24000471]NHAI,JAMMU AND KASHMIR	12/2015	2,168.66 -	06/2019 -	-
539	FOUR LANING OF PATNA TO KOILWAR - [N24000473]NHAI,BIHAR	08/2015	556.07 -	- -	-
540	GURGAON - KOTPUTLI - JAIPUR (SIX LANE) - [N24000477]NHAI,RAJASTHAN	02/2008	1,673.70 -	10/2011 -	-
541	FOUR LANING OF PARWANOO -SOLAN - [N24000479]NHAI,HIMACHAL PRADESH	09/2015	934.46 -	03/2018 -	-
542	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31 - [N24000480]NHAI,BIHAR	12/2015	1,041.10 -	04/2019 -	-
543	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A - [N24000488]NHAI,JAMMU AND KASHMIR	12/2015	2,136.97 -	12/2018 -	-
544	FOUR LANING OF JABALPUR - LAKHNADON - [N24000489]NHAI,MADHYA PRADESH	03/2015	928.83 -	- -	-
545	FOUR LANING OF HOSPET - CHITRADURGA - [N24000490]NHAI,KARNATAKA	03/2015	1,388.00 -	08/2018 -	-
546	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II) - [N24000491]NHAI,UTTAR PRADESH	01/2016	815.28 -	06/2018 -	-
547	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I) - [N24000493]NHAI,UTTAR PRADESH	01/2016	1,027.53 -	06/2018 -	-
548	FOUR LANING OF GWALIOR-SHIVPURI - [N24000494]NHAI,MADHYA PRADESH	05/2013	1,055.00 -	11/2015 -	-
549	FOUR LANING OF SIMGA - SARAGAON - [N24000495]NHAI,CHHATISGARH	12/2015	596.67 -	05/2018 -	-
550	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA - [N24000496]NHAI,MADHYA PRADESH	06/2015	1,012.90 -	03/2016 -	-
551	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III) - [N24000498]NHAI,UTTAR PRADESH	06/2016	667.00 -	07/2018 -	-
552	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II) - [N24000499]NHAI,UTTAR PRADESH	12/2015	667.00 -	06/2018 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
553	FOUR LANING OF FORBESGANJ - JOGBANI - [N24000501]NHAI, BIHAR	08/2015	322.09 247.00	04/2018 -	-
554	FOUR LANING OF SARAGAON - BILASPUR - [N24000502]NHAI, CHHATISGARH	12/2015	509.13 -	04/2018 -	-
555	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV - [N24000504]NHAI, MADHYA PRADESH	03/2015	810.22 -	- -	-
556	FOUR LANING OF BHOJPUR TO BUXAR - [N24000506]NHAI, BIHAR	01/1991	642.41 -	- -	-
557	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31 - [N24000507]NHAI, BIHAR	12/2015	1,167.45 -	- -	-
558	FOUR LANING OF AURANGABAD - YEDISHI - [N24000508]NHAI, MAHARASHTRA	07/2015	1,871.34 -	01/2018 -	-
559	FOUR LANING FROM MPMHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS - [N24000509]NHAI, MAHARASHTRA	04/2010	1,170.52 -	06/2012 -	-
560	SIX-LANING OF BARWA ADDA-PANAGARH - [N24000515]NHAI, WEST BENGAL	04/2014	1,665.00 -	- -	-
561	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44- [N24000517]NHAI, MEGHALAYA	12/2015	479.20 -	05/2018 -	-
562	TWO LANING WITH PS OF BIHARAHARIF -BARBIGHA - MOKAMA - [N24000518]NHAI, BIHAR	08/2015	399.54 -	04/2019 -	-
563	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS - DHOLPUR - [N24000520]NHAI, RAJASTHAN	08/2015	275.90 -	- -	-
564	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ - [N24000521]NHAI, BIHAR	08/2015	854.80 -	- -	-
565	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR - [N24000522]NHAI, BIHAR	08/2015	516.13 -	04/2018 -	-
566	TRICHY - KARUR - [N24000528]NHAI, TAMIL NADU	03/2007	516.00 -	07/2008 -	-
567	MEERUT-BULANDSHAHAR - [N24000539]NHAI, UTTAR PRADESH	01/2016	683.24 -	- -	-
568	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM - [N24000541]NHAI, UTTAR PRADESH	01/2016	1,081.57 -	06/2019 -	-
569	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62 - [N24000542]NHAI, MAHARASHTRA	03/2016	197.69 -	07/2018 -	-
570	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020 - [N24000544]NHAI, UTTAR PRADESH	03/2016	676.73 -	04/2019 -	-
571	FOUR LANNING OF NH-9 FROM VIJAYWADA-MACHLIPATNAM (KM 0.000 TO 63.800) - [N24000545]NHAI, ANDHRA PRADESH	01/2016	1,134.97 -	11/2018 -	-
572	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345) - [N24000546]NHAI, HIMACHAL PRADESH	02/2016	273.20 -	02/2019 -	-
573	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKHPUR) - [N24000547]NHAI, UTTAR PRADESH	03/2016	1,404.50 -	- -	-
574	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR - [N24000549]NHAI, UTTAR PRADESH	03/2016	1,396.74 -	- -	-
575	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION - [N24000550]NHAI, ODISHA	02/2016	1,069.65 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
576	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV] - [N24000551]NHAI,UTTAR PRADESH	03/2016	1,587.49 -	04/2019 -	-
577	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA - [N24000553]NHAI, WEST BENGAL	03/2016	229.37 -	11/2018 -	-
578	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791 - [N24000556]NHAI,UTTAR PRADESH	03/2016	899.00 -	04/2019 -	-
579	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88 - [N24000559]NHAI,UTTARAKHAND	03/2016	720.00 -	- -	-
580	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900 - [N24000562]NHAI,UTTARAKHAND	03/2016	1,443.00 -	- -	-
581	4-LANING OF GAGALHERI- SAHARANPUR- YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (- [N24000563]NHAI,UTTAR PRADESH	03/2016	1,668.00 -	- -	-
582	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00 - [N24000564]NHAI,UTTAR PRADESH	03/2016	1,408.00 -	- -	-
583	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00 - [N24000565]NHAI,UTTAR PRADESH	03/2016	1,737.00 -	- -	-
584	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T - [N24000566]NHAI,KERALA	04/2016	804.97 -	06/2018 -	-
585	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6. - [N24000567]NHAI,GUJARAT	05/2016	998.18 -	- -	-
586	FOUR LANING OF TALAJA - MAHUVA SECTION OF NH - 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR - [N24000568]NHAI,GUJARAT	05/2016	834.64 -	- -	-
587	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST - [N24000569]NHAI,GUJARAT	05/2016	723.64 -	- -	-
588	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU - [N24000570]NHAI,GUJARAT	05/2016	763.08 -	- -	-
589	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME - [N24000571]NHAI,GUJARAT	05/2016	425.60 -	- -	-
590	FOUR LANING OF MAHUVA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM - [N24000587]NHAI,RAJASTHAN	06/2016	763.23 -	06/2019 -	-
591	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF NH-112 (EXISTING KM 0+000TO KM - [N24000589]NHAI,RAJASTHAN	06/2016	649.00 -	06/2019 -	-
592	BALANCE WORK OF 4 LANING OF GORAKPUR -GOPALGANJ - [N24000590]NHAI,BIHAR	05/2015	581.84 -	05/2017 -	-
593	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A - [N24000591]NHAI,RAJASTHAN	07/2016	688.70 -	- -	-
594	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000 - [N24000592]NHAI,GUJARAT	07/2016	829.97 -	- -	-
595	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM - [N24000593]NHAI,RAJASTHAN	07/2016	331.46 -	10/2018 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
596	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH- - [N24000594]NHAI,JHARKHAND	07/2016	458.03 -	- -	-
597	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500 - [N24000599]NHAI,UTTAR PRADESH	08/2016	2,016.00 -	04/2019 -	-
598	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE) - [N24000600]NHAI,PUNJAB	08/2016	1,388.34 -	09/2019 -	-
599	4 LANING FROM PHAGWARA TO RUPNAGAR - [N24000601]NHAI,PUNJAB	08/2016	1,169.61 1,367.00	- -	-
600	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION - [N24000605]NHAI,MADHYA PRADESH	08/2016	227.49 -	01/2019 -	-
601	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS - [N24000606]NHAI,HIMACHAL PRADESH	08/2016	1,583.18 -	- -	-
602	FOUR LANING OF BARHI-HAZARIBAGH NH-33 - [N24000607]NHAI,JHARKHAND	08/2016	323.72 -	08/2018 -	-
603	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH - [N24000613]NHAI,HIMACHAL PRADESH	09/2016	1,273.71 -	- -	-
604	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S - [N24000619]NHAI,ODISHA	09/2016	2,510.04 -	08/2019 -	-
605	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA - [N24000620]NHAI,WEST BENGAL	09/2016	767.03 -	08/2018 -	-
606	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (- [N24000621]NHAI,RAJASTHAN	09/2016	1,239.82 -	- -	-
607	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM - [N24000622]NHAI,KARNATAKA	09/2016	950.69 1,918.36	08/2019 -	-
608	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I - [N24000623]NHAI,RAJASTHAN	09/2016	1,100.19 -	- -	-
609	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP - [N24000624]NHAI,MULTI STATE	09/2016	1,244.10 -	- -	-
610	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI - [N24000629]NHAI,MAHARASHTRA	11/2016	400.25 -	03/2019 -	-
611	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT - [N24000630]NHAI,MAHARASHTRA	11/2016	446.17 -	03/2019 -	-
612	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE - [N24000631]NHAI,MAHARASHTRA	11/2016	290.73 -	- -	-
613	VIJAYAWADA-GUNDUGOLANU SECTION - [N24000632]NHAI,ANDHRA PRADESH	09/2014	1,684.00 -	02/2017 -	-
614	REHABILITAITON AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4 - [N24000633]NHAI,ODISHA	10/2016	1,008.96 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
615	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000) - [N24000634]NHAI,HIMACHAL PRADESH	10/2016	447.75 -	- -	-
616	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION - [N24000635]NHAI,GUJARAT	12/2016	417.19 -	- -	-
617	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T - [N24000637]NHAI,UTTAR PRADESH	12/2016	534.55 -	- -	-
618	4 LANING OF KASHIPUR-SITARGANJ SECTION KM. 175.000 TO KM. 252.20 - [N24000638]NHAI,UTTARAKHAND	11/2012	605.84 -	07/2018 -	-
619	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650 - [N24000648]NHAI,UTTAR PRADESH	01/2017	450.68 -	- -	-
620	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG. - [N24000649]NHAI,GUJARAT	01/2017	1,251.11 1,361.00	- -	-
621	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST - [N24000650]NHAI,MAHARASHTRA	01/2017	244.90 -	05/2019 -	-
622	FOUR LANNING OF TULJAPUR-AUSA SECTION - [N24000651]NHAI,MAHARASHTRA	02/2017	904.16 911.07	02/2020 03/2021	-
623	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C - [N24000654]NHAI,UTTAR PRADESH	03/2017	1,184.71 -	03/2020 -	-
624	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST - [N24000655]NHAI,MAHARASHTRA	03/2017	247.02 -	03/2020 -	-
625	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800) - [N24000656]NHAI,MAHARASHTRA	03/2017	744.64 -	03/2020 -	-
626	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690) - [N24000657]NHAI,MAHARASHTRA	03/2017	1,030.44 -	03/2020 -	-
627	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500) - [N24000658]NHAI,MAHARASHTRA	03/2017	988.34 -	03/2020 -	-
628	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580) - [N24000659]NHAI,MAHARASHTRA	03/2017	1,059.73 -	03/2017 -	-
629	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000) - [N24000660]NHAI,MAHARASHTRA	03/2017	296.19 -	03/2020 -	-
630	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575) - [N24000661]NHAI,MAHARASHTRA	03/2017	1,098.06 -	03/2020 -	-
631	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO - [N24000663]NHAI,UTTAR PRADESH	03/2017	1,989.00 -	03/2020 -	-
632	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN - [N24000665]NHAI,BIHAR	03/2017	672.89 -	03/2020 -	-
633	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000 - [N24000668]NHAI,ANDHRA PRADESH	03/2017	1,041.62 -	03/2020 -	-
634	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHA SECTION FROM KM 311.000 TO KM - [N24000671]NHAI,ODISHA	03/2017	1,288.07 -	03/2020 -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
635	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA - [N24000672]NHAI,UTTAR PRADESH	03/2017	2,064.99 -	03/2020 -	-
636	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA - [N24000674]NHAI,KARNATAKA	03/2017	831.58 -	03/2020 -	-
637	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O - [N24000675]NHAI,KARNATAKA	03/2017	993.16 -	03/2020 -	-
638	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT - [N24000693]NHAI,GUJARAT	06/2017	1,958.88 -	06/2020 -	-
639	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I) - [N24000699]NHAI,ODISHA	07/2017	476.56 -	07/2017 -	-
640	JUNAGADH BYPASS - [N24000701]NHAI,GUJARAT	10/2017	232.49 -	10/2017 -	-
641	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124. - [N24000702]NHAI,MADHYA PRADESH	10/2017	639.97 -	10/2017 -	-
642	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540 - [N24000703]NHAI,RAJASTHAN	10/2017	964.17 -	10/2017 -	-
643	4-LANNING OF THALSERRY-MAHE BYPASS - [N24000704]NHAI,KERALA	09/2017	1,124.11 -	09/2017 -	-
644	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12 - [N24000705]NHAI,MADHYA PRADESH	09/2017	374.40 -	09/2017 -	-
645	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69 - [N24000706]NHAI,MADHYA PRADESH	09/2017	990.61 -	09/2017 -	-
646	4-LANNING OF OTTANCHATRAM BYPASS - [N24000707]NHAI,TAMIL NADU	09/2017	244.27 -	09/2017 -	-
647	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO - [N24000711]NHAI,RAJASTHAN	12/2017	1,308.73 -	- -	-
648	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM - [N24000712]NHAI,UTTAR PRADESH	12/2017	1,232.21 -	- -	-
649	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15 - [N24000714]NHAI,BIHAR	12/2017	2,598.00 1,962.50	- 01/2021	-
650	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO - [N24000715]NHAI,ODISHA	12/2017	686.65 -	- -	-
651	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA - [N24000716]NHAI,ODISHA	12/2017	417.51 -	- -	-
652	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM - [N24000718]NHAI,ANDHRA PRADESH	12/2017	328.67 -	- -	-
653	SIX LANING OF NARASANNAPETA - RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN - [N24000719]NHAI,ANDHRA PRADESH	12/2017	1,323.15 -	- -	-
654	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O - [N24000720]NHAI,ANDHRA PRADESH	12/2017	357.00 -	- -	-
655	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN - [N24000721]NHAI,UTTAR PRADESH	12/2017	207.00 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
656	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O - [N24000722]NHAI,UTTAR PRADESH	12/2017	305.00 -	- -	-
657	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I - [N24000723]NHAI,BIHAR	01/2018	573.70 -	- -	-
658	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION - [N24000724]NHAI,BIHAR	01/2018	895.39 -	- -	-
659	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31 - [N24000725]NHAI,JHARKHAND	01/2018	273.46 -	- -	-
660	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION - [N24000726]NHAI,JHARKHAND	01/2018	1,155.16 -	- -	-
661	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER - [N24000728]NHAI,MADHYA PRADESH	01/2018	770.73 -	- -	-
662	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000) - [N24000730]NHAI,MAHARASHTRA	01/2018	621.00 -	- -	-
663	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2 - [N24000732]NHAI,ODISHA	01/2018	668.86 -	- -	-
664	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (- [N24000733]NHAI,ODISHA	01/2018	633.68 -	- -	-
665	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON - [N24000736]NHAI,ODISHA	01/2018	686.65 -	- -	-
666	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK - [N24000737]NHAI,ODISHA	01/2018	1,522.00 -	- -	-
667	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141 - [N24000738]NHAI,ODISHA	01/2018	999.00 -	- -	-
668	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (- [N24000739]NHAI,ODISHA	01/2018	503.88 -	- -	-
669	VARANASI RING ROAD PKG - I - [N24000740]NHAI,UTTAR PRADESH	01/2018	450.77 -	- -	-
670	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB - [N24000751]NHAI,TELANGANA	03/2017	4,429.00 -	03/2017 -	-
671	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM - [N24000783]NHAI,KARNATAKA	02/2018	486.78 -	- -	-
672	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH - [N24000784]NHAI,KERALA	02/2018	1,424.77 -	- -	-
673	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP - [N24000786]NHAI,UTTAR PRADESH	02/2018	670.50 -	- -	-
674	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA - [N24000789]NHAI,KARNATAKA	02/2018	2,177.80 -	- -	-
675	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA) - [N24000790]NHAI,WEST BENGAL	03/2018	1,261.98 2,145.96	- -	-
676	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS - [N24000792]NHAI,UTTAR PRADESH	03/2018	809.07 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
677	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR. - [N24000793]NHAI,UTTAR PRADESH	03/2018	925.40 -	- -	-
678	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION - [N24000794]NHAI, RAJASTHAN	02/2018	1,103.88 -	- -	-
679	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA - [N24000795]NHAI, RAJASTHAN	02/2018	741.86 -	- -	-
680	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA - [N24000798]NHAI,UTTAR PRADESH	03/2018	2,140.93 -	- -	-
681	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C - [N24000800]NHAI,UTTAR PRADESH	03/2018	1,120.57 -	- -	-
682	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU - [N24000802]NHAI,UTTAR PRADESH	03/2018	1,025.80 -	- -	-
683	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA - [N24000803]NHAI,UTTAR PRADESH	03/2018	1,115.28 -	- -	-
684	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K - [N24000804]NHAI, TELANGANA	03/2018	802.65 -	- -	-
685	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROA - [N24000806]NHAI,UTTAR PRADESH	02/2018	972.77 -	- -	-
686	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K - [N24000808]NHAI,ARUNACHAL PRADESH	03/2018	392.60 -	- -	-
687	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415 - [N24000812]NHAI,ANDHRA PRADESH	03/2018	557.30 -	- -	-
688	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER - [N24000813]NHAI,BIHAR	03/2018	496.20 -	- -	-
689	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM - [N24000822]NHAI, TELANGANA	03/2018	950.63 -	- -	-
690	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM 0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3 - [N24000824]NHAI, TELANGANA	03/2018	857.62 -	- -	-
691	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT - [N24000825]NHAI, TELANGANA	03/2018	828.29 -	- -	-
692	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N - [N24000828]NHAI,TAMIL NADU	03/2018	633.55 -	- -	-
693	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF N - [N24000830]NHAI,TAMIL NADU	03/2018	2,065.96 -	- -	-
694	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67. - [N24000831]NHAI,MULTI STATE	03/2018	1,294.47 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
695	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE - [N24000832]NHAI,MULTI STATE	03/2018	998.70 -	- -	-
696	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR - [N24000834]NHAI,GUJARAT	03/2018	1,161.39 -	- -	-
697	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE - [N24000836]NHAI,HARYANA	03/2018	275.12 -	- -	-
698	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTI - [N24000837]NHAI,HARYANA	03/2018	307.79 -	- -	-
699	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA - [N24000839]NHAI,HARYANA	03/2018	634.70 -	- -	-
700	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM - [N24000840]NHAI,RAJASTHAN	03/2018	1,158.35 -	- -	-
701	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I) - [N24000841]NHAI,HARYANA	03/2018	795.50 906.65	- -	-
702	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN - [N24000842]NHAI,PUNJAB	03/2018	199.90 -	- -	-
703	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI - [N24000843]NHAI,PUNJAB	03/2018	196.05 -	- -	-
704	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000) - [N24000844]NHAI,ODISHA	03/2018	806.11 -	- -	-
705	REHABILITATION AND UPGADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN - [N24000846]NHAI,HARYANA	03/2018	198.05 -	- -	-
706	REHABILITATION AND UPGADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN - [N24000848]NHAI,HARYANA	03/2018	181.78 -	- -	-
707	REDESIGNING, REHABILITATION AND UPGADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS - [N24000850]NHAI,HARYANA	03/2018	551.58 -	- -	-
708	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M - [N24000852]NHAI,HIMACHAL PRADESH	03/2018	478.74 -	- -	-
709	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4 - [N24000853]NHAI,MAHARASHTRA	03/2018	642.13 -	- -	-
710	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K - [N24000854]NHAI,JHARKHAND	03/2018	1,005.08 1,073.10	- 03/2021	-
711	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH - 14 - [N24001185]NHAI,UTTAR PRADESH	11/2017	2,159.00 -	01/2019 -	-
712	ISMAILABAD-NARNAUL PKG-5 - [N24001186]NHAI,HARYANA	01/2019	1,051.91 -	- -	-
713	ISMAILABAD-NARNAUL PKG-6 - [N24001187]NHAI,HARYANA	01/2019	1,120.06 -	- -	-

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
714	ISMAILABAD-NARNAUL PKG-7 - [N24001188]NHAI,HARYANA	01/2019	1,137.42 -	- -	-
715	ISMAILABAD-NARNAUL PKG-8 - [N24001189]NHAI,HARYANA	01/2019	1,033.19 -	- -	-
716	ISMAILABAD-NARNAUL PKG-2 - [N24001190]NHAI,HARYANA	01/2019	1,243.45 -	- -	-
717	ISMAILABAD-NARNAUL PKG-3 - [N24001191]NHAI,HARYANA	01/2019	889.36 -	- -	-
718	ISMAILABAD-NARNAUL PKG-4 - [N24001192]NHAI,HARYANA	01/2019	1,018.79 -	- -	-
719	ISMAILABAD-NARNAUL PKG-1 - [N24001193]NHAI,HARYANA	01/2019	996.65 -	- -	-
720	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T - [N24001234]NHAI,MADHYA PRADESH	02/2019	996.27 -	03/2020 -	-
721	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105 - [N24001298]NHAI,ANDHRA PRADESH	09/2018	597.67 -	01/2020 -	-
722	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA AVUTUPALLI (DESIGN - [N24001299]NHAI,ANDHRA PRADESH	09/2018	617.41 -	02/2019 -	-
723	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0 - [N24001300]NHAI,ANDHRA PRADESH	11/2019	1,226.88 -	02/2021 -	-
724	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881) - [N24001301]NHAI,ANDHRA PRADESH	11/2019	1,601.10 -	02/2021 -	-
725	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT - [N24001303]NHAI,BIHAR	10/2013	649.90 -	12/2020 -	-
726	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE - [N24001304]NHAI,BIHAR	10/2013	446.97 -	11/2020 -	-
727	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA - [N24001305]NHAI,BIHAR	10/2013	464.09 -	11/2020 -	-
728	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N - [N24001371]NHAI,BIHAR	10/2019	1,101.99 -	02/2020 -	-
729	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46 - [N24000172]NHAI,TAMIL NADU	09/2011	1,250.00 -	12/2013 -	-
730	HARIDWAR DEHRADUN APPROVED LENGTH 69 - [N24000212]NHAI,UTTARAKHAND	11/2011	478.51 -	10/2013 -	-
	Total		3,69,005.38 -		
	<u>URBAN DEVELOPMENT</u>				
	<u>Chennai Metro Rail Ltd</u>				
731	CHENNAI METRO RAIL LTD (PHASE 1) - [N28000084]CMRL,TAMIL NADU	02/2009	14,600.00 18,380.00	12/2015 -	-
732	CHENNAI METRO RAIL LTD (PHASE 1 EXT) - [N28000097]CMRL,TAMIL NADU	06/2016	3,770.00 -	03/2018 -	-

Costing Rs. 150 Crore and above					(August 2021)
					Date of Commissioning
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
	<u>Kochi Metro Rail Corporation Ltd</u>				
733	KOCHI METRO RAIL PROJECT - [N28000081]KMRCL,KERALA	07/2012	5,181.79 -	07/2017 09/2020	-
	<u>Lucknow Metro Rail Corporation Limited</u>				
734	LUCKNOW METRO RAIL CORPORATION LTD - [N28000094]LMRCL,UTTAR PRADESH	01/2016	6,928.00 6,928.00	03/2019 -	-
	<u>Nagpur Metro Rail Corporation Ltd</u>				
735	NAGPUR METRO RAIL - [N28000085]NMRL,MAHARASHTRA	08/2014	8,680.00 -	03/2018 -	12/2019
	<u>National Building Construcion Corporation Ltd</u>				
736	REDEVELOPMENT OF EAST KIDWAI NAGAR - [N28000080]NBCC,DELHI	06/2012	4,264.00 -	11/2019 -	-
	Total		43,423.79 -		
	<u>WATER RESOURCES</u>				
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>				
737	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR - [N30000037]BUIDCO,BIHAR	12/2014	225.77 -	03/2020 -	03/2021
738	SEWERAGE SCHEME AT PAHARI ZONE V PATNA - [N30000040]BUIDCO,BIHAR	05/2017	356.37 -	04/2021 -	04/2021
739	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA - [N30000041]BUIDCO,BIHAR	05/2017	184.86 -	05/2021 -	05/2021
740	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK - [N30000044]BUIDCO,BIHAR	03/2017	277.42 -	05/2021 -	05/2021
741	SEWER NETWORK SPS AND STP BEGUSARAI - [N30000026]BUIDCO,BIHAR	03/2018	230.06 -	07/2021 -	07/2021
742	I AND D AND STP WORKS FOR BHAGALPUR - [N30000027]BUIDCO,BIHAR	10/2017	254.13 -	09/2020 -	-
743	I AND D AND STP AT CHAPPRA - [N30000028]BUIDCO,BIHAR	11/2018	236.15 -	12/2020 06/2021	-
744	SAIDPUR SEWER NETWORK PATNA - [N30000039]BUIDCO,BIHAR	04/2015	268.63 -	01/2021 -	-
745	SEWERAGE TREATMENT PLANT AT PAHARI PATNA - [N30000043]BUIDCO,BIHAR	05/2017	191.62 -	11/2020 03/2021	-
	<u>Delhi Jal Board</u>				
746	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI - [N30000017]DJB,DELHI	12/2018	515.07 -	01/2021 -	06/2021
747	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO - [N30000018]DJB,DELHI	05/2017	344.81 -	05/2020 -	-
	<u>Hindustan Steelwork Construction Limited</u>				
748	IRRIGATION WORK OF BAGMATI - [N12000108]HSCL,BIHAR	10/2005	956.00 -	03/2015 -	-
	<u>Kolkata Metropolitan Development Authority</u>				
749	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE - [N30000047]KMDA,WEST BENGAL	12/2014	272.32 -	04/2020 -	03/2021

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
750	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR - [N30000046]KMDA,WEST BENGAL	02/2014	274.76 -	12/2019 05/2021	-
	<u>Uttar Pradesh Jal Nigam</u>				
751	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA - [N30000020]UPJalNigam,UTTAR PRADESH	02/2011	279.91 330.05	12/2019 -	01/2021
752	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE DISTRICT AT RAMANA - [N30000011]UPJalNigam,UTTAR PRADESH	02/2017	161.31 -	11/2019 -	03/2021
753	MATHURA SEWERAGE SCHEME - [N30000019]UPJalNigam,UTTAR PRADESH	12/2017	460.45 -	12/2020 -	05/2021
754	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR - [N30000009]UPJalNigam,UTTAR PRADESH	10/2016	370.40 430.49	08/2020 03/2021	-
	<u>Uttarakhand Pey Jal Nigam</u>				
755	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH - [N30000004]UKJalNigam,UTTARAKHAND	03/2017	158.00 -	11/2019 03/2021	-
	Total		6,018.04 -		
	<u>COMMERCE</u>				
	<u>National Building Construcion Corporation Ltd</u>				
756	CONSTRUCTION OF A NEW STATE OF ART EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI - [N40000003]NBCC,DELHI	06/2018	302.64 302.64	10/2020 -	-
	Total		302.64 -		
	<u>DEPARTMENT OF HIGHER EDUCATION</u>				
	<u>Central Public Works Department</u>				
757	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND - [N28000065]CPWD,HIMACHAL PRADESH	11/2012	270.83 -	11/2014 -	-
758	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD - [N28000067]CPWD,JHARKHAND	09/2012	171.86 -	03/2016 -	-
759	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA - [N28000075]CPWD,KERALA	01/2010	165.23 -	10/2012 -	-
760	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR - [N28000111]CPWD,UTTAR PRADESH	11/2017	171.72 -	03/2020 -	-
761	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI - [N28000117]CPWD,MAHARASHTRA	01/2018	223.37 -	07/2020 -	-
762	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN - [N28000119]CPWD,RAJASTHAN	12/2016	549.31 -	07/2019 -	-
763	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P. - [N28000133]CPWD,ANDHRA PRADESH	02/2019	186.00 199.00	09/2020 -	-
764	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED - [N28000146]CPWD,WEST BENGAL	03/2020	193.83 -	06/2020 -	-
765	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA. - [N42000002]CPWD,GOA	05/2019	303.90 -	03/2020 -	-
766	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE - [N42000005]CPWD,ANDHRA PRADESH	02/2019	655.34 -	06/2020 -	-
	<u>Edcil(India) Limited</u>				

Costing Rs. 150 Crore and above					(August 2021)
				Date of Commissioning	
Sl.No	Project	Date of Approval	Original / Revised Cost (Rs. crore)	Original / Revised	Anticipated
1	2	3	4	5	6
767	STUDY IN INDIA - [N42000003]EDCIL,MULTI STATE	03/2018	150.00 -	04/2018 -	-
	<u>Indian Institute Of Technology, Kharagpur</u>				
768	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION - [N42000004]IITKGP,MULTI STATE	08/2018	418.00 -	03/2019 -	-
	<u>Rail India Technical And Economic Service</u>				
769	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA - [N42000001]RITES,MEGHALAYA	09/2013	484.32 -	09/2014 -	-
	Total		3,943.71 -		
	<u>HOME AFFAIRS</u>				
	<u>Central Public Works Department</u>				
770	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA - [N28000101]CPWD,UTTARAKHAND	12/2008	114.26 266.00	12/2013 -	-
	Total		114.26 -		
	<u>RURAL DEVELOPMENT</u>				
771	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT - [N28000132]CPWD,DELHI	11/2018	361.60 -	07/2021 -	-
	Total		361.60 -		
	<u>DPIIT</u>				
	<u>Delhi Mumbai Industrial Corridor</u>				
772	DELHI MUMBAI INDUSTRIAL CORRIDOR - [N40000001]DMIC,MULTI STATE	09/2011	12,579.09 -	09/2019 01/2014	07/2021
	Total		12,579.09 -		
	Grand Total		6,04,715.52		

List of Delayed Projects w.r.t. Latest Schedule

Costing Rs. 150 Crore and above						(August 2021)			
						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>ATOMIC ENERGY</u>								
	<u>Nuclear Power Corporation Of India Limited</u>								
1	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4 - [N02000010]NPCIL,GUJARAT	10/2009	11,459.00	16,580.00	17,041.00	12/2015	02/2022	74	-
2	RAJASTHAN ATOMIC POWER PROJECT - 7 AND 8 (2X700 MW) - [N02000027]NPCIL,RAJASTHAN	10/2009	12,320.00	17,079.00	13,528.00	12/2016	03/2023	75	-
3	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4 - [N02000028]NPCIL,TAMIL NADU	03/2013	39,849.00	39,849.00	25,029.00	11/2020	11/2023	36	-
	Total		63,628.00	73,508.00	55,598.00				
	<u>CIVIL AVIATION</u>								
	<u>Airport Authority Of India Limited</u>								
4	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR - [N04000076]AAI,DELHI	11/2016	303.80	303.80	180.24	04/2020	03/2022	23	-
5	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT - [N04000089]AAI,ANDHRA PRADESH	08/2017	177.10	177.10	98.00	02/2020	05/2022	27	11
6	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT - [N04000079]AAI,MAHARASHTRA	03/2017	475.39	475.39	162.78	04/2021	08/2022	16	-
7	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN - [N04000085]AAI,UTTARAKHAND	07/2018	456.86	456.86	306.08	09/2020	09/2022	24	-
8	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI - [N04000075]AAI,TAMIL NADU	08/2018	951.28	951.28	437.28	10/2021	10/2022	12	-
9	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT - [N04000078]AAI,LADAKH	07/2018	346.27	480.33	105.53	09/2021	12/2022	15	-
10	UPGRADATION OF JABALPUR AIRPORT - [N04000087]AAI,MADHYA PRADESH	06/2016	412.24	412.24	204.49	06/2021	12/2022	18	-
11	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT - [N04000088]AAI,GUJARAT	01/2018	1,405.00	1,405.00	334.66	08/2022	12/2022	4	-
12	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI - [N04000083]AAI,ASSAM	12/2016	1,142.00	1,232.00	371.33	03/2021	03/2023	24	12
13	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI - [N04000074]AAI,TAMIL NADU	06/2018	2,467.00	2,467.00	689.52	02/2022	12/2023	22	-
14	CCS INTERNATIONAL AIRPORT , LUCKNOW - [N04000077]AAI,UTTAR PRADESH	06/2018	1,383.00	1,383.00	488.53	09/2021	12/2023	27	-
15	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II - [N04000082]AAI,BIHAR	05/2018	1,216.90	1,216.90	211.80	10/2022	12/2023	14	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		10,736.84	10,960.90	3,590.24				
	<u>COAL</u>								
	<u>Bharat Coking Coal Limited</u>								
16	MADHUBAND NLW WASHERY - [N06000126]BCCL,JHARKHAND	08/2010	289.45	289.45	285.43	05/2014	10/2021	89	-
17	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY) - [N06000106]BCCL,JHARKHAND	02/2014	555.52	555.52	5.87	03/2021	03/2022	12	-
18	2.0 MTPA BHOJUDIH NLW WASHERY - [N06000195]BCCL,WEST BENGAL	12/2015	304.13	341.22	64.19	03/2017	03/2022	60	-
19	PATHERDIH 2.5 NLW COAL WASHERY - [N06000194]BCCL,JHARKHAND	10/2015	243.00	334.27	24.70	04/2018	06/2022	50	-
20	MOONIDH XV SEAM UG - [N06000098]BCCL,JHARKHAND	08/2011	1,230.27	1,230.27	493.13	04/2015	02/2023	94	-
21	MURADIDH UG TURN-KEY PROJECT - [N06000096]BCCL,JHARKHAND	02/2011	339.88	339.88	61.16	04/2014	04/2023	108	-
	<u>Central Coal Fields Limited</u>								
22	CHURI BENTI UG (0.81 MTY) - [N06000083]CCL,JHARKHAND	08/2007	163.51	163.51	124.64	03/2011	03/2022	132	-
23	RAJRAPPA RCE OCP (3.0 MTY) - [N06000087]CCL,JHARKHAND	12/2009	510.85	510.85	497.88	03/2016	03/2022	72	-
24	KARMA OCP (1.0MTY) - [N06000088]CCL,JHARKHAND	06/2009	162.46	162.46	89.27	03/2014	03/2022	96	-
	<u>Eastern Coal Fields Limited</u>								
25	SONEPUR BAZARI (COMB) OCP (8.0 MTY) - [N06000109]ECL,WEST BENGAL	08/2012	1,055.05	1,055.05	689.34	03/2018	10/2021	43	-
26	RANIGANJ MASTER PLAN - [N06000163]ECL,WEST BENGAL	08/2009	2,661.73	5,146.48	622.13	08/2019	08/2024	60	-
	<u>Mahanadi Coal Fields Limited</u>								
27	HINGULA OC-II EXP. PH-III (15 MTY) - [N06000068]MCL,ODISHA	11/2008	479.53	703.39	703.39	03/2013	03/2024	132	-
28	BASUNDHARA (WEST) OC EXTN(7.00 MTY) - [N06000112]MCL,ODISHA	05/2014	479.15	479.15	226.00	03/2019	03/2024	60	-
29	GARJANBAHAL OCP - [N06000117]MCL,ODISHA	11/2014	1,375.38	1,375.38	581.31	03/2021	09/2025	54	-
30	BHUBANESWARI EXPENSION OCP(40.0 MTY) - [N06000034]MCL,ODISHA	12/2007	3,145.45	3,145.45	589.39	03/2017	03/2031	168	-
	<u>Neyveli Lignite Corporation</u>								
31	PACHWARA SOUTH COAL BLOCK - [N06000193]NLC,JHARKHAND	07/2013	1,795.01	1,795.01	36.52	08/2022	09/2023	13	-
	<u>Northern Coal Fields Limited</u>								
32	JAYANT EXPANSION OCP 10 TO 20 MTPA - [N06000159]NCL,MADHYA PRADESH	05/2017	1,783.09	1,783.09	738.88	03/2021	03/2022	12	-
33	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA) - [N06000162]NCL,MADHYA PRADESH	11/2017	1,255.17	1,255.17	230.12	03/2022	03/2023	12	-
	<u>Singareni Colliers Company Limited</u>								
34	RFR OF MANUGURU OC PROJECT - [N06000102]SCCL,TELANGANA	11/2012	430.45	415.37	213.44	03/2016	09/2021	66	-
35	KISTARAM OCP - [N06000089]SCCL,TELANGANA	11/2010	242.29	164.04	143.08	03/2015	03/2022	84	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
36	RCE OF INDARAM OCP(1.20 MTPA) - [N06000093]SCCL,TELANGANA	07/2011	162.76 -	349.28	283.01	03/2015 -	03/2022	84	-
37	KALYANIKHANI OPENCAS PROJECT - [N06000101]SCCL,TELANGANA	07/2012	417.33 -	384.32	134.71	07/2016 -	03/2022	68	-
38	KAKATIYAKHANI OPENCAS-2 PROJECT - [N06000129]SCCL,TELANGANA	05/2015	397.09 -	442.42	111.66	03/2019 -	03/2022	36	-
39	KAKATIYAKHANI OPENCAS III PROJECT PHASE-1 - [N06000161]SCCL,TELANGANA	03/2017	413.84 -	413.84	200.14	03/2019 -	03/2022	36	-
40	RAMAGUNDAM OC-II EXTENSION - [N06000078]SCCL,TELANGANA	12/2009	418.97 -	489.62	416.07	03/2012 -	03/2023	132	-
41	JALAGAM VENGALA RAO OCP-II - [N06000094]SCCL,TELANGANA	07/2011	447.06 -	473.22	79.04	03/2015 -	03/2023	96	-
	<u>South-Eastern Coal Fields Limited</u>								
42	JAGANNATHPOR OCP(3.00MTY) - [N06000075]SECL,CHHATISGARH	09/2008	152.43 459.49	459.49	198.78	03/2015 03/2020	03/2022	84	24
43	AMADAND OPENCAS EXPANSION PROJECT - [N06000148]SECL,MADHYA PRADESH	03/2016	869.44 -	869.44	126.15	03/2021 -	03/2022	12	-
44	GEVRA EXPANSION OCP (SECL) (35-70) MTY - [060100093]SECL,CHHATISGARH	06/2010	11,816.40 -	11,816.40	4,583.09	03/2023 03/2016	03/2023	0	84
45	MANIKPUR OC EXPANSION (3.5 MTY) - [N06000081]SECL,CHHATISGARH	12/2009	321.50 -	321.50	210.73	03/2014 -	03/2023	108	-
46	AMERA OC RCE - [N06000123]SECL,CHHATISGARH	02/2015	335.97 -	335.97	49.42	03/2018 -	03/2023	60	-
47	AMGAON OPENCAS PROJECT RCE - [N06000135]SECL,CHHATISGARH	07/2015	316.10 -	316.10	145.17	03/2020 -	03/2023	36	-
48	KANCHAN OC EXPANSION - [N06000125]SECL,MADHYA PRADESH	12/2014	371.04 -	371.04	66.44	03/2021 -	03/2024	36	-
49	BATURA HIGHWALL PROJECT - [N06000134]SECL,MADHYA PRADESH	07/2015	231.92 -	231.92	1.78	03/2022 -	03/2025	36	-
50	KARTALI (EAST) OCP (2.50 MTY) - [N06000076]SECL,CHHATISGARH	07/2008	178.44 -	178.44	11.37	03/2014 -	03/2026	144	-
51	DURGAPUR OPENCAS PROJECT - [N06000136]SECL,CHHATISGARH	02/2015	916.24 -	916.24	11.38	03/2023 -	03/2026	36	-
52	AMRITDHARA OC PROJECT - [N06000122]SECL,MADHYA PRADESH	02/2015	481.60 -	481.60	-	03/2023 -	03/2027	48	-
53	MADANNAGAR OPENCAS PROJECT - [N06000140]SECL,CHHATISGARH	10/2015	1,875.32 -	1,875.32	-	03/2024 -	03/2027	36	-
	<u>Western Coal Fields Limited</u>								
54	AMALGAMATED GONDEGAON GHATROHAN OC - [N06000149]WCL,MAHARASHTRA	02/2016	198.68 325.18	325.18	272.90	03/2019 -	03/2022	36	-
55	BHATADI EXPANSION OC MINE - [N06000150]WCL,MAHARASHTRA	02/2016	304.52 327.41	327.41	160.84	03/2019 -	03/2022	36	-
56	BELLORA-NAIGAON DEEP OC - [N06000180]WCL,MAHARASHTRA	11/2018	252.71 -	252.71	102.41	03/2021 -	09/2022	18	-
57	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY) - [N06000157]WCL,MULTI STATE	02/2017	328.00 -	328.00	296.56	03/2021 -	09/2023	30	-
58	ADASA UG TO OC - [N06000133]WCL,MAHARASHTRA	08/2015	288.90 333.43	333.43	145.08	03/2023 -	03/2024	12	-
	Total		39,997.63 -	43,537.90	14,026.60				
	<u>FERTILISERS</u>								

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>National Fertiliser Limited</u>								
59	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT - [N08000014]NFL,HARYANA	01/2018	215.92 -	215.92	172.01	11/2019 06/2021	10/2021	23	4
	Total		215.92 -	215.92	172.01				
	<u>STEEL</u>								
	<u>Steel Authority Of India Limited (Sail)</u>								
60	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL - [N12000118]SAIL,JHARKHAND	11/2016	262.87 -	262.87	199.74	06/2019 08/2021	10/2021	28	2
61	NEW SINTER PLANT AT BOKARO STEEL PLANT - [N12000095]SAIL,JHARKHAND	03/2015	1,034.01 -	1,034.01	549.60	10/2017 12/2021	11/2022	61	11
	Total		1,296.88 -	1,296.88	749.34				
	<u>PETROLEUM</u>								
	<u>Bharat Petroleum Corporation Limited</u>								
62	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY - [N16000227]BPCL,KERALA	11/2014	4,588.29 5,245.96	5,245.96	5,184.50	08/2018 11/2019	09/2021	37	22
63	RESITEMENT OF RAICHUR DEPOT TO GULBARGA - [N16000347]BPCL,KARNATAKA	10/2018	206.26 -	206.26	149.39	03/2021 -	10/2021	7	-
64	KOCHI SALEM LPG PIPELINE PROJECT - [N16000314]BPCL,KERALA	12/2015	1,112.00 1,507.24	1,507.24	769.00	06/2019 -	02/2022	32	-
65	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY - [N16000397]BPCL,MAHARASHTRA	07/2020	640.00 -	640.00	346.57	12/2021 -	03/2022	3	-
66	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT - [N16000364]BPCL,ANDHRA PRADESH	07/2017	580.20 -	580.20	207.44	02/2021 -	03/2023	25	-
	<u>Chennai Petroleum Corporation Limited</u>								
67	RE-LIQUIFIED NATURAL GAS - [N16000301]CPCL,TAMIL NADU	08/2017	421.00 -	305.00	272.50	08/2020 -	10/2021	14	-
	<u>Gas Authority Of India Limited</u>								
68	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT - [N16000271]GAIL,MULTI STATE	07/2015	2,881.40 -	2,000.00	1,622.70	12/2020 -	10/2021	10	-
69	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE - [N16000233]GAIL,GUJARAT	04/2016	327.78 -	200.00	195.40	04/2018 -	12/2021	44	-
70	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT - [N16000355]GAIL,HARYANA	08/2018	286.42 327.01	327.01	215.40	08/2020 05/2021	12/2021	16	7
71	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT - [N16000390]GAIL,UTTAR PRADESH	08/2018	217.92 217.92	217.92	96.60	04/2021 -	03/2022	11	-
72	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI - [N16000349]GAIL,GUJARAT	09/2018	225.54 247.90	247.90	41.34	02/2021 -	08/2022	18	-
	<u>Hindustan Petroleum Corporation Limited</u>								
73	220 KV GRID SUPPLY - [N16000407]HPCL,ANDHRA PRADESH	10/2020	303.40 -	303.40	211.10	03/2021 -	08/2021	5	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
74	180 TMTA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA - [N16000315]HPCL,MAHARASHTRA	06/2017	249.26	249.26	162.09	06/2020	09/2021	15	-
75	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE - [N16000316]HPCL,JHARKHAND	06/2017	161.50	161.50	102.16	06/2020	09/2021	15	-
76	SWRO II WITH LLPH FACILITIES - [N16000378]HPCL,ANDHRA PRADESH	09/2019	196.26	196.26	92.83	07/2020	09/2021	14	-
	<u>Indian Oil Corporation Limited</u>								
77	ADDITIONAL FACILITIES AT MANMAD FOR COVERSON TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000267]IOCL,MAHARASHTRA	05/2016	212.00	212.00	164.11	01/2021	09/2021	8	-
78	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY - [N16000308]IOCL,ODISHA	08/2017	315.00	315.00	225.95	12/2021 08/2021	09/2021	-3	1
79	BS VI PROJECT AT GUWAHATI REFINERY - [N16000339]IOCL,ASSAM	08/2018	557.00	557.00	537.30	02/2020 06/2021	09/2021	19	3
80	PARADIP LPG IMPORT FACILITY - [N16000196]IOCL,MULTI STATE	01/2015	690.00	690.00	587.17	07/2018 05/2021	10/2021	39	5
81	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000276]IOCL,MAHARASHTRA	05/2016	261.00	261.00	176.30	01/2021	10/2021	9	-
82	SITARGANJ LPG PROJECT - [N16000282]IOCL,UTTARAKHAND	02/2017	160.10	160.10	102.85	02/2020 06/2021	10/2021	20	4
83	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY - [N16000337]IOCL,BIHAR	07/2018	189.00	189.00	166.08	01/2021 06/2021	11/2021	10	5
84	PARADIP SOMNATHPUR HALDIA PIPELINE - [N16000345]IOCL,ODISHA	10/2018	1,297.50	1,297.50	795.89	10/2021	03/2022	5	-
85	LAB REVAMP AT GUJARAT REFINERY - [N16000377]IOCL,GUJARAT	10/2019	403.00	403.00	145.34	12/2021	04/2022	4	-
86	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY - [N16000321]IOCL,HARYANA	04/2018	206.63 340.76	340.76	131.80	02/2020 08/2021	07/2022	29	11
87	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE - [N16000268]IOCL,MAHARASHTRA	05/2016	348.00 437.00	437.00	162.73	01/2021	08/2022	19	-
88	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR - [N16000303]IOCL,UTTAR PRADESH	08/2017	318.80	318.80	162.87	08/2021	11/2022	15	-
89	REVAMPING OF FACILITIES AT VIZAG TERMINAL - [N16000343]IOCL,ANDHRA PRADESH	04/2018	355.00	355.00	120.72	04/2022	02/2023	10	-
90	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY - [N16000393]IOCL,WEST BENGAL	06/2020	1,019.00	1,019.00	85.59	01/2023	05/2023	4	-
91	GRASS ROOT TERMINAL AT MALKAPUR - [N16000351]IOCL,TELANGANA	12/2018	611.00	611.00	89.82	04/2022	08/2023	16	-
	<u>Mangalore Refinery And Petrochemicals Limited</u>								
92	SEA WATER DESALINATION PLANT - [N16000319]MANGALORE REFIN,KARNATAKA	11/2017	581.00 637.00	637.00	519.50	03/2020 11/2020	11/2021	20	12

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
93	BSVI UPGRADATION - [N16000257]MANGALORE REFIN,KARNATAKA	09/2016	1,810.00 1,810.00	1,810.00	1,728.12	12/2019 04/2021	02/2022	26	10
	<u>Oil & Natural Gas Corporation Limited</u>								
94	PIPELINE NETWORK PROJECT GELEKI, ASSAM - [N16000278]ONGC,ASSAM	07/2016	249.85 303.75	303.75	205.92	05/2020 08/2021	11/2021	18	3
	<u>Oil India Limited</u>								
95	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II - [N16000259]OIL,MULTI STATE	09/2016	571.66 -	571.66	479.91	12/2019 -	08/2021	20	-
96	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA - [N16000331]OIL,ASSAM	01/2018	543.91 652.10	638.60	383.44	02/2020 -	12/2021	22	-
97	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I) - [N16000258]OIL,MULTI STATE	05/2016	406.00 -	406.00	269.65	10/2020 -	03/2022	17	-
	Total		23,502.68 -	23,921.08	16,910.08				
	<u>POWER</u>								
	<u>Chenab Valley Power Projects [P] Limited</u>								
98	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW) - [N18000172]CVPPPL,JAMMU AND KASHMIR	10/2014	8,112.12 -	8,112.12	2,022.77	04/2020 -	07/2025	63	-
	<u>National Thermal Power Corporation</u>								
99	BRBCL-NABINAGAR TPP- JV (4X250 MW) - [N18000190]NTPC,BIHAR	01/2007	5,353.00 10,566.00	10,566.00	8,917.95	07/2012 06/2020	10/2021	111	16
100	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL - [N18000276]NTPC,ODISHA	05/2016	1,885.13 2,311.89	2,311.89	1,892.27	12/2018 -	11/2021	35	-
101	DURGAPUR PP-III (2X20 MW) - NSPCL - [N18000277]NTPC,WEST BENGAL	12/2016	529.68 633.80	633.80	461.33	11/2018 -	12/2021	37	-
102	NPCCPL-NABINAGAR STPP - JV (3X660 MW) - [N18000192]NTPC,BIHAR	01/2013	12,964.60 17,304.00	17,304.00	16,096.71	05/2018 -	02/2022	45	-
103	SAMBHU KI BHURJ-II SOLAR 300MW - [N18000286]NTPC,RAJASTHAN	03/2020	1,782.00 -	1,782.00	527.71	09/2021 07/2022	09/2022	12	2
104	TELANGANA SUPER THERMAL POWER PROJECT PHASE I - [N18000212]NTPC,TELANGANA	01/2016	10,598.98 10,997.70	10,997.70	8,740.94	11/2020 07/2022	10/2022	23	3
105	NOKHRA - [N18000282]NTPC,UTTAR PRADESH	03/2020	1,722.14 -	1,722.14	340.93	09/2021 07/2022	01/2023	16	6
106	NORTH KARANPURA STPP (3X660 MW) - [N18000177]NTPC,JHARKHAND	02/2014	14,366.58 -	15,389.42	12,083.75	06/2019 10/2022	12/2023	54	14
107	PATRATU STPP-I (3X800MW) - [N18000275]NTPC,JHARKHAND	11/2017	18,668.00 -	17,112.00	4,073.68	03/2023 -	02/2025	23	-
	<u>Power Grid Corporation Of India Limited</u>								
108	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR-SCHEME-I: RAIGARH-P - [N18000219]PGCIL,MULTI STATE	05/2016	14,733.37 -	14,733.37	11,641.93	11/2019 07/2021	09/2021	22	2
109	EASTERN REGION STRENGTHENING SCHEME- XVIII - [N18000258]PGCIL,MULTI STATE	03/2017	3,500.00 3,500.00	3,994.00	3,029.93	07/2020 12/2020	10/2021	15	10

Costing Rs. 150 Crore and above

(August 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
110	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY - [N18000262]PGCIL,TAMIL NADU	05/2017	186.17 219.66	219.66	158.03	07/2019 07/2021	10/2021	27	3
111	EASTERN REGION STRENGTHENING SCHEME XX - [N18000268]PGCIL,MULTI STATE	11/2017	358.83 -	358.83	259.50	05/2020 08/2021	10/2021	17	2
112	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I - [N18000157]PGCIL,MULTI STATE	01/2014	374.63 -	374.63	252.99	04/2016 12/2017	12/2021	68	48
113	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO - [N18000184]PGCIL,MULTI STATE	03/2015	197.40 -	197.40	90.28	03/2018 -	12/2021	45	-
114	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII - [N18000245]PGCIL,MULTI STATE	03/2017	379.95 -	379.95	235.59	12/2019 09/2021	12/2021	24	3
115	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/- [N18000242]PGCIL,MULTI STATE	02/2017	322.30 -	322.30	204.09	02/2019 09/2021	02/2022	36	5
116	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES - [N18000250]PGCIL,MULTI STATE	12/2014	5,111.33 6,700.00	6,700.00	3,068.24	12/2018 12/2021	03/2022	39	3
	<u>Thdc India Limited</u>								
117	TEHRIPUMPED STORAGE PLANT(1000MW) - [N18000010]THDCIL,UTTARAKHAND	07/2006	1,657.00 4,825.60	4,825.60	4,170.24	02/2016 -	06/2023	88	-
118	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT - [N18000042]THDCIL,UTTARAKHAND	08/2008	2,491.58 3,860.35	3,860.35	2,271.34	06/2013 11/2018	06/2024	132	67
119	KHURJA SUPER THERMAL POWER PROJECT - [N18000272]THDCIL,UTTAR PRADESH	03/2019	11,089.42 -	11,089.42	2,347.19	09/2023 -	08/2024	11	-
	Total		1,16,384.21 -	1,32,986.58	82,887.39				
	<u>HEALTH AND FAMILY WELFARE</u>								
	<u>Central Public Works Department</u>								
120	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST - [N28000112]CPWD,KERALA	09/2017	150.29 -	150.29	52.74	03/2020 -	12/2021	21	-
121	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT - [N28000139]CPWD,PONDICHERRY	03/2018	195.00 -	195.00	16.41	09/2020 -	04/2022	19	-
122	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH - [N28000127]CPWD,HIMACHAL PRADESH	12/2018	260.00 -	260.00	25.38	06/2021 -	05/2022	11	-
	<u>Hil Infra Tech Services Limited</u>								
123	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.) - [N21000025]HITES,UTTAR PRADESH	07/2016	785.00 -	715.06	574.62	04/2020 -	10/2021	18	-
124	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB - [N21000026]HITES,PUNJAB	07/2016	703.00 -	557.48	513.24	06/2020 -	10/2021	16	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Hospital Services Consultancy Corporation Ltd</u>								
125	LHMC NEW DELHI-RE-DEVELOPMENT - [N21000003]HSCC,DELHI	02/2013	414.11 -	655.58	561.94	11/2013 -	09/2021	94	-
126	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL - [N21000018]HSCC, WEST BENGAL	08/2017	355.15 -	355.15	313.77	03/2019 -	09/2021	30	-
127	NEIGRIHMS SHILLONG MEGHALYA - [N21000013]HSCC, MEGHALAYA	10/2016	363.99 -	363.99	246.43	05/2018 -	03/2022	46	-
	<u>National Building Construcion Corporation Ltd</u>								
128	AIIMS BILASPUR - [N21000028]NBCC, HIMACHAL PRADESH	04/2018	1,351.00 -	1,471.00	814.67	09/2021 -	06/2022	9	-
	Total		4,577.54 -	4,723.55	3,119.20				
	<u>RAILWAYS</u>								
	<u>Central Railways</u>								
129	AHMEDNAGAR-PARLI VAIJNATH(NL) CR - [220100181]CR, MAHARASHTRA	02/1997	2,271.50 -	4,794.60	2,831.83	03/2021 -	03/2023	24	-
130	KALYAN-KASARA 3RD LINE - [N22000233]CR, MAHARASHTRA	04/2011	792.89 -	910.93	352.67	03/2021 -	03/2023	24	-
131	WARDHA-BALHARSHAH - 3RD LINE (132 KM) - [N22000356]CR, MAHARASHTRA	02/2015	1,272.19 -	1,283.49	479.21	03/2022 -	03/2023	12	-
132	WARDHA-SEWAGRAM NGP 3RD LINE - [N22000250]CR, MAHARASHTRA	04/2012	540.02 -	540.02	352.20	03/2022 -	03/2024	24	-
133	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM) - [N22000358]CR, MAHARASHTRA	02/2015	2,449.91 -	2,449.91	433.66	03/2023 -	03/2024	12	-
134	MANMAD - JALGAON - 3RD LINE (160 KM) - [N22000361]CR, MAHARASHTRA	02/2016	1,035.16 -	1,035.16	292.56	03/2022 -	03/2024	24	-
135	WARDHA - NAGPUR - 4TH LINE (76 KM) - [N22000362]CR, MAHARASHTRA	02/2016	637.95 -	637.95	199.88	03/2023 -	03/2024	12	-
	<u>East Central Railways</u>								
136	KARAILA ROAD - SHAKTINAGAR DOUBLING - [N22000419]ECR, UTTAR PRADESH	08/2015	528.57 -	528.57	223.40	03/2019 -	03/2022	36	-
137	GARHWA ROAD-RAMNA - [N22000465]ECR, JHARKHAND	03/2015	348.23 -	390.00	366.22	03/2021 -	03/2022	12	-
138	KIUL - GAYA DOUBLING PROJECT - [N22000349]ECR, BIHAR	12/2015	1,200.20 - 1,200.20	1,200.20	970.88	03/2020 -	03/2023	36	-
139	RAMNA - SINGRAULI DOUBLING - [N22000417]ECR, UTTAR PRADESH	08/2015	2,436.21 -	2,436.21	1,283.84	03/2020 -	03/2024	48	-
	<u>East Coast Railway</u>								
140	SAMBALPUR-TALCHER DOUBLING - [N22000315]ECOR, ODISHA	03/2011	1,111.99 -	1,539.28	1,186.14	02/2019 -	12/2021	34	-
141	SAMBALPUR - ANGUL RLY. ELECTRIFICATION - [N22000319]ECOR, ODISHA	03/2012	155.81 - 238.03	238.03	222.65	03/2020 -	03/2022	24	-
142	KORAPUT - SINGAPUR ROAD DOUBLING - [N22000379]ECOR, ODISHA	04/2015	2,361.74 -	2,361.74	450.42	03/2022 -	03/2026	48	-
	<u>Eastern Railways</u>								
143	DEOGHAR - SULTANGANJ (INL), ER - [220100273]ER, MULTI STATE	04/2000	607.09 -	1,425.44	638.19	02/2013 -	03/2024	133	-
144	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER - [220100272]ER, WEST BENGAL	04/2000	1,188.91 -	1,619.48	906.00	03/2019 12/2009	03/2025	72	183

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
145	BARDHAMAN-KATWA (GC) - [N22000091]ER, WEST BENGAL	04/2007	1,106.62 -	1,091.59	1,001.66	12/2010 -	03/2025	171	-
146	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP-BUDAKHALI AND CHANDRANAG - [N22000216]ER, MULTI STATE	04/1987	406.99 -	545.70	149.31	03/2006 -	03/2025	228	-
147	PIRPAINTI-JASIDIH - [N22000219]ER, MULTI STATE	04/2013	915.98 -	2,137.81	409.74	03/2022 -	03/2025	36	-
148	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3 - [N22000224]ER, MULTI STATE	04/2001	923.52 -	995.10	614.44	03/2016 -	03/2025	108	-
149	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL - [N22000225]ER, MULTI STATE	04/2005	595.51 -	769.40	97.40	03/2017 -	03/2025	96	-
150	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL - [N22000228]ER, MULTI STATE	04/2010	277.28 -	266.32	197.54	03/2016 -	03/2025	108	-
151	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA, FURFURA NL - [N22000229]ER, MULTI STATE	04/2010	365.17 -	439.30	454.56	03/2017 -	03/2025	96	-
152	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL - [N22000240]ER, MULTI STATE	04/2010	494.54 -	494.59	30.12	03/2005 -	03/2025	240	-
153	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHNACHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL - [N22000243]ER, MULTI STATE	04/2009	499.96 -	680.68	141.76	02/2012 -	03/2025	157	-
154	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI-JONGALPARA-FURFURA SHARIF NL - [N22000244]ER, MULTI STATE	04/2009	257.42 -	257.42	108.87	03/2014 -	03/2025	132	-
155	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY - [N22000239]ER, MULTI STATE	04/2011	299.60 -	335.62	1.12	03/2017 -	03/2026	108	-
	<u>Indian Railway Construction Company Limited</u>								
156	KHARSIA DHARAMJAIGARH WITH SPUR LINE EAST CORRIDOR-PHASE I - [N22000489]IRCON, CHHATISGARH	04/2013	3,055.00 -	3,055.15	2,666.33	09/2018 -	06/2022	45	-
157	GEVRA ROAD PENDRA ROAD - [N22000488]IRCON, CHHATISGARH	02/2014	2,288.00 -	4,970.11	962.98	03/2022 -	09/2023	18	-
158	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL - [N22000418]IRCON, ODISHA	04/2016	5,200.00 -	962.00	54.75	03/2020 -	03/2024	48	-
	<u>Metropolitan Rapid Transport Projects</u>								
159	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP) - [220100164]MRTP, MAHARASHTRA	03/1996	495.44 -	2,980.41	1,821.99	03/2004 -	03/2022	216	-
	<u>North Central Railway</u>								
160	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING - [N22000495]NCR, UTTAR PRADESH	03/2018	4,329.53 -	4,329.53	63.56	03/2023 -	06/2025	27	-
	<u>North East Frontier Railway</u>								

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
161	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL), NEFR - [220100266]NFR, MULTI STATE	04/2000	1,180.19 2,531.34	4,541.38	3,825.94	12/2008 -	09/2021	153	-
162	AGARTALA-AKHAURA NL - [N22000195]NFR, TRIPURA	04/2012	569.63 -	742.00	200.28	03/2020 -	03/2022	24	-
163	NEW BG LINE FROM JAGBANI TO BIRATNAGAR - [N22000207]NFR, MULTI STATE	04/2010	241.52 -	373.87	333.46	- 12/2021	03/2022	-	3
164	DIGARU-HOJAI (102 KM) - [N22000389]NFR, ASSAM	04/2015	870.96 -	1,873.21	1,397.73	03/2021 -	03/2022	12	-
165	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR - [N22000086]NFR, ASSAM	09/2006	385.20 -	1,105.00	858.45	03/2019 -	03/2023	48	-
166	BONGAIGAON-GOALPARA-GUWAHATI (176 KM) - [N22000388]NFR, ASSAM	04/2015	2,232.32 -	2,950.00	1,758.52	03/2022 -	03/2023	12	-
167	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR) - [220100288]NFR, MANIPUR	04/2003	4,454.17 -	12,264.15	11,303.51	03/2011 -	12/2023	153	-
168	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING - [N22000183]NFR, MULTI STATE	04/2013	1,798.00 2,042.51	2,042.51	219.14	03/2019 -	12/2023	57	-
169	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR - [N22000087]NFR, BIHAR	09/2006	532.87 2,132.03	2,145.00	1,014.54	03/2019 -	03/2024	60	-
170	BHAIRABI SAIRONG, NL, NEFR - [N22000100]NFR, MIZORAM	04/2008	2,393.47 5,021.45	5,521.45	4,169.01	03/2014 -	03/2024	120	-
171	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA) NATIONAL PROJECT (NEFR) - [N22000124]NFR, NAGALAND	04/2006	2,326.52 -	6,911.00	1,300.10	03/2015 -	03/2026	132	-
	<u>North Eastern Railway</u>								
172	INDARA - DOHRIGHAT GAUGE CONVERSION. - [N22000456]NER, UTTAR PRADESH	04/2016	213.00 -	213.35	53.51	04/2016 -	12/2021	68	-
173	CHHAPRA-BALLIA UP - [N22000134]NER, MULTI STATE	03/2013	295.00 -	580.00	521.43	01/2019 -	02/2022	37	-
174	AUNRIHAR - JAUNPUR PATCH DOUBLING. - [N22000469]NER, UTTAR PRADESH	04/2016	600.00 -	366.71	254.12	01/2022 -	03/2022	2	-
175	ETAH - KASGANJ - NEW LINE - [N22000462]NER, UTTAR PRADESH	04/2017	276.90 -	276.90	-	04/2017 -	04/2022	60	-
176	NANPARA - NEPALGANJ GAUGE CONVERSION. - [N22000459]NER, UTTAR PRADESH	04/2017	150.00 -	341.66	-	04/2017 -	10/2022	66	-
177	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI. - [N22000457]NER, UTTAR PRADESH	04/2016	1,900.00 -	1,277.06	-	01/2022 -	03/2025	38	-
	<u>North Western Railway</u>								
178	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR - [N22000152]NWR, RAJASTHAN	04/2013	420.18 -	480.00	371.38	03/2020 -	09/2021	18	-
179	DAUSA-GANGAPUR CITY(NL), NWR - [220100184]NWR, RAJASTHAN	02/1997	410.08 -	860.41	745.83	02/2019 -	06/2022	40	-
180	PHULERA - DIGANA DOUBLING - [N22000326]NWR, MULTI STATE	05/2015	600.00 -	701.81	261.79	03/2020 -	10/2022	31	-
181	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM) - [N22000466]NWR, RAJASTHAN	08/2018	808.85 -	808.85	275.78	08/2022 -	11/2022	3	-
	<u>Northern Railway</u>								
182	UDHAMPUR-SRINAGAR-BARAMULLA (NL), NR - [220100133]NR, JAMMU AND KASHMIR	03/1995	2,500.00 27,949.00	27,949.00	25,191.80	11/2002 -	12/2022	241	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
183	NANGALDAM-TALWARA(NL),NR - [220100188]NR,MULTI STATE	03/1981	450.00 -	2,200.00	-	07/2012 -	03/2024	140	-
184	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI - [N22000502]NR,PUNJAB	06/2009	404.00 -	404.00	190.00	08/2016 -	08/2025	108	-
	<u>Rail Vikas Nigam Ltd.</u>								
185	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD - [N22000213]RVNL,TELANGANA	04/2012	632.68 -	950.00	741.79	03/2016 -	12/2021	69	-
186	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM) - [N22000407]RVNL,MAHARASHTRA	03/2009	713.48 -	2,725.00	2,249.00	03/2020 -	12/2021	21	-
187	SAMBALPUR - TITLAGARH - DOUBLING - [N22000410]RVNL,ODISHA	03/2006	948.04 -	2,009.00	1,532.13	03/2020 -	12/2021	21	-
188	RAIPUR - TITLAGARH - DOUBLING - [N22000411]RVNL,CHHATISGARH	03/2007	1,402.02 -	1,300.00	1,152.05	03/2020 -	12/2021	21	-
189	BINA - KOTA DOUBLING WITH RE - [N22000414]RVNL,MADHYA PRADESH	04/2011	1,485.85 -	1,835.83	1,270.60	12/2020 -	12/2021	12	-
190	PALANPUR-SAMAKHAYALI (DL) - [N22000144]RVNL,GUJARAT	04/2013	1,548.66 -	1,868.89	1,462.02	12/2021 -	03/2022	3	-
191	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM) - [N22000313]RVNL,ANDHRA PRADESH	03/2012	1,503.71 -	3,377.00	2,152.52	03/2020 -	03/2022	24	-
192	SUKINDA ROAD - ANGUL (NL)(ECOR) - [220100325]RVNL,ODISHA	04/1998	1,202.70 -	2,440.53	1,066.19	02/2015 -	06/2022	88	-
193	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC - [N22000404]RVNL,UTTAR PRADESH	04/2011	927.01 -	1,400.00	1,233.65	03/2019 -	06/2022	39	-
194	BANASPANI- JAKHPURA - DOUBLING - [N22000412]RVNL,ODISHA	03/2009	942.95 -	1,536.00	1,054.76	03/2019 -	06/2022	39	-
195	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION - [N22000413]RVNL,UTTAR PRADESH	03/2012	1,183.25 -	1,825.00	1,266.69	12/2020 -	12/2022	24	-
196	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING - [N22000401]RVNL,UTTAR PRADESH	04/2015	943.60 -	1,000.00	544.48	03/2022 -	12/2024	33	-
197	MAU-GHAZIPUR-TARIGHAT NEW LINE - [N22000405]RVNL,UTTAR PRADESH	04/2015	1,765.92 -	1,765.92	746.29	03/2023 -	12/2024	21	-
198	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP) - [N22000110]RVNL,WEST BENGAL	04/2010	3,951.98 -	4,259.48	2,453.42	03/2016 -	03/2025	108	-
199	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH. - [N22000111]RVNL,WEST BENGAL	04/2010	2,913.51 -	4,639.00	888.31	03/2016 -	03/2025	108	-
200	RISHIKESH - KARNAPRAYAG NEW LINE - [N22000406]RVNL,UTTARAKHAND	04/2011	16,216.00 -	22,716.11	2,045.67	12/2024 -	03/2025	3	-
201	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP) - [N22000109]RVNL,WEST BENGAL	04/2010	2,298.42 -	2,733.86	40.46	03/2014 -	12/2025	141	-
202	VIZIANAGARAM -SAMABALPUR 3RD LINE - [N22000409]RVNL,ODISHA	01/1991	2,335.67 -	3,327.72	794.54	12/2024 -	12/2026	24	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>South Central Railway</u>								
203	BHADRACHALAM ROAD-SATTUPALLI - [N22000287]SCR,MULTI STATE	04/2010	704.31 -	927.94	656.85	03/2020 -	11/2021	20	-
204	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K - [N22000432]SCR,TELANGANA	04/2017	119.73 185.00	449.39	7.09	03/2022 -	12/2022	9	-
205	MUNEERABAD-MAHABOBNAGAR(NL),SCR - [220100205]SCR,MULTI STATE	04/1997	1,723.00 1.00	3,421.35	1,989.23	03/2000 -	03/2023	276	-
206	KOTLPALLI-NARASAPUR (NL) (SCR) - [220100265]SCR,ANDHRA PRADESH	12/2001	1,045.20 -	2,120.16	1,009.94	03/2009 -	03/2024	180	-
207	MANOHARABAD-KOTHPALL NEW LINE(SCR) - [N22000032]SCR,TELANGANA	04/2006	1,160.48 -	1,160.48	631.65	03/2010 -	03/2024	168	-
208	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION - [N22000261]SCR,MULTI STATE	04/2012	1,856.95 -	1,952.68	684.12	03/2023 -	03/2024	12	-
209	NADIKUDE-SRI KALAHASTI - [N22000286]SCR,ANDHRA PRADESH	04/2011	2,288.70 -	2,643.25	1,277.06	03/2021 -	03/2024	36	-
210	KAZIPET-BALHRSHA - [N22000367]SCR,MULTI STATE	04/2015	2,063.03 -	2,063.03	1,530.08	03/2021 -	03/2024	36	-
211	GUNTUR-GUNTAKAL - [N22000368]SCR,ANDHRA PRADESH	04/2016	3,631.00 -	3,887.48	1,239.48	03/2022 -	03/2024	24	-
212	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I - [N22000288]SCR,MULTI STATE	04/2008	2,132.77 -	3,037.95	348.32	03/2014 -	03/2027	156	-
	<u>South East Central Railway</u>								
213	ANUPPUR-KATNI - [N22000485]SECR,MADHYA PRADESH	04/2015	1,370.00 -	1,370.94	-	12/2021 -	12/2023	24	-
	<u>South Eastern Railway</u>								
214	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING - [N22000165]SER,JHARKHAND	04/2012	258.20 -	358.68	316.37	12/2018 -	08/2021	32	-
215	ROURKELA JHARSUGUDA THIRD LINE 101 KM - [N22000395]SER,ODISHA	11/2015	969.83 -	1,312.96	1,018.29	03/2020 -	02/2022	23	-
216	BONDAMUNDA RANCHI DOUBLING - [N22000396]SER,JHARKHAND	03/2016	1,724.20 -	1,724.20	896.81	03/2021 -	12/2023	33	-
217	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA - [N22000160]SER,MULTI STATE	04/2010	651.00 -	1,009.00	7.96	03/2015 -	03/2025	120	-
218	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL - [N22000402]SER,WEST BENGAL	04/1998	1,027.40 -	2,373.00	485.04	03/2003 -	03/2030	324	-
	<u>South Western Railway</u>								
219	YELAHANKA-PENUKONDA - [N22000328]SWR,MULTI STATE	05/2015	860.43 -	1,147.00	945.81	03/2020 -	09/2021	18	-
220	HUBLI- CHIKJAJUR - [N22000325]SWR,KARNATAKA	03/2015	1,156.94 -	1,800.59	1,128.98	03/2020 -	03/2023	36	-
221	MARIKUPPAM - KUPPAM - [N22000308]SWR,KARNATAKA	04/2012	279.54 -	279.54	36.82	03/2016 -	12/2023	93	-
222	BANGLORE - SATYAMANGALAM (NL)(SWR) - [220100274]SWR,KARNATAKA	04/1996	1,382.78 -	1,960.00	7.35	03/2002 -	03/2024	264	-
223	SHIMOGA-HARIHAR NL - [N22000278]SWR,KARNATAKA	04/2011	832.47 -	832.47	.94	03/2016 -	03/2024	96	-
224	HOTGI-KUDGI-GADAG - [N22000333]SWR,MULTI STATE	03/2015	1,614.59 1,877.81	1,878.00	1,457.95	03/2019 -	03/2024	60	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
225	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM) - [N22000486]SWR,KARNATAKA	03/1996	644.78 889.00	731.77	465.72	03/2017 -	03/2025	96	-
226	GADAG-WADI NL - [N22000299]SWR,KARNATAKA	04/2013	2,841.84 -	2,841.84	362.40	12/2018 -	06/2025	78	-
227	BAGALKOT-KUDACHI NL - [N22000258]SWR,KARNATAKA	04/2010	986.30 -	1,530.09	311.40	03/2016 -	12/2026	129	-
	<u>Southern Railway</u>								
228	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II) - [N22000441]SR,TAMIL NADU	02/1996	268.87 -	950.00	920.84	03/2005 -	09/2021	198	-
229	MANIYACHI - NAGERCOIL (102 KM) DOUBLING - [N22000449]SR,TAMIL NADU	02/2015	1,700.00 -	1,305.00	756.45	03/2022 -	06/2022	3	-
230	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING - [N22000451]SR,TAMIL NADU	02/2015	760.00 -	1,536.00	1,233.08	03/2020 -	06/2022	27	-
231	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC) - [220100262]SR,TAMIL NADU	09/1995	303.98 -	1,720.00	704.89	03/2020 -	03/2025	60	-
232	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'POND' AGASTIYAMPALLI - [N22000079]SR,TAMIL NADU	09/2007	724.69 -	2,950.00	1,644.43	02/2019 -	03/2025	73	-
233	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM) - [N22000445]SR,TAMIL NADU	02/2017	1,567.00 -	1,567.00	-	03/2024 -	03/2026	24	-
234	MADURAI-TUTICORIN VIA ARUPPUKOTTAI - [N22000215]SR,MULTI STATE	04/2011	120.70 -	2,172.16	273.27	03/2019 -	12/2027	105	-
	<u>West Central Railway</u>								
235	KATNI-BINA 3RD LINE (263 KM) - [N22000415]WCR,MADHYA PRADESH	06/2016	2,478.23 -	2,478.23	477.93	03/2022 -	03/2023	12	-
236	KATNI GRADE SEPARATOR/BYE PASS - [N22000416]WCR,MADHYA PRADESH	08/2016	582.13 1,247.64	1,247.64	415.54	03/2022 -	03/2023	12	-
237	KATNI - SINGRAULI DOUBLING PROJECT - [N22000351]WCR,MADHYA PRADESH	12/2015	1,763.93 -	2,470.00	1,244.18	03/2020 -	03/2024	48	-
238	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR) - [220100232]WCR,MULTI STATE	09/1998	247.66 -	8,248.50	2,131.17	05/2008 -	03/2025	202	-
	Total		1,53,219.90 -	2,55,798.72	1,23,524.21				
	<u>ROAD TRANSPORT AND HIGHWAYS</u>								
	<u>Ministry Of Road Transport And Highways (State Pwds)</u>								
239	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200 - [N24000909]MoRTH,PUNJAB	10/2017	1,069.59 -	1,069.59	728.55	10/2019 -	08/2021	22	-
240	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS - [N24001209]MoRTH,UTTAR PRADESH	03/2016	296.50 -	296.50	237.08	09/2020 -	08/2021	11	-
241	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400 - [N24000475]MoRTH,MADHYA PRADESH	11/2015	628.45 -	628.45	445.35	01/2020 06/2021	09/2021	20	3
242	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93 - [N24000478]MoRTH,MADHYA PRADESH	12/2015	957.54 -	957.54	765.48	02/2020 04/2021	09/2021	19	5

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
243	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS - [N24000872]MoRTH,MADHYA PRADESH	03/2018	166.21 -	173.41	154.26	08/2018 08/2021	09/2021	37	1
244	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A - [N24000896]MoRTH,MADHYA PRADESH	01/2017	373.82 -	373.82	232.63	09/2019 06/2021	09/2021	24	3
245	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM. - [N24001151]MoRTH,MADHYA PRADESH	11/2017	392.33 428.55	428.55	379.29	03/2018 06/2021	10/2021	43	4
246	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C - [N24001177]MoRTH,TRIPURA	10/2016	171.90 -	171.90	142.81	08/2020 -	10/2021	14	-
247	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS - [N24000898]MoRTH,MADHYA PRADESH	01/2016	809.16 -	809.16	615.21	07/2018 05/2021	11/2021	40	6
248	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A - [N24000378]MoRTH,MADHYA PRADESH	06/2015	390.51 -	390.51	271.94	- 03/2021	12/2021	-	9
249	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH. - [N24000886]MoRTH,MADHYA PRADESH	01/2017	205.05 -	205.05	126.89	03/2017 06/2021	12/2021	57	6
250	2L+PS OF THIKRI ANJAD SECTION OF NH-347B - [N24000892]MoRTH,MADHYA PRADESH	11/2017	249.05 -	249.05	198.83	07/2018 08/2021	12/2021	41	4
251	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM - [N24000899]MoRTH,MADHYA PRADESH	03/2016	877.79 -	877.79	741.88	06/2019 04/2021	12/2021	30	8
252	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750 - [N24001206]MoRTH,UTTAR PRADESH	03/2018	263.89 -	242.05	189.09	04/2020 -	12/2021	20	-
253	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J - [N24001208]MoRTH,UTTAR PRADESH	03/2018	288.30 -	288.30	160.68	08/2020 -	12/2021	16	-
254	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H - [N24000874]MoRTH,WEST BENGAL	03/2016	271.17 291.20	291.20	120.14	11/2018 01/2021	03/2022	40	14
255	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA - [N24000875]MoRTH,MADHYA PRADESH	02/2018	169.63 -	169.63	52.44	03/2018 04/2021	04/2022	49	12
256	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION - [N24001384]MoRTH,ANDHRA PRADESH	03/2020	207.79 -	207.79	-	03/2021 -	04/2022	13	-
257	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS - [N24000888]MoRTH,MADHYA PRADESH	03/2018	214.69 -	214.69	78.48	03/2018 09/2021	06/2022	51	9

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
258	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGOUR SECTION BY EXECUTING BALANCE WORK FRO - [N24001241]MoRTH,RAJASTHAN	03/2020	255.23 -	255.23	42.41	08/2020 -	08/2022	24	-
259	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND - [N24000885]MoRTH,WEST BENGAL	03/2016	160.27 213.97	213.97	26.72	08/2019 -	11/2022	39	-
260	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K - [N24001242]MoRTH,RAJASTHAN	08/2020	196.23 -	196.00	28.61	11/2020 -	11/2022	24	-
261	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200 - [N24000513]MoRTH,MADHYA PRADESH	03/2015	511.83 -	511.83	387.81	08/2017 06/2021	12/2022	64	18
262	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR - [N24001385]MoRTH,ANDHRA PRADESH	06/2020	221.40 -	221.40	-	05/2021 -	12/2022	19	-
263	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT - [N24001386]MoRTH,ANDHRA PRADESH	08/2020	222.61 -	222.61	-	03/2021 -	03/2023	24	-
National Highways And Infrastructure Development Corporation Ltd.									
264	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C - [N24000746]NHIDCL,A & N ISLANDS	03/2015	277.17 -	277.17	202.59	04/2017 03/2021	10/2021	54	7
265	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM - [N24000869]NHIDCL,MANIPUR	08/2017	517.57 -	423.93	432.93	10/2018 -	10/2021	36	-
266	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A - [N24000322]NHIDCL,ASSAM	03/2015	168.39 -	168.39	145.72	11/2018 -	11/2021	36	-
267	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9 - [N24000759]NHIDCL,NAGALAND	03/2018	237.72 -	237.72	120.12	09/2018 -	11/2021	38	-
268	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0 - [N24000760]NHIDCL,NAGALAND	03/2018	251.97 -	251.97	146.10	09/2018 -	11/2021	38	-
269	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65. - [N24000761]NHIDCL,NAGALAND	03/2018	282.98 -	282.98	153.26	09/2018 -	11/2021	38	-
270	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO - [N24000762]NHIDCL,NAGALAND	03/2018	215.12 -	215.12	107.31	09/2018 -	11/2021	38	-
271	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240) - [N24000319]NHIDCL,ASSAM	06/2015	437.39 -	437.39	105.09	06/2018 -	12/2021	42	-

Costing Rs. 150 Crore and above

(August 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
272	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5 - [N24000320]NHIDCL, ASSAM	06/2015	463.49 -	463.49	159.34	06/2018 -	12/2021	42	-
273	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS. - [N24000438]NHIDCL, ASSAM	12/2015	289.99 -	289.99	87.90	12/2018 -	12/2021	36	-
274	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD (NEAR ITHUN BRIDGE) TO KM 37 - [N24000616]NHIDCL, ARUNACHAL PRADESH	04/2016	245.79 -	245.79	204.42	- 01/2021	12/2021	-	11
275	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO - [N24000757]NHIDCL, NAGALAND	03/2018	315.03 -	315.03	101.42	09/2018 -	12/2021	39	-
276	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO - [N24000758]NHIDCL, NAGALAND	03/2018	240.64 -	240.64	112.90	09/2018 -	12/2021	39	-
277	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO - [N24000763]NHIDCL, NAGALAND	03/2018	215.79 -	215.79	70.57	09/2018 -	12/2021	39	-
278	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5 - [N24000768]NHIDCL, SIKKIM	11/2017	290.05 -	290.05	119.27	11/2017 -	12/2021	49	-
279	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120. - [N24000944]NHIDCL, ARUNACHAL PRADESH	12/2016	200.44 -	200.44	125.91	- 08/2021	12/2021	-	4
280	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL - [N24000323]NHIDCL, ASSAM	10/2014	588.95 -	588.95	494.25	11/2018 -	02/2022	39	-
281	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM - [N24000305]NHIDCL, ASSAM	05/2015	454.89 -	454.89	328.55	05/2018 -	03/2022	46	-
282	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O - [N24000582]NHIDCL, ASSAM	01/2016	294.17 -	294.17	215.45	01/2016 -	03/2022	74	-
283	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561 - [N24000583]NHIDCL, ASSAM	01/2016	252.00 -	252.00	136.88	01/2016 -	03/2022	74	-
284	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM - [N24000678]NHIDCL, ARUNACHAL PRADESH	03/2017	284.09 284.09	284.09	157.65	04/2017 03/2021	03/2022	59	12
285	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00 - [N24000679]NHIDCL, ARUNACHAL PRADESH	02/2017	195.23 -	252.79	133.92	04/2017 -	03/2022	59	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
286	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST - [N24000680]NHIDCL, ARUNACHAL PRADESH	02/2017	203.36 -	263.31	145.13	04/2017 -	03/2022	59	-
287	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM. - [N24000690]NHIDCL, ARUNACHAL PRADESH	01/2017	198.22 -	252.05	144.26	04/2017 -	03/2022	59	-
288	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399 - [N24000741]NHIDCL, UTTARAKHAND	03/2018	274.31 -	274.31	208.47	05/2018 -	03/2022	46	-
289	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI - [N24000742]NHIDCL, UTTARAKHAND	03/2018	403.36 -	403.36	330.75	06/2018 -	03/2022	45	-
290	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA - [N24000743]NHIDCL, UTTARAKHAND	03/2018	417.24 -	417.24	325.44	05/2018 -	03/2022	46	-
291	2 LANE WITH HARD SHOULDER, REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N - [N24000745]NHIDCL, A & N ISLANDS	03/2017	409.85 -	409.85	135.48	12/2017 03/2021	03/2022	51	12
292	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM - [N24000748]NHIDCL, A & N ISLANDS	02/2018	391.00 -	391.00	77.75	10/2018 -	03/2022	41	-
293	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O - [N24000749]NHIDCL, A & N ISLANDS	03/2018	234.27 -	234.27	75.22	10/2018 09/2020	03/2022	41	18
294	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20. - [N24000752]NHIDCL, NAGALAND	02/2017	387.00 -	387.00	309.45	09/2018 -	03/2022	42	-
295	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL - [N24000823]NHIDCL, ASSAM	03/2015	829.00 -	829.00	415.82	01/2016 -	03/2022	74	-
296	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM - [N24000903]NHIDCL, MEGHALAYA	03/2019	306.28 -	306.28	117.91	05/2019 -	03/2022	34	-
297	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50 - [N24000948]NHIDCL, ARUNACHAL PRADESH	09/2016	568.92 -	568.92	310.07	- 11/2021	03/2022	-	4
298	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5 - [N24000949]NHIDCL, ARUNACHAL PRADESH	12/2016	188.78 -	188.78	104.07	- 03/2021	03/2022	-	12
299	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO - [N24000755]NHIDCL, NAGALAND	03/2018	239.30 -	239.30	112.70	09/2018 -	05/2022	44	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
300	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO - [N24000754]NHIDCL,NAGALAND	03/2018	339.57 -	339.57	161.84	09/2018 -	07/2022	46	-
301	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK) - [N24000855]NHIDCL,UTTARAKHAND	03/2018	1,383.78 -	1,383.78	387.45	07/2018 -	07/2022	48	-
302	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO - [N24000756]NHIDCL,NAGALAND	03/2018	285.68 -	285.68	82.34	09/2018 -	09/2022	48	-
303	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO - [N24000764]NHIDCL,NAGALAND	03/2018	272.89 -	272.89	59.98	09/2018 -	10/2022	49	-
304	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING - [N24000753]NHIDCL,NAGALAND	03/2018	500.09 -	500.09	107.72	09/2018 -	11/2022	50	-
305	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO - [N24000765]NHIDCL,NAGALAND	03/2018	323.98 -	323.98	50.13	09/2018 -	11/2022	50	-
306	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000857]NHIDCL,MIZORAM	04/2017	519.09 -	519.09	71.38	09/2019 -	04/2023	43	-
307	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000859]NHIDCL,MIZORAM	04/2017	642.96 -	642.96	71.41	09/2019 04/2023	06/2023	45	2
308	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000863]NHIDCL,MIZORAM	04/2017	518.53 -	518.53	118.95	09/2019 04/2023	06/2023	45	2
309	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000858]NHIDCL,MIZORAM	04/2017	640.07 -	640.07	93.50	09/2019 06/2023	07/2023	46	1
310	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO - [N24000864]NHIDCL,MIZORAM	04/2017	404.29 -	404.29	33.67	09/2019 03/2024	04/2024	55	1
National Highways Authority Of India									
311	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS - [N24000176]NHAI,TAMIL NADU	05/2010	374.00 -	166.90	69.96	05/2013 -	08/2021	99	-
312	4-LANING OF FARAKA-RAIGANJ - [N24000202]NHAI,WEST BENGAL	02/2011	1,078.84 -	1,078.84	2,301.82	08/2013 -	08/2021	96	-
313	FOUR LANING OF YADGIRI - WARANGAL - [N24000486]NHAI,TELANGANA	12/2015	1,423.96 -	1,056.08	995.39	11/2018 -	08/2021	33	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
314	SIX LANING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH - [N24000713]NHAI,MAHARASHTRA	12/2017	404.94 495.24	448.18	462.99	- 05/2021	08/2021	-	3
315	PUNE-SATARA(NH-4) - [N24000156]NHAI,MAHARASHTRA	10/2010	1,724.55 -	1,724.55	2,615.35	03/2013 -	09/2021	102	-
316	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY - [N24000173]NHAI,TAMIL NADU	06/2011	600.00 -	600.00	4.62	06/2013 -	09/2021	99	-
317	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM - [N24000445]NHAI,RAJASTHAN	08/2014	822.90 -	822.90	844.08	04/2018 -	09/2021	41	-
318	8 LANING OF MUKARBA CHOWK TO PANIPAT - [N24000449]NHAI,HARYANA	07/2015	2,128.72 -	2,128.72	1,577.44	04/2019 -	09/2021	29	-
319	4-LANNING OF END OF PANDOH BYPASS TAKOLI IN H.P - [N24000692]NHAI,HIMACHAL PRADESH	06/2017	2,485.93 -	2,485.93	983.69	06/2020 -	09/2021	15	-
320	DELHI AGRA APPROVED LENGTH 180.0 KM - [N24000224]NHAI,MULTI STATE	10/2012	1,928.22 1,928.22	1,928.22	1,876.06	04/2015 01/2021	12/2021	80	11
321	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K - [N24000557]NHAI,TAMIL NADU	02/2016	641.17 -	641.17	395.10	07/2018 -	12/2021	41	-
322	NAGPUR RING ROAD PACKAGE-1 - [N24000558]NHAI,MAHARASHTRA	03/2016	546.00 -	546.00	309.98	07/2019 -	12/2021	29	-
323	NAGPUR RING ROAD PACKAGE-2 - [N24000560]NHAI,MAHARASHTRA	03/2016	591.66 -	591.66	319.05	07/2019 -	12/2021	29	-
324	FOUR LANNING OF VIKRAVANDI- SETHIAHOPU FROM KM 0.000 TO KM 60.250(DSIGN CHAINAGE KM 0.000 TO KM 65. - [N24000652]NHAI,TAMIL NADU	03/2017	848.45 -	848.45	235.72	03/2020 -	12/2021	21	-
325	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV - [N24000691]NHAI,RAJASTHAN	04/2017	894.00 -	929.32	810.00	04/2020 -	12/2021	20	-
326	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH - [N24000694]NHAI,TAMIL NADU	03/2016	641.17 -	641.17	395.10	07/2016 -	12/2021	65	-
327	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE - [N24001231]NHAI,MADHYA PRADESH	02/2019	990.97 -	990.97	690.00	12/2019 -	12/2021	24	-
328	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENHTH 170 KM) - [N24000213]NHAI,TAMIL NADU	04/2012	624.00 -	624.00	108.46	04/2014 -	01/2022	93	-
329	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH - [N24000555]NHAI,TAMIL NADU	02/2016	707.82 -	707.82	428.72	08/2018 -	01/2022	41	-
330	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31 - [N24000696]NHAI,BIHAR	08/2017	950.64 -	950.64	308.25	08/2017 -	02/2022	54	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
331	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY - [N24000552]NHAI,KARNATAKA	03/2016	701.40 -	701.40	146.05	03/2019 -	03/2022	36	-
332	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS- CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO - [N24001232]NHAI,MADHYA PRADESH	02/2019	847.00 -	847.00	498.00	03/2020 -	04/2022	25	-
333	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG - [N24001233]NHAI,MADHYA PRADESH	03/2019	1,047.00 -	1,047.00	486.00	05/2020 -	05/2022	24	-
334	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB ,SERVICE ROADS ,FOOTPATH FOR RCC DRAINS ON URBAN - [N24000442]NHAI,MAHARASHTRA	12/2015	649.50 -	649.50	233.12	03/2019 12/2021	06/2022	39	6
335	FOUR LANNING OF CHOLOPURAM-THANJAVUR - [N24000697]NHAI,TAMIL NADU	08/2017	1,176.37 -	1,176.37	614.68	08/2017 -	07/2022	59	-
336	4-LANNING OF STHIYATHOPU-CHOLOPURAM - [N24000708]NHAI,TAMIL NADU	09/2017	1,227.87 -	1,227.87	644.68	09/2017 -	07/2022	58	-
337	HOSPET-BELLARY-KARNATAKA AP BORDER - [N24000603]NHAI,KARNATAKA	08/2016	1,167.42 -	870.00	334.82	03/2019 01/2021	09/2022	42	20
338	CONSTRUCTION OF PARTIALLY ACESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN - [N24000662]NHAI,PUNJAB	03/2017	754.54 -	756.27	430.26	03/2020 -	09/2022	30	-
339	VARANASI-AURANGABAD KM.786 TO KM.978.40 - [N24000182]NHAI,MULTI STATE	09/2011	2,848.00 -	3,379.45	3,379.45	03/2014 -	12/2022	105	-
340	4-LANING OF BRAHAMPORE-FARAKA - [N24000203]NHAI,WEST BENGAL	02/2011	998.79 -	998.79	1,890.84	08/2013 -	06/2023	118	-
	Total		58,997.45 -	58,909.57	38,428.70				
	<u>TELECOMMUNICATIONS</u>								
	<u>Bharat Sanchar Nigam Limited</u>								
341	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART - [N26000114]BSNL,MULTI STATE	03/2020	431.16 422.87	422.87	-	06/2021 -	11/2021	5	-
	<u>Central Public Works Department</u>								
342	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT - [N28000115]CPWD,DELHI	10/2014	248.20 -	248.20	145.26	03/2018 -	12/2021	45	-
	<u>Department Of Telecommunication</u>								
343	NETWORK FOR SPECTRUM - [N26000101]DOT,MULTI STATE	03/2012	13,334.00 24,664.00	24,664.00	17,845.00	07/2015 05/2020	03/2022	80	22
	Total		14,013.36 -	25,335.07	17,990.26				
	<u>URBAN DEVELOPMENT</u>								
	<u>Ahmedabad Metro Rail</u>								
344	AHMEDABAD METRO RAIL PROJECT PHASE 1 - [N28000122]MEGA,GUJARAT	11/2014	10,773.00 -	12,787.00	9,144.21	12/2018 -	08/2022	44	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	<u>Bangalore Metro Rail Corporation Limited</u>								
345	BANGALORE METRO RAIL PROJECT PHASE-2 - [N28000058]BMRC,L,KARNATAKA	02/2014	26,405.14 30,695.12	30,695.12	18,226.61	02/2019 -	03/2025	73	-
	<u>Central Public Works Department</u>								
346	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I - [N28000129]CPWD,DELHI	10/2016	1,128.00 1,128.00	1,128.00	28.50	03/2022 -	06/2023	15	-
	<u>Delhi Metro Rail Corporation</u>								
347	DELHI MRTS PHASE-III - [N28000056]DMRC,DELHI	09/2011	38,585.00 -	38,585.00	39,332.34	03/2016 -	08/2021	65	-
348	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND - [N28000136]DMRC,DELHI	05/2017	565.00 -	565.00	468.78	12/2020 -	08/2021	8	-
	<u>Lucknow Metro Rail Corporation Limited</u>								
349	KANPUR METRO RAIL PROJECT - [N28000144]LMRCL,UTTAR PRADESH	05/2019	11,076.48 -	11,076.48	1,690.78	03/2024 -	03/2025	12	-
350	AGRA METRO RAIL PROJECT - [N28000145]LMRCL,UTTAR PRADESH	05/2019	8,379.62 -	8,379.62	364.47	03/2024 -	05/2025	14	-
	Total		96,912.24 -	1,03,216.22	69,255.69				
	<u>WATER RESOURCES</u>								
	<u>Brahmaputra Board</u>								
351	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA - [N30000001]BPPB,MAHARASHTRA	03/2017	233.57 -	233.57	148.83	12/2019 -	12/2021	24	-
	<u>Bihar Urban Infrastructure Development Corporation Ltd</u>								
352	SEWER NETWORKS SPS AND STP HAJIPUR - [N30000035]BUIDCO,BIHAR	03/2018	305.19 -	305.19	24.12	08/2021 -	12/2021	4	-
	<u>Delhi Jal Board</u>								
353	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2 - [N30000015]DJB,DELHI	05/2016	211.79 -	211.79	101.28	12/2021 -	12/2022	12	-
354	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S - [N30000016]DJB,DELHI	05/2016	239.11 -	239.11	138.16	02/2022 -	12/2022	10	-
	<u>Kolkata Metropolitan Development Authority</u>								
355	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA - [N30000032]KMDA, WEST BENGAL	05/2018	198.43 224.69	224.69	-	02/2022 -	06/2022	4	-
356	INTERCEPTION AND DIVERSION WITH STP AT HUGHLI-CHINSURAH - [N30000042]KMDA, WEST BENGAL	05/2018	160.00 154.73	154.73	-	02/2022 -	10/2022	8	-
	<u>Polavaram Project Authority</u>								
357	POLAVARAM IRRIGATION PROJECT - [N30000002]PPA,ANDHRA PRADESH	02/2009	10,151.04 55,548.87	55,548.87	17,935.78	03/2020 11/2021	04/2022	25	5
	<u>Uttar Pradesh Jal Nigam</u>								
358	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH - [N30000025]UPJalNigam,UTTAR PRADESH	03/2019	298.12 213.91	213.91	-	07/2021 -	06/2022	11	-

Costing Rs. 150 Crore and above

(August 2021)

S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Date of Commissioning		Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
						Original / Revised	Anticipated		
1	2	3	4	5	6	7	8	9	10
	Total		11,797.25 -	57,131.86	18,348.17				
	<u>DEFENCE PRODUCTION</u>								
	<u>Central Public Works Department</u>								
359	RESIDENTIAL QUARTERS FOR HAL, BANGLORE - [N28000103]CPWD, KARNATAKA	12/2016	246.31 210.00	210.00	136.16	02/2020 10/2021	12/2021	22	2
	Total		246.31 -	210.00	136.16				
	<u>DEPARTMENT OF HIGHER EDUCATION</u>								
360	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA - [N28000100]CPWD, BIHAR	02/2016	496.18 496.00	498.99	288.03	06/2017 -	03/2022	57	-
361	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB - [N28000120]CPWD, PUNJAB	01/2018	430.00 -	387.83	218.29	05/2020 -	03/2022	22	-
362	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR - [N28000126]CPWD, ODISHA	01/2019	790.79 -	790.79	213.06	03/2022 -	06/2022	3	-
363	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE, KANJIKODE WEST, DISTRICT - PALAKKA - [N28000140]CPWD, KERALA	07/2019	753.63 -	753.63	58.47	03/2021 -	06/2022	15	-
364	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A) - [N42000006]CPWD, KARNATAKA	07/2019	851.00 851.00	851.00	26.10	03/2022 -	09/2022	6	-
365	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB. - [N28000142]CPWD, PUNJAB	10/2019	348.24 -	348.24	23.28	05/2022 -	10/2022	5	-
366	PERMANENT CAMPUS FOR IIM BODH GAYA - [N42000009]CPWD, BIHAR	09/2018	375.00 -	375.00	48.46	09/2020 -	11/2022	26	-
367	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRICT - [N42000007]CPWD, ANDHRA PRADESH	09/2019	588.72 -	588.72	14.80	09/2022 -	01/2023	4	-
	Total		4,633.56 -	4,594.20	890.49				
	<u>HOME AFFAIRS</u>								
368	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI - [N28000071]CPWD, DELHI	10/2013	1,219.21 -	2,000.00	956.28	10/2019 -	03/2022	29	-
369	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDALI - [N45000003]CPWD, UTTAR PRADESH	05/2019	199.31 -	199.31	27.86	01/2022 -	06/2022	5	-
	Total		1,418.52 -	2,199.31	984.14				

Costing Rs. 150 Crore and above

(August 2021)

						Date of Commissioning			
S.No	Project	Date of Approval	Original/ Revised Cost (Rs. crore)	Anticipated Cost (Rs. crore)	Cumulative Expenditure Cost (Rs. crore)	Original / Revised	Anticipated	Delay w.r.t. original (in months)	Delay w.r.t. Revised (in months)
1	2	3	4	5	6	7	8	9	10
	<u>RURAL DEVELOPMENT</u>								
	<u>Hindustan Steelwork Construction Limited</u>								
370	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V - [N12000098]HSCL,TRIPURA	03/2007	149.73 173.00	155.66	144.95	12/2015 -	02/2022	74	-
371	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI - [N12000099]HSCL,TRIPURA	12/2007	202.61 227.00	207.12	190.22	12/2016 -	03/2022	63	-
372	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII - [N12000100]HSCL,TRIPURA	10/2011	175.49 206.71	175.49	124.87	12/2016 -	09/2022	69	-
	Total		527.83 -	538.27	460.04				
	<u>DONER</u>								
373	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGHALAYA UNDER NLCPR - [N12000103]HSCL,MEGHALAYA	04/2014	151.33 -	151.33	149.33	09/2017 -	08/2021	47	-
	Total		151.33 -	151.33	149.33				
	Grand Total		6,02,257.45	7,99,235.36	4,47,220.05				

Details of North East Projects Costing Rs.150 crore and above (as on					31.08.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
1	SUBANSIRI LOWER H.E.P (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	14,059.55 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
2	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [3/2021]	172.75 (-) [172.75]	134.38 (0.00) [0]
3	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (522.86) [522.86]	410.63 (128.86) [0]
4	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [10/2021]	210.50 (-) [210.50]	145.07 (0.00) [-]
5	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	8/2021 (-) [8/2021]	496.47 (-) [496.47]	0.00 (0.00) [0]
6	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	210.90 (0.00) [0]
7	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	8/2021 (-) [8/2021]	437.60 (-) [437.60]	0.00 (0.00) [0]
8	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	0.00 (0.00) [0]
9	BALANCE WORK OF 2-LANING OF LONGDING- TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	0.00 (0.00) [0]
10	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)	3/2019	2/2020 (-) [0/0]	403.68 (-) [403.68]	63.69 (0.00) [0]
11	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	119.81 (0.00) [0]
12	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	37.16 (0.00) [0]
13	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	75.26 (0.00) [0]
14	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	148.75 (0.00) [0]
15	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	93.70 (0.00) [0]

16	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	15.49 (0.00) [0]
17	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	144.45 (0.00) [0]
18	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	50.14 (0.00) [0]
19	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (8/2021) [12/2021]	200.44 (-) [200.44]	125.91 (0.00) [-]
20	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	/ (11/2021) [3/2022]	568.92 (-) [568.92]	310.07 (0.00) [-]
21	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (3/2021) [3/2022]	188.78 (-) [188.78]	104.07 (0.00) [-]
22	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (1/2021) [12/2021]	245.79 (-) [245.79]	204.42 (0.00) [-]
23	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (6/2022) [3/2022]	1,718.59 (-) [1,718.59]	519.92 (0.00) [-]
24	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	23.41 (0.00) [0]
25	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	18.03 (0.00) [0]
26	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [8/2020]	167.28 (-) [167.28]	22.06 (0.00) [0]
27	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
28	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	0.00 (0.00) [0]
29	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (-) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
30	LADDA - BASAI	2/2021	4/2023 (-) [4/2023]	445.96 (-) [445.96]	0.00 (0.00) [0]
31	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
32	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2021) [3/2022]	284.09 (284.09) [284.09]	157.65 (0.00) [59]
33	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	133.92 (57.56) [59]
34	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [3/2022]	203.36 (-) [263.31]	145.13 (59.95) [59]
35	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	144.26 (53.83) [59]
36	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON	2/2017	4/2017	180.57	60.86

	EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX		(-) [2/2021]	(-) [180.57]	(0.00) [0]
37	TWO-LANING OF HAYULIANG– HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/	256.66	16.42
			(-) [3/2021]	(-) [256.66]	(0.00) [0]
38	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/	175.06	87.32
			(4/2022) [4/2022]	(-) [175.06]	(0.00) [-]
39	TWO-LANING OF JORAM – KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/	176.12	73.92
			(4/2022) [4/2022]	(-) [176.12]	(0.00) [-]
40	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/	1,979.00	1,242.64
			(3/2020) [0/0]	(-) [2,036.90]	(57.90) [0]
41	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	9/2021	182.55	0.00
			(-) [9/2021]	(-) [182.55]	(0.00) [0]
	ASSAM				
	Civil Aviation				
42	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021	1,142.00	371.33
			(3/2022) [3/2023]	(-) [1,232.00]	(90.00) [24]
	Health And Family Welfare				
43	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021	875.00	387.54
			(9/2022) [9/2022]	(-) [747.80]	(-127.20) [16]
44	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014	175.57	163.37
			(-) [3/2018]	(-) [175.57]	(0.00) [0]
	Petroleum				
45	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020	557.00	537.30
			(6/2021) [9/2021]	(-) [557.00]	(0.00) [19]
46	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020	224.75	178.00
			(9/2021) [9/2021]	(222.21) [198.00]	(-26.75) [13]
47	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019	423.00	440.03
			(6/2021) [5/2021]	(-) [502.00]	(79.00) [0]
48	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020	543.91	383.44
			(-) [12/2021]	(652.10) [638.60]	(94.69) [22]
49	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024	12,366.00	567.38
			(-) [10/2024]	(-) [12,366.00]	(0.00) [0]
50	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024	10,228.00	285.27
			(-) [10/2024]	(-) [10,228.00]	(0.00) [0]
51	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020	249.85	205.92
			(8/2021) [11/2021]	(303.75) [303.75]	(53.90) [18]
	Railways				
52	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019	314.00	832.55
			(-) [6/2021]	(486.96) [800.00]	(486.00) [0]
53	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022	2,232.32	1,758.52
			(-) [3/2023]	(-) [2,950.00]	(717.68) [12]
54	DIGARU-HOJAI (102 KM)	4/2015	3/2021	870.96	1,397.73
			(-) [3/2022]	(-) [1,873.21]	(1,002.25) [12]

55	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,105.00]	858.45 (719.80) [48]
Road Transport And Highways					
56	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (5/2022) [5/2022]	268.08 (-) [390.73]	318.85 (122.65) [60]
57	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	23.56 (0.00) [0]
58	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
59	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	26.88 (0.00) [0]
60	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	189.59 (0.00) [-]
61	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [2/2022]	588.95 (-) [588.95]	494.25 (0.00) [39]
62	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2021]	289.99 (-) [289.99]	87.90 (0.00) [36]
63	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	136.88 (0.00) [74]
64	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	105.09 (0.00) [42]
65	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	215.45 (0.00) [74]
66	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	10.45 (0.00) [0]
67	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	28.18 (0.00) [0]
68	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [12/2022]	166.94 (-) [166.94]	28.02 (0.00) [24]
69	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010 (-) [7/2019]	217.61 (-) [360.84]	489.84 (143.23) [0]
70	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	0.00 (0.00) [0]
71	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	0.00 (0.00) [0]
72	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
73	DHARAMTUL TO SONAPUR,KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	270.97 (7.98) [0]
74	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	145.72 (0.00) [36]

75	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [3/2023]	818.00 (-) [818.00]	287.52 (0.00) [-]
76	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	159.34 (0.00) [42]
77	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
78	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	328.55 (0.00) [46]
79	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [612.58]	612.58 (332.58) [0]
80	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
81	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	3.23 (0.00) [0]
82	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
83	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
84	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
85	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [2/2021]	208.00 (-) [230.00]	370.56 (22.00) [0]
86	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	390.72 (0.00) [0]
87	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	143.02 (0.00) [-]
88	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	240.36 (-70.66) [0]
89	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0 AN	9/2018	9/2021 (-) [9/2021]	160.00 (-) [160.00]	116.26 (0.00) [0]
90	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [12/2022]	636.42 (-) [636.42]	0.00 (0.00) [0]
91	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
92	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	86.48 (0.00) [0]
93	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	24.01 (0.00) [0]
94	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	27.76 (0.00) [0]
	MANIPUR				

	Power				
95	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (1,311.05) [1,311.05]	155.41 (732.43) [0]
	Railways				
96	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	11,303.51 (7,809.98) [153]
	Road Transport And Highways				
97	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	40.95 (0.00) [0]
98	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	29.70 (0.00) [0]
99	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	32.49 (0.00) [0]
100	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	27.29 (0.00) [0]
101	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	23.02 (0.00) [0]
102	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
103	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	0.00 (0.00) [0]
104	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
105	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]
106	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	2.29 (0.00) [0]
107	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	116.31 (0.00) [0]
108	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	0.00 (0.00) [0]
109	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	0.00 (0.00) [0]
110	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	0.00 (0.00) [0]
111	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [0/0]	235.31 (-) [235.31]	195.72 (0.00) [0]
112	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	0.00 (0.00) [0]
113	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [36]
	MEGHALAYA				

	<u>Department Of Higher Education</u>				
114	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Doner</u>				
115	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [8/2021]	151.33 (-) [151.33]	149.33 (0.00) [47]
	<u>Health And Family Welfare</u>				
116	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [3/2022]	363.99 (-) [363.99]	246.43 (0.00) [46]
	<u>Railways</u>				
117	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.34 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
118	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	40.99 (0.00) [0]
119	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [3/2022]	306.28 (-) [306.28]	117.91 (0.00) [34]
120	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	2.63 (0.00) [0]
121	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	27.54 (0.00) [0]
122	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	12.93 (0.00) [0]
123	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	0.00 (0.00) [0]
124	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4 (KANAI-RONGARA)	10/2020	4/2022 (-) [4/2022]	157.86 (-) [157.86]	17.63 (0.00) [0]
125	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
126	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (9/2021) [9/2021]	553.51 (-) [553.51]	127.99 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
127	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2024]	2,393.47 (5,021.45) [5,521.45]	4,169.01 (3,127.98) [120]
	<u>Road Transport And Highways</u>				
128	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2021) [12/2021]	195.04 (-) [377.99]	368.39 (182.95) [134]
129	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2021) [12/2021]	186.96 (-) [322.24]	304.71 (135.28) [87]
130	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2021) [12/2021]	193.69 (-) [327.92]	323.23 (134.23) [134]
131	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-)	275.02 (-)	22.39 (0.00)

			[10/2022]	[275.02]	[0]
132	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	21.58 (0.00) [0]
133	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	33.63 (0.00) [0]
134	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	37.79 (0.00) [0]
135	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	73.31 (0.00) [0]
136	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	0.00 (0.00) [0]
137	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	0.00 (0.00) [0]
138	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	0.00 (0.00) [0]
139	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
140	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
141	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	71.38 (0.00) [43]
142	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [7/2023]	640.07 (-) [640.07]	93.50 (0.00) [46]
143	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	642.96 (-) [642.96]	71.41 (0.00) [45]
144	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (3/2024) [4/2024]	404.29 (-) [404.29]	33.67 (0.00) [55]
145	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (9/2023) [9/2023]	428.11 (-) [428.11]	71.30 (0.00) [48]
146	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	518.53 (-) [518.53]	118.95 (0.00) [45]
147	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [4/2023]	537.82 (-) [537.82]	121.93 (0.00) [43]
148	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [4/2023]	473.18 (-) [473.18]	108.59 (0.00) [43]
149	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2021) [12/2021]	624.41 (-) [992.67]	890.74 (368.26) [129]
	<u>NAGALAND</u>				
	<u>Railways</u>				
150	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
151	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA)	4/2006	3/2015	2,326.52	1,300.10

	NATIONAL PROJECT (NEFR)		(-) [3/2026]	(-) [6,911.00]	(4,584.48) [132]
	<u>Road Transport And Highways</u>				
152	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	112.70 (0.00) [44]
153	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	82.34 (0.00) [48]
154	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	153.26 (0.00) [38]
155	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	309.45 (0.00) [42]
156	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	107.72 (0.00) [50]
157	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	31.88 (0.00) [0]
158	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	55.79 (0.00) [0]
159	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	23.62 (0.00) [0]
160	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	40.40 (0.00) [0]
161	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	30.14 (0.00) [0]
162	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	68.48 (0.00) [0]
163	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (8/2021) [8/2021]	217.35 (-) [217.35]	97.62 (0.00) [9]
164	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	40.94 (0.00) [0]
165	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
166	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	4.98 (0.00) [0]
167	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	26.41 (0.00) [0]
168	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	2.80 (0.00) [0]
169	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	161.84 (0.00) [46]
170	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	101.42 (0.00) [39]
171	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS	3/2018	9/2018	240.64	112.90

	OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO		(-) [12/2021]	(-) [240.64]	(0.00) [39]
172	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	107.31 (0.00) [38]
173	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	70.57 (0.00) [39]
174	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	59.98 (0.00) [49]
175	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	50.13 (0.00) [50]
176	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	146.10 (0.00) [38]
177	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	120.12 (0.00) [38]
178	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	325.21 (13.93) [0]
179	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	298.94 (0.00) [0]
180	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [2/2021]	429.52 (-) [429.52]	238.28 (0.00) [0]
181	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (369.96) [369.96]	322.13 (33.71) [0]
182	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [9/2021]	167.62 (-) [167.62]	104.39 (0.00) [9]
183	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [9/2021]	172.63 (-) [172.63]	129.65 (0.00) [9]
184	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	7.28 (0.00) [0]
185	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	75.42 (0.00) [0]
	<u>SIKKIM</u>				
	<u>Railways</u>				
186	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	1,656.02 (7,260.52) [96]
	<u>Road Transport And Highways</u>				
187	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	1.29 (0.00) [0]
188	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP BRIDGE AT	10/2020	11/2023 (-) [11/2023]	493.42 (-) [493.42]	0.00 (0.00) [0]
189	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	17.38 (0.00) [0]
190	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING	7/2020	4/2023 (-)	345.38 (-)	74.52 (0.00)

	GEOMETRIC IMPROV		[4/2023]	[345.38]	[0]
191	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (6/2021) [0/0]	182.28 (369.58) [369.58]	340.16 (187.30) [0]
192	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (6/2021) [0/0]	151.59 (369.92) [369.92]	343.48 (218.33) [0]
193	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	0.00 (0.00) [0]
194	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	0.00 (0.00) [0]
195	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (6/2021) [0/0]	166.27 (359.90) [359.90]	302.35 (193.63) [0]
196	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	64.34 (0.00) [0]
197	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [12/2021]	290.05 (-) [290.05]	119.27 (0.00) [49]
198	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
199	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
200	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	44.89 (0.00) [0]
201	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	19.19 (0.00) [0]
202	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	32.98 (0.00) [0]
203	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	2.53 (0.00) [0]
204	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	271.35 (59.37) [0]
205	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
206	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Railways</u>				
207	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
208	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	352.63 (0.00) [0]
209	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	14.98 (0.00) [0]

210	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	29.13 (0.00) [0]
211	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	64.89 (0.00) [0]
212	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	0.00 (0.00) [0]
213	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	0.00 (0.00) [0]
214	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	3.42 (0.00) [0]
215	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	59.20 (0.00) [0]
216	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	7.72 (0.00) [0]
217	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	0.00 (0.00) [0]
218	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	0.00 (0.00) [0]
219	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	6.87 (0.00) [0]
220	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	12.08 (0.00) [0]
221	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	15.01 (0.00) [0]
222	STRENGTHENING OF CHURABARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	95.22 (0.00) [0]
223	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	21.65 (38.51) [0]
224	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [10/2021]	171.90 (-) [171.90]	142.81 (0.00) [14]
Rural Development					
225	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [2/2022]	149.73 (173.00) [155.66]	144.95 (5.93) [74]
226	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [3/2022]	202.61 (227.00) [207.12]	190.22 (4.51) [63]
227	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [9/2022]	175.49 (206.71) [175.49]	124.87 (0.00) [69]
	Total			1,28,203.87 (36,159.99) [1,75,372.61]	64,723.78 (47,168.74)

Details of State wise Projects Costing Rs.150 crore and above (as on					31.08.2021)
Sl.No	Project	Date of Approval (month / year)	Original (Revised) [Anticipated] Date of Commissioning (month / year)	Original (Revised) [Anticipated] Cost (Rs. crore)	Cumulative Expenditure in Rs. crore (Cost Overrun in Rs. crore) [Time Overrun in months]
	<u>A & N ISLANDS</u>				
	<u>Civil Aviation</u>				
1	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT VSI AIRPORT, PORTBLAIR	10/2013	9/2018 (6/2022) [6/2022]	417.23 (707.73) [707.73]	456.88 (290.50) [45]
	<u>Road Transport And Highways</u>				
2	2 LANE WITH HARD SHOLDER , REHABILITATION AND UP GRADATION OF SECTION FROM KM 242.0 TO KM 298.0 OF N	3/2017	12/2017 (3/2021) [3/2022]	409.85 (-) [409.85]	135.48 (0.00) [51]
3	AJANTHA TO BULDHANA	2/2017	7/2019 (-) [0/0]	401.00 (401.00) [401.00]	220.93 (0.00) [0]
4	CONSTRUCTION OF MAJOR BRIDGE OVER HUMPHREY STRAIT CREEK BETWEEN KM. 129.420 TO KM. 130.600 OF NH 4 C	3/2015	4/2017 (3/2021) [10/2021]	277.17 (-) [277.17]	202.59 (0.00) [54]
5	CONSTRUCTION OF MAJOR BRIDGE OVER MIDDLE STRAIT CREEK BETWEEN KM. 106.590 TO KM. 107.762 OF NH 223 (	3/2015	10/2018 (1/2022) [1/2022]	262.97 (-) [262.97]	63.74 (0.00) [39]
6	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (3/2021) [3/2021]	257.34 (-) [238.00]	0.00 (-19.34) [0]
7	REHABILITATION AND UP GRADATION OF SECTION FROM KM 107.760 TO KM 129.445 (AFTER MIDDLE STRAIT TO HUM	2/2018	10/2018 (-) [3/2022]	391.00 (-) [391.00]	77.75 (0.00) [41]
8	REHABILITATION AND UP GRADATION OF SECTION FROM KM 206.00 TO KM 242.00 (NIMBUTALA TO AUSTIN CREEK) O	3/2018	10/2018 (9/2020) [3/2022]	234.27 (-) [234.27]	75.22 (0.00) [41]
9	Rehabilitation and up gradation to 2 lane with paved shoulder configuration from existing km. 122.00	11/2017	11/2019 (10/2021) [10/2021]	237.80 (237.80) [238.00]	148.90 (0.20) [23]
	<u>ANDHRA PRADESH</u>				
	<u>Civil Aviation</u>				
10	C/O OF NITB AND ASSOCIATED WORK AT VIJAYAWADA AIRPORT	4/2020	3/2023 (-) [3/2023]	611.80 (-) [611.80]	33.70 (0.00) [0]
11	EXT AND STR. OF EXISTING RUNWAY 08/26 AT TIRUPATI AIRPORT	8/2017	2/2020 (6/2021) [5/2022]	177.10 (-) [177.10]	98.00 (0.00) [27]
	<u>Department Of Higher Education</u>				
12	C/O PERMANENT CAMPUS FOR NITAP UNDER PHASE 1B AT TADEPALLIGUDEM, A.P.	2/2019	9/2020 (-) [0/0]	186.00 (199.00) [205.00]	130.63 (19.00) [0]
13	CONSTRUCTION OF PERMANENT CAMPUS FOR IISER AT JANGALAPALLI VILLAGE, YERPEDU MANDAL, CHITTOOR DISTRIC	9/2019	9/2022 (-) [1/2023]	588.72 (-) [588.72]	14.80 (0.00) [4]
14	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY TIRUPATI AT MERLAPAKA VILLAGE YE	2/2019	6/2020 (-) [0/0]	655.34 (-) [655.34]	125.17 (0.00) [0]

	<u>Health And Family Welfare</u>				
15	HOSPITAL AND TEACHING- AIIMS GUNTUR	3/2018	/ (-) [9/2021]	601.02 (-) [601.02]	453.44 (0.00) [-]
16	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS- MNAGLAGIRI GUNTUR, ANDHRA PRADESH	8/2017	3/2019 (-) [3/2021]	272.19 (-) [272.54]	268.55 (0.35) [0]
	<u>Petroleum</u>				
17	220 KV GRID SUPPLY	10/2020	3/2021 (-) [8/2021]	303.40 (-) [303.40]	211.10 (0.00) [5]
18	CGD PROJECT AT SRIKAKULAM, VISAKHAPATNAM AND VIZIANAGARAM DISTRICTS	6/2019	8/2027 (-) [8/2027]	2,880.00 (-) [2,880.00]	0.00 (0.00) [0]
19	CONSTRUCTION OF GRASS ROOT PETROLEUM TOP AT ATCHUTAPURAM, ANDHRA PRADESH	8/2018	4/2021 (12/2021) [12/2021]	466.00 (-) [466.00]	280.16 (0.00) [8]
20	CONSTRUCTION OF RAIL FED DEPOT AT GUNTAKAL, AP	8/2017	4/2021 (3/2021) [3/2021]	384.58 (-) [384.58]	269.55 (0.00) [0]
21	DEVELOPMENT OF COASTAL TERMINAL AT KRISHNAPATNAM PORT	7/2017	2/2021 (-) [3/2023]	580.20 (-) [580.20]	207.44 (0.00) [25]
22	KG-DWN-98-2 CLUSTER II DEVELOPMENT PROJECT	3/2016	6/2020 (6/2022) [6/2022]	34,012.00 (-) [25,090.00]	13,580.92 (-8,922.00) [24]
23	LPG BP PROJECT CHITTOOR	7/2019	7/2022 (-) [7/2022]	167.00 (-) [167.00]	9.93 (0.00) [0]
24	REVAMPING OF FACILITIES AT VIZAG TERMINAL	4/2018	4/2022 (-) [2/2023]	355.00 (-) [355.00]	120.72 (0.00) [10]
25	REVAMPING OF VIJAYAWADA TERMINAL FOR CONVERSION TO TOP	10/2018	10/2021 (3/2022) [3/2022]	316.20 (-) [316.20]	116.20 (0.00) [5]
26	RUF PITCH LOADING GANTRY	10/2020	11/2022 (-) [11/2022]	332.61 (-) [332.61]	0.01 (0.00) [0]
27	SULPHUR FORMING UNIT IN SRU	10/2020	8/2021 (-) [8/2021]	210.94 (-) [210.94]	121.18 (0.00) [0]
28	SWRO II WITH LLPH FACILITIES	9/2019	7/2020 (-) [9/2021]	196.26 (-) [196.26]	92.83 (0.00) [14]
29	VISAKH REFINERY MODERNISATION PROJECT	7/2016	7/2020 (7/2022) [7/2022]	20,928.00 (26,264.00) [26,264.00]	16,008.48 (5,336.00) [24]
	<u>Railways</u>				
30	CUMBUM-PRODDATUR	4/2013	/ (-) [0/0]	829.00 (-) [829.00]	0.94 (0.00) [0]
31	DUVVADA-VIJAYAWADA	4/2015	/ (-) [0/0]	3,873.07 (-) [3,873.07]	0.38 (0.00) [0]
32	GUDUR-DURGARAJAPATNAM	4/2011	/ (-) [0/0]	761.37 (-) [761.37]	0.52 (0.00) [0]
33	GUNTUR-GUNTAKAL	4/2016	3/2022 (-) [3/2024]	3,631.00 (-) [3,887.48]	1,239.48 (256.48) [24]
34	KOTLPALLI-NARASAPUR (NL) (SCR)	12/2001	3/2009	1,045.20	1,009.94

			(-) [3/2024]	(-) [2,120.16]	(1,074.96) [180]
35	KOTTAVALSA - KORAPUT DOUBLING	4/2015	3/2022 (3/2024) [3/2024]	2,499.71 (-) [2,499.71]	727.14 (0.00) [24]
36	MULTI MODAL LOGISTICS PARK AT KAKINADA	8/2016	3/2019 (-) [0/0]	234.50 (-) [235.00]	14.14 (0.50) [0]
37	MULTI MODAL LOGISTICS PARK AT VISHAKHAPATNAM	1/2013	3/2018 (-) [0/0]	387.70 (-) [487.13]	434.63 (99.43) [0]
38	NADIKUDE-SRI KALAHASTI	4/2011	3/2021 (-) [3/2024]	2,288.70 (-) [2,643.25]	1,277.06 (354.55) [36]
39	NANDYAL-YERRAGUNTALA(NL),SCR	3/1996	2/2009 (-) [0/0]	164.36 (-) [1,050.00]	999.64 (885.64) [0]
40	VIJAYAWADA-GUDUR	4/2015	12/2023 (-) [12/2023]	3,246.26 (-) [3,548.68]	1,568.77 (302.42) [0]
41	VIJAYWADA-GUDUGOLANU-BHIMAVARAM-NARSAPUR DL (221 KM)	3/2012	3/2020 (-) [3/2022]	1,503.71 (-) [3,377.00]	2,152.52 (1,873.29) [24]
	<u>Road Transport And Highways</u>				
42	6-LANING OF EXISTING 2-LANE (I) NANDIGAMA BYPASS FROM KM 220.700 TO KM 226.600 (DESIGN CHAINAGE FROM	12/2017	/ (-) [0/0]	328.67 (-) [328.67]	266.63 (0.00) [0]
43	6-LANING OF VIJAYAWADA BYPASS FROM CHINNA AVUTUPALLI (DESIGN CH.0+000) TO GOLLAPUDI (DESIGN CH. 30+0	11/2019	2/2021 (-) [0/0]	1,226.88 (-) [1,226.88]	146.49 (0.00) [0]
44	6-LANING OF VIJAYAWADA BYPASS FROM GOLLAPUDI (DESIGN CH. 30+000) TO CHINNAKAKANI (DESIGN CH. 47+881)	11/2019	2/2021 (-) [0/0]	1,601.10 (-) [1,601.10]	10.51 (0.00) [0]
45	CAPACITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHHAPURAM TO NARASANNAPETA IN THE STATE O	12/2017	/ (-) [0/0]	357.00 (-) [357.00]	0.00 (0.00) [0]
46	CAPICITY AUGMENTATION OF THE EXISTING 4 LANE STRETCH FROM ICHAPURAM TO NARASANNAPETA FROM KM 470.415	3/2018	/ (-) [0/0]	557.30 (-) [557.30]	433.20 (0.00) [0]
47	CONSTRUCTION OF 2L+PS FROM PASARLAPUDI-DHINDI (105/700 TO 127.500 OF NH-214) OF NH-216	1/2017	9/2017 (5/2022) [5/2022]	263.45 (381.75) [263.45]	116.24 (0.00) [56]
48	CONSTRUCTION OF 4-LANE BYPASS TO VIJAYANAGARAM TOWN ON NH43 (NEW NH26) FROM 537/6 TO 552/0 (RAIPUR-V	2/2017	11/2017 (1/2022) [0/0]	429.43 (373.05) [429.43]	319.71 (0.00) [0]
49	CONSTRUCTION OF SIX LANING OF DEDICATED PORT ROAD TO KRISHNAPATNAM PORT (PACKAGE-I) KM 0+000 TO KM 1	3/2018	/ (-) [3/2022]	314.43 (-) [314.43]	85.61 (0.00) [-]
50	CONSTRUCTION OF TIMMAPURAM TO GURJANAPALLE SECTION FROM KM 26.150 TO 41.161 OF NH- 214(NH216)(KAKINAD	8/2016	1/2017 (12/2021) [12/2021]	350.61 (-) [350.61]	324.60 (0.00) [59]
51	FOUR LANING OF 5.122 KM OF NH9(NEW NH 65) FROM KM 269.900(DESIGN CH.0.0) TO KM 275/622(DESIGN CH 5.12	10/2015	12/2015 (-) [0/0]	333.21 (-) [353.43]	333.09 (20.22) [0]
52	FOUR LANING OF GUNDUGOLANU-DEVARAPALLI- KOVVURU SECTION OF NH-16 FROM KM 15.320 (EXISTING KM 15.700)	3/2018	3/2021 (10/2021) [4/2021]	1,532.62 (-) [2,499.00]	880.34 (966.38) [0]
53	FOUR LANNING OF NH-9 FROM VIJAYWADA- MACHLIPATNAM (KM 0.000 TO 63.800)	1/2016	11/2018 (-) [0/0]	1,134.97 (-) [1,134.97]	0.00 (0.00) [0]
54	REHABILITAITON AND UPGRADATION OF REPALLE TO	1/2017	1/2018	576.48	369.63

	EEPPURPALEM SECTION FROM KM 128/927 TO KM 195/000 OF NH		(4/2022) [4/2022]	(596.38) [576.48]	(0.00) [51]
55	REHABILITATION UPGRADATION OF NH214(NH216) FROM KM41.161 TO KM59.800(GURJANAPALLI TO POLEKURU SECT	1/2016	8/2016 (12/2021) [7/2021]	348.95 (-) [348.95]	225.76 (0.00) [0]
56	REHABILITATION AND UP GRADATION OF NH-544E FROM KM 56/803 TO KM 99/179 OF MADAKASIRA TO SIRA SECTION	3/2020	3/2021 (-) [4/2022]	207.79 (-) [207.79]	0.00 (0.00) [13]
57	REHABILITATION AND UPGRADATION OF DHINDI-DIGAMARRU SECTION FROM KM126/510 TO KM135/740 OF NH214(NH21	1/2016	5/2016 (7/2021) [0/0]	386.09 (316.06) [386.09]	214.31 (0.00) [0]
58	REHABILITATION AND UPGRADATION OF EXISTING NH-167 FROM KM 14.900 TO KM 70.00 (DESIGN CH.14.900 TO 69	11/2016	5/2017 (8/2021) [8/2021]	290.15 (-) [290.15]	136.41 (0.00) [51]
59	REHABILITATION AND UPGRADATION OF EXISTING NH-565 FROM KM.86.057 TO 133.922 OF NAGARJUNASAGAR DAM T	1/2014	11/2014 (-) [0/0]	195.45 (-) [195.45]	0.00 (0.00) [0]
60	REHABILITATION AND UPGRADATION OF GIDDALUR-VINUKONDA SECTION OF NH-544D FROM DESIGN KM 212.983 (EXIS	3/2018	/ (-) [2/2021]	565.09 (-) [565.09]	651.47 (0.00) [0]
61	REHABILITATION AND UPGRADATION OF KARNATKA/AP BORDER-GOOTY SECTION FROM KM 368.920 TO KM 424.225 O	3/2016	5/2016 (9/2021) [9/2021]	995.09 (995.00) [995.09]	560.85 (0.00) [64]
62	REHABILITATION AND UPGRADATION OF LOSARI-MACHAVARAM SECTION FROM KM34/230 TO KM84/550 OF NH214(NH216	3/2016	9/2016 (8/2021) [8/2021]	444.84 (-) [444.84]	345.48 (0.00) [59]
63	REHABILITATION AND UPGRADATION OF MACHILIPATNAM TO AVANIGADDA SECTION FROM KM84/550 - 124/200 OF NH2	11/2016	8/2017 (12/2021) [12/2021]	376.25 (-) [376.25]	310.33 (0.00) [52]
64	REHABILITATION AND UPGRADATION OF NEW NH-544DD FROM DESIGN CHAINAGE KM 56.00 TO 102.20 OF KALYANDURG	3/2018	8/2018 (11/2021) [11/2021]	289.67 (274.73) [289.67]	206.00 (0.00) [39]
65	REHABILITATION AND UPGRADATION OF NEW NH-544E FROM KM. 0.000 TO KM 56.803 OF KODIKONDA - MADAKASIRA	3/2018	11/2018 (7/2021) [0/0]	504.19 (556.13) [504.19]	465.26 (0.00) [0]
66	REHABILITATION AND UPGRADATION OF NH-219 FROM KM 58-600 TO KM 140-750 IN THE STATE OF ANDHRA PRADES	3/2015	10/2015 (6/2021) [0/0]	271.45 (-) [271.45]	243.29 (0.00) [0]
67	REHABILITATION AND UPGRADATION OF NH-340 FROM KM 0/0 TO KM 60/380 (DESIGN CH. 0/000 TO 60/025 EXCLUD	1/2017	8/2017 (12/2021) [12/2021]	319.28 (-) [319.28]	188.42 (0.00) [52]
68	REHABILITATION AND UPGRADATION OF NH219(NEW NH42) FROM KM 244.930 TO 299.775 (MADANAPALLI PUNGANURU	9/2016	2/2017 (7/2021) [0/0]	372.68 (309.37) [372.68]	244.96 (0.00) [0]
69	REHABILITATION AND UPGRADATION OF NH326A FROM KM 0/0 TO 41/979 (EXCLUDING KM 2/255 TO 3/372 AND KM 3	3/2018	8/2018 (12/2021) [12/2021]	228.32 (202.83) [228.32]	135.54 (0.00) [40]
70	REHABILITATION AND UPGRADATION OF NH565 FROM EXISTING KM 361.330(DORNALA T JUNCTION) TO KM 420.800(P	1/2018	8/2018 (8/2021) [8/2021]	418.03 (381.75) [418.03]	323.62 (0.00) [36]
71	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDERS CONFIGURATION OF PADERU-GONDIGUDA SECT	8/2020	3/2021 (-) [3/2023]	222.61 (-) [222.61]	0.00 (0.00) [24]
72	SIX LANING OF ANANDAPURAM PENDURTHI ANAKAPALLI SECTION OF NH-5 NEW NH-16 FROM KM.681.000 EXISTING KM	2/2018	/ (-) [10/2021]	1,959.00 (-) [1,959.00]	1,308.42 (0.00) [-]
73	SIX LANING OF EXISTING 4-LANE ROAD FROM GUNDUGOLANU (DESIGN KM 1023.280) TO KALAPARRU (DESIGN KM 105	9/2018	1/2020 (-) [0/0]	597.67 (-) [597.67]	189.54 (0.00) [0]
74	SIX LANING OF EXISTING 4-LANE ROAD FROM KALAPARRU (DESIGN KM 1050.680) TO CHINNA	9/2018	2/2019 (-)	617.41 (-)	526.54 (0.00)

	AVUTUPALLI (DESIGN		[0/0]	[617.41]	[0]
75	SIX LANING OF NARASANNAPETA – RANASTALAM SECTION OF NH-16 (OLD NH-5) FROM DESIGN KM 580.671 (EXISTIN	12/2017	/ (-) [0/0]	1,323.15 (-) [1,323.15]	0.00 (0.00) [0]
76	SIX LANING OF NH-140 FROM CHITTOR (DESIGN KM 0.000/EXISTING KM 158.000 OF NH-4) TO MALLAVARAM (DESIG	3/2018	/ (-) [9/2021]	1,550.98 (-) [1,550.98]	1,620.21 (0.00) [-]
77	SIX LANNING OF NELLORE-CHILKALURIPET KM.1182.802 TO KM.1366.547	11/2011	5/2014 (-) [0/0]	1,535.00 (-) [1,535.00]	3,279.25 (0.00) [0]
78	SIX LANNING OF RANASTALAM-ANANDAPURAM SECTION OF NH-16 FROM KM 634.000 TO KM 681.000	3/2017	3/2020 (-) [0/0]	1,041.62 (-) [1,187.10]	962.95 (145.48) [0]
79	TIRUPATI - TIRUTHANI - CHENNAI	4/2011	10/2013 (-) [0/0]	571.00 (-) [571.00]	582.53 (0.00) [0]
80	VIJAYAWADA-GUNDUGOLANU SECTION	9/2014	2/2017 (-) [0/0]	1,684.00 (-) [1,684.00]	0.00 (0.00) [0]
81	WIDENING AND STRENGTHENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 491/000 TO KM 525/200 OF RAIPUR	6/2020	5/2021 (-) [12/2022]	221.40 (-) [221.40]	0.00 (0.00) [19]
	<u>Steel</u>				
82	COKE OVEN BATTERY-5	12/2011	12/2017 (7/2022) [7/2022]	2,858.00 (-) [2,858.00]	1,995.82 (0.00) [55]
	<u>Water Resources</u>				
83	POLAVARAM IRRIGATION PROJECT	2/2009	3/2020 (11/2021) [4/2022]	10,151.04 (55,548.87) [55,548.87]	17,935.78 (45,397.83) [25]
	<u>ARUNACHAL PRADESH</u>				
	<u>Power</u>				
84	SUBANSIRI LOWER H.E.R (8X250 MW) (NHPC)	9/2003	9/2010 (8/2023) [8/2023]	6,285.33 (19,992.43) [19,992.43]	14,059.55 (13,707.10) [155]
	<u>Road Transport And Highways</u>				
85	2 LANING FROM KM. 40.00 TO KM. 58.27 OF CHANGLANG/ TIRAP DISTRICT BOUNDARY TO CHANGLANG OF NH-52B IN	3/2015	/ (-) [3/2021]	172.75 (-) [172.75]	134.38 (0.00) [0]
86	2 LANING FROM LONGDING TO KANUBARI OF NH-52B FROM KM 0 TO KM 47.213 IN ARUNACHAL PRADESH	3/2015	6/2018 (-) [3/2021]	394.00 (522.86) [522.86]	410.63 (128.86) [0]
87	2-LANING OF EXISTING AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM DESIGN KM. 12.000 TO KM. 33.000 (EX	10/2015	/ (-) [10/2021]	210.50 (-) [210.50]	145.07 (0.00) [-]
88	4 LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 40+430 TO KM 51+735 (PACKAGE B) ON EPC	6/2020	8/2021 (-) [8/2021]	496.47 (-) [496.47]	0.00 (0.00) [0]
89	4 LANING OF NH 415 FROM DESIGN CHAINAGE 29/500 TO 40/400 (ITANAGAR TO BANDARDEWA SECTION) IN THE ST	11/2016	/ (-) [9/2020]	243.89 (-) [243.89]	210.90 (0.00) [0]
90	4-LANING OF ITANAGAR TO BANDARDEWA SECTION OF NH-415 FROM KM 51+700 TO KM 59+199 (PACKAGE-C) ON EPC	6/2020	8/2021 (-) [8/2021]	437.60 (-) [437.60]	0.00 (0.00) [0]
91	BALANCE WORK 2-LANING OF LALPUL MANMAO CHANGLANG ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNACH	2/2021	3/2024 (-) [3/2024]	588.09 (-) [588.09]	0.00 (0.00) [0]
92	BALANCE WORK OF 2-LANING OF LONGDING– TISSA-KHONSA ROAD (NH-215) ON EPC MODE IN THE STATE OF ARUNAC	1/2020	2/2024 (-) [2/2024]	358.26 (-) [358.26]	0.00 (0.00) [0]
93	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN	3/2019	2/2020	403.68	63.69

	SECTION OF NH 13 FROM KM 0.00 TO KM 44.35 (PACKAGE 1)		(-) [0/0]	(-) [403.68]	(0.00) [0]
94	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 117.56 TO KM 163.59 (PACKAGE	3/2019	11/2020 (-) [0/0]	543.05 (-) [543.05]	119.81 (0.00) [0]
95	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 163.59 TO KM 206.66 (PACKAGE	3/2019	11/2020 (-) [0/0]	450.65 (-) [450.65]	37.16 (0.00) [0]
96	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 206.66 TO KM 247.05 (PACKAGE	3/2019	10/2020 (-) [0/0]	486.70 (-) [486.70]	75.26 (0.00) [0]
97	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 247.05 TO KM 284.92 (PACKAGE	3/2019	2/2020 (-) [0/0]	560.39 (-) [560.39]	148.75 (0.00) [0]
98	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 284.92 TO KM 314.25 (PACKAGE	3/2019	9/2020 (-) [0/0]	347.78 (-) [347.78]	93.70 (0.00) [0]
99	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 314.25 TO KM 351.383 (PACKAG	3/2019	10/2020 (-) [0/0]	394.27 (-) [394.27]	15.49 (0.00) [0]
100	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 44.35 TO KM 77.95 (PACKAGE 2	3/2019	2/2020 (-) [0/0]	342.55 (-) [342.55]	144.45 (0.00) [0]
101	CONSTRUCTION OF 2 LANE ROAD OF POTIN TO PANGIN SECTION OF NH 13 FROM KM 77.95 TO KM 117.56 (PACKAGE	3/2019	11/2020 (-) [0/0]	421.48 (-) [421.48]	50.14 (0.00) [0]
102	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 106.200 TO KM 120.	12/2016	/ (8/2021) [12/2021]	200.44 (-) [200.44]	125.91 (0.00) [-]
103	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 53.500 TO KM 92.50	9/2016	(11/2021) [3/2022]	568.92 (-) [568.92]	310.07 (0.00) [-]
104	CONSTRUCTION OF 2 LANING OF EXISTING HUNLI-ANINI ROAD ON EPC BASIS FROM DESIGN KM 92.500 TO KM 106.5	12/2016	/ (3/2021) [3/2022]	188.78 (-) [188.78]	104.07 (0.00) [-]
105	CONSTRUCTION OF 2-LANE ROAD FROM EXISTING KM 21.500 OF HUNLI-ANINI ROAD(NEAR ITHUN BRIDGE) TO KM 37	4/2016	/ (1/2021) [12/2021]	245.79 (-) [245.79]	204.42 (0.00) [-]
106	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDERS FROM KM16.00 OF ROING-HUNLI SECTION TO KM 21.500 OF	3/2017	/ (6/2022) [3/2022]	1,718.59 (-) [1,718.59]	519.92 (0.00) [-]
107	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF ARROWA-KHUPA-HAYULIANG SECTION OF NH-113 FROM CH.68.	8/2020	4/2022 (-) [4/2022]	301.06 (-) [301.06]	23.41 (0.00) [0]
108	CONSTRUCTION OF 2-LANING WITH HARD SHOULDERS OF DEMWE-BRAHMAKUND SECTION OF NH-13 FROM CH.0.00 KM TO	9/2020	5/2022 (-) [5/2022]	353.90 (-) [353.90]	18.03 (0.00) [0]
109	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDERS OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM EXI	2/2017	4/2017 (-) [8/2020]	167.28 (-) [167.28]	22.06 (0.00) [0]
110	DEMBUEN - BRUNI	12/2020	3/2023 (-) [3/2023]	606.63 (-) [606.63]	0.00 (0.00) [0]
111	DOGINALA - GAU	12/2020	9/2022 (-) [9/2022]	242.30 (-) [242.30]	0.00 (0.00) [0]
112	FOUR LANE CONNECTIVITY TO VISAKHAPATNAM PORT ROAD FROM KM. 0.000 TO KM.12.700 (DESIGN LENGTH=12.70 K	3/2018	/ (0/0) [0/0]	392.60 (-) [392.60]	0.00 (0.00) [0]
113	LADDA - BASAI	2/2021	4/2023 (-)	445.96 (-)	0.00 (0.00)

			[4/2023]	[445.96]	[0]
114	TADADEGE - HENKAR	2/2021	3/2023 (-) [3/2023]	550.45 (-) [550.45]	13.03 (0.00) [0]
115	TWO LANING OF AKAJAN LIKABALI BAME ROAD ON EPC BASIS FROM EXISTING KM 71.000 TO KM 99.000 (DESIGN KM	3/2017	4/2017 (3/2021) [3/2022]	284.09 (284.09) [284.09]	157.65 (0.00) [59]
116	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 17.000 (KHUPA) TO KM. 34.00	2/2017	4/2017 (-) [3/2022]	195.23 (-) [252.79]	133.92 (57.56) [59]
117	TWO LANING OF EXISTING HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 34.000 TO KM. 51.825 [EXIST	2/2017	4/2017 (-) [3/2022]	203.36 (-) [263.31]	145.13 (59.95) [59]
118	TWO LANING OF EXISTING KHUPA HAYULIANG HAWAI ROAD ON EPC BASIS FROM DESIGN KM. 0.000 (KHUPA) TO KM.	1/2017	4/2017 (-) [3/2022]	198.22 (-) [252.05]	144.26 (53.83) [59]
119	TWO LANING OF JORAM KOLORIANG ROAD (NH 713) ON EPC BASIS FROM DESIGN KM. 138+000 TO KM. 154+036 [EX	2/2017	4/2017 (-) [2/2021]	180.57 (-) [180.57]	60.86 (0.00) [0]
120	TWO-LANING OF HAYULIANG- HAWAI BYPASS ROAD ON EPC BASIS FROM DESIGN KM. 51.825 TO KM. 63.131 EXISTI	1/2017	/ (-) [3/2021]	256.66 (-) [256.66]	16.42 (0.00) [0]
121	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 20+000 TO KM. 32+050 [EXISTING KM 20.0	2/2017	/ (4/2022) [4/2022]	175.06 (-) [175.06]	87.32 (0.00) [-]
122	TWO-LANING OF JORAM - KOLORIANG ROAD (NH-713) FROM DESIGN KM. 32+050 TO KM. 44+000 [EXISTING KM 35.1	2/2017	/ (4/2022) [4/2022]	176.12 (-) [176.12]	73.92 (0.00) [-]
123	WIDENING OF EXISTING ROAD TO 2 LANE NH STANDARDS ALONG WITH IMPROVEMENT AND REALIGNMENT FROM NECHIPU	9/2011	/ (3/2020) [0/0]	1,979.00 (-) [2,036.90]	1,242.64 (57.90) [0]
124	WIDENING OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM HUKANJURI TO KHONSA SECTION OF NH-315A	3/2021	9/2021 (-) [9/2021]	182.55 (-) [182.55]	0.00 (0.00) [0]
	ASSAM				
	Civil Aviation				
125	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING AT LGBI AIRPORT GUWAHATI	12/2016	3/2021 (3/2022) [3/2023]	1,142.00 (-) [1,232.00]	371.33 (90.00) [24]
	Health And Family Welfare				
126	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GUWAHATI, ASSAM	5/2017	5/2021 (9/2022) [9/2022]	875.00 (-) [747.80]	387.54 (-127.20) [16]
127	LGBRIMH-TEZPUR, ASSAM	7/2012	12/2014 (-) [3/2018]	175.57 (-) [175.57]	163.37 (0.00) [0]
	Petroleum				
128	BS VI PROJECT AT GUWAHATI REFINERY	8/2018	2/2020 (6/2021) [9/2021]	557.00 (-) [557.00]	537.30 (0.00) [19]
129	CONSTRUCTION OF 762 MM DIAMETER GAS PIPELINE FROM BAGHJAN TO CGGS, MADHUBAN	6/2016	8/2020 (9/2021) [9/2021]	224.75 (222.21) [198.00]	178.00 (-26.75) [13]
130	DEVELOPMENT OF FACILITIES AT MOINARBAND (SILCHAR) , CACHAR , ASSAM AS RESITEMENT OF RAMNAGAR DEPOT	6/2016	8/2019 (6/2021) [5/2021]	423.00 (-) [502.00]	440.03 (79.00) [0]
131	DEVELOPMENT OF SURFACE FACILITIES FOR PRODUCTION AND EVACUATION OF CRUDE OIL AND NATURAL GAS FROM NA	1/2018	2/2020 (-) [12/2021]	543.91 (652.10) [638.60]	383.44 (94.69) [22]
132	NUMALIGARH REFINERY EXPANSION PROJECT 6 MMTPA REFINARY	1/2019	10/2024 (-)	12,366.00 (-)	567.38 (0.00)

			[10/2024]	[12,366.00]	[0]
133	NUMALIGARH REFINERY EXPANSION PROJECT COIT AND PIPELINES	1/2019	10/2024 (-) [10/2024]	10,228.00 (-) [10,228.00]	285.27 (0.00) [0]
134	PIPELINE NETWORK PROJECT GELEKI, ASSAM	7/2016	5/2020 (8/2021) [11/2021]	249.85 (303.75) [303.75]	205.92 (53.90) [18]
	<u>Railways</u>				
135	AMBARI FALAKATA TO NEW MAYNAGURI	4/2011	3/2019 (-) [6/2021]	314.00 (486.96) [800.00]	832.55 (486.00) [0]
136	BONGAIGAON-GOALPARA-GUWAHATI (176 KM)	4/2015	3/2022 (-) [3/2023]	2,232.32 (-) [2,950.00]	1,758.52 (717.68) [12]
137	DIGARU-HOJAI (102 KM)	4/2015	3/2021 (-) [3/2022]	870.96 (-) [1,873.21]	1,397.73 (1,002.25) [12]
138	NEW B.G. LINE FROM TETELIA TO BYRNIHAT (NATIONAL PROJECT), NEFR	9/2006	3/2019 (-) [3/2023]	385.20 (-) [1,105.00]	858.45 (719.80) [48]
	<u>Road Transport And Highways</u>				
139	2 LANING FROM KANUBARI TO START OF BOGIBEEL BRIDGE APPROACHES OF NH-52B(EXTN) IN ASSAM	11/2010	5/2017 (5/2022) [5/2022]	268.08 (-) [390.73]	318.85 (122.65) [60]
140	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-I)	3/2020	6/2022 (-) [6/2022]	261.13 (-) [261.13]	23.56 (0.00) [0]
141	2-LANING FROM YAINGANGPOKPI TO FINCH CORNER (PKG-II)	3/2020	6/2022 (-) [6/2022]	217.50 (-) [217.50]	34.17 (0.00) [0]
142	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- IB)	3/2020	3/2022 (-) [3/2022]	216.49 (-) [216.49]	26.88 (0.00) [0]
143	4 LANING FROM JAMUGURI TO BISWANATH CHARIALI FROM KM 182 TO KM 208 OF NH-52	1/1991	/ (-) [12/2021]	520.01 (-) [520.01]	189.59 (0.00) [-]
144	4 LANING FROM KALIABOR TINALI TO DOLABARI SECTION FROM KM 0.0 TO KM 17.3 OF NH 37A INCL. ADDITIONAL	10/2014	11/2018 (-) [2/2022]	588.95 (-) [588.95]	494.25 (0.00) [39]
145	4 LANING FROM RANGAGARA TO KALIABHOR TINALI FROM KM 297.00 TO KM 315.315 OF NH-37 ON EPC BASIS.	12/2015	12/2018 (-) [12/2021]	289.99 (-) [289.99]	87.90 (0.00) [36]
146	4 LANING OF NH 37 SECTION BETWEEN END OF MORAN BYPASS TO BOGIBEEL JUNCTION NEAR LAPETKETA (KM. 561	1/2016	1/2016 (-) [3/2022]	252.00 (-) [252.00]	136.88 (0.00) [74]
147	4 LANING OF JORHAT TO JHANJI SECTION FROM KM. 453.00 TO KM. 491.08 (DESIGN KM 403.200 TO KM 454.240)	6/2015	6/2018 (-) [12/2021]	437.39 (-) [437.39]	105.09 (0.00) [42]
148	4 LANING OF NH-37 SECTION BETWEEN DEMOW TO END OF MORAN BYPASS (FROM KM. 534.800 TO KM. 561.700) O	1/2016	1/2016 (-) [3/2022]	294.17 (-) [294.17]	215.45 (0.00) [74]
149	4-L DHUBRI PHULBARI BRIDGE WITH APPROACH ROAD	11/2020	9/2028 (-) [9/2028]	4,997.04 (-) [4,997.04]	10.45 (0.00) [0]
150	4-LANING OF HAPACHARA - TULUNGIA SECTION	3/2020	12/2022 (-) [12/2022]	220.20 (-) [220.20]	28.18 (0.00) [0]
151	BALANCE WORK FOR "IMPROVEMENT OF EXISTING SINGLE INTERMEDIATE LANE ROAD OF NH-44 TO BE 2-LANE ROAD W	3/2020	12/2020 (12/2022) [12/2022]	166.94 (-) [166.94]	28.02 (0.00) [24]
152	BRAHMPUTRA BRIDGE,NH NO-31	12/2003	4/2010	217.61	489.84

			(-) [7/2019]	(-) [360.84]	(143.23) [0]
153	DABOKA KATHKATI PACKAGE-2	3/2021	1/2024 (-) [1/2024]	335.88 (-) [335.88]	0.00 (0.00) [0]
154	DABOKA KATHKATI PACKAGE-4	2/2021	12/2023 (-) [12/2023]	260.07 (-) [260.07]	0.00 (0.00) [0]
155	DABOKA KATHKATI PACKAGE-5	3/2021	1/2023 (-) [1/2023]	288.85 (-) [288.85]	0.00 (0.00) [0]
156	DHARAMTUL TO SONAPUR, KM 205-183 (AS-20)	12/2003	5/2008 (-) [6/2019]	160.00 (-) [167.98]	270.97 (7.98) [0]
157	FOUR LANING FROM GOHPUR TO HOLONGI SECTION FROM KM 264.10 OF NH 52 TO KM 20.37 OF NH 52A	3/2015	11/2018 (-) [11/2021]	168.39 (-) [168.39]	145.72 (0.00) [36]
158	FOUR LANING OF BALACHERA-HARANGAJAO SECTION OF NH-54 (EXT) FROM KM 275.00 TO KM 244.000 IN THE STATE	10/2017	/ (-) [3/2023]	818.00 (-) [818.00]	287.52 (0.00) [-]
159	FOUR LANING OF JHANJHI JN TO DEMOW SECTION FROM KM. 491.050 TO KM. 535.250 (DESIGN KM 490.800 TO KM 5	6/2015	6/2018 (-) [12/2021]	463.49 (-) [463.49]	159.34 (0.00) [42]
160	FOUR LANING OF NH-52 FROM END OF BISWANATH CHARIALI BY-PASS (KM 208.00) TO GOHPUR (KM 265.50) (TOTAL	3/2015	1/2016 (-) [3/2022]	829.00 (-) [829.00]	415.82 (0.00) [74]
161	FOUR LANING OF NUMALIGARH TO JORHAT SECTION FROM KM. 402.500 TO KM. 453.000 (DESIGN KM 403.200 TO KM	5/2015	5/2018 (-) [3/2022]	454.89 (-) [454.89]	328.55 (0.00) [46]
162	HARANGAJO TO MAIBANG (AS-23), KM.126.450 TO KM.140.700	12/2003	2/2009 (-) [0/0]	280.00 (-) [612.58]	612.58 (332.58) [0]
163	HARANGAJO TO MAIBANG, NH-54	12/2003	7/2009 (-) [0/0]	196.00 (-) [655.17]	655.17 (459.17) [0]
164	JIA BHARALI BRIDGE ALONG WITH ITS APPROACH ROAD	12/2020	8/2023 (-) [8/2023]	804.00 (-) [804.00]	3.23 (0.00) [0]
165	MAIBANG TO LUMDING (AS-24), KM.111.000 TO KM.126.450	12/2003	11/2008 (-) [0/0]	155.04 (-) [255.23]	0.00 (100.19) [0]
166	MAIBANG TO LUMDING (AS-25), KM.83.400 TO KM.111.000	12/2003	4/2009 (-) [0/0]	199.81 (-) [340.14]	0.00 (140.33) [0]
167	MAIBANG TO LUMDING (AS-26), KM.60.500 TO KM.83.400, NH-54	12/2003	11/2008 (-) [0/0]	167.64 (-) [435.78]	0.00 (268.14) [0]
168	NALBARI T BIJNI (AS-7)	12/2003	4/2008 (-) [2/2021]	208.00 (-) [230.00]	370.56 (22.00) [0]
169	NALBARI TO BIJNI (AS-6)	12/2003	6/2008 (-) [9/2019]	225.00 (-) [225.00]	390.72 (0.00) [0]
170	OUR LANNING OF DOLABARI TO JAMUGURI SECTION FROM KM 17.300 OF NH 37A TO KM 182.00 OF NH52 IN THE ST	3/2017	/ (-) [12/2021]	1,049.51 (-) [1,049.51]	143.02 (0.00) [-]
171	SONAPUR TO GUWAHTI (AS-3)	12/2003	3/2008 (-) [8/2020]	245.00 (-) [174.34]	240.36 (-70.66) [0]
172	STRENGTHENING WITH PAVED SHOULDER FROM KM 30/0 TO KM 46/0, KM 54/0 TO KM 61/0, KM 69/0 TO KM 80/0	9/2018	9/2021 (-)	160.00 (-)	116.26 (0.00)

	AN		[9/2021]	[160.00]	[0]
173	TULUNGIA-JOGIGHOPA-PAIKAN PKG-5	3/2021	12/2022 (-) [12/2022]	636.42 (-) [636.42]	0.00 (0.00) [0]
174	TULUNGIA-JOGIGHOPA-PAIKAN ROAD PKG-7	3/2021	1/2024 (-) [1/2024]	286.72 (-) [286.72]	0.00 (0.00) [0]
175	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 330 TO KM 350	9/2019	5/2023 (-) [5/2023]	761.54 (-) [761.54]	86.48 (0.00) [0]
176	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM CH.75.330KM TO CH.88.00KM (DESIGN CH.71.800	8/2020	4/2022 (-) [4/2022]	208.84 (-) [208.84]	24.01 (0.00) [0]
177	WIDENING/IMPROVEMENT TO 4-LANE WITH PAVED SHOULDER FROM KM 66.00 TO KM 81.00 (DESIGN CHAINAGE 65.923	8/2020	3/2022 (-) [3/2022]	278.46 (-) [278.46]	27.76 (0.00) [0]
	<u>BIHAR</u>				
	<u>Civil Aviation</u>				
178	CONSTRUCTION OF NEW DORNESTIC TERMINAL BUILDING AND OTHER STRUCTURES, PHASE I AND II	5/2018	10/2022 (-) [12/2023]	1,216.90 (-) [1,216.90]	211.80 (0.00) [14]
	<u>Department Of Higher Education</u>				
179	CONSTRUCTION OF ACADEMIC AND RESIDENTIAL COMPLEX UNDER PHASE-II FOR THE CAMPUS OF IIT PATNA	2/2016	6/2017 (-) [3/2022]	496.18 (496.00) [498.99]	288.03 (2.81) [57]
180	PERMANENT CAMPUS FOR IIM BODH GAYA	9/2018	9/2020 (-) [11/2022]	375.00 (-) [375.00]	48.46 (0.00) [26]
	<u>Petroleum</u>				
181	BARAUNI REFINERY CAPACITY EXPANSION FROM 6.0 TO 9.0 MMTPA	1/2020	4/2023 (-) [4/2023]	14,810.00 (-) [14,810.00]	1,303.20 (0.00) [0]
182	CGD PROJECT AT ARARIA, PURNIA, KATIHAR AND KISHANGANJ DISTRICTS	6/2019	12/2029 (-) [12/2029]	988.00 (-) [988.00]	0.00 (0.00) [0]
183	CGD PROJECT AT ARWAL, JEHANABAD, BHOJPUR AND BUXAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	439.00 (-) [439.00]	0.00 (0.00) [0]
184	CGD PROJECT AT AURANGABAD, KAIMUR AND ROHTAS DISTRICTS	10/2018	8/2027 (-) [8/2027]	176.00 (-) [176.00]	0.00 (0.00) [0]
185	CGD PROJECT AT KHAGARIA, SAHARSA AND MADHEPURA	6/2019	12/2029 (-) [12/2029]	163.00 (-) [163.00]	0.00 (0.00) [0]
186	CGD PROJECT AT LAKHISARAI, MUNGER AND BHAGALPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	347.00 (-) [347.00]	0.00 (0.00) [0]
187	CGD PROJECT AT MUZAFFARPUR, VAISHALI, SARAN AND SAMASTIPUR DISTRICTS	6/2019	2/2028 (-) [2/2028]	2,996.00 (-) [2,996.00]	0.00 (0.00) [0]
188	CITY GAS DISTRIBUTION (CGD) NETWORK PATNA	10/2017	10/2022 (-) [10/2022]	359.25 (-) [359.25]	165.40 (0.00) [0]
189	CONSTRUCTION OF GRASS ROOT POL TERMINAL AT MOTIHARI, BIHAR	4/2018	3/2021 (12/2021) [12/2021]	522.00 (-) [522.00]	373.16 (0.00) [9]
190	DEVLEOPMENT OF GRID INFRASTRUCTURE FOR IMPORTING GRID POWER AT 220 KV AT BARAUNI REFINERY	12/2017	10/2020 (8/2022) [8/2022]	199.36 (-) [199.36]	48.78 (0.00) [22]
191	INSTALLATION OF 'INDJET' UNIT AT BARAUNI REFINERY	7/2018	1/2021 (6/2021)	189.00 (-)	166.08 (0.00)

			[11/2021]	[189.00]	[10]
192	LPG BP PROJECT MOTIHARI	5/2018	3/2021 (9/2021) [9/2021]	206.50 (-) [206.50]	147.35 (0.00) [6]
193	MUZAFFARPUR-MOTIHARI LPG PIPELINE	6/2020	8/2022 (-) [8/2022]	403.00 (-) [403.00]	89.57 (0.00) [0]
	<u>Power</u>				
194	BARH STPP(3X660MW) NTPC	2/2005	10/2011 (7/2023) [7/2023]	8,692.97 (21,312.11) [21,312.11]	19,169.37 (12,619.14) [141]
195	BRBCL-NABINAGAR TPP- JV (4X250 MW)	1/2007	7/2012 (6/2020) [10/2021]	5,353.00 (10,566.00) [10,566.00]	8,917.95 (5,213.00) [111]
196	BUXAR THERMAL POWER PLANT (1320 MW)	3/2019	1/2024 (-) [1/2024]	10,439.09 (10,439.09) [10,439.09]	2,725.87 (0.00) [0]
197	NPGCPL-NABINAGAR STPP - JV (3X660 MW)	1/2013	5/2018 (-) [2/2022]	12,964.60 (17,304.00) [17,304.00]	16,096.71 (4,339.40) [45]
	<u>Railways</u>				
198	ARA-BHABHUA ROAD (NL)	4/2008	/ (-) [0/0]	633.87 (-) [633.87]	0.40 (0.00) [0]
199	ARARIA-SUPAUL (NL)	4/2008	/ (3/2023) [3/2023]	1,605.17 (-) [1,605.17]	61.37 (0.00) [-]
200	BIHTA-AURANGABAD (NL)	4/2008	/ (-) [3/2024]	326.20 (-) [2,995.01]	2.04 (2,668.81) [-]
201	CHHAPRA-MUZAFFARPUR (NL)	4/2006	/ (-) [3/2023]	378.56 (-) [1,858.75]	386.36 (1,480.19) [-]
202	DANIAWAN-BIHARSARIF (NL), ECR	4/2001	/ (-) [0/0]	406.92 (-) [339.00]	200.00 (-67.92) [0]
203	DARBANGHA-KUSHESHWARSTHAN (NL)	4/2005	/ (-) [0/0]	205.00 (-) [205.00]	5.21 (0.00) [0]
204	FATUHA-ISLAMPUR INCL. MM FOR EXTENSION OF NEW LINE FORM BIHARSHARIF-BARBIGHA, DANIIAWAN-BIHARSHARIF,	4/1991	/ (3/2022) [3/2022]	329.39 (-) [1,483.14]	1,219.42 (1,153.75) [-]
205	GAYA-DALTONGANJ VIA RAFIGANJ (NL)	4/2008	/ (-) [0/0]	445.25 (-) [445.25]	1.15 (0.00) [0]
206	HAJIPUR-RAMDAYALUNAGAR DOUBLING	4/2013	/ (10/2019) [10/2019]	213.01 (-) [495.00]	497.30 (281.99) [0]
207	HAJIPUR-SUGAULI VIA VAISHALI (NL), ECR	4/2003	/ (3/2023) [3/2023]	528.65 (2,066.78) [2,066.78]	1,581.82 (1,538.13) [-]
208	JAYANAGAR-DARBHANGA-NARKATIA GANJ(GC),ECR	4/1997	3/2012 (11/2022) [11/2022]	324.73 (898.53) [1,070.00]	1,076.60 (745.27) [128]
209	JAYNAGAR-BIJALPURA INCLUDING EXTENSION BIJALPURA-BARDIBAS(NEPAL) GC	4/2009	3/2020 (3/2023) [3/2023]	548.00 (-) [819.01]	538.55 (271.01) [36]
210	KHAGARIA-KUSHESHWAR ASTHAN (NL) (ECR)	4/1997	/ (-) [12/2023]	162.87 (614.45) [614.45]	352.16 (451.58) [-]
211	KISHANGANJ JALALGARH, NL, NEFR	4/2008	/	333.76	6.74

			(-) [0/0]	(-) [360.00]	(26.24) [0]
212	KIUL - GAYA DOUBLING PROJECT	12/2015	3/2020 (-) [3/2023]	1,200.20 (1,200.20) [1,200.20]	970.88 (0.00) [36]
213	KOSI BRIDGE (NL), ECR	4/2002	3/2020 (-) [0/0]	499.41 (516.02) [516.02]	458.36 (16.61) [0]
214	KURSELA-BIHARIGANJ (NL)	4/2008	/ (-) [0/0]	192.56 (-) [192.56]	0.39 (0.00) [0]
215	MANSI-PURNIA (EXTENSION OF MANSI-SAHARSA) GAN ECR	4/1996	3/2012 (9/2021) [9/2021]	477.88 (751.55) [751.55]	714.87 (273.67) [114]
216	MOTIHARI-SITAMARHI (NL)	4/2006	/ (-) [0/0]	211.00 (-) [1,006.00]	24.16 (795.00) [0]
217	MUZAFFARPUR SAGAULI DOUBLING 100.60 KM	4/2016	3/2021 (3/2024) [3/2024]	731.64 (-) [1,185.73]	269.99 (454.09) [36]
218	MUZAFFARPUR-DARBANGHA (NL)	4/2008	/ (-) [0/0]	281.30 (-) [281.30]	0.60 (0.00) [0]
219	MUZAFFARPUR-KATRA-ORAI-JANAKPUR ROAD (NL)	4/2008	/ (-) [3/2024]	228.05 (-) [228.05]	1.53 (0.00) [-]
220	MUZAFFARPUR-SITAMARHI NEW LINE	1/1991	7/2014 (-) [0/0]	332.15 (-) [546.71]	547.77 (214.56) [0]
221	NAWADA-LAXMIPUR (NL)	4/2008	/ (-) [0/0]	620.57 (-) [620.57]	0.31 (0.00) [0]
222	NEW B.G. LINE FROM ARARIA TO GALGALIA (THAKURGUNG), NEFR	9/2006	3/2019 (-) [3/2024]	532.87 (2,132.03) [2,145.00]	1,014.54 (1,612.13) [60]
223	RAJGIR HISUA TILAIYA (46KM) INCL. MM NATESHWAR ISLAMPUR	4/1998	/ (8/2020) [8/2020]	180.82 (-) [726.31]	546.29 (545.49) [0]
224	RAMPUR DUMRA - TAL - RAJENDRAPUL DOUBLING INCLUDING GANGA BRIDGE	12/2015	3/2020 (3/2023) [3/2023]	1,491.47 (-) [1,491.47]	543.60 (0.00) [36]
225	SAGAULI VALMIKINAGAR DOUBLING 109.7 KM	4/2016	3/2021 (3/2024) [3/2024]	744.04 (-) [1,215.54]	488.59 (471.50) [36]
226	SAKRI-HASANPUR ROAD (NL)	4/1999	/ (-) [3/2021]	325.00 (735.20) [735.20]	388.33 (410.20) [0]
227	SAKRI-NIRMALI AND JHANJHARPUR-LAUKAHABAZAR AND SAHARSA-FORBESGANJ (GC)	4/2004	/ (-) [3/2023]	372.14 (1,470.50) [1,470.50]	1,377.83 (1,098.36) [-]
228	SAMASTIPUR-DARBANGHA	5/2015	/ (-) [3/2025]	380.00 (-) [519.33]	294.63 (139.33) [-]
229	SITAMARHI-JAYNAGAR-NIRMALI VIA SURSAND (NL)	4/2008	/ (-) [0/0]	678.62 (-) [678.62]	17.20 (0.00) [0]
<u>Road Transport And Highways</u>					
230	2 LANNING OF MUZAFFARPUR - SONBARSA	5/2011	11/2013 (-) [0/0]	511.54 (-) [591.00]	578.00 (79.46) [0]
231	2-LANNING WITH PS MOTIHARI-RAXAUL	10/2011	4/2014	375.09	494.33

			(-) [0/0]	(-) [375.09]	(0.00) [0]
232	4-LANNING OF CHAPRA-HAJIPUR	1/2011	7/2013 (12/2021) [0/0]	575.00 (-) [575.00]	501.83 (0.00) [0]
233	BALANCE WORK OF 4 LANING OF GORAKPUR - GOPALGANJ	5/2015	5/2017 (-) [0/0]	581.84 (-) [581.84]	0.00 (0.00) [0]
234	BALANCE WORK OF 4- L ANING OF PATNA-GAYA-DOBHI SECTION (KM.83.00 TO KM. 127.217) OF NH-83 IN THE STA	10/2013	11/2020 (-) [0/0]	464.09 (-) [464.09]	0.00 (0.00) [0]
235	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 0.00 TO KM. 127.217) OF NH-83 IN THE STAT	10/2013	12/2020 (-) [0/0]	649.90 (-) [649.90]	44.00 (0.00) [0]
236	BALANCE WORK OF 4- LANING OF PATNA-GAYA-DOBHI SECTION (KM. 39.00 TO KM. 83.00) OF NH-83 IN THE STATE	10/2013	11/2020 (-) [0/0]	446.97 (-) [446.97]	0.00 (0.00) [0]
237	CONSTRUCTION OF 2 LANE BRIDGE ACROSS RIVER KOSI WITH APPROACH ROAD FROM BHEJA TO BAKAUR SECTION OF N	10/2019	2/2020 (-) [0/0]	1,101.99 (-) [1,101.99]	181.13 (0.00) [0]
238	CONSTRUCTION OF A NEW 4 LANE BRIDGE PARALLEL TO EXISTING MG SETU WITH ITS APPROACHES FROM KM 0.00	2/2019	/ (-) [0/0]	2,926.42 (-) [2,926.42]	211.88 (0.00) [0]
239	CONSTRUCTION OF A NEW 4 LANE MAJOR BRIDGE ACROSS RIVER KOSI AT PHULAUT INCLUDING RHABILITATION AND	9/2018	/ (-) [0/0]	1,478.40 (-) [1,478.40]	27.02 (0.00) [0]
240	CONSTRUCTION OF NEW LINK (NH-133B) FROM KM 0/00 (KM 200/87 OF SAHIBANJ BYPASS) IN JHARKHAND TO KM 15	12/2017	/ (1/2021) [0/0]	2,598.00 (1,962.50) [1,962.50]	235.00 (-635.50) [0]
241	CONSTRUCTION OF ROAD APPROACHES TO RAIL-CUM-ROAD BRIDGE ACROSS RIVER GANGA AT MUNGER GHAT NEAR MUNGE	3/2017	3/2020 (-) [5/2021]	235.48 (-) [227.77]	11.00 (-7.71) [0]
242	DEVELOPMENT OF NEWLY DECLARED NH-527C FROM MAJHAULI TO CHAROUT SECTION TO 2 LANE WITH PAVED SHOULDER	3/2018	/ (-) [0/0]	496.20 (-) [537.17]	58.32 (40.97) [0]
243	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	11/2013	7/2016 (-) [0/0]	683.83 (683.82) [560.70]	691.29 (-123.13) [0]
244	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	553.30 (-) [478.35]	524.35 (-74.95) [0]
245	ENGINEERING, PROCUREMENT, AND CONSTRUCTION OF REHABILITATION AND UPGRADING TO 2-LANES/2 - LANE WITH P	2/2016	5/2016 (-) [0/0]	178.85 (-) [152.62]	139.92 (-26.23) [0]
246	FOUR LANING OF BAKHTIYARPUR - MOKAMA SECTION OF NH-31	12/2015	/ (-) [0/0]	1,167.45 (-) [1,182.94]	267.10 (15.49) [0]
247	FOUR LANING OF BHOJPUR TO BUXAR	1/1991	/ (-) [0/0]	642.41 (-) [681.67]	489.12 (39.26) [0]
248	FOUR LANING OF FORBESGANJ - JOGBANI	8/2015	4/2018 (-) [0/0]	322.09 (247.00) [322.09]	0.00 (0.00) [0]
249	FOUR LANING OF GAYA-HISUA-RAJGIRI-NALANDA-BIHARSHARIF SECTION (KM0.00 TO 92.935) ON NH-82 IN BIHAR	1/2014	10/2016 (-) [0/0]	1,408.85 (2,138.16) [925.87]	1,177.56 (-482.98) [0]
250	FOUR LANING OF KOILWAR TO BHOJPUR	8/2015	/ (-) [10/2021]	814.04 (-) [825.17]	764.04 (11.13) [-]
251	FOUR LANING OF PATNA TO KOILWAR	8/2015	/ (-)	556.07 (-)	0.00 (0.00)

			[0/0]	[556.07]	[0]
252	FOUR OF SIMARIA - KHAGARIA SECTION OF NH-31	12/2015	4/2019 (-) [0/0]	1,041.10 (-) [1,041.10]	377.35 (0.00) [0]
253	PATNA-BAKTZARPUR KM.181.3 TO KM.231.95	9/2011	3/2014 (-) [0/0]	574.00 (-) [574.00]	768.92 (0.00) [0]
254	PATNA-MUZZAFFARPUR	8/2010	2/2013 (-) [0/0]	671.30 (-) [671.30]	0.00 (0.00) [0]
255	REHABILITATION OF 4-LANE 5.575 KM LONG,4-LANE MG SETU OVER GANGA RIVER ON NH-19 FROM KM 212.72 TO KM	8/2016	12/2016 (-) [0/0]	1,742.01 (-) [1,742.01]	1,337.46 (0.00) [0]
256	REHABILITATION AND UPGRADATION OF TWO LANING OF MAHESHKHUNT - SAHARSA - PURNEA SECTION PKG - I	1/2018	/ (-) [0/0]	573.70 (-) [573.70]	76.84 (0.00) [0]
257	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS (KM 40 TO KM 219.945) OF NH-104	1/1991	/ (-) [0/0]	319.68 (-) [369.77]	301.91 (50.09) [0]
258	REHABILITATION AND UPGRADING TO 2 LANES/2 LANE WITH PAVED SHOULDERS CONFIGURATION OF BIRPUR - BIHPUR	1/1991	/ (-) [0/0]	675.00 (780.77) [675.00]	364.81 (0.00) [0]
259	SIX LANING OF AURANGABAD TO BIHAR - JHARKHAND BORDER (CHORDAHA) SECTION	1/2018	/ (-) [0/0]	895.39 (-) [895.39]	0.00 (0.00) [0]
260	SIX LANNING OF AUNTA-SIMARIA(GANGA BRIDGE WITH APPROACH ROADS) SECTION OF NH-31	8/2017	8/2017 (-) [2/2022]	950.64 (-) [950.64]	308.25 (0.00) [54]
261	STRENGTHENING AND WIDENING TO 2 LANE WITH PAVED SHOULDER FROM KM.103.865 TO 142.050 (GAYA-GOH) OF NH	3/2018	/ (-) [0/0]	153.24 (-) [153.24]	82.98 (0.00) [0]
262	TWO LANING WITH PS OF BIHARAHARIF - BARBIGHA - MOKAMA	8/2015	4/2019 (-) [0/0]	399.54 (-) [297.27]	259.67 (-102.27) [0]
263	TWO LANING WITH PS OF CHHAPRA -GOPALGANJ	8/2015	/ (-) [0/0]	854.80 (-) [1,038.56]	1,021.63 (183.76) [0]
264	TWO LANING WITH PS OF CHHAPRA -REWAGHAT - MUZAFFARPUR	8/2015	4/2018 (-) [0/0]	516.13 (-) [649.27]	643.77 (133.14) [0]
265	TWO-LANNING WITH PAVED SHOULDER OF MAHSHKUNT-SAHARSA-PURNEA SECTION FROM EXISTING KM.89.020 (DESIGN	3/2017	3/2020 (-) [0/0]	672.89 (-) [736.01]	74.96 (63.12) [0]
Urban Development					
266	PATNA METRO RAIL CORPORATION LIMITED	2/2019	6/2024 (-) [6/2024]	13,365.77 (13,925.50) [13,925.50]	258.94 (559.73) [0]
Water Resources					
267	I AND D AND STP AT CHAPRA	11/2018	12/2020 (6/2021) [0/0]	236.15 (-) [236.15]	58.03 (0.00) [0]
268	I AND D AND STP WORKS FOR BHAGALPUR	10/2017	9/2020 (-) [0/0]	254.13 (-) [413.29]	0.05 (159.16) [0]
269	IRRIGATION WORK OF BAGMATI	10/2005	3/2015 (-) [0/0]	956.00 (-) [721.37]	712.37 (-234.63) [0]
270	SAIDPUR SEWER NETWORK PATNA	4/2015	1/2021 (-) [0/0]	268.63 (-) [268.63]	317.85 (0.00) [0]
271	SEWER NETWORK SPS AND STP BEGUSARAI	3/2018	7/2021	230.06	82.04

			(-) [7/2021]	(-) [230.06]	(0.00) [0]
272	SEWER NETWORKS SPS AND STP HAJIPUR	3/2018	8/2021 (-) [12/2021]	305.19 (-) [305.19]	24.12 (0.00) [4]
273	SEWER NETWORKS, SPS AND STP, MUNGER	3/2018	10/2021 (-) [10/2021]	294.02 (-) [294.02]	0.00 (0.00) [0]
274	SEWERAGE SCHEME AT PAHARI ZONE IVA S PATNA	5/2017	5/2021 (-) [5/2021]	184.86 (-) [184.86]	168.85 (0.00) [0]
275	SEWERAGE SCHEME AT PAHARI ZONE V PATNA	5/2017	4/2021 (-) [4/2021]	356.37 (-) [356.37]	125.02 (0.00) [0]
276	SEWERAGE SYSTEM AND STP FOR DIGHA ZONE, PATNA	8/2017	6/2022 (-) [6/2022]	824.00 (-) [824.00]	42.75 (0.00) [0]
277	SEWERAGE SYSTEM AND STP FOR KANKARBAG ZONE PATNA	8/2017	6/2022 (-) [6/2022]	578.89 (-) [578.89]	42.75 (0.00) [0]
278	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA BEUR	12/2014	3/2020 (-) [3/2021]	225.77 (-) [398.90]	284.90 (173.13) [0]
279	SEWERAGE SYSTEM WITH SEWER NETWORK PATNA KARMALICHAK	3/2017	5/2021 (-) [5/2021]	277.42 (-) [277.42]	194.56 (0.00) [0]
280	SEWERAGE TREATMENT PLANT AT PAHARI PATNA	5/2017	11/2020 (3/2021) [0/0]	191.62 (-) [191.62]	62.80 (0.00) [0]
	CHHATISGARH				
	Coal				
281	AMERA OC RCE	2/2015	3/2018 (-) [3/2023]	335.97 (-) [335.97]	49.42 (0.00) [60]
282	AMGAON OPENCAST PROJECT RCE	7/2015	3/2020 (-) [3/2023]	316.10 (-) [316.10]	145.17 (0.00) [36]
283	BAROUD OC EXPANSION (3-10 MTY)	8/2020	3/2029 (-) [3/2029]	2,309.80 (-) [2,309.80]	284.31 (0.00) [0]
284	CHHAL OC SEAM -III (6.00 MTY)	12/2013	3/2022 (-) [3/2022]	610.63 (-) [610.63]	159.50 (0.00) [0]
285	DIPKA OC EXPANSION 40 MTY	12/2020	3/2029 (-) [3/2029]	5,241.40 (-) [5,241.40]	1,960.09 (0.00) [0]
286	DURGAPUR OPENCAST PROJECT	2/2015	3/2023 (-) [3/2026]	916.24 (-) [916.24]	11.38 (0.00) [36]
287	GEVRA EXPANSION OCP (SECL) (35-70) MTY	6/2010	3/2023 (3/2016) [3/2023]	11,816.40 (-) [11,816.40]	4,583.09 (0.00) [0]
288	JAGANNATHPOR OCP(3.00MTY)	9/2008	3/2015 (3/2020) [3/2022]	152.43 (459.49) [459.49]	198.78 (307.06) [84]
289	JAMPALI OCP RCE	5/2020	3/2024 (-) [3/2024]	278.64 (-) [278.64]	183.90 (0.00) [0]
290	JHIRIA WEST OPENCAST PROJECT	11/2018	3/2026 (-) [3/2026]	389.97 (-) [389.97]	0.00 (0.00) [0]

291	KARTALI (EAST) OCP (2.50 MTY)	7/2008	3/2014 (-) [3/2026]	178.44 (-) [178.44]	11.37 (0.00) [144]
292	KUSMUNDA EXPN.OCP(SECL)(15-50)MTY	8/2013	3/2023 (-) [3/2023]	7,612.33 (-) [7,612.33]	2,960.03 (0.00) [0]
293	MADANNAGAR OPENCAST PROJECT	10/2015	3/2024 (-) [3/2027]	1,875.32 (-) [1,875.32]	0.00 (0.00) [36]
294	MAHAMAYA OPENCAST PROJECT	5/2018	3/2026 (-) [3/2026]	410.26 (-) [410.26]	40.10 (0.00) [0]
295	MANIKPUR OC EXPANSION (3.5 MTY)	12/2009	3/2014 (-) [3/2023]	321.50 (-) [321.50]	210.73 (0.00) [108]
296	PELMA OCP(15.00MTY)	11/2014	3/2023 (-) [3/2023]	1,624.59 (-) [1,624.59]	9.08 (0.00) [0]
297	PORDA CHINTAPANI OCP (10 MTY)	12/2020	3/2029 (-) [3/2029]	2,310.12 (-) [2,310.12]	0.00 (0.00) [0]
298	VIJAY WEST OPENCAST PROJECT	5/2017	3/2026 (-) [3/2026]	976.95 (-) [976.95]	76.12 (0.00) [0]
	<u>Department Of Higher Education</u>				
299	C/O PERMANENT CAMPUS OF IIT BHILAI AT KUTHELABHATA, DURG CHHATTISGARH, STAGE I PHASE I.	3/2020	7/2022 (-) [7/2022]	808.62 (-) [808.62]	57.42 (0.00) [0]
	<u>Petroleum</u>				
300	AUGMENTATION OF FACILITIES AT THE EXISTING RAIPUR DEPOT	3/2021	3/2024 (-) [3/2024]	456.00 (-) [456.00]	12.89 (0.00) [0]
	<u>Power</u>				
301	TALAIPALLI COAL MINING PROJECT	9/2015	11/2019 (-) [0/0]	3,004.00 (-) [3,004.00]	1,307.03 (0.00) [0]
	<u>Railways</u>				
302	CHAMPA-JHARSUGUDA 3RD LINE	4/2008	12/2019 (10/2020) [10/2020]	872.00 (1,226.51) [1,226.51]	1,153.59 (354.51) [0]
303	CONSTRUCTION OF 3RD LINE BETWEEN PENDRA ROAD AND ANUPPUR (50.1 KM) IN BILASPUR DIVISION OF SEC RAILW	2/2016	3/2020 (-) [0/0]	393.98 (-) [393.98]	339.31 (0.00) [0]
304	GEVRA ROAD PENDRA ROAD	2/2014	3/2022 (-) [9/2023]	2,288.00 (-) [4,970.11]	962.98 (2,682.11) [18]
305	JHARSUGUDA-BILASPUR 4TH LINE	4/2015	3/2021 (12/2023) [12/2023]	1,973.00 (2,135.34) [2,135.34]	648.00 (162.34) [33]
306	KHARSIA DHARAMJAGARH WITH SPUR LINE EAST CORRIDOR-PHASE I	4/2013	9/2018 (-) [6/2022]	3,055.00 (-) [3,055.15]	2,666.33 (0.15) [45]
307	KIRANDUL - JAGDALPUR DOUBLING	12/2012	3/2020 (3/2023) [3/2023]	1,160.00 (1,160.83) [1,160.83]	988.59 (0.83) [36]
308	MULTI MODAL LOGISTICS PARK AT NAYA RAIPUR	5/2014	3/2018 (-) [0/0]	207.00 (-) [207.00]	153.83 (0.00) [0]
309	RAIPUR - TITLAGARH - DOUBLING	3/2007	3/2020 (-) [12/2021]	1,402.02 (-) [1,300.00]	1,152.05 (-102.02) [21]

	Road Transport And Highways				
310	4-LANE WITH PAVED SHOULDER CONFIGURATION OF BILASPUR-PATHRAPALI (KM.0+000 TO KM. 53+300) SECTION OF	3/2018	/ (-) [3/2021]	1,029.96 (-) [1,261.05]	333.72 (231.09) [0]
311	FOUR LANING OF SARAGAON - BILASPUR	12/2015	4/2018 (-) [0/0]	509.13 (-) [509.13]	412.66 (0.00) [0]
312	FOUR LANING OF SIMGA - SARAGAON	12/2015	5/2018 (-) [0/0]	596.67 (-) [596.67]	439.27 (0.00) [0]
313	REHABILITATION AND UP GRADATION OF NH-12A FROM KM191.422-KM 242.300 CHILPI- KAWARDHA SECTION.	12/2015	/ (10/2021) [10/2021]	291.05 (-) [291.05]	231.36 (0.00) [-]
314	REHABILITATION AND UPGRADATION OF NH 111 FROM KM 163.400 TO 215.800 SHIVNAGAR TO AMBIKAPUR SECTION	11/2015	6/2017 (10/2021) [10/2021]	335.32 (-) [335.32]	275.33 (0.00) [52]
315	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 178.944 TO 241.553 BANARI VILLAGE TO MASANIA KALA V	1/2016	9/2016 (12/2021) [12/2021]	476.20 (543.73) [544.00]	400.49 (67.80) [63]
316	REHABILITATION AND UPGRADATION OF NH 216 FROM KM 3.800 TO 90.460 RAIGARH TO SARAIPALLI SECTION	12/2014	3/2015 (3/2022) [3/2022]	496.02 (-) [496.02]	240.54 (0.00) [84]
317	REHABILITATION AND UPGRADATION OF NH 43 KANKER TO BEDMA SECTION KM. 130 TO 180	1/2016	8/2016 (6/2022) [6/2022]	497.14 (572.66) [572.66]	278.09 (75.52) [70]
318	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 373.505 TO 469.300 AMBIKAPUR TO PATHALGAON SECTION	1/2016	10/2016 (12/2021) [12/2021]	624.98 (731.50) [731.50]	460.02 (106.52) [62]
319	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 469.000 TO 531.000 PATTHALGAON TO KUNKURI	3/2016	7/2016 (12/2022) [12/2022]	452.94 (435.61) [435.61]	107.15 (-17.33) [77]
320	REHABILITATION AND UPGRADATION OF NH 78 FROM KM 531.250 TO KM 597.946 KUNKURI TO CG JH BORDER SECTIO	3/2017	1/2018 (10/2021) [10/2021]	423.79 (-) [423.79]	289.08 (0.00) [45]
321	UPGRADATION AND WIDENING OF BILASPUR TO MUNGELI SECTION NH-130A	11/2017	5/2019 (9/2021) [9/2021]	188.80 (-) [188.80]	87.05 (0.00) [28]
322	UPGRADATION AND WIDENING OF MP BORDER TO SURAJPUR SECTION NH 43 FROM KM. 245 TO 331	12/2014	11/2017 (9/2021) [9/2021]	379.16 (-) [379.16]	313.04 (0.00) [46]
	Steel				
323	NMDC INTEGRATED STEEL PLANT	1/2010	5/2015 (1/2022) [1/2022]	15,525.00 (21,940.00) [21,940.00]	18,779.12 (6,415.00) [80]
324	NMDC SLURRY PIPE LINE PROJECT - PHASE-1	11/2015	6/2023 (-) [6/2023]	2,907.00 (-) [2,907.00]	408.71 (0.00) [0]
325	REBUILDING OF COKE OVEN BATTERY NO. 7 and 8 AT BSP	11/2020	12/2023 (-) [12/2023]	542.24 (-) [542.24]	56.59 (0.00) [0]
	Urban Development				
326	CONSTRUCTION 729 QUARTERS (TYPE II-180 TYPE III-364 TYPE IV-112 TYPE V-68 TYPE-VI-5 SHOPS COMMUNI	5/2019	9/2020 (1/2023) [1/2023]	299.97 (299.97) [299.97]	15.87 (0.00) [28]
	DELHI				
	Civil Aviation				
327	CONSTRUCTION OF COMBINED OPERATIONAL OFFICES FOR DGCA, BCAS, AAIB, AERA AND AAI AT SAFDARJUNG AIRPOR	11/2016	4/2020 (-) [3/2022]	303.80 (351.21) [303.80]	180.24 (0.00) [23]
	Commerce				
328	CONSTRUCTION OF A NEW STATE OF ART	6/2018	10/2020	302.64	30.00

	EDUCATIONAL CAMPUS FOR IIFT AT MAIDAN GARHI, NEW DELHI		(-) [0/0]	(302.64) [302.64]	(0.00) [0]
	<u>Dpiit</u>				
329	INDIA INTERNATIONAL CONVENTION AND EXPO CENTRE	11/2017	12/2019 (5/2022) [5/2022]	4,773.00 (-) [5,178.00]	2,744.03 (405.00) [29]
	<u>Health And Family Welfare</u>				
330	AIIMS - MOTHER AND CHILD BLOCK	12/2013	5/2017 (-) [3/2021]	204.44 (-) [250.00]	249.24 (45.56) [0]
331	AIIMS - OPD(NEW)	8/2014	5/2017 (-) [1/2020]	293.65 (-) [325.00]	299.76 (31.35) [0]
332	GERIATRICS BLOCK- AIIMS DLEHI	12/2017	/ (-) [11/2021]	156.56 (-) [190.34]	156.14 (33.78) [-]
333	LHMC NEW DELHI-RE-DEVELOPMENT	2/2013	11/2013 (-) [9/2021]	414.11 (-) [655.58]	561.94 (241.47) [94]
	<u>Heavy Industry</u>				
334	LOPMENT OF ADVANCED ULTRA SUPER CRITICAL TECHNOLOGIES IN THERMAL POWER PLANTS IN INDIA	8/2016	9/2019 (-) [0/0]	1,554.00 (-) [900.00]	815.00 (-654.00) [0]
	<u>Home Affairs</u>				
335	BUILDING OF THE FORCE HEADQUARTER INCLUDING SECTOR HQR RAF	6/2019	7/2022 (10/2022) [10/2022]	277.35 (290.33) [290.33]	27.25 (12.98) [3]
336	ESTABLISHMENT OF CENTRAL ARMED POLICE FORCE INSTITUTE OF MEDICAL SCIENCES(CAPFIMS) AT NEW DELHI	10/2013	10/2019 (-) [3/2022]	1,219.21 (-) [2,000.00]	956.28 (780.79) [29]
	<u>Power</u>				
337	CONSTRUCTION OF ATAL AKSHAY URJA BHAWAN CGO COMPLEX LODHI ROAD NEW DELHI	10/2017	11/2019 (-) [0/0]	271.90 (-) [271.90]	90.99 (0.00) [0]
338	CREATION OF 400/220 KV SUBSTATIONS IN NCT OF DELHI DURING 12TH PLAN PERIOD (PART-A)	3/2015	5/2017 (12/2021) [12/2021]	1,394.52 (-) [1,394.52]	554.29 (0.00) [55]
	<u>Railways</u>				
339	ANAND VIHAR-TILAK BRIDGE 3RD AND 4TH LINE	4/2012	/ (-) [9/2023]	295.68 (-) [419.00]	160.58 (123.32) [-]
340	GRADE SEPERATOR AT DAYABASTI	4/1999	/ (-) [3/2024]	156.65 (-) [359.00]	111.51 (202.35) [-]
	<u>Rural Development</u>				
341	CONSTRUCTION OF GRAMEEN VIKAS BHAWAN (2BASEMENTS+ GROUND+9 FLOORS) FOR MINISTRY OF RURAL DEVELOPMENT	11/2018	7/2021 (-) [0/0]	361.60 (-) [361.60]	12.44 (0.00) [0]
	<u>Telecommunications</u>				
342	SETTING UP PHYSICAL INFRASTRUCTURE FOR THE NATIONAL INSTITUTE OF COMMUNICATION FINANCE(NICF) AT GHIT	10/2014	3/2018 (-) [12/2021]	248.20 (-) [248.20]	145.26 (0.00) [45]
	<u>Urban Development</u>				
343	C/O STEEL STRUCTURE BUILDINGS USING PRE-ENGINEERED TECHNOLOGY AT AFRICA AVENUE AND KG MARG	2/2020	11/2020 (9/2021) [9/2021]	532.00 (532.00) [532.00]	452.00 (0.00) [10]
344	CONSTRUCTION OF 108 NOS. GPRA TYPE-VII FLATS IN POCKET-I AT DEEN DAYAL UPADHYAYA MARG, NEW DELHI	6/2015	4/2019 (2/2022) [2/2022]	197.33 (217.00) [217.00]	142.78 (19.67) [34]
345	DELHI METRO PHASE IV THREE PRIORITY CORRIDORS	7/2019	3/2025 (-)	24,948.65 (-)	2,269.98 (0.00)

			[3/2025]	[24,948.65]	[0]
346	DELHI METRO RAIL EXTENSION FROM NAJAFGARH TO DHANSA BUS STAND	5/2017	12/2020 (-) [8/2021]	565.00 (-) [565.00]	468.78 (0.00) [8]
347	DELHI MRTS PHASE-III	9/2011	3/2016 (-) [8/2021]	38,585.00 (-) [38,585.00]	39,332.34 (0.00) [65]
348	RE-DEVELOPMENT OF GOVT. OF INDIA PRESS, MINTO ROAD, NEW DELHI (SH: CONSTRUCTION OF NEW BUILDING (2 B	11/2017	5/2020 (10/2021) [10/2021]	238.56 (238.56) [238.56]	205.72 (0.00) [17]
349	REDEVELOPMENT OF EAST KIDWAI NAGAR	6/2012	11/2019 (-) [0/0]	4,264.00 (-) [4,720.73]	4,683.08 (456.73) [0]
350	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT SRINIWASPURI NEW DELHI PHASE-I	10/2016	7/2021 (6/2023) [6/2023]	1,180.00 (1,100.80) [1,100.80]	35.70 (-79.20) [23]
351	REDEVELOPMENT OF GENERAL POOL RESIDENTIAL COLONY AT THYAGRAJ NAGAR, NEW DELHI- CONSTRUCTION OF 380 N	10/2016	8/2020 (6/2022) [6/2022]	392.00 (392.00) [392.00]	141.85 (0.00) [22]
352	REDEVELOPMENT OF GPRA AT KASTURBA NAGAR PHASE I	10/2016	3/2022 (-) [6/2023]	1,128.00 (1,128.00) [1,128.00]	28.50 (0.00) [15]
353	REDEVELOPMENT OF GPRA AT MOHAMMADPUR	10/2016	3/2021 (6/2023) [6/2023]	422.00 (422.00) [422.00]	80.75 (0.00) [27]
354	REDEVELOPMENT OF GPRA COLONY AT NAUROJI NAGAR	7/2016	/ (-) [12/2022]	2,694.00 (-) [2,694.00]	817.02 (0.00) [-]
Water Resources					
355	7 NOS PRIORITIZED STPS 1 NO. SPS AND PERIPHERAL SEWERS IN COMMAND AREA OF NAJAFHARH DRAIN DHANSA TO	5/2017	5/2020 (-) [0/0]	344.81 (-) [344.81]	0.00 (0.00) [0]
356	CONSTRUCTION OF 318 MLD WWTP WITH 10 YEARS O AND M AT CORONATION PILLAR DELHI	12/2018	1/2021 (-) [6/2021]	515.07 (-) [515.07]	336.27 (0.00) [0]
357	CONSTRUCTION OF 564 MLD 124 MGD WASTE WATER TREATMENT PLANT WITH EFFLUENT STANDARDS OF BOD – 10MG/L	3/2017	12/2022 (-) [12/2022]	665.78 (-) [665.78]	211.73 (0.00) [0]
358	REHABILITATION AND UP-GRADATION OF PHASE I STP 182 MLD R2	5/2016	12/2021 (-) [12/2022]	211.79 (-) [211.79]	101.28 (0.00) [12]
359	REHABILITATION AND UPGRADATION OF KONDLI PHASE I STP 45 MLD PHASE II STP 114 MLD AND PHASE III S	5/2016	2/2022 (-) [12/2022]	239.11 (-) [239.11]	138.16 (0.00) [10]
GOA					
Department Of Higher Education					
360	CONSTRUCTION OF PERMANENT CAMPUS FOR NATIONAL INSTITUTE OF TECHNOLOGY GOA AT CUNCOLIM, GOA.	5/2019	3/2020 (-) [0/0]	303.90 (-) [303.90]	31.80 (0.00) [0]
Health And Family Welfare					
361	SUPER SPECIALITY BLOCK PMSSY GOA	1/2018	/ (-) [1/2021]	249.01 (-) [249.07]	231.05 (0.06) [0]
Road Transport And Highways					
362	CONST. OF CANACONA BYPASS FROM KM.68/00 (CH.00/00) TO KM. 85/740 (CH. 7/740 ON PANAJI - MANGALORE SE	3/2015	/ (-) [0/0]	280.16 (-) [290.59]	244.36 (10.43) [0]
363	CONST. OF MISSING LINK BETWEEN KM. 11/680 TO KM. 14/020 AND WIDENING OF EXISTING TWO LANE ROAD	3/2015	/ (-) [0/0]	184.05 (-) [184.05]	118.37 (0.00) [0]
364	CONSTRUCTION OF BRIDGE INCLUDING APPROACHES	10/2015	/	936.40	520.09

	ACROSS RIVER ZUARI ON NH-17 (NH-66) ON PANJIM-MANGALORE		(-) [0/0]	(-) [936.40]	(0.00) [0]
365	CONSTRUCTION OF MARGOA WESTERN BYPASS FOR NH-17 (NEW NH-66) FROM KM. 26 /200 (CHAINAGE 00/00) TO K	3/2015	/	298.33	325.55
			(-) [0/0]	(-) [298.33]	(0.00) [0]
366	KARASWADA TO BAMBOLIM	3/2017	12/2019	852.67	190.09
			(-) [0/0]	(-) [852.67]	(0.00) [0]
367	PATRADEVI TO KARASWADA 4L	3/2017	5/2020	634.32	292.34
			(-) [0/0]	(-) [634.32]	(0.00) [0]
368	WIDENING TO 4/6 LANES OF EXISTING NH-17 FROM KM 531/934 (AFTER ZUARI BR.) TO KM 536/250 JN. WITH VER	12/2015	/	773.98	394.63
			(-) [0/0]	(-) [773.98]	(0.00) [0]
369	WIDENING TO 4/6/8 LANES OF EXISTING NH-17 FROM KM 522/615 (NEAR GMC) TO KM 530/850 JOINING NEW ZUIAR	12/2015	/	819.95	362.15
			(-) [0/0]	(-) [819.95]	(0.00) [0]
	<u>GUJARAT</u>				
	<u>Atomic Energy</u>				
370	KAKRAPAR ATOMIC POWER PROJECT - 3 AND 4	10/2009	12/2015	11,459.00	17,041.00
			(-) [2/2022]	(-) [16,580.00]	(5,121.00) [74]
	<u>Civil Aviation</u>				
371	C/O NEW GREENFIELD AIRPORT AT HISSAR, RAJKOT, GUJARAT	1/2018	8/2022	1,405.00	334.66
			(-) [12/2022]	(-) [1,405.00]	(0.00) [4]
	<u>Petroleum</u>				
372	ACRYLICS OR OXO-ALCOHOL PROJECT AT GUJARAT REFINERY	11/2019	5/2023	5,251.00	421.90
			(-) [5/2023]	(-) [5,251.00]	(0.00) [0]
373	AUGMENTATION OF LPG IMPORT TERMINAL FROM 0.6 MMTPA TO 2.5 MMTPA AT KANDLA, GUJARAT	3/2018	/	588.20	128.08
			(5/2023) [5/2023]	(730.20) [730.20]	(142.00) [-]
374	AUGUMENTATION OF SALAYA MATHURA CRUDE OIL PIPELINE SYSTEM	10/2020	8/2023	1,614.00	0.21
			(-) [8/2023]	(-) [1,614.00]	(0.00) [0]
375	CAPACITY AUGMENTATION JAMNAGAR LONI PIPELINE	4/2016	4/2018	327.78	195.40
			(-) [12/2021]	(-) [200.00]	(-127.78) [44]
376	CREATING INFRASTRUCTURE AT GUJARAT REFINERY AND DUMAD FOR KOYALI AHMEDNAGAR SOLAPUR PIPELINE	10/2017	2/2020	906.00	327.90
			(10/2021) [10/2021]	(-) [906.00]	(0.00) [20]
377	LAB REVAMP AT GUJARAT REFINERY	10/2019	12/2021	403.00	145.34
			(-) [4/2022]	(-) [403.00]	(0.00) [4]
378	PETROCHEMICAL AND LUBE INTEGRATION PROJECT AT GUJARAT REFINERY	9/2020	9/2024	18,936.00	763.62
			(-) [8/2024]	(-) [18,936.00]	(0.00) [-1]
379	REDEVELOPMENT OF NANDASAN FIELD	2/2020	8/2022	444.87	103.78
			(-) [8/2022]	(-) [444.87]	(0.00) [0]
380	REDEVELOPMENT OF SANTHAL FIELD	2/2017	3/2026	1,162.56	901.28
			(-) [3/2026]	(-) [970.30]	(-192.26) [0]
381	REPLACEMENT OF EXISTING TWIN 42" OFFSHORE PIPELINES AT VADINAR ALONG WITH TWO EXISTING PIPELINE END	6/2020	12/2022	1,378.00	159.37
			(-) [12/2022]	(-) [1,378.00]	(0.00) [0]
382	SUSTAINED EVACUATION OF GAS FROM GANDHAR FIELDS BY INSTALLING A GAS COMPRESSOR AND PIPELINE CONNECTI	9/2018	2/2021	225.54	41.34
			(-) [8/2022]	(247.90) [247.90]	(22.36) [18]
	<u>Power</u>				

383	150 MW SOLAR PV PROJECT IN GUJARAT (LIMBDI, MESANKA & RADHANPUR)	5/2021	9/2022 (-) [9/2022]	674.92 (-) [674.92]	0.00 (0.00) [0]
384	GUJARAT 200 MW (GUVNL TENDER)	1/2021	7/2022 (-) [6/2022]	842.27 (-) [842.27]	92.08 (0.00) [-1]
385	KAWAS SOLAR 56 MW	8/2020	10/2021 (1/2022) [10/2021]	261.80 (-) [261.80]	63.92 (0.00) [0]
386	SUPPLEMENTARY TRANS. SYSTEM FOR UMSPP AT BANASKANTHA (RADHANESDA) GUJARAT	12/2017	6/2019 (-) [0/0]	193.14 (-) [193.14]	108.80 (0.00) [0]
387	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER PARK AT BANASKANTHA (RADHANESDA) GUJARAT	5/2017	9/2018 (-) [0/0]	175.64 (-) [175.64]	115.43 (0.00) [0]
	Railways				
388	AHMEDABAD-BOTAD (GC)	4/2012	12/2021 (-) [12/2021]	975.62 (-) [1,500.00]	1,261.64 (524.38) [0]
389	AHMEDABAD-HIMMATNAGAR-UDAIPUR (WR)	4/2008	3/2020 (3/2024) [3/2024]	829.74 (1,246.59) [1,886.76]	1,875.42 (1,057.02) [48]
390	BHAVNAGAR-WORKSHOP FACILITIES FOR 50 BG COACHES POH PER MONTH (WR)	4/2006	3/2011 (-) [0/0]	117.36 (196.95) [202.35]	809.40 (84.99) [0]
391	BHILDI-VIRAMGAM GAUGE CONVERSION INCLUDING GC OF MAHESANA-TARANGA HILL AS MATERIAL MODIFICATION	2/1991	3/2019 (10/2021) [10/2021]	551.51 (724.70) [890.76]	773.12 (339.25) [31]
392	BHUJ-NALIYA(GC) WITH EXTENSION FROM NALIYA TO VAYOR (WR)	4/2008	3/2012 (10/2023) [10/2023]	318.24 (321.62) [321.62]	126.36 (3.38) [139]
393	DABHOI-CHANDOD (17.07KM) -GC WITH EXTENSION UPTO KEVADIYA(32.68KM) =49.75KM	4/2017	3/2020 (9/2021) [9/2021]	691.84 (811.60) [890.62]	812.08 (198.78) [18]
394	DHASA-JETALSAR (GC)	4/2012	3/2021 (-) [0/0]	644.38 (-) [872.65]	611.25 (228.27) [0]
395	GANDHINAGAR REDEVELOPMENT OF STATION ALOGWITH CONSTRUCTION OF 300 ROOMS HOTEL ON AIR SPACE OF STATIO	3/2017	/ (-) [0/0]	243.60 (-) [243.60]	0.00 (0.00) [0]
396	MIYAGAM-KARJAN-DABHOI-SAMLAYA (GC)	4/2011	/ (3/2024) [3/2024]	844.10 (844.10) [844.10]	251.82 (0.00) [-]
397	MULTI MODAL LOGISTICS PARK AT VARNAMA	10/2013	3/2019 (-) [0/0]	343.00 (-) [343.00]	222.83 (0.00) [0]
398	PALANPUR KHODIYAR ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 208 211C 214 AND 220	3/2012	/ (-) [0/0]	153.83 (-) [153.83]	0.00 (0.00) [0]
399	PALANPUR-SAMAKHAYALI (DL)	4/2013	12/2021 (-) [3/2022]	1,548.66 (-) [1,868.89]	1,462.02 (320.23) [3]
400	RAJKOT-VERAVAL,WANSJALIA TO JATALSAR WITH NEW MM FOR SHAPUR-SARADIYA AND SOMNATH-KODINAR (GC)	4/1994	3/2019 (3/2023) [3/2023]	320.66 (858.96) [1,378.11]	555.49 (1,057.45) [48]
401	SURENDRA NAGAR RAJKOT	4/2015	3/2021 (12/2022) [12/2022]	1,002.39 (1,002.39) [1,002.39]	730.07 (0.00) [21]
402	VIRAMGAM-SAMAKHIALI (DL)	4/2011	3/2021 (12/2022) [12/2022]	1,037.15 (1,125.53) [1,383.69]	1,199.84 (346.54) [21]

403	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 60 64 66 68 69 71 74 75 77 81 AND 82 ALON	3/2012	/ (-) [0/0]	248.26 (-) [248.26]	0.00 (0.00) [0]
Road Transport And Highways					
404	2-LANE WITH PAVED SHOULDERS OF GADU-PORBANDER SECTION	12/2016	/ (-) [0/0]	417.19 (-) [417.19]	199.86 (0.00) [0]
405	4-LANNING OF KODINAR TO VERAVAL SECTION OF NH-8E FROM KM 221.610 TO KM 263.000	7/2016	/ (-) [0/0]	829.97 (-) [829.97]	190.21 (0.00) [0]
406	4-LANNING OF PORBANDAR DWARKA SECTION IN THE STATE OF GUJARAT	6/2017	6/2020 (-) [0/0]	1,958.88 (-) [1,993.81]	1,116.85 (34.93) [0]
407	AHMEDABAD TO VADODARA SECTION	1/2013	12/2015 (-) [0/0]	2,125.24 (-) [2,125.24]	4,669.71 (0.00) [0]
408	CONSTRUCTION OF 4-LANE LADDOWAL BYPASS	5/2016	/ (-) [8/2021]	364.56 (-) [392.00]	353.42 (27.44) [-]
409	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 254.430 TO KM 279.000 (KIM TO ANKLESHWAR	3/2018	/ (-) [0/0]	1,161.39 (-) [1,161.39]	0.00 (0.00) [0]
410	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 279.00 TO 292.00 (ANKLESHWAR TO MANUBAR S	3/2018	/ (-) [7/2021]	1,437.64 (-) [1,437.64]	564.11 (0.00) [0]
411	CONSTRUCTION OF EIGHT LANE VADODARA KIM EXPRESSWAY FROM KM 355.00 TO KM 378.740 (PADRA TO VADODARA S	3/2018	/ (-) [6/2021]	2,702.05 (-) [2,043.00]	1,888.51 (-659.05) [0]
412	CONSTRUCTION OF MISSING LINKS (SINGLE LANE) IN LAKHPAT GADULI HAJIPUR ODMA KHAVDA DHOLAVIRA MAUVANA	10/2018	5/2019 (-) [0/0]	400.76 (-) [400.76]	166.41 (0.00) [0]
413	CONSTRUCTION OF SIGNATURE BRIDGE BETWEEN DWARKA AND BEY DWARKA AND ITS APPROACHES IN THE STATE OF GU	8/2017	3/2018 (-) [0/0]	962.43 (-) [962.43]	282.94 (0.00) [0]
414	DEVELOPMENT OF CHILODA GANDHINAGAR SARKHEJ OF NH 147 OLD NH 8C FROM KM 0/0 TO KM 44/042 IN THE STATE	12/2017	11/2018 (-) [0/0]	867.97 (-) [867.97]	577.48 (0.00) [0]
415	FOUR LANING OF BHAVNAGAR-TALAJA SECTION OF NH-8E FROM KM. 7.090 TO KM. 53.585 (DESIGN CH FROM KM. 6.	5/2016	/ (-) [0/0]	998.18 (-) [998.18]	732.85 (0.00) [0]
416	FOUR LANING OF KAGAVADAR - UNA SECTION OF NH-8E FROM KM 139.915 TO KM 180.478 (PACKAGE-IV) IN THE ST	5/2016	/ (-) [0/0]	723.64 (-) [723.64]	504.95 (0.00) [0]
417	FOUR LANING OF TALAJA – MAHUVA SECTION OF NH – 8E FROM KM. 53.585 TO KM. 100.100 (DESIGN CHAINAGE FR	5/2016	/ (-) [0/0]	834.64 (-) [834.64]	203.40 (0.00) [0]
418	FOUR LANING OF UNA TO KODINAR OF NH-8E FROM KM. 180.478 TO KM 221.610 (PACKAGE-V) IN THE STATE OF GU	5/2016	/ (-) [0/0]	763.08 (-) [763.08]	398.51 (0.00) [0]
419	GUJARAT/MAHARASHTRA BORDERSURAT-HAZIRA PORT SECTION	3/2010	9/2012 (-) [0/0]	1,509.10 (-) [1,509.10]	3,684.44 (0.00) [0]
420	JUNAGADH BYPASS	10/2017	10/2017 (-) [0/0]	232.49 (-) [232.49]	0.00 (0.00) [0]
421	KANDLA - MUNDRA PORT	1/2011	7/2013 (-) [0/0]	953.88 (-) [953.88]	0.00 (0.00) [0]
422	SIX LANING OF SHAMLA JI TO MOTACHILODHA FROM KM 401.200 TO KM 494.410 (LENGTH 93.210 KM) SECTION OF	2/2018	/ (-) [1/2021]	1,052.21 (-) [1,449.00]	342.39 (396.79) [0]

423	SIX LANNING FROM KM. 401.200 TO 494.410 OF NH-8 ON HYBRID ANNUITY MODE UNDER NHDP-V(PKG VI)REG.	1/2017	/ (-) [0/0]	1,251.11 (1,361.00) [1,361.00]	441.78 (109.89) [0]
424	SIX-LANING OF KAMREJ-CHALTHAN SECTION OF NH-8 FROM KM 248.100 TO KM 264.350 INCLUDING LONG TERM REME	5/2016	/ (-) [0/0]	425.60 (-) [425.60]	0.00 (0.00) [0]
425	UP GRADATION OF NEWLY DECLARED NH 341 TO TWO LANE WITH PAVED SHOULDER CONFIGURATION BETWEEN KM. 65.4	3/2018	6/2021 (-) [6/2021]	351.00 (-) [351.00]	154.34 (0.00) [0]
426	UPGRADATION OF NEW NATIONAL HIGHWAY NO 168 TO TWO LANE WITH PAVED SIDE SHOULDER CONFIGURATION BETWEEN	3/2018	11/2018 (-) [0/0]	464.07 (-) [464.07]	313.82 (0.00) [0]
427	VADODARA-SURAT SECTION	3/2014	8/2016 (-) [0/0]	503.16 (-) [503.16]	0.00 (0.00) [0]
	<u>Urban Development</u>				
428	AHMEDABAD METRO RAIL PROJECT PHASE I	11/2014	12/2018 (-) [8/2022]	10,773.00 (-) [12,787.00]	9,144.21 (2,014.00) [44]
429	AHMEDABAD METRO RAIL PROJECT PHASE II	3/2019	3/2024 (-) [3/2024]	5,384.17 (-) [5,384.17]	193.79 (0.00) [0]
430	SURAT METRO RAIL PROJECT	3/2019	3/2024 (-) [3/2024]	12,020.32 (-) [12,020.32]	177.50 (0.00) [0]
	<u>HARYANA</u>				
	<u>Fertilisers</u>				
431	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL PANIPAT	1/2018	11/2019 (6/2021) [10/2021]	215.92 (-) [215.92]	172.01 (0.00) [23]
	<u>Health And Family Welfare</u>				
432	CONSTRUCTION OF HOSPITAL AND OPD BLOCK NCI JHAJJAR	9/2014	3/2018 (-) [9/2019]	505.58 (-) [585.00]	586.96 (79.42) [0]
	<u>Home Affairs</u>				
433	C/O SEPARATE FAMILY ACCOMMODATION (PHASE-I) WHICH INCLUDES C/O 440 NOS. RESIDENTIAL QTRS. I.E. TYPE-	1/2020	10/2023 (-) [10/2023]	166.98 (167.00) [166.98]	0.00 (0.00) [0]
434	CONSTRUCTION OF SEPARATE FAMILY ACCOMMODATION (440 NOS.) (PHASE- C/O 336 NOS. TYPE- II QTRS , 96	1/2020	5/2022 (-) [5/2022]	166.98 (-) [166.98]	0.29 (0.00) [0]
	<u>Petroleum</u>				
435	CAPACITY EXPANSION OF PANIPAT REFINERY FROM 15 TO 25 MMTA	2/2021	9/2024 (-) [9/2024]	34,627.00 (-) [34,627.00]	445.30 (0.00) [0]
436	2ND GENERATION ETHANOL PLANT AT PANIPAT REFINERY	1/2019	1/2021 (3/2022) [3/2022]	909.00 (-) [909.00]	416.23 (0.00) [14]
437	CATALYST MANUFACTURING UNIT OF 1500 MTPA CAPACITY AT PANIPAT REFINERY	4/2018	2/2020 (8/2021) [7/2022]	206.63 (340.76) [340.76]	131.80 (134.13) [29]
438	CITY GAS DISTRIBUTION PROJECT IN GEOGRAPHICAL AREA OF SONIPAT (EAAA) AND JIND DISTRICTS	9/2018	9/2026 (2/2027) [2/2027]	520.00 (-) [520.00]	144.71 (0.00) [5]
439	COMPRESSED BIO GAS PLANT AT GORAKHPUR	9/2019	7/2021 (3/2022) [3/2022]	164.69 (-) [164.69]	15.02 (0.00) [8]
440	ETHANOL PRODUCTION FROM PSA OFF GAS BASED ON LANZATECH TECHNOLOGY AT PANIPAT REFINERY	10/2018	2/2020 (2/2022) [2/2022]	598.00 (-) [598.00]	391.04 (0.00) [24]
441	INFRASTRUCTURE DEVELOPMENT TO FACILITATE	12/2018	6/2021	278.60	63.96

	IMPORT OF GRID POWER AT 220 KV, PANIPAT		(7/2022) [7/2022]	(-) [278.60]	(0.00) [13]
442	NAPHTHA CRACKER EXPANSION PROJECT AT PANIPAT	8/2018	8/2020 (4/2022) [4/2022]	1,636.00 (-) [1,636.00]	862.17 (0.00) [20]
443	PX-PTA REVAMP AT PANIPAT REFINERY	8/2019	10/2021 (-) [10/2021]	1,255.00 (-) [1,255.00]	255.22 (0.00) [0]
444	R and D CAMPUS II AT FARIDABAD	6/2019	12/2022 (7/2023) [7/2023]	2,281.94 (-) [2,281.94]	539.26 (0.00) [7]
445	SULTANPUR JHAJJAR HISSAR PIPELINE (SJHPL) PROJECT	8/2018	8/2020 (5/2021) [12/2021]	286.42 (327.01) [327.01]	215.40 (40.59) [16]
	<u>Railways</u>				
446	MULTI MODAL LOGISTICS PARK AT BARHI	12/2015	3/2019 (-) [0/0]	346.32 (-) [346.32]	320.28 (0.00) [0]
447	ROHTAK-MEHAM HANSI	4/2012	12/2011 (-) [6/2021]	287.00 (-) [893.45]	717.17 (606.45) [0]
	<u>Road Transport And Highways</u>				
448	4 LANING OF AMBALA - KAITHAL - PACKAGE -1	12/2015	6/2016 (-) [0/0]	602.95 (-) [507.70]	0.00 (-95.25) [0]
449	4 LANING OF AMBALA - KAITHAL - PACKAGE -2	1/2016	7/2018 (-) [0/0]	574.28 (-) [537.16]	0.00 (-37.12) [0]
450	8 LANING OF MUKARBA CHOWK TO PANIPAT	7/2015	4/2019 (-) [9/2021]	2,128.72 (-) [2,128.72]	1,577.44 (0.00) [29]
451	CONSTN. OF 4 LANING IN KM.99.00 TO 114.375 PACKAGE-V (EPC) INCLUDING BHIWANI BYPASS	1/2017	3/2019 (-) [0/0]	247.25 (-) [247.25]	179.30 (0.00) [0]
452	CONSTRUCTION OF 8 LANE DWARKA EXPRESSWAY (NH-248BB PACKAGE IV FROM RAIL OVER BRIDGE (ROB) TILL END P	3/2018	/ (6/2021) [12/2020]	1,484.30 (-) [1,484.30]	262.70 (0.00) [0]
453	DELHI/ HARYANA BORDER TO ROHTAK	4/2007	5/2010 (-) [0/0]	486.00 (-) [486.00]	470.01 (0.00) [0]
454	ISMAILABAD-NARNAUL PKG-1	1/2019	/ (-) [0/0]	996.65 (-) [996.65]	947.82 (0.00) [0]
455	ISMAILABAD-NARNAUL PKG-2	1/2019	/ (-) [0/0]	1,243.45 (-) [1,243.45]	958.21 (0.00) [0]
456	ISMAILABAD-NARNAUL PKG-3	1/2019	/ (-) [0/0]	889.36 (-) [889.36]	637.39 (0.00) [0]
457	ISMAILABAD-NARNAUL PKG-4	1/2019	/ (-) [0/0]	1,018.79 (-) [1,018.79]	703.08 (0.00) [0]
458	ISMAILABAD-NARNAUL PKG-5	1/2019	/ (-) [0/0]	1,051.91 (-) [1,051.91]	807.68 (0.00) [0]
459	ISMAILABAD-NARNAUL PKG-6	1/2019	/ (-) [0/0]	1,120.06 (-) [1,120.06]	831.50 (0.00) [0]
460	ISMAILABAD-NARNAUL PKG-7	1/2019	/ (-) [0/0]	1,137.42 (-) [1,137.42]	903.95 (0.00) [0]

461	ISMAILABAD-NARNAUL PKG-8	1/2019	/	1,033.19	876.52
			(-)	(-)	(0.00)
			[0/0]	[1,033.19]	[0]
462	PANIPAT-JALANDHAR 6 LANE(KM 96 TO 387.1 KM)	5/2009	11/2011	1,108.00	3,450.00
			(-)	(3,485.00)	(1,180.00)
			[0/0]	[2,288.00]	[0]
463	REDESIGNING, REHABILITATION AND UPGRADATION TO FOUR LANE CONFIGURATION STRENGTHENING OF ROHNA/HASS	3/2018	/	551.58	305.46
			(-)	(-)	(0.00)
			[0/0]	[551.58]	[0]
464	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR BHIWANI-MUNDAL-JIND ROAD FROM DE	3/2018	/	275.12	170.81
			(-)	(-)	(0.00)
			[0/0]	[275.12]	[0]
465	REHABILITATION AND UP-GRADATION FROM 2 LANE WITH PAVED SHOULDER FOR JIND - KARNAL SECTION FROM EXISTING	3/2018	/	307.79	197.30
			(-)	(-)	(0.00)
			[0/0]	[307.79]	[0]
466	REHABILITATION AND UPGRADATION OF JHAJJAR-LOHARU SECTION FROM KM 130.770 TO KM 228.630 (DESIGN CHAIN	3/2018	/	181.78	129.84
			(-)	(-)	(0.00)
			[0/0]	[181.78]	[0]
467	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER FROM JIND-GOHANA ROAD FROM DESIGN CHAIN	3/2018	/	198.05	130.78
			(-)	(-)	(0.00)
			[0/0]	[198.05]	[0]
468	SIX LANING AND STRENGTHENING OF NH-248A FROM EXISTING KM 2.740 (RAJIV CHOWK) TO KM 11.682 (PACKAGE-I)	3/2018	/	795.50	353.55
			(-)	(906.65)	(127.14)
			[0/0]	[922.64]	[0]
469	SIX LANING AND STRENGTHENING OF NEW NH-248A FROM EXISTING KM 11+682 TO EXISTING KM 24+400 IN THE STA	3/2018	/	634.70	143.54
			(-)	(-)	(296.51)
			[0/0]	[931.21]	[0]
HIMACHAL PRADESH					
Department Of Higher Education					
470	DIFFERENT BUILDINGS UNDER PHASE 1 NORTH FOR IIT MANDI AT KAMAND	11/2012	11/2014	270.83	226.16
			(-)	(-)	(0.00)
			[0/0]	[270.83]	[0]
471	ESTABLISHMENT OF PERMANENT CAMPUS PHASE 1 OF IIM SIRMAUR	9/2018	6/2022	392.51	38.44
			(-)	(-)	(0.00)
			[6/2022]	[392.51]	[0]
Health And Family Welfare					
472	AIIMS BILASPUR	4/2018	9/2021	1,351.00	814.67
			(-)	(-)	(120.00)
			[6/2022]	[1,471.00]	[9]
473	CONSTRUCTION OF 300 BEDDED HOSPITAL AND TEACHING BLOCK IN DR YS PARMAR GMC AT NAHAN HIMACHAL PRADESH	12/2018	6/2021	260.00	25.38
			(-)	(-)	(0.00)
			[5/2022]	[260.00]	[11]
Power					
474	DHAULASIDH HYDROELECTRIC PROJECT (66 MW)	10/2020	11/2025	687.97	155.02
			(-)	(-)	(0.00)
			[11/2025]	[687.97]	[0]
475	LUHRI HYDROELECTRIC PROJECT (STAGE1)	11/2020	1/2026	1,810.56	486.06
			(-)	(-)	(0.00)
			[1/2026]	[1,810.56]	[0]
476	PARBATI HEP (4X200 MW) (NHPC) II	9/2002	9/2009	3,919.59	9,164.35
			(3/2023)	(9,897.59)	(5,978.00)
			[3/2023]	[9,897.59]	[162]
Railways					
477	BHANUPALI-BILASPUR BERTI NL	4/2008	12/2026	2,966.99	547.68
			(-)	(-)	(3,786.43)
			[12/2025]	[6,753.42]	[-12]
Road Transport And Highways					
478	2 LANE WITH PAVED SHOULDERS ON KULLU TO MANALI (KM 272/00 TO 309/345)	2/2016	2/2019	273.20	668.42
			(-)	(-)	(0.00)
			[0/0]	[273.20]	[0]
479	4-LANING OF END OF PANDOH BYPASS TAKOLI IN H.P	6/2017	6/2020	2,485.93	983.69

			(-) [9/2021]	(-) [2,485.93]	(0.00) [15]
480	FOUR LANING OF KIRATPUR NEAR CHOUK SECTION (73.20 KM TO 186.50 KM)	11/2013	11/2016 (-) [0/0]	1,916.79 (-) [1,916.79]	1,960.92 (0.00) [0]
481	FOUR LANING OF PARWANOO -SOLAN	9/2015	3/2018 (-) [0/0]	934.46 (-) [934.46]	1,298.21 (0.00) [0]
482	FOUR LANING OF SOLAN-KAITHLIGHAT SECTION OF NH-22 (NOW NH-5) FROM KM 106.139 TO KM 129.050, ON EPC M	3/2018	/ (-) [0/0]	478.74 (-) [478.74]	714.50 (0.00) [0]
483	FOUR LANNING OF NERCHOWK-PANDOH BYPASS SECTION OF NH-21(PACKAGE-I KM 190.000 TO KM 221.305) UNDER NH	9/2016	/ (-) [0/0]	1,273.71 (-) [1,273.71]	826.42 (0.00) [0]
484	FOUR LANNING OF TAKOLI-KULLU SECTION OF NH-21 (KM 242+000 TO KM 272+000)	10/2016	/ (-) [0/0]	447.75 (-) [447.75]	1,324.11 (0.00) [0]
485	REHABILITATION AND UPGRADATION TO 2-LANE CONFIGURATION OF HEWNA-ASHYARI SECTION (KM 25.000 TO KM 50.	8/2020	3/2021 (-) [3/2021]	242.80 (-) [242.80]	7.55 (0.00) [0]
486	REHABILITATION AND UPGRADATION TO 2-LANE/2-LANE WITH PAVED SHOULDERS/4-LANE CONFIGURATION OF PAONTA	8/2020	4/2021 (-) [4/2021]	272.98 (-) [272.98]	8.75 (0.00) [0]
487	REHABILITATION AND UPGRADATION TO INTERMEDIATE LANE CONFIGURATION OF SHRI KYARI-GUMMA SECTION (KM 75	8/2020	4/2021 (-) [4/2021]	349.20 (-) [349.20]	0.00 (0.00) [0]
488	TWO LANNING WITH FORMATION OF FOUR LANE OF PROPOSED SHIMLA BYPASS	8/2016	/ (-) [0/0]	1,583.18 (-) [1,583.18]	0.00 (0.00) [0]
	JAMMU AND KASHMIR				
	Department Of Higher Education				
489	CONSTRUCTION OF PERMANENT CAMPUS IIT JAMMU (PHASE 1C)	1/2018	4/2023 (-) [4/2023]	676.00 (-) [676.00]	0.00 (0.00) [0]
490	CONSTRUCTION OF PERMANENT CAMPUS OF IIM JAMMU (PHASE 1)	3/2019	7/2022 (-) [7/2022]	329.00 (-) [329.00]	0.00 (0.00) [0]
	Health And Family Welfare				
491	C/O AIIMS AT AWANTIPORA (KASHMIR) JAMMU AND KASHMIR	3/2019	9/2025 (-) [5/2024]	1,828.00 (-) [1,828.00]	0.00 (0.00) [-16]
492	CONSTRUCTION OF AIIMS AT AWANTIPORA SRINAGAR JAMMU AND SRINAGAR	3/2019	9/2025 (-) [9/2025]	1,577.00 (-) [1,828.00]	0.00 (251.00) [0]
493	CONSTRUCTION OF AIIMS AT JAMMU VIJAYPUR, SAMBA JAMMU AND KASHMIR	3/2019	9/2023 (-) [9/2023]	1,404.00 (-) [1,404.00]	279.98 (0.00) [0]
	Power				
494	KIRU HYDRO ELECTRIC PROJECT	3/2019	/ (8/2024) [8/2024]	4,287.59 (-) [4,287.59]	582.89 (0.00) [-]
495	PAKAL DUL HYDRO ELECTRIC PROJECT (1000 MW)	10/2014	4/2020 (-) [7/2025]	8,112.12 (-) [8,112.12]	2,022.77 (0.00) [63]
	Railways				
496	UDHAMPUR-SRINAGAR-BARAMULLA (NL),NR	3/1995	11/2002 (-) [12/2022]	2,500.00 (27,949.00) [27,949.00]	25,191.80 (25,449.00) [241]
	Road Transport And Highways				
497	CONSTRUCTION OF (I) CONNECTING ROAD FROM Z-MORH TUNNEL TO ZOJILA TUNNEL AND (II) 14.150 KM	8/2020	9/2026 (-)	6,808.69 (-)	176.00 (0.00)

	LONG BI-D		[9/2026]	[6,808.69]	[0]
498	CONSTRUCTION OF STAND ALONE RING ROAD/ BYPASS AROUND JAMMU CITY IN THE STATE OF J AND K ON EPC MODE	12/2017	/ (-) [1/2021]	1,471.75 (1,339.00) [1,339.00]	928.92 (-132.75) [0]
499	CONSTRUCTION, OPERATION AND MAINTENANCE OF Z-MORH TUNNEL INCLUDING APPROACHES ON NH-01 SRINAGAR-SONA	12/2019	12/2023 (-) [12/2023]	2,680.42 (-) [2,680.42]	794.41 (0.00) [0]
500	DONIPAWA TO ASHAJIPORA BYPASS PKG-7	3/2021	12/2022 (-) [12/2022]	260.40 (-) [260.40]	0.00 (0.00) [0]
501	FOUR LANING OF RAMBAN - BANIHAL SECTION OF NH-1A	12/2015	6/2019 (-) [0/0]	2,168.66 (-) [2,168.66]	1,108.16 (0.00) [0]
502	FOUR LANING OF UDHAMBUR - RAMBAN SECTION OF NH-1A	12/2015	12/2018 (-) [0/0]	2,136.97 (-) [2,136.97]	1,719.20 (0.00) [0]
503	JAMMU-UDHAMPUR KM.27.5 TO KM.67.00	7/2010	7/2013 (-) [0/0]	1,813.76 (-) [1,813.76]	2,652.71 (0.00) [0]
504	KHELLANI-KHANABAL PKG-1	3/2021	9/2022 (-) [9/2022]	486.45 (-) [486.45]	14.16 (0.00) [0]
505	KHELLANI-KHANABAL PKG-3	3/2021	12/2022 (-) [12/2022]	398.51 (-) [398.51]	0.00 (0.00) [0]
506	KHELLANI-KHANABAL PKG-6	2/2021	9/2022 (-) [9/2022]	285.28 (-) [285.28]	0.33 (0.00) [0]
507	NASHRI- CHANANI	5/2011	6/2015 (-) [0/0]	2,159.00 (-) [2,519.00]	4,758.92 (360.00) [0]
508	QUAZIGUND-BANIHAL KM.220.00 TO KM.188.00	7/2010	7/2015 (-) [9/2020]	1,987.00 (-) [1,987.00]	3,113.72 (0.00) [0]
509	SRINAGAR TO BANIHAL	6/2011	6/2014 (-) [10/2020]	1,100.70 (-) [1,100.70]	2,932.90 (0.00) [0]
510	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 12.850 TO KM20.300 OF 7.450KM LENGTH ON GOHA-KHEL	7/2020	4/2022 (-) [4/2022]	228.39 (-) [228.39]	9.72 (0.00) [0]
511	UP-GRADATION TO 2-LANE WITH PAVED SHOULDER FROM KM 20.300 TO KM 29.030 OF 8.730 KM LENGTH ON GOHA-K	7/2020	4/2022 (-) [4/2022]	210.79 (-) [210.79]	10.84 (0.00) [0]
512	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR ROAD SECTION OF NH-144A FROM GANESH VIHA	3/2018	7/2019 (-) [0/0]	253.44 (-) [253.44]	72.23 (0.00) [0]
513	UP-GRADATION TO 4-LANE WITH PAVED SHOULDER OF JAMMU-AKHNOOR SECTION OF NH-144A FROM CANAL HEAD (KM 0	3/2018	8/2018 (-) [0/0]	404.17 (-) [404.17]	203.27 (0.00) [0]
514	WIDENING AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENT FROM	3/2018	11/2018 (-) [0/0]	216.00 (-) [216.00]	96.79 (0.00) [0]
	<u>JHARKHAND</u>				
	<u>Coal</u>				
515	CHITRA EAST (RCE) OCP	8/2018	3/2024 (-) [3/2024]	513.98 (-) [513.98]	134.97 (0.00) [0]
516	CHURI BENTI UG (0.81 MTY)	8/2007	3/2011 (-) [3/2022]	163.51 (-) [163.51]	124.64 (0.00) [132]
517	HURA - C OC (3 MTY)	10/2015	3/2022	359.69	249.15

			(-) [3/2022]	(-) [359.69]	(0.00) [0]
518	KARMA OCP (1.0MTY)	6/2009	3/2014 (-) [3/2022]	162.46 (-) [162.46]	89.27 (0.00) [96]
519	MADHUBAND NLW WASHERY	8/2010	5/2014 (-) [10/2021]	289.45 (-) [289.45]	285.43 (0.00) [89]
520	MAGADH EXPANSION OC(51 MTY)	8/2008	7/2012 (3/2028) [3/2028]	6,964.33 (7,254.37) [7,254.37]	729.50 (290.04) [188]
521	MOONIDIH XV SEAM UG	8/2011	4/2015 (-) [2/2023]	1,230.27 (-) [1,230.27]	493.13 (0.00) [94]
522	MURAI DIH UG TURN-KEY PROJECT	2/2011	4/2014 (-) [4/2023]	339.88 (-) [339.88]	61.16 (0.00) [108]
523	NORTH TISRA AND SOUTH TISRA EXPANSION OCP (6MTY)	2/2014	3/2021 (-) [3/2022]	555.52 (-) [555.52]	5.87 (0.00) [12]
524	NORTH URIMARI EXPANSION OCP	3/2019	3/2023 (-) [3/2023]	1,553.06 (-) [1,553.06]	337.20 (0.00) [0]
525	PACHWARA SOUTH COAL BLOCK	7/2013	8/2022 (-) [9/2023]	1,795.01 (-) [1,795.01]	36.52 (0.00) [13]
526	PATHERDIH 2.5 NLW COAL WASHERY	10/2015	4/2018 (-) [6/2022]	243.00 (334.27) [334.27]	24.70 (91.27) [50]
527	PATHERDIH NLW WASHERY	10/2012	4/2014 (-) [4/2020]	269.82 (-) [269.82]	211.94 (0.00) [0]
528	RAJRAPPA RCE OCP (3.0 MTY)	12/2009	3/2016 (-) [3/2022]	510.85 (-) [510.85]	497.88 (0.00) [72]
529	RECAST EPR AMRAPALI OC	2/2012	3/2020 (3/2028) [3/2028]	4,983.58 (4,983.58) [4,983.58]	258.81 (0.00) [96]
530	TETARIAKHAR EXPANSION OCP	11/2019	3/2023 (-) [3/2023]	243.52 (-) [243.52]	37.16 (0.00) [0]
Department Of Higher Education					
531	2000 BOYS HOSTEL(1000 DOUBLE BEDDED ROOM) AT ISM DHANBAD	9/2012	3/2016 (-) [0/0]	171.86 (-) [171.86]	111.29 (0.00) [0]
532	DEVELOPMENT OF PERMANENT CAMPUS OF IIIT RANCHI AND CONSTRUCTION WORK FOR BUILDING AND OTHER AMNETIES	3/2021	10/2023 (-) [10/2023]	127.26 (-) [188.88]	12.73 (61.62) [0]
Petroleum					
533	120 TMTA NEW LPG PLANT AT BARHI JHARKAND STATE	6/2017	6/2020 (-) [9/2021]	161.50 (-) [161.50]	102.16 (0.00) [15]
534	CGD PROJECT AT BOKARO, HAZARIBAGH AND RAMGARH DISTRICTS	10/2018	12/2029 (-) [12/2029]	613.00 (-) [613.00]	0.00 (0.00) [0]
535	CITY GAS DISTRIBUTION (CGD) NETWORK, RANCHI	10/2017	10/2022 (-) [10/2022]	226.45 (-) [226.45]	124.00 (0.00) [0]
536	CITY GAS DISTRIBUTION, JAMSHEDPUR	10/2017	10/2022 (-) [10/2022]	221.45 (-) [221.45]	99.53 (0.00) [0]

537	DEVELOPMENT PLAN OF CBM - BOKARO BLOCK	12/2015	3/2023 (3/2022) [3/2022]	823.27 (1,137.79) [1,137.79]	709.24 (314.52) [-12]
538	RESITEMENT OF RANCHI AND DHANBAD OLD POL DEPOT AT BOKARO.	11/2018	6/2022 (-) [6/2022]	248.55 (-) [248.55]	126.45 (0.00) [0]
	<u>Power</u>				
539	NORTH KARANPURA STPP (3X660 MW)	2/2014	6/2019 (10/2022) [12/2023]	14,366.58 (-) [15,389.42]	12,083.75 (1,022.84) [54]
540	PAKRI BARWADIH COAL MINING PROJECT	10/2004	10/2017 (-) [0/0]	4,237.96 (4,238.00) [4,552.00]	3,785.00 (314.04) [0]
541	PATRATU STPP-I (3X800MW)	11/2017	3/2023 (-) [2/2025]	18,668.00 (-) [17,112.00]	4,073.68 (-1,556.00) [23]
	<u>Railways</u>				
542	BONDAMUNDA RANCHI DOUBLING	3/2016	3/2021 (-) [12/2023]	1,724.20 (-) [1,724.20]	896.81 (0.00) [33]
543	GARHWA ROAD-RAMNA	3/2015	3/2021 (-) [3/2022]	348.23 (-) [390.00]	366.22 (41.77) [12]
544	KODERMA-RANCHI VIA BARKAKANA (NL), ECR	3/1999	/ (3/2022) [3/2022]	1,033.07 (3,020.95) [3,620.00]	3,614.37 (2,586.93) [-]
545	KODERMA-TILAIYA (NL), ECR	4/2002	/ (3/2023) [3/2023]	459.91 (1,625.87) [1,625.87]	890.81 (1,165.96) [-]
546	MANOHARPUR-BONDAMUNDA 3RD LINE DOUBLING	4/2012	12/2018 (-) [8/2021]	258.20 (-) [358.68]	316.37 (100.48) [32]
547	RAJKHARSWAN- CHAKRADHARPUR 3RD LINE (20 KM) JHARKHAND	4/2012	12/2016 (-) [8/2020]	148.77 (-) [377.00]	203.03 (228.23) [0]
	<u>Road Transport And Highways</u>				
548	4-LANING OF LOHA - WARANGA SECTION OF NH-361 FROM KM. 187.800 TO KM. 244.369 (DESIGN LENGTH 56.569 K	3/2018	/ (3/2021) [0/0]	1,005.08 (1,073.10) [1,005.08]	0.00 (0.00) [0]
549	FOUR LANING OF BARHI - KODERMA SECTION OF NH - 31	1/2018	/ (-) [0/0]	273.46 (-) [276.17]	99.20 (2.71) [0]
550	FOUR LANING OF BARHI-HAZARIBAGH NH-33	8/2016	8/2018 (-) [0/0]	323.72 (-) [336.60]	316.60 (12.88) [0]
551	SIX LANING OF BIHAR - JHARKHAND BORDER (CHORDAHA) TO GORHAR SECTION	1/2018	/ (-) [0/0]	1,155.16 (-) [1,155.16]	474.16 (0.00) [0]
552	TWO/FOUR LANNING WITH PAVED SHOULDERS OF GOVINDPUR (RAIGANJ)-CHAS-WEST BENGAL BORDER SECTION OF NH-	7/2016	/ (-) [0/0]	458.03 (-) [486.00]	406.73 (27.97) [0]
553	WIDENING TO 2 LANE WITH PAVED SHOULDERS AND GEOMETRIC IMPROVEMENT OF NH-114A FROM KM 141 TO KM 184 I	12/2016	9/2021 (-) [9/2021]	196.00 (-) [196.00]	100.31 (0.00) [0]
	<u>Steel</u>				
554	NEW SINTER PLANT AT BOKARO STEEL PLANT	3/2015	10/2017 (12/2021) [11/2022]	1,034.01 (-) [1,034.01]	549.60 (0.00) [61]
555	REBUILDING OF COKE OVEN BATTERY NO-8 AT BSL	11/2016	6/2019 (8/2021) [10/2021]	262.87 (-) [262.87]	199.74 (0.00) [28]

	<u>KARNATAKA</u>				
	<u>Defence Production</u>				
556	RESIDENTIAL QUATERS FOR HAL,BANGLORE	12/2016	2/2020 (10/2021) [12/2021]	246.31 (210.00) [210.00]	136.16 (-36.31) [22]
	<u>Department Of Higher Education</u>				
557	CONSTRUCTION OF PERMANENT CAMPUS FOR INDIAN INSTITUTE OF TECHNOLOGY, DHARWAD (PHASE 1A)	7/2019	3/2022 (-) [9/2022]	851.00 (851.00) [851.00]	26.10 (0.00) [6]
	<u>Petroleum</u>				
558	BSVI UPGRADATION	9/2016	12/2019 (4/2021) [2/2022]	1,810.00 (1,810.00) [1,810.00]	1,728.12 (0.00) [26]
559	CONSTRUCTION OF 80000MT LPG CAVERN AT MANGALORE	12/2018	12/2022 (-) [12/2022]	854.00 (-) [854.00]	161.21 (0.00) [0]
560	DEVANGONTHI MARKETING TERMINAL	6/2020	6/2023 (8/2023) [8/2023]	200.00 (-) [200.00]	2.54 (0.00) [2]
561	HASSAN CHERLAPALLI LPG PIPELINE	6/2019	6/2022 (-) [6/2022]	2,166.38 (-) [2,166.38]	1,199.32 (0.00) [0]
562	RESITEMENT OF RAICHUR DEPOT TO GULBARGA	10/2018	3/2021 (-) [10/2021]	206.26 (-) [206.26]	149.39 (0.00) [7]
563	SEA WATER DESALINATION PLANT	11/2017	3/2020 (11/2020) [11/2021]	581.00 (637.00) [637.00]	519.50 (56.00) [20]
564	SETTING UP OF PHASE LL FACILITIES FOR HPCL GREEN R AND D CENTRE AT BENGALURU	6/2018	11/2021 (-) [11/2021]	380.00 (-) [380.00]	263.70 (0.00) [0]
	<u>Power</u>				
565	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE-II (PART-B)	5/2017	2/2019 (-) [0/0]	445.89 (-) [675.73]	372.58 (229.84) [0]
	<u>Railways</u>				
566	ARSIKERE-TUMKUR	3/2015	3/2020 (11/2021) [11/2021]	578.00 (-) [760.00]	639.39 (182.00) [20]
567	BAGALKOT-KUDACHI NL	4/2010	3/2016 (-) [12/2026]	986.30 (-) [1,530.09]	311.40 (543.79) [129]
568	BANGLORE - SATYAMANGALAM (NL)(SWR)	4/1996	3/2002 (-) [3/2024]	1,382.78 (-) [1,960.00]	7.35 (577.22) [264]
569	CHIKBALLA-PUR-GOWRIBIDANUR NL	4/2013	/ (-) [12/2023]	327.25 (-) [327.25]	0.00 (0.00) [-]
570	CHIKBALLA-PUR-PUTTAPARTHY-SRI SATYA SAI NILAYAM NL	4/2013	/ (-) [12/2023]	558.00 (-) [692.00]	0.00 (134.00) [-]
571	GADAG-WADI NL	4/2013	12/2018 (-) [6/2025]	2,841.84 (-) [2,841.84]	362.40 (0.00) [78]
572	HOSPET-HUBLI-LONDA-VASCODAGAMA DL	4/2010	3/2023 (-) [12/2022]	2,127.00 (-) [3,000.00]	1,921.53 (873.00) [-3]
573	HUBLI- CHIKJAJUR	3/2015	3/2020 (-) [3/2023]	1,156.94 (-) [1,800.59]	1,128.98 (643.65) [36]
574	HUBLI-ANKOLA(NL),SWR	4/1997	/	2,315.00	157.01

			(-) [12/2024]	(103.74) [5,174.30]	(2,859.30) [-]
575	KADUR CHIKMAGALUR SAKLESHPUR NEW LINE (93 KM)	3/1996	3/2017 (-) [3/2025]	644.78 (889.00) [731.77]	465.72 (86.99) [96]
576	MARIKUPPAM - KUPPAM	4/2012	3/2016 (-) [12/2023]	279.54 (-) [279.54]	36.82 (0.00) [93]
577	SHIMOGA-HARIHAR NL	4/2011	3/2016 (-) [3/2024]	832.47 (-) [832.47]	0.94 (0.00) [96]
578	TORANAGALLU-RANJITPURA DL	4/2011	/ (-) [12/2023]	146.75 (-) [167.50]	0.34 (20.75) [-]
579	TUMKUR-CHITRADURGA-DAVENGERE NL	4/2011	/ (-) [12/2023]	1,801.01 (-) [2,161.36]	76.42 (360.35) [-]
580	WHITE FIELD-KOLAR NL	4/2011	/ (-) [12/2025]	348.85 (-) [348.85]	0.36 (0.00) [-]
	<u>Road Transport And Highways</u>				
581	HOSPET-BELLARY-KARNATAKA AP BORDER	8/2016	3/2019 (1/2021) [9/2022]	1,167.42 (-) [870.00]	334.82 (-297.42) [42]
582	2 LANING WITH PAVED SHOULDER FROM KM 30.800 TO KM 70.800 AND 2 LANING WITHOUT PAVED SHOULDER FROM KM	2/2018	/ (-) [0/0]	486.78 (-) [486.78]	171.98 (0.00) [0]
583	4-LANING OF GOA/KARNATAKA BORDER-KUNDAPUR SECTION	5/2014	8/2016 (-) [12/2020]	1,655.01 (-) [1,655.01]	1,867.51 (0.00) [0]
584	4-LANNING EXISTING KM 189.700 TO 237.00] HASSAN TO MARANAHALLY	3/2016	3/2019 (-) [3/2022]	701.40 (-) [701.40]	146.05 (0.00) [36]
585	4-LANNING EXISTING KM 263.00 TO 328.00] ADDAHOLE TO BANTAWAL	3/2016	3/2019 (-) [11/2020]	870.00 (-) [870.00]	36.30 (0.00) [0]
586	CONSTRUCTION OF MAJOR BRIDGE ACROSS SHARAVATHI BACKWATERS AND APPROCHES BETWEEN AMBARGODU AND KALASA	3/2019	12/2019 (-) [12/2019]	423.15 (-) [423.15]	157.00 (0.00) [0]
587	CONSTRUCTION OF MAJOR BRIDGE AT KM 180.865 ACROSS RIVER KRISHNA ON NH-167 HAGARI – JADERCELA SECTION	2/2017	5/2019 (-) [0/0]	157.32 (188.00) [157.32]	0.28 (0.00) [0]
588	ESTIMATE FOR WIDENING TWO LANE TO FOUR LANE FROM FROM KM.129.00 TO 144.00 OF NH-63 ANKOLA-GOOTY SECT	5/2018	5/2018 (-) [0/0]	171.60 (-) [171.60]	74.83 (0.00) [0]
589	FOUR LANING OF HOSPET - CHITRADURGA	3/2015	8/2018 (-) [0/0]	1,388.00 (-) [1,388.00]	1,311.00 (0.00) [0]
590	FOUR LANNING OF HUBLI-HOSPET SECTION OF NH-63 FROM KM. 129.249 PHASE-IVB	8/2016	4/2020 (-) [12/2020]	1,664.20 (-) [1,664.20]	1,110.25 (0.00) [0]
591	HUNGUND-SURATHKAL AND MANGALORE-KNT/KERALA BORDER	9/2010	6/2018 (-) [0/0]	946.00 (-) [946.00]	818.53 (0.00) [0]
592	IMPROVEMENT AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 489.845 (NEW KM.58.125) AN	3/2018	10/2018 (-) [0/0]	325.86 (-) [386.41]	341.72 (60.55) [0]
593	IMPROVEMENTS AND RECONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS FROM KM 243.20 TO KM 290.20 OF NH	8/2016	2/2017 (-) [0/0]	175.50 (-) [175.50]	162.58 (0.00) [0]
594	RECONSTRUCTION TO TWO LANE WITH PAVED	3/2018	6/2019	159.97	38.24

	SHOULDERS FROM DS. CH. 442+180 (EX. KM 448.00) TO DS. CH.485+2		(-) [0/0]	(-) [159.97]	(0.00) [0]
595	SIX LANING OF CHITRADURGA-DAVANGERE INCLUDING CHITRADURGA BYPASS(KM 189+000 TO KM 260+000 OF NH-48(O	3/2017	3/2020 (-) [0/0]	993.16 (-) [1,434.00]	1,310.52 (440.84) [0]
596	SIX LANING OF DAVANGERE-HAVERI FROM KM 260+000 TO KM 338+923 OF NH-48(OLD NH-4) STATE OF KARNATAKA	3/2017	3/2020 (-) [0/0]	831.58 (-) [1,177.00]	912.41 (345.42) [0]
597	SIX LANING OF NIDAGATTA-MYSORE SECTION, KM 74.20 TO KM 135.304 OF NH-275, IN THE STATE OF KARNATAKA	2/2018	/ (-) [0/0]	2,177.80 (-) [2,450.00]	2,425.12 (272.20) [0]
598	SIX-LANING OF BANGALORE – NIDAGATTA SECTION, KM 18.000 TO KM 74.200 OF NH-275 IN THE STATE OF KARNAT	2/2018	/ (-) [11/2021]	1,995.34 (-) [2,400.00]	3,368.89 (404.66) [-]
599	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM.106.00 TO 153.00 OF NH-218 BIJAP	3/2015	11/2015 (-) [0/0]	165.67 (-) [165.67]	116.49 (0.00) [0]
600	TWO/FOUR LANNING OF BRT TIGER RESERVE BOUNDARY TO BANGALORE SECTION OF NH-209(EXISTING CHAINAGE FROM	9/2016	8/2019 (-) [0/0]	950.69 (1,918.36) [1,108.00]	1,462.10 (157.31) [0]
601	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 0 TO 54 OF NH-50 UNDER EPC MODE IN THE STATE OF KARN	10/2016	3/2017 (-) [0/0]	396.96 (-) [396.96]	276.73 (0.00) [0]
602	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 34.00 TO 70.900 OF NH-150 UNDER EPC MODE IN THE STAT	11/2016	3/2017 (-) [0/0]	314.90 (-) [314.90]	208.97 (0.00) [0]
603	WIDENING TO 2 LANE WITH PAVED SHOULDERS FROM KM 79.65 TO 118.47 OF NH-150 UNDER EPC MODE IN THE STAT	8/2016	2/2017 (-) [0/0]	329.01 (-) [329.01]	238.10 (0.00) [0]
604	WIDENING TO 2-LANE WITH PAVED SHOULDER FROM KM. 544.20 TO 594.00 (HOSAMANE CROSS TO PANDAVAPURA) SECT	1/2017	9/2017 (-) [9/2017]	264.34 (-) [264.34]	0.00 (0.00) [0]
605	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 194.900 TO KM 243.200 OF NH-234 BANAVARA-HULIYAR	9/2017	10/2018 (-) [0/0]	191.60 (-) [191.60]	110.74 (0.00) [0]
606	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 4.40 TO KM 56.00 OF NH-218 BIJAPURA-HUBLI SECTION U	1/2017	8/2017 (-) [0/0]	291.49 (-) [291.49]	219.48 (0.00) [0]
607	WIDENING TO TWO LANE WITH PAVED SHOULDER FROM KM 544.200 TO KM 594.000 OF NH-150A HOSMANE CROSS – PA	1/2017	9/2017 (-) [0/0]	166.67 (-) [166.67]	184.91 (0.00) [0]
608	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM 24.600 TO 70.063 OF MUDIGERE TO KADUR SECTION OF NH-	12/2017	1/2019 (-) [0/0]	297.30 (-) [318.28]	168.33 (20.98) [0]
609	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 20.150 TO KM 40.00 OF BC ROAD KOTTIGEHARA SECTION	1/2018	7/2018 (-) [0/0]	159.70 (-) [159.70]	112.10 (0.00) [0]
610	WIDENING TWO LANE WITH PAVED SHOULDERS FROM FROM KM.56.00 TO 106.00 OF NH-218 (218-KNT-2014-15-775)	3/2015	1/2016 (-) [0/0]	159.12 (-) [159.12]	0.00 (0.00) [0]
Urban Development					
611	BANGALORE METRO RAIL PROJECT PHASE-2	2/2014	2/2019 (-) [3/2025]	26,405.14 (30,695.12) [30,695.12]	18,226.61 (4,289.98) [73]
KERALA					
Department Of Higher Education					
612	C/O PERMANENT CAMPUS OF IIT PALAKKAD PHASE IA AT PUDESSERY VILLAGE,KANJIKODE WEST, DISTRICT PALAKKA	7/2019	3/2021 (-) [6/2022]	753.63 (-) [753.63]	58.47 (0.00) [15]
613	CONSTRUCTION OF MEGA HOSTEL II FOR NIT CALICUT KERALA	1/2010	10/2012 (-)	165.23 (-)	118.52 (0.00)

			[0/0]	[165.23]	[0]
	<u>Health And Family Welfare</u>				
614	C/O NEW HOSPITAL BLOCK FOR SREE CHITRA TIRUNAL INSTITUTE OF MEDICAL SCIENCE AND TECHNOLOGY (SCTIMST)	9/2017	3/2020 (-) [12/2021]	150.29 (-) [150.29]	52.74 (0.00) [21]
	<u>Petroleum</u>				
615	KOCHI SALEM LPG PIPELINE PROJECT	12/2015	6/2019 (-) [2/2022]	1,112.00 (1,507.24) [1,507.24]	769.00 (395.24) [32]
616	LPG TERMINAL AT KOCHI	10/2015	10/2017 (3/2022) [3/2022]	607.06 (-) [1,236.00]	437.75 (628.94) [53]
617	PROPYLENE DERIVATIVES PETROCHEMICAL PROJECT(PDPP) AT KOCHI REFINERY	11/2014	8/2018 (11/2019) [9/2021]	4,588.29 (5,245.96) [5,245.96]	5,184.50 (657.67) [37]
618	SETTING UP OF FACILITIES FOR PRODUCTION OF POLYOLS, PROPYLENE GLYCOL AND MONO ETHYLENE GLYCOL AT KOC	9/2018	3/2023 (-) [3/2023]	11,130.00 (-) [11,130.00]	422.60 (0.00) [0]
	<u>Power</u>				
619	KAYAMKULAM SOLAR 70 MW	9/2019	6/2021 (12/2021) [12/2021]	403.62 (-) [403.62]	100.92 (0.00) [6]
	<u>Railways</u>				
620	ANGAMALI-SABARIMALA (N.L.)(SR)	10/1998	/	1,566.00	0.00
			(-)	(-)	(1,249.62)
			[0/0]	[2,815.62]	[0]
621	ERNAKULAM-KUMBALAM	4/2010	/	189.24	0.00
			(-)	(-)	(85.97)
			[0/0]	[275.21]	[0]
622	KUMBALAM-TURAVUR	4/2011	/	252.96	0.00
			(-)	(-)	(116.59)
			[0/0]	[369.55]	[0]
623	PALAKKAD - SETTING UP OF RAIL COACH FACTORY	2/2012	3/2016	550.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[550.00]	[0]
624	TRIVANDRUM-KANYAKUMARI DOUBLING	2/2015	/	1,431.90	0.00
			(-)	(-)	(0.00)
			[0/0]	[1,431.90]	[0]
625	TURAVUR-AMBALAPUZHA DOUBLING	2/2015	/	1,000.00	0.00
			(-)	(-)	(246.00)
			[0/0]	[1,246.00]	[0]
	<u>Road Transport And Highways</u>				
626	4 LANING OF KAZHAKKOTTAM TO MUKKOLA SECTION OF NH-47	6/2015	/	845.24	881.72
			(1/2020)	(-)	(95.76)
			[1/2020]	[941.00]	[0]
627	4 LANNING OF MUKKOLA JUNCTION TO KERALA/ TAMIL NADU BORDER FROM KM 26.500 TO KM 43.000 OF NH-47 IN T	4/2016	6/2018	804.97	561.12
			(-)	(-)	(0.00)
			[0/0]	[804.97]	[0]
628	4-LANNING OF THALSERRY -MAHE BYPASS	9/2017	9/2017	1,124.11	628.26
			(-)	(-)	(108.65)
			[0/0]	[1,232.76]	[0]
629	6-LANING OF KOZHIKODE BYPASS (CALICUT BYPASS) (I.E. VENGALAM JN. TO RAMANATTUKARA JN.) SECTION OF NH	2/2018	/	1,424.77	14.19
			(-)	(-)	(428.65)
			[0/0]	[1,853.42]	[0]
630	CONSTRUCTION OF 6.80 KM 2 LANE WITH PAVED SHOULDERS ALAPPUZHA BYPASS ON NH47 NEW NH 66 FROM KM 408.1	1/2014	9/2017	255.75	314.12
			(-)	(348.00)	(92.68)
			[0/0]	[348.43]	[0]
631	SIX LANNING OF VADAKKANCHERRY THRISSURESECTION KM 240 270KM	2/2010	8/2012	617.00	0.00
			(-)	(-)	(0.00)
			[0/0]	[617.00]	[0]
632	WIDENING TO 2 LANES WITH PAVED SHOULDERS FROM	2/2017	8/2017	294.28	126.74

	KM.87/000 TO 133/720 (NATTUKAL TO THANAU JN. IN PALAKK)		(-) [0/0]	(-) [294.26]	(-0.02) [0]
633	WIDENING TO 2-LANE WITH PAVED SHOULDERS FROM KM 119/017 TO KM 161/300 ON NH 85 (OLD NH 49)	2/2017	9/2017 (-) [0/0]	380.76 (-) [380.76]	238.42 (0.00) [0]
	<u>Urban Development</u>				
634	KOCHI METRO RAIL PROJECT	7/2012	7/2017 (9/2020) [0/0]	5,181.79 (-) [6,218.14]	6,059.17 (1,036.35) [0]
	<u>LADAKH</u>				
	<u>Civil Aviation</u>				
635	CONSTRUCTION OF TERMINAL BUILDING AND ASSOCIATED WORKS AT LEH AIRPORT	7/2018	9/2021 (-) [12/2022]	346.27 (-) [480.33]	105.53 (134.06) [15]
	<u>Road Transport And Highways</u>				
636	KARGIL-ZANSKR PACKAGE-1	3/2021	1/2023 (-) [1/2023]	384.23 (-) [384.23]	0.00 (0.00) [0]
637	KARGIL-ZANSKR PACKAGE-2	3/2021	1/2023 (-) [1/2023]	404.89 (-) [404.89]	0.00 (0.00) [0]
638	KARGIL-ZANSKR PACKAGE-3	8/2020	1/2023 (-) [1/2023]	381.01 (-) [381.01]	0.00 (0.00) [0]
639	KARGIL-ZANSKR PACKAGE-5	8/2020	12/2023 (-) [12/2023]	169.79 (-) [169.79]	19.50 (0.00) [0]
640	KARGIL-ZANSKR PACKAGE-6	1/2021	5/2024 (-) [5/2024]	239.81 (-) [239.81]	23.77 (0.00) [0]
641	KARGIL-ZANSKR PACKAGE-7	1/2021	6/2024 (-) [6/2024]	308.86 (-) [308.86]	9.46 (0.00) [0]
642	KARGIL-ZANSKR PACKAGE-8	3/2021	1/2023 (-) [1/2023]	398.37 (-) [398.37]	0.00 (0.00) [0]
	<u>MADHYA PRADESH</u>				
	<u>Civil Aviation</u>				
643	UPGRADATION OF JABALPUR AIRPORT	6/2016	6/2021 (-) [12/2022]	412.24 (-) [412.24]	204.49 (0.00) [18]
	<u>Coal</u>				
644	AMADAND OPENCAST EXPANSION PROJECT	3/2016	3/2021 (-) [3/2022]	869.44 (-) [869.44]	126.15 (0.00) [12]
645	AMRITDHARA OC PROJECT	2/2015	3/2023 (-) [3/2027]	481.60 (-) [481.60]	0.00 (0.00) [48]
646	BATURA HIGHWALL PROJECT	7/2015	3/2022 (-) [3/2025]	231.92 (-) [231.92]	1.78 (0.00) [36]
647	BATURA WEST OC PROJECT (0.80 MTPA)	3/2021	3/2028 (-) [3/2028]	496.28 (-) [496.28]	0.00 (0.00) [0]
648	BLOCK-B EXPANSION OPENCAST PROJECT	7/2019	3/2023 (-) [3/2023]	998.71 (-) [998.71]	0.00 (0.00) [0]
649	DUDHICHUA EXPANSION OCP (10 TO 20 MTPA)	11/2017	3/2022 (-) [3/2023]	1,255.17 (-) [1,255.17]	230.12 (0.00) [12]
650	GANDHIGRAM UG MINE	8/2019	3/2026	414.16	1.00

			(-) [3/2026]	(-) [414.16]	(0.00) [0]
651	JAYANT EXPANSION OCP 10 TO 20 MTPA	5/2017	3/2021 (-) [3/2022]	1,783.09 (-) [1,783.09]	738.88 (0.00) [12]
652	KANCHAN OC EXPANSION	12/2014	3/2021 (-) [3/2024]	371.04 (-) [371.04]	66.44 (0.00) [36]
653	NIGAHI EXPANSION OCP (15 TO 25 MTPA)	11/2020	3/2025 (-) [3/2025]	1,729.68 (-) [1,729.68]	0.00 (0.00) [0]
654	RAJNAGAR OCP RPR (1.70 MTY)	12/2014	3/2021 (4/2024) [4/2024]	357.80 (-) [357.80]	100.65 (0.00) [37]
655	RPR FOR JAMUNIA UG (0.90 MTY)	7/2016	3/2022 (3/2026) [3/2026]	281.25 (-) [281.25]	18.24 (0.00) [48]
656	SEMARIA OPENCAST PROJECT	5/2019	3/2026 (-) [3/2026]	396.58 (-) [396.58]	0.00 (0.00) [0]
657	VISHNUPURI UG TO OC MINE	7/2018	3/2025 (-) [3/2025]	195.57 (-) [195.57]	2.94 (0.00) [0]
	<u>Petroleum</u>				
658	CGD PROJECT AT REWA DISTRICT	10/2018	2/2027 (-) [2/2027]	177.00 (-) [177.00]	0.00 (0.00) [0]
659	PROVISION OF 2ND SPUR FOR TWL GANTRY, TWD FACILITY FOR MS AND HSD, ADDITIONAL TANKS FOR MS,HSD AND	8/2017	6/2020 (9/2021) [9/2021]	236.00 (319.61) [319.61]	195.28 (83.61) [15]
	<u>Power</u>				
660	AMELIA COAL MINE	1/2017	9/2020 (8/2022) [8/2022]	2,104.21 (-) [1,587.16]	592.99 (-517.05) [23]
	<u>Railways</u>				
661	ANUPPUR-KATNI	4/2015	12/2021 (-) [12/2023]	1,370.00 (-) [1,370.94]	0.00 (0.94) [24]
662	BINA - KOTA DOUBLING WITH RE	4/2011	12/2020 (-) [12/2021]	1,485.85 (-) [1,835.83]	1,270.60 (349.98) [12]
663	CHHINDWARA - NAGPUR (GC)(SECR)	4/2005	/ (8/2020) [8/2020]	383.79 (1,413.76) [1,511.50]	1,430.54 (1,127.71) [0]
664	CHHINDWARA NAINPUR MANDLA FORT GAUGE CONVERSION PROJECT	4/2010	2/2019 (12/2021) [12/2021]	585.93 (1,268.32) [1,268.32]	1,058.10 (682.39) [34]
665	INDORE-DEWAS-UJJAIN (80 KMS)	4/2016	6/2020 (3/2023) [3/2023]	700.00 (603.69) [603.69]	314.13 (-96.31) [33]
666	KATNI - SINGRAULI DOUBLING PROJECT	12/2015	3/2020 (-) [3/2024]	1,763.93 (-) [2,470.00]	1,244.18 (706.07) [48]
667	KATNI GRADE SEPARATOR/BYE PASS	8/2016	3/2022 (-) [3/2023]	582.13 (1,247.64) [1,247.64]	415.54 (665.51) [12]
668	KATNI-BINA 3RD LINE (263 KM)	6/2016	3/2022 (-) [3/2023]	2,478.23 (-) [2,478.23]	477.93 (0.00) [12]
669	MULTI MODAL LOGISTICS PARK AT TIHI	12/2015	3/2019 (-)	174.00 (-)	172.08 (0.00)

			[0/0]	[174.00]	[0]
670	RAMGANJMUNDI-BHOPAL (NL),WCR	4/2001	3/2021 (3/2024) [3/2024]	424.60 (-) [2,909.99]	1,282.25 (2,485.39) [36]
671	RATLAM-MHOW-KHANDWA-AKOLA (GC)	4/2008	3/2022 (3/2024) [3/2024]	3,503.69 (5,839.02) [6,171.08]	2,301.98 (2,667.39) [24]
	Road Transport And Highways				
672	2L+PS OF THIKRI ANJAD SECTION OF NH-347B	11/2017	7/2018 (8/2021) [12/2021]	249.05 (-) [249.05]	198.83 (0.00) [41]
673	4-LANING OF DEWAS-UJJAIN OF SECTION NH-148 NG FROM KM 0+000 TO KM 41.42 IN MP ON HAM MODE	11/2019	7/2021 (-) [7/2021]	716.00 (-) [716.00]	0.00 (0.00) [0]
674	ANJANGAON TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	359.00 (359.00) [359.00]	315.85 (0.00) [0]
675	BALANCE WORK FOR FOUR LANING OF ITARSI TO BETUL SECTION OF NH69 FROM KM 63.000 TO KM 137.00 (DESIGN	12/2017	/ (-) [8/2021]	950.27 (-) [950.27]	266.64 (0.00) [-]
676	BALANCE WORK FOR REHABILITATION AND UPGRADATION OF SATNA-BELA SECTION OF NH-75 FROM KM. 155.0 TO KM.	11/2017	3/2018 (6/2021) [10/2021]	392.33 (428.55) [428.55]	379.29 (36.22) [43]
677	BALANCE WORK OF 2-LANE WITH PAVED SHOULDER OF BHOPAL-SANCHI SECTION	8/2016	1/2019 (-) [0/0]	227.49 (-) [227.49]	0.00 (0.00) [0]
678	BALANCE WORK OF 4-LANNING OF LALGHATI TO MUBARAKPUR OF NH-12	9/2017	9/2017 (-) [0/0]	374.40 (-) [204.65]	313.11 (-169.75) [0]
679	BALANCE WORK OF 4-LANNING OF OBEDULLAGANJ TO ITARSI SECTION OF NH-69	9/2017	9/2017 (-) [0/0]	990.61 (-) [990.61]	664.13 (0.00) [0]
680	BARELA-MANDLA SECTION OF NH-12A IN MADHYA PRADESH KM 22/8 TO KM 89/6 OF NH-12A	6/2015	/ (3/2021) [12/2021]	390.51 (-) [390.51]	271.94 (0.00) [-]
681	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BANI VILLAGE TO BARDAWADI V	12/2017	/ (-) [11/2022]	656.98 (-) [840.00]	223.00 (183.02) [-]
682	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM BARDAWADI VILLAGE TO MANDSA	10/2019	/ (-) [12/2021]	743.88 (-) [743.89]	407.00 (0.01) [-]
683	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM JODMI VILLAGE TO BANI VILLA	12/2017	/ (-) [2/2022]	1,094.97 (-) [1,094.97]	737.00 (0.00) [-]
684	CONSTRUCTION OF EIGHT LANE ACCESS CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RAJASTHAN/MP BORDER TO JODM	12/2017	/ (-) [10/2022]	217.96 (-) [884.00]	443.00 (666.04) [-]
685	CONSTRUCTION OF ROAD FROM KM. 1 TO KM. 49/4 OF NH-26A IN THE STATE OF MADHYA PRADESH.	1/2017	3/2017 (6/2021) [12/2021]	205.05 (-) [205.05]	126.89 (0.00) [57]
686	CONSTRUCTION TO TWO LANE WITH PAVED SHOULDERS WITH FLEXIBLE PAVEMENT ON KHALGHAT TO SARWARDEWLA ROAD	1/2019	3/2021 (11/2021) [11/2021]	264.50 (-) [264.50]	106.37 (0.00) [8]
687	FOUR LANING OF GUNA TO BIAORA SECTION OF NH-3 FROM KM 332.100 TO KM. 426.100 IN THE STATE OF MADHYA	6/2015	3/2016 (-) [0/0]	1,012.90 (-) [1,012.90]	226.10 (0.00) [0]
688	FOUR LANING OF GWALIOR-SHIVPURI	5/2013	11/2015 (-) [0/0]	1,055.00 (-) [1,601.77]	1,393.40 (546.77) [0]
689	FOUR LANING OF JABALPUR - LAKHNADON	3/2015	/ (-)	928.83 (-)	867.83 (0.00)

			[0/0]	[928.83]	[0]
690	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -I	3/2015	/	794.30	669.35
			(-)	(-)	(-102.92)
			[0/0]	[691.38]	[0]
691	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -II	3/2015	/	795.76	669.94
			(-)	(-)	(-109.63)
			[0/0]	[686.13]	[0]
692	FOUR LANING OF REWA - KATNI - JABALPUR - PACKAGE -IV	3/2015	/	810.22	742.47
			(-)	(-)	(0.00)
			[0/0]	[810.22]	[0]
693	FOUR LANNING BALANCE WORK FOR BHOPAL-BIAORA SECTION OF NH-12 FROM MUBARAKPUR TO BIAORA FROM KM 124.	10/2017	10/2017	639.97	484.15
			(-)	(-)	(0.00)
			[0/0]	[639.97]	[0]
694	FOUR LANNING WORK FROM HIRAN RIVER TO SINDOOR RIVER	1/2018	/	770.73	409.98
			(-)	(-)	(0.00)
			[0/0]	[770.73]	[0]
695	GOHARGANJ TO BHOPAL SECTION OF NH-12 IN MADHYA PRADESH KM 43 TO 93	12/2015	2/2020	957.54	765.48
			(4/2021)	(-)	(0.00)
			[9/2021]	[957.54]	[19]
696	INDORE-DEWAS(NH-3)	11/2010	5/2013	325.00	469.54
			(-)	(-)	(150.00)
			[0/0]	[475.00]	[0]
697	INDORE-JHABUA-GUJRAT/MP	10/2010	4/2013	1,175.00	1,509.96
			(-)	(-)	(0.00)
			[0/0]	[1,175.00]	[0]
698	JABALPUR TO HIREN RIVER SECTION OF NH-12 IN MADHYA PRADESH KM 11/400 TO 66/400	11/2015	1/2020	628.45	445.35
			(6/2021)	(-)	(0.00)
			[9/2021]	[628.45]	[20]
699	MANGAWA-MP/UP BORDER SECTION OF NH-27 (4L) IN MP	1/2012	4/2015	410.72	392.42
			(-)	(-)	(0.00)
			[0/0]	[410.72]	[0]
700	PACKAGE-21 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM KAMLIYA VILLAGE	2/2019	12/2019	990.97	690.00
			(-)	(-)	(0.00)
			[12/2021]	[990.97]	[24]
701	PACKAGE-23 CONSTRUCTION OF DELHI-VADODARA EIGHT LANE ACCESS- CONTROLLED EXPRESSWAY FROM BAWDI VILLAG	3/2019	5/2020	1,047.00	486.00
			(-)	(-)	(0.00)
			[5/2022]	[1,047.00]	[24]
702	PACKAGE-24 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM RANNI VILLAGE TO	2/2019	3/2020	847.00	498.00
			(-)	(-)	(0.00)
			[4/2022]	[847.00]	[25]
703	PACKAGE-25 CONSTRUCTION OF EIGHTLANE ACCESS-CONTROLLED EXPRESSWAY CARRIAGEWAY FROM MIYATI VILLAGE T	2/2019	3/2020	996.27	560.00
			(-)	(-)	(0.00)
			[0/0]	[996.27]	[0]
704	REHABILITATION AND UP-GRADATION OF EXISTING INTERMEDIATE LANE FLEXIBLE PAVEMENT TO 2L+PS FLEXIBLE PA	2/2018	3/2018	169.63	52.44
			(4/2021)	(-)	(0.00)
			[4/2022]	[169.63]	[49]
705	REHABILITATION AND UPGRADATION OF BARELI TO GOHARGANJ SECTION OF NH-12 FROM EXISTING KM 193/0 TO KM	3/2016	6/2019	877.79	741.88
			(4/2021)	(-)	(0.00)
			[12/2021]	[877.79]	[30]
706	REHABILITATION AND UPGRADATION OF SINDOOR RIVER TO START OF BARELI BYPASS SECTION OF NH-12 FROM EXIS	1/2016	7/2018	809.16	615.21
			(5/2021)	(-)	(0.00)
			[11/2021]	[809.16]	[40]
707	UMARIYA TO SHAHDOL SECTION OF NH-78 IN MADYA PRADESH KM 68/4 TO 142/200	3/2015	8/2017	511.83	387.81
			(6/2021)	(-)	(0.00)
			[12/2022]	[511.83]	[64]
708	UPGRADATION OF BIAORA-MAKSUDANGARH ROAD TO 2L + PS	11/2017	2/2018	254.17	175.37
			(3/2022)	(-)	(0.00)
			[3/2022]	[254.17]	[49]
709	UPGRADATION OF DABOH-UP BORDER ROAD TO 2L + PS	3/2018	3/2018	233.04	165.60
			(10/2021)	(-)	(0.00)
			[10/2021]	[233.04]	[43]

710	UPGRADATION OF MAKSUDANGARH-SIRONJ ROAD TO 2L + PS	2/2018	3/2018 (11/2021) [11/2021]	279.44 (-) [279.44]	203.95 (0.00) [44]
711	UPGRADATION OF MORENA-PORSA ROAD TO 2L + PS	3/2018	8/2018 (8/2021) [9/2021]	166.21 (-) [173.41]	154.26 (7.20) [37]
712	UPGRADATION OF PACHORE- SHUJALPUR ROAD TO 2L + PS	11/2017	2/2018 (9/2021) [9/2021]	184.62 (-) [184.62]	125.42 (0.00) [43]
713	UPGRADATION OF PAWAI-SALEHA-JASSO-NAGOD ROAD TO 2L + PS	3/2018	3/2018 (9/2021) [6/2022]	214.69 (-) [214.69]	78.48 (0.00) [51]
714	UPGRADATION OF PORSA-BHIND ROAD TO 2L + PS	3/2018	8/2018 (9/2021) [9/2021]	217.22 (-) [226.88]	173.03 (9.66) [37]
715	UPGRADATION OF REWA-SIRMOUR ROAD TO 2L + PS	3/2018	3/2018 (10/2021) [10/2021]	162.56 (-) [162.56]	137.02 (0.00) [43]
716	WIDENING TO 2 LANE PS WITH RECONSTRUCTION OF BRIDGES CULVERT IN KM. 182 TO 266 OF NH-59A	1/2017	9/2019 (6/2021) [9/2021]	373.82 (-) [373.82]	232.63 (0.00) [24]
	<u>Urban Development</u>				
717	BHOPAL METRO RAIL	11/2018	2/2023 (-) [2/2023]	6,941.40 (-) [6,941.40]	228.95 (0.00) [0]
718	INDORE METRO RAIL	11/2018	2/2023 (-) [2/2023]	7,500.80 (-) [7,500.80]	138.49 (0.00) [0]
	<u>MAHARASHTRA</u>				
	<u>Civil Aviation</u>				
719	CONSTRUCTION OF NEW INTEGRATED TERMINAL BUILDING, RECONSTRUCTION OF OLD TERMINAL BUILDING, MODIFICAT	3/2017	4/2021 (-) [8/2022]	475.39 (-) [475.39]	162.78 (0.00) [16]
	<u>Coal</u>				
720	ADASA UG TO OC	8/2015	3/2023 (-) [3/2024]	288.90 (333.43) [333.43]	145.08 (44.53) [12]
721	AMALGAMATED GONDEGAON GHATROHAN OC	2/2016	3/2019 (-) [3/2022]	198.68 (325.18) [325.18]	272.90 (126.50) [36]
722	AMALGAMATED PAUNI-II III OC MINE	6/2015	3/2021 (-) [3/2021]	483.69 (499.00) [499.00]	253.70 (15.31) [0]
723	AMALGAMATED YEKONA-I YEKONA-II	8/2015	3/2025 (-) [3/2025]	727.28 (745.03) [745.03]	390.11 (17.75) [0]
724	BELLORA-NAIGAON DEEP OC	11/2018	3/2021 (-) [9/2022]	252.71 (-) [252.71]	102.41 (0.00) [18]
725	BHANEGAON OC	2/2015	3/2023 (-) [3/2023]	187.94 (409.68) [409.68]	86.90 (221.74) [0]
726	BHATADI EXPANSION OC MINE	2/2016	3/2019 (-) [3/2022]	304.52 (327.41) [327.41]	160.84 (22.89) [36]
727	GHONSA EXPANSION DEEP OC	3/2021	3/2028 (-) [3/2028]	241.72 (-) [241.72]	57.00 (0.00) [0]
728	KOLAR PIMPRI EXTENSION OC	3/2017	3/2020 (9/2022) [9/2022]	362.73 (402.90) [402.90]	336.00 (40.17) [30]

729	NEW MAJRI UG TO OC	5/2015	3/2019 (3/2022) [3/2022]	295.56 (299.67) [299.67]	164.36 (4.11) [36]
730	PR FOR DINESH(MAKARDHOKRA III) EXPANSION OC (8.0 MTY)	11/2014	3/2020 (3/2027) [3/2027]	1,184.33 (-) [1,184.33]	392.88 (0.00) [84]
731	REVISED PR FOR AMALGAMATED INDER KAMPTEE DEEP OC (3.2 MTY)	11/2015	3/2021 (3/2024) [3/2024]	313.34 (-) [313.34]	149.32 (0.00) [36]
732	RPR FOR MUNGOLI NIORGUDA EXTENSION (DEEP) OC (4.375 MTY)	11/2015	3/2020 (3/2026) [3/2026]	851.60 (826.80) [826.80]	233.76 (-24.80) [72]
733	SASTI EXPANSION OC	8/2020	3/2026 (-) [3/2026]	371.59 (-) [371.59]	52.55 (0.00) [0]
734	SINGHORI OC MINE	6/2015	3/2020 (9/2021) [9/2021]	205.49 (-) [205.49]	138.58 (0.00) [18]
735	UKNI DEEP OC	11/2018	3/2021 (9/2022) [9/2022]	318.14 (-) [318.14]	217.47 (0.00) [18]
<u>Department Of Higher Education</u>					
736	CONSTRUCTION OF IITB RESEARCH PARK AT IIT BOMBAY, POWAI, MUMBAI	1/2018	7/2020 (-) [0/0]	223.37 (-) [223.37]	61.35 (0.00) [0]
<u>Fertilisers</u>					
737	GAS TURBINE GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT AT RCF TROMBAY	4/2018	4/2020 (10/2021) [10/2021]	426.72 (-) [426.72]	295.13 (0.00) [18]
<u>Health And Family Welfare</u>					
738	HOSPITAL AND TEACHING- AIIMS NAGPUR	3/2018	(-) [9/2021]	582.99 (-) [582.99]	522.60 (0.00) [-]
739	RESIDENTIAL COMPLEX AND OPD BLOCK, AIIMS, NAGPUR MAHARASTRA	8/2017	3/2019 (-) [1/2021]	274.19 (-) [274.19]	259.46 (0.00) [0]
<u>Petroleum</u>					
740	180 TMTPA NEW LPG PLANT AT PATALGANGA(DIST RAIGAD), MAHARASHTRA	6/2017	6/2020 (-) [9/2021]	249.26 (-) [249.26]	162.09 (0.00) [15]
741	ADDITIONAL FACILITIES AT AHMEDNAGAR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELI	5/2016	1/2021 (-) [10/2021]	261.00 (-) [261.00]	176.30 (0.00) [9]
742	ADDITIONAL FACILITIES AT MANMAD FOR COVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [9/2021]	212.00 (-) [212.00]	164.11 (0.00) [8]
743	ADDITIONAL FACILITIES AT SOLAPUR FOR CONVERSION TO TOP ON KOYALI-MANMAD-AHMEDNAGAR-SOLAPUR PIPELINE	5/2016	1/2021 (-) [8/2022]	348.00 (437.00) [437.00]	162.73 (89.00) [19]
744	CONVERSION OF RIG SAGAR SAMRAT TO MOBILE OFFSHORE PRODUCTION UNIT(MOPS)	3/2011	5/2013 (2/2022) [2/2022]	861.79 (1,846.46) [2,001.34]	1,568.64 (1,139.55) [105]
745	DEVELOPMENT OF NEW MARGINAL FIELD WO 24-3, D30 AND B192 ALONG WITH FACILITY FOR CO2 MITIGATION	2/2019	5/2021 (12/2021) [12/2021]	2,292.46 (-) [2,203.71]	1,995.31 (-88.75) [7]
746	DEVELOPMENT OF R-SERIES FIELDS INCLUDING REVIVAL OF R 12 (RATNA)	2/2017	5/2021 (5/2021) [5/2021]	4,006.83 (4,475.92) [3,596.00]	3,517.17 (-410.83) [0]
747	ENHANCING PRODUCTION OF LUBE OIL BASE STOCK (LOBS) PROJECT AT MUMBAI REFINERY	7/2020	12/2021 (-) [3/2022]	640.00 (-) [640.00]	346.57 (0.00) [3]

748	HEERA REDEVELOPMENT - PHASE III	6/2019	3/2022 (-) [3/2022]	2,494.68 (-) [2,354.72]	1,603.69 (-139.96) [0]
749	KEROSENE HYDROTREATER (KHT) UNIT INTEGRATED WITH EXISTING DIESEL HYDROTREATER (DHT) UNIT AT MUMBAI R	8/2020	3/2023 (-) [3/2023]	697.00 (-) [697.00]	195.24 (0.00) [0]
750	KOYALI AHMEDNAGAR SOLAPUR PIPELINE	5/2016	2/2022 (-) [2/2022]	1,945.00 (-) [1,945.00]	1,529.03 (0.00) [0]
751	LIFE EXTENSION OF WALL PLATFORMS OF MUMBAI HIGH AND HEERA FIELDS	12/2015	4/2018 (5/2022) [5/2022]	3,190.69 (3,375.90) [3,375.90]	2,876.04 (185.21) [49]
752	MUMBAI HIGH NORTH REDEVELOPMENT PHASE-IV	4/2019	3/2022 (5/2023) [5/2023]	3,228.80 (3,976.67) [3,976.67]	1,307.63 (747.87) [14]
753	MUMBAI HIGH SOUTH REDEVELOPMENT PHASE-IV	5/2019	5/2021 (1/2022) [1/2022]	3,660.71 (3,740.05) [3,740.05]	2,997.59 (79.34) [8]
754	PIPELINE REPLACEMENT PROJECT (PRP-VI)	5/2019	12/2020 (12/2021) [12/2021]	763.92 (-) [733.86]	791.46 (-30.06) [12]
	<u>Railways</u>				
755	3RD LINE BETWEEN BHUSAWAL-JALGAON	4/2011	3/2019 (-) [0/0]	184.06 (-) [325.00]	324.93 (140.94) [0]
756	AHMEDNAGAR-PARLI VAIJNATH(NL) CR	2/1997	3/2021 (-) [3/2023]	2,271.50 (-) [4,794.60]	2,831.83 (2,523.10) [24]
757	BELAPUR-SEAWOOD-URAN ELECTRIFIED DOUBLE LINE(MTP)	3/1996	3/2004 (-) [3/2022]	495.44 (-) [2,980.41]	1,821.99 (2,484.97) [216]
758	DAUND - MANMAD (236 KM)	2/2016	3/2023 (-) [3/2023]	1,876.00 (-) [2,081.27]	565.94 (205.27) [0]
759	DAUND-GULBARGA - DOUBLING (224.9 KM) AND PUNE-GUNTAKAL -ELECTRIFICATION (641.37 KM)	3/2009	3/2020 (-) [12/2021]	713.48 (-) [2,725.00]	2,249.00 (2,011.52) [21]
760	DIGHI PORT NEW LINE	4/2015	12/2025 (-) [3/2025]	723.78 (-) [723.78]	0.19 (0.00) [-9]
761	INDORE - MANMAD VIA MALEGAON (368 KM)	2/2016	3/2024 (-) [3/2024]	9,968.00 (-) [9,968.00]	0.00 (0.00) [0]
762	ITARSI-NAGPUR (BAL.) - 3RD LINE (267 KM)	2/2015	3/2023 (-) [3/2024]	2,449.91 (-) [2,449.91]	433.66 (0.00) [12]
763	KALYAN-KASARA 3RD LINE	4/2011	3/2021 (-) [3/2023]	792.89 (-) [910.93]	352.67 (118.04) [24]
764	MANMAD - JALGAON - 3RD LINE (160 KM)	2/2016	3/2022 (-) [3/2024]	1,035.16 (-) [1,035.16]	292.56 (0.00) [24]
765	MULTI MODAL LOGISTICS TRANSPORT AT MIHAN	10/2013	3/2019 (-) [0/0]	305.00 (-) [305.00]	269.73 (0.00) [0]
766	MUMBAI CENTRAL VIRAR VADODARA AHMEDABAAD TRAIN PROTECTION SYSTEM 500 RKM	3/2010	/ (-) [0/0]	265.88 (-) [265.88]	0.00 (0.00) [0]
767	MUMBAI URBAN TRANSPORT PROJECT PHASE-II	4/2008	3/2014 (-) [0/0]	5,300.00 (-) [918.53]	284.75 (-4,381.47) [0]

768	PUNE-MIRAJ-LONDA (467 KM)	2/2015	3/2024 (-) [3/2023]	3,627.47 (3,627.00) [3,627.47]	1,557.30 (0.00) [-12]
769	PUNE-NASIK (265 KM)	2/2016	3/2024 (-) [3/2024]	2,425.00 (-) [5,341.68]	0.00 (2,916.68) [0]
770	RAJNANDGAON - NAGPUR - 3RD LINE (SECR)	9/2016	3/2023 (12/2023) [12/2023]	1,908.51 (3,176.60) [3,176.60]	1,334.01 (1,268.09) [9]
771	RUNNING OF 12 CAR TRAINS ON HARBOUR LINE	4/2012	4/2016 (-) [0/0]	714.10 (-) [714.10]	65.20 (0.00) [0]
772	VAIBHAVWADI - KOLHAPUR (107 KM)	2/2016	3/2024 (-) [0/0]	2,750.00 (-) [3,438.51]	0.00 (688.51) [0]
773	VIRAR SURAT ROAD OVER BRIDGE IN LIEU OF LEVEL CROSSING NOS 42 46A 48 52 55 102 106 108 130 AND 137 A	3/2012	/ (-) [0/0]	217.38 (-) [217.38]	0.00 (0.00) [0]
774	WADSA-GADHCHIROLI NEW LINE (52.36 KM)	6/2018	12/2021 (12/2024) [12/2024]	229.00 (1,096.00) [1,096.00]	40.47 (867.00) [36]
775	WARDHA - NAGPUR - 4TH LINE (76 KM)	2/2016	3/2023 (-) [3/2024]	637.95 (-) [637.95]	199.88 (0.00) [12]
776	WARDHA-BALHARSHAH - 3RD LINE (132 KM)	2/2015	3/2022 (-) [3/2023]	1,272.19 (-) [1,283.49]	479.21 (11.30) [12]
777	WARDHA-NANDED MAHARASHTRA	4/2008	3/2023 (-) [3/2023]	3,168.29 (-) [3,445.48]	1,401.51 (277.19) [0]
778	WARDHA-SEWAGRAM NGP 3RD LINE	4/2012	3/2022 (-) [3/2024]	540.02 (-) [540.02]	352.20 (0.00) [24]
Road Transport And Highways					
779	4 LANING OF FAGNE - MAH-GUJ BORDER (PKG-3)	7/2015	5/2019 (-) [0/0]	1,885.74 (-) [1,885.74]	1,636.02 (0.00) [0]
780	4 LANING OF SOLAPUR YEDISHI SECTION OF NH-211	1/2015	7/2017 (-) [0/0]	972.50 (-) [972.50]	1,492.00 (0.00) [0]
781	4-LANING FROM AURANGABAD TO KARODI (KM 290.200 TO 320.104)	1/2018	/ (-) [8/2021]	607.00 (-) [607.00]	510.71 (0.00) [-]
782	4-LANING FROM KARODI TO TELWADI (KM 320.104 TO 375.000)	1/2018	/ (-) [0/0]	621.00 (-) [621.00]	595.00 (0.00) [0]
783	4-LANING OF SOLAPUR - MAHARASHTRA/ KARNATKA SECTION	6/2014	11/2016 (-) [0/0]	923.04 (-) [923.04]	866.79 (0.00) [0]
784	4-LANNING OF BODHRE-DHULE SECTION(KM 390.000 TO 452.800)	3/2017	3/2020 (-) [0/0]	744.64 (-) [982.00]	0.00 (237.36) [0]
785	4-LANNING OF CHIKHLI TO TARSOD (FROM KM 360-422.700)	11/2016	/ (10/2021) [7/2021]	1,071.61 (-) [1,048.10]	1,091.93 (-23.51) [0]
786	4-LANNING OF KODEBAD-DHAMTARI SECTION OF NH-43 (FROM KM. 43.400 TO KM. 82.209) IN THE STATE OF CHHAT	11/2016	3/2019 (-) [0/0]	446.17 (-) [446.17]	112.52 (0.00) [0]
787	4-LANNING OF MAHAGAON-YAVATMAL SECTION(KM 320.580 TO 400.575)	3/2017	3/2020 (-) [0/0]	1,098.06 (-) [1,160.64]	0.00 (62.58) [0]

788	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 161/600 TO 205/400 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,142.62 (-) [1,142.62]	978.04 (0.00) [0]
789	4-LANNING OF NH17 AND NEW NO. NH66 FROM KM 241/300 TO 281/300 UNDER HYBRID ANNUITY MODE	3/2016	/ (-) [0/0]	1,101.58 (-) [1,101.58]	334.55 (0.00) [0]
790	4-LANNING OF RAIPUR-KODEBAD SECTION OF NH-43 (FROM KM. 10.200 TO KM. 43.400) IN THE STATE OF CHHATTI	11/2016	3/2019 (-) [0/0]	400.25 (-) [400.25]	140.57 (0.00) [0]
791	4-LANNING OF TARSOD-FAGNE(FROM KM 422.700-510.00)	11/2016	/ (1/2022) [7/2021]	1,064.88 (-) [1,021.00]	409.21 (-43.88) [0]
792	4-LANNING OF WARANGA-MAHAGAON SECTION(KM 253.7000 TO 320.580)	3/2017	3/2017 (-) [0/0]	1,059.73 (-) [1,071.00]	18.75 (11.27) [0]
793	4-LANNING OF WARDHA- BUTIBORI SECTION(KM 465.500 TO 524.690)	3/2017	3/2020 (-) [0/0]	1,030.44 (-) [1,065.51]	0.00 (35.07) [0]
794	4-LANNING OF YAVATMAL-WARDHA SECTION(KM 400.575 TO 465.500)	3/2017	3/2020 (-) [0/0]	988.34 (-) [1,043.28]	0.00 (54.94) [0]
795	6/8 LANING OF ROAD PORT CONNECTIVITY JNPT PHASE II -CONSTRUCTION OF NH-348 - PKG3	8/2015	5/2018 (4/2019) [6/2021]	505.00 (-) [504.00]	415.26 (-1.00) [0]
796	AHMADPUR TO PIMPLA	1/2017	8/2019 (-) [0/0]	422.38 (-) [422.38]	224.47 (0.00) [0]
797	AHMEDNAGAR TO BARAMATI	1/2017	8/2019 (-) [0/0]	955.40 (-) [955.40]	459.15 (0.00) [0]
798	AKOLA TO AKOT	1/2017	6/2019 (-) [0/0]	313.95 (-) [313.95]	68.33 (0.00) [0]
799	AKOT TO ANJANGAON	1/2017	6/2019 (-) [0/0]	245.77 (246.00) [245.77]	202.72 (0.00) [0]
800	AMD I TO SAONER	1/2017	6/2019 (-) [0/0]	396.91 (397.00) [396.91]	280.56 (0.00) [0]
801	ARDHAPUR TO HIMAYATNAGAR	12/2017	6/2020 (-) [0/0]	426.06 (426.00) [426.06]	190.63 (0.00) [0]
802	ARNI TO NAIGAINBANDI	12/2017	12/2019 (-) [0/0]	309.94 (310.00) [309.94]	186.03 (0.00) [0]
803	AURANGABAD TO SILLOD	2/2017	6/2019 (-) [0/0]	456.32 (-) [456.32]	330.00 (0.00) [0]
804	BALANCE WORK OF 4-LANNING FROM KM 153.000 TO KM 175.000 OF NAGPUR- HYDERABAD SECTION NS-62	3/2016	7/2018 (-) [0/0]	197.69 (-) [197.69]	0.00 (0.00) [0]
805	BAMNI TO NAVAEGAON	9/2017	4/2020 (-) [0/0]	241.69 (242.00) [241.69]	166.84 (0.00) [0]
806	BARASGAON TO RAHATEE	7/2016	9/2018 (-) [0/0]	289.11 (290.00) [289.11]	101.90 (0.00) [0]
807	BHADGAON TO CHALISGAON	1/2018	11/2019 (-) [0/0]	259.55 (260.00) [259.55]	204.49 (0.00) [0]
808	BHANDARA TO GHOTITOK	1/2017	6/2019	392.83	273.42

			(-) [0/0]	(393.00) [392.83]	(0.00) [0]
809	BHOGAN KHURD TO KASHEDI	9/2017	6/2021 (-) [0/0]	743.21 (743.00) [743.21]	290.00 (0.00) [0]
810	BHOKAR TO SARSAM	2/2017	7/2019 (-) [0/0]	295.09 (-) [295.99]	169.64 (0.90) [0]
811	BODHWAD TO STATE BORDER	1/2017	7/2019 (-) [0/0]	178.26 (-) [178.26]	159.96 (0.00) [0]
812	CHALISGAON TO NANDGAON	3/2018	12/2019 (-) [0/0]	206.97 (207.00) [206.97]	142.46 (0.00) [0]
813	CHIKALI TO DHAD	3/2018	12/2019 (-) [0/0]	189.46 (189.00) [189.46]	107.85 (0.00) [0]
814	CHIKALI TO KHAMGAON	2/2017	6/2019 (-) [0/0]	548.03 (548.00) [548.03]	387.91 (0.00) [0]
815	CHIKLI TO TAKARKHED	3/2018	12/2019 (-) [0/0]	393.10 (393.00) [393.10]	224.68 (0.00) [0]
816	CHIMUR TO WARORA	11/2016	3/2019 (-) [0/0]	467.70 (-) [467.70]	164.90 (0.00) [0]
817	CONSTRUCTION OF 8 LANING OF EXISTING 4 LANE VADAPE TO THANE FROM KM 539.202 TO KM 563.000 SECTION OF	3/2018	/ (-) [7/2021]	1,162.92 (-) [1,162.92]	60.06 (0.00) [0]
818	CONSTRUCTION OF FLYOVER AT KM.544.650 INCLUDING ROB, SERVICE ROADS, FOOTPATH FOR RCC DRAINS ON URBAN	12/2015	3/2019 (12/2021) [6/2022]	649.50 (-) [649.50]	233.12 (0.00) [39]
819	CONSTRUCTION OF FLYOVER AT LAKHANI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [2/2022]	291.53 (-) [291.53]	197.49 (0.00) [-]
820	CONSTRUCTION OF FLYOVER FROM LIBERTY CINEMA TO MENTAL HOSPITAL ON NAGPUR OBEDULLAGANJ ROAD IN THE ST	1/2017	5/2019 (-) [0/0]	244.90 (-) [244.90]	251.87 (0.00) [0]
821	CONSTRUCTION OF FLYOVER IN SAKOLI TOWN ON NH-53 (OLD NH-6)	3/2018	/ (-) [1/2022]	289.21 (-) [289.21]	224.45 (0.00) [-]
822	CONSTRUCTION OF GAVANPHATA INTERCHANGE FROM 14.740 TO KM 15.894 (OLD SH -54) PKG-2	10/2015	5/2018 (3/2022) [3/2022]	593.26 (716.78) [716.78]	617.58 (123.52) [46]
823	CONSTRUCTION OF KARALPHATA INTERCHANGE FROM 3.600 TO KM 6.073 OF NH4B AND FROM 5.300 TO KM 7.422 (	10/2015	5/2018 (3/2022) [3/2022]	531.13 (-) [744.73]	685.76 (213.60) [46]
824	CONSTRUCTION OF MAJOR BRIDGE WITH APPROACHES ACROSS PRANHITA RIVER AT KM 57.300 ON NH-63(16)	3/2015	/ (-) [0/0]	168.30 (-) [168.30]	106.56 (0.00) [0]
825	CONSTRUCTION OF MAJOR/MINOR BRIDGE AND ROB IN 4 LANNING OF NH-66(17) MUMBAI-GOIA ROAD FROM KM 161 TO	8/2014	7/2016 (-) [0/0]	187.79 (-) [187.79]	82.95 (0.00) [0]
826	CONSTRUCTION OF NEW 4-LANE BRIDGE ACROSS VARSOVA CREEK AND ITS APPROACHES WITH INTERCHANGE IN THE ST	3/2017	3/2020 (-) [0/0]	247.02 (-) [157.49]	31.97 (-89.53) [0]
827	CONSTRUCTION OF NH-4B FROM KM.21.200 TO KM.27.270(D TO E SECTION) AND FROM KM.0.000 TO KM.4.492 (D	9/2015	5/2018 (11/2020) [11/2020]	414.51 (-) [414.00]	409.16 (-0.51) [0]
828	DAHEGAON TO KUIHI	1/2017	6/2019 (-)	228.89 (229.00)	154.69 (0.00)

			[0/0]	[228.89]	[0]
829	DASTAPUR TO KARANJA	3/2018	12/2019 (-) [0/0]	182.63 (-) [182.63]	137.99 (0.00) [0]
830	DEORI TO AMGAON	1/2017	5/2019 (-) [0/0]	409.62 (410.00) [409.62]	227.76 (0.00) [0]
831	DEULGAON SAKARSHA TO MEHKAR	3/2018	12/2019 (-) [0/0]	219.91 (-) [219.91]	123.76 (0.00) [0]
832	DEVELOPMENT OF MULTILANE CARRIAGEWAY FROM KANHAN TO AUTOMATIVE SQUARE (KM 704.200 TO KM 723.000)	3/2017	3/2020 (-) [0/0]	296.19 (-) [254.00]	254.85 (-42.19) [0]
833	DHAD BHOKARDAN TO BHOKARDHAN SILLOD	3/2018	12/2019 (-) [0/0]	336.21 (336.00) [336.21]	208.61 (0.00) [0]
834	DHANGIIMPRI TO JALNA AND AMBAD CHOWK TO MANTH CHOWK	3/2018	2/2020 (-) [0/0]	217.14 (217.00) [217.14]	134.90 (0.00) [0]
835	DIGRAS DARWAH KARANJA	1/2017	6/2019 (-) [0/0]	391.06 (391.00) [391.06]	235.49 (0.00) [0]
836	FARDAPUR TO JALGAON	2/2017	6/2019 (-) [0/0]	456.45 (-) [456.45]	285.49 (0.00) [0]
837	FOUR LANING FROM MPMAHARASHTRA BORDER TO NAGPUR IC KAMPTEE KANOON AND NAGPUR BYPASS	4/2010	6/2012 (-) [0/0]	1,170.52 (-) [1,170.52]	2,051.36 (0.00) [0]
838	FOUR LANING OF AKKALKOT-SOLAPUR SECTION OF NH-150E WITH PAVED SHOULDER FROM DESIGN CHAINAGE KM. 99.4	3/2018	/ (-) [0/0]	642.13 (-) [807.00]	691.19 (164.87) [0]
839	FOUR LANING OF AURANGABAD - YEDISHI	7/2015	1/2018 (-) [0/0]	1,871.34 (-) [1,871.34]	0.00 (0.00) [0]
840	FOUR LANNING OF TULJAPUR-AUSA SECTION	2/2017	2/2020 (3/2021) [0/0]	904.16 (911.07) [904.16]	0.00 (0.00) [0]
841	GADCHIROLI TO MUL	12/2016	6/2019 (-) [0/0]	484.15 (-) [484.15]	321.93 (0.00) [0]
842	HELWAK TO KARAD	2/2017	7/2019 (-) [0/0]	416.99 (-) [416.99]	223.81 (0.00) [0]
843	HIMAYATNAGAR TO PHULSAWANGI	3/2018	12/2019 (-) [0/0]	294.87 (295.00) [294.87]	120.82 (0.00) [0]
844	INDAPUR TO AGARDANDA	1/2017	7/2019 (-) [0/0]	355.17 (-) [355.17]	269.58 (0.00) [0]
845	INDAPUR TO VADPALE	1/2017	12/2019 (-) [0/0]	1,202.52 (1,203.00) [1,202.52]	973.05 (0.00) [0]
846	JAHIRABAD TO LATUR	1/2017	11/2019 (-) [0/0]	461.96 (-) [461.96]	303.98 (0.00) [0]
847	JALGAON TO BHADGAON	1/2018	11/2019 (-) [0/0]	307.54 (308.00) [307.54]	200.06 (0.00) [0]
848	JALGAON TO NANDURA	3/2018	12/2019 (-) [0/0]	177.84 (177.00) [177.84]	110.20 (0.00) [0]

849	JALKOT TO TOGRI	7/2018	8/2020 (-) [0/0]	299.92 (300.00) [299.92]	164.11 (0.00) [0]
850	JINTUR TO PARBHANI	1/2017	/	356.66	122.34
			(-) [0/0]	(-) [356.66]	(0.00) [0]
851	KAJJ TO KUSALAM	1/2017	7/2019 (-) [0/0]	554.78 (-) [554.78]	292.74 (0.00) [0]
852	KALMAB TO RALEGAON	1/2017	6/2019 (-) [0/0]	467.78 (-) [467.78]	210.81 (0.00) [0]
853	KALMATH TO ZARAP	9/2016	3/2020 (-) [0/0]	1,338.13 (1,338.00) [1,338.13]	1,346.39 (0.00) [0]
854	KANTE TO WAKED	3/2016	11/2019 (-) [0/0]	1,230.02 (1,230.00) [1,230.02]	631.68 (0.00) [0]
855	KARAD PATAN CHIPLUN GUHAGAR	2/2017	6/2019 (-) [0/0]	407.19 (407.00) [407.19]	175.93 (0.00) [0]
856	KARAD TO TAGAON	1/2017	6/2019 (-) [0/0]	537.81 (538.00) [537.81]	173.98 (0.00) [0]
857	KARAD TO VITA	1/2018	12/2019 (-) [0/0]	344.85 (245.00) [344.85]	210.84 (0.00) [0]
858	KARWANDI TO RAJURI	3/2018	12/2019 (-) [0/0]	276.95 (277.00) [276.95]	253.47 (0.00) [0]
859	KATOL TO WARUD	1/2017	6/2019 (-) [0/0]	463.62 (664.00) [463.62]	258.30 (0.00) [0]
860	KHAMGAON TO DEULGAON SAKARSHA	3/2018	12/2019 (-) [0/0]	249.29 (-) [249.29]	155.48 (0.00) [0]
861	KHAMGAON TO SHEGAON	2/2017	5/2019 (-) [0/0]	203.21 (203.00) [203.21]	150.09 (0.00) [0]
862	KHERDA TO NAGZARI	3/2018	12/2019 (-) [0/0]	181.30 (-) [181.30]	137.37 (0.00) [0]
863	KHUDUS TO DHARAMPURI PACKAGE 3 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [11/2019]	594.75 (-) [594.75]	0.00 (0.00) [0]
864	KOLDE TO KHETIYA	1/2017	7/2019 (-) [0/0]	509.18 (-) [509.18]	228.82 (0.00) [0]
865	KOLHA TO NASRATPUR	4/2016	4/2019 (-) [0/0]	281.78 (282.00) [281.78]	281.73 (0.00) [0]
866	KOTHARI TO DHANORA	9/2018	8/2020 (-) [0/0]	301.38 (301.00) [301.38]	144.50 (0.00) [0]
867	KUMBHARI PHTA TO DEULGAON RAJA	2/2017	6/2019 (-) [0/0]	406.51 (-) [406.51]	290.64 (0.00) [0]
868	KUNDRAI TO WAZAR	1/2018	12/2019 (-) [0/0]	225.25 (225.00) [225.25]	199.34 (0.00) [0]
869	KURUDWADI TO PANDHARPUR	1/2017	7/2019	307.63	190.69

			(-) [0/0]	(-) [307.63]	(0.00) [0]
870	KUSUMBA TO MALEGAON	3/2018	12/2019 (-) [0/0]	243.45 (244.00) [243.45]	154.68 (0.00) [0]
871	LATUR TO PANGAON	3/2018	12/2019 (-) [0/0]	336.47 (336.00) [336.47]	185.03 (0.00) [0]
872	MAHAD TO RAIGAD FORT	7/2018	5/2020 (-) [0/0]	237.40 (-) [237.40]	9.66 (0.00) [0]
873	MALE VILLAGE TO PUNE RAIGARH DISTRICT BORDER	3/2018	12/2019 (-) [0/0]	256.15 (-) [256.15]	174.63 (0.00) [0]
874	MALEGAON TO RISOD	2/2018	12/2019 (-) [0/0]	303.24 (303.00) [303.24]	193.15 (0.00) [0]
875	MALEWADA TO CHIMUR	10/2016	6/2019 (-) [0/0]	322.55 (-) [322.55]	189.60 (0.00) [0]
876	MANGAON TO DIGHI PORT	1/2017	7/2019 (-) [0/0]	457.52 (-) [457.52]	352.94 (0.00) [0]
877	MANGRUPHIR TO MAHAN	3/2018	11/2019 (-) [0/0]	222.13 (222.00) [222.13]	156.87 (0.00) [0]
878	MANJUSUMBA TO CHUMBALI	1/2017	8/2019 (-) [0/0]	228.54 (-) [228.54]	159.32 (0.00) [0]
879	MANSAR TO SALAIKHURD	1/2018	12/2019 (-) [0/0]	418.36 (-) [418.36]	263.13 (0.00) [0]
880	MANTHA TALUKAS BORDER TO PARTUR	1/2017	7/2019 (-) [0/0]	486.19 (-) [486.19]	303.24 (0.00) [0]
881	MEHKAR TO AJISPUR	1/2017	7/2019 (-) [0/0]	232.77 (-) [232.77]	151.60 (0.00) [0]
882	MEHKAR TO CHIKALI	2/2017	5/2019 (-) [0/0]	322.48 (322.00) [322.48]	230.03 (0.00) [0]
883	MHASWAD TO TEMBHURNI	1/2017	7/2019 (-) [0/0]	488.60 (-) [488.60]	224.72 (0.00) [0]
884	MOHOL TO WAKHARI PACKAGE1 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [11/2019]	731.89 (-) [731.89]	0.00 (0.00) [0]
885	MORSHI TO ACHALPUR	1/2017	6/2019 (-) [0/0]	341.16 (341.00) [341.16]	228.07 (0.00) [0]
886	MORSHI TO MAH/MP BORDER	1/2017	6/2019 (-) [0/0]	471.61 (472.00) [471.61]	321.02 (0.00) [0]
887	MUL TO CHANDRAPUR	12/2016	7/2019 (-) [0/0]	162.34 (-) [162.34]	48.40 (0.00) [0]
888	NAGAJ TO VAJJAPUR	1/2017	6/2019 (-) [0/0]	376.72 (377.00) [376.72]	261.86 (0.00) [0]
889	NAGBHID TO ARMORI	9/2016	7/2019 (-)	269.05 (-)	222.40 (0.00)

			[0/0]	[269.05]	[0]
890	NAGPUR RING ROAD PACKAGE-1	3/2016	7/2019 (-) [12/2021]	546.00 (-) [546.00]	309.98 (0.00) [29]
891	NAGPUR RING ROAD PACKAGE-2	3/2016	7/2019 (-) [12/2021]	591.66 (-) [591.66]	319.05 (0.00) [29]
892	NAIGAONBANDI TO MANGRULPIR	12/2017	3/2019 (-) [0/0]	244.04 (244.00) [244.04]	161.70 (0.00) [0]
893	NALDURG TO AKKALKOT	2/2018	12/2019 (-) [0/0]	274.50 (275.00) [274.50]	143.39 (0.00) [0]
894	NANDED TO JALKOT	12/2017	9/2019 (-) [0/0]	456.93 (457.00) [456.93]	155.00 (0.00) [0]
895	NANDGAON TO MORSHI	1/2017	6/2019 (-) [0/0]	385.87 (386.00) [385.87]	258.29 (0.00) [0]
896	NASHIK TO PETH	12/2015	11/2018 (-) [0/0]	289.60 (-) [289.60]	210.10 (0.00) [0]
897	NASRATPUR TO BARASGAON	7/2016	9/2019 (-) [0/0]	406.54 (407.00) [406.54]	172.47 (0.00) [0]
898	NILAJPHATA TO BHANDARA	1/2018	5/2020 (-) [0/0]	420.63 (421.00) [420.63]	155.97 (0.00) [0]
899	OMREGA TO AUSA	3/2018	12/2019 (-) [0/0]	272.04 (272.00) [272.04]	218.03 (0.00) [0]
900	OSMANNAGAR TO KUNDRAL	9/2017	8/2020 (-) [0/0]	344.25 (344.00) [344.25]	139.00 (0.00) [0]
901	PAHUR TO BODHWAD	1/2017	5/2020 (-) [0/0]	244.93 (-) [244.93]	159.96 (0.00) [0]
902	PAITHAN TO SHIRUR	3/2017	6/2019 (-) [0/0]	341.80 (-) [341.80]	134.43 (0.00) [0]
903	PALPHATA TO PHULAMBAR	3/2018	12/2019 (-) [0/0]	227.19 (227.00) [227.19]	134.75 (0.00) [0]
904	PANCHARAL TO MANDANGHAR	7/2018	5/2020 (-) [0/0]	381.08 (302.00) [381.08]	9.66 (0.00) [0]
905	PANDHARPUR TO SANGOLA	7/2017	7/2019 (-) [0/0]	218.38 (-) [218.38]	170.80 (0.00) [0]
906	PARBHANI TO GANGKHED	3/2018	12/2019 (-) [0/0]	238.19 (238.00) [238.19]	154.05 (0.00) [0]
907	PARLI PIMPLA DAHIGUDA	2/2017	6/2019 (-) [0/0]	205.72 (206.00) [205.72]	71.12 (0.00) [0]
908	PARSHURAM GHAT TO ARAWALI	4/2016	12/2019 (-) [0/0]	983.14 (983.00) [983.14]	709.06 (0.00) [0]
909	PARTUR TO MAJALGAON	1/2017	7/2019 (-) [0/0]	420.57 (-) [420.57]	261.37 (0.00) [0]

910	PATGAON KHOPOLI SECTION I	1/2018	12/2019 (-) [0/0]	170.00 (-) [170.00]	118.19 (0.00) [0]
911	PEN TO KHOPOLI	3/2018	3/2018 (-) [0/0]	301.39 (302.00) [301.39]	78.99 (0.00) [0]
912	PIMPLA TO MANJARUMBHA	1/2017	8/2019 (-) [0/0]	595.77 (-) [595.77]	286.10 (0.00) [0]
913	PUNE RAIGARH DISTRICT BORDER TO MANGAON	3/2018	12/2019 (-) [0/0]	223.46 (-) [223.46]	52.22 (0.00) [0]
914	PUNE TO MALE VILLAGE	3/2018	12/2019 (-) [0/0]	228.31 (-) [228.31]	73.45 (0.00) [0]
915	PUNE-SATARA(NH-4)	10/2010	3/2013 (-) [9/2021]	1,724.55 (-) [1,724.55]	2,615.35 (0.00) [102]
916	RALEGAON TO RAMTIRTH	1/2017	7/2019 (-) [0/0]	210.81 (-) [210.81]	210.81 (0.00) [0]
917	REHABILITATION AND UPGRADATION OF NH-222(61) FOM KM 342.00 TO 444.00	1/2014	/ (-) [0/0]	446.77 (-) [446.77]	303.72 (0.00) [0]
918	REHABILITATION AND UPGRADATION OF END OF AHMEDNAGAR BYPASS TO KHARWANDI KASAR SECTION OF NH-222 FROM	1/2015	/ (-) [0/0]	225.81 (-) [225.81]	107.34 (0.00) [0]
919	REHABILITATION AND UPGRADATION OF NH 200 FROM KM 241.553 TO 312.600 MASANIAKALA TO RENGAPALI ODISHA	3/2016	12/2019 (12/2021) [12/2021]	536.65 (356.00) [536.65]	550.22 (0.00) [24]
920	RISOD TO HINGOLI	2/2018	12/2019 (-) [0/0]	355.99 (-) [355.99]	238.22 (0.00) [0]
921	SAKOLI TO BHANDARA	1/2017	6/2019 (-) [0/0]	362.96 (-) [362.96]	148.22 (0.00) [0]
922	SALAIKHURD TO TIRORA	1/2018	12/2019 (-) [0/0]	415.25 (415.25) [415.25]	262.66 (0.00) [0]
923	SANGOLA TO JATH	1/2018	12/2019 (-) [0/0]	257.38 (257.00) [257.38]	147.24 (0.00) [0]
924	SARAD VANI PIMPALGAON	1/2017	7/2019 (-) [0/0]	250.46 (-) [250.46]	174.16 (0.00) [0]
925	SARSAM TO KOTHARI	2/2016	7/2019 (-) [0/0]	545.64 (-) [545.64]	177.20 (0.00) [0]
926	SATARA MURVAD PILLOV PANDHARPUR	1/2017	/ (-) [0/0]	388.44 (-) [388.44]	199.61 (0.00) [0]
927	SATARA TO MHASWAD	1/2017	7/2019 (-) [0/0]	653.46 (-) [653.46]	258.53 (0.00) [0]
928	SELDOH TO PANVAR	7/2018	5/2020 (-) [0/0]	404.33 (404.00) [404.33]	22.40 (0.00) [0]
929	SHAHPUR PATGAON SECTION I	1/2018	12/2019 (-) [0/0]	150.79 (-) [150.79]	59.88 (0.00) [0]
930	SHEGAON TO DEORI PHATA	2/2017	5/2019	373.10	314.20

			(-) [0/0]	(373.00) [373.10]	(0.00) [0]
931	SHIROD SHAHPURER TO NANDED	1/2017	7/2019 (-) [0/0]	211.34 (-) [211.34]	128.55 (0.00) [0]
932	SHIRUR TO KHARDA	2/2017	6/2019 (-) [0/0]	381.77 (-) [381.77]	177.79 (0.00) [0]
933	SHIVUR TO YEOLA	3/2018	12/2019 (-) [0/0]	181.08 (-) [181.08]	97.86 (0.00) [0]
934	SILLOD TO FARDAPUR	2/2017	6/2019 (-) [0/0]	337.46 (-) [337.46]	231.00 (0.00) [0]
935	SIX LANNING OF PIMPALGAON-NASHIK-GONDE SECTION OF NH-3 FROM KM 380.000 TO 440.000 IN THE STATE OF MAH	12/2017	/ (5/2021) [8/2021]	404.94 (495.24) [448.18]	462.99 (43.24) [-]
936	SIX LANNING FROM EXISTING KM 494.410(DESIGN CHAINAGE 540.595) TO EXISTING KM 509.550(DESIGN CHAINAGE	11/2016	/ (0/0)	290.73 (-) [315.00]	246.70 (24.27) [0]
937	TAKARKHED TO JALNA	9/2017	6/2019 (-) [0/0]	417.90 (418.00) [417.90]	217.12 (0.00) [0]
938	TALEGAON TO GONAPUR	1/2018	3/2019 (-) [0/0]	264.41 (264.00) [264.41]	173.14 (0.00) [0]
939	TALGAON TO KALMATH	10/2016	3/2020 (-) [0/0]	904.70 (905.00) [904.70]	969.90 (0.00) [0]
940	TASGAON TO SHIRDHON	1/2017	11/2019 (-) [0/0]	195.64 (196.00) [195.64]	116.30 (0.00) [0]
941	TEMBHURNI PANDHARPUR MANGALWEDHA MARWADE UMDI	2/2017	7/2019 (-) [0/0]	422.02 (422.00) [422.02]	297.76 (0.00) [0]
942	VADPALE TO BHOGAN KHURD	1/2017	11/2019 (-) [0/0]	1,598.47 (1,560.00) [1,598.47]	1,020.24 (0.00) [0]
943	VITA TO NAGAJ	3/2018	12/2019 (-) [0/0]	304.58 (305.00) [304.58]	120.71 (0.00) [0]
944	WADI TO ASOLA	1/2017	9/2019 (-) [0/0]	363.82 (364.00) [363.82]	39.43 (0.00) [0]
945	WADIGODRI TO DHANGRIPIMPRI	3/2018	2/2020 (-) [0/0]	194.23 (194.00) [194.23]	106.45 (0.00) [0]
946	WAKAN PALI KHOPOLI	1/2017	5/2019 (-) [0/0]	376.19 (-) [376.19]	70.16 (0.00) [0]
947	WAKED TO TALEGAON	2/2016	2/2019 (-) [0/0]	1,244.75 (1,245.00) [1,244.75]	840.10 (0.00) [0]
948	WAKHARI TO KHUDUS PACKAGE2 SANT DNYANESHWAR MAHARAJ PALKHI MARG SECTION OF NH965	2/2019	11/2019 (-) [11/2019]	362.46 (-) [362.46]	0.00 (0.00) [0]
949	WARDHA TO ARVI	2/2018	4/2020 (-) [0/0]	313.58 (-) [313.58]	164.00 (0.00) [0]
950	WARDHA TO HINGAGHAT	1/2018	12/2019 (-)	216.90 (217.00)	144.43 (0.00)

			[0/0]	[216.90]	[0]
951	WASHIM TO DASTAPUR	3/2018	12/2019 (-) [0/0]	165.51 (-) [165.51]	133.93 (0.00) [0]
952	WIDENING NH-848 FROM KM 16.000 TO 34.000, 39.000 TO 57.000 AND KM 62.000 TO 65/600/JOB NO 992/15-16	10/2015	/	289.60	160.70
			(-) [0/0]	(-) [289.60]	(0.00) [0]
953	WIDENING OF KHED-SINNAR STRETCH OF PUNE NASHIK SECTION OF NH-50	5/2013	2/2014 (-) [0/0]	1,348.20 (-) [1,348.20]	1,792.90 (0.00) [0]
	<u>Urban Development</u>				
954	MUMBAI METRO LINE 3 (COLABA-BANDRA-SEEPZ)	7/2013	3/2020 (3/2023) [3/2023]	23,136.00 (-) [33,406.00]	18,788.65 (10,270.00) [36]
955	NAGPUR METRO RAIL	8/2014	3/2018 (-) [12/2019]	8,680.00 (-) [8,680.00]	8,260.83 (0.00) [0]
956	PUNE METRO RAIL PROJECT (PHASE 1)	12/2016	11/2021 (12/2022) [12/2022]	11,420.00 (11,420.00) [11,420.00]	6,845.77 (0.00) [13]
	<u>Water Resources</u>				
957	PROTECTION OF MAJULI ISLAND FROM FLOOD AND EROSION OF RIVER BRAHMAPUTRA	3/2017	12/2019 (-) [12/2021]	233.57 (-) [233.57]	148.83 (0.00) [24]
	<u>MANIPUR</u>				
	<u>Power</u>				
958	LOKTAK D/S HEP(NHPC)	12/1999	6/2006 (-) [0/0]	578.62 (1,311.05) [1,311.05]	155.41 (732.43) [0]
	<u>Railways</u>				
959	JIRIBAM TO IMPHAL (TUPUI)(NL)(NEFR)	4/2003	3/2011 (-) [12/2023]	4,454.17 (-) [12,264.15]	11,303.51 (7,809.98) [153]
	<u>Road Transport And Highways</u>				
960	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (1A PACKAGES)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	40.95 (0.00) [0]
961	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2A)	3/2020	6/2022 (-) [6/2022]	292.24 (-) [292.24]	29.70 (0.00) [0]
962	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 2B)	6/2020	8/2022 (-) [8/2022]	365.53 (-) [365.53]	32.49 (0.00) [0]
963	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4A)	3/2020	6/2022 (-) [6/2022]	167.95 (-) [167.95]	27.29 (0.00) [0]
964	2-LANING OF CHURACHANDPUR TUIVAI SECTION OF NH-102B (PKG- 4B)	7/2020	8/2022 (-) [8/2022]	177.76 (-) [177.76]	23.02 (0.00) [0]
965	IMPHAL - KHONGSANG PKG-2	3/2021	12/2022 (-) [12/2022]	195.14 (-) [195.14]	0.00 (0.00) [0]
966	IMPHAL – MOREH PACKAGE- 3	3/2021	12/2022 (-) [12/2022]	259.31 (-) [259.31]	0.00 (0.00) [0]
967	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM DAILI TO KURAOPOKPI SECTIO	8/2020	4/2022 (-) [4/2022]	268.98 (-) [268.98]	0.00 (0.00) [0]
968	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM KURAOPOKPI TO SEKMAI SECTI	8/2020	4/2022 (-) [4/2022]	228.97 (-) [228.97]	0.00 (0.00) [0]

969	IMPROVEMENT/UPGRADATION OF EXISTING 2-LANE TO 4-LANE DIVIDED HIGHWAY FROM TAPHOU KUKI TO DAILI SECTI	8/2020	4/2022 (-) [4/2022]	379.39 (-) [379.39]	2.29 (0.00) [0]
970	IMPROVEMENT/WIDENING TO 2 LANING OF STRETCH FROM KHONGSANG TO TAMENGLONG OF NH-137	3/2019	7/2022 (-) [7/2022]	471.00 (-) [471.00]	116.31 (0.00) [0]
971	MARIAM - PEREN (PKG 1B)	2/2021	12/2022 (-) [12/2022]	188.36 (-) [188.36]	0.00 (0.00) [0]
972	MARIAM - PEREN PKG-1A	2/2021	12/2022 (-) [12/2022]	226.32 (-) [226.32]	0.00 (0.00) [0]
973	MARIAM - PEREN PKG-2B	2/2021	12/2022 (-) [12/2022]	232.26 (-) [232.26]	0.00 (0.00) [0]
974	STRENGTHENING OF EXISTING TWO LANE I/C PAVED SHOULDER FROM MAO - SENAPATI FROM KM 212.325 TO KM 260.	10/2016	11/2020 (-) [0/0]	235.31 (-) [235.31]	195.72 (0.00) [0]
975	TAMENGLONG - MAHUR PKG-3	3/2021	12/2022 (-) [12/2022]	234.08 (-) [234.08]	0.00 (0.00) [0]
976	TWO- LANE WITH PAVED SHOULDER CONFIGURATION OF IMPHAL - MOREH SECTION OF NH-39 FROM KM 350.00 TO KM	8/2017	10/2018 (-) [10/2021]	517.57 (-) [423.93]	432.93 (-93.64) [36]
	<u>MEGHALAYA</u>				
	<u>Department Of Higher Education</u>				
977	CONSTRUCTION AND DEVELOPMENT OF NATINAL INSTITUTE OF TECHNOLOGY MEGHALAYA PERMANENT CAMPUS AT SOHRA	9/2013	9/2014 (-) [0/0]	484.32 (-) [626.26]	0.00 (141.94) [0]
	<u>Doner</u>				
978	CONSTRUCTION OF INTERNATIONAL CENTRE FOR PERFORMING ARTS AND CULTURE,SHILONG IN MEGALAYA UNDER NLCPR	4/2014	9/2017 (-) [8/2021]	151.33 (-) [151.33]	149.33 (0.00) [47]
	<u>Health And Family Welfare</u>				
979	NEIGRIHMS SHILLONG MEGHALYA	10/2016	5/2018 (-) [3/2022]	363.99 (-) [363.99]	246.43 (0.00) [46]
	<u>Railways</u>				
980	NEW BG LINE FROM BYRNIHAT TO SHILLONG	4/2010	3/2021 (-) [0/0]	906.46 (1,202.33) [4,083.02]	264.34 (3,176.56) [0]
	<u>Road Transport And Highways</u>				
981	IMPROVEMENT/WIDENING TO 2-L WITH PAVED SHOULDER FROM (DESIGN KM 0.00 TO KM 10.670) / 4-LANING FROM (	11/2020	12/2023 (-) [12/2023]	351.12 (-) [351.12]	40.99 (0.00) [0]
982	IMPROVEMENT/WIDENING TO 2-LANE WITH EARTHEN SHOULDERS FROM RANIKOR TO NONGJRI EXISTING CHAINAGE FROM	3/2019	5/2019 (-) [3/2022]	306.28 (-) [306.28]	117.91 (0.00) [34]
983	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER / 4-LANING FROM (DESIGN KM 63.530 TO KM 71.520) B	11/2020	12/2023 (-) [12/2023]	284.21 (-) [284.21]	2.63 (0.00) [0]
984	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 10.670 TO KM 37.550) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	525.68 (-) [525.68]	27.54 (0.00) [0]
985	IMPROVEMENT/WIDENING TO 2-LANE WITH PAVED SHOULDER FROM (DESIGN KM 45.760 TO KM 63.530) BETWEEN SHIL	11/2020	12/2023 (-) [12/2023]	445.51 (-) [445.51]	12.93 (0.00) [0]
986	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-3	3/2021	12/2022 (-) [12/2022]	260.21 (-) [260.21]	0.00 (0.00) [0]
987	RANIKOR-MAHESHKHOLA- BAGHMARA (RMB) PKG-4	10/2020	4/2022	157.86	17.63

	(KANAI-RONGARA)		(-) [4/2022]	(-) [157.86]	(0.00) [0]
988	TWO LANING WITH PS OF JOWAI -MEHALAYA /ASSAM BORDER SECTION OF NH-44	12/2015	5/2018 (-) [0/0]	479.20 (-) [479.20]	712.89 (0.00) [0]
989	WIDENING TO 2-LANE WITH GEOMETRIC IMPROVEMENTS OF TURA DALU ROAD UNDER JICA FUNDING FROM KM 85.000 T	4/2017	/ (9/2021) [9/2021]	553.51 (-) [553.51]	127.99 (0.00) [-]
	<u>MIZORAM</u>				
	<u>Railways</u>				
990	BHAIRABI SAIRONG, NL, NEFR	4/2008	3/2014 (-) [3/2024]	2,393.47 (5,021.45) [5,521.45]	4,169.01 (3,127.98) [120]
	<u>Road Transport And Highways</u>				
991	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 0.00 (ON NH-54 NEAR LAWNGTLAI)	8/2010	10/2010 (12/2021) [12/2021]	195.04 (-) [377.99]	368.39 (182.95) [134]
992	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 38/00 TO 71/00 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	9/2014 (12/2021) [12/2021]	186.96 (-) [322.24]	304.71 (135.28) [87]
993	CONSTRUCTION OF A NEW 2-LANE HIGHWAY FROM KM 71/00 TO 99/83 IN MIZORAM TO SUPPORT KALADAN MULTI MOD	8/2010	10/2010 (12/2021) [12/2021]	193.69 (-) [327.92]	323.23 (134.23) [134]
994	CONSTRUCTION OF CHHIATHLANG -SERCHHIP BYPASS (PKG-1) ON AIZAWL-TUIPANG SECTION OF NH-54	9/2020	10/2022 (-) [10/2022]	275.02 (-) [275.02]	22.39 (0.00) [0]
995	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-I)	3/2020	7/2022 (-) [7/2022]	206.88 (-) [206.88]	21.58 (0.00) [0]
996	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-II)	3/2020	7/2022 (-) [7/2022]	216.49 (-) [216.49]	33.63 (0.00) [0]
997	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-III)	3/2020	7/2022 (-) [7/2022]	292.24 (-) [292.24]	37.79 (0.00) [0]
998	CONSTRUCTION OF TWO LANE WITH PAVED SHOULDER OF SELLING-DULTE SECTION OF NH-06 (PKG-IV)	3/2020	7/2022 (-) [7/2022]	281.78 (-) [281.78]	73.31 (0.00) [0]
999	DULTE- KWALKULH - CHAMPAI PKG.1	3/2021	12/2022 (-) [12/2022]	374.39 (-) [374.39]	0.00 (0.00) [0]
1000	DULTE- KWALKULH - CHAMPAI PKG.2	3/2021	12/2022 (-) [12/2022]	233.25 (-) [233.25]	0.00 (0.00) [0]
1001	DULTE- KWALKULH - CHAMPAI PKG.3	3/2021	6/2023 (-) [6/2023]	674.71 (-) [674.71]	0.00 (0.00) [0]
1002	TLABUNG - LUNGLEI PKG-A	3/2021	12/2022 (-) [12/2022]	698.44 (-) [698.44]	0.00 (0.00) [0]
1003	TLABUNG - LUNGLEI PKG-B	3/2021	1/2023 (-) [1/2023]	740.58 (-) [740.58]	0.00 (0.00) [0]
1004	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (-) [4/2023]	519.09 (-) [519.09]	71.38 (0.00) [43]
1005	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [4/2023]	473.18 (-) [473.18]	108.59 (0.00) [43]
1006	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC	4/2017	9/2019 (4/2023)	518.53 (-)	118.95 (0.00)

	IMPROVEMENTS FRO		[6/2023]	[518.53]	[45]
1007	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (9/2023) [9/2023]	428.11 (-) [428.11]	71.30 (0.00) [48]
1008	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (3/2024) [4/2024]	404.29 (-) [404.29]	33.67 (0.00) [55]
1009	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [4/2023]	537.82 (-) [537.82]	121.93 (0.00) [43]
1010	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (6/2023) [7/2023]	640.07 (-) [640.07]	93.50 (0.00) [46]
1011	WIDENING AND UP-GRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION AND GEOMETRIC IMPROVEMENTS FRO	4/2017	9/2019 (4/2023) [6/2023]	642.96 (-) [642.96]	71.41 (0.00) [45]
1012	WIDENING TO 2 LANE, RE-ALIGNMENT AND GEOMETRIC IMPROVEMENT FROM KM 11/00 TO KM 114/618 OF NH-44A IN	11/2010	3/2011 (12/2021) [12/2021]	624.41 (-) [992.67]	890.74 (368.26) [129]
	<u>MULTI STATE</u>				
	<u>Coal</u>				
1013	BINA KAKRI AMALGAMATION OCP 14 MTPA	8/2020	3/2024 (-) [3/2024]	836.42 (-) [836.42]	60.07 (0.00) [0]
1014	DURGAPUR EXTENSION (DEEP) OC (3.0 MTY)	2/2017	3/2021 (-) [9/2023]	328.00 (-) [328.00]	296.56 (0.00) [30]
1015	NILJAI EXPANSION (DEEP) OC (3.5 MTY)	8/2016	3/2022 (-) [3/2022]	319.76 (404.45) [404.45]	246.02 (84.69) [0]
1016	RECAST PR FOR DHANKASA UG (1.00 MTY)	9/2016	3/2022 (3/2025) [3/2025]	289.29 (-) [289.30]	36.10 (0.01) [36]
	<u>Department Of Higher Education</u>				
1017	SCHEME FOR PROMOTION OF ACADEMIC AND RESEARCH COLLABORATION	8/2018	3/2019 (-) [0/0]	418.00 (-) [418.00]	110.00 (0.00) [0]
1018	STUDY IN INDIA	3/2018	4/2018 (-) [0/0]	150.00 (-) [150.00]	0.00 (0.00) [0]
	<u>Dpiit</u>				
1019	DELHI MUMBAI INDUSTRIAL CORRIDOR	9/2011	9/2019 (1/2014) [7/2021]	12,579.09 (-) [13,812.30]	9,346.57 (1,233.21) [0]
	<u>Heavy Industry</u>				
1020	NATIONAL AUTOMOTIVE TESTING AND RD INFRASTRUCTURE PROJECT (NATRIP)	4/2011	9/2011 (3/2021) [3/2021]	1,718.00 (3,727.30) [3,727.30]	3,517.10 (2,009.30) [0]
	<u>Petroleum</u>				
1021	AUGMENTATION OF PARADIP-HALDIA-DURGAPUR LPG PIPELINE AND ITS EXTENSION UPTO PATNA AND MUZAFFARPUR	1/2015	3/2021 (12/2021) [12/2021]	1,823.00 (3,027.90) [3,027.90]	2,117.81 (1,204.90) [9]
1022	AUGMENTATION OF PUMPING CAPACITY OF BARAUNI-BONGAIGAON SECTOR PHASE II	9/2016	12/2019 (-) [8/2021]	571.66 (-) [571.66]	479.91 (0.00) [20]
1023	BARAUNI-GUWAHATI PIPELINE	6/2018	12/2021 (-) [12/2021]	3,308.00 (3,060.00) [3,060.00]	2,312.50 (-248.00) [0]
1024	BARMER PALANPUR PIPELINE	11/2019	11/2022 (-) [11/2022]	776.00 (-) [776.00]	307.06 (0.00) [0]

1025	BOKARO-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	3,437.00 (3,048.00) [3,048.00]	2,009.10 (-389.00) [12]
1026	CGD PROJECT AT NAWADA AND KODERMA DISTRICTS	6/2019	12/2029 (-) [12/2029]	169.00 (-) [169.00]	0.00 (0.00) [0]
1027	CGD PROJECT AT SHEIKHPURA, JAMUI AND DEOGHAR DISTRICTS	6/2019	2/2028 (-) [2/2028]	303.00 (-) [303.00]	0.00 (0.00) [0]
1028	DHAMRA HALDIA PIPELINE PROJECT	3/2020	11/2022 (-) [11/2022]	1,030.65 (-) [1,030.65]	335.00 (0.00) [0]
1029	DOBHI-DURGAPUR PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	2,433.00 (-) [2,433.00]	2,147.10 (0.00) [12]
1030	EXTENSION OF VISAKH-VIJAYAWADA-SECUNDERABAD PIPELINE (VVSPL) FROM VIJAYAWADA TO DHARMAPURI AND CONST	9/2017	6/2021 (8/2022) [7/2022]	2,677.00 (-) [3,072.00]	2,443.16 (395.00) [13]
1031	KOCHI-KOOTTANAD-BANGALORE-MANGALORE PIPELINE PHASE-II	6/2009	12/2012 (2/2022) [2/2022]	2,915.00 (5,909.00) [5,909.00]	3,786.80 (2,994.00) [110]
1032	LAYING OF VIJAIPUR-AURAIYA PIPELINE SECTION OF VIJAIPUR-AURAIYA-PHULPUR PIPELINE PROJECT	7/2015	12/2020 (-) [10/2021]	2,881.40 (-) [2,000.00]	1,622.70 (-881.40) [10]
1033	MUMBAI NAGPUR JHARSUGUDA PIPELINE PROJECT	6/2020	5/2023 (-) [5/2023]	7,844.25 (-) [7,844.25]	1,504.40 (0.00) [0]
1034	PARADIP HYDERABAD PIPELINE	1/2015	12/2020 (3/2022) [3/2022]	2,321.00 (3,338.00) [3,338.00]	2,996.28 (1,017.00) [15]
1035	PARADIP LPG IMPORT FACILITY	1/2015	7/2018 (5/2021) [10/2021]	690.00 (-) [690.00]	587.17 (0.00) [39]
1036	PIPELINE REHABILITATION PROJECT OF 575 KM (PHASE I)	5/2016	10/2020 (-) [3/2022]	406.00 (-) [406.00]	269.65 (0.00) [17]
1037	SRIKAKULAM ANGUL PIPELINE PROJECT	9/2019	7/2022 (-) [7/2022]	2,658.34 (-) [2,658.34]	340.70 (0.00) [0]
	<u>Power</u>				
1038	400 KV D/C BAHARAMPUR (PG) - BHERAMERE (B'DESH) LINE CKT II (INDIA PORTION)	9/2017	9/2019 (-) [0/0]	198.49 (-) [198.49]	132.15 (0.00) [0]
1039	COMPREHENSIVE SCHEME FOR THE STRENGTHENING OF THE TRANSMISSION AND DISTRIBUTION SYSTEM IN A P	12/2014	12/2018 (3/2024) [3/2024]	4,754.42 (9,129.32) [9,129.32]	2,480.78 (4,374.90) [63]
1040	EASTERN REGION STRENGTHENING SCHEME XX	11/2017	5/2020 (8/2021) [10/2021]	358.83 (-) [358.83]	259.50 (0.00) [17]
1041	EASTERN REGION STRENGTHENING SCHEME-V	10/2013	4/2016 (-) [0/0]	1,364.52 (-) [1,891.41]	1,290.03 (526.89) [0]
1042	EASTERN REGION STRENGTHENING SCHEME-XII	5/2014	11/2016 (12/2021) [12/2021]	522.29 (546.36) [546.36]	480.43 (24.07) [61]
1043	EASTERN REGION STRENGTHENING SCHEME-XVIII	3/2017	7/2020 (12/2020) [10/2021]	3,500.00 (3,500.00) [3,994.00]	3,029.93 (494.00) [15]
1044	EASTERN REGION STRENGTHENING SCHEME XVII(PART B)	2/2017	6/2019 (11/2021) [11/2021]	235.53 (-) [235.53]	155.39 (0.00) [29]

1045	ESTABLISHMENT OF 220/66KV GIS AT UT CHANDIGARH ALONG WITH 220KV D/C LINE FROM CHANDIGARH GIS TO 400/	2/2017	2/2019 (9/2021) [2/2022]	322.30 (-) [322.30]	204.09 (0.00) [36]
1046	ESTABLISHMENT OF FIBER OPTIC COMMUNICATION SYSTEM IN NR UNDER FIBER OPTIC EXPANSION PROJECT (ADDITIO	3/2015	3/2018 (-) [12/2021]	197.40 (-) [197.40]	90.28 (0.00) [45]
1047	GREEN ENERGY CORRIDORS - INTER STATE TRANSSMISSION SCHEME PART-D	5/2016	5/2019 (-) [0/0]	3,519.59 (-) [3,519.59]	2,562.41 (0.00) [0]
1048	HVDC BIPOLE LINK BETWEEN WESTERN REGION (RAIGARH, CHATTISGARH) AND SOUTHERN REGION (PUGALAR, TM) NOR	2/2017	4/2020 (9/2021) [6/2021]	5,070.13 (-) [5,070.13]	4,138.57 (0.00) [0]
1049	HVDC BIPOLE LINK BETWEEN WR (RAIGARH, CHATTISGARH) AND SR (PUGALUR-NORTH TRICHUR- SCHEME-I: RAIGARH-P	5/2016	11/2019 (7/2021) [9/2021]	14,733.37 (-) [14,733.37]	11,641.93 (0.00) [22]
1050	HVDC BIPOLE LINK BETWEEN WR AND SR -NORTH TRICHUR - SCHEME -II AC SYSTEM STRENGTHENING AT PUGALUR EN	8/2017	2/2020 (9/2021) [9/2021]	1,931.39 (-) [1,931.39]	1,783.23 (0.00) [19]
1051	NORTH EASTERN REGION POWER SYSTEM IMPROVEMENT PROJECT (NERPSIP) FOR SIX (6) STATES	12/2014	12/2018 (12/2021) [3/2022]	5,111.33 (6,700.00) [6,700.00]	3,068.24 (1,588.67) [39]
1052	NORTH- EAST NORTH WESTERN INTERCONNECTOR I PROJECT	2/2009	8/2013 (11/2022) [8/2022]	11,130.19 (14,719.10) [14,719.10]	12,953.79 (3,588.91) [108]
1053	S/S WORK ASSOCIATED WITH ADDITIONAL INTER REGIONAL AC LINK FOR IMPORT IN TO SOUTHERN REGION I.E WARO	3/2017	11/2019 (-) [0/0]	283.72 (-) [283.72]	196.10 (0.00) [0]
1054	STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	12/2015	4/2019 (-) [0/0]	3,654.00 (-) [3,654.00]	3,508.04 (0.00) [0]
1055	SUB STATION WORK ASSOCIATED WITH STRENGTHENING OF TRANSMISSION SYSTEM BEYOND VEMAGIRI	10/2016	4/2019 (-) [0/0]	608.24 (-) [608.24]	425.04 (0.00) [0]
1056	SYSTEM STRENGTHENING IN SOUTHERN REGION - XXIII	1/2015	7/2017 (-) [0/0]	203.28 (-) [260.03]	200.16 (56.75) [0]
1057	SYSTEM STRENGTHENING SCHEME IN NORTH REGION XXXVII	3/2017	12/2019 (9/2021) [12/2021]	379.95 (-) [379.95]	235.59 (0.00) [24]
1058	SYTEM STRENGTHENING XIII OF SR GRID	10/2011	6/2014 (-) [0/0]	487.49 (-) [639.46]	590.30 (151.97) [0]
1059	TR. SYSTEM ASSOCIATED WITH MUNDRA ULTRA MEGA POWER PROJECT	10/2008	10/2012 (-) [0/0]	4,824.12 (-) [5,071.94]	4,612.66 (247.82) [0]
1060	TRANSMISSION SYSTEM ASSOICATED WITH TEHRI PUMP STORAGE PLANT (PSP)	1/2015	10/2017 (-) [0/0]	871.62 (-) [902.49]	628.13 (30.87) [0]
1061	TRANSMISSION SYSTEM FOR ULTRA MEGA SOLAR POWER AT TUMKUR (PAVAGADA) KARNATAKA PHASE -II (PART II)	10/2016	1/2019 (-) [0/0]	408.46 (-) [516.12]	369.27 (107.66) [0]
1062	TRANSMISSION SYSTEM STRENGTHENING IN WR-NR TRANSMISSION CORRIDOR FOR IPPS IN CHHATTISGARH	6/2014	3/2018 (-) [0/0]	5,151.37 (-) [5,151.37]	3,269.93 (0.00) [0]
1063	TRANSMISSION SYSTEM STRENTHENNING IN INDIAN SYSTEM FOR TRANSFER OF POWER FROM MANGDECHHU HYDROELECTR	3/2016	1/2018 (7/2021) [6/2021]	808.63 (-) [808.63]	678.82 (0.00) [0]
1064	UNIFIED REAL TIME DYNAMIC STATE MEASUREMENT PHASE-I	1/2014	4/2016 (12/2017) [12/2021]	374.63 (-) [374.63]	252.99 (0.00) [68]
	<u>Railways</u>				

1065	MUMBAI AHMEDABAD HIGH SPEED RAIL PROJECT	12/2015	12/2023 (-) [12/2023]	1,08,000.00 (-) [1,08,000.00]	14,605.32 (0.00) [0]
1066	BANDEL-BOINCHI 3RD LINE	4/2011	/ (-) [3/2021]	288.35 (-) [502.48]	508.72 (214.13) [0]
1067	BARIARPIUR-MANANPURVIA KHARAGPUER, LACHIMPUR-BARAHAT	4/2007	/ (-) [3/2025]	450.55 (-) [250.55]	20.11 (-200.00) [-]
1068	BHADRACHALAM ROAD-SATTUPALLI	4/2010	3/2020 (-) [11/2021]	704.31 (-) [927.94]	656.85 (223.63) [20]
1069	BOINCHI-SHAKTIGARH 3RD LINE	4/2011	/ (-) [3/2022]	175.80 (-) [495.10]	299.53 (319.30) [-]
1070	CHANDIGARH-BADDI	4/2007	3/2023 (-) [3/2023]	328.14 (-) [1,540.13]	242.31 (1,211.99) [0]
1071	CHANDPARA-BANGAON DOUBLING WITH EXENSION TO CHANDBAZAR AND NEW MM FOR BONGAON-PORAMAHESHTALA AND CHA	4/2003	/ (-) [3/2025]	337.96 (-) [336.96]	40.65 (-1.00) [-]
1072	CHENNAI-CUDDALORE VIA MAMALLAPURAM	4/2008	/ (-) [3/2024]	523.52 (-) [1,205.00]	2.28 (681.48) [-]
1073	CHHAPRA-BALLIA UP	3/2013	1/2019 (-) [2/2022]	295.00 (-) [580.00]	521.43 (285.00) [37]
1074	CHHITAUNI TAMKUHI ROAD KUSHINAGAR GOPALGANJ UP	3/2007	12/2021 (-) [12/2021]	243.78 (-) [895.00]	114.63 (651.22) [0]
1075	CHINPAI-SAINTHIA DOUBLING, MM FOR PRANTI-SURI, CHOWRIGACHA-SAINTHIA VIA KANDI NL	4/2005	3/2017 (-) [3/2025]	595.51 (-) [769.40]	97.40 (173.89) [96]
1076	CHOTTAUDEPUR-DHAR(NL)	4/2007	3/2022 (3/2023) [3/2023]	1,347.26 (1,524.68) [1,524.68]	974.69 (177.42) [12]
1077	DAHOD-INDORE VIA SARDARPUR, JHABUA AND DHAR (NL)	4/2007	3/2022 (3/2023) [3/2023]	1,640.04 (1,873.10) [1,873.10]	869.58 (233.06) [12]
1078	DANKUNI-CHANDANPUR 4TH LINE, 1ST PHASE OF DANKUNI-SHAKTIGARH 4TH LINE WITH MM BARUIPARA FURFURA NL	4/2010	3/2017 (-) [3/2025]	365.17 (-) [439.30]	454.56 (74.13) [96]
1079	DEOBAND (MUZAFFARNAGAR)- ROORKEE NL	4/2007	/ (-) [3/2023]	336.91 (-) [791.39]	574.59 (454.48) [-]
1080	DEOGHAR - SULTANGANJ (INL), ER	4/2000	2/2013 (-) [3/2024]	607.09 (-) [1,425.44]	638.19 (818.35) [133]
1081	DHOLPUR-SIRMUTTRA WITH EXTENSION TO GANGAPURCITY AND MOHARI-TANTPUR AND TANPUR-BANSI PAHARPUR	4/2010	/ (-) [0/0]	2,030.50 (-) [2,030.50]	0.00 (0.00) [0]
1082	DIGHA-JALESWAR INCLUDING MM FOR DIGHA-EGRA	4/2010	3/2015 (-) [3/2025]	651.00 (-) [1,009.00]	7.96 (358.00) [120]
1083	EASTERN DEDICATED FREIGHT CORRIDOR PROJECT	10/2006	/ (-) [0/0]	11,589.00 (30,357.00) [28,181.00]	0.00 (16,592.00) [0]
1084	GAYA-CHATRA (NL)	4/2008	/ (-) [0/0]	415.67 (-) [549.75]	15.58 (134.08) [0]
1085	GONDIA-JABALPUR(GC),(SECR)	2/1997	4/2020	511.86	1,849.61

			(3/2021) [3/2021]	(1,756.00) [2,005.25]	(1,493.39) [0]
1086	GOOTY-DHARMAVARAM-BANGLORE	4/2015	/	636.38	0.00
			(-)	(-)	(0.00)
			[0/0]	[636.38]	[0]
1087	GWALIOR-SEOPURKALA WITH EXTENSION TO KOTA (GC)	4/2011	3/2022 (12/2024) [12/2024]	2,912.96 (-) [3,845.60]	303.16 (932.64) [33]
1088	HAJIPUR - BACHAWARA	5/2015	3/2019 (12/2021) [12/2021]	678.54 (678.54) [929.86]	863.90 (251.32) [33]
1089	HANSDIHA-GODDA NL	4/2011	3/2020 (-) [3/2021]	542.18 (-) [663.13]	544.63 (120.95) [0]
1090	HANSNABAD-HINGALGANJ NEW BG LINE	4/2010	/	172.03	11.77
			(-)	(-)	(88.07)
			[3/2025]	[260.10]	[-]
1091	HATHUA-BHATNI (N L) (NER)	4/2005	12/2022 (-) [12/2022]	230.03 (-) [230.03]	277.14 (0.00) [0]
1092	HOTGI-KUDGI-GADAG	3/2015	3/2019 (-) [3/2024]	1,614.59 (1,877.81) [1,878.00]	1,457.95 (263.41) [60]
1093	HOWRAH DIVISION- PLATFORM SHELTER (40 C CATEGORY STATIONS)	4/2010	11/2018 (-) [3/2021]	157.94 (-) [157.94]	51.74 (0.00) [0]
1094	HOWRAH-DEVELOPMENT OF STATION INCLUDING SEGRAGATION OF AARIVAL/DEPARTURE AND OTHER AMENITIES	4/2011	/	166.89	0.02
			(-)	(-)	(0.00)
			[3/2025]	[166.89]	[-]
1095	JALANDHAR-PATHANKOT-JAMMU TAWI	3/2002	3/2016 (-) [0/0]	625.00 (-) [859.00]	852.73 (234.00) [0]
1096	KADAPA-BANGALORE (NL), KADAPA-PENDLIMARRI PH-I	4/2008	3/2014 (-) [3/2027]	2,132.77 (-) [3,037.95]	348.32 (905.18) [156]
1097	KALINARAYANPUR-KRISHNANAGAR DOUBLING ALONGWITH KRISHNANAGAR - CHAPRA NEW LINE AND NAIHATI-RANAGHAT 3	4/2001	3/2016 (-) [3/2025]	923.52 (-) [995.10]	614.44 (71.58) [108]
1098	KALINARAYANPUR-SHANTIPUR DOUBLING WITH NEW MM FOR RANAGHAT-DUTTAPHULIA NEW LINE	4/2010	/	174.56	71.43
			(-)	(-)	(0.00)
			[3/2025]	[174.56]	[-]
1099	KAZIPET-BALHRSHA	4/2015	3/2021 (-) [3/2024]	2,063.03 (-) [2,063.03]	1,530.08 (0.00) [36]
1100	KAZIPET-VIJAYAWADA 3RD LINE WITH ELECTRIFICATION	4/2012	3/2023 (-) [3/2024]	1,856.95 (-) [1,952.68]	684.12 (95.73) [12]
1101	KURUPPANTHARA-CHINGAVANAM	4/2007	/	270.14	0.00
			(-)	(-)	(186.94)
			[12/2021]	[457.08]	[-]
1102	LAKSHMIKANTAPUR-NAMKHANA SUBSEQUENTLY MM FOR NAMKHANA-CHANDRANAGAR, KAKDWIP- BUDAKHALI AND CHANDRANAG	4/1987	3/2006 (-) [3/2025]	406.99 (-) [545.70]	149.31 (138.71) [228]
1103	LALITPUR-SATNA-REWA-SINGRULI NL, (NCR)	9/1998	5/2008 (-) [3/2025]	247.66 (-) [8,248.50]	2,131.17 (8,000.84) [202]
1104	LILUAH-DANKUNI 3RD LINE, MM FOR DANKUNI- JONGALPARA-FURFURA SHARIF NL	4/2009	3/2014 (-) [3/2025]	257.42 (-) [257.42]	108.87 (0.00) [132]
1105	MADURAI-TUTICORIN VIA ARUPPUKOTTAI	4/2011	3/2019 (-)	120.70 (-)	273.27 (2,051.46)

			[12/2027]	[2,172.16]	[105]
1106	MAGRAHAT-DIAMOND HARBOUR WITH MM SANGRAMPUR-KRISHANCHANDPUR AND DIAMOND HATBOUR - BAHRAHAT-KULPI NL	4/2009	2/2012 (-) [3/2025]	499.96 (-) [680.68]	141.76 (180.72) [157]
1107	MONIGRAM- NIMTITA	4/2012	/ (-) [3/2024]	250.93 (-) [310.70]	377.47 (59.77) [-]
1108	MUNEERABAD-MAHABOBNAGAR(NL),SCR	4/1997	3/2000 (-) [3/2023]	1,723.00 (1.00) [3,421.35]	1,989.23 (1,698.35) [276]
1109	MURKONGSELEK-PASIGHAT NL	4/2011	3/2020 (-) [0/0]	414.84 (-) [750.00]	156.80 (335.16) [0]
1110	NANGALDAM-TALWARA(NL),NR	3/1981	7/2012 (-) [3/2024]	450.00 (-) [2,200.00]	0.00 (1,750.00) [140]
1111	NEW ALIPUR TO AKRA, MM FOR BUDGE BUDGE-PUJALI NL, PUJALI-ULUBERIA(BIRSHIVPUR) AND PUJALI-BAHRAHAT NL	4/2010	3/2005 (-) [3/2025]	494.54 (-) [494.59]	30.12 (0.05) [240]
1112	NEW BG LINE FROM BALURGHAT TO HILLY NFR	4/2010	3/2020 (-) [0/0]	242.22 (-) [471.00]	76.57 (228.78) [0]
1113	NEW BG LINE FROM JAGBANI TO BIRATNAGAR	4/2010	/ (12/2021) [3/2022]	241.52 (-) [373.87]	333.46 (132.35) [-]
1114	NEW BONGAIGAON-RANGIA-KAMAKGHYA DOUBLING	4/2013	3/2019 (-) [12/2023]	1,798.00 (2,042.51) [2,042.51]	219.14 (244.51) [57]
1115	NEW JALPAIGURI SILIGURI NEW BONGAIGAON INCLUDING BR LINE AND MM CHALSA NAXAL RAJABHATKHOWA JAINTI	4/1999	/ (-) [0/0]	819.23 (-) [1,871.00]	1,082.01 (1,051.77) [0]
1116	NEW MAYNAGURI TO JOGIGHOPA VIA CHANGRABANDHA (NL),NEFR	4/2000	12/2008 (-) [9/2021]	1,180.19 (2,531.34) [4,541.38]	3,825.94 (3,361.19) [153]
1117	PHULERA - DIGANA DOUBLING	5/2015	3/2020 (-) [10/2022]	600.00 (-) [701.81]	261.79 (101.81) [31]
1118	PIRPAINTI-BHAGALPUR	4/2011	/ (-) [5/2019]	261.38 (-) [565.00]	552.51 (303.62) [0]
1119	PIRPAINTI-JASIDIH	4/2013	3/2022 (-) [3/2025]	915.98 (-) [2,137.81]	409.74 (1,221.83) [36]
1120	PRINCEPGHAT-MAJERHAT DOUBLING OF CIRCULAR RAILWAY	4/2011	3/2017 (-) [3/2026]	299.60 (-) [335.62]	1.12 (36.02) [108]
1121	RATLAM-DUNGARPUR VIA BANSWARA (NL)	4/2011	/ (-) [0/0]	2,082.75 (-) [4,262.36]	186.14 (2,179.61) [0]
1122	RAYADURGA-TUMKUR NL	4/2007	/ (-) [12/2025]	2,062.30 (-) [2,432.50]	1,126.08 (370.20) [-]
1123	SONARPUR-CANNING WITH NEW MM FOR KALIKAPUR-MINAKHAN VIA GHATAKPUR NL	4/2000	/ (-) [3/2025]	297.47 (-) [298.22]	36.13 (0.75) [-]
1124	SONDALIA-CHAMPAPUKUR DOUBLING WITH NEW MM FOR BIRA-CHAKIA NL	4/2010	3/2016 (-) [3/2025]	277.28 (-) [266.32]	197.54 (-10.96) [108]
1125	SRINIVASA-PURA-MADANAPALLI NL	4/2013	/ (-) [12/2023]	296.00 (-) [466.65]	0.00 (170.65) [-]

1126	SULTANGANJ-KATURIA VIA ASARGANJ, TARAPUR AND BELHAR	4/2007	/ (-) [3/2025]	450.00 (-) [1,261.34]	0.00 (811.34) [-]
1127	TARAKESHWAR-MAGRA NEW BG LINE	4/2010	/ (-) [3/2025]	365.17 (-) [527.54]	1.76 (162.37) [-]
1128	WESTERN DEDICATED FREIGHT CORRIDOR	11/2007	3/2020 (-) [0/0]	16,592.00 (51,101.00) [51,101.00]	22,485.00 (34,509.00) [0]
1129	YELAHANKA-PENUKONDA	5/2015	3/2020 (-) [9/2021]	860.43 (-) [1,147.00]	945.81 (286.57) [18]
Road Transport And Highways					
1130	4 LANING OF NAGPUR-BETUL	2/2011	8/2014 (-) [0/0]	2,498.76 (-) [2,498.76]	2,531.46 (0.00) [0]
1131	DELHI AGRA APPROVED LENGTH 180.0 KM	10/2012	4/2015 (1/2021) [12/2021]	1,928.22 (1,928.22) [1,928.22]	1,876.06 (0.00) [80]
1132	FOUR LANING OF PUDUCHERRY - POONDIYANKUPPAM SECTION OF NH 45 A (NEW NH 332) FROM KM 29.000 TO KM 67.	3/2018	/ (-) [0/0]	1,294.47 (-) [1,296.00]	0.00 (1.53) [0]
1133	FOUR LANING OF VILUPPURAM - PUDUCHERRY SECTION OF NH 45 A (NEW NH 32) FROM KM 0.000 TO KM 29.000 (DE	3/2018	/ (-) [0/0]	998.70 (-) [962.00]	0.00 (-36.70) [0]
1134	GWALIOR-JHANSI, NH-75	12/2003	12/2009 (9/2020) [9/2020]	604.00 (-) [364.59]	332.18 (-239.41) [0]
1135	MUZAFFARNAGAR-HARIDWAR	9/2011	3/2013 (-) [0/0]	754.00 (-) [754.00]	1,364.18 (0.00) [0]
1136	SIX LANNING FROM KM 287.400 TO KM 401.200 SECTION OF NH- 8 IN THE STATE OF RAJASTHAN AND GUJARAT(APP	9/2016	/ (-) [0/0]	1,244.10 (-) [1,244.10]	1,663.00 (0.00) [0]
1137	SURAT- DAHISAR(SIX LANE) KM 263 TO KM 502	2/2009	8/2011 (-) [0/0]	1,693.75 (-) [1,693.75]	2,848.49 (0.00) [0]
1138	VARANASI-AURANGABAD KM.786 TO KM.978.40	9/2011	3/2014 (-) [12/2022]	2,848.00 (-) [3,379.45]	3,379.45 (531.45) [105]
Shipping And Ports					
1139	JAL MARG VIKAS PROJECT	1/2018	3/2023 (-) [3/2023]	5,369.18 (4,633.81) [4,633.81]	1,901.76 (-735.37) [0]
Telecommunications					
1140	NETWORK FOR SPECTRUM	3/2012	7/2015 (5/2020) [3/2022]	13,334.00 (24,664.00) [24,664.00]	17,845.00 (11,330.00) [80]
1141	PHASE-I OF CONSOLIDATION OF EXISTING CDR DATA CENTERS AND NIB-P3 DATA CENTERS WITH STATE OF THE ART	3/2020	6/2021 (-) [11/2021]	431.16 (422.87) [422.87]	0.00 (-8.29) [5]
Urban Development					
1142	DELHI GHAZIABAD MEERUT RRTS CORRIDOR	3/2019	6/2025 (-) [6/2025]	30,274.00 (-) [30,274.00]	4,567.75 (0.00) [0]
NAGALAND					
Railways					
1143	DIMAPUR-TIZIT NL	4/2013	3/2020 (-) [0/0]	4,274.00 (-) [4,274.00]	0.00 (0.00) [0]
1144	NEW LINE FROM DIMAPUR TO ZUBZA(KOHIMA)	4/2006	3/2015	2,326.52	1,300.10

	NATIONAL PROJECT (NEFR)		(-) [3/2026]	(-) [6,911.00]	(4,584.48) [132]
	<u>Road Transport And Highways</u>				
1145	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 25.760 TO	3/2018	9/2018 (-) [5/2022]	239.30 (-) [239.30]	112.70 (0.00) [44]
1146	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 52.370 TO	3/2018	9/2018 (-) [9/2022]	285.68 (-) [285.68]	82.34 (0.00) [48]
1147	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 40.090 TO KM65.	3/2018	9/2018 (-) [11/2021]	282.98 (-) [282.98]	153.26 (0.00) [38]
1148	(I) CONSTRUCTION OF FOUR/SIX LANING FROM KM 132.375 TO KM 158.058 (TOTAL NEW ALIGNMENT LENGTH OF 20.	2/2017	9/2018 (-) [3/2022]	387.00 (-) [387.00]	309.45 (0.00) [42]
1149	(II) CONSTRUCTION OF DIMAPUR BYPASS (ASSAM PORTION) OF 4/6 LANE PAVEMENT ON EPC BASIS FROM EXISTING	3/2018	9/2018 (-) [11/2022]	500.09 (-) [500.09]	107.72 (0.00) [50]
1150	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE I)	3/2020	6/2022 (-) [6/2022]	320.97 (-) [320.97]	31.88 (0.00) [0]
1151	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE II)	3/2020	6/2022 (-) [6/2022]	355.79 (-) [355.79]	55.79 (0.00) [0]
1152	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE III)	3/2020	6/2022 (-) [6/2022]	361.53 (-) [361.53]	23.62 (0.00) [0]
1153	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE IV)	3/2020	12/2021 (-) [12/2021]	330.78 (-) [330.78]	40.40 (0.00) [0]
1154	2 LANING OF KOHIMA - JESSAMI SECTION (PACKAGE V)	4/2020	12/2021 (-) [12/2021]	330.80 (-) [330.80]	30.14 (0.00) [0]
1155	2-LANING OF CHANGTONGYA TO LONGLENG ROAD OF NH-702 (PKG-I)	3/2020	6/2022 (-) [6/2022]	278.95 (-) [278.95]	68.48 (0.00) [0]
1156	CONSTRUCTION OF 2 LANE WITH PAVED SHOULDER FROM KM. 168 TO 183.783 (YESEMYONG TO UNGER) ON MOKOKCHUN	3/2017	11/2020 (8/2021) [8/2021]	217.35 (-) [217.35]	97.62 (0.00) [9]
1157	CONSTRUCTION OF 2-LANE WITH HARD SHOULDER OF PEREN-DIMAPUR SECTION ON NH129A FROM DESIGN KM109.494 T	9/2020	4/2022 (-) [4/2022]	257.15 (-) [257.15]	40.94 (0.00) [0]
1158	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DSIGN KM32.0 TO KM43.454 [DES	8/2020	4/2022 (-) [4/2022]	202.36 (-) [202.36]	0.00 (0.00) [0]
1159	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM 0.00 TO KM 10.500 [D	8/2020	4/2022 (-) [4/2022]	232.29 (-) [232.29]	4.98 (0.00) [0]
1160	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM10.500 TO 21.00KM [D	9/2020	10/2022 (-) [10/2022]	277.44 (-) [277.44]	26.41 (0.00) [0]
1161	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF KOHIMA-BYPASS ROAD FROM DESIGN KM21.0 TO KM32.0 [DESIG	8/2020	10/2022 (-) [10/2022]	159.85 (-) [159.85]	2.80 (0.00) [0]
1162	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [7/2022]	339.57 (-) [339.57]	161.84 (0.00) [46]
1163	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM 79.040 TO	3/2018	9/2018 (-) [12/2021]	315.03 (-) [315.03]	101.42 (0.00) [39]
1164	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS	3/2018	9/2018	240.64	112.90

	OF CHAKABAMA-ZUNHEBOTO ROAD FROM EXISTING KM100.345 TO		(-) [12/2021]	(-) [240.64]	(0.00) [39]
1165	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 00.000 TO	3/2018	9/2018 (-) [11/2021]	215.12 (-) [215.12]	107.31 (0.00) [38]
1166	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 20.456 TO	3/2018	9/2018 (-) [12/2021]	215.79 (-) [215.79]	70.57 (0.00) [39]
1167	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 41.065 TO	3/2018	9/2018 (-) [10/2022]	272.89 (-) [272.89]	59.98 (0.00) [49]
1168	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF MERANGKONG-TAMLU-MON ROAD FROM EXISTING KM 60.345 TO	3/2018	9/2018 (-) [11/2022]	323.98 (-) [323.98]	50.13 (0.00) [50]
1169	CONSTRUCTION OF TWO LANE WITH HARD SHOULDERS OF PFUTSERO-PHEK ROAD FROM EXISTING KM 19.900 TO KM40.0	3/2018	9/2018 (-) [11/2021]	251.97 (-) [251.97]	146.10 (0.00) [38]
1170	CONSTRUCTION OF TWO-LANE WITH HARD SHOULDERS OF PFUTSERO PHEK ROAD FROM EXISTING KM 00.000 TO KM19.9	3/2018	9/2018 (-) [11/2021]	237.72 (-) [237.72]	120.12 (0.00) [38]
1171	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 123.840 TO KM 138.775 (EXISTING KM 124.100 TO KM 1	3/2016	8/2016 (-) [5/2021]	373.07 (-) [387.00]	325.21 (13.93) [0]
1172	FOUR LANING OF DIMAPUR KOHIMA ROAD FROM DESIGN KM 138.775 TO KM 152.490 (EXISTING KM 140.000 TO KM 1	3/2016	8/2016 (-) [5/2021]	396.52 (-) [396.52]	298.94 (0.00) [0]
1173	FOUR LANING OF EXISTING DIMAPUR KOHIMA ROAD FROM DESIGN KM 152.490 TO KM 166.700 (EXISTING KM 156.00	3/2016	8/2016 (-) [2/2021]	429.52 (-) [429.52]	238.28 (0.00) [0]
1174	IMPROVEMENT OF CITY PORTION OF KOHIMA AND DIMAPUR CITY OF NH-39 IN THE STATE OF NAGALAND UNDER EPC M	11/2016	9/2019 (-) [0/0]	336.25 (369.96) [369.96]	322.13 (33.71) [0]
1175	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [9/2021]	167.62 (-) [167.62]	104.39 (0.00) [9]
1176	STRENGTHENING AND WIDENING TO TWO LANE WITH PAVED SHOULDER OF NH-61 FROM KM 40.00 TO KM 72.40 UNDER	10/2016	12/2020 (9/2021) [9/2021]	172.63 (-) [172.63]	129.65 (0.00) [9]
1177	UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KOHIMA TO MAO FROM KM 185.540 TO KM	9/2020	4/2022 (-) [4/2022]	315.63 (-) [315.63]	7.28 (0.00) [0]
1178	WIDENING OF EXISTING SINGLE/INTERMEDIATE LANE ROAD TO 2 LANE ROAD FROM KM. 83.00 TO KM 101.00 ON NH-	3/2019	12/2022 (-) [12/2022]	237.51 (-) [237.51]	75.42 (0.00) [0]
	ODISHA				
	Coal				
1179	ANANTA OC EXPANSION PH-III (15.0 MTY)	8/2008	3/2012 (-) [3/2021]	207.28 (-) [207.28]	204.49 (0.00) [0]
1180	BASUNDHARA (WEST) OC EXTN(7.00 MTY)	5/2014	3/2019 (-) [3/2024]	479.15 (-) [479.15]	226.00 (0.00) [60]
1181	BHUBANESWARI EXPENSION OCP(40.0 MTY)	12/2007	3/2017 (-) [3/2031]	3,145.45 (-) [3,145.45]	589.39 (0.00) [168]
1182	EXPANSION PR OF BALRAM EXPANSION OCP(15 MTY)	12/2007	3/2010 (3/2029) [3/2029]	3,504.21 (3,504.21) [3,504.21]	589.67 (0.00) [228]
1183	EXPANSION PR OF GOPAL JI KANIHA OCP(30.0 MTY)	12/2007	3/2013 (3/2028) [3/2028]	8,416.19 (8,416.19) [8,416.19]	918.79 (0.00) [180]

1184	GARJANBAHAL OCP	11/2014	3/2021 (-) [9/2025]	1,375.38 (-) [1,375.38]	581.31 (0.00) [54]
1185	HINGULA OC-II EXP. PH-III (15 MTY)	11/2008	3/2013 (-) [3/2024]	479.53 (-) [703.39]	703.39 (223.86) [132]
1186	INTEGRATED LAKHANPUR-BELPAHAR-LILARI OCP	5/2018	3/2027 (-) [3/2027]	2,434.75 (-) [2,434.75]	499.88 (0.00) [0]
1187	NAINI COAL MINE	3/2020	3/2024 (-) [3/2024]	494.30 (-) [494.30]	73.09 (0.00) [0]
1188	REORGANISATION OF BHARATPUR OCP EXPANSION	11/2018	3/2029 (-) [3/2029]	2,838.87 (-) [2,838.87]	1,271.62 (0.00) [0]
1189	SIARMAL OCP (40.00MTY)	5/2014	3/2026 (-) [3/2026]	3,756.36 (-) [3,756.36]	2,180.34 (0.00) [0]
1190	TALABIRA II AND III OCP	7/2017	7/2020 (-) [4/2020]	2,401.07 (-) [2,401.07]	802.61 (0.00) [0]
	<u>Department Of Higher Education</u>				
1191	INDIAN INSTITUTE OF SCIENCE EDUCATION AND RESEARCH BERHAMPUR	1/2019	3/2022 (-) [6/2022]	790.79 (-) [790.79]	213.06 (0.00) [3]
	<u>Mines</u>				
1192	5TH STREAM ALUMINA REFINERY EXPANSION PROJECT	12/2014	4/2021 (12/2022) [12/2022]	5,540.00 (6,435.90) [5,540.00]	788.26 (0.00) [20]
1193	CONVERSION OF FLAT BOTTOM SETTLERS AND WASHERS WITH A SINGLE TRAIN OF HRDS AND DCWS IN STREAMS 1 AND	12/2015	11/2020 (-) [2/2021]	355.00 (-) [355.00]	95.45 (0.00) [0]
1194	SOURCING OF BAUXITE ARRANGEMENT FOR 5TH STREAM ALUMINA REFINERY FROM SOUTH BLOCK MINING LEASE OF PAN	11/2017	4/2021 (3/2023) [3/2023]	483.00 (483.00) [483.00]	2.68 (0.00) [23]
1195	UTKAL D AND E COAL BLOCK	5/2016	1/2020 (-) [0/0]	534.00 (-) [534.00]	349.66 (0.00) [0]
	<u>Petroleum</u>				
1196	2ND GENERATION LIGNOCELLUOSIC BIOMASS ETHANOL BIOFUEL REFINERY AT BARGARH (ODISHA)	8/2019	8/2022 (-) [8/2022]	1,607.00 (-) [1,607.00]	263.13 (0.00) [0]
1197	ADDITIONAL STORAGE TANKS AT PARADIP	11/2018	9/2021 (6/2022) [6/2022]	462.30 (-) [462.30]	87.24 (0.00) [9]
1198	CAPTIVE NATURAL GAS PIPELINE FROM DAHEJ TO KOYALI REFINERY	8/2017	12/2021 (8/2021) [9/2021]	315.00 (-) [315.00]	225.95 (0.00) [-3]
1199	CITY GAS DISTRIBUTION (CGD) NETWORK BHUBANESHWAR	7/2017	7/2022 (-) [7/2022]	243.53 (-) [243.53]	132.46 (0.00) [0]
1200	CITY GAS DISTRIBUTION (CGD) NETWORK, CUTTACK	7/2017	7/2022 (-) [7/2022]	182.20 (-) [182.20]	85.28 (0.00) [0]
1201	DHAMRA-ANGUL PIPELINE PROJECT	3/2017	12/2020 (12/2021) [12/2021]	1,933.00 (-) [1,933.00]	1,456.60 (0.00) [12]
1202	ETHYLENE GLYCOL PROJECT AT PARADIP	4/2018	10/2021 (-) [10/2021]	5,654.00 (-) [5,654.00]	3,161.40 (0.00) [0]
1203	Fuel Quality Upgradation Project at Paradip Refinery	5/2019	8/2021	3,361.00	1,977.07

			(9/2022) [9/2022]	(-) [3,361.00]	(0.00) [13]
1204	INFRASTRUCTURE DEVELOPMENT FOR UTILIZATION OF NATURAL GAS AT PARADIP REFINERY	1/2020	7/2022 (-) [7/2022]	202.16 (-) [202.16]	16.19 (0.00) [0]
1205	INSTALLATION OF STANDBY SRU TRAIN OF 525 TPD ALONGWITH INCINERATOR AT PARADIP REFINERY	6/2019	9/2022 (3/2023) [3/2023]	371.00 (427.00) [427.00]	25.79 (56.00) [6]
1206	INTEGRATED PARA XYLENE (PX) AND PURIFIED TEREPHTHALIC ACID (PTA) PROJECT AT PARADIP REFINERY	7/2020	1/2024 (-) [1/2024]	13,805.00 (-) [13,805.00]	295.70 (0.00) [0]
1207	LPG BP PROJECT KHORDHA	12/2016	12/2019 (3/2022) [3/2022]	161.59 (-) [161.59]	53.22 (0.00) [27]
1208	PARADIP SOMNATHPUR HALDIA PIPELINE	10/2018	10/2021 (-) [3/2022]	1,297.50 (-) [1,297.50]	795.89 (0.00) [5]
	<u>Power</u>				
1209	ROURKELA PP-II EXPANSION (1X250 MW) - NSPCL	5/2016	12/2018 (-) [11/2021]	1,885.13 (2,311.89) [2,311.89]	1,892.27 (426.76) [35]
	<u>Railways</u>				
1210	BANASPANI- JAKHPURA - DOUBLING	3/2009	3/2019 (-) [6/2022]	942.95 (-) [1,536.00]	1,054.76 (593.05) [39]
1211	BHADRAK - NERGUNDI 3RD LINE	3/2013	10/2020 (3/2024) [3/2024]	843.04 (843.04) [843.04]	248.28 (0.00) [41]
1212	BUDHAPANK - SALEGAON VIA RAJATGARH 3RD AND 4TH LINE	4/2015	12/2018 (3/2024) [3/2024]	1,172.92 (1,172.92) [1,172.92]	653.15 (0.00) [63]
1213	CHAMPAJHARAN-BIMALGARH DOUBLING EXTENSION	4/2010	3/2015 (-) [0/0]	149.90 (-) [230.00]	54.46 (80.10) [0]
1214	EXECUTION OF RAIL CONNECTIVITY PROJECT FOR COAL TRANSPORTATION IN ODISHA FOR MCRL	4/2016	3/2020 (-) [3/2024]	5,200.00 (-) [962.00]	54.75 (-4,238.00) [48]
1215	HARIDASPUR-PARADEEP(NL)	4/1996	12/2017 (-) [0/0]	1,185.64 (-) [1,844.47]	1,883.44 (658.83) [0]
1216	JAGADALPUR-KORAPUT DOUBLING	4/2015	3/2022 (3/2023) [3/2023]	1,547.38 (1,547.38) [1,547.38]	678.19 (0.00) [12]
1217	JARAPADA - BUDHAPANK WITH FLY OVER AT TALCHER ROAD 3RD AND 4TH LINE	4/2015	11/2018 (3/2024) [3/2024]	701.61 (-) [810.02]	192.59 (108.41) [64]
1218	KHURDA ROAD - BARANG 3RD LINE (DL) (ECOR)	4/2000	3/2009 (3/2009) [0/0]	133.41 (207.00) [396.00]	388.21 (262.59) [0]
1219	KHURDA ROAD-BOLANGIR(NL)ECOR	4/1994	3/2009 (3/2026) [3/2026]	2,923.13 (3,791.66) [3,791.66]	1,602.15 (868.53) [204]
1220	KORAPUT - SINGAPUR ROAD DOUBLING	4/2015	3/2022 (-) [3/2026]	2,361.74 (-) [2,361.74]	450.42 (0.00) [48]
1221	ROURKELA JHARSUGUDA THIRD LINE 101 KM	11/2015	3/2020 (-) [2/2022]	969.83 (-) [1,312.96]	1,018.29 (343.13) [23]
1222	SAMBALPUR - ANGUL RLY. ELECTRIFICATION	3/2012	3/2020 (-) [3/2022]	155.81 (238.03) [238.03]	222.65 (82.22) [24]

1223	SAMBALPUR - TITLAGARH - DOUBLING	3/2006	3/2020 (-) [12/2021]	948.04 (-) [2,009.00]	1,532.13 (1,060.96) [21]
1224	SAMBALPUR-TALCHER DOUBLING	3/2011	2/2019 (-) [12/2021]	1,111.99 (-) [1,539.28]	1,186.14 (427.29) [34]
1225	SUKINDA ROAD - ANGUL (NL)(ECOR)	4/1998	2/2015 (-) [6/2022]	1,202.70 (-) [2,440.53]	1,066.19 (1,237.83) [88]
1226	TALCHER-BIMALAGARH(NL)(ECOR)	4/2005	6/2021 (3/2025) [3/2025]	810.78 (1,928.07) [1,928.07]	895.94 (1,117.29) [45]
1227	VIZIANAGARAM -SAMBALPUR 3RD LINE	1/1991	12/2024 (-) [12/2026]	2,335.67 (-) [3,327.72]	794.54 (992.05) [24]
	Road Transport And Highways				
1228	4 LANING OF BAHARAGORA - SINGHARA	7/2015	/ (-) [0/0]	1,282.94 (-) [1,282.94]	720.08 (0.00) [0]
1229	DEVELOPMENT OF FOUR LANNING OF ANGUL-SAMBALPUR SECTION OF NATIONAL HIGHWAY NH-42 (NEW NH-55 IN THE S	9/2016	8/2019 (-) [0/0]	2,510.04 (-) [2,510.04]	633.26 (0.00) [0]
1230	FOUR LANING WITH PS TALEBANI -SMBALPUR	12/2015	/ (-) [3/2022]	752.28 (-) [752.28]	272.74 (0.00) [-]
1231	JHARPOKHARIA-BARIPADA-BALESHWAR SECTION	2/2016	/ (-) [0/0]	1,069.65 (-) [1,069.65]	836.93 (0.00) [0]
1232	PANIKHOLI-RIMOLI	3/2012	9/2014 (-) [0/0]	1,410.00 (-) [1,410.00]	11.20 (0.00) [0]
1233	REHABILITATION AND UPGRADATION TO FOUR LANING OF BINJHABAHAL TO TELEBANI SECTION, KM 414.000 TO KM 4	10/2016	/ (-) [0/0]	1,008.96 (-) [1,008.96]	1,125.65 (0.00) [0]
1234	REHABILITATION AND UP GRADATION OF EXISTING 2-LANE TO 4-LANE STANDARDS TO END OF KAMAKHYANAGAR BYPAS	1/2018	/ (-) [8/2021]	564.66 (-) [564.66]	341.88 (0.00) [-]
1235	REHABILITATION AND UP-GRADATION OF BIRAMITRAPUR TO BRAHMANI BYPASS (PKG-I)	7/2017	7/2017 (-) [0/0]	476.56 (-) [476.56]	189.84 (0.00) [0]
1236	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF DUBURI (KM 388.376) TO CHANDIKHOLE (	1/2018	/ (-) [0/0]	633.68 (-) [633.68]	118.00 (0.00) [0]
1237	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF KOIDA (KM206.20) TO RAJAMUNDA (KM 25	1/2018	/ (-) [3/2022]	953.09 (-) [953.09]	438.00 (0.00) [-]
1238	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO 4 LANE OF RIMULI (KM 163.0) TO KOIDA (KM 206.2	1/2018	/ (-) [0/0]	668.86 (-) [668.86]	372.00 (0.00) [0]
1239	REHABILITATION AND UP-GRADATION OF EXISTING 2-LANE TO FOUR LANE FROM TALCHAR TO END OF KAMAKHYANAG	1/2018	/ (-) [8/2021]	614.48 (-) [614.48]	277.00 (0.00) [-]
1240	REHABILITATION AND UP-GRADATION TO 4-LANING OF RAJAMUNDA-BARKOTE SECTION OF NH-23 (NEW NH NO. 143) (	1/2018	/ (-) [0/0]	503.88 (-) [503.88]	100.21 (0.00) [0]
1241	REHABILITATION AND UPGRADATION BY 4-LANING OF SINGHARA TO BINJHABAHAL SECTION FROM KM 311.000 TO KM	3/2017	3/2020 (-) [0/0]	1,288.07 (-) [1,420.00]	1,021.47 (131.93) [0]
1242	REHABILITATION AND UPGRADATION OF CUTTACK ANGUL SECTION OF NH-42 (NEW NH-55) TO 4 LANE (KM. 0+400 TO	12/2017	/ (-) [0/0]	686.65 (-) [686.65]	290.00 (0.00) [0]

1243	REHABILITATION AND UPGRADATION OF CUTTACK-ANGUL SECTION TO 4 LANE (KM 60.20) TO (KM 112.0) PKG II ON	1/2018	/	686.65	254.00
			(-)	(-)	(0.00)
			[0/0]	[686.65]	[0]
1244	REHABILITATION AND UPGRADATION OF FOUR LANING OF NH-23 (NEW NH NO. 143) FROM KM. 240.250 I.E. BRAHMA	12/2017	/	417.51	213.88
			(-)	(-)	(0.00)
			[0/0]	[417.51]	[0]
1245	REHABILITATION AND UPGRADATION OF SIX LANING OF BHADRAK BALESHWAR SECTION (KM 136.50) TO (KM 199.141)	1/2018	/	999.00	178.00
			(-)	(-)	(0.00)
			[0/0]	[999.00]	[0]
1246	REHABILITATION AND UPGRADING TO 2 LANE WITH PAVED SHOULDER CONFIGURATION AND STRENGTHENING OF NAUPAR	8/2013	6/2016	171.96	100.67
			(-)	(172.00)	(0.04)
			[0/0]	[172.00]	[0]
1247	REHABILITATION SIX LANING UPGRADATION CHANDIKHOLE BHADRAK	1/2018	/	1,522.00	512.80
			(-)	(-)	(0.00)
			[0/0]	[1,522.00]	[0]
1248	SIX LANING OF CHANDIKHOL-JAGATPUR-BHUBANESWAR	12/2011	6/2014	1,047.00	1,873.47
			(-)	(-)	(0.00)
			[0/0]	[1,047.00]	[0]
1249	SIX LANNING OF NH-5 (NEW NH-16) FROM TANGI TO BHUBANESHWAR (KM 355.000 TO KM 414.000)	3/2018	/	806.11	320.00
			(-)	(-)	(0.00)
			[0/0]	[806.11]	[0]
1250	WIDENING AND STRENGTHENING OF EXISTING SL IL TO 2 LANE CARRIAGEWAY WITH PAVED SHOULDER INCLUDING GEO	3/2014	5/2016	191.50	183.94
			(-)	(192.00)	(0.50)
			[0/0]	[192.00]	[0]
1251	WIDENING TO 2 LANE AND IMPROVEMENT VIJAYWADA RANCI ROUTE FROM KM 377-700 TO 471-900 (BERHMAPUR-TAPTA)	12/2011	8/2015	191.08	182.41
			(-)	(-)	(0.00)
			[0/0]	[191.08]	[0]
1252	WIDENING TO 2LPS FROM 0/0 TO 119/0 OF NH-157 IN THE STATE OF ODISHA.	8/2016	2/2017	287.70	208.32
			(-)	(-)	(0.00)
			[0/0]	[287.70]	[0]
1253	WIDENING TO 2LPS FROM 173/37 TO 229/40 OF NH-59 IN THE STATE OF ODISHA	3/2018	8/2018	214.23	108.98
			(-)	(-)	(0.00)
			[0/0]	[214.23]	[0]
1254	WIDENING TO 2LPS FROM 239/9 TO 294/3 OF NH-57 (NAYAGARH TO KHURDA) IN THE STATE OF ODISHA	12/2016	8/2018	223.50	134.34
			(-)	(-)	(0.00)
			[0/0]	[223.50]	[0]
1255	WIDENING TO 2LPS FROM 269/30 TO 328/20 OF NH-49 IN THE STATE OF ODISHA	3/2018	8/2018	199.16	122.77
			(-)	(-)	(0.00)
			[0/0]	[199.16]	[0]
1256	WIDENING TO 2LPS FROM 50/0 TO 140/9 OF NH-57 (SONEPUR TO MADHAPUR) IN THE STATE OF ODISHA	9/2016	2/2017	295.67	201.80
			(-)	(-)	(0.00)
			[0/0]	[295.67]	[0]
1257	WIDENING TO 2LPS FROM 58/00 TO 116/10 OF NH-153B (NAKTIDEUL TO BOUDH) IN THE STATE OF ODISHA	12/2016	4/2018	206.88	123.55
			(-)	(-)	(0.00)
			[0/0]	[206.88]	[0]
	<u>Steel</u>				
1258	REBUILDING OF COKE OVEN BATTERY-2 ALONGWITH AUGMENTATION OF COKE HANDLING AND GAS HANDLING FACILITY	11/2020	5/2023	377.18	37.11
			(-)	(-)	(0.00)
			[5/2023]	[377.18]	[0]
	<u>PONDICHERRY</u>				
	<u>Health And Family Welfare</u>				
1259	CONST OF 152 QTRS 240 BOYS 240 GIRLS 150 NURSES HOSTEL AND OTHER BUILDINGS INCLUDING DEVELOPMENT	3/2018	9/2020	195.00	16.41
			(-)	(-)	(0.00)
			[4/2022]	[195.00]	[19]
	<u>PUNJAB</u>				
	<u>Department Of Higher Education</u>				
1260	CONSTRUCTION OF PERMANENT CAMPUS OF INDIAN INSTITUTE OF MANAGEMENT (IIM) AMRITSAR, PUNJAB.	10/2019	5/2022	348.24	23.28
			(-)	(-)	(0.00)
			[10/2022]	[348.24]	[5]
1261	CONSTRUCTION OF VARIOUS BUILDINGS UNDER PHASE 1C AT IIT ROPAR, PUNJAB	1/2018	5/2020	430.00	218.29
			(-)	(-)	(-42.17)

			[3/2022]	[387.83]	[22]
	Fertilisers				
1262	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL BATHINDA	1/2018	11/2019 (5/2021) [4/2021]	218.83 (-) [218.83]	194.44 (0.00) [0]
1263	GAS TURBO GENERATOR AND HEAT RECOVERY STEAM GENERATOR PROJECT NFL NANGAL	1/2018	11/2019 (5/2021) [4/2021]	239.81 (-) [239.81]	204.01 (0.00) [0]
	Health And Family Welfare				
1264	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT BATHINDA, PUNJAB	7/2016	6/2020 (-) [10/2021]	703.00 (-) [557.48]	513.24 (-145.52) [16]
1265	SATELLITE CENTRE PGI CHANDIGARH SANGRUR PUNJAB	7/2016	2/2018 (-) [3/2021]	152.95 (-) [177.92]	164.17 (24.97) [0]
	Petroleum				
1266	SECOND GENERATION ETHANOL BIOREFINERY PROJECT, BATHINDA, PUNJAB	5/2020	2/2023 (-) [2/2023]	1,421.46 (-) [1,244.50]	101.45 (-176.96) [0]
	Railways				
1267	MANSA-BHATINDA (PHASE-I), INCL. NEW MATERIAL MODIFICATION FOR RAMA MANDI (RAMAN) - SADA SINGHWALA VI	6/2009	8/2016 (-) [8/2025]	404.00 (-) [404.00]	190.00 (0.00) [108]
1268	QADIAN-BEAS	4/2011	/ (-) [3/2024]	205.22 (-) [841.90]	1.73 (636.68) [-]
	Road Transport And Highways				
1269	4 LANING FROM PHAGWARA TO RUPNAGAR	8/2016	/ (-) [0/0]	1,169.61 (1,367.00) [2,280.00]	1,367.00 (1,110.39) [0]
1270	4-LANING OF MOGA -TALLEWAL SECTION OF NH-71 FROM KM 77.200 TO 114.00	11/2015	/ (-) [0/0]	889.24 (-) [904.82]	766.98 (15.58) [0]
1271	4/6 LANING FROM KHARAR TO LUDHIYANA FROM KM 10.185 (DESIGN CHAINAGE) TO KM 86.199(DESIGN CHAINAGE)	8/2016	9/2019 (-) [0/0]	1,388.34 (-) [1,588.29]	798.71 (199.95) [0]
1272	CONSTRUCTION OF PARTIALLY ACCESS CONTROLLED FOUR LANE ELEVATED HIGHWAY BETWEEN SAMRALA CHOWK (DESIGN	3/2017	3/2020 (-) [9/2022]	754.54 (-) [756.27]	430.26 (1.73) [30]
1273	FOUR LANING OF EXISTING TWO LANE WITH PS FROM TALWANDI BHAI TO FEROZPUR IN THE STATE OF PUNJAB	2/2018	/ (-) [7/2021]	261.76 (-) [207.00]	201.67 (-54.76) [0]
1274	FOUR LANNING OF LUDHIYANA- TALWANDI SECTION	9/2014	/ (-) [3/2022]	479.00 (-) [479.00]	456.80 (0.00) [-]
1275	JALANDHAR-HOSHIARPUR SECTION OF NH-70 [NEW NH NO. 3] FROM EXISTING KM 11.400 TO KM 49.200	10/2017	10/2019 (-) [8/2021]	1,069.59 (-) [1,069.59]	728.55 (0.00) [22]
1276	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-21) OF SECTION KHEMKARAN TOWN TO START OF AMRI	3/2018	/ (-) [0/0]	196.05 (-) [196.05]	143.03 (0.00) [0]
1277	REHABILITATION AND AUGMENTATION OF NEW NH 354 (OLD-SH-25) OF SECTION RAMDAS TO GURDASPUR FROM DESIGN	3/2018	/ (-) [0/0]	199.90 (-) [199.90]	124.52 (0.00) [0]
1278	REHABILITATION AND UP GRADATION TO 2 LANE WITH PAVED SHOULDER OF NH-703A FROM MAKHU (DESIGN CH 0 000	3/2018	11/2020 (-) [0/0]	170.57 (-) [170.57]	65.41 (0.00) [0]
1279	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHOULDER OF MOGA (DESIGN CH 0.000) TO MAKHU (DES	3/2018	8/2020 (-) [0/0]	293.64 (-) [293.64]	259.00 (0.00) [0]
1280	WIDENING AND PAVED SHOULDER OF TOHANA (IN	3/2018	8/2020	293.10	166.39

	HARYANA) PUNJAB/HARYANA BORDER TO MOONAK-JAKHAL-BUDHLADA		(-) [0/0]	(-) [293.10]	(0.00) [0]
	<u>RAJASTHAN</u>				
	<u>Atomic Energy</u>				
1281	RAJASTHAN ATOMIC POWER PROJECT -7 AND 8 (2X700 MW)	10/2009	12/2016 (-) [3/2023]	12,320.00 (-) [17,079.00]	13,528.00 (4,759.00) [75]
	<u>Coal</u>				
1282	BARSINGSAR THERMAL POWER STATION EXTENSION	3/2015	9/2020 (-) [0/0]	2,112.60 (-) [2,112.60]	93.05 (0.00) [0]
1283	BITHNOK LIGNITE MINE PROJECT (2.25 MTPA)	3/2015	12/2019 (-) [0/0]	513.63 (-) [513.63]	175.30 (0.00) [0]
1284	BITHNOK LIGNITE THERMAL POWER STATION	3/2015	9/2020 (-) [0/0]	2,196.30 (-) [2,196.30]	143.95 (0.00) [0]
1285	HADLA LIGNITE MINE PROJECT(1.90 MTPA)	3/2015	9/2019 (-) [0/0]	522.45 (-) [522.45]	9.88 (0.00) [0]
	<u>Department Of Higher Education</u>				
1286	DEVELOPMENT OF PERMANENT CAMPUS FOR IIT JODHPUR (PHASE II) AT KARWAR, JODHPUR RAJASTHAN	12/2016	7/2019 (-) [0/0]	549.31 (-) [559.47]	458.38 (10.16) [0]
	<u>Petroleum</u>				
1287	LPG BP PROJECT JODHPUR	3/2018	/ (5/2022) [5/2022]	229.80 (-) [229.80]	85.09 (0.00) [-]
	<u>Power</u>				
1288	ANTA SOLAR 90 MW	1/2021	3/2022 (-) [3/2022]	382.22 (-) [382.22]	0.00 (0.00) [0]
1289	BHENSARA 320 MW	1/2021	7/2022 (-) [7/2022]	1,221.73 (-) [1,221.73]	137.36 (0.00) [0]
1290	CHHATTARGARH 150 MW	2/2021	7/2022 (-) [7/2022]	599.99 (-) [559.98]	60.85 (-40.01) [0]
1291	FATEHGARH SOLAR 296MW	3/2020	9/2021 (2/2022) [2/2022]	1,749.31 (-) [1,749.31]	1,125.51 (0.00) [5]
1292	JETSAR SOLAR 160 MW	12/2019	3/2021 (11/2021) [11/2021]	702.28 (-) [702.28]	529.41 (0.00) [8]
1293	SAMBHU KI BHURJ SOLAR 250 MW	1/2020	9/2021 (10/2022) [1/2022]	1,522.71 (-) [1,522.71]	894.14 (0.00) [4]
1294	SAMBHU KI BHURJ-II SOLAR 300MW	3/2020	9/2021 (7/2022) [9/2022]	1,782.00 (-) [1,782.00]	527.71 (0.00) [12]
	<u>Railways</u>				
1295	AJMER(NASIRABAD)- SAWAI MADHOPUR (CHAUTH KA BARWARA) VIS TONK NL	5/2015	/ (-) [0/0]	873.71 (-) [2,215.27]	4.60 (1,341.56) [0]
1296	AJMER-BANGURGRAM	4/2011	11/2019 (-) [3/2021]	213.39 (-) [375.00]	361.04 (161.61) [0]
1297	AJMER-KOTA (NASIRABAD-JAUNDRI)	4/2013	/ (-) [0/0]	822.00 (-) [821.64]	0.00 (-0.36) [0]
1298	ALWAR-BANDIKUI DOUBLING	4/2013	2/2019	242.09	473.86

			(-) [2/2020]	(-) [525.00]	(282.91) [0]
1299	BANGURGRAM-GURIYA PATCH DOUBLING	4/2012	12/2019 (-) [3/2021]	246.08 (-) [395.00]	366.38 (148.92) [0]
1300	DAUSA-GANGAPUR CITY(NL),NWR	2/1997	2/2019 (-) [6/2022]	410.08 (-) [860.41]	745.83 (450.33) [40]
1301	JODHPUR (RAI KA BAGH) - DEGANA DOUBLING (145 KM)	8/2018	8/2022 (-) [11/2022]	808.85 (-) [808.85]	275.78 (0.00) [3]
1302	MAVLI JUNCTION-BARI SADRI, MM OF AJMER-CHITTSURGARH-UDAIPUR	4/2013	3/2020 (-) [9/2021]	420.18 (-) [480.00]	371.38 (59.82) [18]
1303	MULTI MODAL LOGISTICS PARK AT KATHUWAS	1/2011	3/2018 (-) [0/0]	493.17 (-) [493.17]	464.53 (0.00) [0]
1304	PUSHKAR-MERTA	4/2013	/ (-) [0/0]	323.00 (-) [322.98]	0.00 (-0.02) [0]
1305	THIYAT HAMIRA-SANU	4/2013	10/2018 (-) [1/2020]	236.93 (-) [350.45]	287.39 (113.52) [0]
	<u>Road Transport And Highways</u>				
1306	NAGAU-BIKANER SECTION FROM KM 177.00 TO KM 267.325 ON NH-89	3/2020	8/2022 (-) [8/2022]	370.36 (-) [370.36]	178.51 (0.00) [0]
1307	2 LANING WITH PS OF GULABPURA - UNIARA	10/2015	10/2017 (-) [0/0]	597.00 (-) [597.00]	0.00 (0.00) [0]
1308	2-LANE WITH PAVED SHOULDER WITH PROVISION OF CAPACITY AUGMENTATION OF RAJASTHAN BORDER-FATEHPUR-SALA	11/2012	8/2016 (-) [6/2020]	530.07 (-) [530.07]	556.02 (0.00) [0]
1309	4/2 LANNING WITH PS DAUSA-LALSOT-KAUTHUN SECTION OF NH-11A	7/2016	/ (-) [0/0]	688.70 (-) [688.70]	870.48 (0.00) [0]
1310	6-LANNING OF KISHANGARH TO GULABPURA SECTION OF NH-79A AND NH-79 IN THE STATE OF RAJASATHAN(PACKAGE-	12/2016	/ (-) [3/2022]	1,031.95 (-) [1,031.95]	0.00 (0.00) [-]
1311	ALWAR NUH SECTION ON EPC MODE IN THE STATE OF RAJASTHAN.	3/2019	/ (-) [0/0]	178.13 (-) [178.13]	158.26 (0.00) [0]
1312	BIKANER - PHALODI SECTION TO FOUR LANING FROM KM.4.200 TO KM 55.25 AND TWO-LANE PAVED SHOULDER FROM	8/2014	4/2018 (-) [9/2021]	822.90 (-) [822.90]	844.08 (0.00) [41]
1313	CONSTRUCTION / UP-GRADATION OF 2-LANE WITH PAVED SHOULDER OF NH-70 FROM MUNABAO (NH-25E)-TANOT FROM	3/2018	/ (-) [0/0]	1,158.35 (-) [1,158.35]	496.04 (0.00) [0]
1314	CONSTRUCTION OF TWO LANE FLEXIBLE PAVEMENT WITH PAVED SHOULDER FROM KM 3.650 TO KM 58.325 OF NH-709	11/2017	4/2018 (-) [7/2020]	163.95 (-) [163.95]	116.47 (0.00) [0]
1315	CONSTRUCTION/ UP-GRATION OF FOUR/TWO LANE WITH PAVED SHOULDER OF NH68 FROM TANOT-RAMGARH BHADASAR-JA	2/2018	/ (-) [0/0]	741.86 (-) [741.86]	225.92 (0.00) [0]
1316	FOUR LANING OF DANGIAWAS (KM 96.595 TO NH-112) TO JAJIWAL (KM 283.500 OF NH 65 NAGAU ROAD) SECTIO	12/2017	/ (-) [0/0]	1,308.73 (-) [1,308.73]	330.46 (0.00) [0]
1317	FOUR LANING OF MAHUA TO KAGAVADAR OF NH-8E FROM KM. 100.100 TO KM 139.915 (DESIGN CHAINAGE FROM KM	6/2016	6/2019 (-) [0/0]	763.23 (-) [763.23]	191.80 (0.00) [0]
1318	FOUR LANNING OF BAR-BILARA-JODHPUR SECTION OF	6/2016	6/2019	649.00	646.79

	NH-112 (EXISTING KM 0+000 TO KM		(-) [0/0]	(-) [649.00]	(0.00) [0]
1319	FOUR LANNING OF DARAH-JHALWAR-TEENDHAR FROM KM 29.000 TO KM 346.540	10/2017	10/2017 (-) [0/0]	964.17 (-) [964.17]	904.00 (0.00) [0]
1320	GURGAON - KOTPUTLI - JAIPUR (SIX LANE)	2/2008	10/2011 (-) [0/0]	1,673.70 (-) [1,673.70]	3,326.93 (0.00) [0]
1321	REHABILITATION AND UPGRADATION TO 2 LANE WITH PAVED SHPULDERS CONFIGURATION OF BEAWAR-ASIND SECTION (K	8/2020	11/2020 (-) [11/2022]	196.23 (-) [196.00]	28.61 (-0.23) [24]
1322	SIX LANNING OF CHITTORGARH-UDAIPUR SECTION OF NH-76 FROM DESIGN CHAINAGE KM. 214.870 TO KM 308.370 I	9/2016	/ (-) [0/0]	1,100.19 (-) [1,145.31]	1,355.00 (45.12) [0]
1323	SIX LANNING OF KISHANGARH UDAIPUR AHMEDABAD SECTION FROM KM.90.000 (NEAR GULABPURA) TO KM. 214.870 (	9/2016	/ (-) [0/0]	1,239.82 (-) [1,727.66]	1,691.00 (487.84) [0]
1324	SIX-LANNING OF GREENFIELD PROPOSED UDAIPUR BYPASS PKG-IV	4/2017	4/2020 (-) [12/2021]	894.00 (-) [929.32]	810.00 (35.32) [20]
1325	TWO LANING WITH PAVED SHOULDER OF KARAUJI - DHOLPUR	9/2014	9/2016 (-) [0/0]	425.19 (-) [425.19]	276.40 (0.00) [0]
1326	TWO LANING WITH PS OF UNCHA NAGLA - KHANUWARA - ROPPAS -DHOLPUR	8/2015	/ (-) [0/0]	275.90 (-) [275.90]	289.13 (0.00) [0]
1327	TWO LANNING WITH PAVED SHOULDER OF MANOHARPUR-DAUSA SECTION OF NH-11A(NEW NH-148) FROM KM 62.100 KM	7/2016	10/2018 (-) [0/0]	331.46 (-) [331.46]	267.94 (0.00) [0]
1328	TWO LANNING WITH PAVED SHOULDER OF SALASAR-NAGPUR	6/2016	6/2019 (-) [9/2019]	637.18 (-) [637.18]	550.35 (0.00) [0]
1329	UP-GRADATION TO TWO LANING WITH PAVED SHOULDER OF AJMER-NAGPUR SECTION BY EXECUTING BALANCE WORK FRO	3/2020	8/2020 (-) [8/2022]	255.23 (-) [255.23]	42.41 (0.00) [24]
1330	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF KHAJUWALA-POOGAL SECTION AND POOGLE - DANTOUR-JA	3/2018	/ (8/2021) [8/2021]	874.25 (866.55) [866.55]	862.73 (-7.70) [-]
1331	UPGRADATION TO 2 LANE WITH PAVED SHOULDER FROM KM . 0/0 TO 43/900 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	6/2018 (-) [0/0]	370.30 (-) [370.30]	316.21 (0.00) [0]
1332	UPGRADATION TO 2 LANE WITH PAVED SHOULDER/4 LANE OF GAGARIA - BAORI KALAN - SERWA - BAKHASAR SECTION	2/2018	/ (-) [0/0]	1,103.88 (-) [1,103.88]	696.24 (0.00) [0]
1333	UPGRADATION TO 2LANE WITH PAVED SHOULDER FROM KM . 43/900 TO 91/0 OF KUNDAL-NAYA KHEDA-JHADOL-SOM-	2/2018	5/2018 (-) [0/0]	341.79 (-) [341.79]	241.14 (0.00) [0]
1334	WIDENING, STRENGTHENING AND RECONSTRUCTION OF NH-552- EXTN FROM KM 76/600 TO 112/00 (SAWAI MADHOPUR	11/2017	4/2018 (-) [0/0]	187.82 (-) [187.82]	131.74 (0.00) [0]
	SIKKIM				
	Railways				
1335	SEVOK RANGPO, NEFR	4/2008	12/2015 (12/2023) [12/2023]	1,339.48 (4,084.69) [8,600.00]	1,656.02 (7,260.52) [96]
	Road Transport And Highways				
1336	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM KM27.200 (END OF RO	8/2020	4/2023 (-) [4/2023]	230.45 (-) [230.45]	1.29 (0.00) [0]
1337	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER FROM NEW ROLEP	10/2020	11/2023 (-)	493.42 (-)	0.00 (0.00)

	BRIDGE AT		[11/2023]	[493.42]	[0]
1338	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	8/2020	4/2023 (-) [4/2023]	311.00 (-) [311.00]	17.38 (0.00) [0]
1339	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROV	7/2020	4/2023 (-) [4/2023]	345.38 (-) [345.38]	74.52 (0.00) [0]
1340	CONSTRUCTION OF 2-LANE MELLI MANPUR NAMCHI ROAD IN SOUTH SIKKIM	1/2013	2/2013 (6/2021) [0/0]	182.28 (369.58) [369.58]	340.16 (187.30) [0]
1341	CONSTRUCTION OF 2-LANE NAYABAZAR - LEGSHIP ROAD IN WEST SIKKIM.	4/2013	8/2013 (6/2021) [0/0]	151.59 (369.92) [369.92]	343.48 (218.33) [0]
1342	CONSTRUCTION OF 2-LANE ROAD WITH PAVED SHOULDER (GREENFIELD ALIGNMENT) OF EXISTING STRETCH BETWEEN L	9/2020	5/2022 (-) [5/2022]	183.31 (-) [183.31]	0.00 (0.00) [0]
1343	CONSTRUCTION OF 2-LANE SPECIFICATION ROAD WITH PAVED SHOULDER AS REALIGNMENT (GREENFIELD ALIGNMENT)	9/2020	5/2023 (-) [5/2023]	262.84 (-) [262.84]	0.00 (0.00) [0]
1344	CONSTRUCTION OF 2-LANE TARKU DAMTHANG NAMCHI ROAD IN SOUTH SIKKIM.	4/2013	8/2013 (6/2021) [0/0]	166.27 (359.90) [359.90]	302.35 (193.63) [0]
1345	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 0.000 TO KM 16.00	3/2017	/ (-) [0/0]	375.80 (-) [375.80]	64.34 (0.00) [0]
1346	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEMENT FROM KM 16.000 TO KM 32.5	11/2017	11/2017 (-) [12/2021]	290.05 (-) [290.05]	119.27 (0.00) [49]
1347	CONSTRUCTION OF 2-LANE WITH PAVED SHOULDER OF NEW GREEN FIELD ALIGNMENT FROM CHOCHENPHERI AT KM 52.0	10/2020	12/2023 (-) [12/2023]	816.79 (-) [816.79]	2.20 (0.00) [0]
1348	CONSTRUCTION/UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IMPROVEM	3/2018	6/2018 (-) [0/0]	264.84 (-) [264.84]	63.83 (0.00) [0]
1349	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 0.00 TO KM 13.00 N	3/2019	4/2022 (-) [4/2022]	402.94 (-) [402.94]	44.89 (0.00) [0]
1350	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 13.00 TO KM 25.600	8/2020	4/2023 (-) [4/2023]	295.97 (-) [295.97]	19.19 (0.00) [0]
1351	CONSTRUCTION/UPGRADATION OF EXISTING HIGHWAY TO 2 LANE WITH PAVED SHOULDER FROM KM 26.10 TO KM 40.00	3/2020	6/2022 (-) [6/2022]	242.97 (-) [242.97]	32.98 (0.00) [0]
1352	REHABILITATION AND UPGRADATION OF EXISTING ROAD TO 2-LANE WITH PAVED SHOULDER INCLUDING GEOMETRIC IM	8/2020	5/2022 (-) [5/2022]	292.80 (-) [292.80]	2.53 (0.00) [0]
1353	RHENOK-RORATHANG-PAKYONG ON NH 717A	4/2017	10/2017 (-) [0/0]	388.00 (-) [447.37]	271.35 (59.37) [0]
1354	RISHI BORDER- ROLEP- MENLA PKG- 2A	1/2021	9/2023 (-) [9/2023]	332.20 (-) [332.20]	0.00 (0.00) [0]
1355	RISHI BORDER- ROLEP- MENLA PKG- 3B	12/2020	2/2024 (-) [2/2024]	410.60 (-) [410.60]	0.00 (0.00) [0]
	TAMIL NADU				
	Atomic Energy				
1356	KUDANKULAM NUCLEAR POWER PROJECT UNIT-3 and 4	3/2013	11/2020 (-) [11/2023]	39,849.00 (-) [39,849.00]	25,029.00 (0.00) [36]
1357	PROTOTYPE FAST BREEDER REACTOR (BHAVINI, 500	9/2003	9/2010	3,492.00	5,986.57

	MWE)		(10/2022) [10/2022]	(6,840.00) [6,840.00]	(3,348.00) [145]
	<u>Civil Aviation</u>				
1358	DEVELOPMENT OF TUTICORIN AIRPORT	6/2019	3/2022 (12/2023) [12/2023]	380.87 (-) [380.87]	12.79 (0.00) [21]
1359	MODERNIZATION OF CHENNAI AIRPORT PHASE II, CHENNAI	6/2018	2/2022 (-) [12/2023]	2,467.00 (-) [2,467.00]	689.52 (0.00) [22]
1360	UPGRADATION OF PASSENGER TERMINAL BUILDING AND AIRSIDE FACILITIES AT TIRUCHIRAPALLI INTERNATIONAL AI	8/2018	10/2021 (-) [10/2022]	951.28 (-) [951.28]	437.28 (0.00) [12]
	<u>Coal</u>				
1361	EXPANSION OF MINE-I (LEASE AREA) AND MINE-I A (3.0 TO 7.0 MTPA)	4/2013	6/2015 (3/2025) [3/2025]	1,458.17 (709.06) [709.06]	492.01 (-749.11) [117]
1362	NEYVELI NEW THERMAL POWER PROJECT(2X500 MW)	6/2011	12/2015 (-) [2/2021]	5,907.11 (7,980.79) [7,980.79]	7,407.39 (2,073.68) [0]
	<u>Finance</u>				
1363	C/O OF 152 NOS TYPE-II,304 NOS,TYPE-III,76 NOS, TYPE-IV QTRS. FOR INCOME TAX DEPARTMENT AT CHENNAI	12/2015	10/2019 (-) [7/2021]	209.00 (-) [208.96]	205.75 (-0.04) [0]
1364	CONSTRUCTION OF 726 Nos RESIDENTIAL QUARTERS CHENNAI	11/2017	11/2021 (-) [11/2021]	348.77 (-) [348.77]	163.31 (0.00) [0]
	<u>Mines</u>				
1365	25.5 MW WIND POWER PROJECT AT KAYATHAR IN TAMILNADU	9/2017	6/2019 (12/2021) [12/2020]	166.62 (163.17) [163.17]	135.00 (-3.45) [0]
	<u>Petroleum</u>				
1366	AUGMENTATION OF CTMPL	12/2016	11/2021 (-) [11/2021]	228.00 (-) [228.00]	150.39 (0.00) [0]
1367	BS-VI PROJECTS	9/2017	12/2019 (-) [0/0]	1,858.00 (-) [1,858.00]	1,528.75 (0.00) [0]
1368	CGD PROJECT AT COIMBATORE DISTRICT	10/2018	3/2030 (-) [3/2030]	2,998.00 (-) [2,998.00]	0.00 (0.00) [0]
1369	CGD PROJECT AT SALEM DISTRICT	10/2018	3/2030 (-) [3/2030]	1,304.00 (-) [1,304.00]	0.00 (0.00) [0]
1370	CONSTRUCTION OF CAPTIVE POL LPG JETTY AT KAMARAJAR PORT, CHENNAI	10/2020	9/2023 (2/2024) [12/2023]	921.00 (-) [921.00]	5.26 (0.00) [3]
1371	CONSTRUCTION OF GRASS ROOT POL TOP AT ASANUR, TAMIL NADU	12/2017	10/2020 (1/2022) [1/2022]	466.43 (-) [466.43]	235.77 (0.00) [15]
1372	ENNORE THIRUVALLUR BENGALURU PUDUCHERRY NAGAPATTINAM MADURAITUTICORIN GAS PIPELINE	5/2016	12/2018 (2/2022) [2/2022]	4,497.00 (6,025.00) [6,025.00]	3,897.13 (1,528.00) [38]
1373	ENNORE-TRICHY-MADURAI LPG PIPELINE	5/2013	6/2020 (-) [0/0]	711.00 (-) [711.00]	11.12 (0.00) [0]
1374	Field Development Plan of Madanam NELP-IV Block CY-ONN-2002	11/2015	3/2019 (9/2021) [9/2021]	650.82 (-) [624.35]	453.71 (-26.47) [30]
1375	IRUGUR-DEVANGONTHI POL PIPELINE	11/2012	2/2017 (8/2022) [8/2022]	678.00 (1,472.00) [1,472.00]	19.44 (794.00) [66]

1376	RE-LIQUIFIED NATURAL GAS	8/2017	8/2020 (-) [10/2021]	421.00 (-) [305.00]	272.50 (-116.00) [14]
1377	SETTING UP LUBE COMPLEX AT VILLAGES AMULLAVOYAL AND VAIKKADU, CHENNAI AS RESITEMENT OF EXISTING FACI	10/2020	12/2023 (-) [9/2023]	1,398.00 (-) [1,398.00]	88.76 (0.00) [-3]
	<u>Power</u>				
1378	ETTAYAPURAM SOLAR 230MW	3/2020	9/2021 (2/2022) [2/2022]	1,316.22 (-) [1,316.22]	650.94 (0.00) [5]
1379	TRANSMISSION SYSTEM FOR EVACUATION OF POWER FROM NEYVELI LIGNITE CORP LTD TS - I (REPLACEMENT) IN NEY	5/2017	7/2019 (7/2021) [10/2021]	186.17 (219.66) [219.66]	158.03 (33.49) [27]
	<u>Railways</u>				
1380	ATTIPATTU - KORUKKUPETTAI : 3RD LINE (18 KM) DOUBLING	2/1999	3/2018 (-) [0/0]	257.00 (257.00) [154.46]	153.84 (-102.54) [0]
1381	ATTIPPATTU PUTTUR	4/2008	2/2019 (-) [0/0]	151.84 (-) [527.37]	2.59 (375.53) [0]
1382	CHENGALPATTU-VILLUPURAM DOUBLING WITH NEW MM FOR TAMBARAM-CHENGALPATTU 3RD LINE GC ALONWITH ELECTRIF	4/2007	/ (8/2021) [8/2021]	931.98 (-) [1,121.00]	969.72 (189.02) [-]
1383	CUDDALORE-SALEM VIA VRIDDHACHALAM GC	4/1999	/ (-) [3/2024]	198.68 (-) [559.95]	273.32 (361.27) [-]
1384	ERODE-PALANI	4/2008	/ (-) [0/0]	288.57 (-) [603.23]	1.63 (314.66) [0]
1385	EXTENSION OF MRTS FROM VELACHERY TO STN. THOMAS, MTP	4/2006	6/2013 (7/2022) [7/2022]	495.74 (-) [734.01]	472.27 (238.27) [109]
1386	MADURAI - MANIYACHI - TUTICORIN (160 KM) DOUBLING	2/2015	3/2020 (-) [6/2022]	760.00 (-) [1,536.00]	1,233.08 (776.00) [27]
1387	MADURAI-BODINAYAKKANUR	4/2008	/ (12/2021) [12/2021]	164.41 (-) [608.13]	389.96 (443.72) [-]
1388	MANIYACHI - NAGERCOIL (102 KM) DOUBLING	2/2015	3/2022 (-) [6/2022]	1,700.00 (-) [1,305.00]	756.45 (-395.00) [3]
1389	MAYLADUTHURAI-THIRUVARUR-KARAIKUDI-THIRU 'PONDI'-AGASTIYAMPALLI	9/2007	2/2019 (-) [3/2025]	724.69 (-) [2,950.00]	1,644.43 (2,225.31) [73]
1390	OMALUR-METTURDAM- DOUBLINGWITH ELCTRIFICATION 28.93KM	10/2013	4/2014 (-) [0/0]	187.26 (-) [327.00]	275.03 (139.74) [0]
1391	SRIPERUMBUDUR-GUDUVANCHERY WITH SPUR TO IRUNGATTUKKOTTAI-AVADI-SRIPERUMBUDUR	4/2013	/ (-) [0/0]	839.00 (-) [839.01]	0.63 (0.01) [0]
1392	THIRUMAILA - VELACHERY : MASS RAPID TRANSIT SYSTEM (PHASE II)	2/1996	3/2005 (-) [9/2021]	268.87 (-) [950.00]	920.84 (681.13) [198]
1393	TIDIVANAM-NAGARI (NL)	9/2006	/ (-) [12/2025]	582.83 (-) [3,150.00]	239.49 (2,567.17) [-]
1394	TINDIVANAM-GINGEE-TIRUVANNAMALAI (NL)	9/2006	/ (-) [0/0]	227.40 (-) [227.40]	65.02 (0.00) [0]
1395	TIRUCHIRAPPALI-NAGORE-KARAIKKAL(SR)(GC)	9/1995	3/2020 (-)	303.98 (-)	704.89 (1,416.02)

			[3/2025]	[1,720.00]	[60]
1396	TRANSMISSION LINE BETWEEN CHENNAI-HOWRAH ROUTE (1662 KM)	2/2017	3/2024 (-) [3/2026]	1,567.00 (-) [1,567.00]	0.00 (0.00) [24]
	Road Transport And Highways				
1397	2-LANING OF KRISHNAGIRI-TINDIVANAM (APPROVED LENH 170 KM)	4/2012	4/2014 (-) [1/2022]	624.00 (-) [624.00]	108.46 (0.00) [93]
1398	4-LANING OF OTTANCHATRAM BYPASS	9/2017	9/2017 (-) [0/0]	244.27 (-) [244.27]	178.41 (0.00) [0]
1399	4-LANING OF STHIYATHOPU-CHOLOPURAM	9/2017	9/2017 (-) [7/2022]	1,227.87 (-) [1,227.87]	644.68 (0.00) [58]
1400	CONSTRUCTION OF PAVED SHOULDERS IN KM.81/0 TO 203/0 INCLUDING RECONSTRUCTION AND WIDENING OF CULVERT	3/2015	8/2015 (-) [0/0]	258.97 (273.27) [268.92]	229.77 (9.95) [0]
1401	DEVELOPMENT OF ADIQUATE ROAD CONNECTIVITY TO CHENNAI- ENNORE PORT CONNECTIVITY	6/2011	6/2013 (-) [9/2021]	600.00 (-) [600.00]	4.62 (0.00) [99]
1402	FOUR LANING OF KALAGAM TO KARUPPUR FROM KM.38+700 TO KM. 50+382 AND TWO LANING WITH PAVED SHOULDERS	3/2018	/ (-) [1/2022]	1,016.92 (-) [1,071.00]	299.56 (54.08) [-]
1403	FOUR LANING OF MADURAI - RAMANATHAPURAM (KM 5. TO KM 81) AND TWO LANING WITH PS KM 81 TO KM 120	5/2015	11/2017 (-) [0/0]	1,387.11 (-) [1,387.11]	980.46 (0.00) [0]
1404	FOUR LANING OF MADURAI- CHETTICKULAM SECTION OF NH-785 FROM MADURAI (KM 0/000) TO CHETTICKULAM (7/300)	3/2018	/ (-) [3/2022]	628.71 (-) [628.71]	358.35 (0.00) [-]
1405	FOUR LANING OF POONDIYANKUPPAM TO SATTANATHAPURAM (DESIGN CH KM. 67.000 TO KM. 123+800) SECTION OF NH-785	3/2018	/ (-) [0/0]	2,065.96 (-) [2,169.00]	0.00 (103.04) [0]
1406	FOUR LANING OF TRICHY TO KALLAGAM SECTION ON NH-227 IN THE STATE OF TAMIL NADU	2/2018	/ (-) [1/2022]	1,166.26 (-) [1,296.93]	346.17 (130.67) [-]
1407	FOUR LANING OF VILLUKURI KANNIYAKUMAR ROAD OF KM 70.250 TO 96.700 AND NAGERCOIL TO KAVALKINARU OF NH	3/2016	7/2016 (-) [12/2021]	641.17 (-) [641.17]	395.10 (0.00) [65]
1408	FOUR LANING OF CHETTICKULAM TO NATHAM SECTION OF NH-785 FROM CHETTICKULAM (KM 7.300) TO NATHAM (KM. 3	3/2018	/ (-) [12/2022]	505.35 (-) [505.35]	255.05 (0.00) [-]
1409	FOUR LANNING OF CHOLOPURAM-THANJAVUR	8/2017	8/2017 (-) [7/2022]	1,176.37 (-) [1,176.37]	614.68 (0.00) [59]
1410	FOUR LANNING OF TAMIL NADU KERALA BORDER TO VILLUKURI FROM KM. 43.00 TO 70.25 OF NH-47 UNDER NHDP-PH	2/2016	8/2018 (-) [1/2022]	707.82 (-) [707.82]	428.72 (0.00) [41]
1411	FOUR LANNING OF VIKRAVANDI-SETHIYAHOPU FROM KM 0.000 TO KM 60.250(DESIGN CHAINAGE KM 0.000 TO KM 65.	3/2017	3/2020 (-) [12/2021]	848.45 (-) [848.45]	235.72 (0.00) [21]
1412	FOUR LANNING OF VILLUKURI TO KANYAKUMARI SECTION FROM KM 70.25 TO 96.714 OF NH-47 AND NAGERCOIL TO K	2/2016	7/2018 (-) [12/2021]	641.17 (-) [641.17]	395.10 (0.00) [41]
1413	PREPARATION OF FEASIBILITY/DPR OF CONSTRUCTION OF NEW 4-LANE ELEVATED ROAD FROM CHENNAI PORT TO MADURAI	7/2020	12/2021 (-) [12/2021]	3,426.00 (-) [3,426.00]	0.00 (0.00) [0]
1414	SIX LANING OF CHENNAI-TADA SECTION OF NH-5 FROM KM 11/0 TO KM 54/4 IN THE STATE OF TAMIL NADU TO BE	12/2017	/ (-) [3/2021]	379.90 (-) [379.90]	231.42 (0.00) [0]
1415	SIX LANNING OF KRISHNAGIRI- WALAJHAPET SECTION KM.0.00 TO KM.148.3 NH-46	9/2011	12/2013 (-)	1,250.00 (-)	1,342.23 (0.00)

			[0/0]	[1,250.00]	[0]
1416	THIRUMAYAM - MANAMADURAI SECTION	7/2014	1/2017 (-) [0/0]	401.11 (-) [401.11]	273.89 (0.00) [0]
1417	TRICHY - KARUR	3/2007	7/2008 (-) [0/0]	516.00 (-) [516.00]	886.96 (0.00) [0]
1418	TWO LANING OF TRICHY - KARAUKUDI AND TRYCHI BYPASS	5/2010	5/2013 (-) [8/2021]	374.00 (-) [166.90]	69.96 (-207.10) [99]
1419	TWO LANING WITH PAVED SHOULDER OF MEENSURUTTI (KM. 98.433) TO CHIDAMBARM (KM. 129.965.) SECTION OF N	3/2018	/ (-) [0/0]	633.55 (-) [482.04]	0.00 (-151.51) [0]
1420	TWO LANING WITH PS OF NAGAPATTINAM - THANJAVUR	6/2015	12/2017 (-) [0/0]	563.92 (-) [563.92]	0.00 (0.00) [0]
1421	WIDENING AND STRENGTHENING FROM 2 LANE TO 2 LANE WITH PAVED SHOULDER IN AN AGGREGATE LENGTH OF 38 KM	3/2018	6/2019 (-) [0/0]	240.38 (204.73) [240.38]	107.69 (0.00) [0]
1422	WIDENING EXISTING 2 LANE TO 4 LANE WITH PAVED SHOULDER INCLUDING STRENGTHENING CARRIAGEWAY FROM KM 8	8/2020	2/2021 (-) [2/2021]	302.62 (-) [302.62]	11.50 (0.00) [0]
1423	WIDENING FROM 2 LANE TO 4 LANE AND STRENGTHENING THE EXISTING CARRIAGE WAY FROM KM 36/0 -80/0 OF SALE	3/2019	11/2019 (-) [0/0]	297.55 (-) [297.55]	156.11 (0.00) [0]
	<u>Urban Development</u>				
1424	CHENNAI METRO RAIL LTD (PHASE 1 EXT)	6/2016	3/2018 (-) [0/0]	3,770.00 (-) [3,770.00]	2,959.83 (0.00) [0]
1425	CHENNAI METRO RAIL LTD (PHASE 1)	2/2009	12/2015 (-) [0/0]	14,600.00 (18,380.00) [18,380.00]	17,619.68 (3,780.00) [0]
	<u>TELANGANA</u>				
	<u>Civil Aviation</u>				
1426	CO CIVIL AVIATION RESEARCH ORG. (PH-II) AT BEGUMPET AIRPORT, HYDRABAD	5/2020	5/2022 (-) [5/2022]	353.61 (-) [353.61]	67.32 (0.00) [0]
	<u>Coal</u>				
1427	GODAVARIKHANI COAL MINE	7/2019	3/2023 (-) [3/2023]	438.98 (-) [438.98]	73.60 (0.00) [0]
1428	JALAGAM VENGALA RAO OCP-II	7/2011	3/2015 (-) [3/2023]	447.06 (-) [473.22]	79.04 (26.16) [96]
1429	KAKATIYAKHANI OPENCAST III PROJECT PHASE-1	3/2017	3/2019 (-) [3/2022]	413.84 (-) [413.84]	200.14 (0.00) [36]
1430	KAKATIYAKHANI OPENCAST-2 PROJECT	5/2015	3/2019 (-) [3/2022]	397.09 (-) [442.42]	111.66 (45.33) [36]
1431	KALYANIKHANI OPENCAST PROJECT	7/2012	7/2016 (-) [3/2022]	417.33 (-) [384.32]	134.71 (-33.01) [68]
1432	KISTARAM OCP	11/2010	3/2015 (-) [3/2022]	242.29 (-) [164.04]	143.08 (-78.25) [84]
1433	RAMAGUNDAM OC-II EXTENSION	12/2009	3/2012 (-) [3/2023]	418.97 (-) [489.62]	416.07 (70.65) [132]
1434	RCE OF INDARAM OCP(1.20 MTPA)	7/2011	3/2015 (-)	162.76 (-)	283.01 (186.52)

			[3/2022]	[349.28]	[84]
1435	RFR OF MANUGURU OC PROJECT	11/2012	3/2016 (-) [9/2021]	430.45 (-) [415.37]	213.44 (-15.08) [66]
1436	SRP OC-II EXPANSION PROJECT	11/2016	/ (-) [3/2022]	272.73 (-) [272.73]	153.75 (0.00) [-]
1437	VENKATESH KHANI COAL MINE	10/2020	3/2023 (-) [3/2023]	484.51 (-) [484.51]	23.39 (0.00) [0]
	Health And Family Welfare				
1438	ESTABLISHMENT OF NATIONAL ANIMAL RESOURCE FACILITY FOR BIOMEDICAL RESEARCH AT HYDERABAD	10/2016	3/2020 (-) [5/2021]	209.84 (-) [209.84]	154.21 (0.00) [0]
	Petroleum				
1439	GRASS ROOT TERMINAL AT MALKAPUR	12/2018	4/2022 (-) [8/2023]	611.00 (-) [611.00]	89.82 (0.00) [16]
	Power				
1440	RAMAGUNDAM FLOATING SOLAR 100 MW	6/2019	4/2021 (10/2021) [10/2021]	401.90 (-) [401.90]	153.54 (0.00) [6]
1441	TELANGANA SUPER THERMAL POWER PROJECT PHASE I	1/2016	11/2020 (7/2022) [10/2022]	10,598.98 (10,997.70) [10,997.70]	8,740.94 (398.72) [23]
	Railways				
1442	MULTI MODAL TRANSPORT SYSTEM(MMTS) PHASE-II HYDERABAD	4/2012	3/2016 (-) [12/2021]	632.68 (-) [950.00]	741.79 (317.32) [69]
1443	DOUBLING OF TRACK BETWEEN GOOTY AND DHARMAVARAM OF SOUTH CENTRAL RAILWAY	3/2015	3/2021 (-) [0/0]	636.38 (-) [636.38]	613.12 (0.00) [0]
1444	MANMAD-PARBHANI-NANDED-SECUNDERABAD-GADWAL-DHONE- GUNTAKAL - TRAIN COLLISION AVOIDANCE SYSTEM (958 K	4/2017	3/2022 (-) [12/2022]	119.73 (185.00) [449.39]	7.09 (329.66) [9]
1445	MANOHARABAD-KOTHPALL NEW LINE(SCR)	4/2006	3/2010 (-) [3/2024]	1,160.48 (-) [1,160.48]	631.65 (0.00) [168]
1446	MANUGURU-RAMAGUNDAM	4/2013	/ (-) [0/0]	1,112.00 (-) [2,911.84]	0.92 (1,799.84) [0]
1447	SECUNDERABAD-MAHABUBNAGAR DOUBLING	4/2015	12/2024 (-) [12/2024]	773.94 (-) [850.00]	618.69 (76.06) [0]
	Road Transport And Highways				
1448	4 LANNING OF MH-KNT BORDER SANGAREDDY SECTION OF NH-9	4/2014	9/2016 (-) [0/0]	1,266.60 (-) [1,544.00]	1,446.45 (277.40) [0]
1449	6 LANING FROM KM 9.90 TO KM 19.948 (ARAMGARH-SAMSHABAD SECTION) OF HYDERABAD-SAMSHABAD SECTION OF NH	1/2018	5/2020 (-) [0/0]	283.15 (-) [283.15]	130.89 (0.00) [0]
1450	CONSTRUCTION OF SIX LANE ELEVATED CORRIDOR FROM KM.7.950 (UPPAL) TO KM.14.200 OF NH-163 TO DE-CONGES	3/2018	7/2020 (-) [0/0]	626.76 (-) [626.76]	201.15 (0.00) [0]
1451	EPC- CORRIDOR APPROACH WORKS - NH (O): WIDENING EXISTING 2 LANE TO 2 LANE WITH PAVED SHOULDERS IN KM	3/2015	1/2017 (-) [0/0]	153.21 (-) [153.21]	100.95 (0.00) [0]
1452	FOUR LANING OF KHAMMAM-ASHWARAOPET SECTION OF NH 365BB	3/2017	3/2017 (-) [0/0]	4,429.00 (-) [4,429.00]	0.00 (0.00) [0]
1453	FOUR LANING OF NH 161 FROM KANDI (DESIGN KM	3/2018	/	857.62	291.66

	0.000) (KM 498.250 OF NH 65) TO RAMSANPALLE (DESIGN KM 3		(-) [0/0]	(-) [857.62]	(0.00) [0]
1454	FOUR LANING OF NH 161 FROM MANGLOOR (DESIGN KM 135.751 EXISTING KM 140.873) (DESIGN LENGTH 48.963 K	3/2018	/	802.65	436.81
			(-) [0/0]	(-) [802.65]	(0.00) [0]
1455	FOUR LANING OF NH 161 FROM RAMSANPALLE (DESIGN KM 39.980 EXISTING KM 44.757) TO MANGLOOR (DESIGN KM	3/2018	/	950.63	608.25
			(-) [0/0]	(-) [950.63]	(0.00) [0]
1456	FOUR LANING OF NH-363 FROM REPALLEWADA (DESIGN KM 40.000/EXISTING KM 288.510) TO TELANGANA/MAHARASHT	3/2018	/	828.29	0.00
			(-) [0/0]	(-) [828.29]	(0.00) [0]
1457	FOUR LANING OF YADGIRI - WARANGAL	12/2015	11/2018	1,423.96	995.39
			(-) [8/2021]	(-) [1,056.08]	(-367.88) [33]
1458	REHABILITATION AND UP GRADATION FROM KM. 121/0 TO 154/0 OF NAKAREKAL – MALLAMPALLY SECTION OF NH-365	3/2018	7/2019	192.67	158.92
			(-) [0/0]	(-) [192.67]	(0.00) [0]
1459	REHABILITATION AND UP-GRADATION TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/0 TO 72/6 OF NH-365 (NAKR	1/2017	10/2019	605.08	403.26
			(-) [0/0]	(-) [605.08]	(0.00) [0]
1460	REHABILITATION AND UPGRADATION OF HYDERABAD OUTER RING ROAD TO MEDAK SECTION OF NH-765D FROM EXISTIN	2/2018	4/2020	426.52	391.52
			(-) [0/0]	(-) [426.52]	(0.00) [0]
1461	REHABILITATION AND UPGRADATION OF NH -565 FROM KM 1.00 TO 86.057 (NAKREKAL TO NAGARJUNSAGAR DAM SECT	1/2014	3/2016	270.00	0.00
			(-) [0/0]	(-) [270.00]	(0.00) [0]
1462	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.113.900 TO 154.479 (MALLEPALLY - HALIYA SECT	2/2018	11/2019	294.13	141.10
			(-) [0/0]	(-) [294.13]	(0.00) [0]
1463	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.157.707 TO 187.723 (DESIGN LENGTH 30.016 KMS	2/2018	11/2019	220.28	137.20
			(-) [0/0]	(-) [220.28]	(0.00) [0]
1464	REHABILITATION AND UPGRADATION OF NH-167 FROM DESIGN KM.187.723 TO 234.434 (MIRYALAGUDA TO KODAD SEC	3/2018	9/2020	322.81	177.32
			(-) [0/0]	(-) [322.81]	(0.00) [0]
1465	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 180.60 TO KM 223.00 OF NH-63 ON NIZ	10/2016	3/2019	248.83	124.12
			(-) [0/0]	(-) [248.83]	(0.00) [0]
1466	WIDENING TO TWO/FOUR LANE WITH PAVED SHOULDERS FROM EXISTING KM 182.120 TO KM 227.600 OF NH-167 ON	10/2016	2/2019	298.32	120.90
			(-) [0/0]	(-) [298.32]	(0.00) [0]
1467	WIDENING AND STRENGTHENING OF EXISTING 2-LANE TO 2-LANE WITH PAVED SHOULDERS FROM KM.159/0 TO 165/4	1/2018	12/2019	230.03	209.06
			(-) [0/0]	(-) [230.03]	(0.00) [0]
1468	WIDENING AND STRENGTHENING OF EXISTING CARRIAGEWAY IN 2 LANE WITH PAVED SHOULDERS FROM KM.25/0 TO 59	2/2018	6/2020	206.13	171.69
			(-) [0/0]	(-) [206.13]	(0.00) [0]
1469	WIDENING AND STRENGTHENING/ RECONSTRUCTION OF EXISTING PAVEMENT TO FOUR ALNE WITH PAVED SHOULDERS FR	1/2019	/	193.19	88.25
			(-) [0/0]	(-) [193.19]	(0.00) [0]
1470	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 0/970 TO KM 40/410 OF JANAGAON- THIRUMALAGIRI OF NH	1/2017	10/2019	196.52	115.81
			(-) [0/0]	(-) [196.52]	(0.00) [0]
1471	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 15.525 TO KM 62.880 OF JADCHERLA- KALWAKURTHY SECTI	1/2017	12/2019	283.00	229.21
			(-) [0/0]	(-) [283.00]	(0.00) [0]
1472	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 40/410 TO KM 84/037OF THIRUMALAGIRI TO SURYAPET SE	1/2017	5/2019	244.54	164.60
			(-) [0/0]	(-) [244.54]	(0.00) [0]
1473	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 59.500 TO KM 132.033 OF MANNEGUDA-	1/2017	5/2019	359.27	299.11
			(-) [0/0]	(-) [359.27]	(0.00) [0]

	RAVULAPALLY SECT		[0/0]	[359.27]	[0]
1474	WIDENING TO TWO LANE WITH PAVED SHOULDERS FROM KM 67.00 TO 114.425 OF KALWAKURTHY-MALLEPALLY SECTION	1/2017	5/2019 (-) [0/0]	300.00 (-) [300.00]	201.76 (0.00) [0]
	<u>TRIPURA</u>				
	<u>Railways</u>				
1475	AGARTALA-AKHAURA NL	4/2012	3/2020 (-) [3/2022]	569.63 (-) [742.00]	200.28 (172.37) [24]
	<u>Road Transport And Highways</u>				
1476	2 LANING WITH PAVED SHOULDER OF AGARTALA-UDAIPUR SECTION OF NH-44 FROM KM 6.800 TO KM 55.00 IN THE S	10/2014	3/2018 (-) [0/0]	369.00 (-) [369.00]	352.63 (0.00) [0]
1477	2-LANING FROM JOLAIBARI - BELONIA	6/2020	1/2022 (-) [1/2022]	201.99 (-) [201.99]	14.98 (0.00) [0]
1478	2-LANING FROM MANU-SIMLUNG (PKG I)	3/2020	1/2022 (-) [1/2022]	247.76 (-) [247.76]	29.13 (0.00) [0]
1479	2-LANING FROM MANU-SIMLUNG (PKG III)	6/2020	1/2022 (-) [1/2022]	347.36 (-) [347.36]	64.89 (0.00) [0]
1480	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 31.300 TO KM 45.300 OF NH-208A PKG-3	9/2020	4/2022 (-) [4/2022]	173.17 (-) [173.17]	0.00 (0.00) [0]
1481	2-LANING OF KHOWAI -AGARTALA SECTION FROM DESIGN KM 6.500 TO KM 19.300 OF NH-208A PKG-1	3/2020	7/2022 (-) [7/2022]	165.54 (-) [165.54]	0.00 (0.00) [0]
1482	KAILASHAHAR TO KHOWAI PKG-2	11/2020	7/2022 (-) [7/2022]	206.78 (-) [206.78]	3.42 (0.00) [0]
1483	KAILASHAHAR TO KHOWAI PKG-3	11/2020	7/2022 (-) [7/2022]	280.91 (-) [280.91]	59.20 (0.00) [0]
1484	KAILASHAHAR TO KHOWAI PKG-4	11/2020	6/2022 (-) [6/2022]	159.13 (-) [159.13]	7.72 (0.00) [0]
1485	KAILASHAHAR TO KHOWAI PKG-5	11/2020	7/2022 (-) [7/2022]	332.14 (-) [332.14]	0.00 (0.00) [0]
1486	MANU-SIMLUNG (PKG 4)	3/2021	12/2022 (-) [12/2022]	354.79 (-) [354.79]	0.00 (0.00) [0]
1487	REHABILITATION AND UP-GRADATION OF ROAD FROM DESIGN KM 11.800 TO KM 25.250 OF KAILASHAHAR-KURTI BRID	3/2020	7/2022 (-) [7/2022]	178.43 (-) [178.43]	6.87 (0.00) [0]
1488	REHABILITATION AND UPGRADATION OF ROAD FROM DESIGN KM 0.00 TO KM 11.800 OF KAILASHAHAR-KURTI BRIDGE	3/2020	7/2022 (-) [7/2022]	154.51 (-) [154.51]	12.08 (0.00) [0]
1489	REHABILITATION AND UPGRADATION OF ROAD FROM KM 0.00 TO KM 18.600 OF KUMARGHAT-KAILASHAHAR SECTION	6/2020	1/2022 (-) [1/2022]	277.50 (-) [277.50]	15.01 (0.00) [0]
1490	STRENGTHENING OF CHURAI BARI - AGARTALA SECTION OF NH-08	6/2020	1/2022 (-) [1/2022]	257.96 (-) [257.96]	95.22 (0.00) [0]
1491	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C GEOMETRIC IMPROVEMENT FROM KM 397.00 TO KM 422.00 (25 K	1/2017	12/2022 (-) [12/2022]	197.67 (-) [236.18]	21.65 (38.51) [0]
1492	WIDENING TO 2-LANE WITH PAVED SHOULDER IN/C. GEOMETRIC IMPROVEMENT FROM KM 318.00 TO KM 339.940 ON C	10/2016	8/2020 (-) [10/2021]	171.90 (-) [171.90]	142.81 (0.00) [14]

	<u>Rural Development</u>				
1493	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE V	3/2007	12/2015 (-) [2/2022]	149.73 (173.00) [155.66]	144.95 (5.93) [74]
1494	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VI	12/2007	12/2016 (-) [3/2022]	202.61 (227.00) [207.12]	190.22 (4.51) [63]
1495	CONSTRUCTION AND MAINTAINANCE OF RURAL ROAD UNDER PMGSY PHASE VIII	10/2011	12/2016 (-) [9/2022]	175.49 (206.71) [175.49]	124.87 (0.00) [69]
	<u>UTTAR PRADESH</u>				
	<u>Civil Aviation</u>				
1496	CCS INTERNATIONAL AIRPORT , LUCKNOW	6/2018	9/2021 (-) [12/2023]	1,383.00 (1,938.00) [1,383.00]	488.53 (0.00) [27]
	<u>Coal</u>				
1497	KHADIA EXPANSION OCP	6/2021	3/2025 (-) [3/2025]	491.67 (-) [491.67]	0.00 (0.00) [0]
1498	NEYVELI UTTAR PRADESH POWER PROJECT LIMITED 1980 MW	7/2016	11/2021 (11/2022) [11/2022]	17,237.00 (-) [17,237.80]	12,346.08 (0.80) [12]
	<u>Department Of Higher Education</u>				
1499	CONSTRUCTION OF ENGINEERING CORE LAB FOR IIT KANPUR	11/2017	3/2020 (-) [0/0]	171.72 (-) [171.72]	53.94 (0.00) [0]
	<u>Health And Family Welfare</u>				
1500	ALL INDIA INSTITUTE OF MEDICAL SCIENCE AT GORAKHPUR (U.P.)	7/2016	4/2020 (-) [10/2021]	785.00 (-) [715.06]	574.62 (-69.94) [18]
1501	HOSPITAL AND MEDICAL COLLEGE AIIMS RAEBARELI	3/2018	(-) [3/2021]	268.84 (-) [268.84]	243.92 (0.00) [0]
	<u>Home Affairs</u>				
1502	CONSTRUCTION OF 683 VARIOUS TYPE FAMILY QUARTERS AT GROUP CENTRE CRPF CHANDAULI	5/2019	1/2022 (-) [6/2022]	199.31 (-) [199.31]	27.86 (0.00) [5]
	<u>Petroleum</u>				
1503	AUGMENTATION OF MATHURA-TUNDLA PIPELINE AND ITS EXTENSION FOR HOOK UP WITH BARAUNI-KANPUR PIPELINE A	3/2018	8/2022 (-) [8/2022]	676.00 (-) [676.00]	464.35 (0.00) [0]
1504	CITY GAS DISTRIBUTION (CGD) NETWORK VARANASI	4/2017	4/2022 (-) [4/2022]	287.49 (345.15) [345.15]	231.37 (57.66) [0]
1505	CITY GAS DISTRIBUTION IN UP AND UK	3/2019	3/2029 (8/2029) [8/2029]	3,450.20 (-) [3,450.20]	276.62 (0.00) [5]
1506	HARIDWAR RISHIKESH DEHRADUN PIPELINE PROJECT	8/2018	4/2021 (-) [3/2022]	217.92 (217.92) [217.92]	96.60 (0.00) [11]
1507	INFRASTRUCTURE DEVELOPMENT TO FACILITATE BULK IMPORT OF GRID POWER AT 220 KV AT MATHURA REFINERY	8/2017	8/2020 (3/2022) [3/2022]	255.40 (-) [255.40]	90.08 (0.00) [19]
1508	MULTI PRODUCT PIPELINE FROM BINA TERMINAL TO PANKI KANPUR TERMINAL	12/2017	12/2021 (-) [12/2021]	1,524.06 (-) [1,524.06]	905.06 (0.00) [0]
1509	REVAMPING OF EXISTING FACILITIES/ AUGMENTATION OF FACILITIES AT BAITALPUR DEPOT FOR	8/2017	8/2021 (-) [11/2022]	318.80 (-) [318.80]	162.87 (0.00) [15]
	<u>Power</u>				
1510	DEVIKOT SOLAR 150MW	1/2020	9/2021	798.24	273.17

			(2/2022) [2/2022]	(-) [798.24]	(0.00) [5]
1511	DEVIKOT SOLAR 90MW	3/2020	9/2021 (2/2022) [2/2022]	501.29 (-) [501.29]	343.39 (0.00) [5]
1512	KHURJA SUPER THERMAL POWER PROJECT	3/2019	9/2023 (-) [8/2024]	11,089.42 (-) [11,089.42]	2,347.19 (0.00) [11]
1513	NOKHRA	3/2020	9/2021 (7/2022) [1/2023]	1,722.14 (-) [1,722.14]	340.93 (0.00) [16]
	<u>Railways</u>				
1514	ANANDNAGAR GHUGHALI VIA MAHRAJGANJ UP	3/2013	/	307.00	0.00
			(-) [0/0]	(-) [1,409.09]	(1,102.09) [0]
1515	AUNRIHAR - JAUNPUR PATCH DOUBLING .	4/2016	1/2022 (-) [3/2022]	600.00 (-) [366.71]	254.12 (-233.29) [2]
1516	BAHRAICH - MAILANI GAUGE CONVERSION INCLUDING BY-PASS AT MAILANI.	4/2016	1/2022 (-) [3/2025]	1,900.00 (-) [1,277.06]	0.00 (-622.94) [38]
1517	BHIMSEN - JHANSI DOUBLING WITH ELECTRIFICATION	3/2012	12/2020 (-) [12/2022]	1,183.25 (-) [1,825.00]	1,266.69 (641.75) [24]
1518	BURHWAL - GONDA - 3RD RUNNING LINE.	4/2016	/	602.50	88.04
			(-) [12/2023]	(-) [714.34]	(111.84) [-]
1519	ELECTRIFICATION OF KHURJA-MEERUT-SAHARANPUR AND G'BAD-MEERUT	2/2008	3/2012 (-) [0/0]	171.10 (-) [275.08]	141.55 (103.98) [0]
1520	ETAH - KASGANJ - NEW LINE	4/2017	4/2017 (-) [4/2022]	276.90 (-) [276.90]	0.00 (0.00) [60]
1521	ETAWAH-MAINPURI (NL),NCR	4/1997	12/2008 (-) [0/0]	120.00 (-) [346.00]	345.51 (226.00) [0]
1522	GHAZIPUR - AUNRIHAR (40 KM)	4/2014	/	182.92	0.00
			(-) [0/0]	(-) [197.73]	(14.81) [0]
1523	INDARA - DOHRIGHAT GAUGE CONVERSION.	4/2016	4/2016 (-) [12/2021]	213.00 (-) [213.35]	53.51 (0.35) [68]
1524	JHANSI BINA DOUBLING	9/2016	3/2021 (12/2022) [12/2022]	2,001.00 (-) [2,001.00]	948.08 (0.00) [21]
1525	JHANSI MANIKPUR AND KHAIRAR BHIMSEN DOUBLING	3/2018	3/2023 (-) [6/2025]	4,329.53 (-) [4,329.53]	63.56 (0.00) [27]
1526	KAPILVASTU-BASTI VIA BANSI SIDHARTHANAGAR BASTI NAUGARH UP	3/2013	/	643.00	0.00
			(-) [0/0]	(-) [644.00]	(1.00) [0]
1527	KARAILA ROAD - SHAKTINAGAR DOUBLING	8/2015	3/2019 (-) [3/2022]	528.57 (-) [528.57]	223.40 (0.00) [36]
1528	LUCKNOW- PILIBHIT VIA SITAPUR, LAKHIMPUR GC	4/2011	3/2019 (-) [6/2022]	927.01 (-) [1,400.00]	1,233.65 (472.99) [39]
1529	MATHURA-JHANSI-3RD LINE (273.80 KM)	6/2016	12/2023 (-) [12/2023]	3,677.76 (-) [3,677.76]	446.65 (0.00) [0]
1530	MATHURA-PLWAL 4TH LINE (80KM)	4/2015	3/2020	668.70	330.00

			(-) [0/0]	(668.00) [680.00]	(11.30) [0]
1531	MAU-GHAZIPUR-TARIGHAT NEW LINE	4/2015	3/2023 (-) [12/2024]	1,765.92 (-) [1,765.92]	746.29 (0.00) [21]
1532	NANPARA - NEPALGANJ GAUGE CONVERSION.	4/2017	4/2017 (-) [10/2022]	150.00 (-) [341.66]	0.00 (191.66) [66]
1533	PADRAUNA - KUSHINAGAR VIA GORAKHPUR - NEW LINE	4/2017	1/2018 (-) [0/0]	1,343.00 (-) [1,476.15]	0.00 (133.15) [0]
1534	PILIBHIT - SHAHJAHANPUR GAUGE CONVERSION	4/2017	4/2017 (-) [3/2021]	622.50 (427.00) [590.00]	508.15 (-32.50) [0]
1535	RAMNA - SINGRAULI DOUBLING	8/2015	3/2020 (-) [3/2024]	2,436.21 (-) [2,436.21]	1,283.84 (0.00) [48]
1536	ROSA-SITAPUR CANTT-BURHWAL DOUBLING	3/2015	3/2022 (-) [3/2022]	1,295.42 (-) [1,758.00]	1,143.78 (462.58) [0]
1537	SHAHGANJ-BHATNI-PHEPHNA-INDARA, MAU-SHAHGANJ (EXCL. MAU-INDARA) PATCH DOUBLING.	4/2016	12/2019 (-) [4/2021]	1,177.96 (-) [1,028.95]	176.68 (-149.01) [0]
1538	UNCHAHAR-AMETHI	4/2012	/ (-) [3/2023]	1,229.00 (-) [489.64]	105.51 (-739.36) [-]
1539	VARANASI-MODHOSINGH-ALLAHABAD DOUBLING	4/2015	3/2022 (-) [12/2024]	943.60 (-) [1,000.00]	544.48 (56.40) [33]
Road Transport And Highways					
1540	2-LANING WITH PAVED SHOULDER OF SITARGANJ - TANAKUR SECTION OF NH-125	9/2015	9/2016 (-) [0/0]	368.73 (-) [368.73]	242.67 (0.00) [0]
1541	2-LANING WITH PAVED SHOULDERS OF RAEBARELI - BANDA SECTION OF NH-232	4/2014	1/2016 (-) [0/0]	351.34 (-) [417.68]	433.68 (66.34) [0]
1542	2-LANING WITH PAVED SHOULDERS OF TANDA - RAEBARELI	4/2014	1/2016 (-) [0/0]	495.78 (-) [627.93]	633.24 (132.15) [0]
1543	2-LANING WITH PS RAIBAREILI TO ALLAHABAD	7/2012	1/2014 (-) [0/0]	291.36 (-) [469.31]	459.07 (177.95) [0]
1544	4 LANNING OF LUCKNOW-SULTANPUR SECTION OF NH-56 FROM KM 11.500	8/2016	4/2019 (-) [0/0]	2,016.00 (-) [2,016.00]	1,996.00 (0.00) [0]
1545	4-LANING OF ALIGARH-KANPUR SECTION FROM KM 229.000 (DESIGN CHAINAGE 240.897) TO KM 289.000 (DESIGN C	3/2018	/ (-) [0/0]	1,120.57 (-) [1,332.00]	1,441.15 (211.43) [0]
1546	4-LANING OF GAGALHERI- SAHARANPUR-YAMUNANAGAR (UP/HARYANA BORDER) SECTION OF NH-73 FROM KM 33.000 (	3/2016	/ (-) [0/0]	1,668.00 (-) [1,668.00]	946.08 (0.00) [0]
1547	4-LANING OF GHAGHRA BRIDGE TO VARANSI (PACKAGE -I)	12/2015	6/2016 (-) [0/0]	611.65 (-) [611.65]	728.24 (0.00) [0]
1548	4-LANNING OF HARIDWAR-NAGINA SECTION OF NH-74 FROM KM 0.000 (KM 204.300 OF NH-58) TO KM 73.00	3/2016	/ (-) [0/0]	1,408.00 (-) [1,408.00]	442.70 (0.00) [0]
1549	4-LANNING OF NAGINA-KASHIPUR SECTION OF NH-74 FROM KM 73.00 TO KM 175.00	3/2016	/ (-) [0/0]	1,737.00 (-) [1,737.00]	1,159.07 (0.00) [0]
1550	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-	3/2016	/	1,404.50	2,977.58

	29 FROM 12.00 TO 88.00 KM [PACKAGE-II] (GORAKPUR)		(-) [0/0]	(-) [1,404.50]	(0.00) [0]
1551	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 148.00 TO 208.300 KM [PACKAGE-IV]	3/2016	4/2019 (-) [0/0]	1,587.49 (-) [2,982.00]	276.87 (1,394.51) [0]
1552	4-LANNING OF VARANASI GORAKHPUR SECTION OF NH-29 FROM 88.00 TO 148.00 KM 4-LANNING OF VARANASI GORAKHPUR	3/2016	/ (-) [0/0]	1,396.74 (-) [1,396.74]	227.26 (0.00) [0]
1553	6-LANNING OF HANDIA-VARANASI SECTION OF NH-2 FROM KM 713.146 TO KM 785.544 IN THE STATE OF UTTAR PRA	3/2017	3/2020 (-) [0/0]	2,064.99 (-) [2,447.00]	2,118.76 (382.01) [0]
1554	ADDITIONAL FACILITY FOR 4-LANE DIVIDED HIGHWAY OF KM 52.250 TO KM 130.560 OF NH-58 (MEERUT-MUZAFFARN)	12/2017	/ (-) [0/0]	207.00 (-) [207.00]	0.00 (0.00) [0]
1555	ALIGARH MORADABAD SECTION OF NH-93 FROM KM 85.650 TO KM 232.020	3/2016	4/2019 (-) [0/0]	676.73 (-) [676.73]	0.00 (0.00) [0]
1556	CONSTRUCTION OF 4 LANE NH-29 BYPASS PHASE-II CONNECTING NH-29 WITH NH-2 AS PART OF VARANASI RING ROAD	2/2018	/ (-) [0/0]	972.77 (-) [972.77]	494.71 (0.00) [0]
1557	CONSTRUCTION OF GORAKHPUR BYPASS FROM EXISTING KM 79.670 OF NH-29E TO EXISTING KM 251.700 OF NH-28 T	12/2016	/ (-) [0/0]	534.55 (-) [531.00]	433.62 (-3.55) [0]
1558	CONSTRUCTION OF NH-24 4-LANE BYPASS STARTING FROM KM 479.500 OF NH-24 AND TERMINATING AT KM 17.600 O	12/2017	/ (-) [0/0]	305.00 (-) [305.00]	0.00 (0.00) [0]
1559	CONSTRUCTION OF NH-24 EXTENSION 4-LANE BYPASS STARTING FROM BEHTA ROAD AND TERMINATING AT SITAPUR ROAD	3/2018	/ (-) [12/2021]	1,117.84 (-) [1,117.84]	0.00 (0.00) [-]
1560	CONSTRUCTION OF NH-28 4-LANE BYPASS STARTING FROM KM 17.600 OF MDR-77C AND TERMINATING AT KM 15.650	1/2017	/ (-) [0/0]	450.68 (-) [450.68]	397.62 (0.00) [0]
1561	CONSTRUCTION OF RING ROAD FOR RAEBARELI CITY (PHASE -I) ON EASTERN SIDE OF NH 24B	1/2014	3/2016 (-) [0/0]	282.41 (-) [282.41]	155.53 (0.00) [0]
1562	DELHI-MEERUT EXPRESSWAY PKG-III 6 LANNING FROM KM 27.740 TO 49.346 KM	1/2016	6/2019 (-) [0/0]	1,081.57 (-) [1,057.60]	480.25 (-23.97) [0]
1563	DESIGN AND CONSTRUCTION OF DELHI-MEERUT EXPRESSWAY FROM DASNA TO MEERUT FROM 27.740 OF NH-24 TO KM	12/2017	/ (-) [0/0]	1,232.21 (-) [1,087.00]	562.94 (-145.21) [0]
1564	DEVELOPMENT OF DELHI MEERUT EXPRESSWAY FROM KM.0.000 TO KM 27.500 INCLUDING 6/8 LANNING OF NH-24 FRO	3/2017	3/2020 (-) [0/0]	1,989.00 (-) [1,989.00]	521.56 (0.00) [0]
1565	ETAWAH CHAKERI	3/2013	9/2015 (-) [0/0]	1,573.00 (-) [1,573.00]	2,093.25 (0.00) [0]
1566	FOR REHABILITATION AND UPGRADATION FROM 2-LANE TO 4-LANE OF VARANASI - DEGAMAPUR (PKG-1) UNDER NHDP	2/2018	/ (-) [0/0]	670.50 (-) [670.50]	75.10 (0.00) [0]
1567	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-I FROM ALIGARH - BHADWAS	3/2018	/ (-) [0/0]	809.07 (-) [809.07]	751.07 (0.00) [0]
1568	FOUR LANING OF ALIGARH - KANPUR SECTION PKG-II FROM BHADWAS - KALYANPUR.	3/2018	/ (-) [0/0]	925.40 (-) [1,197.00]	1,176.70 (271.60) [0]
1569	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-II)	12/2015	6/2018 (-) [0/0]	667.00 (-) [667.00]	549.07 (0.00) [0]
1570	FOUR LANING OF GHAGHRA BRIDGE TO VARANASI (PKG-III)	6/2016	7/2018 (-)	667.00 (-)	464.05 (0.00)

			[0/0]	[667.00]	[0]
1571	FOUR LANING OF SULTANPUR TO VARANASI (PKG-I)	1/2016	6/2018 (-) [0/0]	1,027.53 (-) [1,027.53]	601.13 (0.00) [0]
1572	FOUR LANING OF SULTANPUR TO VARANASI (PKG-II)	1/2016	6/2018 (-) [0/0]	815.28 (-) [815.28]	520.89 (0.00) [0]
1573	FOUR LANING OF VARANASI BYPASS	5/2015	5/2017 (-) [0/0]	261.09 (-) [261.09]	240.96 (0.00) [0]
1574	FOUR LANING WIDENING AND STRENGTHENING OF NH-29E FROM KM 81.420 TO 99.00 SONAULI - GORAKHPUR ROAD (J)	3/2018	8/2020 (-) [12/2021]	288.30 (-) [288.30]	160.68 (0.00) [16]
1575	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-I) FROM KM 0.00 TO KM 76.3(EXISTING KM 106.300 OF NH-2	3/2017	3/2020 (12/2021) [12/2021]	1,373.28 (-) [1,373.28]	1,285.22 (0.00) [21]
1576	FOUR LANNING OF JHANSI-KHAJURAHO SECTION(PKG-II) OF NH-75/76 FROM DESIGN CHAINAGE KM 76.3(EXISTING C	3/2017	3/2020 (-) [0/0]	1,184.71 (-) [1,310.00]	1,286.42 (125.29) [0]
1577	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 0.000 (KM. 190.000 OF NH-24) TO KM 42.791	3/2016	4/2019 (-) [0/0]	899.00 (-) [899.00]	450.47 (0.00) [0]
1578	GHAZIABAD-ALIGARH NH-91	2/2011	8/2013 (-) [0/0]	1,141.00 (-) [1,141.00]	1,715.00 (0.00) [0]
1579	IMPROVEMENT AND UP-GRADATION OF EXISITING CARRIAGEWAY TO TWO LANE WITH PAVED SHOULDER FROM KM 0.00 T	11/2018	/ (-) [0/0]	281.45 (-) [281.45]	0.00 (0.00) [0]
1580	MEERUT-BULANDSHAHR	1/2016	/ (-) [0/0]	683.24 (-) [987.94]	0.00 (304.70) [0]
1581	R AND U OF KHUTAR - LAKHIMPUR SECTION (KM 82.00 TO KM140.00) OF NH-730 TO 2L WITH PS	11/2016	/ (-) [12/2021]	326.99 (327.00) [326.99]	122.02 (0.00) [-]
1582	R AND U OF LAKHIMPUR - SISIYA SECTION (KM140.00 TO 188.800) OF NH-730 TO 2L WITH PS	3/2016	9/2020 (-) [8/2021]	296.50 (-) [296.50]	237.08 (0.00) [11]
1583	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP IV B FOR LALGANJ-HANU	3/2018	/ (-) [0/0]	1,025.80 (-) [677.07]	222.94 (-348.73) [0]
1584	REHABILITATION AND UP-GRADATION FROM 2 LANE TO 4 LANE OF NH STRETCH UNDER NHDP-IVB FOR DAGAMAGPUR-LA	3/2018	/ (-) [0/0]	1,115.28 (-) [770.04]	332.69 (-345.24) [0]
1585	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO 2 LANE WITH PS FROM KM 537.000 TO KM 564.750	3/2018	4/2020 (-) [12/2021]	263.89 (-) [242.05]	189.09 (-21.84) [20]
1586	REHABILITATION AND UPGRADATION OF RAMNAGAR TO SISWA BABU SECTION FROM KM 484.000 TO KM 505.120 OF	3/2018	2/2020 (-) [0/0]	185.18 (-) [185.18]	124.59 (0.00) [0]
1587	REHABILITATION AND UPGRADATION OF TULSIPUR - BARHANI SECTION FROM KM 351.000 TO KM 385.000 OF NH-730	3/2016	5/2019 (-) [5/2021]	249.50 (-) [249.50]	228.82 (0.00) [0]
1588	REHABILITATION AND UPGRADATION OF ALLAHABAD - MIRZAPUR SECTION FROM KM 450.000 TO KM 486.770 (EXCEPT	10/2016	3/2020 (-) [0/0]	218.90 (-) [218.90]	145.28 (0.00) [0]
1589	REHABILITATION AND UPGRADATION OF EXISTING PAVEMENT TO FOUR LANE WITH PAVED SHOULDER FROM KM 135.230	3/2018	/ (-) [9/2021]	306.59 (-) [306.59]	168.16 (0.00) [-]
1590	REHABILITATION AND UPGRADATION OF KABRAI-BANDA FROM KM 178.00 TO KM 215.00 OF NH-76 TO 2-LANE WITH P	11/2016	9/2019 (-) [10/2019]	215.16 (215.00) [215.16]	145.76 (0.00) [0]

1591	REHABILITATION AND UPGRADATION OF KALUPUR-LALTA FROM KM 285.00 TO KM 326.00 OF NH-76 TO 2-LANE WITH	3/2016	1/2020 (-) [0/0]	240.30 (240.00) [240.30]	210.10 (0.00) [0]
1592	REHABILITATION AND UPGRADATION OF SULTANPUR BYPASS SECTION OF NH-96 FROM KM 60.000 TO KM 90.865 TO	7/2016	10/2019 (-) [0/0]	208.88 (-) [208.88]	175.79 (0.00) [0]
1593	SIX LANING OF CHAKERI TO ALLAHABAD SECTION OF NH-2 FROM KM 483.687 TO KM 628.753 (DESIGN LENGTH – 14	11/2017	1/2019 (-) [0/0]	2,159.00 (-) [2,159.00]	1,602.06 (0.00) [0]
1594	SIX LANING OF HAPUR BYPASS TO MORADABAD SECTION INCLUDING HAPUR BYPASS FROM KM 50.000 (DESIGN CHAINA	3/2018	/ (-) [0/0]	2,140.93 (-) [2,140.93]	1,315.69 (0.00) [0]
1595	TWO / FOUR LANING OF RAEBARELI - JAGDISHPUR SECTION OF NH-330A FROM KM. 0.000 TO KM. 47.800 (DESIGN	10/2020	3/2023 (-) [3/2023]	724.60 (720.81) [724.60]	0.00 (0.00) [0]
1596	VARANASI RING ROAD PKG - I	1/2018	/ (-) [0/0]	450.77 (-) [450.77]	0.00 (0.00) [0]
1597	WIDNG WITH PS AND STRNG FROM KM.0.00 TO 50.675 OF NH-730A EPC MODE	5/2013	8/2015 (-) [0/0]	164.54 (-) [164.54]	128.54 (0.00) [0]
	<u>Steel</u>				
1598	FORGED WHEEL PLANT	4/2014	9/2018 (9/2021) [9/2021]	1,682.85 (-) [2,100.00]	1,704.90 (417.15) [36]
	<u>Urban Development</u>				
1599	AGRA METRO RAIL PROJECT	5/2019	3/2024 (-) [5/2025]	8,379.62 (-) [8,379.62]	364.47 (0.00) [14]
1600	KANPUR METRO RAIL PROJECT	5/2019	3/2024 (-) [3/2025]	11,076.48 (-) [11,076.48]	1,690.78 (0.00) [12]
1601	LUCKNOW METRO RAIL CORPORATION LTD	1/2016	3/2019 (-) [0/0]	6,928.00 (6,928.00) [6,928.00]	6,928.00 (0.00) [0]
	<u>Water Resources</u>				
1602	FARRUKHABAD I AND D AND STP WORKS HAM	10/2017	3/2022 (-) [3/2022]	213.62 (261.12) [261.12]	0.00 (47.50) [0]
1603	INTEGRATED PROJECT FOR DEVELOPMENT OF STPS IN ALLAHABAD ALONG WITH EXISTING ASSETS	3/2018	9/2021 (-) [9/2021]	904.00 (-) [904.00]	148.55 (0.00) [0]
1604	INTERCEPTION AND DIVERSION WORKS AND SEWAGE TREATMENT PLANT AT JAUNPUR UTTAR PRADESH	1/2019	10/2021 (-) [10/2021]	206.05 (-) [206.05]	53.62 (0.00) [0]
1605	INTERCEPTION AND DIVERSION WORKS AND STP AT MUZAFFARNAGAR UTTAR PRADESH	1/2019	12/2021 (-) [12/2021]	231.79 (-) [234.03]	0.00 (2.24) [0]
1606	INTERCEPTION AND DIVERSION WORKS WITH STP AT BAREILLY, UTTAR PRADESH	3/2019	8/2021 (-) [8/2021]	271.39 (-) [271.39]	0.00 (0.00) [0]
1607	INTERCEPTION AND DIVERSION WORKS WITH STP AT LUCKNOW UTTAR PRADESH	3/2019	7/2021 (-) [6/2022]	298.12 (213.91) [213.91]	0.00 (-84.21) [11]
1608	INTERCEPTION, DIVERSION AND TREATMENT WORKS FOR NAINI DISTRICT G PHAPHAMAU DISTRICT F AND JHUSI AREA	5/2017	9/2021 (-) [9/2021]	767.59 (-) [767.59]	112.27 (0.00) [0]
1609	MATHURA SEWERAGE SCHEME	12/2017	12/2020 (-) [5/2021]	460.45 (-) [460.45]	248.16 (0.00) [0]
1610	SEWAGE TREATMENT PLANT FOR ASSI-BHU SEWERAGE	2/2017	11/2019	161.31	91.38

	DISTRICT AT RAMANA		(-) [3/2021]	(-) [161.31]	(0.00) [0]
1611	SEWERAGE SCHEME INTERCEPTION AND DIVERSION WITH STP WORKS AT MEERUT UTTAR PRADESH	2/2019	6/2022 (-) [6/2022]	681.78 (-) [690.71]	0.00 (8.93) [0]
1612	SEWERAGE SYSTEM AND STP WORKS PHASE I AT MORADABAD RAMGANGA	2/2011	12/2019 (-) [1/2021]	279.91 (330.05) [330.05]	244.84 (50.14) [0]
1613	SEWERAGE WORKS IN SEWERAGE DISTRICT I OF KANPUR	10/2016	8/2020 (3/2021) [0/0]	370.40 (430.49) [430.49]	396.14 (60.09) [0]
1614	STP AT PANKHA KANPUR AND INTEGRATION WITH EXISTING STPS	3/2018	9/2021 (-) [9/2021]	967.23 (-) [967.23]	51.66 (0.00) [0]
	<u>UTTARAKHAND</u>				
	<u>Civil Aviation</u>				
1615	CONSTRUCTION OF DOMESTIC PASSENGER TERMINAL BUILDING AT DEHRADUN AIRPORT, DEHRADUN	7/2018	9/2020 (-) [9/2022]	456.86 (-) [456.86]	306.08 (0.00) [24]
	<u>Home Affairs</u>				
1616	CONSTRUCTION OF ITBP ROAD TO INDO-CHINA BORDER FROM NYU SOBLA SELA TO TEDANG IN THE STATE OF UTTARA	12/2008	12/2013 (-) [0/0]	114.26 (266.00) [266.00]	0.00 (151.74) [0]
	<u>Petroleum</u>				
1617	SITARGANJ LPG PROJECT	2/2017	2/2020 (6/2021) [10/2021]	160.10 (-) [160.10]	102.85 (0.00) [20]
	<u>Power</u>				
1618	LATA-TAPOVAN HYDRO ELECTRIC POWER PROJECT 3X57 MW	7/2012	8/2017 (-) [0/0]	1,527.00 (-) [1,801.07]	149.93 (274.07) [0]
1619	NAITWAR MORI HEP	10/2017	12/2021 (6/2022) [6/2022]	648.33 (-) [947.89]	657.62 (299.56) [6]
1620	TAPOVAN-VISHNUGAD HEP (4X130MW)	11/2006	3/2013 (12/2021) [0/0]	2,978.48 (5,867.38) [5,867.38]	5,045.40 (2,888.90) [0]
1621	TEHRI PUMPED STORAGE PLANT(1000MW)	7/2006	2/2016 (-) [6/2023]	1,657.00 (4,825.60) [4,825.60]	4,170.24 (3,168.60) [88]
1622	VISHNUGAD PIPALKOTI HYDRO ELECTRIC PROJECT	8/2008	6/2013 (11/2018) [6/2024]	2,491.58 (3,860.35) [3,860.35]	2,271.34 (1,368.77) [132]
	<u>Railways</u>				
1623	HARIDWAR-LAKSAR	4/2012	/ (-) [0/0]	219.83 (-) [346.63]	204.53 (126.80) [0]
1624	KICHHA-KHATIMA (NL) - NER	4/2003	/ (-) [0/0]	142.45 (-) [228.40]	0.15 (85.95) [0]
1625	RISHIKESH - KARNAPRAYAG NEW LINE	4/2011	12/2024 (-) [3/2025]	16,216.00 (-) [22,716.11]	2,045.67 (6,500.11) [3]
	<u>Road Transport And Highways</u>				
1626	2 LANE WITH PAVED SHOULDER FROM KM 399.00 TO KM 430.00 OF KARANPARYAG TO CHAMOLI UNDER CHARDHAM PARI	3/2018	6/2018 (-) [3/2022]	403.36 (-) [403.36]	330.75 (0.00) [45]
1627	2 LANE WITH PAVED SHOULDER FROM KM 430.00 TO KM 468.00 OF CHAMOLI TO PAINI UNDER CHARDHAM PARIYOJNA	3/2018	5/2018 (-) [3/2022]	417.24 (-) [417.24]	325.44 (0.00) [46]
1628	4 LANING OF KASHIPUR-SITARGANJ SECTION KM.	11/2012	7/2018	605.84	722.46

	175.000 TO KM. 252.20		(-) [0/0]	(-) [722.46]	(116.62) [0]
1629	4-LANNING OF CHUTMALPUR-GANESHPUR SECTION OF NH-72A FROM KM 0.000 (KM 22.825 OF MH-73) TO KM 17.900	3/2016	/	1,443.00	1,246.85
			(-) [0/0]	(-) [1,443.00]	(0.00) [0]
1630	CONSTRUCTION AND UPGRADATION OF EXISTING ROAD TO 2 LANE WITH PAVED SHOULDER FROM KM 368.00 TO KM 399	3/2018	5/2018 (-) [3/2022]	274.31 (-) [274.31]	208.47 (0.00) [46]
1631	CONSTRUCTION OF 4.5 KM LONG SILKYARA TUNNEL BETWEEN KM 25.40 TO 50.25 KM (TUNNEL WORK)	3/2018	7/2018 (-) [7/2022]	1,383.78 (-) [1,383.78]	387.45 (0.00) [48]
1632	CONSTRUCTION OF KUND BYPASS FROM EXISTING KM 33+130 TO KM 41+260 (EXISTING LENGTH: 8.130 KM); DESIGN	5/2018	5/2020 (12/2021) [12/2021]	248.00 (-) [248.00]	109.23 (0.00) [19]
1633	FOUR LANNING OF RAMPUR- KATHGODAM SECTION OF NH-87 FROM KM 42.791 (DESIGN CHAINAGE 43.446) TO KM 88	3/2016	/	720.00	206.32
			(-) [0/0]	(-) [720.00]	(0.00) [0]
1634	HARIDWAR DEHRADUN APPROVED LENGTH 69	11/2011	10/2013 (-) [0/0]	478.51 (-) [478.00]	315.11 (-0.51) [0]
1635	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF EXISTING TWO LANE TO 2- LANE WITH PAVED SHOULDERS CONFIG	11/2017	11/2019 (7/2021) [7/2021]	232.81 (-) [232.81]	171.22 (0.00) [0]
1636	RECONSTRUCTION WITH GEOMETIC IMPROVEMENT OF SINGLE LANE TO 2- LANE WITH PAVED SHOULDER CONFIGURATION	11/2017	11/2019 (5/2021) [5/2021]	283.51 (-) [283.51]	246.37 (0.00) [0]
1637	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (7/2021) [7/2021]	257.34 (-) [257.34]	214.90 (0.00) [0]
1638	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	12/2017	12/2019 (7/2021) [7/2021]	200.34 (-) [200.34]	185.44 (0.00) [0]
1639	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING 2 LANE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	6/2017	6/2019 (12/2021) [12/2021]	282.08 (-) [282.08]	201.79 (0.00) [30]
1640	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2 LANE WITH EAR	2/2018	2/2020 (9/2021) [9/2021]	418.88 (-) [418.88]	287.56 (0.00) [19]
1641	RECONSTRUCTION WITH GEOMETRIC IMPROVEMENT OF EXISTING SINGLE/INTERMEDIATE LANE TO 2LANE WITH PAVED S	11/2017	11/2019 (11/2019) [11/2019]	266.52 (-) [266.52]	0.00 (0.00) [0]
1642	RECONSTRUCTION WITH GEOMETRIC IMPROVMENT OF EXISTING INTERMEDIATE LANE TO 2 LANE WITH PAVED SHOULDER	8/2016	12/2017 (12/2019) [12/2019]	234.88 (-) [208.89]	0.00 (-25.99) [0]
1643	REHABILITATION AND UP GRADATION OF 2 LANE/ 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 172.900 TO K	2/2018	/	293.68	179.19
			(10/2021) [10/2021]	(-) [293.68]	(0.00) [-]
1644	REHABILITATION AND UPGRADATION OF 2 LANE WITH PAVED SHOULDER FROM EXISTING KM. 195.175 TO KM. 220.00	3/2018	/	460.73	116.25
			(-) [0/0]	(-) [461.00]	(0.27) [0]
1645	WIDENING OF EXISTING SINGLE LANE ROAD TO TWO LANE WITH PAVED SHOULDERS CONFIGURATION FROM KM. 235.00	12/2017	12/2019 (8/2021) [8/2021]	248.22 (-) [248.22]	234.12 (0.00) [20]
	<u>Water Resources</u>				
1646	INTERCEPTION AND DIVERSION WITH STP AT RISHIKESH	3/2017	11/2019 (3/2021) [0/0]	158.00 (-) [158.00]	84.05 (0.00) [0]
	<u>WEST BENGAL</u>				
	<u>Civil Aviation</u>				
1647	AIRSIDE CAPACITY ENHANCEMENT OF NSBI AIRPORT, KOLKATA	1/2019	11/2021 (1/2023)	389.71 (-)	191.88 (0.00)

			[1/2023]	[389.71]	[14]
1648	CONSTRUCTION OF ATC TOWER AND TECHNICAL BLOCK AT NSCBI AIRPORT KOLKATA	1/2016	3/2020 (7/2022) [7/2022]	458.00 (-) [458.00]	149.44 (0.00) [28]
	<u>Coal</u>				
1649	2.0 MTPA BHOJUDIH NLW WASHERY	12/2015	3/2017 (-) [3/2022]	304.13 (341.22) [341.22]	64.19 (37.09) [60]
1650	EXPANSION PR OF JHANJRA UG(5.00 MTY)	11/2015	3/2022 (3/2029) [3/2029]	1,210.12 (-) [1,210.12]	49.04 (0.00) [84]
1651	NAKRAKONDA KUMARDIH B OCP	8/2018	3/2029 (-) [3/2029]	502.68 (-) [502.68]	15.70 (0.00) [0]
1652	PARASEA- BELBAID REORGANISATION UG MINE	7/2019	3/2027 (-) [3/2027]	826.42 (-) [826.42]	0.19 (0.00) [0]
1653	RANIGANJ MASTER PLAN	8/2009	8/2019 (-) [8/2024]	2,661.73 (-) [5,146.48]	622.13 (2,484.75) [60]
1654	SHYAMSUNDARPUR UG INCLUDING SAPI UNIT	4/2020	3/2025 (-) [3/2025]	483.65 (-) [483.65]	4.39 (0.00) [0]
1655	SIDULI MINE (OC AND UG)	5/2018	3/2026 (-) [3/2026]	535.18 (-) [535.18]	1.53 (0.00) [0]
1656	SONEPUR BAZARI (COMB) OCP (8.0 MTY)	8/2012	3/2018 (-) [10/2021]	1,055.05 (-) [1,055.05]	689.34 (0.00) [43]
1657	TILABONI UG MINE	2/2019	3/2027 (-) [3/2027]	916.62 (-) [916.62]	1.17 (0.00) [0]
	<u>Department Of Higher Education</u>				
1658	CONSTRUCTION OF TWO NOS GIRLS HOSTELS AND ONE NO BOYS HOSTEL OF 500 CAPACITY EACH G PLUS 8 STOREYED	3/2020	6/2020 (-) [0/0]	193.83 (-) [193.83]	0.45 (0.00) [0]
	<u>Health And Family Welfare</u>				
1659	CNCI KOLKATA WEST BENGAL	8/2016	9/2018 (-) [5/2019]	244.00 (-) [248.00]	224.92 (4.00) [0]
1660	CONSTRUCTION OF HOSPITAL BLOCK, IIT, KHARAGPUR	12/2014	5/2017 (-) [7/2019]	168.90 (-) [191.20]	169.51 (22.30) [0]
1661	HOSPITAL AND TEACHING- AIIMS KALYANI	4/2018	/ (-) [9/2021]	651.99 (-) [651.99]	568.10 (0.00) [-]
1662	RESIDENTIALCOMPLEX AND OPD BLOCK, AIIMS, KALYANI WEST BENGAL	8/2017	3/2019 (-) [9/2021]	355.15 (-) [355.15]	313.77 (0.00) [30]
	<u>Home Affairs</u>				
1663	NSG AT KOLKATA	10/2014	4/2018 (12/2021) [12/2021]	162.88 (238.00) [238.00]	172.12 (75.12) [44]
	<u>Petroleum</u>				
1664	30 INCH CRUDE OIL PIPELINE IN HALDIA-BARAUNI SECTION OF PHBPL AND CONVERSION OF EXISTING 18 INCH HAL	3/2018	9/2022 (-) [3/2022]	3,712.00 (-) [3,696.00]	2,213.96 (-16.00) [-6]
1665	CITY GAS DISTRIBUTION IN WEST BENGAL	3/2019	3/2031 (8/2031) [8/2031]	5,830.20 (-) [5,830.20]	120.62 (0.00) [5]
1666	DURGAPUR-HALDIA PIPELINE PROJECT	3/2017	12/2020	1,740.00	912.00

			(12/2021) [12/2021]	(-) [1,740.00]	(0.00) [12]
1667	INSTALLATION OF SECOND CATALYTIC DEWAXING UNIT (CDW-II) AT HALDIA REFINERY	6/2020	1/2023 (-) [5/2023]	1,019.00 (-) [1,019.00]	85.59 (0.00) [4]
1668	KHARAGPUR LPG BOTTLING PLANT	4/2017	4/2020 (10/2021) [10/2021]	163.02 (207.36) [207.36]	122.11 (44.34) [18]
	<u>Power</u>				
1669	DURGAPUR PP-III (2X20 MW) - NSPCL	12/2016	11/2018 (-) [12/2021]	529.68 (633.80) [633.80]	461.33 (104.12) [37]
1670	EASTERN REGION STRENGTHENING SCHEME-XV	4/2016	4/2018 (3/2021) [6/2021]	454.11 (-) [454.11]	344.89 (0.00) [0]
1671	RAMMAM-III HEPP (3X40 MW)	9/2014	9/2019 (12/2024) [12/2024]	1,381.84 (-) [1,381.54]	704.78 (-0.30) [63]
	<u>Railways</u>				
1672	BANKURA DAMODAR VALLEY RLY LINE 96 KM GC WITH 6MMS FOR NL	4/1998	3/2003 (-) [3/2030]	1,027.40 (-) [2,373.00]	485.04 (1,345.60) [324]
1673	BARDHAMAN-KATWA (GC)	4/2007	12/2010 (-) [3/2025]	1,106.62 (-) [1,091.59]	1,001.66 (-15.03) [171]
1674	BAZAR SAU -AZIMGANJ JN. DOUBLING	4/2012	/ (-) [3/2022]	255.64 (-) [272.20]	283.69 (16.56) [-]
1675	BOWAICHANDI-ARAMBAGH	4/2010	/ (-) [3/2025]	267.37 (-) [620.00]	40.99 (352.63) [-]
1676	CIRCULAR RAILWAY INCLUDING REMOUNT ROAD TO SANTOSH PUR	4/2009	/ (-) [3/2025]	573.78 (-) [268.52]	0.03 (-305.26) [-]
1677	EAST WEST METRO CORRIDOR FROM HOWRAH MAIDAN TO SALT LAKE	3/2013	3/2016 (-) [0/0]	4,874.58 (-) [8,574.97]	5,892.72 (3,700.39) [0]
1678	HOWRAH-AMTA-CHAMPADANGA NL (SER)	4/1974	3/2007 (3/2007) [0/0]	393.46 (154.30) [1,026.00]	182.49 (632.54) [0]
1679	NEW BG LINE FROM KALIYAGANJ TO BUNIADPUR	4/2010	/ (-) [0/0]	221.42 (-) [380.00]	38.20 (158.58) [0]
1680	NEW BG RLY LINE FROM EKLAKHI-BALURGHAT INCLUDING GAZOLE-ITAHAR(NL),NEFR	4/1983	3/2019 (-) [0/0]	297.32 (200.34) [614.00]	275.06 (316.68) [0]
1681	NEW JALPAIGURI-SILIGURI-NEW BONGAIGAON GC WITH MM OF NEW LINE OF CHALSA-NAXAL AND RAJABHATKHAWA-JAIN	2/1999	4/2010 (-) [0/0]	380.60 (-) [1,090.60]	1,089.12 (710.00) [0]
1682	NEW MAYNAGURI-GUMANIHAT-DOUBLING OF REMAINING PORTION (51.65 KM)	4/2016	12/2021 (-) [9/2021]	602.27 (-) [2,144.78]	977.32 (1,542.51) [-3]
1683	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM BARANAGAR TO BARRACKPORE AND DAKSHINESHWAR (MTP)	4/2010	3/2014 (-) [12/2025]	2,298.42 (-) [2,733.86]	40.46 (435.44) [141]
1684	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM JOKA TO BINOY BADAL DINESH BAGH.	4/2010	3/2016 (-) [3/2025]	2,913.51 (-) [4,639.00]	888.31 (1,725.49) [108]
1685	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NOAPARA-BARASAI VIA BIMANBANDER (MTP)	4/2010	3/2016 (-) [0/0]	2,397.72 (-) [2,397.72]	197.20 (0.00) [0]

1686	NEW WORK FOR CONSTRUCTION OF METRO RAILWAY FROM NSCB AIRPORT TO NEW GARIA VIA RAJARHAT (MTP)	4/2010	3/2016 (-) [3/2025]	3,951.98 (-) [4,259.48]	2,453.42 (307.50) [108]
1687	TARAKESWAR - BISHNUPUR NEW BG LINE (NL), ER	4/2000	3/2019 (12/2009) [3/2025]	1,188.91 (-) [1,619.48]	906.00 (430.57) [72]
1688	TOLLYGANJ-GARIA WITH EXTENSION TO DUM DUM-NOAPARA AND NOAPARA-NSCB AIRPORT(MTP)	3/2000	12/2006 (-) [0/0]	1,049.69 (-) [3,404.92]	3,837.57 (2,355.23) [0]
Road Transport And Highways					
1689	4 LANING OF NH-31D FROM GHOSHPUKUR - SALSALABARI (KM 0.00 TO KM . 83.785)	12/2015	6/2018 (-) [0/0]	1,083.00 (2,587.75) [1,827.15]	989.55 (744.15) [0]
1690	4-LANING OF BRAHAMPORE-FARAKA	2/2011	8/2013 (-) [6/2023]	998.79 (-) [998.79]	1,890.84 (0.00) [118]
1691	4-LANING OF FARAKA-RAIGANJ	2/2011	8/2013 (-) [8/2021]	1,078.84 (-) [1,078.84]	2,301.82 (0.00) [96]
1692	6-LANING OF DHANKUNI-KHARAGPUR SECTION	4/2012	9/2014 (-) [0/0]	1,396.18 (-) [1,396.18]	1,396.18 (0.00) [0]
1693	CONSTRUCTION OF ISLAMPUR BY PASS	10/2015	/ (-) [0/0]	361.15 (363.93) [363.93]	277.34 (2.78) [0]
1694	CONSTRUCTION OF NEW ROAD AT THE MISSING LINK PORTION OF NH-81 ALONG THE APPROVED ALIGNMENT BETWEEN H	3/2016	11/2018 (1/2021) [3/2022]	271.17 (291.20) [291.20]	120.14 (20.03) [40]
1695	CONSTRUCTION OF ROB AND ITS APPROACHES IN LIEU OF UNMANNED LEVEL CROSSING AT KM 303.9 ON NH-60 (PAND	3/2016	8/2019 (-) [11/2022]	160.27 (213.97) [213.97]	26.72 (53.70) [39]
1696	CONSTRUCTION OF ROB -FLYOVER AT RANICHAK, HALDIA	3/2016	11/2018 (-) [0/0]	229.37 (-) [229.37]	0.00 (0.00) [0]
1697	CONSTRUCTION OF TWINS 2-LANE ROB AND ITS APPROACHES IN REPLACEMENT OF EXISTING LEVEL CROSSING GATE N	6/2016	8/2019 (8/2022) [8/2022]	236.78 (263.26) [263.26]	72.02 (26.48) [36]
1698	DEVELOPMENT OF 4-LANING SECTION OF NH-31 FROM KM 551.36 (GHOSHPUKUR) TO KM 563.26 (BIHAR MORE, BAGDO	3/2018	10/2020 (3/2021) [6/2021]	254.30 (254.30) [254.30]	116.66 (0.00) [0]
1699	FOUR LANNING OF CHICHRA-KHARAGPUR SECTION OF NH-6 FROM KM 185.150 TO KM 134.400 INCLUDING REHABILITA	9/2016	8/2018 (-) [0/0]	767.03 (-) [767.03]	696.60 (0.00) [0]
1700	REHABILITATION AND UP GRADATION TO FOUR LANING OF NH-31D FROM KM 113.200 TO KM 154.854 (PACKAGE IIA)	3/2018	/ (-) [0/0]	1,261.98 (2,145.96) [1,952.20]	97.16 (690.22) [0]
1701	REHABILITATION AND UPGRADATION OF PUNDIBARI TO BAXIRHAT (WB/ASSAM BORDER) SECTION OF NH-31 FROM KM 7	4/2014	8/2017 (-) [2/2020]	279.70 (398.52) [398.52]	331.86 (118.82) [0]
1702	REHABILITATION AND UPGRADATION TO 2-LANE WITH PAVED SHOULDER CONFIGURATION OF NANDAKUMAR-CONTAI-CHAN	1/2017	9/2019 (11/2021) [10/2021]	396.86 (396.86) [396.86]	271.47 (0.00) [25]
1703	SIX-LANING OF BARWA ADDA-PANAGARH	4/2014	/ (-) [0/0]	1,665.00 (-) [2,360.65]	4,495.94 (695.65) [0]
1704	UPGRADATION OF NH-512 WITH A MINIMUM 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM CH 82.4	2/2018	11/2020 (4/2021) [6/2021]	218.70 (218.70) [218.70]	104.19 (0.00) [0]
1705	UPGRADATION OF NH-81 WITH A MINIMUM OF 2-LANE WITH PAVED SHOULDER CONFIGURATION STARTING FROM KM 19.	2/2018	9/2020 (1/2022) [1/2022]	426.18 (426.18) [426.18]	254.29 (0.00) [16]

	<u>Steel</u>				
1706	REPLACEMENT OF CONVERTER SHELLS TOGETHER WITH BOTTOM STIRRING SYSTEM AND INSTALLATION OF SECONDARY E	12/2018	9/2020 (9/2021) [8/2021]	263.36 (-) [263.36]	253.46 (0.00) [11]
	<u>Water Resources</u>				
1707	SEWERAGE SYSTEM AND STP WORKS AT HALISHAHR	2/2014	12/2019 (5/2021) [0/0]	274.76 (-) [274.76]	217.98 (0.00) [0]
1708	DETAILED PROJECT REPORT FOR I AND D SEWERAGE SYSTEM AND STP FOR ASANSOL AND KULTI TOWNS	1/2019	4/2022 (-) [4/2022]	384.96 (-) [384.96]	0.00 (0.00) [0]
1709	I AND D AND STP WORKS AT BURDWAN WEST BENGAL	12/2018	4/2022 (-) [4/2022]	234.31 (-) [234.31]	0.00 (0.00) [0]
1710	INTEGRATION OF STPS WITH REHABILITATION AND O AND M OF EXISTING ASSETS	3/2018	6/2022 (-) [6/2022]	165.16 (-) [165.16]	0.00 (0.00) [0]
1711	INTERCEPTION AND DIVERSION WITH STP AT HUGHLY-CHINSURAH	5/2018	2/2022 (-) [10/2022]	160.00 (154.73) [154.73]	0.00 (-5.27) [8]
1712	INTERCEPTION AND DIVERSION WORKS WITH STP FOR DRAINS FALLING IN RIVER DAMODAR AT DURGAPURL	3/2019	4/2022 (-) [4/2022]	287.53 (-) [287.53]	0.00 (0.00) [0]
1713	INTERCEPTION AND DIVERSION WITH STP AT BALLY	10/2017	12/2021 (-) [12/2021]	164.93 (-) [164.93]	0.00 (0.00) [0]
1714	INTERCEPTION AND DIVERSION WITH STP AT MAHESHTALA	5/2018	2/2022 (-) [6/2022]	198.43 (224.69) [224.69]	0.00 (26.26) [4]
1715	INTERCEPTION DIVERSION TREATMENT WORKS AT TOLLYS NULLAH ADI GANGA	8/2017	9/2022 (-) [9/2022]	307.12 (-) [307.12]	0.00 (0.00) [0]
1716	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT BARANAGAR AND KAMARAHATI	1/2018	12/2021 (-) [12/2021]	172.10 (-) [172.10]	0.00 (0.00) [0]
1717	INTERCEPTION, DIVERSION AND TREATMENT WORKS AT HOWRAH	8/2017	12/2021 (-) [12/2021]	185.22 (-) [185.22]	0.00 (0.00) [0]
1718	SEWERAGE SYSTEM WITH SEWER NETWORK AT BARRACKPORE	12/2014	4/2020 (-) [3/2021]	272.32 (-) [272.32]	248.86 (0.00) [0]
	Total			21,99,181.52 (7,63,229.74) [26,36,710.50]	12,52,298.40 (4,37,528.98)
